

# ***YEAR 2 MONITORING REPORT***

## **ADKIN BRANCH STREAM RESTORATION PROJECT PHASE 1 – WASHINGTON AVE. TO LINCOLN ST.**

Lenoir County, North Carolina  
EEP IMS No. 7



Submitted to:



**NCDENR-Ecosystem Enhancement Program**  
217 West Jones Street, Suite 3000A  
Raleigh, North Carolina 27603

Construction Completed: April 2011  
Morphology Data Collected: October/November 2012  
Vegetation Data Collected: August 2012  
Submitted: January 2013



Prepared by:



&  
Axiom Environmental, Inc.  
218 Snow Avenue  
Raleigh, North Carolina 27603

Design Firm:  
**Florence & Hutcheson, Inc.**  
**5121 Kingdom Way, Suite 100**  
**Raleigh, North Carolina 27607**  
919.851.6066  
919.851.6846 (fax)

I HEREBY CERTIFY THAT THE DOCUMENTS CONTAINED HEREIN, ADKIN BRANCH YEAR 1 MONITORING REPORT WERE PREPARED BY ME OR UNDER MY DIRECT SUPERVISION.

SIGNED SEALED, AND DATED THIS 30<sup>TH</sup> DAY OF JANUARY 2013.



Chris L. Smith, PE







## TABLE OF CONTENTS

<b><u>SECTION</u></b>	<b><u>PAGE</u></b>
<b>1.0 EXECUTIVE SUMMARY.....</b>	<b>2</b>
1.1 GOALS AND OBJECTIVES .....	2
1.2 VEGETATION .....	3
1.3 STREAM STABILITY .....	4
1.4 WETLANDS.....	5
1.5 NOTE.....	5
<b>2.0 METHODOLOGY.....</b>	<b>5</b>
<b>3.0 RERFERENCES.....</b>	<b>6</b>
APPENDIX A. PROJECT VICINITY MAP AND BACKGROUND TABLES.....	7
APPENDIX B. VISUAL ASSESSMENT DATA .....	14
APPENDIX C. VEGETATION PLOT DATA .....	41
APPENDIX D. STREAM SURVEY DATA.....	46
APPENDIX E. HYDROLOGIC DATA.....	76
APPENDIX F. CREDIT CALCULATION FIGURES .....	77

### LIST OF FIGURES

<b><u>FIGURE</u></b>	<b><u>PAGE</u></b>
Figure 1. Vicinity Map.....	8
Figures 2.0-2.12. Current Condition Plan View .....	15
Figures 3.1-3.20. Vegetation Plot Photos and Problem Areas.....	33
Figures 4.1-4.17. Cross Section Plots and Photos .....	47
Figures 5.1-5.3. Longitudinal Profile Plots.....	65
Figures 6.1 & 6.2 Crest Gauge Photos.....	76
Figures D.1-D.5. Credit Calculation Figures.....	77

### LIST OF TABLES

<b><u>TABLE</u></b>	<b><u>PAGE</u></b>
Table 1. Project Components and Mitigation Credits.....	10
Table 2. Project Activity and Reporting History .....	11
Table 3. Project Contacts Table .....	12
Table 4. Project Attributes Table .....	13
Table 5.1-5.3. Visual Stream Morphology Stability Assessment.....	29
Table 6. Vegetation Condition Assessment.....	32
Table 7. Vegetation Plot Criteria Attainment .....	41
Table 8. CVS Vegetation Plot Metadata.....	42
Table 9.1-9.2. CVS Stem Count Total and Planted by Plot and Species.....	43
Table C.1&C.2 Bare Root/Ball and Burlap Species Replanted at Adkin Branch.....	45
Table 10.1-10.3. Baseline Stream Data Summary .....	69
Table 11. Monitoring Data - Dimensional Morphology Summary .....	72
Table 12.1-12.3. Monitoring Data - Stream Reach Data Summary.....	73
Table 13. Verification of Bankfull Events .....	76



## 1.0 EXECUTIVE SUMMARY

The following report summarizes the vegetation establishment and stream stability for Year 2 monitoring for Phase 1 of the Adkin Branch Stream Restoration Project (Site) in Lenoir County, North Carolina.

### 1.1 Goals and Objectives

The primary goals of the Adkin Branch Stream Restoration Project focus on:

- Restoring a stable dimension, pattern, and profile to Adkin Branch and UT to Adkin Branch (UT)
- Improving water quality
- Decreasing floodwater levels
- Restoring aquatic and riparian habitat
- Implementing best management practices (BMPs) for stormwater quality and retention

These goals will be achieved through the following objectives:

- Reducing sediment input to Adkin Branch by restoring 7,579 linear feet of stream to a stable dimension, pattern, and profile, and establishing a vegetated stream bank, floodplain, and terrace forest. Forest vegetation species were selected by studying a Reference Forest Ecosystem located directly upstream of the Project and reviewing species listed in *Classification of the Natural Communities of North Carolina: Third Approximation* (Schafale and Weakley 1990) for a Coastal Plain Levee Forest. A total of 32.44 acres of the conservation easement were reforested.
- Promoting floodwater attenuation and decreasing floodwater levels by excavating a gently sloping floodplain that begins at the bankfull discharge elevation and slopes up to the terrace elevation, in addition to increasing roughness in the floodplain by establishing a vegetated riparian buffer.
- Improving aquatic habitat by enhancing stream bed variability (ripple-pool sequence), and introducing woody debris in the form of rootwads, log vanes, and log sills. A ripple-pool sequence and woody debris structures will provide places for forage, cover, and reproduction for fauna and flora.
- Improving terrestrial habitat by restoring a forested riparian corridor through a highly urbanized environment, which has historically experienced vegetation maintenance and forest segmentation. This corridor will provide a diversity of habitats such as mature forest, early successional forest, riparian wetlands and uplands.
- Reducing nonpoint source pollution associated with urban land uses (i.e. maintained ball fields, roadways, residential communities, etc.) by providing a vegetated riparian buffer adjacent to streams to treat surface runoff. Reforestation of the Project resulted in a total of 1,171,272 sq. ft. (26.89 acres) of Neuse River Riparian Buffers (area within 200' of top of bank of channel that is at least 50' wide).
- Improving water quality by creating 0.69 acres of riparian stormwater wetland adjacent to the UT, implementing six (6) sand filter device BMPs along Adkin Branch for

stormwater runoff to retain sediments and nutrients prior to entering Adkin Branch, and removing creosote timber retaining walls throughout the project.

## 1.2 Vegetation

### Stream Vegetation Success Criteria

Vegetation monitoring will be considered successful for stream mitigation credit if at least 260 stems/acre (trees and shrubs), both, volunteer and planted, are surviving at the end of five years. The interim measure of vegetative success for the site will be the survival of at least 320 3-year old stems per acre at the end of year three of the monitoring period and 280 4-year old stems per acre at the end of year four of the monitoring period (USACE et al. 2003).

### Riparian Buffer Vegetation Success Criteria

Vegetation monitoring will be considered successful for riparian buffer mitigation credit if at least 320 native planted hardwood stems/acre (trees only) are surviving at the end of year five. Planted vegetation must include a minimum of at least two planted native hardwood tree species. There is no interim measure of vegetative success for riparian buffers.

### Monitoring Results

In general, vegetation within the Site was doing poorly in Year 1 (2011) and many of the planted trees had died over the summer of 2011 as the result of extreme hot, dry conditions followed by Hurricane Irene. Due to poor planted stem survivability in Year 1, vegetation warranty Site assessments were conducted in September 2011 by EEP and Axiom Environmental, Inc. (Axiom) as described in the EEP letter to Fluvial Solutions, Inc. dated January 25, 2012 (Appendix C). The results of the Site assessment required Fluvial Solutions, Inc. to replant bare root seedlings in four areas as depicted on the Supplemental Planting Map provided in Appendix C. A total of 11 ball and burlap trees were also replanted. Fluvial Solutions, Inc. contracted Bruton Natural Systems, Inc. to replant the Site. Replanting was completed on March 8, 2012. The list of species replanted at the Site is provided in Tables C1 and C2 (Appendix C).

Despite replanting the Site in 2012, planted tree growth within the Site is still poor. Based on the number of stems counted, average densities were measured at 491 planted stems per acre (excluding livestakes) surviving in year 2 (2012). The dominant species identified at the Site were planted stems of silky dogwood (*Cornus amomum*), river birch (*Betula nigra*), and southern red oak (*Quercus falcata*). Fourteen of the twenty-two individual vegetation plots met success criteria when counting planted stems alone. Three plots (Plots 9, 10, and 11) didn't meet success criteria based on planted stems alone; however, when including appropriate naturally recruited stems of hickory (*Carya* sp.), these plots were well-above success criteria. In addition, a large pecan tree fell within Plot 11 contributing to numerous missing planted stems. Lespedeza is dominating the floodplain in the vicinity of Plots 7 and 8, making it difficult for planted stems to survive. Several small areas along stream benches were characterized by exposed soils with little vegetation in Year 1; however, herbaceous vegetation is beginning to fill in these areas. Areas that continue to exhibit sparse vegetation are depicted on the Current Conditions Plan View (CCPV) and in Figure 3.26 (Appendix B).

Several small areas of invasive species occur within the Site including Chinese privet, Johnson grass, and Japanese honeysuckle. Lespedeza is dominating the left and right floodplain between stations 90+00 and 96+00 and currently out-competing planted woody vegetation. It is recommended that an herbicide approved for use in or near aquatic sites be applied to this area to control lespedeza. Locations of invasive species are depicted on the CCPV (Appendix B).

Plant coverage within the stormwater wetlands should be assessed and documented each growing season. If a minimum of 70 percent coverage is not achieved after the second growing season, supplemental planting should be completed. Plant coverage of 90 to 95 percent is desirable. Currently plant coverage within the stormwater bmp is greater than 95 percent.

### **1.3 Stream Stability**

Year 2 monitoring surveys along Adkin Branch and its UT occurred in October and November, 2012. Reach 1 experienced little change from Year 1 except between stations 39+00 to 41+00 where the pools became deeper and longer. Log structures are stable through this section and continue to maintain grade control (Figure 5.1). The profile along Reach 2 provides evidence of the fluctuating nature of a sand bed system. Some pools became deeper and longer (station 65+00 to 69+00) while others filled in and shortened (station 82+50 to 86+00) (Figure 5.2). In general, Reach 2 is somewhat unstable due to erosion along approximately 45 percent of the stream banks within the Reach. The erosion can be attributed to a lack of vegetation and several large storm events that have resulted in severe shear stress along the exposed sandy banks. A repair plan has been developed to correct the eroded stream banks and will be implemented in the Spring of 2013. Fluctuation in channel bed features is expected to continue throughout the monitoring period, but the overall stream reach should stabilize once woody vegetation establishes along the stream banks. Reach 3 experienced aggradation between Stations 10+00 and 12+35 due to dense herbaceous vegetation forming in the channel and trapping sediment (Figure 5.3). However, the stream remains stable and flood waters are accessing the adjacent stormwater wetlands as intended.

Only minor shifting of pools and riffles was observed throughout the remainder of the profile, which is expected in a sand bed system. The majority of stream banks and structures throughout the project are stable and functioning as intended. There is no evidence of trends toward significant change in channel pattern. Cross-sectional data indicates that the channel width to depth ratio is lowering as the channel matures (Figures 4.1-4.17). This change is expected as detailed in the proposed success criteria from the Baseline Monitoring Document (NCDENR, 2011).

Reach 2 contains the majority of problem areas on the Site. Four riffle segments were noted as unstable in Reach 2 as a result of the scour from large storm events, most notably, events associated with Hurricane Irene. Approximately 45 percent of the stream banks in Reach 2 are unstable due to a lack of vegetation. Fifteen bank segments (504 ft) were noted as moderately eroded and 13 bank segments (916 ft) have experienced mass wasting (Figures 3.21-3.25). Two log cross vanes have been compromised in Reach 2 as a result of stream bank erosion around the

vane arms (Figures 3.29 and 3.30). Six log structures are experiencing erosion on greater than 15 percent of the stream banks within their extent of influence. Table 5.2 provides a summary of the unstable sections within Reach 2. A Repair Plan has been developed to correct these problem areas, which includes the use of soil lifts, bank grading, and erosion control matting. The repair plan is expected to be implemented in the Spring of 2013. A beaver dam was observed at Station 69+60 and appears to have formed on top of rip rap that was placed in the channel by local residents. Rip rap was also observed in the channel near station 81+25. The beaver dam and rip rap will be removed when Hurricane Irene repairs are conducted. Problem areas are depicted on the CCPV and photos are presented in Appendix B.

The soil lifts that were installed in January and February, 2011 are stable and the willow cuttings are well established along the stream banks.

Crest gauges installed on-site were inspected in October and November 2011. Crest Gauge 2 near station 75+25 was damaged during Hurricane Irene, but was reinstalled on November 8, 2012. The remaining crest gauges revealed that a bankfull event occurred at least once during 2012 (Table 13). Additional overbank evidence includes debris lines, and vegetation bent in the downstream direction. Evidence of bankfull events can be found in Appendix E.

#### **1.4 Wetlands**

No wetland monitoring areas were established for this project report.

#### **1.5 Note**

Summary information/data related to the occurrence of items such as beaver or encroachment and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report (formerly Mitigation Plan) and in the Mitigation Plan (formerly the Restoration Plan) documents available on EEP's website. All raw data supporting the tables and figures in the appendices is available from EEP upon request.

## **2.0 METHODOLOGY**

The Year 2 Monitoring survey was completed using a Total Station. Each cross section is marked with two rebar monuments at their beginning and ending points. The rebar has been located vertically and horizontally in NAD 83-State Plane. Surveying these monuments throughout the Site ensured proper orientation. The survey data was imported into MicroStation for verification. The longitudinal stationing was developed from total station data and compared with previous year's data to ensure consistent beginning and ending points. RIVERMorph was used to analyze the profile and cross section data. Tables and figures were created using Microsoft Excel. The channel is entirely a sand bed system; therefore a pebble count was not conducted.

Vegetation was measured at twenty-two sample vegetation plots (10-meter by 10-meter) within the Site in August 2012 for Year 2 (2012) monitoring per guidelines established in *CVS-EEP Protocol for Recording Vegetation, Version 4.2* (Lee et al. 2008). The taxonomic standard for vegetation used for this document was *Flora of the Carolinas, Virginia, Georgia, and Surrounding Areas* (Weakley 2006). Vegetation plots are permanently monumented with 4-foot metal garden posts at each corner. In each sample plot, vegetation parameters monitored included species composition and species density. Visual observations of the percent cover of shrub and herbaceous species were documented by photograph. Photographs and vegetation plot information can be found in Appendices B and C.

Stormwater BMP devices will be monitored and maintained periodically, as necessary, to ensure the life of the devices. The City of Kinston has agreed to provide maintenance for the sand filter BMP devices and the stormwater wetland for the life of the BMPs (30 years). A maintenance guideline manual will be provided to the City of Kinston by EEP.

### 3.0 REFERENCES

- Lee, Michael T., R. K. Peet, S. D. Roberts, and T. R. Wentworth. 2006. CVS-EEP Protocol for Recording Vegetation, Version 4.0 (<http://cvs.bio.unc.edu/methods.htm>).
- NCDENR-Ecosystem Enhancement Program. 2011. Baseline Monitoring Document and As-Built Baseline Report, Adkin Branch Stream Restoration Project, Phase 1 – Washington Ave. to Lincoln St., Lenoir County, North Carolina.
- Weakley, Alan S. 2006. *Flora of the Carolinas, Virginia, Georgia, and Surrounding Areas* (online). Available: [http://www.herbarium.unc.edu/FloraArchives/WeakleyFlora\\_2006-Jan.pdf](http://www.herbarium.unc.edu/FloraArchives/WeakleyFlora_2006-Jan.pdf) [January 6, 2006]. University of North Carolina Herbarium, North Carolina Botanical Garden, University of North Carolina, Chapel Hill, North Carolina.
- Schafale, M.P. and A.S. Weakley. 1990. *Classification of the Natural Communities of North Carolina: Third Approximation*. North Carolina Natural Heritage Program, Division of Parks and Recreation, North Carolina Department of Environment, Health, and Natural Resources. Raleigh, North Carolina.
- United States Army Corps of Engineers, United States Environmental Protection Agency, North Carolina Wildlife Resources Commission, North Carolina Division of Water Quality (USACE et al.). 2003. *Stream Mitigation Guidelines*.




## APPENDICES

### **Appendix A. Project Vicinity Map and Background Tables**



# Lenoir County North Carolina

## PROJECT AREA



Date: 06/15/11


Figure: 1

# Vicinity/Asset Map

Adkin Branch Phase I  
PROJECT NO. 050656101  
Lenoir County, North Carolina




**Florence & Hutcheson**  
CONSULTING ENGINEERS  
5121 KINGDOM WAY, SUITE 100  
RALEIGH, N.C. 27607  
(919) 851-6066  
License No: F-0258

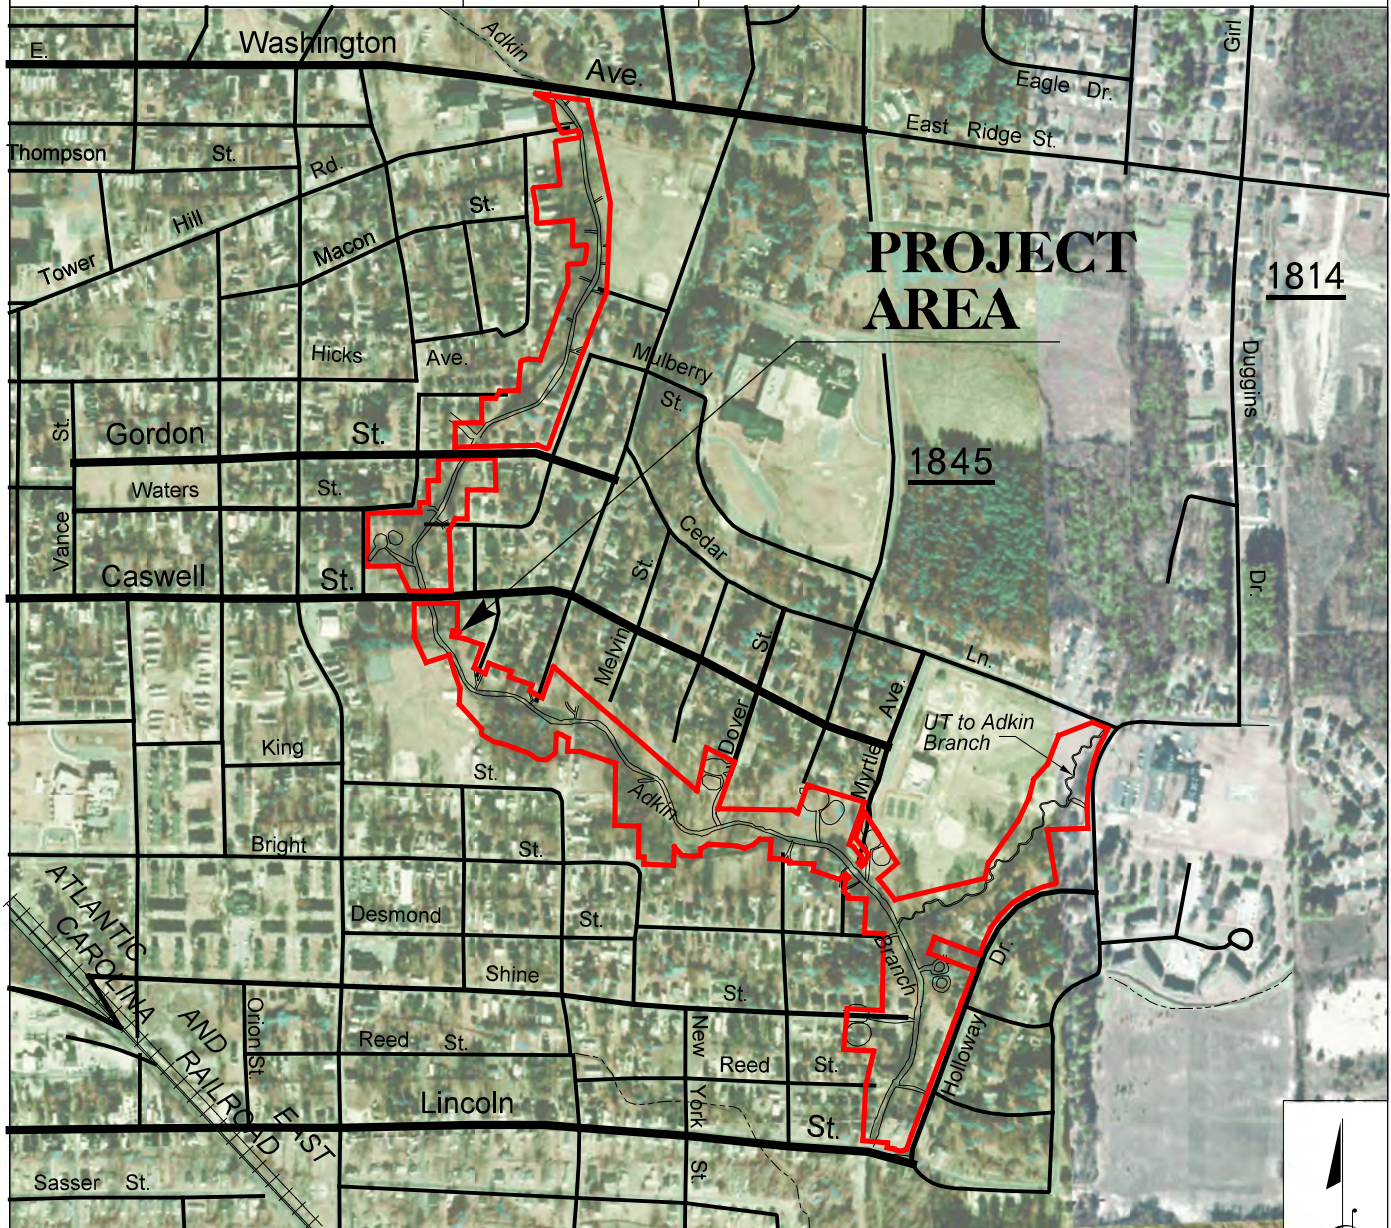

### FROM RALEIGH:

- Take I-40 East for approximately 6.5 miles to US 70 East
- Take US Hwy 70 East for approximately 68.5 miles to NC 1155
- Turn left and travel Northeast on NC 1155 thru Kinston for 1.7 miles
- Turn left onto Martin Luther King Jr Blvd. and travel for 0.5 miles
- Turn right onto the East Washington Ave. and travel 0.4 miles to the intersection with Adkin Branch Project. Site is Southeast of Washington Ave.

"The subject project site is an environmental restoration site of the NCDENR Ecosystem Enhancement Program (EEP) and is encompassed by a recorded conservation easement, but is bordered by land under private ownership. Accessing the site may require traversing areas near or along the easement boundary and therefore access by the general public is not permitted. Access by authorized personnel of state and federal agencies or their designees/contractors involved in the development, oversight and stewardship of the restoration site is permitted within the terms and timeframes of their defined roles. Any intended site visitation or activity by any person outside of these previously sanctioned roles and activities requires prior coordination with EEP."



## **Project Location and Directions**

The Project is located on the southeast side of the City of Kinston, in Lenoir County, North Carolina and includes Adkin Branch and an unnamed tributary (UT) to Adkin Branch (Figure 1, Appendix A). Phase I of the Project begins at Washington Ave. and ends at Lincoln Street.

### Directions to the Site:

- From Raleigh, North Carolina take I-40 east for approximately 6.5 miles to US Highway 70 east.
- Take US 70 east for approximately 68.5 miles to NC Highways 11 and 55
- Take a left turn and travel northeast on NC 11/55 through Kinston for 2.6 miles to the intersection with Adkin Branch
- The project study area is southeast of NC 11/55.

*The subject project is an environmental restoration site of the NCDENR Ecosystem Enhancement Program (EEP) and is encompassed by a recorded conservation easement, but is bordered by land under private ownership. Accessing the site may require traversing areas near or along the easement boundary and therefore access by the general public is not permitted. Access by authorized personnel of state and federal agencies or their designees/contractors involved in the development, oversight and stewardship of the restoration site is permitted within the terms and timeframes of their defined roles. Any intended site visitation or activity by any person outside of these previously sanctioned roles and activities requires prior coordination with EEP.*

**Table 1. Project Components and Mitigation Credits**

<b>Mitigation Credits</b>										
	Stream	Riparian Wetland		Non-riparian Wetland		Riparian Buffer **		Nitrogen Nutrient Offset		
								Pound Reduction	Buffer Restoration **	
Type	R	R	RE	R	RE	50'	50' - 200'	<= 50'	50' - 200'	
Totals	7,787 *	N/A	N/A	N/A	N/A	562,799	696,704 *	3,990	0	31,751
<b>Project Components</b>										
Project Component -or- Reach ID	Stationing/Location			Existing Footage/Acreage	Approach (PI, PII etc.)	Restoration - or- Restoration Equivalent	Restoration Footage or Acreage	Mitigation Ratio		
Reach 1	Washington Ave. to Gordon St.			1,680	PII	R	1,727	Varies*		
Reach 2	Gordon St. to Lincoln St.			4,224	PII	R	4,270	Varies*		
Reach 3	UT to Adkin Branch.			1,200	PII	R	1,582	Varies*		
Riparian Buffers	50'			7.58	-	R	12.92	1 to 1		
	50' - 200'					R	13.97	Varies*		
<b>Component Summation</b>										
Restoration Level	Stream (linear feet)	Riparian Wetland (acres)		Non-riparian Wetland (acres)	Buffer (square ft.)	Upland (acres)				
		Riverine	Non-Riverine							
Restoration	7,579	N/A	N/A	N/A	1,171,272	N/A				
Enhancement		N/A	N/A	N/A	N/A	N/A				
Enhancement II	N/A									
Enhancement II	N/A									
Creation		N/A	N/A	N/A						
Preservation	N/A	N/A	N/A	N/A		N/A				
High Quality Preservation	N/A	N/A	N/A	N/A		N/A				
<b>BMP Elements</b>										
Element	Location	Purpose/Function		30 yr. Total Nitrogen Reduction (lbs)		Notes				
Stormwater Wetland	UT Adkin	Water Quality / Nutrient Uptake		N/A		-				
BMP #4 - Sand Filter	Miller St.	Water Quality / Infiltration		300		-				
BMP #5 - Sand Filter	Dover St.	Water Quality / Infiltration		750		-				
BMP #6 - Sand Filter	Seacrest St.	Water Quality / Infiltration		1,170		-				
BMP #7 - Sand Filter	Myrtle Ave.	Water Quality / Infiltration		600		-				
BMP #8 - Sand Filter	Holloway Dr.	Water Quality / Infiltration		180		-				
BMP #9 - Sand Filter	Shine St.	Water Quality / Infiltration		990		-				
<p>* - Stream &amp; Riparian Buffer Mitigation Credit numbers were adjusted based on proposed DWQ guidelines (DRAFT Regulatory Guidance for the Calculation of Stream and Buffer Mitigation Credit for Buffer Widths Different from Standard Minimum Widths, Version 4.5, July 20, 2010). See Appendix D for further explanation.</p>										
<p>** - Riparian Buffer areas may be used for stream &amp; wetland mitigation, stream &amp; riparian buffer mitigation, or nutrient offset credit (Estimating/Calculating Riparian Buffer Credits, EEP PPPM Section 8.3.1.2).</p>										



**Table 2. Project Activity and Reporting History**

<b>Activity or Report</b>	<b>Data Collection Complete</b>	<b>Completion or Delivery</b>
Restoration Plan		March 2007
Final Design – Construction Plans		May 2007
Bid Opening		October 2008
Begin Construction		March 2009
<i>Tropical Storm Ida</i>	<i>November 2009</i>	
Article 29 declared on original contractor		January 2010
Surety Contractor Begin Construction		June 2010
Tropical Storm Repairs Bid Opening		September 2010
<i>Tropical Storm Nicole</i>	<i>October 2010</i>	
Begin Tropical Storm Repairs Construction		December 2010
Construction Complete		April 2011
Baseline Monitoring Document	March 2011	July 2011
<i>Hurricane Irene</i>	<i>August 2011</i>	
Year 1 Monitoring	October 2011	November 2011
Year 2 Monitoring	November 2012	January 2013
Year 3 Monitoring		
Year 4 Monitoring		
Year 5 Monitoring		

**Table 3. Project Contacts Table**

<b>Designer</b>	Florence & Hutcheson, Inc. 5121 Kingdom Way, Suite 100 Raleigh, North Carolina 27607 Kevin Williams (919) 851-6066
<b>Original Contractor</b>	Appalachian Environmental Services 1165 W. Main St. Sylva, NC 28779 Mickey B. Henson
<b>Surety Contractor</b>	Environmental Quality Resources, LLC 1405 Benson Court, Suite C Baltimore, MD 21227 John Talley (443) 304-3310
<b>Repair Contractor</b>	Fluvial Solutions P.O. Box 28749 Raleigh, NC 27611 Peter Jelenevsky (919) 821-4300
<b>Planting Contractor</b>	Bruton Natural Systems (Fluvial Solutions Sub-contractor) PO Box 1197 Fremont, NC 27830 Charlie Bruton (919) 242-6555
<b>Seeding Contractor</b>	See Original Contractor, Surety Contractor, & Repair Contractor above.
Nursery Stock Suppliers	1) ArborGen - South Carolina SuperTree Nursery 2) Evergreen Partners of Raleigh 3) NC Division of Forest Resources
<b>Monitoring Performers</b>	
Stream Monitoring	Florence & Hutcheson, Inc. 5121 Kingdom Way, Suite 100 Raleigh, North Carolina 27607 Ryan Smith (919) 851-6066
Vegetation Monitoring	Axiom Environmental, Inc. 218 Snow Avenue Raleigh, North Carolina 27603 Corri Faquin (919) 414-2471

**Table 4. Project Attributes Table**

<b>Project Information</b>				
Project Name		Adkin Branch Stream Restoration Project – Phase I		
County		Lenoir		
Project Area (acres)		36		
Project Coordinates		035° 15' 13" N, 77° 33' 36" W (@ Lincoln St.)		
<b>Project Watershed Summary Information</b>				
Physiographic Province		Coastal Plain		
River Basin		Neuse		
USGS 8-digit HUC	3020202		USGS 14-digit HUC	3020202060030
NCDWQ Subbasin		03-04-05		
Project Drainage Area		5.46 sq. mi (at Lincoln St.)		
Watershed Land Use	Urban Land	76%	Agricultural Land	13%
	Mixed Forest / Disturbed Forest	7%	Evergreen Forest	4%
<b>Reach Summary Information</b>				
Parameters	Adkin Branch		UT to Adkin	
	Washington Ave. to Gordon St.	Gordon St. to Lincoln St.		
Length of reach (linear ft)	1727	4270	1582	
Valley Classification	VIII		VIII	
Drainage Area (acres)	3220	3495	78	
NCDWQ stream ID score	39.5		27	
NCDWQ Classification	C		C	
Pre-Existing Stream Type	G5	B5c	E5	
As-built Stream Type	B5c	B5c	C/E5	
Underlying mapped soils	Bibb		Kenansville	
Drainage Class	Poorly Drained		Well-drained	
Soil Hydric Status	Hydric		Non-Hydric	
Slope	0.0016	0.0014	0.0022	
FEMA Classification	AE			
Native Vegetation Community	Coastal Plain Levee Forest / Streamside Assemblage			
Percent composition of exotic invasive vegetation	5%	10%	5%	
<b>Wetland Summary Information</b>				
N/A				
<b>Regulatory Considerations</b>				
Regulation	Applicable	Resolved	Supporting Documentation	
Waters of the U.S. –Sections 404 and 401	Yes	Yes	Restoration Plan	
Endangered Species Act	Yes	Yes	Restoration Plan	
Historic Preservation Act	Yes	Yes	Restoration Plan	
CZMA/CAMA	No	--	--	
FEMA Floodplain Compliance	Yes	Yes	Restoration Plan	
Essential Fisheries Habitat	No	--	--	







## Appendix B. Visual Assessment Data


**Figures 2.0-2.12. Current Condition Plan View**

**CURRENT CONDITIONS PLAN VIEW (CCPV)  
OVERVIEW**

PROJECT REFERENCE NO. ADKIN BRANCH	FIGURE NO. 2.0
---------------------------------------	-------------------



**NOT TO SCALE**




***BEGIN UT TO  
ADKIN BRANCH  
MONITORING***

***BEGIN ADKIN BRANCH  
MONITORING***

***END UT TO  
ADKIN BRANCH  
MONITORING***

***END ADKIN BRANCH  
MONITORING***

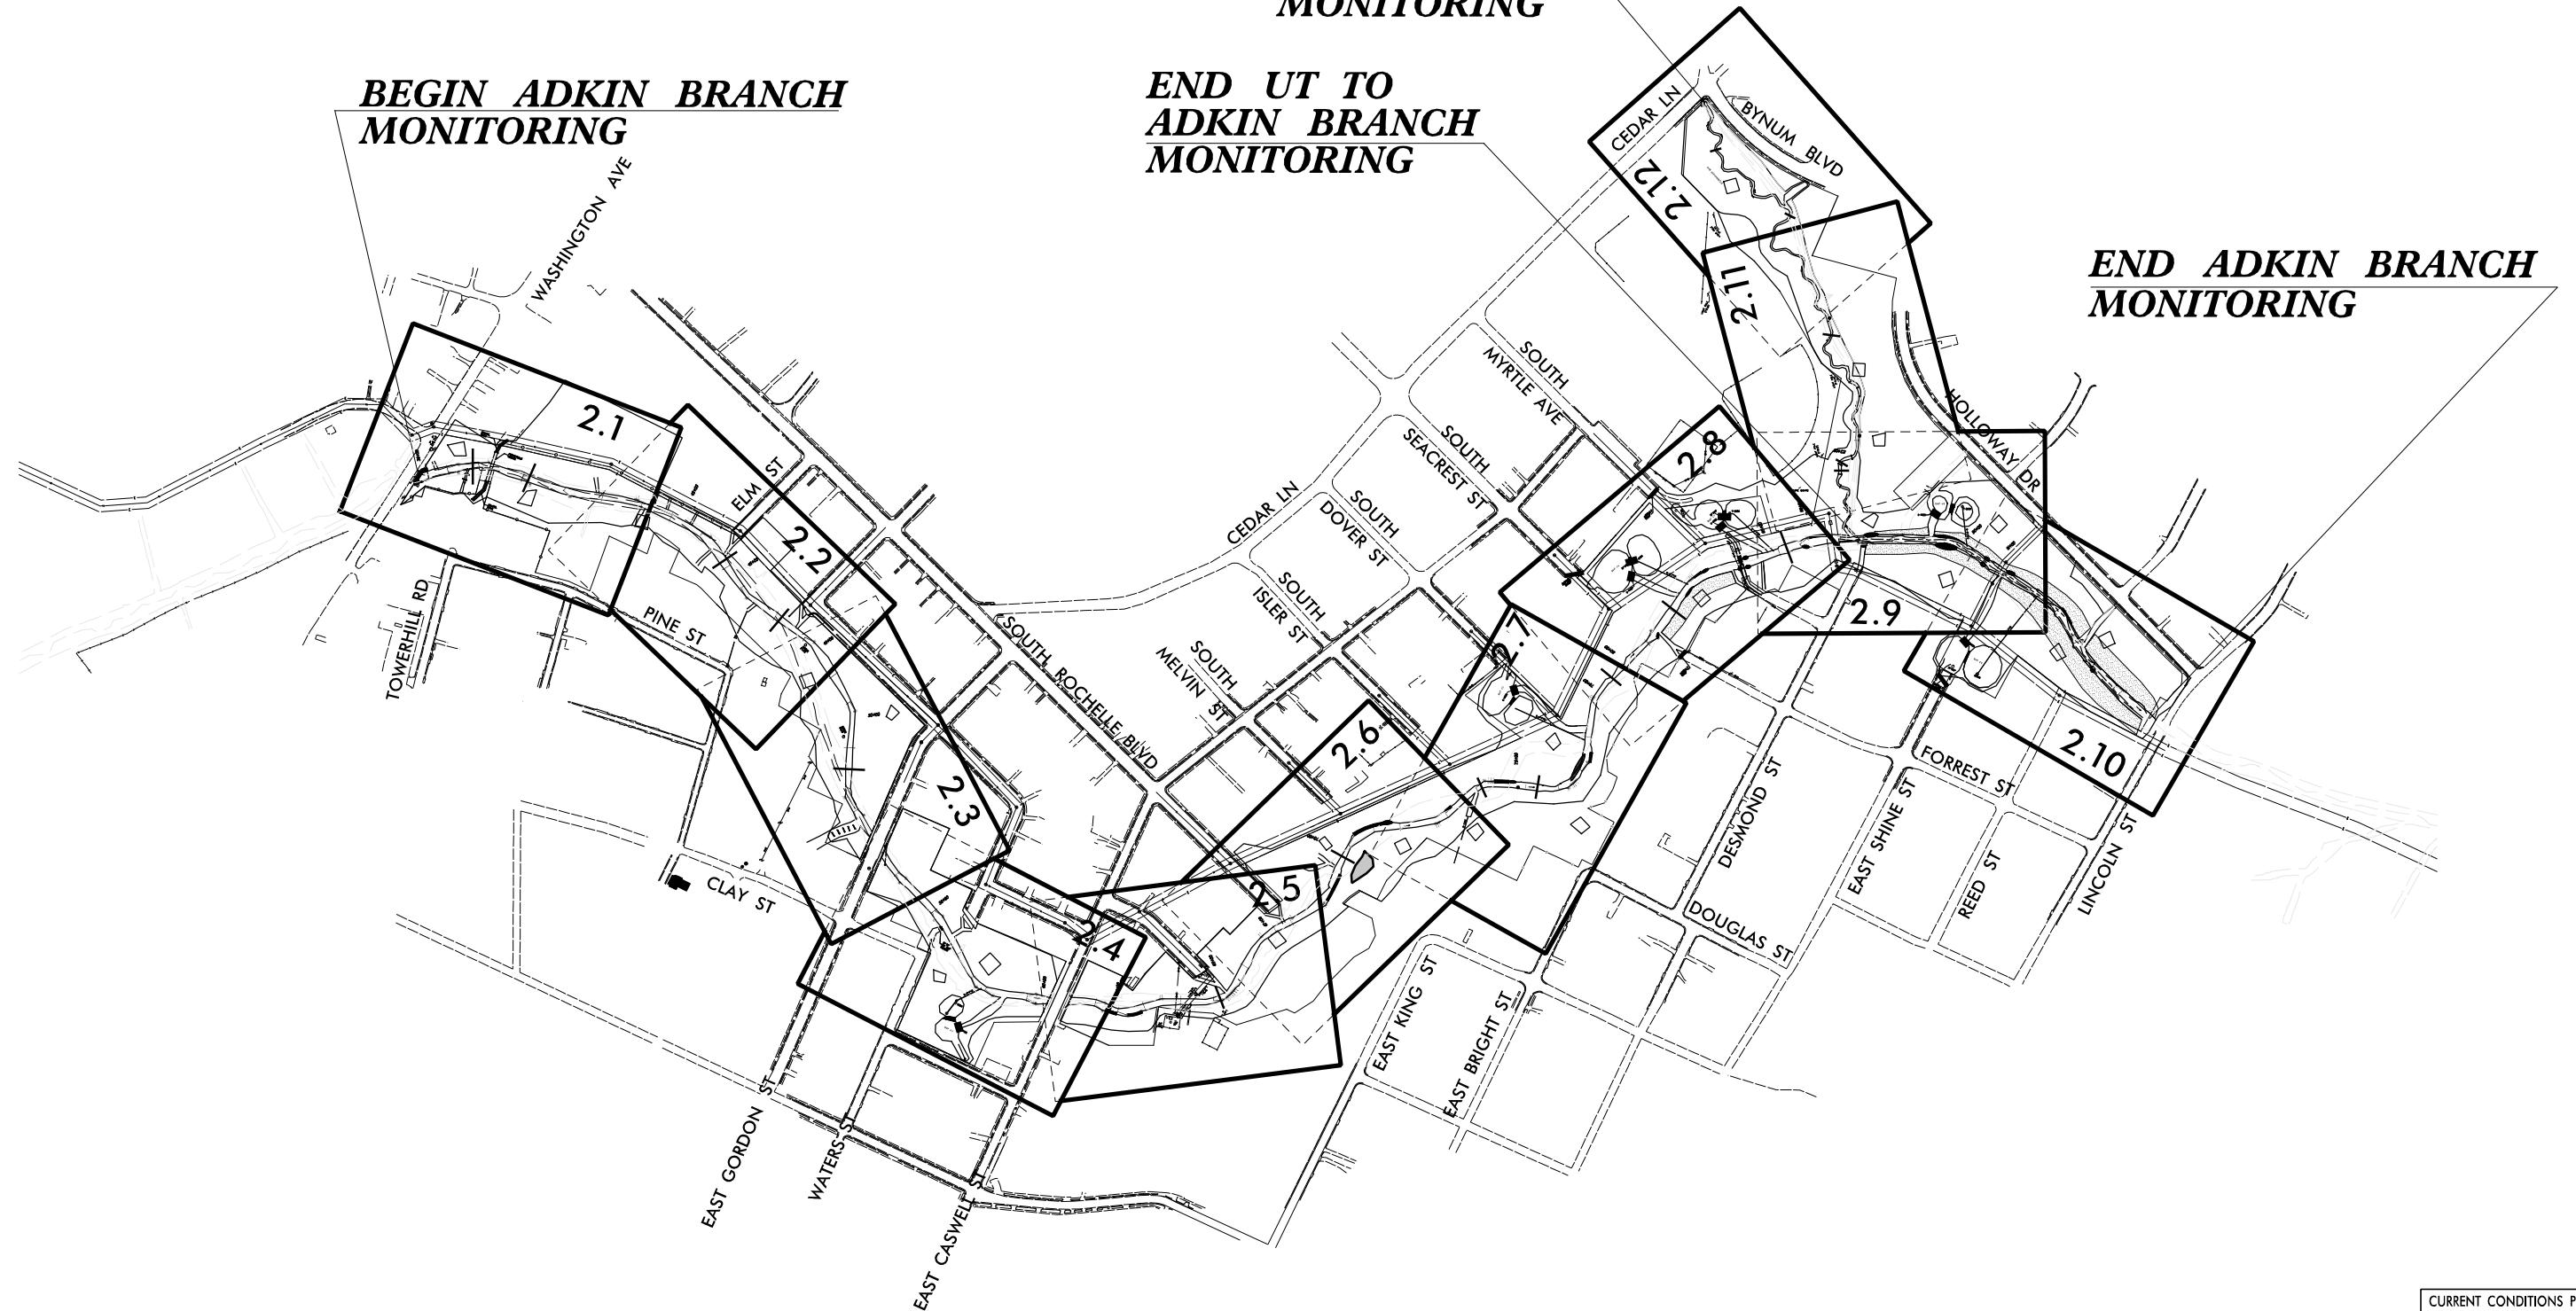


11/27/2012 H:\Stream\Pro\Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_1.dgn Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOP: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12



### CURRENT CONDITIONS PLAN VIEW (CCPV)

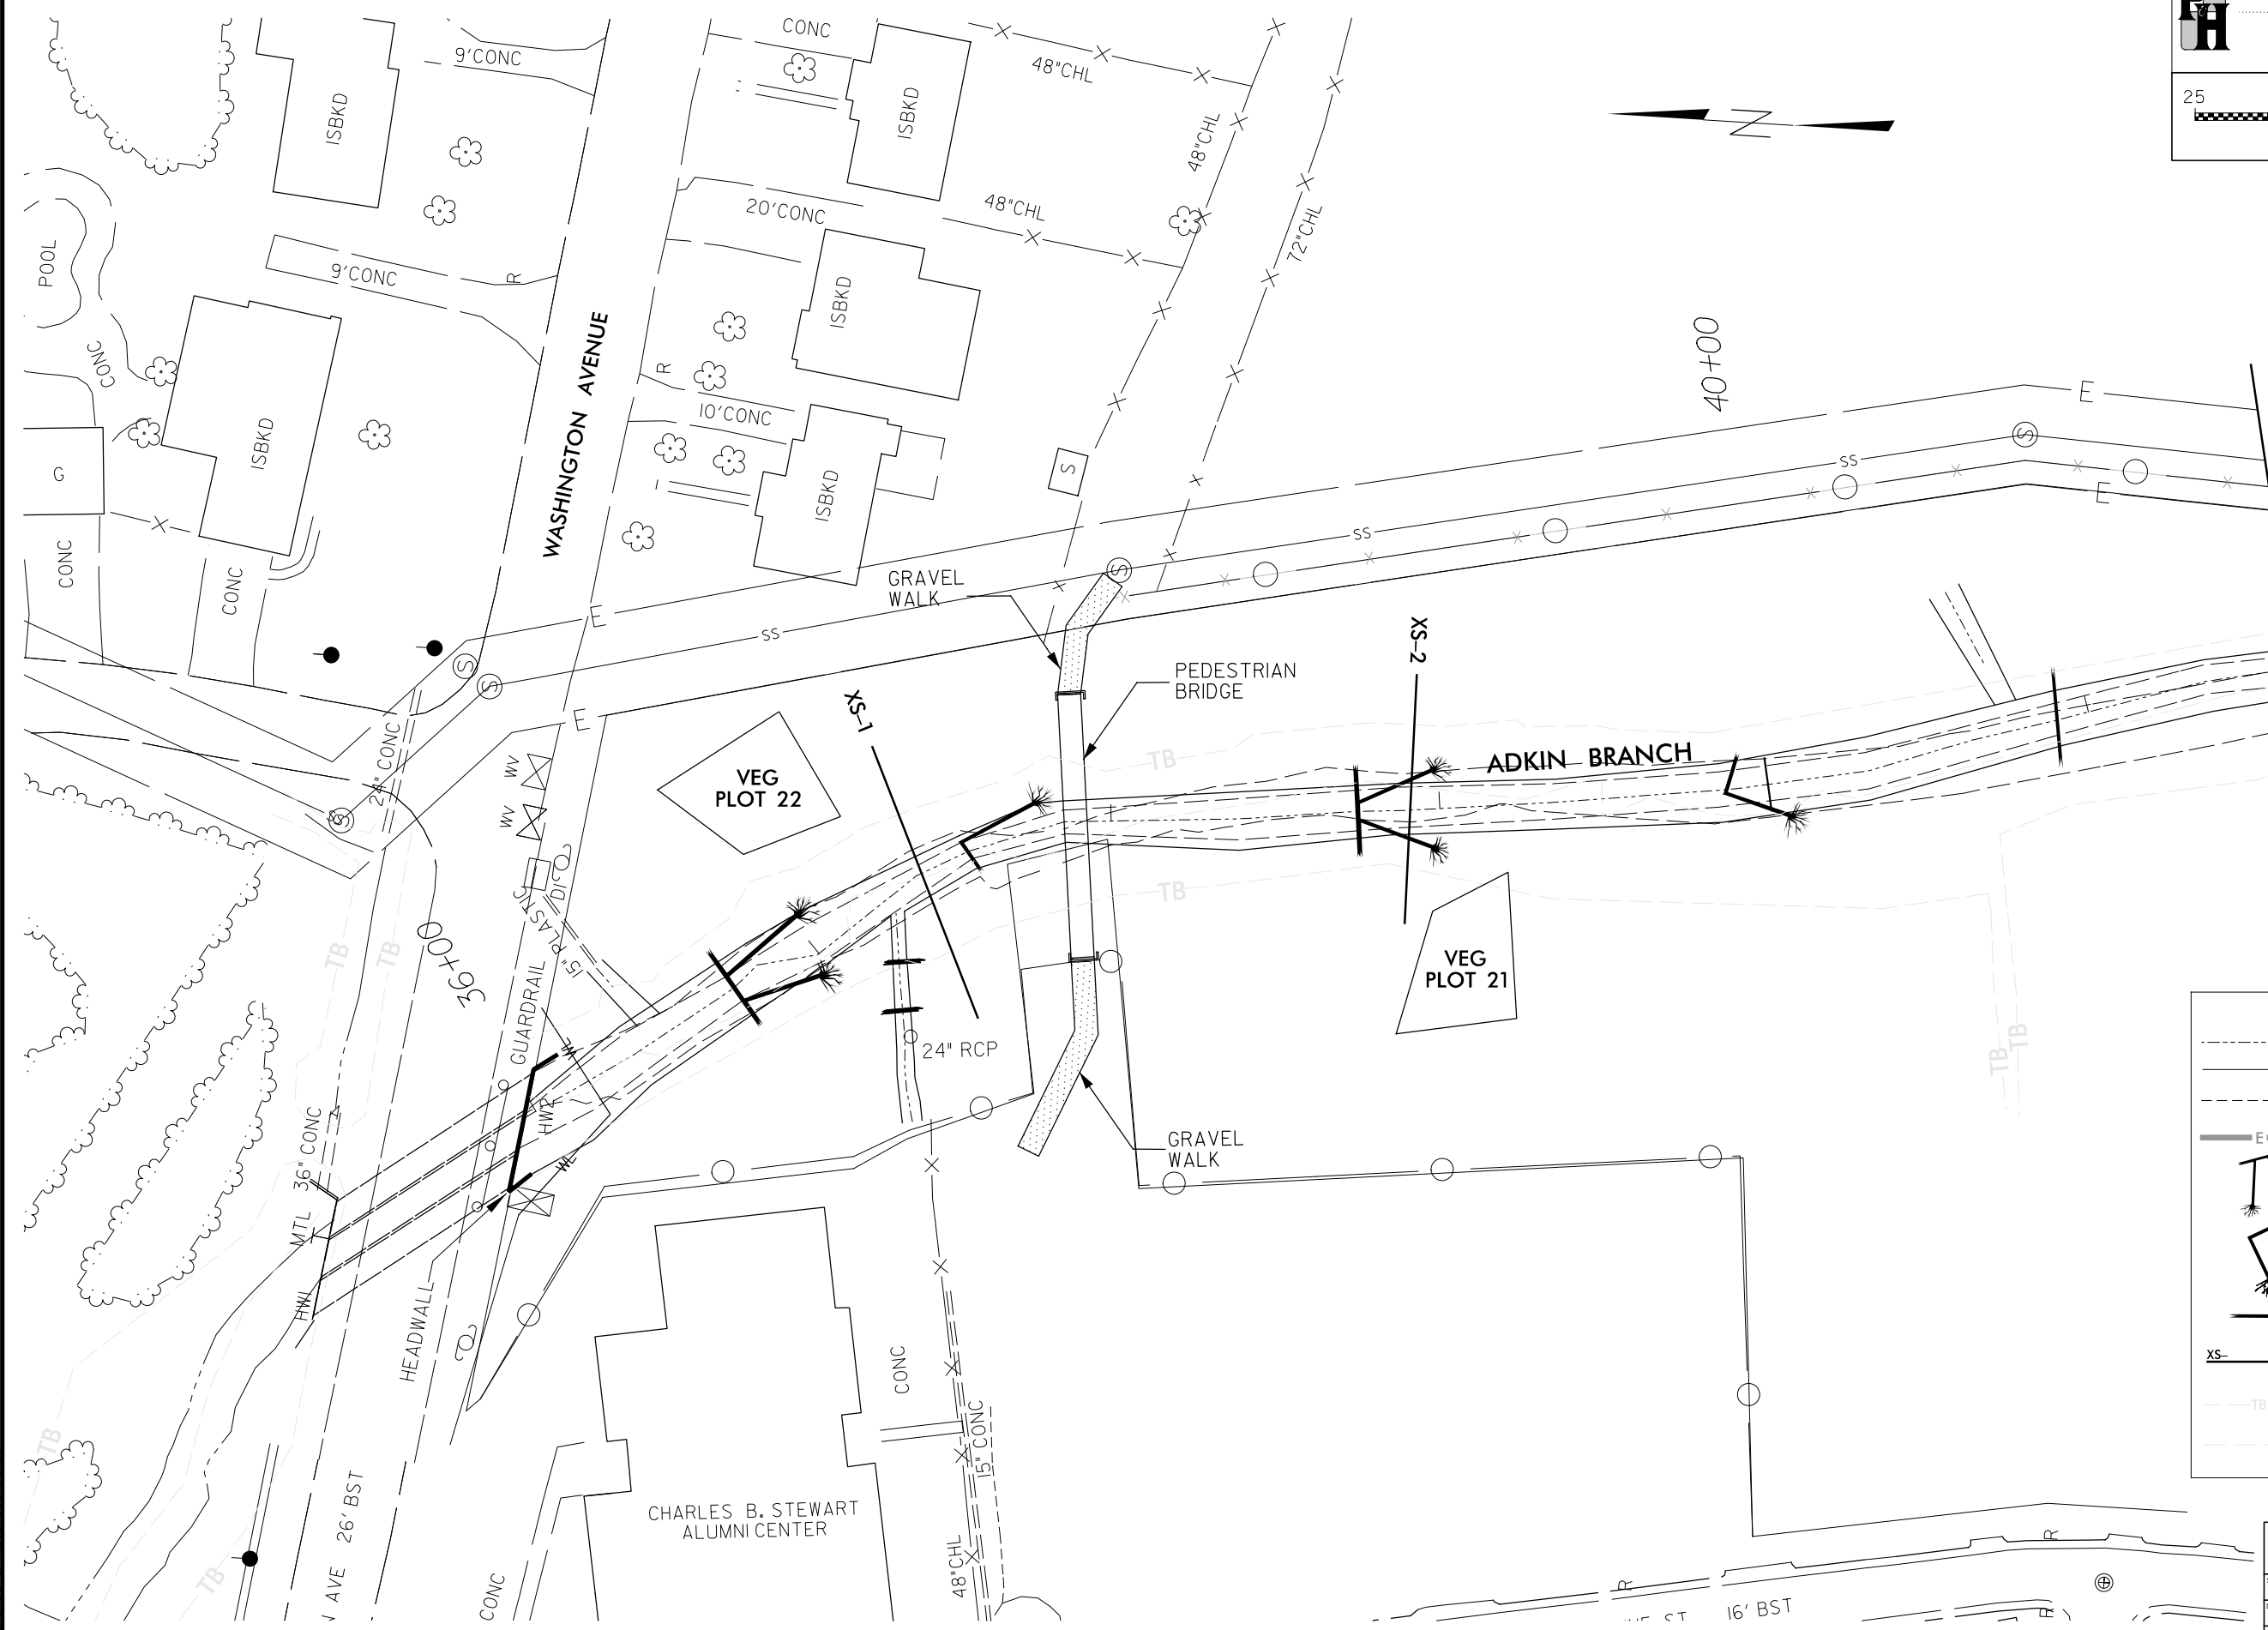


-MATCHLINE- SEE FIGURE NO. 2.2

LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	LOG CROSS VANE
	LOG VANE
	LOG SILL
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE: 11/12	

11/21/2012 Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_2.dgn  
Florence & Hutcheson, Inc.

# CURRENT CONDITIONS PLAN VIEW (CCPV)

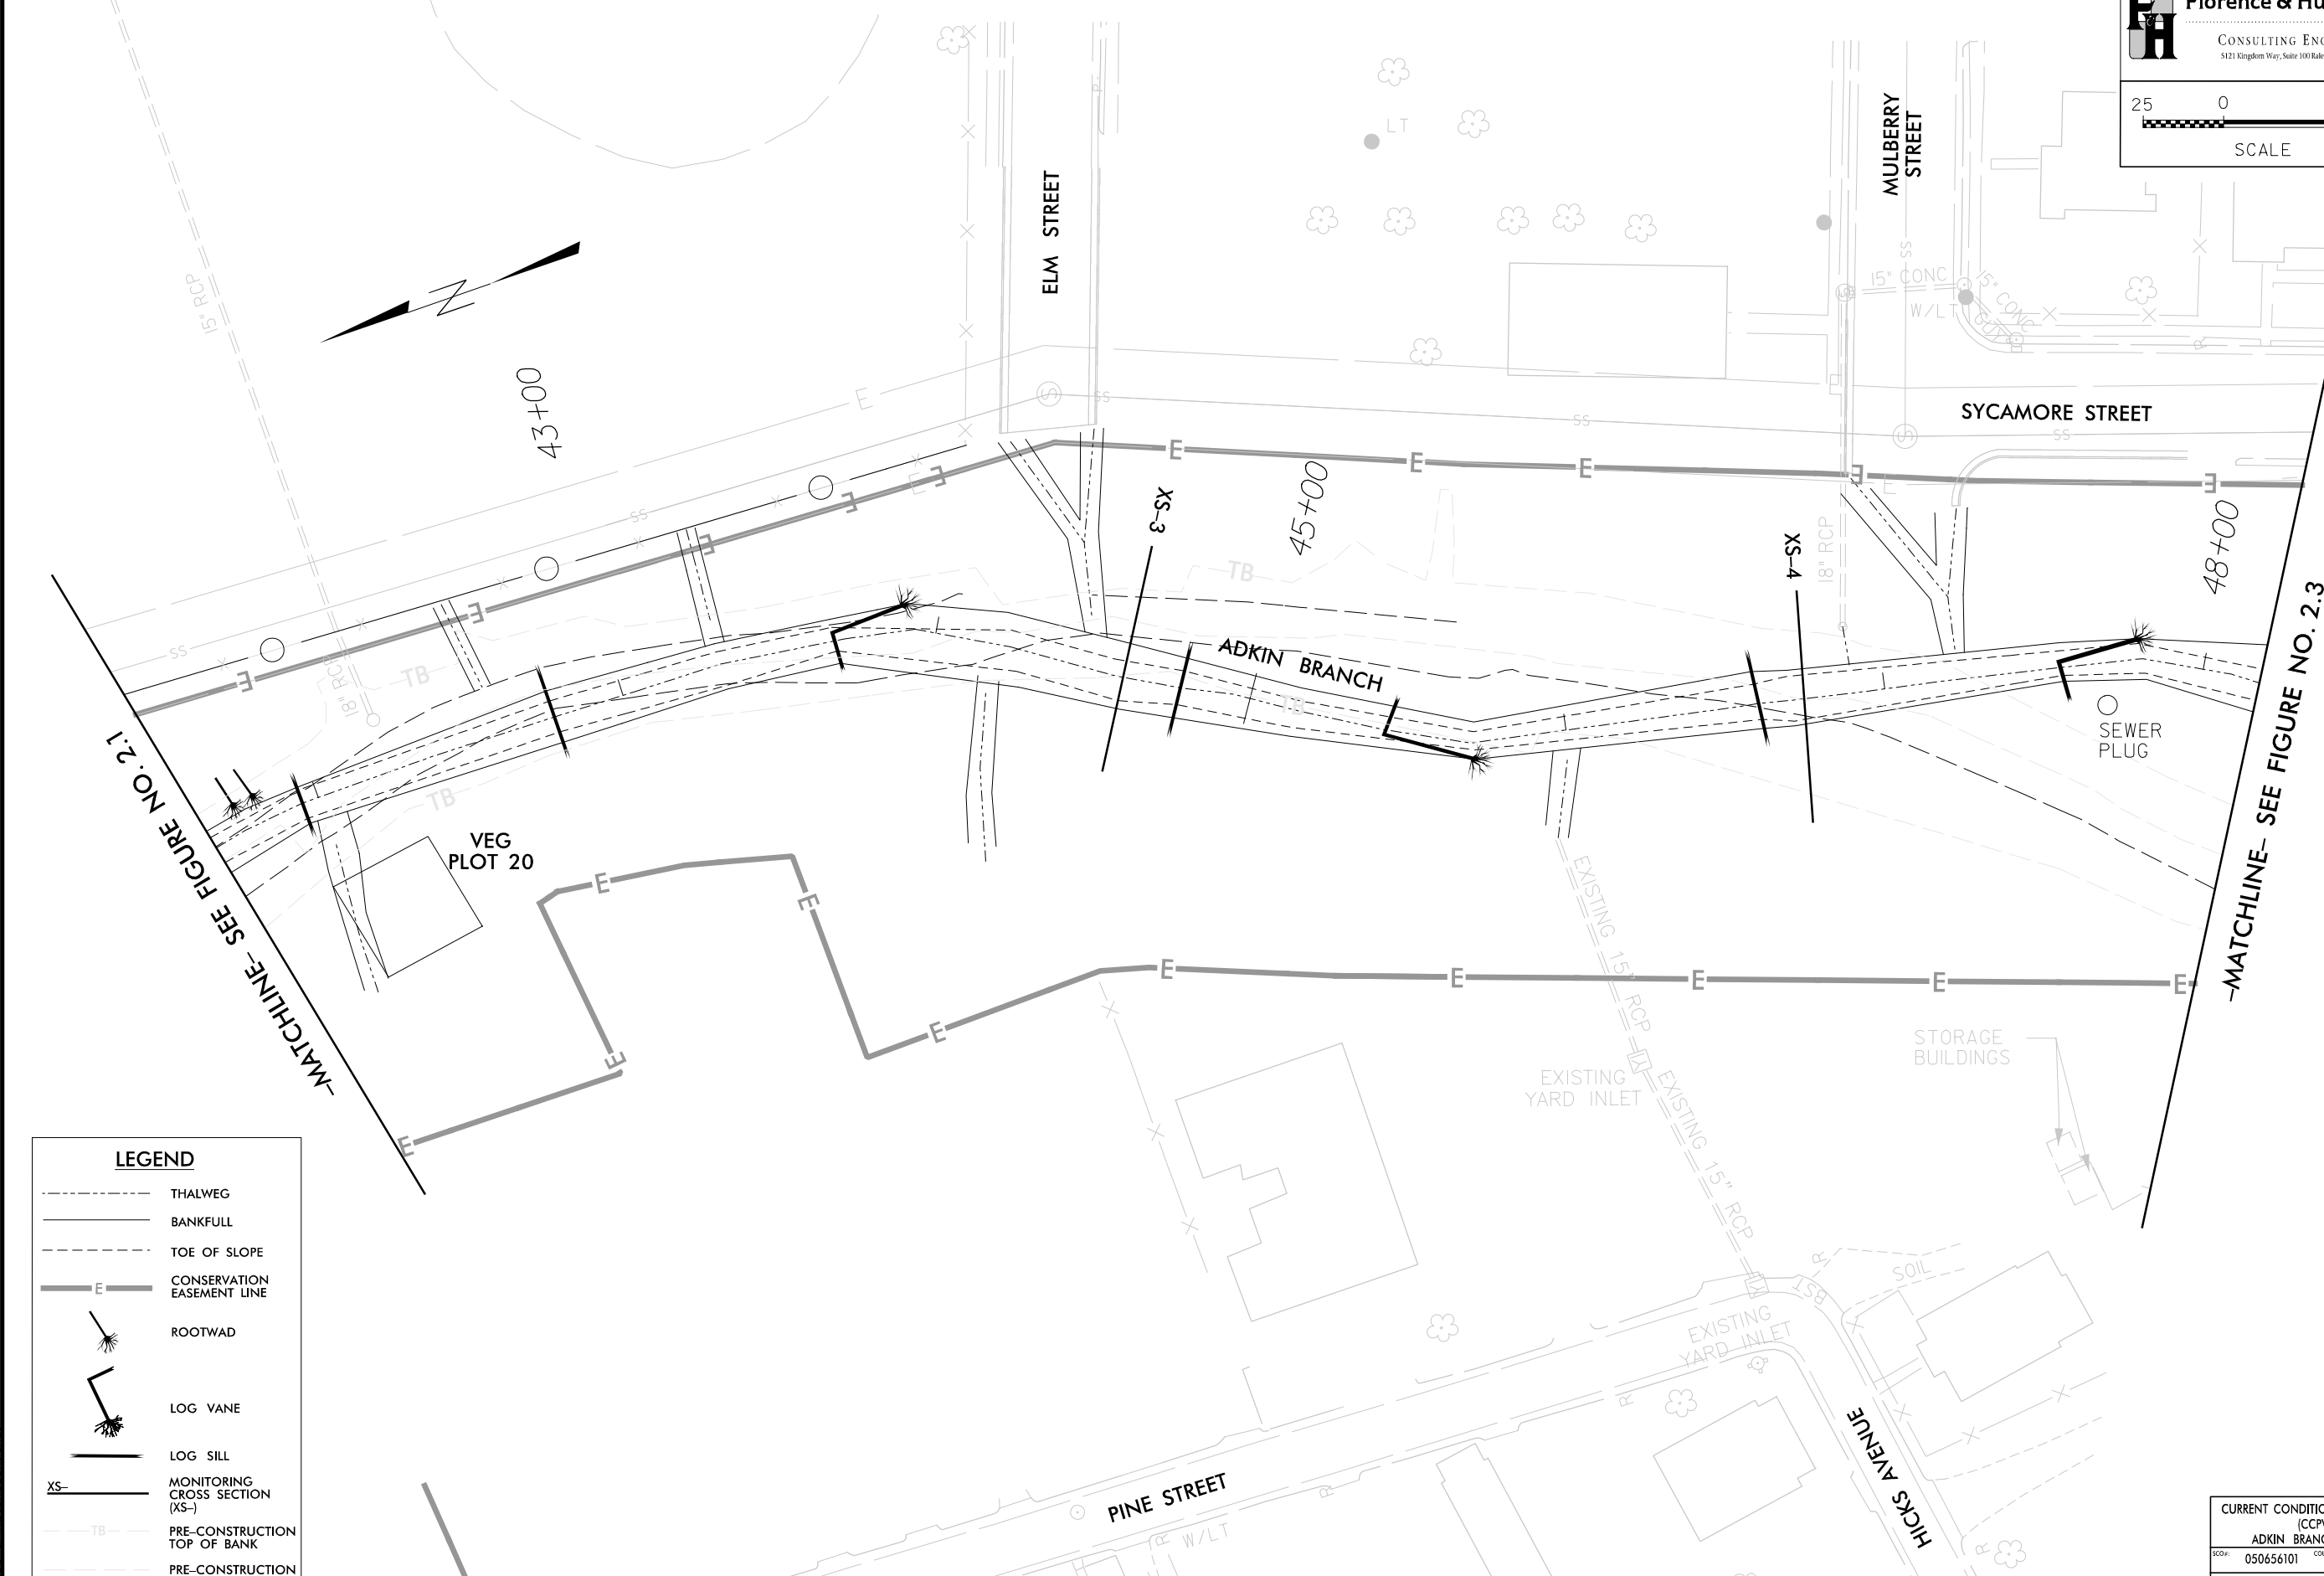

LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	ROOTWAD
	LOG VANE
	LOG SILL
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG

-MATCHLINE- SEE FIGURE NO. 2.1

-MATCHLINE- SEE FIGURE NO. 2.3

I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\YR1\_psh\_3.dgn  
Florence & Hutcheson, Inc.


CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12

# CURRENT CONDITIONS PLAN VIEW (CCPV)

PROJECT REFERENCE NO.	FIGURE NO.
ADKIN BRANCH	2.3

**Florence & Hutcheson**  
CONSULTING ENGINEERS  
5121 Kingdom Way, Suite 100 Raleigh, NC 27607  
NC License No. F-0058

SCALE

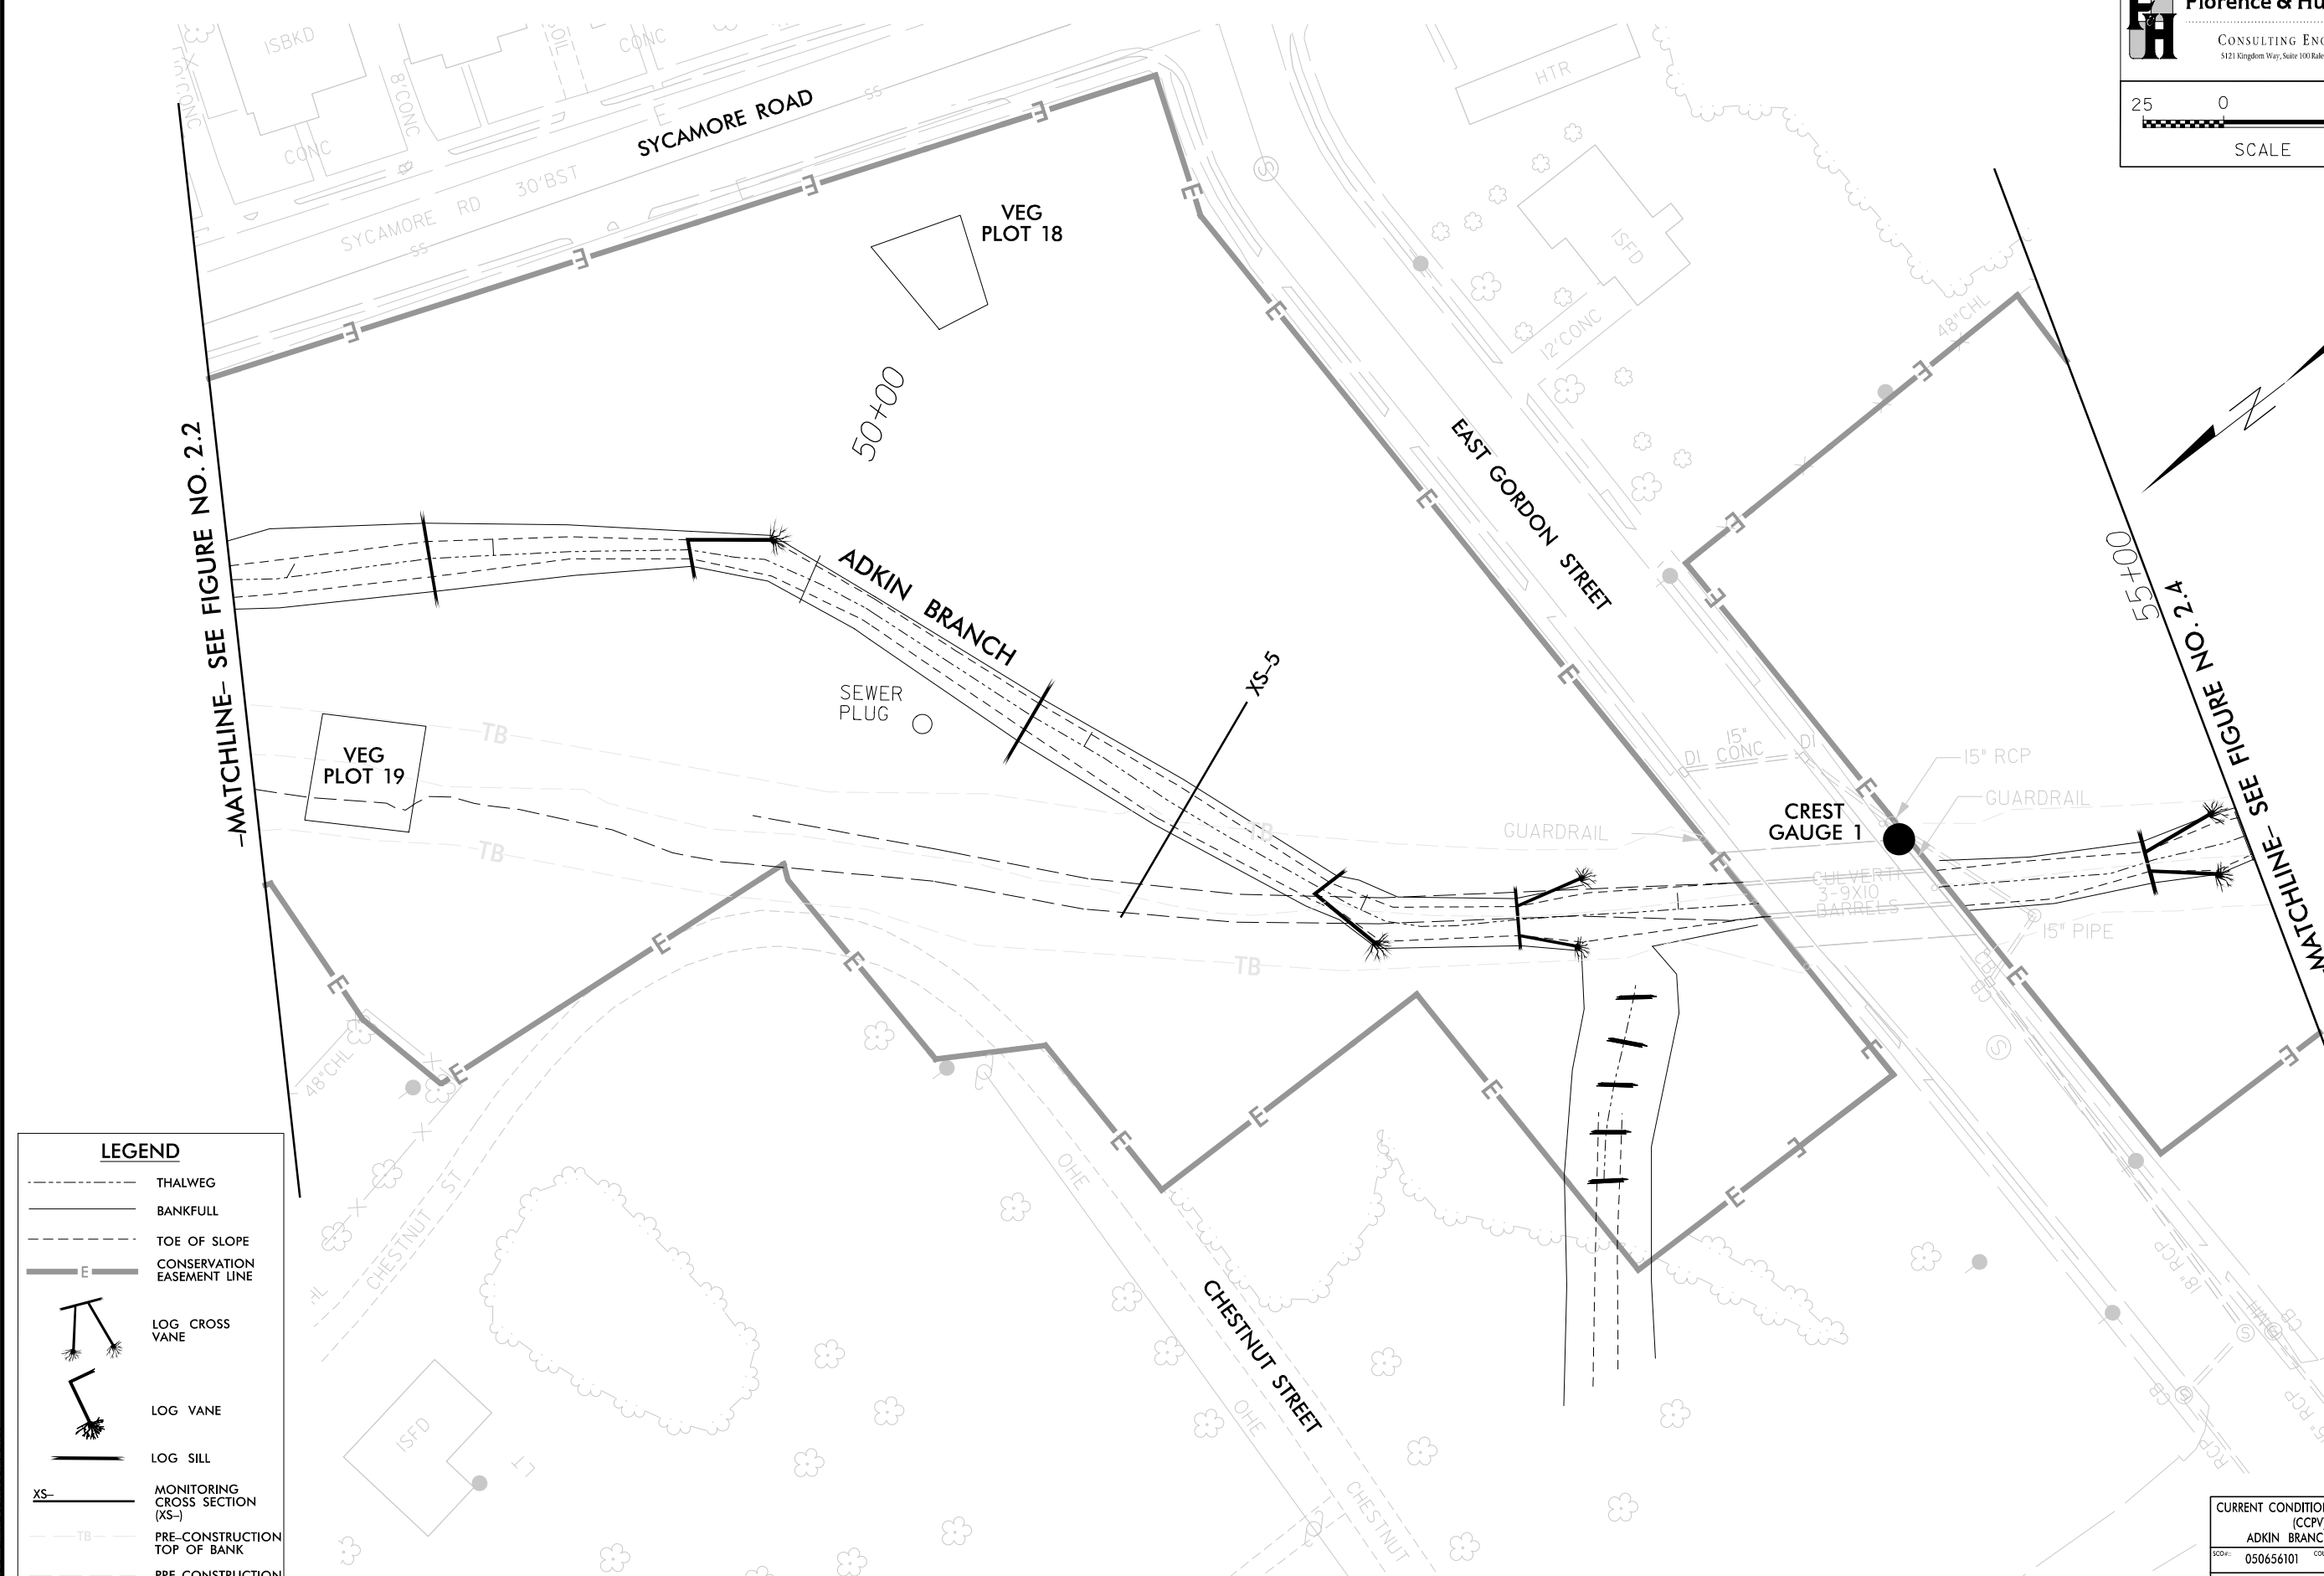


**LEGEND**

- THALWEG
- BANKFULL
- TOE OF SLOPE
- CONSERVATION EASEMENT LINE
- LOG CROSS VANE
- LOG VANE
- LOG SILL
- MONITORING CROSS SECTION (XS-)
- PRE-CONSTRUCTION TOP OF BANK
- PRE-CONSTRUCTION THALWEG


I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_4.dgn  
Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCALE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE: 1/12	

### CURRENT CONDITIONS PLAN VIEW (CCPV)



LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	LOG CROSS VANE
	LOG VANE
	LOG SILL
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG
	MODERATE EROSION

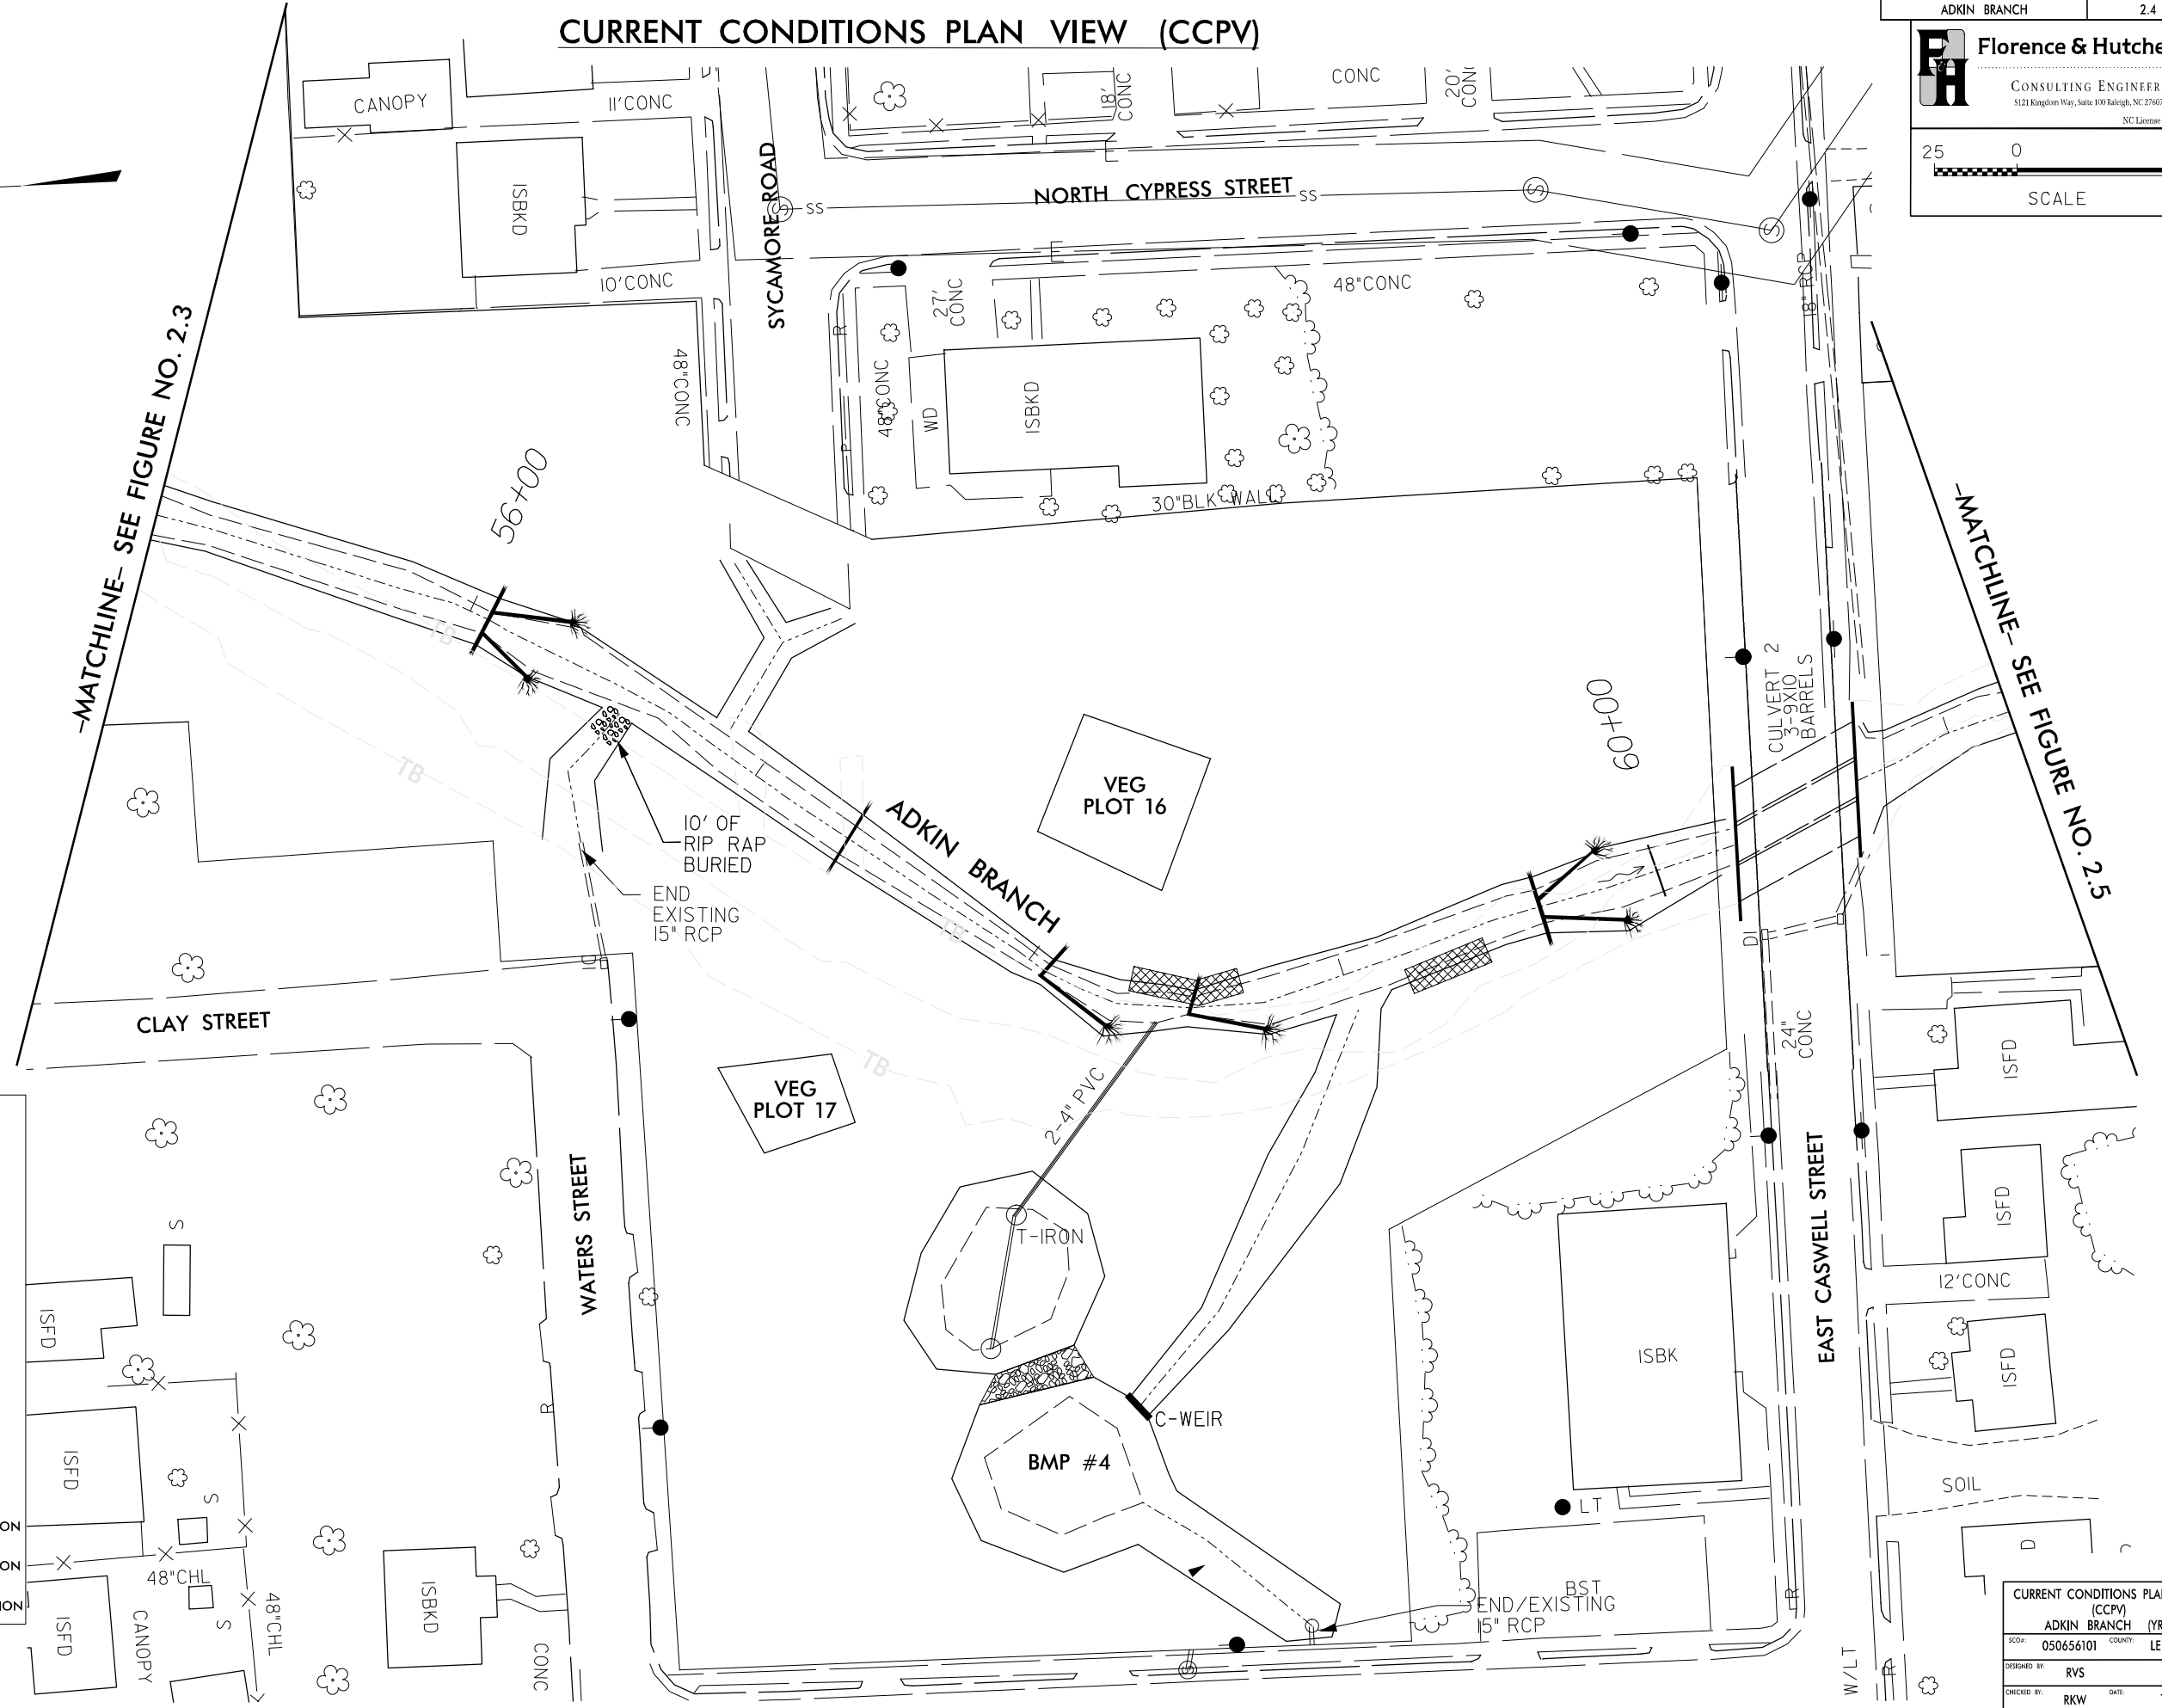














11/21/2012  
 C:\Stream\_Proj\Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_5.dgn  
 Florence & Hutcheson, Inc.


CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCD: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE:	DATE: 11/2



# CURRENT CONDITIONS PLAN VIEW (CCPV)

**LEGEND**

-  THALWEG
-  BANKFULL
-  TOE OF SLOPE
-  CONSERVATION EASEMENT LINE
-  ROOTWAD
-  LOG CROSS VANE
-  LOG VANE
-  LOG SILL
-  SOIL LIFT
-  MONITORING CROSS SECTION (XS-)
-  PRE-CONSTRUCTION TOP OF BANK
-  PRE-CONSTRUCTION THALWEG
-  SEVERE EROSION

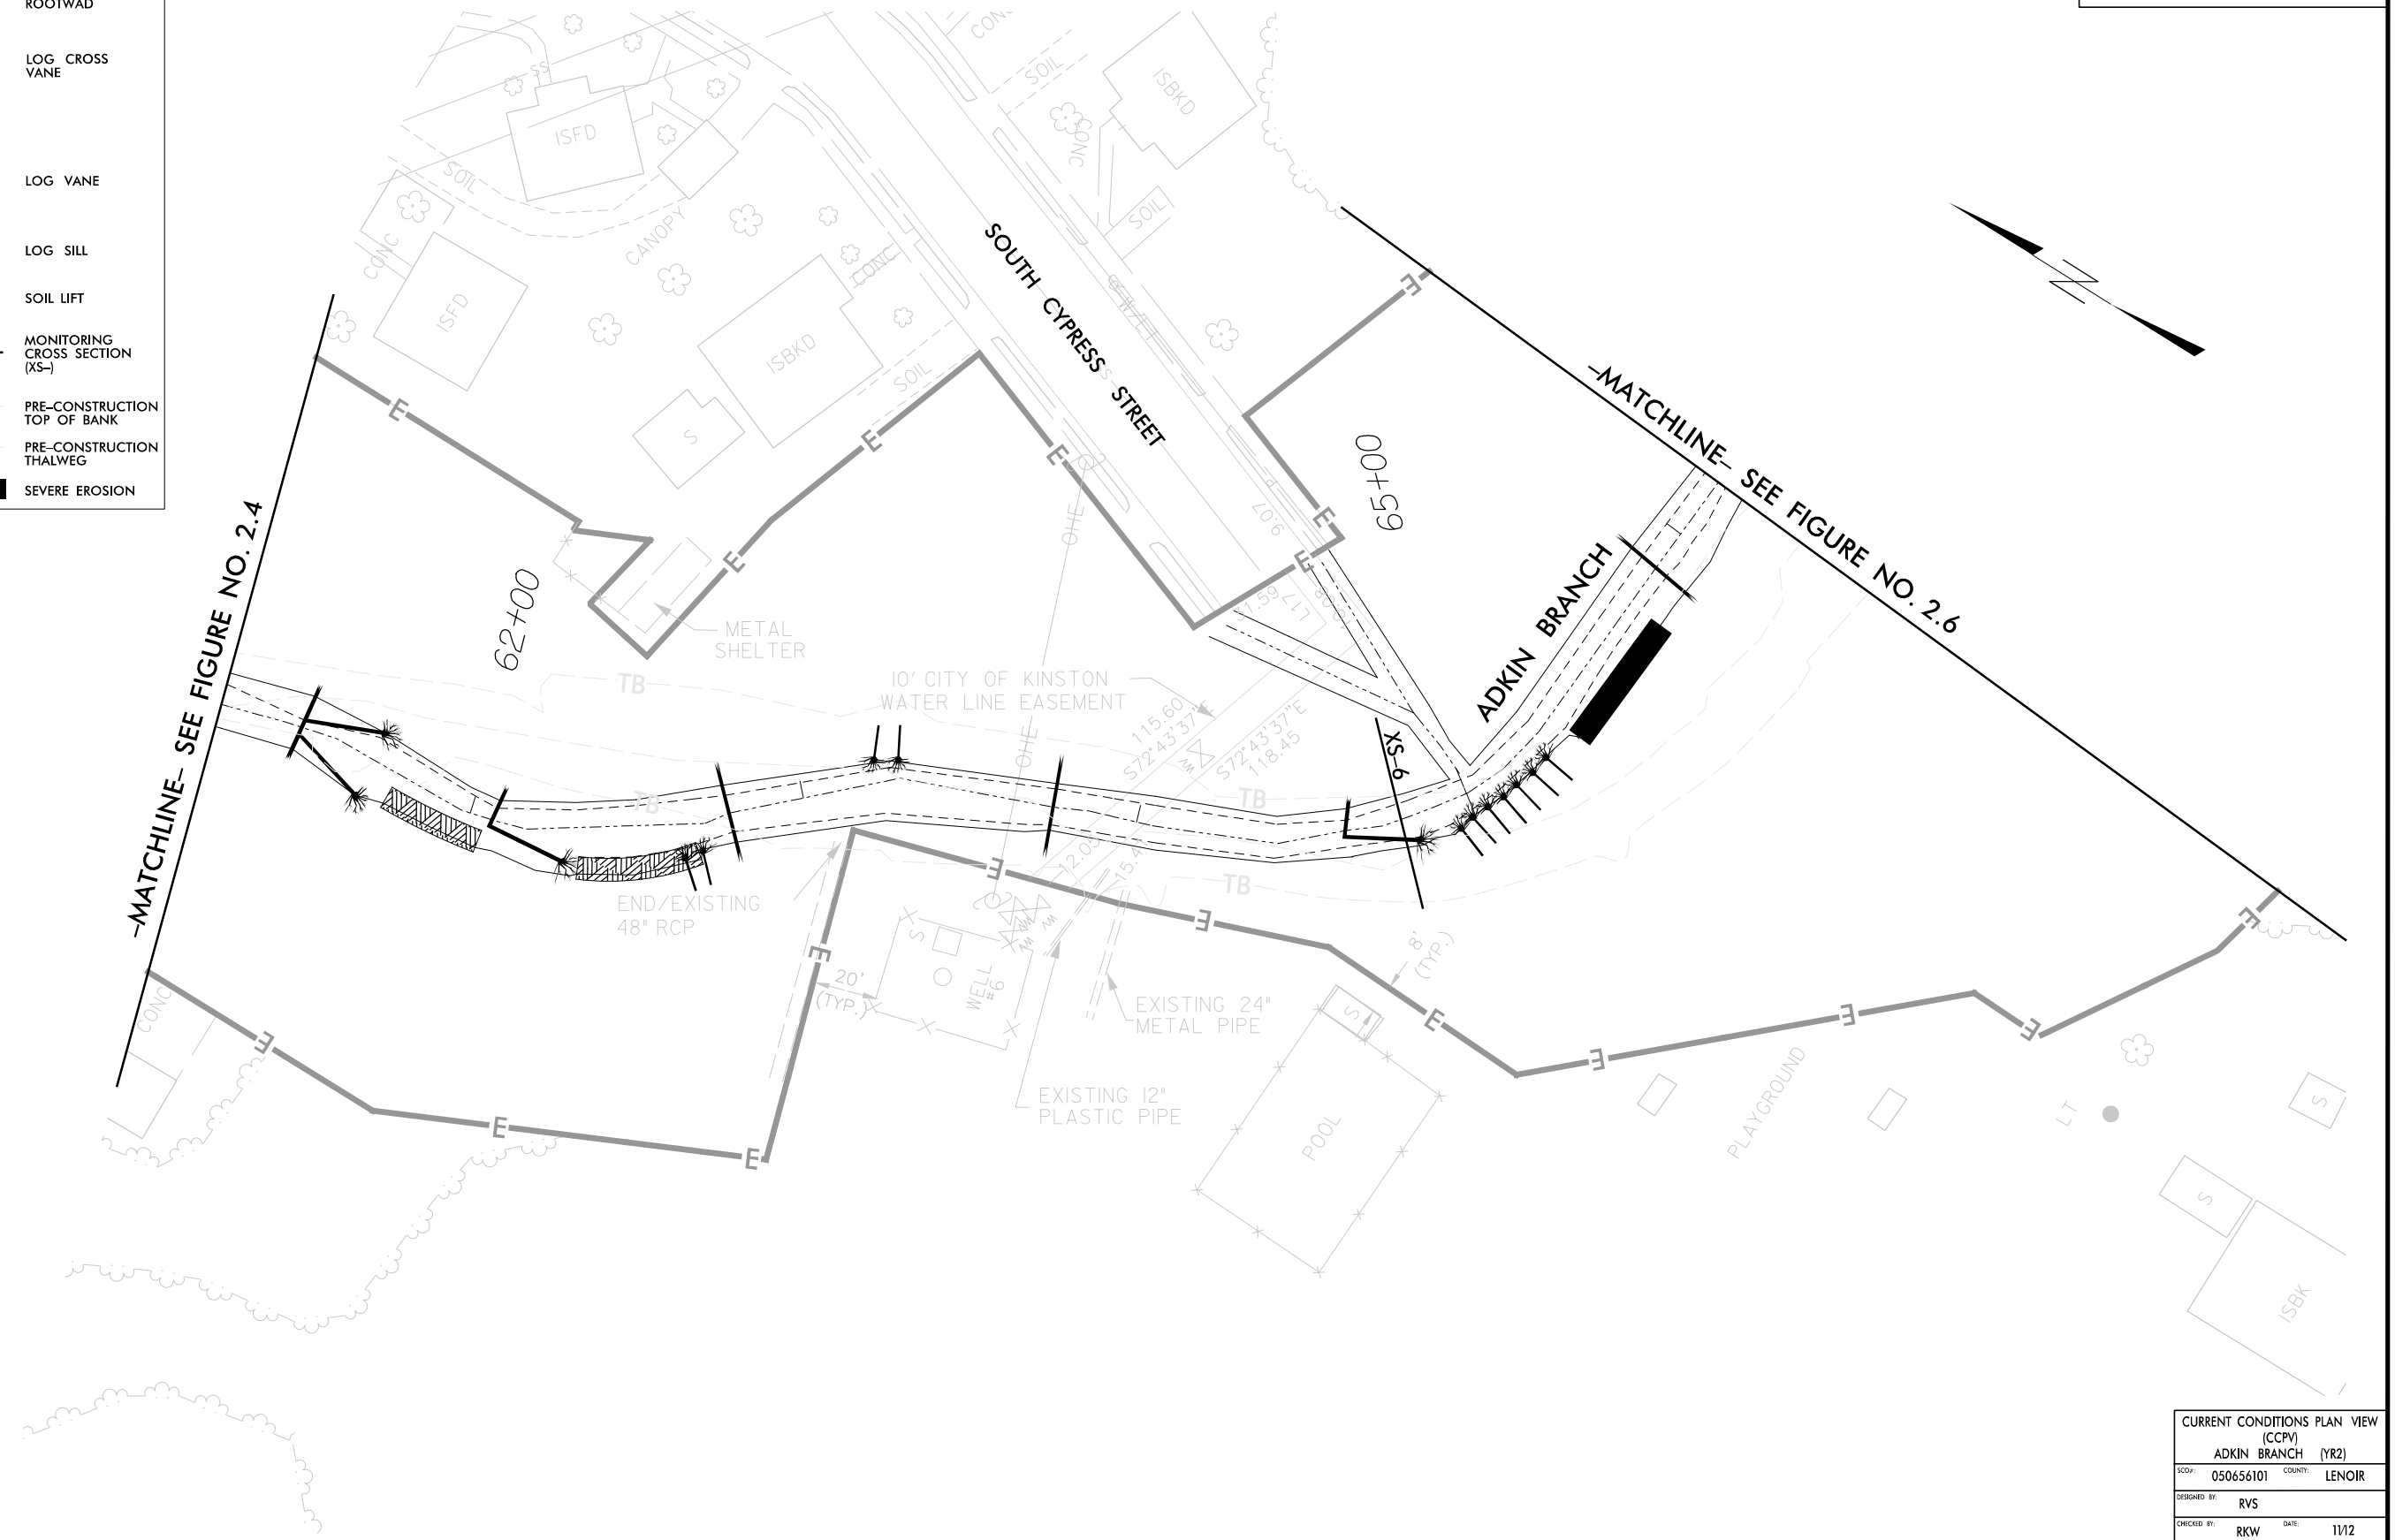


I:\21\2012\Stream\_Proj\Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_6.dgn  
 Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12

# CURRENT CONDITIONS PLAN VIEW (CCPV)

PROJECT REFERENCE NO. ADKIN BRANCH	FIGURE NO. 2.6
<b>Florence &amp; Hutcheson</b> CONSULTING ENGINEERS 5121 Kingdom Way, Suite 100 Raleigh, NC 27607 NC License No. F-0058	
SCALE	

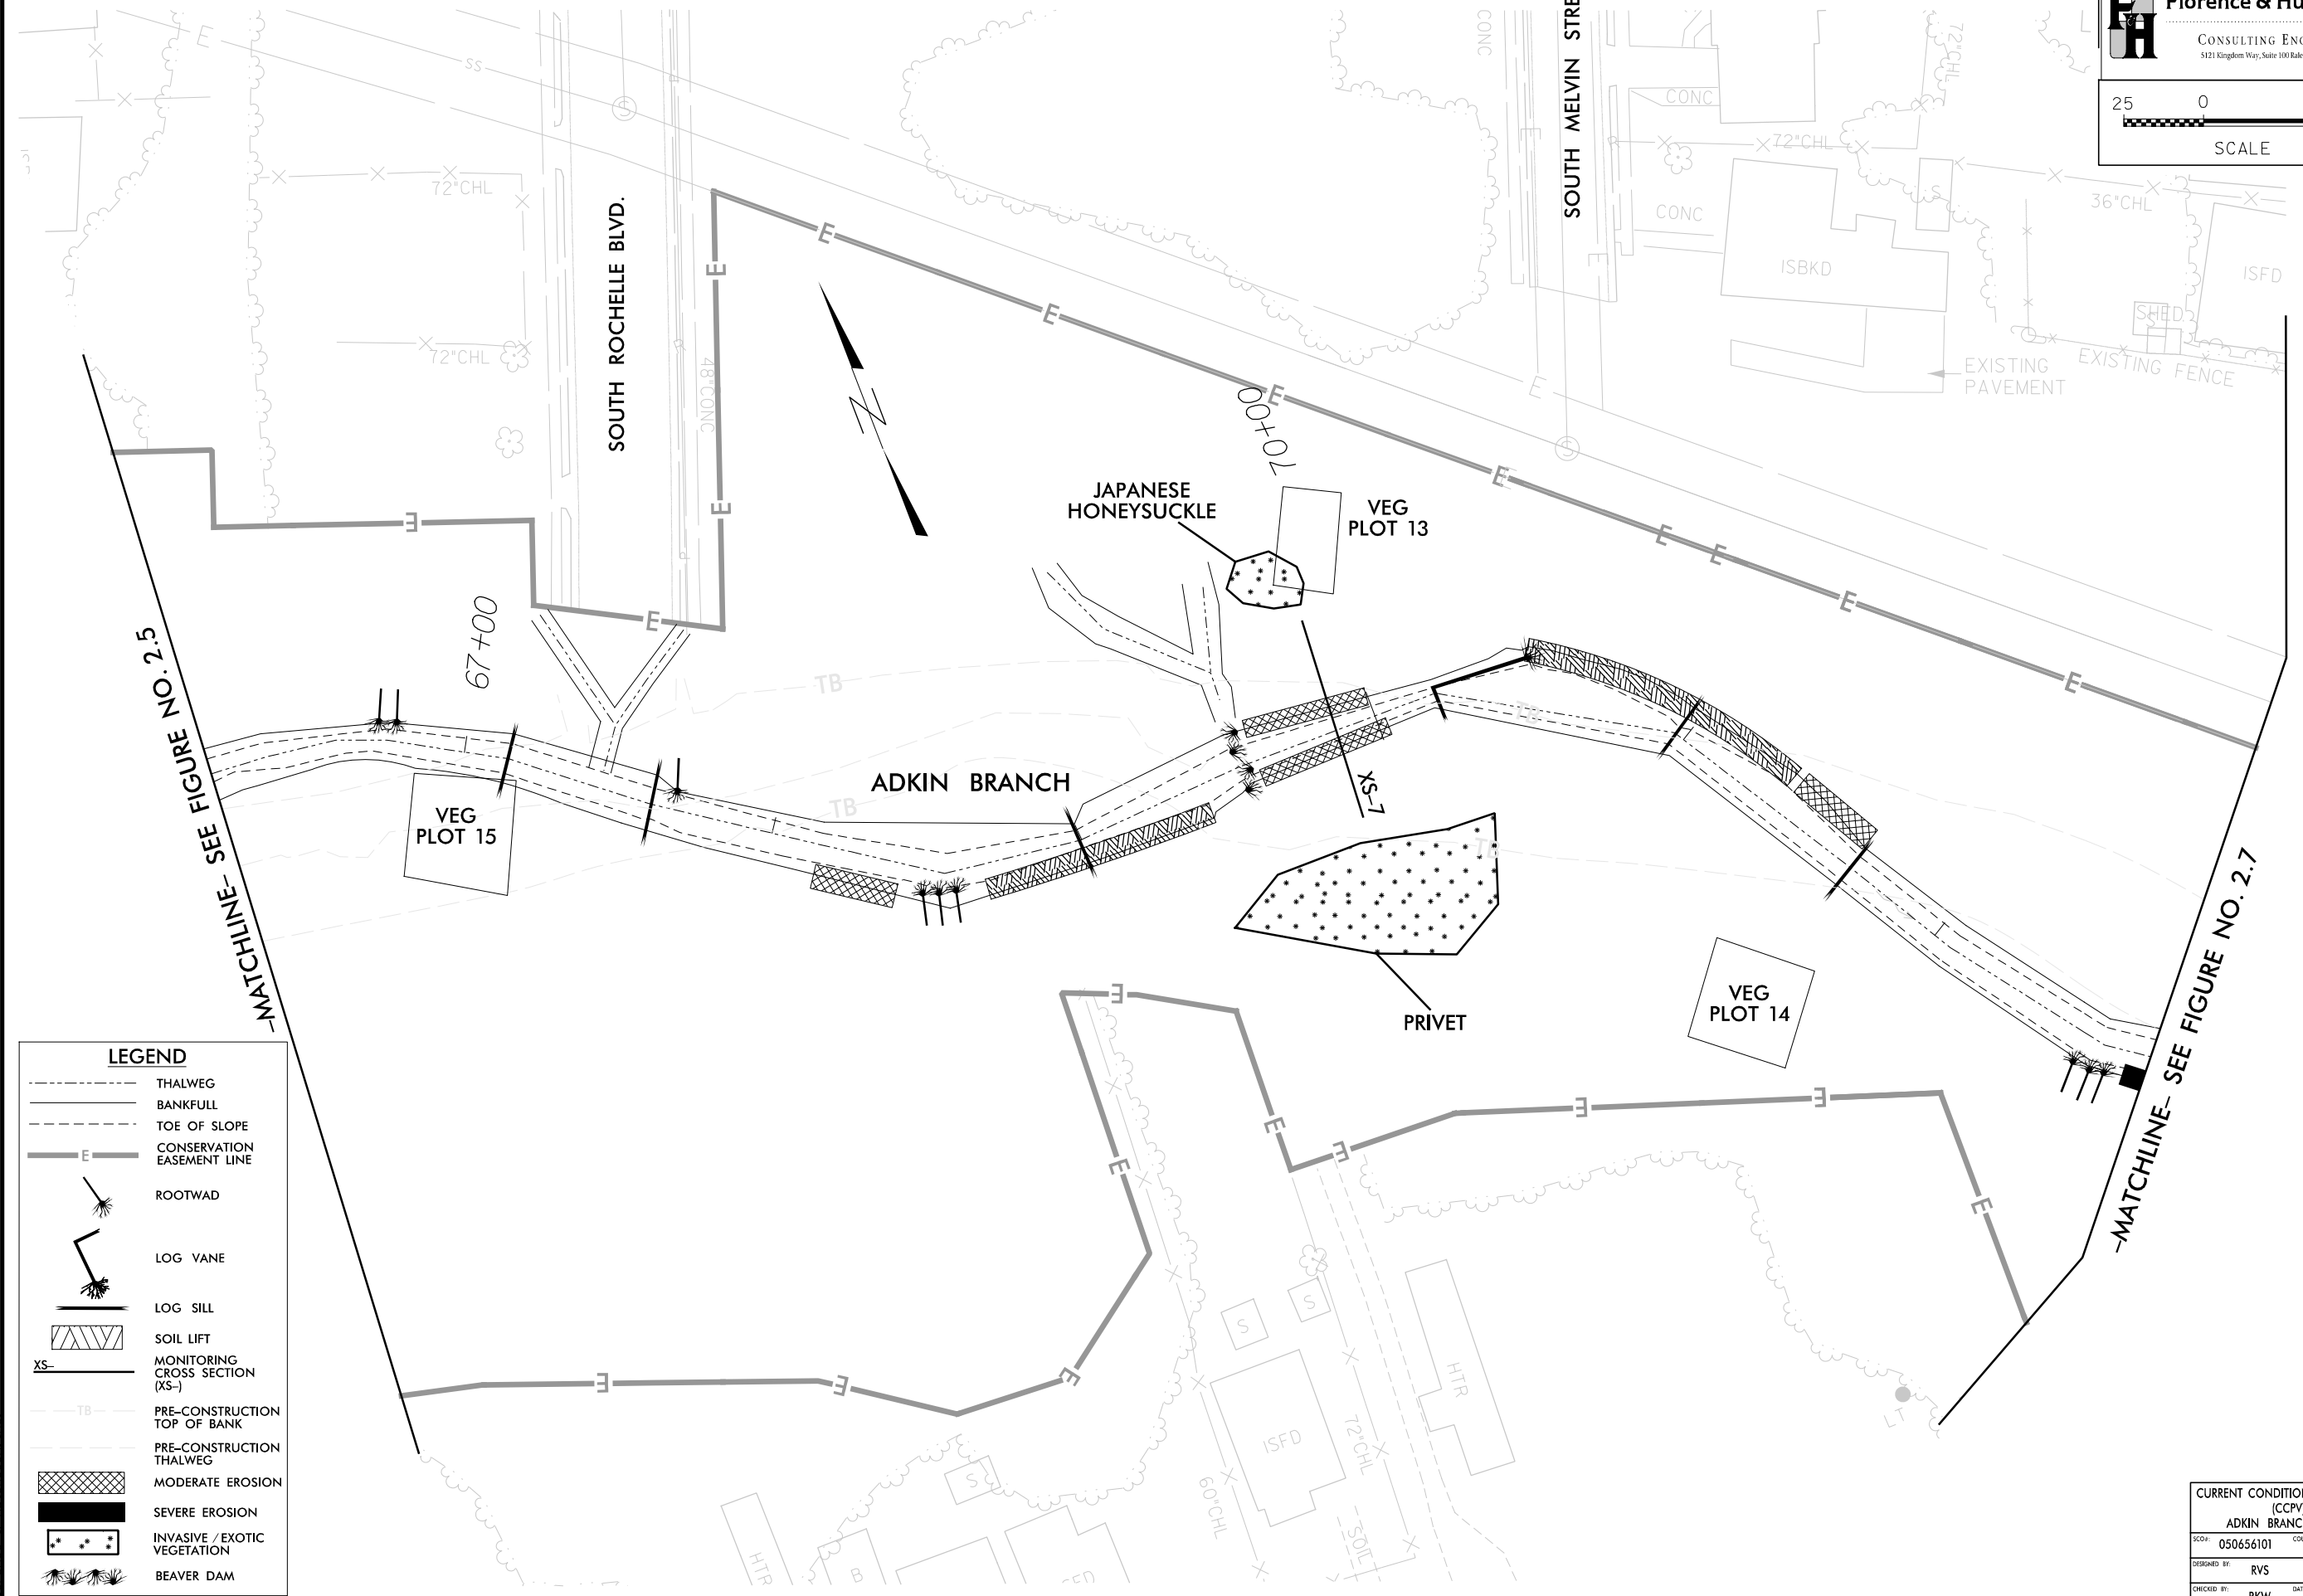

**LEGEND**















- THALWEG
- BANKFULL
- TOE OF SLOPE
- CONSERVATION EASEMENT LINE
- ROOTWAD
- LOG VANE
- LOG SILL
- SOIL LIFT
- MONITORING CROSS SECTION (XS-)
- PRE-CONSTRUCTION TOP OF BANK
- PRE-CONSTRUCTION THALWEG
- MODERATE EROSION
- SEVERE EROSION
- INVASIVE / EXOTIC VEGETATION
- BEAVER DAM


I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_7.dgn  
 Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCO#: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12

# CURRENT CONDITIONS PLAN VIEW (CCPV)

**LEGEND**

-  THALWEG
-  BANKFULL
-  TOE OF SLOPE
-  CONSERVATION EASEMENT LINE
-  ROOTWAD
-  LOG VANE
-  LOG SILL
-  SOIL LIFT
-  MONITORING CROSS SECTION (XS-)
-  PRE-CONSTRUCTION TOP OF BANK
-  PRE-CONSTRUCTION THALWEG
-  MODERATE EROSION
-  SEVERE EROSION
-  INVASIVE / EXOTIC VEGETATION

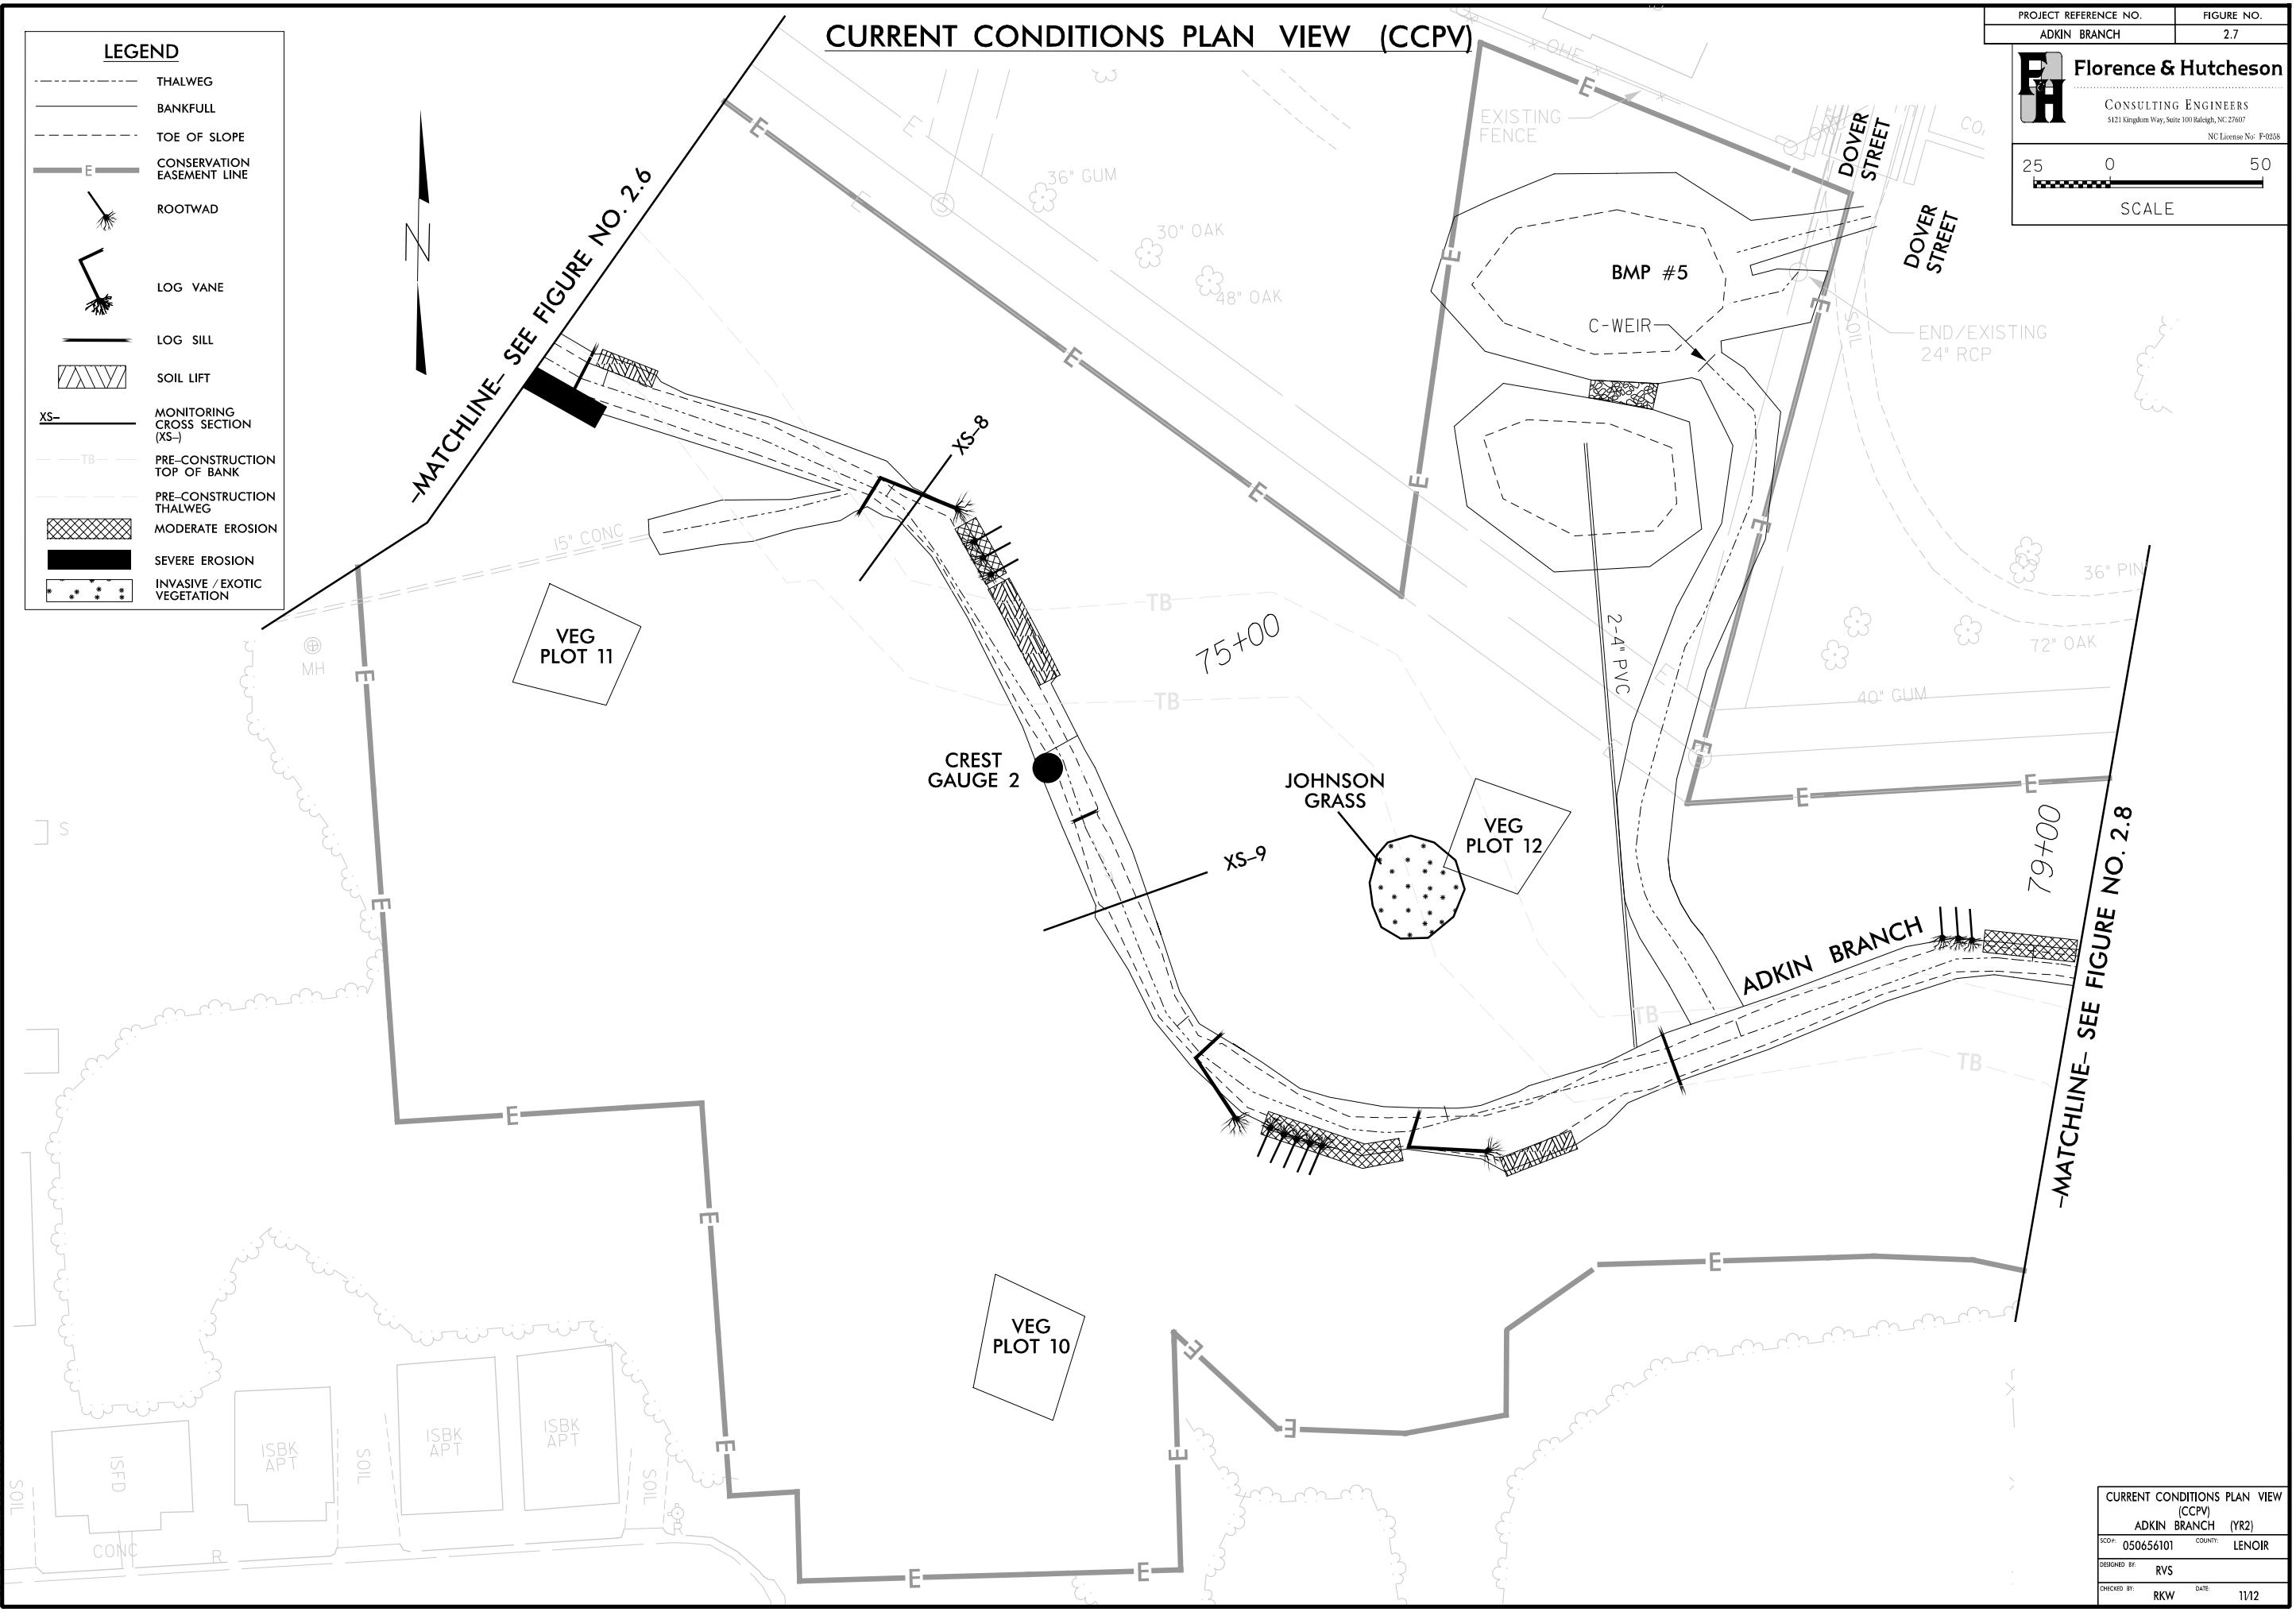

-MATCHLINE- SEE FIGURE NO. 2.6

-MATCHLINE- SEE FIGURE NO. 2.8


I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_8.dgn  
 Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOP: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12



### CURRENT CONDITIONS PLAN VIEW (CCPV)

LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	ROOTWAD
	LOG CROSS VANE
	LOG SILL
	SOIL LIFT
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG
	MODERATE EROSION
	SEVERE EROSION
	RIP-RAP

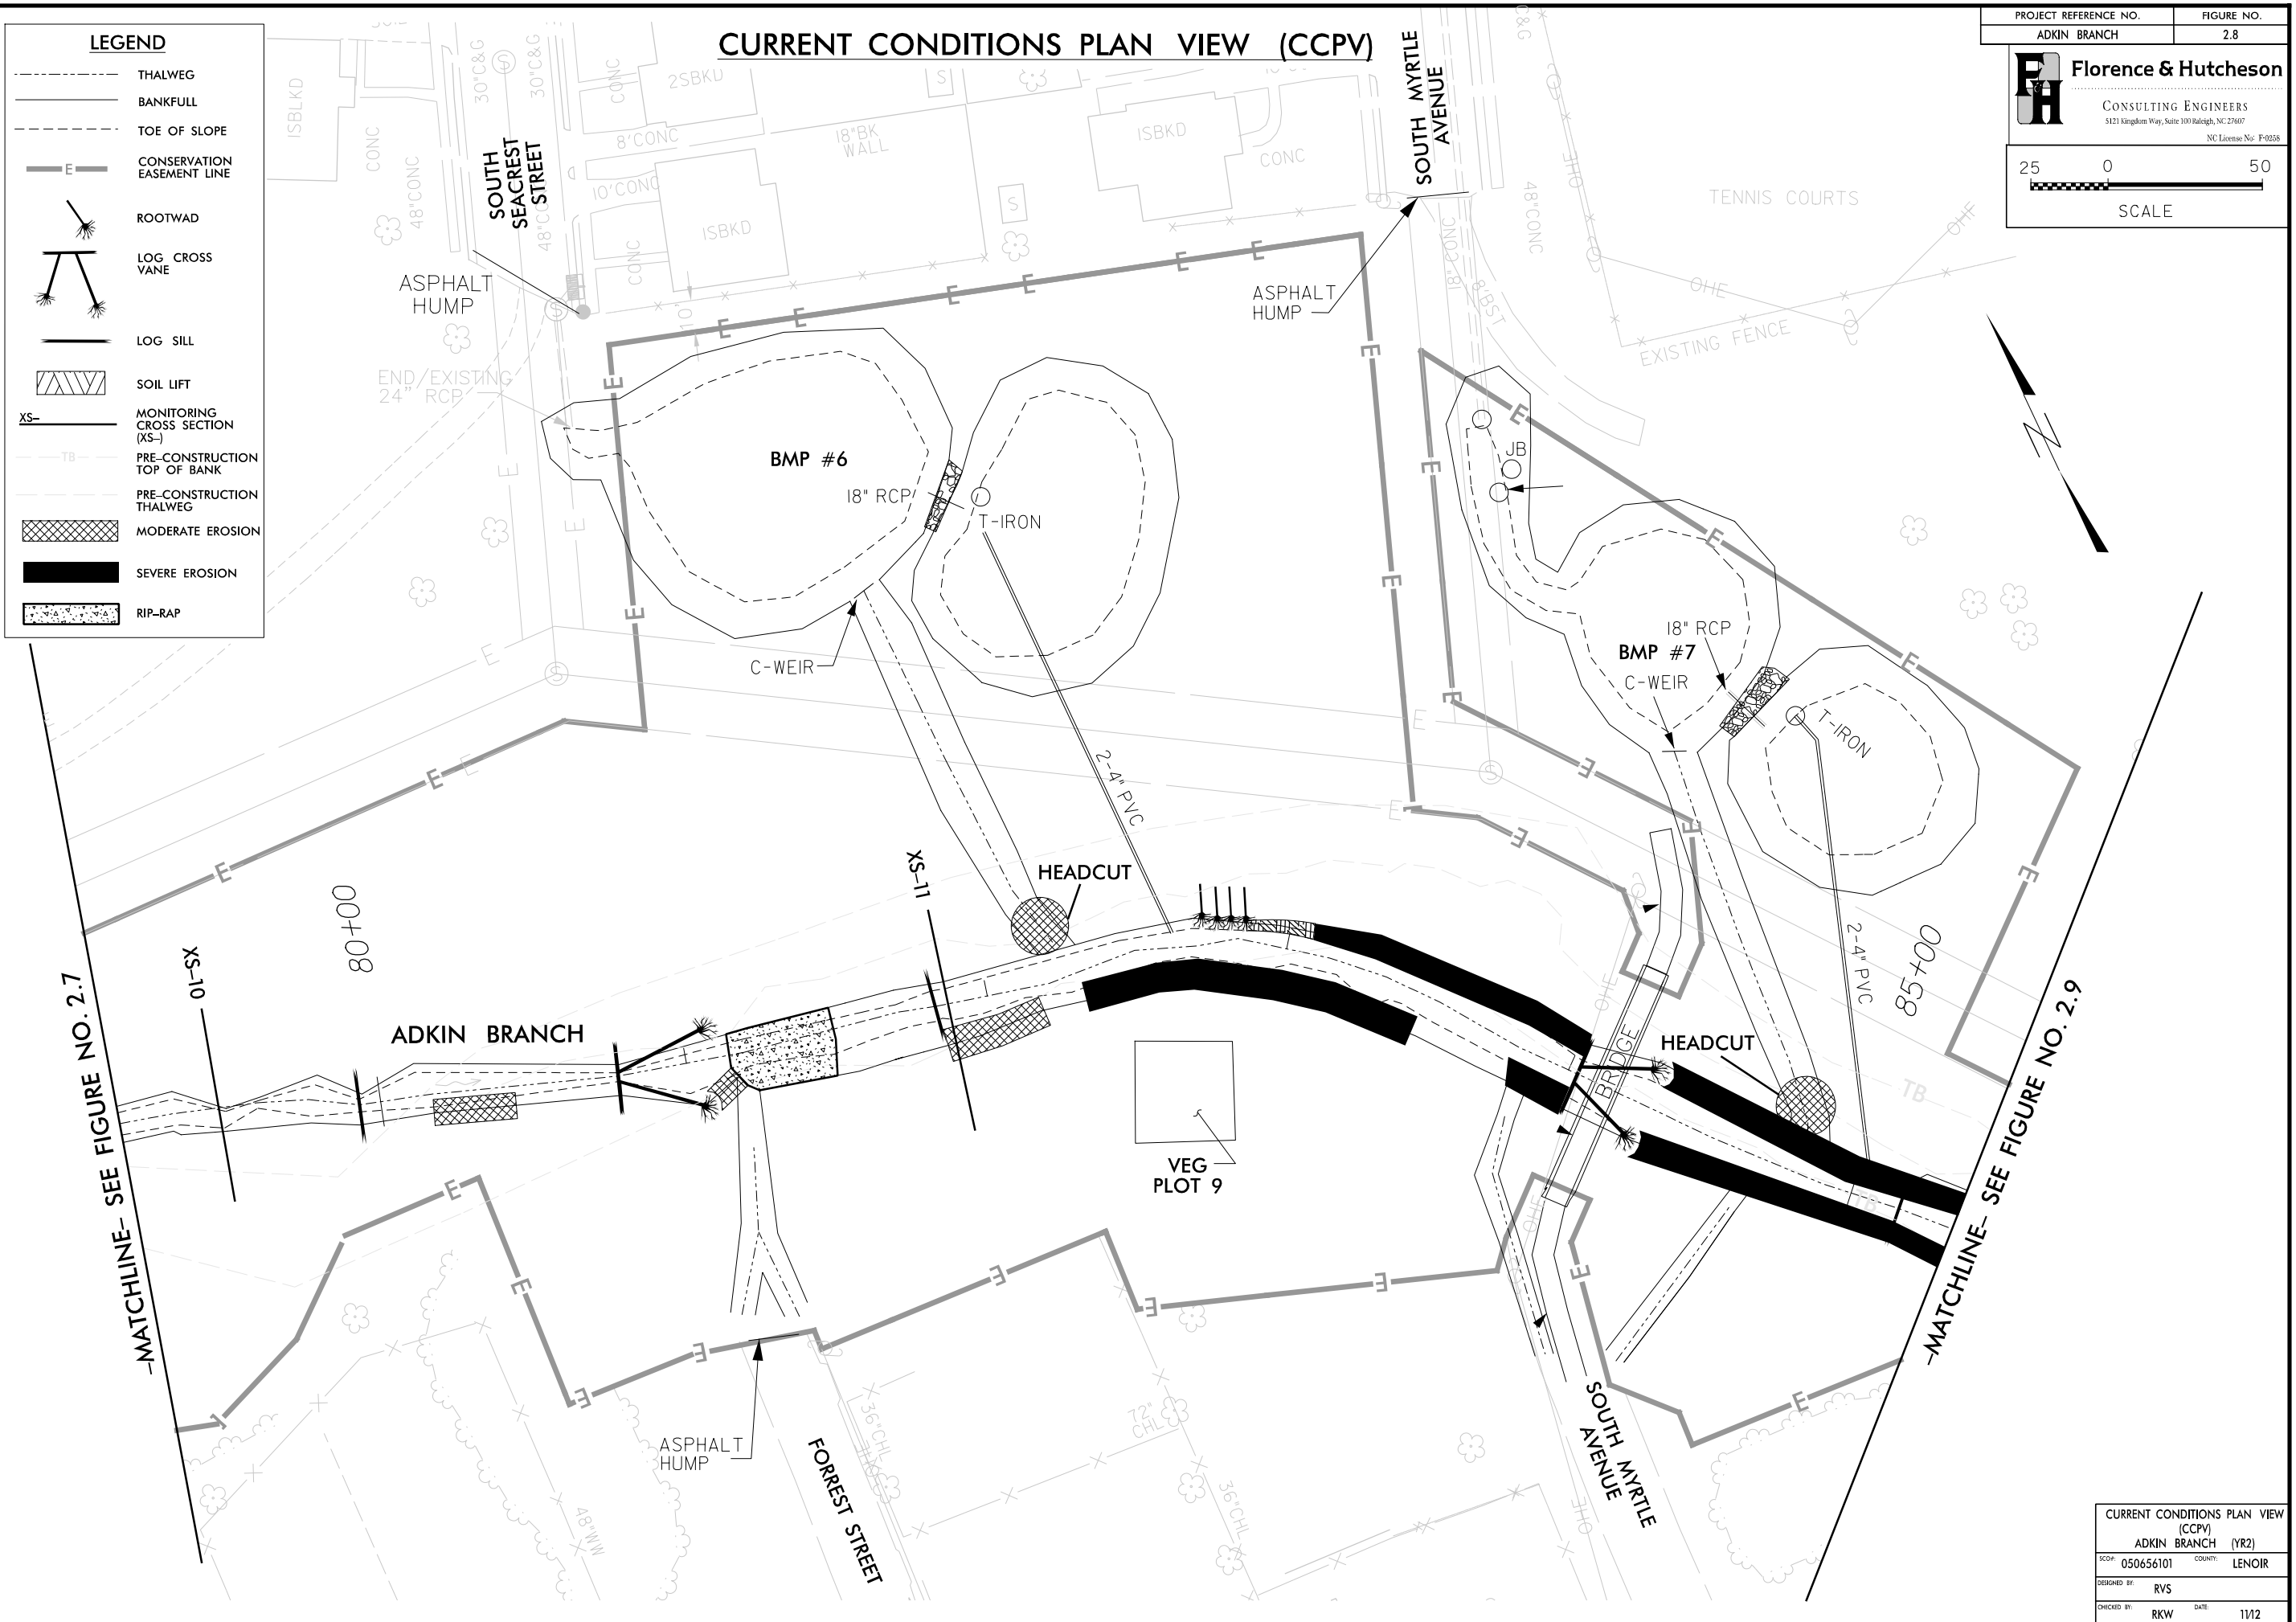

-MATCHLINE- SEE FIGURE NO. 2.7

-MATCHLINE- SEE FIGURE NO. 2.9

I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_9.dgn  
 Florence & Hutcheson, Inc.


CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOP: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12

# CURRENT CONDITIONS PLAN VIEW (CCPV)

PROJECT REFERENCE NO. ADKIN BRANCH	FIGURE NO. 2.9
CONSULTING ENGINEERS 5121 Kingdom Way, Suite 100 Raleigh, NC 27607 NC License No. F-0058	
25 0 50 SCALE	

### LEGEND

	THALWEG		SOIL LIFT
	BANKFULL		FLOODPLAIN INTERCEPTOR (FPI)
	TOE OF SLOPE		MONITORING CROSS SECTION (XS-)
	CONSERVATION EASEMENT LINE		PRE-CONSTRUCTION TOP OF BANK
	ROOTWAD		PRE-CONSTRUCTION THALWEG
	LOG CROSS VANE		MODERATE EROSION
	LOG VANE		SEVERE EROSION
	LOG SILL		INVASIVE / EXOTIC VEGETATION

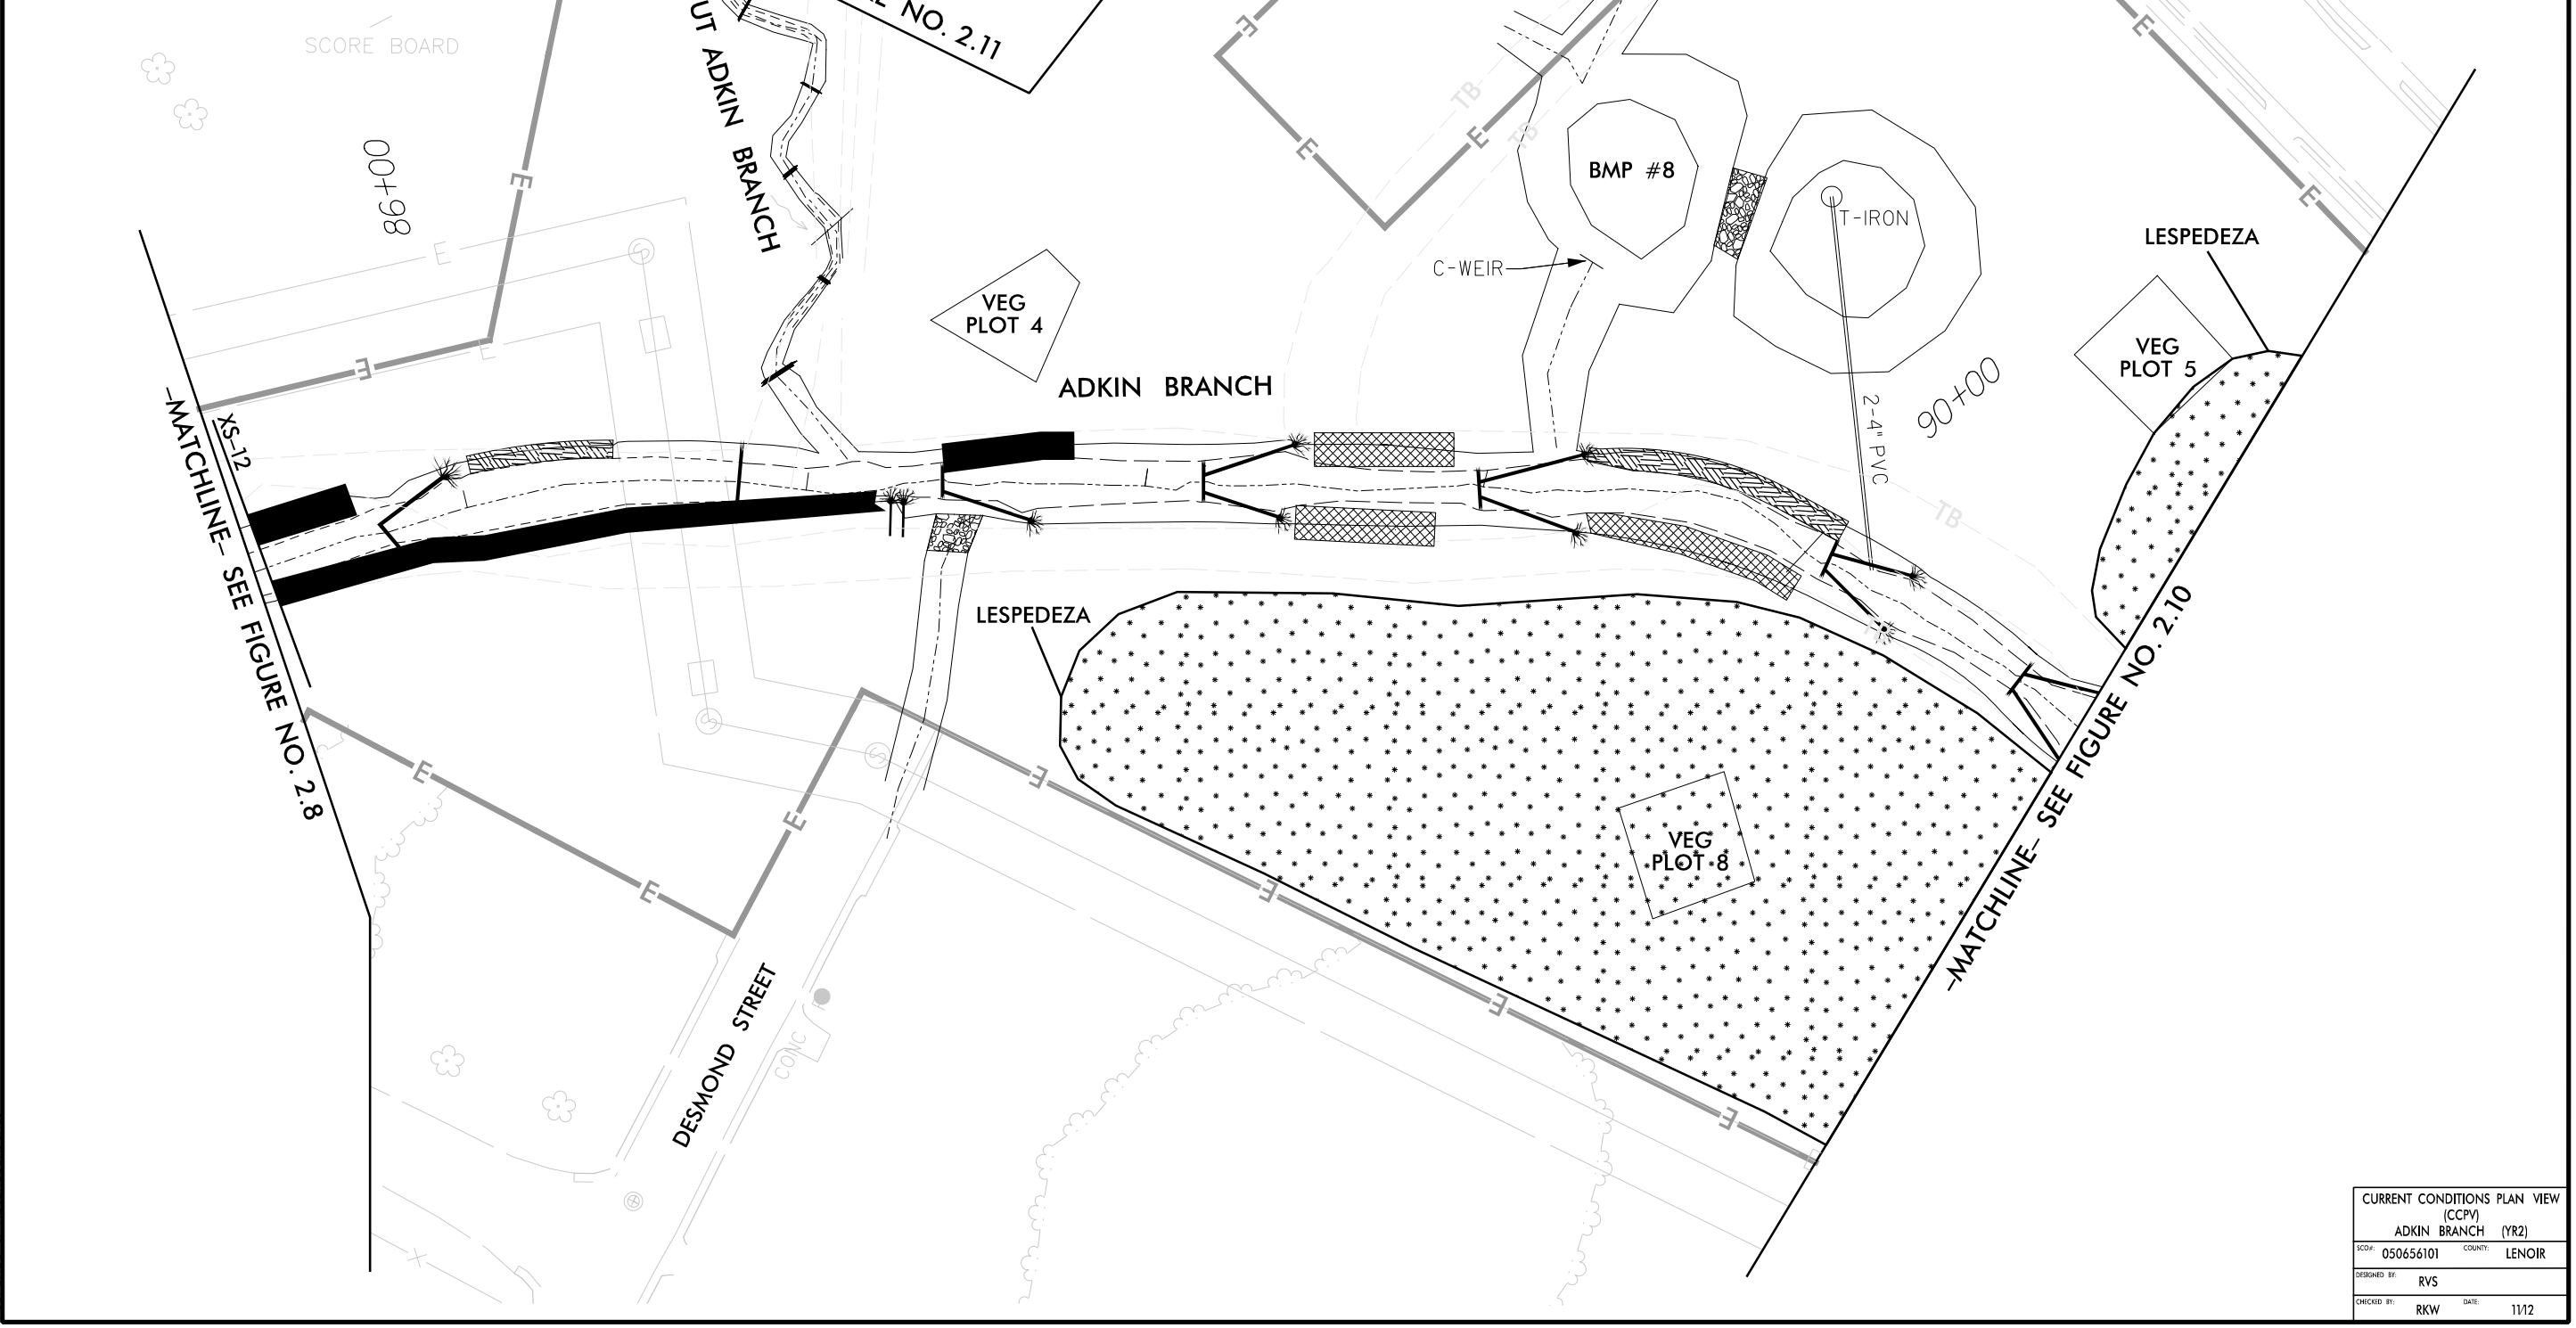

I:\21\2012\Stream\_Proj\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_10.dgn  
 Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	
CHECKED BY: RKW	DATE: 11/12

# CURRENT CONDITIONS PLAN VIEW (CCPV)


PROJECT REFERENCE NO. ADKIN BRANCH  
 FIGURE NO. 2.10

**Florence & Hutcheson**  
 CONSULTING ENGINEERS  
 5121 Kingdom Way, Suite 100 Raleigh, NC 27607  
 NC License No. F-0058



LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	LOG CROSS VANE
	DOUBLE STEP LOG CROSS VANE
	DOUBLE STEP LOG VANE
	LOG SILL
	SOIL LIFT
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG
	MODERATE EROSION
	SEVERE EROSION
	THIN GRASS
	INVASIVE / EXOTIC VEGETATION

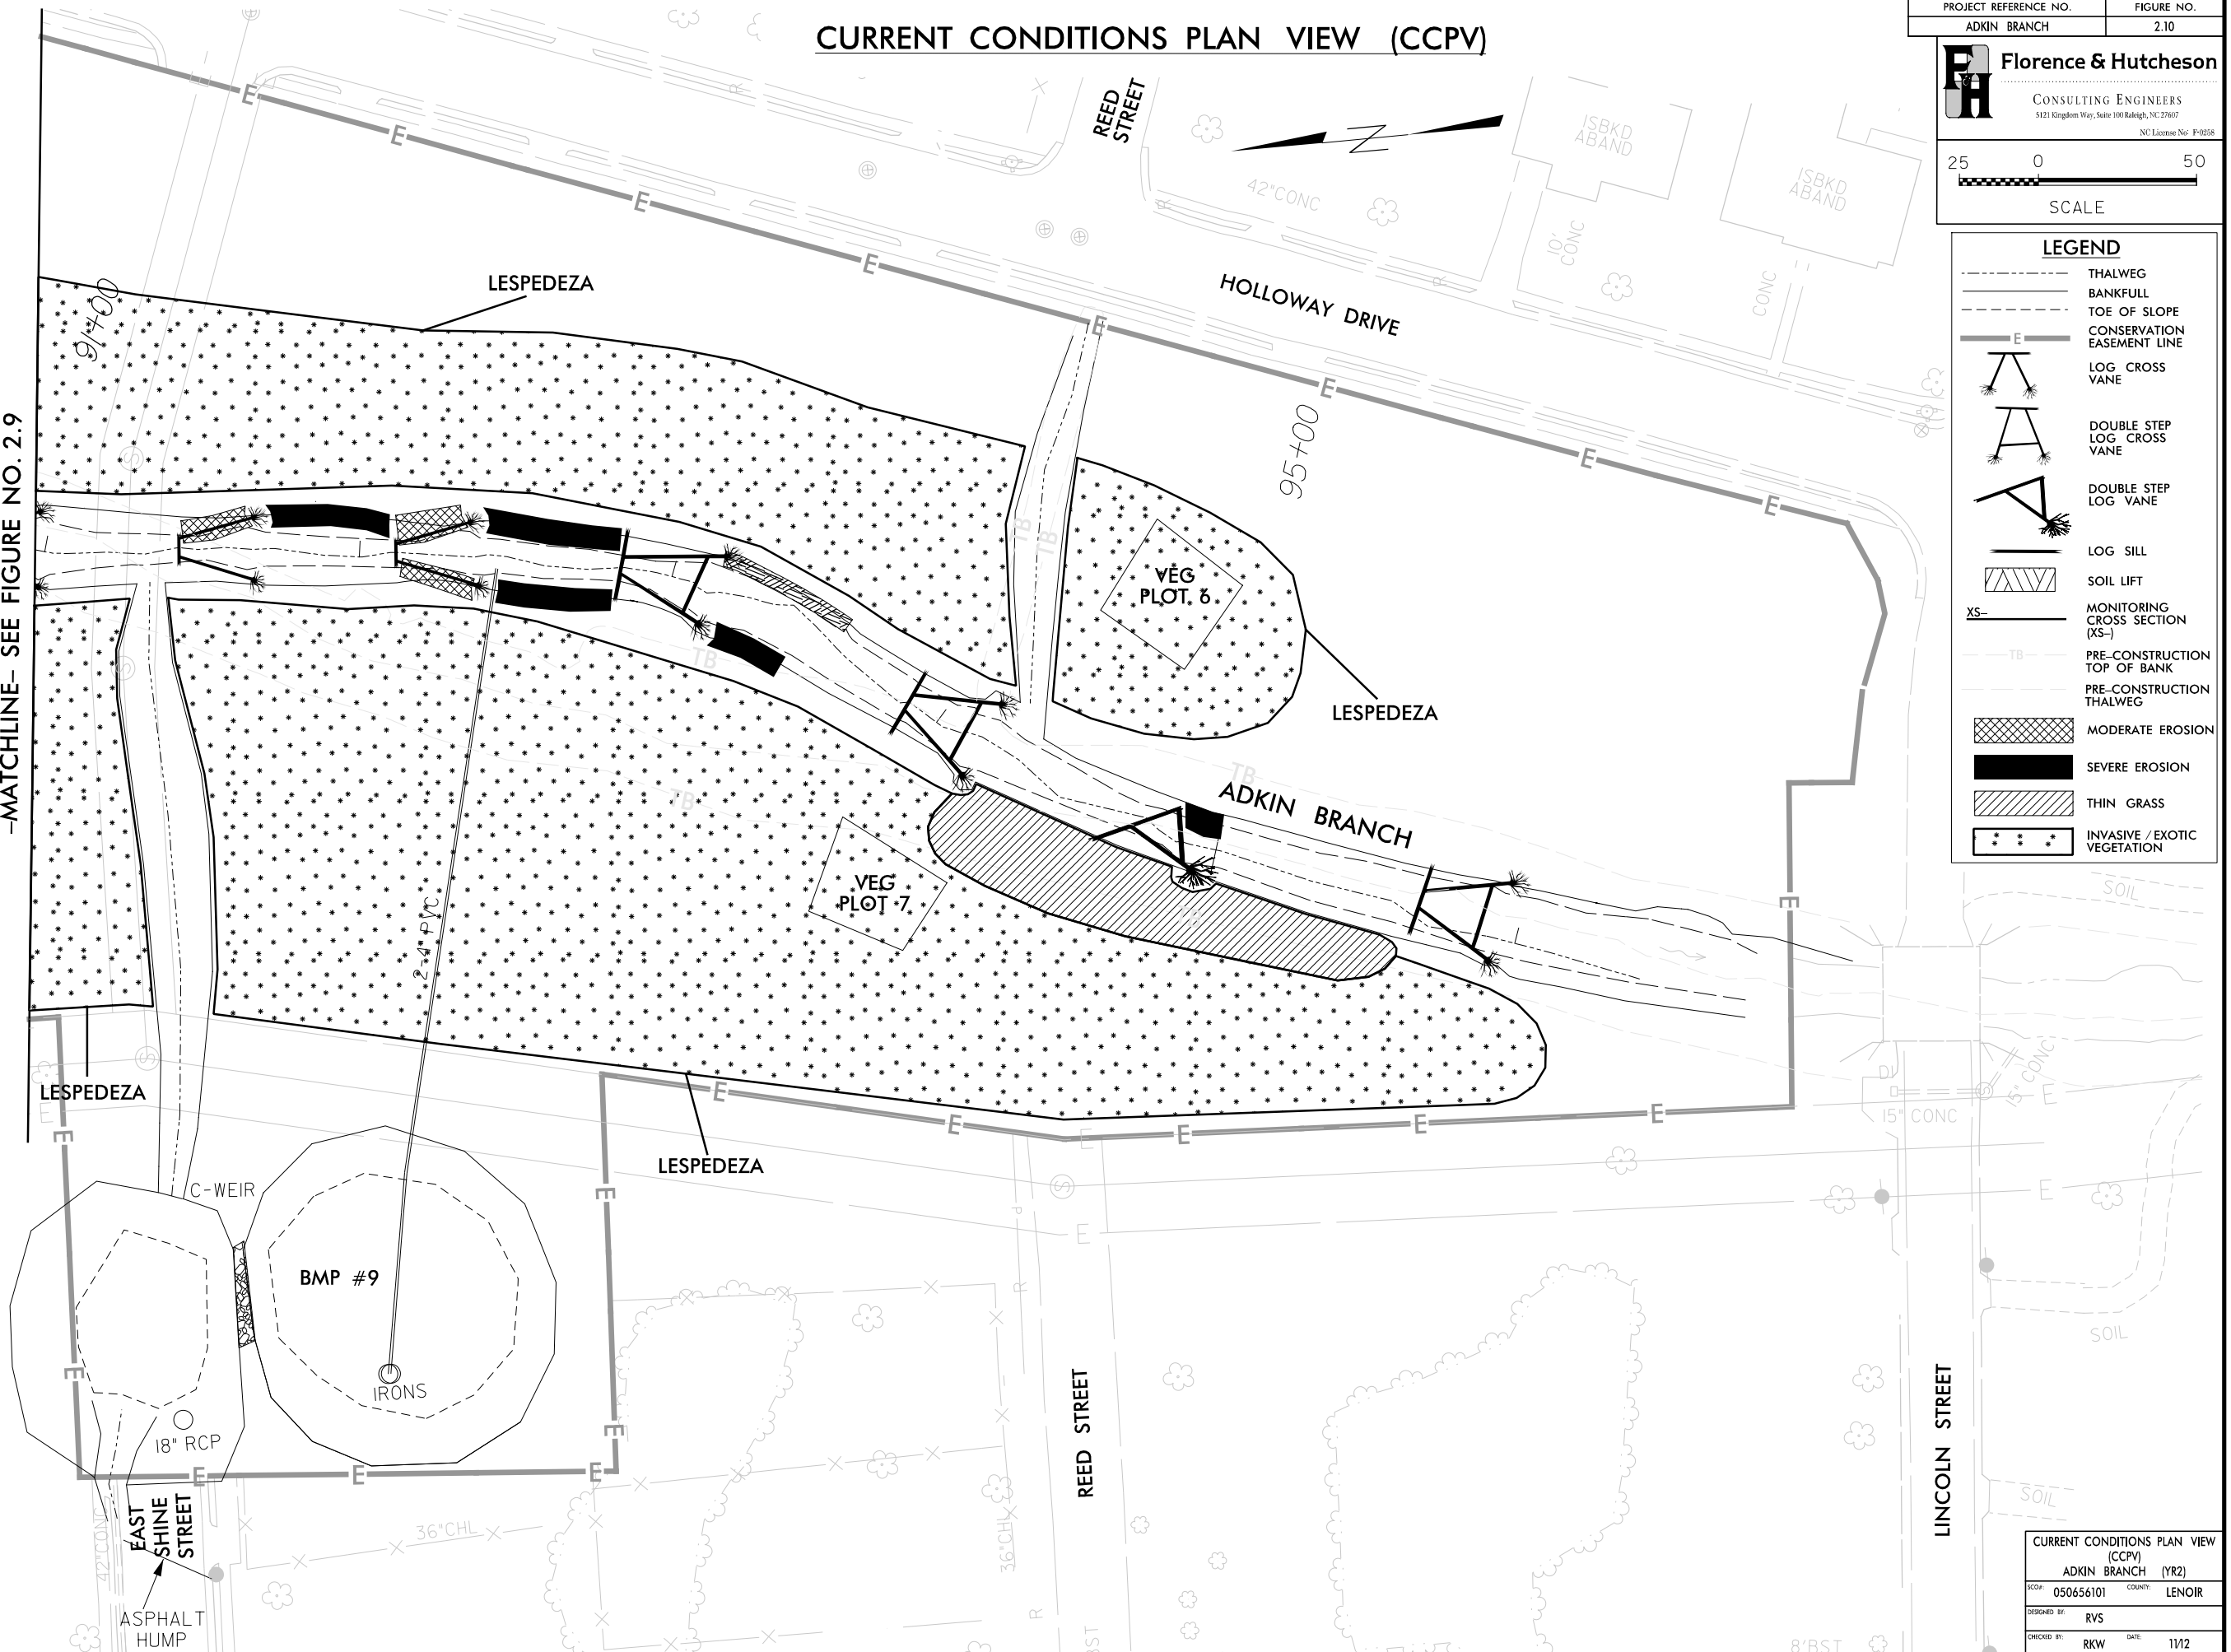

-MATCHLINE- SEE FIGURE NO. 2.9




11/27/2012  
 C:\Stream\_Proj\Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh.11.dgn  
 Florence & Hutcheson, Inc.

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE: 1/12	

# CURRENT CONDITIONS PLAN VIEW (CCPV)

PROJECT REFERENCE NO. ADKIN BRANCH	FIGURE NO. 2.11
 <b>Florence &amp; Hutcheson</b> CONSULTING ENGINEERS <small>5121 Kingdom Way, Suite 100 Raleigh, NC 27607          NC License No. F-0035</small>	
 SCALE	

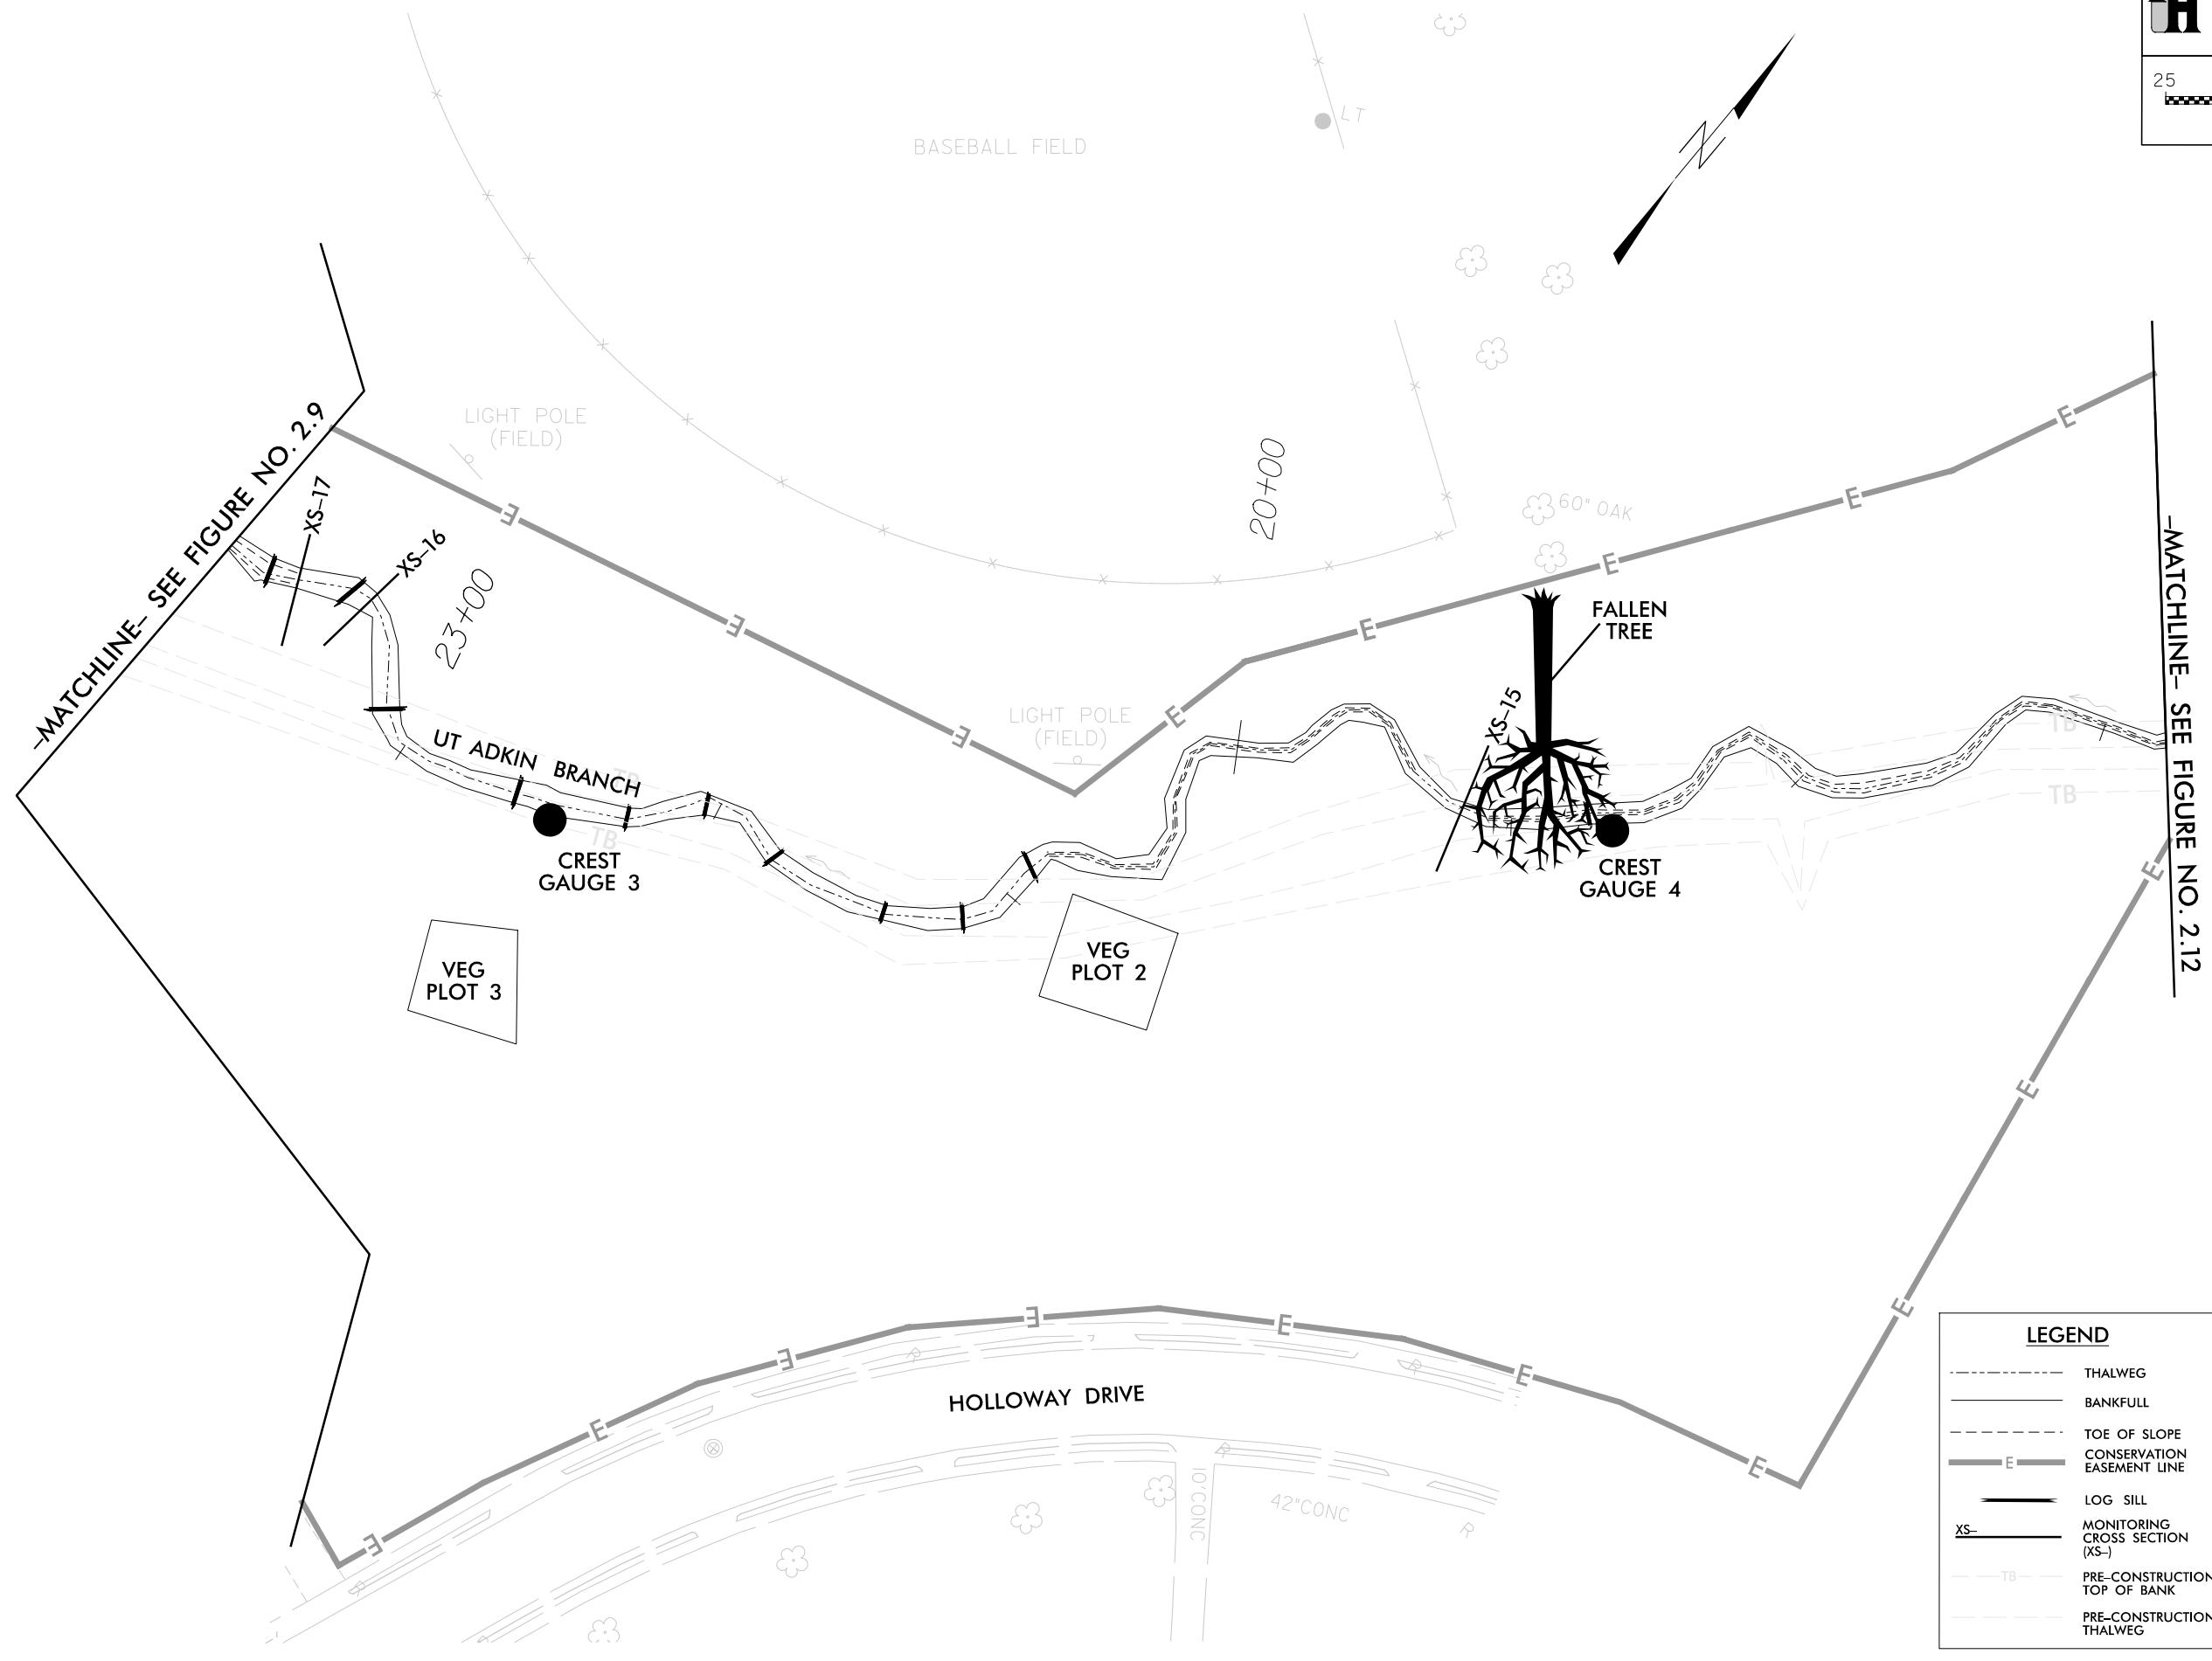



LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	LOG SILL
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG


CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCO: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE: 11/12	

I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_12.dgn  
 Florence & Hutcheson, Inc.



# CURRENT CONDITIONS PLAN VIEW (CCPV)

PROJECT REFERENCE NO. ADKIN BRANCH	FIGURE NO. 2.12
 <b>Florence &amp; Hutcheson</b> CONSULTING ENGINEERS <small>5121 Kingdom Way, Suite 100 Raleigh, NC 27607</small> <small>NC License No. F-0058</small>	
 SCALE	

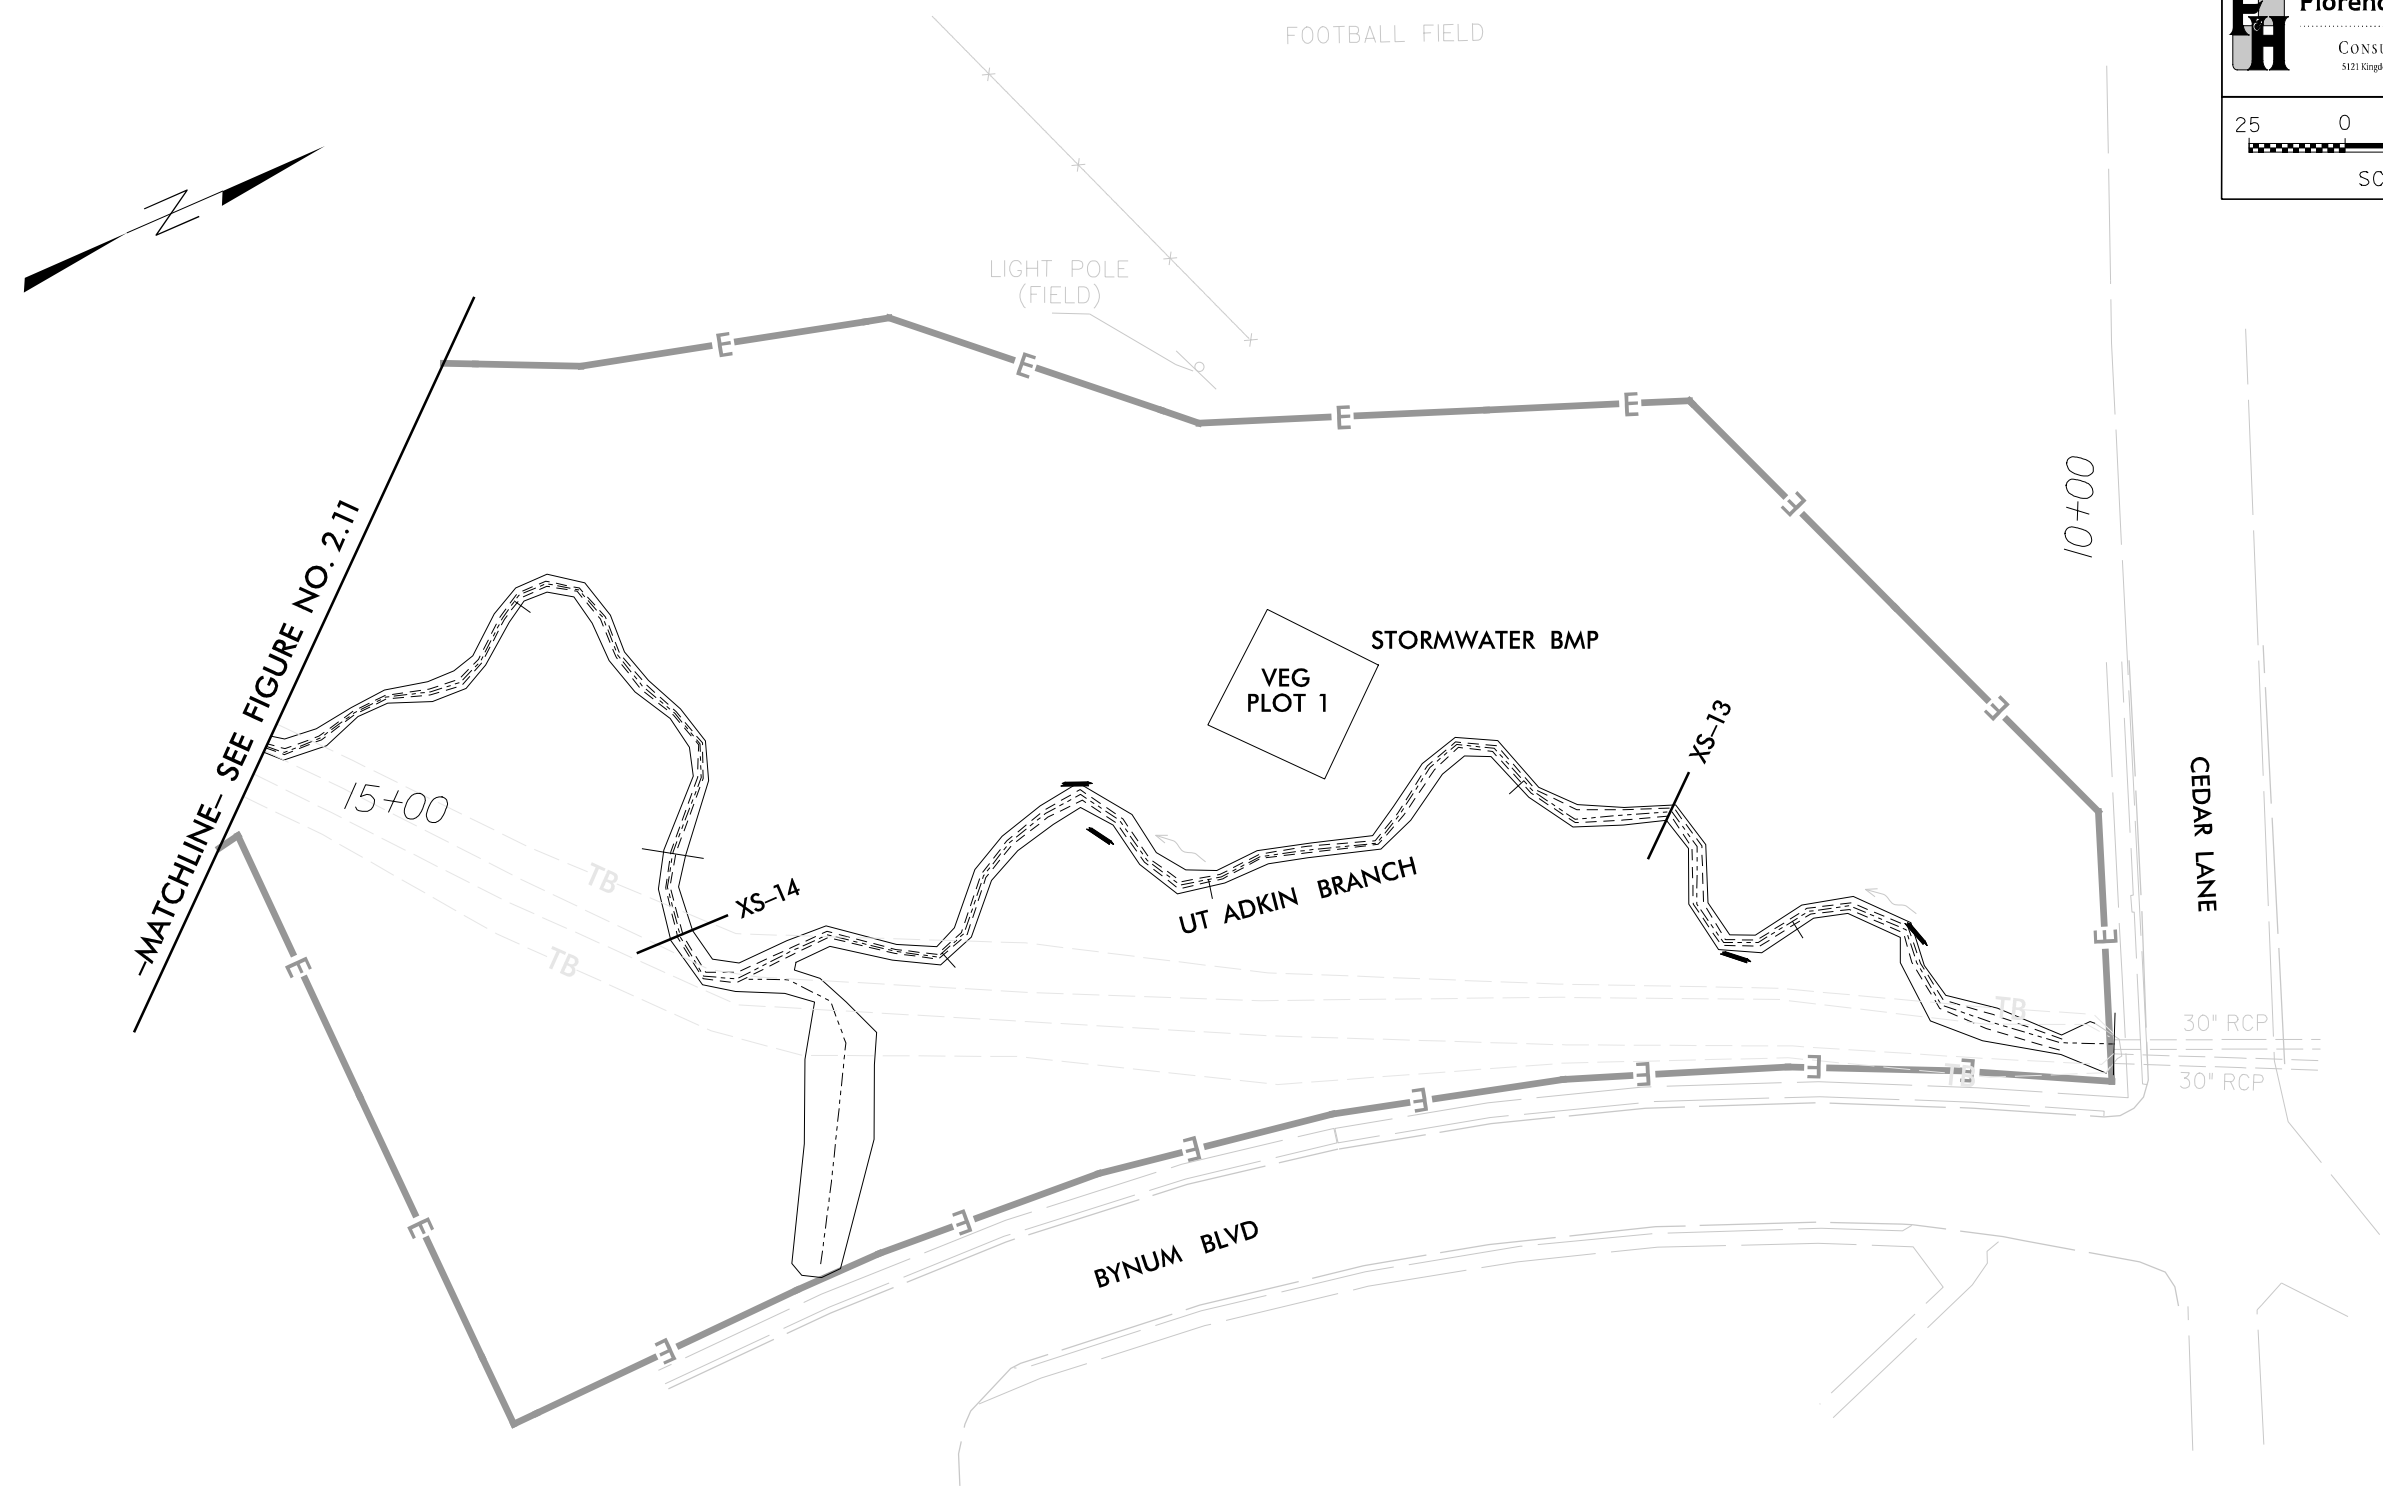

LEGEND	
	THALWEG
	BANKFULL
	TOE OF SLOPE
	CONSERVATION EASEMENT LINE
	LOG SILL
	MONITORING CROSS SECTION (XS-)
	PRE-CONSTRUCTION TOP OF BANK
	PRE-CONSTRUCTION THALWEG

CURRENT CONDITIONS PLAN VIEW (CCPV)	
ADKIN BRANCH (YR2)	
SCOPE: 050656101	COUNTY: LENOIR
DESIGNED BY: RVS	CHECKED BY: RKW
DATE: 11/12	

I:\21\2012\Stream\_Monitoring\Year 2\AdkinBranch\_Monitoring\RI\_psh\_13.dgn  
 Florence & Hutcheson, Inc.



**Table 5.1 Visual Stream Morphology Stability Assessment**  
**Adkin Branch Stream Restoration Project, Phase I, EEP IMS No. 7**  
**Adkin Branch Reach 1 - Washington Ave. to Gordon St. - 1,764 feet assessed**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			2	110	94%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	All	N/A			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient	9	9			100%			
		2. <u>Length</u> appropriate	9	9			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	All	N/A			100%			
2. Thalweg centering at downstream of meander (Glide)		All	N/A			100%				
<b>Totals</b>					0	0	100%	N/A	N/A	N/A
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	N/A	N/A	N/A
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <b>NOT</b> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	N/A	N/A	N/A
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	17	17			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	17	17			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	17	17			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <b>not</b> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	17	17			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio > 1.6 Rootwads/logs providing some cover at base-flow.	18	18			100%			

**Table 5.2 Visual Stream Morphology Stability Assessment**  
**Adkin Branch Stream Restoration Project, Phase I, EEP IMS No. 7**  
**Adkin Branch Reach 2 - Gordon St. to Lincoln St. - 3,131 feet assessed (4,270 ft. total reach length)**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
<b>1. Bed</b>	<b>1. Vertical Stability</b> (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			4	285	91%			
	<b>2. Riffle Condition</b>	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	N/A	N/A			100%			
	<b>3. Meander Pool Condition</b>	1. <u>Depth</u> Sufficient	14	14			100%			
		2. <u>Length</u> appropriate	14	14			100%			
	<b>4. Thalweg Position</b>	1. Thalweg centering at upstream of meander bend (Run)	All	N/A			100%			
2. Thalweg centering at downstream of meander (Glide)		All	N/A			100%				
<b>Totals</b>					28	1420	55%	0%	0%	55%
<b>3. Engineered Structures</b>	<b>1. Overall Integrity</b>	Structures physically intact with no dislodged boulders or logs	29	31			94%			
	<b>2. Grade Control</b>	Grade control structures exhibiting maintenance of grade across the sill.	31	31			100%			
	<b>2a. Piping</b>	Structures lacking any substantial flow underneath sills or arms.	31	31			100%			
	<b>3. Bank Protection</b>	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	25	31			81%			
	<b>4. Habitat</b>	Pool forming structures maintaing ~ Max Pool Depth : Mean Bankfull Depth ratio > 1.6 Rootwads/logs providing some cover at base-flow.	31	31			100%			

**Table 5.3 Visual Stream Morphology Stability Assessment**  
**Adkin Branch Stream Restoration Project, Phase I, EEP IMS No. 7**  
**UT to Adkin Branch: 1,622 feet assessed**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
<b>1. Bed</b>	<b>1. Vertical Stability</b> (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	<b>2. Riffle Condition</b>	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	All	N/A			100%			
	<b>3. Meander Pool Condition</b>	1. <u>Depth</u> Sufficient	26	28			93%			
		2. <u>Length</u> appropriate	26	28			93%			
	<b>4. Thalweg Position</b>	1. Thalweg centering at upstream of meander bend (Run)	All	N/A			100%			
2. Thalweg centering at downstream of meander (Glide)		All	N/A			100%				
<b>2. Bank</b>	<b>1. Scoured/Eroding</b>	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	N/A	N/A	N/A
	<b>2. Undercut</b>	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <b>NOT</b> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	<b>3. Mass Wasting</b>	Bank slumping, calving, or collapse			0	0	100%	N/A	N/A	N/A
<b>Totals</b>					0	0	100%	N/A	N/A	N/A
<b>3. Engineered Structures</b>	<b>1. Overall Integrity</b>	Structures physically intact with no dislodged boulders or logs	16	16			100%			
	<b>2. Grade Control</b>	Grade control structures exhibiting maintenance of grade across the sill.	16	16			100%			
	<b>2a. Piping</b>	Structures lacking any substantial flow underneath sills or arms.	16	16			100%			
	<b>3. Bank Protection</b>	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	16	16			100%			
	<b>4. Habitat</b>	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio > 1.6 Rootwads/logs providing some cover at base-flow.	14	16			88%			

**Table 6** **Vegetation Condition Assessment**

**Adkin Branch Restoration Site (EEP IMS No. 7)**

Planted Acreage<sup>1</sup> **33**

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	A few small areas along stream benches throughout the Site have exposed soils with very little vegetative cover.	0.02	See CCPV legend	1	0.08	0.2%
2. Low Stem Density Areas	Stem densities throughout the Site are low due to death of planted seedlings as the result of extreme dry, hot temperatures over the summers of 2011 and 2012.	None	NA	0	0.00	0.0%
<b>Total</b>				1	0.08	0.2%
3. Areas of Poor Growth Rates or Vigor	Vegetation growth throughout the Site in general is poor.	None	NA	0	0.00	0.0%
<b>Cumulative Total</b>				1	0.08	0.2%

Easement Acreage<sup>2</sup> **40.5**

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern <sup>4</sup>	Several small areas of invasives including Chinese privet, Johnson grass, lespedeza, and Japanese honeysuckle.	0.02	NA	5	2.30	5.7%
5. Easement Encroachment Areas <sup>3</sup>	NA	NA	NA	0	0.00	0.0%


<sup>1</sup> = Enter the planted acreage within the easement. This number is calculated as the easement acreage minus any existing mature tree stands that were not subject to supplemental planting of the understory, the channel acreage, crossings or any other elements not directly planted as part of the project effort.

<sup>2</sup> = The acreage within the easement boundaries.

<sup>3</sup> = Encroachment may occur within or outside of planted areas and will therefore be calculated against the overall easement acreage. In the event a polygon is cataloged into items 1, 2 or 3 in the table and is the result of encroachment, the associated acreage should be tallied in the relevant item (i.e., item 1,2 or 3) as well as a parallel tally in item 5.

<sup>4</sup> = Invasives may occur in or out of planted areas, but still within the easement and will therefore be calculated against the overall easement acreage. Invasives of concern/interest are listed below. The list of high concern species are those with the potential to directly outcompete native, young, woody stems in the short-term (e.g. monitoring period or shortly thereafter) or affect the community structure for existing, more established tree/shrub stands over timeframes that are slightly longer (e.g. 1-2 decades). The low/moderate concern group are those species that generally do not have this capacity over the timeframes discussed and therefore are not expected to be mapped with regularity, but can be mapped, if in the judgement of the observer their coverage, density or distribution is suppressing the viability, density, or growth of planted woody stems. Decisions as to whether remediation will be needed are based on the integration of risk factors by EEP such as species present, their coverage, distribution relative to native biomass, and the practicality of treatment. For example, even modest amounts of Kudzu or Japanese Knotweed early in the projects history will warrant control, but potentially large coverages of Microstegium in the herb layer will not likely trigger control because of the limited capacities to impact tree/shrub layers within the timeframes discussed and the potential impacts of treating extensive amounts of ground cover. Those species with the "watch list" designator in gray shade are of interest as well, but have yet to be observed across the state with any frequency. Those in *red italics* are of particular interest given their extreme risk/threat level for mapping as points where isolated specimens are found, particularly early in a projects monitoring history. However, areas of discrete, dense patches will of course be mapped as polygons. The symbology scheme below was one that was found to be helpful for symbolizing invasives polygons, particularly for situations where the condition for an area is somewhere between isolated specimens and dense, discrete patches. In any case, the point or polygon/area feature can be symbolized to describe things like high or low concern and species can be listed as a map inset, in legend items if the number of species are limited or in the narrative section of the executive summary.

**Figures 3.1-3.20. Vegetation Plot Photos and Problem Areas**

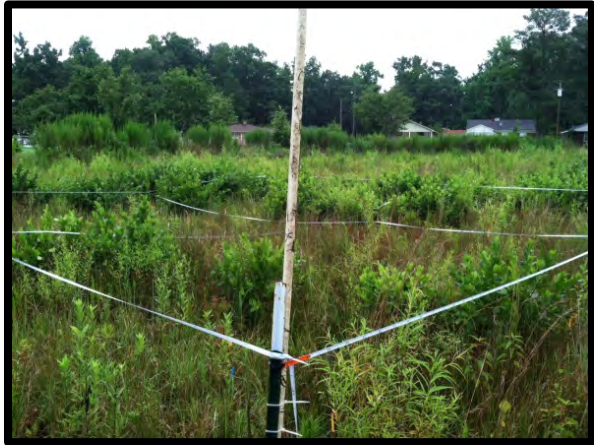

**3.1 Vegetation Plot 1**



**3.2 Vegetation Plot 2**




**3.3 Vegetation Plot 3**



**3.4 Vegetation Plot 4**




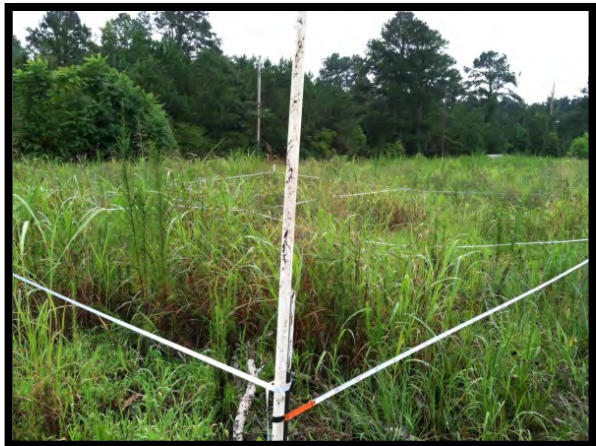


**3.5 Vegetation Plot 5**



**3.6 Vegetation Plot 6**

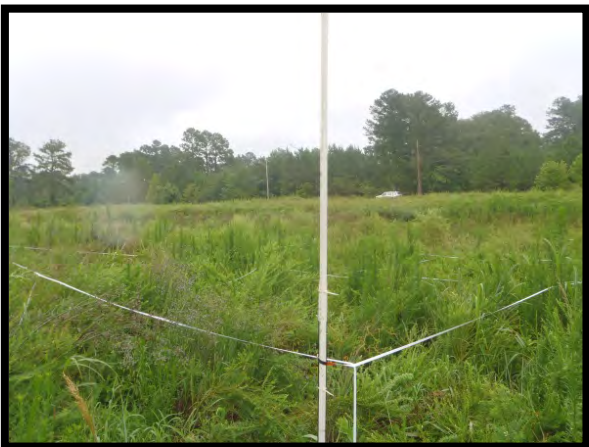

**3.7 Vegetation Plot 7**

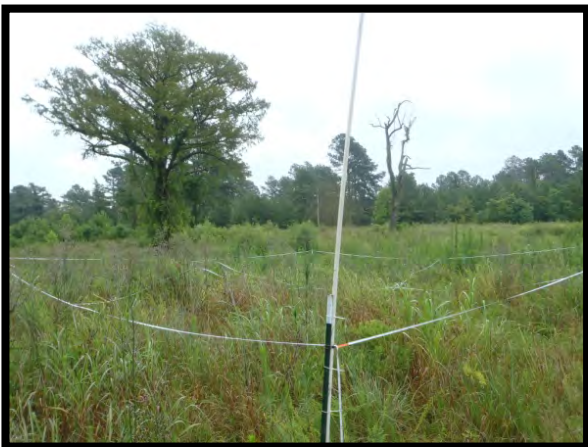

**3.8 Vegetation Plot 8**




**3.9 Vegetation Plot 9**



**3.10 Vegetation Plot 10**



**3.11 Vegetation Plot 11**

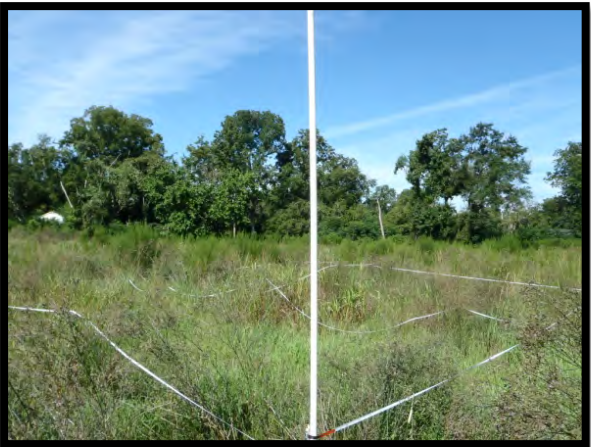

**3.12 Vegetation Plot 12**





**3.13 Vegetation Plot 13**



**3.14 Vegetation Plot 14**




**3.15 Vegetation Plot 15**



**3.16 Vegetation Plot 16**



**3.17 Vegetation Plot 17**

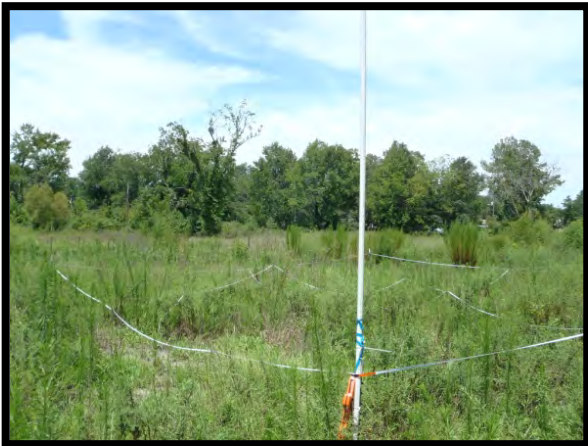

**3.18 Vegetation Plot 18**



**3.19 Vegetation Plot 19**



**3.20 Vegetation Plot 20**





**3.19 Vegetation Plot 21**



**3.20 Vegetation Plot 22**



**3.21 Severe bank erosion near 65+35**



**3.22 Severe erosion downstream of pedestrian bridge (84+30).**



**3.23 Severe erosion upstream of pedestrian bridge (83+50)**



**3.24 Severe erosion near 86+70**



**3.25 Severe erosion near 92+50**



**3.26 Area of thin grass near 95+00**





**3.27 Rip-rap/beaverdam near 69+50**



**3.28 Tree across UT near 19+00**



**3.29 Severe erosion around vane arm  
2011 (87+50)**



**3.30 Severe erosion around vane arm  
2012 (87+50)**



**Appendix C. Vegetation Plot Data**

**Table 7. Vegetation Plot Criteria Attainment**

Vegetation Plot ID	Stream Vegetation Survival Threshold Met?	Buffer Vegetation Survival Threshold Met?	Tract Mean
1	Yes	Yes	Stream Veg. = 64% Buffer Veg. = 64%
2	Yes	Yes	
3	Yes	Yes	
4	Yes	Yes	
5	Yes	Yes	
6	Yes	Yes	
7	No	No	
8	No	No	
9	No*	No*	
10	No*	No*	
11	No*	No*	
12	Yes	Yes	
13	Yes	Yes	
14	No	No	
15	Yes	Yes	
16	No	No	
17	Yes	Yes	
18	No	No	
19	Yes	Yes	
20	Yes	Yes	
21	Yes	Yes	
22	Yes	Yes	

\*Based on planted stems alone, these plots didn't meet success criteria; however, when including naturally recruited stems of appropriate species such as hickory (*Carya* sp.) these plots were above 320 stems per acre.

**Table 8. CVS Vegetation Plot Metadata**

<b>Report Prepared By</b>	Corri Faquin 8/13/2012 16:58
<b>Date Prepared</b>	
<b>database name</b>	Axiom-EEP-2012-A.mdb
<b>database location</b>	C:\Axiom\Business\CVS
<b>computer name</b>	CORRI-PC
<b>file size</b>	53547008
<b>DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----</b>	
<b>Metadata</b>	Description of database file, the report worksheets, and a summary of project(s) and project data.
<b>Proj, planted</b>	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
<b>Proj, total stems</b>	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
<b>Plots</b>	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
<b>Vigor</b>	Frequency distribution of vigor classes for stems for all plots.
<b>Vigor by Spp</b>	Frequency distribution of vigor classes listed by species.
<b>Damage</b>	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
<b>Damage by Spp</b>	Damage values tallied by type for each species.
<b>Damage by Plot</b>	Damage values tallied by type for each plot.
<b>Planted Stems by Plot and Spp</b>	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
<b>ALL Stems by Plot and spp</b>	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
<b>PROJECT SUMMARY-----</b>	
<b>Project Code</b>	7
<b>project Name</b>	Adkin Branch
<b>Description</b>	Stream restoration
<b>River Basin</b>	
<b>length(ft)</b>	
<b>stream-to-edge width (ft)</b>	
<b>area (sq m)</b>	
<b>Required Plots (calculated)</b>	
<b>Sampled Plots</b>	22



Table 9. 2012 (Year 2) Total Planted and Natural Recruits Stems by Plot and Species

Adkin Branch			Current Plot Data (MY2 2012)																																						
			E7-AXE-0001			E7-AXE-0002			E7-AXE-0003			E7-AXE-0004			E7-AXE-0005			E7-AXE-0006			E7-AXE-0007			E7-AXE-0008			E7-AXE-0009			E7-AXE-0010			E7-AXE-0011			E7-AXE-0012			E7-AXE-0013		
Scientific Name	Common Name	Species Type	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T			
Acer rubrum	red maple	Tree																																							
Alnus serrulata	hazel alder	Shrub	14	17	20																																				
Baccharis halimifolia	eastern baccharis	Shrub												1																											
Betula nigra	river birch	Tree	11	11	20	5	5	5	2	2	2	2	2	2	1	1	1				2	2	2	3	3	3	1	1	1	1	1	1	1	4	4	4	7	7	7		
Carpinus caroliniana	American hornbeam	Tree																																							
Carya	hickory	Tree				1	1	34	4	4	8																														
Cephalanthus occidentalis	common buttonbush	Shrub																																							
Cercis canadensis	eastern redbud	Tree				1	1	1							6	6	6																								
Cornus amomum	silky dogwood	Shrub	30	33	33																																				
Crataegus	hawthorn	Tree																																							
Liquidambar styraciflua	sweetgum	Tree						75						9																											
Morus alba	white mulberry	Exotic																																							
Pinus	pine	Tree																																							
Pinus taeda	loblolly pine	Tree			2			5						1																											
Platanus occidentalis	American sycamore	Tree																																							
Populus deltoides	eastern cottonwood	Tree																																							
Prunus serotina	black cherry	Tree																																							
Pyrus	pear	Tree																																							
Quercus	oak	Tree		1	1				1	1	1	2	2	2	3	3	3	1	1	1				1	1	1															
Quercus falcata	southern red oak	Tree				8	8	8	7	7	7	2	2	2	4	4	4	6	6	6	1	1	1	3	3	3	5	5	5	2	2	2	2	2	2	2	3	3	3		
Quercus nigra	water oak	Tree							2	2	2	2	2	2				1	1	1																					
Quercus phellos	willow oak	Tree				1	1	1	2	2	10																														
Quercus rubra	northern red oak	Tree																																							
Robinia pseudoacacia	black locust	Tree																																							
Salix nigra	black willow	Tree	2	11	27																																				
Sassafras albidum	sassafras	Tree																																							
Taxodium distichum	bald cypress	Tree				1	1	1																																	
Ulmus	elm	Tree																																							
Ulmus alata	winged elm	Tree																																							
Unknown		Shrub or Tree										2	2	2																											
	Stem count		57	73	103	17	17	138	18	18	44	10	10	11	14	14	15	8	8	8	4	4	4	7	7	7	7	7	9	4	4	37	7	7	28	11	11	12			
	size (ares)		1			1			1			1			1			1			1			1			1			1			1			1					
	size (ACRES)		0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02					
	Species count		4	5	6	6	6	10	6	6	9	5	5	6	4	4	5	3	3	3	3	3	3	3	3	3	5	3	3	6	3	3	7	3	3	4					
	Stems per ACRE		2307	2954	4168	688	688	5585	728.4	728.4	1781	404.7	404.7	445.2	566.6	566.6	607	323.7	323.7	323.7	161.9	161.9	161.9	283.3	283.3	283.3	283.3	283.3	364.2	161.9	161.9	1497	283.3	283.3	1133						

Color for Density  
 Exceeds requirements by 10%  
 Exceeds requirements, but by less than 10%  
 Fails to meet requirements, by less than 10%  
 Fails to meet requirements by more than 10%

PnoLS = Planted stems excluding livestakes  
 P-all= Planted stems including livestakes  
 T = Planted stems and natural recruits  
 Total includes stems of natural recruits

Table 9. 2012 (Year 2) Total Planted and Natural Recruits Stems by Plot and Species (continued)

Adkin Branch			Annual Means																																			
Scientific Name	Common Name	Species Type	E7-AXE-0015			E7-AXE-0016			E7-AXE-0017			E7-AXE-0018			E7-AXE-0019			E7-AXE-0020			E7-AXE-0021			E7-AXE-0022			MY2 (2012)			MY1 (2011)			MY0 (2011)					
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T			
Acer rubrum	red maple	Tree																																	3			
Alnus serrulata	hazel alder	Shrub																									14	17	20	15	18	18	1	1	1			
Baccharis halimifolia	eastern baccharis	Shrub						1							1						3										6			1				
Betula nigra	river birch	Tree	3	3	3	2	2	2	2	2	2				1	1	1	4	4	4	2	2	2	2	2	2	55	55	64	45	45	45	82	82	82			
Carpinus caroliniana	American hornbeam	Tree													6	6	6	4	4	4							12	12	12	14	14	14	48	48	48			
Carya	hickory	Tree	2	2	2						1	1	5	3	3	3	1	1	1	2	2	2	1	1	2			18	18	101	18	18	52	30	30	30		
Cephalanthus occidentalis	common buttonbush	Shrub																																44	44	44		
Cercis canadensis	eastern redbud	Tree	1	1	1								1	1	1					1	1	1	2	2	2	2	2	2	17	17	17	7	7	7				
Cornus amomum	silky dogwood	Shrub	5	5	5					1	1	1				2	2	2									38	41	41	51	55	55	70	70	70			
Crataegus	hawthorn	Tree																																		1		
Liquidambar styraciflua	sweetgum	Tree																																		92		
Morus alba	white mulberry	Exotic			1																																70	
Pinus	pine	Tree																																			4	
Pinus taeda	loblolly pine	Tree																	1																		10	
Platanus occidentalis	American sycamore	Tree																																			7	
Populus deltoides	eastern cottonwood	Tree																																			5	
Prunus serotina	black cherry	Tree			1																1						1	1	18	2	2	18	8	8	8			
Pyrus	pear	Tree																																			2	
Quercus	oak	Tree										2	2	2			2	2	2								14	15	15	18	19	19	48	48	48			
Quercus falcata	southern red oak	Tree	3	3	3	3	3	3	2	2	2	2	2	2	2	4	4	4	5	5	5	5	5	5	5	76	76	76	63	63	63	135	135	135				
Quercus nigra	water oak	Tree	1	1	1									1	1	1				2	2	2				9	9	9	9	9	9	7	7	7				
Quercus phellos	willow oak	Tree	3	3	3	1	1	1	1	1	1															8	8	16	4	4	36							
Quercus rubra	northern red oak	Tree																								1	1	1	1	1	1							
Robinia pseudoacacia	black locust	Tree																																			4	
Salix nigra	black willow	Tree																								2	11	27	2	11	11	1	22	22				
Sassafras albidum	sassafras	Tree																																			4	
Taxodium distichum	bald cypress	Tree																								1	1	1	1	1	1							
Ulmus	elm	Tree																								2	2	3										
Ulmus alata	winged elm	Tree																																			1	
Unknown		Shrub or Tree																								2	2	2	4	4	4	4	4	4	4	4		13
<b>Stem count</b>			18	18	20	6	6	7	9	9	15	6	6	6	15	15	16	15	15	17	12	12	19	9	9	11	270	286	545	254	271	475	479	500	592			
<b>size (ares)</b>			1			1			1			1			1			1			1					22			22									
<b>size (ACRES)</b>			0.02			0.02			0.02			0.02			0.02			0.02			0.02					0.54			0.54									
<b>Species count</b>			7	7	9	3	3	4	6	6	7	3	3	3	7	7	8	5	5	7	5	5	8	3	3	4	16	16	23	15	15	23	13	13	18			
<b>Stems per ACRE</b>			728.4	728.4	809.4	242.8	242.8	283.3	364.2	364.2	607	242.8	242.8	242.8	607	607	647.5	607	607	688	485.6	485.6	768.9	364.2	364.2	445.2	496.7	526.1	1003	467.2	498.5	873.8	881.1	919.7	1089			

**Color for Density**  
 Exceeds requirements by 10%  
 Exceeds requirements, but by less than 10%  
 Fails to meet requirements, by less than 10%  
 Fails to meet requirements by more than 10%

PnoLS = Planted stems excluding livestockes  
 P-all= Planted stems including livestockes  
 T = Planted stems and natural recruits  
 Total includes stems of natural recruits



January 25, 2012

Mr. Peter Jelenevsky  
 Fluvial Solutions, Inc.  
 P.O. Box 28749  
 Raleigh, NC 27611

Re: Vegetation Warranty Site Assessment Findings  
 Adkin Branch Tropical Storm Repairs  
 SCO # 05-06561-01B

Mr. Jelenevsky:

As stated in the January 25, 2012 letter from Ed Hajnos, a significant portion the Adkin Branch project site did not meet the vegetation warranty criteria as stated in contract documents. As per SCO contract 05-06561-01B, Special Provision Section 6.0, bare roots were to survive at a rate of 80%. Subsequently, Change Order No.1 allowed the addition of eighty-six (86) Ball and Burlap plantings (at Holloway Park) which are also under the 80% survival rate. The warranty period began 4/1/2011 and will expire 4/1/2012.

Planted vegetation at the Adkin Branch site was assessed in September 2011 by the project design firm's subconsultant, Axiom Environmental, Inc. (Axiom). Data collected during the sampling efforts report significantly higher plant mortality than contractually permissible. Warranty replant numbers are based on the data collected. Field methodology and data are described below.

### **September 2011 Vegetation Inspection**

Twenty-two (22) CVS vegetation plots were established, each 1,076 sq ft (10m x 10m). All planted bare roots present within the plot were counted towards the warranty criteria, including those that were top-dead but were re-sprouting at their base. The spatial location of the 22 CVS plots is shown on the attached Vegetation Inspection Map.

The Ball and Burlap trees planted along the tributary at Holloway Park were also inspected while on site for viability.

### **Results**

In Coastal Plain Levee Forest Planting Zones, 680 stems were required to be planted per acre. In order to satisfy the 80% warranty survival rate, 544 stems per acre are required to survive the warranty period, which is equivalent to 12 living stems per inspection plot.

*Restoring... Enhancing... Protecting Our State*

North Carolina Ecosystem Enhancement Program, 1652 Mail Service Center, Raleigh, NC 27699-1652 / 919-715-0476 / [www.nceep.net](http://www.nceep.net)





Of the 22 inspection plots, 15 did not meet the 80% survival warranty. A total of twenty-eight (28) of the 86 Ball and Burlap trees have died or appear to be in poor health.

### Coastal Plain Levee Forest Planting Zone - CVS Inspection plot results

Plot	Living bare roots and shrubs	Required stems per plot	Warranty met	Supplemental planting density/acre needed to meet warranty
1	70	12	Yes	None
2	12	12	Yes	None
3	18	12	Yes	None
4	15	12	Yes	None
5	15	12	Yes	None
6	9	12	No	131
7	4	12	No	348
8	4	12	No	348
9	1	12	No	479
10	6	12	No	261
11	4	12	No	348
12	5	12	No	305
13	11	12	No	44
14	1	12	No	479
15	20	12	Yes	None
16	3	12	No	392
17	8	12	No	174
18	7	12	No	218
19	11	12	No	44
20	11	12	No	44
21	12	12	Yes	None
22	7	12	No	218

### Coastal Plain Levee Forest Planting Zone – Warranty Inspection plot results

Twenty (20) warranty inspection plots (non-CVS vegetation data) were established by Axiom, each 1,612 sq feet (25m x 6m). All planted bare roots present within the plot were counted towards the warranty criteria, including those that were top-dead but were re-sprouting at their base. Given 680 stems were planted per acre, 544 per acre were required to survive 1 year, or 20 per plot to meet the 80% warranty. None of the 20 sample plots met the survival criteria (Vegetation Inspection Map attached).

Plot	Living bare roots and shrubs	Required stems per plot	Warranty met	Supplemental planting density/acre needed to meet warranty
1	4	20	No	432
2	9	20	No	297
3	3	20	No	459
4	4	20	No	432
5	14	20	No	162
6	1	20	No	513
7	7	20	No	351
8	2	20	No	486
9	4	20	No	432
10	5	20	No	405
11	7	20	No	351
12	5	20	No	405
13	10	20	No	270
14	9	20	No	297
15	10	20	No	270
16	11	20	No	243
17	10	20	No	270
18	5	20	No	405
19	10	20	No	270
20	4	20	No	432

### Supplemental Planting

The table below shows the number of stems needed to be planted in 4 areas. These areas are also depicted on the Supplemental Planting Map (attached). The planting zone for each is Coastal Plain Levee Forest (CPLF). The number of stems needed in each area was calculated by multiplying the average number of stems needed to meet warranty per plot by the acreage of the given area. Areas 1-4 were sectioned off due to similar plant deficiencies or a topographic break and are shown on the attached Supplemental Planting Map. A total of 11 Ball and Burlap trees also need to be replanted to meet the warranty.

*Restoring... Enhancing... Protecting Our State*





### Bare Root – Supplemental Planting

Area	Station (Looking Downstream)	Planting Zone	Average stems/ac needed	Acres	Total plants needed	Approximate stem spacing
Area 1	Washington St. to East Gordon Street	CPLF	226	6.21	1403	13 ft
Area 2	East Gordon St to STA 65+20	CPLF	333	4.97	1655	11 ft
Area 3	STA 67+65 to STA 81+20	CPLF	338	6.30	2129	11 ft
Area 4	STA 81+20 to Lincoln St.	CPLF	344	8.52	2931	11 ft
				<b>26</b>	<b>8,118</b>	

### Instructions

- The Supplemental Planting effort needs to be coordinated with EEP so we can arrange to be on site.
- All replant materials must conform to the original project specification (dormant season planting, species composition, size, vigor, etc.).
- The Supplemental Planting effort must take place in the dormant season for Lenoir County; November 15th – March 15th
- ATVs and trucks will be permitted to be used during the replant; however, vehicles are to be driven in upland areas only where no bare roots, shrubs or Ball and Burlap trees were planted.
- Dead trees need to be removed from the site.

Although the warranty for this project doesn't expire until April 1, 2012, EEP does not intend to reassess this site for additional warranty compliance. Plants installed during the warranty replant will not themselves have a warranty placed on them. Once Fluvial Solutions, Inc. complies with this replanting, an Article 27 Satisfaction Letter will be awarded.

As stated in Ed Hajnos's January 25, 2012 letter, please call me at your earliest convenience with questions regarding the supplemental planting at Adkin Branch. My contact information can be found below.

Thank you,

*Kristie F. Corson*

Kristie Corson


NC Department of Environment and Natural Resources  
Ecosystem Enhancement Program  
Eastern Project Manager  
Raleigh, NC  
Office (919) 715-1954  
Cell (919) 218-1373  
Kristie.Corson@ncdenr.gov

cc: Bobbi D. Pendleton, Attorney In Fact, Western Surety Company  
Clyde Carl, SCO Project Monitor  
Jeff Jurek, EEP  
Jeff Schaffer, EEP  
Ed Hajnos, EEP  
Lin Xu, EEP Review Coordinator





# Adkin Branch Vegetation Inspection Map

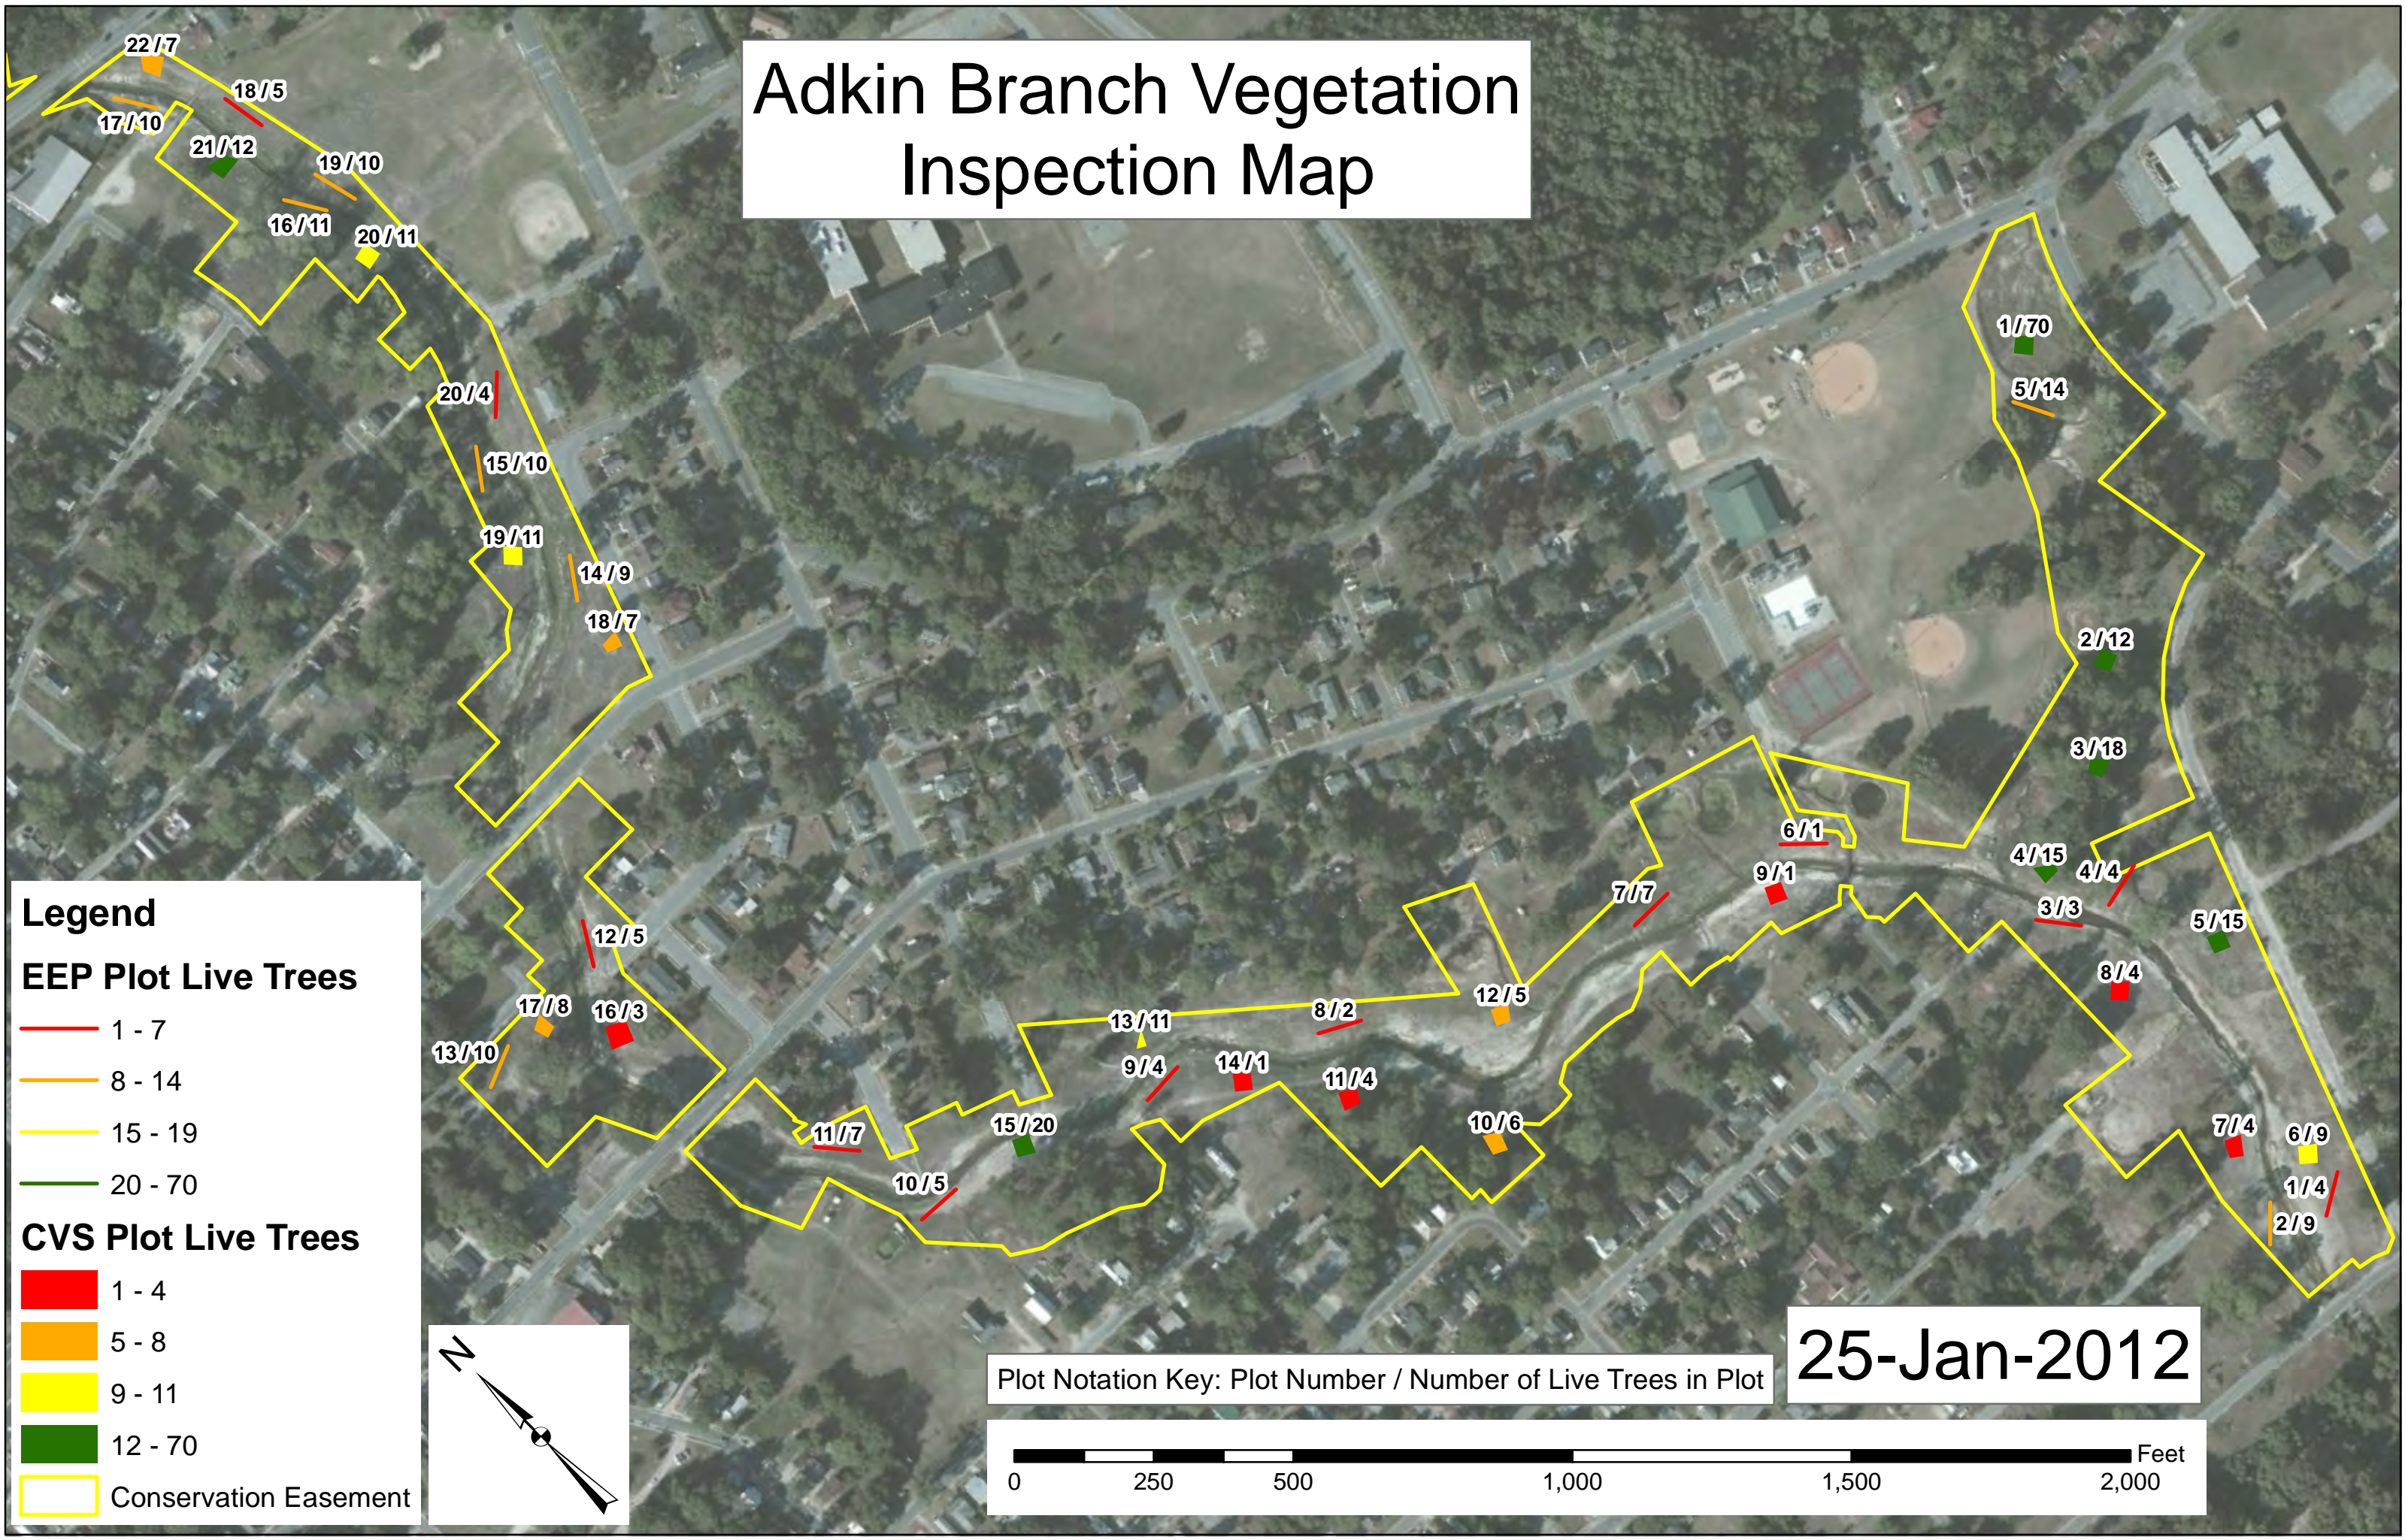

**Legend**


**EEP Plot Live Trees**

- 1 - 7
- 8 - 14
- 15 - 19
- 20 - 70

**CVS Plot Live Trees**

- 1 - 4
- 5 - 8
- 9 - 11
- 12 - 70

Conservation Easement

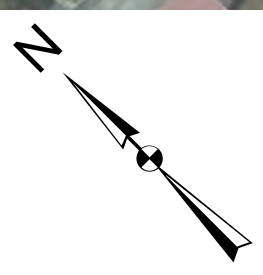

Plot Notation Key: Plot Number / Number of Live Trees in Plot

25-Jan-2012









# Adkin Branch Bare Root Supplemental Planting Map

Area 1  
1403  
stems

Area 2  
1655  
stems

Area 3  
2129  
stems

Area 4  
2931  
stems

**Legend**

**EEP Plot Live Trees**



- 1 - 7
- 8 - 14
- 15 - 19
- 20 - 70

**CVS Plot Live Trees**

- 1 - 4
- 5 - 8
- 9 - 11
- 12 - 70

**Planting Areas**

- Area 1
- Area 2
- Area 3
- Area 4
- Conservation Easement

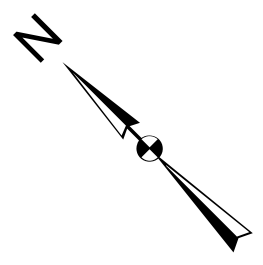

25-Jan-2012







**Table C1. Bare Root Species Replanted at Adkin Branch (March 8, 2012)**

<b>Common Name</b>	<b>Scientific Name</b>	<b>Number Planted</b>
Black cherry	<i>Prunus serotina</i>	1,000
Ironwood	<i>Carpinus caroliniana</i>	1,000
Mockernut hickory	<i>Carya tomentosa</i>	1,000
Riverbirch	<i>Betula nigra</i>	1,118
Slippery elm	<i>Ulmus rubra</i>	1,000
Southern red oak	<i>Quercus falcata</i>	1,000
Water oak	<i>Quercus nigra</i>	1,000
Winged elm	<i>Ulmus alata</i>	1,000

**Table C2. Ball and Burlap Species Replanted at Adkin Branch (March 8, 2012)**

<b>Common Name</b>	<b>Scientific Name</b>	<b>Number Planted</b>
Green ash	<i>Fraxinus pennsylvanica</i>	3
Riverbirch	<i>Betula nigra</i>	3
Sycamore	<i>Platanus occidentalis</i>	3
Willow oak	<i>Quercus phellos</i>	2




## Appendix D. Stream Survey Data

**Figures 4.1-4.17. Cross Section Plots and Photos**

### Adkin Branch, 05065611, Reach 1


XS-1 Riffle, Sta. 37+42

Baseline		MY1		MY2	
Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
0.00	36.38	0.00	36.37	0.00	36.37
9.86	34.88	7.34	35.19	4.36	35.78
16.62	33.21	11.50	34.38	10.66	34.59
24.51	32.12	16.09	33.34	15.70	33.40
25.95	32.31	22.92	32.75	19.48	33.14
27.26	31.91	28.30	32.23	23.80	32.55
29.31	31.89	30.00	32.00	29.16	32.23
31.49	31.34	32.35	31.56	32.15	31.62
33.99	31.05	33.78	31.27	33.84	31.32
35.11	30.06	35.08	30.30	34.52	30.99
36.12	28.42	36.45	27.99	35.08	30.04
36.41	28.32	37.87	27.71	35.05	27.96
37.29	27.83	40.95	27.74	37.28	27.61
38.32	27.76	42.41	27.91	39.61	27.76
41.02	27.67	43.87	27.90	41.91	27.58
42.56	27.78	46.09	29.85	42.76	27.78
43.94	28.17	46.85	29.93	44.16	27.82
44.35	29.19	47.15	30.18	45.12	27.64
45.81	29.62	48.83	30.49	45.93	28.04
47.84	30.09	51.70	31.01	46.14	29.29
49.03	30.44	54.46	31.52	47.49	30.28
51.68	30.46	55.03	31.46	48.32	31.01
54.61	31.10	56.16	31.09	51.93	31.18
61.87	31.23	59.51	31.32	54.76	31.64
65.51	31.78	64.40	32.12	57.30	31.37
76.01	33.81	69.56	32.78	61.23	31.71
88.18	35.44	76.64	34.02	66.79	32.31
		83.37	34.75	73.26	33.41
		88.23	35.45	81.76	34.51
				88.35	35.43

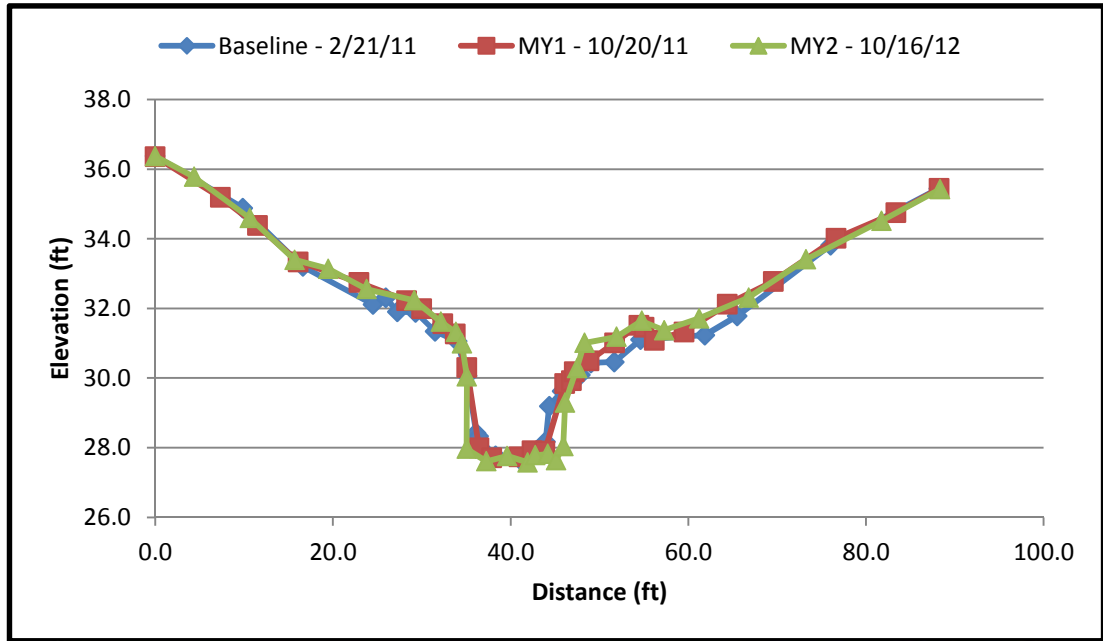

### Adkin Branch, 05065611, Reach 1


	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
XS-2 Pool, Sta. 38+94	0.00	34.25	0.00	34.25	0.00	34.23
	8.48	33.22	7.85	33.40	6.14	33.64
	17.26	32.07	15.07	32.32	12.34	32.87
	23.59	31.03	21.85	31.54	17.29	32.27
	24.98	30.53	25.29	30.76	23.27	31.37
	28.19	30.53	27.97	30.78	27.98	30.84
	29.98	30.03	30.68	30.60	30.81	30.24
	32.23	29.44	31.72	29.57	31.65	29.91
	33.36	27.87	33.17	28.37	33.30	29.80
	35.19	27.83	34.15	27.78	34.23	27.42
	37.22	27.51	37.13	27.55	38.14	26.71
	40.78	27.20	41.68	27.30	39.77	26.48
	43.31	27.42	46.75	27.74	42.39	26.41
	45.59	27.62	48.16	29.58	42.48	26.63
	46.73	27.99	49.13	30.60	42.70	26.10
	47.22	28.30	50.42	31.25	46.16	26.66
	48.68	30.06	54.76	31.31	47.93	27.15
	49.68	30.87	60.32	32.07	47.96	30.32
	52.71	31.19	69.40	32.89	50.90	31.43
	54.58	31.01	75.04	33.37	55.87	31.39
	59.11	31.81			60.73	32.12
66.89	32.70			65.44	32.61	
75.41	33.42			71.35	33.03	
				75.65	33.41	

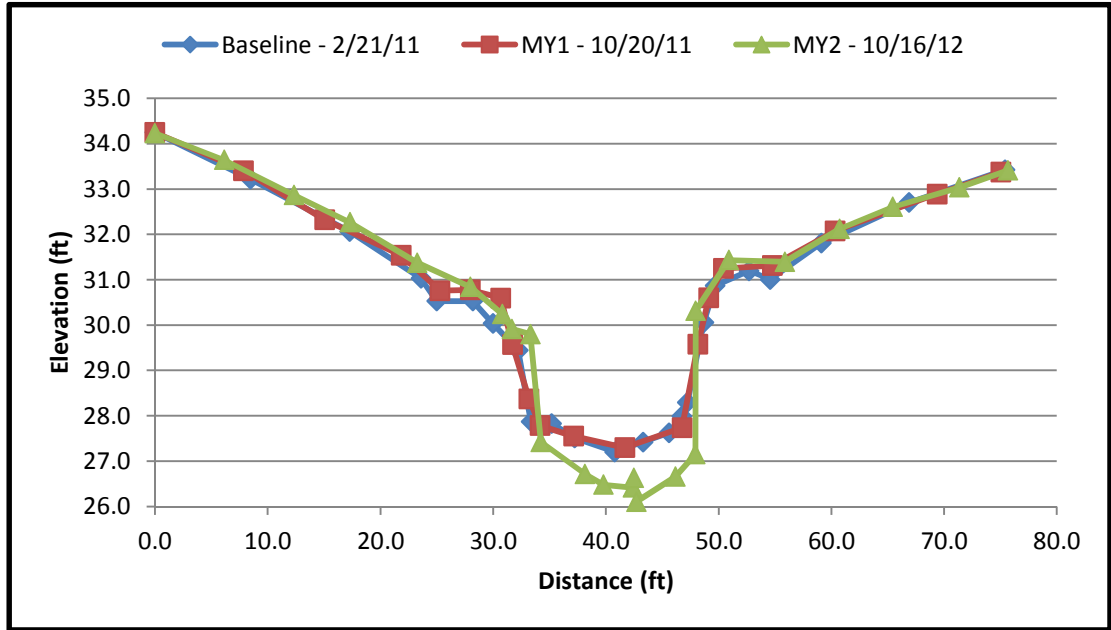



# Adkin Branch, 05065611, Reach 1


XS-3 Riffle, Sta. 44+67	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	34.68	0.00	34.65	0.00	34.67
	5.04	33.96	9.47	33.04	2.59	34.50
	13.96	32.14	17.77	31.45	9.13	33.23
	22.51	30.31	23.88	30.25	16.91	31.54
	27.04	29.77	28.88	29.69	22.05	30.66
	31.37	28.98	32.78	28.80	26.70	30.15
	32.48	28.31	34.56	28.24	29.50	30.15
	33.27	28.11	35.32	27.29	31.29	29.69
	34.34	27.84	38.06	26.72	35.26	28.94
	35.11	27.51	41.20	26.81	35.81	27.59
	36.05	27.31	42.66	27.07	36.77	27.06
	37.20	26.90	44.87	27.40	38.35	26.75
	40.71	26.93	46.91	28.74	40.72	26.90
	43.22	26.96	49.53	29.48	43.31	26.97
	44.45	27.35	53.45	29.45	45.18	27.19
	46.78	27.91	56.69	30.43	45.98	28.40
	49.43	28.97	62.83	31.49	49.44	29.49
	51.83	29.32	67.46	32.44	51.30	29.49
	52.60	29.12	71.00	33.27	54.31	29.83
	57.19	30.42			57.50	30.50
	64.81	31.73			61.07	31.28
	71.17	33.27			65.47	31.99
					67.99	32.52
					69.31	32.83
					71.61	33.28

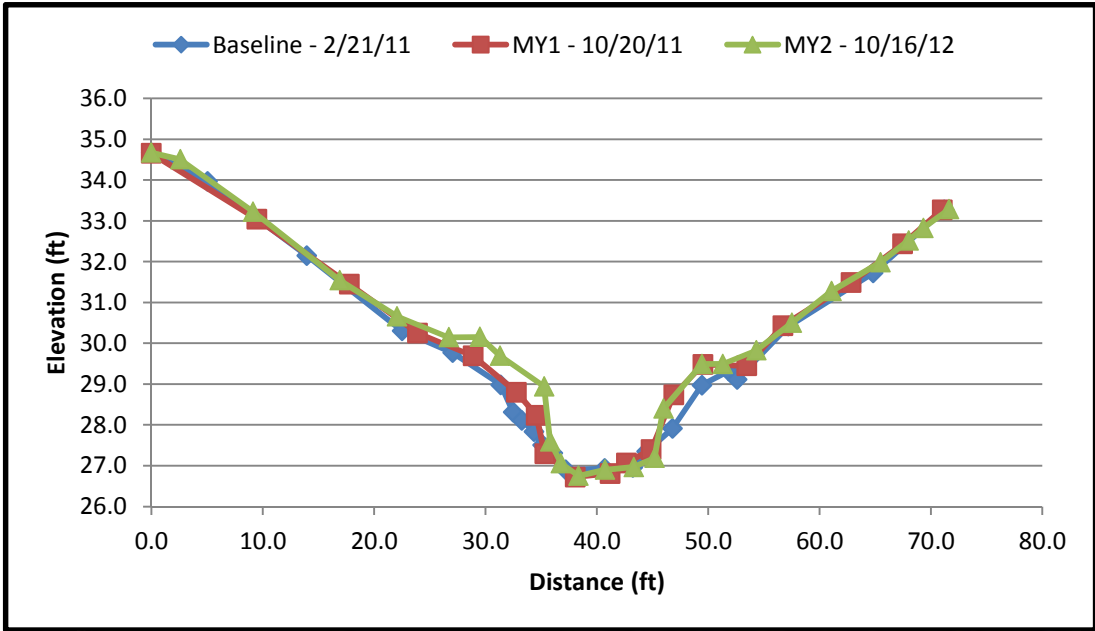



### Adkin Branch, 05065611, Reach 1

XS-4 Pool, Sta. 46+81	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	33.26	0.00	33.25	0.00	33.27
	6.80	31.49	4.64	32.15	4.11	32.34
	9.47	31.14	10.74	31.01	7.10	31.51
	21.52	28.84	16.16	29.97	12.04	30.95
	24.22	28.46	20.27	29.21	16.69	29.92
	25.32	27.87	23.29	29.03	20.99	29.35
	26.50	27.73	25.51	28.82	24.36	29.38
	27.87	27.05	25.89	28.32	26.13	28.86
	29.15	26.40	26.84	27.40	26.79	26.64
	31.16	26.69	28.01	26.90	29.16	25.81
	35.70	26.65	29.61	27.03	31.36	25.62
	38.06	26.48	32.56	26.47	33.76	25.58
	39.91	27.10	34.68	26.88	34.58	25.63
	40.99	27.77	36.07	26.81	35.81	25.57
	41.64	28.45	38.75	26.99	38.50	26.12
	45.49	29.36	40.21	27.14	39.36	26.80
	49.30	30.12	41.73	28.64	39.70	28.38
	59.69	31.31	43.87	29.13	40.96	29.18
	71.76	32.43	45.81	29.32	44.20	29.46
			46.83	29.84	46.45	29.94
			53.19	30.66	49.79	30.39
			59.66	31.43	54.67	30.83
			66.17	32.13	61.07	31.57
			71.22	32.40	67.43	32.26
					71.92	32.39

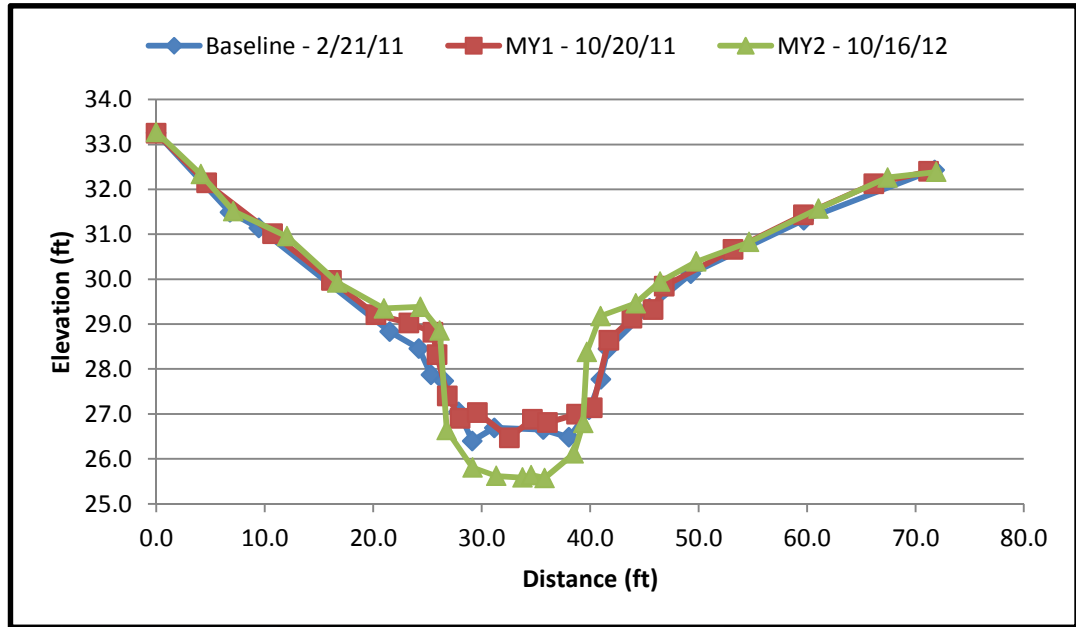


16Oct2012

### Adkin Branch, 05065611, Reach 1

XS-5 Riffle, Sta. 51+47

Baseline		MY1		MY2	
Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
0.00	31.97	0.00	31.94	0.00	31.95
9.93	30.85	10.41	30.71	7.99	30.98
19.77	29.78	20.29	29.67	13.92	30.51
25.24	28.98	26.27	28.51	19.27	29.87
28.26	28.18	30.50	27.53	23.25	29.33
29.51	27.58	32.79	27.20	24.24	29.07
30.76	27.26	33.94	26.70	25.25	28.50
32.09	26.91	34.66	25.68	26.82	28.23
33.29	26.29	35.74	25.16	28.34	27.74
34.40	25.91	38.34	25.69	31.18	27.71
35.72	25.88	39.54	26.90	32.01	27.42
36.05	26.21	41.60	26.25	34.67	25.71
37.13	26.13	42.45	26.47	36.25	25.69
37.42	25.81	43.86	26.86	37.08	25.19
38.94	25.78	45.98	27.71	37.86	25.47
39.65	25.96	50.73	28.33	39.84	25.58
41.28	26.38	56.05	29.10	40.90	25.43
43.58	26.75	68.09	30.73	41.13	25.69
45.04	26.82	76.66	31.44	42.55	26.43
45.66	27.28			43.22	27.17
47.79	27.86			45.69	27.34
53.02	28.51			47.32	28.15
62.00	30.27			52.26	28.37
77.07	31.48			56.82	29.38
				67.74	30.71
				77.13	31.42

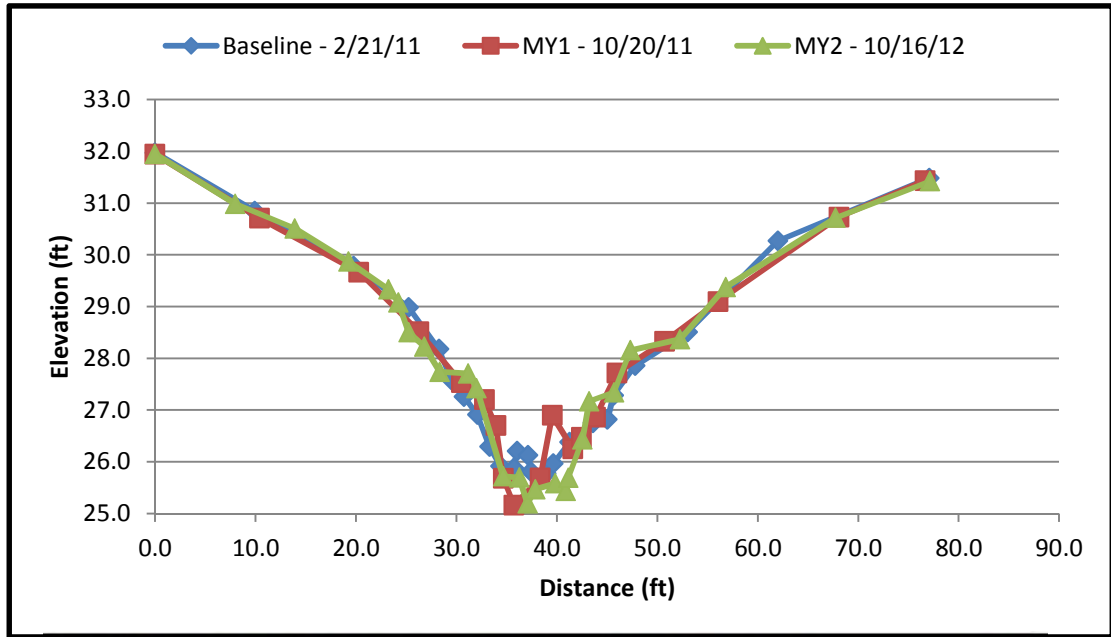




## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	28.96	0.00	28.97	0.00	28.89
	7.02	28.18	6.82	28.17	6.19	28.11
	11.82	27.13	8.32	27.81	10.58	27.3
	13.15	26.66	10.62	27.39	13.33	26.93
	17.98	26.08	12.11	27.21	14.82	26.55
	18.99	26.23	14.48	26.61	16.62	26.44
	20.64	26.63	17.51	26.27	17.76	25.6
	23.57	26.31	18.95	26.5	18.76	25.08
	24.13	25.60	20.94	26.6	20.49	23.92
	24.68	25.28	22.30	25.41	21.56	23.24
	24.68	23.77	23.66	23.77	23.30	20.8
	27.84	22.22	24.43	22.89	27.43	20.3
	30.39	21.92	25.79	22.12	29.26	20.55
	31.86	22.19	27.26	21.75	32.69	20.88
	33.54	22.48	28.97	21.87	35.59	21.4
	35.54	23.06	30.95	22.19	36.97	25.69
	35.50	24.22	32.79	22.9	38.62	26.78
	36.01	25.11	35.54	23.17	40.38	27.27
	37.14	25.43	36.52	25.33	43.12	27.67
	37.75	25.99	37.51	25.72	44.92	28.1
	41.07	27.13	39.90	27.15	50.22	28.02
	43.93	27.64	44.55	27.92	56.48	28.87
	46.39	28.20	47.08	27.69		
	46.83	27.64	53.27	28.35		
	53.08	28.32	57.49	28.84		
	57.39	28.93				


XS-6 Pool, Sta. 64+81

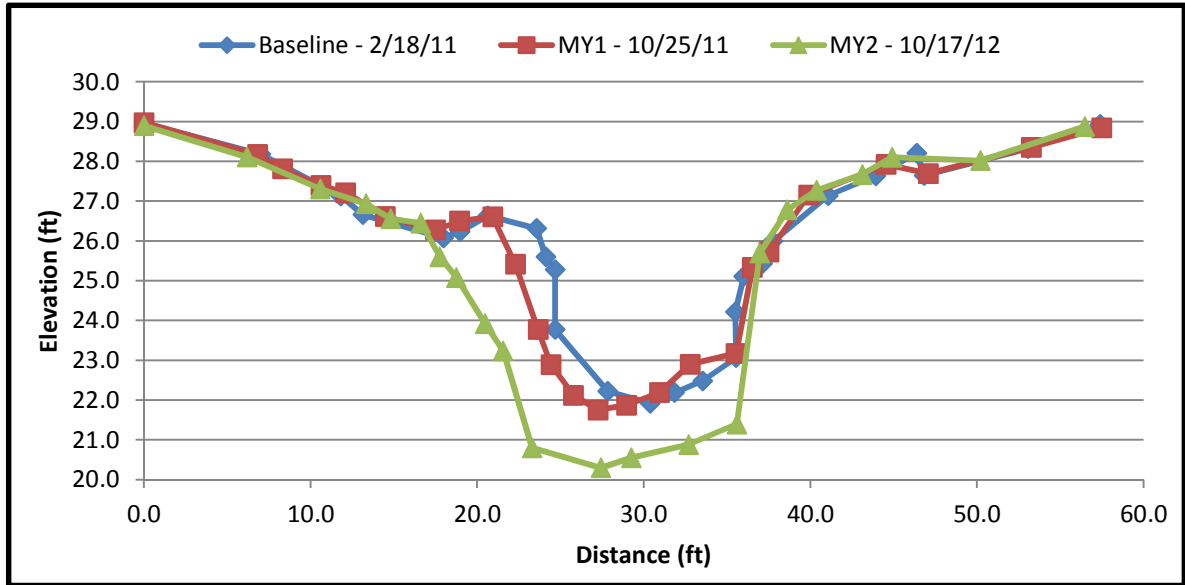

## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	28.97	0.00	28.94	0.00	28.84
	10.03	27.78	5.37	28.42	6.08	28.29
	19.73	26.44	12.29	27.57	9.86	27.71
	23.60	26.43	14.97	27.11	14.30	27.38
	25.40	24.69	19.28	26.39	16.24	27.08
	27.14	23.81	23.36	26.20	18.59	26.61
	28.16	22.91	24.78	25.12	22.54	26.07
	31.71	22.99	26.93	23.31	23.49	25.85
	35.41	22.94	27.76	22.57	24.92	24.85
	37.91	23.17	29.58	21.63	25.76	24.11
	38.15	23.50	32.22	21.34	26.57	22.74
	38.72	24.10	34.49	21.00	28.70	22.27
	39.07	24.73	35.67	21.14	30.00	22.29
	40.37	25.16	36.86	21.85	33.07	22.69
	42.38	25.59	37.72	23.15	35.58	22.67
	43.48	25.59	39.28	23.28	39.40	22.21
	44.04	25.73	40.25	24.11	40.75	23.22
	44.71	25.88	40.75	25.26	42.31	23.90
	45.38	26.12	44.21	25.94	44.32	26.08
	47.07	26.24	45.80	26.40	49.59	26.69
	49.69	26.73	51.40	26.82	57.67	27.47
	51.10	26.64	56.41	27.29	64.27	28.28
	52.80	27.04	61.50	28.09		
	56.19	27.27	64.23	28.34		
	64.14	28.37				

XS-7 Riffle, Sta. 70+00

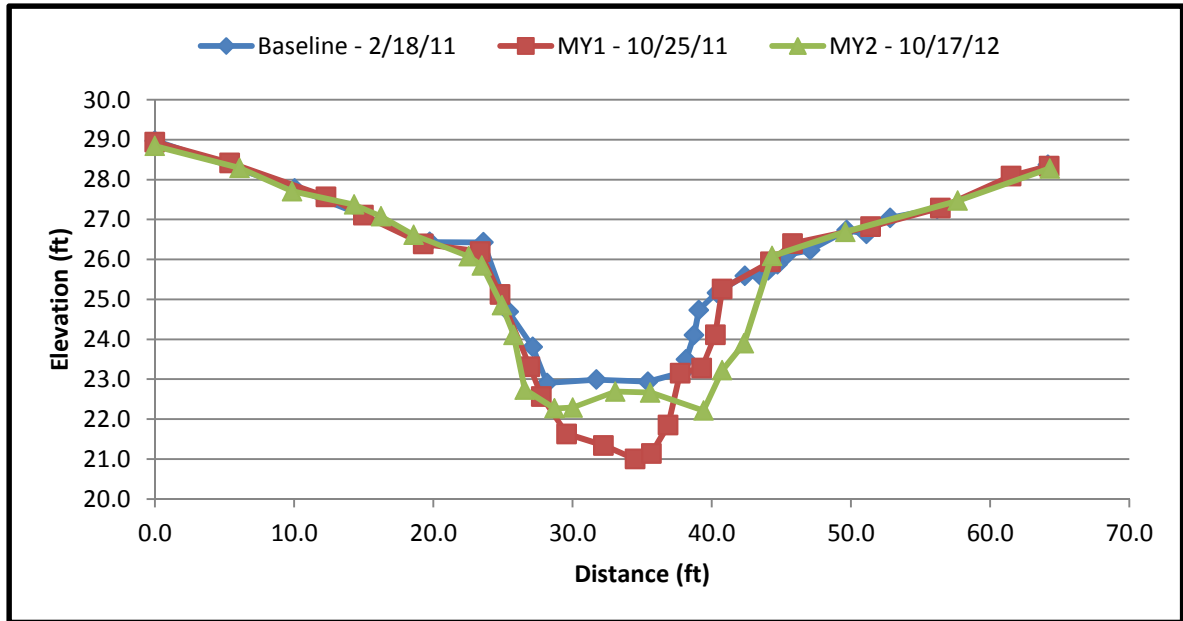




### Adkin Branch, 05065611, Reach 2

XS-8 Pool, Sta. 74+30


Baseline		MY1		MY2	
Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
0.00	26.81	0.00	26.71	0.00	26.74
3.48	26.81	5.61	26.62	5.91	26.53
5.42	26.72	8.41	26.01	9.04	25.70
7.59	26.33	11.70	25.23	12.72	25.02
10.42	25.65	13.96	24.83	15.54	24.69
13.75	24.87	15.46	24.90	17.44	24.08
15.67	24.76	16.73	24.35	18.52	23.52
16.46	24.22	17.51	24.04	19.24	19.54
17.26	24.03	18.78	23.26	21.28	19.35
17.55	23.77	19.50	21.10	24.89	19.55
18.71	23.53	21.17	20.96	26.79	20.17
19.12	22.31	23.49	20.22	29.35	21.50
20.33	21.48	25.14	19.92	30.53	22.22
21.79	21.04	26.70	20.33	31.33	24.37
23.56	21.08	28.88	23.07	32.63	25.04
25.70	21.38	29.83	24.31	33.97	25.06
26.90	21.83	31.43	24.81	35.16	24.66
27.19	22.03	34.36	24.75	42.05	24.69
27.84	22.62	35.54	24.29	46.23	25.88
28.51	23.54	40.92	24.51	50.41	25.89
29.74	24.08	42.66	24.75		
31.02	24.29	44.89	25.74		
32.55	24.55	47.75	25.93		
34.42	24.39	50.57	26.10		
36.00	24.05				
39.62	24.20				
41.26	24.48				
42.56	24.69				
44.07	25.09				
45.16	25.92				
47.95	26.05				
50.57	26.19				

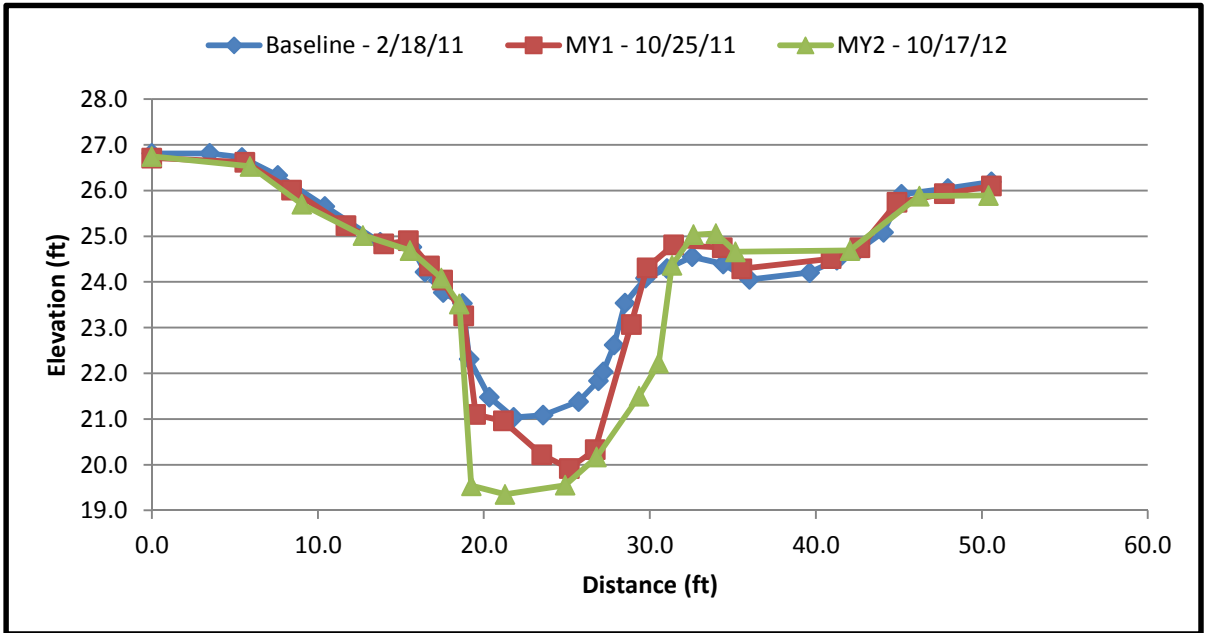

## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	25.93	0.00	25.85	0.00	25.85
	7.66	25.57	9.82	25.57	10.20	25.63
	17.12	25.22	18.42	25.31	13.67	25.53
	19.27	24.81	21.37	25.10	15.45	25.84
	21.25	24.71	23.69	23.98	18.37	25.91
	22.90	23.68	24.36	22.91	19.00	25.67
	24.09	22.76	24.84	22.08	21.73	24.03
	25.35	22.18	25.48	21.43	23.26	22.43
	26.15	21.99	27.92	21.72	26.86	22.07
	28.07	22.10	30.41	21.44	31.47	21.37
	30.42	22.06	32.18	21.30	33.42	21.36
	32.76	22.03	33.76	21.47	35.76	21.41
	34.84	22.18	34.93	21.83	36.25	22.03
	35.40	22.48	36.29	22.99	39.00	24.43
	36.25	22.93	39.05	24.14	43.19	25.12
	37.35	23.46	41.47	24.68	49.01	26.12
	37.90	23.96	46.43	25.70	53.24	26.45
	38.87	24.20	50.70	26.30	56.68	26.48
	40.34	24.53	56.70	26.47		
	44.53	25.45				
	47.94	26.17				
	53.57	26.57				
	56.49	26.59				


XS-9 Rifle, Sta. 75+78

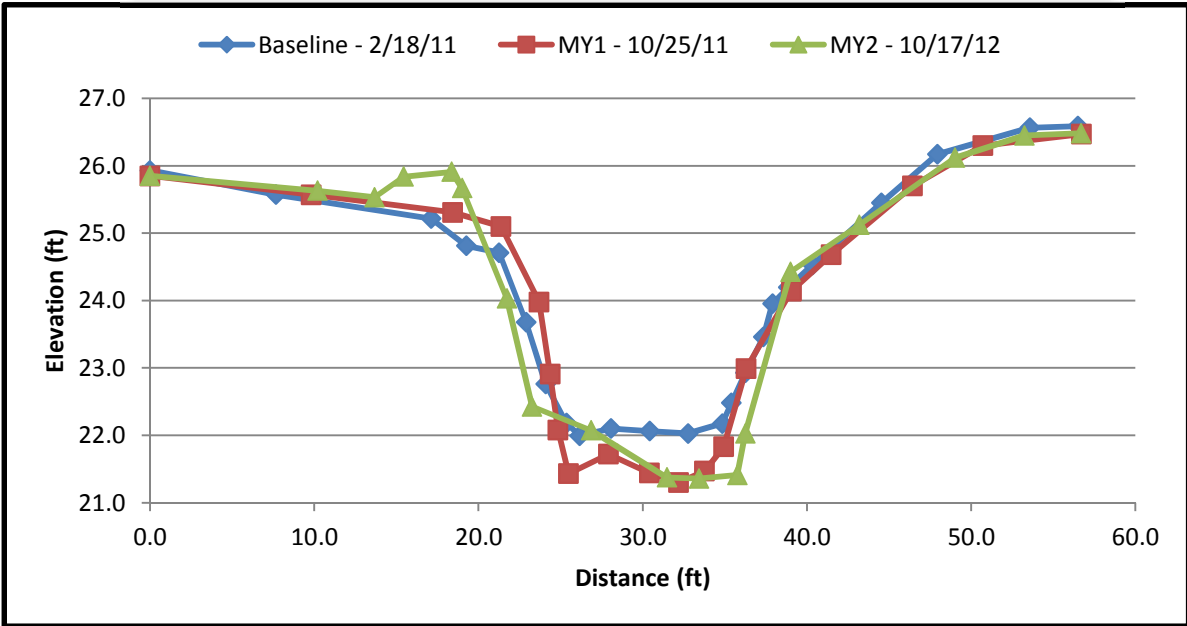

17Oct2012

## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
XS-10 Rifle, Sta. 79+82	0.00	27.66	0.00	27.60	0.00	27.62
	4.16	27.29	5.62	27.04	4.93	27.14
	9.94	26.38	10.79	26.16	9.84	26.30
	13.82	25.77	15.97	25.05	13.95	25.75
	14.67	25.38	18.44	24.69	15.40	25.03
	16.45	25.02	22.19	24.05	20.49	24.57
	18.00	24.75	24.47	23.63	23.69	24.35
	19.93	24.67	26.19	23.10	25.76	23.52
	22.47	23.84	27.45	22.55	27.28	22.91
	23.45	23.72	29.13	22.55	28.04	21.03
	24.08	23.35	30.09	21.94	29.83	20.67
	25.81	23.30	30.88	21.49	33.12	20.55
	27.52	22.08	32.29	21.17	35.97	20.77
	29.35	21.92	33.79	21.02	38.56	20.96
	31.31	21.71	36.21	20.79	40.06	21.23
	32.90	21.51	38.21	20.82	41.80	23.63
	36.04	21.37	39.77	21.19	43.92	23.78
	36.87	21.00	40.99	22.64	46.43	24.23
	38.52	21.10	42.97	23.39	54.27	24.62
	39.08	21.33	45.15	24.00	59.85	24.60
	39.74	21.90	48.55	24.39	62.98	24.60
	42.09	23.26	57.04	24.64		
	43.46	23.61	63.22	24.61		
	45.42	24.02				
	48.91	24.55				
	57.40	24.68				
	62.89	24.70				

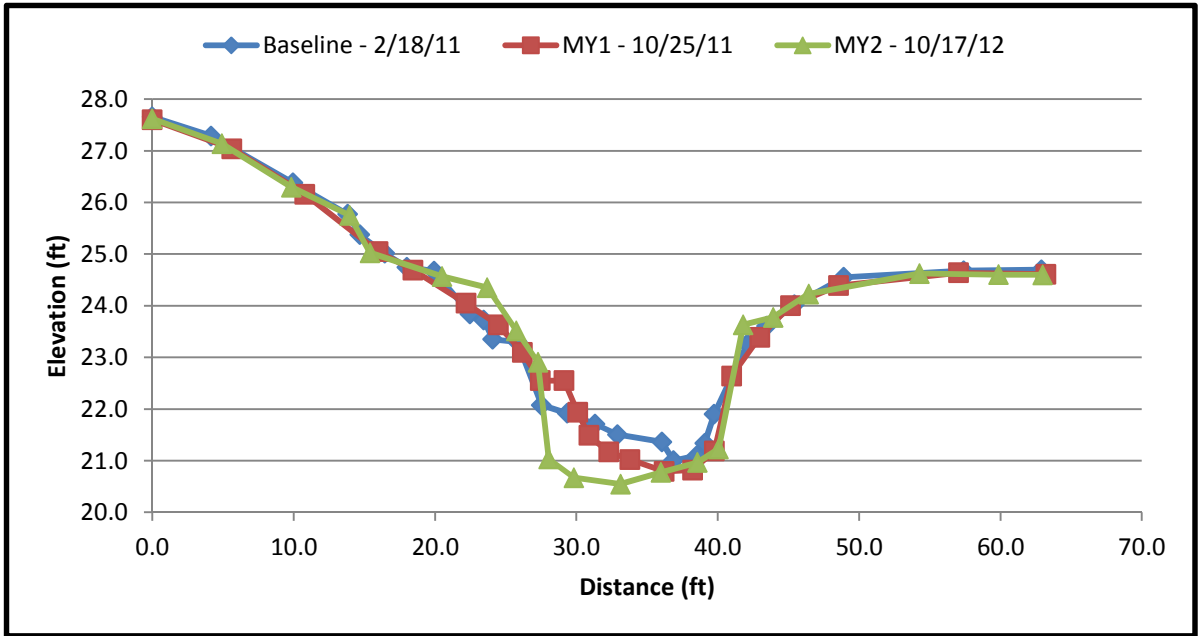




## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	25.95	0.00	25.92	0.00	25.98
	7.89	25.57	5.93	25.63	6.64	25.54
	13.55	24.56	11.34	24.82	11.63	24.84
	16.93	23.93	16.52	23.83	15.21	24.25
	20.82	23.23	19.62	23.35	17.91	23.99
	21.95	23.23	22.66	23.43	19.97	23.79
	23.29	23.19	23.72	20.27	23.46	23.39
	23.99	22.17	26.17	19.31	24.51	22.21
	24.66	22.05	29.54	18.51	25.90	19.73
	24.81	19.95	33.82	18.00	27.02	19.72
	26.88	19.74	35.36	18.53	29.73	19.54
	27.90	19.03	37.52	22.69	32.10	19.42
	32.61	18.48	41.20	23.56	33.92	18.95
	34.85	19.10	43.95	24.40	35.78	19.17
	36.94	20.18	55.09	25.09	38.40	23.04
	37.83	22.98	65.84	26.02	42.09	22.99
	39.80	23.21	73.06	26.48	43.22	24.29
	40.88	23.62			49.73	24.69
	43.90	24.42			60.56	25.28
	55.95	25.20			72.92	26.48
	63.52	25.89				
	72.56	26.58				


XS-11 Pool, Sta. 82+30

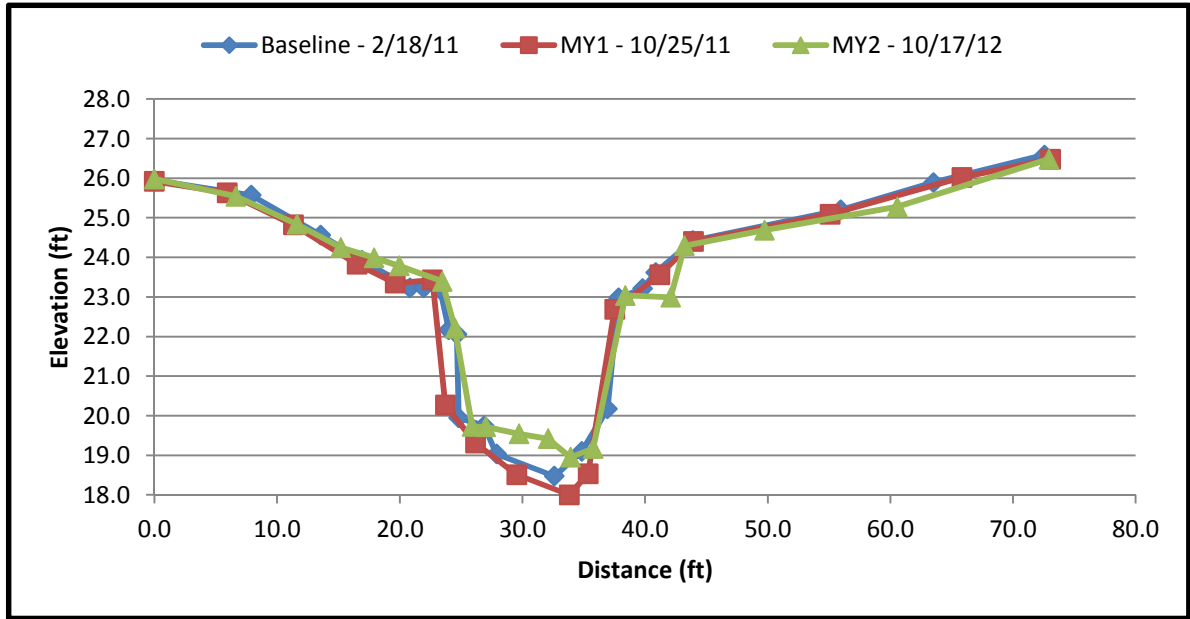

## Adkin Branch, 05065611, Reach 2

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	26.87	0.00	26.82	0.00	26.77
	9.90	26.42	10.23	26.34	11.26	26.33
	20.27	25.71	18.48	25.77	24.13	25.29
	25.17	25.13	24.44	25.21	29.25	24.31
	27.75	24.59	28.45	24.37	32.91	23.67
	30.14	24.11	31.61	23.79	35.58	23.20
	32.91	23.61	33.25	23.30	36.88	22.66
	36.16	22.23	35.04	22.71	38.31	21.91
	38.20	21.28	37.43	22.37	38.65	20.47
	39.57	20.54	37.80	21.92	40.61	19.61
	39.96	19.63	38.37	20.91	46.71	18.91
	41.51	18.93	39.67	18.07	49.92	19.72
	44.70	19.29	41.51	17.63	52.91	20.16
	47.63	19.85	52.49	18.04	55.11	20.87
	50.43	20.45	52.66	19.66	56.75	21.69
	51.78	20.71	53.28	20.09	58.01	23.72
	53.07	21.65	54.79	21.05	59.25	24.20
	54.55	22.44	54.89	23.33	63.34	24.71
	56.58	23.61	55.80	23.61	71.74	25.66
	61.64	24.50	58.85	24.03	82.69	26.87
	64.51	25.16	62.90	24.53		
	75.28	26.09	64.20	25.13		
	82.52	26.90	69.12	25.34		
			72.54	25.85		
			79.36	26.51		
			82.77	26.83		


XS-12 Pool, Sta. 85+88

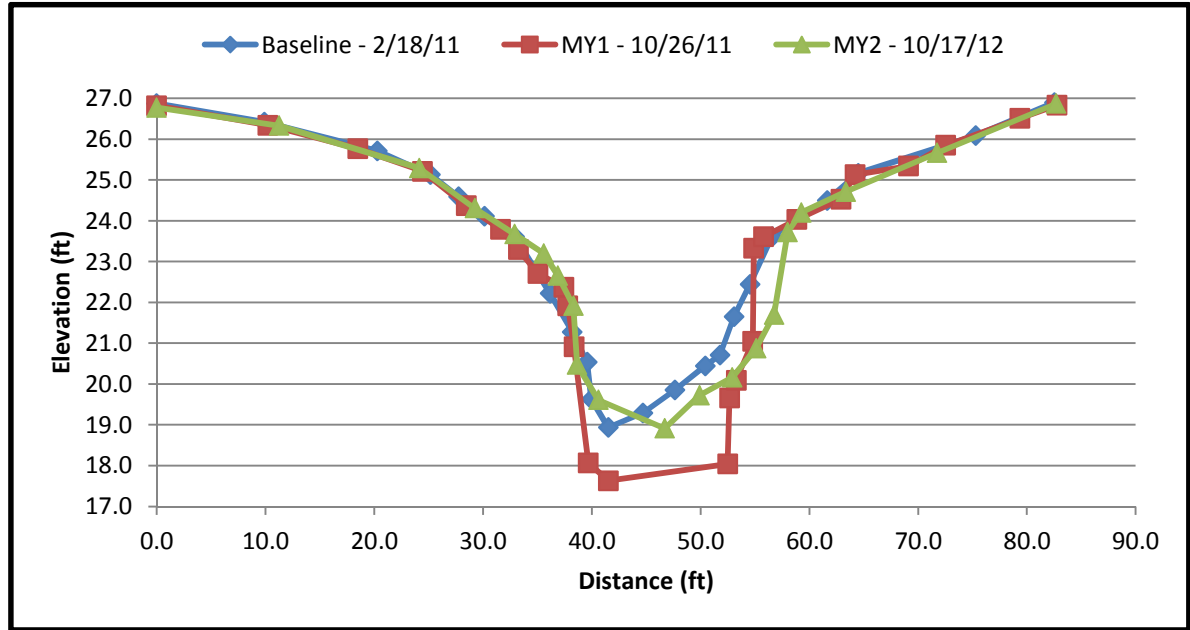




### Adkin Branch, 05065611, Reach 3

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
XS-13 Pool, Sta. 11+64	0.00	31.88	0.00	31.86	0.00	31.94
	1.96	31.88	5.27	31.88	0.35	32.09
	2.82	31.88	8.53	31.81	3.86	32.10
	4.88	31.82	10.08	32.07	7.54	31.97
	7.13	31.90	11.50	31.63	10.99	31.93
	9.06	31.90	12.45	31.50	11.94	31.72
	9.86	31.87	13.28	31.37	13.19	31.61
	10.37	31.74	13.88	31.30	13.92	31.74
	11.06	31.67	14.37	31.45	14.65	31.96
	12.03	31.61	14.95	31.61	18.14	31.96
	12.62	31.53	16.18	31.97	24.23	32.06
	13.17	31.34	18.97	32.00		
	13.88	31.16	24.40	32.05		
	14.36	31.40				
	15.15	31.72				
	15.65	31.85				
	16.41	32.00				
	19.34	31.99				
	21.87	31.99				
	24.27	31.98				
24.44	32.04					

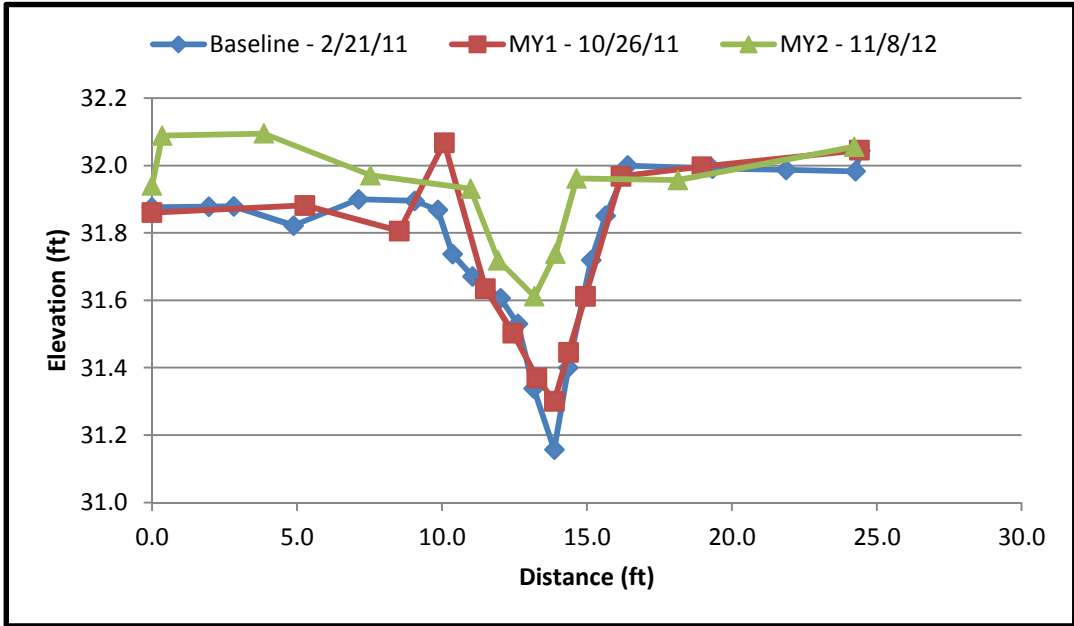

### Adkin Branch, 05065611, Reach 3

XS-14 Riffle, Sta. 14+89	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	31.64	0.00	31.61	0.00	31.56
	1.38	31.49	3.27	31.38	5.45	31.35
	2.83	31.36	5.60	31.29	8.56	31.17
	4.92	31.33	8.34	31.22	10.03	31.12
	6.91	31.28	9.34	31.11	11.05	30.69
	8.50	31.24	10.53	30.92	11.64	30.54
	9.40	31.12	11.01	30.67	12.21	30.58
	10.03	31.02	11.83	30.55	14.08	30.82
	10.44	30.86	12.72	30.63	14.94	31.06
	10.60	30.80	13.61	30.74	18.46	31.29
	10.71	30.71	14.38	30.90	22.74	31.25
	11.02	30.66	15.92	31.22	24.83	31.22
	11.21	30.58	17.64	31.29		
	11.58	30.63	21.76	31.26		
	12.11	30.59	25.05	31.24		
	12.54	30.52				
	12.93	30.68				
	13.48	30.79				
	13.97	30.89				
	14.38	30.88				
	15.13	31.11				
	16.12	31.24				
	18.44	31.31				
	22.90	31.30				
	25.11	31.27				

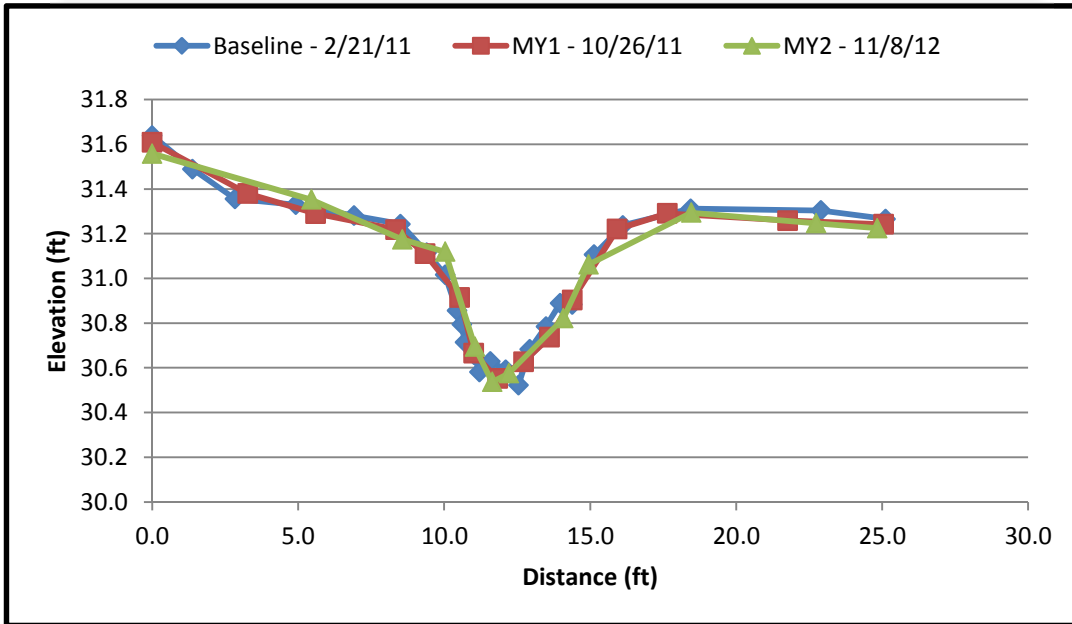




### Adkin Branch, 05065611, Reach 3

	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
XS-15 Riffle, Sta. 19+28	0.00	30.66				
	3.30	30.56				
	8.61	30.26				
	13.27	30.23				
	16.31	30.25				
	17.22	30.22				
	17.98	29.94				
	18.60	29.73				
	18.81	29.70				
	19.03	29.59				
	19.26	29.32				
	19.86	29.33				
	20.39	29.47				
	20.64	29.66				
	20.90	29.87				
	21.92	30.01				
	23.19	30.22				
	25.19	30.49				
	28.07	30.62				
	32.50	30.92				
35.34	31.18					
38.62	31.46					
40.05	31.60					

No Data - Fallen Tree over Channel


No Data - Fallen Tree over Channel

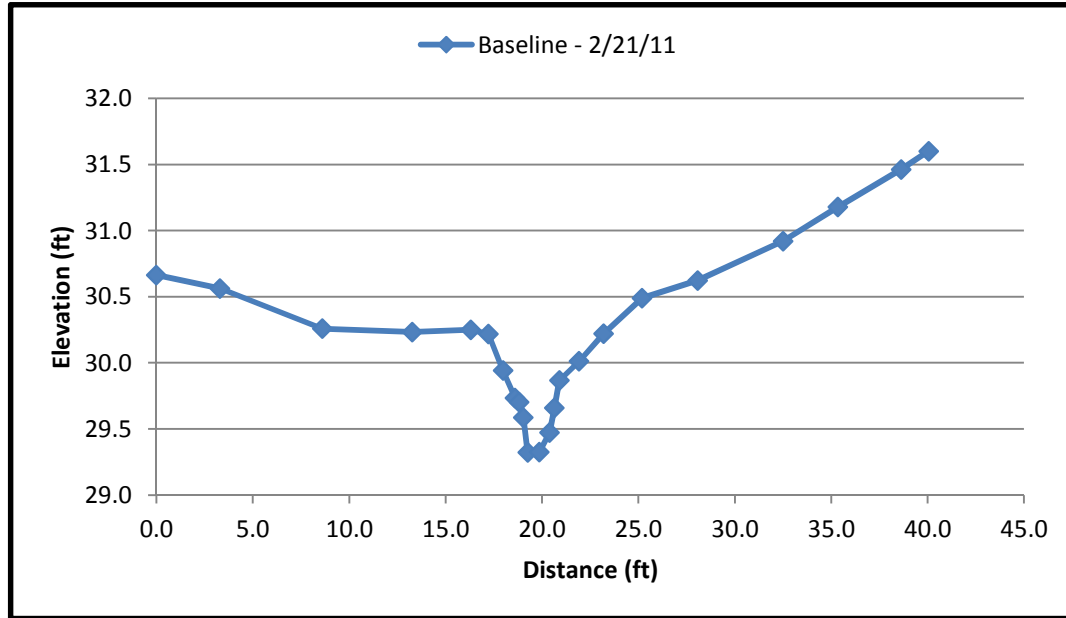




### Adkin Branch, 05065611, Reach 3

XS-16 Pool, Sta.23+64	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	25.98	0.00	25.98	0.00	25.89
	4.96	25.72	6.84	25.58	6.52	25.52
	10.01	25.44	13.28	25.18	12.56	25.23
	13.01	25.18	15.96	24.85	14.97	24.92
	14.66	24.95	16.79	24.74	16.97	24.60
	16.29	24.81	17.94	24.69	18.66	24.34
	18.05	24.63	18.70	24.33	19.64	24.04
	18.59	24.33	19.22	24.27	20.67	24.32
	18.86	24.19	19.92	24.12	23.35	25.04
	19.43	24.13	20.71	24.34	27.00	25.21
	19.97	24.09	21.69	24.69	30.23	25.78
	20.33	24.25	22.47	24.82		
	21.01	24.44	23.20	25.08		
	21.98	24.77	25.85	25.20		
	23.04	25.05	27.47	25.36		
	23.97	25.20	30.40	25.86		
	26.34	25.22				
	27.54	25.34				
	28.93	25.73				
	30.42	25.82				

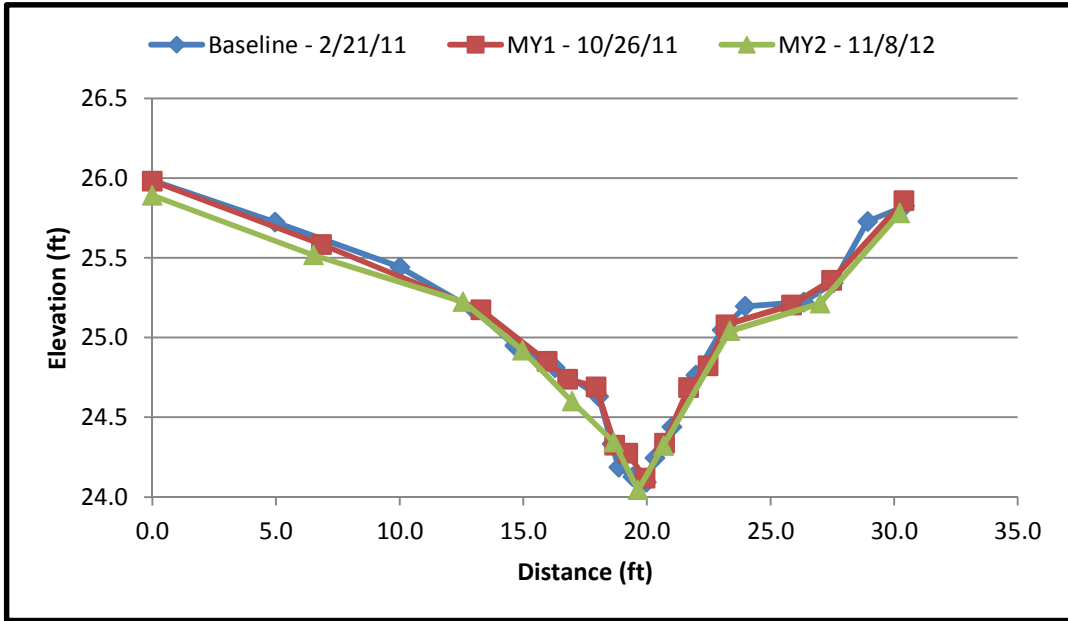

### Adkin Branch, 05065611, Reach 3

XS-17 Riffle, Sta. 23+87	Baseline		MY1		MY2	
	Sta.	Elev.	Sta.	Elev.	Sta.	Elev.
	0.00	26.01	0.00	26.03	0.00	25.94
	4.97	25.78	7.42	25.51	6.91	25.48
	8.45	25.52	11.90	24.98	12.42	25.01
	11.09	25.05	15.17	24.69	16.18	24.50
	14.03	24.80	16.79	24.53	18.29	24.09
	16.48	24.55	17.76	24.37	18.72	23.79
	17.40	24.37	18.54	24.03	19.71	23.65
	18.15	24.09	19.07	23.79	20.81	23.84
	18.64	23.89	19.53	23.65	22.43	24.08
	19.05	23.83	20.46	23.76	23.95	24.59
	19.61	23.79	20.94	23.93	29.61	24.60
	20.10	23.80	21.78	23.99	33.95	25.71
	20.44	23.80	22.97	24.17		
	20.81	23.96	24.01	24.59		
	21.79	23.98	27.80	24.67		
	22.85	24.06	28.74	24.59		
	23.96	24.61	29.57	24.59		
	26.35	24.64	31.01	25.16		
	29.26	24.54	33.77	25.77		
	29.95	24.77				
	32.07	25.44				
	33.67	25.73				

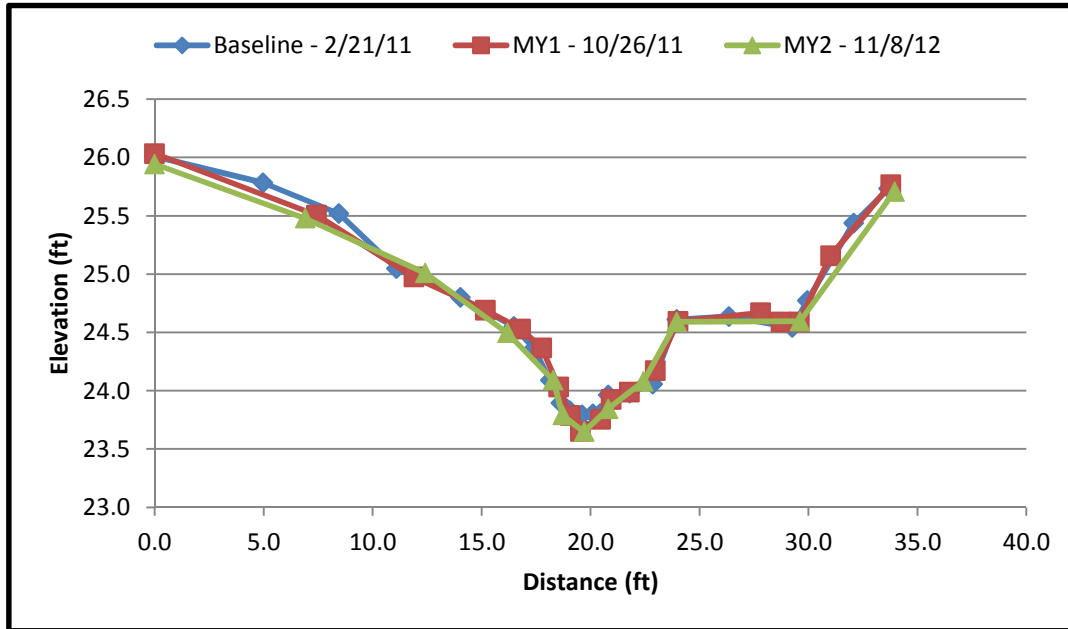

**Figures 5.1-5.3. Longitudinal Profile Plots**

Figure 5.1 Reach 1 (Washington Ave. to Gordon St.) - Longitudinal Profile

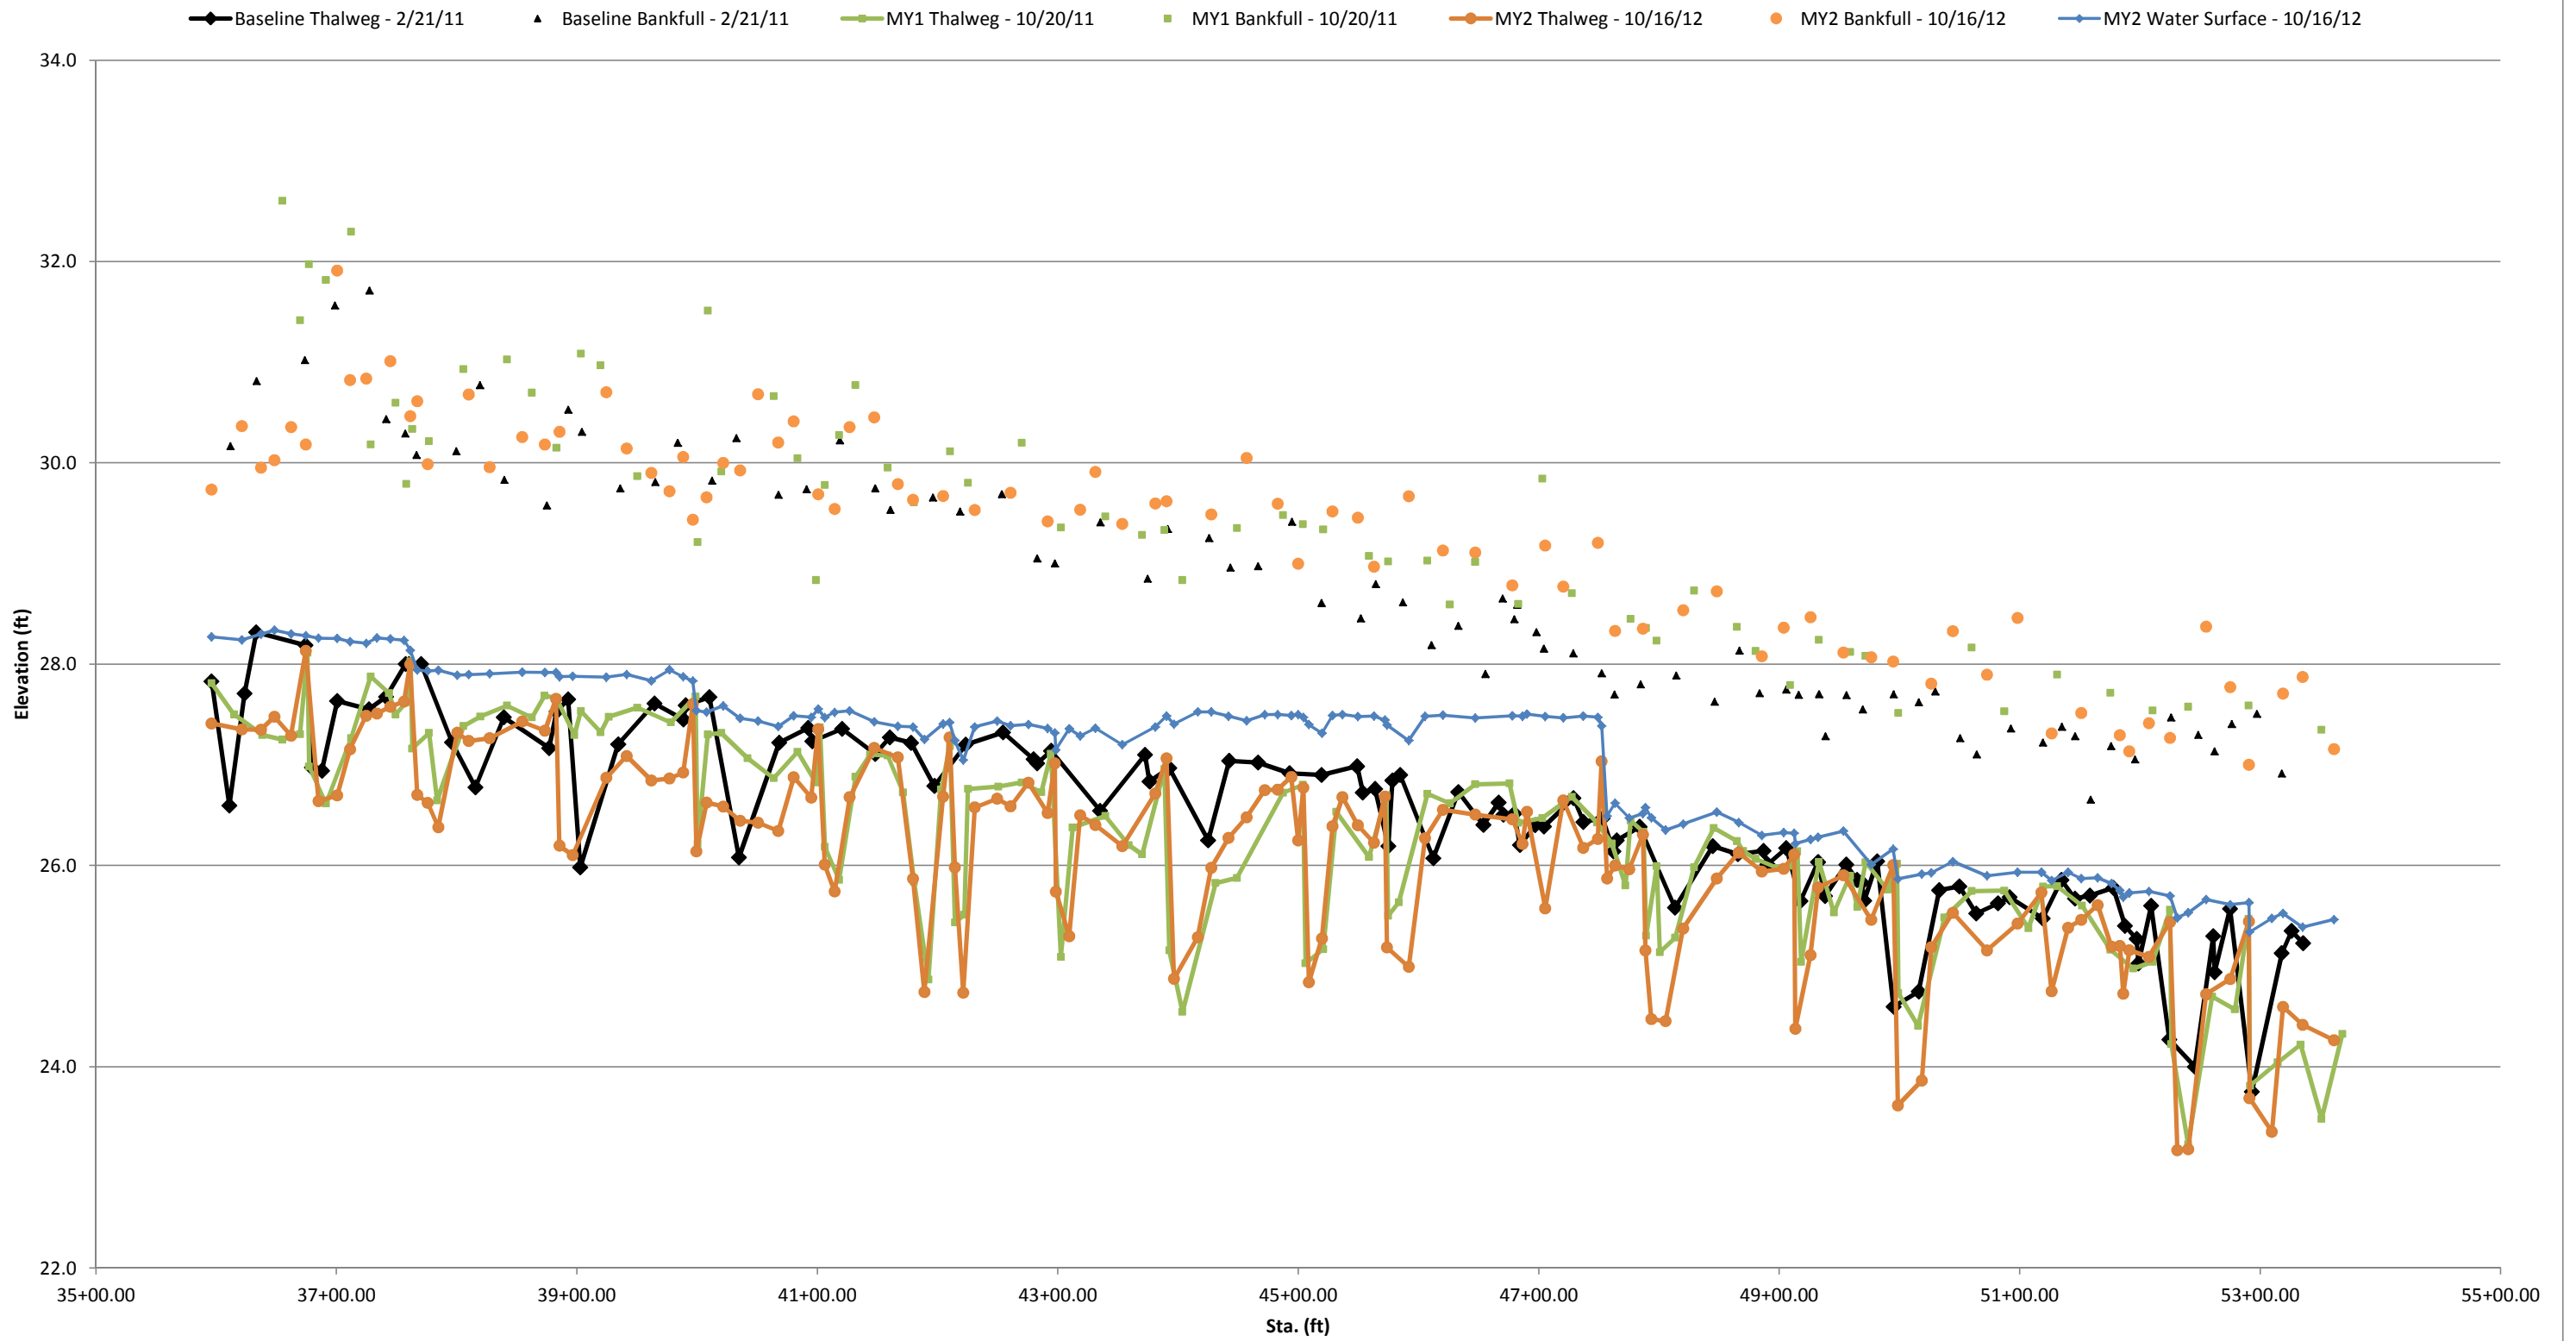




Figure 5.2 Reach 2 (Gordon St. to Lincoln St.) - Longitudinal Profile

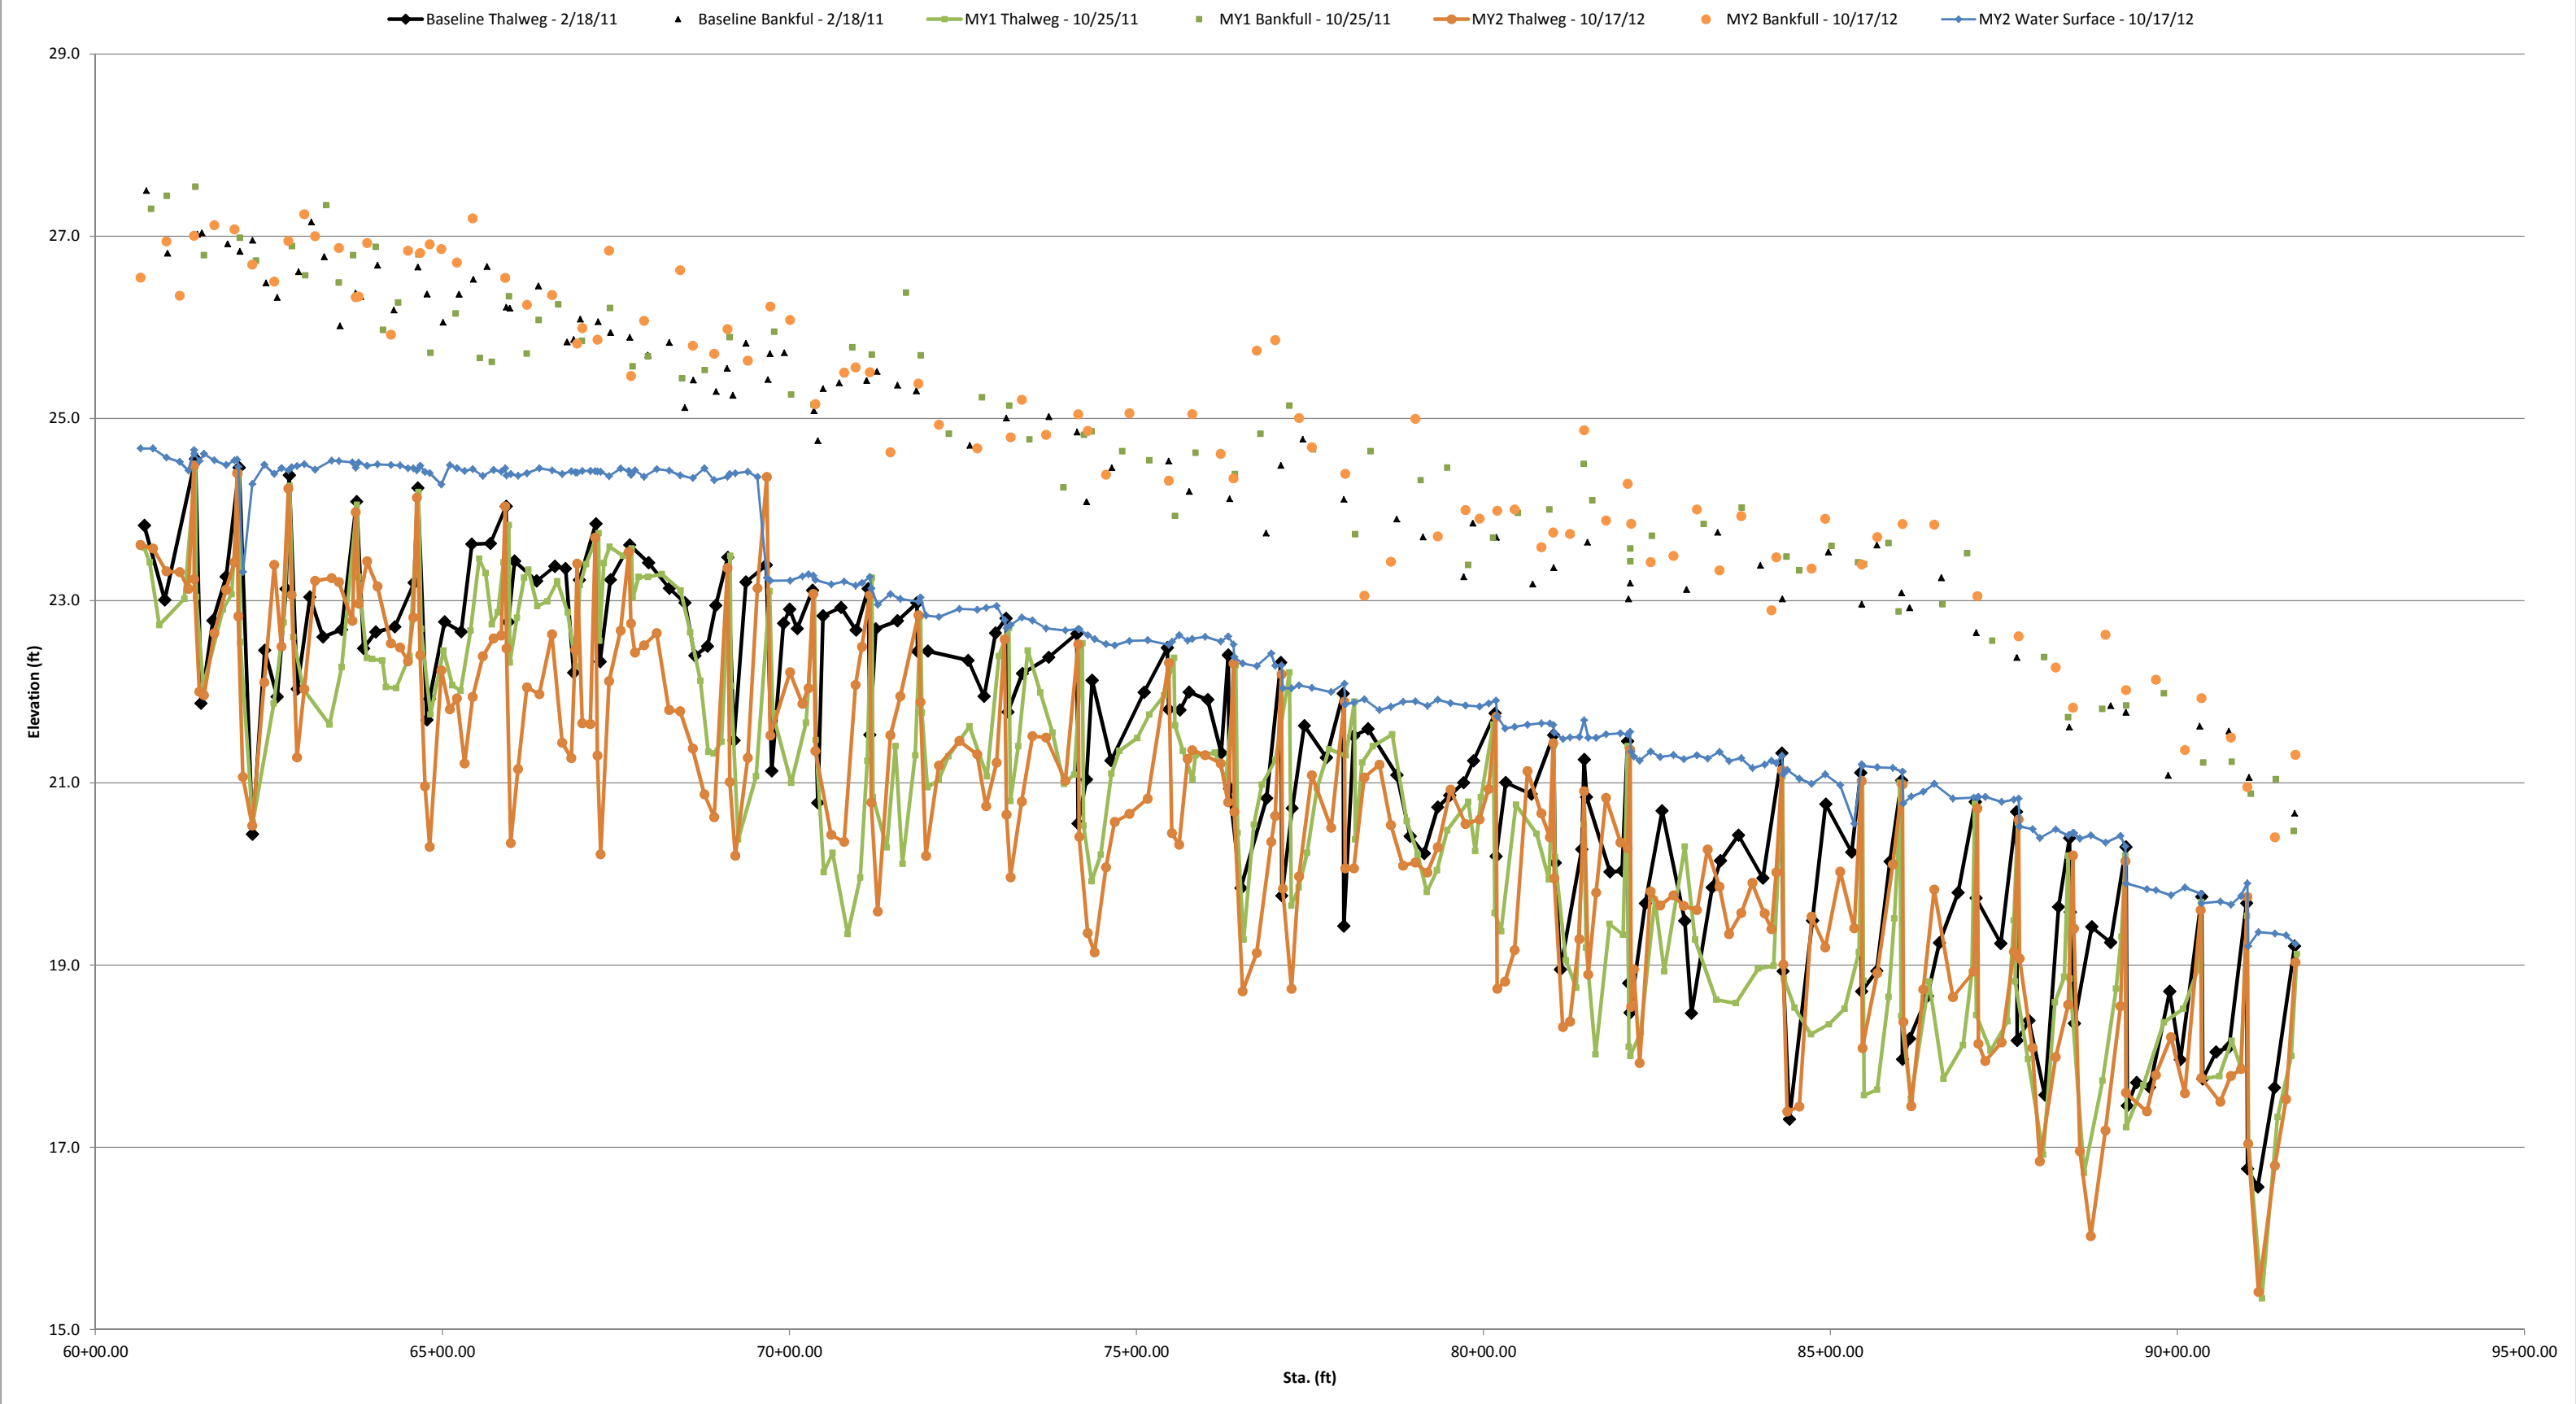
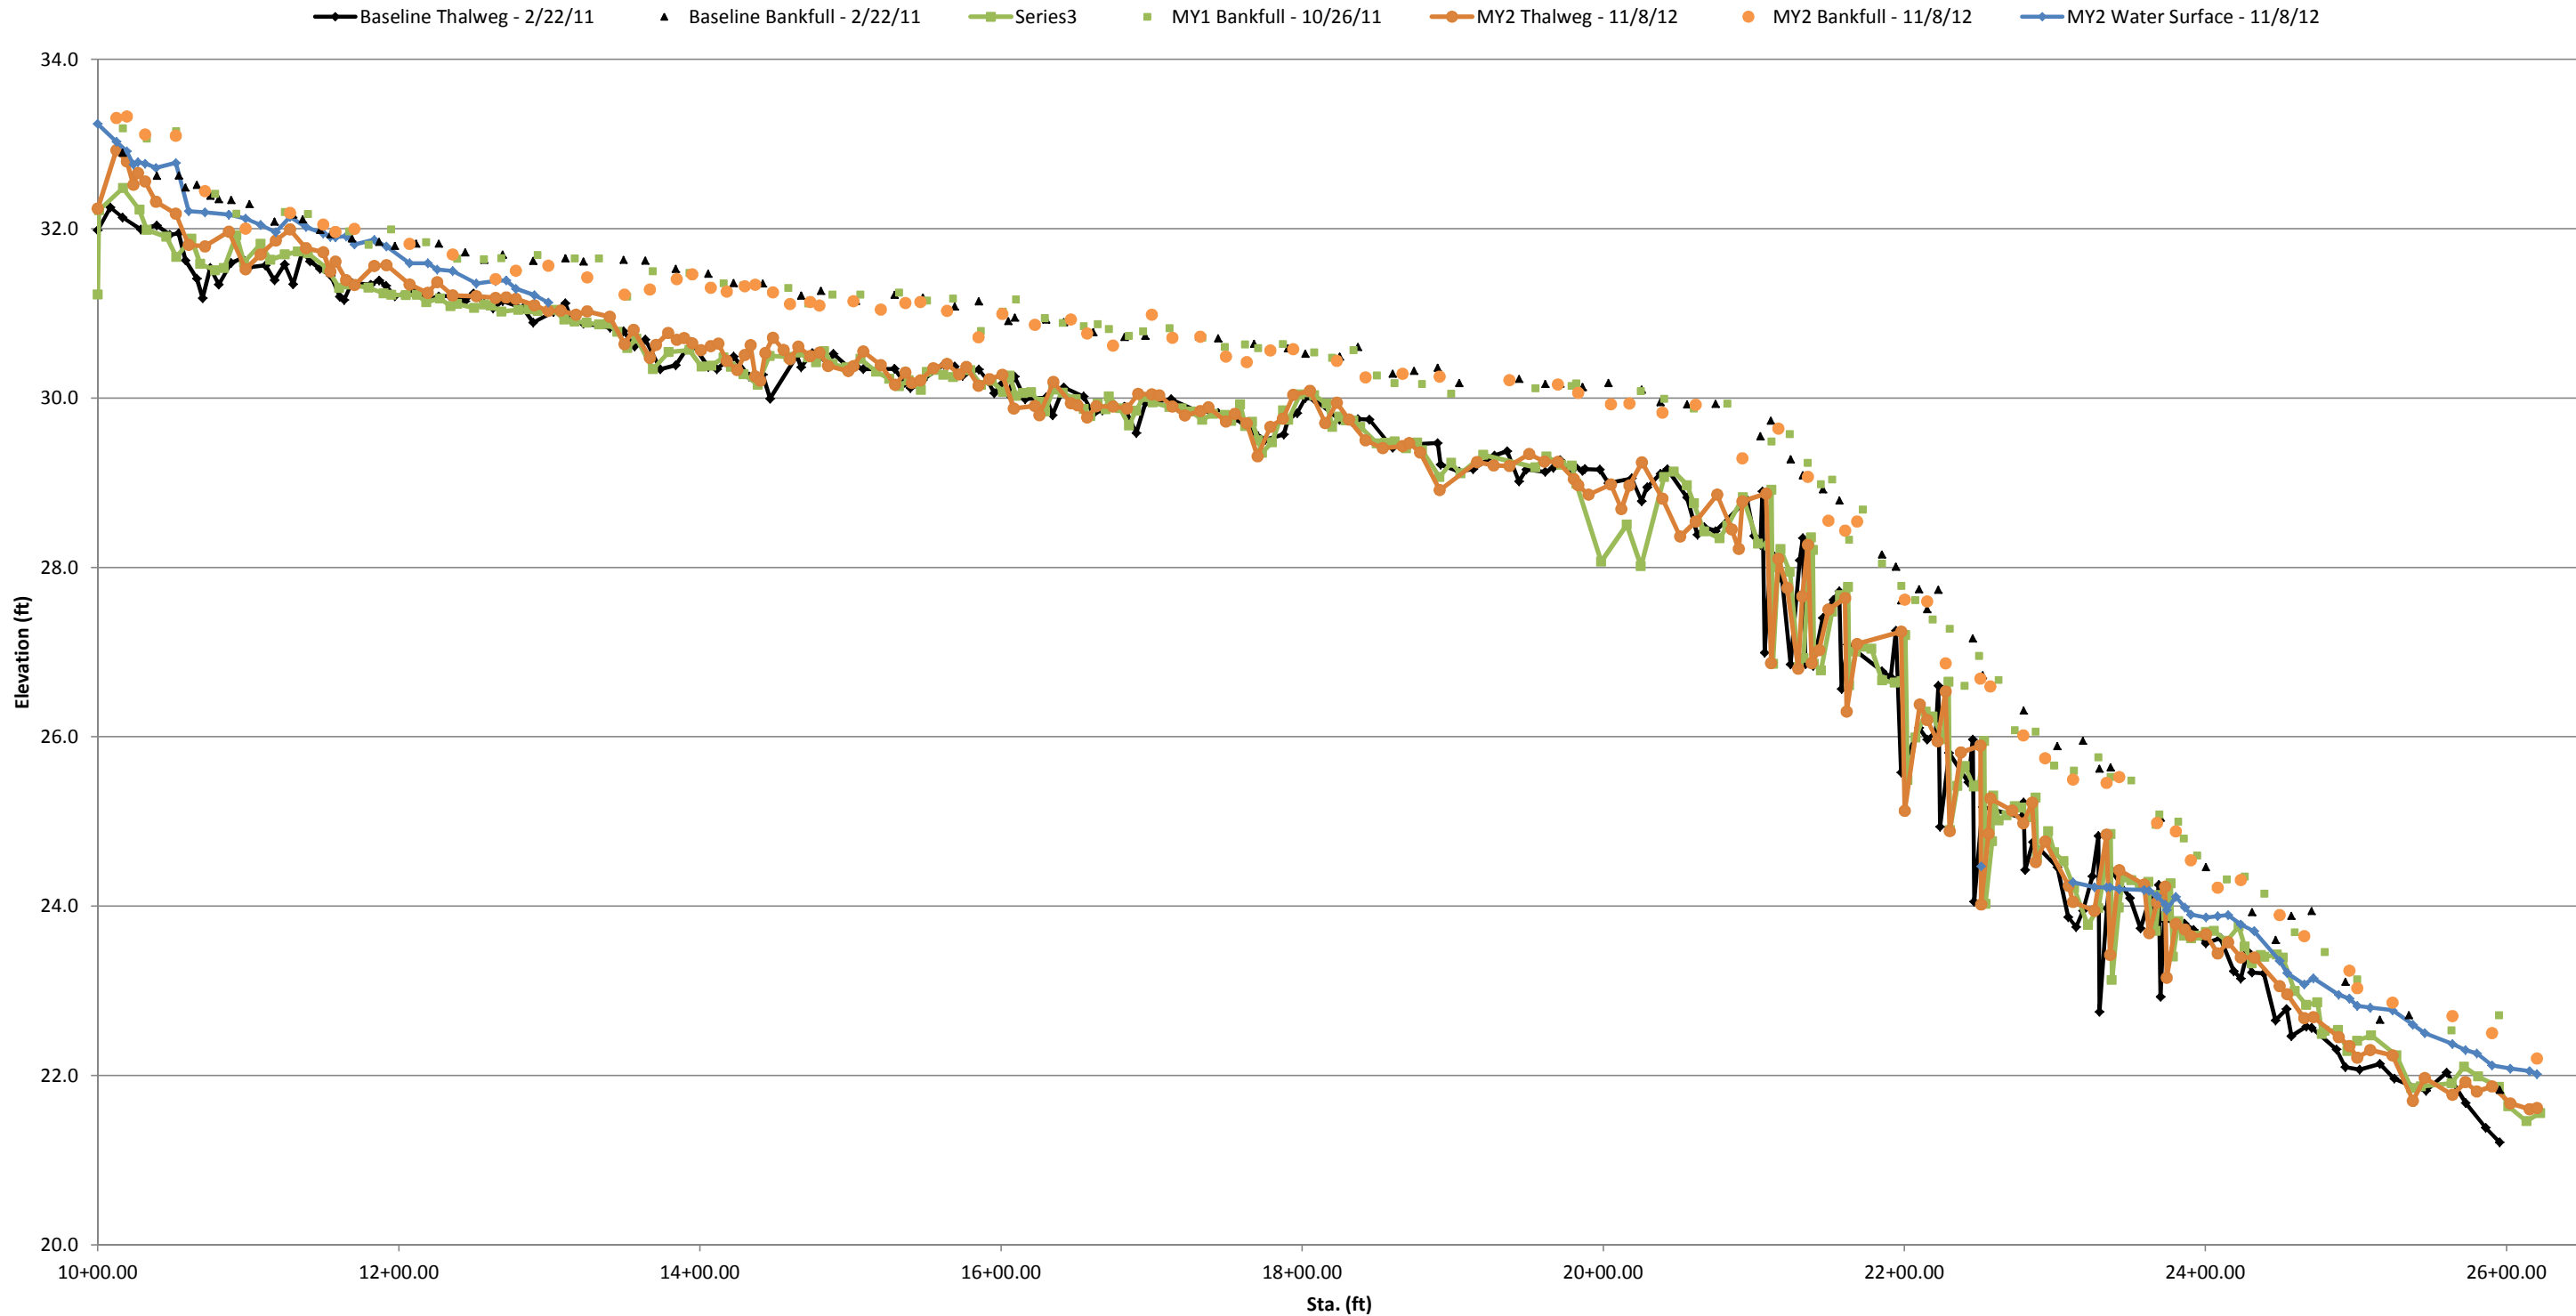




Figure 5.3 Reach 3 (UT to Adkin Branch) - Longitudinal Profile





**Table 10a. Baseline Stream Data Summary**  
**Adkin Branch Stream Restoration Project - Phase I - Contract No. 070708001**  
**Reach 1**

Parameter	Existing Condition (Wash Ave. to Gordon)	Reference Reach (Johnson Mill)	Proposed (Wash Ave. to Gordon)	Reach 1 Baseline (Washington Ave. to Gordon St.)					
				Min	Mean	Med	Max	SD	n
<b>Dimension and Substrate - Riffle</b>									
Bankfull Width (ft)	20.90	21.20	22.00	14.84	15.95	14.99	18.03	1.80	3
Floodprone Width (ft)	29.40	34.90	40.00	28.45	42.14	41.72	56.25	13.90	3
Bankfull Mean Depth (ft)	1.95	2.25	1.38	0.92	1.35	1.42	1.70	0.40	3
Bankfull Max Depth (ft)	2.26	2.42	1.65	1.50	2.11	2.07	2.77	0.64	3
Bankfull Cross Sectional Area (ft <sup>2</sup> )	40.90	47.60	30.30	13.78	21.57	25.23	25.69	6.75	3
Width/Depth Ratio	10.70	9.40	16.00	8.73	12.57	12.70	16.29	3.78	3
Entrenchment Ratio	1.40	1.60	1.80	1.90	2.67	2.31	3.79	0.99	3
Bank Height Ratio	-	-	-	1.00	1.00	1.00	1.00	0.00	3
d50 (mm)	-	-	-						
<b>Profile</b>									
Riffle Length (ft)	-	-	-	13.69	88.32	82.84	173.90	51.83	14
Riffle Slope (ft/ft)	0.0012	0.00001	0.0026	0.0002	0.0016	0.0013	0.0062	0.0016	14
Pool Length (ft)	-	-	-	11.36	24.52	24.15	46.88	8.60	19
Pool Max depth (ft)	3.18	3.56	3.44	2.11	2.99	2.86	4.33	0.72	19
Pool Spacing (ft)	183 - 231	91.1 - 130.0	88 - 132	22.73	95.81	94.46	180.40	41.64	18
<b>Pattern</b>									
Channel Beltwidth (ft)	30 - 50	50 - 1500	44 - 176						
Radius of Curvature (ft)	150 - 320	43 - 235	66 - 110						
Rc: Bankfull Width (ft/ft)	7.2 - 15.3	2.0 - 11.1	3.0 - 5.0						
Meander Wavelength (ft)	175 - 400	250 - 400	264 - 418						
Meander Width Ratio	1.43 - 2.39	2.4 - 70.9	2.0 - 8.0						
<b>Substrate, bed and transport parameters</b>									
Ri% / P%	-	-	-	73% / 27%					
SC% / Sa% / G% / C% / B% / Be%	-	-	-						
d16 / d35 / d50 / d84 / d95/ d <sub>p</sub> / d <sub>sp</sub> (mm)	-	-	-						
Reach Shear Stress (competency) lb/ft <sup>2</sup>	N/A		N/A	N/A					
Max part size (mm) mobilized at bankfull	-		-	-					
Unit Stream Power (transport capacity) lbs/ft.s	0.075	0.197	0.220	0.325					
<b>Additional Reach Parameters</b>									
Drainage Area (SM)	4.60	13.50	5.03						
Impervious cover estimate (%)	-	-	-						
Rosgen Classification	G5	B5c	B5c	B5c					
Bankfull Velocity (fps)	1.20	1.70	1.70	1.95					
Bankfull Discharge (cfs)	50.00	80.90	50.00						
Valley length (ft)	-	-	1685	1685					
Channel Thalweg length (ft)	-	-	1750	1727					
Sinuosity (ft)	1.04	1.10	1.04	1.03					
Water Surface Slope (Channel) (ft/ft)	0.0005	0.0010	0.0016	0.00166					
BF slope (ft/ft)	-	-	-	0.00240					
Bankfull Floodplain Area (acres)	-	-	-						
Proportion over wide (%)	-	-	-						
Entrenchment Class (ER Range)	-	-	-						
Incision Class (BHR Range)	-	-	-						
BEHI VL% / L% / M% / H% / VH% / E%	-	-	-						
Channel Stability or Habitat Metric	-	-	-						
Biological or Other	-	-	-						

It should be noted that As-built conditions were completed at the end of construction. Many storm events had occurred between beginning of construction and end of construction that naturally modified constructed parameters.

**Table 10b. Baseline Stream Data Summary**  
**Adkin Branch Stream Restoration Project - Phase I - Contract No. 070708001**  
**Reach 2**

Parameter	Existing Condition (Gordon to Lincoln)	Reference Reach (Johnson Mill)	Proposed (Gordon to Lincoln)	Reach 2 Baseline (Gordon St. to Lincoln St.)					
				Min	Mean	Med	Max	SD	n
<b>Dimension and Substrate - Riffle</b>									
Bankfull Width (ft)	23.60	21.20	22.00	16.23	16.98	16.81	17.91	0.85	3
Floodprone Width (ft)	45.00	34.90	40.00	48.33	52.40	51.29	57.58	4.72	3
Bankfull Mean Depth (ft)	1.83	2.25	1.47	1.46	1.66	1.64	1.88	0.21	3
Bankfull Max Depth (ft)	2.98	2.42	1.76	2.21	2.38	2.26	2.68	0.26	3
Bankfull Cross Sectional Area (ft <sup>2</sup> )	43.30	47.60	32.30	23.68	28.32	27.58	33.70	5.05	3
Width/Depth Ratio	12.90	9.40	15.00	9.53	10.30	10.25	11.12	0.80	3
Entrenchment Ratio	1.90	1.60	1.80	2.99	3.09	3.05	3.22	0.12	3
Bank Height Ratio	-	-	-	1.00	1.00	1.00	1.00	0.00	3
d50 (mm)	-	-	-	-	-	-	-	-	-
<b>Profile</b>									
Riffle Length (ft)	-	-	-	27.43	62.71	62.38	93.27	19.56	10
Riffle Slope (ft/ft)	0.0024	0.00001	0.0031	0.0002	0.0013	0.0010	0.0039	0.0013	10
Pool Length (ft)	-	-	-	14.20	56.38	56.82	113.64	27.38	39
Pool Max depth (ft)	4.14	3.56	3.67	2.74	4.23	4.22	6.48	0.76	39
Pool Spacing (ft)	59.62 - 117.86	91.1 - 130.0	88.0 - 132.0	17.05	73.45	69.60	164.78	32.96	38
<b>Pattern</b>									
Channel Beltwidth (ft)	75 - 120	50 - 1500	44.0 - 176.0						
Radius of Curvature (ft)	40 - 146	43 - 235	66.0 - 110.0						
Rc: Bankfull Width (ft/ft)	1.7 - 6.2	2.0 - 11.1	3.0 - 5.0						
Meander Wavelength (ft)	224 - 260	250 - 400	264.0 - 418.0						
Meander Width Ratio	3.18 - 5.08	2.4 - 70.9	2.0 - 8.0						
<b>Substrate, bed and transport parameters</b>									
Ri% / P%	-	-	-	29% / 71% *					
SC% / Sa% / G% / C% / B% / Be%	-	-	-						
d16 / d35 / d50 / d84 / d95/ d <sub>p</sub> / d <sub>sp</sub> (mm)	-	-	-						
Reach Shear Stress (competency) lb/ft <sup>2</sup>	N/A		N/A	N/A					
Max part size (mm) mobilized at bankfull	-		-	-					
Unit Stream Power (transport capacity) lbs/ft.s	0.106	0.197	0.230	0.321					
<b>Additional Reach Parameters</b>									
Drainage Area (SM)	5.30	13.50	5.50						
Impervious cover estimate (%)	-	-	-						
Rosgen Classification	B5	B5c	B5c	B5c					
Bankfull Velocity (fps)	1.30	1.70	1.80	1.99					
Bankfull Discharge (cfs)	55.00	80.90	55.00						
Valley length (ft)	-	-	4106	4106					
Channel Thalweg length (ft)	-	-	4246	4270					
Sinuosity (ft)	1.12	1.10	1.03	1.04					
Water Surface Slope (Channel) (ft/ft)	0.0007	0.0010	0.0014	0.0016					
BF slope (ft/ft)	-	-	-	0.0018					
Bankfull Floodplain Area (acres)	-	-	-						
Proportion over wide (%)	-	-	-						
Entrenchment Class (ER Range)	-	-	-						
Incision Class (BHR Range)	-	-	-						
BEHI VL% / L% / M% / H% / VH% / E%	-	-	-						
Channel Stability or Habitat Metric	-	-	-						
Biological or Other	-	-	-						

It should be noted that As-built conditions were completed at the end of construction. Many storm events had occurred between beginning of construction and end of construction that naturally modified constructed parameters.

\* Reach 2 is a predominately pool system due to need to drop grade at the lower end of the project.



**Table 10c. Baseline Stream Data Summary**  
**Adkin Branch Stream Restoration Project - Phase I - Contract No. 070708001**  
**Reach 3**

Parameter	Existing Condition (UT to Adkin Branch)	Reference Reach (UT to Wildcat Branch)	Proposed (UT to Adkin Branch)	Reach 3 Baseline (UT to Adkin Branch)					
				Min	Mean	Med	Max	SD	n
<b>Dimension and Substrate - Riffle</b>									
Bankfull Width (ft)	Mean 3.60	Mean 7.70	Mean 6.00	6.06	7.27	7.69	8.06	1.06	3
Floodprone Width (ft)	8.30	130.00	15.00	23.07	27.62	25.11	34.69	6.20	3
Bankfull Mean Depth (ft)	0.47	1.03	0.55	0.35	0.42	0.40	0.50	0.08	3
Bankfull Max Depth (ft)	3.40	1.56	0.85	0.72	0.81	0.82	0.90	0.09	3
Bankfull Cross Sectional Area (ft <sup>2</sup> )	1.70	7.90	3.30	2.43	3.04	2.68	4.00	0.84	3
Width/Depth Ratio	7.60	7.50	11.00	15.15	17.75	16.12	21.97	3.69	3
Entrenchment Ratio	2.30	16.90	2.50	2.86	3.95	3.26	5.72	1.55	3
Bank Height Ratio	-	-	-	1.00	1.00	1.00	1.00	0.00	3
d50 (mm)	-	-	-						
<b>Profile</b>									
Riffle Length (ft)	-	-	-	9.59	34.33	26.34	165.84	30.38	28
Riffle Slope (ft/ft)	0.0002	0.0021	0.0032	0.0012	0.0051	0.0044	0.0121	0.0031	28
Pool Length (ft)	-	-	-	4.26	21.38	23.26	52.81	12.04	32
Pool Max depth (ft)	1.45	1.90	1.36	0.64	1.59	1.32	2.95	0.70	32
Pool Spacing (ft)	21.63	14.0 - 16.6	12.0 - 36.0	13.49	42.26	37.22	93.07	20.82	30
<b>Pattern</b>									
Channel Beltwidth (ft)	50.00	13.8 - 19.4	12.0 - 36.0						
Radius of Curvature (ft)	93 - 105	10.9 - 15.3	12.0 - 18.0						
Rc: Bankfull Width (ft/ft)	26.0 - 29.3	1.4 - 2.0	2.0 - 3.0						
Meander Wavelength (ft)	212 - 517	22.5 - 29.0	18.0 - 48.0						
Meander Width Ratio	13.97	1.8 - 2.5	2.0 - 6.0						
<b>Substrate, bed and transport parameters</b>									
Ri% / P%	-	-	-	58% / 42%					
SC% / Sa% / G% / C% / B% / Be%	-	-	-						
d16 / d35 / d50 / d84 / d95/ d <sup>p</sup> / d <sup>sp</sup> (mm)	-	-	-						
Reach Shear Stress (competency) lb/ft <sup>2</sup>	N/A		N/A	N/A					
Max part size (mm) mobilized at bankfull	-		-	-					
Unit Stream Power (transport capacity) lbs/ft.s	0.007	0.140	0.080	0.083					
<b>Additional Reach Parameters</b>									
Drainage Area (SM)	0.12	0.44	0.12						
Impervious cover estimate (%)	-	-	-						
Rosgen Classification	E5	E5	E5	E5					
Bankfull Velocity (fps)	2.10	1.20	1.10	1.44					
Bankfull Discharge (cfs)	3.50	9.20	3.50						
Valley length (ft)	1200	-	1200	1200					
Channel Thalweg length (ft)	1200	-	1615	1582					
Sinuosity (ft)	1.00	1.15	1.35	1.32					
Water Surface Slope (Channel) (ft/ft)	0.0001	0.0024	0.0022	0.0028					
BF slope (ft/ft)	-	-	-	0.0030					
Bankfull Floodplain Area (acres)	-	-	-						
Proportion over wide (%)	-	-	-						
Entrenchment Class (ER Range)	-	-	-						
Incision Class (BHR Range)	-	-	-						
BEHI VL% / L% / M% / H% / VH% / E%	-	-	-						
Channel Stability or Habitat Metric	-	-	-						
Biological or Other	-	-	-						

It should be noted that As-built conditions were completed at the end of construction. Many storm events had occurred between beginning of construction and end of construction that naturally modified constructed parameters.



**Table 11. Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters - Cross Section)  
Adkin Branch Stream Restoration Project - Phase I  
Contract No. 070708001**

	Cross Section 1 (Riffle)							Cross Section 2 (Pool)							Cross Section 3 (Riffle)							Cross Section 4 (Pool)							Cross Section 5 (Riffle)																					
Dimension and substrate <sup>1</sup>	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+															
Bankfull Width (ft)	14.84	12	12.55					24.28	18.49	17.14					18.03	19.72	17.07					17.42	16.08	15.95					14.99	16.25	10.88																			
Floodprone Width (ft)	56.25	44.63	50.14					72.2	71.85	75.65					41.72	52.82	52.88					39.81	42.63	69.79					28.45	49.93	31.85																			
Bankfull Mean Depth (ft)	1.7	1.85	2.29					1.97	2.57	2.98					1.42	1.61	1.66					1.46	1.59	2.76					0.92	1.16	1.29																			
Bankfull Max Depth (ft)	2.77	2.47	2.7					3.33	3.89	4.14					2.07	2.76	2.74					2.05	2.17	3.61					1.5	2.55	1.98																			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	25.23	22.2	28.71					47.75	47.44	51.08					25.69	31.85	28.32					25.48	25.55	44.04					13.78	18.8	14.06																			
Bankfull Width/Depth Ratio	8.73	6.49	5.48					12.32	7.19	5.75					12.7	12.25	10.28					11.93	10.11	5.78					16.29	14.01	8.43																			
Bankfull Entrenchment Ratio	3.79	3.72	4					2.97	3.89	4.41					2.31	2.68	3.1					2.29	2.65	4.38					1.9	3.07	2.93																			
Bankfull Bank Height Ratio	1	1	1					1	1	1					1	1	1					1	1	1					1	1	1																			
	Cross Section 6 (Pool)							Cross Section 7 (Riffle)							Cross Section 8 (Pool)							Cross Section 9 (Riffle)							Cross Section 10 (Riffle)																					
Dimension and substrate <sup>1</sup>	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+															
Bankfull Width (ft)	15.1	18.04	21.48					17.91	16.15	21.82					16.57	15.76	15.61					16.81	15.69	17.96					16.23	17.72	16.32																			
Floodprone Width (ft)	57.39	57.49	56.48					57.58	64.23	64.27					50.57	50.57	50.41					51.29	56.7	56.68					48.33	51.64	55.58																			
Bankfull Mean Depth (ft)	2.94	3.16	4.21					1.88	2.85	2.81					1.93	2.76	3.49					1.64	2.01	2.23					1.46	1.61	2.35																			
Bankfull Max Depth (ft)	4.39	4.85	6.14					2.68	4.26	3.87					3.51	4.89	5.18					2.21	2.84	3.07					2.26	2.6	3.08																			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	44.41	57.01	90.46					33.7	45.98	61.35					31.92	43.57	54.47					27.58	31.55	40.05					23.68	28.48	38.34																			
Bankfull Width/Depth Ratio	5.14	5.71	5.1					9.53	5.67	7.77					8.59	5.71	4.47					10.25	7.81	8.05					11.12	11.01	6.94																			
Bankfull Entrenchment Ratio	3.8	3.19	2.63					3.22	3.98	2.95					3.05	3.21	3.23					3.05	3.61	3.16					2.99	2.91	3.41																			
Bankfull Bank Height Ratio	1	1	1					1	1	1					1	1	1					1	1	1					1	1	1																			
	Cross Section 11 (Pool)							Cross Section 12 (Pool)							Cross Section 13 (Pool)							Cross Section 14 (Riffle)							Cross Section 15 (Riffle)																					
Dimension and substrate <sup>1</sup>	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+															
Bankfull Width (ft)	16.31	17.99	14.96					23.66	17.42	22.13					5.89	5.97	3.55					7.69	7.63	5.82					6.06	N/A	N/A																			
Floodprone Width (ft)	72.56	73.06	72.92					82.52	82.77	82.69					24.44	24.4	24.23					25.11	25.05	24.83					34.69	N/A	N/A																			
Bankfull Mean Depth (ft)	3.19	3.51	2.94					2.72	3.87	2.92					0.31	0.35	0.19					0.35	0.34	0.31					0.4	N/A	N/A																			
Bankfull Max Depth (ft)	4.71	5.43	4.09					4.68	4.74	4.29					0.71	0.67	0.32					0.72	0.67	0.58					0.9	N/A	N/A																			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	52.00	63.18	44.06					64.42	67.38	64.51					1.81	2.09	0.68					2.68	2.6	1.8					2.43	N/A	N/A																			
Bankfull Width/Depth Ratio	5.11	5.13	5.09					8.7	4.5	7.58					19	17.06	18.68					21.97	22.44	18.77					15.15	N/A	N/A																			
Bankfull Entrenchment Ratio	4.45	4.06	4.87					3.49	4.75	3.74					4.15	4.09	6.82					3.26	3.28	4.27					5.72	N/A	N/A																			
Bankfull Bank Height Ratio	1	1	1					1	1	1					1	1	1					1	1	1					1	N/A	N/A																			
	Cross Section 16 (Pool)							Cross Section 17 (Riffle)							<p align="center"><b>NOTE:</b></p> <p>Reach 1 - Washington Ave. to Gordon St. - Cross-Sections 1 through 5</p> <p>Reach 2 - Gordon St. to Lincoln St. - Cross-Sections 6 - 12</p> <p>Reach 3 - UT to Adkin Branch - Cross-Sections 13-17</p> <p>Cross-section 15: Not able to survey due to fallen tree across cross-section</p>																																			
Dimension and substrate <sup>1</sup>	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+																													Base	MY1	MY2	MY3	MY4	MY5	MY+	
Bankfull Width (ft)	11.59	9.14	9.32					8.06	7.82	8.93																																								
Floodprone Width (ft)	30.42	30.4	30.23					23.07	25.58	27.18																																								
Bankfull Mean Depth (ft)	0.46	0.43	0.46					0.5	0.48	0.46																																								
Bankfull Max Depth (ft)	1.11	0.96	1.00					0.82	0.94	0.94																																								
Bankfull Cross Sectional Area (ft <sup>2</sup> )	5.34	3.91	4.25					4	3.76	4.14																																								
Bankfull Width/Depth Ratio	25.2	21.26	20.26					16.12	16.29	19.41																																								
Bankfull Entrenchment Ratio	2.62	3.33	3.24					2.86	3.27	3.04																																								
Bankfull Bank Height Ratio	1	1	1					1	1	1																																								

<sup>1</sup> = Based on current bankfull elevation, determined by field indicators of bankfull.





**Table 12.1 Monitoring Data - Stream Reach Data Summary**  
**Adkin Branch Stream Restoration Project - Phase I - Contract No. 070708001**

**Reach 1 (Washington Ave. to Gordon St.)**

Parameter	Baseline						MY-1						MY-2						MY-3						MY-4						MY-5					
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n
<b>Dimension and substrate - Riffle only</b>																																				
Bankfull Width (ft)	14.84	15.95	14.99	18.03	1.80	3	12.00	15.99	16.25	19.72	3.87	3	10.88	13.50	12.55	17.07	3.20	3																		
Floodprone Width (ft)	28.45	42.14	41.72	56.25	13.90	3	44.63	49.13	49.93	52.82	4.15	3	31.85	44.96	50.14	52.88	11.43	3																		
Bankfull Mean Depth (ft)	0.92	1.35	1.42	1.70	0.40	3	1.16	1.54	1.61	1.85	0.35	3	1.29	1.75	1.66	2.29	0.51	3																		
<sup>1</sup> Bankfull Max Depth (ft)	1.50	2.11	2.07	2.77	0.64	3	2.47	2.59	2.55	2.76	0.15	3	1.98	2.47	2.70	2.74	0.43	3																		
Bankfull Cross Sectional Area (ft <sup>2</sup> )	13.78	21.57	25.23	25.69	6.75	3	18.80	24.28	22.20	31.85	6.77	3	14.06	23.70	28.32	28.71	8.35	3																		
Width/Depth Ratio	8.73	12.57	12.70	16.29	3.78	3	6.49	10.92	12.25	14.01	3.93	3	5.48	8.06	8.43	10.28	2.42	3																		
Entrenchment Ratio	1.90	2.67	2.31	3.79	0.99	3	2.68	3.16	3.07	3.72	0.53	3	2.93	3.34	3.10	4.00	0.58	3																		
<sup>1</sup> Bank Height Ratio	1	1	1	1	0	3	1	1	1	1	0	3	1	1	1	1	0	3																		
<b>Profile</b>																																				
Riffle Length (ft)	13.69	88.32	82.84	173.90	51.83	14	15.63	69.32	55.40	193.19	46.86	15	21.13	51.68	46.23	82.17	21.21	17																		
Riffle Slope (ft/ft)	0.000	0.002	0.001	0.006	0.002	14	0.000	0.003	0.003	0.012	0.003	15	0.000	0.001	0.001	0.004	0.001	17																		
Pool Length (ft)	11.36	24.52	24.15	46.88	8.60	19	12.78	38.13	38.35	90.91	20.95	19	5.61	32.08	28.41	81.70	19.25	25																		
Pool Max Depth (ft)	2.11	2.99	2.86	4.33	0.72	19	2.76	4.00	4.34	5.39	0.79	19	2.32	3.29	3.13	5.22	0.72	25																		
Pool Spacing (ft)	22.73	95.81	94.46	180.40	41.64	18	12.78	91.39	88.78	217.34	59.08	18	10.02	67.33	65.93	125.74	36.64	24																		
<b>Pattern</b>																																				
Channel Beltwidth (ft)																																				
Radius of Curvature (ft)																																				
Rc:Bankfull Width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
<b>Additional Reach Parameters</b>																																				
Rosgen Classification				B5c						B5c						B5c/E5																				
Channel Thalweg length (ft)				1727						1764						1765																				
Sinuosity (ft)				1.03						1.05						1.05																				
Water Surface Slope (Channel) (ft/ft)				0.00166						0.0016						0.0016																				
BF slope (ft/ft)				0.0024						0.00263						0.0019																				
<sup>3</sup> Ri% / P%				73% / 27%						59% / 41%						52% / 48%																				
<sup>3</sup> SC% / Sa% / G% / C% / B% / Be%																																				
<sup>3</sup> d16 / d35 / d50 / d84 / d95																																				
<sup>2</sup> % of Reach with Eroding Banks																																				
Channel Stability or Habitat Metric																																				
Biological or Other																																				

Shaded cells indicate that these will typically not be filled in.

<sup>1</sup> = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile.

<sup>2</sup> = Proportion of reach exhibiting banks that are eroding based on the visual survey from visual assessment table

<sup>3</sup> = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave

**Table 12.2 Monitoring Data - Stream Reach Data Summary**  
**Adkin Branch Stream Restoration Project - Phase I - Contract No. 070708001**  
**Reach 2 (Caswell St. to Lincoln St.)**

Parameter	Baseline					MY-1					MY-2					MY-3					MY-4					MY-5										
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n
<b>Dimension and substrate - Riffle only</b>																																				
Bankfull Width (ft)	16.23	16.98	16.81	17.91	0.85	3	15.69	16.52	16.15	17.72	1.06	3	16.32	18.70	17.96	21.82	2.82	3																		
Floodprone Width (ft)	48.33	52.40	51.29	57.58	4.72	3	51.64	57.52	56.70	64.23	6.34	3	55.58	58.84	56.68	64.27	4.73	3																		
Bankfull Mean Depth (ft)	1.46	1.66	1.64	1.88	0.21	3	1.61	2.16	2.01	2.85	0.63	3	2.23	2.46	2.35	2.81	0.31	3																		
Bankfull Max Depth (ft)	2.21	2.38	2.26	2.68	0.26	3	2.60	3.23	2.84	4.26	0.90	3	3.07	3.34	3.08	3.87	0.46	3																		
Bankfull Cross Sectional Area (ft <sup>2</sup> )	23.68	28.32	27.58	33.70	5.05	3	28.48	35.34	31.55	45.98	9.34	3	38.34	46.58	40.05	61.35	12.82	3																		
Width/Depth Ratio	9.53	10.30	10.25	11.12	0.80	3	5.67	8.16	7.81	11.01	2.69	3	6.94	7.59	7.77	8.05	0.58	3																		
Entrenchment Ratio	2.99	3.09	3.05	3.22	0.12	3	2.91	3.50	3.61	3.98	0.54	3	2.95	3.17	3.16	3.41	0.23	3																		
Bank Height Ratio	1	1	1	1	0	3	1	1	1	1	0	3	1	1	1	1	0	3																		
<b>Profile</b>																																				
Riffle Length (ft)	27.43	62.71	62.38	93.27	19.56	10	5.23	34.74	35.95	61.27	16.12	11	14.79	33.08	24.52	69.01	16.99	18																		
Riffle Slope (ft/ft)	0.0002	0.0013	0.0010	0.0039	0.0013	10	0.0003	0.0029	0.0015	0.0132	0.0039	11	0.000	0.003	0.002	0.008	0.002	18																		
Pool Length (ft)	14.20	56.38	56.82	113.64	27.38	39	7.56	65.31	61.25	157.78	33.20	45	15.05	42.46	40.28	85.81	17.24	45																		
Pool Max Depth (ft)	2.74	4.23	4.22	6.48	0.76	39	2.60	4.80	4.97	6.54	0.89	45	2.00	4.39	4.40	6.61	1.01	45																		
Pool Spacing (ft)	17.05	73.45	69.60	164.78	32.96	38	11.36	63.92	56.82	139.21	28.40	44	25.91	67.24	67.02	130.53	23.07	44																		
<b>Pattern</b>																																				
Channel Beltwidth (ft)																																				
Radius of Curvature (ft)																																				
Re:Bankfull Width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
<b>Additional Reach Parameters</b>																																				
Rosgen Classification	B5c					B5c					B5c/E5																									
Channel Thalweg length (ft)	3096					3131					3105																									
Sinuosity (ft)	1.04					1.04					1.04																									
Water Surface Slope (Channel) (ft/ft)	0.0016					0.00175					0.0016																									
BF slope (ft/ft)	0.0018					0.00204					0.0017																									
<sup>a</sup> Ri% / P%	29% / 71%					5% / 95%					24% / 76%																									
<sup>3</sup> SC% / Sa% / G% / C% / B% / Be%																																				
<sup>3</sup> d16 / d35 / d50 / d84 / d95																																				
<sup>2</sup> % of Reach with Eroding Banks																																				
Channel Stability or Habitat Metric																																				
Biological or Other																																				

Shaded cells indicate that these will typically not be filled in.

\* Reach 2 is a predominately pool system due to need to drop grade at the lower end of the project.

1 = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile.

2 = Proportion of reach exhibiting banks that are eroding based on the visual survey from visual assessment table

3 = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave







## Appendix E. Hydrologic Data

**Table 13. Verification of Bankfull Events**

Date	Crest Gauge Info		Gauge Reading (ft)	Gauge Elevation (ft)	Crest Elevation (ft)	Bankfull Elevation (ft)	Height above Bankfull (ft)	Photo
	Site	Sta.						
11/8/2012	1	54+00	4.0	25.27	29.27	27.03	2.24	6.1 & 6.2



**Figures 6.1 & 6.2 Crest Gauge Photos**



## Appendix F. Credit Calculation Figures


Figure D.1 – D.5, Credit Calculation Figures





**LEGEND**



- E— EASEMENT BOUNDARY
- AS-BUILT TOP OF BANK
- ◻ < 50' BUFFER (0 RIPARIAN BUFFER OR NUTRIENT OFFSET BUFFER CREDIT)
- ◻ 50' BUFFER
- ◻ 50' – 200' BUFFER
- ◻ SEWER EASEMENT
- ◻ DITCH BUFFER CREDIT DEDUCTION
- ◻ VEGETATION PLOT

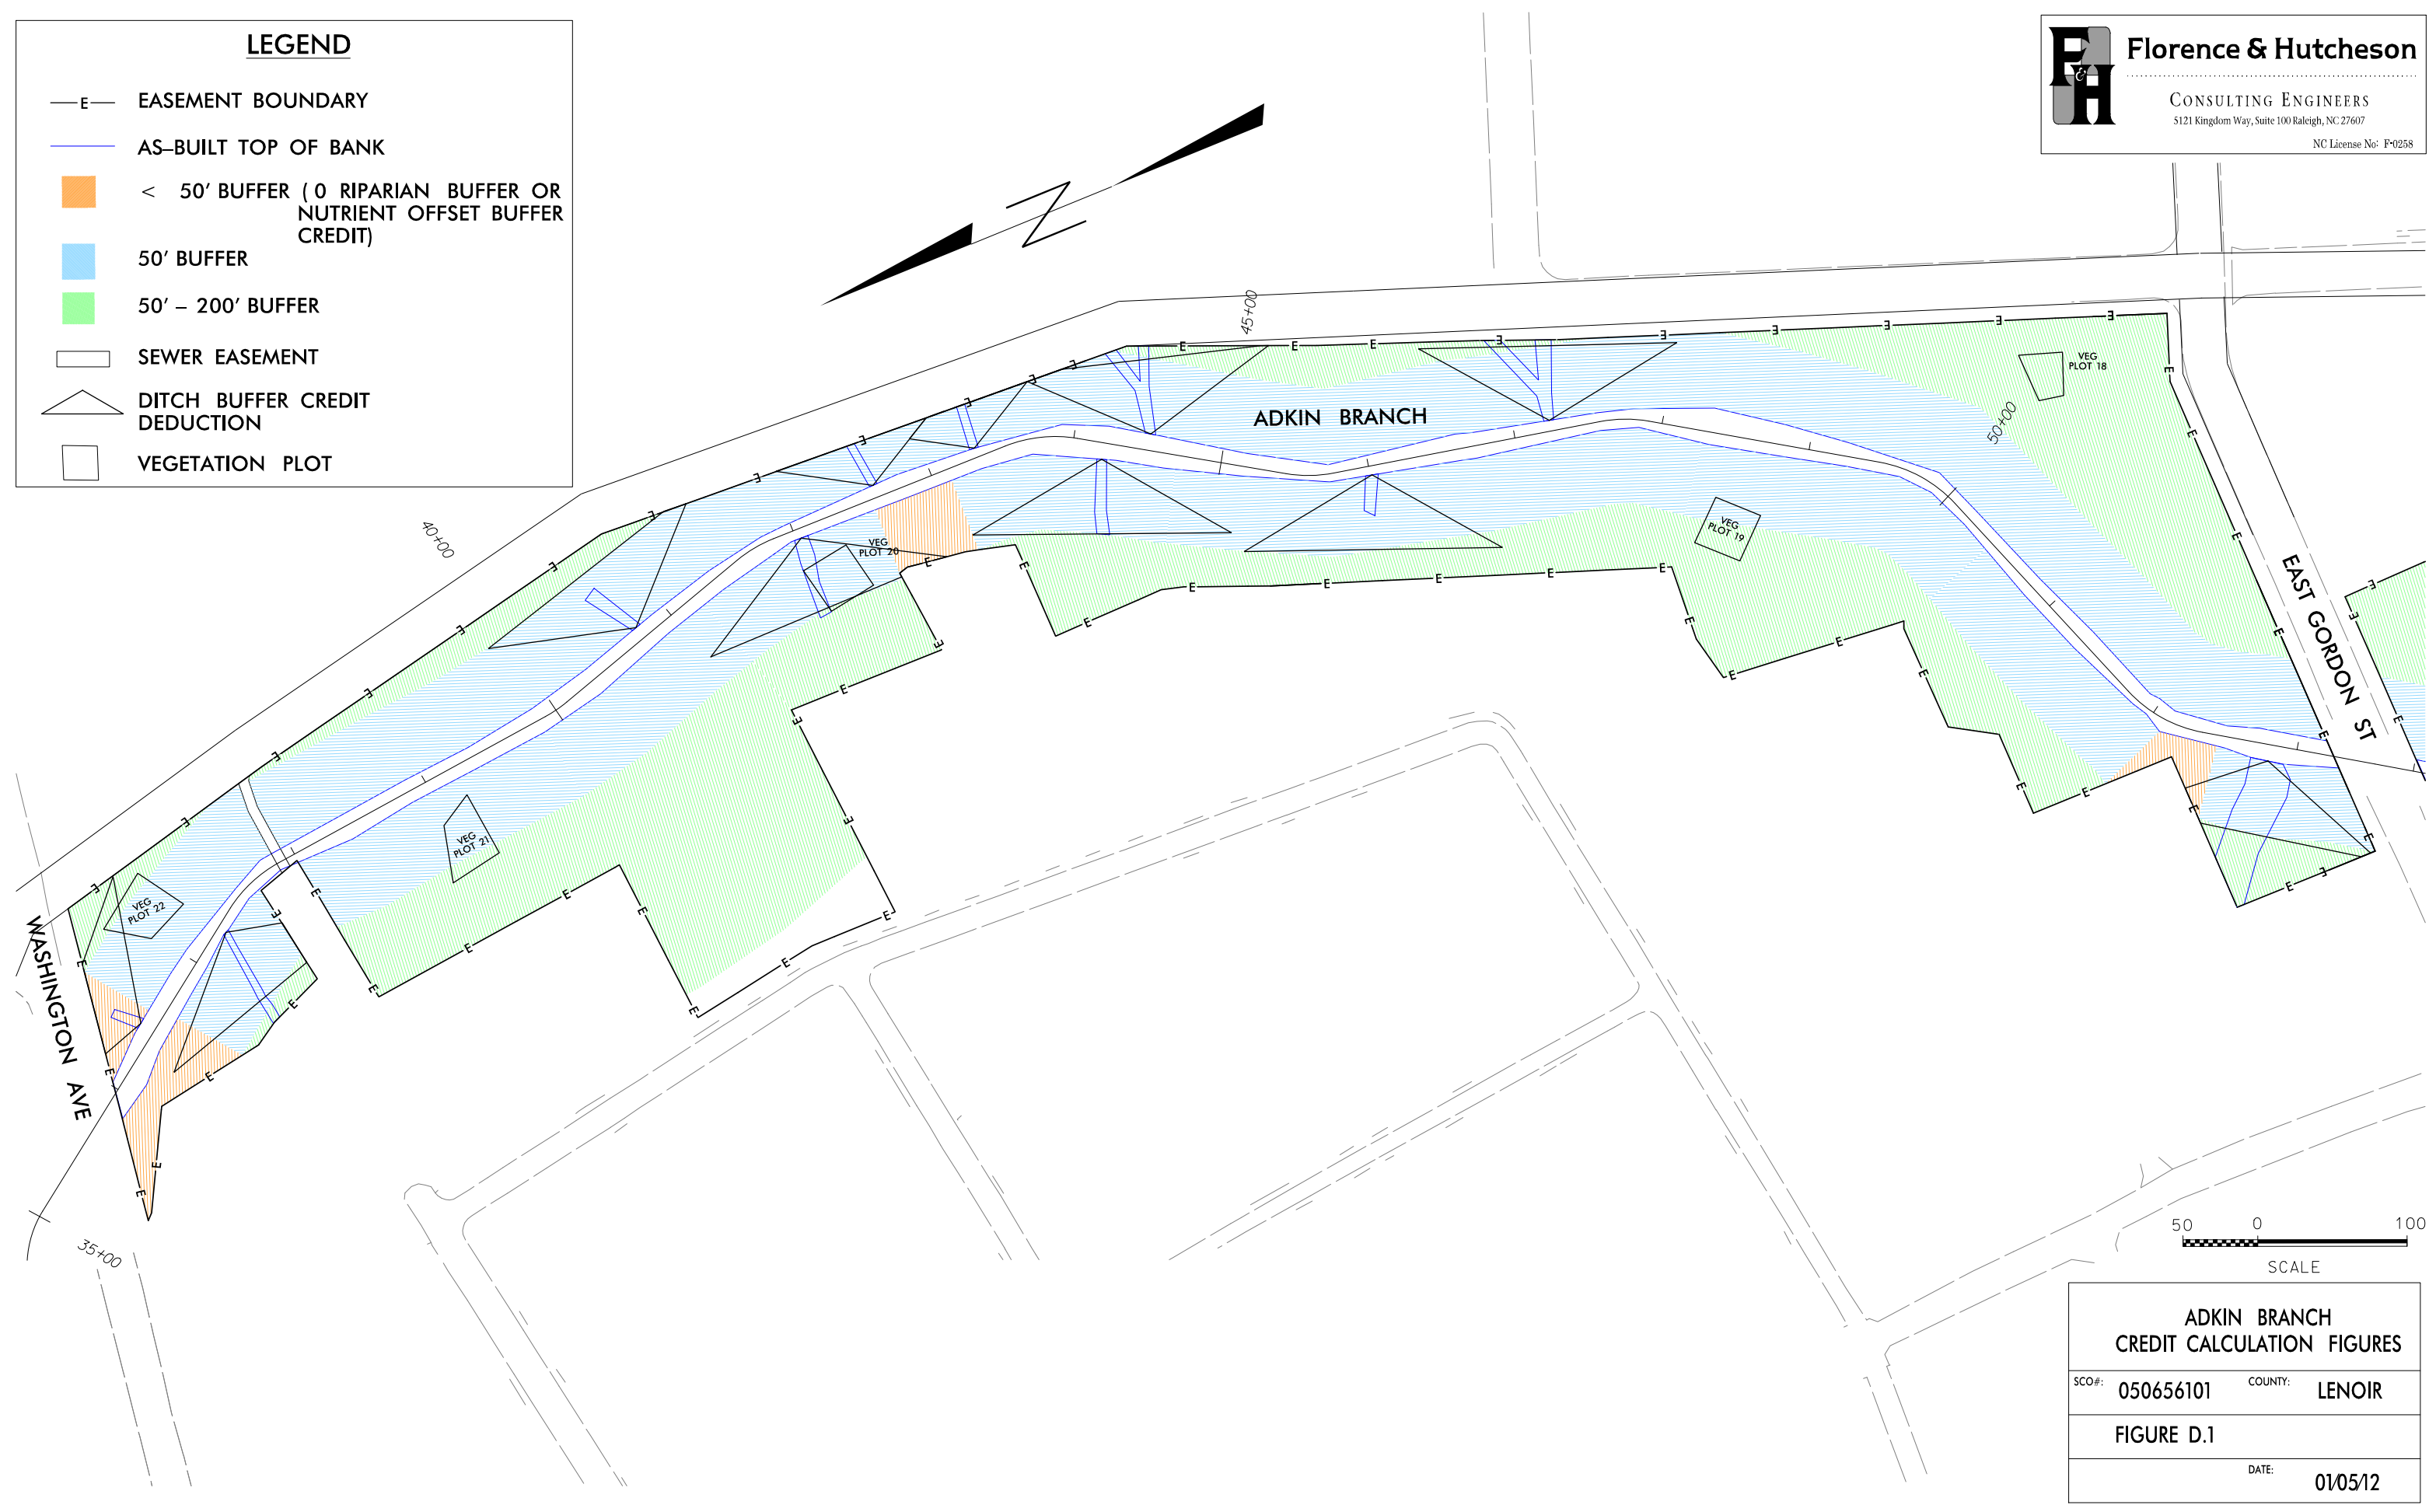

<b>ADKIN BRANCH CREDIT CALCULATION FIGURES</b>	
SCO#: 050656101	COUNTY: LENOIR
<b>FIGURE D.1</b>	
DATE: 01/05/12	

**LEGEND**




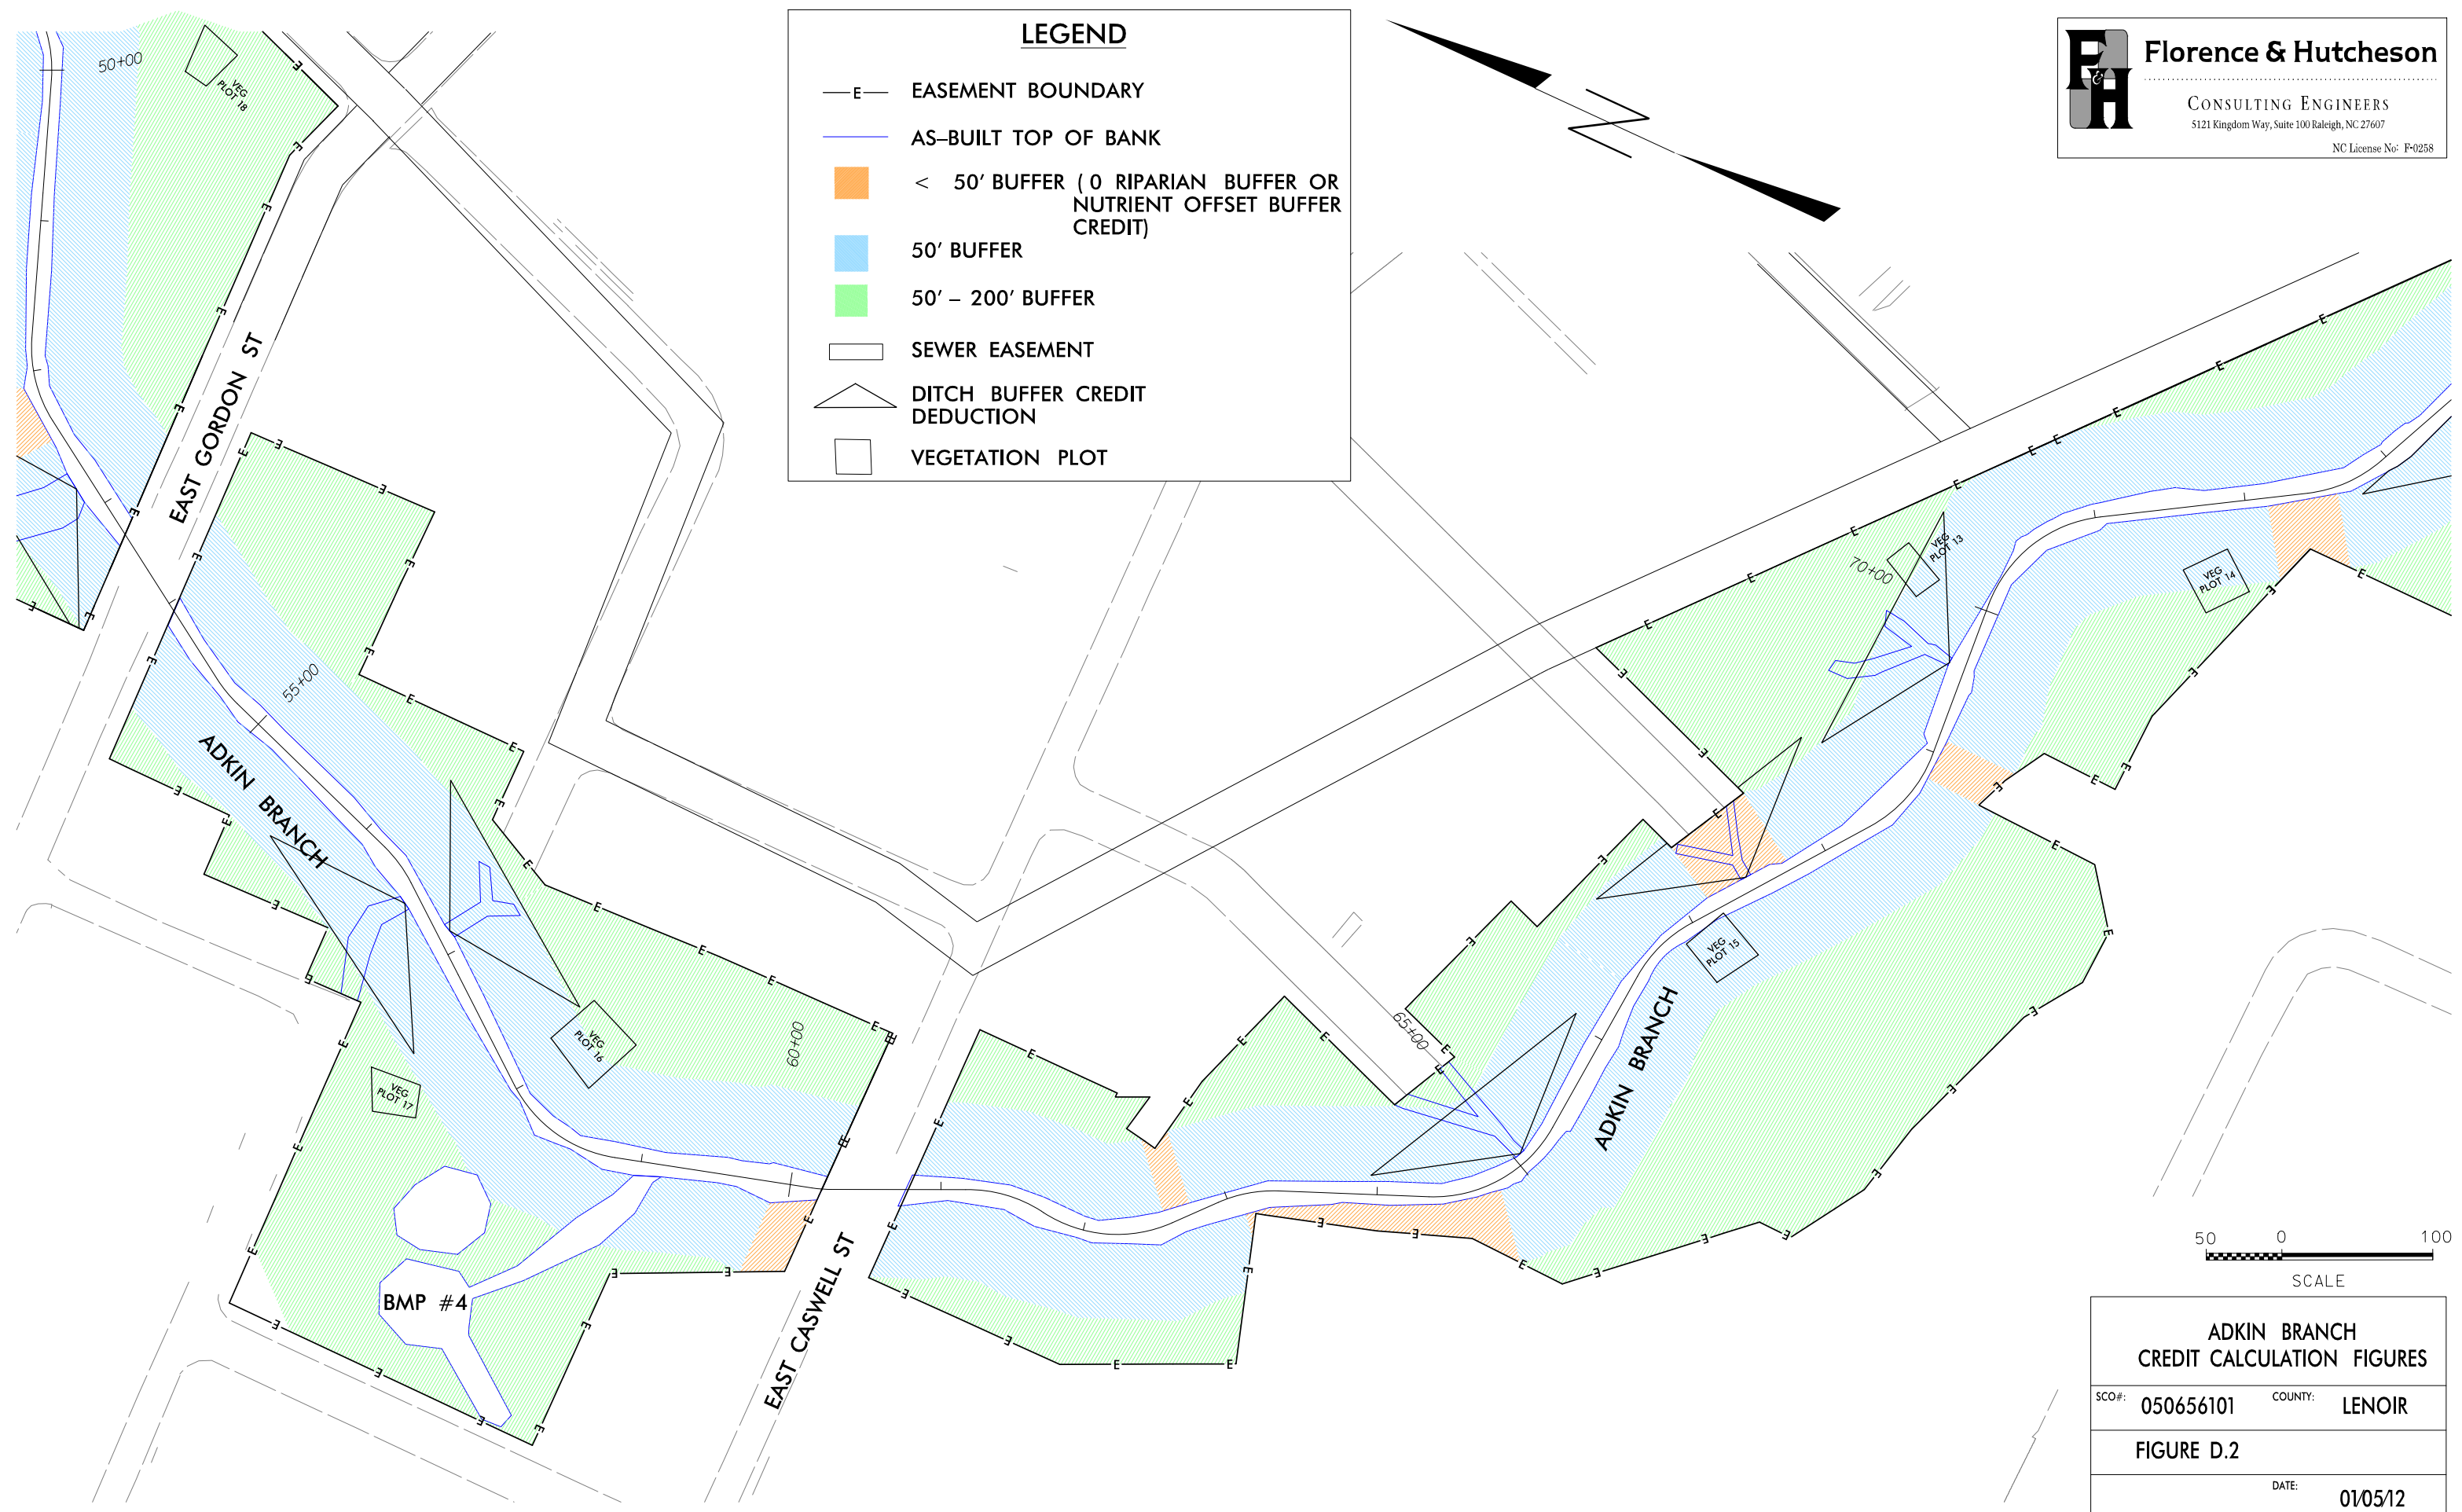




- EASEMENT BOUNDARY
- AS-BUILT TOP OF BANK
- < 50' BUFFER (0 RIPARIAN BUFFER OR NUTRIENT OFFSET BUFFER CREDIT)
- 50' BUFFER
- 50' - 200' BUFFER
- SEWER EASEMENT
- DITCH BUFFER CREDIT DEDUCTION
- VEGETATION PLOT




ADKIN BRANCH CREDIT CALCULATION FIGURES	
SCO#: 050656101	COUNTY: LENOIR
FIGURE D.2	
DATE: 01/05/12	





**LEGEND**

-  EASEMENT BOUNDARY
-  AS-BUILT TOP OF BANK
-  < 50' BUFFER (0 RIPARIAN BUFFER OR NUTRIENT OFFSET BUFFER CREDIT)
-  50' BUFFER
-  50' - 200' BUFFER
-  SEWER EASEMENT
-  DITCH BUFFER CREDIT DEDUCTION
-  VEGETATION PLOT

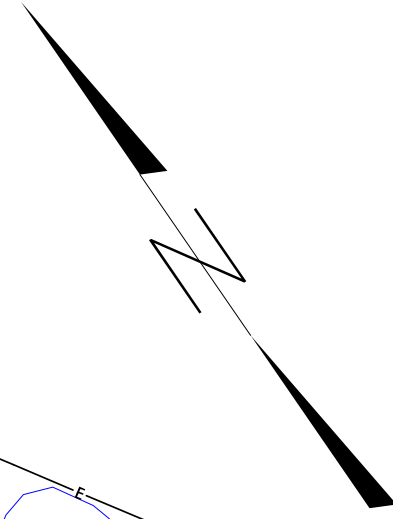

ADKIN BRANCH CREDIT CALCULATION FIGURES	
SCO#: 050656101	COUNTY: LENOIR
FIGURE D.3	
DATE: 01/05/12	

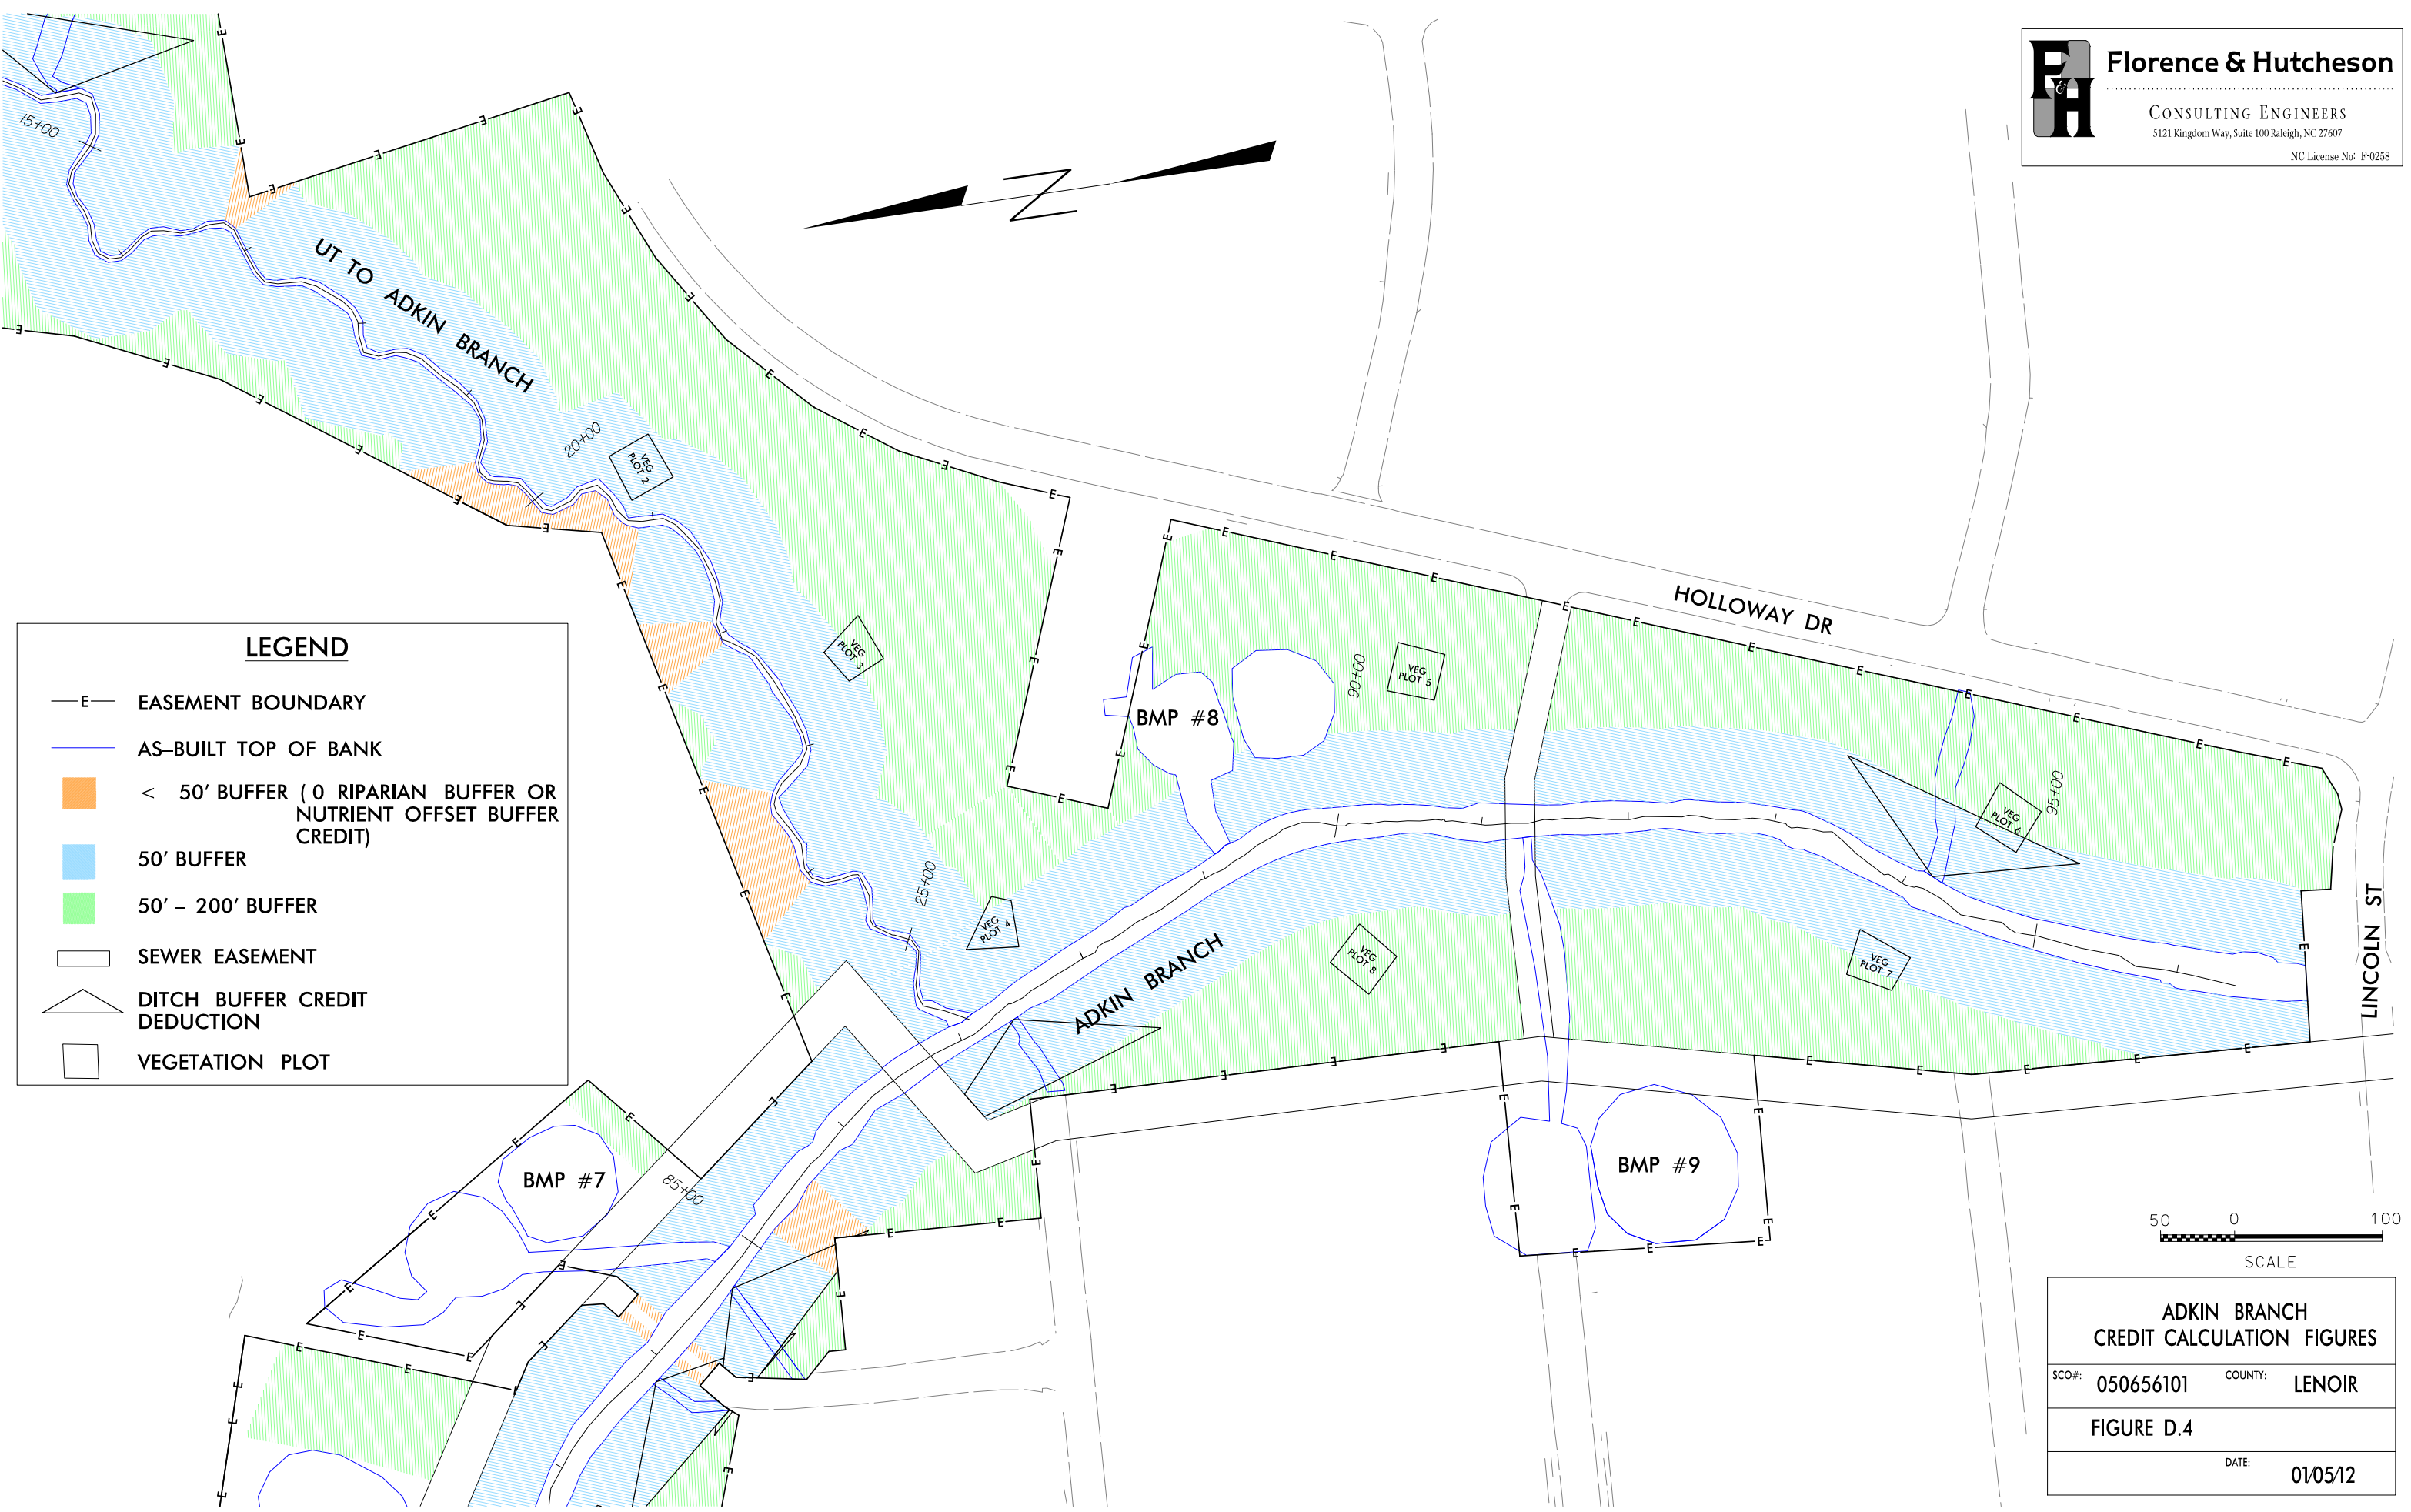



**LEGEND**

- EASEMENT BOUNDARY
- AS-BUILT TOP OF BANK
- < 50' BUFFER (0 RIPARIAN BUFFER OR NUTRIENT OFFSET BUFFER CREDIT)
- 50' BUFFER
- 50' - 200' BUFFER
- SEWER EASEMENT
- DITCH BUFFER CREDIT DEDUCTION
- VEGETATION PLOT




<b>ADKIN BRANCH CREDIT CALCULATION FIGURES</b>	
SCO#: 050656101	COUNTY: LENOIR
<b>FIGURE D.4</b>	
DATE: 01/05/12	



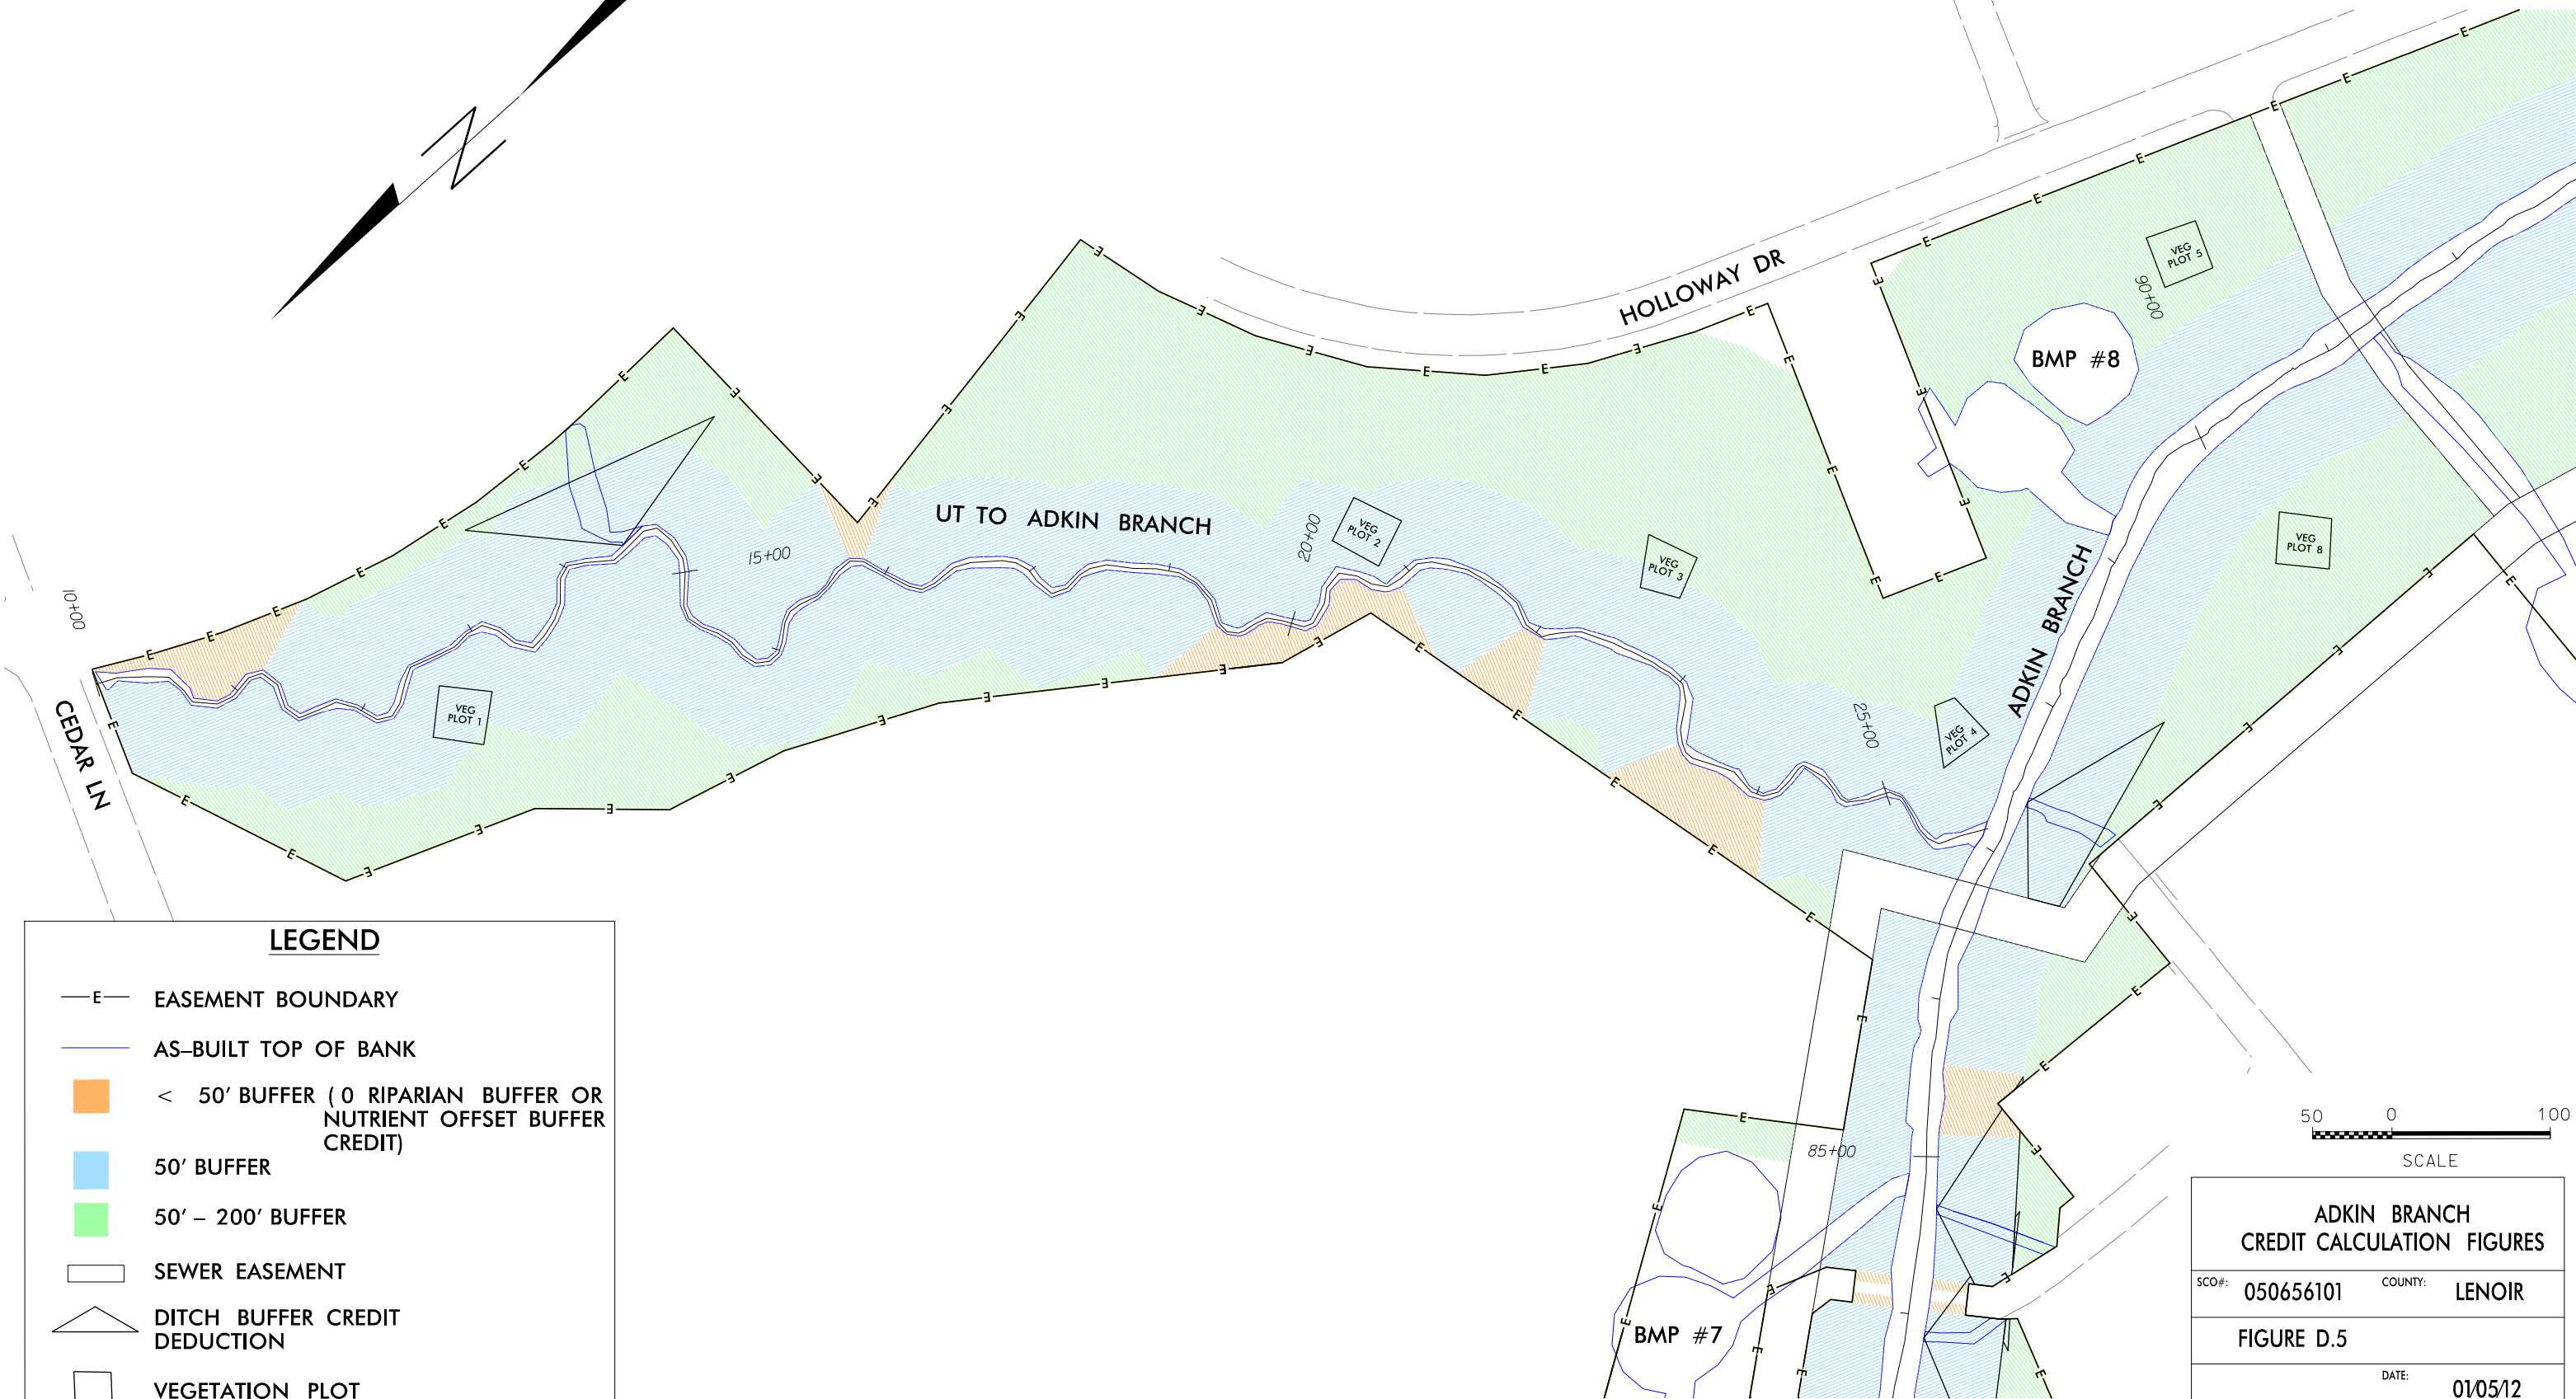

**LEGEND**

- EASEMENT BOUNDARY
- AS-BUILT TOP OF BANK
- < 50' BUFFER (0 RIPARIAN BUFFER OR NUTRIENT OFFSET BUFFER CREDIT)
- 50' BUFFER
- 50' - 200' BUFFER
- SEWER EASEMENT
- DITCH BUFFER CREDIT DEDUCTION
- VEGETATION PLOT



<b>ADKIN BRANCH CREDIT CALCULATION FIGURES</b>	
SCO#: 050656101	COUNTY: LENOIR
<b>FIGURE D.5</b>	
DATE: 01/05/12	
