



MONITORING YEAR 3 ANNUAL REPORT

Final

AGONY ACRES MITIGATION SITE

Guilford County, NC

NCDEQ Contract 004949

DMS Project Number 95716

USACE Action ID Number 2012-1909

NCDWR Project Number 13-1305

Data Collection Period: March 2017 – October 2017

Draft Submission Date: November 21, 2017

Final Submission Date: January 5, 2018

PREPARED FOR:



NC Department of Environmental Quality Division of Mitigation Services

1652 Mail Service Center

Raleigh, NC 27699-1652



January 5, 2018

Jeff Schaffer
N.C. Division of Mitigation Services
1652 Mail Service Center
Raleigh, NC 27699-1652

RECEIVED

JAN 05 2017

DIVISION OF
MITIGATION SERVICES

RE: Draft Monitoring Year 3 Report for Agony Acres Mitigation Site (95716)
Cape Fear River Basin (03030002)
Guilford County, North Carolina
Contract No. 004949

Dear Mr. Schaffer,

We have reviewed the comments on the Monitoring Year 3 Report for the above referenced project dated December 22, 2017 and have revised the report based on these comments. The revised documents are submitted with this letter. Below are responses to each of your comments. For your convenience, the comments are reprinted with our response in italics.

- 1) The digital data and drawings have been reviewed and determined to meet DMS requirements. However, DMS is calling to your attention that while Wildlands did provide reach breakdowns and mitigation approaches for each reach, in future submittals, please provide the reach lengths and acreages/square footage for buffer assets as required by contract and stated in DMS's Format, Data Requirements, and Content Guidance for Electronic Drawings Submitted to EEP version 1.0 (03/27/08).

GIS files have been submitted with stream reach lengths, and acreages and square feet for buffer assets.

- 2) Add the USACE Action ID number (2012-1909) and NCDWR Project number (13-1305) to the cover page.

The USACE Action ID number and NCDWR Project number have been added to the cover page.

- 3) Section 1.2.1: In this section, you state that "At the end of MY2 a supplemental planting was performed in an area along Reedy Fork that was determined to have low stem densities during MY2." The report goes on to state both in this section and Table 9 that, "Plot 10 had a planted stem density of 242 stems per acre." Please explain why Plot 10 is not meeting, and in fact has fewer planted stems, after a supplemental planting effort.

An explanation was added as to why vegetation plot 10 still has a low stem density after supplemental planting was performed.

- 4) Section 1.2.6, page 5: the following should be included in the Maintenance Plan discussion:



- a. Plot 10 still has low planted stem density despite a supplemental planting effort which may necessitate an additional supplemental plant.

This statement was added to section 1.2.6.

- b. The treatment of tree of heaven, the subsequent re-sprouting that has occurred and the continued monitoring and treatment as needed.

The treatment of tree of heaven was added to section 1.2.6.

5) Appendix 1:

- a. Table 1: Revise the note at the bottom to read "Credit calculations were originally calculated along the as-built thalweg and updated to be calculated along stream centerlines as stated in the approved Mitigation Plan for Monitoring Year 3 after discussions with NC IRT."

The note at the bottom of Table 1 has been revised.

- b. Table 4: Verify the linear footage of UT1A. DMS calculated 2,278 linear feet for this reach.

The linear footage was change to 2,278.

- 6) Appendix 2, Table 6: Given the low stem density in veg. plot 10, DMS expected to see this reflected in Table 6, especially since Wildlands did show it for the low stem density in the vicinity of plot 10 in MY 2. Please explain or update Table 6.

The CCPV Map has been updated to show an area of low stem density around vegetation plot 10, and the area has been added to Table 6.

- 7) Appendix 4: For any morphological tables, provide a footnote with the tables that describes the method by which Wildlands is calculating Bank Height Ratio and Entrenchment Ratio. In addition, please provide context to any observed changes in these calculated ratios in the report narrative. DMS has proposed a method for these calculations that can be found in the As Built baseline template guidance AS-built Baseline Monitoring Report – June 2017 Page 22, specifically the paragraphs 8 and 9.

A footnote was added to morphological tables in Appendix 4 describing the method used to calculate Bank Height Ratio, and Entrenchment Ratio.

- 8) Based upon the change in credit calculations directed by the IRT, the total SMUs determined by DMS are 9 SMU below the contracted amount of 6,488 SMUs, therefore the contract value would need to be reduced \$3,015.00 from \$2,441,312.00 to \$2,325,465.00 based on the shortfall of SMUs. To reconcile the overpayment for Task 1 through 8 resulting from the 9 SMU shortfall, please adjust the Task 9 payment downward to a revised amount of \$35,180.35. The remaining future milestone invoice amounts will be revised.

The task 9 payment has been adjusted to reflect a decrease of 9 SMUs.



If you have any questions, please contact me by phone (919) 851-9986, or by email (jlorch@wildlandseng.com).

Sincerely,

A handwritten signature in black ink, appearing to read "Jason Lorch".

Jason Lorch, *Monitoring Coordinator*

PREPARED BY:



Wildlands Engineering, Inc.
312 West Millbrook Road, Suite 225
Raleigh, NC 27609

Jason Lorch
jlorch@wildlandseng.com
Phone: 919.851.9986

EXECUTIVE SUMMARY

Wildlands Engineering, Inc. (Wildlands) completed a full delivery project at the Agony Acres Mitigation Site (Site) for the North Carolina Division of Mitigation Services (DMS) to restore, enhance, and preserve a total of 9,078 linear feet (LF) of perennial and intermittent stream in Guilford County, NC. The Site provides 6,479 Stream Mitigation Units (SMUs) and 3.0 Buffer Mitigation Units (BMUs). The Site is located in the Reedy Fork Watershed within Cape Fear River Basin Hydrologic Unit Code (HUC) 03030002 (Cape Fear 02) near Ossipee, NC (Figure 1). The streams are all unnamed tributaries (UT) to Reedy Fork and are referred to herein as UT1, UT1A, UT1B, and UT2. The Site also includes 3.0 acres of riparian buffer restoration along Reedy Fork and UT1.

The Site is located within the Jordan Lake Water Supply Watershed which has been designated as a Nutrient Sensitive Water. The Site's watershed is within Cape Fear local watershed HUC 03030002020070, which was not identified as a Cape Fear 02 Targeted Local Watershed (TLW) in DMS's 2009 Cape Fear River Basin Restoration Priority (RBRP) plan; however, this local watershed was later designated as a Targeted Resource Area (TRA) in the 2011 Request for Proposals (RFP) in the Cape Fear 02. The Agony Acres Mitigation Site fully supports the Cataloging Unit (CU)-wide functional objectives stated in the 2011 RFP to reduce and control nutrient inputs, reduce and control sediment inputs, and protect and augment Significant Natural Heritage Areas in the Cape Fear 02 River Basin. The Site will contribute to meeting the CU-wide Functional Improvement Objectives by establishing the following project goals:

- Reduce sediment inputs by removing cattle from streams and restoring degraded and eroding stream channels;
- Return a network of streams to a stable form that is capable of supporting biological functions;
- Reduce fecal coliform, nitrogen, and phosphorous inputs through removing cattle from streams and establishing and augmenting a forested riparian corridor;
- Protect existing high quality streams and forested buffers; and
- Improve and protect hydrologic inputs to the adjacent Reedy Fork Aquatic Habitat Significant Natural Heritage Area.

The project is helping meet the goals for the watershed outlined in the RBRP and provides numerous ecological benefits within the Cape Fear River Basin. While many of these benefits are limited to the Agony Acres project area; others, such as pollutant removal, reduced sediment loading, and improved aquatic and terrestrial habitat, have farther-reaching effects.

Stream restoration and enhancement construction efforts were completed in September 2014. Baseline as-built monitoring activities (MY0) were completed between October and December 2014. A conservation easement is in place on 30.78 acres of stream and riparian corridors to protect them in perpetuity.

Monitoring Year 3 (MY3) assessment and site visits were completed between March and October 2017 to assess the conditions of the project. Overall, the Site has met the required vegetation, stream, and hydrology success criteria for MY3. The overall average stem density for the Site in MY3 is 503 stems per acre, which is greater than the 320 stems per acre density required for MY3. All restored and enhanced streams are stable and functioning as designed and have recorded multiple bankfull events. UT1B has two pressure transducers installed to monitor stream flow. Both stream gages on UT1B met the hydrologic criteria for MY3 (Appendix 5).

AGONY ACRES MITIGATION SITE
Monitoring Year 3 Annual Report

TABLE OF CONTENTS

Section 1: PROJECT OVERVIEW 1

 1.1 Project Goals and Objectives 2

 1.2 Monitoring Year 3 Data Assessment..... 3

 1.2.1 Vegetative Assessment 3

 1.2.2 Vegetation Areas of Concern 4

 1.2.3 Stream Assessment..... 4

 1.2.4 Stream Areas of Concern 4

 1.2.5 Hydrology Assessment..... 4

 1.2.6 Maintenance Plan 5

 1.3 Monitoring Year 3 Summary 5

Section 2: METHODOLOGY..... 6

Section 3: REFERENCES 7

APPENDICES

Appendix 1

General Tables and Figures

Figure 1 Project Vicinity Map

Figure 2 Project Component/ Asset Map

Table 1 Project Components and Mitigation Credits

Table 2 Project Activity and Reporting History

Table 3 Project Contact Table

Table 4 Project Information and Attributes

Appendix 2

Visual Assessment Data

Figures 3.0 - 3.3 Integrated Current Condition Plan View

Tables 5a-d Visual Stream Morphology Stability Assessment Table

Table 6 Vegetation Condition Assessment Table

Stream Photographs

Vegetation Photographs

Appendix 3

Vegetation Plot Data

Table 7 Vegetation Plot Criteria Attainment

Table 8 CVS Vegetation Plot Metadata

Table 9 Planted and Total Stem Counts

Appendix 4

Morphological Summary Data and Plots

Tables 10a-d Baseline Stream Data Summary

Table 11 Morphology and Hydraulic Summary (Dimensional Parameters – Cross Section)

Tables 12a-f Monitoring Data – Stream Reach Data Summary

Cross Section Plots

Reachwide and Cross Section Pebble Count Plots

Appendix 5

Hydrology Summary Data and Plots

Table 13 Verification of Bankfull Events

Monthly Rainfall Data

Stream Flow Gage Plots

Section 1: PROJECT OVERVIEW

The Agony Acres Mitigation Site (Site) is located in northeastern Guilford County, north of Gibsonville (Figure 1). From Gibsonville take NC 61 north 5.5 miles. Turn right on Sockwell Road and travel 1.4 miles. The project site is located north of Sockwell Road and is bound on the north by Reedy Fork. The Site is located in the Carolina Slate Belt of the Piedmont Physiographic Province. The project watershed is classified as approximately 65% managed herbaceous cover, 30% mixed upland hardwoods, 3% cultivated, 2% southern yellow pine, and the remaining 1% is low intensity development. The drainage area for the Agony Acres Mitigation Site is 358 acres.

The Site is located in the Reedy Fork Watershed within the Jordan Lake Water Supply Watershed which has been designated a Nutrient Sensitive Water. The project streams flow directly into Reedy Fork which flows into the Haw River and eventually into the Jordan Lake Reservoir. The Site's watershed is within Hydrologic Unit Code (HUC) 03030002020070 which was not identified as a Cape Fear 02 Targeted Local Watershed (TLW) in DMS's 2009 Cape Fear River Basin Restoration Priority (RBRP) plan; however, this HUC was later designated as a Targeted Resource Area (TRA) in the 2011 Request for Proposals (RFP) in the Cape Fear 02. The Site connects to Reedy Fork and three separate but connected Significant Natural Heritage areas. Reedy Fork Aquatic Habitat, Reedy Fork Slopes at NC 61, and Altamahaw Alluvial Forest are all listed on the NC Natural Heritage GIS database and are immediately adjacent to the Site. There are also records for several state threatened, special concern, and significantly rare mussel species in Reedy Fork.

North Carolina Division of Mitigation Services (DMS) completed a Local Watershed Plan (LWP) in 2008 on the HUC immediately downstream which begins at the confluence of Reedy Fork and the Haw River and includes Travis and Tickle Creeks. The Site is located less than one mile outside of the LWP area and has a very similar land use pattern. The 2008 Little Alamance, Travis, and Tickle Creeks LWP identified nutrient inputs from agriculture and stream bank erosion in altered reaches as major stressors within this TLW. The Site was identified as a stream and buffer restoration and cattle exclusion opportunity to improve water quality and buffers within the TRA.

The Site consists of four tributaries to Reedy Fork which are located within the North Carolina Division of Water Resources (NCDWR) subbasin 03-06-02 of the Cape Fear River Basin. The project stream reaches include UT1, UT1A, UT1B, and UT2.

Mitigation work within the Site included restoration, enhancement, and preservation of 9,078 linear feet (LF) of perennial and intermittent stream channel and 3.0 acres (ac) of riparian buffer restoration. The Site provides 6,479 Stream Mitigation Units (SMUs) and 3.0 Buffer Mitigation Units (BMUs). The stream areas were also planted with native vegetation to improve habitat and protect water quality.

The final mitigation plan was submitted and accepted by the DMS in March 2014. Construction activities were completed by Land Mechanic Designs, Inc. in September 2014. The planting was completed by Bruton Natural Systems, Inc. in December 2014. The baseline as-built survey was completed by Kee Mapping and Surveying, in October 2014. Annual monitoring will be conducted for seven years with the close-out anticipated to occur in 2022 given the success criteria are met. Appendix 1 provides more detailed project activity, history, contact information, directions, and watershed/site background information for this project.



1.1 Project Goals and Objectives

Prior to construction activities, the stream channels exhibited varying degrees of degradation across the Site. The Site was used as agricultural and pasture land and most of the buffers had been reduced to narrow corridors. Cattle had free access to the streams, which resulted in sporadic degraded stream banks and poor bed forms.

The restored stream channels on the Site were previously incised and overwidened in many locations, likely as a result of historic channelization. The alterations of the Site to promote cattle grazing and farming resulted in elimination of many of the ecological functions of this small stream complex. Specifically, functional losses at the Site included degraded aquatic habitat, altered hydrology (related to loss of floodplain connection and lowered water table), and a reduction of the quality and quantity of riparian wetland habitats and related water quality benefits. Ongoing bank erosion was also occurring at some locations due to high, overly steep banks, and lack of bank vegetation. Table 4 in Appendix 1 and Tables 10a-d in Appendix 4 present the pre-restoration conditions in detail.

The mitigation project is intended to provide numerous ecological benefits within the Cape Fear River Basin. While many of these benefits are limited to the Agony Acres Mitigation Site project area; others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Expected improvements to water quality and ecological processes are outlined below as project goals and objectives. These project goals were established and completed with careful consideration of goals and objectives that were described in the RBRP and to meet DMS's mitigation needs while maximizing the ecological and water quality uplift within the watershed.

The following project specific goals established in the Agony Acres Mitigation Plan (Wildlands, 2014) include:

- Reduce sediment inputs by removing cattle from streams and restoring degraded and eroding stream channels;
- Return a network of streams to a stable form that is capable of supporting biological functions important to sensitive species within and adjacent to the project site;
- Reduce fecal coliform, nitrogen, and phosphorous inputs through removing cattle from streams and establishing and augmenting a forested riparian corridor;
- Protect existing high quality streams and forested buffers that provide habitat important to sensitive species within and adjacent to the project site;
- Improve and protect hydrologic inputs to the adjacent Reedy Fork Aquatic Habitat Significant Natural Heritage Area; and
- Improve and protect hydrologic inputs to Reedy Fork, which is listed as impaired on the 2012 NC 303(d) list for impaired aquatic life and for elevated fecal coliform levels.

The project goals will be addressed through the following project objectives:

- On-site nutrient inputs were decreased by removing cattle from streams, re-establishing floodplain connectivity, and filtering on-site runoff through buffer zones. Off-site nutrient input will be absorbed on-site by filtering flood flows through restored floodplain areas, where flood flow will spread through native vegetation. Vegetation is expected to uptake excess nutrients.
- Stream bank erosion which contributes sediment load to the creeks was greatly reduced, if not eliminated, in the project area. Eroding stream banks were stabilized using bioengineering, natural channel design techniques, and grading to reduce bank angles and bank height. Storm flow containing grit and fine sediment is filtered through restored floodplain areas, where flow will spread through native vegetation. Spreading flood flows also reduces velocity and allows



sediment to settle out. Sediment transport capacity of restored reaches was improved so that capacity balances more closely to load. Sediment load reduction will be monitored through assessing bank stability with cross section surveys and visual assessment through photo documentation which serves as an accepted surrogate for direct turbidity measurements.

- Restored riffle/pool sequences promote aeration of water and create deep water zones, helping to lower water temperature. Establishment and maintenance of riparian buffers creates long-term shading of the channel flow to minimize thermal heating. Lower water temperatures will help maintain dissolved oxygen concentrations.
- In-stream structures were constructed to improve habitat diversity and trap detritus. Wood habitat structures were included in the stream as part of the restoration design. Such structures include log drops and rock structures that incorporate woody debris and native onsite rock.
- Adjacent buffer and riparian habitats were restored with native vegetation as part of the project. Native vegetation provides cover and food for terrestrial creatures. Native plant species were planted and invasive species treated. Eroding and unstable areas were stabilized with vegetation as part of this project.
- The restored land is protected in perpetuity through a conservation easement.

The design streams were restored to the appropriate form based on the surrounding landscape, climate, and natural vegetation communities but also with strong consideration to existing watershed conditions and trajectory. Specifically, the site design was developed to restore a small stream complex directly adjacent to Reedy Fork. Other key factors addressed in the design were to create stable habitats, improve riparian buffers, and restore the natural migration patterns for fish spawning. Figure 2 and Table 1 in Appendix 1 present the stream mitigation components for the Agony Acres Mitigation Site.

1.2 Monitoring Year 3 Data Assessment

Annual monitoring and quarterly site visits were conducted during MY3 to assess the condition of the project. The stream and buffer success criteria for the Site follow the approved success criteria presented in the Agony Acres Mitigation Plan (Wildlands, 2014).

1.2.1 Vegetative Assessment

Planted woody vegetation is being monitored in accordance with the guidelines and procedures developed by the Carolina Vegetation Survey-DMS Level 2 Protocol (Lee et al., 2006). A total of 16 vegetation plots were established during the baseline monitoring within the project easement areas. All of the plots were installed using a standard 10 meter by 10 meter plot. The final vegetative success criteria for the stream restoration and enhancement areas will be the survival of 210 planted stems per acre in the riparian corridor at the end of the required monitoring period (MY7). The interim measure of vegetative success will be the survival of at least 320 planted stems per acre at the end of the third monitoring year (MY3) and at least 260 stems per acre at the end of the fifth year of monitoring (MY5). Planted vegetation must average 10 feet in height in each plot at the end of the seventh year of monitoring. If this success criteria is met by MY5 and stem density is trending towards success (i.e., no less than 260 five year old stems per acre), monitoring of vegetation on the Site may be terminated provided written approval is provided by the United States Army Corps of Engineers in consultation with the NC Interagency Review Team. The final vegetative success criteria for the buffer restoration areas will be the survival of 320 planted stems per acre in the riparian corridor at the end of the required monitoring period (MY5). However, Wildlands plans to monitor these areas the same as the rest of the project for seven years and have the same success criteria of 210 stems per acre at the end of MY7.

At the end of MY2 a supplemental planting was performed in an area along Reedy Fork that was determined to have low stem densities during MY2. This one acre area was planted with 200 American

sycamore (*Platanus occidentalis*), 200 River Birch (*Betula nigra*), and 100 tulip poplar (*Liriodendron tulipifera*) bareroots. Unfortunately, the planting contractor planted the area upstream of vegetation plot 10 and did not replant vegetation plot 10 or the area downstream of it. This area may necessitate an additional planting in subsequent monitoring years. Refer to the Integrated Current Condition Plan View Map (CCPV) in Appendix 2 for the area of supplemental planting.

The MY3 vegetative survey was completed in August 2017. The 2017 vegetation monitoring resulted in an average stem density of 503 stems per acre, which is greater than the interim requirement of 320 stems per acre required at MY3, but approximately 23% less than the baseline density recorded at MY0. There is an average of 12 stems per plot which is a slight decrease from 13 stems per plot in MY2. All but one of the 16 plots are on track to meet the success criteria required for MY7 (Table 9, Appendix 3). Plot 10 had a planted stem density of 242 stems per acre. This plot will be monitored and supplemental planting will be performed as necessary. Refer to Appendix 2 for vegetation plot photographs and the vegetation condition assessment table and Appendix 3 for vegetation data tables.

1.2.2 Vegetation Areas of Concern

During MY2 tree of heaven (*Ailanthus altissima*) was observed growing sporadically in the easement downstream of the confluence of UT1 and UT1B (CCPV Figure 3.1, Appendix 2). A chemical treatment was performed in this area to control the tree of heaven. While the amount of tree of heaven decreased from the treatment during MY2, some re-sprouting occurred. Re-sprouts were either removed by hand, or cut and stem treated with glyphosate during MY3. This area will continue to be monitored for new seedlings and will be treated with the appropriate herbicide as needed. Since portions of the adjacent land are an organic farm, spraying herbicide is prohibited along the active pasture or cropland. Any invasive plant species identified within this area will be hand pulled.

Japanese hops (*Humulus japonicus*) was observed growing in a portion of the buffer restoration area along Reedy Fork (Figure 3.3, CCPV). A pre-emergent herbicide with the active ingredient sulfometuron methyl will be used in mid-March 2018 to control Japanese hops. This herbicide should cause minimal or no damage to surrounding vegetation while effectively controlling Japanese hops. This area will continue to be monitored for new growth and will be treated with the appropriate herbicide as needed.

1.2.3 Stream Assessment

Morphological surveys for the MY3 were conducted in April 2017. All streams within the Site are stable with little to no erosion and have met the success criteria for MY3. While there have been some minor post-construction adjustments within the restored channels; the cross sections show little to no change in the bankfull area, maximum depth, or width-to-depth ratio. Surveyed riffle cross sections fell within the parameters defined for channels of the appropriate Rosgen stream type. Pebble counts indicated coarser materials in the riffle features and finer particles in the pool features.

Longitudinal profile surveys are not required on the project unless visual inspection indicates reach wide vertical stability concerns. Refer to Appendix 2 for the visual stability assessment table, CCPV Map, and reference photographs. Refer to Appendix 4 for the morphological data and plots.

1.2.4 Stream Areas of Concern

No stream areas of concern were identified during MY3.

1.2.5 Hydrology Assessment

Two bankfull flow events within separate years must be documented on the restoration and enhancement reaches within the seven-year monitoring period. In addition, the presence of baseflow

must be documented along portions of UT1B constructed with a Priority I restoration approach. Baseflow must be present for at least some portion of the year (most likely in the winter/early spring) during years with normal rainfall conditions.

Multiple bankfull events were recorded during MY3 at the Site. UT1B and UT1 each showed four bankfull events and UT1A and UT2 each recorded three bankfull events. During MY1 and MY2, each stream recorded at least one bankfull event. Therefore, the Site has met the bankfull stream hydrology criteria.

Baseflow was documented in UT1B for all of MY3 with the exception of several short periods during the Fall. UT1B has met baseflow criteria for MY1, MY2, and MY3. Refer to Appendix 5 for hydrologic data and graphs.

1.2.6 Maintenance Plan

The area along Reedy Fork with the invasive Japanese hops population will be treated in spring 2018 as described in section 1.2.2 above. Tree of heaven will continue to be monitored throughout the Site. Any new seedlings, or subsequent re-sprouting that may occur will be treated as necessary.

Vegetation plot 10 still has a low planted stem density despite supplemental planting efforts during MY2. This area may necessitate an additional supplemental planting during MY4.

1.3 Monitoring Year 3 Summary

Vegetation, stream, and hydrology criteria were met for MY3 on the Site. The average stem density for the Site is on track to meeting the MY7 success criteria; with all but one individual vegetation plot meeting the MY3 success criteria as noted in the CCPV Map. All streams within the Site are stable and functioning as designed. All streams on the Site have recorded bankfull events and UT1B has met the baseflow success criteria. Therefore, the hydrological success criteria has been met for MY3.

Summary information and data related to the performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Mitigation Plan documents available on DMS's website. All raw data supporting the tables and figures in the appendices are available from DMS upon request.

Section 2: METHODOLOGY

Geomorphic data was collected following the standards outlined in *The Stream Channel Reference Site: An Illustrated Guide to Field Techniques* (Harrelson et al., 1994) and in *Stream Restoration: A Natural Channel Design Handbook* (Doll et al., 2003). All Integrated Current Condition Plan View Mapping was recorded using a Trimble handheld GPS with sub-meter accuracy and processed using Pathfinder and ArcView. Crest gages were installed in surveyed riffle cross sections and monitored quarterly. Hydrology attainment installation and monitoring methods are in accordance with the USACE (USACE, 2003) standards. Vegetation monitoring protocols followed the Carolina Vegetation Survey-DMS Level 2 Protocol (Lee et al., 2006). Reporting follows the DMS Monitoring Report Template and Guidance Version 1.3 (DMS, 2010).



Section 3: REFERENCES

- Doll, B.A., Grabow, G.L., Hall, K.A., Halley, J., Harman, W.A., Jennings, G.D., and Wise, D.E. 2003. Stream Restoration A Natural Channel Design Handbook.
- Harrelson, Cheryl C; Rawlins, C.L.; Potyondy, John P. 1994. *Stream Channel Reference Sites: An Illustrated Guide to Field Technique*. Gen. Tech. Rep. RM-245. Fort Collins, CO: U.S. Department of Agriculture, Forest Service, Rocky Mountain Forest and Range Experiment Station. 61 p.
- Lee, Michael T., Peet, Robert K., Steven D., Wentworth, Thomas R. 2006. CVS-DMS Protocol for Recording Vegetation Version 4.0. Retrieved from <http://www.ncdms.net/business/monitoring/veg/datasheets.htm>.
- Multi-Resolution Land Characteristics Consortium (MRLC). 2001. National Land Cover Database. <http://www.mrlc.gov/nlcd.php>
- North Carolina Division of Water Resources (NCDWR). 2011. Surface Water Classifications. <http://portal.ncdeq.org/web/wq/ps/csu/classifications>
- North Carolina Division of Water Resources, 2005. Cape Fear River Basinwide Water Quality Plan. <http://h20.enr.state.nc.us/basinwide/draftCPFApril2005.htm>
- Rosgen, D. L. 1994. A classification of natural rivers. *Catena* 22:169-199.
- Rosgen, D.L. 1996. Applied River Morphology. Pagosa Springs, CO: Wildland Hydrology Books.
- United States Army Corps of Engineers (USACE), 2003. Stream Mitigation Guidelines. USACE, NCDEQ-DWR, USEPA, NCWRC.
- United States Geological Survey (USGS), 1998. North Carolina Geology. <http://www.geology.enr.state.nc.us/usgs/carolina.htm>
- Wildlands Engineering, Inc (2014). Agony Acres Mitigation Site Mitigation Plan. DMS, Raleigh, NC.



APPENDIX 1. General Tables and Figures


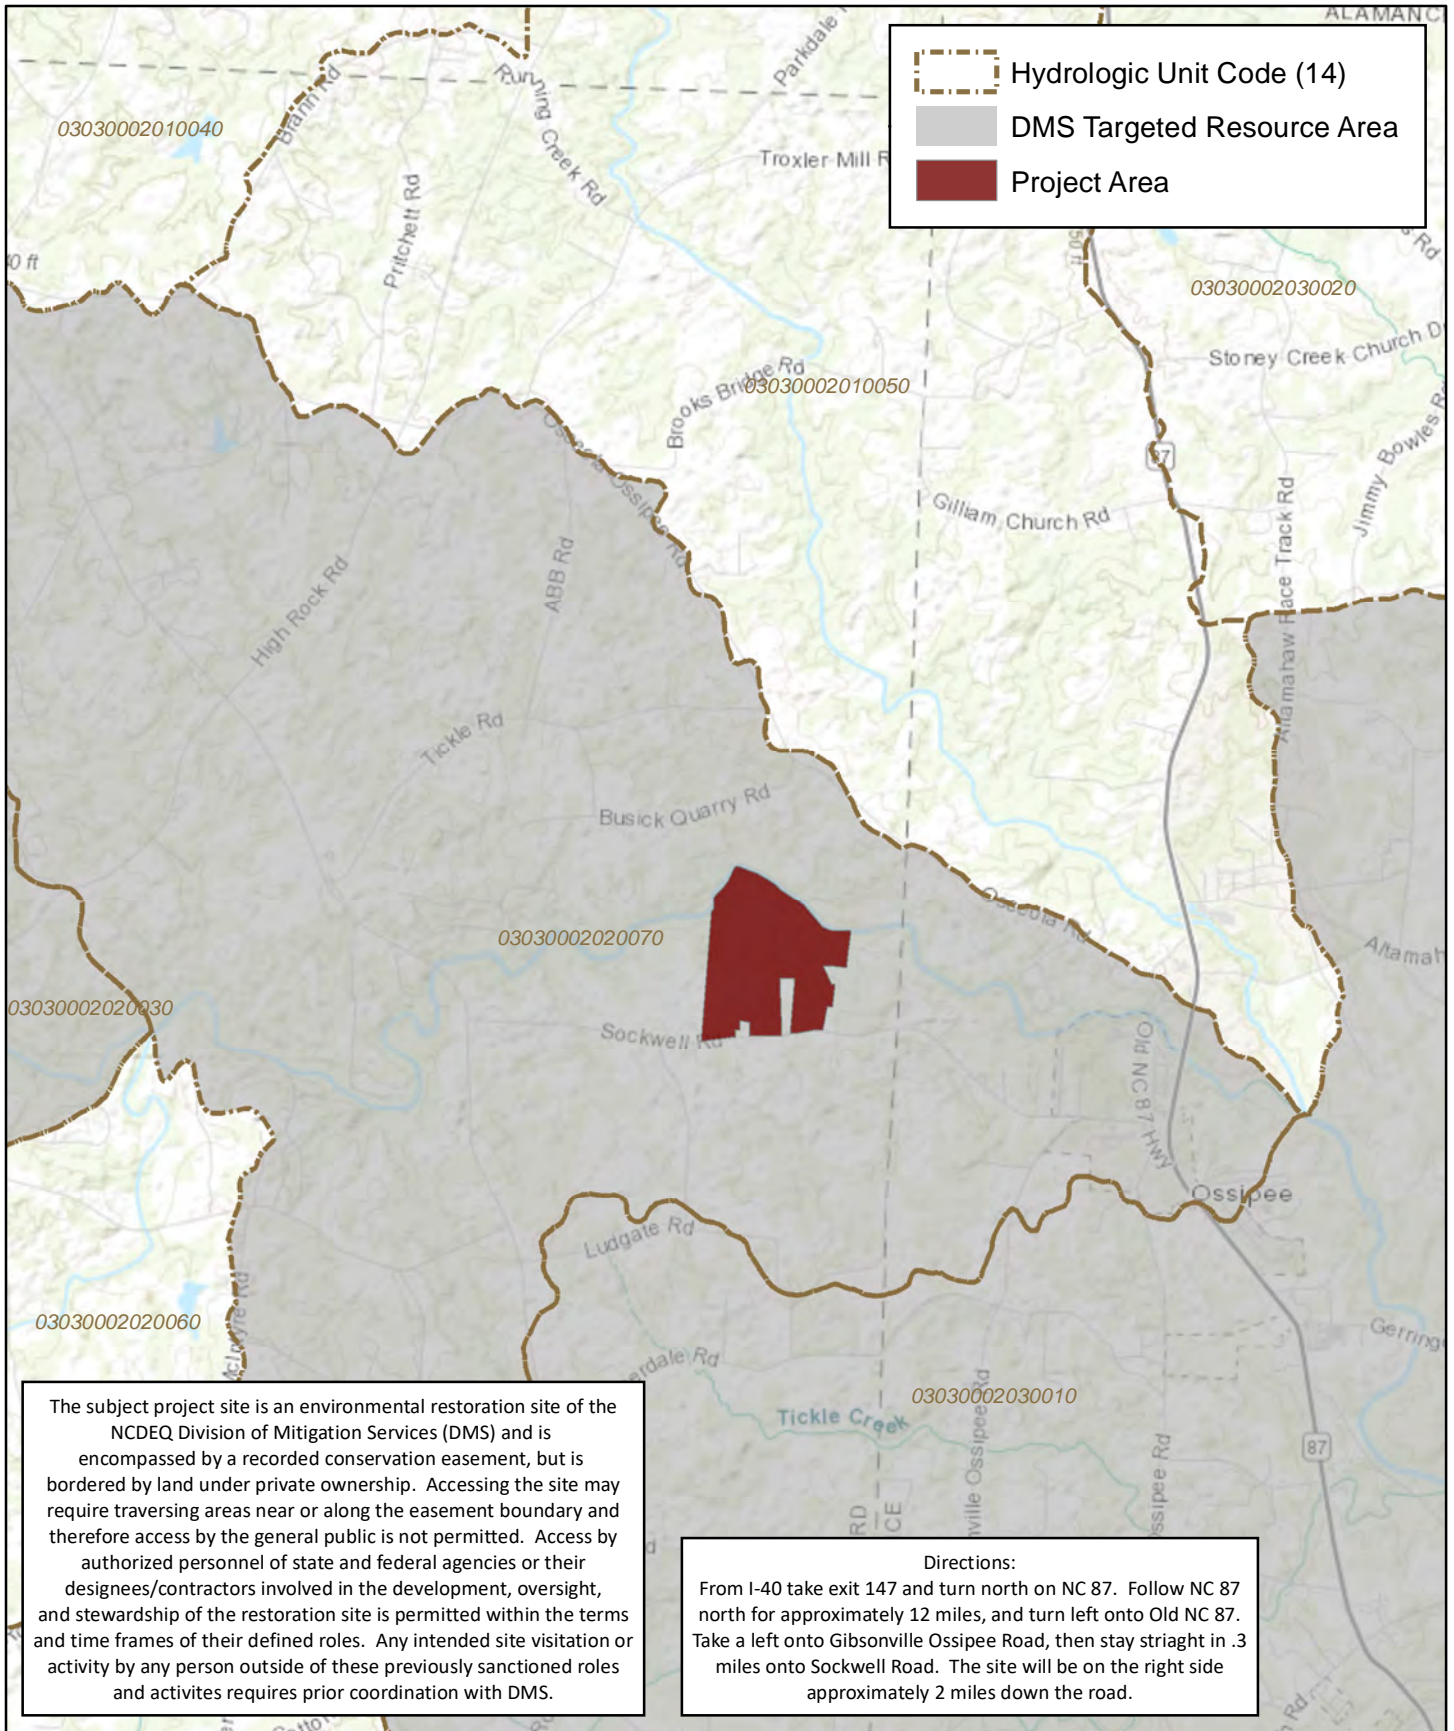


Figure 1 Project Vicinity Map
 Agony Acres Mitigation Site
 DMS Project No. 95716
 Monitoring Year 3 - 2017

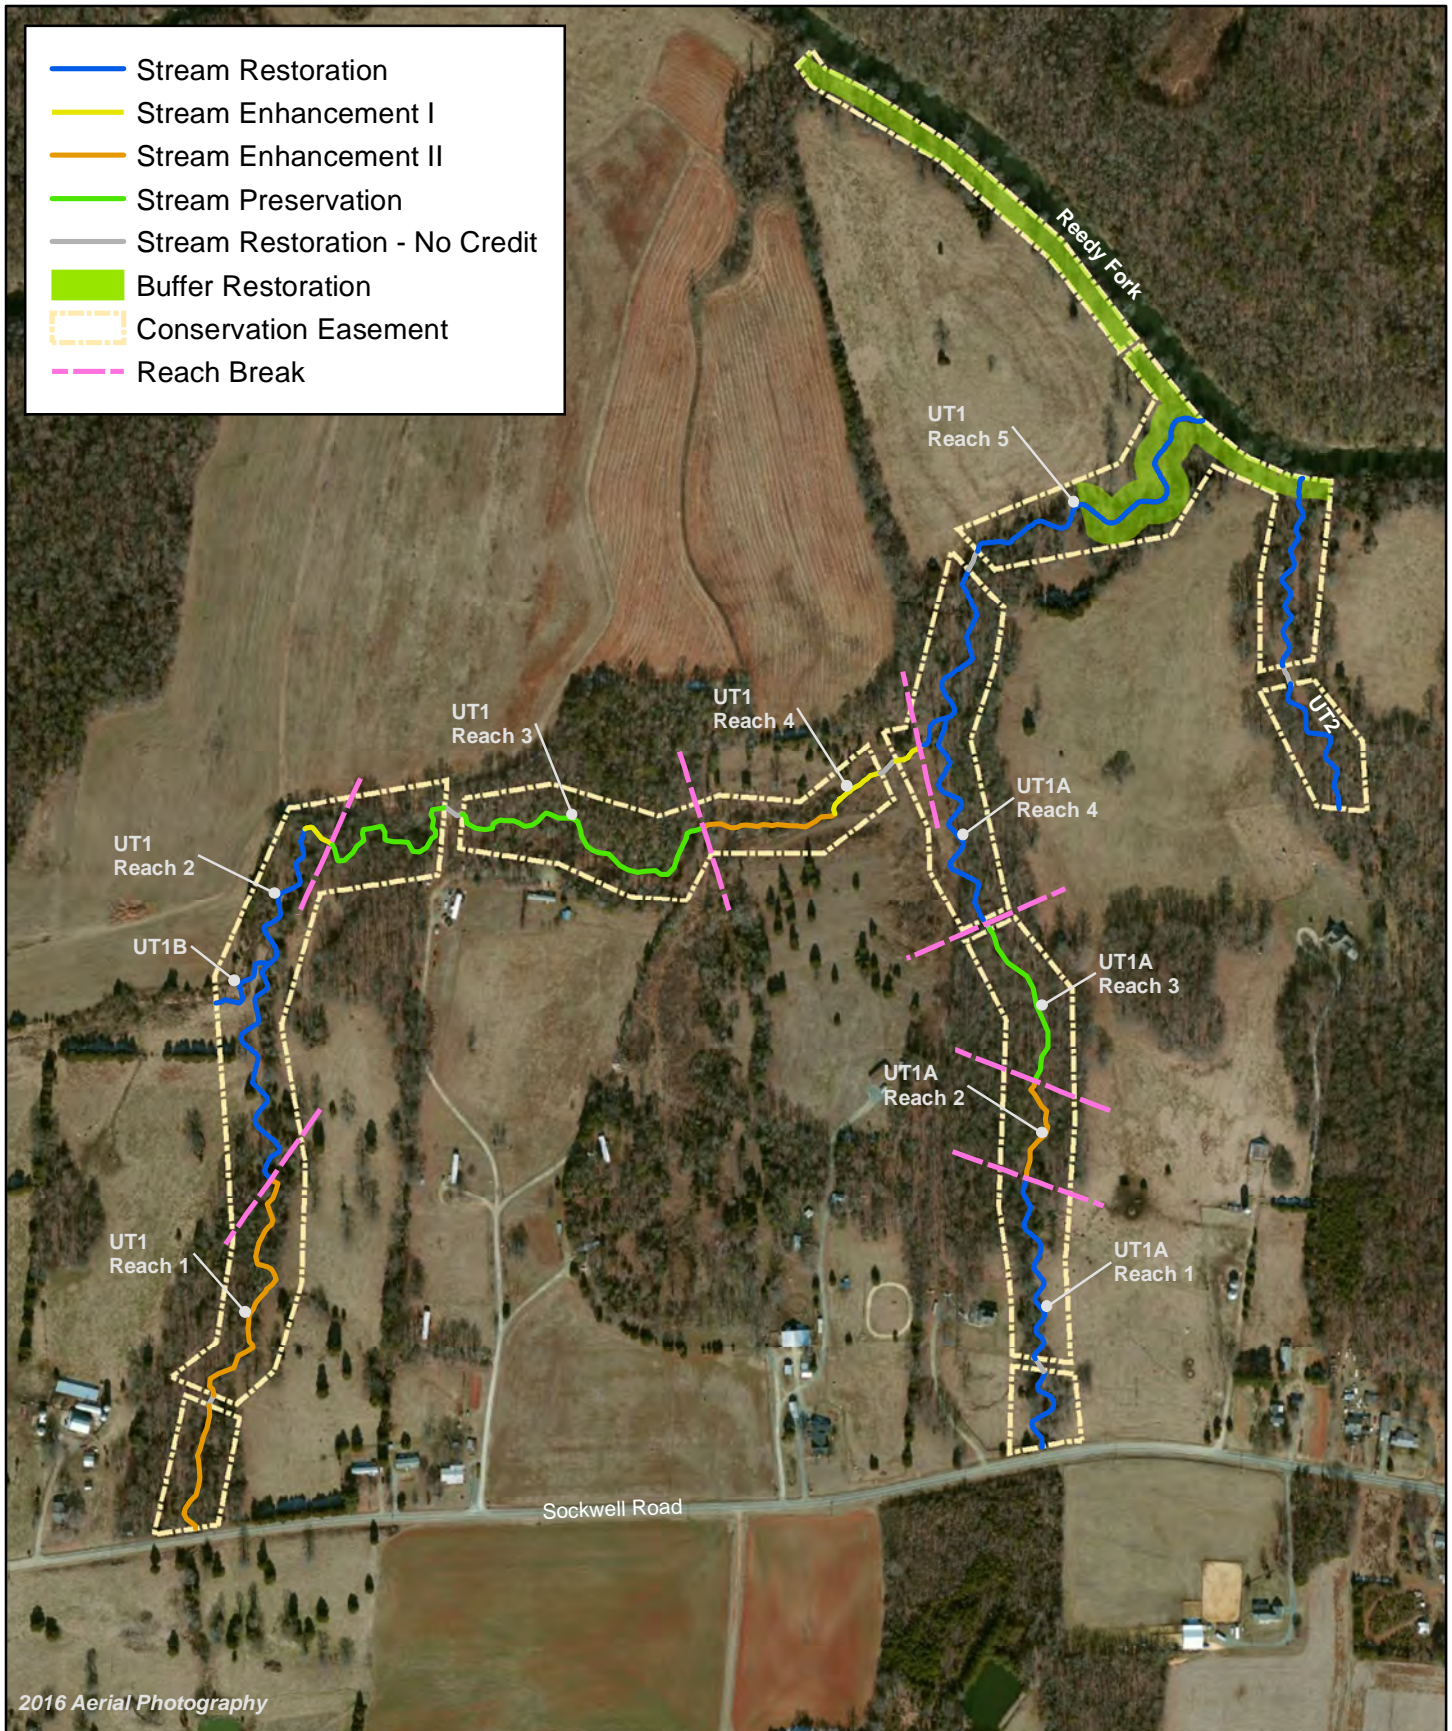


Figure 2 Project Component/ Asset Map
 Agony Acres Mitigation Site
 DMS Project No. 95716
 Monitoring Year 3 - 2017




Table 1. Project Components and Mitigation Credits
 Agony Acres Mitigation Site (DMS Project No.95716)
 Monitoring Year 3 - 2017

MITIGATION CREDITS									
	Stream		Riparian Wetland		Non-Riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset
Type	R	RE	R	RE	R	RE			
Totals	6,118	361	N/A	N/A	N/A	N/A	3.0	N/A	N/A
PROJECT COMPONENTS									
Reach ID	As-Built Stationing/ Location	Existing Footage/ Acreage	Approach	Restoration or Restoration Equivalent	Restoration Footage/ Acreage	Mitigation Ratio	Credits (SMU/ WMU)		
STREAMS									
UT1-Reach 1 (DOT ROW)	100+00 to 100+14	14	EII	Enhancement (No Credit)	14	---	---		
UT1-Reach 1	100+14 to 103+62; 103+93 to 111+24	1,079	EII	Enhancement	1,079	2.5	432		
UT1-Reach 1 (Easement Break)	103+62 to 103+93	31	EII	Enhancement (No Credit)	31	---	---		
UT1-Reach 2	111+24 to 122+38	1,039	P1	Restoration	1,114	1	1,114		
UT1-Reach 2	122+38 to 123+31	93	EI	Enhancement	93	1.5	62		
UT1-Reach 3	123+31 to 128+50; 129+06 to 137+37	1,350		Preservation	1,350	5	270		
UT1-Reach 3 (Easement Break)	128+50 to 129+06	56		Preservation (No Credit)	56	---	---		
UT1-Reach 4	137+37 to 140+92	355	EII	Enhancement	355	2.5	142		
UT1-Reach 4	140+92 to 142+66; 143+20 to 144+06	260	EI	Enhancement	260	1.5	173		
UT1-Reach 4 (Easement Break)	142+66 to 143+20	54	EI	Enhancement (No Credit)	54	---	---		
UT1-Reach 5	144+06 to 149+65; 150+20 to 158+94	1,355	P1/2	Restoration	1,433	1	1,433		
UT1-Reach 5 (Easement Break)	149+65 to 150+20	65	P1	Restoration (No Credit)	55	---	---		
UT1A-Reach 1 (DOT ROW)	200+00 to 200+05	5	P1	Restoration (No Credit)	5	---	---		
UT1A-Reach 1	200+05 to 202+64; 203+04 to 208+49	738	P1	Restoration	804	1	804		
UT1A-Reach 1 (Easement Break)	202+64 to 203+04	32	P1	Restoration (No Credit)	40	---	---		
UT1A-Reach 2	208+49 to 211+41	292	EII	Enhancement	292	2.5	117		
UT1A-Reach 3	211+41 to 215+98	457		Preservation	457	5	91		
UT1A-Reach 3 (Easement Break)	215+98 to 216+28	30	EII	Enhancement (No Credit)	30	---	---		
UT1A-Reach 4	216+28 to 222+78	461	P1	Restoration	650	1	650		
UT1B	300+00 to 302+19	243	P1	Restoration	219	1	219		
UT2	400+00 to 404+16; 404+67 to 410+23	975	P1	Restoration	972	1	972		
UT2 (Easement Break)	404+16 to 404+67	53	P1/2	Restoration (No Credit)	51	---	---		

COMPONENT SUMMATION						
Restoration Level	Stream (LF)	Riparian Wetland (acres)		Non-Riparian Wetland (acres)	Buffer (acres)	Upland (acres)
		Riverine	Non-Riverine			
Restoration	5,192	-	-	-	3.0	-
Enhancement		-	-	-	-	-
Enhancement I	353					
Enhancement II	1,726					
Creation		-	-	-		
Preservation	1,807	-	-	-		-
High Quality Preservation	-	-	-	-		-

N/A: not applicable

* Credit calculations were originally calculated along the as-built thalweg and updated to be calculated along stream centerlines as stated in the approved Mitigation Plan for Monitoring Year 3 after discussions with NC IRT.

Table 2. Project Activity and Reporting History

Agony Acres Mitigation Site (DMS Project No.95716)

Monitoring Year 3 - 2017

Activity or Report	Date Collection Complete	Completion or Scheduled Delivery
Mitigation Plan	October 2013- March 2014	March 2014
Final Design - Construction Plans	April 2014- June 2014	June 2014
Construction	June 2014- September 2014	September 2014
Temporary S&E mix applied to entire project area ¹	September 2014	September 2014
Permanent seed mix applied to reach/segments	September 2014	September 2014
Bare root and live stake plantings for reach/segments	December 2014	December 2014
Baseline Monitoring Document (Year 0)	Stream Survey	October 2014
	Vegetation Survey	December 2014
Year 1 Monitoring	Stream Survey	May 2015
	Vegetation Survey	September 2015
Year 2 Monitoring	Stream Survey	March 2016
	Vegetation Survey	June 2016
Supplemental Planting		December 2016
Year 3 Monitoring	Stream Survey	April 2017
	Vegetation Survey	August 2017
Year 4 Monitoring	Stream Survey	2018
	Vegetation Survey	2018
Year 5 Monitoring	Stream Survey	2019
	Vegetation Survey	2019
Year 6 Monitoring	Stream Survey	2020
	Vegetation Survey	2020
Year 7 Monitoring	Stream Survey	2021
	Vegetation Survey	2021

¹Seed and mulch is added as each section of construction is completed.

Table 3. Project Contact Table

Agony Acres Mitigation Site (DMS Project No.95716)


Monitoring Year 3 - 2017

Designer Nicole Macaluso, PE, CFM	Wildlands Engineering, Inc. 312 West Millbrook Road, Suite 225 Raleigh, NC 27609 919.851.9986
Construction Contractor	Land Mechanic Designs, Inc. 126 Circle G Lane Willow Spring, NC 27592
Planting Contractor	Bruton Natural Systems, Inc P.O. Box 1197 Fremont, NC 27830
Seeding Contractor	Land Mechanic Designs, Inc. 126 Circle G Lane Willow Spring, NC 27592
Seed Mix Sources	Green Resource, LLC
Nursery Stock Suppliers	
Bare Roots	Dykes and Son Nursery
Live Stakes	Bruton Natural Systems, Inc
Monitoring Performers Monitoring, POC	Wildlands Engineering, Inc. Jason Lorch 919.851.9986, ext. 107

Table 4. Project Information and Attributes
 Agony Acres Mitigation Site (DMS Project No.95716)
 Monitoring Year 3 - 2017

PROJECT INFORMATION						
Project Name	Agony Acres Mitigation Site					
County	Guilford County					
Project Area (acres)	30.78 acres					
Project Coordinates (latitude and longitude)	36° 10' 40" N, 79° 33' 02" W					
PROJECT WATERSHED SUMMARY INFORMATION						
Physiographic Province	Piedmont					
River Basin	Cape Fear River					
USGS Hydrologic Unit 8-digit	03030002					
USGS Hydrologic Unit 14-digit	03030002020070					
DWR Sub-basin	03-06-02					
Project Drainage Area (acres)	358 acres					
Project Drainage Area Percentage of Impervious Area	<1%					
CGIA Land Use Classification	65% Managed Herbaceous Cover, 30% Mixed Upland Hardwoods, 3% Cultivated, 2% Southern Yellow Pine, <1% Low Intensity Development					
REACH SUMMARY INFORMATION						
Parameters	UT1 - Reaches 1 -3	UT1 - Reaches 4 & 5	UT1A	UT1B	UT2	
Length of reach (linear feet) - Post-Restoration	3,737	2,157	2,278	219	1,023	
Drainage area (acres)	228	358	103	61	61	
NCDWR stream identification score	42.5	46.5	41	29.25	32.25	
NCDWR Water Quality Classification	WS-V					
Morphological Description (stream type)	P	P	P/I	P	P	
Evolutionary trend (Simon's Model) - Pre- Restoration	I, III	III, IV	I, II/III	II/III	II/III	
Underlying mapped soils	Cecil sandy loam, Congaree loam, Coronaca clay loam, Enon fine sandy loam, Enon clay loam, Madison clay loam, Mecklenburg sandy clay loam, Wehadkee loam					
Drainage class	---	---	---	---	---	---
Soil Hydric status	---	---	---	---	---	---
Slope	---	---	---	---	---	---
FEMA classification	N/A					
Native vegetation community	Piedmont bottomland forest					
Percent composition exotic invasive vegetation -Post-Restoration	0%					
REGULATORY CONSIDERATIONS						
Regulation	Applicable?	Resolved?	Supporting Documentation			
Waters of the United States - Section 404	Yes	Yes	USACE Nationwide Permit No.27 and DWQ 401 Water Quality Certification No. 3885.			
Waters of the United States - Section 401	Yes	Yes	USACE Nationwide Permit No.27 and DWQ 401 Water Quality Certification No. 3885.			
Division of Land Quality (Dam Safety)	No	N/A	N/A			
Endangered Species Act	Yes	Yes	Agony Acres Mitigation Plan; Wildlands determined "no effect" on Guilford County listed endangered species.			
Historic Preservation Act	Yes	Yes	No historic resources were found to be impacted (letter from SHPO dated 1/15/13).			
Coastal Zone Management Act (CZMA)/Coastal Area Management Act (CAMA)	No	N/A	N/A			
FEMA Floodplain Compliance	N/A	N/A	The project streams do not have an associated regulatory floodplain; however portions of UT1, UT1A, and UT2 are located within the floodway and flood fringe of Reedy Fork (FEMA Zone AE, FIRM panels 8838 and 8848).			
Essential Fisheries Habitat	No	N/A	N/A			

APPENDIX 2. Visual Assessment Data

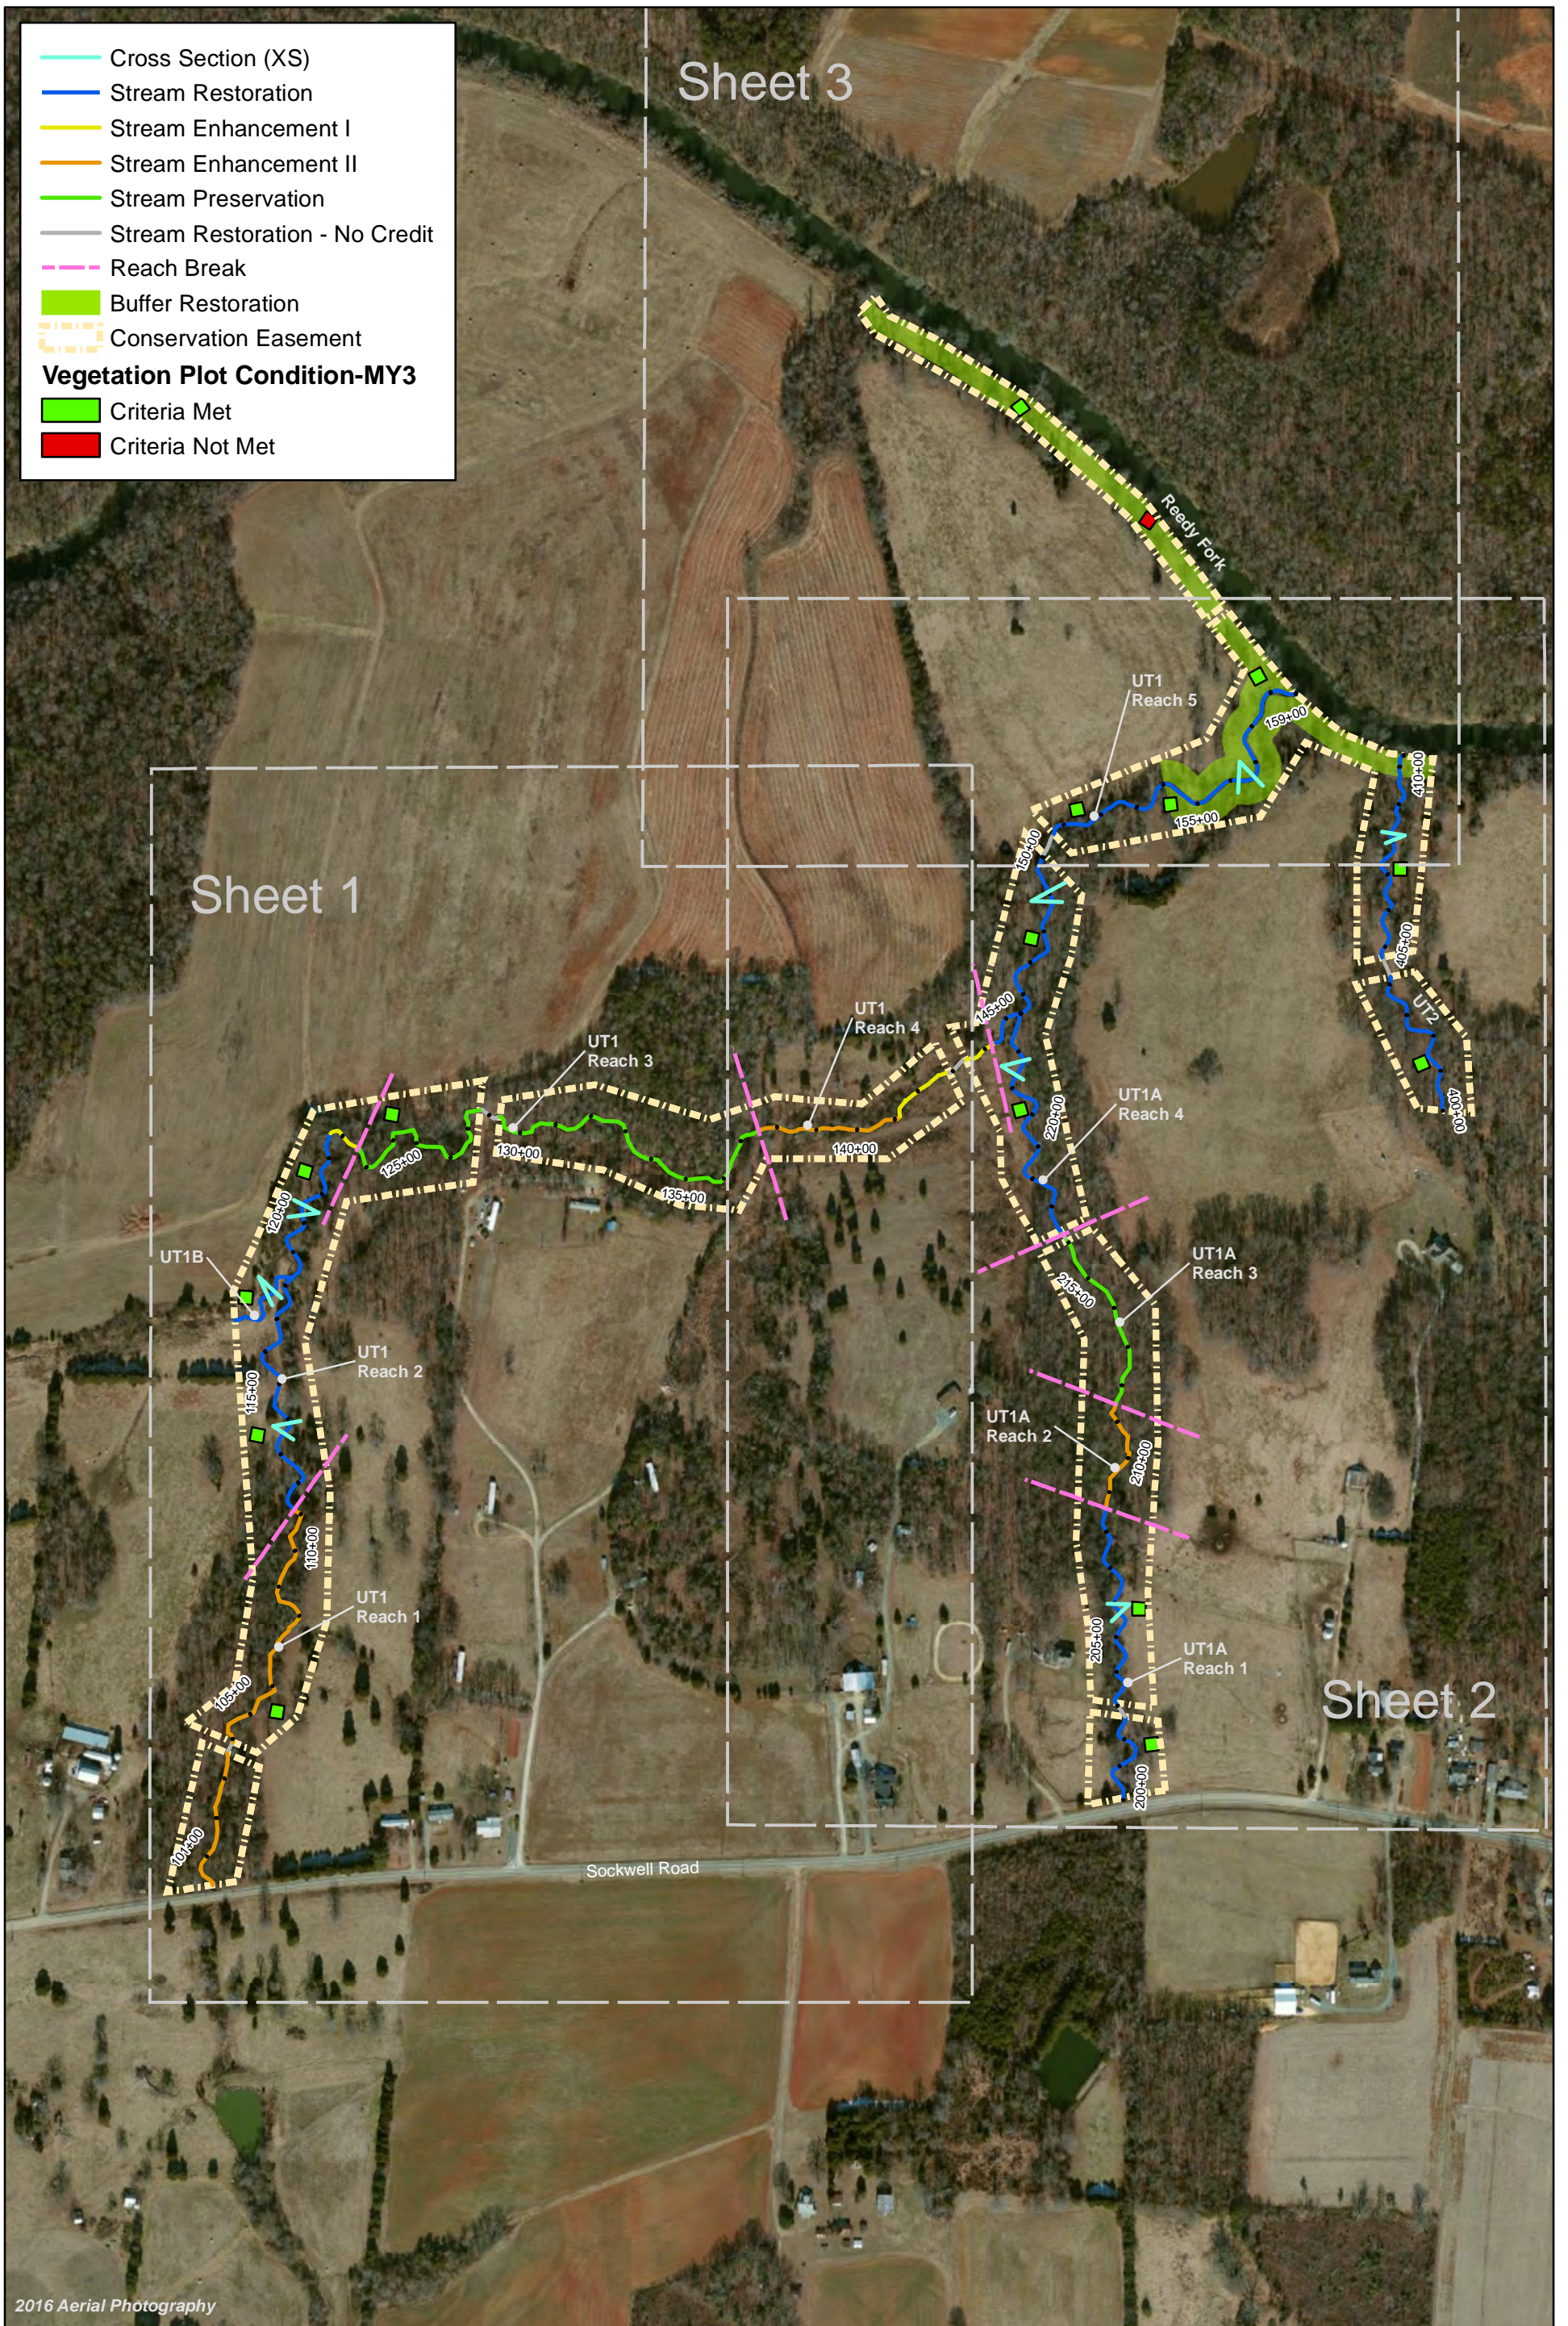

2016 Aerial Photography




0 250 500 Feet




Figure 3.0 Integrated Current Condition Plan View (Key)

Agony Acres Mitigation Site
DMS Project No. 95716
Monitoring Year 3 - 2017

Guilford County, NC

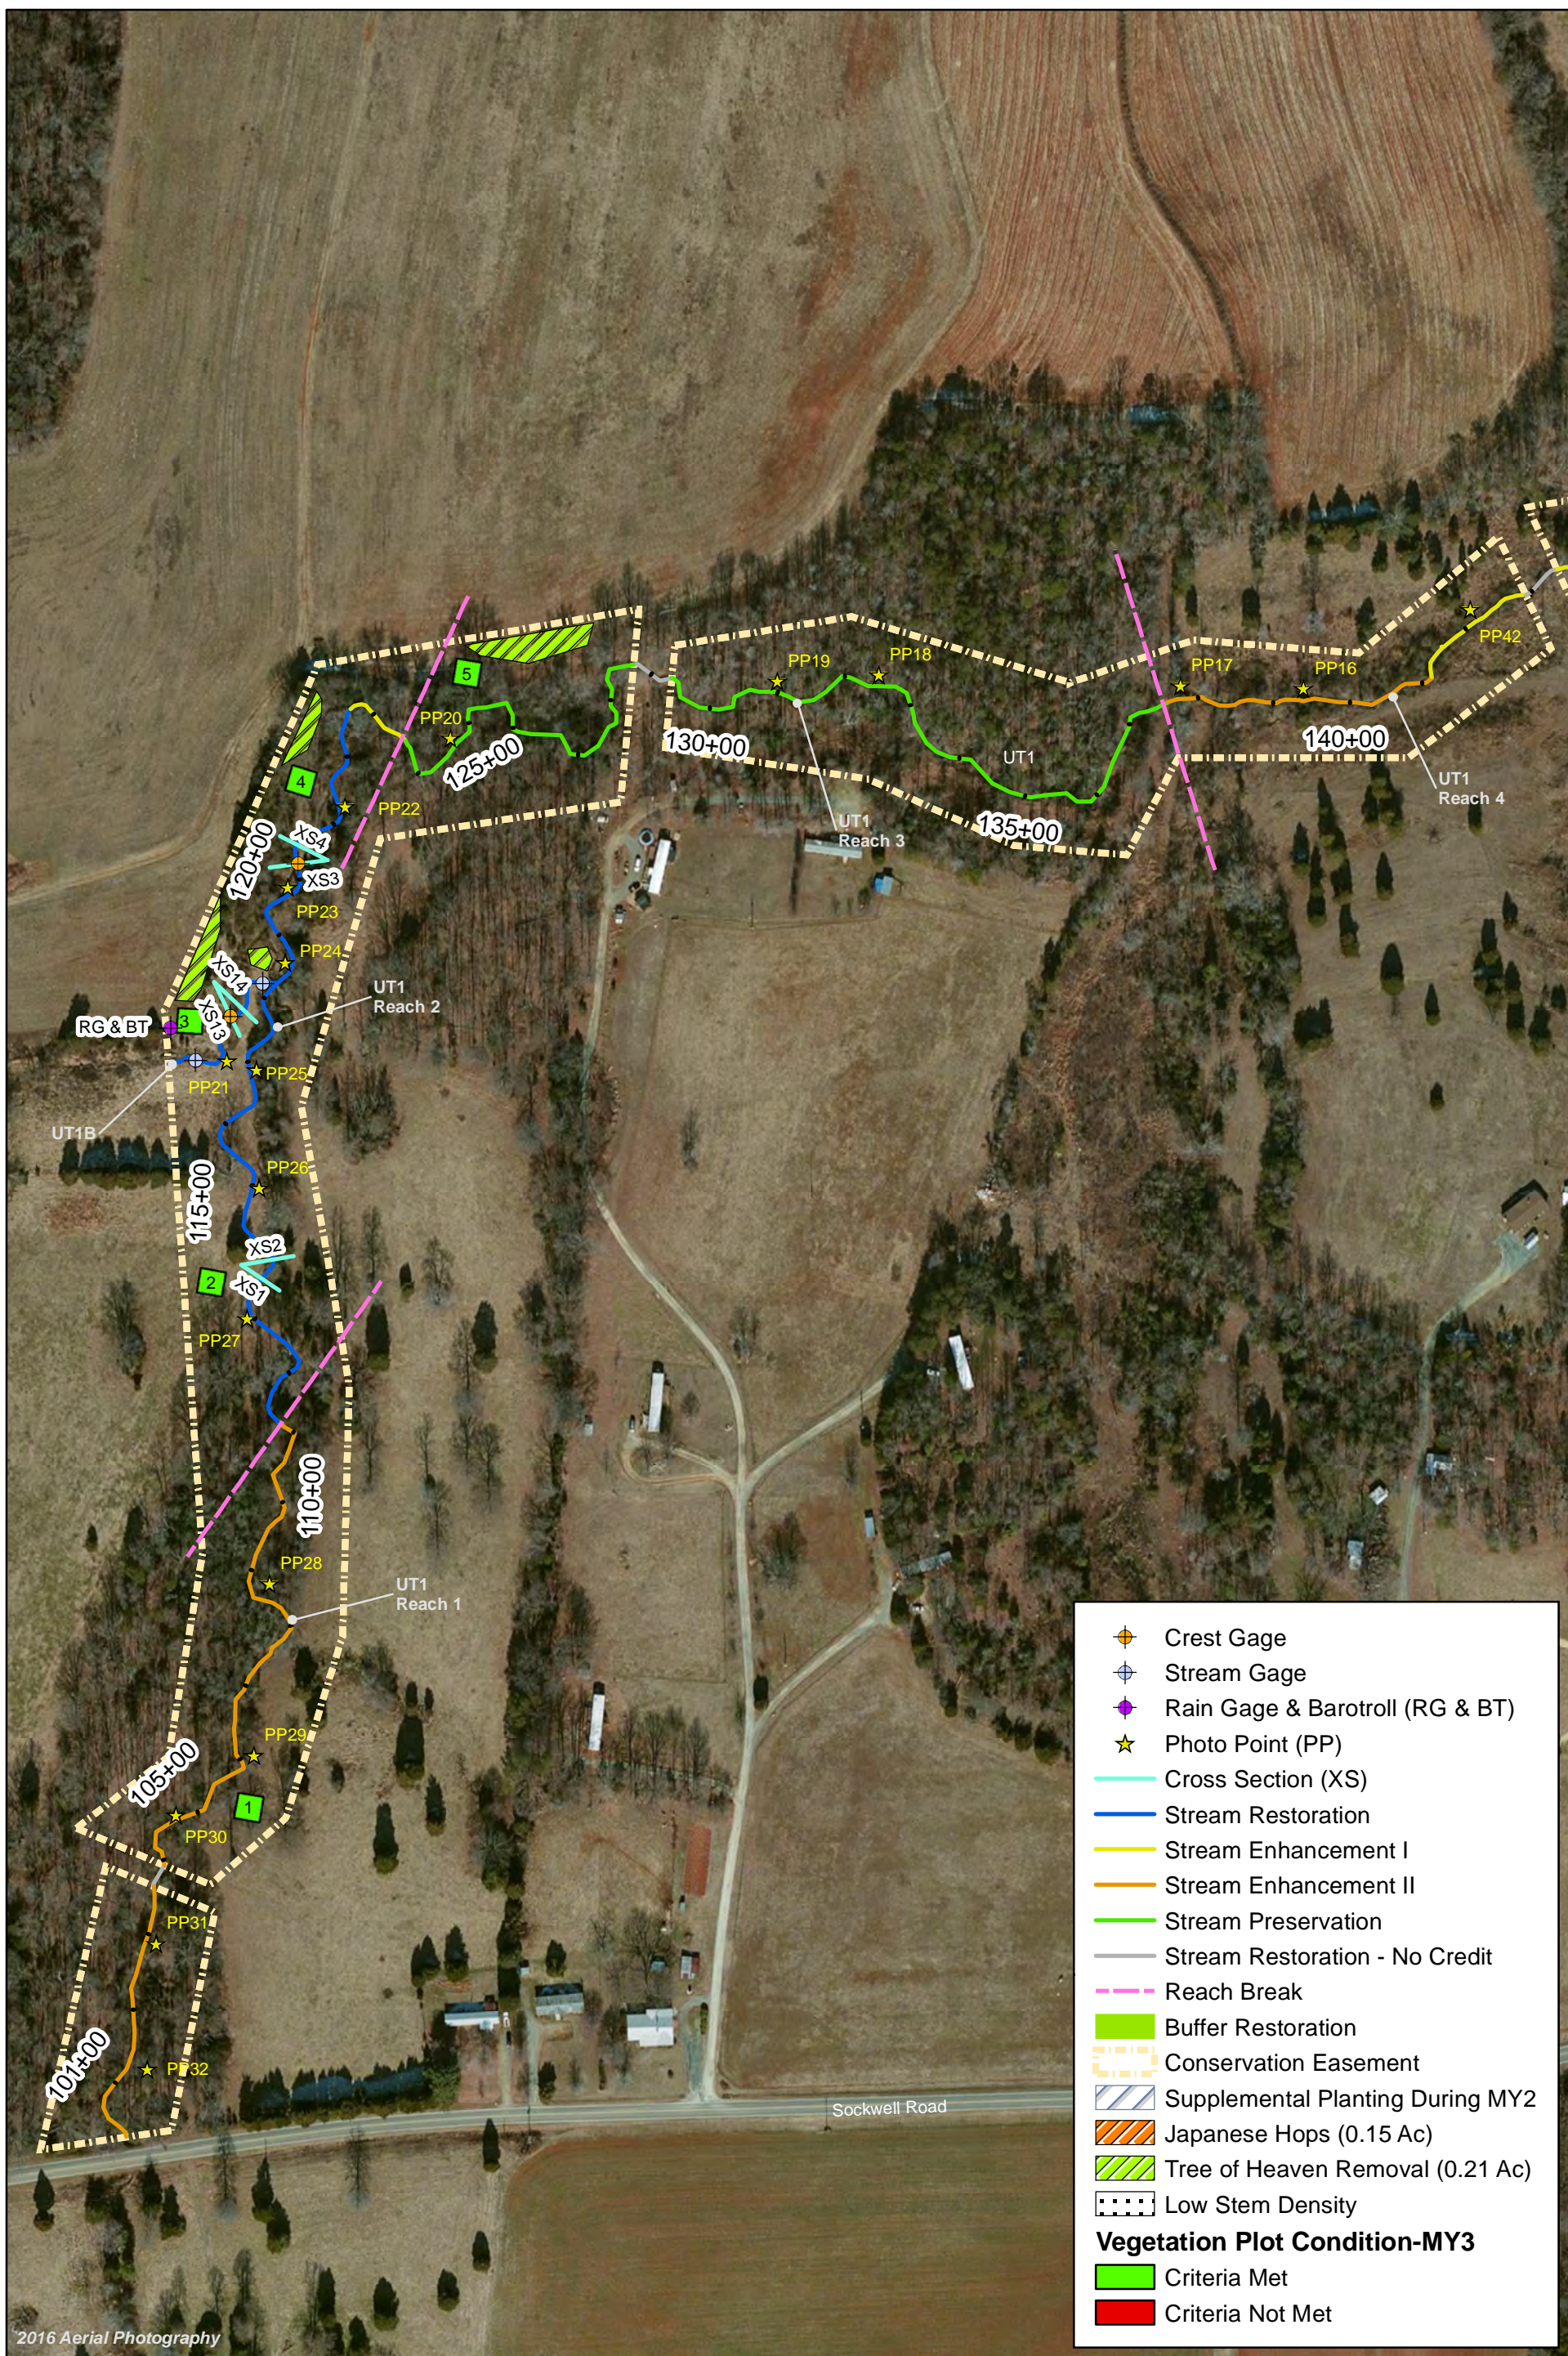

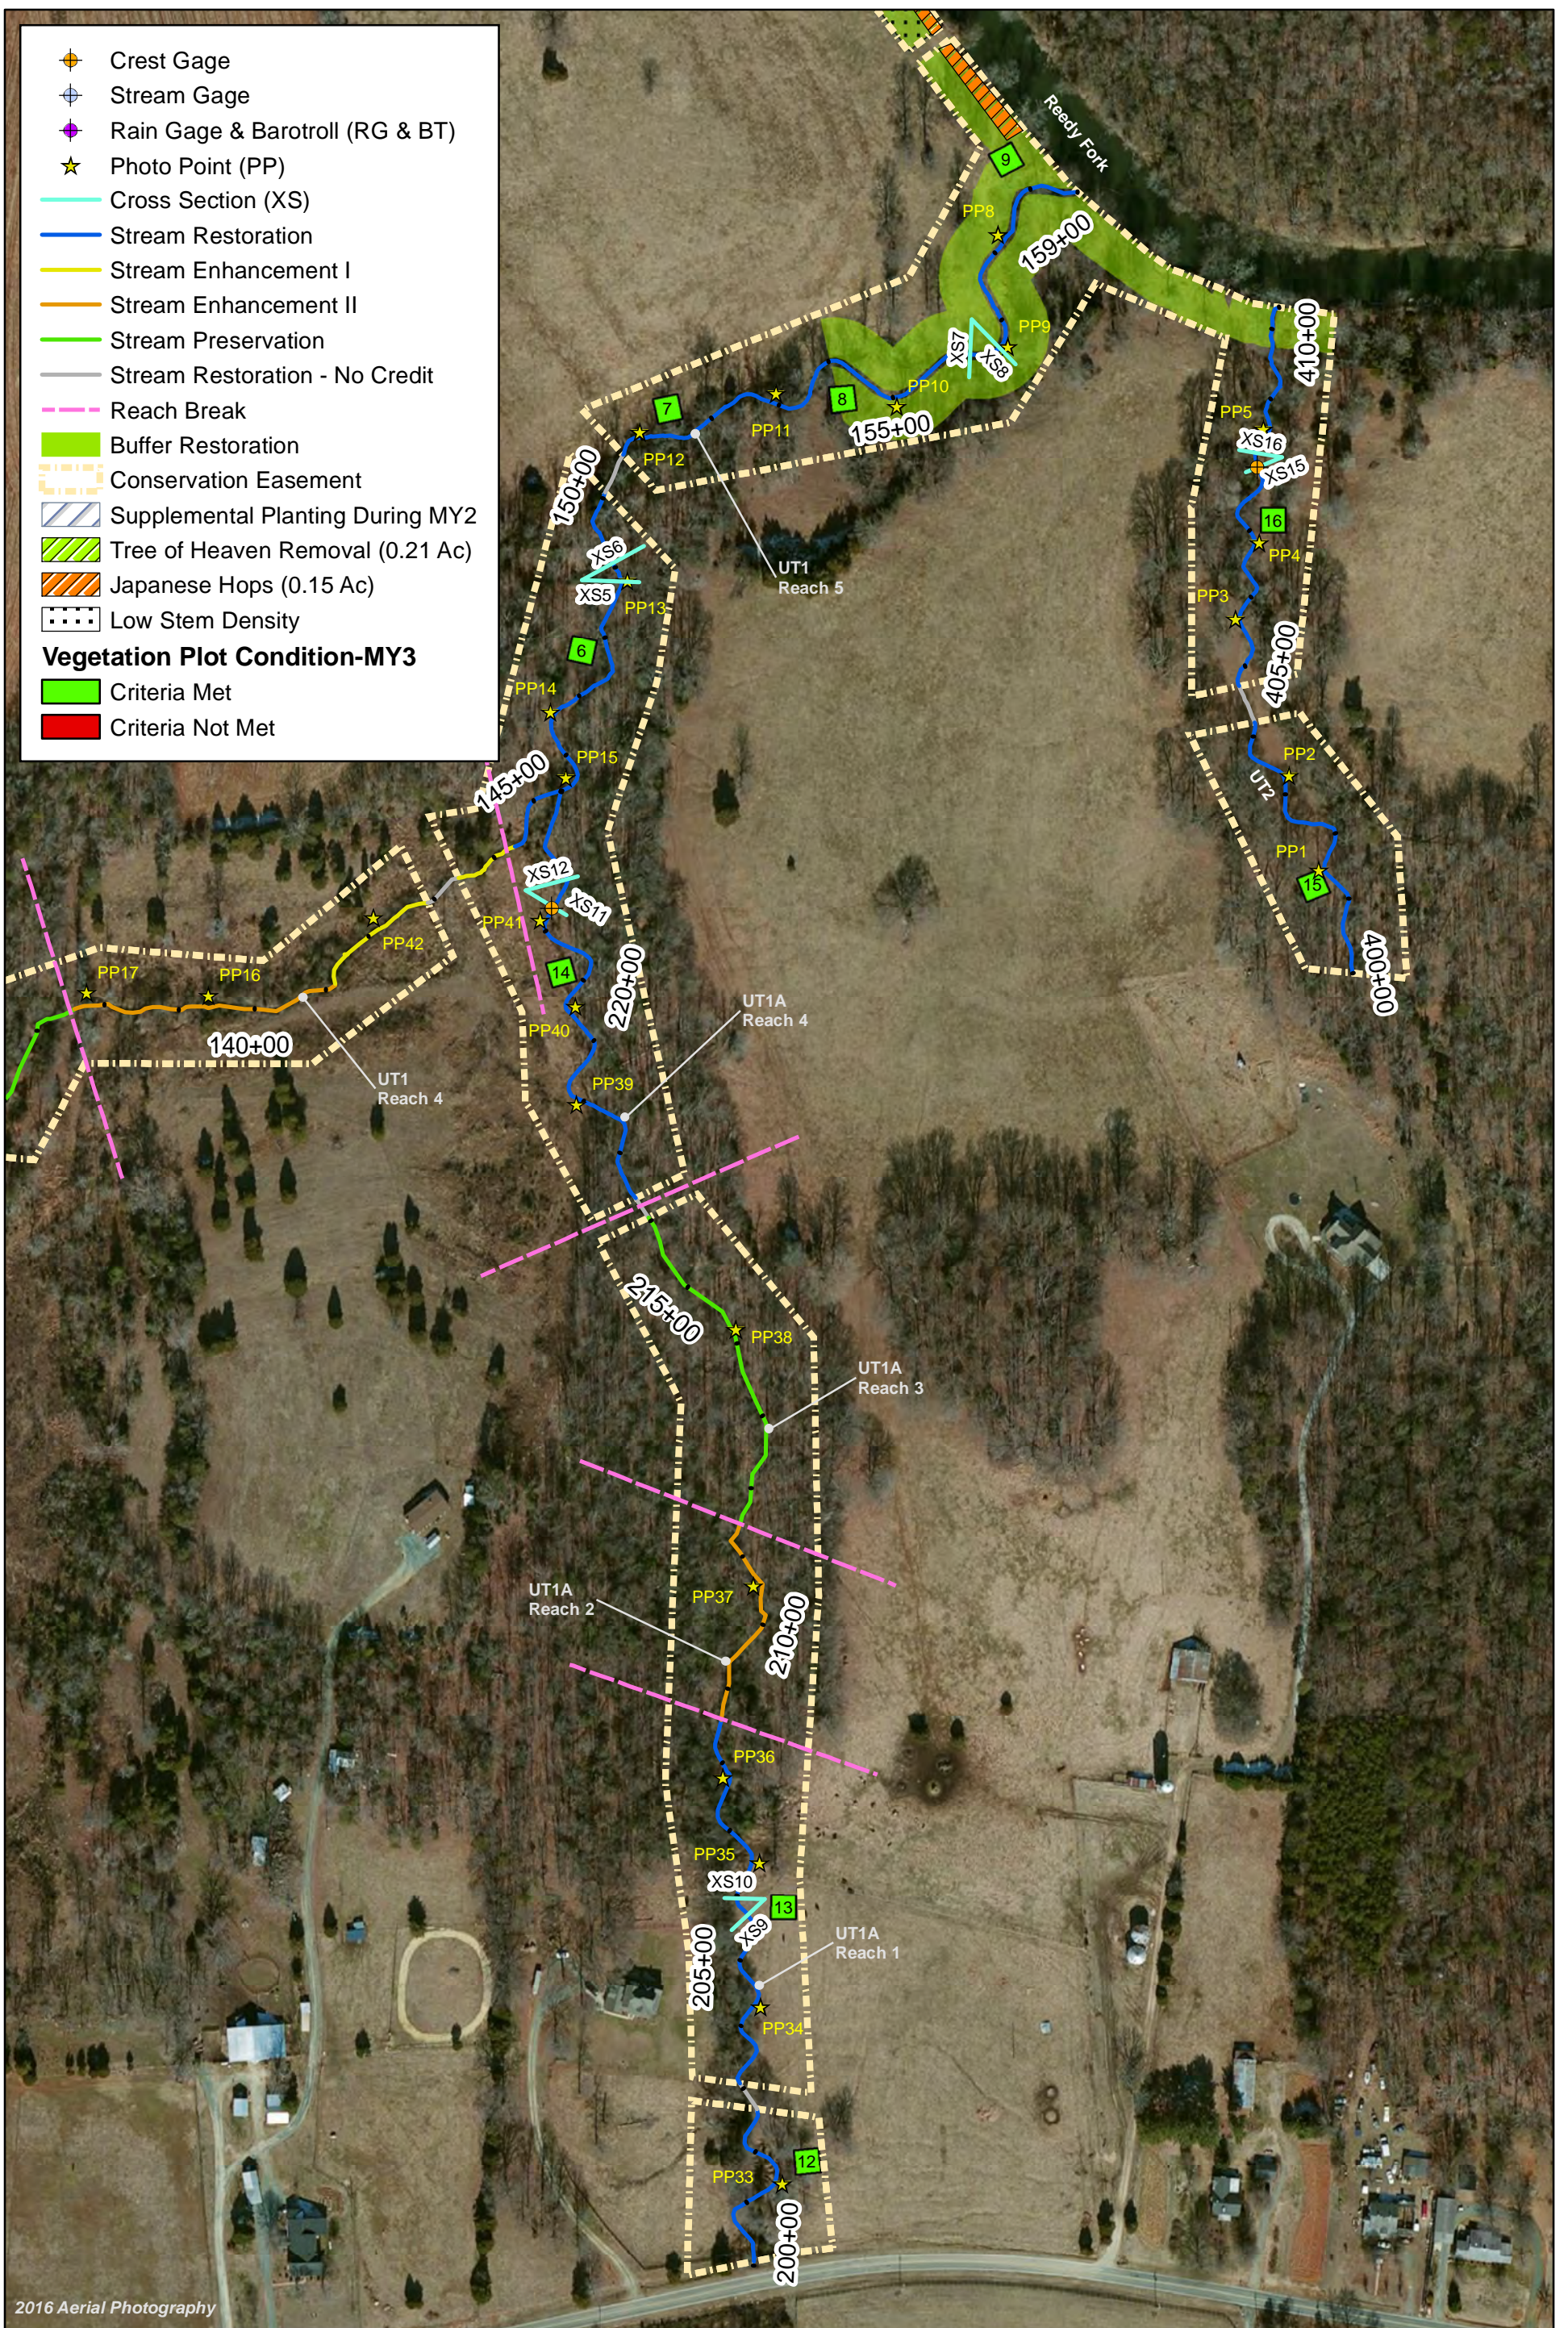


2016 Aerial Photography



0 250 500 Feet



Figure 3.2 Integrated Current Condition Plan View
 (Sheet 2 of 3)
 Agony Acres Mitigation Site
 DMS Project No. 95716
 Monitoring Year 3 - 2017
 Guilford County, NC

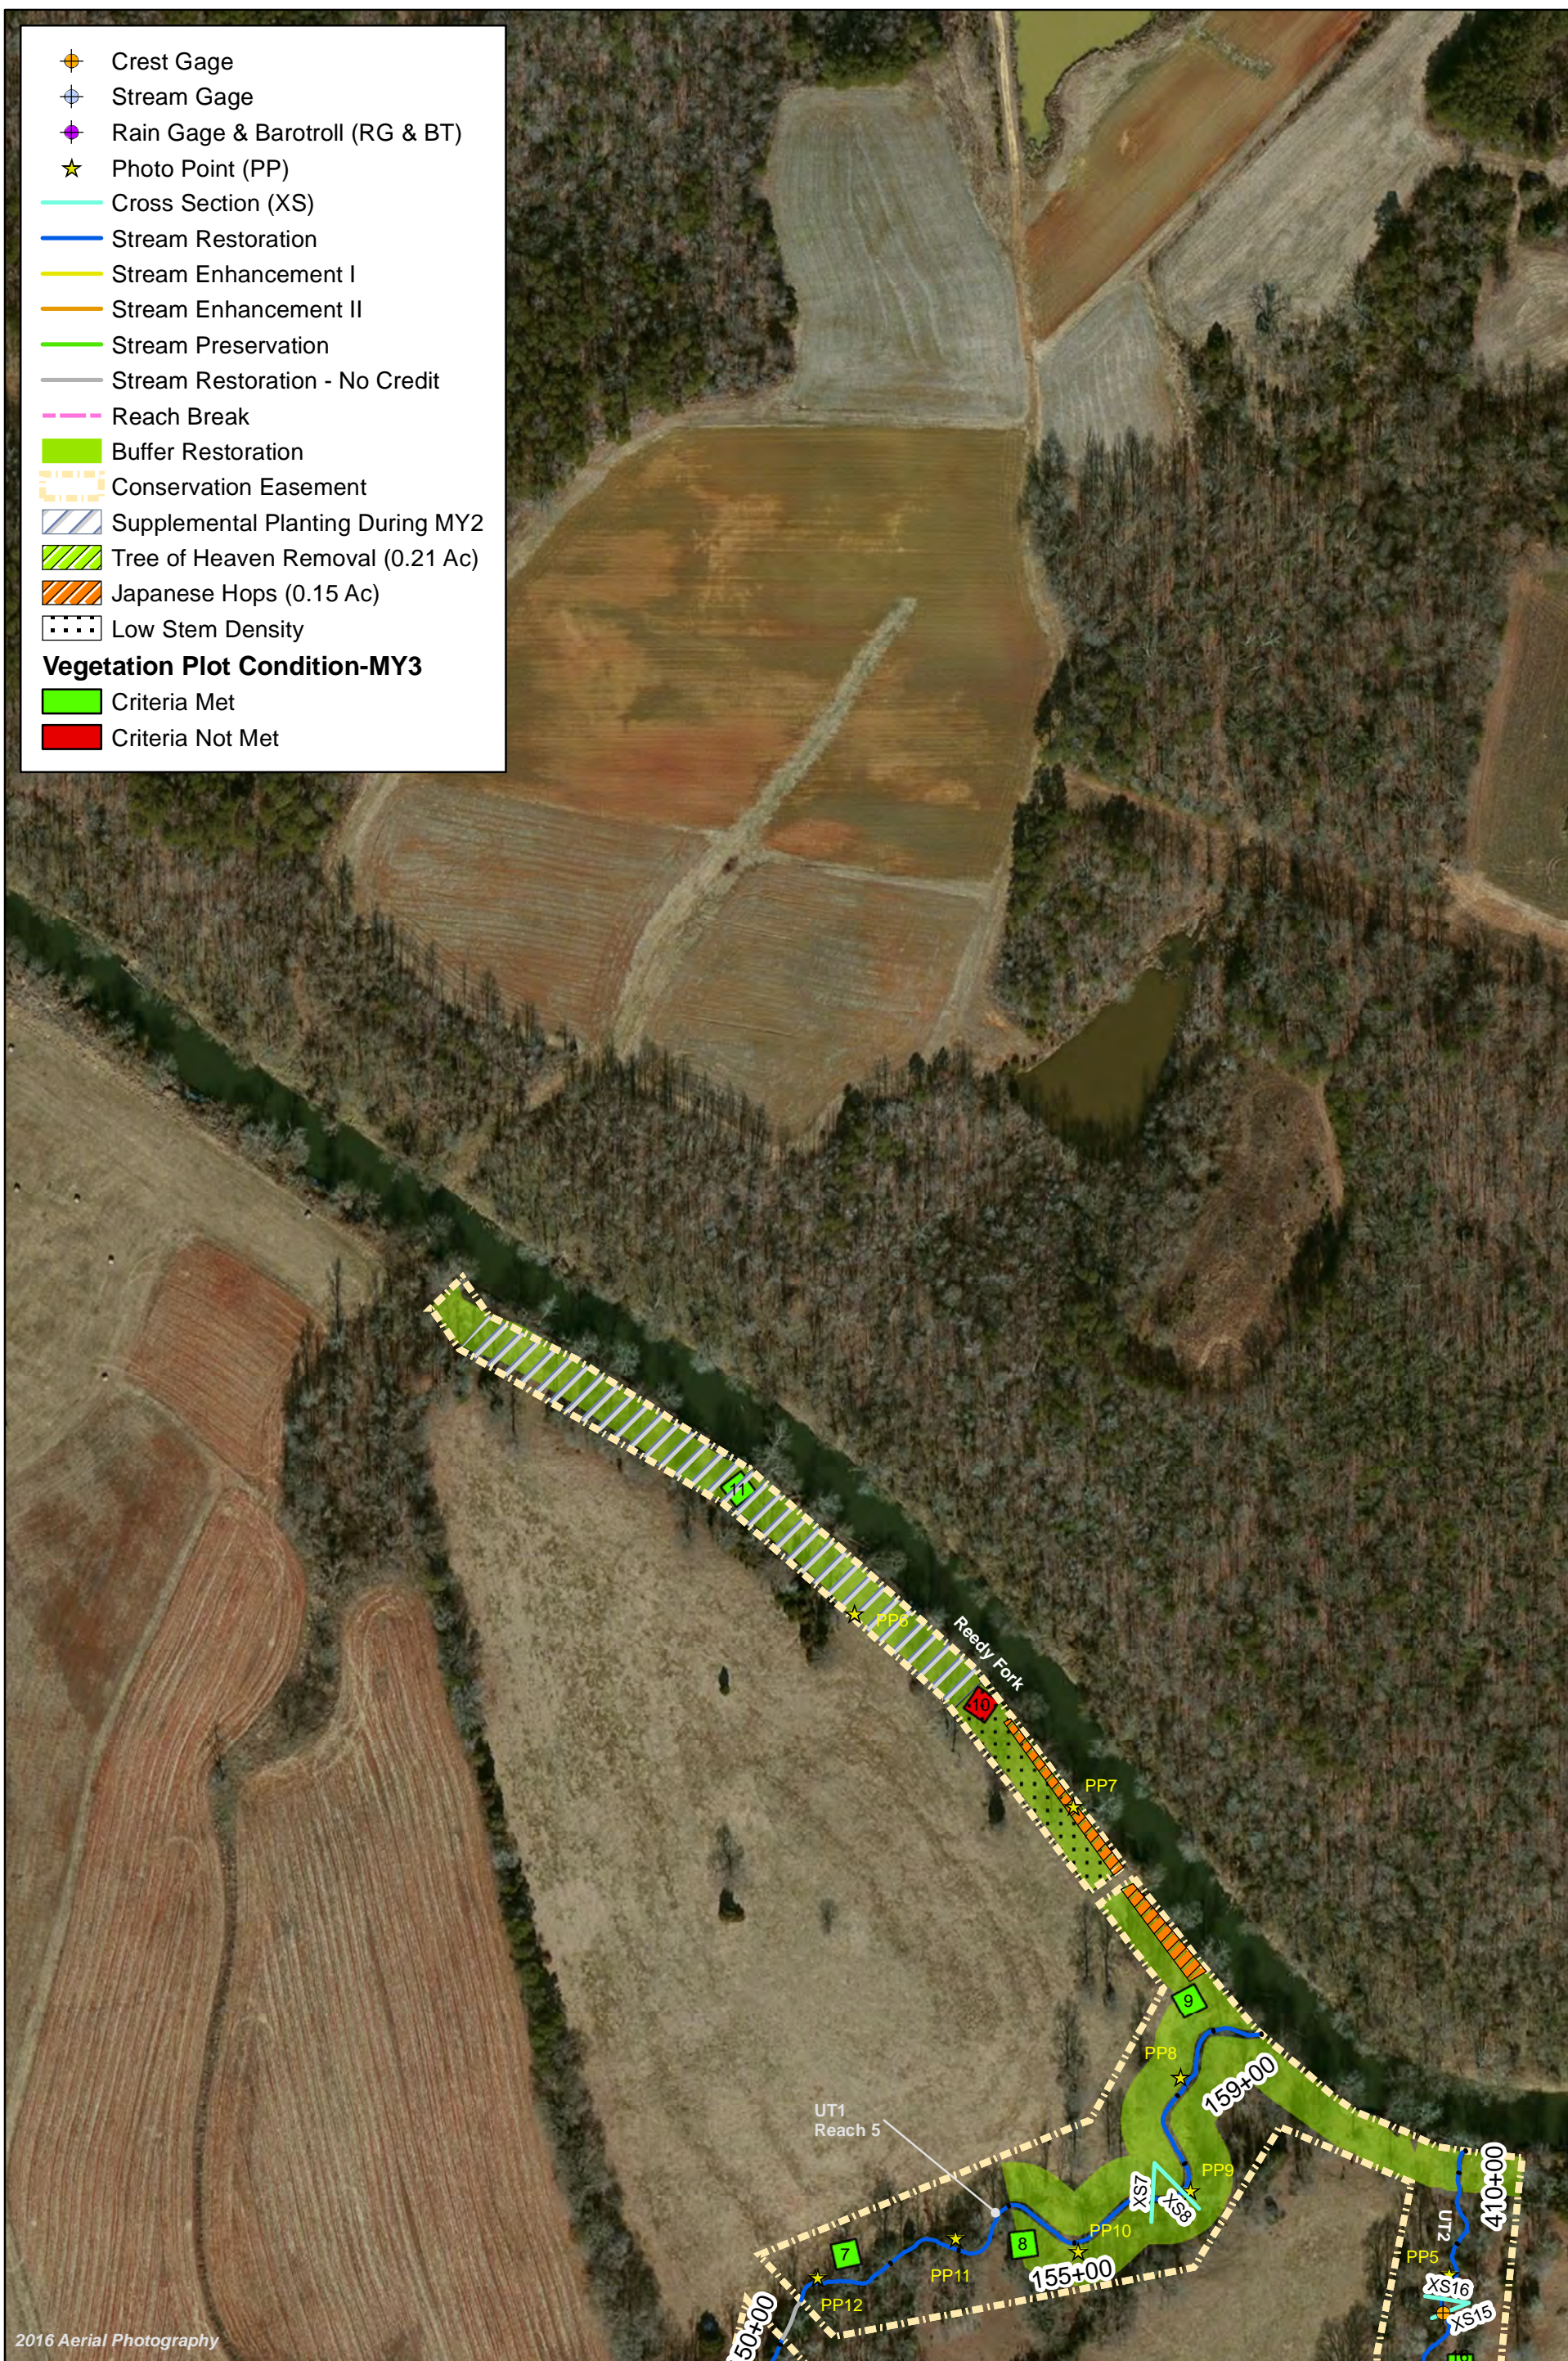

2016 Aerial Photography



0 250 500 Feet



Figure 3.3 Integrated Current Condition Plan View
 (Sheet 3 of 3)
 Agony Acres Mitigation Site
 DMS Project No. 95716
 Monitoring Year 3 - 2017
 Guilford County, NC

Table 5a. Visual Stream Morphology Stability Assessment Table

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	42	42			100%			
	3. Meander Pool Condition	Depth Sufficient	39	39			100%			
		Length Appropriate	39	39			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	39	39			100%			
Thalweg centering at downstream of meander bend (Glide)		39	39	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
TOTALS					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	16	16			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	16	16			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	16	16			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	16	16			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	16	16			100%			

Table 5b. Visual Stream Morphology Stability Assessment Table

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1A

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	26	26		100%				
	3. Meander Pool Condition	Depth Sufficient	26	26		100%				
		Length Appropriate	26	26		100%				
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	26	26		100%				
Thalweg centering at downstream of meander bend (Glide)		26	26	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
TOTALS					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	3	3			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	3	3			100%			

Table 5c. Visual Stream Morphology Stability Assessment Table

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1B

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	6	6			100%			
	3. Meander Pool Condition	Depth Sufficient	5	5			100%			
		Length Appropriate	5	5			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	5	5			100%			
Thalweg centering at downstream of meander bend (Glide)		5	5	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
TOTALS					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	1	1			100%			

Table 5d. Visual Stream Morphology Stability Assessment Table

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT2

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	20	20			100%			
	3. Meander Pool Condition	Depth Sufficient	21	21			100%			
		Length Appropriate	21	21			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	21	21			100%			
Thalweg centering at downstream of meander bend (Glide)		21	21	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
TOTALS					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	5	5			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	5	5			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	5	5			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	5	5			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	5	5			100%			

Table 6. Vegetation Condition Assessment Table
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

Planted Acreage 18

Vegetation Category	Definitions	Mapping Threshold (Ac)	Number of Polygons	Combined Acreage	% of Planted Acreage
Bare Areas	Very limited cover of both woody and herbaceous material	0.1	0	0	0.0%
Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1	1	0.4	2.0%
			Total	1	0.4
Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 Ac	0	0	0%
			Cumulative Total	1	0.4
				0.4	2%

Easement Acreage 31

Vegetation Category	Definitions	Mapping Threshold (SF)	Number of Polygons	Combined Acreage	% of Planted Acreage
Invasive Areas of Concern	Areas or points (if too small to render as polygons at map scale).	1,000	2	0.15	0.5%
Easement Encroachment Areas	Areas or points (if too small to render as polygons at map scale).	none	0	0	0%

**STREAM PHOTOGRAPHS
UT2
Monitoring Year 3**



PHOTO POINT 1 – looking upstream (04/19/2017)



PHOTO POINT 1 – looking downstream (04/19/2017)



PHOTO POINT 2 – looking upstream (04/19/2017)



PHOTO POINT 2 – looking downstream (04/19/2017)





PHOTO POINT 3 – looking upstream (04/19/2017)



PHOTO POINT 3 – looking downstream (04/19/2017)



PHOTO POINT 4 – looking upstream (04/19/2017)



PHOTO POINT 4 – looking downstream (04/19/2017)



PHOTO POINT 5 – looking upstream (04/19/2017)



PHOTO POINT 5 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
Reedy Fork (Buffer)
Monitoring Year 3



PHOTO POINT 6 – looking upstream (04/19/2017)



PHOTO POINT 6 – looking downstream (04/19/2017)



PHOTO POINT 7 – looking upstream (04/19/2017)



PHOTO POINT 7 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1 Reach 5
Monitoring Year 3



PHOTO POINT 8 – looking upstream (04/19/2017)



PHOTO POINT 8 – looking downstream (04/19/2017)



PHOTO POINT 9 – looking upstream (04/19/2017)



PHOTO POINT 9 – looking downstream (04/19/2017)





PHOTO POINT 10 – looking upstream (04/19/2017)



PHOTO POINT 10 – looking downstream (04/19/2017)



PHOTO POINT 11 – looking upstream (04/19/2017)



PHOTO POINT 11 – looking downstream (04/19/2017)



PHOTO POINT 12 – looking upstream (04/19/2017)



PHOTO POINT 12 – looking downstream (04/19/2017)





PHOTO POINT 13 – looking upstream (04/19/2017)



PHOTO POINT 13 – looking downstream (04/19/2017)



PHOTO POINT 14 – looking upstream (04/19/2017)



PHOTO POINT 14 – looking downstream (04/19/2017)



PHOTO POINT 15 – looking upstream (04/19/2017)



PHOTO POINT 15 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1 Reach 4
Monitoring Year 3



PHOTO POINT 16 – looking upstream (04/19/2017)



PHOTO POINT 16 – looking downstream (04/19/2017)



PHOTO POINT 17 – looking upstream (04/19/2017)

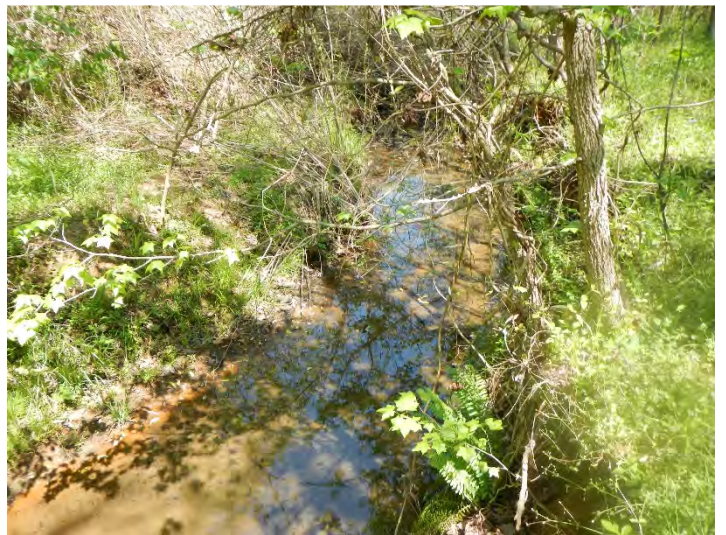


PHOTO POINT 17 – looking downstream (04/19/2017)





PHOTO POINT 42 – looking upstream (04/19/2017)



PHOTO POINT 42 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1 Reach 3
Monitoring Year 3



PHOTO POINT 18 – looking upstream (04/19/2017)



PHOTO POINT 18 – looking downstream (04/19/2017)

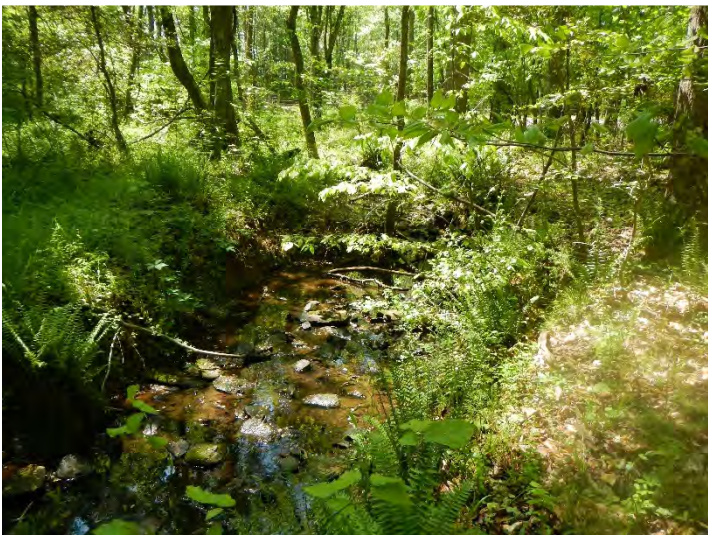


PHOTO POINT 19 – looking upstream (04/19/2017)



PHOTO POINT 19 – looking downstream (04/19/2017)





PHOTO POINT 20 – looking upstream (04/19/2017)



PHOTO POINT 20 – looking downstream (04/19/2017)



**STREAM PHOTOGRAPHS
UT1B
Monitoring Year 3**



PHOTO POINT 21 – looking upstream (04/19/2017)



PHOTO POINT 21 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1 Reach 2
Monitoring Year 3



PHOTO POINT 22 – looking upstream (04/19/2017)



PHOTO POINT 22 – looking downstream (04/19/2017)



PHOTO POINT 23 – looking upstream (04/19/2017)



PHOTO POINT 23 – looking downstream (04/19/2017)





PHOTO POINT 24 – looking upstream (04/19/2017)



PHOTO POINT 24 – looking downstream (04/19/2017)



PHOTO POINT 25 – looking upstream (04/19/2017)



PHOTO POINT 25 – looking downstream (04/19/2017)



PHOTO POINT 26 – looking upstream (04/19/2017)



PHOTO POINT 26 – looking downstream (04/19/2017)





PHOTO POINT 27 – looking upstream (04/19/2017)



PHOTO POINT 27 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1 Reach 1
Monitoring Year 3



PHOTO POINT 28 – looking upstream (04/19/2017)



PHOTO POINT 28 – looking downstream (04/19/2017)



PHOTO POINT 29 – looking upstream (04/19/2017)



PHOTO POINT 29 – looking downstream (04/19/2017)





PHOTO POINT 30 – looking upstream (04/19/2017)



PHOTO POINT 30 – looking downstream (04/19/2017)



PHOTO POINT 31 – looking upstream (04/19/2017)



PHOTO POINT 31 – looking downstream (04/19/2017)



PHOTO POINT 32 – looking upstream (04/19/2017)



PHOTO POINT 32 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1A Reach 1
Monitoring Year 3



PHOTO POINT 33 – looking upstream (04/19/2017)



PHOTO POINT 33 – looking downstream (04/19/2017)



PHOTO POINT 34 – looking upstream (04/19/2017)



PHOTO POINT 34 – looking downstream (04/19/2017)





PHOTO POINT 35 – looking upstream (04/19/2017)



PHOTO POINT 35 – looking downstream (04/19/2017)



PHOTO POINT 36 – looking upstream (04/19/2017)



PHOTO POINT 36 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1A Reach 2
Monitoring Year 3



PHOTO POINT 37 – looking upstream (04/19/2017)



PHOTO POINT 37 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1A Reach 3
Monitoring Year 3



PHOTO POINT 38 – looking upstream (04/19/2017)



PHOTO POINT 38 – looking downstream (04/19/2017)



STREAM PHOTOGRAPHS
UT1A Reach 4
Monitoring Year 3



PHOTO POINT 39 – looking upstream (04/19/2017)



PHOTO POINT 39 – looking downstream (04/19/2017)



PHOTO POINT 40 – looking upstream (04/19/2017)



PHOTO POINT 40 – looking downstream (04/19/2017)





PHOTO POINT 41 – looking upstream (04/19/2017)



PHOTO POINT 41 – looking downstream (04/19/2017)



VEGETATION PHOTOGRAPHS
Agony Acres
Monitoring Year 3



VEG PLOT 1 (08/1/2017)



VEG PLOT 2 (08/1/2017)



VEG PLOT 3 (08/1/2017)



VEG PLOT 4 (08/1/2017)





VEG PLOT 5 (08/1/2017)



VEG PLOT 6 (08/1/2017)



VEG PLOT 7 (08/1/2017)



VEG PLOT 8 (08/1/2017)



VEG PLOT 9 (08/1/2017)



VEG PLOT 10 (08/1/2017)





VEG PLOT 11 (08/1/2017)



VEG PLOT 12 (08/1/2017)



VEG PLOT 13 (08/1/2017)



VEG PLOT 14 (08/1/2017)



VEG PLOT 15 (08/1/2017)



VEG PLOT 16 (08/1/2017)



APPENDIX 3. Vegetation Plot Data

Table 7. Vegetation Plot Criteria Attainment
 Agony Acres Mitigation Site (DMS Project No. 95716)
Monitoring Year 3 - 2017

Plot	Success Criteria Met (Y/N)	Tract Mean
1	Y	94%
2	Y	
3	Y	
4	Y	
5	Y	
6	Y	
7	Y	
8	Y	
9	Y	
10	N	
11	Y	
12	Y	
13	Y	
14	Y	
15	Y	
16	Y	

Table 8. CVS Vegetation Plot Metadata

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Database name	Agony Acres- MY3- v2.3.1.mdb
Database location	F:\Projects\005-02136 Agony Acres\Monitoring\Monitoring Year 3\Vegetation Assessment
Computer name	JASON-PC
File size	68157440
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Proj, planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Proj, total stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY	
Project Code	95716
project Name	Agony Acres Mitigation Site
Description	Stream & Buffer Site
River Basin	Cape Fear
Sampled Plots	16

Table 9. Planted and Total Stem Counts

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

			Current Plot Data (MY3 2017)														
Scientific Name	Common Name	Species Type	95716-WEI-0001			95716-WEI-0002			95716-WEI-0003			95716-WEI-0004			95716-WEI-0005		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree															
Acer rubrum	red maple	Tree															
Alnus serrulata	hazel alder	Shrub							1	1	2	1	1	1			
Betula nigra	river birch	Tree				1	1	1	2	2	2	3	3	3			
Cornus amomum	silky dogwood	Shrub															
Fraxinus pennsylvanica	green ash	Tree	5	5	5	4	4	4	3	3	3	2	2	2	2	2	2
Gleditsia triacanthos	honeylocust	Tree															
Ilex opaca	American holly	Tree			1												
Juglans nigra	black walnut	Tree															
Juniperus virginiana	eastern redcedar	Tree			3												
Liquidambar styraciflua	sweetgum	Tree			12		12			2			7				
Liriodendron tulipifera	tuliptree	Tree			2								2				
Platanus occidentalis	American sycamore	Tree	4	4	4				4	4	5	4	4	20	2	2	2
Quercus michauxii	swamp chestnut oak	Tree							1	1	1	2	2	2	5	5	5
Quercus pagoda	cherrybark oak	Tree	2	2	2	4	4	4	2	2	2	2	2	2			
Quercus phellos	willow oak	Tree	2	2	2	1	1	1	2	2	2	1	1	1	1	1	1
Quercus rubra	northern red oak	Tree															
Rhus	sumac	Shrub															
Rhus copallinum	flameleaf sumac	Shrub															
Ulmus	elm	Tree															
Stem count			13	13	31	10	10	22	15	15	19	15	15	40	10	10	10
size (ares)			1			1			1			1			1		
size (ACRES)			0.02			0.02			0.02			0.02			0.02		
Species count			4	4	8	4	4	5	7	7	8	7	7	9	4	4	4
Stems per ACRE			526	526	1,255	405	405	890	607	607	769	607	607	1,619	405	405	405

Color Coding for Table

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

Table 9. Planted and Total Stem Counts

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

			Current Plot Data (MY3 2017)														
Scientific Name	Common Name	Species Type	95716-WEI-0006			95716-WEI-0007			95716-WEI-0008			95716-WEI-0009			95716-WEI-0010		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree						2			1			13			
Acer rubrum	red maple	Tree						4									
Alnus serrulata	hazel alder	Shrub	4	4	4												
Betula nigra	river birch	Tree	4	4	4	4	4	5	1	1	1						
Cornus amomum	silky dogwood	Shrub															
Fraxinus pennsylvanica	green ash	Tree	2	2	2	3	3	3	5	5	5	6	6	11	2	2	3
Gleditsia triacanthos	honeylocust	Tree						1									
Ilex opaca	American holly	Tree															
Juglans nigra	black walnut	Tree															
Juniperus virginiana	eastern redcedar	Tree															
Liquidambar styraciflua	sweetgum	Tree			46			7			5			6			
Liriodendron tulipifera	tuliptree	Tree			25			2						1			
Platanus occidentalis	American sycamore	Tree	2	2	69	3	3	5	6	6	6	6	6	8	1	1	1
Quercus michauxii	swamp chestnut oak	Tree	2	2	2	4	4	4	3	3	3	1	1	1	1	1	1
Quercus pagoda	cherrybark oak	Tree	1	1	1										2	2	2
Quercus phellos	willow oak	Tree										1	1	1			
Quercus rubra	northern red oak	Tree			6												
Rhus	sumac	Shrub						1									
Rhus copallinum	flameleaf sumac	Shrub						1									
Ulmus	elm	Tree						8									
Stem count			15	15	159	14	14	43	15	15	21	14	14	41	6	6	7
size (ares)			1			1			1			1			1		
size (ACRES)			0.02			0.02			0.02			0.02			0.02		
Species count			6	6	9	4	4	12	4	4	6	4	4	7	4	4	4
Stems per ACRE			607	607	6,435	567	567	1,740	607	607	850	567	567	1,659	243	243	283

Color Coding for Table

Exceeds requirements by 10%
Exceeds requirements, but by less than 10%
Fails to meet requirements, by less than 10%
Fails to meet requirements by more than 10%
Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

Table 9. Planted and Total Stem Counts

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

			Current Plot Data (MY3 2017)																	
Scientific Name	Common Name	Species Type	95716-WEI-0011			95716-WEI-0012			95716-WEI-0013			95716-WEI-0014			95716-WEI-0015			95716-WEI-0016		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree																		
Acer rubrum	red maple	Tree																		
Alnus serrulata	hazel alder	Shrub	1	1	1	1	1	1				1	1	1				1	1	1
Betula nigra	river birch	Tree	2	2	2				2	2	3	2	2	2						
Cornus amomum	silky dogwood	Shrub																		
Fraxinus pennsylvanica	green ash	Tree	8	8	15	2	2	4	2	2	2				3	3	4	2	2	2
Gleditsia triacanthos	honeylocust	Tree																		
Ilex opaca	American holly	Tree																		
Juglans nigra	black walnut	Tree																		
Juniperus virginiana	eastern redcedar	Tree																		
Liquidambar styraciflua	sweetgum	Tree			4								17							11
Liriodendron tulipifera	tuliptree	Tree									1		8		1					32
Platanus occidentalis	American sycamore	Tree	3	3	3	4	4	4				3	3	46	4	4	5	3	3	57
Quercus michauxii	swamp chestnut oak	Tree				2	2	2	6	6	6	4	4	4	2	2	2	1	1	1
Quercus pagoda	cherrybark oak	Tree				1	1	1	2	2	2	1	1	1	1	1	1			
Quercus phellos	willow oak	Tree	1	1	1	1	1	1				1	1	1	1	1	1	4	4	4
Quercus rubra	northern red oak	Tree																		
Rhus	sumac	Shrub																		
Rhus copallinum	flameleaf sumac	Shrub														1				
Ulmus	elm	Tree									1									
Stem count			15	15	26	11	11	13	12	12	15	12	12	80	11	11	15	11	11	108
size (ares)			1			1			1			1			1			1		
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02		
Species count			5	5	6	6	6	6	4	4	6	6	6	8	5	5	7	5	5	7
Stems per ACRE			607	607	1,052	445	445	526	486	486	607	486	486	3,237	445	445	607	445	445	4,371

Color Coding for Table

Exceeds requirements by 10%
Exceeds requirements, but by less than 10%
Fails to meet requirements, by less than 10%
Fails to meet requirements by more than 10%
Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

Table 9. Planted and Total Stem Counts

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Scientific Name	Common Name	Species Type	Annual Means											
			MY3 (2017)			MY2 (2016)			MY1 (2015)			MY0 (2015)		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree			16						2			
Acer rubrum	red maple	Tree			4			30			10			
Alnus serrulata	hazel alder	Shrub	10	10	11	15	15	15	26	26	26	27	27	27
Betula nigra	river birch	Tree	21	21	23	20	20	20	27	27	27	28	28	28
Cornus amomum	silky dogwood	Shrub						2						
Fraxinus pennsylvanica	green ash	Tree	51	51	67	52	52	82	55	55	56	55	55	55
Gleditsia triacanthos	honeylocust	Tree			1									
Ilex opaca	American holly	Tree			1			3						
Juglans nigra	black walnut	Tree									1			
Juniperus virginiana	eastern redcedar	Tree			3									
Liquidambar styraciflua	sweetgum	Tree			129			30			10			
Liriodendron tulipifera	tuliptree	Tree			74			71			32			
Platanus occidentalis	American sycamore	Tree	49	49	235	50	50	115	56	56	101	56	56	56
Quercus michauxii	swamp chestnut oak	Tree	34	34	34	35	35	35	36	36	36	36	36	36
Quercus pagoda	cherrybark oak	Tree	18	18	18	20	20	20	25	25	25	25	25	25
Quercus phellos	willow oak	Tree	16	16	16	18	18	18	30	30	30	30	30	30
Quercus rubra	northern red oak	Tree			6			40			10			
Rhus	sumac	Shrub			1									
Rhus copallinum	flameleaf sumac	Shrub			2									
Ulmus	elm	Tree			9									
Stem count			199	199	650	210	210	481	255	255	366	257	257	257
size (ares)			16			16			16			16		
size (ACRES)			0.40			0.40			0.40			0.40		
Species count			7	7	18	7	7	13	7	7	13	7	7	7
Stems per ACRE			503	503	1,644	531	531	1,217	645	645	926	650	650	650

Color Coding for Table

Exceeds requirements by 10%
Exceeds requirements, but by less than 10%
Fails to meet requirements, by less than 10%
Fails to meet requirements by more than 10%
Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

APPENDIX 4. Morphological Summary Data and Plots

Table 10a. Baseline Stream Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1

Parameter	Gage	PRE-RESTORATION CONDITION		REFERENCE REACH DATA									DESIGN				AS-BUILT/BASELINE						
		UT1 - Reach 2	UT1 - Reach 5	Onsite Reference Reach - UT1A - Reach 3		UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1 - Reach 2		UT1 - Reach 5		UT1 - Reach 2		UT1 - Reach 5			
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max		
Dimension and Substrate - Riffle																							
Bankfull Width (ft)	N/A	6.5	13.9	16.0	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	10.2		12.8		10.2	10.4	11.9	13.6		
Floodprone Width (ft)		10	20	>50	25	25	65	60	>114	14	125	31		22	51	28	64	60	100	200			
Bankfull Mean Depth		0.8	1.5	4.3	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.8		0.9		0.6	0.9	0.8	0.9		
Bankfull Max Depth		1.4	1.9	5.2	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	1.0	1.2	1.2	1.5	1.1	1.4	1.3	1.6		
Bankfull Cross Sectional Area (ft ²)		5.2	24.6	59.0	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	7.9		12.0		6.2	9.0	9.1	11.9		
Width/Depth Ratio		8.2	3.3	10.4	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	13.1		13.6		12.0	16.8	15.5	15.7		
Entrenchment Ratio ¹		1.5	1.2	>3.6	2	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5		2.2	5.0	2.2	5.0	5.9	9.6	14.7	16.8		
Bank Height Ratio ²		2.3	1.0	2.0	1.0	1.0	1.1	1.0		1.0	1.0	--	--	1.0	1.0	1.0	1.0	1.0		1.0			
D50 (mm)		3.47	14.60		---		---		---		---		---		---		---		Silt/Clay		0.11		
Profile																							
Riffle Length (ft)	N/A	---		---		---		---		---		---		---		---		13.9	73.2	23.7	81.3		
Riffle Slope (ft/ft)		---		N/A		0.0040	0.0470	0.0130		0.0184	0.0343	0.0188	0.0704	0.0148	0.0453	0.0118	0.0363	0.0078	0.0317	0.0090	0.0304		
Pool Length (ft)		---		---		---		---		---		---		---		---		17.2		42.8	17.6	76.6	
Pool Max Depth (ft)		2.4	2.5		1.6		1.8		3.3		1.2	1.8	2.6		0.9	3.2	1.1	3.9	1.6	3.7	2.0	4.9	
Pool Spacing (ft)		---		N/A		34	52	71		9	46	27	73	13	67	17	84	31	78	35	103		
Pool Volume (ft ³)		---		---		---		---		---		---		---		---		---		---			
Pattern																							
Channel Beltwidth (ft)	N/A	12	20	48	157	N/A		28	50	38	41	10	50	102		16	74	20	93	20	68	34	72
Radius of Curvature (ft)		6	18	13	86	N/A		19	50	11	15	12	85	23	38	18	31	23	38	18	26	23	38
Rc:Bankfull Width (ft/ft)		0.8	2.3	1.6	10.9	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0	1.8	2.5	1.9	2.8	
Meander Length (ft)		27	45	176	260	N/A		--	--	--	--	53	178	--	--	31	151	38	192	70	120	97	160
Meander Width Ratio		1.5	2.5	6.1	19.9	N/A		3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	1.6	7.3	2.0	6.5	2.9	5.3
Substrate, Bed and Transport Parameters																							
Ri%/Ru%/P%/G%/S%	N/A	---		---		---		---		---		---		---		---		---		---			
SC%/Sa%/G%/C%/B%/Be%		---		---		---		---		---		---		---		---		---		---			
d16/d35/d50/d84/d95/d100		0.33/1.88/3.47/45.0/117/256		0.18/3.2/14.6/128/234/2048		---		---		---		---		---		---		SC/SC/SC/41.3/79.2/128.0		SC/SC/0.11/45.0/104.7/180.0			
Reach Shear Stress (Competency) lb/ft ²		0.43	1.26		---		---		---		---		---		0.49		0.63		0.38	0.56			
Max part size (mm) mobilized at bankfull		---		---		---		---		---		---		---		---		---		---			
Stream Power (Capacity) W/m ²		---		---		---		---		---		---		---		---		---		---			
Additional Reach Parameters																							
Drainage Area (SM)	N/A	0.25		0.56		0.15		0.41		0.96		0.37		0.29		0.25		0.56		0.25		0.56	
Watershed Impervious Cover Estimate (%)		<1%		<1%		---		---		---		---		---		<1%		<1%		<1%		<1%	
Rosgen Classification		G4		E4, G4		B3		E4		E4		E4		C4/E4		C4		C4		C4		C4	
Bankfull Velocity (fps)		2.7	1.7	5.7	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8		2.5-5	2.5-5	2.6	3.4	3.3	3.6				
Bankfull Discharge (cfs)		14	129		37		20		97		35		40		25.0		46.0		17.0	30.9	30.3	42.9	
Q-NFF regression		---		---		---		---		---		---		---		---		---		---			
Q-USGS extrapolation		---		---		---		---		---		---		---		---		---		---			
Q-Mannings		---		---		---		---		---		---		---		---		---		---			
Valley Length (ft)		---		---		---		---		---		---		---		907		1,232		---			
Channel Thalweg Length (ft)		1,132		1,417		---		---		---		---		---		1,114		1,488		1,137		1,535	
Sinuosity		1.14		1.24		1.04		1.40		2.32		1.00	1.30	1.40		1.20	1.30	1.20	1.30	1.20		1.22	
Water Surface Slope (ft/ft) ²		---		---		---		---		---		---		---		---		---		0.0111		0.0122	
Bankfull Slope (ft/ft)		0.0093	0.0190	0.0005	0.0130	0.0490		0.0120		0.0047		0.0190	0.0220	0.0150		0.0070	0.0150	0.0054	0.0172	0.0096		0.0104	

(---): Data was not provided

N/A: Not Applicable

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 10b. Baseline Stream Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1A

Parameter	Gage	PRE-RESTORATION CONDITION				REFERENCE REACH DATA								DESIGN				AS-BUILT/BASELINE					
		UT1A - Reach 1		UT1A - Reach 4		Onsite Reference Reach - UT1A - Reach 3		UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1A - Reach 1		UT1A - Reach 4		UT1A - Reach 1		UT1A - Reach 4	
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																							
Bankfull Width (ft)	N/A	5.8	9.3	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	8.0	8.2	8.0	8.1							
Floodprone Width (ft)	N/A	15	>80	25	25	65	60	>114	14	125	31	18	40	18	41	50	200						
Bankfull Mean Depth	N/A	1.1	1.0	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.6	0.6	0.5	0.6							
Bankfull Max Depth	N/A	1.4	1.5	1.0	1.4	1.7	2.1	2.6	1	1.2	1.2	1.6	0.7	0.9	0.8	1.0	0.9	1.8					
Bankfull Cross Sectional Area (ft ²)	N/A	6.3	9.3	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	4.8	5.0	4.0	5.0							
Width/Depth Ratio	N/A	5.3	9.0	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	13.4	13.6	15.9	13.2							
Entrenchment Ratio ¹	N/A	2.6	>8.6	2	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5	2.2	5.0	2.2	5.0	6.3	24.8						
Bank Height Ratio ²	N/A	1.7	1.5	1.0	1.0	1.1	1.0	1.0	1.0	1.0	--	--	1.0	1.0	1.0	1.0	1.0						
D50 (mm)	N/A	4.31	5.06	---	---	---	---	---	---	---	---	---	---	---	---	---	1.41	0.25					
Profile																							
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	15.5	42.0	20.5	51.9			
Riffle Slope (ft/ft)	N/A	---	---	N/A	0.0040	0.0470	0.0130	0.0184	0.0343	0.0188	0.0704	0.0148	0.0453	0.0212	0.0652	0.0077	0.0505	0.0109	0.0449				
Pool Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	5.4	52.2	9.1	35.5			
Pool Max Depth (ft)	N/A	1.8	3.6	1.6	1.8	3.3	1.2	1.8	2.6	0.7	2.4	0.7	2.5	1.6	3.5	1.4	3.1						
Pool Spacing (ft)	N/A	---	---	N/A	34	52	71	9	46	27	73	10	53	11	54	20	85	45	82				
Pool Volume (ft ³)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---					
Pattern																							
Channel Beltwidth (ft)	N/A	30	35	N/A	N/A	N/A	28	50	38	41	10	50	102	13	58	13	60	24	60	35	55		
Radius of Curvature (ft)	N/A	12	57	N/A	N/A	N/A	19	50	11	15	12	85	23	38	14	24	15	25	14	23	15	23	
Rc:Bankfull Width (ft/ft)	N/A	1.5	7.2	N/A	N/A	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0	1.8	2.9	1.9	2.8	
Meander Length (ft)	N/A	89	104	N/A	N/A	N/A	--	--	--	--	53	178	--	--	24	120	25	123	70	112	96	117	
Meander Width Ratio	N/A	3.8	4.4	N/A	N/A	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	1.6	7.3	3.0	7.5	4.3	6.8	
Substrate, Bed and Transport Parameters																							
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---				
SC%/Sa%/G%/C%/B%/Be%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---				
d16/d35/d50/d84/d95/d100	N/A	0.15/2.18/4.31/16/139/256	0.45/2.71/5.06/67.7/122/362	---	---	---	---	---	---	---	---	---	---	---	---	---	SC/SC/1.41/33.4/64.0/128.0	SC/SC/0.25/26.2/75.9/180.0					
Reach Shear Stress (Competency) lb/ft ²	N/A	0.50	1.76	---	---	---	---	---	---	---	---	---	0.48	0.54	0.38	0.49							
Max part size (mm) mobilized at bankfull	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---							
Stream Power (Capacity) W/m ²	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---							
Additional Reach Parameters																							
Drainage Area (SM)	N/A	0.12	0.16	0.15	0.41	0.96	0.37	0.29	0.12	0.16	0.12	0.16											
Watershed Impervious Cover Estimate (%)	N/A	<1%	<1%	---	---	---	---	---	<1%	<1%	<1%	<1%											
Rosgen Classification	N/A	E4	E4	83	E4	E4	E4	C4/E4	C4	C4	C4	C4											
Bankfull Velocity (fps)	N/A	3.3	5.2	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8	2.5-5	2.5-5	2.6	3.0								
Bankfull Discharge (cfs)	N/A	21	50	37	20	97	35	40	14.0	17.0	15.9	15.0											
Q-NFF regression	N/A	---	---	---	---	---	---	---	---	---	---	---											
Q-USGS extrapolation	N/A	---	---	---	---	---	---	---	---	---	---	---											
Q-Mannings	N/A	---	---	---	---	---	---	---	---	---	---	---											
Valley Length (ft)	N/A	---	---	---	---	---	---	---	673	530	---	---											
Channel Thalweg Length (ft)	N/A	770	461	---	---	---	---	---	849	650	857	666											
Sinuosity	N/A	1.12	1.03	1.04	1.40	2.32	1.00	1.30	1.40	1.20	1.30	1.20	1.30	1.21	1.25								
Water Surface Slope (ft/ft) ²	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	0.0126	N/A							
Bankfull Slope (ft/ft)	N/A	0.0095	0.0150	0.0490	0.0120	0.0047	0.0190	0.0220	0.0150	0.0103	0.0175	0.0141	0.0153	0.0137	0.0129								

(---): Data was not provided

N/A: Not Applicable

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 10c. Baseline Stream Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1B

Parameter	Gage	PRE-RESTORATION		REFERENCE REACH DATA								DESIGN		AS-BUILT/BASELINE		
		UT1B	Onsite Reference Reach - UT1A - Reach 3	UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1B	UT1B			
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
Dimension and Substrate - Riffle																
Bankfull Width (ft)	N/A	4.9	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	7.3		7.7		
Floodprone Width (ft)		36	25	25	65	60	>114	14	125	31		16	37	70		
Bankfull Mean Depth		1.1	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.6		0.5		
Bankfull Max Depth		1.9	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	0.7	0.9	0.7		
Bankfull Cross Sectional Area (ft ²)		5.4	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	5.2		3.5		
Width/Depth Ratio		4.4	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	12.6		17.0		
Entrenchment Ratio ¹		7.5	2.3	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5		2.2	5.0	9.1		
Bank Height Ratio ²		1.6	1.0	1.0	1.1	1.0		1.0	1.0	--	--	1.0	1.0	1.0		
D50 (mm)		---	---	---	---	---	---	---	---	---	---	---	---	---	Silt/Clay	
Profile																
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	12.1	24.4	
Riffle Slope (ft/ft)		---	N/A	0.0040	0.0470	0.0130		0.0184	0.0343	0.0188	0.0704	0.0222	0.0680	0.0219	0.0425	
Pool Length (ft)		---	---	---	---	---	---	---	---	---	---	---	---	11.9	30.9	
Pool Max Depth (ft)		2.5	1.6	1.8		3.3		1.2	1.8	2.6		0.7	2.4	1.7	2.5	
Pool Spacing (ft)		---	N/A	34	52	71		9	46	27	73	9	48	30	45	
Pool Volume (ft ³)		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Pattern																
Channel Beltwidth (ft)	N/A	N/A	N/A	N/A	28	50	38	41	10	50	102		12	53	25	40
Radius of Curvature (ft)		N/A	N/A	N/A	19	50	11	15	12	85	23	38	13	22	14	20
Rc:Bankfull Width (ft/ft)		N/A	N/A	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	2.6
Meander Length (ft)		N/A	N/A	N/A	--	--	--	--	53	178	--	--	22	110	60	72
Meander Width Ratio		N/A	N/A	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	3.2	5.2
Substrate, Bed and Transport Parameters																
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
SC%/Sa%/G%/C%/B%/Be%		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
d16/d35/d50/d84/d95/d100		---	---	---	---	---	---	---	---	---	---	---	---	---	SC/SC/SC/ 19.5/40.2/90.0	
Reach Shear Stress (Competency) lb/ft ²		---	---	---	---	---	---	---	---	---	---	---	---	---	0.21	
Max part size (mm) mobilized at bankfull		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Stream Power (Capacity) W/m ²		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Additional Reach Parameters																
Drainage Area (SM)	N/A	0.10	0.15	0.41		0.96		0.37		0.29		0.10		0.10		
Watershed Impervious Cover Estimate (%)		<1%	---	---	---	---	---	---	---	---	---	---	---	---	---	
Rosgen Classification		E4	B3	E4		E4		E4		C4/E4		C4		C4		
Bankfull Velocity (fps)		4.6	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8		1.5-4		1.9		
Bankfull Discharge (cfs)		25	37	20		97		35		40		11		6.6		
Q-NFF regression		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-USGS extrapolation		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-Mannings		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Valley Length (ft)		---	---	---	---	---	---	---	---	---	---	---	199	---	---	
Channel Thalweg Length (ft)		243	---	---	---	---	---	---	---	---	---	---	219	---	232	
Sinuosity		1.06	1.04	1.40		2.32		1.00	1.30	1.40		1.20	1.30	1.34		
Water Surface Slope (ft/ft) ²		---	---	---	---	---	---	---	---	---	---	---	---	---	0.0095	
Bankfull Slope (ft/ft)		0.0200	0.0490	0.0120		0.0047		0.0190	0.0220	0.0150		0.0100	0.0200	0.0181		

(---): Data was not provided

N/A: Not Applicable

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 10d. Baseline Stream Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT2

Parameter	Gage	PRE-RESTORATION		REFERENCE REACH DATA								DESIGN		AS-BUILT/BASELINE		
		UT2	Onsite Reference Reach - UT1A - Reach 3	UT to Polecat Creek	Spencer Creek 1	Spencer Creek 2	UT To Cane Creek	UT2	UT2							
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
Dimension and Substrate - Riffle																
Bankfull Width (ft)		6.2	9.6	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	6.6	6.7		
Floodprone Width (ft)		>20		25	25	65	60	>114	14	125	31		15	33	50	
Bankfull Mean Depth		0.6	1.1	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.5	0.5		
Bankfull Max Depth		1.0	2.0	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	0.6	0.8	0.7	
Bankfull Cross Sectional Area (ft ²)	N/A	5.2	7.0	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	3.4	3.4		
Width/Depth Ratio		5.5	15.5	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	12.8	12.9		
Entrenchment Ratio ¹		>2.4		2.3	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5		2.2	5.0	7.5	
Bank Height Ratio ²		1.0	2.1	1.0	1.0	1.1	1.0	1.0	1.0	1.0	--	--	1.0	1.0	1.0	
D50 (mm)		2.11		---	---	---	---	---	---	---	---	---	---	---	Silt/Clay	
Profile																
Riffle Length (ft)		---		---	---	---	---	---	---	---	---	---	---	13.9	51.7	
Riffle Slope (ft/ft)		---		N/A	0.0040	0.0470	0.0130	0.0184	0.0343	0.0188	0.0704	0.0179	0.0549	0.0146	0.0525	
Pool Length (ft)		---		---	---	---	---	---	---	---	---	---	---	10.0	28.4	
Pool Max Depth (ft)	N/A	1.4		1.6		1.8		3.3	1.2	1.8		2.6	0.6	2.1	1.0	2.4
Pool Spacing (ft)		---		N/A	34	52	71	9	46	27	73	9	44	25	66	
Pool Volume (ft ³)		---		---	---	---	---	---	---	---	---	---	---	---	---	
Pattern																
Channel Beltwidth (ft)		32	54	N/A	28	50	38	41	10	50	102	11	48	19	50	
Radius of Curvature (ft)		12	43	N/A	19	50	11	15	12	85	23	38	12	20	12	20
Rc:Bankfull Width (ft/ft)	N/A	1.5	5.4	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0
Meander Length (ft)		102	103	N/A	--	--	--	--	53	178	--	--	20	99	58	98
Meander Width Ratio		4.1	6.8	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	2.8	7.5
Substrate, Bed and Transport Parameters																
Ri%/Ru%/P%/G%/S%		---		---	---	---	---	---	---	---	---	---	---	---	---	
SC%/Sa%/G%/C%/B%/Be%		---		---	---	---	---	---	---	---	---	---	---	---	---	
d16/d35/d50/d84/d95/d100	N/A	0.2/0.68/2.11/20.7/98.3/256		---	---	---	---	---	---	---	---	---	---	---	SC/SC/SC/30.2/64.0/128.0	
Reach Shear Stress (Competency) lb/ft ²		---		---	---	---	---	---	---	---	---	---	---	0.64		
Max part size (mm) mobilized at bankfull		---		---	---	---	---	---	---	---	---	---	---	---		
Stream Power (Capacity) W/m ²		---		---	---	---	---	---	---	---	---	---	---	---		
Additional Reach Parameters																
Drainage Area (SM)		0.09		0.15		0.41		0.96		0.37		0.29		0.09		0.09
Watershed Impervious Cover Estimate (%)		<1%		---		---		---		---		---		<1%		<1%
Rosgen Classification		E4		B3		E4		E4		E4		C4/E4		C4		C4
Bankfull Velocity (fps)		3.0	5.1	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8		2.5-5		3.4	
Bankfull Discharge (cfs)		23		37		20		97		35		40		11.0		11.5
Q-NFF regression		---		---		---		---		---		---		---		---
Q-USGS extrapolation		---		---		---		---		---		---		---		---
Q-Mannings		---		---		---		---		---		---		---		---
Valley Length (ft)		---		---		---		---		---		---		905		---
Channel Thalweg Length (ft)		1,028		---		---		---		---		---		1,023		1,032
Sinuosity		1.06		1.04		1.40		2.32	1.00	1.30		1.40	1.20	1.30		1.16
Water Surface Slope (ft/ft) ²		---		---		---		---		---		---		---		0.0207
Bankfull Slope (ft/ft)		0.0130	0.0220	0.0490	0.0120	0.0047	0.0190	0.0220	0.0150	0.0121	0.0231	0.0195				0.0195

(---): Data was not provided

N/A: Not Applicable

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 11. Morphology and Hydraulic Summary (Dimensional Parameters - Cross Section)

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 2																																
Cross Section 1 (Riffle)								Cross Section 2 (Pool)								Cross Section 3 (Riffle)								Cross Section 4 (Pool)								
Dimension and Substrate	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7
<i>based on fixed bankfull elevation (ft)</i>	651.7	651.7	651.7	651.7					651.0	651.0	651.0	651.0					644.0	644.0	644.0	644.0					643.6	643.6	643.6	643.6				
Bankfull Width (ft)	10.4	9.9	10.5	10.9					9.6	9.3	9.3	8.9					10.6	10.2	9.7	9.2					13.5	13.7	12.9	13.3				
Floodprone Width (ft)	100	100	100	100					N/A	N/A	N/A	N/A					60	60	60	60					N/A	N/A	N/A	N/A				
Bankfull Mean Depth (ft)	0.9	0.8	0.7	0.7					1.2	1.1	1.2	1.2					0.6	0.6	0.5	0.5					1.1	1.0	1.0	1.0				
Bankfull Max Depth (ft)	1.4	1.4	1.4	1.4					2.1	1.9	2.0	1.9					1.1	1.1	1.1	1.0					1.9	1.8	1.9	1.9				
Bankfull Cross Sectional Area (ft ²)	9.0	8.0	7.8	7.9					11.6	10.4	11.2	10.3					6.2	6.2	5.3	4.9					14.7	14.2	13.3	13.6				
Bankfull Width/Depth Ratio	12.0	12.2	14.2	15.1					7.9	8.3	7.7	7.6					18.2	16.7	17.7	17.5					12.4	13.2	12.5	13.1				
Entrenchment Ratio ¹	9.6	10.1	9.5	9.2					N/A	N/A	N/A	N/A					5.6	5.9	6.2	6.5					N/A	N/A	N/A	N/A				
Bankfull Bank Height Ratio ²	1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0				
d50 (mm)	18.0	64.0	10.4	27.2					N/A	N/A	N/A	N/A					13.3	46.6	22.6	23.0					N/A	N/A	N/A	N/A				
UT1 Reach 5																																
Cross Section 5 (Pool)								Cross Section 6 (Riffle)								Cross Section 7 (Riffle)								Cross Section 8 (Pool)								
<i>based on fixed bankfull elevation (ft)</i>	610.4	610.4	610.4	610.4					610.0	610.0	610.0	610.0					600.9	600.9	600.9	600.9					600.6	600.6	600.6	600.6				
Bankfull Width (ft)	15.9	16.5	16.7	17.1					15.3	15.2	16.0	15.1					11.9	11.9	11.8	12.0					15.2	15.7	16.1	16.1				
Floodprone Width (ft)	N/A	N/A	N/A	N/A					200	200	200	200					200	200	200	200					N/A	N/A	N/A	N/A				
Bankfull Mean Depth (ft)	1.2	1.1	1.2	1.1					0.8	0.8	0.8	0.8					0.8	0.8	0.8	0.7					1.4	1.4	1.3	1.3				
Bankfull Max Depth (ft)	2.4	2.2	2.4	2.4					1.6	1.7	1.8	1.8					1.3	1.5	1.4	1.3					2.7	2.8	2.8	2.7				
Bankfull Cross Sectional Area (ft ²)	18.5	18.1	19.3	19.4					12.0	12.6	12.5	12.5					9.1	10.1	9.3	8.8					21.3	21.8	21.1	20.4				
Bankfull Width/Depth Ratio	13.6	15.1	14.4	15.1					19.5	18.4	20.5	18.2					15.7	14.0	14.9	16.3					10.9	11.3	12.3	12.7				
Entrenchment Ratio ¹	N/A	N/A	N/A	N/A					13.1	13.1	12.5	13.3					16.8	16.8	17.0	16.7					N/A	N/A	N/A	N/A				
Bankfull Bank Height Ratio ²	1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0				
d50 (mm)	N/A	N/A	N/A	N/A					15.4	30.8	57.9	29.6					16.0	52.1	70.5	40.2					N/A	N/A	N/A	N/A				
UT1A Reach 1														UT1A Reach 4																		
Cross Section 9 (Riffle)								Cross Section 10 (Pool)								Cross Section 11 (Riffle)								Cross Section 12 (Pool)								
<i>based on fixed bankfull elevation (ft)</i>	656.4	656.4	656.4	656.4					656.0	656.0	656.0	656.0					615.8	615.8	615.8	615.8					615.1	615.1	615.1	615.1				
Bankfull Width (ft)	8.0	7.3	7.2	6.7					10.5	10.0	10.2	9.4					8.1	8.2	8.2	8.9					10.6	10.5	10.5	10.8				
Floodprone Width (ft)	50	50	50	50					N/A	N/A	N/A	N/A					200	200	200	200					N/A	N/A	N/A	N/A				
Bankfull Mean Depth (ft)	0.5	0.5	0.5	0.5					0.7	0.7	0.7	0.7					0.6	0.8	0.8	0.8					1.2	1.2	1.2	1.1				
Bankfull Max Depth (ft)	0.9	0.9	0.8	0.8					1.5	1.2	1.3	1.3					1.8	1.9	1.9	1.8					2.7	2.6	2.6	2.5				
Bankfull Cross Sectional Area (ft ²)	4.0	3.9	3.8	3.3					7.8	7.0	6.7	6.5					5.0	6.6	6.5	6.7					12.3	13.2	13.1	12.4				
Bankfull Width/Depth Ratio	15.9	13.7	13.8	13.4					14.1	14.4	15.5	13.5					13.2	10.1	10.4	11.7					9.1	8.4	8.4	9.4				
Entrenchment Ratio ¹	6.3	6.8	6.9	7.5					N/A	N/A	N/A	N/A					24.8	24.4	24.4	22.6					N/A	N/A	N/A	N/A				
Bankfull Bank Height Ratio ²	1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0				
d50 (mm)	18.0	17.8	25.2	38.8					N/A	N/A	N/A	N/A					18.3	42.1	28.5	22.6					N/A	N/A	N/A	N/A				
UT1B														UT2																		
Cross Section 13 (Riffle)								Cross Section 14 (Pool)								Cross Section 15 (Riffle)								Cross Section 16 (Pool)								
<i>based on fixed bankfull elevation (ft)</i>	647.1	647.1	647.1	647.1					646.9	646.9	646.9	646.9					602.9	602.9	602.9	602.9					602.4	602.4	602.4	602.4				
Bankfull Width (ft)	7.7	7.8	7.7	7.4					9.7	10.1	9.8	10.0					7.1	7.0	6.8	6.6					9.5	9.5	9.9	9.9				
Floodprone Width (ft)	70	70	70	70					N/A	N/A	N/A	N/A					50	50	50	50					N/A	N/A	N/A	N/A				
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4					0.8	0.7	0.7	0.7					0.5	0.5	0.5	0.5					0.6	0.6	0.6	0.6				
Bankfull Max Depth (ft)	0.7	0.9	0.8	0.8					1.4	1.3	1.4	1.3					0.7	0.9	0.9	0.8					1.3	1.3	1.3	1.3				
Bankfull Cross Sectional Area (ft ²)	3.5	3.6	3.2	2.7					7.8	7.2	7.2	6.6					3.4	3.8	3.5	3.3					5.8	5.5	5.8	5.7				
Bankfull Width/Depth Ratio	17.0	16.9	18.3	20.6					12.1	14.2	13.5	15.0					14.7	12.9	13.5	13.5					15.5	16.3	16.8	17.0				
Entrenchment Ratio ¹	9.1	9.0	9.1	9.4					N/A	N/A	N/A	N/A					7.0	7.2	7.3	7.5					N/A	N/A	N/A	N/A				
Bankfull Bank Height Ratio ²	1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0					1.0	1.0	1.0	1.0				
d50 (mm)	21.3	43.9	26.9	23.2					N/A	N/A	N/A	N/A					19.7	25.0	23.5	29.3					N/A	N/A	N/A	N/A				

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12a. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1 Reach 2																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	10.2	10.4	9.9	10.2	9.7	10.5	9.2	10.9								
Floodprone Width (ft)	60	100	60	100	60	100	60	100								
Bankfull Mean Depth	0.6	0.9	0.6	0.8	0.5	0.7	0.5	0.7								
Bankfull Max Depth	1.1	1.4	1.1	1.4	1.1	1.4	1.0	1.4								
Bankfull Cross Sectional Area (ft ²)	6.2	9.0	6.2	8.0	5.3	7.8	4.9	7.9								
Width/Depth Ratio	12.0	16.8	12.2	16.7	14.2	17.7	15.1	17.5								
Entrenchment Ratio ¹	5.9	9.6	5.9	10.1	6.2	9.5	6.5	9.2								
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	13.3	18.0	46.6	64.0	10.4	22.6	23.0	27.2								
Profile																
Riffle Length (ft)	13.9	73.2														
Riffle Slope (ft/ft)	0.0078	0.0317														
Pool Length (ft)	17.2	42.8														
Pool Max Depth (ft)	1.6	3.7														
Pool Spacing (ft)	31	78														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	20	68														
Radius of Curvature (ft)	18	26														
Rc:Bankfull Width (ft/ft)	1.8	2.5														
Meander Wave Length (ft)	70	120														
Meander Width Ratio	2.0	6.5														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,137															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0111															
Bankfull Slope (ft/ft)	0.0096															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC/41.3/79.2/128.0		SC/0.28/9.9/93.6/145.5/180.0		0.56\2.57\4.8\64.0\117.2\512.0		0.52\2.43\4.6\34.3\102.1\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12b. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1 Reach 5																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	11.9	13.6	11.9	15.2	11.8	16.0	12.0	15.1								
Floodprone Width (ft)	200		200		200		200									
Bankfull Mean Depth	0.8	0.9	0.8	0.8	0.8	0.8	0.7	0.8								
Bankfull Max Depth	1.3	1.6	1.5	1.7	1.4	1.8	1.3	1.8								
Bankfull Cross Sectional Area (ft ²)	9.1	11.9	10.1	12.6	9.3	12.5	8.8	12.5								
Width/Depth Ratio	15.5	15.7	14.0	18.4	14.9	20.5	16.3	18.2								
Entrenchment Ratio ¹	14.7	16.8	13.1	16.8	12.5	17.0	13.3	16.7								
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	15.4	16.0	30.8	52.1	57.9	70.5	29.6	40.2								
Profile																
Riffle Length (ft)	23.7	81.3														
Riffle Slope (ft/ft)	0.0090	0.0304														
Pool Length (ft)	17.6	76.6														
Pool Max Depth (ft)	2.0	4.9														
Pool Spacing (ft)	35	103														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	34	72														
Radius of Curvature (ft)	23	38														
Rc:Bankfull Width (ft/ft)	1.9	2.8														
Meander Wave Length (ft)	97	160														
Meander Width Ratio	2.9	5.3														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,535															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0122															
Bankfull Slope (ft/ft)	0.0104															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC/0.11/45.0/104.7/180.0		SC/4.47\20.1\74.9\128.0\362.0		0.18\4.00\20.7\75.9\139.4\512.0		SC/0.50\17.1\70.2\104.7\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12c. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1A Reach 1																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	8.0		7.3		7.2		6.7									
Floodprone Width (ft)	50		50		50		50									
Bankfull Mean Depth	0.5		0.5		0.5		0.5									
Bankfull Max Depth	0.9		0.9		0.8		0.8									
Bankfull Cross Sectional Area (ft ²)	4.0		3.9		3.8		3.3									
Width/Depth Ratio	15.9		13.7		13.8		13.4									
Entrenchment Ratio ¹	6.3		6.8		6.9		7.5									
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	18.0		17.8		25.2		38.8									
Profile																
Riffle Length (ft)	15.5	41.97														
Riffle Slope (ft/ft)	0.0077	0.0505														
Pool Length (ft)	5.4	52.2														
Pool Max Depth (ft)	1.6	3.5														
Pool Spacing (ft)	20	85														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	24	60														
Radius of Curvature (ft)	14	23														
Rc:Bankfull Width (ft/ft)	1.8	2.9														
Meander Wave Length (ft)	70	112														
Meander Width Ratio	3.0	7.5														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	857															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0126															
Bankfull Slope (ft/ft)	0.0137															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC\1.41\33.4\64.0\128.0		0.16\2.24\11.0\42.0\73.4\180.0		0.50\6.01\15.2\52.1\75.9\1512.0		SC\0.95\17.3\56.3\83.4\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12d. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1A Reach 4																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	8.1		8.2		8.2		8.9									
Floodprone Width (ft)	200		200		200		200									
Bankfull Mean Depth	0.6		0.8		0.8		0.8									
Bankfull Max Depth	1.8		1.9		1.9		1.8									
Bankfull Cross Sectional Area (ft ²)	5.0		6.6		6.5		6.7									
Width/Depth Ratio ¹	13.2		10.1		10.4		11.7									
Entrenchment Ratio ¹	24.8		24.4		24.4		22.6									
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	18.3		42.1		28.5		22.6									
Profile																
Riffle Length (ft)	20.5	51.9														
Riffle Slope (ft/ft)	0.0109	0.0449														
Pool Length (ft)	9.1	35.5														
Pool Max Depth (ft)	1.4	3.1														
Pool Spacing (ft)	45	82														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	35	55														
Radius of Curvature (ft)	15	23														
Rc:Bankfull Width (ft/ft)	1.9	2.8														
Meander Wave Length (ft)	96	117														
Meander Width Ratio	4.3	6.8														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	666															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	N/A															
Bankfull Slope (ft/ft)	0.0129															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC/0.25/26.2/75.9/180.0		SC\4.00\23.4\77.8\119.3\180.0		0.50\7.10\27.6\93.2\143.4\256.0		0.14\0.63\11.4\53.2\106.9\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12e. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT1B																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	7.7		7.8		7.7		7.4									
Floodprone Width (ft)	70		70		70		70									
Bankfull Mean Depth	0.5		0.5		0.4		0.4									
Bankfull Max Depth	0.7		0.9		0.8		0.8									
Bankfull Cross Sectional Area (ft ²)	3.5		3.6		3.2		2.7									
Width/Depth Ratio	17.0		16.9		18.3		20.6									
Entrenchment Ratio ¹	9.1		9.0		9.1		9.4									
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	21.3		43.9		26.9		23.2									
Profile																
Riffle Length (ft)	12.1	24.4														
Riffle Slope (ft/ft)	0.0219	0.0425														
Pool Length (ft)	11.9	30.9														
Pool Max Depth (ft)	1.7	2.5														
Pool Spacing (ft)	30	45														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	25	40														
Radius of Curvature (ft)	14	20														
Rc:Bankfull Width (ft/ft)	1.8	2.6														
Meander Wave Length (ft)	60	72														
Meander Width Ratio	3.2	5.2														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	232															
Sinuosity (ft)	1.3															
Water Surface Slope (ft/ft)	0.0095															
Bankfull Slope (ft/ft)	0.0181															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC/SC/19.5/40.2/90.0		SC\0.71\5.6\64.0\107.3\180.0		SC\0.40\3.3\40.2\95.4\128.0		SC\0.62\2.5\62.2\144.6\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.

²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 12f. Monitoring Data - Stream Reach Data Summary
 Agony Acres Mitigation Site (DMS Project No. 95716)
 Monitoring Year 3 - 2017

UT2																
Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	7.1		7.0		6.8		6.6									
Floodprone Width (ft)	50		50		50		50									
Bankfull Mean Depth	0.5		0.5		0.5		0.5									
Bankfull Max Depth	0.7		0.9		0.9		0.8									
Bankfull Cross Sectional Area (ft ²)	3.4		3.8		3.5		3.3									
Width/Depth Ratio	14.7		12.9		13.5		13.5									
Entrenchment Ratio ¹	7.0		7.2		7.3		7.5									
Bank Height Ratio ²	1.0		1.0		1.0		1.0									
D50 (mm)	19.7		25.0		23.5		29.3									
Profile																
Riffle Length (ft)	13.9	51.7														
Riffle Slope (ft/ft)	0.0146	0.0525														
Pool Length (ft)	10.0	28.4														
Pool Max Depth (ft)	1.0	2.4														
Pool Spacing (ft)	25	66														
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	19	50														
Radius of Curvature (ft)	12	20														
Rc:Bankfull Width (ft/ft)	1.8	3.0														
Meander Wave Length (ft)	58	98														
Meander Width Ratio	2.8	7.5														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,032															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0207															
Bankfull Slope (ft/ft)	0.0195															
Ri%/Ru%/P%/G%/S%																
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100	SC/SC/30.2/64.0/128.0		SC\2.80\10.7\35.9\75.9\180.0		SC\3.23\12.9\43.6\80.3\180.0		SC\SC\1.3\26.9\64.0\180.0									
% of Reach with Eroding Banks	0%		0%		0%		0%									

¹Entrenchment Ratio is the flood prone width divided by the bankfull width.


²Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 1-UT1 Reach 2

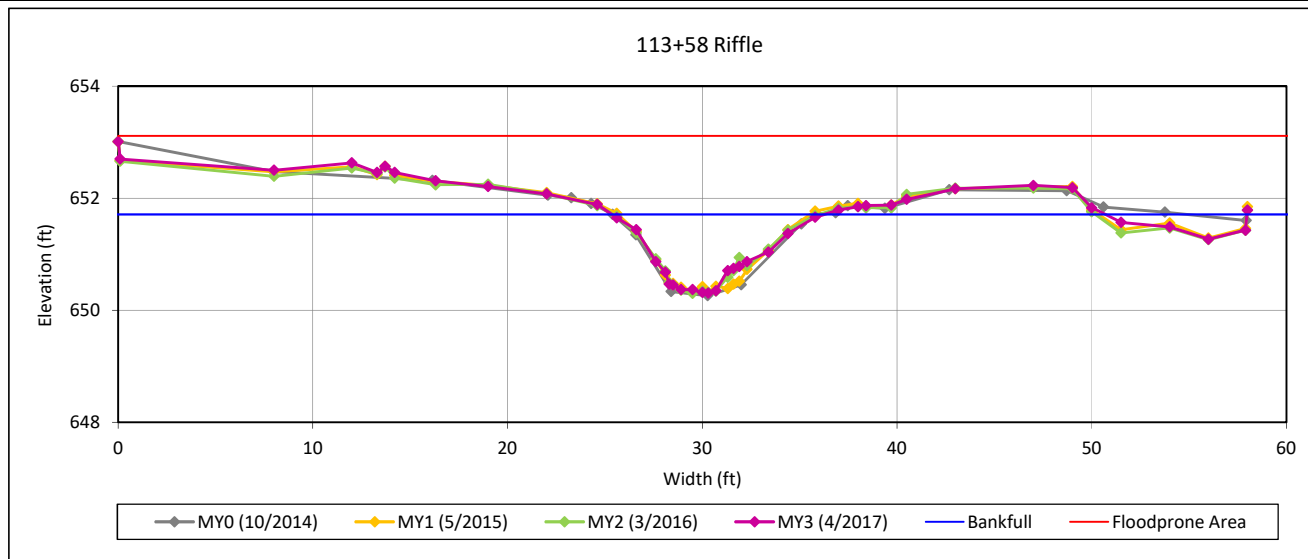

Bankfull Dimensions

7.9	x-section area (ft.sq.)
10.9	width (ft)
0.7	mean depth (ft)
1.4	max depth (ft)
11.4	wetted parimeter (ft)
0.7	hyd radi (ft)
15.1	width-depth ratio
100.0	W flood prone area (ft)
9.2	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 2-UT1 Reach 2

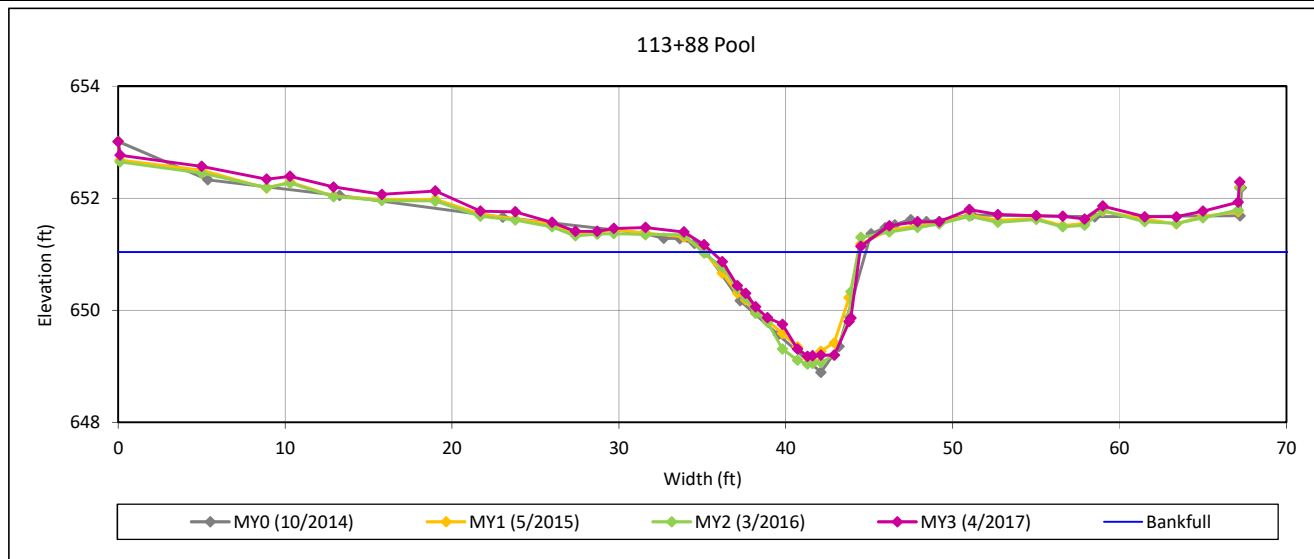

Bankfull Dimensions

10.3	x-section area (ft.sq.)
8.9	width (ft)
1.2	mean depth (ft)
1.9	max depth (ft)
10.2	wetted parimeter (ft)
1.0	hyd radi (ft)
7.6	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 3-UT1 Reach 2

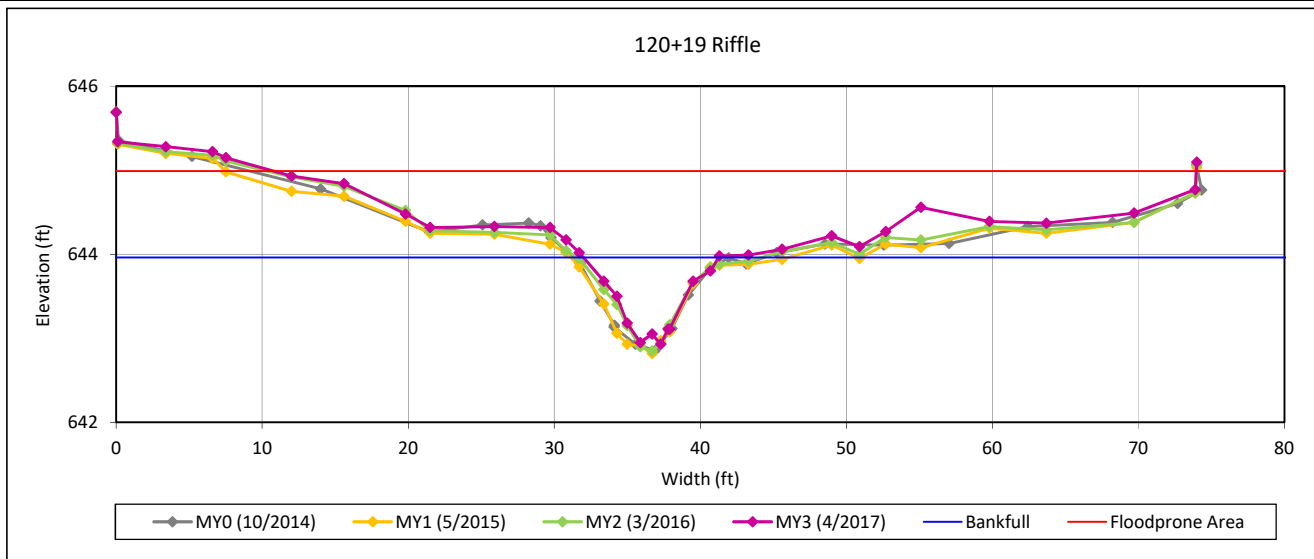

Bankfull Dimensions

4.9	x-section area (ft.sq.)
9.2	width (ft)
0.5	mean depth (ft)
1.0	max depth (ft)
9.6	wetted parimeter (ft)
0.5	hyd radi (ft)
17.5	width-depth ratio
60.0	W flood prone area (ft)
6.5	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 4-UT1 Reach 2

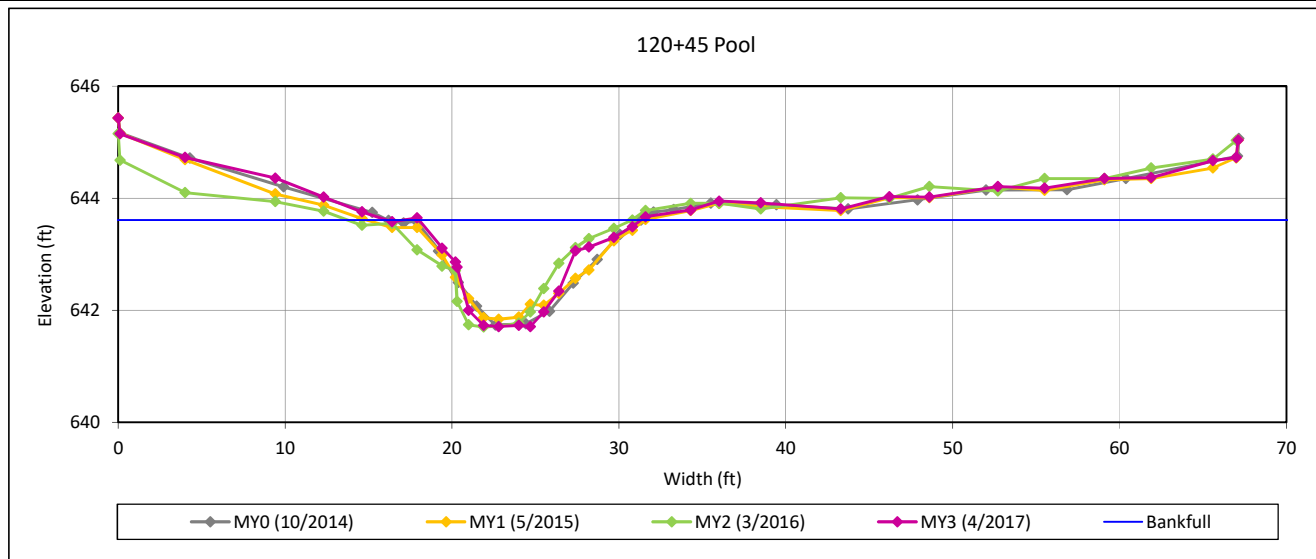

Bankfull Dimensions

13.6	x-section area (ft.sq.)
13.3	width (ft)
1.0	mean depth (ft)
1.9	max depth (ft)
14.3	wetted parimeter (ft)
1.0	hyd radi (ft)
13.1	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 5-UT1 Reach 5

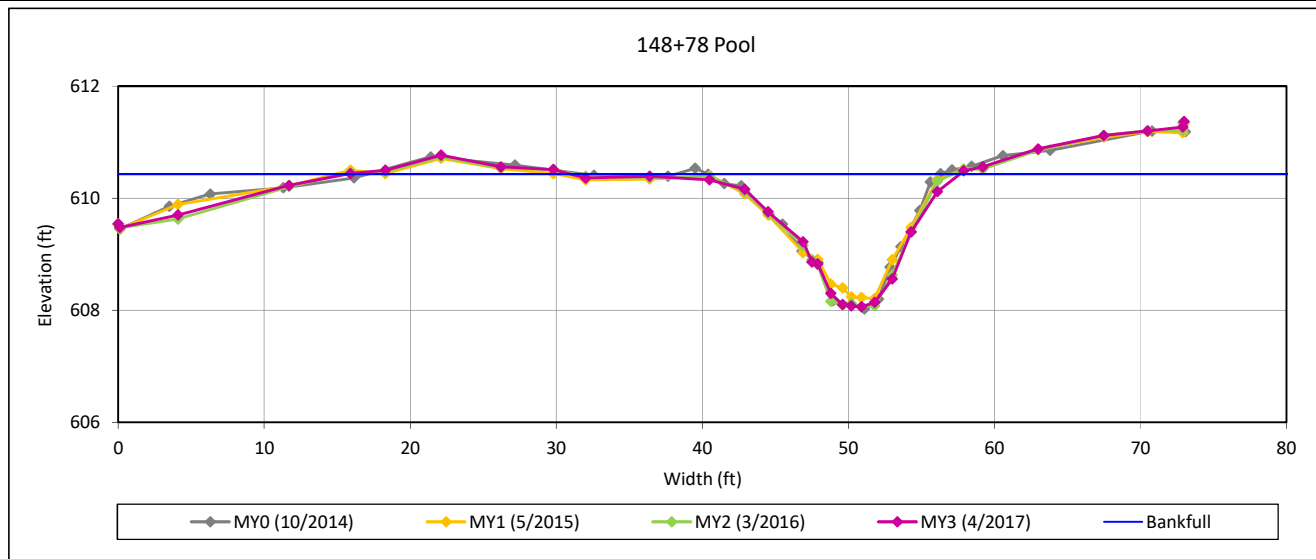

Bankfull Dimensions

19.4	x-section area (ft.sq.)
17.1	width (ft)
1.1	mean depth (ft)
2.4	max depth (ft)
18.0	wetted parimeter (ft)
1.1	hyd radi (ft)
15.1	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

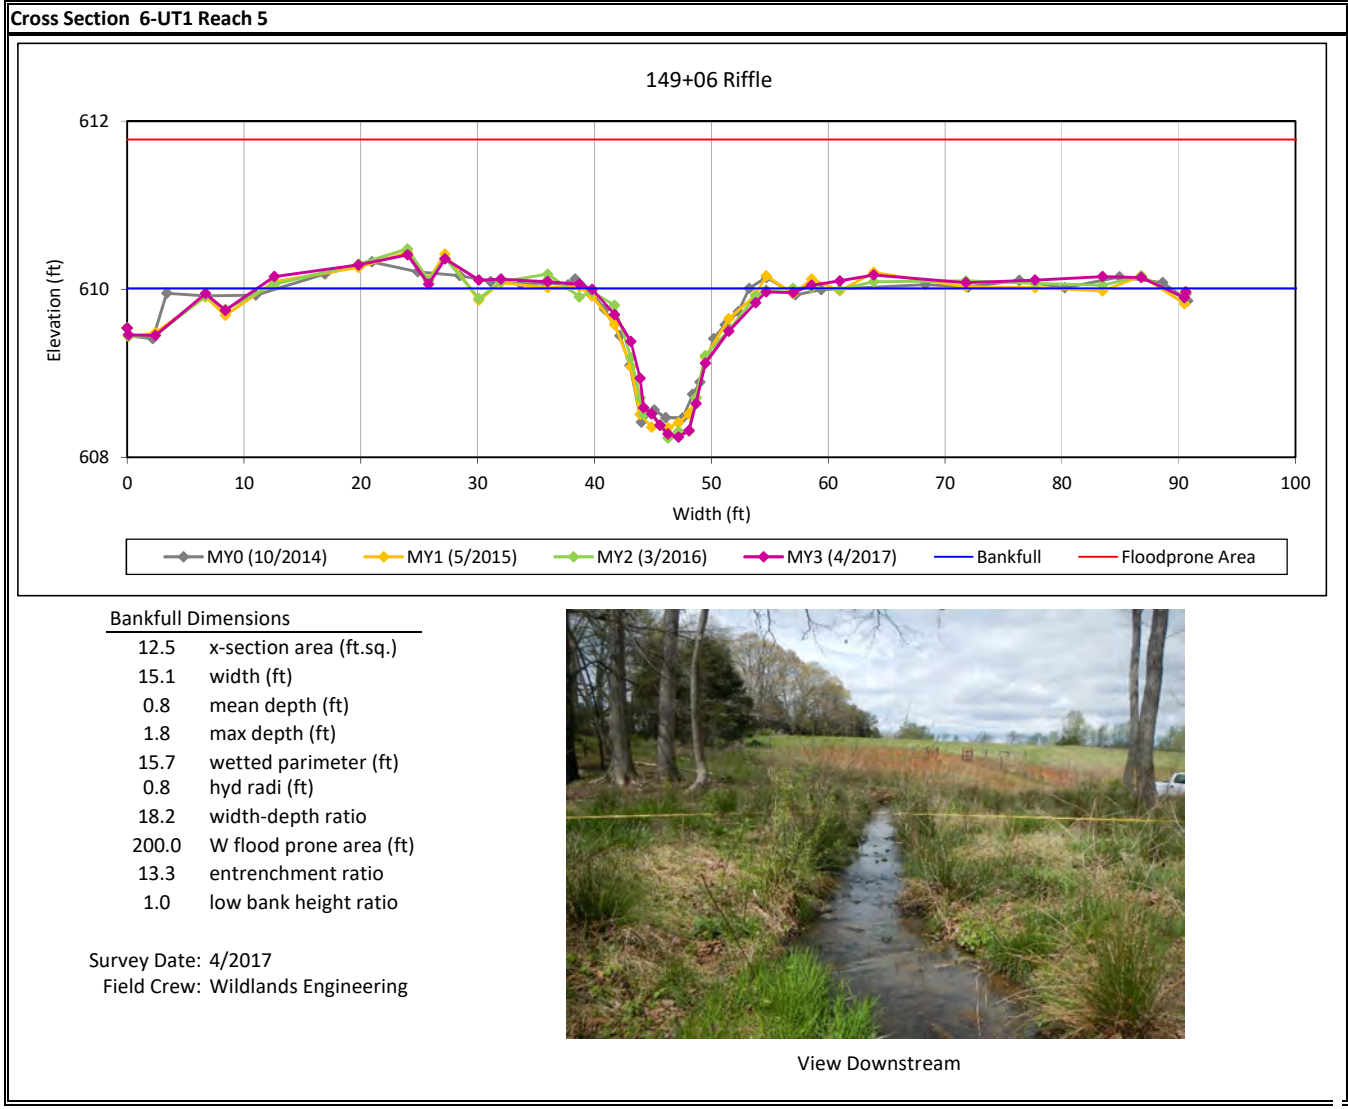


Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 7-UT1 Reach 5

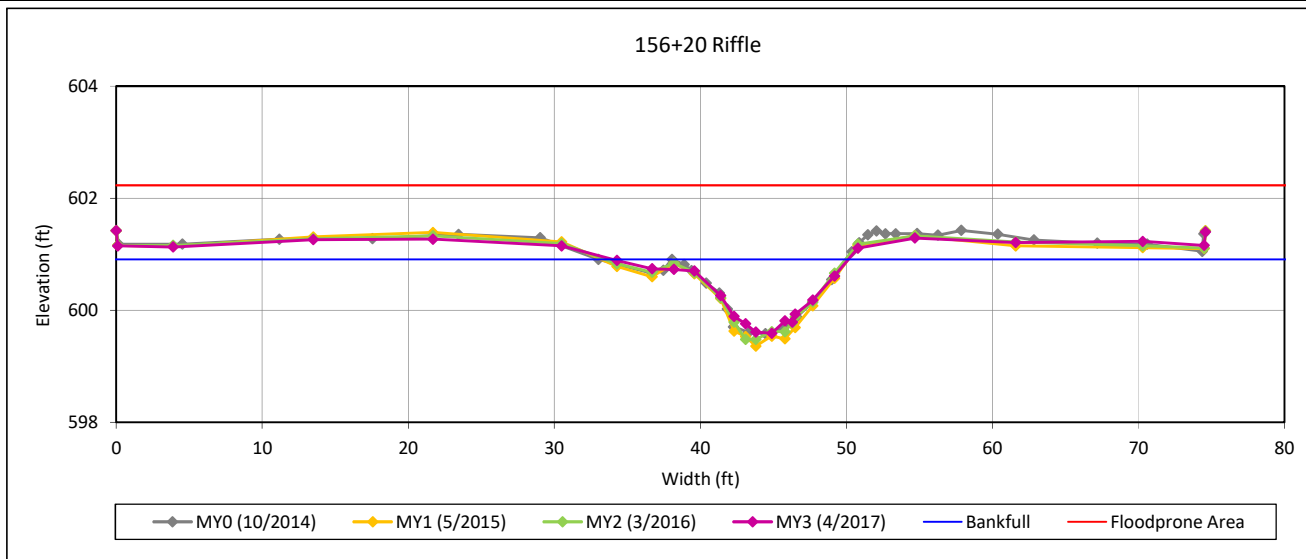

Bankfull Dimensions

8.8	x-section area (ft.sq.)
12.0	width (ft)
0.7	mean depth (ft)
1.3	max depth (ft)
12.3	wetted parimeter (ft)
0.7	hyd radi (ft)
16.3	width-depth ratio
200.0	W flood prone area (ft)
16.7	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 8-UT1 Reach 5

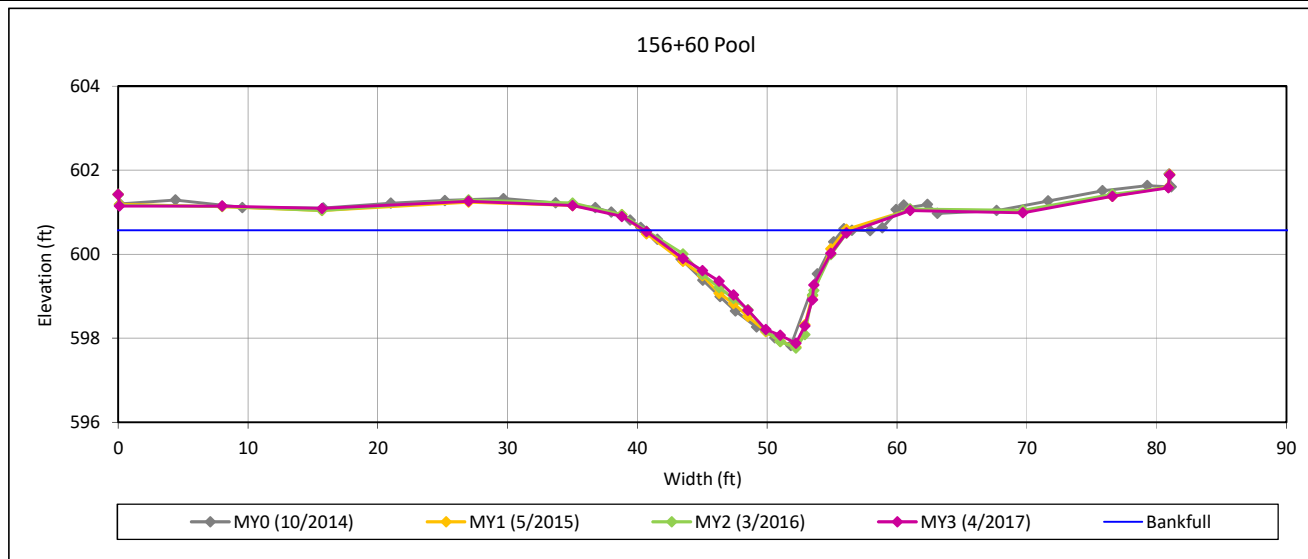

Bankfull Dimensions

20.4	x-section area (ft.sq.)
16.1	width (ft)
1.3	mean depth (ft)
2.7	max depth (ft)
17.4	wetted parimeter (ft)
1.2	hyd radi (ft)
12.7	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 9-UT1A Reach 1

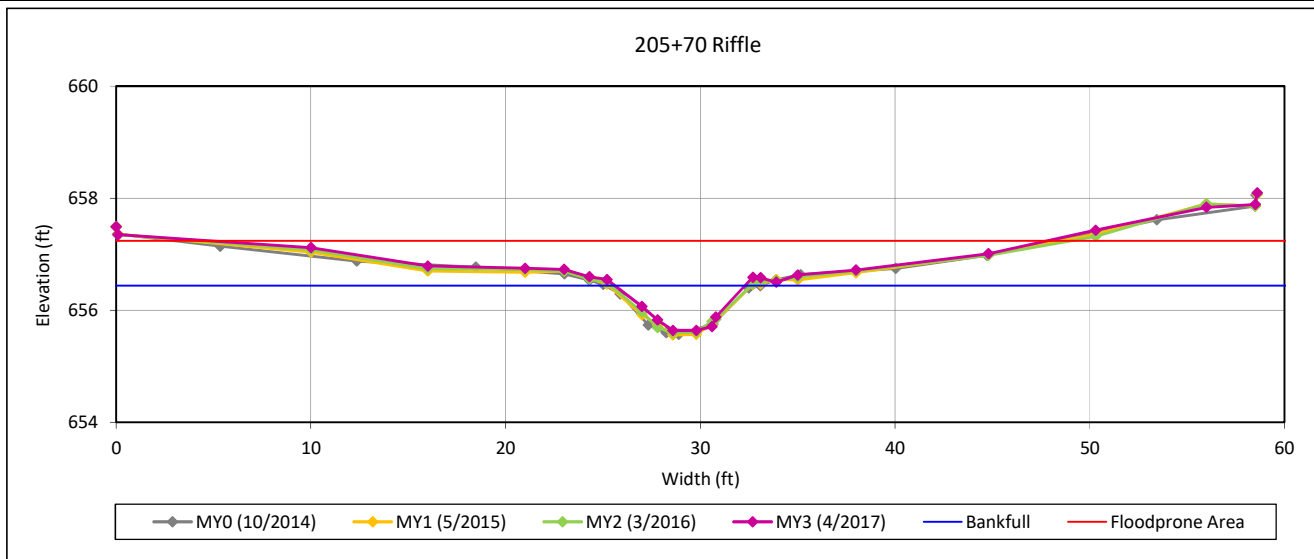

Bankfull Dimensions

3.3	x-section area (ft.sq.)
6.7	width (ft)
0.5	mean depth (ft)
0.8	max depth (ft)
7.0	wetted parimeter (ft)
0.5	hyd radi (ft)
13.4	width-depth ratio
50.0	W flood prone area (ft)
7.5	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 10-UT1A Reach 1

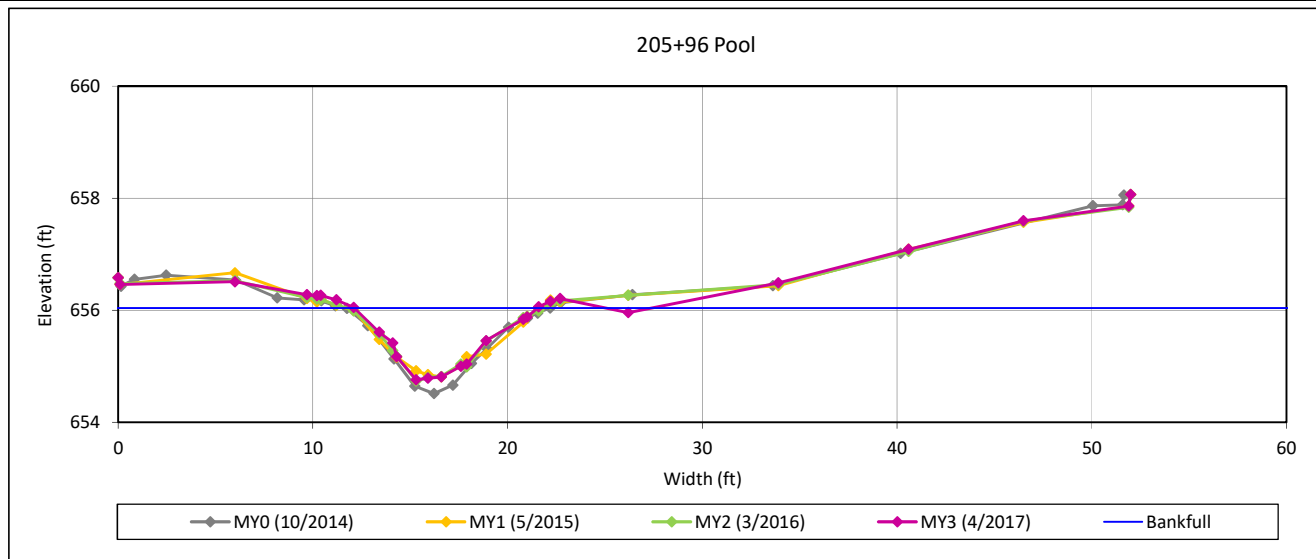

Bankfull Dimensions

6.5	x-section area (ft.sq.)
9.4	width (ft)
0.7	mean depth (ft)
1.3	max depth (ft)
9.9	wetted parimeter (ft)
0.7	hyd radi (ft)
13.5	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 11-UT1A Reach 4

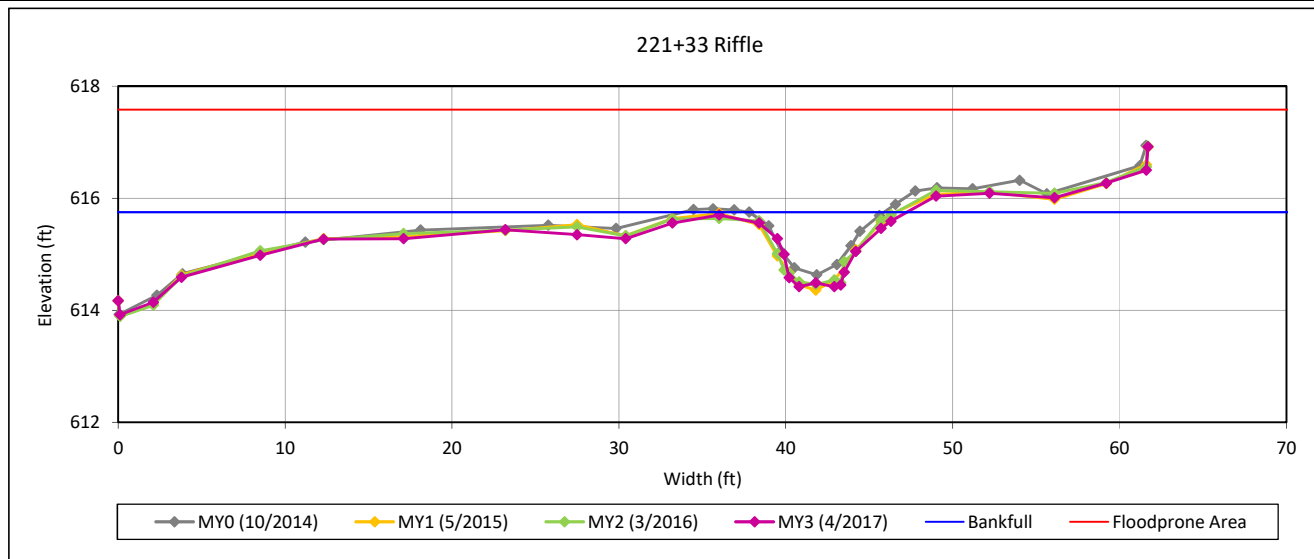

Bankfull Dimensions

6.7	x-section area (ft.sq.)
8.9	width (ft)
0.8	mean depth (ft)
1.8	max depth (ft)
9.5	wetted perimeter (ft)
0.7	hyd radi (ft)
11.7	width-depth ratio
200.0	W flood prone area (ft)
22.6	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 12-UT1A Reach 4

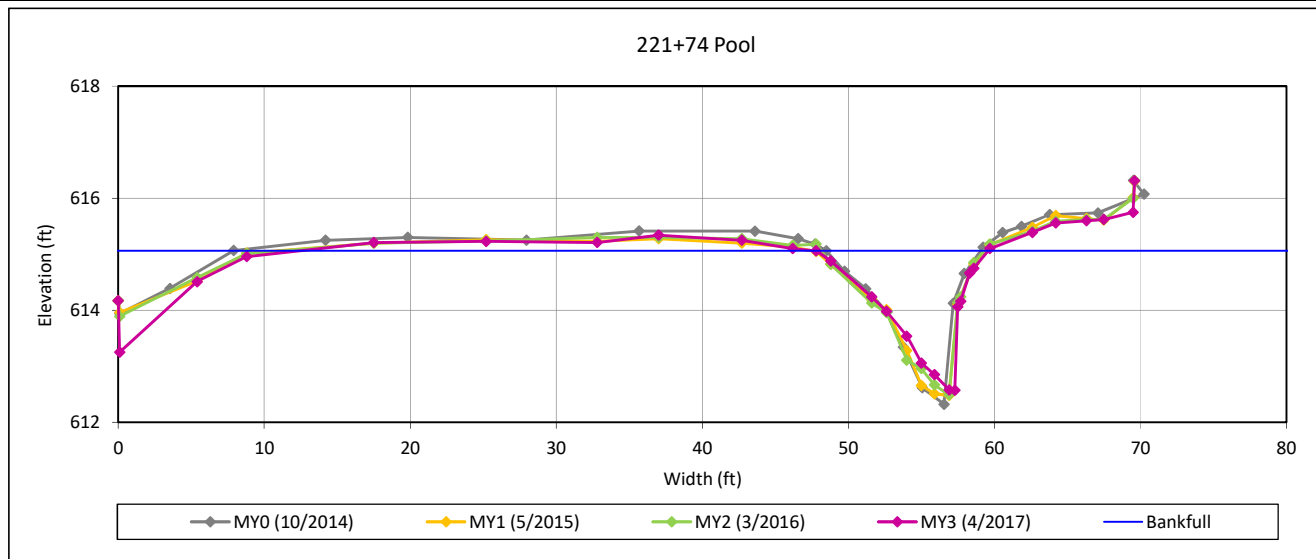

Bankfull Dimensions

12.4	x-section area (ft.sq.)
10.8	width (ft)
1.1	mean depth (ft)
2.5	max depth (ft)
12.7	wetted perimeter (ft)
1.0	hyd radi (ft)
9.4	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 13-UT1B

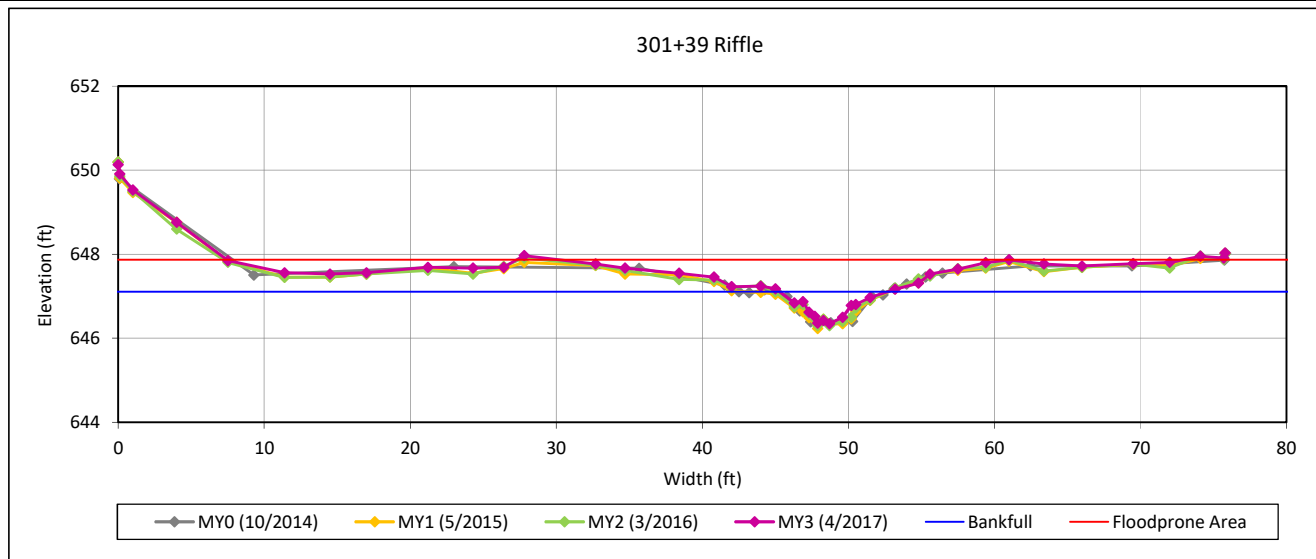

Bankfull Dimensions

2.7	x-section area (ft.sq.)
7.4	width (ft)
0.4	mean depth (ft)
0.8	max depth (ft)
7.7	wetted parimeter (ft)
0.3	hyd radi (ft)
20.6	width-depth ratio
70.0	W flood prone area (ft)
9.4	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 14-UT1B

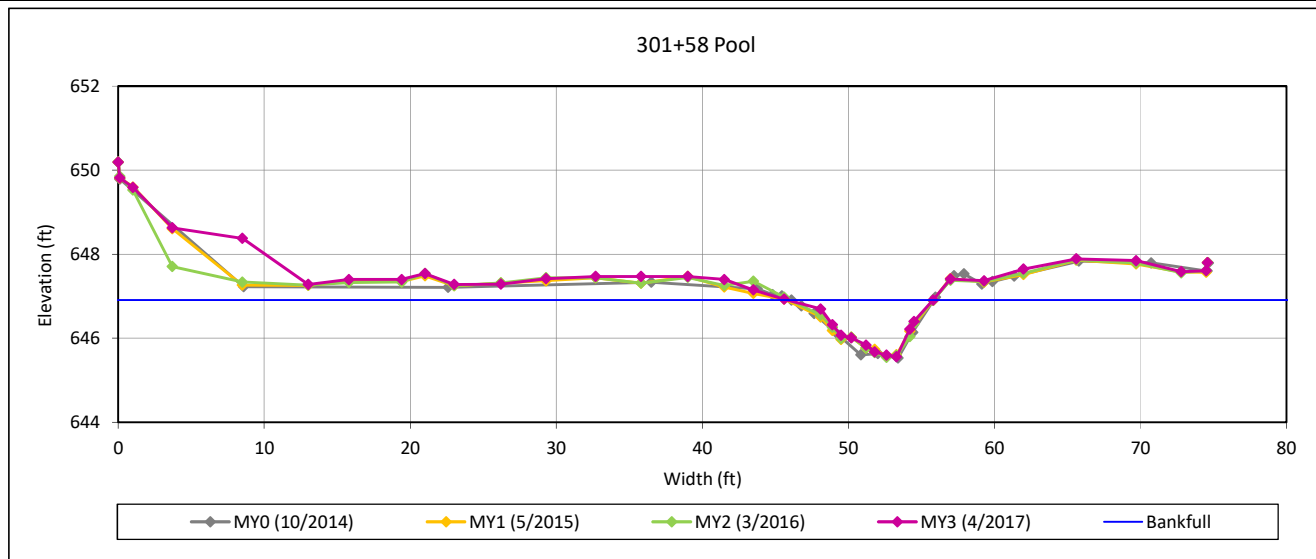

Bankfull Dimensions

6.6	x-section area (ft.sq.)
10.0	width (ft)
0.7	mean depth (ft)
1.3	max depth (ft)
10.5	wetted parimeter (ft)
0.6	hyd radi (ft)
15.0	width-depth ratio

Survey Date: 4/2017
Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 15-UT2

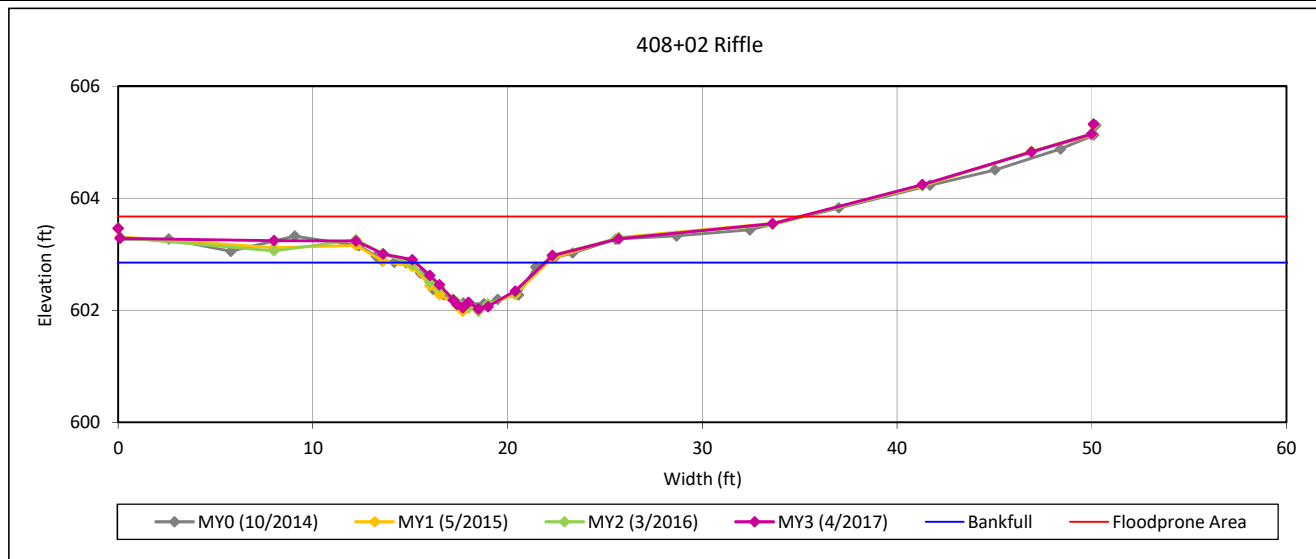

Bankfull Dimensions

3.3	x-section area (ft.sq.)
6.6	width (ft)
0.5	mean depth (ft)
0.8	max depth (ft)
6.9	wetted parimeter (ft)
0.5	hyd radi (ft)
13.5	width-depth ratio
50.0	W flood prone area (ft)
7.5	entrenchment ratio
1.0	low bank height ratio

Survey Date: 4/2017

Field Crew: Wildlands Engineering




View Downstream

Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

Cross Section 16-UT2

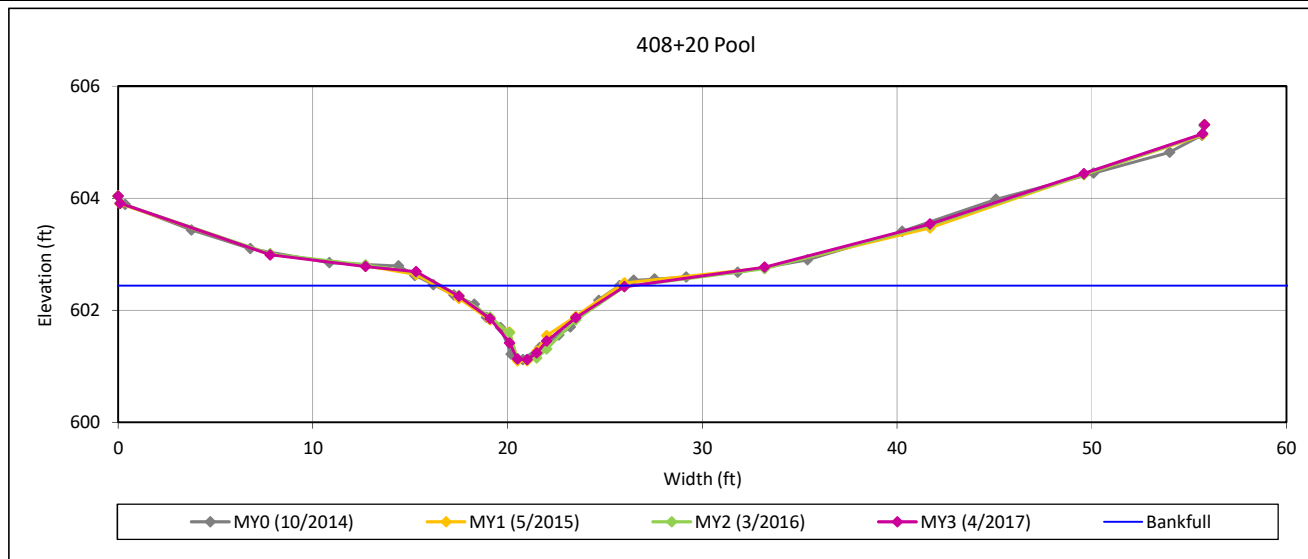

Bankfull Dimensions

5.7	x-section area (ft.sq.)
9.9	width (ft)
0.6	mean depth (ft)
1.3	max depth (ft)
10.3	wetted parimeter (ft)
0.6	hyd radi (ft)
17.0	width-depth ratio



View Downstream

Survey Date: 4/2017
Field Crew: Wildlands Engineering

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	5	8	13	12	12
SAND	Very fine	0.062	0.125		1	1	1	13
	Fine	0.125	0.250					13
	Medium	0.25	0.50	1	2	3	3	15
	Coarse	0.5	1.0	3	6	9	8	24
	Very Coarse	1.0	2.0	4	5	9	8	32
GRAVEL	Very Fine	2.0	2.8	2	4	6	5	37
	Very Fine	2.8	4.0	5	4	9	8	45
	Fine	4.0	5.6	4	8	12	11	56
	Fine	5.6	8.0	4	6	10	9	65
	Medium	8.0	11.0	2	6	8	7	73
	Medium	11.0	16.0	4	4	8	4	76
	Coarse	16.0	22.6	2	2	4	2	78
	Coarse	22.6	32	6	6	12	5	84
	Very Coarse	32	45	2	2	4	2	85
Very Coarse	45	64	2	2	4	2	87	
COBBLE	Small	64	90	6	6	12	5	93
	Small	90	128	7	7	14	6	99
	Large	128	180	1	1	2	1	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	50	110	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	0.52
D ₃₅ =	2.43
D ₅₀ =	4.6
D ₈₄ =	34.3
D ₉₅ =	102.1
D ₁₀₀ =	180.0

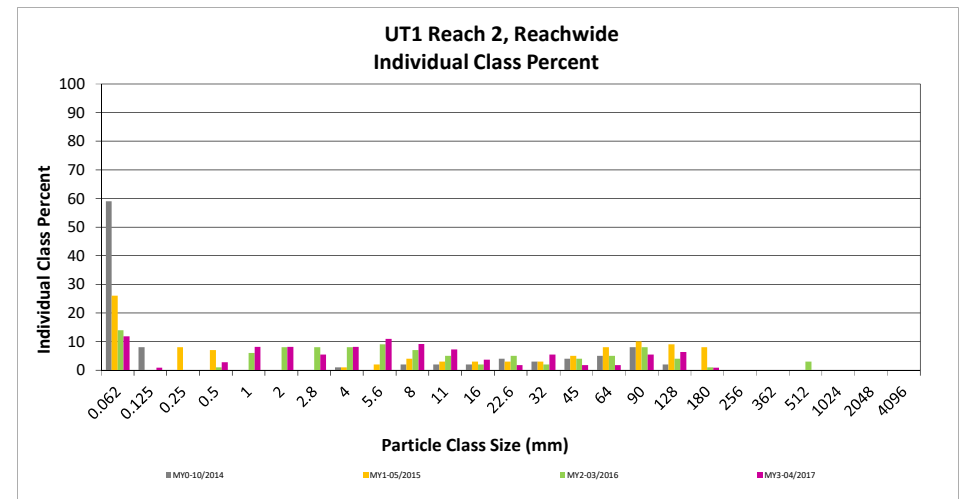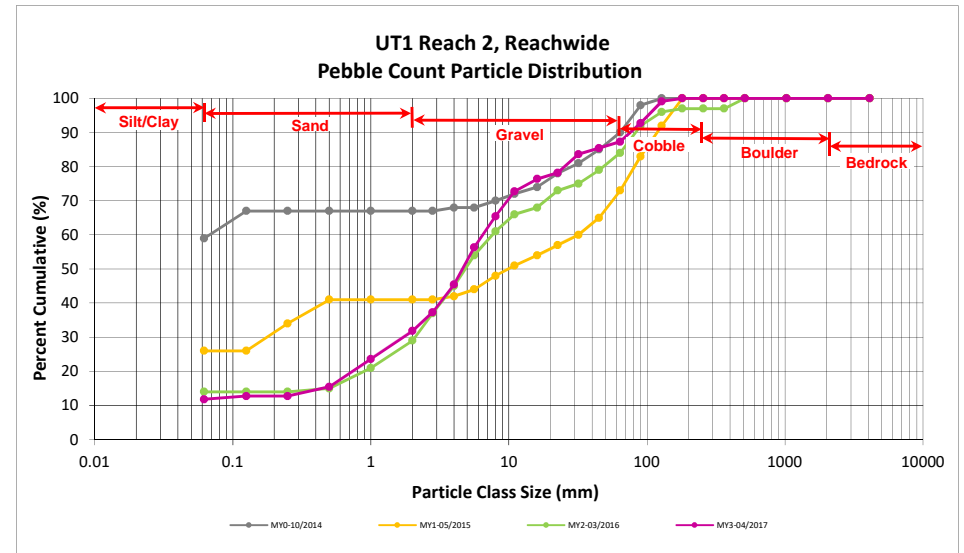

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 2, Cross Section 1

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	2	2	6
GRAVEL	Very Fine	2.0	2.8	7	7	13
	Very Fine	2.8	4.0	5	5	18
	Fine	4.0	5.6	6	6	24
	Fine	5.6	8.0	4	4	28
	Medium	8.0	11.0	4	4	32
	Medium	11.0	16.0	4	4	36
	Coarse	16.0	22.6	6	6	42
	Coarse	22.6	32	15	15	57
	Very Coarse	32	45	7	7	64
	Very Coarse	45	64	13	13	77
COBBLE	Small	64	90	10	10	87
	Small	90	128	6	6	93
	Large	128	180	6	6	99
	Large	180	256	1	1	100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				100	100	100

Cross Section 1	
Channel materials (mm)	
D ₁₆ =	3.47
D ₃₅ =	14.57
D ₅₀ =	27.2
D ₈₄ =	81.3
D ₉₅ =	143.4
D ₁₀₀ =	256.0

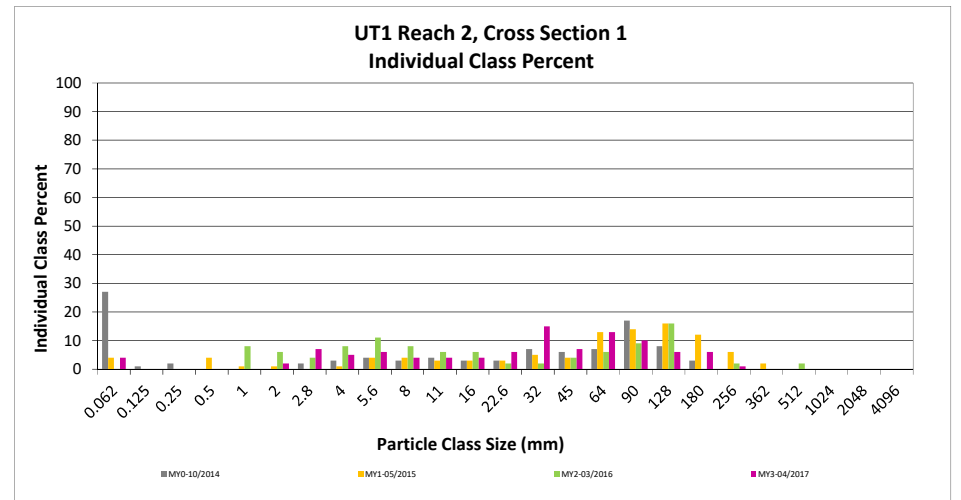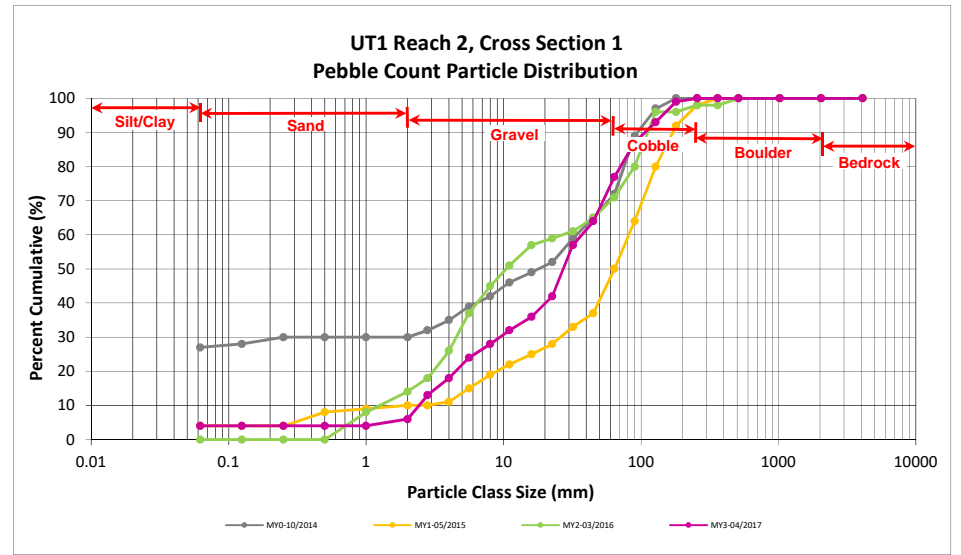

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 2, Cross Section 3

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	6	6	6
SAND	Very fine	0.062	0.125			6
	Fine	0.125	0.250			6
	Medium	0.25	0.50			6
	Coarse	0.5	1.0			6
	Very Coarse	1.0	2.0	2	2	8
GRAVEL	Very Fine	2.0	2.8	2	2	10
	Very Fine	2.8	4.0	4	4	14
	Fine	4.0	5.6	3	3	17
	Fine	5.6	8.0	6	6	23
	Medium	8.0	11.0	8	8	31
	Medium	11.0	16.0	7	7	38
	Coarse	16.0	22.6	12	12	50
	Coarse	22.6	32	10	10	59
	Very Coarse	32	45	13	13	72
	Very Coarse	45	64	7	7	79
COBBLE	Small	64	90	13	13	92
	Small	90	128	4	4	96
	Large	128	180	4	4	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				101	100	100

Cross Section 3	
Channel materials (mm)	
D ₁₆ =	5.10
D ₃₅ =	13.88
D ₅₀ =	23.0
D ₈₄ =	72.7
D ₉₅ =	116.7
D ₁₀₀ =	180.0

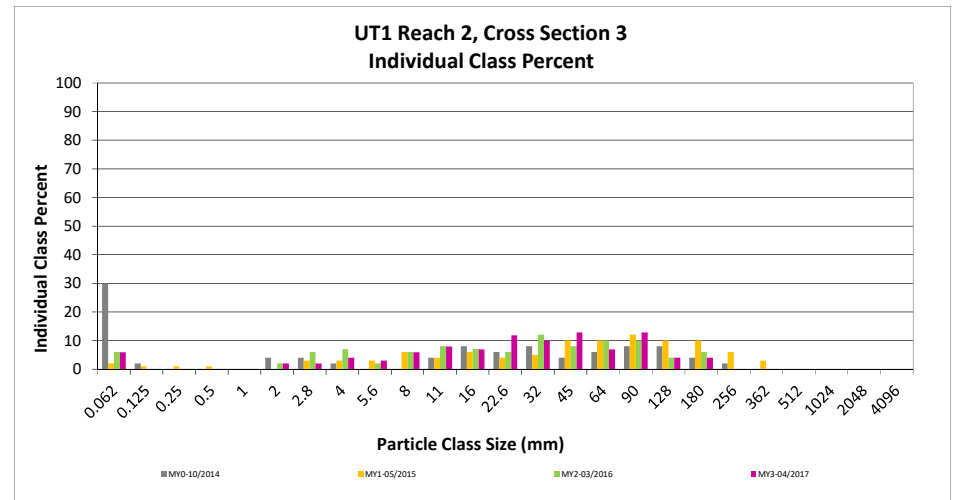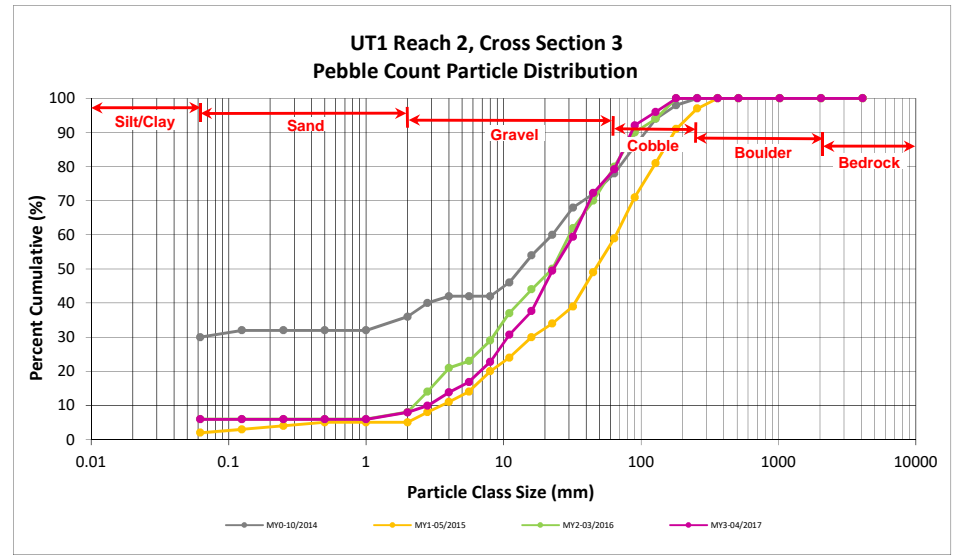

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 4, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	5	12	17	17	17
SAND	Very fine	0.062	0.125					17
	Fine	0.125	0.250					17
	Medium	0.25	0.50					17
	Coarse	0.5	1.0		6	6	6	23
	Very Coarse	1.0	2.0	2	5	7	7	30
GRAVEL	Very Fine	2.0	2.8	2	3	5	5	35
	Very Fine	2.8	4.0	1	4	5	5	40
	Fine	4.0	5.6		3	3	3	43
	Fine	5.6	8.0		6	6	6	49
	Medium	8.0	11.0		1	1	1	50
	Medium	11.0	16.0	1	1	1	1	51
	Coarse	16.0	22.6	1	1	1	1	52
	Coarse	22.6	32	8	8	8	8	60
	Very Coarse	32	45	4	4	4	4	64
Very Coarse	45	64	7	7	7	7	71	
COBBLE	Small	64	90	6	6	6	6	77
	Small	90	128	8	8	8	8	85
	Large	128	180	7	7	7	7	92
	Large	180	256	1	1	1	1	93
BOULDER	Small	256	362	3	3	3	3	96
	Small	362	512	4	4	4	4	100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	40	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	2.80
D ₅₀ =	11.0
D ₈₄ =	122.5
D ₉₅ =	322.5
D ₁₀₀ =	512.0

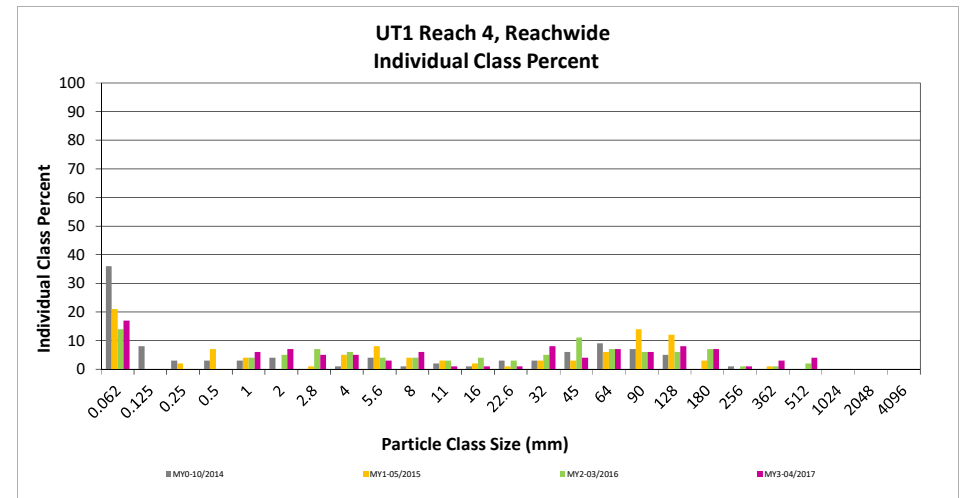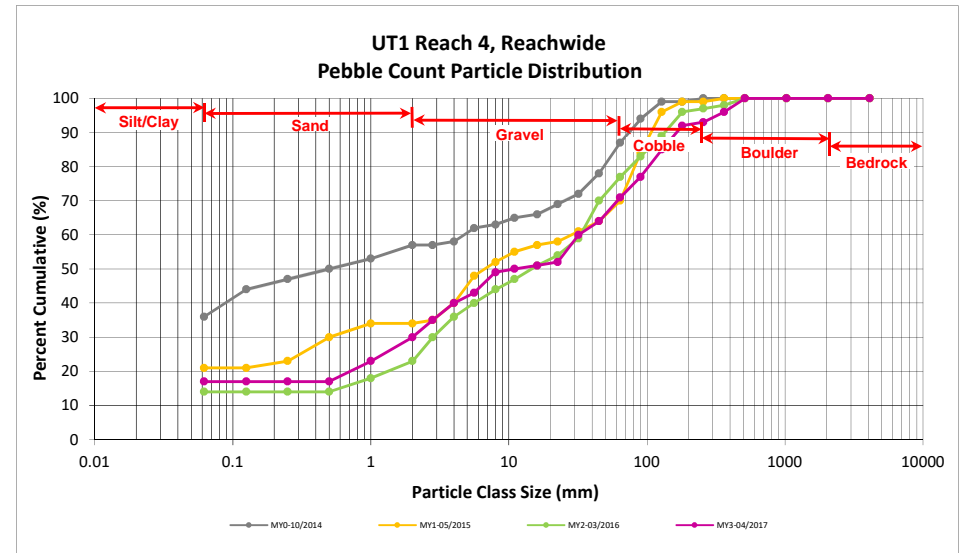

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 5, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	1	20	21	21	21
SAND	Very fine	0.062	0.125					21
	Fine	0.125	0.250		2	2	2	23
	Medium	0.25	0.50	2	10	12	12	35
	Coarse	0.5	1.0	1	4	5	5	40
	Very Coarse	1.0	2.0					40
GRAVEL	Very Fine	2.0	2.8					40
	Very Fine	2.8	4.0					40
	Fine	4.0	5.6		1	1	1	41
	Fine	5.6	8.0		2	2	2	43
	Medium	8.0	11.0					43
	Medium	11.0	16.0	5	1	6	6	49
	Coarse	16.0	22.6	5		5	5	54
	Coarse	22.6	32	8		8	8	62
	Very Coarse	32	45	7		7	7	69
Very Coarse	45	64	12		12	12	81	
COBBLE	Small	64	90	11		11	11	92
	Small	90	128	7		7	7	99
	Large	128	180	1		1	1	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	40	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	0.50
D ₅₀ =	17.1
D ₈₄ =	70.2
D ₉₅ =	104.7
D ₁₀₀ =	180.0

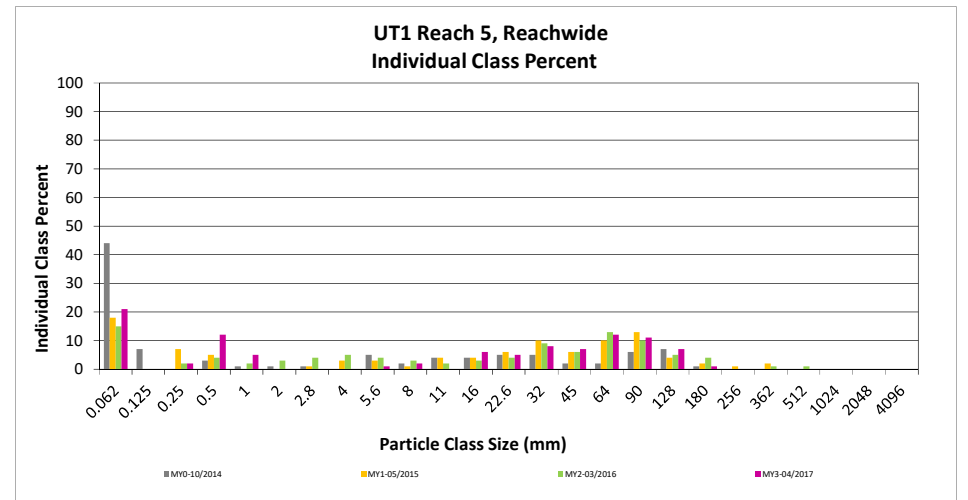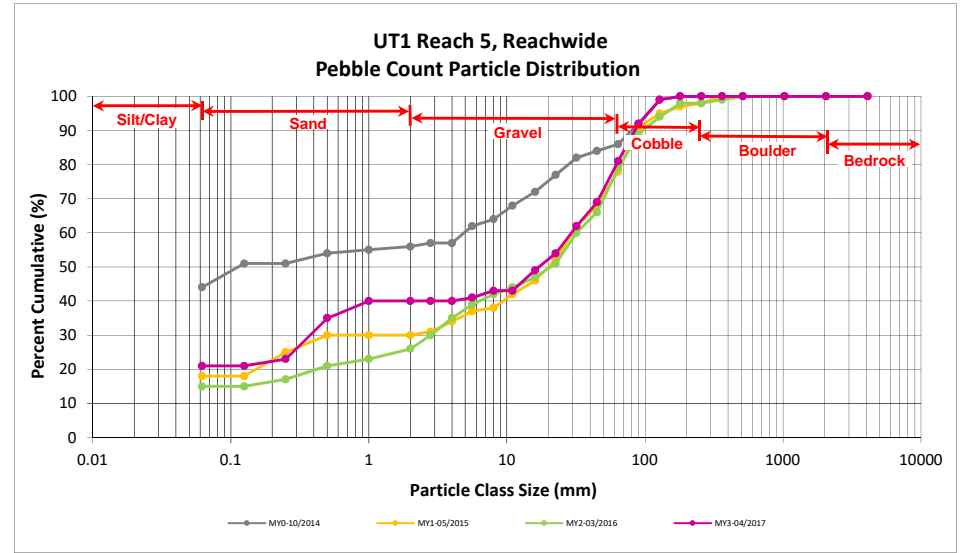

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 5, Cross Section 6

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0	2	2	6
	Very Coarse	1.0	2.0	4	4	10
GRAVEL	Very Fine	2.0	2.8	4	4	13
	Very Fine	2.8	4.0	5	5	18
	Fine	4.0	5.6	4	4	22
	Fine	5.6	8.0	6	6	28
	Medium	8.0	11.0	4	4	31
	Medium	11.0	16.0	8	8	39
	Coarse	16.0	22.6	3	3	42
	Coarse	22.6	32	11	10	52
	Very Coarse	32	45	9	9	61
	Very Coarse	45	64	10	10	70
COBBLE	Small	64	90	7	7	77
	Small	90	128	5	5	82
	Large	128	180	10	10	91
	Large	180	256	6	6	97
BOULDER	Small	256	362	3	3	100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				105	100	100

Cross Section 6	
Channel materials (mm)	
D ₁₆ =	3.42
D ₃₅ =	13.11
D ₅₀ =	29.6
D ₈₄ =	138.0
D ₉₅ =	224.3
D ₁₀₀ =	362.0

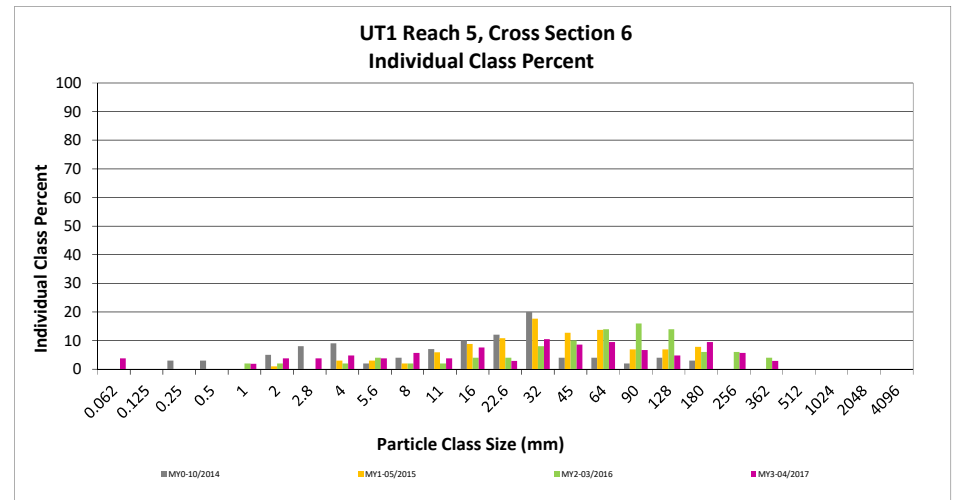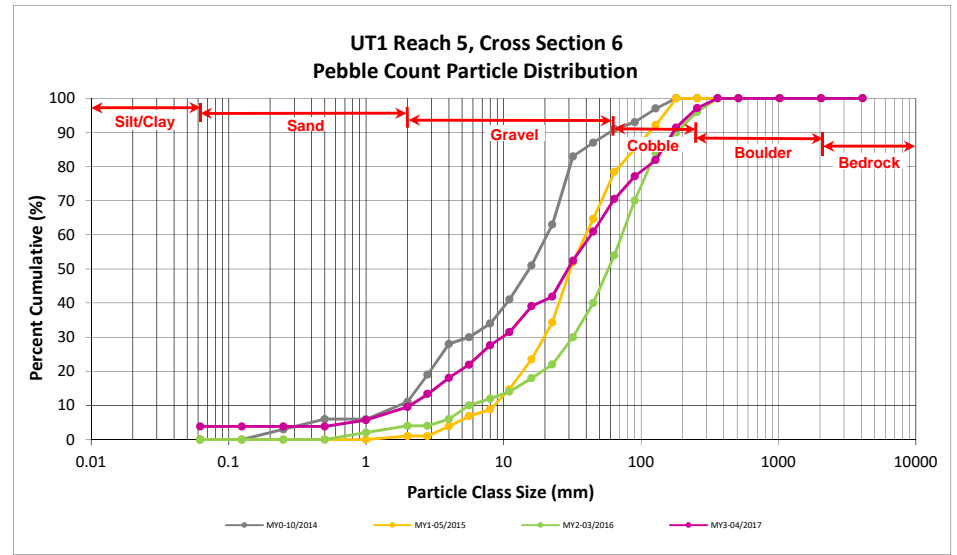

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1 Reach 5, Cross Section 7

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	8	8	8
SAND	Very fine	0.062	0.125			8
	Fine	0.125	0.250			8
	Medium	0.25	0.50			8
	Coarse	0.5	1.0			8
	Very Coarse	1.0	2.0			8
GRAVEL	Very Fine	2.0	2.8			8
	Very Fine	2.8	4.0			8
	Fine	4.0	5.6			8
	Fine	5.6	8.0	2	2	10
	Medium	8.0	11.0	8	8	18
	Medium	11.0	16.0	14	14	32
	Coarse	16.0	22.6	6	6	38
	Coarse	22.6	32	8	8	46
	Very Coarse	32	45	6	6	52
	Very Coarse	45	64	6	6	58
COBBLE	Small	64	90	14	14	72
	Small	90	128	16	16	88
	Large	128	180	10	10	98
	Large	180	256	2	2	100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				100	100	100

Cross Section 7	
Channel materials (mm)	
D ₁₆ =	10.16
D ₃₅ =	19.02
D ₅₀ =	40.2
D ₈₄ =	117.2
D ₉₅ =	162.5
D ₁₀₀ =	256.0

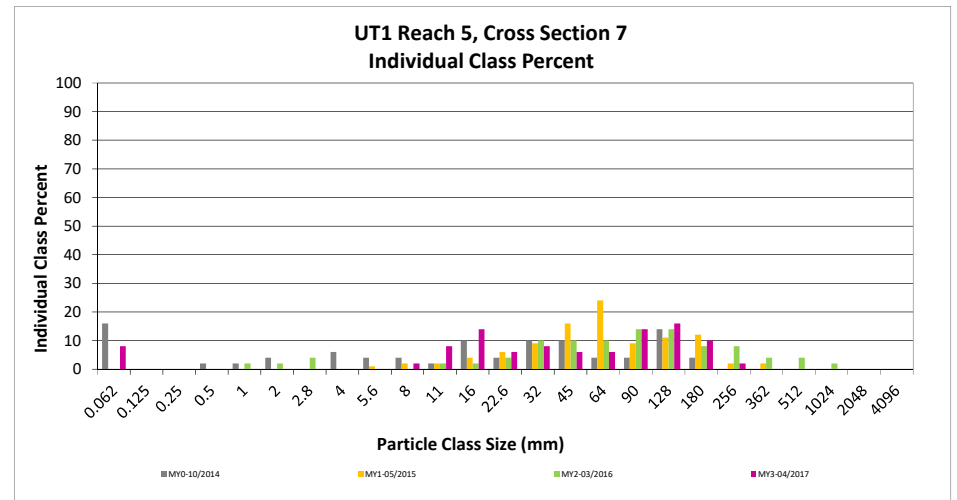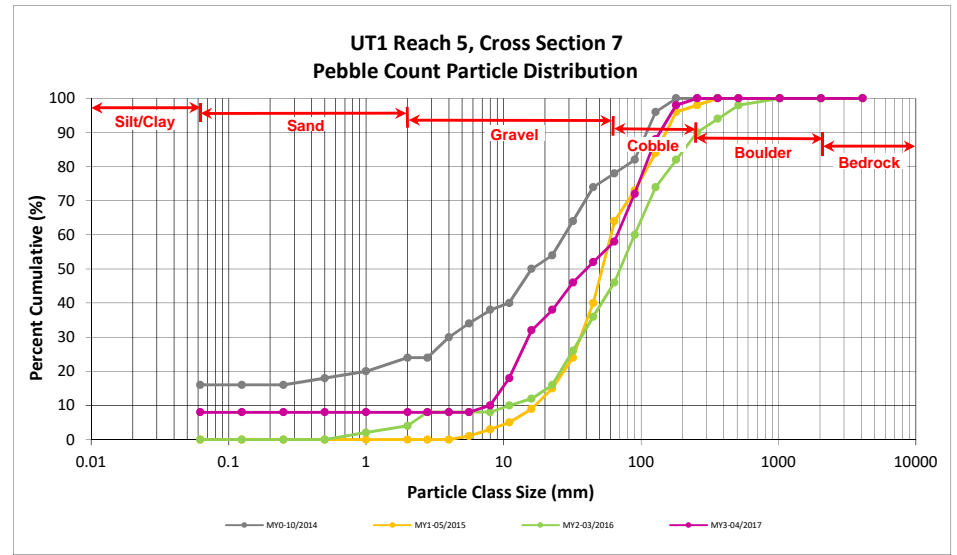

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1A Reach 1, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062		17	17	17	17
SAND	Very fine	0.062	0.125					17
	Fine	0.125	0.250					17
	Medium	0.25	0.50		5	5	5	22
	Coarse	0.5	1.0		14	14	14	36
	Very Coarse	1.0	2.0		1	1	1	37
GRAVEL	Very Fine	2.0	2.8					37
	Very Fine	2.8	4.0		1	1	1	38
	Fine	4.0	5.6		1	1	1	39
	Fine	5.6	8.0	1	1	2	2	41
	Medium	8.0	11.0	2		2	2	43
	Medium	11.0	16.0	5		5	5	48
	Coarse	16.0	22.6	9		9	9	57
	Coarse	22.6	32	8		8	8	65
	Very Coarse	32	45	12		12	12	77
Very Coarse	45	64	11		11	11	88	
COBBLE	Small	64	90	9		9	9	97
	Small	90	128	2		2	2	99
	Large	128	180	1		1	1	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	40	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	0.95
D ₅₀ =	17.3
D ₈₄ =	56.3
D ₉₅ =	83.4
D ₁₀₀ =	180.0

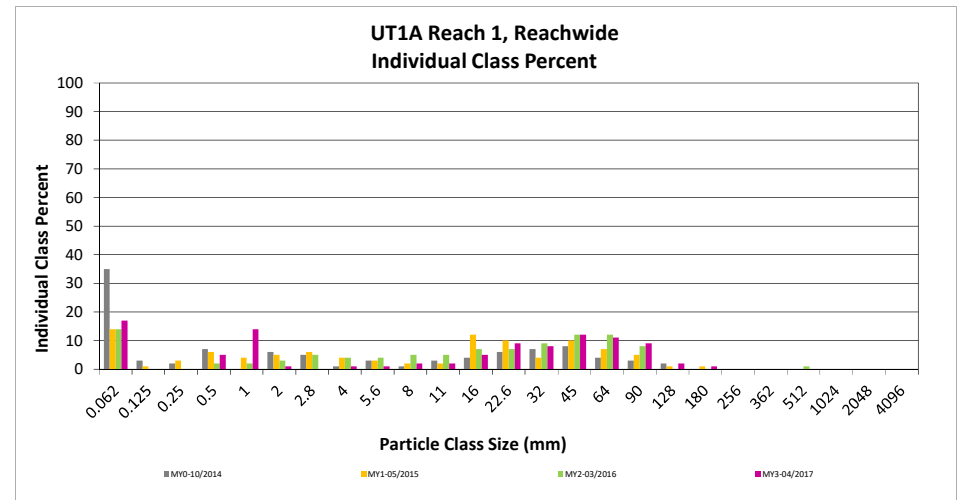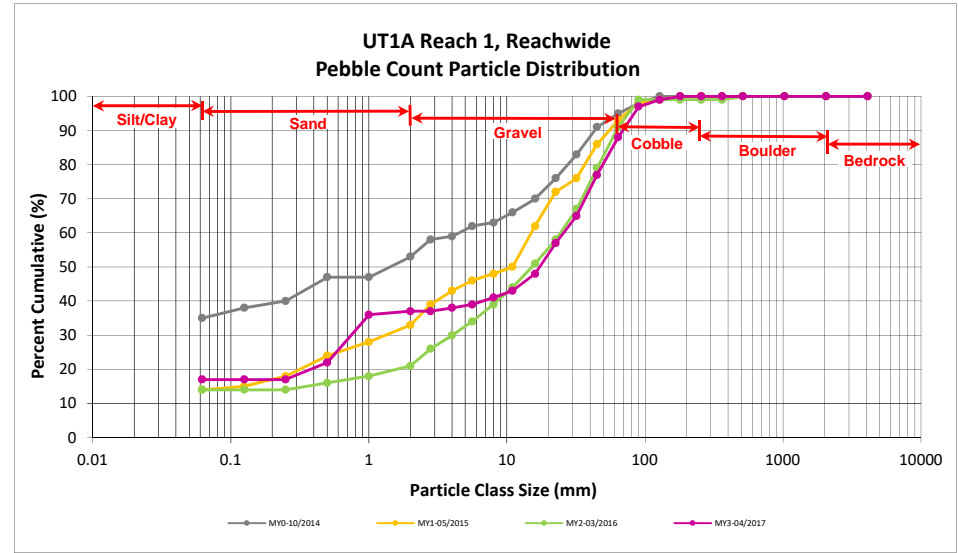

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1A Reach 1, Cross Section 9

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062			0
SAND	Very fine	0.062	0.125			0
	Fine	0.125	0.250			0
	Medium	0.25	0.50			0
	Coarse	0.5	1.0			0
	Very Coarse	1.0	2.0	2	2	2
GRAVEL	Very Fine	2.0	2.8			2
	Very Fine	2.8	4.0			2
	Fine	4.0	5.6	4	4	5
	Fine	5.6	8.0	4	4	9
	Medium	8.0	11.0	4	4	13
	Medium	11.0	16.0	6	5	18
	Coarse	16.0	22.6	12	11	29
	Coarse	22.6	32	14	13	42
	Very Coarse	32	45	16	15	56
	Very Coarse	45	64	20	18	75
COBBLE	Small	64	90	20	18	93
	Small	90	128	6	5	98
	Large	128	180	2	2	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				110	100	100

Cross Section 9	
Channel materials (mm)	
D ₁₆ =	13.77
D ₃₅ =	26.56
D ₅₀ =	38.8
D ₈₄ =	76.4
D ₉₅ =	104.2
D ₁₀₀ =	180.0

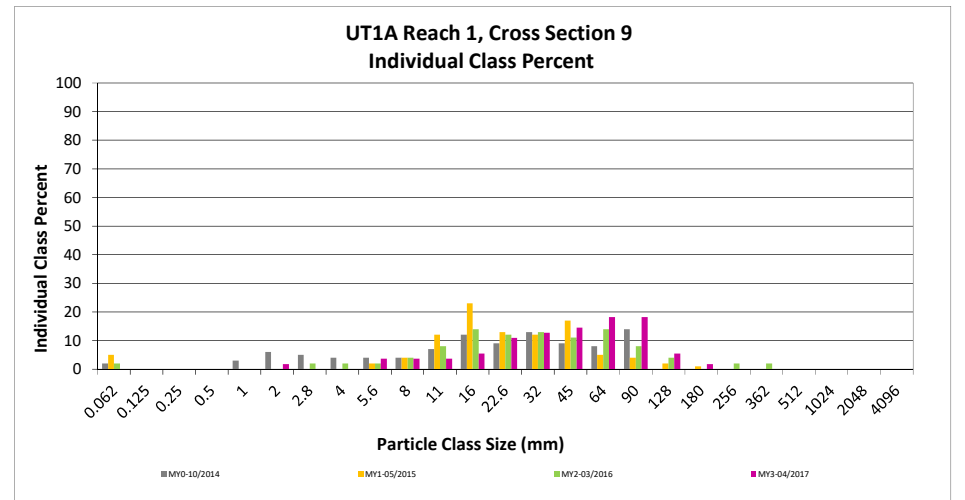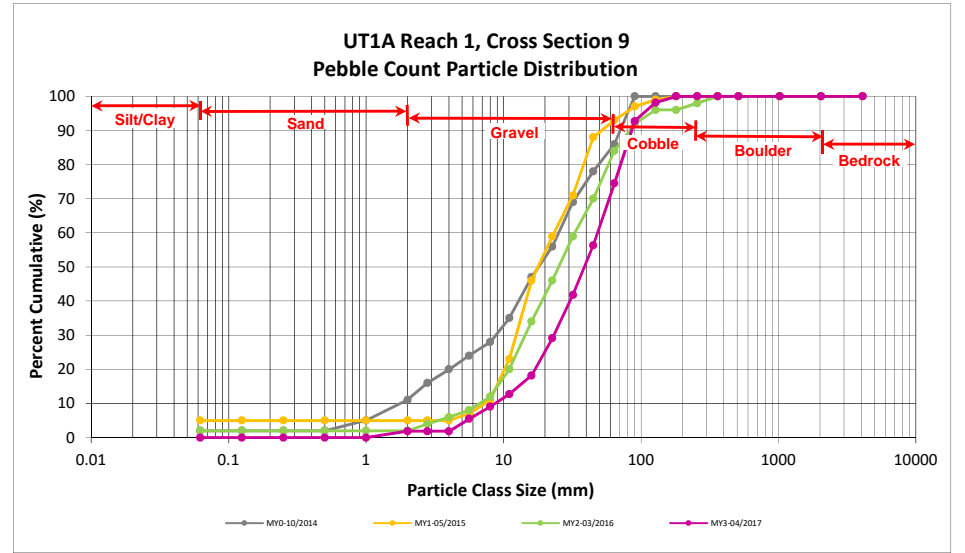

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1A Reach 4, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062		15	15	15	15
SAND	Very fine	0.062	0.125					15
	Fine	0.125	0.250		6	6	6	21
	Medium	0.25	0.50	1	12	13	13	34
	Coarse	0.5	1.0		4	4	4	38
	Very Coarse	1.0	2.0		2	2	2	40
GRAVEL	Very Fine	2.0	2.8					40
	Very Fine	2.8	4.0	1		1	1	41
	Fine	4.0	5.6					41
	Fine	5.6	8.0	4	1	5	5	46
	Medium	8.0	11.0	4		4	4	50
	Medium	11.0	16.0	6		6	6	55
	Coarse	16.0	22.6	6		6	6	61
	Coarse	22.6	32	10		10	10	71
	Very Coarse	32	45	10		10	10	81
Very Coarse	45	64	6		6	6	87	
COBBLE	Small	64	90	6		6	6	93
	Small	90	128	4		4	4	97
	Large	128	180	3		3	3	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				61	40	101	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	0.14
D ₃₅ =	0.63
D ₅₀ =	11.35
D ₈₄ =	53.2
D ₉₅ =	106.9
D ₁₀₀ =	180.0

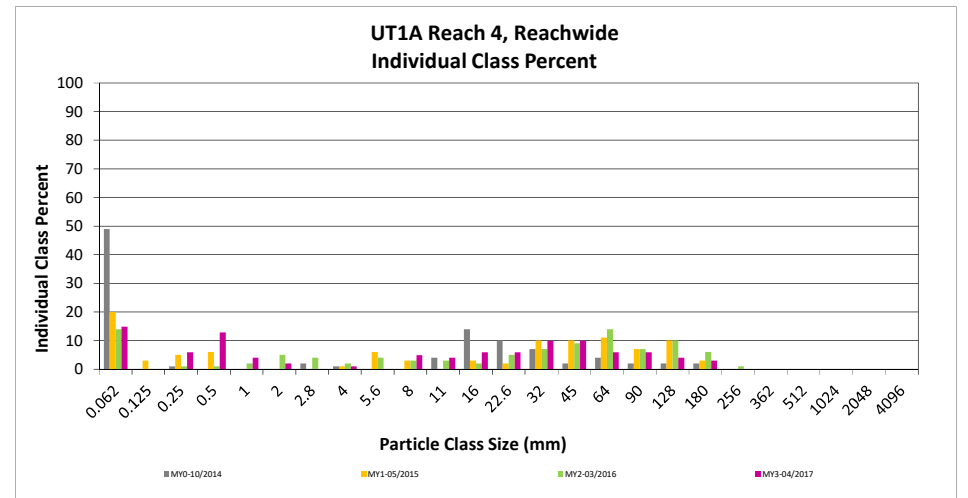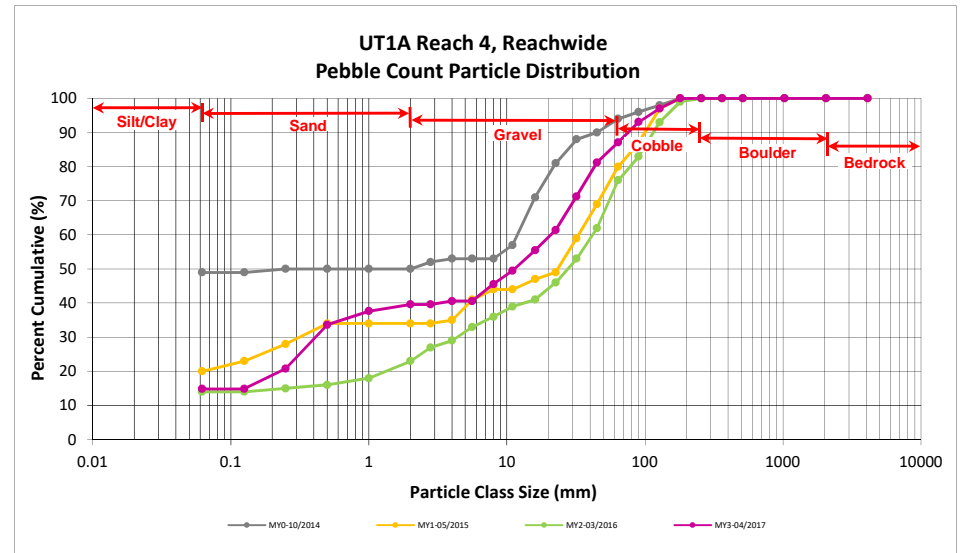

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1A Reach 4, Cross Section 11

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062			0
SAND	Very fine	0.062	0.125			0
	Fine	0.125	0.250			0
	Medium	0.25	0.50			0
	Coarse	0.5	1.0			0
	Very Coarse	1.0	2.0	3	6	6
GRAVEL	Very Fine	2.0	2.8	3	6	12
	Very Fine	2.8	4.0	2	4	16
	Fine	4.0	5.6	3	6	22
	Fine	5.6	8.0	2	4	26
	Medium	8.0	11.0	3	6	32
	Medium	11.0	16.0	5	10	42
	Coarse	16.0	22.6	4	8	50
	Coarse	22.6	32	2	4	54
	Very Coarse	32	45	6	12	66
	Very Coarse	45	64	6	12	78
COBBLE	Small	64	90	2	4	82
	Small	90	128	4	8	90
	Large	128	180	3	6	96
	Large	180	256	2	4	100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				50	100	100

Cross Section 11	
Channel materials (mm)	
D ₁₆ =	4.00
D ₃₅ =	12.31
D ₅₀ =	22.6
D ₈₄ =	98.3
D ₉₅ =	170.1
D ₁₀₀ =	256.0

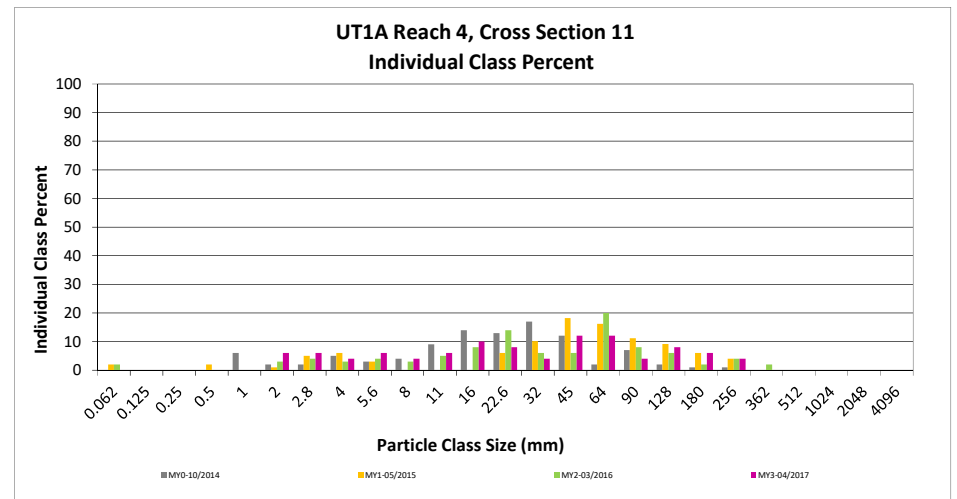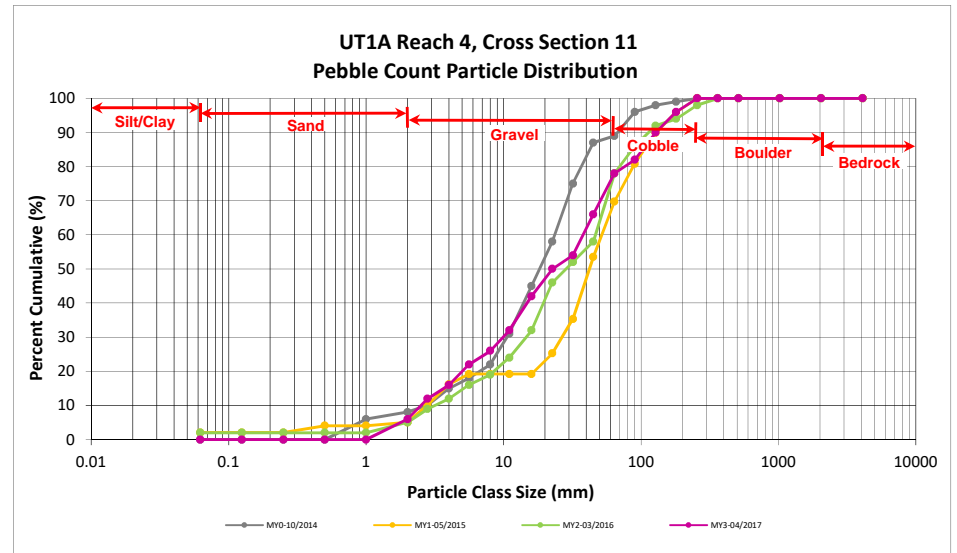

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1B, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	12	14	26	29	29
SAND	Very fine	0.062	0.125					29
	Fine	0.125	0.250		2	2	2	31
	Medium	0.25	0.50	2		2	2	33
	Coarse	0.5	1.0	3	2	5	6	39
	Very Coarse	1.0	2.0	2	4	6	7	46
GRAVEL	Very Fine	2.0	2.8	2	4	6	7	52
	Very Fine	2.8	4.0	2	2	4	4	57
	Fine	4.0	5.6	4	2	6	7	63
	Fine	5.6	8.0	3		3	3	67
	Medium	8.0	11.0					67
	Medium	11.0	16.0					67
	Coarse	16.0	22.6					67
	Coarse	22.6	32	6		6	7	73
	Very Coarse	32	45	5		5	6	79
Very Coarse	45	64	5		5	6	84	
COBBLE	Small	64	90					84
	Small	90	128	7		7	8	92
	Large	128	180	7		7	8	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	30	90	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	0.62
D ₅₀ =	2.5
D ₈₄ =	62.2
D ₉₅ =	144.6
D ₁₀₀ =	180.0

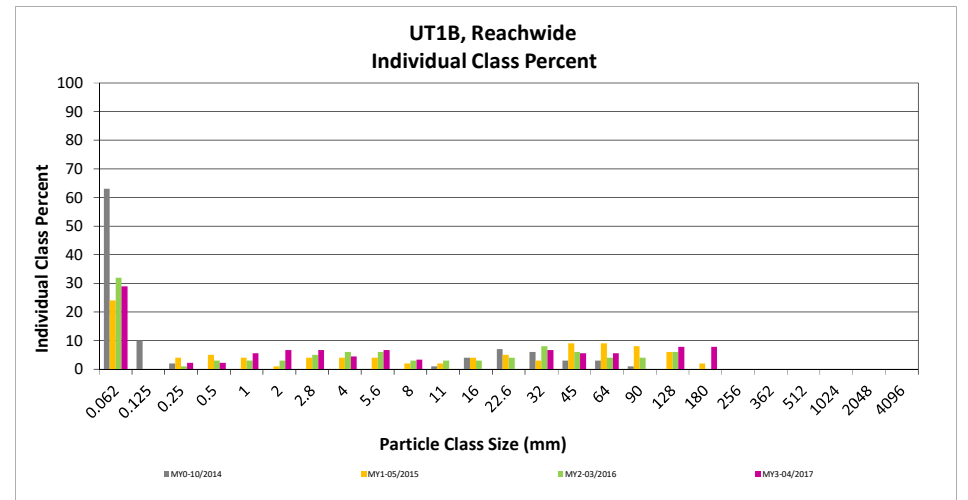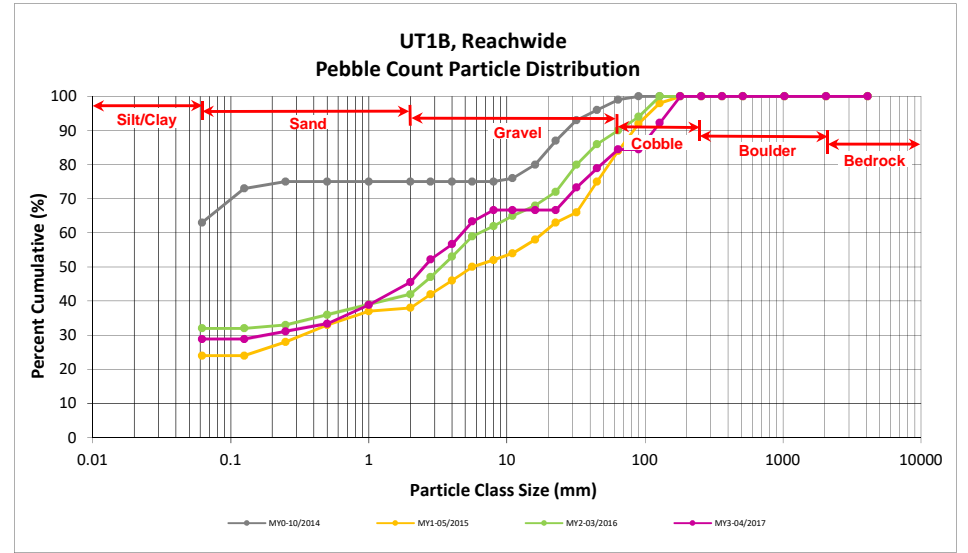

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT1B, Cross Section 13

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	10	9	9
SAND	Very fine	0.062	0.125	2	2	11
	Fine	0.125	0.250	4	4	15
	Medium	0.25	0.50			15
	Coarse	0.5	1.0			15
	Very Coarse	1.0	2.0	2	2	16
GRAVEL	Very Fine	2.0	2.8	4	4	20
	Very Fine	2.8	4.0	2	2	22
	Fine	4.0	5.6	4	4	25
	Fine	5.6	8.0	2	2	27
	Medium	8.0	11.0	6	5	33
	Medium	11.0	16.0	10	9	42
	Coarse	16.0	22.6	8	7	49
	Coarse	22.6	32	14	13	62
	Very Coarse	32	45	6	5	67
	Very Coarse	45	64	14	13	80
COBBLE	Small	64	90	10	9	89
	Small	90	128	10	9	98
	Large	128	180	2	2	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				110	100	100

Cross Section 13	
Channel materials (mm)	
D ₁₆ =	1.74
D ₃₅ =	12.08
D ₅₀ =	23.2
D ₈₄ =	74.4
D ₉₅ =	113.2
D ₁₀₀ =	180.0

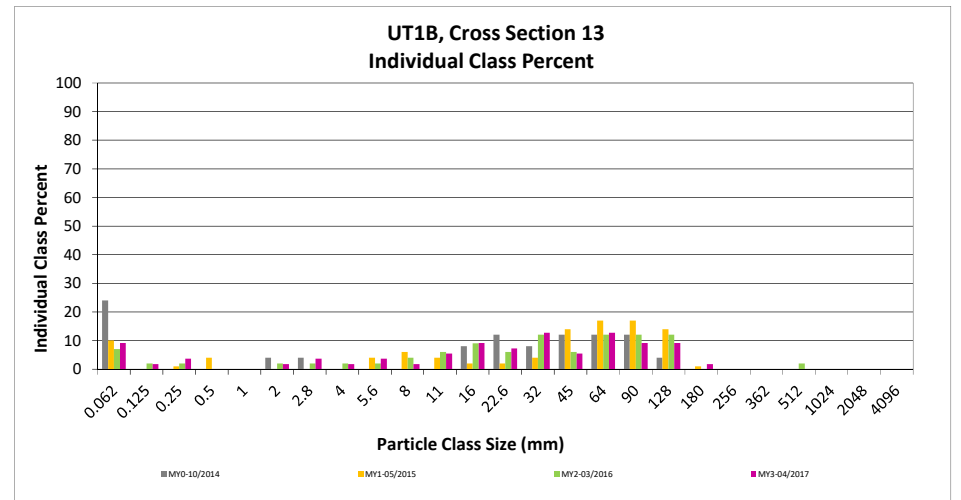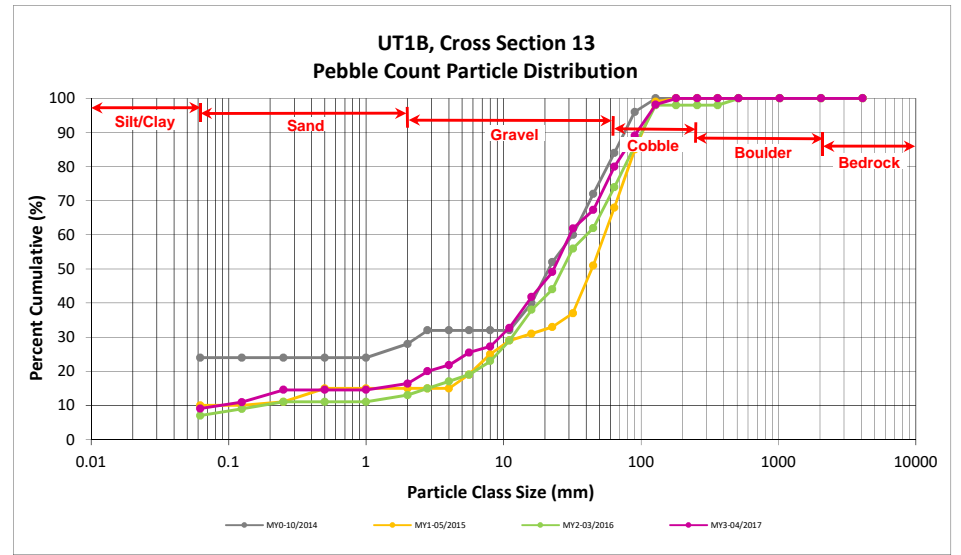

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	10	27	37	37	37
SAND	Very fine	0.062	0.125					37
	Fine	0.125	0.250					37
	Medium	0.25	0.50	1	5	6	6	43
	Coarse	0.5	1.0	3	3	6	6	49
	Very Coarse	1.0	2.0	1	2	3	3	52
GRAVEL	Very Fine	2.0	2.8					52
	Very Fine	2.8	4.0	2	2	4	4	56
	Fine	4.0	5.6	1	1	2	2	58
	Fine	5.6	8.0	3		3	3	61
	Medium	8.0	11.0	4		4	4	65
	Medium	11.0	16.0	8		8	8	73
	Coarse	16.0	22.6	9		9	9	82
	Coarse	22.6	32	4		4	4	86
	Very Coarse	32	45	6		6	6	92
Very Coarse	45	64	3		3	3	95	
COBBLE	Small	64	90	3		3	3	98
	Small	90	128	1		1	1	99
	Large	128	180	1		1	1	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
BEDROCK	Bedrock	2048	>2048					100
Total				60	40	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	Silt/Clay
D ₅₀ =	1.3
D ₈₄ =	26.9
D ₉₅ =	64.0
D ₁₀₀ =	180.0

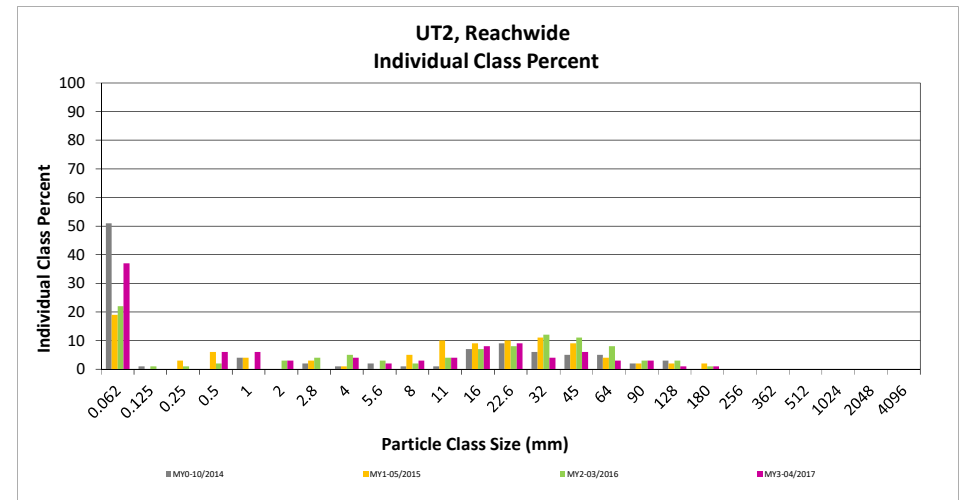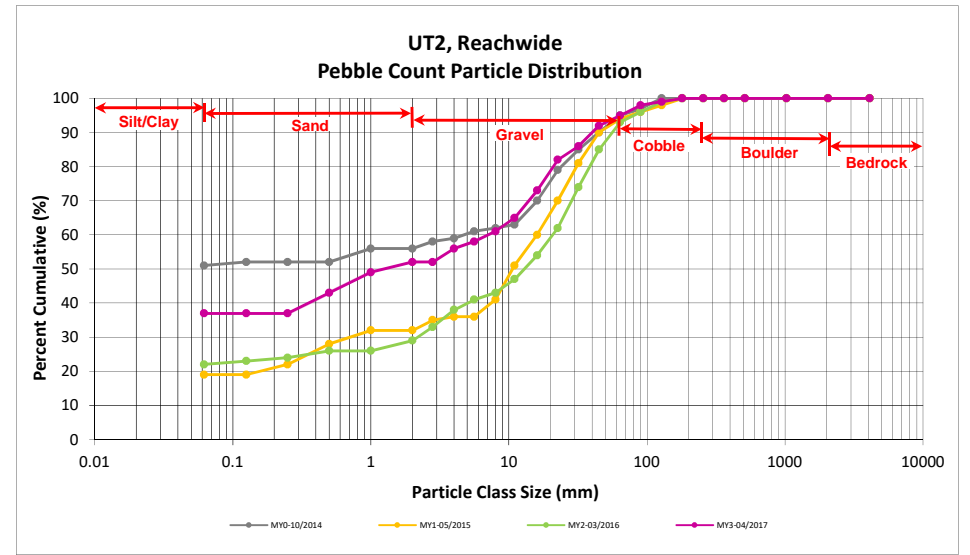

Reachwide and Cross Section Pebble Count Plots



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

UT2, Cross Section 15

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	6	6	6
SAND	Very fine	0.062	0.125			6
	Fine	0.125	0.250			6
	Medium	0.25	0.50			6
	Coarse	0.5	1.0	4	4	10
	Very Coarse	1.0	2.0			10
GRAVEL	Very Fine	2.0	2.8			10
	Very Fine	2.8	4.0			10
	Fine	4.0	5.6			10
	Fine	5.6	8.0	2	2	12
	Medium	8.0	11.0	2	2	14
	Medium	11.0	16.0	10	10	24
	Coarse	16.0	22.6	14	14	38
	Coarse	22.6	32	16	16	54
	Very Coarse	32	45	12	12	66
	Very Coarse	45	64	10	10	76
COBBLE	Small	64	90	14	14	90
	Small	90	128	8	8	98
	Large	128	180	2	2	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
BEDROCK	Bedrock	2048	>2048			100
Total				100	100	100

Cross Section 15	
Channel materials (mm)	
D ₁₆ =	11.86
D ₃₅ =	20.99
D ₅₀ =	29.3
D ₈₄ =	77.8
D ₉₅ =	112.2
D ₁₀₀ =	180.0

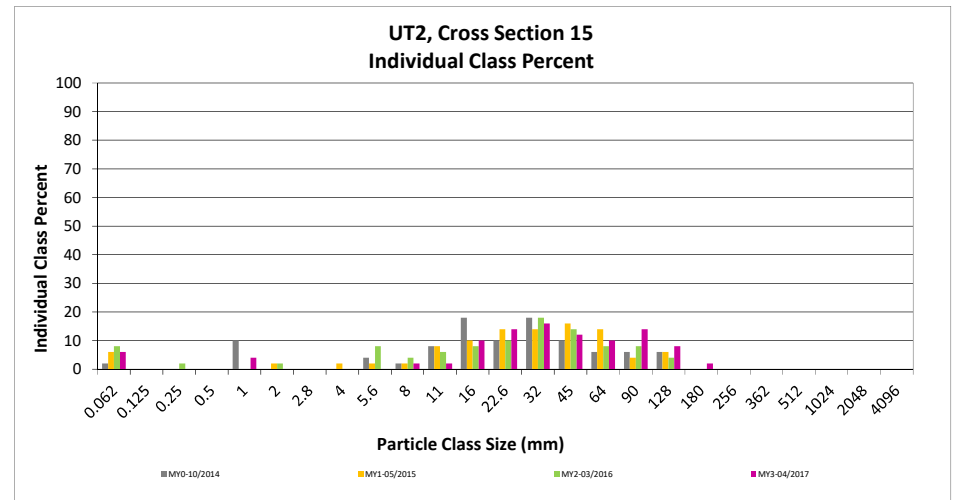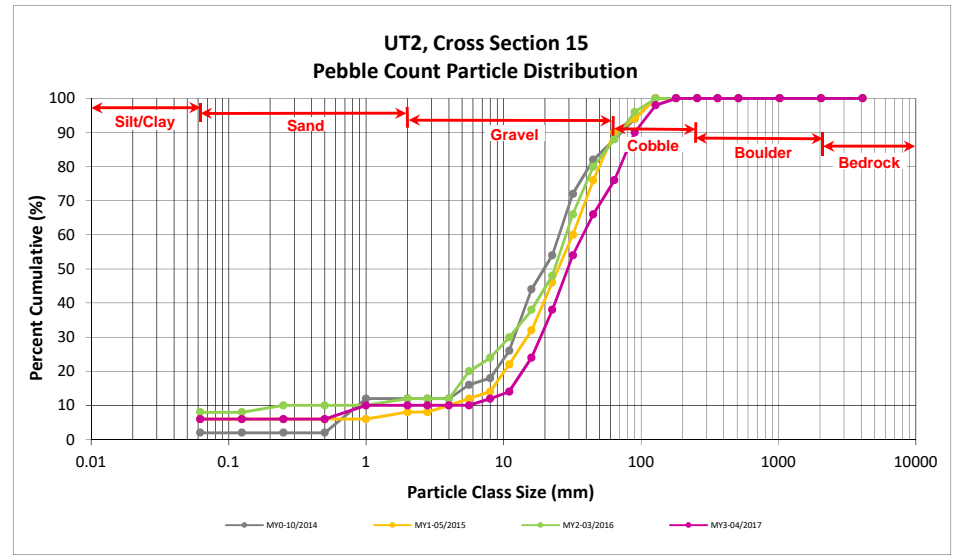

APPENDIX 5. Hydrology Summary Data and Plots


Table 13. Verification of Bankfull Events

Agony Acres Mitigation Site (DMS Project No. 95716)
Monitoring Year 3 - 2017

Reach	Date of Data Collection	Date of Occurrence	Method
UT1	8/1/2017	4/24/2017	Crest Gage/ Pressure Transducer
	8/1/2017	5/23/2017	
	8/1/2017	6/19/2017	
	10/24/2017	9/1/2017	
UT1A	8/1/2017	4/24/2017	
	8/1/2017	5/23/2017	
	8/1/2017	6/19/2017	
UT1B	8/1/2017	4/24/2017	
	8/1/2017	5/23/2017	
	8/1/2017	6/19/2017	
	10/24/2017	9/1/2017	
UT2	8/1/2017	4/24/2017	
	8/1/2017	5/23/2017	
	8/1/2017	6/19/2017	

Monthly Rainfall Data

Agony Acres Mitigation Site (DMS Project No. 95716)
Monitoring Year 3 - 2017

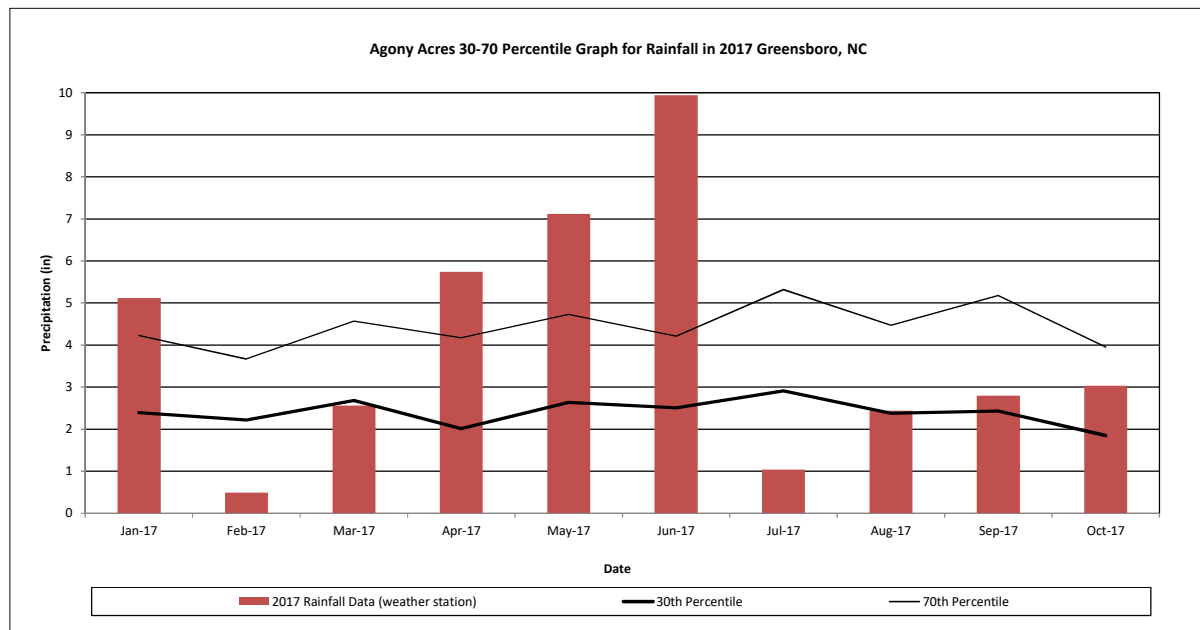


¹ 2017 monthly rainfall collected from weather station NC723, at Piedmont Triad Intl AP, NC (USDA, 2002).

² 30th and 70th percentile rainfall data collected from weather station NC723, at Piedmont Triad Intl AP, NC (USDA, 2002).

Stream Flow Gage Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

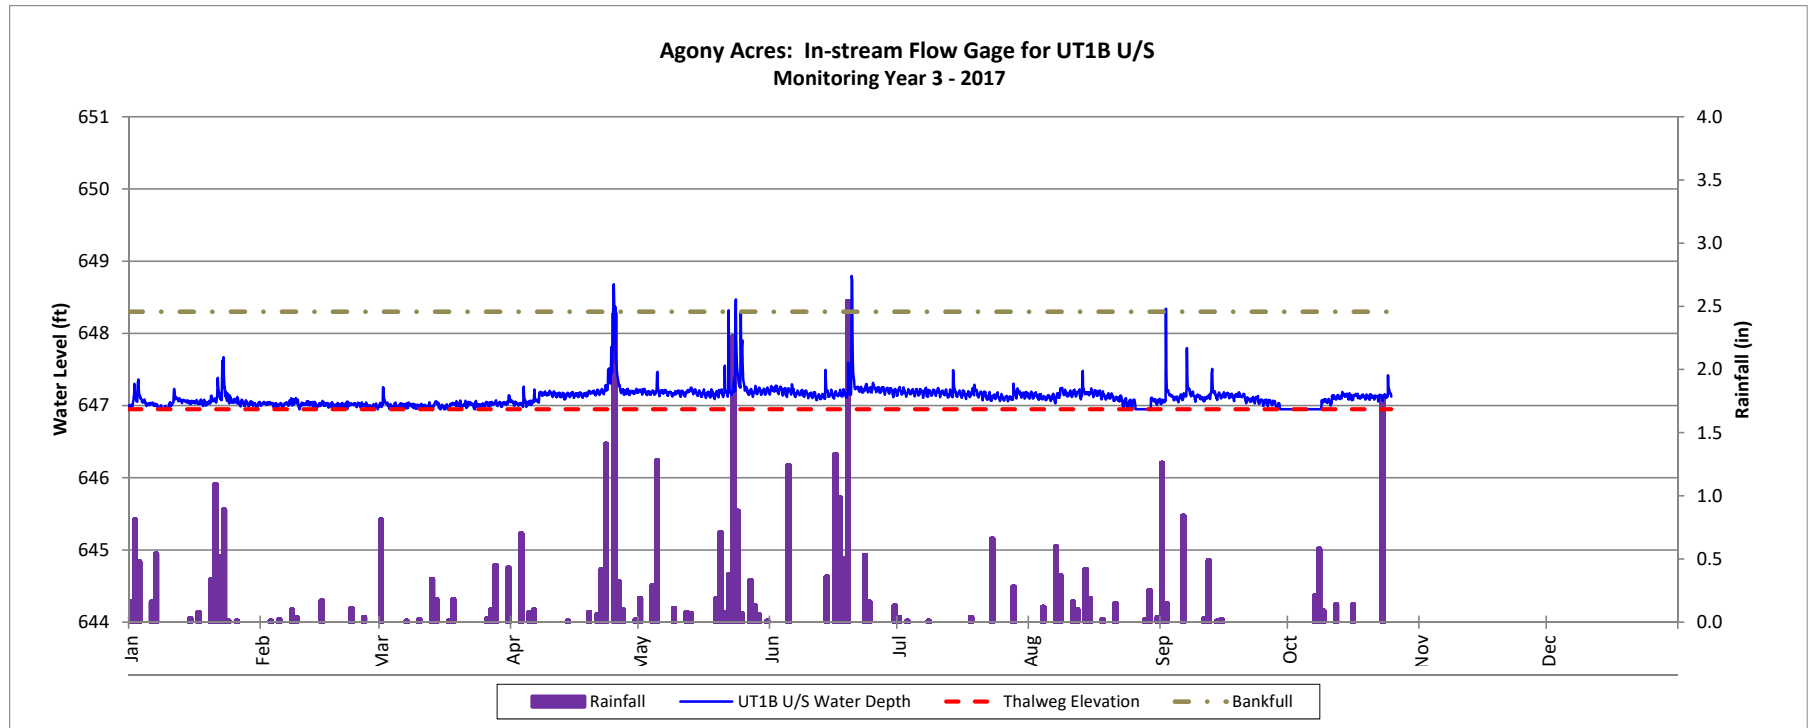

Stream Flow Gage Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 3 - 2017

