



# **MONITORING YEAR 5 ANNUAL REPORT**

Final

## **AGONY ACRES MITIGATION SITE**

Guilford County, NC

NCDEQ Contract 004949

DMS Project Number 95716

USACE Action ID Number 2012-1909

NCDWR Project Number 2013-1305

Data Collection Period: March 2019 – October 2019

Draft Submission Date: November 4, 2019

Final Submission Date: November 13, 2019

---

### **PREPARED FOR:**



### **NC Department of Environmental Quality Division of Mitigation Services**

1652 Mail Service Center

Raleigh, NC 27699-1652



November 13, 2019

Jeremiah Dow  
N.C. Division of Mitigation Services  
1652 Mail Service Center  
Raleigh, NC 27699-1652

RE: Monitoring Year 5 Report for Agony Acres Mitigation Site (95716)  
Cape Fear River Basin (03030002)  
Guilford County, North Carolina  
Contract No. 004949

Dear Mr. Dow,

We have reviewed the comments on the Monitoring Year 5 Report for the above referenced project dated November 7, 2019 and have revised the report based on these comments. The revised documents are submitted with this letter. Below are responses to each of your comments. For your convenience, the comments are reprinted with our response in italics.

1. Section 1.2  
Per the IRT site visit on Nov. 6, please add a section detailing the fence and gate damage caused by a fallen tree at an easement break stream crossing, and briefly discuss the rationale for not repairing the damage.  
*A discussion of the damage and rationale for not repairing the damage has been added.*
2. Section 1.2.1  
First paragraph, page 3 – Please remove or reword the last sentence. This sentence could be interpreted as assigning a 210 stem per acre success criteria for the buffer restoration areas at MY7.  
  
The last sentence has been reworded to avoid misinterpretation.
3. Section 1.2.5  
Per IRT comments during the site visit on Nov. 6, please include a brief discussion of UT1A flow gauge data here.  
*A discussion of the UT1A flow gauge data has been added.*
4. Appendix 2  
Figure 3.2 – Please add UT1A flow gauges to CCPV.  
*UT1A flow gauges have been added to the CCPV.*



5. Appendix 5

Please add flow gauge data for UT1A.

*UT1A flow gauge data has been added.*

If you have any questions, please contact me by phone (919) 851-9986, or by email (jlorch@wildlandseng.com).

Sincerely,

A handwritten signature in black ink, appearing to read "Jason Lorch".

**Jason Lorch, Monitoring Coordinator**

**PREPARED BY:**

---



**Wildlands Engineering, Inc.**  
312 West Millbrook Road, Suite 225  
Raleigh, NC 27609

**Jason Lorch**  
jlorch@wildlandseng.com  
Phone: 919.851.9986

## EXECUTIVE SUMMARY

Wildlands Engineering, Inc. (Wildlands) completed a full delivery project at the Agony Acres Mitigation Site (Site) for the North Carolina Division of Mitigation Services (DMS) to restore, enhance, and preserve a total of 9,052 linear feet (LF) of perennial and intermittent stream and restore 3.0 acres of riparian buffer in Guilford County, NC. The Site provides 6,468.3 Stream Mitigation Units (SMUs) and 3.0 Buffer Mitigation Units (BMUs). The Site is located in the Reedy Fork Watershed within Cape Fear River Basin Hydrologic Unit Code (HUC) 03030002 (Cape Fear 02) near Ossipee, NC (Figure 1). The streams are all unnamed tributaries (UT) to Reedy Fork and are referred to herein as UT1, UT1A, UT1B, and UT2. The buffer restoration component is adjacent to Reedy Fork and lower UT1.

The Site is located within the Jordan Lake Water Supply Watershed which has been designated as a Nutrient Sensitive Water. The Site's watershed is within Cape Fear local watershed HUC 03030002020070, which was not identified as a Cape Fear 02 Targeted Local Watershed (TLW) in DMS's 2009 Cape Fear River Basin Restoration Priority (RBRP) plan; however, this local watershed was later designated as a Targeted Resource Area (TRA) in the 2011 Request for Proposals (RFP) in the Cape Fear 02. The Agony Acres Mitigation Site fully supports the Cataloging Unit (CU)-wide functional objectives stated in the 2011 RFP to reduce and control nutrient inputs, reduce and control sediment inputs, and protect and augment Significant Natural Heritage Areas in the Cape Fear 02 River Basin. The Site will contribute to meeting the CU-wide Functional Improvement Objectives by establishing the following project goals:

- Reduce sediment inputs by removing cattle from streams and restoring degraded and eroding stream channels;
- Return a network of streams to a stable form that is capable of supporting biological functions;
- Reduce fecal coliform, nitrogen, and phosphorous inputs through removing cattle from streams and establishing and augmenting a forested riparian corridor;
- Protect existing high quality streams and forested buffers; and
- Improve and protect hydrologic inputs to the adjacent Reedy Fork Aquatic Habitat Significant Natural Heritage Area.

The project is helping meet the goals for the watershed outlined in the RBRP and provides numerous ecological benefits within the Cape Fear River Basin. While many of these benefits are limited to the Agony Acres project area; others, such as pollutant removal, reduced sediment loading, and improved aquatic and terrestrial habitat, have farther-reaching effects.

Stream restoration and enhancement construction efforts were completed in September 2014. Baseline as-built monitoring activities (MY0) were completed between October and December 2014. A conservation easement is in place on 30.74 acres of stream and riparian corridors to protect them in perpetuity.

Monitoring Year 5 (MY5) assessment and site visits were completed between March and October 2019 to assess the conditions of the project. Overall, the Site has met the required vegetation, stream, and hydrology success criteria for MY5. The overall stem density for the Site in MY5 is 473 stems per acre, which is greater than the interim success criterion of 260 stems per acre. All restored and enhanced streams are stable and functioning as designed and have recorded multiple bankfull events. UT1B has two pressure transducers installed to monitor stream flow. Both stream gages on UT1B met the hydrologic criteria for MY5 (Appendix 5).



**AGONY ACRES MITIGATION SITE**  
Monitoring Year 5 Annual Report

**TABLE OF CONTENTS**

**Section 1: PROJECT OVERVIEW .....1**

    1.1 Project Goals and Objectives ..... 2

    1.2 Monitoring Year 5 Data Assessment..... 3

        1.2.1 Vegetative Assessment ..... 3

        1.2.2 Vegetation Areas of Concern ..... 4

        1.2.3 Stream Assessment..... 4

        1.2.4 Stream Areas of Concern ..... 4

        1.2.5 Hydrology Assessment..... 4

        1.2.6 Maintenance Plan ..... 5

    1.3 Monitoring Year 5 Summary ..... 5

**Section 2: METHODOLOGY.....6**

**Section 3: REFERENCES .....7**

**APPENDICES**

**Appendix 1**

**General Tables and Figures**

Figure 1 Project Vicinity Map

Figure 2 Project Component/ Asset Map

Table 1 Project Components and Mitigation Credits

Table 2 Project Activity and Reporting History

Table 3 Project Contact Table

Table 4 Project Information and Attributes

**Appendix 2**

**Visual Assessment Data**

Figures 3.0 - 3.3 Integrated Current Condition Plan View

Tables 5a-d Visual Stream Morphology Stability Assessment Table

Table 6 Vegetation Condition Assessment Table

Stream Photographs

Vegetation Photographs

**Appendix 3**

**Vegetation Plot Data**

Table 7 Vegetation Plot Criteria Attainment

Table 8 CVS Vegetation Plot Metadata

Table 9 Planted and Total Stem Counts

**Appendix 4**

**Morphological Summary Data and Plots**

Tables 10a-d Baseline Stream Data Summary

Table 11 Morphology and Hydraulic Summary (Dimensional Parameters – Cross Section)

Tables 12a-f Monitoring Data – Stream Reach Data Summary

Cross Section Plots

Reachwide and Cross Section Pebble Count Plots

**Appendix 5**

**Hydrology Summary Data and Plots**

Table 13 Verification of Bankfull Events

Monthly Rainfall Data

Recorded In-Stream Flow Events

## Section 1: PROJECT OVERVIEW

---

The Agony Acres Mitigation Site (Site) is located in northeastern Guilford County, north of Gibsonville (Figure 1). From Gibsonville take NC 61 north 5.5 miles. Turn right on Sockwell Road and travel 1.4 miles. The project site is located north of Sockwell Road and is bound on the north by Reedy Fork. The Site is located in the Carolina Slate Belt of the Piedmont Physiographic Province. The project watershed is classified as approximately 65% managed herbaceous cover, 30% mixed upland hardwoods, 3% cultivated, 2% southern yellow pine, and the remaining 1% is low intensity development. The drainage area for the Agony Acres Mitigation Site is 358 acres.

The Site is located in the Reedy Fork Watershed within the Jordan Lake Water Supply Watershed which has been designated a Nutrient Sensitive Water. The project streams flow directly into Reedy Fork which flows into the Haw River and eventually into the Jordan Lake Reservoir. The Site's watershed is within Hydrologic Unit Code (HUC) 03030002020070 which was not identified as a Cape Fear 02 Targeted Local Watershed (TLW) in DMS's 2009 Cape Fear River Basin Restoration Priority (RBRP) plan; however, this HUC was later designated as a Targeted Resource Area (TRA) in the 2011 Request for Proposals (RFP) in the Cape Fear 02. The Site connects to Reedy Fork and three separate but connected Significant Natural Heritage areas. Reedy Fork Aquatic Habitat, Reedy Fork Slopes at NC 61, and Altamahaw Alluvial Forest are all listed on the NC Natural Heritage GIS database and are immediately adjacent to the Site. There are also records for several state threatened, special concern, and significantly rare mussel species in Reedy Fork.

North Carolina Division of Mitigation Services (DMS) completed a Local Watershed Plan (LWP) in 2008 on the HUC immediately downstream which begins at the confluence of Reedy Fork and the Haw River and includes Travis and Tickle Creeks. The Site is located less than one mile outside of the LWP area and has a very similar land use pattern. The 2008 Little Alamance, Travis, and Tickle Creeks LWP identified nutrient inputs from agriculture and stream bank erosion in altered reaches as major stressors within this TLW. The Site was identified as a stream and buffer restoration and cattle exclusion opportunity to improve water quality and buffers within the TRA.

The Site consists of four tributaries to Reedy Fork which are located within the North Carolina Division of Water Resources (NCDWR) subbasin 03-06-02 of the Cape Fear River Basin. The project stream reaches include UT1, UT1A, UT1B, and UT2.

Mitigation work within the Site included restoration, enhancement, and preservation of 9,052 linear feet (LF) of perennial and intermittent stream channel and 3.0 acres (ac) of riparian buffer restoration. The Site provides 6,468.3 Stream Mitigation Units (SMUs) and 3.0 Buffer Mitigation Units (BMUs). The stream areas were also planted with native vegetation to improve habitat and protect water quality.

The final mitigation plan was submitted and accepted by the DMS in March 2014. Construction activities were completed by Land Mechanic Designs, Inc. in September 2014. The planting was completed by Bruton Natural Systems, Inc. in December 2014. The baseline as-built survey was completed by Kee Mapping and Surveying, in October 2014. Annual monitoring will be conducted for seven years with the close-out anticipated to occur in 2022 given the success criteria are met. Appendix 1 provides more detailed project activity, history, contact information, directions, and watershed/site background information for this project.

## 1.1 Project Goals and Objectives

Prior to construction activities, the stream channels exhibited varying degrees of degradation across the Site. The Site was used as agricultural and pasture land and most of the buffers had been reduced to narrow corridors. Cattle had free access to the streams, which resulted in sporadic degraded stream banks and poor bed forms.

The restored stream channels on the Site were previously incised and overwidened in many locations, likely as a result of historic channelization. The alterations of the Site to promote cattle grazing and farming resulted in elimination of many of the ecological functions of this small stream complex. Specifically, functional losses at the Site included degraded aquatic habitat, altered hydrology (related to loss of floodplain connection and lowered water table), and a reduction of the quality and quantity of riparian wetland habitats and related water quality benefits. Ongoing bank erosion was also occurring at some locations due to high, overly steep banks, and lack of bank vegetation. Table 4 in Appendix 1 and Tables 10a-d in Appendix 4 present the pre-restoration conditions in detail.

The mitigation project is intended to provide numerous ecological benefits within the Cape Fear River Basin. While many of these benefits are limited to the Agony Acres Mitigation Site project area; others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Expected improvements to water quality and ecological processes are outlined below as project goals and objectives. These project goals were established and completed with careful consideration of goals and objectives that were described in the RBRP and to meet DMS's mitigation needs while maximizing the ecological and water quality uplift within the watershed.

The following project specific goals established in the Agony Acres Mitigation Plan (Wildlands, 2014) include:

- Reduce sediment inputs by removing cattle from streams and restoring degraded and eroding stream channels;
- Return a network of streams to a stable form that is capable of supporting biological functions important to sensitive species within and adjacent to the project site;
- Reduce fecal coliform, nitrogen, and phosphorous inputs through removing cattle from streams and establishing and augmenting a forested riparian corridor;
- Protect existing high quality streams and forested buffers that provide habitat important to sensitive species within and adjacent to the project site;
- Improve and protect hydrologic inputs to the adjacent Reedy Fork Aquatic Habitat Significant Natural Heritage Area; and
- Improve and protect hydrologic inputs to Reedy Fork, which is listed as impaired on the 2012 NC 303(d) list for impaired aquatic life and for elevated fecal coliform levels.

The project goals will be addressed through the following project objectives:

- On-site nutrient inputs were decreased by removing cattle from streams, re-establishing floodplain connectivity, and filtering on-site runoff through buffer zones. Off-site nutrient input will be absorbed on-site by filtering flood flows through restored floodplain areas, where flood flow will spread through native vegetation. Vegetation is expected to uptake excess nutrients.
- Stream bank erosion which contributes sediment load to the creeks was greatly reduced, if not eliminated, in the project area. Eroding stream banks were stabilized using bioengineering, natural channel design techniques, and grading to reduce bank angles and bank height. Storm flow containing grit and fine sediment is filtered through restored floodplain areas, where flow will spread through native vegetation. Spreading flood flows also reduces velocity and allows





sediment to settle out. Sediment transport capacity of restored reaches was improved so that capacity balances more closely to load. Sediment load reduction will be monitored through assessing bank stability with cross section surveys and visual assessment through photo documentation which serves as an accepted surrogate for direct turbidity measurements.

- Restored riffle/pool sequences promote aeration of water and create deep water zones, helping to lower water temperature. Establishment and maintenance of riparian buffers creates long-term shading of the channel flow to minimize thermal heating. Lower water temperatures will help maintain dissolved oxygen concentrations.
- In-stream structures were constructed to improve habitat diversity and trap detritus. Wood habitat structures were included in the stream as part of the restoration design. Such structures include log drops and rock structures that incorporate woody debris and native onsite rock.
- Adjacent buffer and riparian habitats were restored with native vegetation as part of the project. Native vegetation provides cover and food for terrestrial creatures. Native plant species were planted and invasive species treated. Eroding and unstable areas were stabilized with vegetation as part of this project.
- The restored land is protected in perpetuity through a conservation easement.

The design streams were restored to the appropriate form based on the surrounding landscape, climate, and natural vegetation communities but also with strong consideration to existing watershed conditions and trajectory. Specifically, the site design was developed to restore a small stream complex directly adjacent to Reedy Fork. Other key factors addressed in the design were to create stable habitats, improve riparian buffers, and restore the natural migration patterns for fish spawning. Figure 2 and Table 1 in Appendix 1 present the stream mitigation components for the Agony Acres Mitigation Site.

## 1.2 Monitoring Year 5 Data Assessment

Annual monitoring and quarterly site visits were conducted during MY5 to assess the condition of the project. The stream and buffer success criteria for the Site follow the approved success criteria presented in the Agony Acres Mitigation Plan (Wildlands, 2014). During an IRT site visit on November 6, 2019, the group observed and discussed damage to fencing and gates at the external easement crossing between UT1A Reach 3 and UT1A Reach 4. A tree had fallen perpendicularly across the crossing damaging the fence and gates on both sides. The fence was not repaired because no livestock are moved through this crossing. Attendees of the site visit agreed that it was not necessary to repair fencing at this location and elsewhere on the project site so long as livestock remained excluded from the conservation easement.

### 1.2.1 Vegetative Assessment

Planted woody vegetation was monitored in accordance with the guidelines and procedures developed by the Carolina Vegetation Survey-DMS Level 2 Protocol (Lee et al., 2006). A total of 16 10 meter by 10 meter vegetation plots were established during the baseline monitoring within the project easement areas. The final vegetative success criteria for the stream restoration and enhancement areas will be the survival of 210 planted stems per acre in the riparian corridor at the end of the required monitoring period (MY7). The interim measure of vegetative success is the survival of at least 260 stems per acre at the end of the fifth year of monitoring (MY5). Planted vegetation must average 10 feet in height in each plot at the end of the seventh year of monitoring. The final vegetative success criteria for the buffer restoration areas will be the survival of 320 planted stems per acre in the riparian corridor at the end of the required monitoring period. Wildlands plans to monitor the buffer restoration area on the same schedule as the rest of the project.

The MY5 vegetation survey was completed in August 2019. The 2019 vegetation monitoring resulted in a site-wide average stem density of 473 planted stems per acre, which is greater than the interim requirement of 260 planted stems per acre at MY5, but approximately 27% less than the baseline density recorded at MY0. Fifteen out of the 16 plots exceed the MY5 stem density criterion of 260 planted stems per acre. Plot 10 represents a density of 202 planted stems per acre but represents a density of 405 stems per acre when including volunteers (Table 9, Appendix 3). Site-wide average and median values for planted stem height are 11.0 feet and 9.6 feet, respectively. With the exception of plot 10, average and median heights within individual plots have either exceeded or are approaching 10 feet (data not shown). Both the average and median value for planted stem height in plot 10 is 2.3 feet. Refer to Appendix 2 for vegetation plot photographs and the vegetation condition assessment table and Appendix 3 for vegetation data tables.

### **1.2.2 Vegetation Areas of Concern**

During MY5, defined populations of Chinese privet (*Ligustrum sinense*), multiflora rose (*Rosa multiflora*), Japanese honeysuckle (*Lonicera japonica*), and callery pear (*Pyrus calleryana*) were identified throughout the site (Figures 3.1-3.3). Japanese hops (*Humulus japonica*) and sweet autumn virginsbower (*Clematis terniflora*) were identified within the buffer restoration area along Reedy Fork (Figure 3.3). All of these defined populations of invasive vegetation were treated during June and October of 2019. Vegetation plot 1 is within a callery pear removal area, but no surviving callery pear stems were present in the plot at the time of inventory. Additionally, the entire site was spot treated for scattered invading invasive individuals to prevent spreading. This treatment included in the tree of heaven (*Ailanthus altissima*) stems recorded in vegetation plot five. In general, the individuals targeted in this treatment were dispersed at low density.

### **1.2.3 Stream Assessment**

Morphological surveys for MY5 were conducted in March 2019. All streams within the Site are stable with little to no erosion and have met the success criteria for MY5. While there have been some minor post-construction adjustments within the restored channels; the cross sections show little to no change in the bankfull area, maximum depth, or width-to-depth ratio. Surveyed riffle cross sections fell within the parameters defined for channels of the appropriate Rosgen stream type. Pebble counts indicated coarser materials in the riffle features and finer particles in the pool features.

Visual assessment indicated streams are laterally and vertically stable throughout the project. Refer to Appendix 2 for the visual stability assessment table, CCPV Maps, and reference photographs. Refer to Appendix 4 for the morphological data and plots.

### **1.2.4 Stream Areas of Concern**

Beaver activity occurred on UT1 where it approaches the Reedy Fork floodplain (Figure 3.2). Beaver activity was identified in September and removal was completed in October. Minimal damage occurred to the stream channels and tree community.

### **1.2.5 Hydrology Assessment**

Two bankfull flow events within separate years must be documented on the restoration and enhancement reaches within the seven-year monitoring period. In addition, the presence of baseflow must be documented along portions of UT1B constructed with a Priority I restoration approach. Baseflow must be present for at least some portion of the year (most likely in the winter/early spring) during years with normal rainfall conditions.

Multiple bankfull events were recorded on all streams at the Site during MY5 (Table 13). Bankfull Events on all streams have been recorded during previous monitoring years; therefore, the Site has met the bankfull stream hydrology criterion for the duration of the monitoring period.

The downstream flow gage in UT1B recorded flow above the thalweg elevation throughout MY5 with the exception of few, scattered two to eight hour periods during July, August, and September. The upstream flow gage in UT1B recorded baseflow throughout the year except for September 11<sup>th</sup> through October 19<sup>th</sup> which was during a drought with below normal precipitation (Appendix 5). UT1B has met the baseflow criterion for MY1 through MY5.

Stream flow was recorded at five locations in UT1A during MY5, but there is no hydrology performance standard for this stream other than the bankfull flow requirement (Figure 3.2). Flow gages 1, 3, 4, and 5 indicate that UT1A had consistent flow from the beginning of the year through June. From June through the remainder of the 2019 monitoring year, UT1A had sporadic stream flow. Flow gage 2 recorded short interruptions to baseflow during July and August and a longer interruption to baseflow during September and October. Below normal rainfall was recorded during May, July, September, and October which likely contributed to these results (Appendix 5). Stream flow on UT1A will continue to be monitored through the duration of the monitoring period.

#### **1.2.6 Maintenance Plan**

The entire site will continue to be monitored and treated for invasive species as necessary. The seed bank of the Japanese hops area along Reedy Fork has been substantially reduced but will likely require additional treatment. The Site will continue to be monitored for beaver activity.

### **1.3 Monitoring Year 5 Summary**

Vegetation, stream, and hydrology criteria were met for MY5. Fifteen out the 16 vegetation plots attained the interim planted stem density requirement of 260 stems per acre. Plot 10 had a planted stem density of 202 planted stems per acre but had a density of 405 stems per acre when including volunteer species. All steams at the Site are stable and functioning as designed. UT1B attained the baseflow criterion and multiple bankfull events were recorded on all streams during MY5.

## Section 2: METHODOLOGY

---

Geomorphic data was collected following the standards outlined in The Stream Channel Reference Site: An Illustrated Guide to Field Techniques (Harrelson et al., 1994) and in the Stream Restoration: A Natural Channel Design Handbook (Doll et al., 2003). Crest gages were installed in surveyed riffle cross sections and monitored quarterly. Hydrology attainment installation and monitoring methods are in accordance with the USACE (USACE, 2003) standards. Vegetation monitoring protocols followed the Carolina Vegetation Survey-DMS Level 2 Protocol (Lee et al., 2006). Reporting follows the DMS Monitoring Report Template and Guidance Version 1.3 (DMS, 2010).



## Section 3: REFERENCES

---

- Doll, B.A., Grabow, G.L., Hall, K.A., Halley, J., Harman, W.A., Jennings, G.D., and Wise, D.E. 2003. Stream Restoration A Natural Channel Design Handbook.
- Harrelson, Cheryl C; Rawlins, C.L.; Potyondy, John P. 1994. *Stream Channel Reference Sites: An Illustrated Guide to Field Technique*. Gen. Tech. Rep. RM-245. Fort Collins, CO: U.S. Department of Agriculture, Forest Service, Rocky Mountain Forest and Range Experiment Station. 61 p.
- Lee, Michael T., Peet, Robert K., Steven D., Wentworth, Thomas R. 2006. CVS-DMS Protocol for Recording Vegetation Version 4.0. Retrieved from <http://www.ncdms.net/business/monitoring/veg/datasheets.htm>.
- Multi-Resolution Land Characteristics Consortium (MRLC). 2001. National Land Cover Database. <http://www.mrlc.gov/nlcd.php>
- North Carolina Division of Water Resources (NCDWR). 2011. Surface Water Classifications. <http://portal.ncdeq.org/web/wq/ps/csu/classifications>
- North Carolina Division of Water Resources, 2005. Cape Fear River Basinwide Water Quality Plan. <http://h20.enr.state.nc.us/basinwide/draftCPFApril2005.htm>
- Rosgen, D. L. 1994. A classification of natural rivers. *Catena* 22:169-199.
- Rosgen, D.L. 1996. Applied River Morphology. Pagosa Springs, CO: Wildland Hydrology Books.
- United States Army Corps of Engineers (USACE), 2003. Stream Mitigation Guidelines. USACE, NCDEQ-DWR, USEPA, NCWRC.
- United States Geological Survey (USGS), 1998. North Carolina Geology. <http://www.geology.enr.state.nc.us/usgs/carolina.htm>
- Wildlands Engineering, Inc (2014). Agony Acres Mitigation Site Mitigation Plan. DMS, Raleigh, NC.



## **APPENDIX 1. General Tables and Figures**


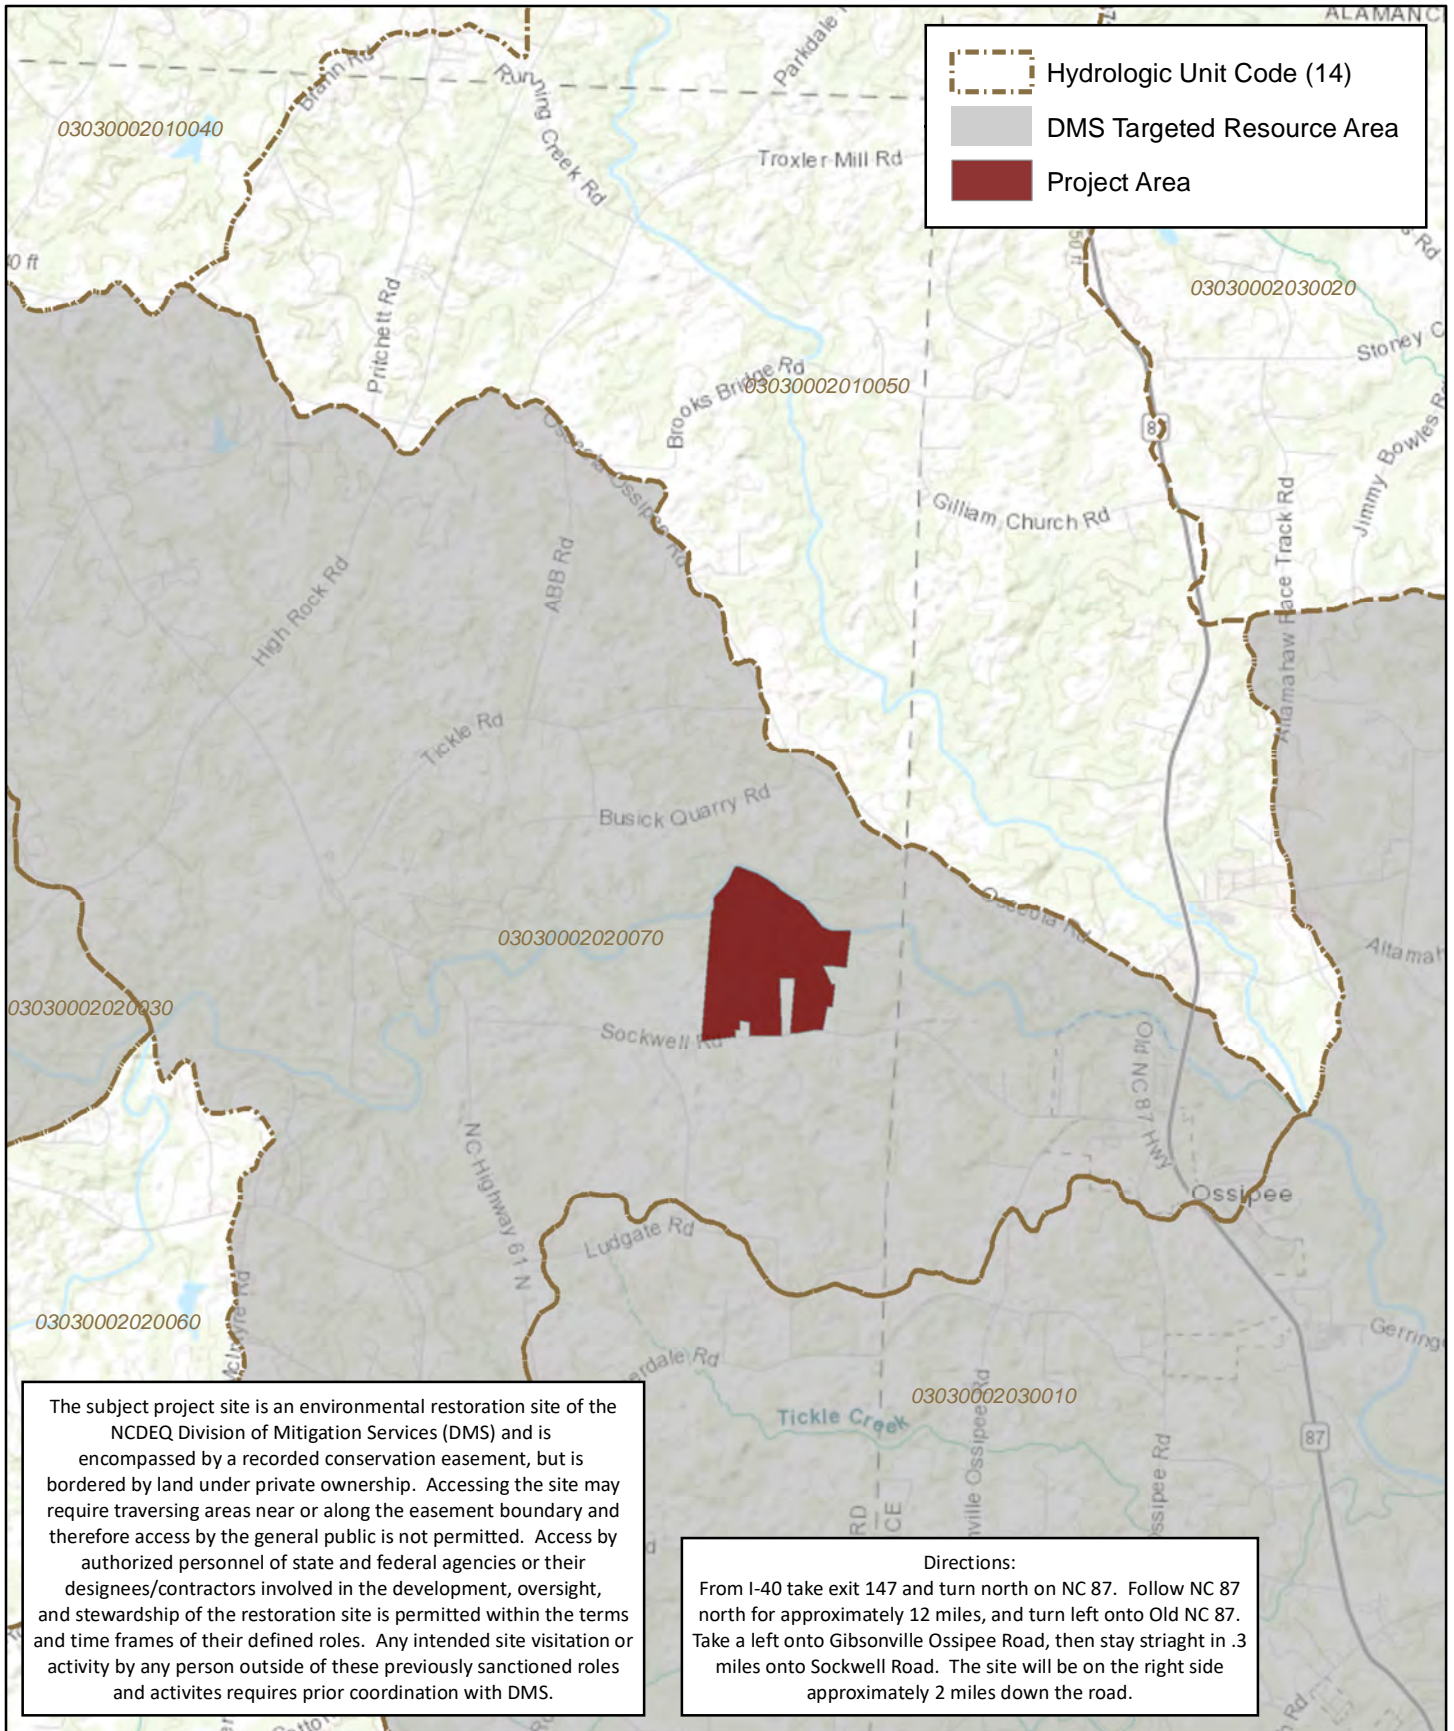


Figure 1. Project Vicinity Map  
 Agony Acres Mitigation Site  
 DMS Project No. 95716  
 Monitoring Year 5 - 2019


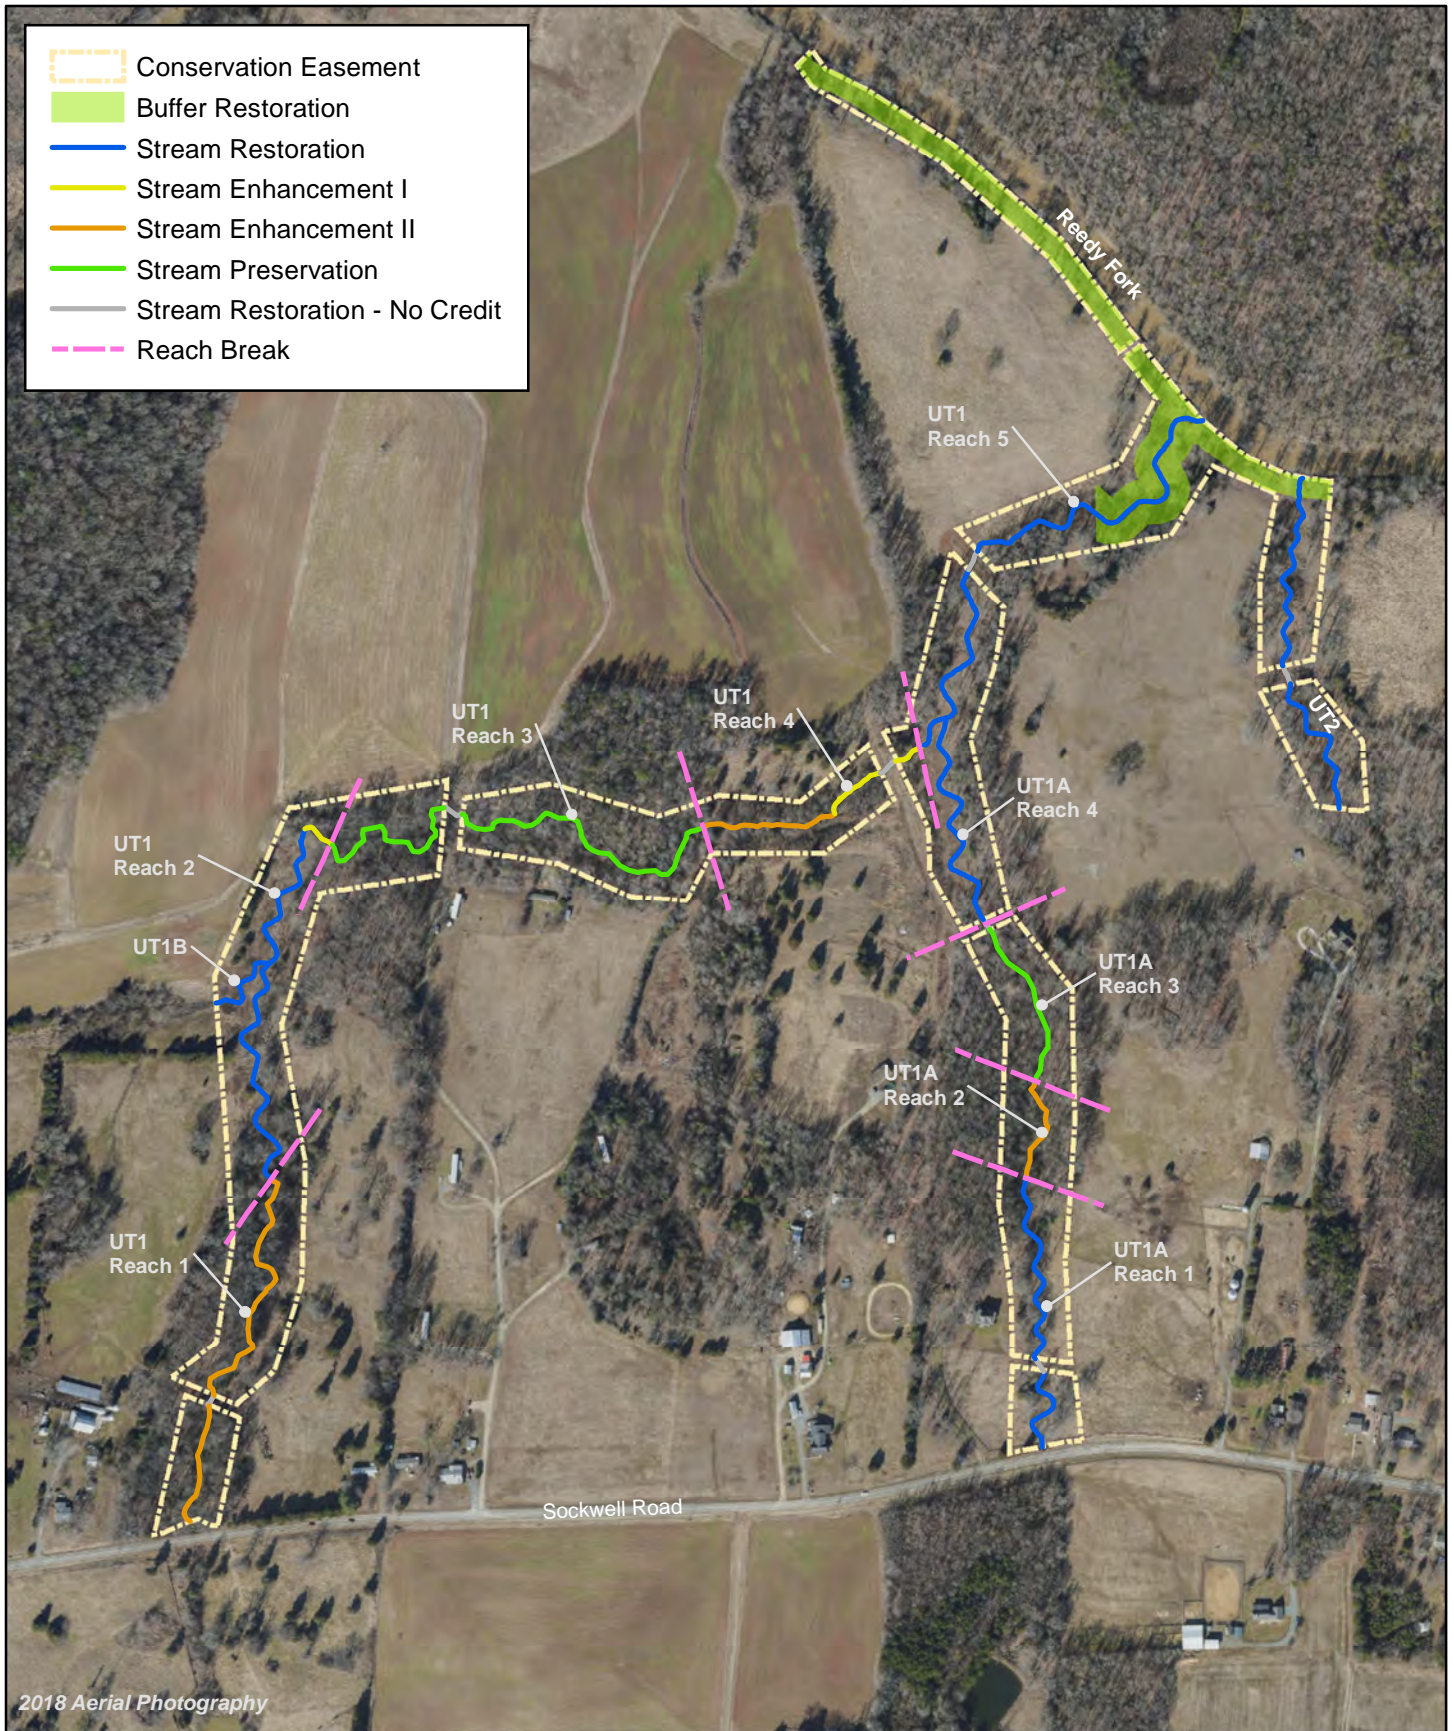


Figure 2. Project Component/Asset Map  
 Agony Acres Mitigation Site  
 DMS Project No. 95716  
 Monitoring Year 5 - 2019





**Table 1. Project Components and Mitigation Credits**

Agony Acres Mitigation Site (DMS Project No.95716)

Monitoring Year 5 - 2019

MITIGATION CREDITS									
	Stream		Riparian Wetland		Non-Riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset
Type	R	RE	R	RE	R	RE			
Totals	6,107.3**	361	N/A	N/A	N/A	N/A	130,680	N/A	N/A
PROJECT COMPONENTS									
Reach ID	As-Built Stationing/ Location	Existing Footage/ Acreage	Approach	Restoration or Restoration Equivalent	Restoration Footage/ Acreage	Mitigation Ratio	Credits (SMU/ WMU/BMU)		
STREAMS									
UT1-Reach 1 (DOT ROW)	100+00 to 100+14	40**	EII	Enhancement (No Credit)	40**	---	---		
UT1-Reach 1	100+14 to 103+62; 103+93 to 111+24	1,053**	EII	Enhancement	1,053**	2.5	421.2**		
UT1-Reach 1 (Easement Break)	103+62 to 103+93	31	EII	Enhancement (No Credit)	31	---	---		
UT1-Reach 2	111+24 to 122+38	1,039	P1	Restoration	1,114	1	1,114		
UT1-Reach 2	122+38 to 123+31	93	EI	Enhancement	93	1.5	62		
UT1-Reach 3	123+31 to 128+50; 129+06 to 137+37	1,350		Preservation	1,350	5	270		
UT1-Reach 3 (Easement Break)	128+50 to 129+06	56		Preservation (No Credit)	56	---	---		
UT1-Reach 4	137+37 to 140+92	355	EII	Enhancement	355	2.5	142		
UT1-Reach 4	140+92 to 142+66; 143+20 to 144+06	260	EI	Enhancement	260	1.5	173		
UT1-Reach 4 (Easement Break)	142+66 to 143+20	54	EI	Enhancement (No Credit)	54	---	---		
UT1-Reach 5	144+06 to 149+65; 150+20 to 158+94	1,355	P1/2	Restoration	1,433	1	1,433		
UT1-Reach 5 (Easement Break)	149+65 to 150+20	65	P1	Restoration (No Credit)	55	---	---		
UT1A-Reach 1 (DOT ROW)	200+00 to 200+05	5	P1	Restoration (No Credit)	5	---	---		
UT1A-Reach 1	200+05 to 202+64; 203+04 to 208+49	738	P1	Restoration	804	1	804		
UT1A-Reach 1 (Easement Break)	202+64 to 203+04	32	P1	Restoration (No Credit)	40	---	---		
UT1A-Reach 2	208+49 to 211+41	292	EII	Enhancement	292	2.5	117		
UT1A-Reach 3	211+41 to 215+98	457		Preservation	457	5	91		
UT1A-Reach 3 (Easement Break)	215+98 to 216+28	30	EII	Enhancement (No Credit)	30	---	---		
UT1A-Reach 4	216+28 to 222+78	461	P1	Restoration	650	1	650		
UT1B	300+00 to 302+19	243	P1	Restoration	219	1	219		
UT2	400+00 to 404+16; 404+67 to 410+23	975	P1	Restoration	972	1	972		
UT2 (Easement Break)	404+16 to 404+67	53	P1/2	Restoration (No Credit)	51	---	---		
Riparian Buffer Area	---	---	---	Restoration	3.0 (130,680 ft <sup>2</sup> )	1	130,680		

COMPONENT SUMMATION						
Restoration Level	Stream (LF)	Riparian Wetland (acres)		Non-Riparian Wetland (acres)	Buffer (acres)	Upland (acres)
		Riverine	Non-Riverine			
Restoration	5,192	-	-	-	3.0	-
Enhancement		-	-	-	-	-
Enhancement I	353					
Enhancement II	1,700**					
Creation		-	-	-		
Preservation	1,807	-	-	-		-
High Quality Preservation	-	-	-	-		-

N/A: not applicable

\* Credit calculations were originally calculated along the as-built thalweg and updated to be calculated along stream centerlines as stated in the approved Mitigation Plan for Monitoring Year 3 after discussions with NC IRT.

\*\*Values updated during MY4 to account for DOT culvert replacement project.

**Table 2. Project Activity and Reporting History**  
 Agony Acres Mitigation Site (DMS Project No.95716)  
 Monitoring Year 5 - 2019

Activity or Report	Date Collection Complete	Completion or Scheduled Delivery
Mitigation Plan	October 2013- March 2014	March 2014
Final Design - Construction Plans	April 2014- June 2014	June 2014
Construction	June 2014- September 2014	September 2014
Temporary S&E mix applied to entire project area <sup>1</sup>	September 2014	September 2014
Permanent seed mix applied to reach/segments	September 2014	September 2014
Bare root and live stake plantings for reach/segments	December 2014	December 2014
Baseline Monitoring Document (Year 0)	Stream Survey	October 2014
	Vegetation Survey	December 2014
Year 1 Monitoring	Stream Survey	May 2015
	Vegetation Survey	September 2015
Year 2 Monitoring	Stream Survey	March 2016
	Vegetation Survey	June 2016
Supplemental Planting		December 2016
Year 3 Monitoring	Stream Survey	April 2017
	Vegetation Survey	August 2017
Invasive Vegetation Treatment		September-October 2018
Year 4 Monitoring	Stream Survey	N/A
	Vegetation Survey	N/A
Invasive Vegetation Treatment		June 2019
Invasive Vegetation Treatment		October 2019
Beaver Removal		October 2019
Year 5 Monitoring	Stream Survey	March 2019
	Vegetation Survey	August 2019
Year 6 Monitoring	Stream Survey	2020
	Vegetation Survey	2020
Year 7 Monitoring	Stream Survey	2021
	Vegetation Survey	2021

<sup>1</sup>Seed and mulch is added as each section of construction is completed.


**Table 3. Project Contact Table**  
 Agony Acres Mitigation Site (DMS Project No.95716)  
 Monitoring Year 5 - 2019

<b>Designer</b> Nicole Macaluso, PE, CFM	<b>Wildlands Engineering, Inc.</b> 312 West Millbrook Road, Suite 225 Raleigh, NC 27609 919.851.9986
<b>Construction Contractor</b>	<b>Land Mechanic Designs, Inc.</b> 126 Circle G Lane Willow Spring, NC 27592
<b>Planting Contractor</b>	<b>Bruton Natural Systems, Inc</b> P.O. Box 1197 Fremont, NC 27830
<b>Seeding Contractor</b>	<b>Land Mechanic Designs, Inc.</b> 126 Circle G Lane Willow Spring, NC 27592
<b>Seed Mix Sources</b>	<b>Green Resource, LLC</b>
<b>Nursery Stock Suppliers</b>	
<b>Bare Roots</b>	<b>Dykes and Son Nursery</b>
<b>Live Stakes</b>	<b>Bruton Natural Systems, Inc</b>
<b>Monitoring Performers</b> Monitoring, POC	<b>Wildlands Engineering, Inc.</b> Jason Lorch 919.851.9986, ext. 107

**Table 4. Project Information and Attributes**  
 Agony Acres Mitigation Site (DMS Project No.95716)  
 Monitoring Year 5 - 2019

PROJECT INFORMATION						
Project Name	Agony Acres Mitigation Site					
County	Guilford County					
Project Area (acres)	30.74 acres					
Project Coordinates (latitude and longitude)	36° 10' 40" N, 79° 33' 02" W					
PROJECT WATERSHED SUMMARY INFORMATION						
Physiographic Province	Piedmont					
River Basin	Cape Fear River					
USGS Hydrologic Unit 8-digit	03030002					
USGS Hydrologic Unit 14-digit	03030002020070					
DWR Sub-basin	03-06-02					
Project Drainage Area (acres)	358 acres					
Project Drainage Area Percentage of Impervious Area	<1%					
CGIA Land Use Classification	65% Managed Herbaceous Cover, 30% Mixed Upland Hardwoods, 3% Cultivated, 2% Southern Yellow Pine, <1% Low Intensity Development					
REACH SUMMARY INFORMATION						
Parameters	UT1 - Reaches 1 -3	UT1 - Reaches 4 & 5	UT1A	UT1B	UT2	
Length of reach (linear feet) - Post-Restoration	3,711	2,157	2,278	219	1,023	
Drainage area (acres)	228	358	103	61	61	
NCDWR stream identification score	42.5	46.5	41	29.25	32.25	
NCDWR Water Quality Classification	WS-V					
Morphological Description (stream type)	P	P	P/I	P	P	
Evolutionary trend (Simon's Model) - Pre- Restoration	I, III	III, IV	I, II/III	II/III	II/III	
Underlying mapped soils	Cecil sandy loam, Congaree loam, Coronaca clay loam, Enon fine sandy loam, Enon clay loam, Madison clay loam, Mecklenburg sandy clay loam, Wehadkee loam					
Drainage class	---	---	---	---	---	---
Soil Hydric status	---	---	---	---	---	---
Slope	---	---	---	---	---	---
FEMA classification	N/A					
Native vegetation community	Piedmont bottomland forest					
Percent composition exotic invasive vegetation -Post-Restoration	0%					
REGULATORY CONSIDERATIONS						
Regulation	Applicable?	Resolved?	Supporting Documentation			
Waters of the United States - Section 404	Yes	Yes	USACE Nationwide Permit No.27 and DWQ 401 Water Quality Certification No. 3885.			
Waters of the United States - Section 401	Yes	Yes	Certification No. 3885.			
Division of Land Quality (Dam Safety)	No	N/A	N/A			
Endangered Species Act	Yes	Yes	Agony Acres Mitigation Plan; Wildlands determined "no effect" on Guilford County listed endangered species.			
Historic Preservation Act	Yes	Yes	No historic resources were found to be impacted (letter from SHPO dated 1/15/13).			
Coastal Zone Management Act (CZMA)/Coastal Area Management Act (CAMA)	No	N/A	N/A			
FEMA Floodplain Compliance	N/A	N/A	The project streams do not have an associated regulatory floodplain; however portions of UT1, UT1A, and UT2 are located within the floodway and flood fringe of Reedy Fork (FEMA Zone AE, FIRM panels 8838 and 8848).			
Essential Fisheries Habitat	No	N/A	N/A			

## APPENDIX 2. Visual Assessment Data

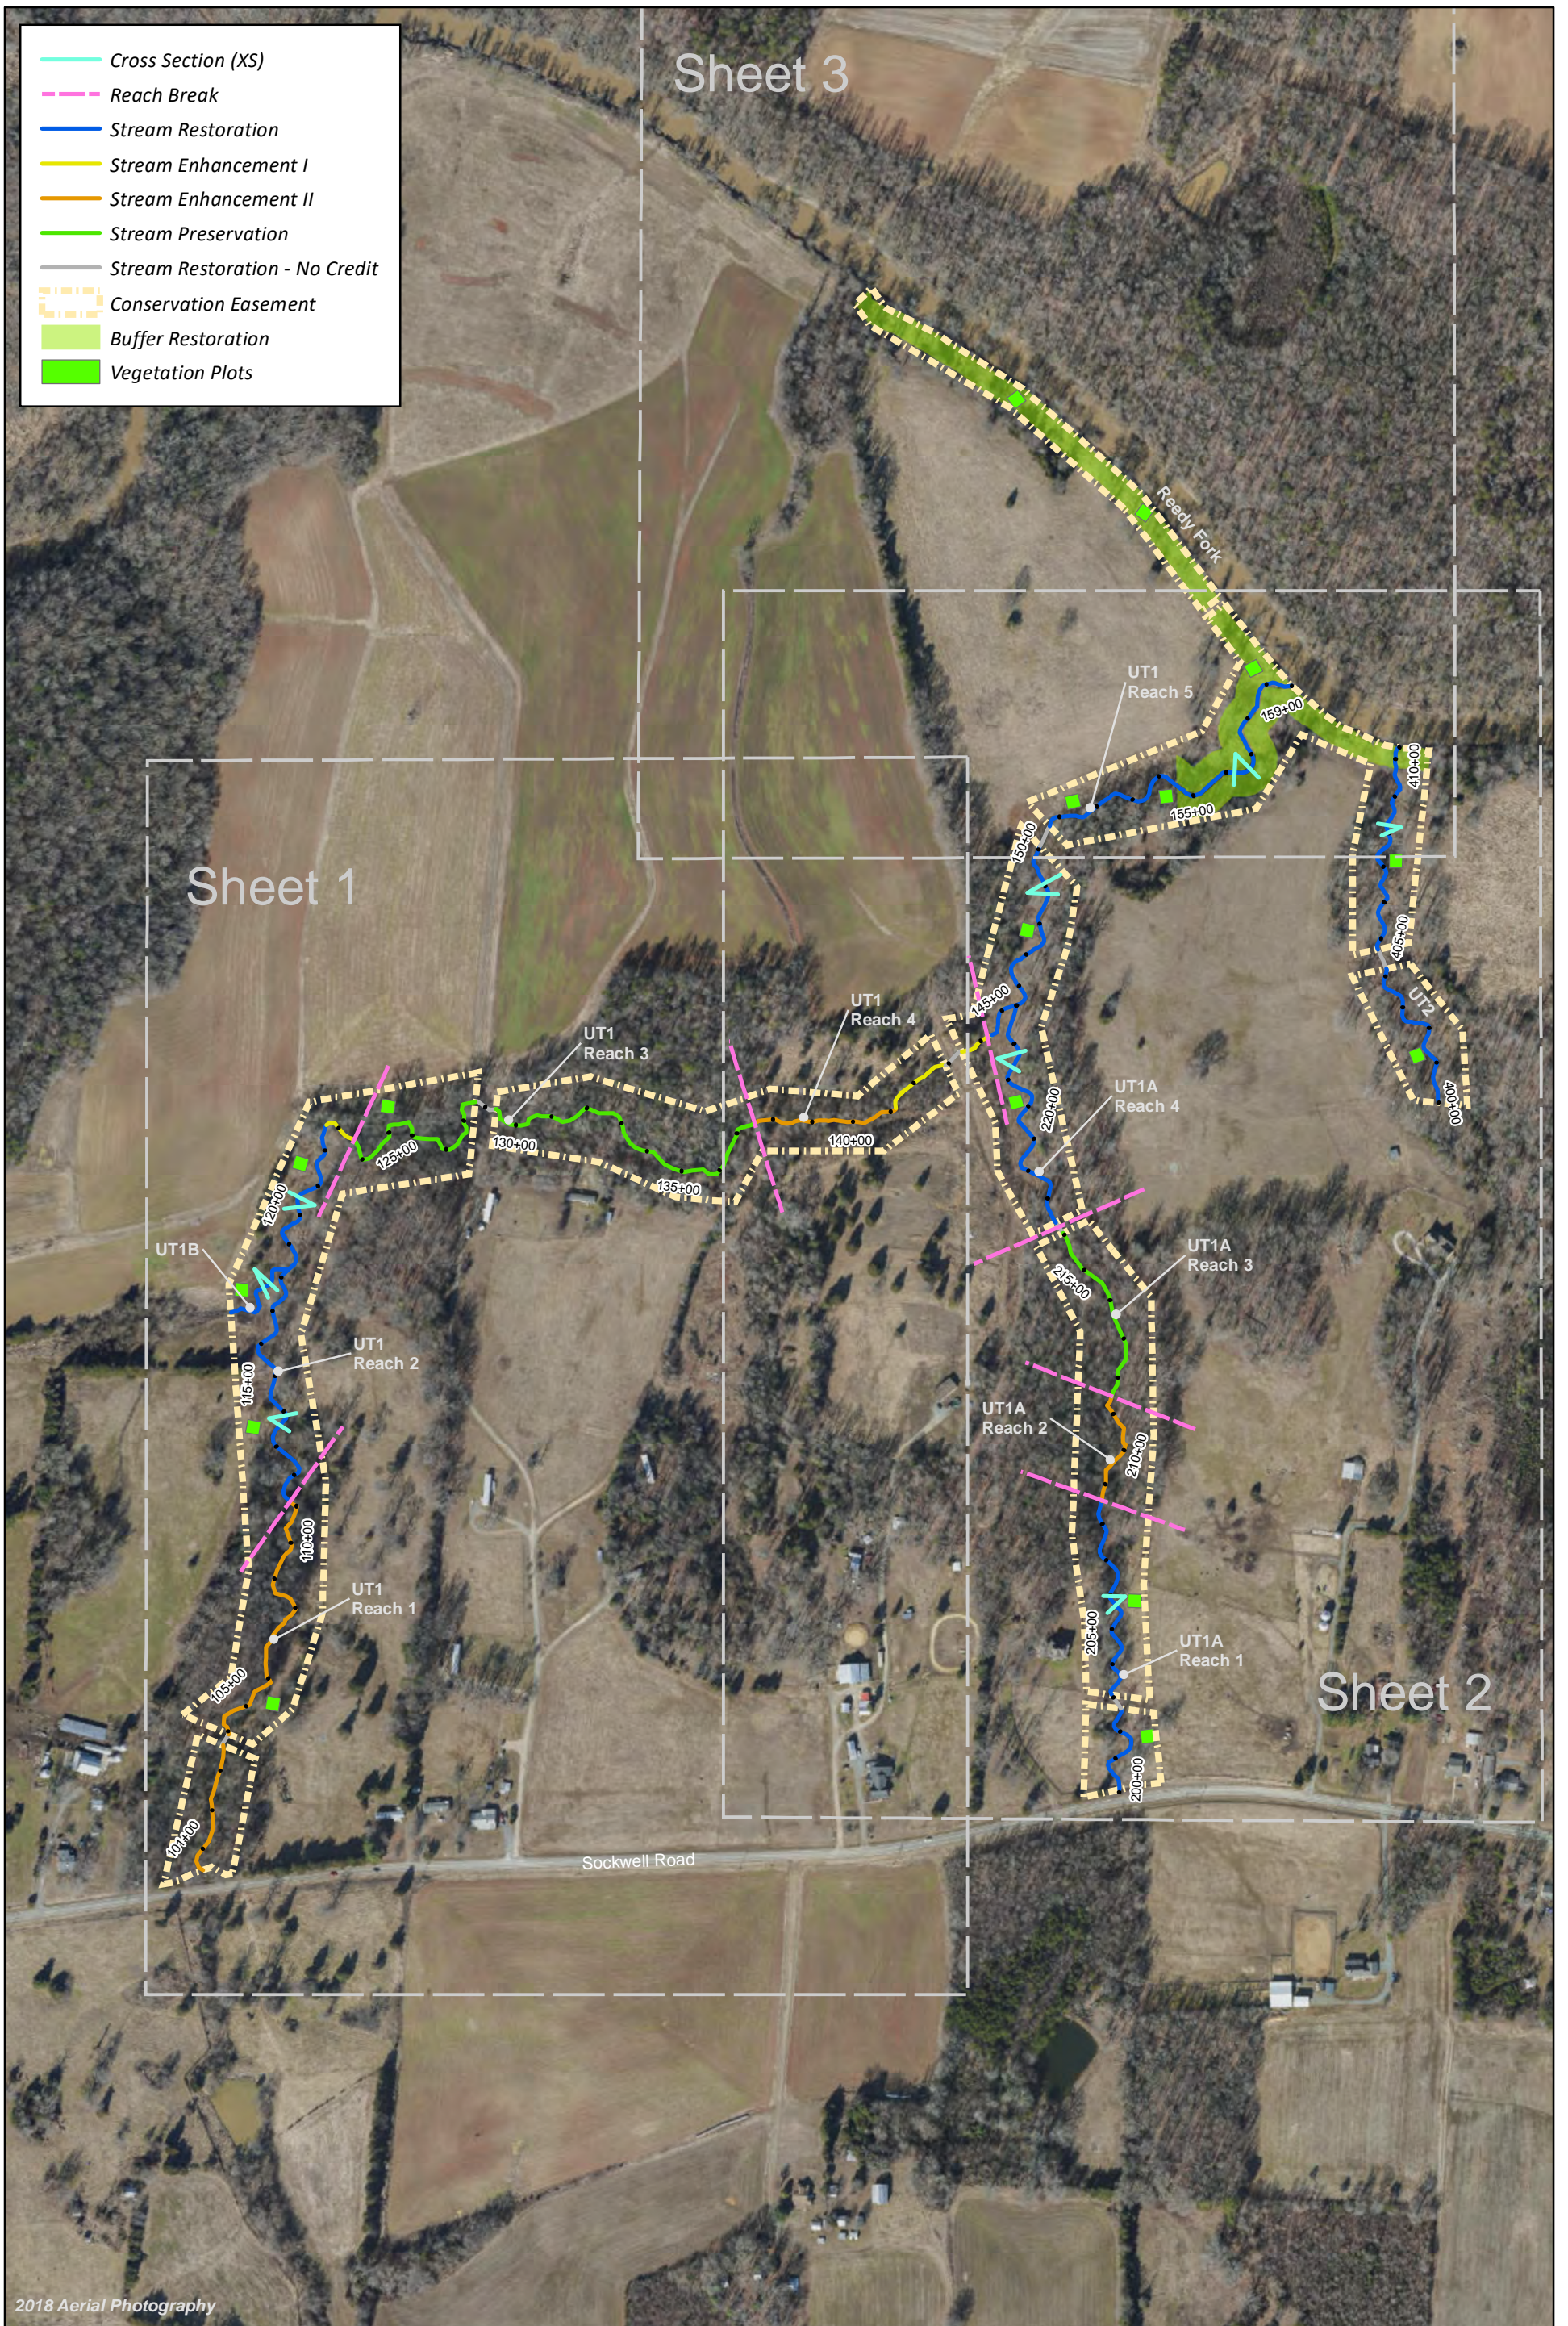

2018 Aerial Photography




0 250 500 Feet




Figure 3.0 Integrated Current Condition Plan View (Key)


Agony Acres Mitigation Site  
DMS Project No. 95716  
Monitoring Year 5 - 2019

Guilford County, NC

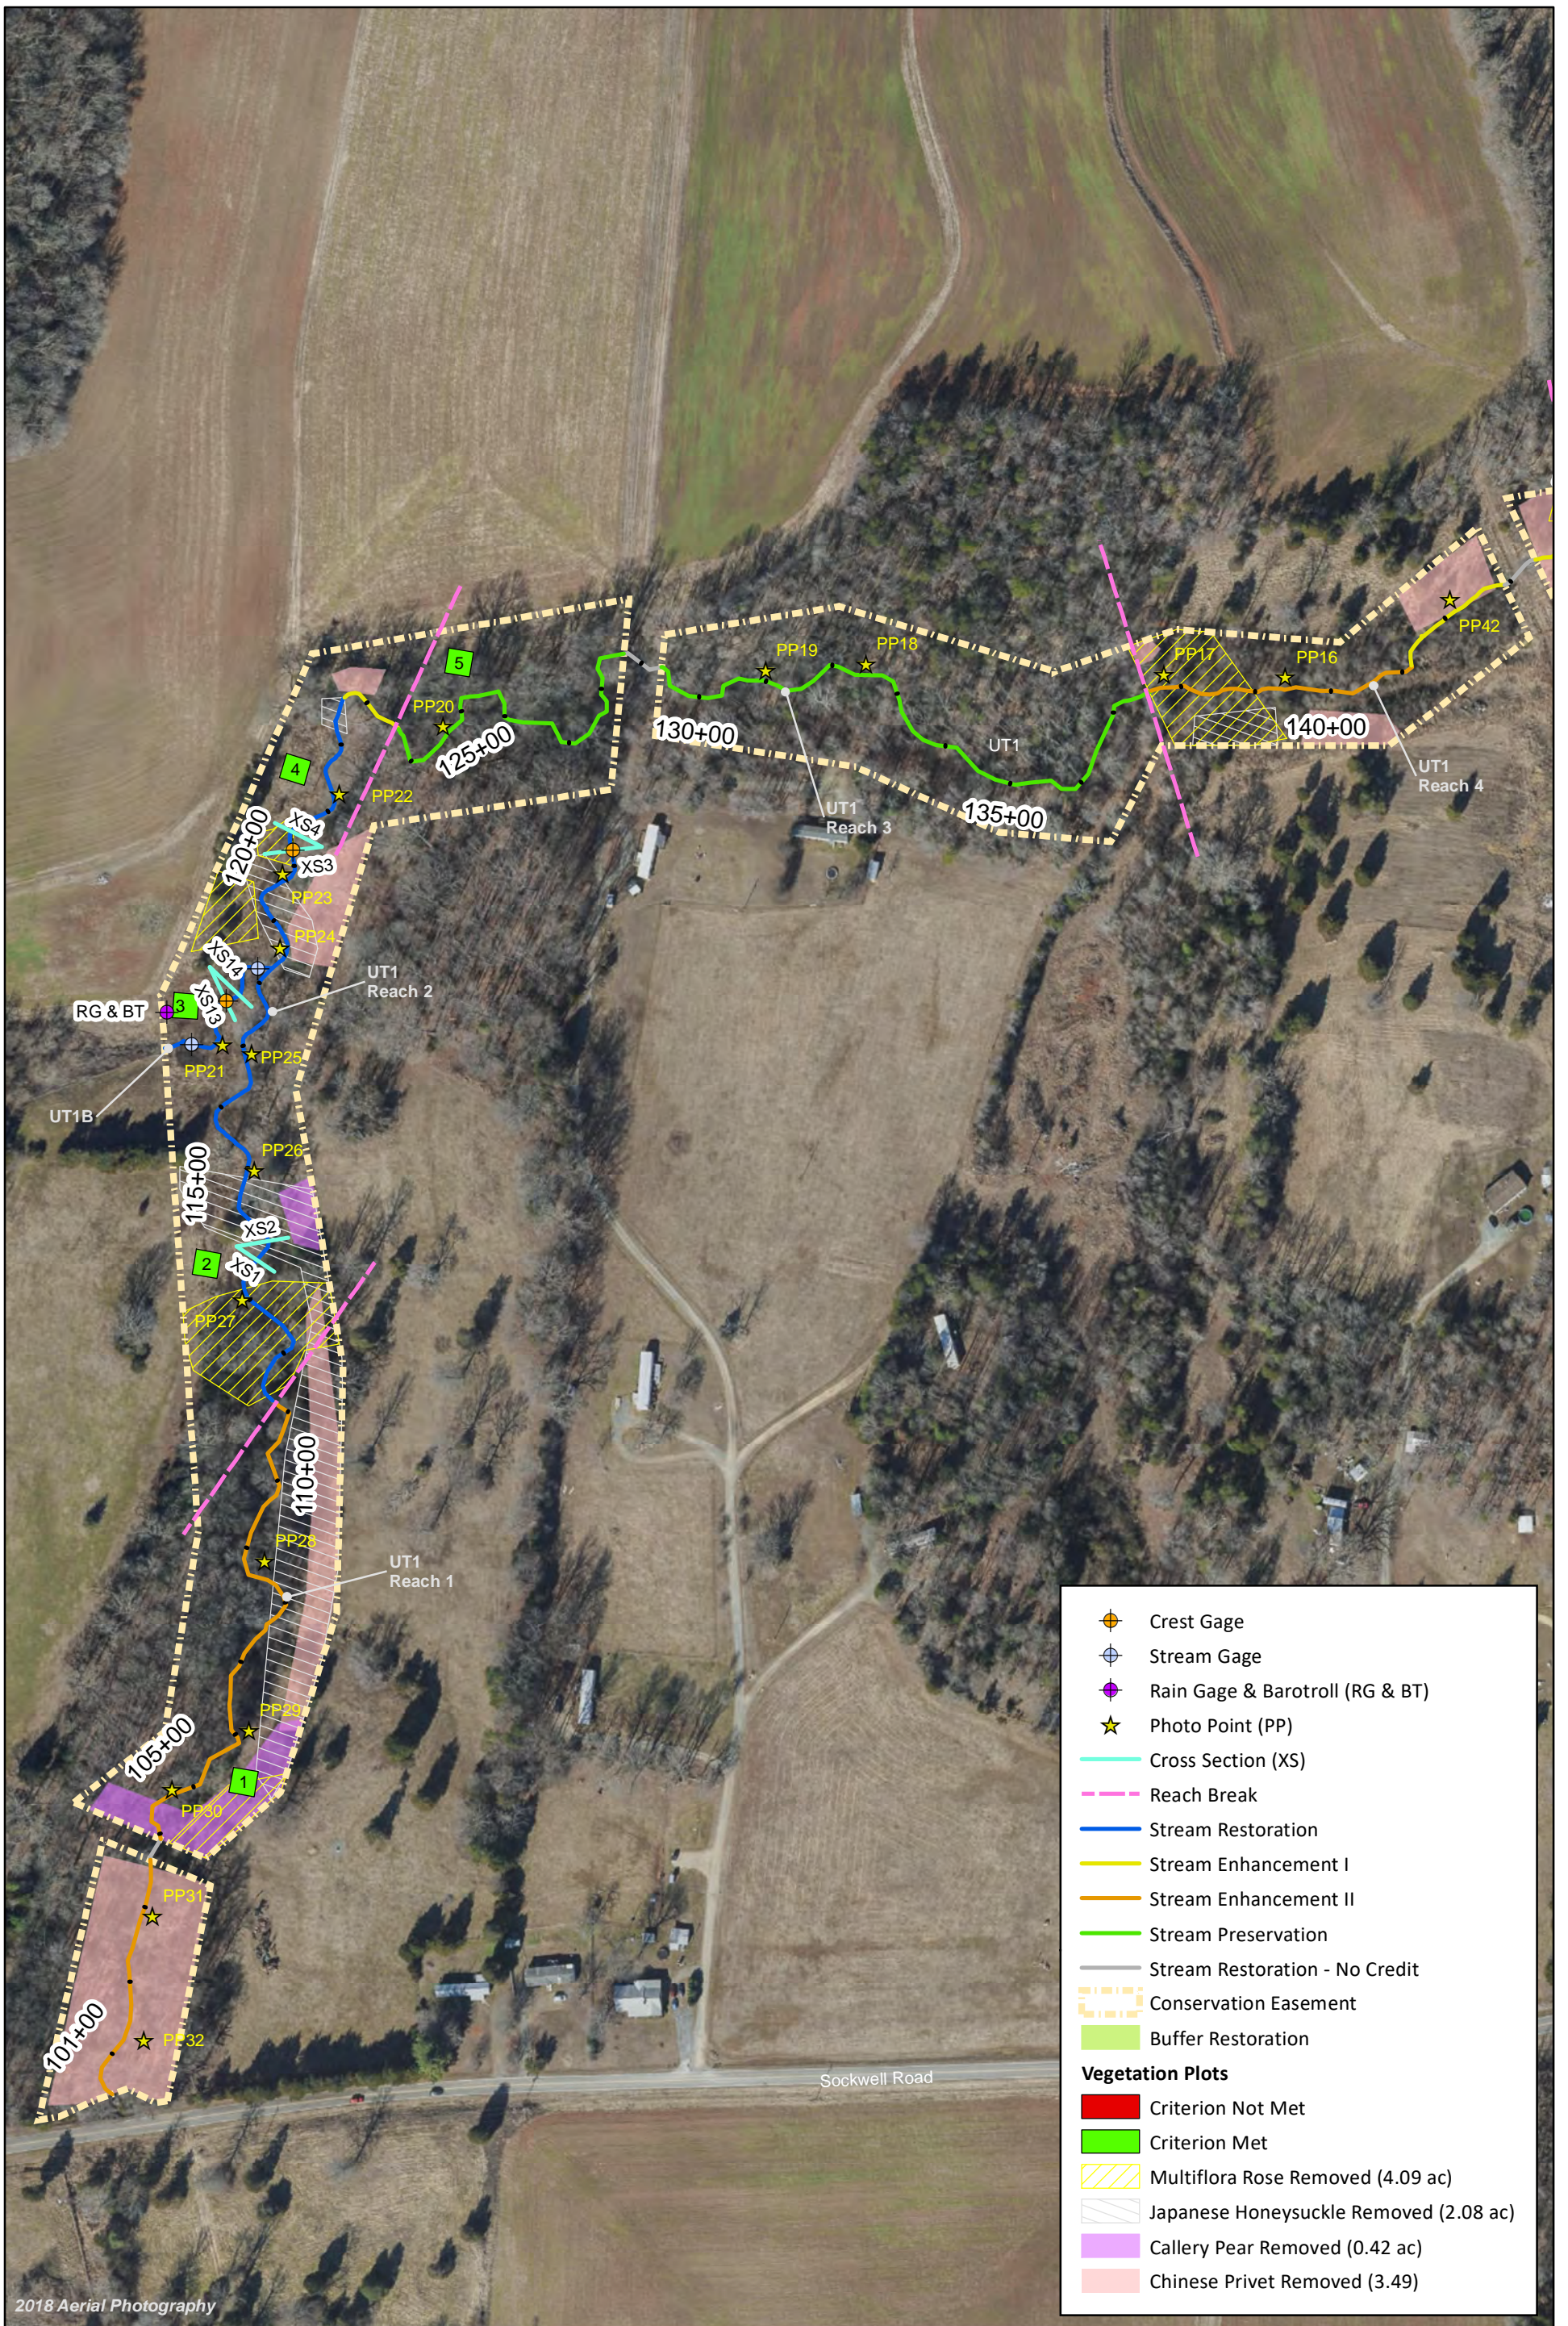

2018 Aerial Photography

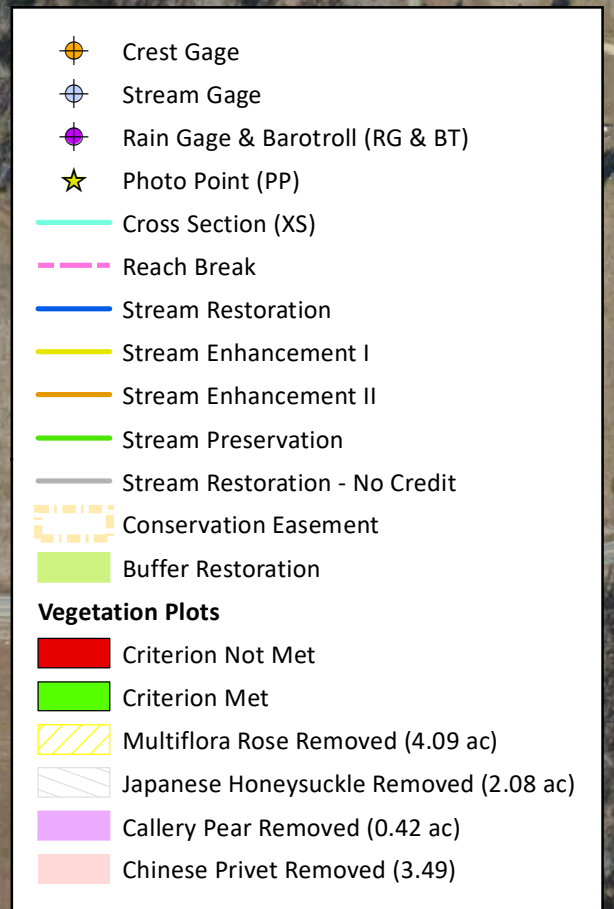

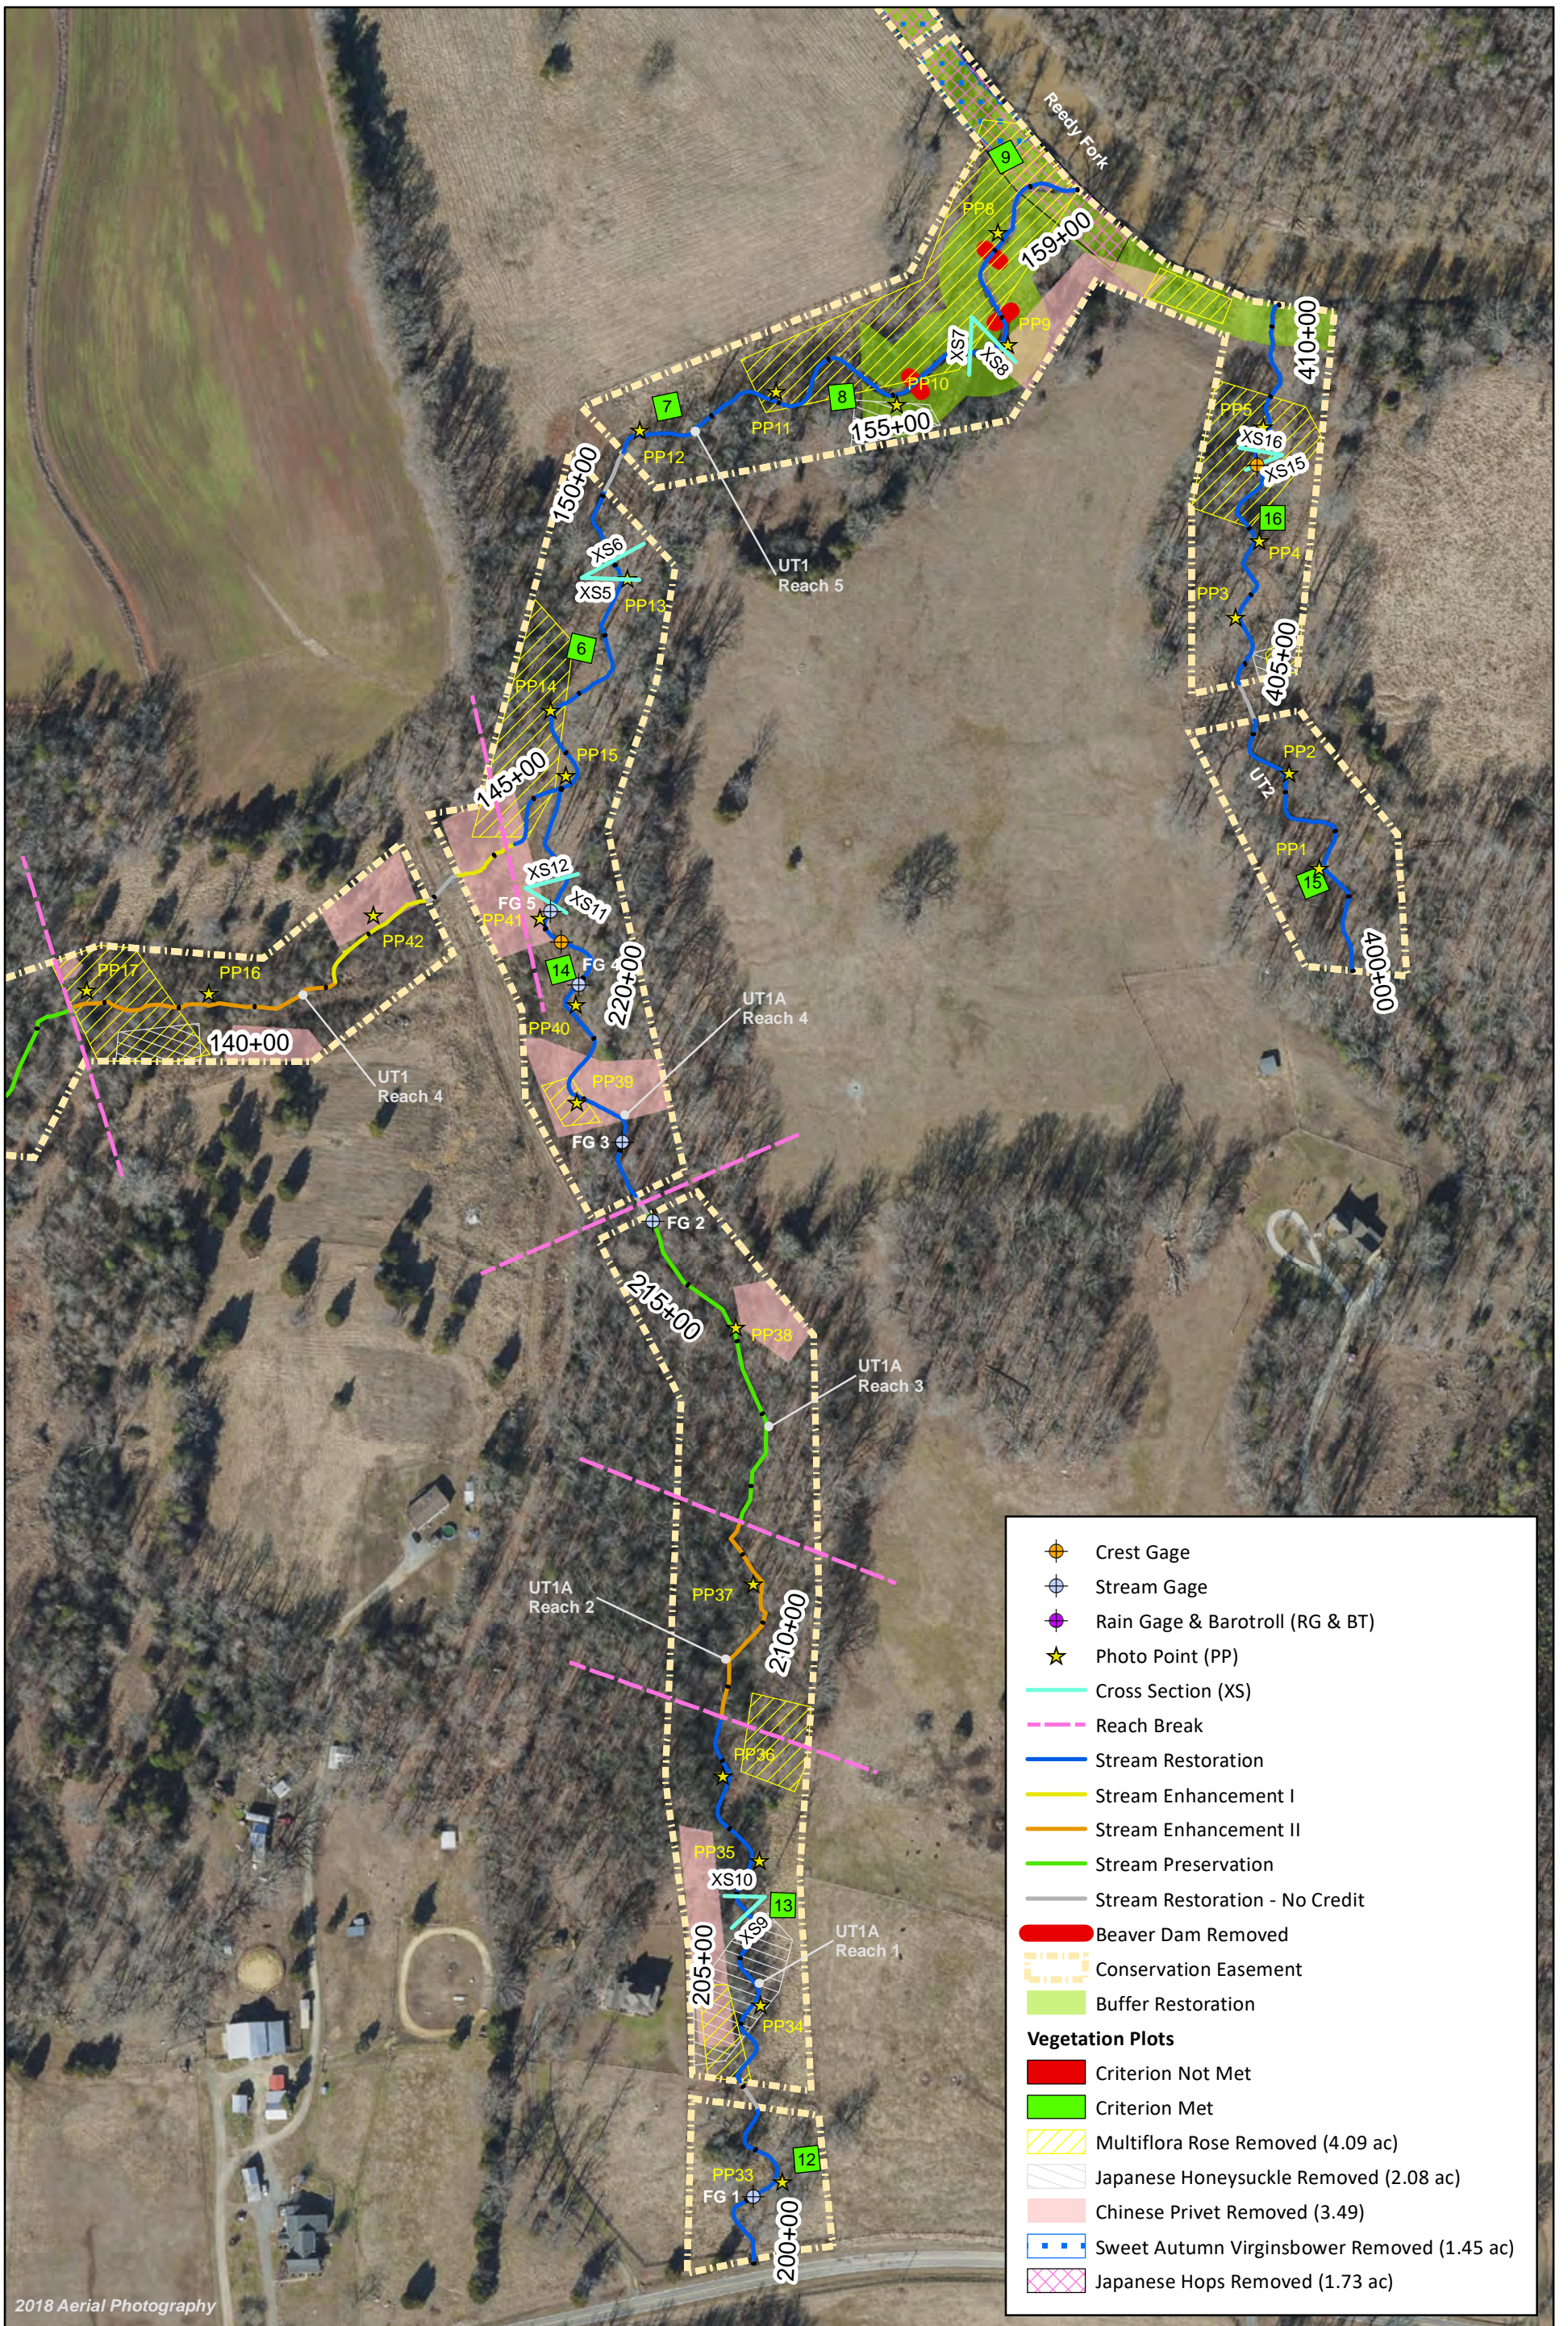


2018 Aerial Photography



0 250 500 Feet



Figure 3.2. Integrated Current Condition Plan View  
 (Sheet 2 of 3)  
 Agony Acres Mitigation Site  
 DMS Project No. 95716  
 Monitoring Year 5 - 2019  
 Guilford County, NC

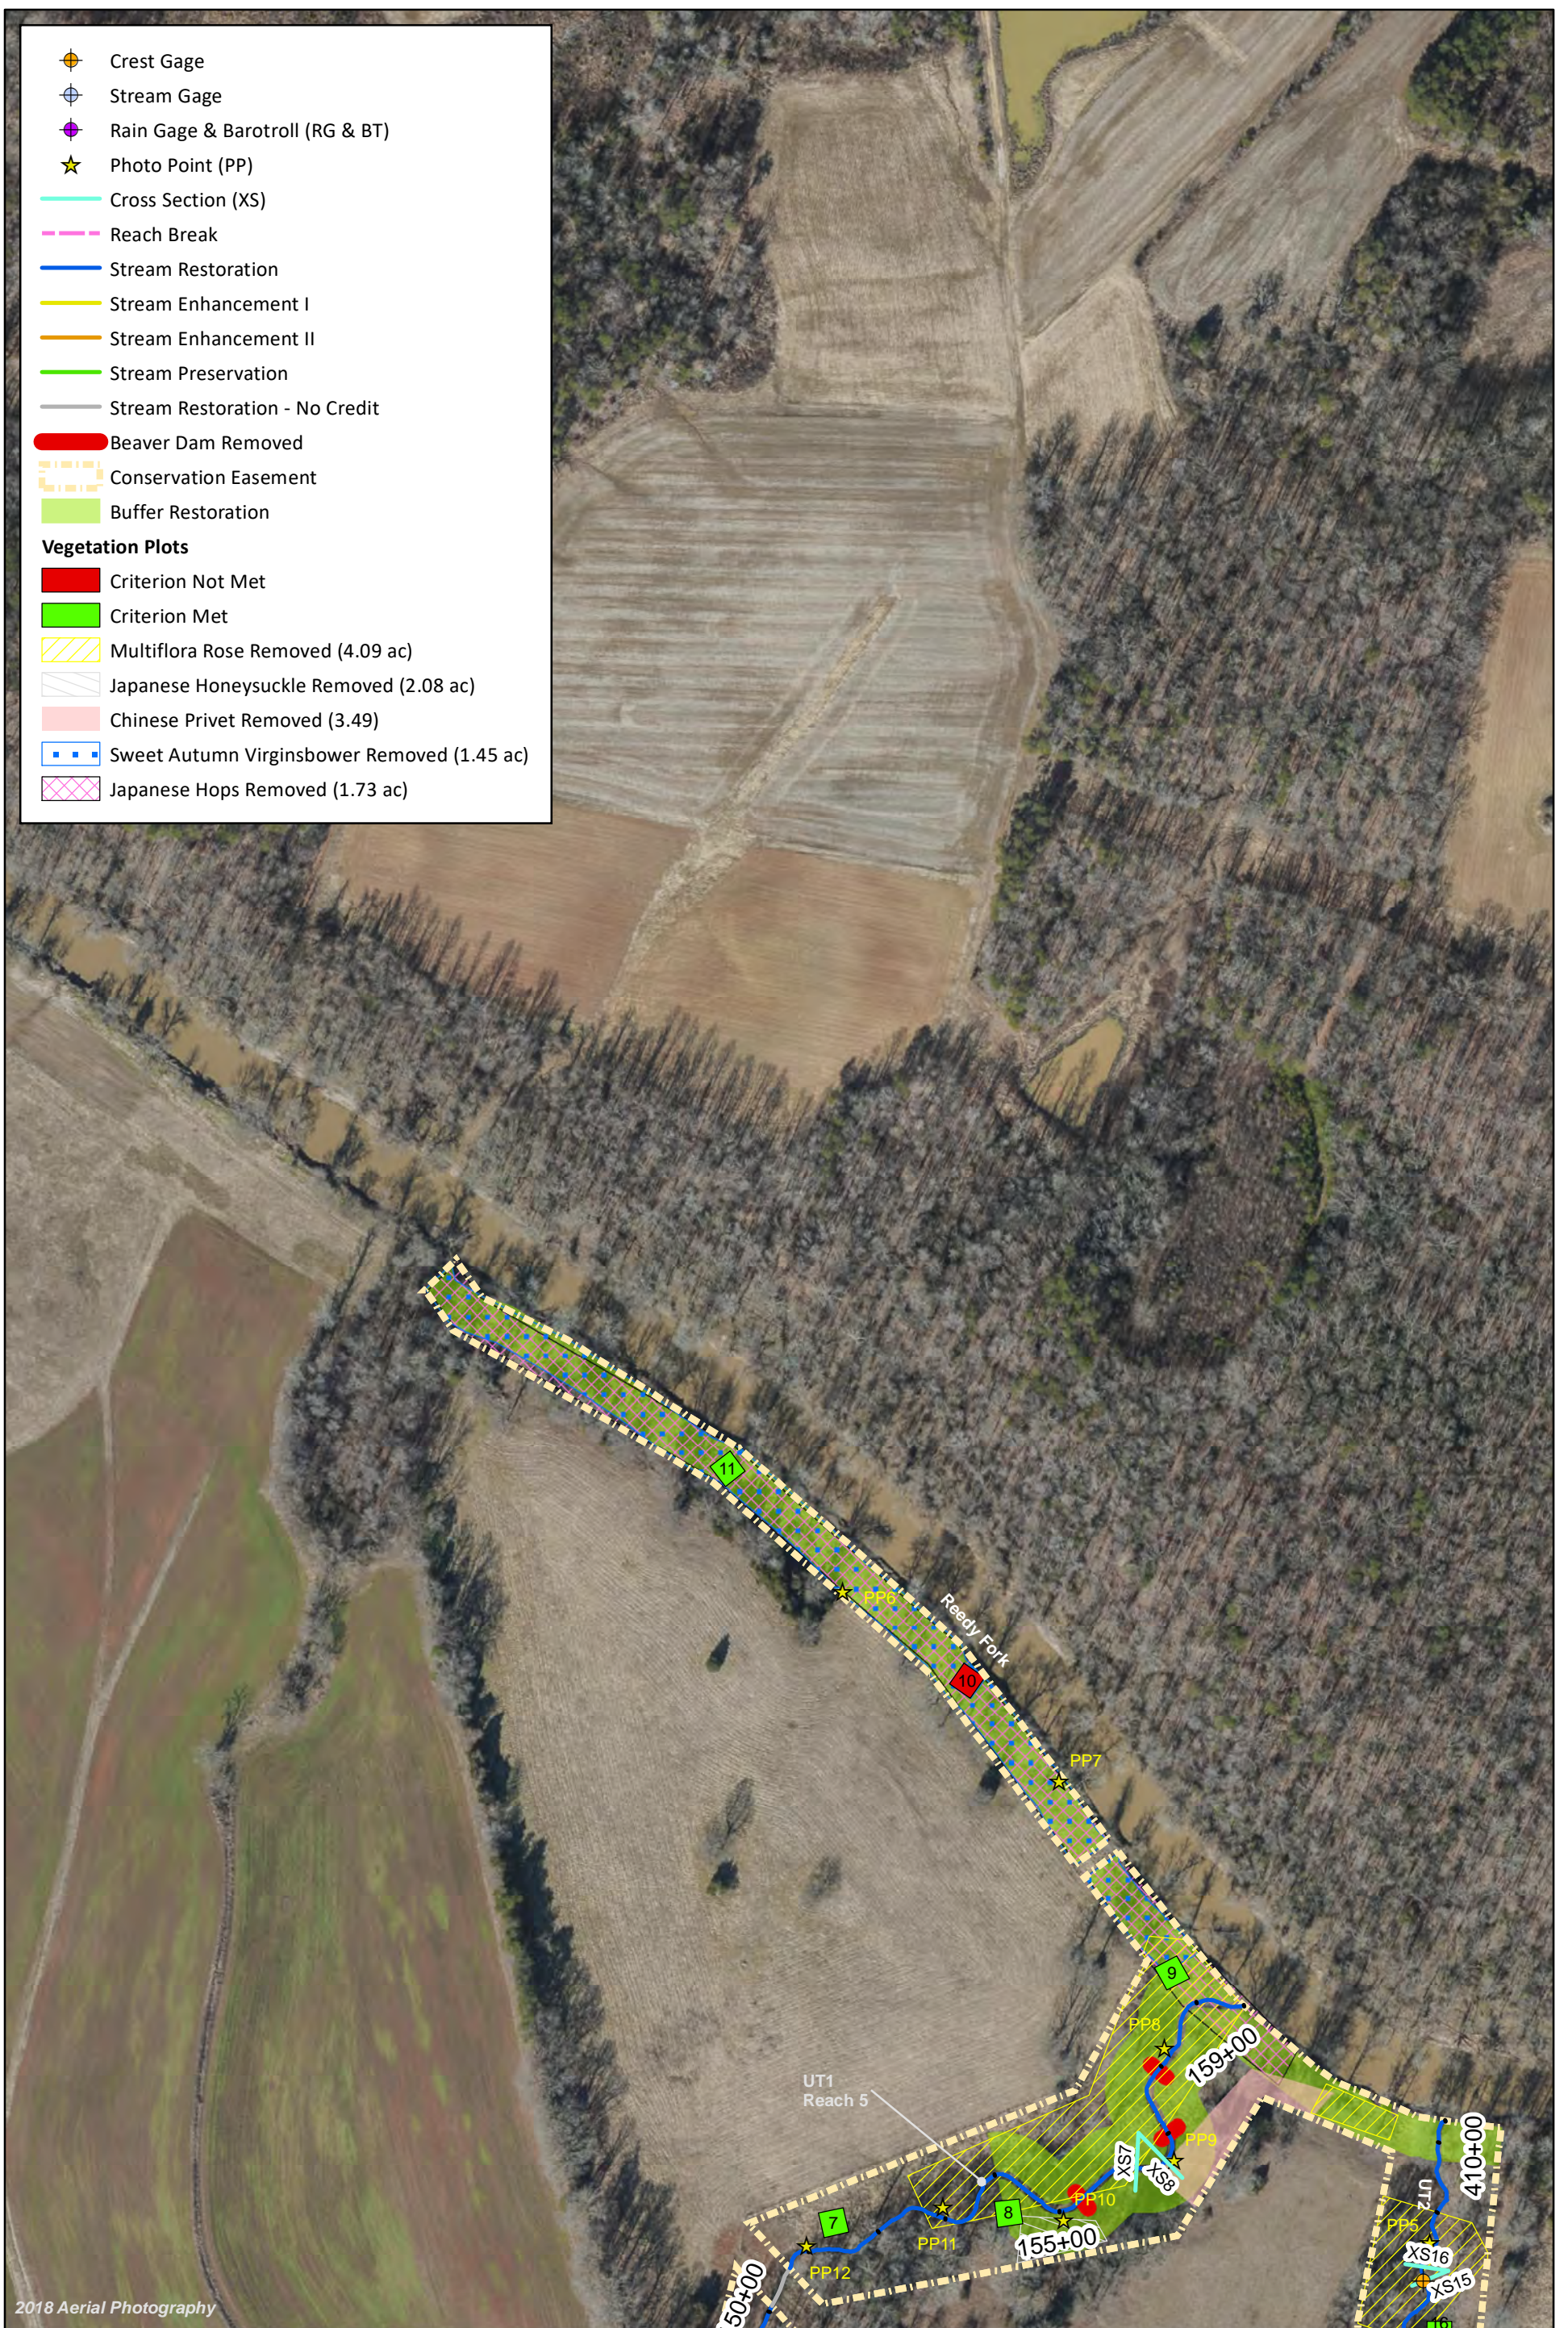



**Table 5a. Visual Stream Morphology Stability Assessment Table**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	42	42			100%			
	3. Meander Pool Condition	Depth Sufficient	39	39			100%			
		Length Appropriate	39	39			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	39	39			100%			
Thalweg centering at downstream of meander bend (Glide)		39	39	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
<b>TOTALS</b>					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	16	16			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	16	16			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	16	16			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	16	16			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	16	16			100%			

**Table 5b. Visual Stream Morphology Stability Assessment Table**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1A**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	26	26			100%			
	3. Meander Pool Condition	Depth Sufficient	26	26			100%			
		Length Appropriate	26	26			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	26	26			100%			
Thalweg centering at downstream of meander bend (Glide)		26	26	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
<b>TOTALS</b>					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	3	3			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	3	3			100%			

**Table 5c. Visual Stream Morphology Stability Assessment Table**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1B**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
<b>1. Bed</b>	<b>1. Vertical Stability (Riffle and Run units)</b>	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	<b>2. Riffle Condition</b>	Texture/Substrate	6	6			100%			
	<b>3. Meander Pool Condition</b>	Depth Sufficient	5	5			100%			
		Length Appropriate	5	5			100%			
	<b>4. Thalweg Position</b>	Thalweg centering at upstream of meander bend (Run)	5	5			100%			
Thalweg centering at downstream of meander bend (Glide)		5	5	100%						
<b>2. Bank</b>	<b>1. Scoured/Eroded</b>	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	<b>2. Undercut</b>	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	<b>3. Mass Wasting</b>	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
<b>TOTALS</b>					0	0	100%	n/a	n/a	n/a
<b>3. Engineered Structures</b>	<b>1. Overall Integrity</b>	Structures physically intact with no dislodged boulders or logs	1	1			100%			
	<b>2. Grade Control</b>	Grade control structures exhibiting maintenance of grade across the sill	1	1			100%			
	<b>2a. Piping</b>	Structures lacking any substantial flow underneath sills or arms	1	1			100%			
	<b>3. Bank Protection</b>	Bank erosion within the structures extent of influence does not exceed 15%	1	1			100%			
	<b>4. Habitat</b>	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	1	1			100%			

**Table 5d. Visual Stream Morphology Stability Assessment Table**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT2**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	20	20			100%			
	3. Meander Pool Condition	Depth Sufficient	21	21			100%			
		Length Appropriate	21	21			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	21	21			100%			
Thalweg centering at downstream of meander bend (Glide)		21	21	100%						
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, caving, or collapse			0	0	100%	n/a	n/a	n/a
<b>TOTALS</b>					0	0	100%	n/a	n/a	n/a
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs	5	5			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	5	5			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms	5	5			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%	5	5			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow	5	5			100%			

**Table 6. Vegetation Condition Assessment Table**  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

**Planted Acreage 18**

Vegetation Category	Definitions	Mapping Threshold (Ac)	Number of Polygons	Combined Acreage	% of Planted Acreage
<b>Bare Areas</b>	Very limited cover of both woody and herbaceous material	0.1	0	0	0.0%
<b>Low Stem Density Areas</b>	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1	0	0.0	0.0%
			<b>Total</b>	<b>0</b>	<b>0.0%</b>
<b>Areas of Poor Growth Rates or Vigor</b>	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 Ac	0	0	0%
			<b>Cumulative Total</b>	<b>0</b>	<b>0%</b>

**Easement Acreage 31**

Vegetation Category	Definitions	Mapping Threshold (SF)	Number of Polygons	Combined Acreage	% of Planted Acreage
<b>Invasive Areas of Concern</b>	Areas or points (if too small to render as polygons at map scale).	1,000	0	0	0.0%
<b>Easement Encroachment Areas</b>	Areas or points (if too small to render as polygons at map scale).	none	0	0	0%



**PHOTO POINT 1 UT2 – looking upstream (03/26/2019)**



**PHOTO POINT 1 UT2 – looking downstream (03/26/2019)**



**PHOTO POINT 2 UT2 – looking upstream (03/26/2019)**



**PHOTO POINT 2 UT2 – looking downstream (03/26/2019)**



**PHOTO POINT 3 UT2 – looking upstream (03/26/2019)**



**PHOTO POINT 3 UT2 – looking downstream (03/26/2019)**





**PHOTO POINT 4 UT2 – looking upstream (03/26/2019)**



**PHOTO POINT 4 UT2 – looking downstream (03/26/2019)**



**PHOTO POINT 5 UT2 – looking upstream (03/26/2019)**



**PHOTO POINT 5 UT2 – looking downstream (03/26/2019)**



**PHOTO POINT 6 Reedy Fork – looking upstream (03/26/2019)**



**PHOTO POINT 6 Reedy Fork – looking downstream (03/26/2019)**





**PHOTO POINT 7 Reedy Fork – looking upstream (03/26/2019)**



**PHOTO POINT 7 Reedy Fork – looking downstream (03/26/2019)**



**PHOTO POINT 8 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 8 UT1 R5 – looking downstream (03/26/2019)**



**PHOTO POINT 9 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 9 UT1 R5 – looking downstream (03/26/2019)**







**PHOTO POINT 10 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 10 UT1 R5 – looking downstream (03/26/2019)**



**PHOTO POINT 11 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 11 UT1 R5 – looking downstream (03/26/2019)**



**PHOTO POINT 12 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 12 UT1 R5 – looking downstream (03/26/2019)**





**PHOTO POINT 13 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 13 UT1 R5 – looking downstream (03/26/2019)**



**PHOTO POINT 14 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 14 UT1 R5 – looking downstream (03/26/2019)**



**PHOTO POINT 15 UT1 R5 – looking upstream (03/26/2019)**



**PHOTO POINT 15 UT1 R5 – looking downstream (03/26/2019)**





**PHOTO POINT 16 UT1 R4 – looking upstream (03/27/2019)**



**PHOTO POINT 16 UT1 R4 – looking downstream (03/27/2019)**



**PHOTO POINT 17 UT1 R4 – looking upstream (03/27/2019)**



**PHOTO POINT 17 UT1 R4 – looking downstream (03/27/2019)**



**PHOTO POINT 42 UT1 R4 – looking upstream (03/27/2019)**



**PHOTO POINT 42 UT1 R4 – looking downstream (03/27/2019)**





**PHOTO POINT 18 UT1 R3** – looking upstream (03/28/2019)



**PHOTO POINT 18 UT1 R3** – looking downstream (03/28/2019)



**PHOTO POINT 19 UT1 R3** – looking upstream (03/28/2019)



**PHOTO POINT 19 UT1 R3** – looking downstream (03/28/2019)



**PHOTO POINT 20 UT1 R3** – looking upstream (03/28/2019)



**PHOTO POINT 20 UT1 R3** – looking downstream (03/28/2019)





**PHOTO POINT 21 UT1B – looking upstream (03/27/2019)**



**PHOTO POINT 21 UT1B – looking downstream (03/27/2019)**



**PHOTO POINT 22 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 22 UT1 R2 – looking downstream (03/28/2019)**



**PHOTO POINT 23 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 23 UT1 R2 – looking downstream (03/28/2019)**





**PHOTO POINT 24 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 24 UT1 R2 – looking downstream (03/28/2019)**



**PHOTO POINT 25 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 25 UT1 R2 – looking downstream (03/28/2019)**



**PHOTO POINT 26 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 26 UT1 R2 – looking downstream (03/28/2019)**





**PHOTO POINT 27 UT1 R2 – looking upstream (03/28/2019)**



**PHOTO POINT 27 UT1 R2 – looking downstream (03/28/2019)**



**PHOTO POINT 28 UT1 R1 – looking upstream (03/28/2019)**



**PHOTO POINT 28 UT1 R1 – looking downstream (03/28/2019)**



**PHOTO POINT 29 UT1 R1 – looking upstream (03/28/2019)**



**PHOTO POINT 29 UT1 R1 – looking downstream (03/28/2019)**





**PHOTO POINT 30 UT1 R1 – looking upstream (03/28/2019)**



**PHOTO POINT 30 UT1 R1 – looking downstream (03/28/2019)**



**PHOTO POINT 31 UT1 R1 – looking upstream (03/28/2019)**



**PHOTO POINT 31 UT1 R1 – looking downstream (03/28/2019)**



**PHOTO POINT 32 UT1 R1 – looking upstream (03/28/2019)**



**PHOTO POINT 32 UT1 R1 – looking downstream (03/28/2019)**







**PHOTO POINT 33 UT1A R1** – looking upstream (03/27/2019)



**PHOTO POINT 33 UT1A R1** – looking downstream (03/27/2019)



**PHOTO POINT 34 UT1A R1** – looking upstream (03/27/2019)



**PHOTO POINT 34 UT1A R1** – looking downstream (03/27/2019)



**PHOTO POINT 35 UT1A R1** – looking upstream (03/27/2019)



**PHOTO POINT 35 UT1A R1** – looking downstream (03/27/2019)





**PHOTO POINT 36 UT1A R1 – looking upstream (03/27/2019)**



**PHOTO POINT 36 UT1A R1 – looking downstream (03/27/2019)**



**PHOTO POINT 37 UT1A R2 – looking upstream (03/27/2019)**



**PHOTO POINT 37 UT1A R2 – looking downstream (03/27/2019)**



**PHOTO POINT 38 UT1A R3 – looking upstream (03/27/2019)**



**PHOTO POINT 38 UT1A R3 – looking downstream (03/27/2019)**





**PHOTO POINT 39 UT1A R4** – looking upstream (03/27/2019)



**PHOTO POINT 39 UT1A R4** – looking downstream (03/27/2019)



**PHOTO POINT 40 UT1A R4** – looking upstream (03/27/2019)



**PHOTO POINT 40 UT1A R4** – looking downstream (03/27/2019)



**PHOTO POINT 41 UT1A R4** – looking upstream (03/27/2019)



**PHOTO POINT 41 UT1A R4** – looking downstream (03/27/2019)



**VEGETATION PHOTOGRAPHS**  
**Agony Acres**  
**Monitoring Year 5**



**VEG PLOT 1 (08/13/2019)**



**VEG PLOT 2 (08/13/2019)**



**VEG PLOT 3 (08/8/2019)**



**VEG PLOT 4 (08/8/2019)**





**VEG PLOT 5 (08/8/2019)**



**VEG PLOT 6 (08/8/2019)**



**VEG PLOT 7 (08/8/2019)**



**VEG PLOT 8 (08/8/2019)**



**VEG PLOT 9 (08/13/2019)**



**VEG PLOT 10 (08/13/2019)**





**VEG PLOT 11** (08/13/2019)




**VEG PLOT 12** (08/8/2019)




**VEG PLOT 13** (08/8/2019)



**VEG PLOT 14** (08/8/2019)

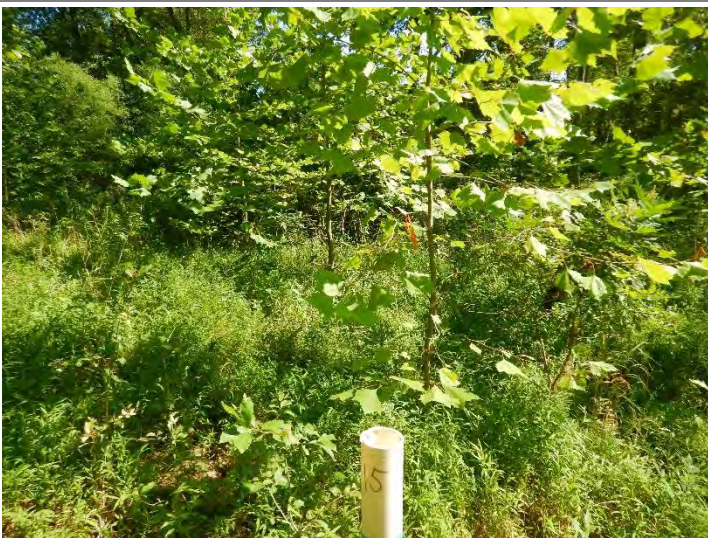

**VEG PLOT 15** (08/8/2019)

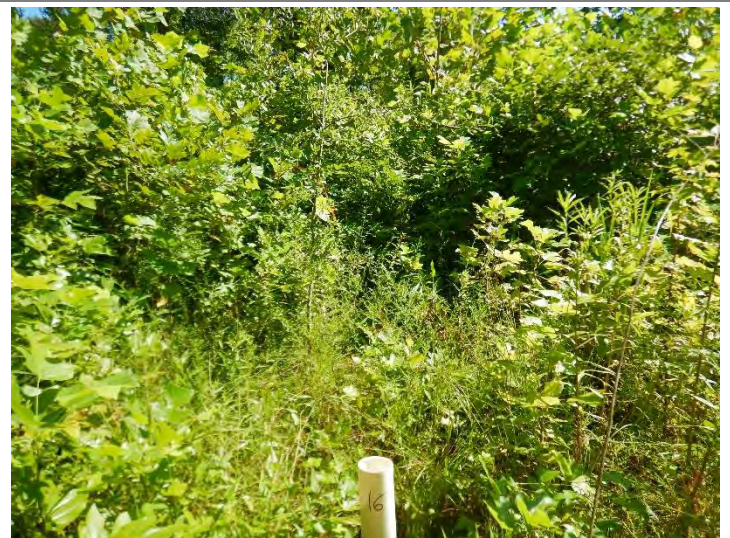

**VEG PLOT 16** (08/8/2019)



## APPENDIX 3. Vegetation Plot Data

**Table 7. Vegetation Plot Criteria Attainment**  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
**Monitoring Year 5 - 2019**

Plot	Success Criteria Met (Y/N)	Tract Mean
1	Y	94%
2	Y	
3	Y	
4	Y	
5	Y	
6	Y	
7	Y	
8	Y	
9	Y	
10	N	
11	Y	
12	Y	
13	Y	
14	Y	
15	Y	
16	Y	



**Table 8. CVS Vegetation Plot Metadata**

Agony Acres Mitigation Site (DMS Project No. 95716)

**Monitoring Year 5 - 2019**

<b>Database name</b>	Agony Acres- MY5- v2.3.1.mdb
<b>Database location</b>	F:\Projects\005-02136 Agony Acres\Monitoring\Monitoring Year 5\Vegetation Assessment
<b>Computer name</b>	JASON-PC
<b>File size</b>	68157440
<b>DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT</b>	
<b>Metadata</b>	Description of database file, the report worksheets, and a summary of project(s) and project data.
<b>Proj, planted</b>	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
<b>Proj, total stems</b>	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
<b>Plots</b>	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
<b>Vigor</b>	Frequency distribution of vigor classes for stems for all plots.
<b>Vigor by Spp</b>	Frequency distribution of vigor classes listed by species.
<b>Damage</b>	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
<b>Damage by Spp</b>	Damage values tallied by type for each species.
<b>Damage by Plot</b>	Damage values tallied by type for each plot.
<b>Planted Stems by Plot and Spp</b>	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
<b>ALL Stems by Plot and spp</b>	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
<b>PROJECT SUMMARY</b>	
<b>Project Code</b>	95716
<b>project Name</b>	Agony Acres Mitigation Site
<b>Description</b>	Stream & Buffer Site
<b>River Basin</b>	Cape Fear
<b>Sampled Plots</b>	16

**Table 9. Planted and Total Stem Counts**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

Scientific Name	Common Name	Species Type	Current Plot Data (MY5 2019)														
			VP 1			VP 2			VP 3			VP 4			VP 5		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree															
Acer rubrum	red maple	Tree															
Ailanthus altissima	tree of heaven	Exotic														6	
Alnus serrulata	hazel alder	Shrub							1	1	1						
Betula nigra	river birch	Tree				1	1	1	2	2	2	3	3	3			
Cornus amomum	silky dogwood	Shrub															
Diospyros virginiana	common persimmon	Tree															
Fraxinus pennsylvanica	green ash	Tree	5	5	5	4	4	4	3	3	3	2	2	4	2	2	2
Gleditsia triacanthos	honeylocust	Tree															
Ilex opaca	American holly	Tree															
Juglans nigra	black walnut	Tree															
Juniperus virginiana	eastern redcedar	Tree															
Liquidambar styraciflua	sweetgum	Tree			17			2						11			
Liriodendron tulipifera	tuliptree	Tree			11									6			
Nyssa sylvatica	blackgum	Tree															
Platanus occidentalis	American sycamore	Tree	3	3	3				4	4	4	4	4	13	2	2	2
Quercus michauxii	swamp chestnut oak	Tree				1	1	1	1	1	1	1	1	1	5	5	5
Quercus pagoda	cherrybark oak	Tree	2	2	2	3	3	3	1	1	1	2	2	2			
Quercus phellos	willow oak	Tree	2	2	2	1	1	1	2	2	2	1	1	1	1	1	1
Quercus rubra	northern red oak	Tree															
Quercus velutina	black oak	Tree															
Rhus	sumac	shrub															
Rhus copallinum	flameleaf sumac	shrub															
Ulmus	elm	Tree															
	<b>Stem count</b>		12	12	40	10	10	12	14	14	14	13	13	41	10	10	10
	<b>size (ares)</b>		1			1			1			1			1		
	<b>size (ACRES)</b>		0.02			0.02			0.02			0.02			0.02		
	<b>Species count</b>		4	4	6	5	5	6	7	7	7	6	6	8	4	4	5
	<b>Stems per ACRE</b>		486	486	1,619	405	405	486	567	567	567	526	526	1,659	405	405	405

**Color Coding for Table**

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

**Table 9. Planted and Total Stem Counts**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

Scientific Name	Common Name	Species Type	Current Plot Data (MY5 2019)														
			VP 6			VP 7			VP 8			VP 9			VP 10		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree						2			2			18			4
Acer rubrum	red maple	Tree															
Ailanthus altissima	tree of heaven	Exotic															
Alnus serrulata	hazel alder	Shrub	4	4	4												
Betula nigra	river birch	Tree	3	3	3	3	3	3	1	1	1						
Cornus amomum	silky dogwood	Shrub															
Diospyros virginiana	common persimmon	Tree															
Fraxinus pennsylvanica	green ash	Tree	2	2	2	3	3	3	5	5	5	5	5	21	2	2	3
Gleditsia triacanthos	honeylocust	Tree						1									
Ilex opaca	American holly	Tree															
Juglans nigra	black walnut	Tree															
Juniperus virginiana	eastern redcedar	Tree															
Liquidambar styraciflua	sweetgum	Tree			36			9			4		4				
Liriodendron tulipifera	tuliptree	Tree			58			2									
Nyssa sylvatica	blackgum	Tree															
Platanus occidentalis	American sycamore	Tree	2	2	45	3	3	5	6	6	6	6	6	14	1	1	1
Quercus michauxii	swamp chestnut oak	Tree	2	2	2	4	4	4	1	1	1	1	1	1	1	1	1
Quercus pagoda	cherrybark oak	Tree	1	1	1										1	1	1
Quercus phellos	willow oak	Tree										1	1	1			
Quercus rubra	northern red oak	Tree															
Quercus velutina	black oak	Tree			1												
Rhus	sumac	shrub															
Rhus copallinum	flameleaf sumac	shrub						7									
Ulmus	elm	Tree															
<b>Stem count</b>			14	14	152	13	13	36	13	13	19	13	13	59	5	5	10
<b>size (ares)</b>			1			1			1			1			1		
<b>size (ACRES)</b>			0.02			0.02			0.02			0.02			0.02		
<b>Species count</b>			6	6	9	4	4	9	4	4	6	4	4	6	4	4	5
<b>Stems per ACRE</b>			567	567	6,151	526	526	1,457	526	526	769	526	526	2,388	202	202	405

**Color Coding for Table**

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

**Table 9. Planted and Total Stem Counts**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

Scientific Name	Common Name	Species Type	Current Plot Data (MY5 2019)																	
			VP 11			VP 12			VP 13			VP 14			VP 15			VP 16		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree			9														6	
Acer rubrum	red maple	Tree																		
Ailanthus altissima	tree of heaven	Exotic																		
Alnus serrulata	hazel alder	Shrub	1	1	1							1	1	1				1	1	1
Betula nigra	river birch	Tree	1	1	1				3	3	3	2	2	2						
Cornus amomum	silky dogwood	Shrub																		
Diospyros virginiana	common persimmon	Tree						3												
Fraxinus pennsylvanica	green ash	Tree	7	7	7	3	3	3	2	2	2				3	3	4	2	2	4
Gleditsia triacanthos	honeylocust	Tree																		
Ilex opaca	American holly	Tree																		
Juglans nigra	black walnut	Tree																		
Juniperus virginiana	eastern redcedar	Tree																		
Liquidambar styraciflua	sweetgum	Tree											100							2
Liriodendron tulipifera	tuliptree	Tree											50			4				70
Nyssa sylvatica	blackgum	Tree			4											3				
Platanus occidentalis	American sycamore	Tree	2	2	2	4	4	4				3	3	15	4	4	4	3	3	87
Quercus michauxii	swamp chestnut oak	Tree				1	1	1	6	6	6	4	4	4	2	2	2	1	1	1
Quercus pagoda	cherrybark oak	Tree				1	1	1	2	2	2	2	2	2	1	1	1			
Quercus phellos	willow oak	Tree	1	1	1	1	1	1				1	1	1	1	1	1	4	4	4
Quercus rubra	northern red oak	Tree																		
Quercus velutina	black oak	Tree																		
Rhus	sumac	shrub																		
Rhus copallinum	flameleaf sumac	shrub															1			15
Ulmus	elm	Tree																		
<b>Stem count</b>			12	12	25	10	10	13	13	13	13	13	13	175	11	11	20	11	11	190
<b>size (ares)</b>			1			1			1			1			1			1		
<b>size (ACRES)</b>			0.02			0.02			0.02			0.02			0.02			0.02		
<b>Species count</b>			5	5	7	5	5	6	4	4	4	6	6	8	5	5	8	5	5	9
<b>Stems per ACRE</b>			486	486	1,012	405	405	526	526	526	526	526	526	7,082	445	445	809	445	445	7,689

**Color Coding for Table**

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

**Table 9. Planted and Total Stem Counts**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

Scientific Name	Common Name	Species Type	Annual Means														
			MY5 (2019)			MY3 (2017)			MY2 (2016)			MY1 (2015)			MY0 (2015)		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree			42			16						2			
Acer rubrum	red maple	Tree						4			30			10			
Ailanthus altissima	tree of heaven	Exotic			6												
Alnus serrulata	hazel alder	Shrub	8	8	8	10	10	11	15	15	15	26	26	26	27	27	27
Betula nigra	river birch	Tree	19	19	19	21	21	23	20	20	20	27	27	27	28	28	28
Cornus amomum	silky dogwood	Shrub									2						
Diospyros virginiana	common persimmon	Tree			3												
Fraxinus pennsylvanica	green ash	Tree	50	50	73	51	51	67	52	52	82	55	55	56	55	55	55
Gleditsia triacanthos	honeylocust	Tree			1			1									
Ilex opaca	American holly	Tree						1			3						
Juglans nigra	black walnut	Tree												1			
Juniperus virginiana	eastern redcedar	Tree						3									
Liquidambar styraciflua	sweetgum	Tree			185			129			30			10			
Liriodendron tulipifera	tuliptree	Tree			201			74			71			32			
Nyssa sylvatica	blackgum	Tree			7												
Platanus occidentalis	American sycamore	Tree	47	47	205	49	49	235	50	50	115	56	56	101	56	56	56
Quercus michauxii	swamp chestnut oak	Tree	31	31	31	34	34	34	35	35	35	36	36	36	36	36	36
Quercus pagoda	cherrybark oak	Tree	16	16	16	18	18	18	20	20	20	25	25	25	25	25	25
Quercus phellos	willow oak	Tree	16	16	16	16	16	16	18	18	18	30	30	30	30	30	30
Quercus rubra	northern red oak	Tree						6			40			10			
Quercus velutina	black oak	Tree			1												
Rhus	sumac	shrub						1									
Rhus copallinum	flameleaf sumac	shrub			23			2									
Ulmus	elm	Tree						9									
<b>Stem count</b>			187	187	837	199	199	650	210	210	481	255	255	366	257	257	257
<b>size (ares)</b>			16			16			16			16			16		
<b>size (ACRES)</b>			0.40			0.40			0.40			0.40			0.40		
<b>Species count</b>			7	7	16	7	7	18	7	7	13	7	7	13	7	7	7
<b>Stems per ACRE</b>			473	473	2,117	503	503	1,644	531	531	1,217	645	645	926	650	650	650

**Color Coding for Table**

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteer species included in total

PnoLS: Number of Planted stems excluding live stakes

P-all: Number of planted stems including live stakes,

T: Total Stems

## **APPENDIX 4. Morphological Summary Data and Plots**

Table 10a. Baseline Stream Data Summary  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

UT1

Parameter	Gage	PRE-RESTORATION CONDITION		REFERENCE REACH DATA										DESIGN				AS-BUILT/BASELINE				
		UT1 - Reach 2	UT1 - Reach 5	Onsite Reference Reach - UT1A - Reach 3		UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1 - Reach 2		UT1 - Reach 5		UT1 - Reach 2		UT1 - Reach 5		
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
<b>Dimension and Substrate - Riffle</b>																						
Bankfull Width (ft)	N/A	6.5	13.9	16.0	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	10.2	12.8	10.2	10.4	11.9	13.6			
Floodprone Width (ft)		10	20	>50	25	25	65	60	>114	14	125	31		22	51	28	64	60	100	200		
Bankfull Mean Depth		0.8	1.5	4.3	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.8	0.9			0.6	0.9	0.8	0.9	
Bankfull Max Depth		1.4	1.9	5.2	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	1.0	1.2	1.2	1.5	1.1	1.4	1.3	1.6	
Bankfull Cross Sectional Area (ft <sup>2</sup> )		5.2	24.6	59.0	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	7.9	12.0			6.2	9.0	9.1	11.9	
Width/Depth Ratio		8.2	3.3	10.4	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	13.1				12.0	16.8	15.5	15.7	
Entrenchment Ratio <sup>1</sup>		1.5	1.2	>3.6	2	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5		2.2	5.0	2.2	5.0	5.9	9.6	14.7	16.8	
Bank Height Ratio <sup>2</sup>		2.3	1.0	2.0	1.0	1.0	1.1	1.0	1.0	1.0	1.0	--	--	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	
D50 (mm)		3.47		14.60	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	Silt/ Clay	0.11	
<b>Profile</b>																						
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	13.9	73.2	23.7	81.3	
Riffle Slope (ft/ft)		---	---	---	N/A	0.0040	0.0470	0.0130	0.0184	0.0343	0.0188	0.0704	0.0148	0.0453	0.0118	0.0363	0.0078	0.0317	0.0090	0.0304		
Pool Length (ft)		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	17.2	42.8	17.6	76.6	
Pool Max Depth (ft)		2.4	2.5	---	1.6	1.8	---	3.3	1.2	1.8	---	2.6	---	0.9	3.2	1.1	3.9	1.6	3.7	2.0	4.9	
Pool Spacing (ft)		---	---	---	N/A	34	52	71	9	46	27	73	13	67	17	84	31	78	35	103		
Pool Volume (ft <sup>3</sup> )		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
<b>Pattern</b>																						
Channel Beltwidth (ft)	N/A	12	20	48	157	N/A	28	50	38	41	10	50	102	16	74	20	93	20	68	34	72	
Radius of Curvature (ft)		6	18	13	86	N/A	19	50	11	15	12	85	23	38	18	31	23	38	18	26	23	38
Rc:Bankfull Width (ft/ft)		0.8	2.3	1.6	10.9	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0	1.8	2.5	1.9	2.8
Meander Length (ft)		27	45	176	260	N/A	---	---	---	---	53	178	---	---	31	151	38	192	70	120	97	160
Meander Width Ratio		1.5	2.5	6.1	19.9	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	1.6	7.3	2.0	6.5	2.9	5.3
<b>Substrate, Bed and Transport Parameters</b>																						
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
SC%/Sa%/G%/C%/B%/Be%		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
d16/d35/d50/d84/d95/d100		0.33/1.88/3.47/45.0/117/256	0.18/3.2/14.6/128/234/2048	---	---	---	---	---	---	---	---	---	---	---	---	---	---	SC/ SC/SC/ 41.3/79.2/128.0	SC/SC/0.11/ 45.0/104.7/180.0	---	---	
Reach Shear Stress (Competency) lb/ft <sup>2</sup>		0.43	1.26	---	---	---	---	---	---	---	---	---	---	0.49	0.63	---	---	0.38	0.56	---	---	
Max part size (mm) mobilized at bankfull		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Stream Power (Capacity) W/m <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
<b>Additional Reach Parameters</b>																						
Drainage Area (SM)	N/A	0.25	0.56	---	0.15	0.41	---	0.96	0.37	---	0.29	---	---	0.25	0.56	---	---	0.25	0.56	---	---	
Watershed Impervious Cover Estimate (%)		<1%	<1%	---	---	---	---	---	---	---	---	---	---	<1%	<1%	---	---	<1%	<1%	---	---	
Rosgen Classification		G4	E4, G4	---	B3	E4	---	E4	E4	---	C4/E4	---	---	C4	C4	---	---	C4	C4	---	---	
Bankfull Velocity (fps)		2.7	1.7	5.7	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8	---	2.5-5	2.5-5	---	---	2.6	3.4	3.3	3.6	
Bankfull Discharge (cfs)		14	129	---	37	20	---	97	35	---	40	---	---	25.0	46.0	---	---	17.0	30.9	30.3	42.9	
Q-NFF regression		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-USGS extrapolation		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-Mannings		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Valley Length (ft)		---	---	---	---	---	---	---	---	---	---	---	---	907	1,232	---	---	---	---	---	---	
Channel Thalweg Length (ft)		1,132	1,417	---	---	---	---	---	---	---	---	---	---	1,114	1,488	---	---	1,137	1,535	---	---	
Sinuosity		1.14	1.24	---	1.04	1.40	---	2.32	1.00	1.30	---	1.40	---	1.20	1.30	1.20	1.30	1.20	1.20	---	---	
Water Surface Slope (ft/ft) <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	0.0111	0.0122	
Bankfull Slope (ft/ft)		0.0093	0.0190	0.0005	0.0130	0.0490	0.0120	0.0047	0.0190	0.0220	0.0150	---	---	0.0070	0.0150	0.0054	0.0172	0.0096	0.0104	---	---	

(---): Data was not provided

N/A: Not Applicable

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 10b. Baseline Stream Data Summary  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

UT1A

Parameter	Gage	PRE-RESTORATION CONDITION				REFERENCE REACH DATA								DESIGN				AS-BUILT/BASELINE					
		UT1A - Reach 1		UT1A - Reach 4		Onsite Reference Reach - UT1A - Reach 3		UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1A - Reach 1		UT1A - Reach 4		UT1A - Reach 1		UT1A - Reach 4	
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>																							
Bankfull Width (ft)	N/A	5.8	9.3	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	8.0	8.2	8.0	8.1							
Floodprone Width (ft)	N/A	15	>80	25	25	65	60	>114	14	125	31	18	40	18	41	50	200						
Bankfull Mean Depth	N/A	1.1	1.0	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.6	0.6	0.5	0.6							
Bankfull Max Depth	N/A	1.4	1.5	1.0	1.4	1.7	2.1	2.6	1	1.2	1.2	1.6	0.7	0.9	0.8	1.0	0.9	1.8					
Bankfull Cross Sectional Area (ft <sup>2</sup> )	N/A	6.3	9.3	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	4.8	5.0	4.0	5.0							
Width/Depth Ratio	N/A	5.3	9.0	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	13.4	13.6	15.9	13.2							
Entrenchment Ratio <sup>1</sup>	N/A	2.6	>8.6	2	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5	2.2	5.0	2.2	5.0	6.3	24.8						
Bank Height Ratio <sup>2</sup>	N/A	1.7	1.5	1.0	1.0	1.1	1.0	1.0	1.0	1.0	--	--	1.0	1.0	1.0	1.0	1.0	1.0					
D50 (mm)	N/A	4.31	5.06	---	---	---	---	---	---	---	---	---	---	---	---	---	1.41	0.25					
<b>Profile</b>																							
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	15.5	42.0	20.5	51.9			
Riffle Slope (ft/ft)	N/A	---	---	N/A	0.0040	0.0470	0.0130	0.0184	0.0343	0.0188	0.0704	0.0148	0.0453	0.0212	0.0652	0.0077	0.0505	0.0109	0.0449				
Pool Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	5.4	52.2	9.1	35.5			
Pool Max Depth (ft)	N/A	1.8	3.6	1.6	1.8	3.3	1.2	1.8	2.6	0.7	2.4	0.7	2.5	1.6	3.5	1.4	3.1						
Pool Spacing (ft)	N/A	---	---	N/A	34	52	71	9	46	27	73	10	53	11	54	20	85	45	82				
Pool Volume (ft <sup>3</sup> )	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---					
<b>Pattern</b>																							
Channel Beltwidth (ft)	N/A	30	35	N/A	N/A	N/A	28	50	38	41	10	50	102	13	58	13	60	24	60	35	55		
Radius of Curvature (ft)	N/A	12	57	N/A	N/A	N/A	19	50	11	15	12	85	23	38	14	24	15	25	14	23	15	23	
Rc:Bankfull Width (ft/ft)	N/A	1.5	7.2	N/A	N/A	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0	1.8	2.9	1.9	2.8	
Meander Length (ft)	N/A	89	104	N/A	N/A	N/A	---	---	---	---	53	178	---	---	24	120	25	123	70	112	96	117	
Meander Width Ratio	N/A	3.8	4.4	N/A	N/A	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	1.6	7.3	3.0	7.5	4.3	6.8	
<b>Substrate, Bed and Transport Parameters</b>																							
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
SC%/Sa%/G%/C%/B%/Be%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
d16/d35/d50/d84/d95/d100	N/A	0.15/2.18/4.31/16/139/256	0.45/2.71/5.06/67.7/122/362	---	---	---	---	---	---	---	---	---	---	---	---	---	SC/SC/1.41/33.4/64.0/128.0	SC/SC/0.25/26.2/75.9/180.0					
Reach Shear Stress (Competency) lb/ft <sup>2</sup>	N/A	0.50	1.76	---	---	---	---	---	---	---	---	---	---	0.48	0.54	0.38	0.49						
Max part size (mm) mobilized at bankfull	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---					
Stream Power (Capacity) W/m <sup>2</sup>	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---					
<b>Additional Reach Parameters</b>																							
Drainage Area (SM)	N/A	0.12	0.16	0.15	0.41	0.96	0.37	0.29	0.12	0.16	0.12	0.16											
Watershed Impervious Cover Estimate (%)	N/A	<1%	<1%	---	---	---	---	---	<1%	<1%	<1%	<1%											
Rosgen Classification	N/A	E4	E4	83	E4	E4	E4	C4/E4	C4	C4	C4	C4											
Bankfull Velocity (fps)	N/A	3.3	5.2	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8	2.5-5	2.5-5	2.6	3.0								
Bankfull Discharge (cfs)	N/A	21	50	37	20	97	35	40	14.0	17.0	15.9	15.0											
Q-NFF regression	N/A	---	---	---	---	---	---	---	---	---	---	---											
Q-USGS extrapolation	N/A	---	---	---	---	---	---	---	---	---	---	---											
Q-Mannings	N/A	---	---	---	---	---	---	---	---	---	---	---											
Valley Length (ft)	N/A	---	---	---	---	---	---	---	673	530	---	---											
Channel Thalweg Length (ft)	N/A	770	461	---	---	---	---	---	849	650	857	666											
Sinuosity	N/A	1.12	1.03	1.04	1.40	2.32	1.00	1.30	1.40	1.20	1.30	1.20	1.30	1.21	1.25								
Water Surface Slope (ft/ft) <sup>2</sup>	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	0.0126	N/A						
Bankfull Slope (ft/ft)	N/A	0.0095	0.0150	0.0490	0.0120	0.0047	0.0190	0.0220	0.0150	0.0103	0.0175	0.0141	0.0153	0.0137	0.0129								

(---): Data was not provided

N/A: Not Applicable

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.



Table 10c. Baseline Stream Data Summary  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

UT1B

Parameter	Gage	PRE-RESTORATION		REFERENCE REACH DATA								DESIGN		AS-BUILT/ BASELINE		
		UT1B	Onsite Reference Reach - UT1A - Reach 3	UT to Polecat Creek		Spencer Creek 1		Spencer Creek 2		UT To Cane Creek		UT1B	UT1B			
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
<b>Dimension and Substrate - Riffle</b>																
Bankfull Width (ft)	N/A	4.9	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	7.3		7.7		
Floodprone Width (ft)		36	25	25	65	60	>114	14	125	31		16	37	70		
Bankfull Mean Depth		1.1	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.6		0.5		
Bankfull Max Depth		1.9	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	0.7	0.9	0.7		
Bankfull Cross Sectional Area (ft <sup>2</sup> )		5.4	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	5.2		3.5		
Width/Depth Ratio		4.4	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	12.6		17.0		
Entrenchment Ratio <sup>1</sup>		7.5	2.3	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5		2.2	5.0	9.1		
Bank Height Ratio <sup>2</sup>		1.6	1.0	1.0	1.1	1.0		1.0	1.0	--	--	1.0	1.0	1.0		
D50 (mm)		---	---	---	---	---	---	---	---	---	---	---	---	---	Silt/Clay	
<b>Profile</b>																
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	12.1	24.4	
Riffle Slope (ft/ft)		---	N/A	0.0040	0.0470	0.0130		0.0184	0.0343	0.0188	0.0704	0.0222	0.0680	0.0219	0.0425	
Pool Length (ft)		---	---	---	---	---	---	---	---	---	---	---	---	11.9	30.9	
Pool Max Depth (ft)		2.5	1.6	1.8		3.3	1.2	1.8	2.6		0.7	2.4	1.7	2.5	---	
Pool Spacing (ft)		---	N/A	34	52	71		9	46	27	73	9	48	30	45	
Pool Volume (ft <sup>3</sup> )		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
<b>Pattern</b>																
Channel Beltwidth (ft)	N/A	N/A	N/A	N/A	28	50	38	41	10	50	102		12	53	25	40
Radius of Curvature (ft)		N/A	N/A	N/A	19	50	11	15	12	85	23	38	13	22	14	20
Rc:Bankfull Width (ft/ft)		N/A	N/A	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	2.6
Meander Length (ft)		N/A	N/A	N/A	--	--	--	--	53	178	--	--	22	110	60	72
Meander Width Ratio		N/A	N/A	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	3.2	5.2
<b>Substrate, Bed and Transport Parameters</b>																
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
SC%/Sa%/G%/C%/B%/Be%		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
d16/d35/d50/d84/d95/d100		---	---	---	---	---	---	---	---	---	---	---	---	---	SC/SC/SC/ 19.5/40.2/90.0	
Reach Shear Stress (Competency) lb/ft <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	---	---	0.21	
Max part size (mm) mobilized at bankfull		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Stream Power (Capacity) W/m <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
<b>Additional Reach Parameters</b>																
Drainage Area (SM)	N/A	0.10	0.15	0.41		0.96		0.37		0.29		0.10		0.10		
Watershed Impervious Cover Estimate (%)		<1%	---	---	---	---	---	---	---	---	---	---	<1%	<1%		
Rosgen Classification		E4	83	E4		E4		E4		C4/E4		C4		C4		
Bankfull Velocity (fps)		4.6	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8		1.5-4		1.9		
Bankfull Discharge (cfs)		25	37	20		97		35		40		11		6.6		
Q-NFF regression		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-USGS extrapolation		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-Mannings		---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Valley Length (ft)		---	---	---	---	---	---	---	---	---	---	---	199	---		
Channel Thalweg Length (ft)		243	---	---	---	---	---	---	---	---	---	---	219	232		
Sinuosity		1.06	1.04	1.40		2.32		1.00	1.30	1.40		1.20	1.30	1.34		
Water Surface Slope (ft/ft) <sup>3</sup>		---	---	---	---	---	---	---	---	---	---	---	---	---	0.0095	
Bankfull Slope (ft/ft)		0.0200	0.0490	0.0120		0.0047		0.0190	0.0220	0.0150		0.0100	0.0200	0.0181		

(---): Data was not provided

N/A: Not Applicable

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 10d. Baseline Stream Data Summary  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

UT2

Parameter	Gage	PRE-RESTORATION		REFERENCE REACH DATA								DESIGN		AS-BUILT/ BASELINE		
		UT2	Onsite Reference Reach - UT1A - Reach 3	UT to Polecat Creek	Spencer Creek 1	Spencer Creek 2	UT To Cane Creek	UT2	UT2							
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
<b>Dimension and Substrate - Riffle</b>																
Bankfull Width (ft)	N/A	6.2	9.6	11.1	5.3	10.9	10.7	11.2	6.3	9.3	11.5	12.3	6.6	6.7		
Floodprone Width (ft)		>20	25	25	65	60	>114	14	125	31	15	33	50			
Bankfull Mean Depth		0.6	1.1	0.7	1.0	1.1	1.6	1.8	0.8	1.0	0.8	1.0	0.5			
Bankfull Max Depth		1.0	2.0	1.0	1.4	1.7	2.1	2.6	1.0	1.2	1.2	1.6	0.6	0.8	0.7	
Bankfull Cross Sectional Area (ft <sup>2</sup> )		5.2	7.0	7.4	5.4	12.4	17.8	19.7	6.6	8.7	8.9	12.2	3.4	3.4		
Width/Depth Ratio		5.5	15.5	16.6	5.2	9.6	5.8	7.1	7.9	9.3	12.3	14.4	12.8	12.9		
Entrenchment Ratio <sup>1</sup>		>2.4	2.3	3.2	8.3	5.5	>10.2	1.7	4.3	>2.5	2.2	5.0	7.5			
Bank Height Ratio <sup>2</sup>		1.0	2.1	1.0	1.0	1.1	1.0	1.0	1.0	--	--	1.0	1.0	1.0		
D50 (mm)		2.11	---	---	---	---	---	---	---	---	---	---	---	Silt/Clay		
<b>Profile</b>																
Riffle Length (ft)	N/A	---	---	---	---	---	---	---	---	---	---	---	---	13.9	51.7	
Riffle Slope (ft/ft)		---	N/A	0.0040	0.0470	0.0130	0.0184	0.0343	0.0188	0.0704	0.0179	0.0549	0.0146	0.0525		
Pool Length (ft)		---	---	---	---	---	---	---	---	---	---	---	---	10.0	28.4	
Pool Max Depth (ft)		1.4	1.6	1.8	3.3	1.2	1.8	2.6	0.6	2.1	1.0	2.4				
Pool Spacing (ft)		---	N/A	34	52	71	9	46	27	73	9	44	25	66		
Pool Volume (ft <sup>3</sup> )		---	---	---	---	---	---	---	---	---	---	---	---			
<b>Pattern</b>																
Channel Beltwidth (ft)	N/A	32	54	N/A	28	50	38	41	10	50	102	11	48	19	50	
Radius of Curvature (ft)		12	43	N/A	19	50	11	15	12	85	23	38	12	20	12	20
Rc:Bankfull Width (ft/ft)		1.5	5.4	N/A	2.0	5.3	1.3	1.4	1.9	9.1	2.0	3.1	1.8	3.0	1.8	3.0
Meander Length (ft)		102	103	N/A	--	--	--	--	53	178	--	--	20	99	58	98
Meander Width Ratio		4.1	6.8	N/A	3.0	5.3	3.4	3.6	1.6	5.4	8.3	8.9	1.6	7.3	2.8	7.5
<b>Substrate, Bed and Transport Parameters</b>																
Ri%/Ru%/P%/G%/S%	N/A	---	---	---	---	---	---	---	---	---	---	---	---	---		
SC%/Sa%/G%/C%/B%/Be%		---	---	---	---	---	---	---	---	---	---	---	---			
d16/d35/d50/d84/d95/d100		0.2/0.68/2.11/20.7/98.3/256	---	---	---	---	---	---	---	---	---	---	SC/SC/SC/30.2/64.0/128.0			
Reach Shear Stress (Competency) lb/ft <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	0.64			
Max part size (mm) mobilized at bankfull		---	---	---	---	---	---	---	---	---	---	---	---			
Stream Power (Capacity) W/m <sup>2</sup>		---	---	---	---	---	---	---	---	---	---	---	---			
<b>Additional Reach Parameters</b>																
Drainage Area (SM)	N/A	0.09	0.15	0.41	0.96	0.37	0.29	0.09	0.09							
Watershed Impervious Cover Estimate (%)		<1%	---	---	---	---	---	---	<1%	<1%						
Rosgen Classification		E4	B3	E4	E4	E4	C4/E4	C4	C4							
Bankfull Velocity (fps)		3.0	5.1	4.9	2.2	3.5	4.9	5.4	5.0	5.6	3.8	2.5-5	3.4			
Bankfull Discharge (cfs)		23	37	20	97	35	40	11.0	11.5							
Q-NFF regression		---	---	---	---	---	---	---	---							
Q-USGS extrapolation		---	---	---	---	---	---	---	---							
Q-Mannings		---	---	---	---	---	---	---	---							
Valley Length (ft)		---	---	---	---	---	---	---	905	---						
Channel Thalweg Length (ft)		1,028	---	---	---	---	---	---	1,023	1,032						
Sinuosity		1.06	1.04	1.40	2.32	1.00	1.30	1.40	1.20	1.30	1.16					
Water Surface Slope (ft/ft) <sup>3</sup>		---	---	---	---	---	---	---	---	---	0.0207					
Bankfull Slope (ft/ft)		0.0130	0.0220	0.0490	0.0120	0.0047	0.0190	0.0220	0.0150	0.0121	0.0231	0.0195				

(---): Data was not provided

N/A: Not Applicable

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

Table 11. Morphology and Hydraulic Summary (Dimensional Parameters - Cross Section)  
 Agony Acres Mitigation Site (DMS Project No. 95716)  
 Monitoring Year 5 - 2019

UT1 Reach 2																								
		Cross Section 1 (Riffle)					Cross Section 2 (Pool)					Cross Section 3 (Riffle)					Cross Section 4 (Pool)							
Dimension and Substrate	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7
Bankfull Elevation (ft)	651.7	651.7	651.7	651.7	651.8		651.0	651.0	651.0	651.0	651.2		644.0	644.0	644.0	644.0	644.0		643.6	643.6	643.6	643.6	643.6	
Low Bank Elevation (ft)	651.7	651.7	651.7	651.7	651.8		651.0	651.0	651.0	651.0	651.2		644.0	644.0	644.0	644.0	644.0		643.6	643.6	643.6	643.6	643.6	
Bankfull Width (ft)	10.4	9.9	10.5	10.9	12.0		9.6	9.3	9.3	8.9	10.0		10.6	10.2	9.7	9.2	9.7		13.5	13.7	12.9	13.3	12.8	
Floodprone Width (ft)	100	100	100	100	100		N/A	N/A	N/A	N/A	N/A		60	60	60	60	60		N/A	N/A	N/A	N/A	N/A	
Bankfull Mean Depth (ft)	0.9	0.8	0.7	0.7	0.7		1.2	1.1	1.2	1.2	1.2		0.6	0.6	0.5	0.5	0.6		1.1	1.0	1.0	1.0	1.0	
Bankfull Max Depth (ft)	1.4	1.4	1.4	1.4	1.5		2.1	1.9	2.0	1.9	2.2		1.1	1.1	1.1	1.0	1.1		1.9	1.8	1.9	1.9	2.0	
Bankfull Cross Sectional Area (ft <sup>2</sup> )	9.0	8.0	7.8	7.9	8.7		11.6	10.4	11.2	10.3	11.9		6.2	6.2	5.3	4.9	6.2		14.7	14.2	13.3	13.6	12.4	
Bankfull Width/Depth Ratio	12.0	12.2	14.2	15.1	16.5		7.9	8.3	7.7	7.6	8.3		18.2	16.7	17.7	17.5	15.1		12.4	13.2	12.5	13.1	13.2	
Entrenchment Ratio <sup>1</sup>	9.6	10.1	9.5	9.2	8.4		N/A	N/A	N/A	N/A	N/A		5.6	5.9	6.2	6.5	6.2		N/A	N/A	N/A	N/A	N/A	
Bankfull Bank Height Ratio <sup>2</sup>	1.0	1.0	1.0	1.0	<1.0		1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.0	
d50 (mm)	18.0	64.0	10.4	27.2	56.1		N/A	N/A	N/A	N/A	N/A		13.3	46.6	22.6	23.0	22.6		N/A	N/A	N/A	N/A	N/A	
UT1 Reach 5																								
		Cross Section 5 (Pool)					Cross Section 6 (Riffle)					Cross Section 7 (Riffle)					Cross Section 8 (Pool)							
Dimension and Substrate	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7
Bankfull Elevation (ft)	610.4	610.4	610.4	610.4	610.3		610.0	610.0	610.0	610.0	610.0		600.9	600.9	600.9	600.9	600.8		600.6	600.6	600.6	600.6	600.5	
Low Bank Elevation (ft)	610.4	610.4	610.4	610.4	610.3		610.0	610.0	610.0	610.0	610.0		600.9	600.9	600.9	600.9	600.8		600.6	600.6	600.6	600.6	600.5	
Bankfull Width (ft)	15.9	16.5	16.7	17.1	14.4		15.3	15.2	16.0	15.1	15.3		11.9	11.9	11.8	12.0	10.9		15.2	15.7	16.1	16.1	14.3	
Floodprone Width (ft)	N/A	N/A	N/A	N/A	N/A		200	200	200	200	200		200	200	200	200	200		N/A	N/A	N/A	N/A	N/A	
Bankfull Mean Depth (ft)	1.2	1.1	1.2	1.1	1.2		0.8	0.8	0.8	0.8	1.0		0.8	0.8	0.8	0.7	0.8		1.4	1.4	1.3	1.3	1.4	
Bankfull Max Depth (ft)	2.4	2.2	2.4	2.4	2.3		1.6	1.7	1.8	1.8	2.0		1.3	1.5	1.4	1.3	1.5		2.7	2.8	2.8	2.7	3.2	
Bankfull Cross Sectional Area (ft <sup>2</sup> )	18.5	18.1	19.3	19.4	17.0		12.0	12.6	12.5	12.5	14.7		9.1	10.1	9.3	8.8	8.4		21.3	21.8	21.1	20.4	19.4	
Bankfull Width/Depth Ratio	13.6	15.1	14.4	15.1	12.2		19.5	18.4	20.5	18.2	15.9		15.7	14.0	14.9	16.3	14.1		10.9	11.3	12.3	12.7	10.5	
Entrenchment Ratio <sup>1</sup>	N/A	N/A	N/A	N/A	N/A		13.1	13.1	12.5	13.3	13.1		16.8	16.8	17.0	16.7	18.4		N/A	N/A	N/A	N/A	N/A	
Bankfull Bank Height Ratio <sup>2</sup>	1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.1		1.0	1.0	1.0	1.0	<1.0		1.0	1.0	1.0	1.0	1.0	
d50 (mm)	N/A	N/A	N/A	N/A	N/A		15.4	30.8	57.9	29.6	33.5		16.0	52.1	70.5	40.2	31.0		N/A	N/A	N/A	N/A	N/A	
UT1A Reach 1											UT1A Reach 4													
		Cross Section 9 (Riffle)					Cross Section 10 (Pool)					Cross Section 11 (Riffle)					Cross Section 12 (Pool)							
Dimension and Substrate	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7
Bankfull Elevation (ft)	656.4	656.4	656.4	656.4	656.5		656.0	656.0	656.0	656.0	656.2		615.8	615.8	615.8	615.8	615.7		615.1	615.1	615.1	615.1	615.1	
Low Bank Elevation (ft)	656.4	656.4	656.4	656.4	656.5		656.0	656.0	656.0	656.0	656.2		615.8	615.8	615.8	615.8	615.7		615.1	615.1	615.1	615.1	615.1	
Bankfull Width (ft)	8.0	7.3	7.2	6.7	6.6		10.5	10.0	10.2	9.4	10.7		8.1	8.2	8.2	8.9	8.5		10.6	10.5	10.5	10.8	12.0	
Floodprone Width (ft)	50	50	50	50	50		N/A	N/A	N/A	N/A	N/A		200	200	200	200	200		N/A	N/A	N/A	N/A	N/A	
Bankfull Mean Depth (ft)	0.5	0.5	0.5	0.5	0.6		0.7	0.7	0.7	0.7	0.7		0.6	0.8	0.8	0.8	0.8		1.2	1.2	1.2	1.1	1.1	
Bankfull Max Depth (ft)	0.9	0.9	0.8	0.8	1.2		1.5	1.2	1.3	1.3	1.7		1.8	1.9	1.9	1.8	1.7		2.7	2.6	2.6	2.5	2.8	
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.0	3.9	3.8	3.3	4.0		7.8	7.0	6.7	6.5	8.0		5.0	6.6	6.5	6.7	6.9		12.3	13.2	13.1	12.4	13.0	
Bankfull Width/Depth Ratio	15.9	13.7	13.8	13.4	10.9		14.1	14.4	15.5	13.5	14.4		13.2	10.1	10.4	11.7	10.4		9.1	8.4	8.4	9.4	1.0	
Entrenchment Ratio <sup>1</sup>	6.3	6.8	6.9	7.5	7.8		N/A	N/A	N/A	N/A	N/A		24.8	24.4	24.4	22.6	23.5		N/A	N/A	N/A	N/A	N/A	
Bankfull Bank Height Ratio <sup>2</sup>	1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.2		1.0	1.0	1.0	1.0	1.0	
d50 (mm)	18.0	17.8	25.2	38.8	20.9		N/A	N/A	N/A	N/A	N/A		18.3	42.1	28.5	22.6	24.7		N/A	N/A	N/A	N/A	N/A	
UT1B											UT2													
		Cross Section 13 (Riffle)					Cross Section 14 (Pool)					Cross Section 15 (Riffle)					Cross Section 16 (Pool)							
Dimension and Substrate	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7	Base	MY1	MY2	MY3	MY5	MY7
Bankfull Elevation (ft)	647.1	647.1	647.1	647.1	647.1		646.9	646.9	646.9	646.9	646.9		602.9	602.9	602.9	602.9	603.0		602.4	602.4	602.4	602.4	602.4	
Low Bank Elevation (ft)	647.1	647.1	647.1	647.1	647.1		646.9	646.9	646.9	646.9	646.9		602.9	602.9	602.9	602.9	603.0		602.4	602.4	602.4	602.4	602.4	
Bankfull Width (ft)	7.7	7.8	7.7	7.4	8.7		9.7	10.1	9.8	10.0	9.8		7.1	7.0	6.8	6.6	6.8		9.5	9.5	9.9	9.9	9.0	
Floodprone Width (ft)	70	70	70	70	70		N/A	N/A	N/A	N/A	N/A		50	50	50	50	50		N/A	N/A	N/A	N/A	N/A	
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4	0.5		0.8	0.7	0.7	0.7	0.7		0.5	0.5	0.5	0.5	0.6		0.6	0.6	0.6	0.6	0.6	
Bankfull Max Depth (ft)	0.7	0.9	0.8	0.8	0.9		1.4	1.3	1.4	1.3	1.4		0.7	0.9	0.9	0.8	1.1		1.3	1.3	1.3	1.3	1.4	
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.5	3.6	3.2	2.7	4.0		7.8	7.2	7.2	6.6	7.1		3.4	3.8	3.5	3.3	3.9		5.8	5.5	5.8	5.7	5.2	
Bankfull Width/Depth Ratio	17.0	16.9	18.3	20.6	19.2		12.1	14.2	13.5	15.0	13.7		14.7	12.9	13.5	13.5	12.1		15.5	16.3	16.8	17.0	15.3	
Entrenchment Ratio <sup>1</sup>	9.1	9.0	9.1	9.4	8.0		N/A	N/A	N/A	N/A	N/A		7.0	7.2	7.3	7.5	7.3		N/A	N/A	N/A	N/A	N/A	
Bankfull Bank Height Ratio <sup>2</sup>	1.0	1.0	1.0	1.0	1.1		1.0	1.0	1.0	1.0	1.0		1.0	1.0	1.0	1.0	1.1		1.0	1.0	1.0	1.0	1.0	
d50 (mm)	21.3	43.9	26.9	23.2	72.7		N/A	N/A	N/A	N/A	N/A		19.7	25.0	23.5	29.3	29.6		N/A	N/A	N/A	N/A	N/A	

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

**Table 12a. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1 Reach 2**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	10.2	10.4	9.9	10.2	9.7	10.5	9.2	10.9	9.7	12.0		
Floodprone Width (ft)	60	100	60	100	60	100	60	100	60	100		
Bankfull Mean Depth	0.6	0.9	0.6	0.8	0.5	0.7	0.5	0.7	0.6	0.7		
Bankfull Max Depth	1.1	1.4	1.1	1.4	1.1	1.4	1.0	1.4	1.1	1.5		
Bankfull Cross Sectional Area (ft <sup>2</sup> )	6.2	9.0	6.2	8.0	5.3	7.8	4.9	7.9	6.2	8.7		
Width/Depth Ratio	12.0	16.8	12.2	16.7	14.2	17.7	15.1	17.5	15.1	16.5		
Entrenchment Ratio <sup>1</sup>	5.9	9.6	5.9	10.1	6.2	9.5	6.5	9.2	6.2	8.4		
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		<1.0	1.0		
D50 (mm)	13.3	18.0	46.6	64.0	10.4	22.6	23.0	27.2	22.6	56.1		
<b>Profile</b>												
Riffle Length (ft)	13.9	73.2										
Riffle Slope (ft/ft)	0.0078	0.0317										
Pool Length (ft)	17.2	42.8										
Pool Max Depth (ft)	1.6	3.7										
Pool Spacing (ft)	31	78										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	20	68										
Radius of Curvature (ft)	18	26										
Rc:Bankfull Width (ft/ft)	1.8	2.5										
Meander Wave Length (ft)	70	120										
Meander Width Ratio	2.0	6.5										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	1,137											
Sinuosity (ft)	1.2											
Water Surface Slope (ft/ft)	0.0111											
Bankfull Slope (ft/ft)	0.0096											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/SC/41.3/79.2/128.0		SC/0.28/9.9/93.6/145.5/180.0		0.56\2.57\4.8\64.0\117.2\512.0		0.52\2.43\4.6\34.3\102.1\180.0		SC/1.12/14.1/98.3/180.0/1024.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

**Table 12b. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1 Reach 5**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	11.9	13.6	11.9	15.2	11.8	16.0	12.0	15.1	10.9	15.3		
Floodprone Width (ft)	200		200		200		200		200			
Bankfull Mean Depth	0.8	0.9	0.8	0.8	0.8	0.8	0.7	0.8	0.8	1.0		
Bankfull Max Depth	1.3	1.6	1.5	1.7	1.4	1.8	1.3	1.8	1.5	2.0		
Bankfull Cross Sectional Area (ft <sup>2</sup> )	9.1	11.9	10.1	12.6	9.3	12.5	8.8	12.5	8.4	14.7		
Width/Depth Ratio	15.5	15.7	14.0	18.4	14.9	20.5	16.3	18.2	14.1	15.9		
Entrenchment Ratio <sup>1</sup>	14.7	16.8	13.1	16.8	12.5	17.0	13.3	16.7	13.1	18.4		
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		<1.0	1.1		
D50 (mm)	15.4	16.0	30.8	52.1	57.9	70.5	29.6	40.2	31.0	33.5		
<b>Profile</b>												
Riffle Length (ft)	23.7	81.3										
Riffle Slope (ft/ft)	0.0090	0.0304										
Pool Length (ft)	17.6	76.6										
Pool Max Depth (ft)	2.0	4.9										
Pool Spacing (ft)	35	103										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	34	72										
Radius of Curvature (ft)	23	38										
Rc:Bankfull Width (ft/ft)	1.9	2.8										
Meander Wave Length (ft)	97	160										
Meander Width Ratio	2.9	5.3										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	1,535											
Sinuosity (ft)	1.2											
Water Surface Slope (ft/ft)	0.0122											
Bankfull Slope (ft/ft)	0.0104											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/0.11/45.0/104.7/180.0		SC(4.47\20.1\74.9\128.0\362.0		0.18\4.00\20.7\75.9\139.4\512.0		SC\0.50\17.1\70.2\104.7\180.0		SC/0.88/14.8/97.3/168.1/362.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

**Table 12c. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1A Reach 1**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	8.0		7.3		7.2		6.7		6.6			
Floodprone Width (ft)	50		50		50		50		50			
Bankfull Mean Depth	0.5		0.5		0.5		0.5		0.6			
Bankfull Max Depth	0.9		0.9		0.8		0.8		1.2			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.0		3.9		3.8		3.3		4.0			
Width/Depth Ratio	15.9		13.7		13.8		13.4		10.9			
Entrenchment Ratio <sup>1</sup>	6.3		6.8		6.9		7.5		7.8			
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		1.0			
D50 (mm)	18.0		17.8		25.2		38.8		20.9			
<b>Profile</b>												
Riffle Length (ft)	15.5	41.97										
Riffle Slope (ft/ft)	0.0077	0.0505										
Pool Length (ft)	5.4	52.2										
Pool Max Depth (ft)	1.6	3.5										
Pool Spacing (ft)	20	85										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	24	60										
Radius of Curvature (ft)	14	23										
Rc:Bankfull Width (ft/ft)	1.8	2.9										
Meander Wave Length (ft)	70	112										
Meander Width Ratio	3.0	7.5										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	857											
Sinuosity (ft)	1.2											
Water Surface Slope (ft/ft)	0.0126											
Bankfull Slope (ft/ft)	0.0137											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/1.41/33.4/64.0/128.0		0.16\2.24\11.0\42.0\73.4\180.0		0.50\6.01\15.2\52.1\75.9\512.0		SC\0.95\17.3\56.3\83.4\180.0		SC/SC/2.4/39.3/85.0/256.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

**Table 12d. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1A Reach 4**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	8.1		8.2		8.2		8.9		8.5			
Floodprone Width (ft)	200		200		200		200		200			
Bankfull Mean Depth	0.6		0.8		0.8		0.8		0.8			
Bankfull Max Depth	1.8		1.9		1.9		1.8		1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	5.0		6.6		6.5		6.7		6.9			
Width/Depth Ratio	13.2		10.1		10.4		11.7		10.4			
Entrenchment Ratio <sup>1</sup>	24.8		24.4		24.4		22.6		23.5			
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		1.0			
D50 (mm)	18.3		42.1		28.5		22.6		24.7			
<b>Profile</b>												
Riffle Length (ft)	20.5	51.9										
Riffle Slope (ft/ft)	0.0109	0.0449										
Pool Length (ft)	9.1	35.5										
Pool Max Depth (ft)	1.4	3.1										
Pool Spacing (ft)	45	82										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	35	55										
Radius of Curvature (ft)	15	23										
Rc:Bankfull Width (ft/ft)	1.9	2.8										
Meander Wave Length (ft)	96	117										
Meander Width Ratio	4.3	6.8										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	666											
Sinuosity (ft)	1.2											
Water Surface Slope (ft/ft)	N/A											
Bankfull Slope (ft/ft)	0.0129											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/0.25/26.2/75.9/180.0		SC(4.00\23.4\77.8\119.3\180.0		0.50\7.10\27.6\93.2\143.4\256.0		0.14\0.63\11.4\53.2\106.9\180.0		0.30\1.05\9.89\80.3\151.8\512.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

**Table 12e. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT1B**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	7.7		7.8		7.7		7.4		8.7			
Floodprone Width (ft)	70		70		70		70		70			
Bankfull Mean Depth	0.5		0.5		0.4		0.4		0.5			
Bankfull Max Depth	0.7		0.9		0.8		0.8		0.9			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.5		3.6		3.2		2.7		4.0			
Width/Depth Ratio	17.0		16.9		18.3		20.6		19.2			
Entrenchment Ratio <sup>1</sup>	9.1		9.0		9.1		9.4		8.0			
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		1.1			
D50 (mm)	21.3		43.9		26.9		23.2		72.7			
<b>Profile</b>												
Riffle Length (ft)	12.1	24.4										
Riffle Slope (ft/ft)	0.0219	0.0425										
Pool Length (ft)	11.9	30.9										
Pool Max Depth (ft)	1.7	2.5										
Pool Spacing (ft)	30	45										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	25	40										
Radius of Curvature (ft)	14	20										
Rc:Bankfull Width (ft/ft)	1.8	2.6										
Meander Wave Length (ft)	60	72										
Meander Width Ratio	3.2	5.2										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	232											
Sinuosity (ft)	1.3											
Water Surface Slope (ft/ft)	0.0095											
Bankfull Slope (ft/ft)	0.0181											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/SC/19.5/40.2/90.0		SC\0.71\5.6\64.0\107.3\180.0		SC\0.40\3.3\40.2\95.4\128.0		SC\0.62\2.5\62.2\144.6\180.0		SC/2.00/14.8/102.7/139.4/256.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.

<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.



**Table 12f. Monitoring Data - Stream Reach Data Summary**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

**UT2**

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY5		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
<b>Dimension and Substrate - Riffle</b>												
Bankfull Width (ft)	7.1		7.0		6.8		6.6		6.8			
Floodprone Width (ft)	50		50		50		50		50			
Bankfull Mean Depth	0.5		0.5		0.5		0.5		0.6			
Bankfull Max Depth	0.7		0.9		0.9		0.8		1.1			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.4		3.8		3.5		3.3		3.9			
Width/Depth Ratio	14.7		12.9		13.5		13.5		12.1			
Entrenchment Ratio <sup>1</sup>	7.0		7.2		7.3		7.5		7.3			
Bank Height Ratio <sup>2</sup>	1.0		1.0		1.0		1.0		1.0			
D50 (mm)	19.7		25.0		23.5		29.3		29.6			
<b>Profile</b>												
Riffle Length (ft)	13.9	51.7										
Riffle Slope (ft/ft)	0.0146	0.0525										
Pool Length (ft)	10.0	28.4										
Pool Max Depth (ft)	1.0	2.4										
Pool Spacing (ft)	25	66										
Pool Volume (ft <sup>3</sup> )												
<b>Pattern</b>												
Channel Beltwidth (ft)	19	50										
Radius of Curvature (ft)	12	20										
Rc:Bankfull Width (ft/ft)	1.8	3.0										
Meander Wave Length (ft)	58	98										
Meander Width Ratio	2.8	7.5										
<b>Additional Reach Parameters</b>												
Rosgen Classification	C4											
Channel Thalweg Length (ft)	1,032											
Sinuosity (ft)	1.2											
Water Surface Slope (ft/ft)	0.0207											
Bankfull Slope (ft/ft)	0.0195											
Ri%/Ru%/P%/G%/S%												
SC%/Sa%/G%/C%/B%/Be%												
d16/d35/d50/d84/d95/d100	SC/SC/SC/30.2/64.0/128.0		SC\2.80\10.7\35.9\75.9\180.0		SC\3.23\12.9\43.6\80.3\180.0		SC\SC\1.3\26.9\64.0\180.0		SC/0.5/8.0/57.6/95.4/128.0			
% of Reach with Eroding Banks	0%		0%		0%		0%		0%			

<sup>1</sup>Entrenchment Ratio is the flood prone width divided by the bankfull width.


<sup>2</sup>Bank Height Ratio is the bank height divided by the max depth of the bankfull channel.

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 1-UT1 Reach 2

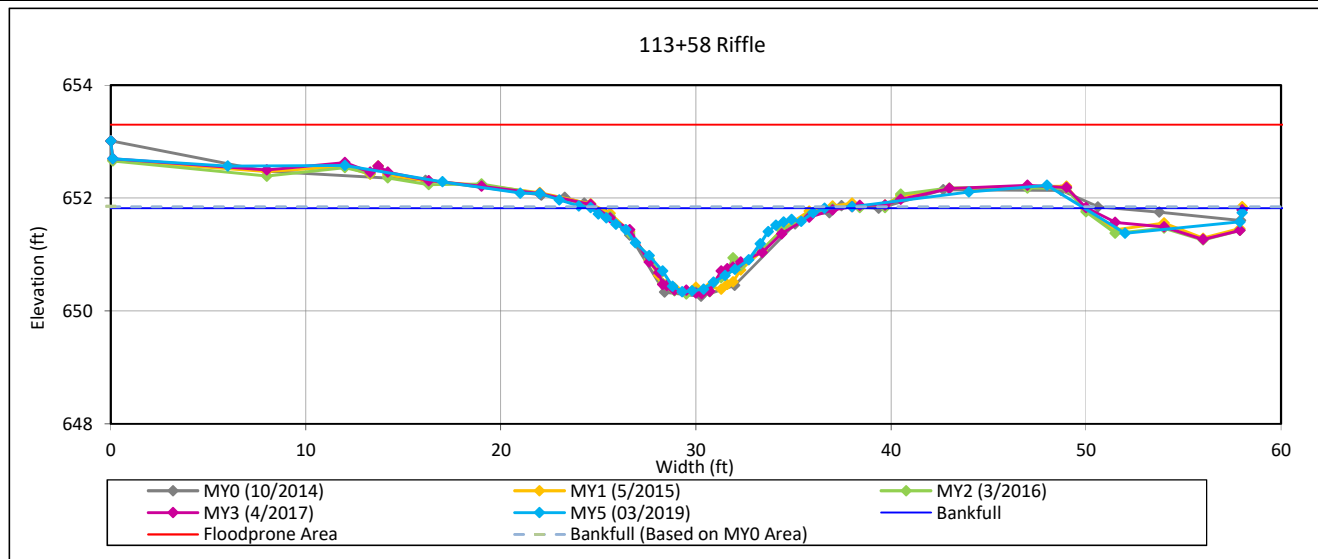

#### Bankfull Dimensions

8.7	x-section area (ft.sq.)
12.0	width (ft)
0.7	mean depth (ft)
1.5	max depth (ft)
12.4	wetted perimeter (ft)
0.7	hyd radi (ft)
16.5	width-depth ratio
100.0	W flood prone area (ft)
8.4	entrenchment ratio
< 1.0	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 2-UT1 Reach 2

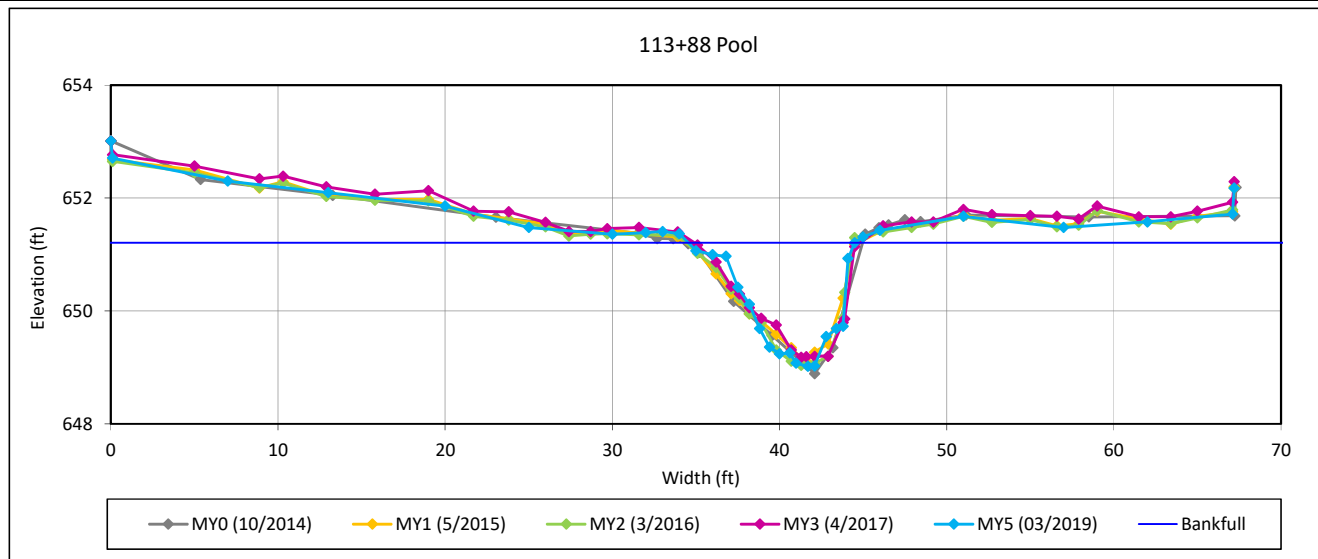

#### Bankfull Dimensions

11.9	x-section area (ft.sq.)
10.0	width (ft)
1.2	mean depth (ft)
2.2	max depth (ft)
11.7	wetted parimeter (ft)
1.0	hyd radi (ft)
8.3	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 3-UT1 Reach 2

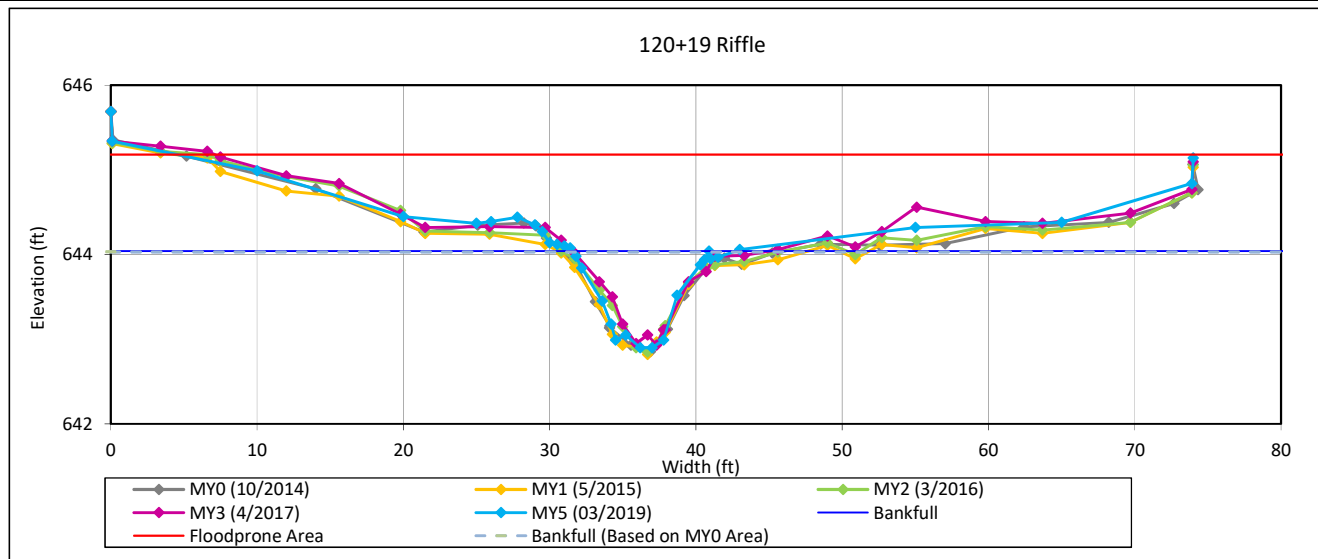

#### Bankfull Dimensions

6.2	x-section area (ft.sq.)
9.7	width (ft)
0.6	mean depth (ft)
1.1	max depth (ft)
10.2	wetted parimeter (ft)
0.6	hyd radi (ft)
15.1	width-depth ratio
60.0	W flood prone area (ft)
6.2	entrenchment ratio
1.0	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 4-UT1 Reach 2

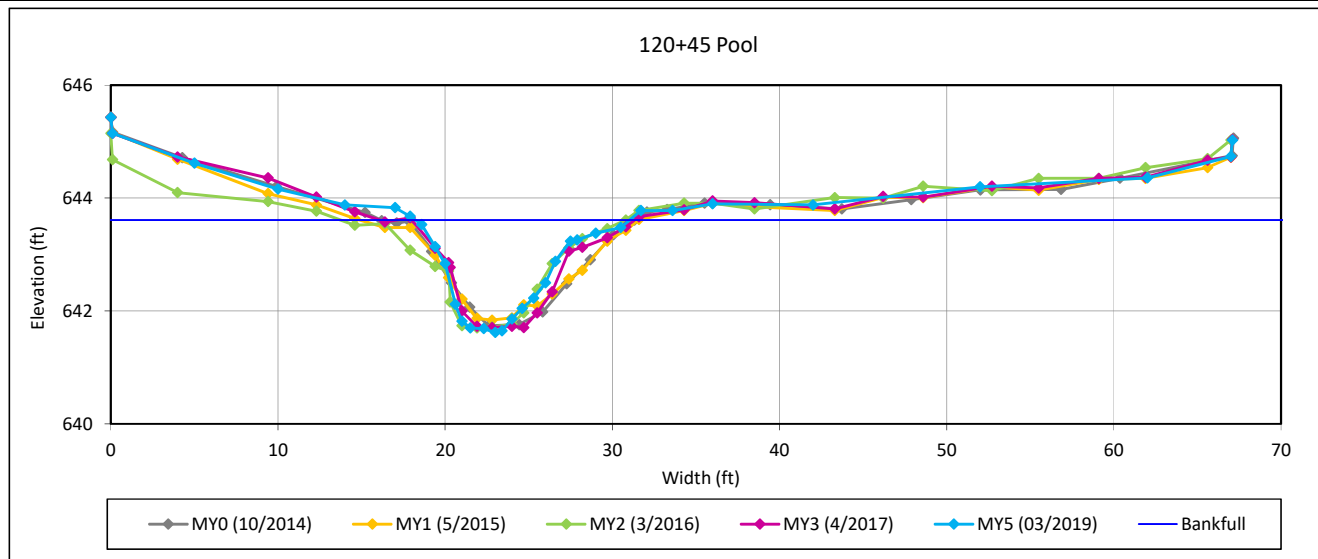

#### Bankfull Dimensions

12.4	x-section area (ft.sq.)
12.8	width (ft)
1.0	mean depth (ft)
2.0	max depth (ft)
13.8	wetted parimeter (ft)
0.9	hyd radi (ft)
13.2	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

**Cross Section Plots**

Agony Acres Mitigation Site (DMS Project No. 95716)

**Monitoring Year 5 - 2019**

**Cross Section 5-UT1 Reach 5**

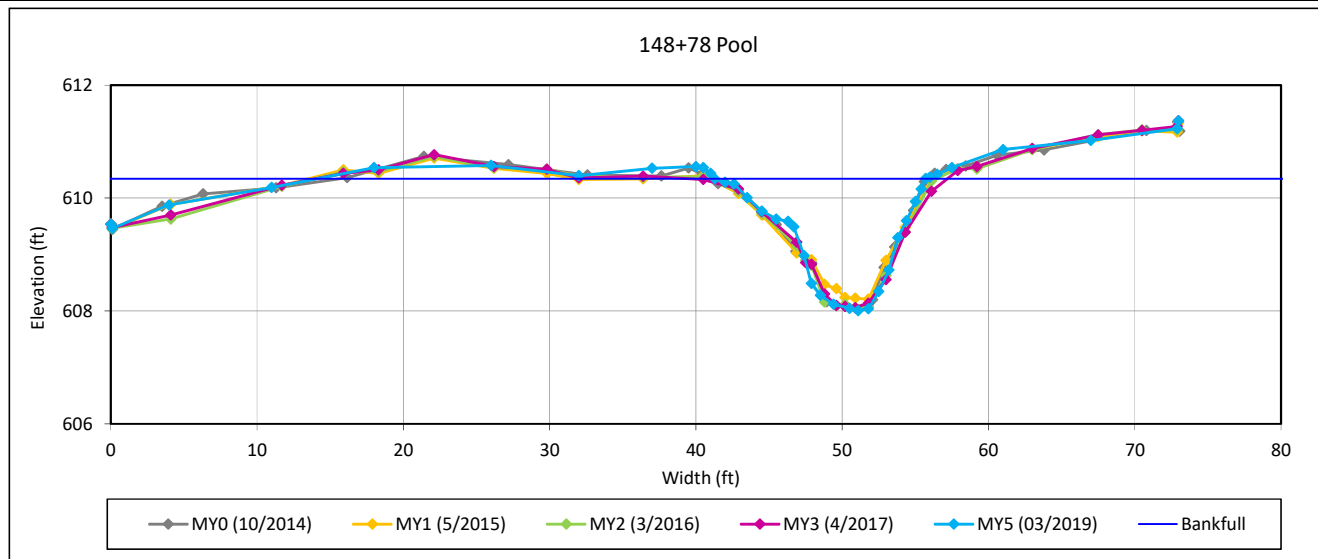

**Bankfull Dimensions**

17.0	x-section area (ft.sq.)
14.4	width (ft)
1.2	mean depth (ft)
2.3	max depth (ft)
15.5	wetted parimeter (ft)
1.1	hyd radi (ft)
12.2	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 6-UT1 Reach 5

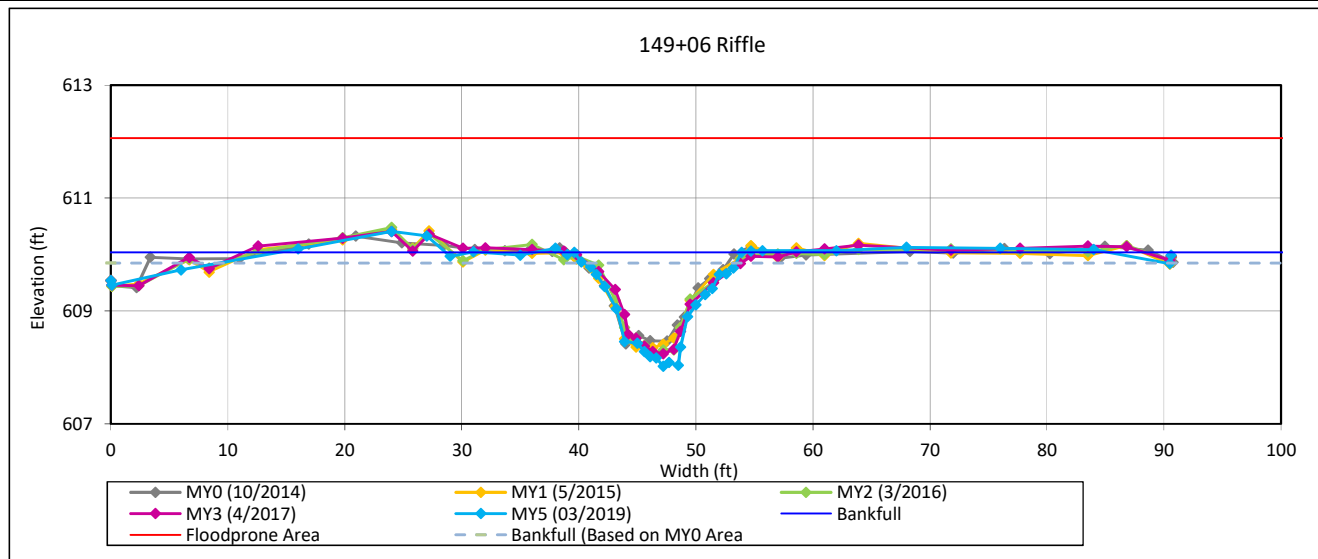

#### Bankfull Dimensions

14.7	x-section area (ft.sq.)
15.3	width (ft)
1.0	mean depth (ft)
2.0	max depth (ft)
16.2	wetted perimeter (ft)
0.9	hyd radi (ft)
15.9	width-depth ratio
200.0	W flood prone area (ft)
13.1	entrenchment ratio
1.1	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 7-UT1 Reach 5

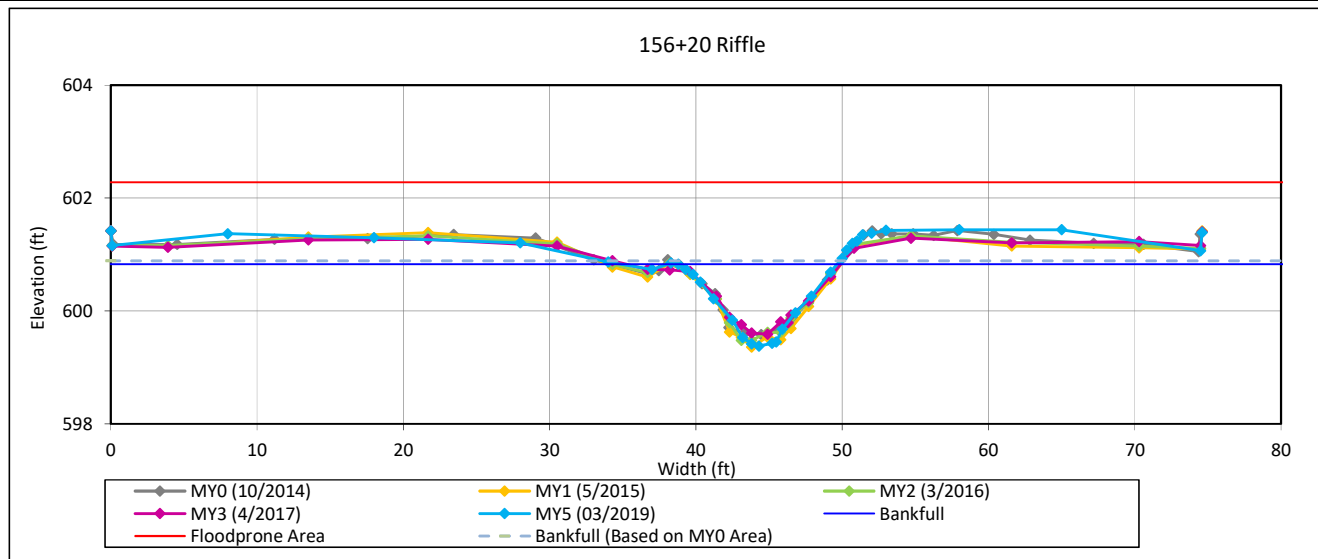

#### Bankfull Dimensions

8.4	x-section area (ft.sq.)
10.9	width (ft)
0.8	mean depth (ft)
1.5	max depth (ft)
11.3	wetted parimeter (ft)
0.7	hyd radi (ft)
14.1	width-depth ratio
200.0	W flood prone area (ft)
18.4	entrenchment ratio
< 1.0	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering



View Downstream




### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 8-UT1 Reach 5

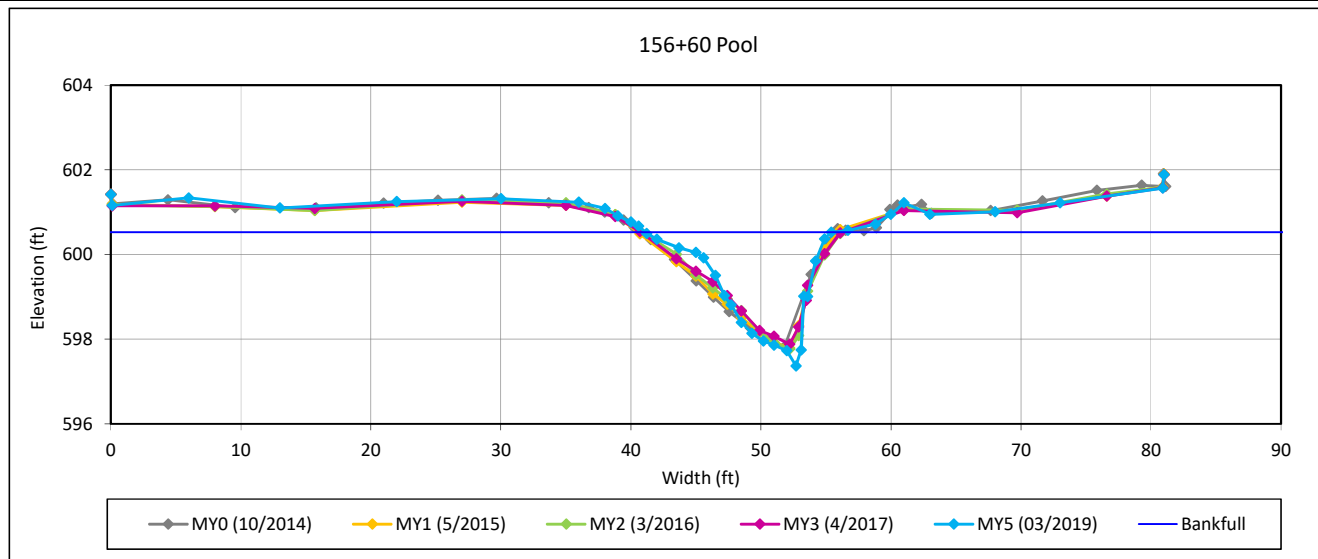

#### Bankfull Dimensions

19.4	x-section area (ft.sq.)
14.3	width (ft)
1.4	mean depth (ft)
3.2	max depth (ft)
16.8	wetted parimeter (ft)
1.2	hyd radi (ft)
10.5	width-depth ratio



View Downstream


Survey Date: 03/2019  
Field Crew: Wildlands Engineering

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 9-UT1A Reach 1

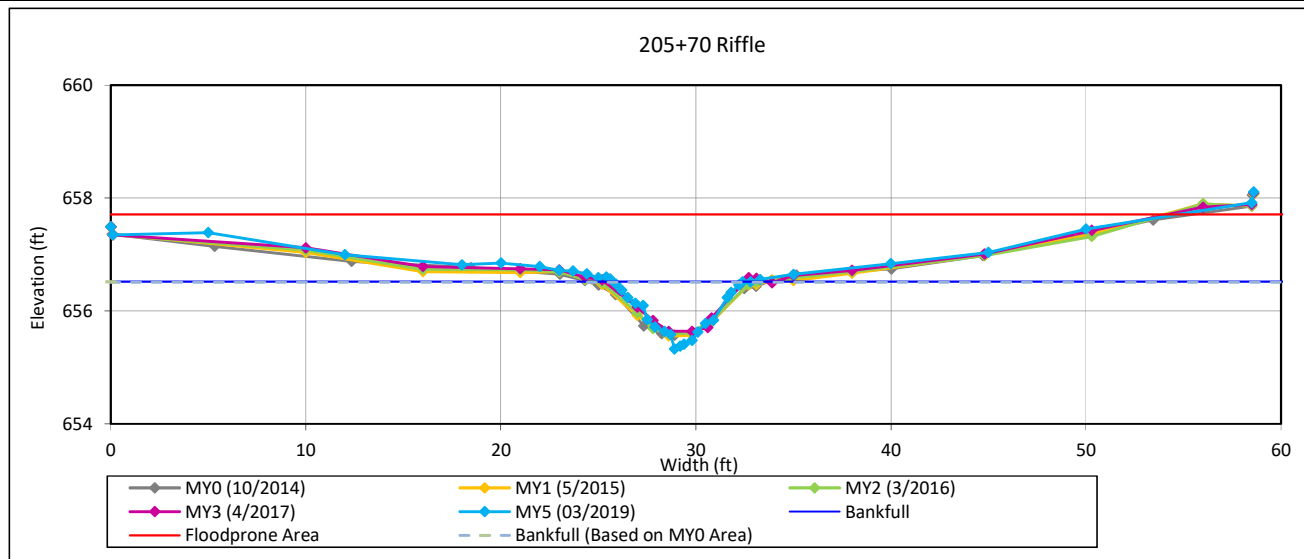

#### Bankfull Dimensions

4.0	x-section area (ft.sq.)
6.6	width (ft)
0.6	mean depth (ft)
1.2	max depth (ft)
7.2	wetted parimeter (ft)
0.6	hyd radi (ft)
10.9	width-depth ratio
51.8	W flood prone area (ft)
7.8	entrenchment ratio
1.0	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering




View Downstream

**Cross Section Plots**

Agony Acres Mitigation Site (DMS Project No. 95716)

**Monitoring Year 5 - 2019**

**Cross Section 10-UT1A Reach 1**

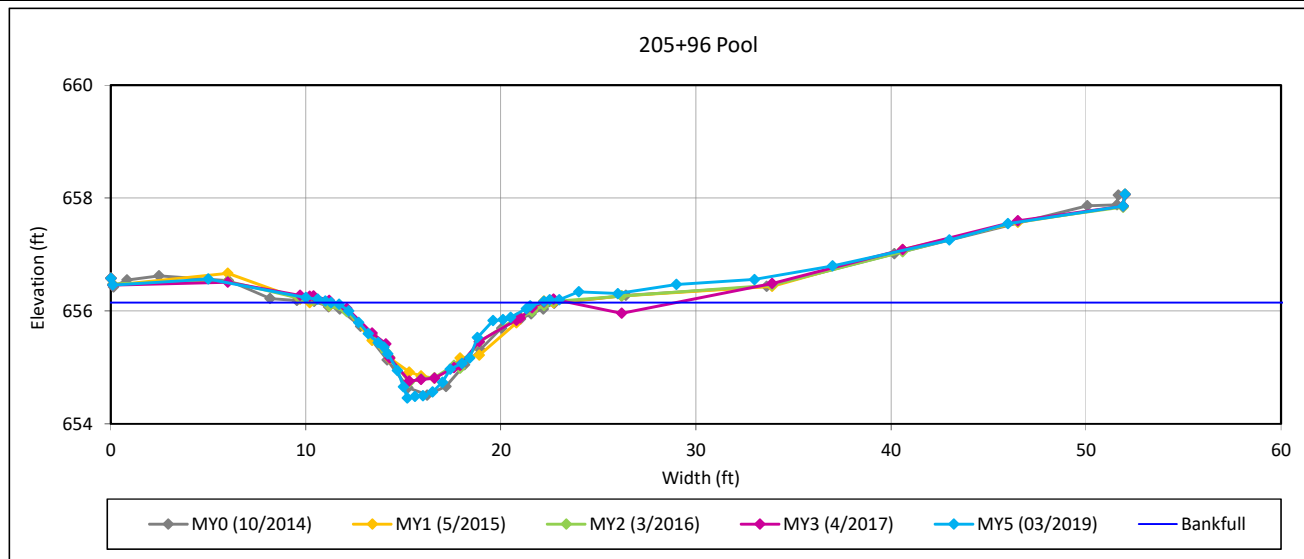

Bankfull Dimensions

8.0	x-section area (ft.sq.)
10.7	width (ft)
0.7	mean depth (ft)
1.7	max depth (ft)
11.5	wetted parimeter (ft)
0.7	hyd radi (ft)
14.4	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

**Cross Section Plots**

Agony Acres Mitigation Site (DMS Project No. 95716)

**Monitoring Year 5 - 2019**

**Cross Section 11-UT1A Reach 4**

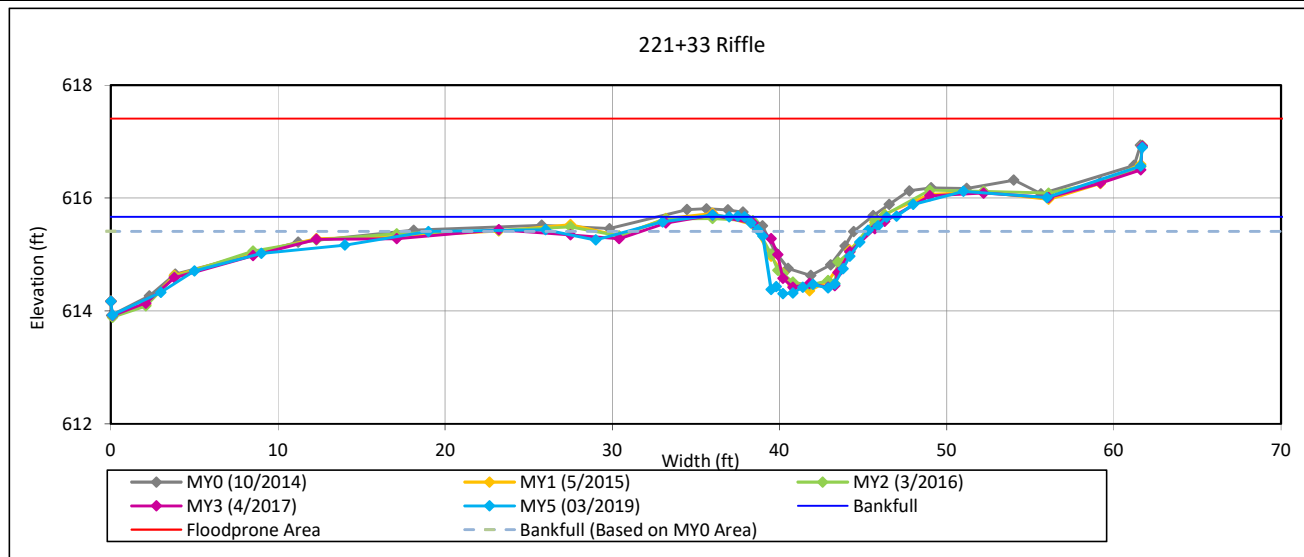

**Bankfull Dimensions**

6.9	x-section area (ft.sq.)
8.5	width (ft)
0.8	mean depth (ft)
1.7	max depth (ft)
9.4	wetted parimeter (ft)
0.7	hyd radi (ft)
10.4	width-depth ratio
200.0	W flood prone area (ft)
23.5	entrenchment ratio
1.2	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 12-UT1A Reach 4

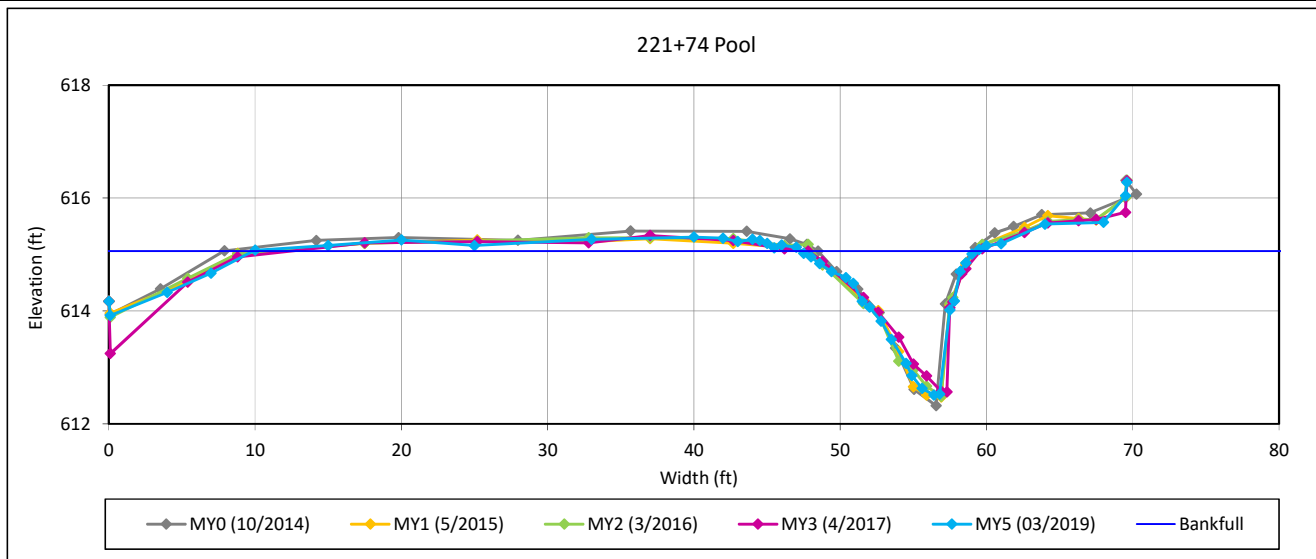

#### Bankfull Dimensions

13.0	x-section area (ft.sq.)
12.0	width (ft)
1.1	mean depth (ft)
2.5	max depth (ft)
13.7	wetted parimeter (ft)
0.9	hyd radi (ft)
11.0	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

**Cross Section Plots**

Agony Acres Mitigation Site (DMS Project No. 95716)

**Monitoring Year 5 - 2019**

**Cross Section 13-UT1B**

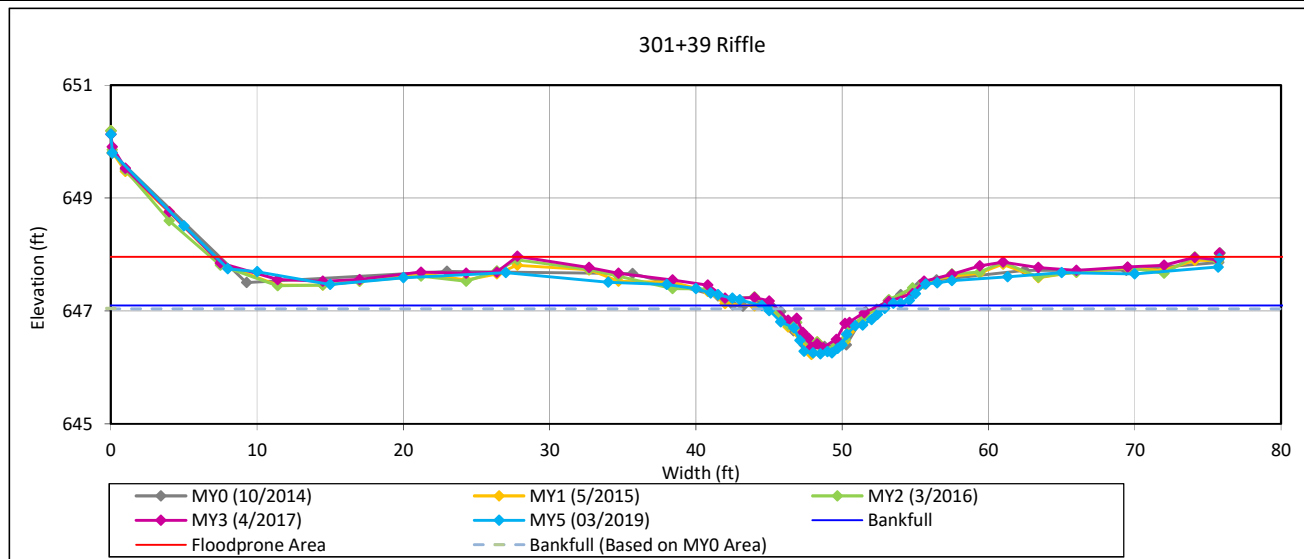

**Bankfull Dimensions**

- 4.0 x-section area (ft.sq.)
- 8.7 width (ft)
- 0.5 mean depth (ft)
- 0.9 max depth (ft)
- 9.0 wetted parimeter (ft)
- 0.4 hyd radi (ft)
- 19.2 width-depth ratio
- 70.0 W flood prone area (ft)
- 8.0 entrenchment ratio
- 1.1 low bank height ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 14-UT1B

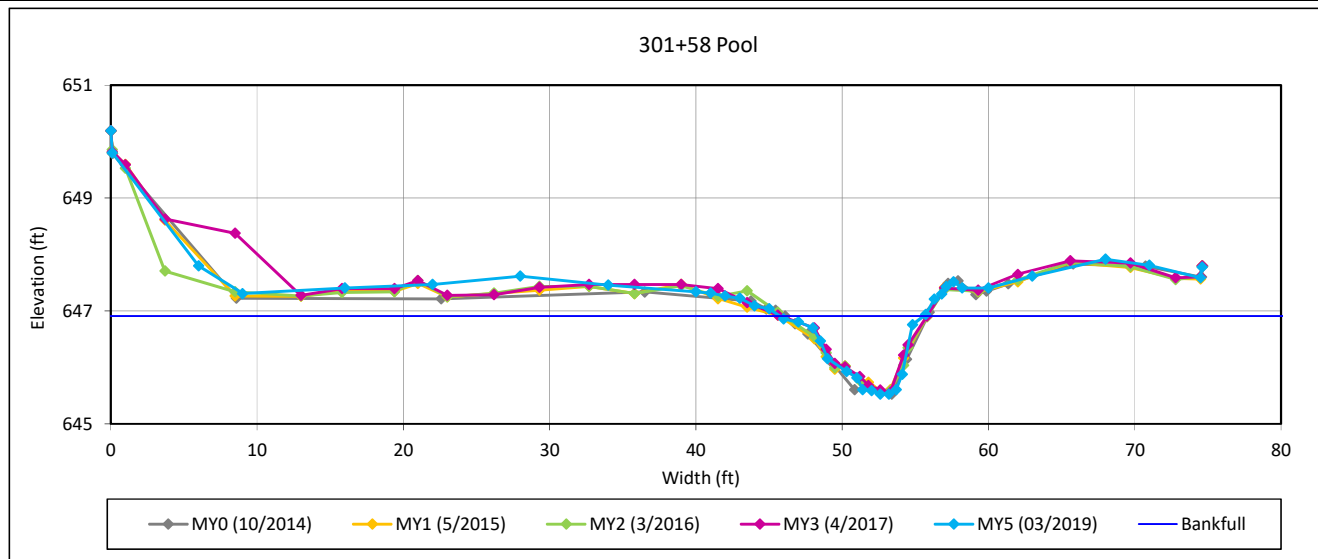

#### Bankfull Dimensions

7.1	x-section area (ft.sq.)
9.8	width (ft)
0.7	mean depth (ft)
1.4	max depth (ft)
10.6	wetted parimeter (ft)
0.7	hyd radi (ft)
13.7	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering




View Downstream

### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 15-UT2

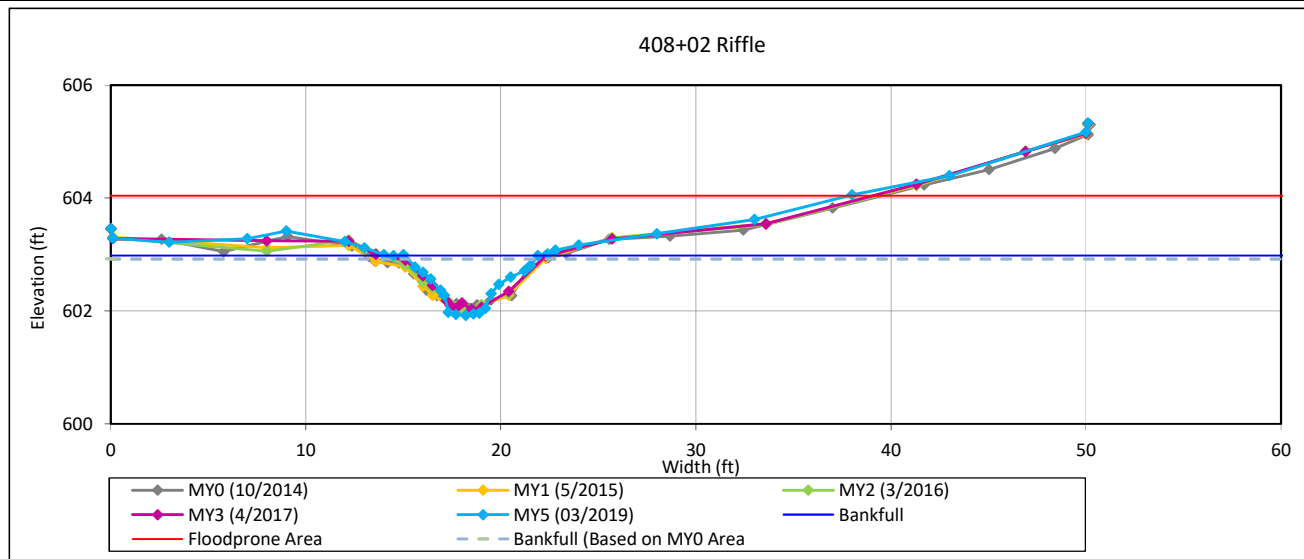

#### Bankfull Dimensions

3.9	x-section area (ft.sq.)
6.8	width (ft)
0.6	mean depth (ft)
1.1	max depth (ft)
7.3	wetted parimeter (ft)
0.5	hyd radi (ft)
12.1	width-depth ratio
50.0	W flood prone area (ft)
7.3	entrenchment ratio
1.1	low bank height ratio

Survey Date: 03/2019

Field Crew: Wildlands Engineering



View Downstream




### Cross Section Plots

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

#### Cross Section 16-UT2

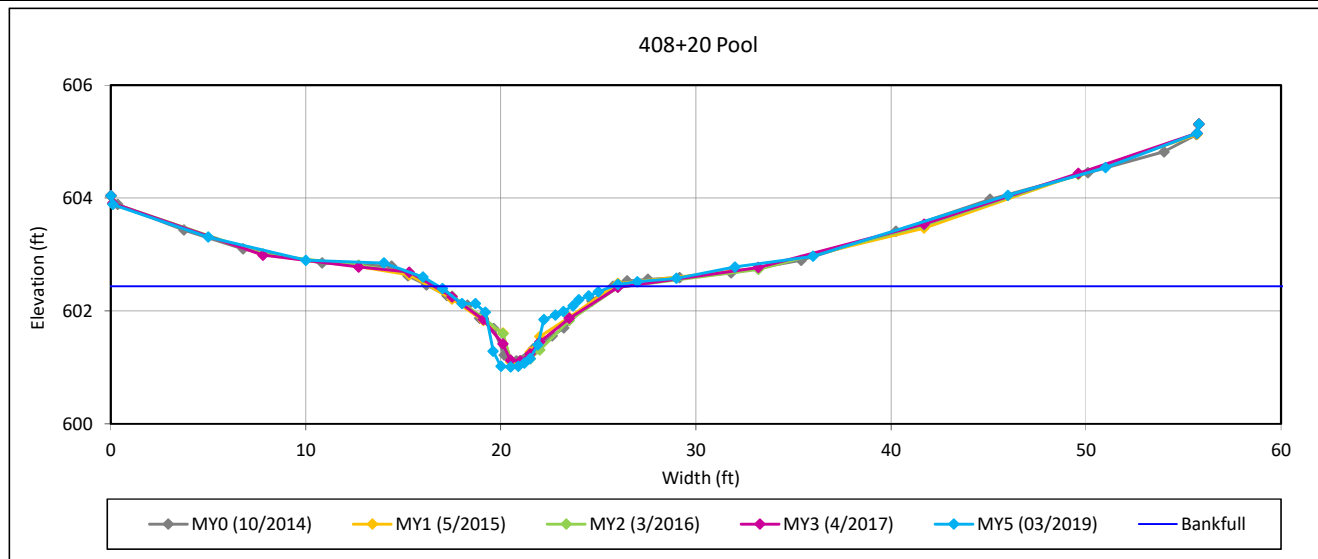

#### Bankfull Dimensions

5.2	x-section area (ft.sq.)
9.0	width (ft)
0.6	mean depth (ft)
1.4	max depth (ft)
9.9	wetted parimeter (ft)
0.5	hyd radi (ft)
15.3	width-depth ratio

Survey Date: 03/2019  
Field Crew: Wildlands Engineering



View Downstream

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	3	24	27	27	27
<b>SAND</b>	Very fine	0.062	0.125					27
	Fine	0.125	0.250					27
	Medium	0.25	0.50	1	2	3	3	30
	Coarse	0.5	1.0		3	3	3	33
	Very Coarse	1.0	2.0	8	4	12	12	45
<b>GRAVEL</b>	Very Fine	2.0	2.8					45
	Very Fine	2.8	4.0					45
	Fine	4.0	5.6					45
	Fine	5.6	8.0					45
	Medium	8.0	11.0	2	1	3	3	48
	Medium	11.0	16.0	2	1	3	3	51
	Coarse	16.0	22.6	1	3	4	4	55
	Coarse	22.6	32	4		4	4	59
	Very Coarse	32	45	4		4	4	63
	Very Coarse	45	64	6	1	7	7	70
<b>COBBLE</b>	Small	64	90	12		12	12	82
	Small	90	128	8		8	8	90
	Large	128	180	5		5	5	95
	Large	180	256	2	1	3	3	98
<b>BOULDER</b>	Small	256	362					98
	Small	362	512	1		1	1	99
	Medium	512	1024	1		1	1	100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	1.12
D <sub>50</sub> =	14.1
D <sub>84</sub> =	98.3
D <sub>95</sub> =	180.0
D <sub>100</sub> =	1024.0

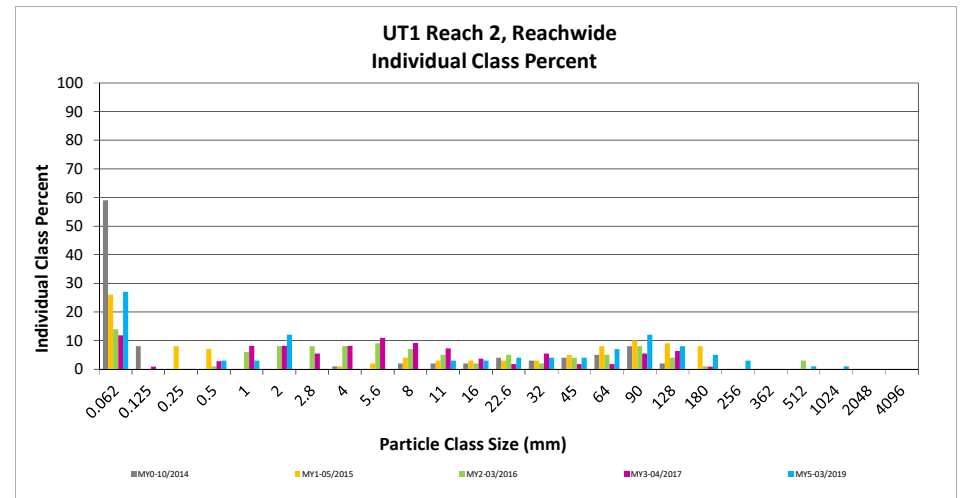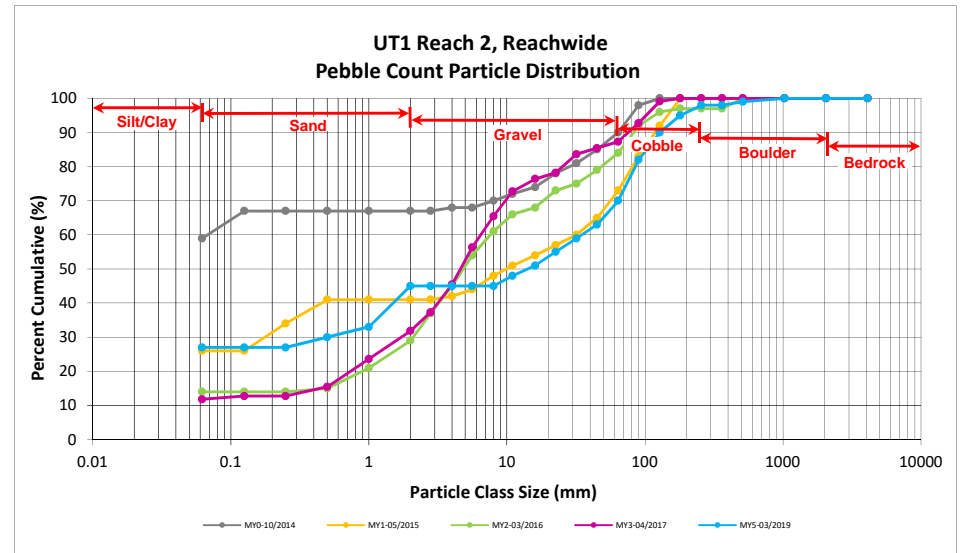

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 4, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	10	9	19	19	19
<b>SAND</b>	Very fine	0.062	0.125					19
	Fine	0.125	0.250					19
	Medium	0.25	0.50	2	6	8	8	27
	Coarse	0.5	1.0	7	15	22	22	49
	Very Coarse	1.0	2.0	2	7	9	9	58
<b>GRAVEL</b>	Very Fine	2.0	2.8					58
	Very Fine	2.8	4.0					58
	Fine	4.0	5.6	1		1	1	59
	Fine	5.6	8.0					59
	Medium	8.0	11.0	3	1	4	4	63
	Medium	11.0	16.0	6		6	6	69
	Coarse	16.0	22.6					69
	Coarse	22.6	32	4	1	5	5	74
	Very Coarse	32	45	3	1	4	4	78
Very Coarse	45	64	9		9	9	87	
<b>COBBLE</b>	Small	64	90	8		8	8	95
	Small	90	128	3		3	3	98
	Large	128	180	1		1	1	99
	Large	180	256	1		1	1	100
<b>BOULDER</b>	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	0.64
D <sub>50</sub> =	1.1
D <sub>84</sub> =	56.9
D <sub>95</sub> =	90.0
D <sub>100</sub> =	256.0

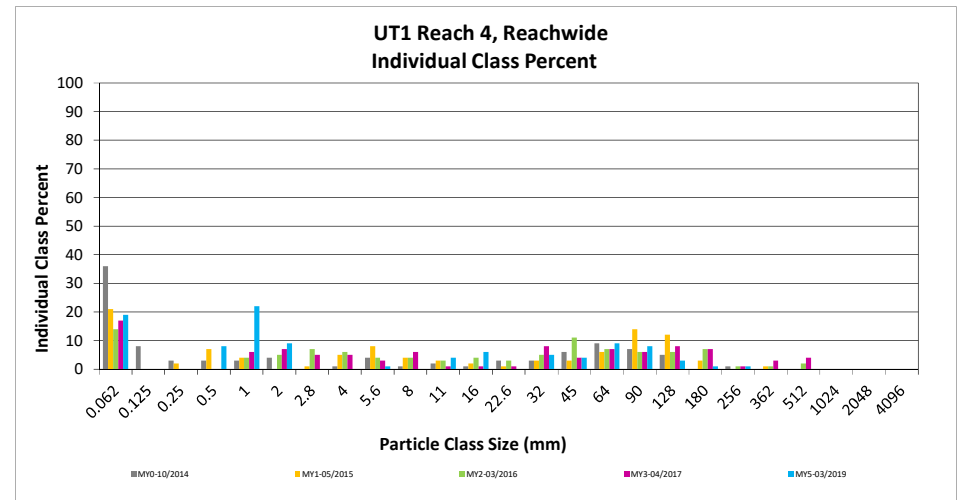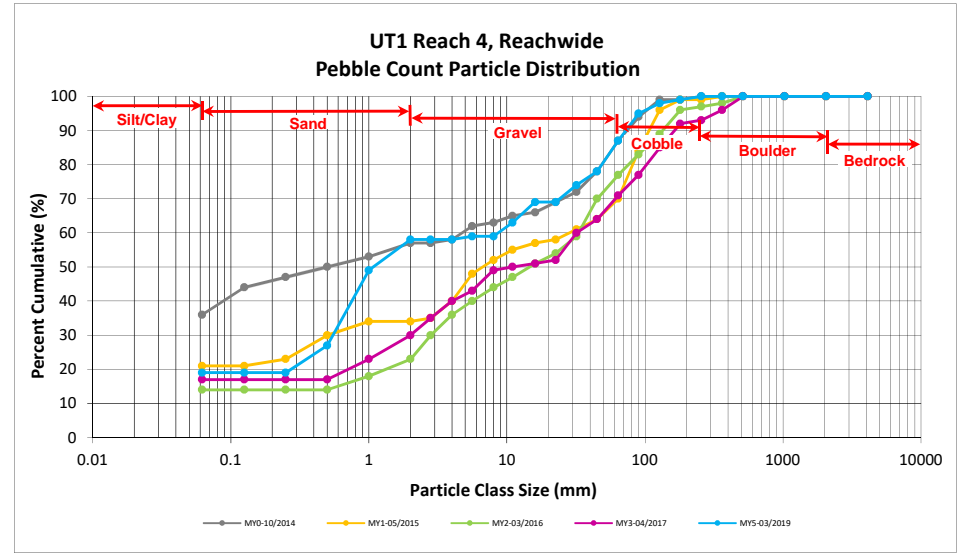

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 5, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	1	23	24	24	24
<b>SAND</b>	Very fine	0.062	0.125					24
	Fine	0.125	0.250					24
	Medium	0.25	0.50		2	2	2	26
	Coarse	0.5	1.0	2	9	11	11	37
	Very Coarse	1.0	2.0	4	1	5	5	42
<b>GRAVEL</b>	Very Fine	2.0	2.8					42
	Very Fine	2.8	4.0					42
	Fine	4.0	5.6	1		1	1	43
	Fine	5.6	8.0	2		2	2	45
	Medium	8.0	11.0		1	1	1	46
	Medium	11.0	16.0	5		5	5	51
	Coarse	16.0	22.6	5	2	7	7	58
	Coarse	22.6	32	4	1	5	5	63
	Very Coarse	32	45	5		5	5	68
Very Coarse	45	64	5		5	5	73	
<b>COBBLE</b>	Small	64	90	9		9	9	82
	Small	90	128	9		9	9	91
	Large	128	180	5		5	5	96
	Large	180	256	2	1	3	3	99
<b>BOULDER</b>	Small	256	362	1		1	1	100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	0.88
D <sub>50</sub> =	14.8
D <sub>84</sub> =	97.3
D <sub>95</sub> =	168.1
D <sub>100</sub> =	362.0

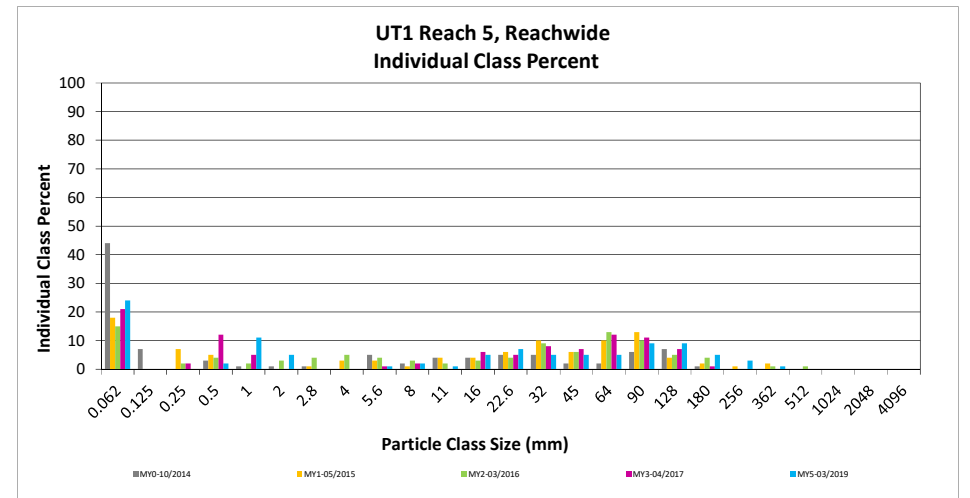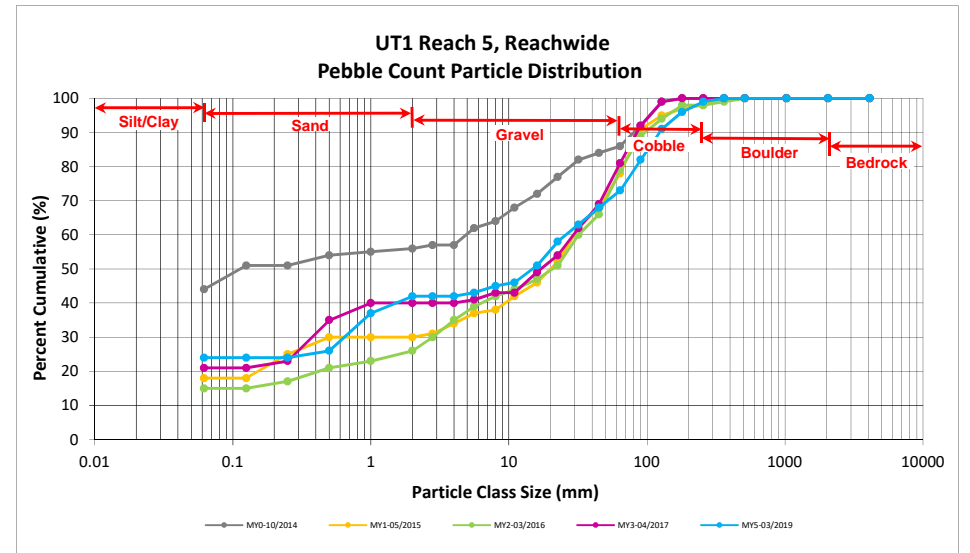

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1A Reach 1, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062		17	17	17	17
<b>SAND</b>	Very fine	0.062	0.125					17
	Fine	0.125	0.250					17
	Medium	0.25	0.50		5	5	5	22
	Coarse	0.5	1.0		14	14	14	36
	Very Coarse	1.0	2.0		1	1	1	37
<b>GRAVEL</b>	Very Fine	2.0	2.8					37
	Very Fine	2.8	4.0		1	1	1	38
	Fine	4.0	5.6		1	1	1	39
	Fine	5.6	8.0	1	1	2	2	41
	Medium	8.0	11.0	2		2	2	43
	Medium	11.0	16.0	5		5	5	48
	Coarse	16.0	22.6	9		9	9	57
	Coarse	22.6	32	8		8	8	65
	Very Coarse	32	45	12		12	12	77
Very Coarse	45	64	11		11	11	88	
<b>COBBLE</b>	Small	64	90	9		9	9	97
	Small	90	128	2		2	2	99
	Large	128	180	1		1	1	100
	Large	180	256					100
<b>BOULDER</b>	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	0.95
D <sub>50</sub> =	17.3
D <sub>84</sub> =	56.3
D <sub>95</sub> =	83.4
D <sub>100</sub> =	180.0

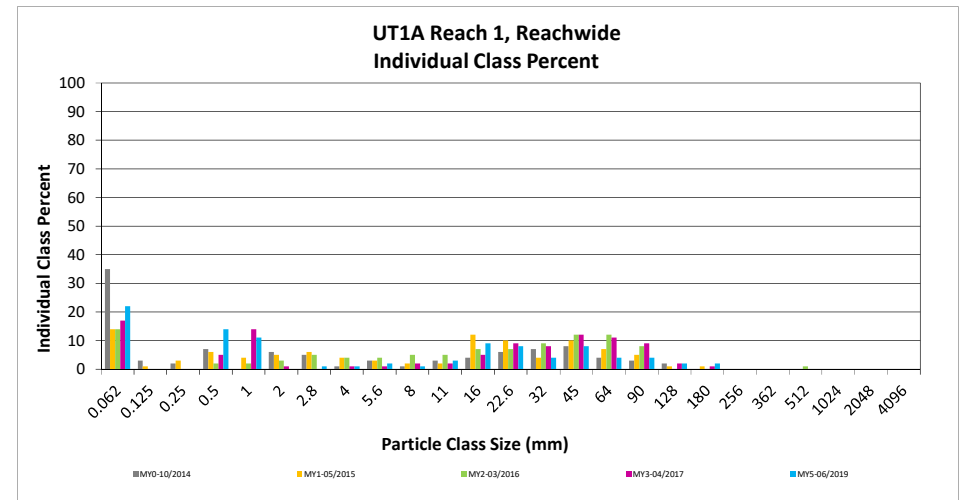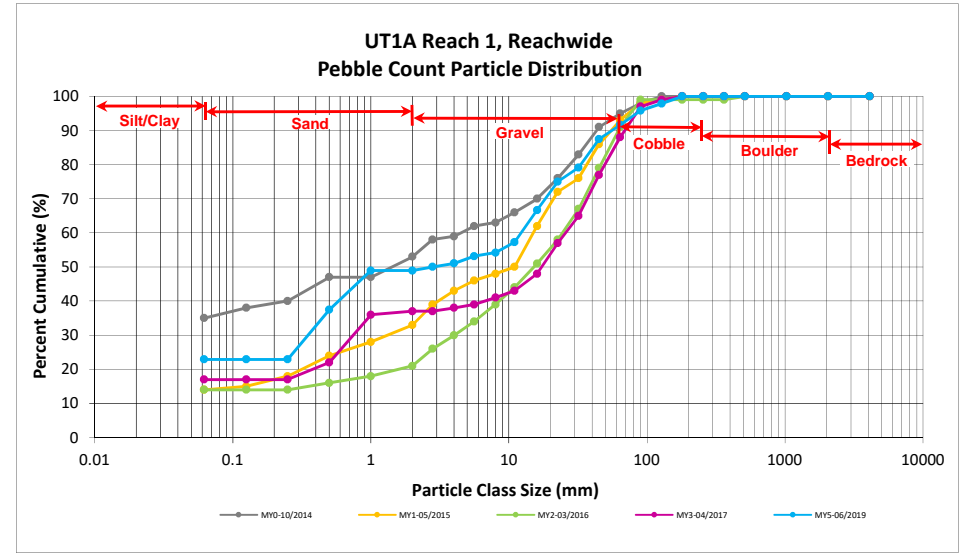

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1A Reach 4, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	6	5	11	11	11
<b>SAND</b>	Very fine	0.062	0.125					11
	Fine	0.125	0.250		1	1	1	12
	Medium	0.25	0.50		14	14	14	26
	Coarse	0.5	1.0	2	6	8	8	34
	Very Coarse	1.0	2.0	8	5	13	13	47
<b>GRAVEL</b>	Very Fine	2.0	2.8					47
	Very Fine	2.8	4.0					47
	Fine	4.0	5.6					47
	Fine	5.6	8.0		1	1	1	48
	Medium	8.0	11.0		3	3	3	51
	Medium	11.0	16.0	1	4	5	5	56
	Coarse	16.0	22.6	3	1	4	4	60
	Coarse	22.6	32	7		7	7	67
	Very Coarse	32	45	6		6	6	73
	Very Coarse	45	64	7		7	7	80
<b>COBBLE</b>	Small	64	90	6		6	6	86
	Small	90	128	6		6	6	92
	Large	128	180	6		6	6	98
	Large	180	256	1	1	1	1	99
<b>BOULDER</b>	Small	256	362					99
	Small	362	512	1		1	1	100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	0.30
D <sub>35</sub> =	1.05
D <sub>50</sub> =	9.89
D <sub>84</sub> =	80.3
D <sub>95</sub> =	151.8
D <sub>100</sub> =	512.0

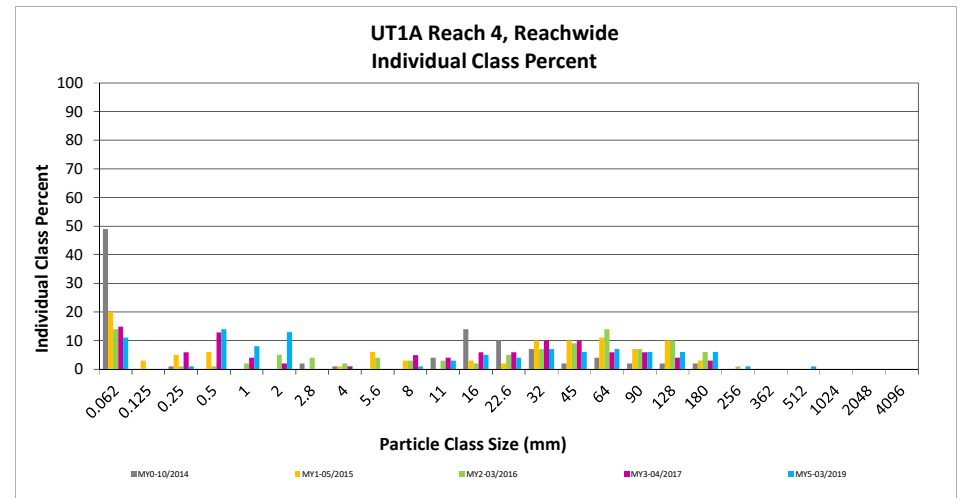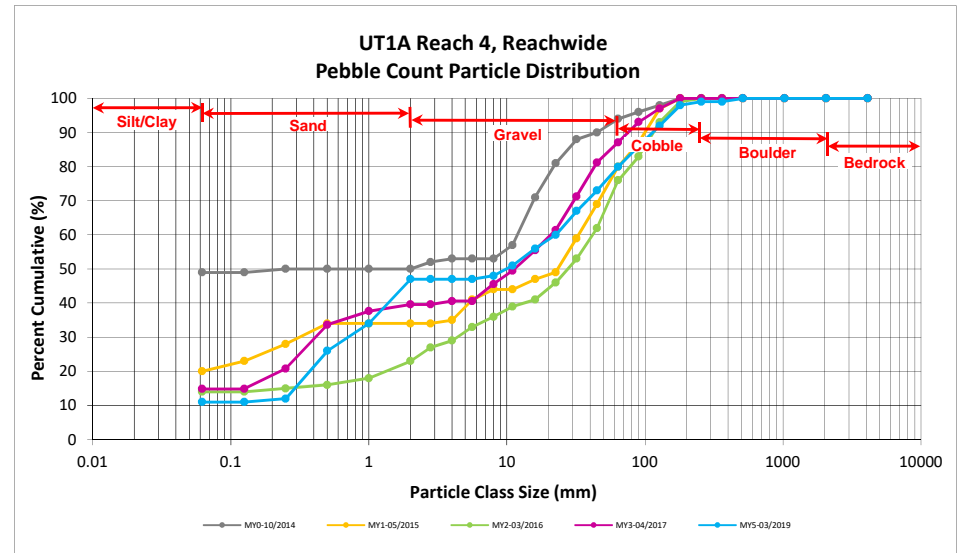

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1B, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	3	24	27	27	27
<b>SAND</b>	Very fine	0.062	0.125					27
	Fine	0.125	0.250		2	2	2	29
	Medium	0.25	0.50		1	1	1	30
	Coarse	0.5	1.0		1	1	1	31
	Very Coarse	1.0	2.0	2	2	4	4	35
<b>GRAVEL</b>	Very Fine	2.0	2.8					35
	Very Fine	2.8	4.0					35
	Fine	4.0	5.6		1	1	1	36
	Fine	5.6	8.0	1	2	3	3	39
	Medium	8.0	11.0	5	2	7	7	46
	Medium	11.0	16.0	3	2	5	5	51
	Coarse	16.0	22.6	2		2	2	53
	Coarse	22.6	32	4	1	5	5	58
	Very Coarse	32	45	4		4	4	62
Very Coarse	45	64	7	1	8	8	70	
<b>COBBLE</b>	Small	64	90	8		8	8	78
	Small	90	128	15	1	16	16	94
	Large	128	180	4		4	4	98
	Large	180	256	2		2	2	100
<b>BOULDER</b>	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	2.00
D <sub>50</sub> =	14.8
D <sub>84</sub> =	102.7
D <sub>95</sub> =	139.4
D <sub>100</sub> =	256.0

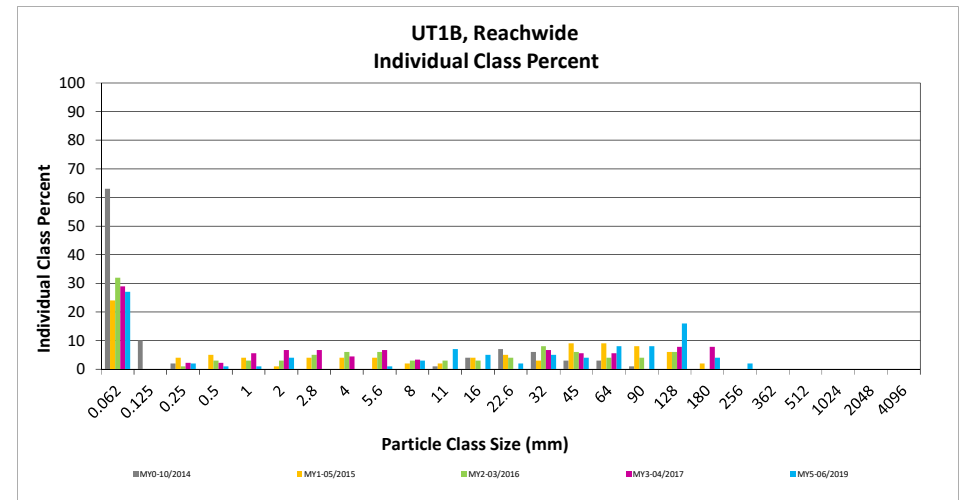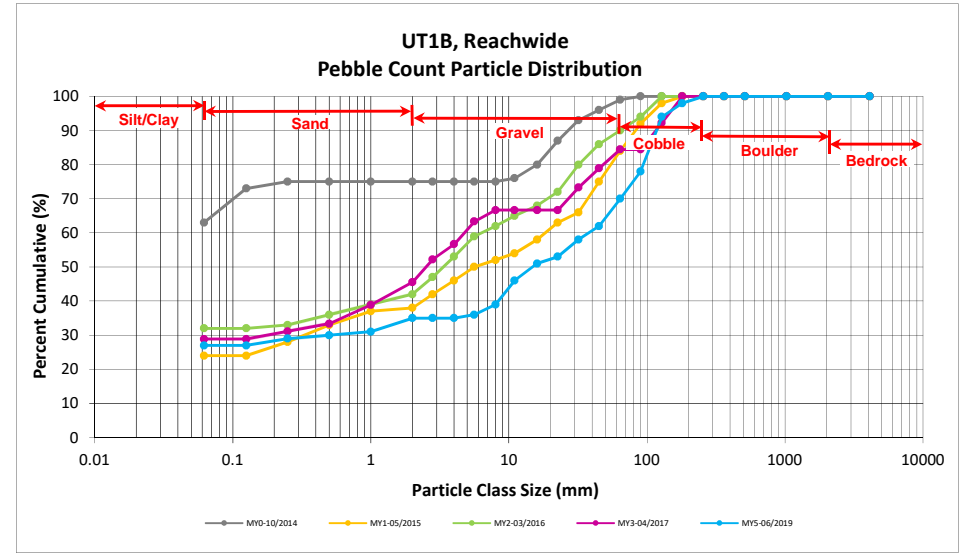

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
<b>SILT/CLAY</b>	Silt/Clay	0.000	0.062	5	25	30	30	30
<b>SAND</b>	Very fine	0.062	0.125					30
	Fine	0.125	0.250		3	3	3	33
	Medium	0.25	0.50		2	2	2	35
	Coarse	0.5	1.0	5	2	7	7	42
	Very Coarse	1.0	2.0	5	1	6	6	48
<b>GRAVEL</b>	Very Fine	2.0	2.8					48
	Very Fine	2.8	4.0					48
	Fine	4.0	5.6		1	1	1	49
	Fine	5.6	8.0		1	1	1	50
	Medium	8.0	11.0	1		1	1	51
	Medium	11.0	16.0	2		2	2	53
	Coarse	16.0	22.6	4	1	5	5	58
	Coarse	22.6	32	8	1	9	9	67
	Very Coarse	32	45	9	1	10	10	77
Very Coarse	45	64	8	2	10	10	87	
<b>COBBLE</b>	Small	64	90	7		7	7	94
	Small	90	128	6		6	6	100
	Large	128	180					100
	Large	180	256					100
<b>BOULDER</b>	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
	Large/Very Large	1024	2048					100
<b>BEDROCK</b>	Bedrock	2048	>2048					100
<b>Total</b>				<b>60</b>	<b>40</b>	<b>100</b>	<b>100</b>	<b>100</b>

Reachwide Channel materials (mm)	
D <sub>16</sub> =	Silt/Clay
D <sub>35</sub> =	0.50
D <sub>50</sub> =	8.0
D <sub>84</sub> =	57.6
D <sub>95</sub> =	95.4
D <sub>100</sub> =	128.0

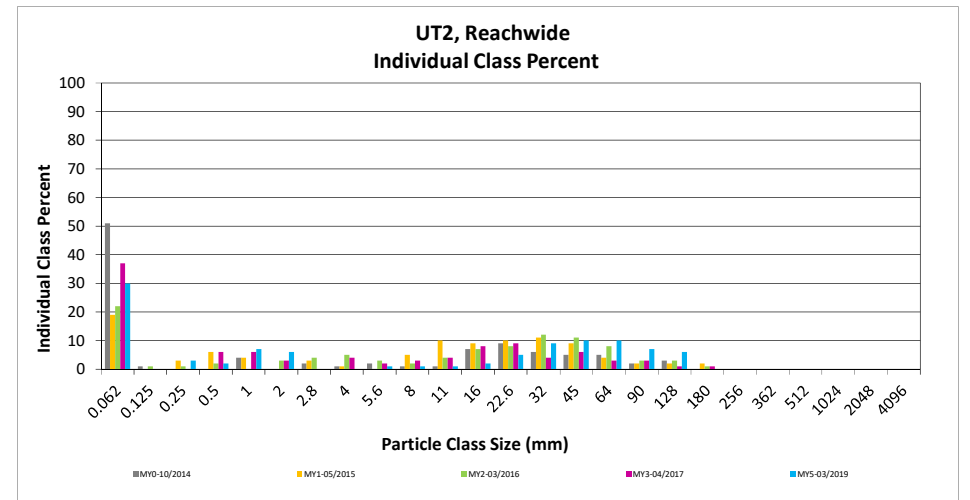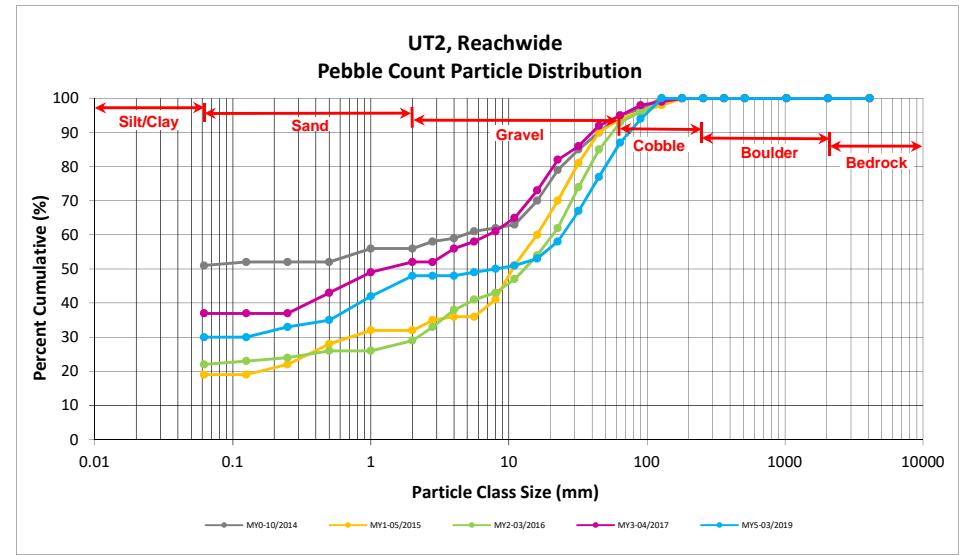



**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 2, Cross Section 1

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	7	7	7
<b>SAND</b>	Very fine	0.062	0.125			7
	Fine	0.125	0.250	2	2	9
	Medium	0.25	0.50	2	2	11
	Coarse	0.5	1.0	5	5	16
	Very Coarse	1.0	2.0	8	8	24
<b>GRAVEL</b>	Very Fine	2.0	2.8			24
	Very Fine	2.8	4.0			24
	Fine	4.0	5.6	2	2	26
	Fine	5.6	8.0	3	3	29
	Medium	8.0	11.0	4	4	33
	Medium	11.0	16.0	5	5	38
	Coarse	16.0	22.6	1	1	39
	Coarse	22.6	32	2	2	41
	Very Coarse	32	45	4	4	45
	Very Coarse	45	64	8	8	53
<b>COBBLE</b>	Small	64	90	13	13	66
	Small	90	128	13	13	79
	Large	128	180	14	14	93
	Large	180	256	5	5	98
<b>BOULDER</b>	Small	256	362	2	2	100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 1	
Channel materials (mm)	
D <sub>16</sub> =	1.00
D <sub>35</sub> =	12.78
D <sub>50</sub> =	56.1
D <sub>84</sub> =	144.6
D <sub>95</sub> =	207.2
D <sub>100</sub> =	362.0

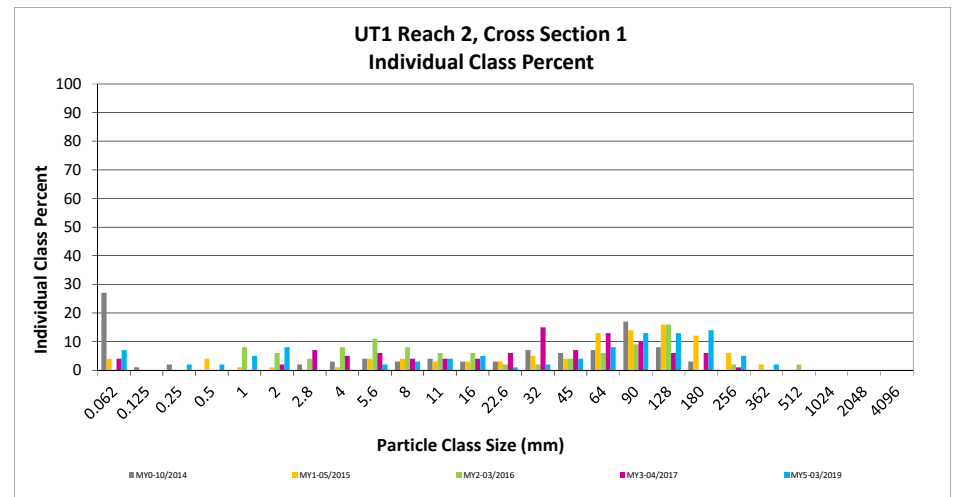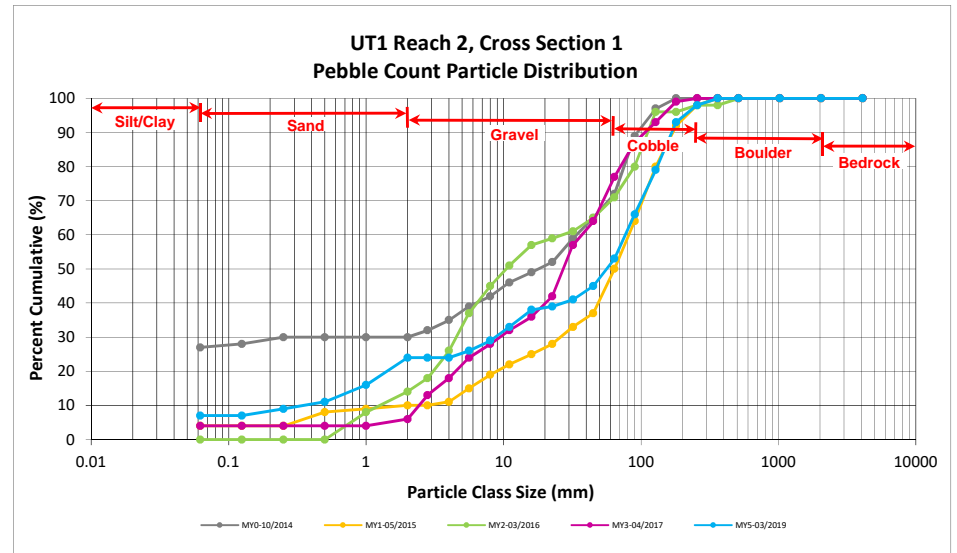

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 2, Cross Section 3

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	3	3	3
<b>SAND</b>	Very fine	0.062	0.125			3
	Fine	0.125	0.250	1	1	4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	4	4	8
<b>GRAVEL</b>	Very Fine	2.0	2.8	2	2	10
	Very Fine	2.8	4.0	4	4	14
	Fine	4.0	5.6	5	5	19
	Fine	5.6	8.0	5	5	24
	Medium	8.0	11.0	7	7	31
	Medium	11.0	16.0	10	10	41
	Coarse	16.0	22.6	9	9	50
	Coarse	22.6	32	7	7	57
	Very Coarse	32	45	8	8	65
	Very Coarse	45	64	5	5	70
<b>COBBLE</b>	Small	64	90	7	7	77
	Small	90	128	16	16	93
	Large	128	180	4	4	97
	Large	180	256	2	2	99
<b>BOULDER</b>	Small	256	362	1	1	100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 3	
Channel materials (mm)	
D <sub>16</sub> =	4.58
D <sub>35</sub> =	12.78
D <sub>50</sub> =	22.6
D <sub>84</sub> =	105.0
D <sub>95</sub> =	151.8
D <sub>100</sub> =	362.0

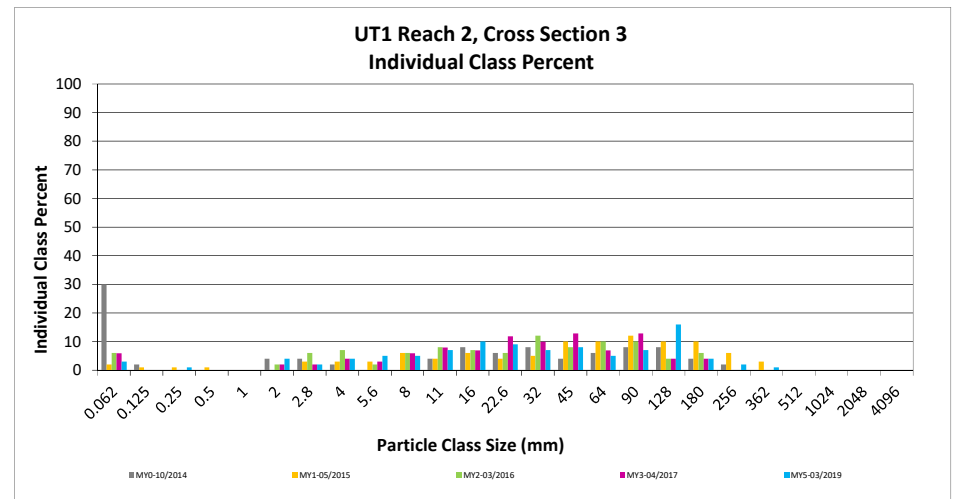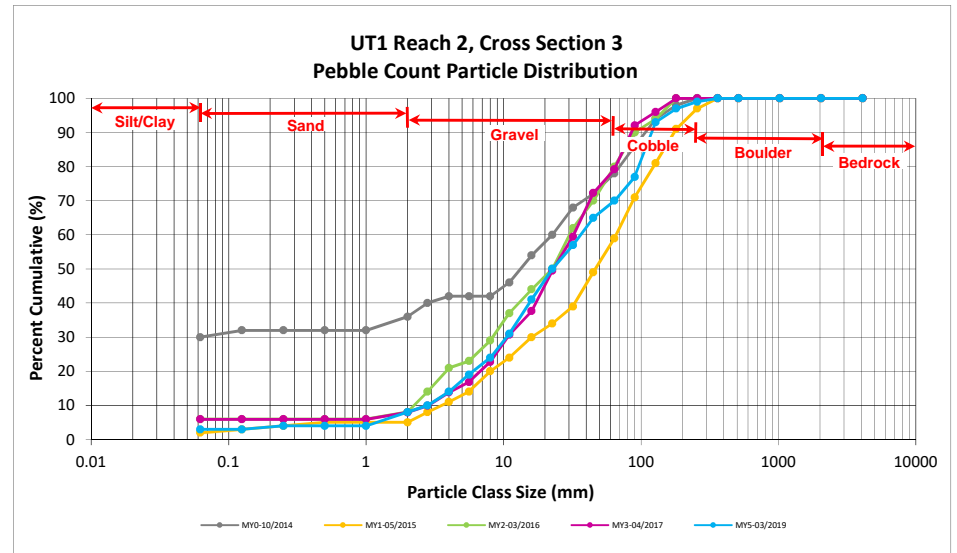

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 5, Cross Section 6

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	6	6	6
<b>SAND</b>	Very fine	0.062	0.125			6
	Fine	0.125	0.250	1	1	7
	Medium	0.25	0.50	2	2	9
	Coarse	0.5	1.0	3	3	12
	Very Coarse	1.0	2.0	12	12	24
<b>GRAVEL</b>	Very Fine	2.0	2.8			24
	Very Fine	2.8	4.0			24
	Fine	4.0	5.6	2	2	26
	Fine	5.6	8.0			26
	Medium	8.0	11.0	2	2	28
	Medium	11.0	16.0	4	4	32
	Coarse	16.0	22.6	8	8	40
	Coarse	22.6	32	8	8	48
	Very Coarse	32	45	15	15	63
	Very Coarse	45	64	7	7	70
<b>COBBLE</b>	Small	64	90	8	8	78
	Small	90	128	5	5	83
	Large	128	180	8	8	91
	Large	180	256	5	5	96
<b>BOULDER</b>	Small	256	362	2	2	98
	Small	362	512	2	2	100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 6	
Channel materials (mm)	
D <sub>16</sub> =	1.26
D <sub>35</sub> =	18.21
D <sub>50</sub> =	33.5
D <sub>84</sub> =	133.6
D <sub>95</sub> =	238.6
D <sub>100</sub> =	512.0

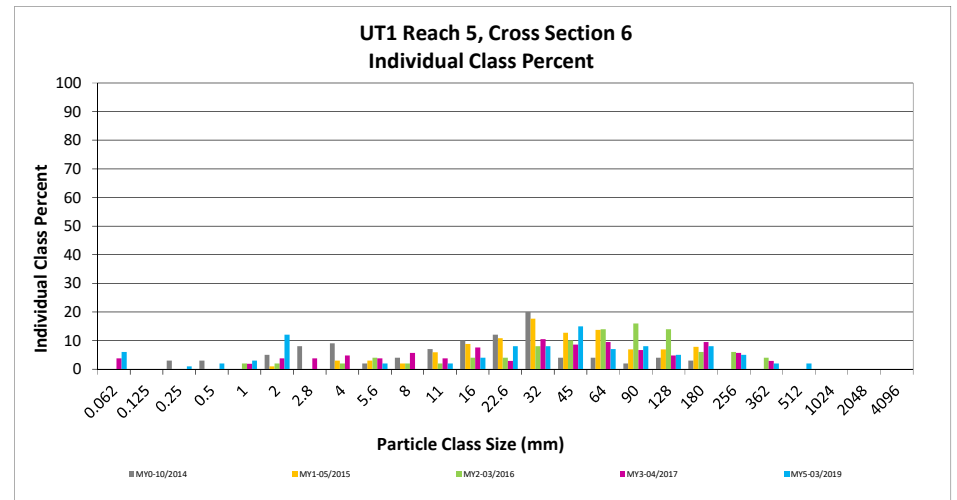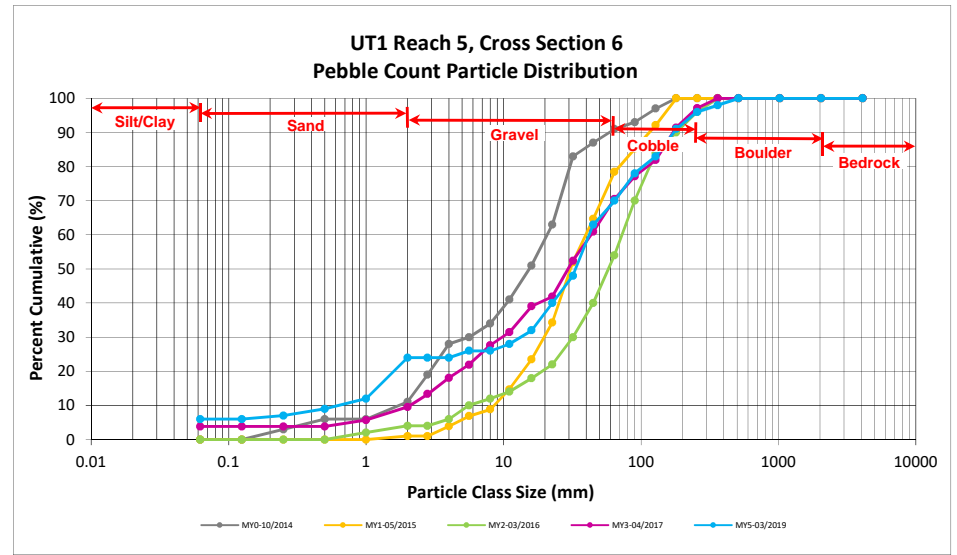

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1 Reach 5, Cross Section 7

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062			0
<b>SAND</b>	Very fine	0.062	0.125			0
	Fine	0.125	0.250			0
	Medium	0.25	0.50	1	1	1
	Coarse	0.5	1.0	1	1	2
	Very Coarse	1.0	2.0	20	20	22
<b>GRAVEL</b>	Very Fine	2.0	2.8			22
	Very Fine	2.8	4.0			22
	Fine	4.0	5.6	1	1	23
	Fine	5.6	8.0	2	2	25
	Medium	8.0	11.0	4	4	29
	Medium	11.0	16.0	8	8	37
	Coarse	16.0	22.6	3	3	40
	Coarse	22.6	32	11	11	51
	Very Coarse	32	45	9	9	60
	Very Coarse	45	64	7	7	67
<b>COBBLE</b>	Small	64	90	12	12	79
	Small	90	128	8	8	87
	Large	128	180	6	6	93
	Large	180	256	4	4	97
<b>BOULDER</b>	Small	256	362	1	1	98
	Small	362	512	1	1	99
	Medium	512	1024	1	1	100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 7	
Channel materials (mm)	
D <sub>16</sub> =	1.62
D <sub>35</sub> =	14.57
D <sub>50</sub> =	31.0
D <sub>84</sub> =	112.2
D <sub>95</sub> =	214.7
D <sub>100</sub> =	1024.0

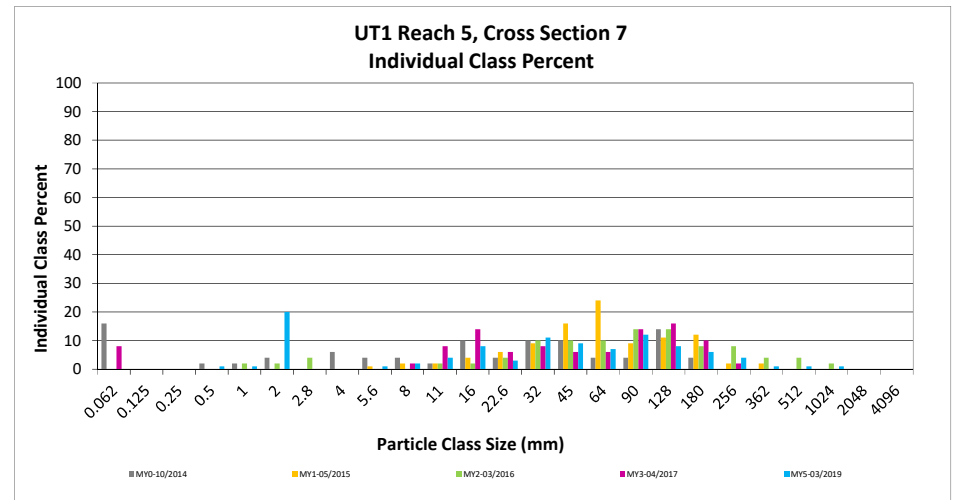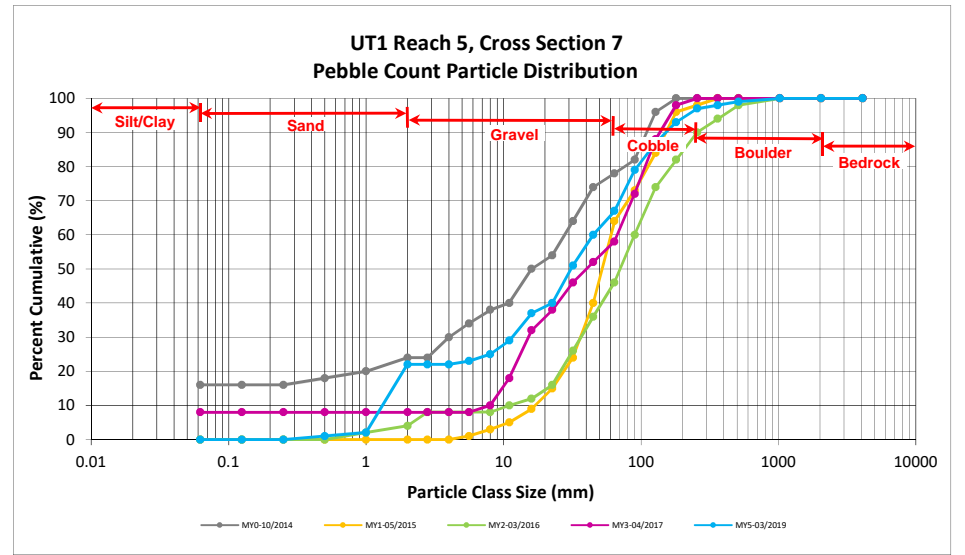

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1A Reach 1, Cross Section 9

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	8	8	8
<b>SAND</b>	Very fine	0.062	0.125			8
	Fine	0.125	0.250	1	1	9
	Medium	0.25	0.50			9
	Coarse	0.5	1.0	1	1	10
	Very Coarse	1.0	2.0	5	5	15
<b>GRAVEL</b>	Very Fine	2.0	2.8			15
	Very Fine	2.8	4.0	1	1	16
	Fine	4.0	5.6	3	3	19
	Fine	5.6	8.0	5	5	24
	Medium	8.0	11.0	7	7	31
	Medium	11.0	16.0	9	9	40
	Coarse	16.0	22.6	13	13	53
	Coarse	22.6	32	12	12	65
	Very Coarse	32	45	13	13	78
	Very Coarse	45	64	11	11	89
<b>COBBLE</b>	Small	64	90	2	2	91
	Small	90	128	2	2	93
	Large	128	180	3	3	96
	Large	180	256	4	4	100
<b>BOULDER</b>	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 9	
Channel materials (mm)	
D <sub>16</sub> =	4.00
D <sub>35</sub> =	12.99
D <sub>50</sub> =	20.9
D <sub>84</sub> =	54.5
D <sub>95</sub> =	160.7
D <sub>100</sub> =	256.0

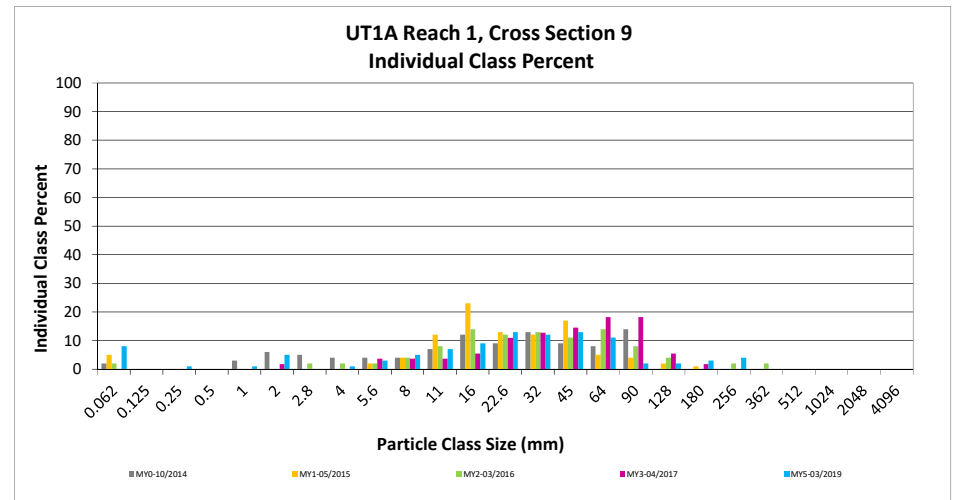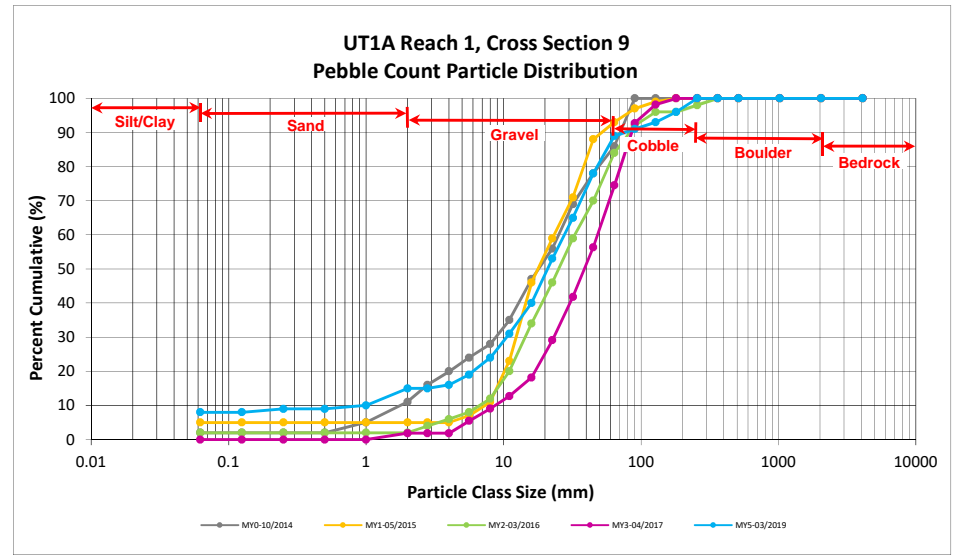

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1A Reach 4, Cross Section 11

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	9	9	9
<b>SAND</b>	Very fine	0.062	0.125			9
	Fine	0.125	0.250			9
	Medium	0.25	0.50	3	3	12
	Coarse	0.5	1.0	1	1	13
	Very Coarse	1.0	2.0	12	12	25
<b>GRAVEL</b>	Very Fine	2.0	2.8			25
	Very Fine	2.8	4.0			25
	Fine	4.0	5.6			25
	Fine	5.6	8.0	3	3	28
	Medium	8.0	11.0	4	4	32
	Medium	11.0	16.0	5	5	37
	Coarse	16.0	22.6	8	8	45
	Coarse	22.6	32	20	20	65
	Very Coarse	32	45	14	14	79
	Very Coarse	45	64	6	6	85
<b>COBBLE</b>	Small	64	90	4	4	89
	Small	90	128	5	5	94
	Large	128	180	3	3	97
	Large	180	256	2	2	99
<b>BOULDER</b>	Small	256	362			99
	Small	362	512	1	1	100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 11	
Channel materials (mm)	
D <sub>16</sub> =	1.19
D <sub>35</sub> =	13.77
D <sub>50</sub> =	24.7
D <sub>84</sub> =	60.4
D <sub>95</sub> =	143.4
D <sub>100</sub> =	512.0

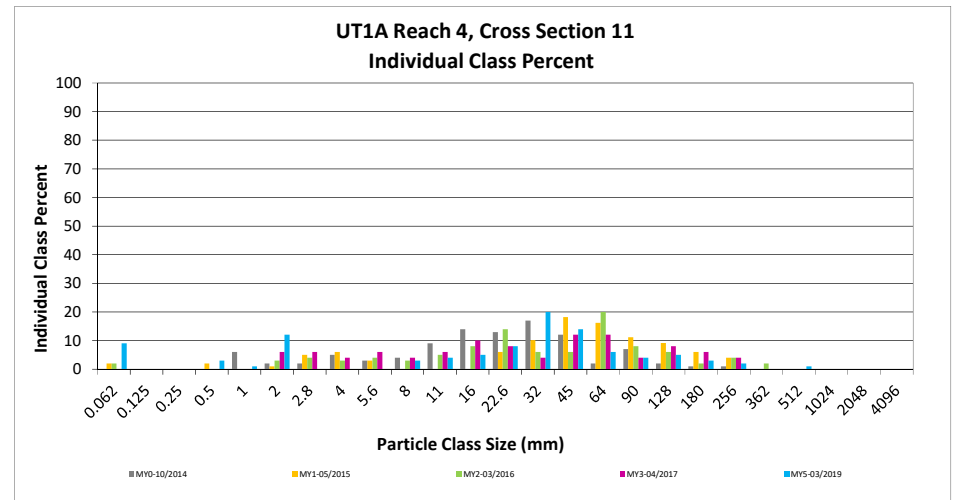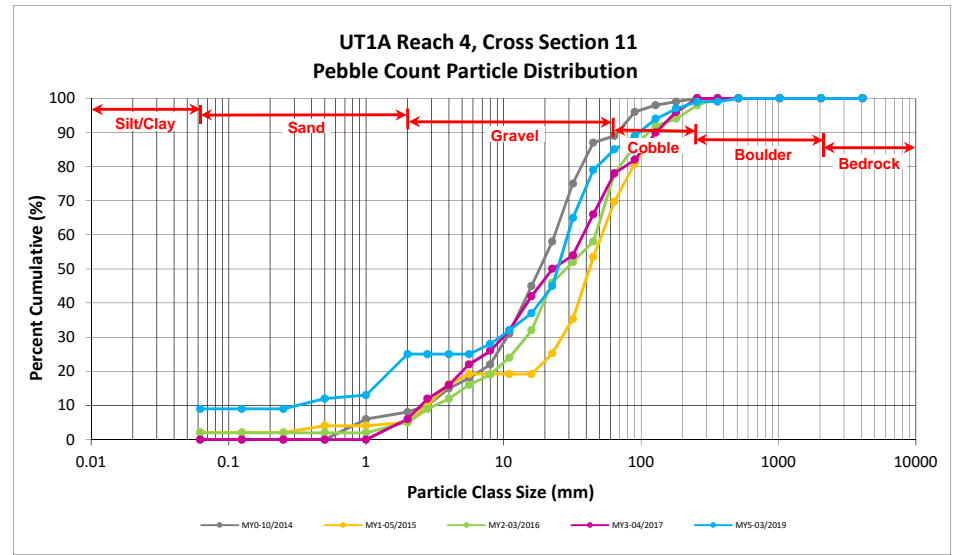

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT1B, Cross Section 13

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	4	4	4
<b>SAND</b>	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0	1	1	5
	Very Coarse	1.0	2.0	3	3	8
<b>GRAVEL</b>	Very Fine	2.0	2.8			8
	Very Fine	2.8	4.0			8
	Fine	4.0	5.6			8
	Fine	5.6	8.0	2	2	10
	Medium	8.0	11.0	2	2	12
	Medium	11.0	16.0	3	3	15
	Coarse	16.0	22.6	2	2	17
	Coarse	22.6	32	3	3	20
	Very Coarse	32	45	11	11	31
	Very Coarse	45	64	13	13	44
<b>COBBLE</b>	Small	64	90	16	16	60
	Small	90	128	23	23	83
	Large	128	180	14	14	97
	Large	180	256	2	2	99
<b>BOULDER</b>	Small	256	362	1	1	100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 13	
Channel materials (mm)	
D <sub>16</sub> =	19.02
D <sub>35</sub> =	50.15
D <sub>50</sub> =	72.7
D <sub>84</sub> =	131.2
D <sub>95</sub> =	171.4
D <sub>100</sub> =	362.0

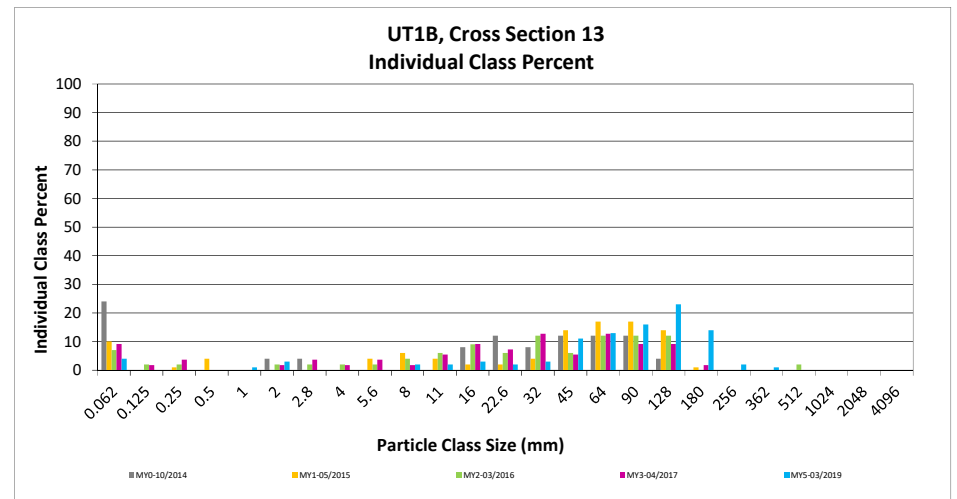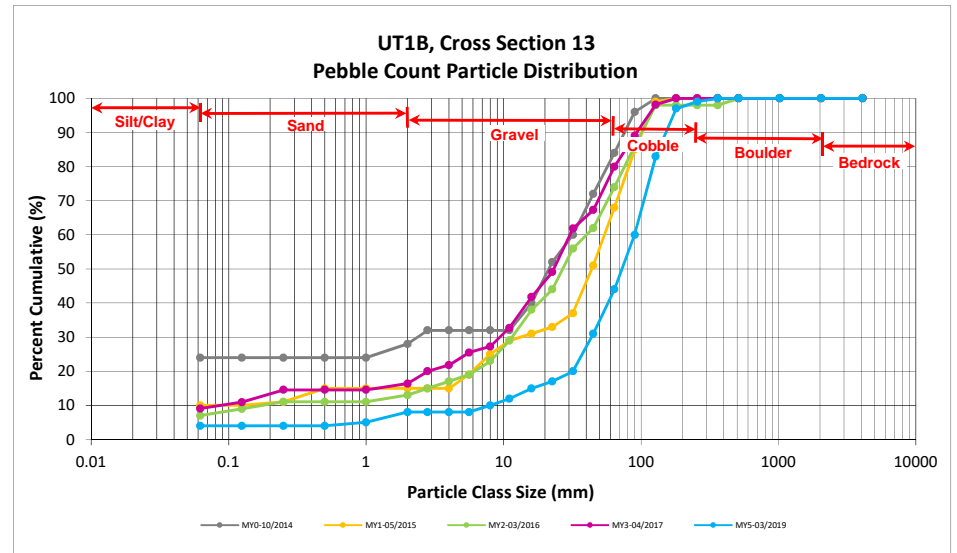

**Reachwide and Cross Section Pebble Count Plots**



Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

UT2, Cross Section 15

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
<i>SILT/CLAY</i>	Silt/Clay	0.000	0.062	1	1	1
<b>SAND</b>	Very fine	0.062	0.125			1
	Fine	0.125	0.250			1
	Medium	0.25	0.50	1	1	2
	Coarse	0.5	1.0	10	10	12
	Very Coarse	1.0	2.0			12
<b>GRAVEL</b>	Very Fine	2.0	2.8			12
	Very Fine	2.8	4.0			12
	Fine	4.0	5.6	3	3	15
	Fine	5.6	8.0	4	4	19
	Medium	8.0	11.0	6	6	25
	Medium	11.0	16.0	8	8	33
	Coarse	16.0	22.6	10	10	43
	Coarse	22.6	32	9	9	52
	Very Coarse	32	45	15	15	67
	Very Coarse	45	64	13	13	80
<b>COBBLE</b>	Small	64	90	12	12	92
	Small	90	128	8	8	100
	Large	128	180			100
	Large	180	256			100
<b>BOULDER</b>	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
	Large/Very Large	1024	2048			100
<b>BEDROCK</b>	Bedrock	2048	>2048			100
<b>Total</b>				<b>100</b>	<b>100</b>	<b>100</b>

Cross Section 15	
Channel materials (mm)	
D <sub>16</sub> =	6.12
D <sub>35</sub> =	17.14
D <sub>50</sub> =	29.6
D <sub>84</sub> =	71.7
D <sub>95</sub> =	102.7
D <sub>100</sub> =	128.0

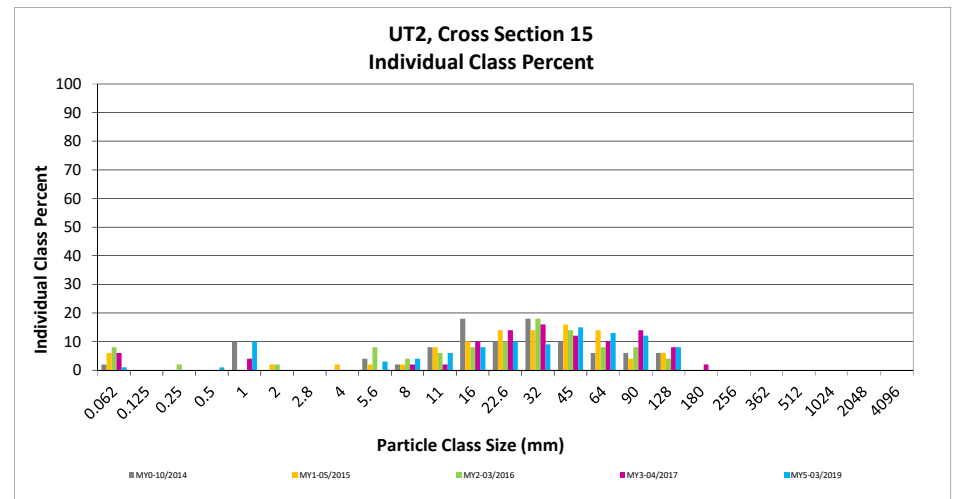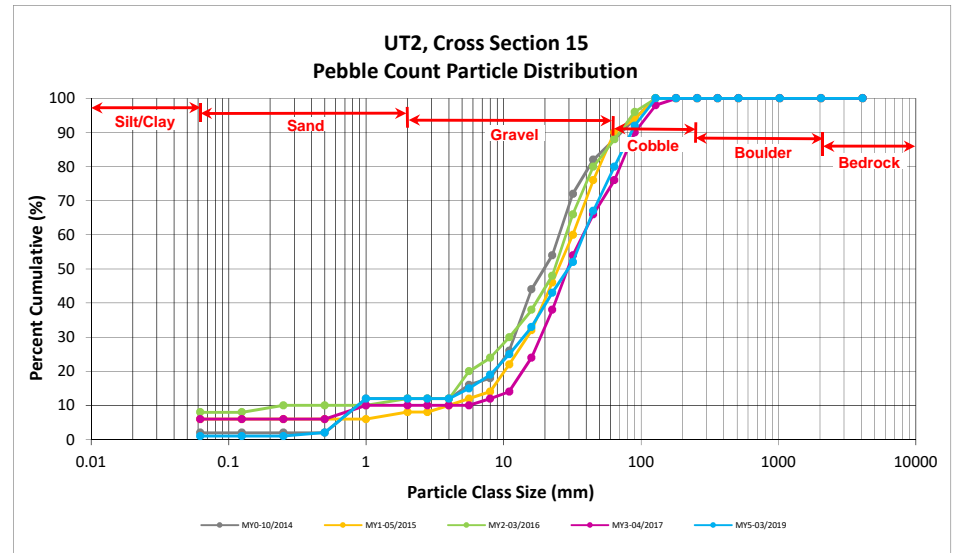



## **APPENDIX 5. Hydrology Summary Data and Plots**

**Table 13. Verification of Bankfull Events**

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

Reach	Date of Data Collection	Date of Occurrence	Method
UT1	2/6/2019	1/21/2019	Crest Gage/ Pressure Transducer
		1/24/2019	
		2/1/2019	
	6/27/2019	2/18/2019	
		2/23/2019	
		3/1/2019	
		3/7/2019	
		3/21/2019	
6/27/2019	4/19/2019		
	2/6/2019	1/21/2019	
	6/27/2019	1/24/2019	
		2/18/2019	
		2/23/2019	
UT1A	2/6/2019	3/1/2019	
		3/21/2019	
		4/19/2019	
	6/27/2019	1/4/2019	
		1/13/2019	
		1/20/2019	
		1/24/2019	
2/18/2019			
UT1B	2/6/2019	2/23/2019	
		3/1/2019	
		3/21/2019	
	6/27/2019	4/19/2019	
		1/21/2019	
		1/24/2019	
		2/18/2019	
UT2	2/6/2019	2/23/2019	
		6/8/2019	
	6/27/2019	8/1/2019	
		10/29/2019	

**Monthly Rainfall Data**

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

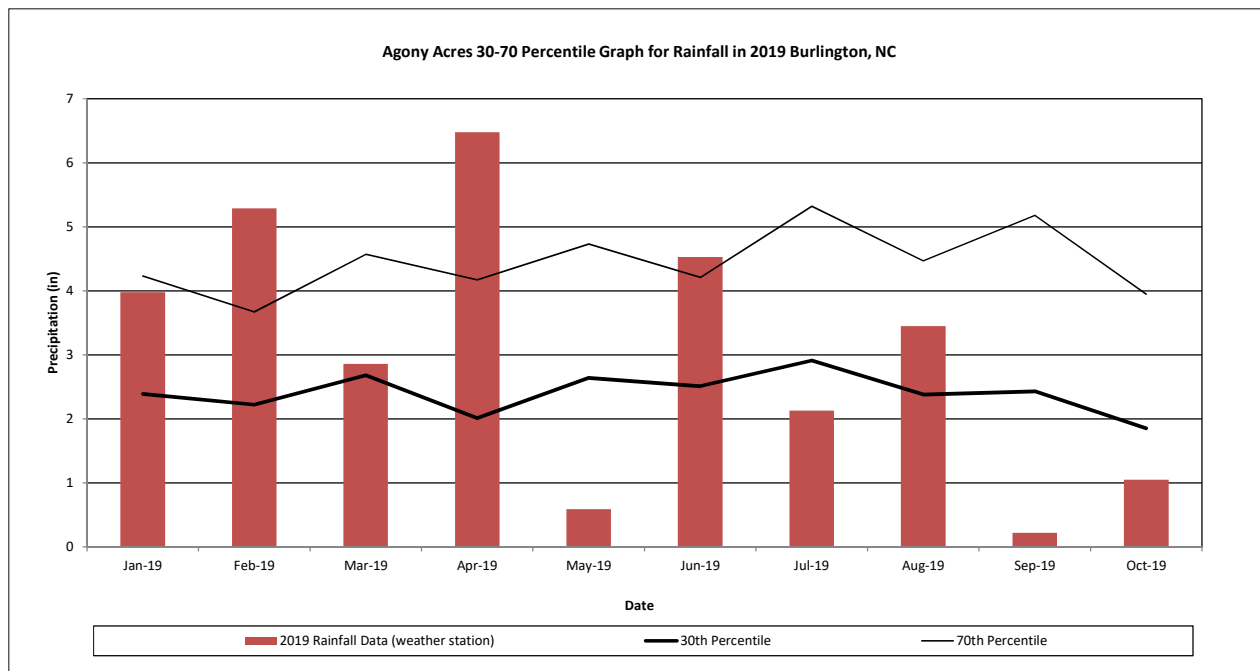


<sup>1</sup> 2019 monthly rainfall collected from weather station 93783, at Burlington Alamance Regional AP, NC (USDA, 2002).

<sup>2</sup> 30th and 70th percentile rainfall data collected from weather station NC723, at Piedmont Tiad Intl AP, NC (USDA, 2002).

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

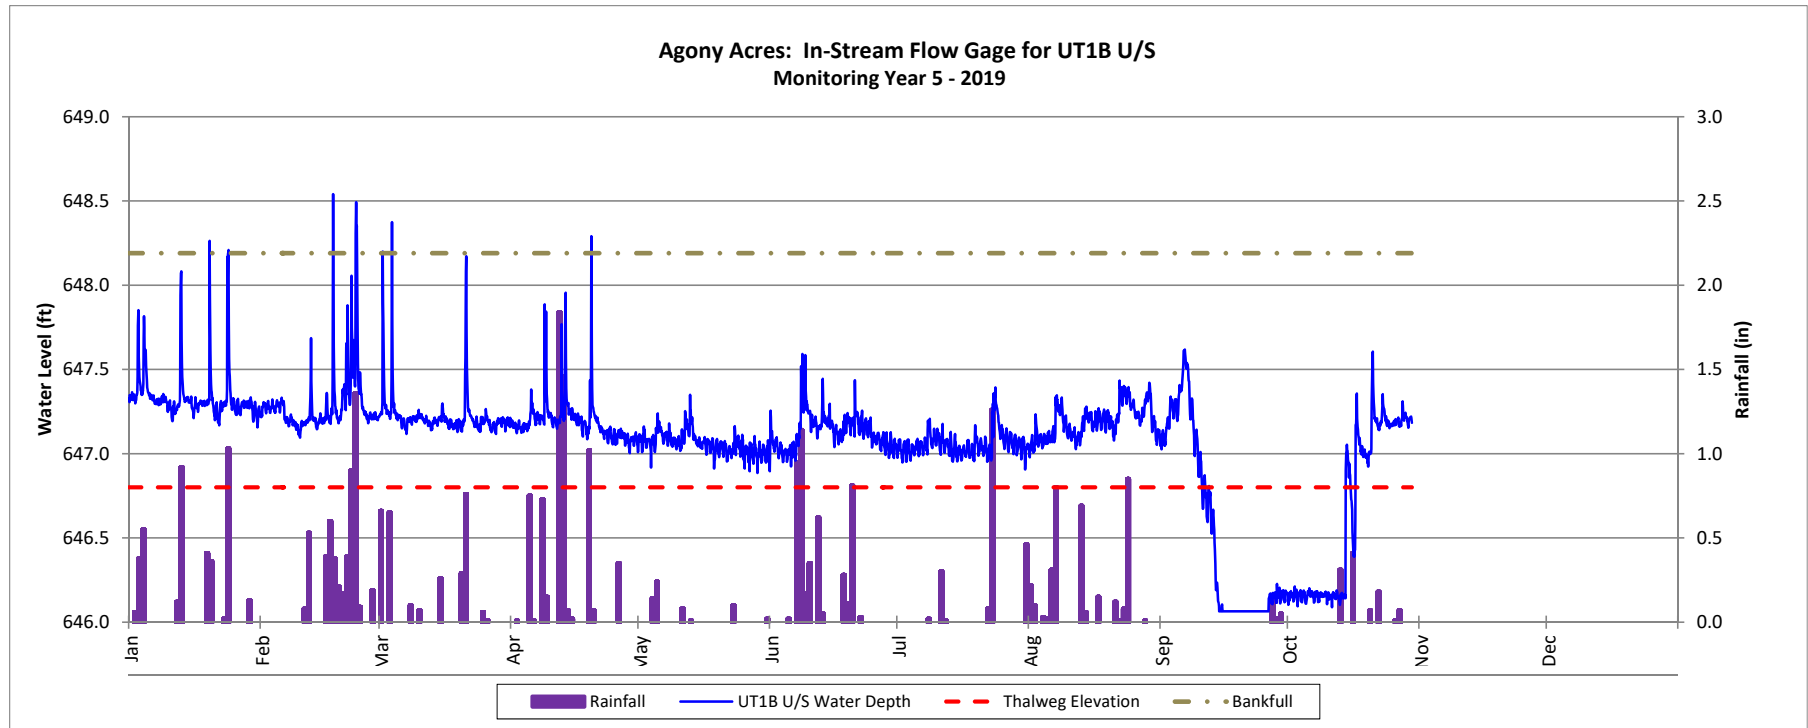

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

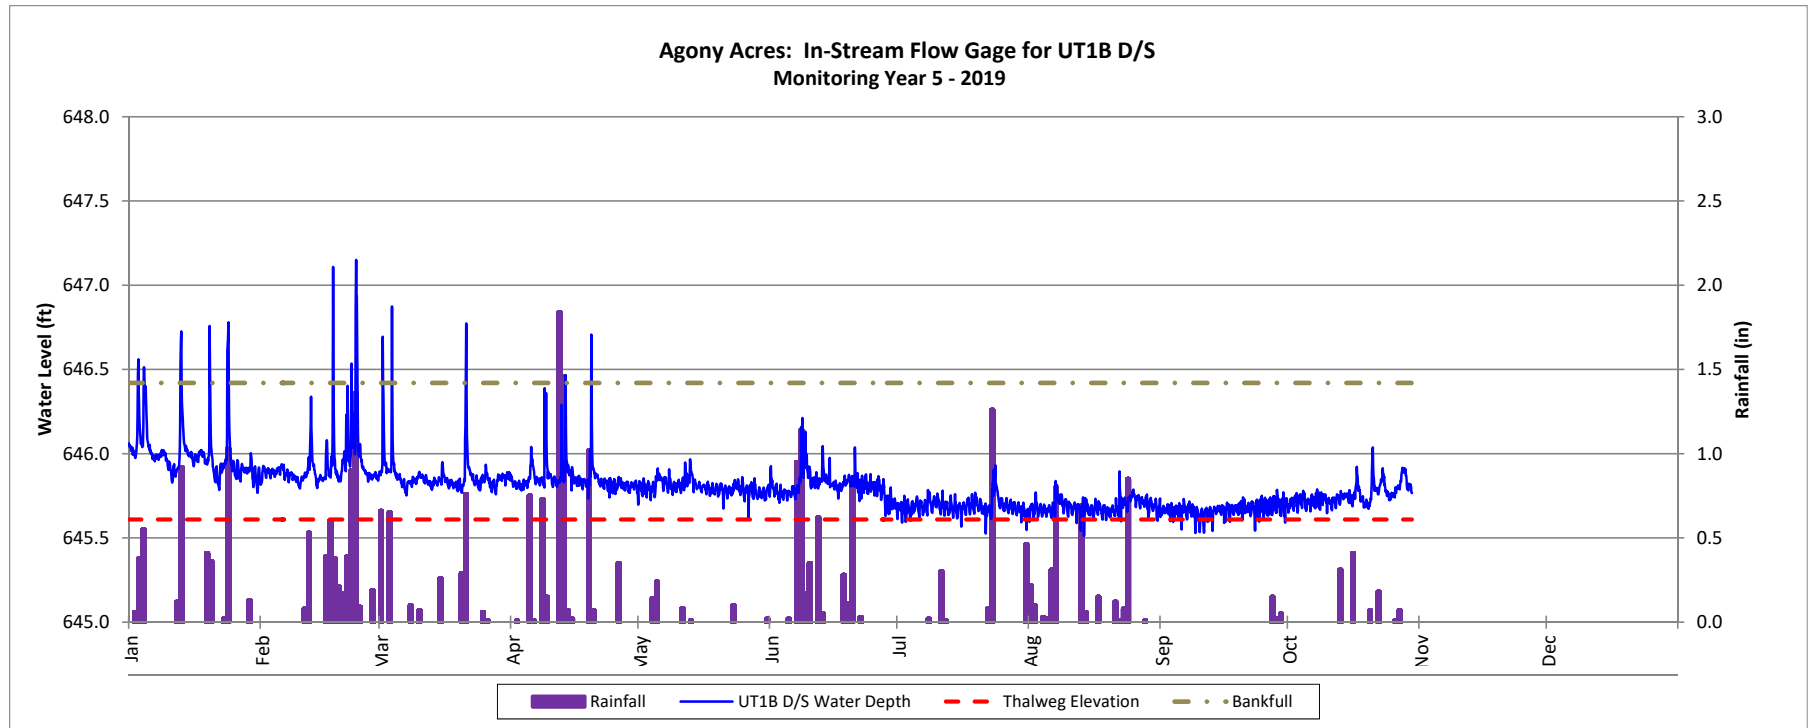

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

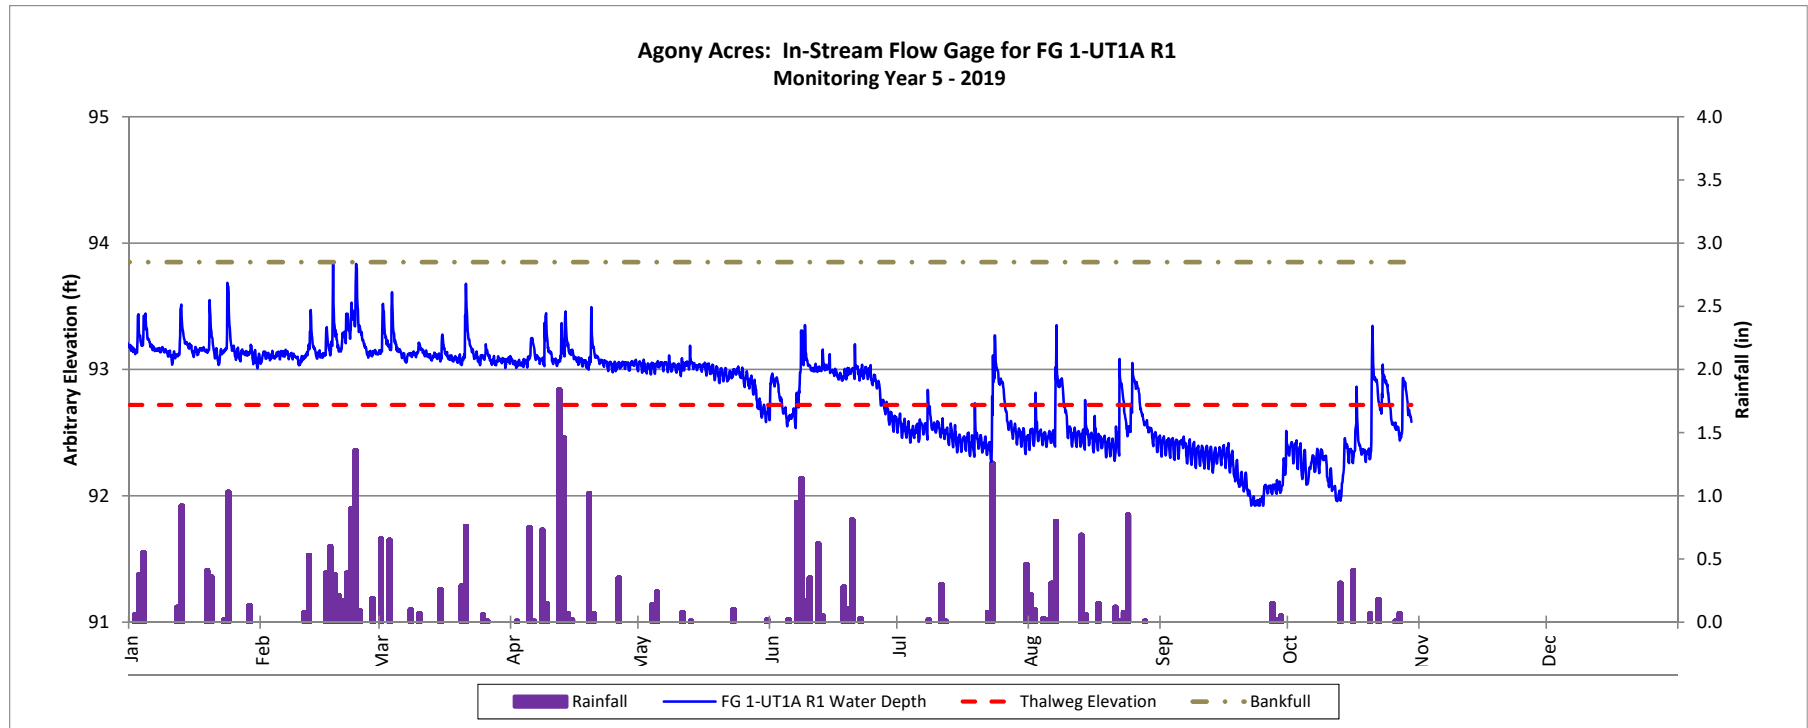

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

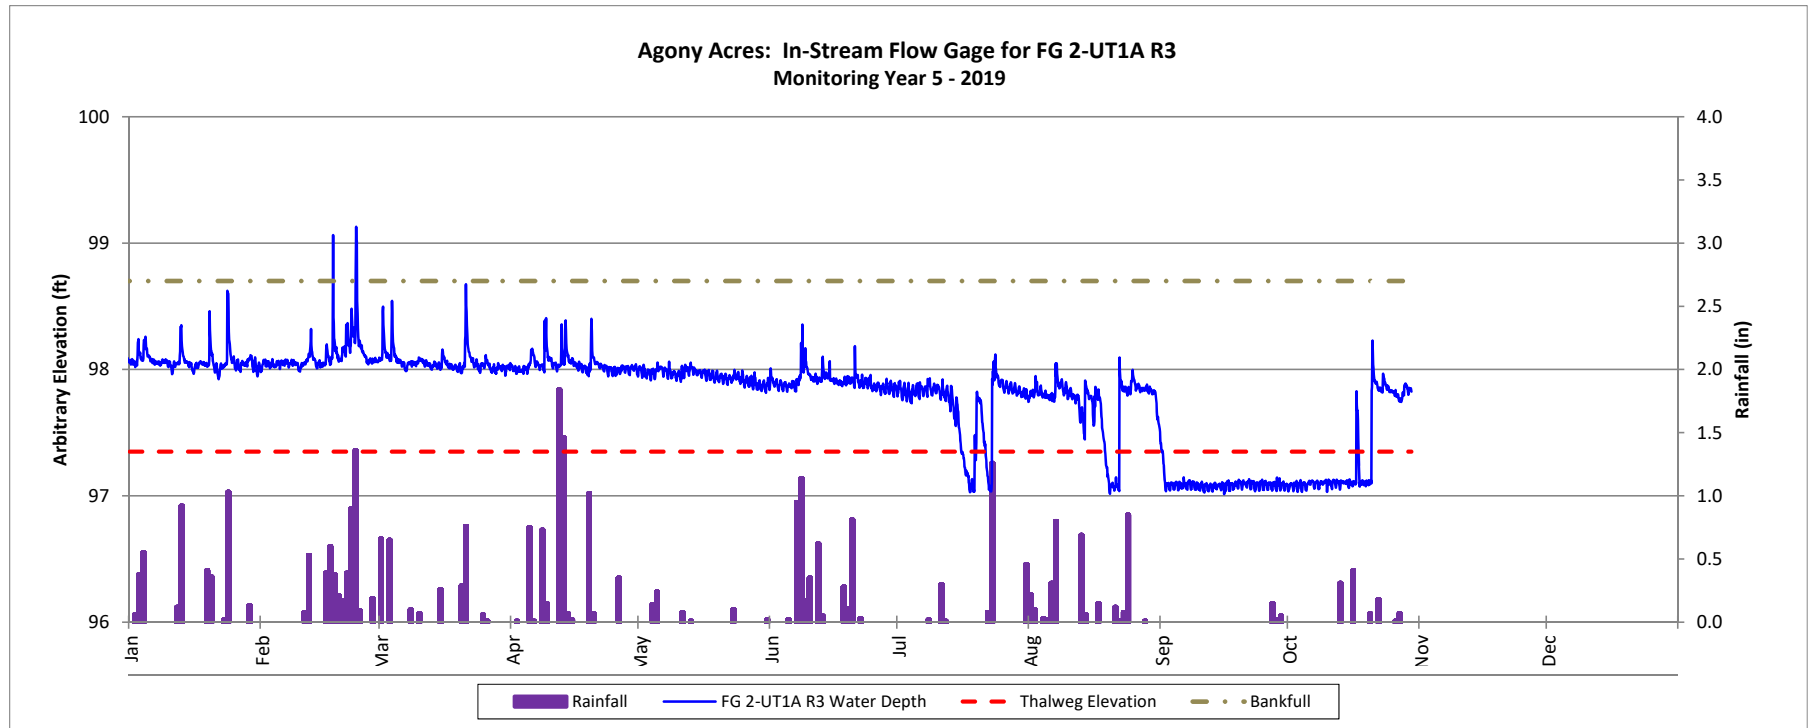

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)


Monitoring Year 5 - 2019

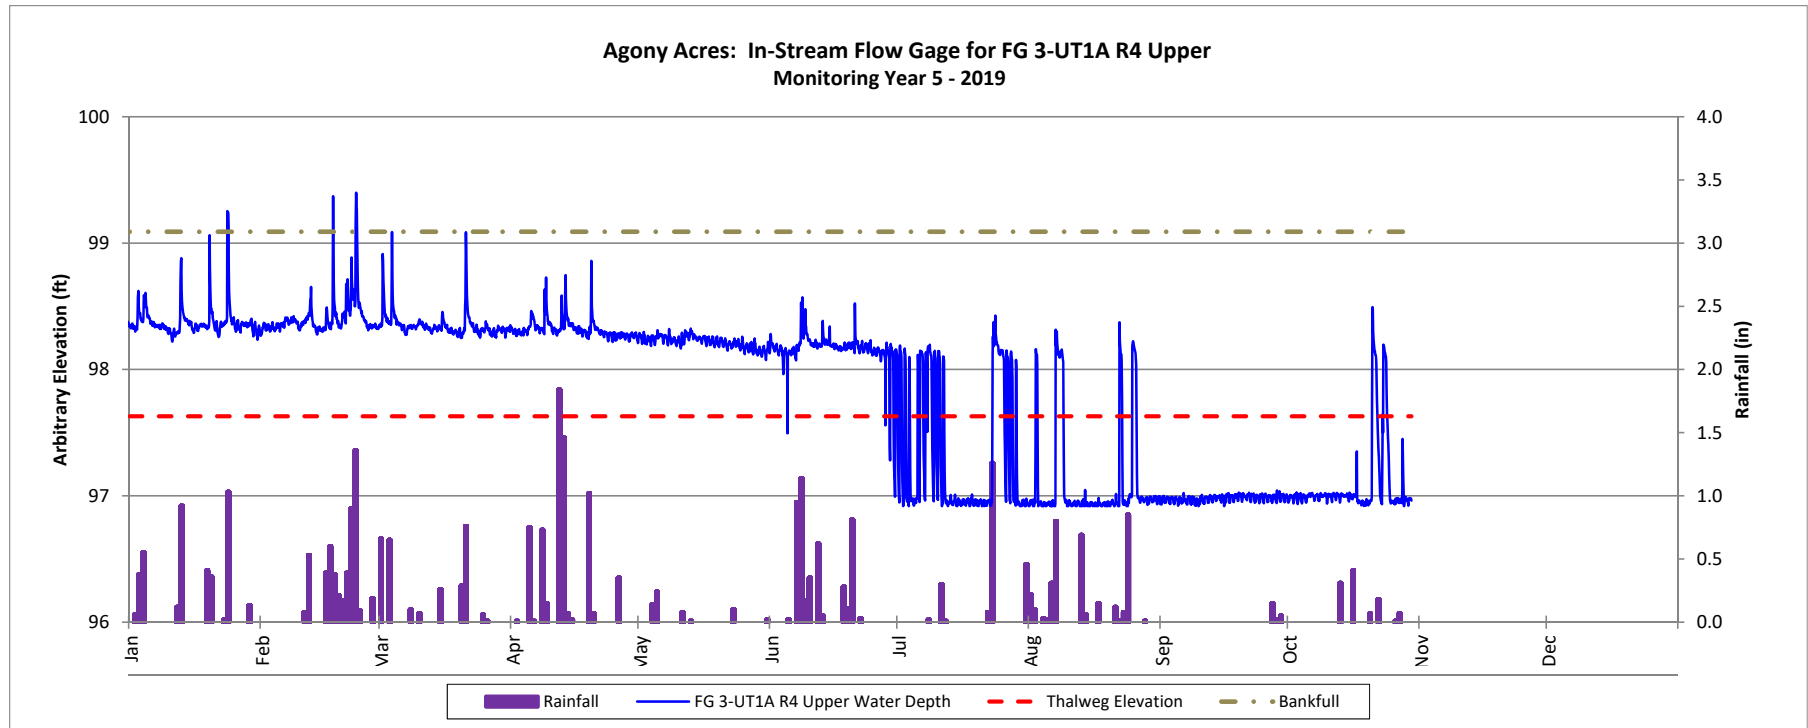

### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

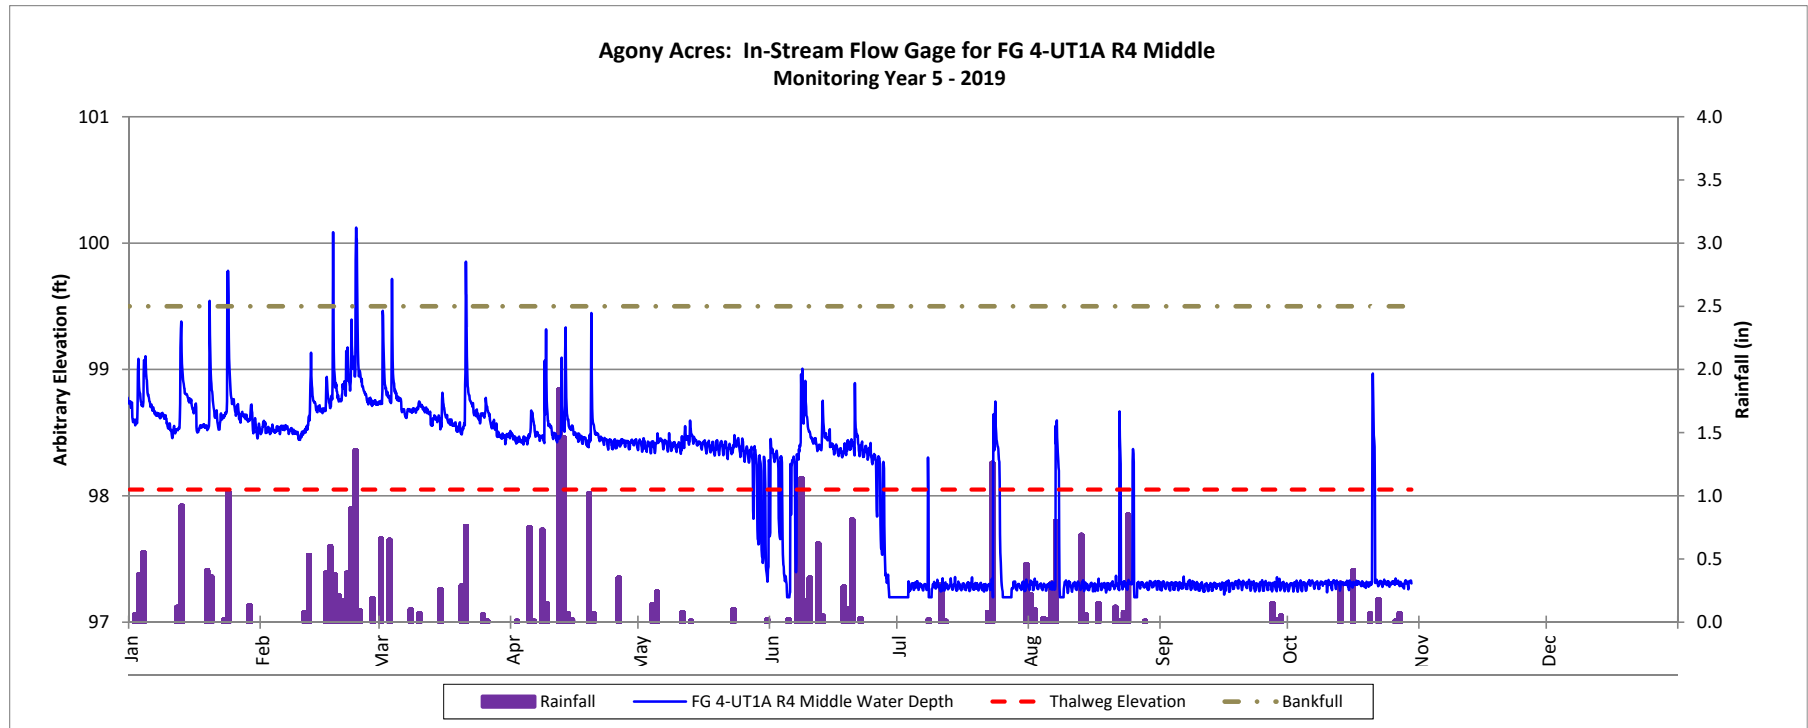



### Recorded In-Stream Flow Events

Agony Acres Mitigation Site (DMS Project No. 95716)

Monitoring Year 5 - 2019

