

**BEST STREAM AND WETLAND RESTORATION PROJECT  
MONITORING REPORT  
MONITORING YEAR 3  
FINAL**

DUPLIN COUNTY, NORTH CAROLINA  
CONTRACT No. 004631 - PROJECT No. 95353  
USACE Action ID No. 2012-01384 -NCDWR Project No. 13-0865



Prepared for:

**Division of Mitigation Services**

North Carolina Department of Environment and Natural Resources  
1652 Mail Service Center  
Raleigh, NC 27699-1652

February 2018



302 Jefferson Street, Suite 110  
Raleigh, NC 27605

**Corporate Headquarters**  
5020 Montrose Blvd. Suite 650  
Houston, TX 77006  
Main: 713.520.5400

February 8, 2018

Jeff Schaffer  
NC DEQ Division of Mitigation Services  
217 West Jones Street  
Raleigh, NC 27604

RE: Best Stream and Wetland Restoration Site: MY3 Monitoring Report (NCDMS ID 95353)

Listed below are comments provided by DMS on January 31, 2018 regarding the Best Stream and Wetland Restoration Site: Year 3 Monitoring Report and RES' responses.

At the 2016 IRT credit release, this project was released as proposed with the following notes: "Credit modification request under review (by IRT). Adjust as needed at the 2017 credit release. Explain in detail differences in stream footage from Mitigation Plan to As-Built. Were there changes to this easement?"

- a. Has RES submitted asset revisions to and received approval from the IRT?  
[No. RES does not plan on submitting an asset revision and will revert to the Approved Mitigation Plan assets.](#)
- b. If no, please provide response to these questions in the Monitoring report and be prepared to discuss at the upcoming Credit Release meeting is April 2108.

Digital drawings: Label components and problem areas as required by contract and stated in DMS's Format, Data Requirements, and Content Guidance for Electronic Drawings Submitted to EEP version 1.0 (03/27/08).

[Shapefiles have been cleaned up and updated in Support Files. The MY3 CCPV Condition shapefile contains vegetation problem areas only as the stream problem areas were marked with callouts on the maps.](#)

Add the USACE Action ID number (2012-01384) and NCDWR Project number (13-0865) to the cover page.

[Done.](#)

Executive Summary, page iii: Explain why gauges AW8 and AW9 failed to collect data for the first half of the growing season and whether these gauges have been repaired.

[Done.](#)

Executive Summary, table on page iv:

- a. Reach designations are not correct. Change as follows: UT5 Enhancement I to UT6; UT6 SP & BE to UT7; UT7 Enhancement I to UT8; UT8 SP & BE to UT9; UT9 SP & BE to UT10; and UT 10 SP & BE to Muddy Creek.



b. Based on the approved mitigation plan and DMS calculations the proposed SMU's should be 10,213 (10,212.87) not 10,216. Please correct.

c. Based on DMS calculations, Baseline SMUs are 10,178 (10,177.87) not 10,180. Please correct.

d. Based on the approved mitigation plan. The proposed WMUs for W2 are 0.29. Please correct.

Based on the approved mitigation plan and DMS calculations the total proposed WMUs are 5.12. Please correct.

All of the above has been corrected.

Section 1.3, Table 1a: Based on DMS calculations, the total SMUs are 10,178 (10,177.87). It appears that there is a rounding error to get the 10,180 total shown.

Done.

Section 2.2, page 12: RES refers to the Sampson County growing season when this project is in Duplin County. Please correct.

The Sampson County WETs table was used because Duplin County did not have one at the time of the Baseline Report.

Section 4.2: Again, explain why gauges AW8 and AW9 failed to collect data during 48 days of the growing season and whether these gauges have been repaired.

Done.

Section 4.3:

- a. VPA 1, 4 and 6 – state what RES plans to do to address low stem density in these areas.

RES will supplemental plant these areas in early 2018.

- b. VPA 5, 7 and 10 – state if RES has address the encroachment/over spraying with the landowner and what if any action is needed to address woody stem mortality in these areas.

RES will communicate with landowners and install additional easement marker in these areas. Woody stem mortality will be assessed in MY4 and supplemental plantings will be performed if necessary.

Section 5.1.4: Please clearly state whether this site has met the required bankfull standard.

Crest Gauges 1,2,3,5, and 6 have met the required bankfull standard. According to the Mitigation Plan and the Baseline Report the success criteria for Crest Gauge 4, located on a headwater valley restoration reach, is to document seasonal or intermittent flow. In more recent guidance this has been determined to be 30 days of continuous flow. Flow days for Crest Gauge 4 will be reported in MY4 and previous years will be recalculated and reported. This has been updated in the report.

Appendix A, Table 1:

- a. In the Mitigation Credits section at the top of Table 1, Stream R credits are comprised of Restoration, Enhancement I and Enhancement II approaches while Stream RE credits are comprised of Preservation. Please make the following changes:

(1) Change Stream R from 5,023 to 6,217 (6,216.47)

(2) Change Stream RE from 5,157 to 3,961 (3,961.40)

- b. Project Component Section: change R/RE designations for each reach based on 10.a. above

All of the above has been completed.



Appendix D, Table 11: DMS realizes that there are various methods used to calculate Bank Height Ratio from year to year. One of these is to hold the bankfull depth static (denominator) while allowing the Low Top of Bank max depth (numerator) to vary. Another method that has been proposed and is being evaluated is to hold the As-built cross-sectional area static within each year's new cross-section and allow that to determine the max bankfull depth for each year. However, if there are large changes in the W/D ratio either method can make for somewhat distorted BHR values depending upon the direction and magnitude of the change in the W/D ratio. Please update the calculations to reflect changes observed in the overlays and explain in detail as footnote with the tables that describes the method by which RES is calculating Bank Height Ratio and Entrenchment Ratio. In addition, please provide context to any observed changes in these calculated ratios in the report narrative. RES must be prepared to defend the method used for credit release and justify through context whether or not any changes observed in a cross section represent an issue.

BHR was calculated on riffles using the baseline bankfull elevation. This method was used because the dimension of the channels has not changed enough to alter the bankfull elevation. None of the restoration riffle cross sections exceeded a 1.2 BHR. Two cross sections on Enhancement I reaches did exceed 1.2 but both have baseline bankfull elevations below top of bank. This has been added to the report and as a footnote to Table 11.

Appendix E, Table 15b: This table shows that AW7 failed to meet success of 9% for MY2 and MY3 after meeting in MY1. Please explain in report narrative, possibly Section 4.2, the reason for not meeting the past two years. This could lead to these credits being at risk.

AW7 is located in Marvyn and Gritney soils. Marvyn and Gritney are typically upland soils that are well drained. Gritney, however, is in the same Taxonomic Subgroup as Helena which according to the IRT's Wetland Saturation Threshold Table has a wetland hydroperiod range of 6-8% of the growing season. This means that AW7 was in or above the wetland hydroperiod range in MY1 and MY2 and only missed the range by one day in MY3. This has been added to Section 4.2.

**Best  
Duplin County, North Carolina  
DMS Project ID 95353**

**Cape Fear River Basin  
HUC 03030007060010**

**Prepared by:**



**Resource Environmental Solutions, LLC  
302 Jefferson Street, Suite 110  
Raleigh, NC 27605  
919-209-1061**

## **EXECUTIVE SUMMARY**

The Best Site Stream & Wetland Mitigation Project is located within an agricultural watershed in Duplin County, North Carolina, approximately two miles east of Beulaville. The project streams were significantly impacted by channelization and agricultural practices. The project involved the restoration and protection of streams and wetlands in the Muddy Creek watershed. The purpose of this restoration project is to restore and enhance a stream/wetland complex located within the Cape Fear River Basin.

The project lies within USGS Hydrologic Unit Code 03030007060010 (USGS, 1998) and within the North Carolina Division of Water Quality (NCDWQ) Cape Fear River Sub-basin 03-06-22 (NCDENR, 2005). The 2009 Cape Fear River Basin Plan identified HUC 03030007060010 as a Targeted Local Watershed. The watershed is characterized by 52 percent agricultural land use area with Muddy Creek identified as Impaired for aquatic life because of a Fair benthic community rating. The plan listed water quality and animal operations as major stressors within this TLW, and the planning goals include identifying restoration and stormwater BMP needs.

The Best stream and wetland mitigation project is located within the northern (upstream) portion of the TLW and includes sections of Muddy Creek (303d listed) and headwater streams that discharge into Muddy Creek. The stream and wetland restoration and enhancement activities on this project will provide numerous ecological and water quality benefits within the Cape Fear River Basin. These benefits will address the degraded water quality and nutrient inputs from agriculture that were identified as major watershed stressors in the 2009 Cape Fear River Basin Plan.

The Best Site consists of stream and wetland restoration on tributaries that are located directly adjacent to Muddy Creek and includes 19,807 linear feet of Stream Preservation and Buffer Enhancement along Muddy Creek and its tributaries. Stream restoration has been completed for two tributaries, headwater valley restoration along a portion of one tributary, stream enhancement along three tributaries, and stream preservation and buffer enhancement for the remaining streams.

This Year 3 Annual Monitoring Report presents the data from 23 vegetation monitoring plots, six manual crest gauges, six auto crest gauges, an auto-logging rain gauge, nine wetland restoration groundwater gauges, three reference groundwater gauges, 31 stream cross sections, eight sets of bank pins, and photo reference locations, as required by the approved Mitigation Plan for the site.

The Best Year 3 Monitoring activities were completed in November 2017. All Year 3 monitoring data is presented below and in the appendices. Data presented shows the site has a few localized areas of bank erosion and relic channel floodplain erosion on UT2 and UT4. Most vegetation plots (87%) are above the year 3 success criteria. The site is on track to meeting stream, wetland and vegetation interim success criteria.

Throughout the Year 3 monitoring season, the restoration and enhancement reaches remained stable and continued to provide the intended habitat and hydrologic functions. Minimal changes were noted for Year 3 cross section surveys resulting from stable bed and bank conditions. Five of six crest gauges recorded bankfull events during the Year 3 monitoring period. Four stream problem areas were noted during the Year 3 monitoring period. Minor bank erosion on UT2, UT4 exhibited floodplain erosion associated with the relic channel from overland flows. Easement fencing was damaged along UT3 by a fallen tree and will be fixed in late 2017 or early 2018. No cattle are accessing the easement area. The problem areas are addressed below in the report detailing the severity and repair recommendations.

Six of the nine wetland restoration gauges achieved the success criteria by remaining continuously within the 12 inches of the soil surface for at least nine percent of the growing season. The three remaining wetland restoration gauges nearly achieved success with 13, 16, and 14 days (5%, 7%, and 6%, respectively) consecutively within 12 inches of the soil surface. Gauges AW8 and AW9 (7% and 6%), were stolen therefore failed to collect data in the first half of the growing season. These gauges have been replaced and are now collecting data. Groundwater gauge data indicate the hydroperiods being very responsive to rainfall events. The Best Site wetland restoration areas are performing as designed and are on track to meeting wetland success criteria.

The Year 3 vegetation observations are summarized in this report. Planted-stem survival for 20 out of 23 Vegetation Plots (VP) at the Best Site were above the interim success criterion of 320 trees per acre at the end of Monitoring Year 3. The average stem density (excluding live stakes) across all vegetation plots was 765 stems per acre. Sweetgum (*Liquidambar styraciflua*), Baccharis (*Baccharis halimifolia*), Black Cherry (*Prunus serotina*), Loblolly Pine (*Pinus taeda*), Red Maple (*Acer rubrum*), Winged Sumac (*Rhus copallinum*), Persimmon (*Diospyros virginiana*), and Tuliptree (*Liriodendron tulipifera*) volunteers were noted in a few vegetation plots on the site. Ten vegetation problems were noted during the Year 3 monitoring period. Four areas consisted of low stem density areas along UT1, UT3, and UT4; two areas consisted of poor growth/vigor areas along UT1 and UT2; one invasive species area along UT1; and three small areas of encroachment along UT2 and UT8.

Following 2016 monitoring the NCIRT requested a review of the differential between the Approved Mitigation Plan and Baseline Monitoring Report. The table below details the discrepancies by reach. UT1 is the only significant change and the cause of increased baseline SMUs is survey methodology (thalweg vs. centerline). The Mitigation Plan lengths were based on centerline. UT8 credits decreased due to a construction phase decision to transition from Enhancement I to Buffer Enhancement at a point above what was designed. Other minor discrepancies in channel length are due to survey adjustments and modifications to treatment break points. Wetland restoration areas W1 and W2 increased from 3.66 to 3.77 and 0.29 to 0.31, respectively, from Mitigation Plan to As-Built. This increase was caused by an inconsistency between GIS, CAD, and survey data. RES does not plan on submitting an asset revision and will revert to the Approved Mitigation Plan assets. Stream and wetland credits are detailed in the table below. The 147.7-acre easement area did not change from Mitigation Plan to Baseline Monitoring.

Reach	Mitigation Type*	Proposed Length (LF)	Mitigation Ratio	Proposed SMUs	Baseline SMUs
UT1	P1 Restoration	1,723	1:1	1,723	1,757
UT1	SP & BE	303	1:5	61	56
UT2	P1 Restoration	2,770	1:1	2,770	2,772
UT2	SP & BE	309	1:5	62	66
UT3	Enhancement II	812	1:2.5	325	325
UT3	SP & BE	64	1:5	13	13
UT4	HV Restoration	510	1:1	510	494
UT4	SP & BE	655	1:5	131	129
UT5	SP & BE	4,043	1:5	809	809
UT6	Enhancement I	538	1:1.5	359	359
UT7	SP & BE	3,183	1:5	637	637
UT8	Enhancement I	825	1:1.5	550	510
UT8	SP & BE	313	1:5	63	63
UT9	SP & BE	1,171	1:5	234	221
UT10	SP & BE	768	1:5	154	154
<b>Muddy Creek</b>	SP & BE	9,073	1:5	1,815	1,815
<b>Total</b>		<b>27,060</b>		<b>10,213</b>	<b>10,178</b>

\*P1=Priority 1, SP & BE= Stream Preservation and Buffer Enhancement, HV= Headwater Valley  
 \*\*The contracted amount of credits for this Site is 10,133 SMUs

Wetland	Mitigation Type	Mitigation Area (ac)	Mitigation Ratio	Proposed WMUs	Baseline WMUs
W1	Restoration	3.66	1:1	3.66	3.77
W2	Restoration	0.29	1:1	0.29	0.31
W3A	Restoration	0.58	1:1	0.58	0.58
W3B	Restoration	0.59	1:1	0.59	0.59
<b>Total</b>		<b>5.12</b>		<b>5.12</b>	<b>5.25</b>

\*The contracted amount of credits for this Site is 4.40 WMUs



## TABLE OF CONTENTS

1	PROJECT GOALS, BACKGROUND AND ATTRIBUTES.....	3
1.1	Location and Setting.....	3
1.2	Project Goals and Objectives.....	3
1.3	Project Structure .....	5
1.3.1	Restoration Type and Approach.....	5
1.4	Project History, Contacts and Attribute Data .....	11
1.4.1	Project History.....	11
1.4.2	Project Watersheds .....	11
2	Success Criteria .....	11
2.1	Stream Restoration .....	11
2.1.1	Bankfull Events .....	11
2.1.2	Cross Sections .....	12
2.1.3	Bank Pin Arrays .....	12
2.1.4	Digital Image Stations .....	12
2.2	Wetland Restoration.....	12
2.3	Vegetation Success Criteria.....	13
2.4	Scheduling/Reporting.....	13
3	MONITORING PLAN.....	13
3.1	Stream Restoration .....	13
3.1.1	As-Built Survey.....	13
3.1.2	Bankfull Events .....	13
3.1.3	Cross Sections .....	14
3.1.4	Digital Image Stations .....	14
3.1.5	Bank Pin Arrays .....	14
3.1.6	Visual Assessment Monitoring.....	14
3.1.7	Surface Flow.....	14
3.2	Wetland Hydrology .....	15
3.3	Vegetation .....	15
4	Maintenance and Contingency plan .....	15
4.1	Stream.....	15
4.2	Wetlands.....	15
4.3	Vegetation .....	16
5	Year 2 Monitoring Conditions (MY2) .....	17
5.1	Year 2 Monitoring Data Collection.....	17
5.1.1	Morphological State of the Channel.....	17
5.1.2	Vegetation.....	18
5.1.3	Photo Documentation .....	18
5.1.4	Stream Hydrology .....	18
5.1.5	Wetland Hydrology .....	18
6	REFERENCES.....	19

## Appendices

### Appendix A. General Tables and Figures

- Table 1. Project Components and Mitigation Credits
- Table 2. Project Activity and Reporting History
- Table 3. Project Contacts
- Table 4. Project Information Summary
- Figure 1. Project Vicinity Map
- Figure 2. Project USGS Map

### Appendix B. Visual Assessment Data

- Figure 3. Current Conditions Plan View Map (CCPV)
- Table 5. Visual Stream Morphology Stability Assessment
- Table 6. Vegetation Condition Assessment
- Table 7. Stream Problem Areas
- Table 8. Vegetation Problem Areas
- Figure 4. Vegetation Plot Photos
- Figure 5. Stream Problem Photos
- Figure 6. Vegetation Problem Photos

### Appendix C. Vegetation Plot Data

- Table 9a. Vegetation Plot Criteria Attainment Summary
- Table 9b. CVS Vegetation Plot Metadata
- Table 9c. Planted and Total Stem Counts (Species by Plot)

### Appendix D. Stream Geomorphology Data

- Table 10. Morphological Parameters Summary Data
- Table 11. Dimensional Morphology Summary – Cross Sections Data
- Table 12. Bank Pin Array Summary Data
- Figure 7. Cross Section Plots

### Appendix E. Hydrology Data

- Table 13. Documentation of Geomorphologically Significant Flow Events
- Table 14. Rainfall Summary
- Table 15a. Wetland Hydrology Criteria Attainment
- Table 15b. MY1-MY3 Wetland Hydrology Summary
- Chart 1. 2017 Precipitation Data for Best Site
- Chart 2. 2017 Groundwater Monitoring Gauge Hydrographs
- Figure 8. Crest Gauge Verification Photos

## 1 PROJECT GOALS, BACKGROUND AND ATTRIBUTES

### 1.1 Location and Setting

The Best Stream and Wetland Site is located in Duplin County approximately two miles east of Beulaville, NC (**Figure 1**). To access the downstream end of the site from the town of Beulaville, travel 0.6 miles east on NC HWY 24, take a right onto Lyman Road (SR 1801), and continue 1.6 miles southeast to the crossing with Muddy Creek. Reaches UT7, UT8, UT9, UT10 and the lower end of Muddy Creek may all be accessed from Lyman Road. Reaches UT5 and UT6 are located just south of NC HWY 24, approximately 1.9 miles east of Beulaville. The upstream portion of the site may be accessed from two locations. Reaches UT1, UT2 and Muddy Creek are located to the south of NC HWY 24, opposite of the intersection of NC HWY 24 and Penny Road (SR 1720), approximately 2.8 miles east of Beulaville. To access reaches UT3, UT4 and Muddy Creek, travel 3.2 miles east on NC HWY 24 from Beulaville to Edwards Road (SR 1835), continue south for approximately 1.0 mile, turn right onto Put Lane, and follow the road down to Reaches UT3 and UT4.

### 1.2 Project Goals and Objectives

The Best stream and wetland mitigation project will provide numerous ecological and water quality benefits within the Cape Fear River Basin. While many of these benefits are limited to the project area, others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Expected improvements to water quality, hydrology, and habitat are outlined below.

#### Design Goals and Objectives

<b>Benefits Related to Water Quality</b>	
Nutrient removal	Benefit will be achieved through filtering of runoff from adjacent CAFOs through buffer areas, the conversion of active farm fields to forested buffers, improved denitrification and nutrient uptake through buffer zones, and installation of BMPs at the headwaters of selected reaches and ditch outlets.
Sediment removal	Benefit will be achieved through the stabilization of eroding stream banks and reduction of sediment loss from field areas due to lack of vegetative cover. Channel velocities will also be decreased through a reduction in slope, therefore decreasing erosive forces.
Increase dissolved oxygen concentration	Benefit will be achieved through the construction of instream structures to increase turbulence and dissolved oxygen concentrations and lower water temperature to increase dissolved oxygen capacity.
Runoff filtration	Benefit will be achieved through the restoration of buffer areas that will receive and filter runoff, thereby reducing nutrients and sediment concentrations reaching water bodies downstream.
<b>Benefits to Flood Attenuation</b>	
Water storage	Benefit will be achieved through the restoration of buffer areas which will infiltrate more water during precipitation events than under current site conditions.
Improved groundwater recharge	Benefit will be achieved through the increased storage of precipitation in buffer areas, ephemeral depressions, and reconnection of existing floodplain. Greater storage of water will lead to improved infiltration and groundwater recharge.
Improved/restored hydrologic connections	Benefit will be achieved by restoring the stream to a natural meandering pattern with an appropriately sized channel, such that the channel's floodplain will be flooded more frequently at flows greater than the bankfull stage.
<b>Benefits Related to Ecological Processes</b>	
Restoration of habitats	Benefit will be achieved by restoring riparian buffer habitat to appropriate bottomland hardwood ecosystem.

Improved substrate and instream cover	Benefit will be achieved through the construction of instream structures designed to improve bedform diversity and to trap detritus. Substrate will become coarser as a result of the stabilization of stream banks and an overall decrease in the amount of fine materials deposited in the stream.
Addition of large woody debris	Benefit will be achieved through the addition of wood structures as part of the restoration design. Such structures may include log vanes, root wads, and log weirs.
Reduced temperature of water due to shading	Benefit will be achieved through the restoration of canopy tree species to the stream buffer areas.
Restoration of terrestrial habitat	Benefit will be achieved through the restoration of riparian buffer bottomland hardwood habitats.

The North Carolina Division of Mitigation Services (NCDMS) develops River Basin Restoration Priorities (RBRP) to guide its restoration activities within each of the state’s 54 cataloging units. RBRPs delineate specific watersheds that exhibit both the need and opportunity for wetland, stream and riparian buffer restoration. These TLWs receive priority for DMS planning and restoration project funds. Currently, no Local Watershed Plan (LWP) is available for the project area.

The 2009 Cape Fear River Basin River Basin Restoration Priorities (RBRP) identified HUC 03030007060010 as a Targeted Local Watershed (TLW). The watershed is characterized by 52 percent agricultural land use area with Muddy Creek identified as Impaired for aquatic life because of a Fair benthic community rating. The Best Stream and Wetland Restoration Project was identified as a stream and wetland opportunity to improve water quality, habitat, and hydrology within the TLW.

The project goals address stressors identified in the TLW and include the following:

- Nutrient removal,
- Sediment removal,
- Reducing runoff from animal operations,
- Filtration of runoff, and
- Improved aquatic and terrestrial habitat.

The project goals will be addressed through the following project objectives:

- Establishing riparian buffer areas adjacent to CAFOs,
- Converting active farm field to forested buffers,
- Stabilization of eroding stream banks,
- Improving and protecting portions of headwater systems that discharge to a 303d listed stream,
- Reduction in stream bank slope,
- Restoration of riparian buffer bottomland hardwood habitats, and
- Construction of in-stream structures designed to improve bedform diversity and trap detritus.

The Best stream and wetland mitigation project is located within the northern (upstream) portion of the TLW and includes sections of Muddy Creek (303d listed) and headwater streams that discharge into Muddy Creek. Due to its location and improvements, the project provides numerous ecological and water quality benefits within the Cape Fear River Basin. While many of these benefits are limited to the project area, others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Many of the project design goals and objectives, including restoration of riparian buffers to filter runoff from agricultural operations and improve terrestrial habitat, and construction of in-stream structures to improve habitat diversity, addresses the degraded water quality and nutrient input from farming that were identified as major watershed stressors in the 2009 Cape Fear RBRP.

### 1.3 Project Structure

**Table 1a. Best Site Project Components – Stream Mitigation**

Reach	Mitigation Type*	As-Built Stationing (Existing)		Existing Length (LF)	As-Built Length (LF)	Mitigation Ratio	SMUs
UT1	P1 Restoration	0+46	to 18+63	1,551	1,757	1 : 1.0	1,757
UT1	SP & BE	18+63	to 21+42	303	279	1 : 5.0	56
UT2	P1 Restoration	2+30	to 30+64	2,552	2,772	1 : 1.0	2,772
UT2	SP & BE	30+64	to 33+95	331	331	1 : 5.0	66
UT3	Enhancement II	0+00	to 8+42	1,458	812	1 : 2.5	325
UT3	SP & BE	14+58	to 15+22	64	64	1 : 5.0	13
UT4	HV Restoration	5+63	to 11+19	534	494	1 : 1.0	494
UT4	SP & BE	11+19	to 17+65	655	646	1 : 5.0	129
UT5	SP & BE	0+00	to 40+86	4,086	4,043	1 : 5.0	809
UT6	Enhancement I	0+62	to 6+00	538	538	1 : 1.5	359
UT7	SP & BE	0+44	to 32+27	3,183	3,183	1 : 5.0	637
UT8	Enhancement I	0+75	to 9+00	825	765	1 : 1.5	510
UT8	SP & BE	9+00	to 12+13	313	313	1 : 5.0	63
UT9	SP & BE	0+64	to 11+71	1,107	1,107	1 : 5.0	221
UT10	SP & BE	3+37	to 11+05	768	768	1 : 5.0	154
<b>Muddy Creek</b>	SP & BE	0+35	to 92+49	9,214	9,073	1 : 5.0	1,815
<b>Total</b>				<b>27,482</b>	<b>26,945</b>		<b>10,178</b>

\*P1 = Priority 1, SP & BE= Stream Preservation and Buffer Enhancement, HV = Headwater Valley

**Table 1b. Best Site Project Components – Wetland Mitigation**

Wetland	Mitigation Type	As-Built Mitigation Area (ac)	Mitigation Ratio	WMUs
W1	Restoration	3.77	1:1	3.77
W2	Restoration	0.31	1:1	0.31
W3A	Restoration	0.58	1:1	0.58
W3B	Restoration	0.59	1:1	0.59
<b>Total</b>		<b>5.25</b>		<b>5.25</b>

#### 1.3.1 Restoration Type and Approach

##### UT1

Priority Level 1 restoration was completed for UT1 to address all existing impairments, particularly the greatly oversized channel and lack of bedform diversity. The design approach included meandering the channel within the natural valley and backfilling the existing stream. A minimum 50 foot buffer was established and planted with native riparian vegetation. Because the pre-existing

buffer was devoid of significant woody vegetation, woody debris was installed along the bed to improve in-stream habitat. Livestock was excluded with fencing installed along the easement boundary. An existing CMP culvert located along the middle of the reach was removed and replaced downstream at station 13+75 to allow the landowner access to both sides of the property. Stream Preservation and Buffer Enhancement was completed for the downstream section of the channel where it flows through a forested buffer down to the confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

## **UT2**

Similar to UT1, Priority 1 restoration was completed for UT2 to address historic straightening and channel enlargement. The existing channel was backfilled, and the restored channel was relocated such that it meanders within the existing valley. A diffuse flow structure was installed at the ditch adjacent to the proposed crossing. The structure was placed such that flows from the existing ditch will be attenuated to establish sheet flow as the water enters the restored channel. All areas within the minimum 50 foot buffer were planted with native riparian vegetation. An existing 60" CMP culvert located at station 20+25 of the reach was removed and replaced with a 48" HDPE culvert to allow the landowner access to the entire property. Additionally, the existing culvert at the upstream end of UT2 was upgraded to a 48" HDPE culvert and reset to more effectively transition the existing channel upstream into the project stream. Priority Level I restoration was appropriate for this channel because it was the only mitigation approach that would address bed and bank instability, establish a forested riparian buffer, and significantly enhance aquatic habitat. Stream Preservation and Buffer Enhancement was completed for the most downstream section, where the channel enters the existing forested buffer, down to its confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

## **UT3**

Enhancement Level II was completed on Reach UT3 due to the channel's stability and appropriate size. The design approach on this reach focused on improving the riparian buffer. The existing hog lagoon located within buffer on the west side of the reach has remained in place, preventing the generation of stream credits for approximately 600 linear feet. Through this section, the left buffer was extended out to a minimum of 75 feet along the left bank, and the right buffer was extended just past top of bank. The existing crossing located at station 8+50 was replaced and upgraded with a 30" HDPE pipe, allowing the landowner continued access across his property. Additional bank grading

and stabilization was included in the culvert replacement. The grading of pools and the installation of woody debris structures was performed along the reach to improve aquatic habitat. Upstream of the crossing, a 75-foot buffer was restored along the east bank where the channel currently flowed through an active pasture. A 100-foot buffer was implemented for the headwater origin point to further protect water quality from cattle access. Cattle have been excluded with fencing. All areas within the buffer were planted with native riparian vegetation. Stream Preservation and Buffer Enhancement was implemented along the downstream end where the channel enters the Muddy Creek floodplain. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

#### **UT4**

Headwater valley restoration was completed for the upper section of UT4. The existing channel was backfilled, and flow was directed from its current position east back to the historic valley location. A minor amount of earthwork was completed in the headwater valley restoration apart from ditch plugging to tie the existing ditch back to the natural valley. Areas within the 100 foot buffer that were disturbed or lacked riparian vegetation were planted. Cattle were excluded from the buffer through the installation of fencing. An existing 15" CPP culvert crossing located at station 8+50 of the reach was removed and replaced with triple 18" HDPE culverts. This crossing was relocated to the low spot in the valley to allow the landowner continued access to an agricultural field west of the channel. Downstream of the crossing, a smaller low flow channel was constructed within the natural valley. This segment now connects the upstream headwater valley section to the existing channel approximately 230 feet below the crossing. Due to the stable nature of the buffer along the downstream reach of UT4, Stream Preservation and Buffer Enhancement was implemented from just downstream of the crossing to the confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

#### **UT5**

Stream Preservation and Buffer Enhancement was completed on UT5. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional

treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

#### **UT6**

Enhancement Level I was completed on UT6. The mitigation approach on this reach focused on bank stabilization, bedform diversity, and improving the riparian buffer. The existing channel was impaired by channelization, vertical un-vegetated banks, and a dense privet understory within the buffer. The grading of pools, grade control structures, and the installation of woody debris structures were implemented along the reach to improve aquatic habitat. All disturbed areas within the riparian buffer were planted with native riparian vegetation.

#### **UT7**

Stream Preservation and Buffer Enhancement was completed on UT7. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

#### **UT8**

Enhancement Level I was completed on UT8. The mitigation approach on this reach focused on bank stabilization, bedform diversity, and riparian buffer restoration. The existing channel was impaired by channelization, localized bank instability, and cleared agricultural land in the buffer. Stabilization activities included grading a floodplain bench, installing grade control structures, and installing woody debris structures to improve hydraulic efficiency and aquatic habitat. All disturbed areas within the riparian buffer were planted with native riparian vegetation. Stream Preservation and Buffer Enhancement was completed on 313 linear feet where the channel enters the existing forested buffer, down to its confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.



## **UT9**

Stream Preservation and Buffer Enhancement was completed on UT9. The stream is channelized, but stable throughout the easement. The active channel is meandering within the larger excavated channel bottom. The riparian buffer is intact hardwood forest with localized areas of privet. The easement boundary extends a minimum of 50 feet outward from the stream channel, or to the limit of adjacent riparian wetlands, whichever is wider. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

## **UT10**

Stream Preservation and Buffer Enhancement was completed on UT10. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

## **Muddy Creek**

Stream Preservation and Buffer Enhancement was completed for the majority of Muddy Creek. The buffer was restored and increased to a width of 75 feet along the south side. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

## **Wetland W1**

Wetland W1 is located at the headwater of UT1 and has a natural constriction at the outlet. The soil is a sandy loam/loamy sandy underlain by clayey textured subsoil that forms an effective restrictive

layer to groundwater loss. This area receives runoff from NC HWY 24. Based upon soil and landscape position, it is likely this area has a seasonal seepage along the upper boundary.

Site modifications included removal of dredged and excavated materials, plugging the ditch, and raising the streambed elevation to bring the water table closer to the ground surface. Additional temporal habitat was constructed to eliminate surface leveling and smoothing for agricultural use. The temporal habitat is variable to mimic sloughs, oxbows, root-tips and other shallow natural features. During monitoring, beaver activity will be controlled to allow the site to stabilize and vegetative community to establish. After the monitoring period, the site is designed to promote and tolerate beaver activity. No hydrologic trespass is anticipated due to beaver activity in this wetland. These modifications will increase storage and eliminate the rapid loss of surface water. This area may receive limited overbank flows due to location in the headwater of UT1. Subsoil ripping and roughing of the soil surface were performed to ameliorate soil compaction and create an uneven surface more conducive for surface water retention, infiltration, and increase storage that would be present in natural wetland systems.

### **Wetland W2**

Wetland W2 is located at the toe slope along Muddy Creek and UT2. The soil is a sandy loam/loamy sandy underlain by sandy clay loam and sandy clay. This site is at a low elevation and is influenced by the water table on the floodplain of Muddy Creek. It is unlikely that groundwater loss is significant during most of the year. This area has a small watershed, but flooding from UT2 and Muddy Creek will increase hydrologic storage.

Hydrology was restored by removing dredge material along the channel and raising the streambed elevation, bringing the water table closer to the ground surface. Site modifications included subsoil ripping, crown removal, and surface roughing of the area. Additional temporal habitat was constructed to eliminate the surface leveling and smoothing for agricultural use. The temporal habitat is variable to mimic sloughs, root-tips and other shallow natural features. This ameliorates past soil leveling and compaction and creates an uneven surface more conducive of infiltration and storage that would be present in natural wetland systems.

### **Wetland W3**

Wetland W3 is composed of two similar area (W3a and W3b) located at the toe slope along Muddy Creek. A low finger of soil separates them. The soil in these areas is a loamy sand/sandy loam. The surrounding upland is underlain by clayey subsoil that forms an effective restrictive layer that lateral flow rides provide additional hydrological input. A ditch is located upslope of these areas and alongside W3a that drains to Muddy Creek.

The soil is a sandy loam/loamy sand. The surrounding upland has a sandy clay loam and sandy clay that form an effective restrictive layer that lateral flow rides provide additional hydrological input. Both areas have small watersheds, but W3b receives groundwater seepage along the toe of slope diverted by the upslope ditch.

Hydrology was restored by filling ditches and enhancing the concave topography by removing soil material where cultivation had filled low features and leveled the surface to facilitate cultivation. Additional groundwater seepage diverted by the ditch was restored to these wetlands. Temporal habitat was constructed to eliminate the surface leveling and smoothing for agricultural use. Subsoil ripping and surface roughing of the area was performed to ameliorate soil compaction and create an uneven surface more conducive of infiltration and storage that would be present in natural wetland systems.

## 1.4 Project History, Contacts and Attribute Data

### 1.4.1 Project History

The Best Stream and Wetland Restoration Site was restored by Resource Environmental Solutions, LLC (RES) through a full-delivery contract awarded by NCDMS in 2012. **Tables 2, 3, and 4 in Appendix A** provide a time sequence and information pertaining to the project activities, history, contacts, and baseline information.

### 1.4.2 Project Watersheds

The easement totals 142.7 acres and the project streams include ten unnamed tributaries to Muddy Creek and a portion of Muddy Creek extending from approximately 0.3 miles west of Edwards Road to 0.4 miles past Lyman Road. The total drainage area at the downstream limits of the project is 2,928 acres (4.58 mi<sup>2</sup>). The land use in the project watershed is approximately 47 percent cultivated cropland, 21 percent evergreen and deciduous forest, 13 percent shrub/scrub, ten percent bottomland forest/hardwood swamp, three percent developed, and six percent managed herbaceous cover and pasture.

UT1 has a drainage area of 0.06 square miles (41 acres), and flows in a southerly direction to the confluence with Muddy Creek. UT2 flows south to its confluence with Muddy Creek and has a drainage area of 0.23 square miles (146 acres). UT3 is located to the south of Muddy Creek, opposite of UT2, and flows to the north and into Muddy Creek. This reach has a drainage area of 0.09 square miles (56 acres). UT4 is located to the west of UT3 and discharges to Muddy Creek. This reach has a drainage area of 0.13 square miles (82 acres). UT5 flows in a southerly direction from NC HWY 24 to Muddy Creek and has a drainage area of 0.59 square miles (380 acres). UT6 flows southeast to its confluence with UT5 and has a drainage area of 0.12 square miles (79 acres). UT7 flows in a southerly direction east of Lyman Road down to its confluence with UT5 before discharging to Muddy Creek. UT7 has a drainage area of 0.60 square miles (387 acres). UT8 has a drainage area of 0.09 square miles (56 acres), and flows in an easterly direction through a cultivated field east of Lyman Road down to the confluence with UT7. UT9 flows southeast to its confluence with Muddy Creek and has a drainage area of 0.06 square miles (36 acres). UT10 is the downstream-most tributary within the Best Site and flows in a westerly direction from a farm crossing west of Lyman Road down to Muddy Creek. UT10 has a drainage area of 0.48 square miles (306 acres). Muddy Creek is a stable swamp stream system with intact hardwood forest floodplain, extending from approximately 0.3 miles west of Edwards Road to 0.5 miles south of Lyman Road. Muddy Creek has a drainage area of 4.6 square miles (2,930 acres) at the downstream limits and has an existing length of 9,214 linear feet.

## 2 Success Criteria

The success criteria for the Best Site will follow accepted and approved success criteria presented in the USACE Stream Mitigation Guidelines and subsequent NCDMS and agency guidance. Specific success criteria components are presented below.

### 2.1 Stream Restoration

#### 2.1.1 Bankfull Events

Two bankfull flow events must be documented within the seven-year monitoring period. The two bankfull events must occur in separate years. Otherwise, the stream monitoring will continue until

two bankfull events have been documented in separate years. Bankfull events will be documented using crest gauges, auto-logging crest gauges, photographs, and visual assessments for evidence of debris rack lines.

### **2.1.2 Cross Sections**

There should be little change in as-built cross-sections. If changes do take place, they should be evaluated to determine if they represent a movement toward a less stable condition (for example down-cutting or erosion), or are minor changes that represent an increase in stability (for example settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). Starting in MY3, BHR was calculated on riffles using the baseline bankfull elevation. This method was used because the dimension of the channels has not changed enough to alter the bankfull elevation. None of the restoration riffle cross sections exceeded a 1.2 BHR. Two cross sections on Enhancement I reaches did exceed 1.2 but both have baseline bankfull elevations below top of bank. Cross-sections are classified using the Rosgen stream classification method, and all monitored cross-sections should fall within the quantitative parameters defined for channels of the design stream type.

### **2.1.3 Bank Pin Arrays**

Bank pin arrays will be used as a supplemental method to monitor erosion on selected meander bends where there is not a cross section. Bank pin arrays will be installed along the outer bend of the meander. Bank pins will be installed just above the water surface and every two feet above the lowest pin. Bank pin exposure will be recorded at each monitoring event, and the exposed pin will be driven flush with the bank, there should be little change in as-built cross-sections. If changes do take place, they should be evaluated to determine if they represent a movement toward a less stable condition (for example down-cutting or erosion), or are minor changes that represent an increase in stability (for example settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). Cross-sections shall be classified using the Rosgen stream classification method, and all monitored cross-sections should fall within the quantitative parameters defined for channels of the design stream type.

### **2.1.4 Digital Image Stations**

Digital images are used to subjectively evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, and effectiveness of erosion control measures. Longitudinal images should not indicate the absence of developing bars within the channel or an excessive increase in channel depth. Lateral images should not indicate excessive erosion or continuing degradation of the banks over time. A series of images over time should indicate successional maturation of riparian vegetation.

## **2.2 Wetland Restoration**

Success criteria and monitoring for wetland hydrology within the wetland restoration areas on the site follows NCDMS Guidance dated 7 November 2011. The target minimum wetland hydroperiod is 9 percent of the growing season. Stream hydrology and water balance calculations indicate the wetland area will meet jurisdictional criteria (5 percent hydroperiod). However, due to immature vegetation and reduced PET, a longer success criterion is appropriate. Auto recording gauges are used to measure daily groundwater elevations throughout the Sampson County growing season in all 7 years of monitoring.

If a hydrology gauge location fails to meet these success criteria in the seven year monitoring period then monitoring may be extended, remedial actions may be undertaken, or groundwater modeling may be used to demonstrate the limits of wetland restoration.

### **2.3 Vegetation Success Criteria**

Specific and measurable success criteria for plant density within the wetland restoration and riparian buffers on the site will follow NCDMS Guidance dated 7 November 2011. Vegetation monitoring plots are a minimum of 0.02 acres in size, and cover a minimum of two percent of the planted area. The following data is recorded for all trees in the plots: species, height, planting date (or volunteer), and grid location. Monitoring occurs in the fall of Years 1, 2, 3, 5, and 7. The interim measures of vegetative success for the site is the survival of at least 320 three-year old planted trees per acre at the end of Year 3, and 260 planted trees per acre at the end of Year 5. The final vegetative success criteria is the survival of 210 planted trees per acre at the end of Year 7 of the monitoring period.

Invasive and noxious species will be monitored and controlled so that none become dominant or alter the desired community structure of the site. If necessary, RES will develop a species-specific control plan.

### **2.4 Scheduling/Reporting**

The monitoring program will be implemented to document system development and progress toward achieving the success criteria. The restored stream morphology is assessed to determine the success of the mitigation. The monitoring program will be undertaken for seven years or until the final success criteria are achieved, whichever is longer.

Monitoring reports will be prepared in the fall of each year of monitoring and submitted to NCDMS. The monitoring reports will include all information, and be in the format required by NCDMS in Version 2.0 of the NCDMS Monitoring Report Template (Oct. 2010).

## **3 MONITORING PLAN**

Annual monitoring data will be reported using the DMS monitoring template. Annual monitoring shall be conducted for stream, wetland, and vegetation monitoring parameters as noted below.

### **3.1 Stream Restoration**

#### **3.1.1 As-Built Survey**

An as-built survey was conducted following construction to document channel size, condition, and location. The survey includes a complete profile of thalweg, water surface, bankfull, and top of bank to compare with future geomorphic data. Longitudinal profiles will not be required in annual monitoring reports unless requested by NCDMS or USACE.

#### **3.1.2 Bankfull Events**

Six sets of manual and auto-logging crest gauges were installed on the site, one along UT1, UT2, UT3, UT4, UT6, and one along UT8. The auto logging crest gauges were installed within the channel and will continuously record flow conditions at an hourly interval. Manual crest gauges were installed on the bank at bankfull elevation. Crest gauges will be checked during each site visit to determine if a bankfull event has occurred since the last site visit. Crest gauge readings and debris rack lines will be photographed to document evidence of bankfull events. Flow days will be reported on headwater valley restoration reaches.

---

### **3.1.3 Cross Sections**

A total of 31 permanent cross sections were installed to monitor channel dimensions and stability. Twelve cross sections were installed along UT1 where Priority 1 restoration was performed. Twelve cross sections (six pools and six shallows) were installed along UT2 also. UT4 has a total of two cross sections installed throughout its length. Stream segment UT6 has two cross sections installed along its length where enhancement activities were performed. On the UT8 side of the project, a total of three cross sections were installed. Cross sections were typically located at representative riffle and pool sections along each stream reach. Each cross section was permanently marked with 3/8 rebar pin to establish a monument location at each end. A marker pole was also installed at both ends of each cross section to allow ease locating during monitoring activities. Cross section surveys will be performed once a year during annual monitoring years 1, 2, 3, 5, and 7 and will include all breaks in slope including top of bank, bottom of bank, streambed, edge of water, and thalweg.

### **3.1.4 Digital Image Stations**

Digital photographs will be taken at least once a year to visually document stream and vegetation conditions. This monitoring practice will continue for seven years following construction and planting. Permanent photo point locations at cross sections and vegetation plots have been established so that the same directional view and location may be repeated each monitoring year. Monitoring photographs will also be used to document any stream and vegetation problematic areas such as erosion, stream and bank instability, easement encroachment and vegetation damage.

### **3.1.5 Bank Pin Arrays**

Eight bank pin array sets have been installed at pool cross sections located along UT1 and UT2. These bank pin arrays were installed along the upstream and downstream third of the meander. Bank pins are a minimum of three feet long, and have been installed just above the water surface and every two feet above the lowest pin. Bank pin exposure will be recorded at each monitoring event, and the exposed pin will be driven flush with the bank.

### **3.1.6 Visual Assessment Monitoring**

Visual monitoring of all mitigation areas is conducted a minimum of twice per monitoring year by qualified individuals. The visual assessments include vegetation density, vigor, invasive species, and easement encroachments. Visual assessments of stream stability include a complete stream walk and structure inspection. Digital images are taken at fixed representative locations to record each monitoring event as well as any noted problem areas or areas of concern. Results of visual monitoring are presented in a plan view exhibit with a brief description of problem areas and digital images. Photographs will be used to subjectively evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, and effectiveness of erosion control measures. Longitudinal photos should indicate the absence of developing bars within the channel or an excessive increase in channel depth. Lateral photos should not indicate excessive erosion or continuing degradation of the banks over time. A series of photos over time should indicate successional maturation of riparian vegetation.

### **3.1.7 Surface Flow**

The headwater valley restoration area on UT4 will be monitored to document intermittent or seasonal surface flow. This will be accomplished through direct observation, photo documentation of dye tests, and continuous flow monitoring devices (pressure transducers). An auto logging crest gauge has been installed within the headwater valley channel and will continuously record flow conditions at an hourly interval. This gauge will be downloaded during each site visit to determine if intermittent or seasonal flows conditions are present.

### 3.2 Wetland Hydrology

Wetland hydrology will be monitored to document hydric conditions in the wetland restoration areas. This will be accomplished with automatic recording pressure transducer gauges installed in representative locations across the restoration areas and reference wetland areas. A total of twelve automatic recording pressure transducers (Auto-Wells) have been installed on the site. Nine auto-wells have been installed within the wetland restoration area and three within reference areas. The gauges will be downloaded quarterly and wetland hydroperiods will be calculated during the growing season. Gauge installation followed current regulatory and DMS guidance. Visual observations of primary and secondary wetland hydrology indicators will also be recorded during quarterly site visits.

### 3.3 Vegetation

A total of 23 vegetation plots were randomly established within the planted stream riparian buffer easement. Vegetation plots measure 10 meters by 10 meters or 5 meters by 20 meters (0.02 acres) and have all four corners marked with metal posts. Planted woody vegetation was assessed within each plot to establish a baseline dataset. Within each vegetation plot, each planted stem was identified for species, “X” and “Y” origin located, and measured for height. Reference digital photographs were also captured to document baseline conditions. Species composition, density, growth patterns, damaged stems, and survival ratios will be measured and reported on an annual basis. Vegetation plot data will be reported for each plot as well as an overall site average.

## 4 MAINTENANCE AND CONTINGENCY PLAN

All identified problematic areas or areas of concern such as stream bank erosion/instability, aggradation/degradation, lack of targeted vegetation, and invasive/exotic species which prevent the site from meeting performance success criteria will be evaluated on a case by case basis. These areas will be documented and remedial actions will be discussed amongst NCDMS staff to determine a plan of action. If it is determined remedial action is required, a plan will be provided.

### 4.1 Stream

Four stream problems were identified during the Year 3 monitoring period and have been mapped on the Current Conditions Plan View (CCPV) (**Figure 3**). Stream problem area 1 (SPA1) is located on UT3 at station 7+50. Fence has been damaged due to fallen trees. Stream problem area 2 (SPA2) consists of minor bank erosion on UT4 at station 5+60 and station 7+00. These areas appear stable and RES plans to continue to monitor these areas to see if they worsen. If conditions continue to worsen, livestock and additional bank matting will be installed along the banks. Stream problem area 3 (SPA3) is located on UT4 from station 8+47 to 8+67. This area consists of ponding on the road, due to downstream issue at SPA4. The area involves adding fill material to eliminate the ponding on the road. SPA4 is located on UT4 from station 8+75 to 11+03, and is attributed to the subsidence of the plug that had been installed at construction. This problem is a continued portion of (MY1-SPA6, MY2-SPA3) and is associated with the relic stream channel. Fill material needs to be added to raise the plug elevation in the relic channel. All stream problem areas are localized and the overall condition of the project streams on site are stable. Remedial action repair work is planned for spring 2018.

### 4.2 Wetlands

No wetland problems areas were noted during the Year 3 monitoring period. Wetland hydrology and vegetation represent typical conditions of a site in Year 3 post construction monitoring. If any wetland problem areas are identified in the future, they will be documented and mapped on the CCPV (**Figure 3**) as part of the annual monitoring report. Six of the nine wetland gauges achieved the

---

success criteria by remaining continuously within 12 inches of the soil surface for at least nine percent of the growing season. The three remaining wetland gauges reported 13, 16, and 14 days (5%, 7%, and 6%, respectively) consecutively within 12 inches of the soil surface. Gauge AW7 is located in Marvyn and Gritney soils. Maryvn and Gritney are typically upland soils that are well drained. Gritney, however, is in the same Taxonomic Subgroup as Helena which according to the IRT's Wetland Saturation Threshold Table has a wetland hydroperiod range of 6-8% of the growing season. This means that AW7 was in or above the wetland hydroperiod range in MY1 and MY2 and only missed the range by one day in MY3. Gauges AW8 and AW9, which recorded only 16 and 14 consecutive days within 12 inches of the soil surface, were stolen therefore did not collect data for the first 48 days (~20%) of the growing season (**Table 15**). These gauges have been replaced and are now collecting data. The Best Site wetland restoration areas are performing as designed and are on track to meeting wetland success criteria.

### 4.3 Vegetation

Ten vegetation problems were identified during the Year 3 monitoring period. These vegetation problem areas are documented and mapped on the CCPV (**Figure 3**) as part of the annual monitoring report. Vegetation problem area 1 (VPA1) is a low stem density area along UT1 and Wetland 1. This area is approximately half an acre in size and is well vegetated with herbaceous cover but lacks woody planted stems. Vegetation problem area 2 (VPA2) is an area where the invasive species mimosa (*Albizia julibrissin*) and Chinese privet (*Ligustrum sinense*) are present along UT1 and Wetland 1. This area is approximately a tenth of an acre in size, and is well vegetated with native trees and native herbaceous cover. RES plans to treat the invasive species in this area in 2018. Vegetation problem area 3 (VPA3) is a low stem density area along UT1. This area is approximately half an acre in size and is well vegetated with herbaceous cover but lacks woody planted stems. Therefore, RES will perform an additional supplemental replant within this area in the spring 2018 with one gallon-containerized trees. Vegetation problem area 4 (VPA4) is a poor growth/vigor area along UT1. This area is approximately a quarter of an acre in size and is vegetated with herbaceous cover, however planted stems have poor vigor. Vegetation problem area 5 (VPA5) is an encroachment area along UT2. This area is less than a tenth of an acre in size and has been subject to overspray from the adjacent farming operation. Vegetation problem area 6 (VPA6) is a poor growth/vigor area along UT2. This area is approximately a quarter of an acre in size and is vegetated with herbaceous cover however, planted stems have poor vigor. Vegetation problem area 7 (VPA7) is an encroachment area along UT2. This area is approximately a tenth of an acre in size and has been subject to overspray from the adjacent farming operation. Vegetation problem area 8 (VPA8) is an area of low stem density. Vegetation plot 17 within this area exhibited complete mortality; therefore, RES will perform an additional supplemental replant within this area in the spring 2018. It should be noted that VPA8 was replanted in 2016 but likely did not have survival due to extensive herbaceous overgrowth and shading of planted stems. Spraying or mowing this area may be considered prior to replanting one gallon-containerized trees. Vegetation problem area 9 (VPA9) is a low stem density area along UT4. This area is approximately a sixth of an acre in size and is well vegetated with herbaceous cover but lacks woody planted stems. Therefore, RES will perform an additional supplemental replant within this area in the spring 2018. Vegetation problem area 10 (VPA10) is an encroachment area along UT8. This area is less than a tenth of an acre in size and has been subject to overspray from the adjacent farming operation.

Overall these areas are minimal and the Best Site is on track to meet the Year 3 vegetation survival success criterion of 320 trees per acre as specified in the Mitigation Plan (**Table 9a**).



## 5 YEAR 3 MONITORING CONDITIONS (MY3)

The Best Site Year 3 Monitoring activities were completed November 2017. All Year 3 monitoring data is present below and in the appendices. Data presented shows the site has four stream problem areas and ten vegetation problem areas. Stream problem areas consist of localized bank erosion and subsidence of plugs on a relic channel. Ten vegetation problems were noted during the Year 3 monitoring period. Four areas consisted of low stem density areas along UT1, UT3 and UT4; two areas consisted of poor growth/vigor areas along UT1 and UT2; one invasive species area along UT1; and three small areas of encroachment along UT2 and UT8. This site is on track to meeting stream, wetland and vegetation interim success criteria.

### 5.1 Year 3 Monitoring Data Collection

#### 5.1.1 Morphological State of the Channel

All morphological stream data for the MY3 dimensions were collected during the annual monitoring survey performed during late August 2017. **Appendix D** includes summary data tables, morphological parameters, and stream photographs.

##### *Profile*

The baseline (MY-0) profiles closely matches the proposed design profiles. The plotted longitudinal profiles can be found on the As-Built Drawings. Longitudinal profiles will not be performed in annual monitoring reports unless requested by NCEEP or USACE. Morphological summary data tables can be found in **Table 10**.

##### *Dimension*

The Year 3 (MY3) cross sectional dimensions closely match the baseline and MY1 cross section parameters. Minimal changes were noted during Year 3 cross section surveys resulting from stable bed and bank conditions. Cross sections 12, 13, 24, and 26 did show some changes during MY2, which were associated with repair work during 2016 or minor aggradation resulting from Hurricane Matthew. Little to no further changes resulted between MY2 and MY3 at those cross sections. MY3 cross section surveys document all stream reaches are currently stable. All cross section plots and data tables can be found in **Table 11 and Figure 7**.

##### *Sediment Transport*

The Year 3 conditions show that shear stress and velocities have been reduced for all six restoration reaches. Pre-construction conditions documented all six reaches as sand bed channels and remain classified as sand bed channels post-construction. Visual assessments (**Table 5**) show the channels are transporting sediment as designed and will continue to be monitored for aggradation and degradation.

##### *Bank Pin Arrays*

Eight pool cross section locations with bank pin arrays were observed and measured for bank erosion located on the outside meander bends. If bank pin exposure was noticeable, it was measured, recorded, photographed, and then driven flush with the bank at each monitoring location. No bank pin array readings were recorded during the Year 3 monitoring season. Bank pin array data tables can be found in **Table 12**.

---

### 5.1.2 Vegetation

The Year 3 monitoring (MY3) vegetation survey was completed in November 2017 and resulted in an average of 765 planted stems per acre, well above the interim survival density of 320 stems per acre at the end of Year 3 monitoring. The average stems per vegetation plot was 19 planted stems. The minimum planted stem per plot was 0 stems and the maximum was 32 stems per plot. Sweetgum (*Liquidambar styraciflua*), Baccharis (*Baccharis halimifolia*), Black Cherry (*Prunus serotina*), Loblolly Pine (*Pinus taeda*), Red Maple (*Acer rubrum*), Winged Sumac (*Rhus copallinum*), Persimmon (*Diospyros virginiana*), and Tuliptree (*Liriodendron tulipifera*) volunteers were noted in a few vegetation plots on the site and were recorded within the CVS-EEP Data entry tool. Vegetation summary data tables can be found in **Tables 9a-c** and vegetation plot photos in **Figure 4**.

### 5.1.3 Photo Documentation

Permanent photo point locations have been established at cross sections, vegetation plots, stream crossings, and stream structures by RES staff. Any additional problem areas or areas of concern will also be documented with a digital photograph during monitoring activities. Stream digital photographs can be found in **Figure 5 and 7** and **Figures 4 and 6** for vegetation photos.

### 5.1.4 Stream Hydrology

Six sets of manual and auto-logging crest gauges were installed on the site, one along UT1, UT2, UT3, UT4, UT6, and one along UT8. The auto logging crest gauges were installed within the channel and will continuously record flow conditions at an hourly interval. Five of six crest gauges recorded bankfull events during the Year 3 monitoring period (**Table 13; Figure 8**). Crest Gauges 1,2,3,5, and 6 have all met the required bankfull standard. The one crest gauge that did not record a bankfull event was Crest Gauge 4. This crest gauge is located on a headwater valley restoration reach and it's success criteria is 30 days of continuous flow. This will be reported in MY4 and previous years flow days will be recalculated and reported using the correction from MY4.

### 5.1.5 Wetland Hydrology

A total of twelve wetland hydrology gauges are installed at the Best Site, nine in areas of wetland restoration and three as reference gauges in existing on-site wetland. Six of the nine wetland restoration gauges achieved the success criteria by remaining continuously within the 12 inches of the soil surface for at least nine percent of the growing season. The three remaining wetland gauges reported 13, 16, and 14 days (5%, 7%, and 6%, respectively) consecutively within 12 inches of the soil surface. Groundwater gauge data indicate the hydroperiods being responsive to rainfall events. Rainfall data reported by CRONOS station Albert Ellis Airport (KOAJ) indicated rainfall was below average during the months of March, June, July, September, and October. Onsite rain gauge data documented similar conditions throughout the growing season, although no data was recorded after July 10 due to auto rain gauge failure. All three reference gauges met the nine percent success criteria with hydroperiods of 10 percent or greater. Year 3 wetland hydrology monitoring data will represent the second full growing season. Wetland gauge and rainfall data is presented in **Tables 14 and 15 and Charts 1 and 2**.

## 6 REFERENCES

- Chow, Ven Te. 1959. Open-Channel Hydraulics, McGraw-Hill, New York.
- Cowardin, L.M., V. Carter, F.C. Golet and E.T. LaRoe. 1979. Classification of Wetlands and DDMSwater Habitats of the United States. U.S. Fish and Wildlife Service, Office of Biological Services, FWS/OBS-79/31. U.S. Department of the Interior, Washington, DC.
- Environmental Banc & Exchange (2013). The Best Stream and Wetland Restoration Project Final Mitigation Plan. North Carolina Ecosystems Enhancement Program, Raleigh, NC.
- Horton, J. Wright Jr. and Victor A. Zullo. 1991. The Geology of the Carolinas, Carolina Geological Society Fiftieth Anniversary Volume. The University of Tennessee Press. Knoxville, TN.
- Johnson PA. 2006. Assessing stream channel stability at bridges in physiographic regions. U.S. Department of Transportation. Federal Highway Administration. Report Number FHWA-HRT-05-072.
- Lee, Michael T., R.K. Peet, S.S. Roberts, and T.R. Wentworth. 2008. CVS-EEP Protocol for Recording Vegetation, Version 4.2 (<http://cvs.bio.unc.edu/methods.htm>)
- Natural Resources Conservation Service (NRCS). 2007. Stream Restoration Design Handbook (NEH 654), USDA
- NCDENR. "Water Quality Stream Classifications for Streams in North Carolina." Water Quality Section. <http://h2o.enr.state.nc.us/wqhome/html> (June 2005).
- Radford, A.E., H.E. Ahles and F.R. Bell. 1968. Manual of the Vascular Flora of the Carolinas. The University of North Carolina Press, Chapel Hill, North Carolina.
- Schafale, M.P. and A.S. Weakley. 1990. Classification of the Natural Communities of North Carolina, Third Approximation. North Carolina Natural Heritage Program, Division of Parks and Recreation, NCDENR, Raleigh, NC.

# **Appendix A**

## **Project Background Data and Maps**

Table 1. Project Components and Mitigation Credits

Table 2. Project Activity and Reporting History

Table 3. Project Contacts

Table 4. Project Information and Attributes

Figure 1. Project Vicinity Map

Figure 2. Project USGS Map

Monitoring Report Year 3

**Table 1. Project Components and Mitigation Credits**

<b>Project Components and Mitigation Credits</b>									
<b>Best Stream and Wetland Restoration Project/DMS Project # 95353</b>									
<b>Mitigation Credits</b>									
	Stream		Riparian Wetland		Non-riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset
Type	R	RE	R	RE	R	RE			
Totals	6217	3961	5.25	N/A	N/A	N/A	N/A	N/A	N/A
<b>Project Components</b>									
Project Component -or- Reach ID	As-Built Stationing/Location (LF)		Existing Footage/Acreage		Approach (PI, PII etc.)	Restoration - or-Restoration Equivalent	Restoration Footage or Acreage	Mitigation Ratio	SMUs/ WMUs
UT1	0+46 to 18+63		1,551		PI	R	1,757	1 : 1.0	1,757
UT1	18+63 to 21+42		303		Preservation & BE	RE	279	1 : 5.0	56
UT2	2+30 to 30+64		2,552		PI	R	2,772	1 : 1.0	2,772
UT2	30+64 to 33+95		309		Preservation & BE	RE	331	1 : 5.0	66
UT3	0+00 to 8+42		1,458		EII	R	812	1 : 2.5	325
UT3	14+58 to 15+22		64		Preservation & BE	RE	64	1 : 5.0	13
UT4	5+63 to 11+19		534		HV Restoration	R	494	1 : 1.0	494
UT4	11+19 to 17+65		655		Preservation & BE	RE	646	1 : 5.0	129
UT5	0+00 to 40+86		4,086		Preservation & BE	RE	4,043	1 : 5.0	809
UT6	0+62 to 6+00		538		EI	R	538	1 : 1.5	359
UT7	0+44 to 32+27		3,183		Preservation & BE	RE	3,183	1 : 5.0	637
UT8	0+75 to 9+00		825		EI	R	765	1 : 1.5	510
UT8	9+00 to 12+13		313		Preservation & BE	RE	313	1 : 5.0	63
UT9	0+64 to 11+71		1,171		Preservation & BE	RE	1,107	1 : 5.0	221
UT10	3+37 to 11+05		768		Preservation & BE	RE	768	1 : 5.0	154
Muddy Creek	0+35 to 92+49		9,214		Preservation & BE	RE	9,073	1 : 5.0	1,815
Wetland 1	---		3.66		Restoration	RE	3.77	1 : 1.0	3.77
Wetland 2	---		0.29		Restoration	RE	0.31	1 : 1.0	0.31
Wetland 3A	---		0.58		Restoration	RE	0.58	1 : 1.0	0.58
Wetland 3B	---		0.59		Restoration	RE	0.59	1 : 1.0	0.59

Component Summation						
Restoration Level	Stream (linear feet)	Riparian Wetland (acres)		Non-riparian Wetland	Buffer (square feet)	Upland (acres)
		Riverine	Non-Riverine			
Restoration	4,529	5.25				
Headwater Valley	494					
Enhancement I	1,303					
Enhancement II	812					
Creation						
Preservation	19,807					
High Quality Preservation						
BMP Elements						
Element	Location	Purpose/Function		Notes		
---	---	---		---		
---	---	---		---		
---	---	---		---		
<u>BMP Elements</u>						
BR = Bioretention Cell; SF = Sand Filter; SW = Stormwater Wetland; WDP = Wet Detention Pond; DDP = Dry Detention Pond; FS = Filter Strip; S = Grassed Swale; LS = Level Spreader; NI = Natural Infiltration Area; FB = Forested Buffer						

**Table 2. Project Activity and Reporting History**

Project Activity and Reporting History Best Stream and Wetland Restoration Project / DMS Project #95353		
Activity or Report	Data Collection Complete	Completion or Delivery
Mitigation Plan	NA	October 2013
Final Design – Construction Plans	NA	November 2014
Construction Completed	April 2015	May 2015
Site Planting Completed	May 2015	May 2015
Baseline Monitoring Document (Year 0 Monitoring – baseline)	July 2015	October 2015
Year 1 Monitoring	December 2015	March 2016
Year 2 Supplemental Replant/Repair Work		April 2016
Year 2 Monitoring	November 2016	January 2017
Year 3 Monitoring	November 2017	February 2018
Year 4 Monitoring		
Year 5 Monitoring		
Year 6 Monitoring		
Year 7 Monitoring		

**Table 3. Project Contacts**

<b>Project Contacts Table</b> <b>Best Stream and Wetland Restoration Project /DMS Project # 95353</b>	
<b>Designer</b>	WK Dickson and Co., Inc. 720 Corporate Center Drive Raleigh, NC 27607 (919) 782-0495 Frasier Mullen, PE
<b>Construction Contractor</b>	Wright Contracting PO Box 545 Siler City, NC 27344 (919) 663-0810 Joseph Wright
<b>Planting Contractor</b>	Resource Environmental Solutions, LLC 302 Jefferson Street, Suite 110 Raleigh, NC 27605 (919) 209-1061 David Godley
<b>Seeding Contractor</b>	Wright Contracting PO Box 545 Siler City, NC 27344 (919) 663-0810 Joseph Wright
Seed Mix Sources	Green Resource
Nursery Stock Suppliers	Arbogen, NC Forestry Services Nursery
<b>Full Delivery Provider</b>	Resource Environmental Solutions, LLC 302 Jefferson Street, Suite 110 Raleigh, NC 27605 (919) 209-1061
Project Manager:	Daniel Ingram
<b>Monitoring Performers</b>	Resource Environmental Solutions, LLC 302 Jefferson Street, Suite 110 Raleigh, NC 27605 (919) 209-1061
Project Manager:	Brian Hockett, PLS

**Table 4. Project Information Summary**

<b>Project Information</b>	
Project Name	Best Stream and Wetland Restoration Project
County	Duplin
Project Area (acres)	142.7
Project Coordinates (latitude and longitude)	34° 54' 44.011" N 77° 44' 57.344" W

<b>Project Watershed Summary Information</b>	
Physiographic Province	Outer Coastal Plain
River Basin	Cape Fear
USGS Hydrologic Unit 8-digit	03030007
USGS Hydrologic Unit 14-digit	03030007060010
DWQ Sub-basin	03-06-22
Project Drainage Area (acres)	2,928 acres
Project Drainage Area Percentage of Impervious Area	6%
CGIA Land Use Classification	Woody wetlands, emergent herbaceous wetlands, cultivated crops, evergreen forest

<b>Reach Summary Information (As-Built Conditions)</b>						
<b>Parameters</b>	<b>UT1</b>	<b>UT2</b>	<b>UT3</b>	<b>UT4</b>	<b>UT5</b>	<b>UT6</b>
Length of reach (linear feet)	2,036	3,103	876	1,140	4,043	538
Valley Classification	X	X	X	X	X	X
Drainage area (acres)	41	146	56	82	380	79
NCDWQ stream identification score	32.50	31.50	33.00	33.75	36.75	30.50
NCDWQ Water Quality Classification	N/A	C Sw	N/A	N/A	C Sw	N/A
Morphological Description (stream type)	G5c	G5c	E5	G5c/E5	C5	E5
Evolutionary trend	Stage II	Stage II	Stage VI	Stage II/VI	Stage I	Stage II
Underlying mapped soils	GoA MkA NbB RaA	AuB McC MkA NbA NbB	McC MkA NbB	McC MkA NbB	MkA NbB	NbA NbB
Drainage class	well; mod. well; poorly	well; poorly	well; poorly	well; poorly	well; poorly	well
Soil Hydric status	Hydric	Hydric	Hydric	Hydric	Hydric	Not hydric
Slope	0.66%	0.44%	0.93%	0.42%	0.40%	0.12%
FEMA classification	N/A	N/A	N/A	N/A	AE (high risk)	N/A
Native vegetation community	pasture, cultivated	cultivated	pasture	mixed hardwood forest	mixed hardwood forest	mixed hardwood forest
Percent composition of exotic invasive vegetation	0	0	5	5	<40	<25




Appendix A. General Tables and Figures



<b>Reach Summary Information (continued)</b>					
<b>Parameters</b>	<b>UT7</b>	<b>UT8</b>	<b>UT9</b>	<b>UT10</b>	<b>Muddy Creek</b>
Length of reach (linear feet)	3,183	1,078	1,107	768	9,214
Valley Classification	X	X	X	X	X
Drainage area (acres)	387	56	36	306	2930
NCDWQ stream identification score	38.50	30.50	32.00	34.00	43.25
NCDWQ Water Quality Classification	C Sw	N/A	N/A	C Sw	C Sw
Morphological Description (stream type)	C5	F5	E5	C5	E5
Evolutionary trend	Stage I	Stage II	Stage VI	Stage VI	Stage VI
Underlying mapped soils	McC MkA NbB	McC NbA NbB	McC MkA	McC MkA	McC MkA
Drainage class	well; poorly	well	well; poorly	well; poorly	well; poorly
Soil Hydric status	Hydric	Hydric	Hydric	Hydric	Hydric
Slope	0.40%	0.29%	0.80%	0.40%	0.11%
FEMA classification	AE (high risk)	N/A	AE (high risk)	AE (high risk)	AE (high risk)
Native vegetation community	mixed hardwood forest	cultivated	mixed hardwood forest	mixed hardwood forest	mixed hardwood forest
Percent composition of exotic invasive vegetation	<40	<5	<15	<20	<45

<b>Wetland Summary Information</b>				
<b>Parameters</b>	<b>Wetland 1</b>	<b>Wetland 2</b>	<b>Wetland 3A</b>	<b>Wetland 3B</b>
Size of Wetland (acres)	3.77	0.31	0.58	0.59
Wetland Type (non-riparian, riparian)	Riparian	Riparian	Riparian	Riparian
Mapped Soil Series	Rains, Goldston	Noboco, Autyville, Marvyn, Gritney	Marvyn, Gritney, Muckalee loam	Marvyn, Gritney, Muckalee loam
Drainage class	Poorly	Mod. Well, Poorly	Poorly, Well	Poorly, Well
Soil Hydric Status	Yes	Hydric with Hydric Inclusions	Hydric with Hydric Inclusions	Hydric with Hydric Inclusions
Source of Hydrology	Runoff/Groundwater Discharge	Runoff/Groundwater Discharge	Runoff, Flooding, Groundwater Discharge	Runoff, Flooding, Groundwater Discharge
Hydrologic Impairment	Grazing Cattle and Incised Channel	Incised Channel	Ditched	Ditched
Native vegetation community	Forested	Cultivated	Cultivated	Cultivated
Percent composition of exotic invasive	0	0	0	0
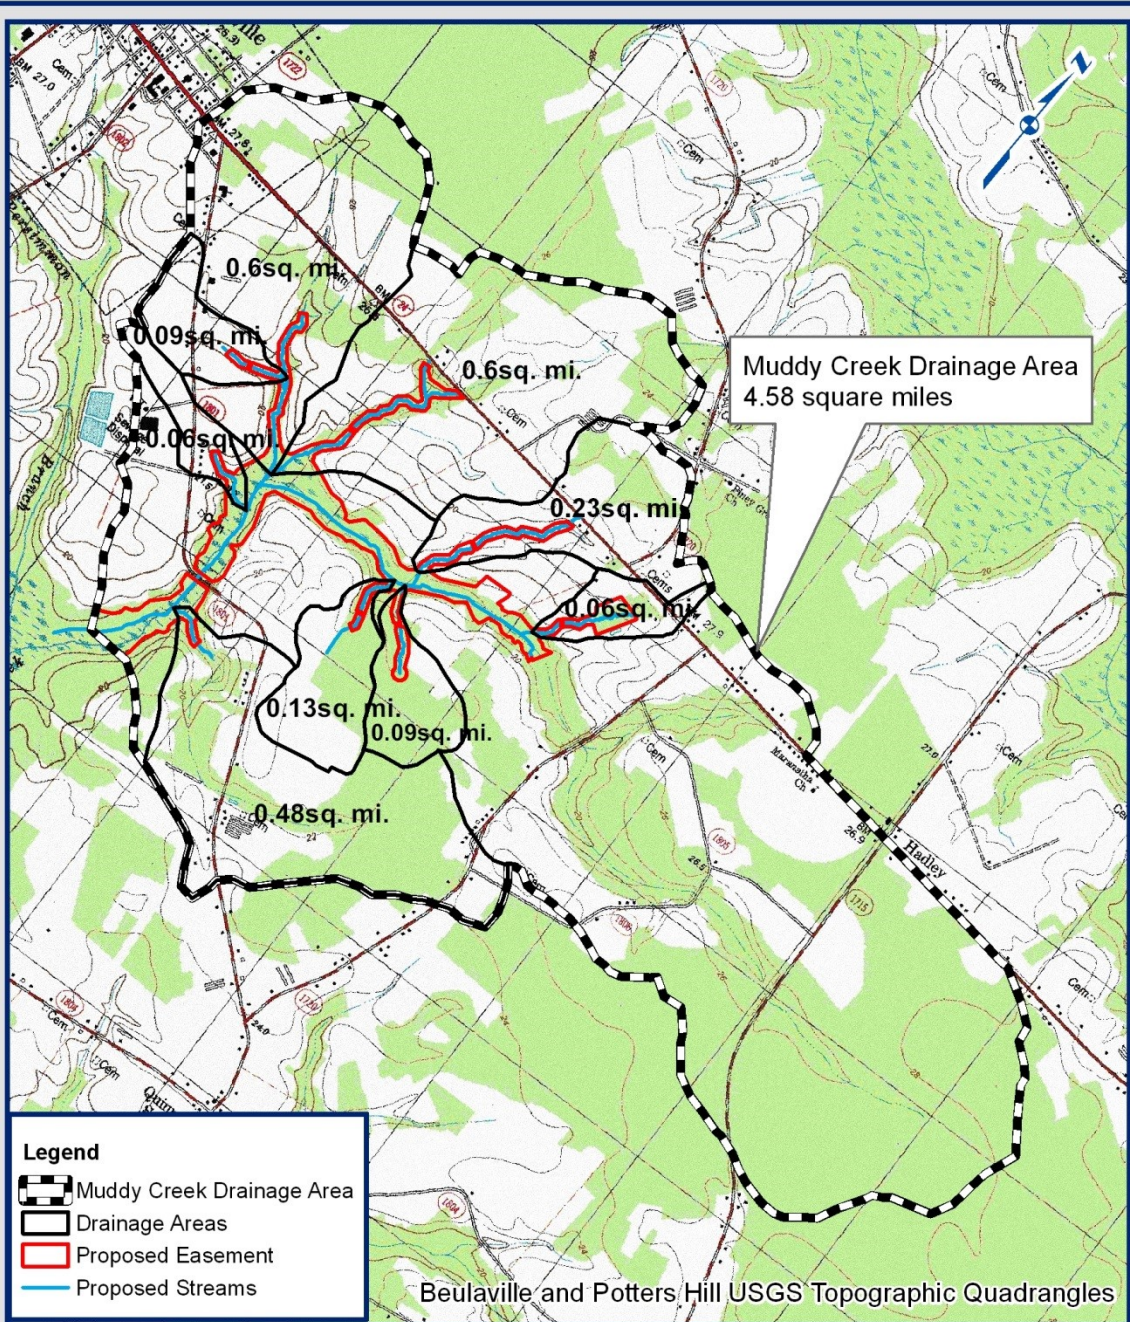
<b>Regulatory Considerations</b>			
<b>Regulation</b>	<b>Applicable</b>	<b>Resolved</b>	<b>Supporting Documentation</b>
Waters of the United States - Section 404	Yes	Yes	SAW-2012-01384
Waters of the United States - Section 401	Yes	Yes	DWR # 13-0865
Endangered Species Act	Yes	Yes	USFWS (Corr. Letter)
Historic Preservation Act	Yes	Yes	SHPO (Corr. Letter)
Coastal Zone Management Act (CZMA)/Coastal Area Management Act (CAMA)	No	NA	N/A
FEMA Floodplain Compliance	Yes	Yes	EEP Floodplain Requirements Checklist
Essential Fisheries Habitat	No	NA	N/A



**Legend**

-  Muddy Creek Drainage Area
-  Drainage Areas
-  Proposed Easement
-  Proposed Streams


Beulaville and Potters Hill USGS Topographic Quadrangles

Figure 2.  
 USGS Map  
 Best Stream and Wetland Mitigation Site

0 1,500 3,000 6,000 Feet

1 inch = 3,000 feet



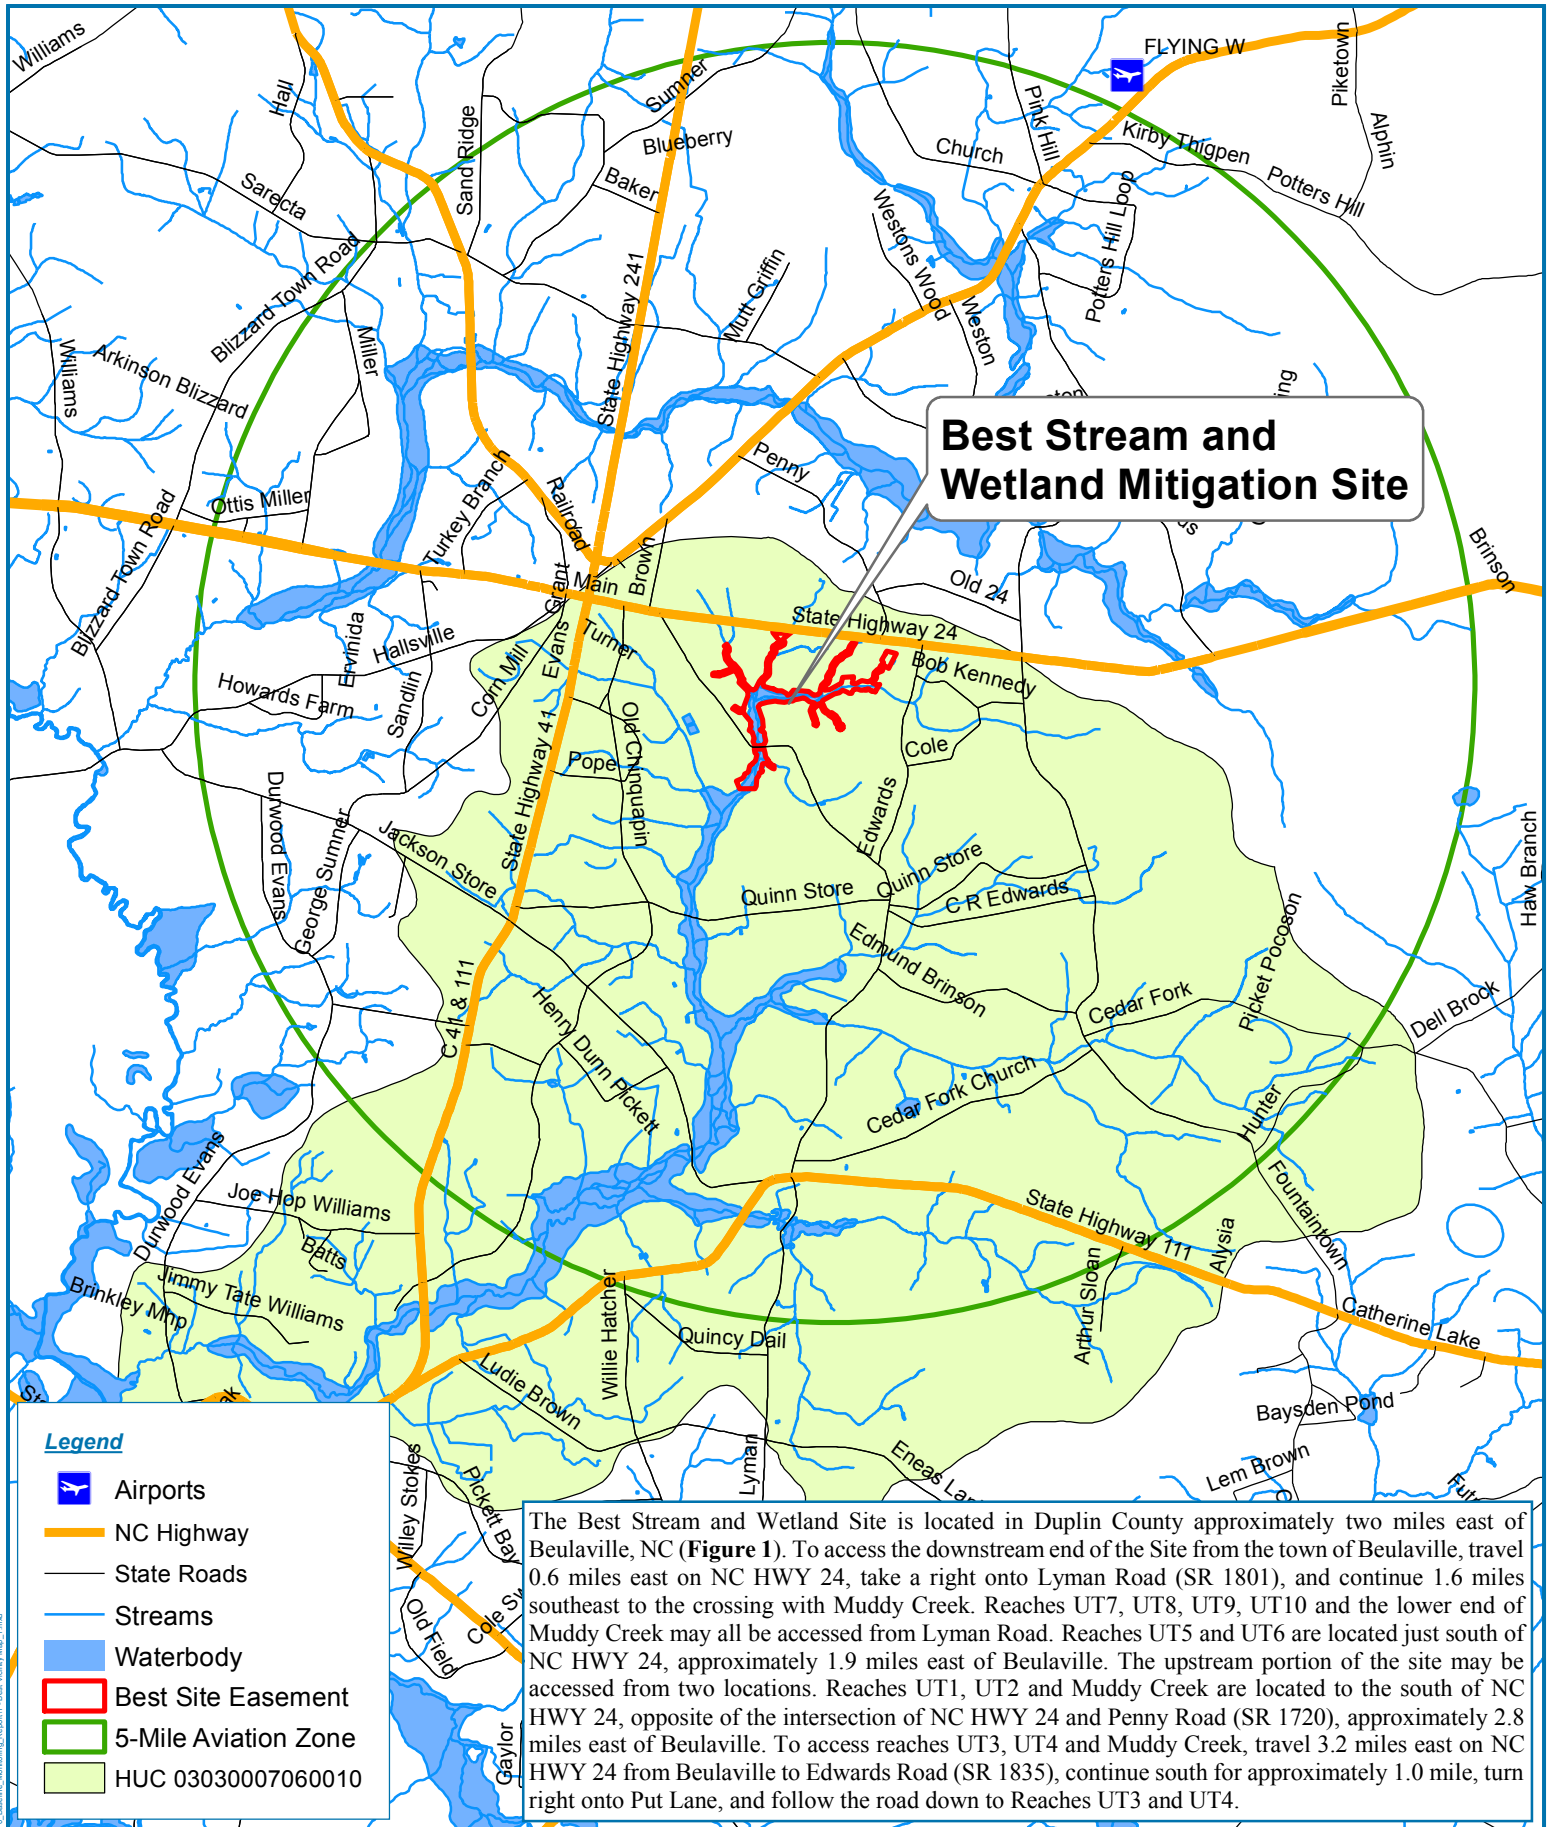


**Best Stream and Wetland Mitigation Site**

**Legend**

- Airports
- NC Highway
- State Roads
- Streams
- Waterbody
- Best Site Easement
- 5-Mile Aviation Zone
- HUC 03030007060010

The Best Stream and Wetland Site is located in Duplin County approximately two miles east of Beulaville, NC (**Figure 1**). To access the downstream end of the Site from the town of Beulaville, travel 0.6 miles east on NC HWY 24, take a right onto Lyman Road (SR 1801), and continue 1.6 miles southeast to the crossing with Muddy Creek. Reaches UT7, UT8, UT9, UT10 and the lower end of Muddy Creek may all be accessed from Lyman Road. Reaches UT5 and UT6 are located just south of NC HWY 24, approximately 1.9 miles east of Beulaville. The upstream portion of the site may be accessed from two locations. Reaches UT1, UT2 and Muddy Creek are located to the south of NC HWY 24, opposite of the intersection of NC HWY 24 and Penny Road (SR 1720), approximately 2.8 miles east of Beulaville. To access reaches UT3, UT4 and Muddy Creek, travel 3.2 miles east on NC HWY 24 from Beulaville to Edwards Road (SR 1835), continue south for approximately 1.0 mile, turn right onto Put Lane, and follow the road down to Reaches UT3 and UT4.

**Figure 1**  
**Project Vicinity Map**  
**Best Stream and Wetland Restoration Site**  
**Duplin County, North Carolina**



Date: 9/15/2015

Drawn by: BSH



# **Appendix B**

## **Visual Assessment Data**

Figure 3. Current Conditions Plan View Map (CCPV)

Table 5. Visual Stream Morphology Stability Assessment

Table 6. Vegetation Condition Assessment



Table 7. Stream Problem Areas

Table 8. Vegetation Problem Areas

Stream Photos

Vegetation Photos

Stream and Vegetation Problem Area Photos

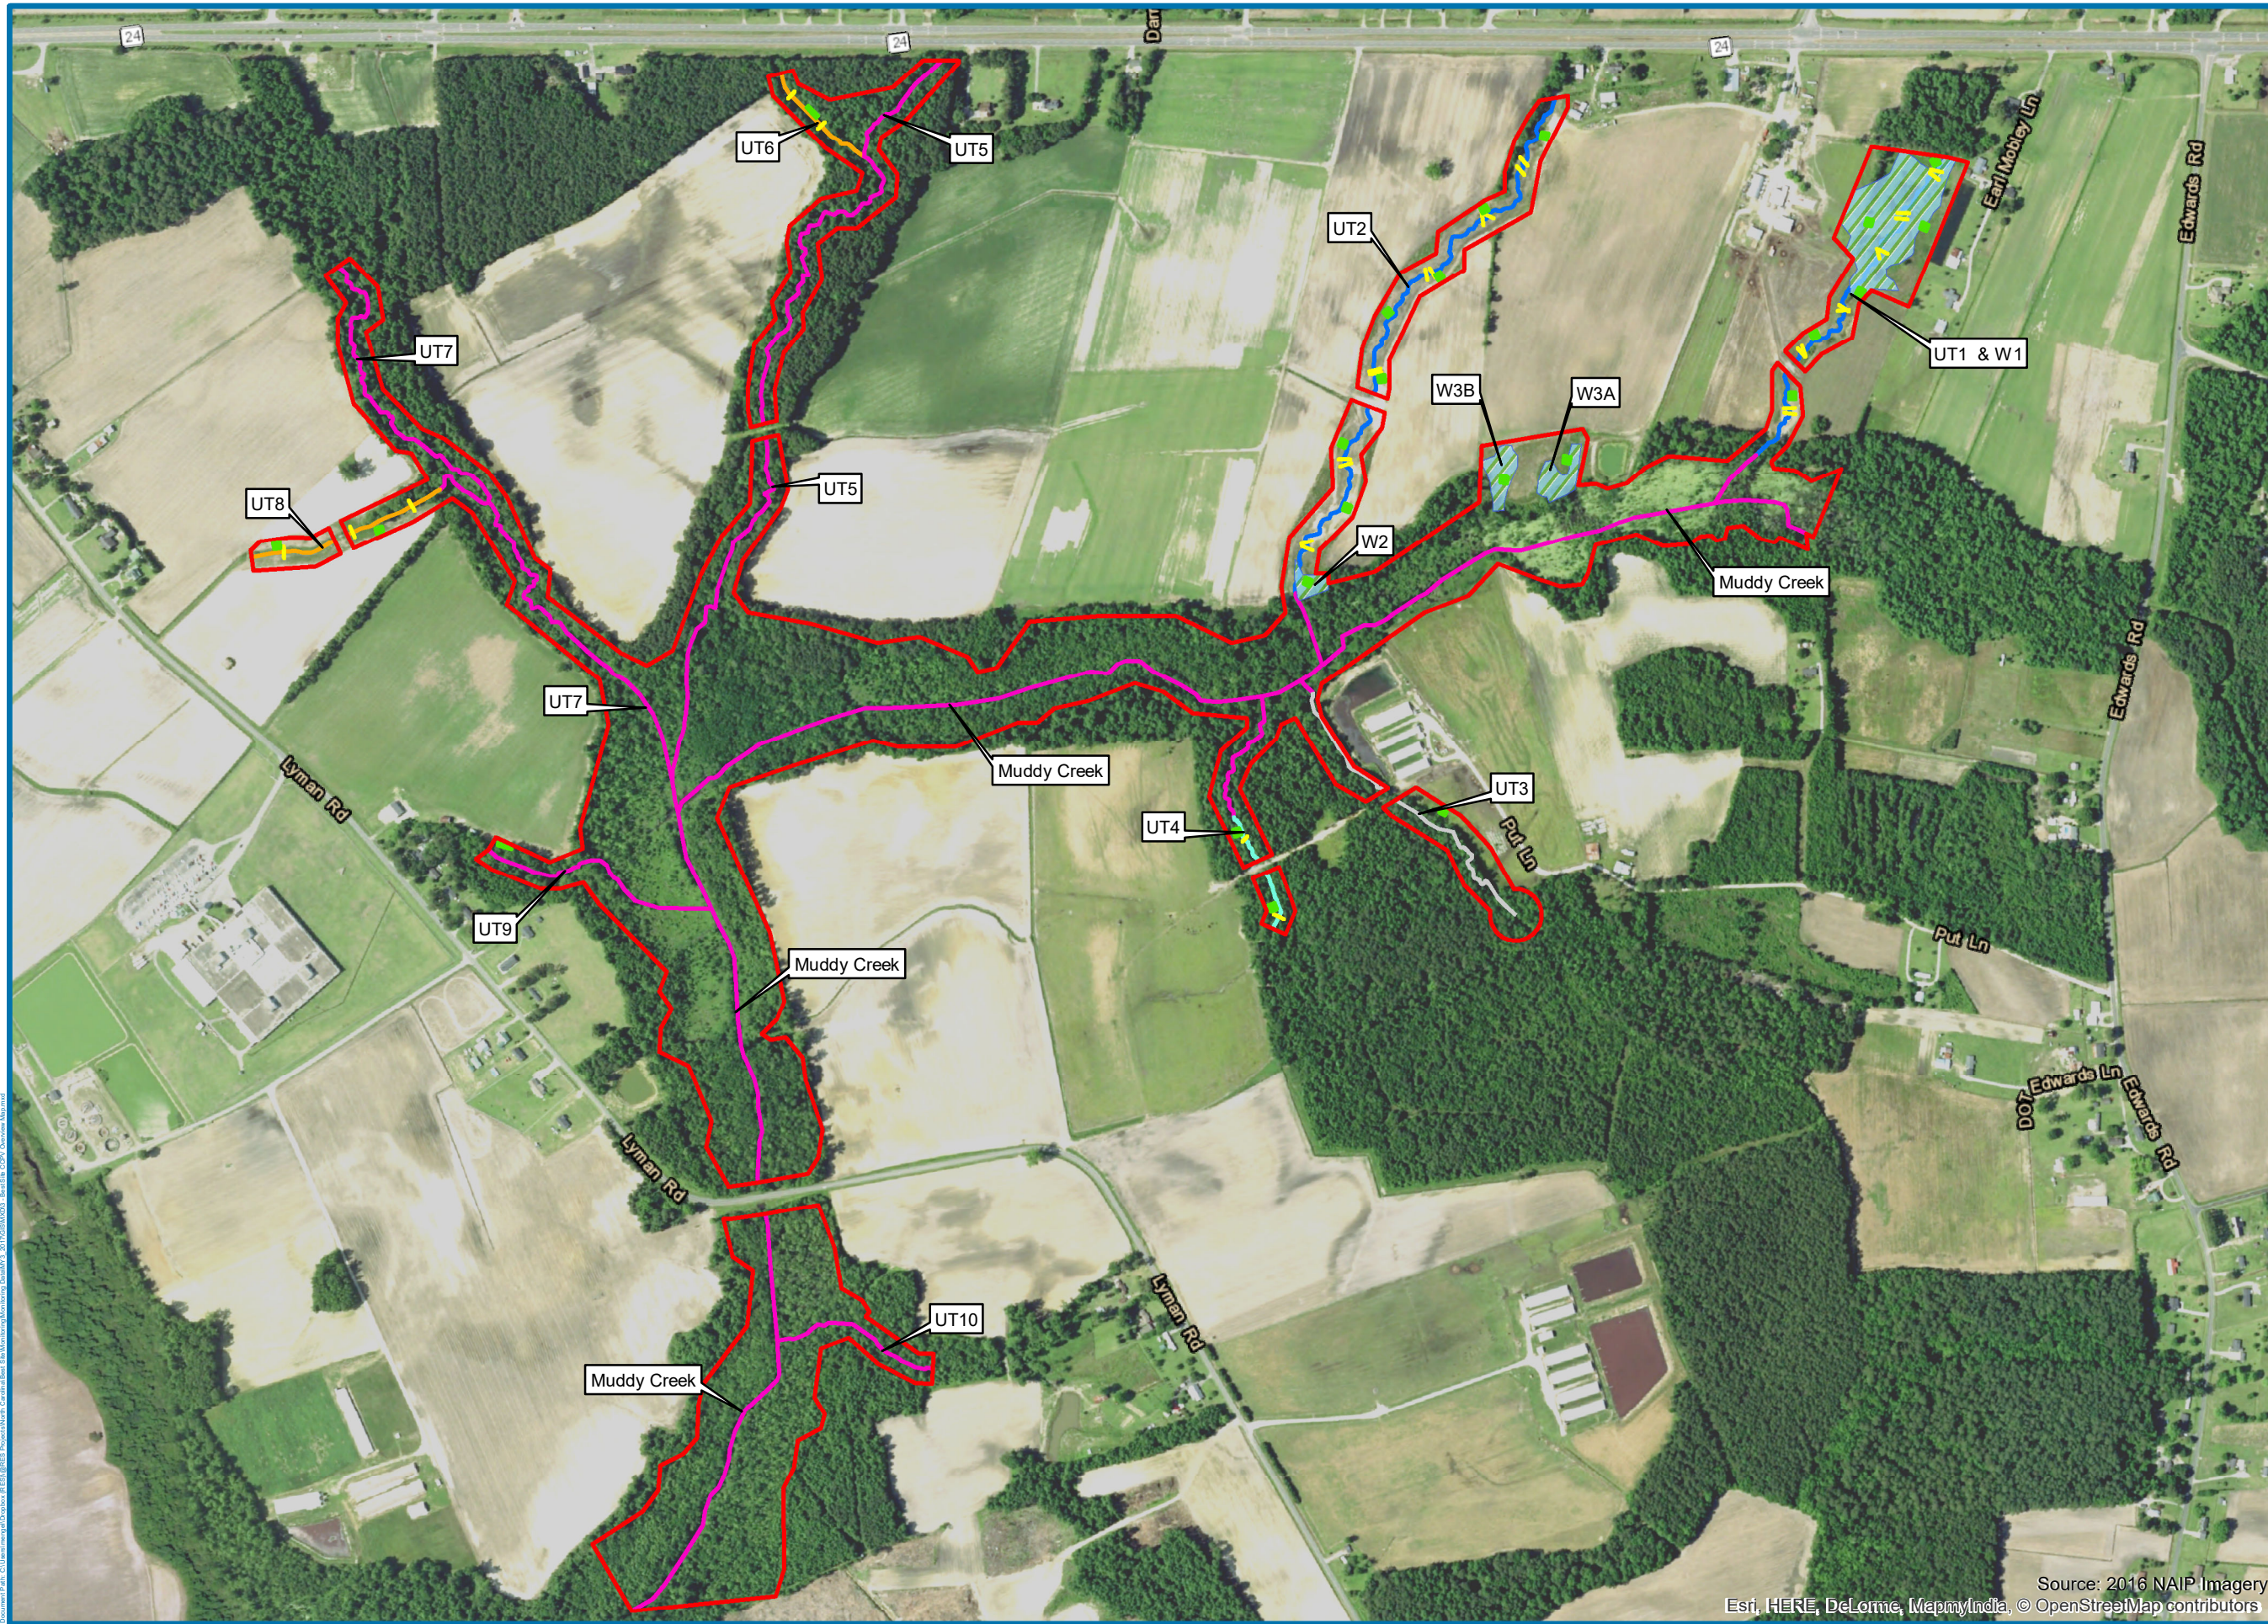

**Figure 3**  
**Best Stream and Wetland**  
**Restoration Project**  
**MY 3 2017**  
**Current Conditions**  
**Overview Map**

Date: 11/22/2017      Drawn by: MDE  
 Review by: xxxxx

- Legend**
- ▭ Conservation Easement
  - ▭ Vegetation Plots
  - ▭ Cross Sections
  - ▭ Wetland Restoration Areas
  - ▭ BE & Preservation
  - ▭ Enhancement I
  - ▭ Enhancement II
  - ▭ Headwater Valley Rest.
  - ▭ P1 Restoration

**Riparian Buffer Conditions**

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill	<span style="background-color: yellow;">▭</span>	<span style="background-color: red;">▭</span>
Present	<span style="background-color: yellow;">▭</span>	<span style="background-color: yellow;">▭</span>	<span style="background-color: red;">▭</span>
Common	<span style="background-color: red;">▭</span>	<span style="background-color: red;">▭</span>	<span style="background-color: red;">▭</span>

Source: 2016 NAIP Imagery  
 Esri, HERE, DeLorme, MapmyIndia, © OpenStreetMap contributors


### Success Criteria

#### Vegetation Plots

- Meeting Success Criteria
- Not Meeting Success Criteria

#### Well Hydroperiod

- ⊗ ≥ 9%
- ⊗ 5-8%
- ⊗ < 5%



**Figure 3a**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT1 & W1**  
**Current Conditions**  
**Plan View Map**

Date: 12/4/2017      Drawn by: MDE  
 Review by: xxxx

### Legend


- Conservation Easement
- Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- ★ Crest Gauge/RG Locations
- Wetland Restoration Areas

### Riparian Buffer Conditions

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			



Source: 2016 NC Onemap Aerial Imagery



**Figure 3b**  
Best Stream and Wetland  
Restoration Project  
MY 3 2017  
**UT1 & Muddy Creek  
Current Conditions  
Plan View Map**


Date: 1/29/2018 Drawn by: MDE  
Review by: xxxx

**Legend**

- Conservation Easement
- + Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- ★ Crest Gauge/RG Locations
- Wetland Restoration Areas

**Riparian Buffer Conditions**

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			

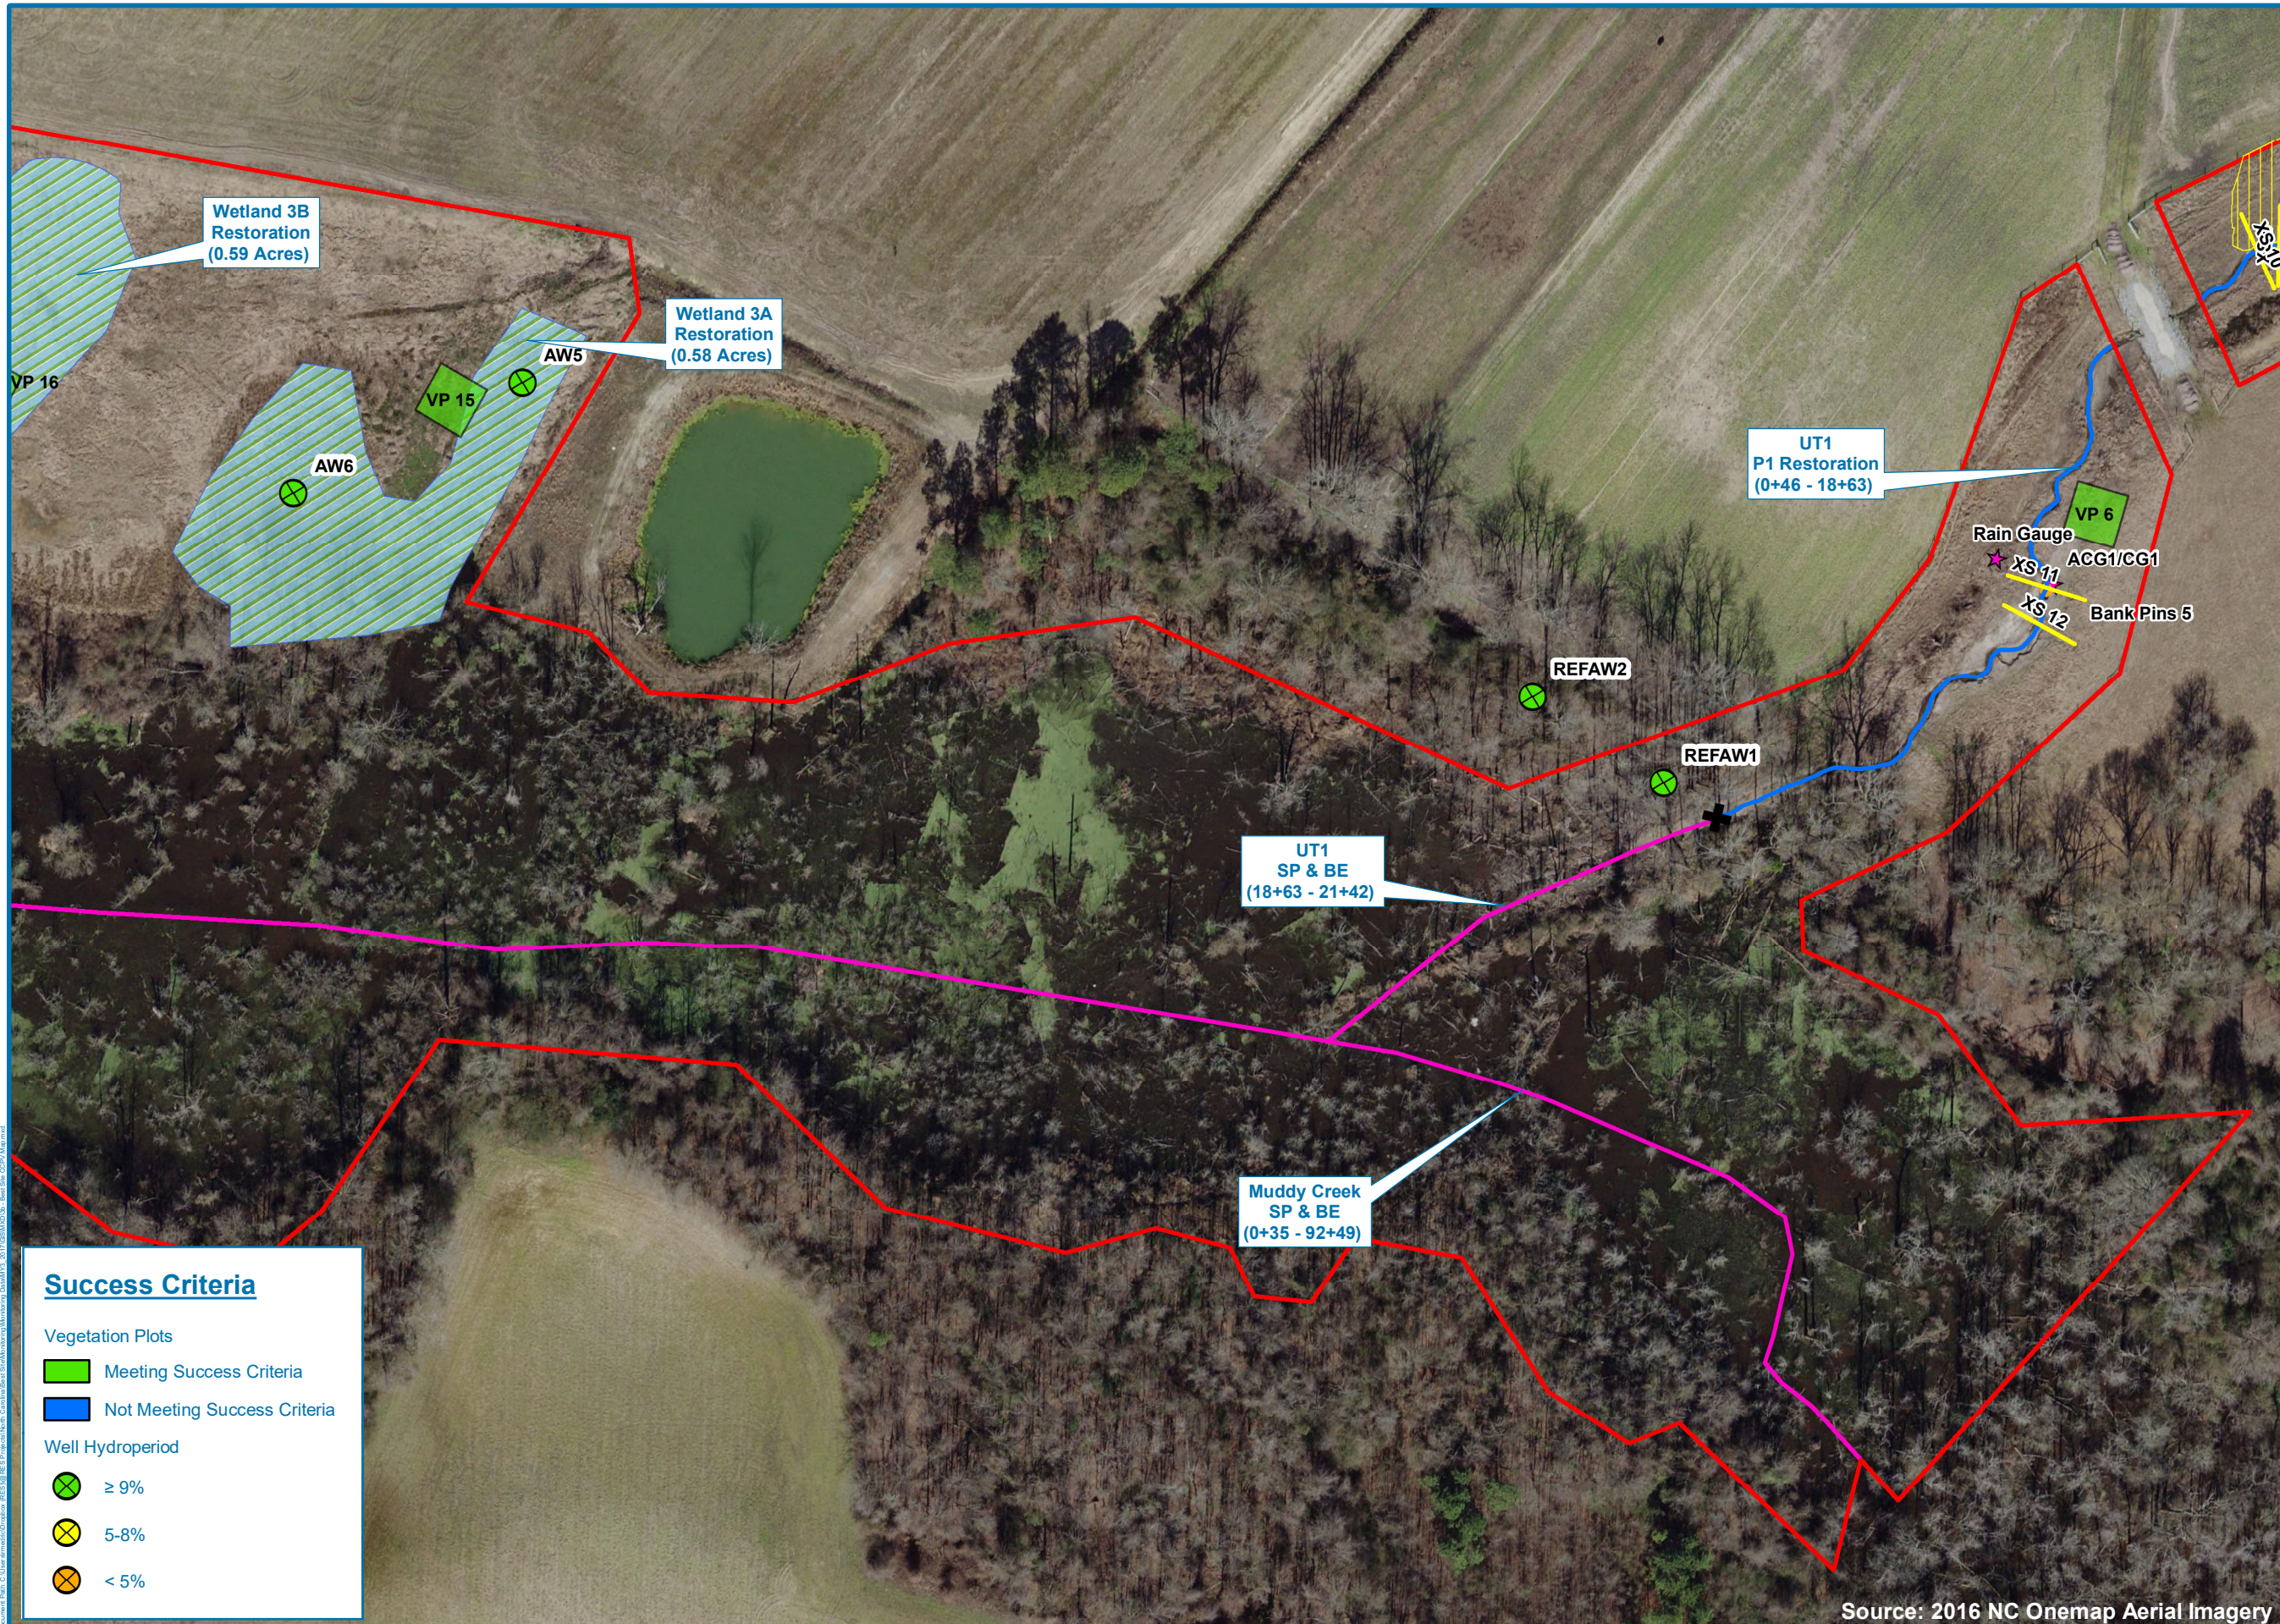


**Success Criteria**

- Vegetation Plots**
- Meeting Success Criteria
  - Not Meeting Success Criteria
- Well Hydroperiod**
- ≥ 9%
  - 5-8%
  - < 5%

Source: 2016 NC Onemap Aerial Imagery

Document Path: C:\Users\mde\Documents\RES\GIS\Projects\Wetland\WetlandRestoration\MapDocs\20170201\03b - Best Site CCM Map.mxd





**Figure 3c**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT2 & Muddy Creek**  
**Current Conditions**  
**Plan View Map**

Date: 12/4/2017 Drawn by: MDE  
 Review by: xxxx

**Success Criteria**

Vegetation Plots

- Meeting Success Criteria
- Not Meeting Success Criteria

Well Hydroperiod


- ≥ 9%
- 5-8%
- < 5%

**Legend**

- Conservation Easement
- Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- Crest Gauge/RG Locations
- Wetland Restoration Areas

**Riparian Buffer Conditions**


Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			

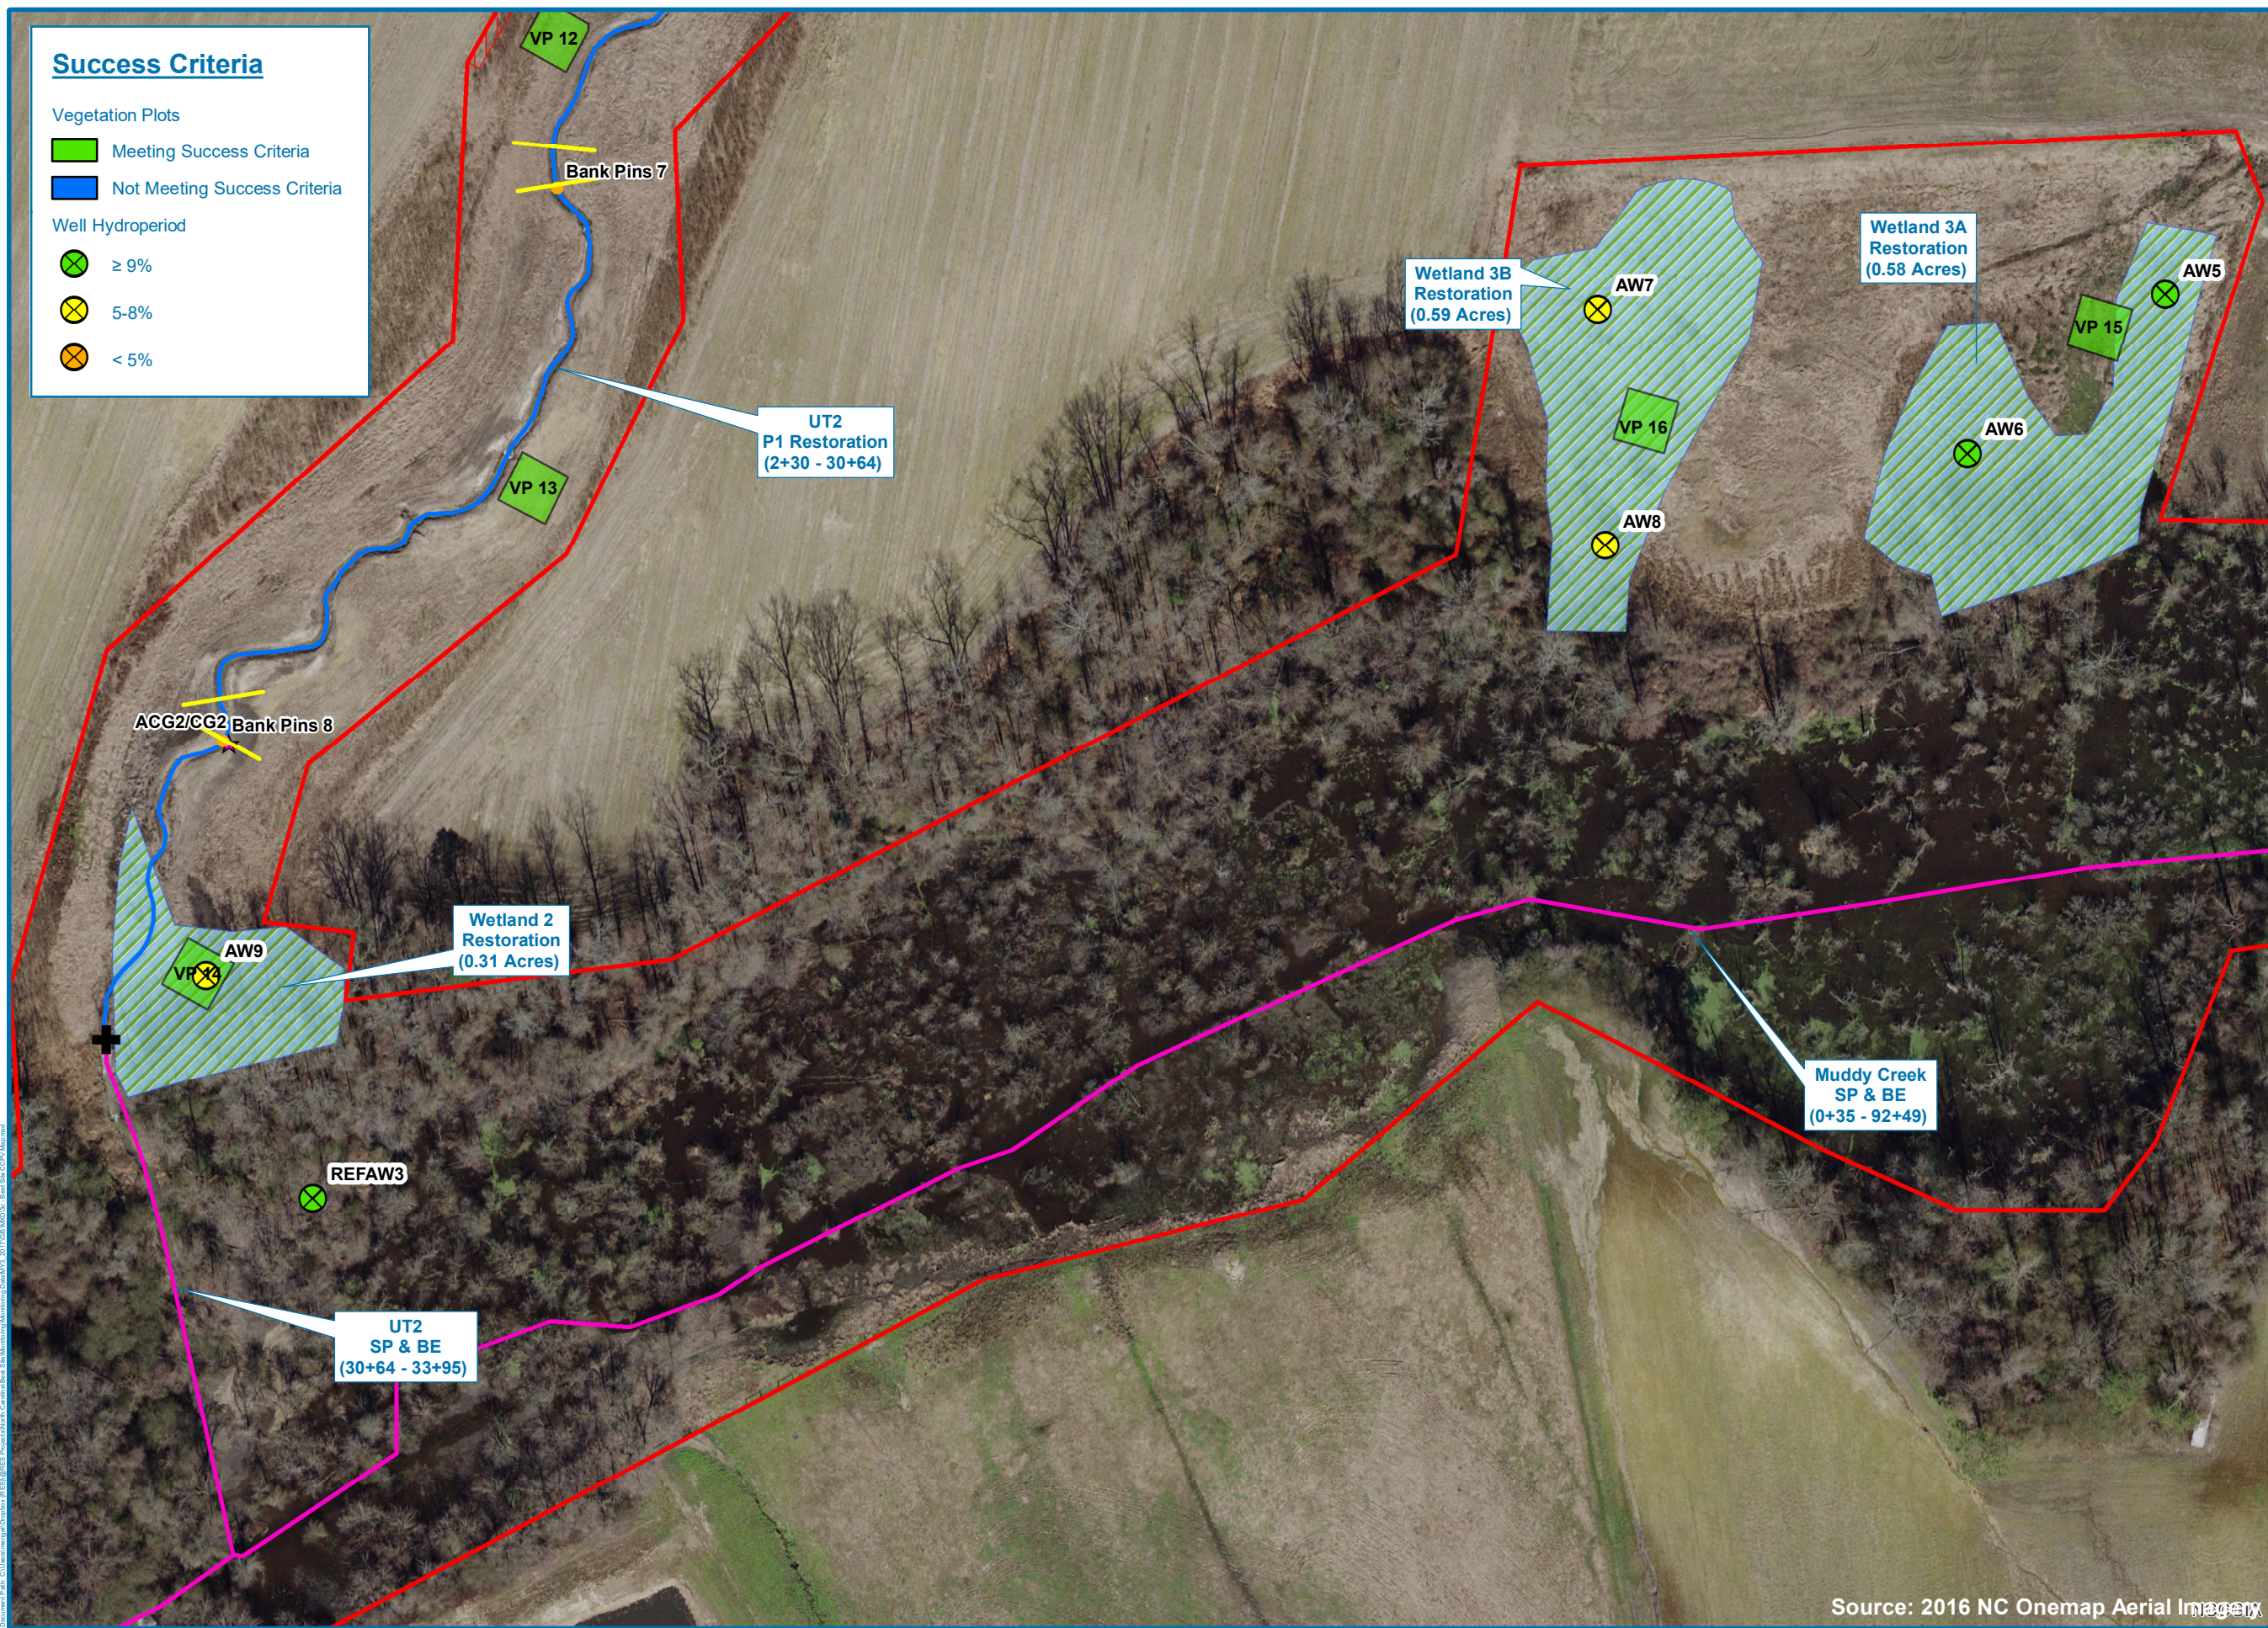

Source: 2016 NC Onemap Aerial Imagery

### Success Criteria

- Vegetation Plots**
- Meeting Success Criteria
  - Not Meeting Success Criteria
- Well Hydroperiod**
- ≥ 9%
  - 5-8%
  - < 5%



**Figure 3d**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT2**  
**Current Conditions**  
**Plan View Map**

Date: 12/4/2017 Drawn by: MDE  
 Review by: xxx

### Legend

- Conservation Easement
- Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- Crest Gauge/RG Locations
- Wetland Restoration Areas

### Riparian Buffer Conditions

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			



Source: 2016 NC Onemap Aerial Imagery


### Success Criteria

#### Vegetation Plots

- Meeting Success Criteria
- Not Meeting Success Criteria

#### Well Hydroperiod

- + ≥ 9%
- + 5-8%
- + < 5%



1 inch = 100 feet

**Figure 3e**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT2 & Muddy Creek**  
**Current Conditions**  
**Plan View Map**

Date: 12/4/2017 Drawn by: MDE  
 Review by: xxxx

### Legend

- Conservation Easement
- + Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- + Bankpin Locations
- Cross Sections
- ★ Crest Gauge/RG Locations
- Wetland Restoration Areas

### Riparian Buffer Conditions

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			



Source: 2016 NC Onemap Aerial Imagery




**Success Criteria**

Vegetation Plots

- Meeting Success Criteria
- Not Meeting Success Criteria

Well Hydroperiod

- ≥ 9%
- 5-8%
- < 5%



**Figure 3f**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT3**  
**Current Conditions**  
**Plan View Map**


Date: 12/12/2017 Drawn by: MDE  
 Review by: xxxx

**Legend**

- Conservation Easement
- Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- Crest Gauge/RG Locations
- Wetland Restoration Areas

**Riparian Buffer Conditions**

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			

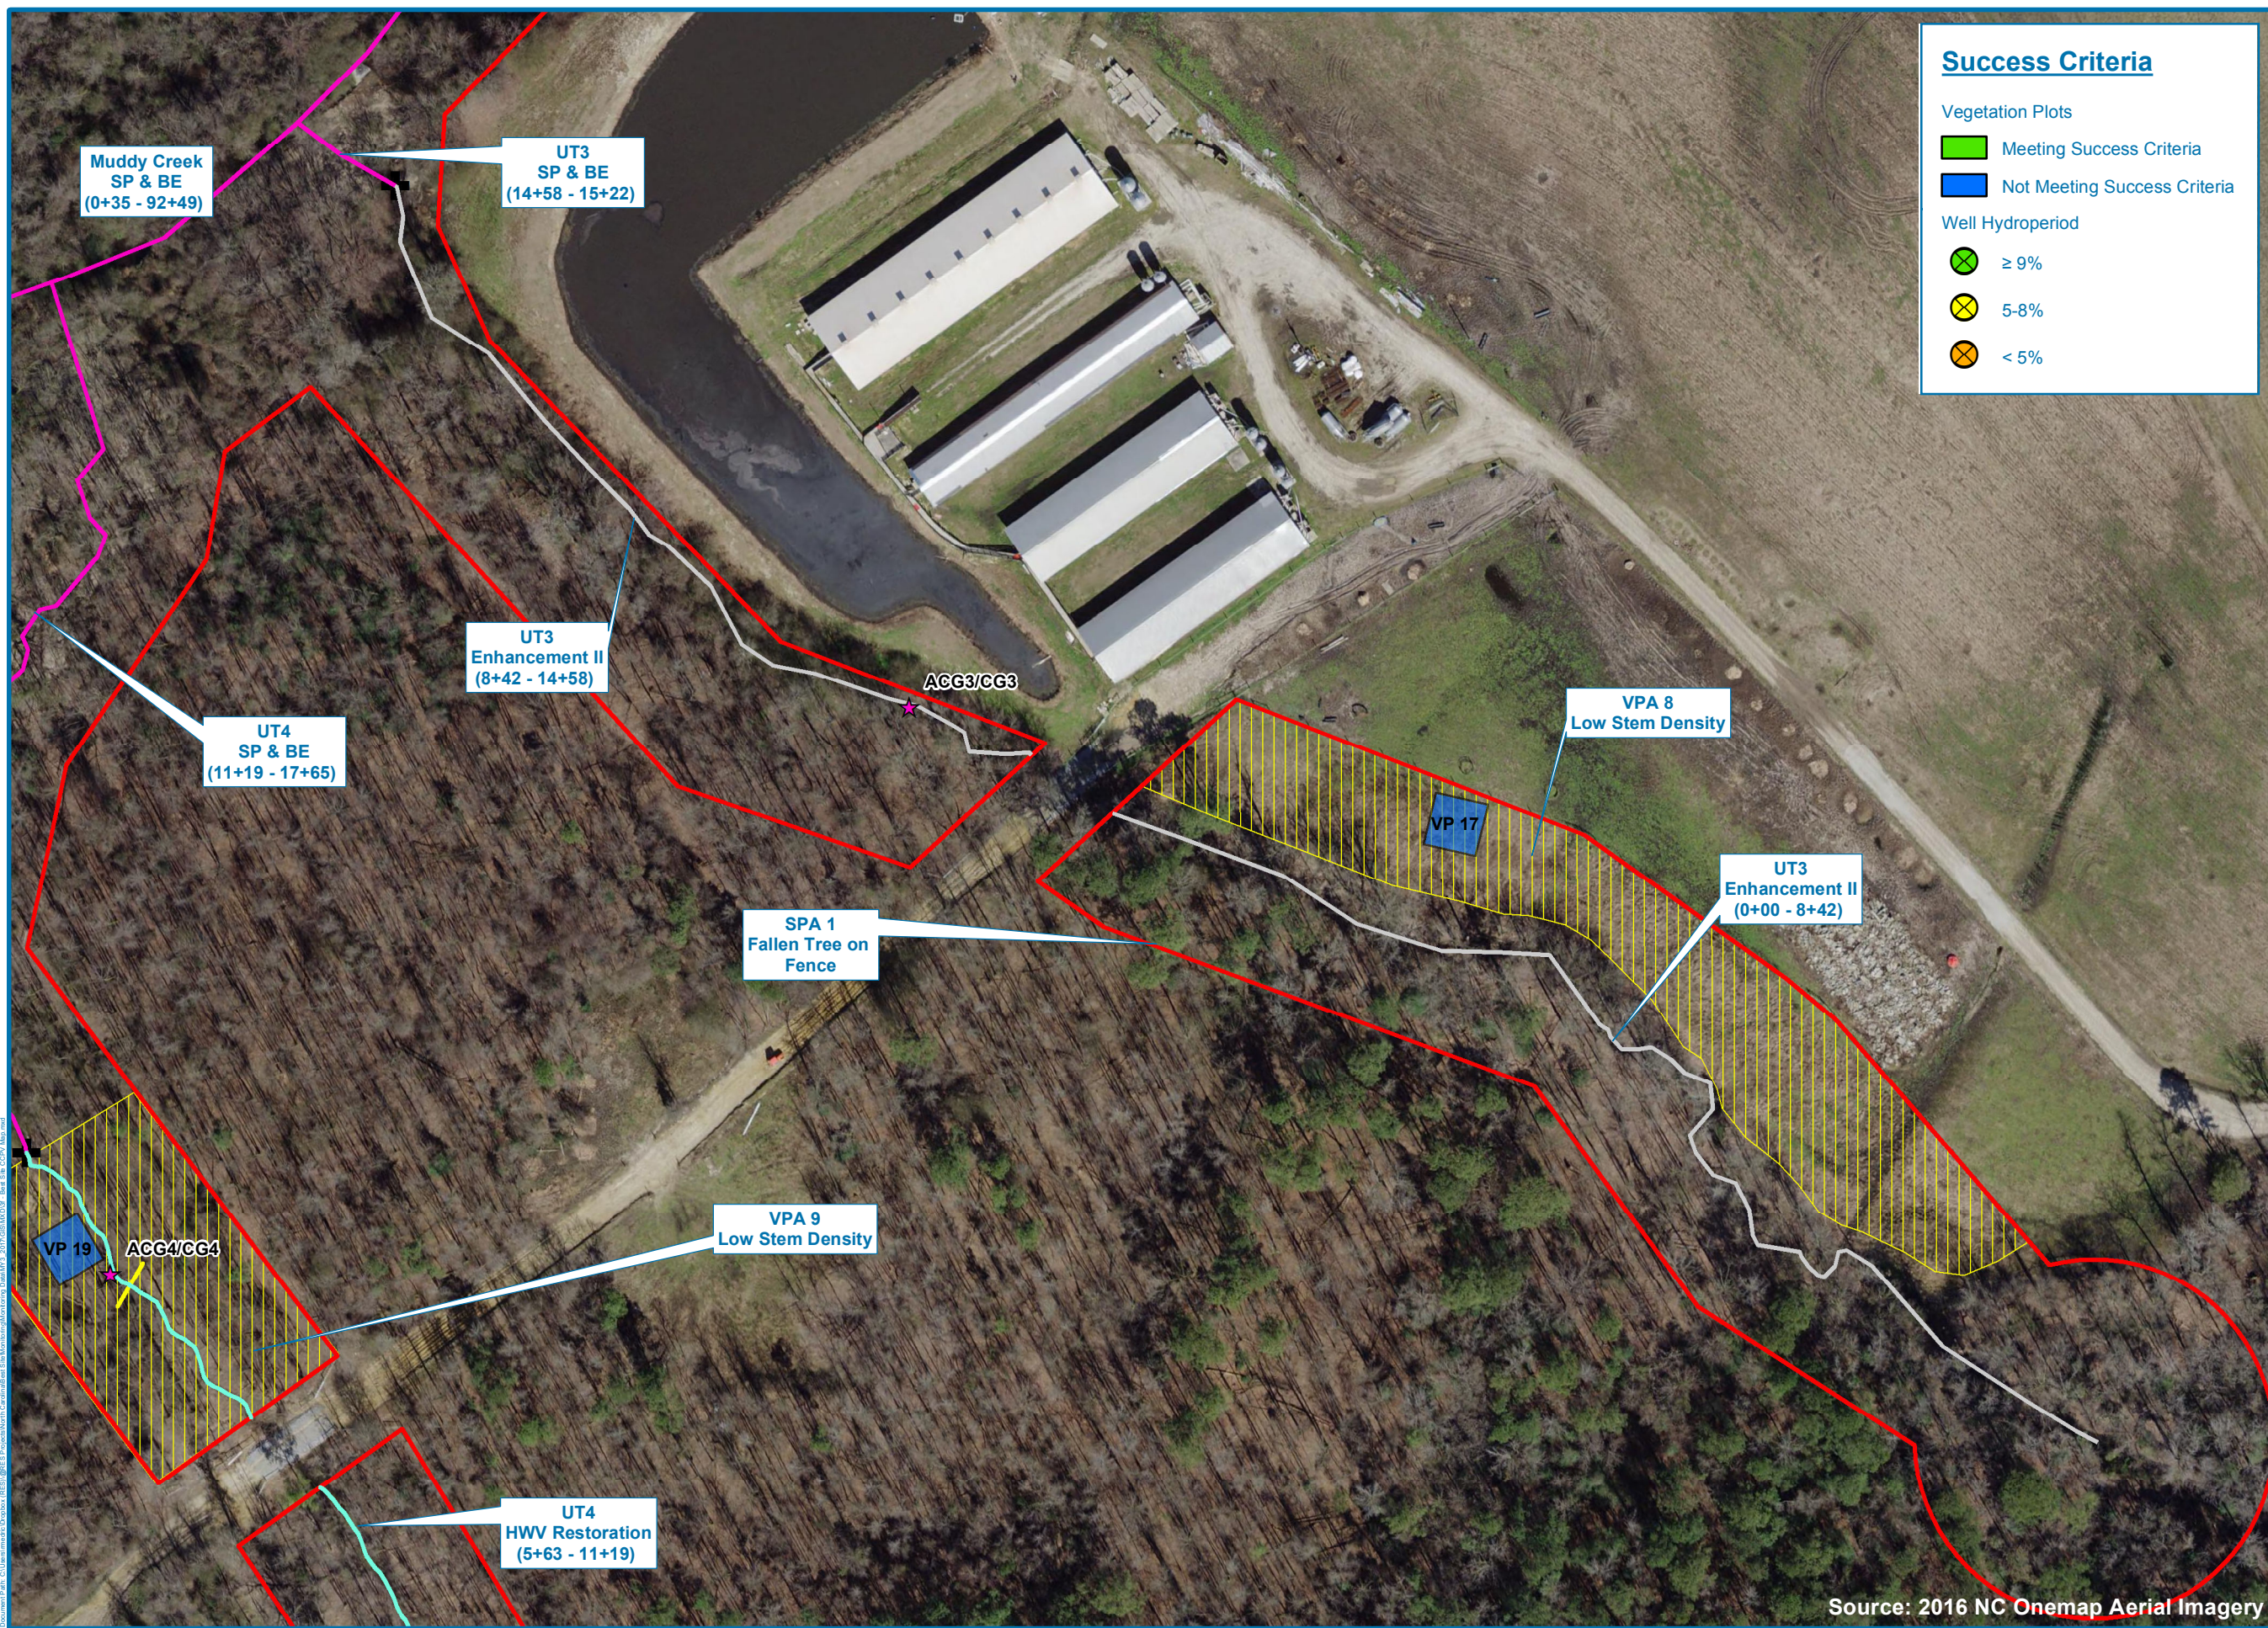

Source: 2016 NC Onemap Aerial Imagery



### Success Criteria

#### Vegetation Plots

- Meeting Success Criteria
- Not Meeting Success Criteria

#### Well Hydroperiod

- ⊗ ≥ 9%
- ⊗ 5-8%
- ⊗ < 5%



1 inch = 100 feet

**Figure 3g**

### Best Stream and Wetland Restoration Project MY 3 2017

### UT4 & Muddy Creek Current Conditions Plan View Map


Date: 12/4/2017 Drawn by: MDE  
Review by: xxxx

#### Legend

- Conservation Easement
- + Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- ★ Crest Gauge/RG Locations
- Wetland Restoration Areas

#### Riparian Buffer Conditions

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			

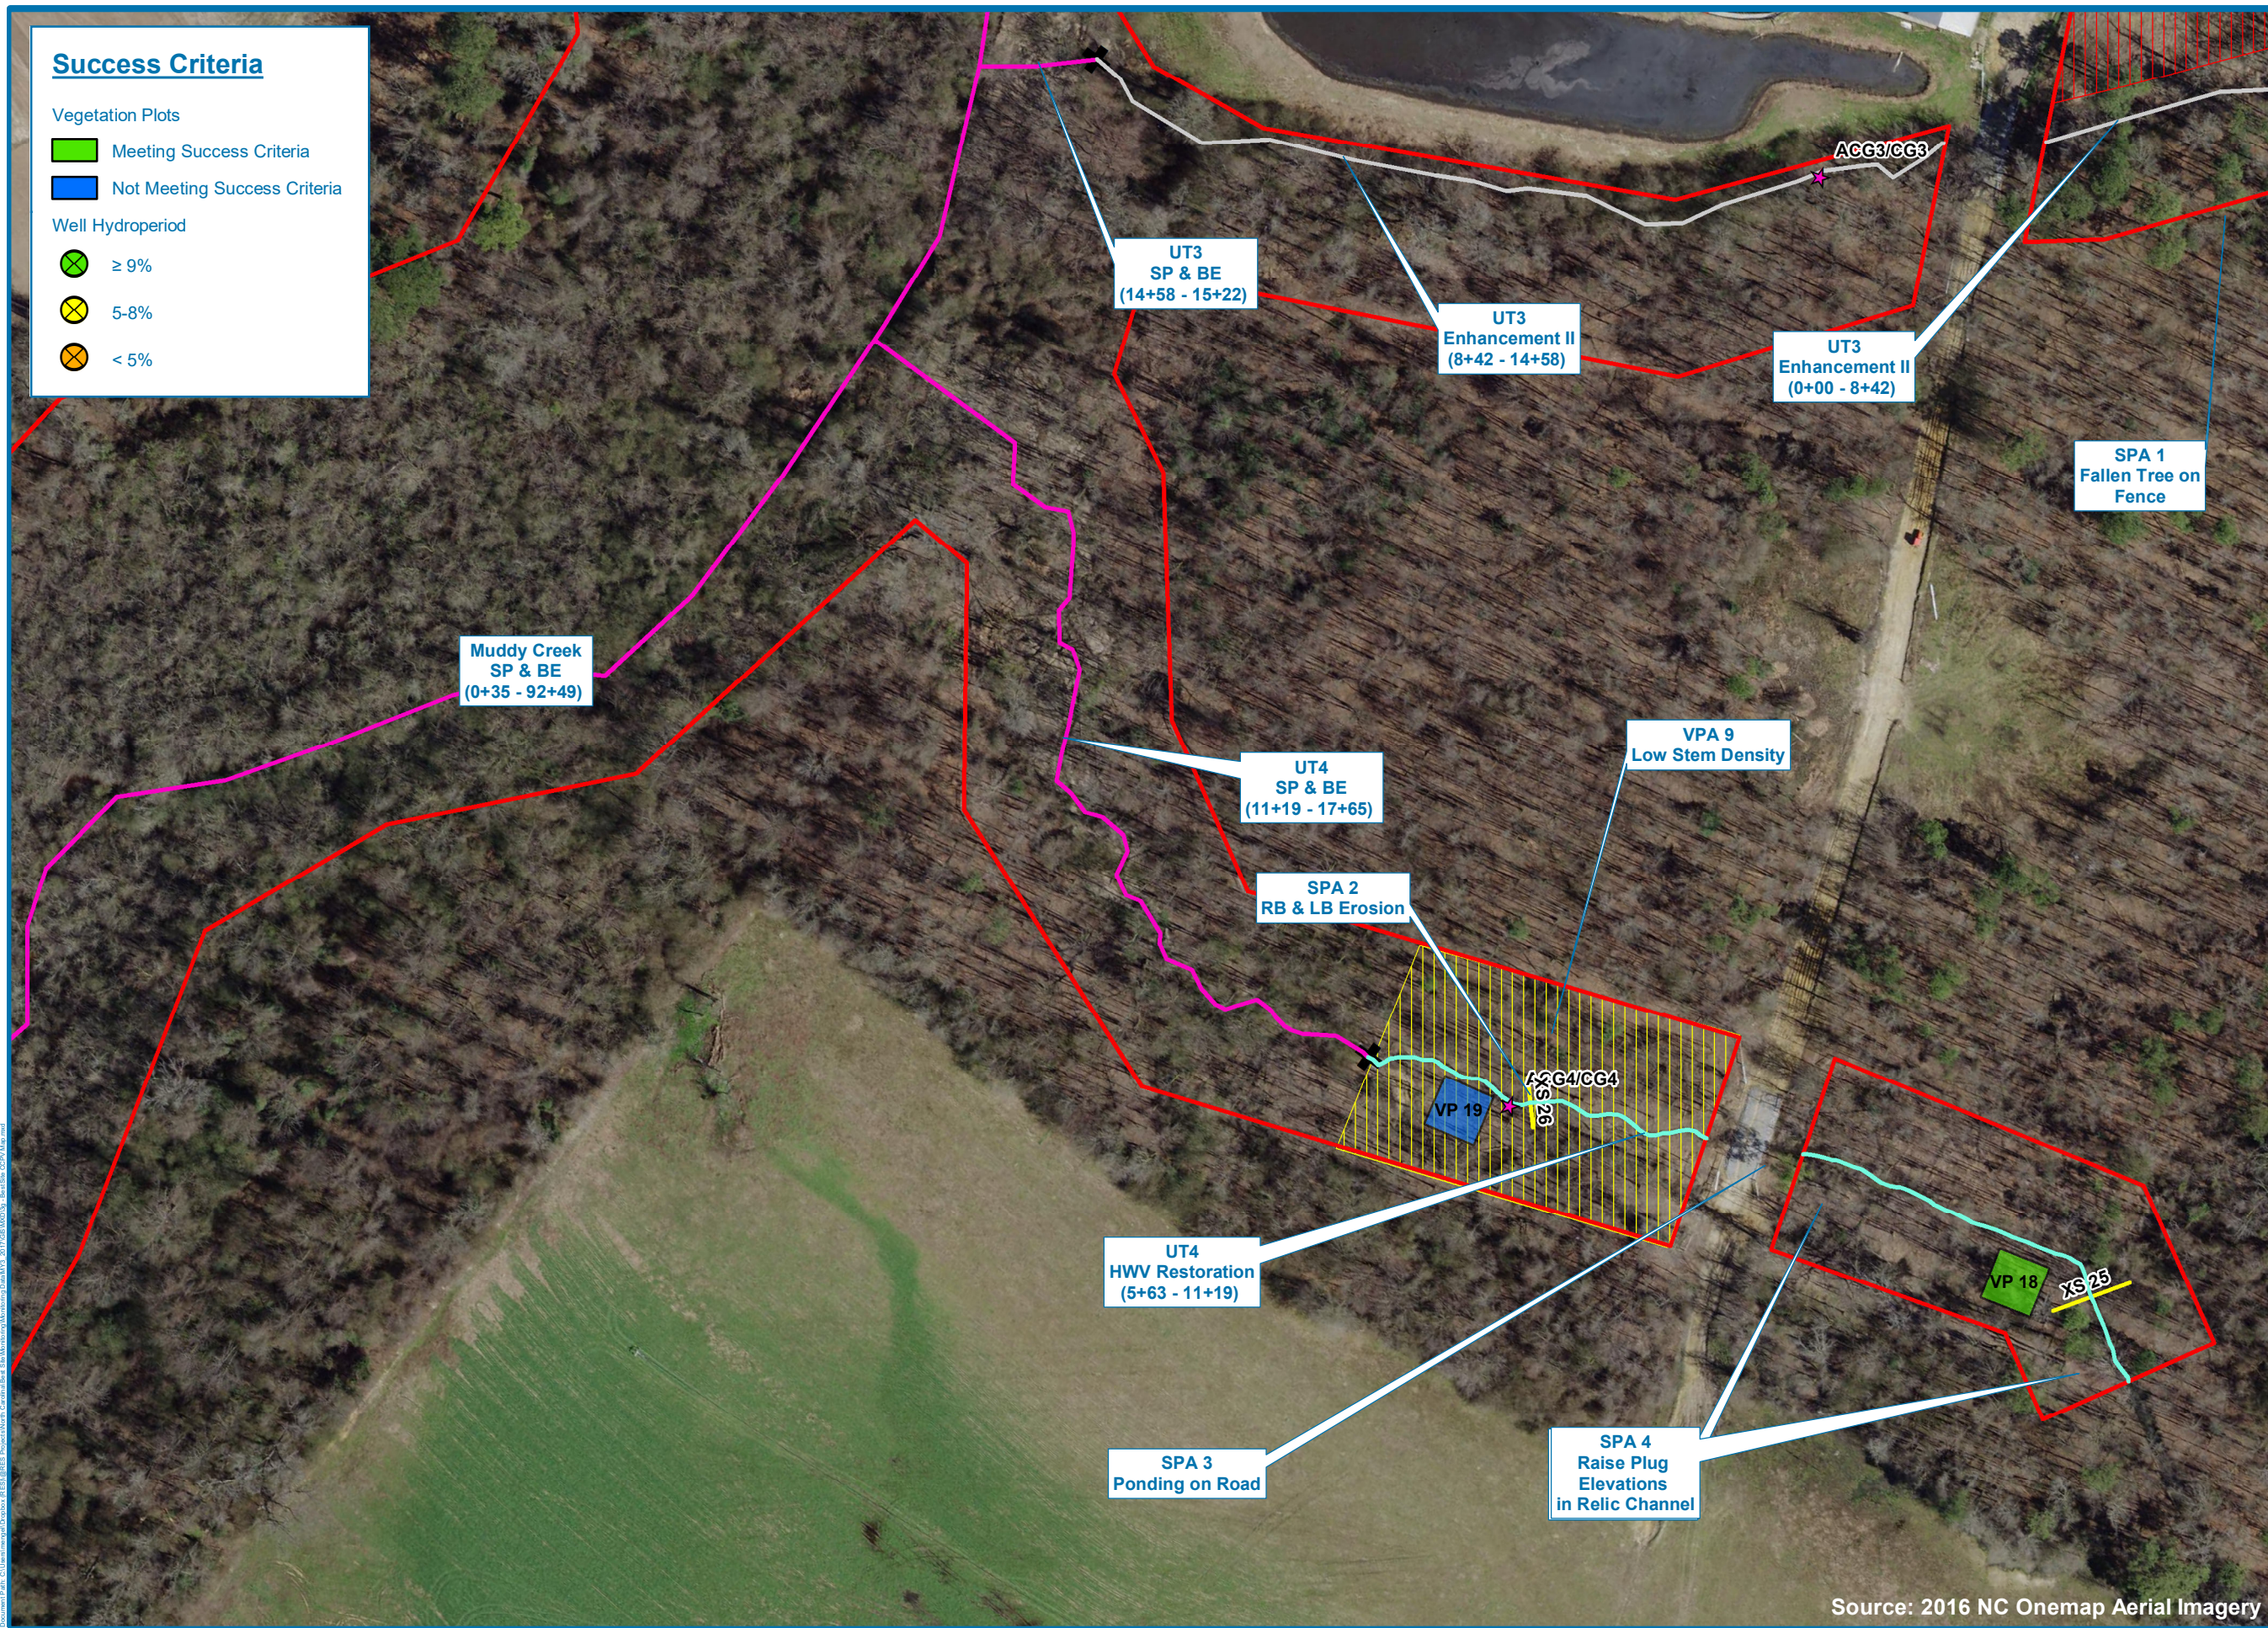


Source: 2016 NC Onemap Aerial Imagery

Document Path: C:\arcgis\work\Documents\GIS\BIES\Project\Outputs\Carto\Map3\Map3\_20170810\_MXD\3g\_BestStreamWetlandRestorationProject\_My3\_2017\_UT4\_MuddyCreek\_CurrentConditions\_PlanViewMap.mxd

### Success Criteria

- Vegetation Plots**
- Meeting Success Criteria
  - Not Meeting Success Criteria
- Well Hydroperiod**
- ≥ 9%
  - 5-8%
  - < 5%



**Figure 3h**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT5, UT6, UT7, UT8**  
**Current Conditions**  
**Plan View Map**


Date: 12/4/2017 Drawn by: MDE  
 Review by: xxxx

### Legend

- Conservation Easement
- Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- Crest Gauge/RG Locations
- Wetland Restoration Areas

### Riparian Buffer Conditions

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			

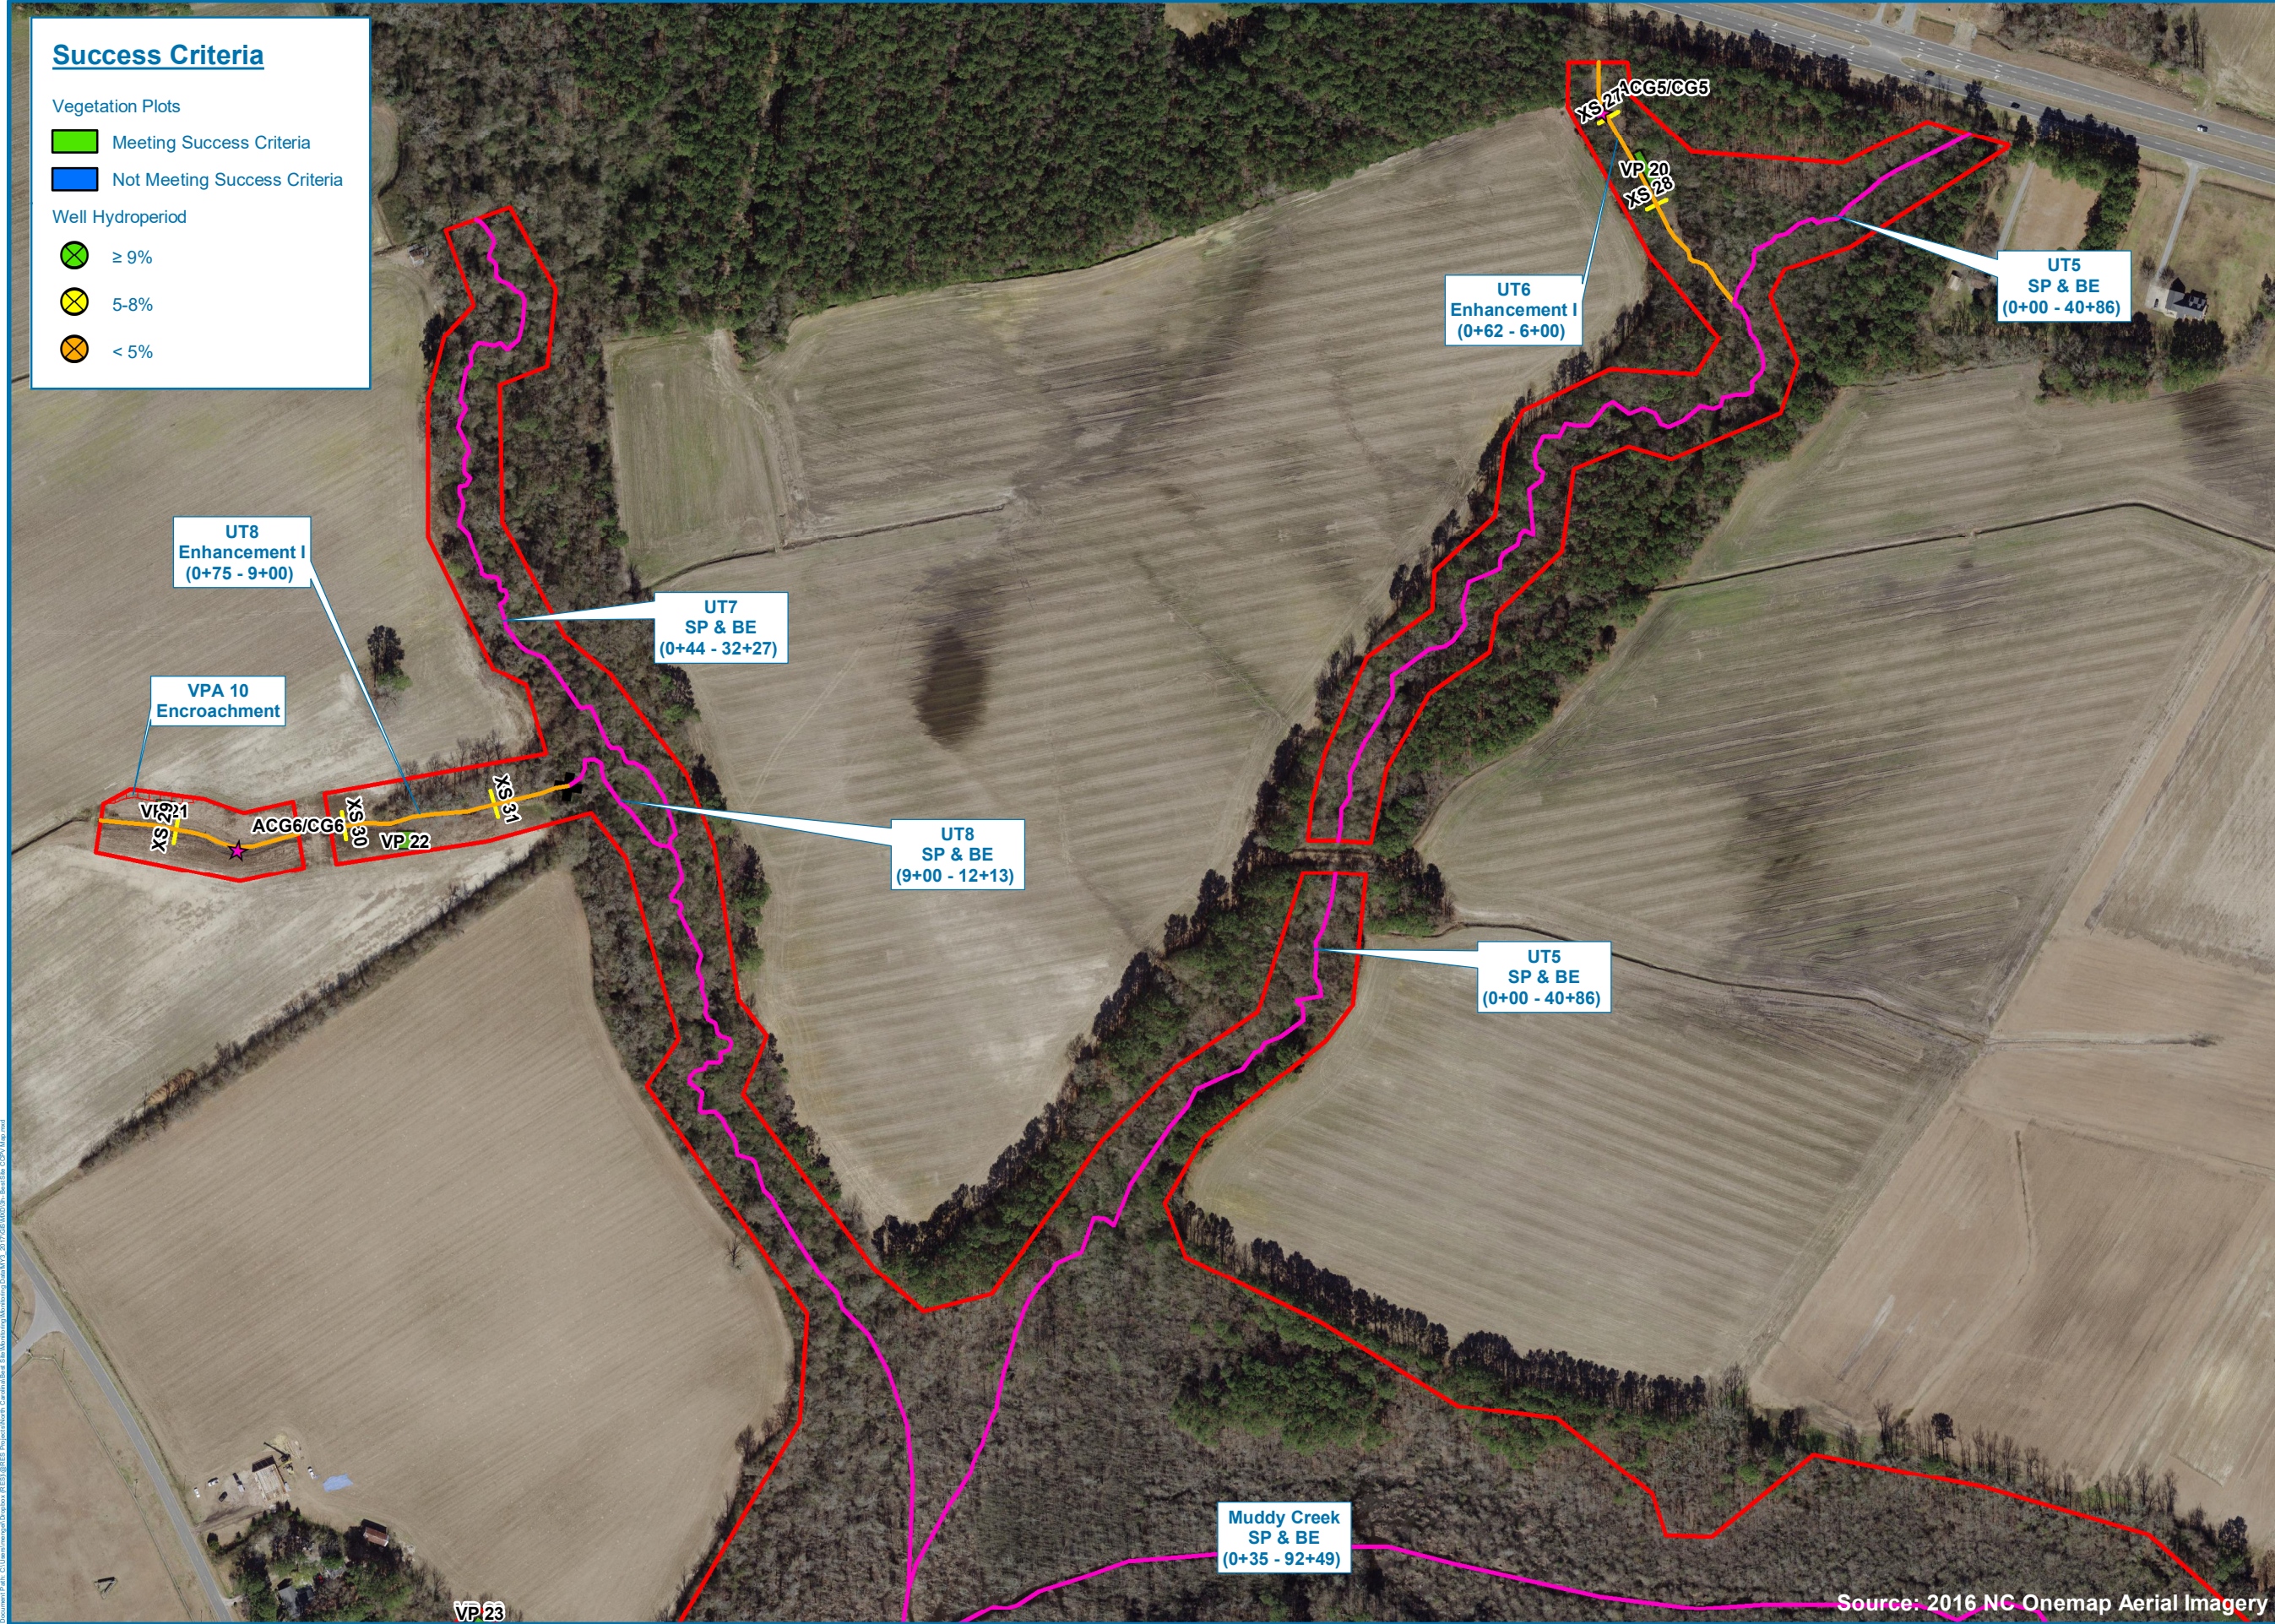


Source: 2016 NC Onemap Aerial Imagery

Document Path: C:\Users\mde\OneDrive\Documents\GIS\BIES\Projects\Stream\Current\Map\Map3h\Map3h\_CCPV\_Map.mxd

**Success Criteria**

- Vegetation Plots
- Meeting Success Criteria
  - Not Meeting Success Criteria
- Well Hydroperiod
- ≥ 9%
  - 5-8%
  - < 5%



**Figure 3i**  
**Best Stream and Wetland Restoration Project**  
**MY 3 2017**  
**UT9, UT10, & Muddy Creek**  
**Current Conditions**  
**Plan View Map**

Date: 12/4/2017      Drawn by: MDE  
 Review by: xxxx

**Legend**

- Conservation Easement
- + Reach Breaks
- BE & Preservation
- Enhancement I
- Enhancement II
- Headwater Valley Rest.
- P1 Restoration
- Stream Structures
- Bankpin Locations
- Cross Sections
- Crest Gauge/RG Locations
- Wetland Restoration Areas

**Riparian Buffer Conditions**

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			
Common			



Source: 2016 NC Onemap Aerial Imagery

Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT1  
 Assessed Length 2036

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	19	19			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	19	19			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	19	19			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence doesnot exceed 15%. (See guidance for this table in EEP monitoring guidance document)	19	19			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq$ 1.6 Rootwads/logs providing some cover at base-flow.	19	19			100%			



Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT2  
 Assessed Length 3103

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	23	23			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	23	23			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	23	23			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence doesnot exceed 15%. (See guidance for this table in EEP monitoring guidance document)	23	23			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq 1.6$ Rootwads/logs providing some cover at base-flow.	23	23			100%			

Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT3  
 Assessed Length 876

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	1	1			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq$ 1.6 Rootwads/logs providing some cover at base-flow.	1	1			100%			

Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT4  
 Assessed Length 1140

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			1	20	99%	0	20	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				1	20	99%	0	0	99%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	6	6			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	6	6			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	6	6			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	6	6			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq 1.6$ Rootwads/logs providing some cover at base-flow.	6	6			100%			

Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT6  
 Assessed Length 538

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	3	3			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq 1.6$ Rootwads/logs providing some cover at base-flow.	3	3			100%			

Table 5 Visual Stream Morphology Stability Assessment  
 Reach ID UT8  
 Assessed Length 765

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank *	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	<b>Totals</b>				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	3	3			100%			
	4. Habitat	Pool forming structures maintaining – Max Pool Depth : Mean Bankfull Depth ratio $\geq$ 1.6 Rootwads/logs providing some cover at base-flow.	3	3			100%			

<b>Table 7. Stream Problem Areas</b>			
<b>Best Stream and Wetland Restoration Project - Project # 95353</b>			
<b>Feature Issue</b>	<b>Station # / Range</b>	<b>Suspected Cause; Repair</b>	<b>Photo Number</b>
<b>Fence Damage</b>	UT 3 - Sta. 7+50	Tree fell on cattle fencing; fence repair needed	SPA 1
<b>Minor Bank Erosion</b>	UT 4 - Sta. 5+60 and 7+00	Rain events and high flows; seems stable, continue to monitor	SPA 2
<b>Ponding on Road</b>	UT 4 - Sta. 8+47 to 8+67	Rain events and high flow; add fill to road to reduce ponding	SPA 3
<b>Relic Channel and Plug Subsidence</b>	UT4- Sta. 8+75 to 11+03	Rain events and high flows; add fill material to raise plugs in relic channel.	SPA 4

<b>Table 8. Vegetation Problem Areas</b>			
<b>Best Stream and Wetland Restoration Project - Project # 95353</b>			
<b>Feature Category</b>	<b>Station Numbers</b>	<b>Suspected Cause; Repair</b>	<b>Photo Number</b>
<b>Low Stem Density</b>	UT1- Sta. 3+00 to 8+50 (0.47 ac)	Low Soil Fertility and compaction; Re-plant area with gallon containerized trees.	VPA 1
<b>Invasives present</b>	UT1 - Sta. 0+00 (0.13 ac)	Invasives present in easement due to offsite seed source; remove invasive by cutting down and herbiciding	VPA 2
<b>Low Stem Density</b>	UT1 - Sta. 4+00 to 6+00 (0.49 ac)	Low Soil Fertility, compaction, and competition with native weeds; Re-plant area with gallon containerized trees.	VPA 3
<b>Poor Growth/Vigor</b>	UT1 - Sta. 11+00 to 13+00 (0.21 ac)	Low Soil Fertility and compaction; continue to monitor	VPA 4
<b>Encroachment</b>	UT2 - Sta. 25+00 to 26+50 (0.04 ac)	Oversprary from farming operation; continue to monitor	VPA 5
<b>Poor Growth/Vigor</b>	UT2 - Sta. 19+00 to 21+00 (0.22 ac)	Low Soil Fertility and compaction; continue to monitor	VPA 6
<b>Encroachment</b>	UT2 - Sta. 4+50 & 12+00 (0.10 ac)	Oversprary from farming operation; continue to monitor	VPA 7
<b>Low Stem Density</b>	UT3 - Sta. 0+50 to 8+42 (0.96 ac)	Native weeds outcompeting planted trees; replant with gallon containerized trees and continue to monitor	VPA 8
<b>Low Stem Density</b>	UT4 - Sta. 5+63 to 8+25 (0.65 ac)	Shaded area and heavy deer browse; replant shade tolerant gallon containerized trees	VPA 9
<b>Encroachment</b>	UT8 - Sta. 0+00 to 1+50 (0.05 ac)	Oversprary from farming operation; plant gallon containerized trees and continue to monitor	VPA 10

**Figure 4. Vegetation Plot Photos**



Vegetation Plot 1 (11/15/2017)



Vegetation Plot 2 (11/15/2017)



Vegetation Plot 3 (11/15/2017)



Vegetation Plot 4 (11/15/2017)



Vegetation Plot 5 (11/15/2017)



Vegetation Plot 6 (11/15/2017)



Vegetation Plot 7 (11/14/2017)



Vegetation Plot 8 (11/14/2017)



Vegetation Plot 9 (11/14/2017)



Vegetation Plot 10 (11/14/2017)



Vegetation Plot 11 (11/14/2017)



Vegetation Plot 12 (11/14/2017)





Vegetation Plot 13 (11/14/2017)



Vegetation Plot 14 (11/14/2017)



Vegetation Plot 15 (11/14/2017)



Vegetation Plot 16 (11/14/2017)



Vegetation Plot 17 (11/15/2017)



Vegetation Plot 18 (11/16/2017)



Vegetation Plot 19 (11/16/2017)



Vegetation Plot 20 (11/15/2017)



Vegetation Plot 21 (11/16/2017)



Vegetation Plot 22 (11/16/2017)



Vegetation Plot 23 (11/16/2017)

**Figure 5. MY3 Stream Problem Area Photos**



SPA1 – Fence Damage UT3 @ Sta. 7+50



SPA2 – Minor Bank Erosion UT 4 @ Sta. 5+60 to 7+00



SPA3 – Ponding on Road UT 4 @ Sta. 8+47 to 8+67



SPA4 – Relic Channel Floodplain Plug Subsidence UT4 @ Sta. 8+75 to 11+03

**Figure 6. Vegetation Problem Area Photos**



VPA 2 – Invasives Present UT1 @ Sta. 0+00  
(0.13ac)



VPA 3 – Low Stem Density UT1 @ Sta. 4+00  
to 6+00 (0.49 ac)



VPA 4 – Poor Growth/Vigor UT1 @ Sta.  
11+00 to 13+00 (0.21 ac)



VPA 5 – Encroachment UT 2 @ Sta. 25+00 to  
26+50 (0.04 ac)



VPA 6 – Poor Growth/Vigor - UT2 @ Sta. 4+50 & 12+00 (0.10 ac)



VPA 7- Encroachment UT2 @ Sta. 4+50 & 12+00 (0.10 ac)



VPA 7- Encroachment UT2 @ Sta. 4+50 & 12+00 (0.10 ac)



VPA 8 – Low Stem Density UT3 @ Sta. 0+50 to 8+42 (0.96 ac)



VPA 9 – Low Stem Density UT4 @ Sta. 5+63 to 8+25 (0.65 ac)



VPA 10 – Encroachment UT8 @ Sta. 0+00 to 1+50 (0.05 ac)

# **Appendix C**

## **Vegetation Plot Data**

Table 9a. Planted Stem Count Summary

Table 9b. Planted Species Totals

Table 9c. Planted and Total Stem Counts (Species by Plot)

<b>Table 9a. Vegetation Plot Criteria Attainment</b>					
<b>Best Stream and Wetland Restoration Site</b>					
<b>Plot #</b>	<b>Planted Stems/Acre</b>	<b>Volunteers</b>	<b>Total</b>	<b>AVG Tree Height* (cm)</b>	<b>Success Criteria Met?</b>
1	364	1497	1862	258	Yes
2	202	567	769	137	No
3	405	162	567	179	Yes
4	1133	364	1497	463	Yes
5	688	81	769	168	Yes
6	1295	1255	2550	186	Yes
7	688	202	890	147	Yes
8	688	40	728	251	Yes
9	1174	243	1416	250	Yes
10	809	202	1012	268	Yes
11	1255	40	1295	116	Yes
12	1174	405	1578	239	Yes
13	1052	81	1133	151	Yes
14	1012	8620	9632	353	Yes
15	688	0	688	197	Yes
16	688	5382	6070	218	Yes
17	0	0	0	0	No
18	526	0	526	78	Yes
19	243	0	283	36	No
20	931	40	971	523	Yes
21	1012	0	1012	290	Yes
22	688	162	850	113	Yes
23	890	2711	3602	108	Yes
<b>Project Avg</b>	<b>765</b>	<b>959</b>	<b>1726</b>	<b>206</b>	<b>Yes</b>

\* The tallest eight trees were averaged, representing 320 stems/acre

<b>Table 9b. CVS Vegetation Plot Data Best Stream and Wetland Restoration Site</b>	
<b>Report Prepared By</b>	Eric Teitsworth
<b>Date Prepared</b>	11/17/2017 14:37
<b>database name</b>	Best_MY3_CVS_Entrytool.mdb
<b>database location</b>	C:\Users\eteitsworth\Dropbox (RES)\@RES Projects\North Carolina\Best Site\Monitoring\Monitoring Data\MY3_2017\Vegetation Data
<b>computer name</b>	D4V0KKGH2
<b>file size</b>	75464704
<b>DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT</b>	
<b>Metadata</b>	Description of database file, the report worksheets, and a summary of project(s) and project data.
<b>Proj, planted</b>	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
<b>Proj, total stems</b>	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
<b>Plots</b>	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
<b>Vigor</b>	Frequency distribution of vigor classes for stems for all plots.
<b>Vigor by Spp</b>	Frequency distribution of vigor classes listed by species.
<b>Damage</b>	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
<b>Damage by Spp</b>	Damage values tallied by type for each species.
<b>Damage by Plot</b>	Damage values tallied by type for each plot.
<b>Planted Stems by Plot and Spp</b>	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
<b>ALL Stems by Plot and spp</b>	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
<b>PROJECT SUMMARY</b>	
<b>Project Code</b>	95353
<b>project Name</b>	Best Stream/Wetland Restoration Site
<b>Description</b>	
<b>River Basin</b>	Cape Fear
<b>length(ft)</b>	
<b>stream-to-edge width (ft)</b>	
<b>area (sq m)</b>	
<b>Required Plots (calculated)</b>	
<b>Sampled Plots</b>	23





# **Appendix D**

## **Stream Geomorphology Data**

Table 10. Morphological Parameters Summary Data

Table 11. Dimensional Morphology Summary – Cross Sections Data

Table 12. Bank Pin Array Summary Data

Figure 7. Cross Section Plots

**Table 10. Best Site Morphological Parameters**

Feature	Reference Reach			Existing <sup>1</sup>												Design				As-Built/Baseline			
	Pool	Run	Shallow	UT1	UT2	UT3	UT4 (US)	UT4 (DS)	UT5	UT6	UT7	UT8	UT9	UT10	Muddy Creek	UT1	UT2	UT1	UT2	UT1	UT2		
Drainage Area (ac)	286			41	146	59	82	82	380	79	387	56	36	306	2930	41	146	41	146	41	146		
Drainage Area (mi <sup>2</sup> )	0.45			0.06	0.23	0.09	0.13	0.13	0.59	0.12	0.60	0.09	0.06	0.48	4.58	0.06	0	0.06	0	0.06	0		
NC Regional Curve Discharge (cfs) <sup>2</sup>	---	---	9.3	2.3	5.7	3.0	3.8	3.8	11.4	3.7	11.5	2.9	2.1	9.7	49.5	2.3	6	6	2.3	6			
NC Regional Curve Discharge (cfs) <sup>3</sup>	---	---	4.8	1.1	2.9	1.4	1.8	1.8	5.9	1.8	6.0	1.4	1.0	5.0	27.9	1.1	3	3	1.1	3			
Design/Calculated Discharge (cfs)	---	---	13	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---			
<b>Dimension</b>																							
BF Width (ft)	10.9	8.9	7.0	5.1	4.8	9.8	6.4	7.5	11.0	5.1	10.1	9.5	6.5	13.7	15.7	6.2	7.1	9.4	10.8	6.6	7.8	10.0	11.9
Floodprone Width (ft)	100	100	100	9	9	22	10	>50	>100	>50	>50	12	>50	84	>50	>50	>50	>50	>50	>50	>50	>50	>50
BF Cross Sectional Area (ft <sup>2</sup> )	11.4	8.4	5.0	3.2	4.6	8.1	6.4	6.2	6.0	4.3	6.1	4.9	3.6	7.8	21.2	3.9	6.1	8.9	14.2	3.0	5.1	10.2	15.0
BF Mean Depth (ft)	1.0	0.9	0.8	0.6	1.0	0.8	0.9	0.8	0.5	0.8	0.6	0.5	0.6	0.6	1.4	0.6	0.9	1.0	1.3	0.5	0.7	1.0	1.3
BF Max Depth (ft)	2.1	1.7	1.3	1.1	1.3	1.2	1.1	1.2	1.0	1.2	1.1	0.7	1.1	0.9	2.3	1.0	1.4	1.5	2.2	0.8	1.3	1.8	2.3
Width/Depth Ratio	10.4	9.5	8.8	8.1	5.0	11.8	8.4	9.1	20.2	6.2	16.7	18.2	11.8	24.0	11.6	9.9	8.3	9.9	8.2	14.8	12.3	9.9	9.5
Entrenchment Ratio	9.2	11.2	15.1	1.8	1.9	2.2	1.4	>2.2	>2.2	>2.2	>2.2	1.3	>2.2	6.1	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2
Wetted Perimeter (ft)	12.8	9.7	7.4	5.8	6.3	10.8	8.1	8.3	11.3	6.0	10.5	9.8	7.2	13.9	17.0	6.6	7.7	10.0	11.8	6.8	8.3	10.8	13.0
Hydraulic Radius (ft)	0.9	0.9	0.7	0.6	0.7	0.8	0.8	0.8	0.5	0.7	0.6	0.5	0.5	0.6	1.2	0.6	0.8	0.9	1.2	0.4	0.6	0.9	1.2
<b>Substrate</b>																							
	Fine Sand			Fine Sand												Fine Sand		Fine Sand		Fine Sand		Fine Sand	
<b>Pattern</b>																							
	Min	Max	Med	---	---	---	---	---	---	---	---	---	---	---	---	Min	Max	Min	Max	Min	Max	Min	Max
Channel Beltwidth (ft)	13.6	31.8	23.1	---	---	---	---	---	---	---	---	---	---	---	---	11	28	20	41	13	33	21	48
Radius of Curvature (ft)	11.0	27.6	17.6	---	---	---	---	---	---	---	---	---	---	---	---	9	27	17	37	9	34	14	44
Radius of Curvature Ratio	1.5	3.7	2.3	---	---	---	---	---	---	---	---	---	---	---	---	1.5	4.4	1.8	3.9	1.4	5.1	1.4	4.4
Meander Wavelength (ft)	34.9	68.3	54.5	---	---	---	---	---	---	---	---	---	---	---	---	32	71	44	106	31	67	35	108
Meander Width Ratio	1.8	4.2	3.1	---	---	---	---	---	---	---	---	---	---	---	---	1.8	4.5	2.1	4.4	1.9	5.0	2.1	4.8
<b>Profile</b>																							
Shallow Length (ft)	3.1	30.7	12.6	---	---	---	---	---	---	---	---	---	---	---	---	4	23	6	41	5	26	8	45
Run Length (ft)	2.2	33.2	11.3	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
Pool Length (ft)	4.2	9.5	5.8	---	---	---	---	---	---	---	---	---	---	---	---	3	10	7	12	5	14	8	15
Pool -to-Pool Spacing (ft)	17.5	59.8	36.3	---	---	---	---	---	---	---	---	---	---	---	---	16	49	25	68	18	55	30	74
<b>Additional Reach Parameters</b>																							
Valley Length (ft)	274			1826	2818	1417	253	686	2843	567	2192	942	725	1042	9021	1510	2529	1510	2529	1510	2529		
Channel Length (ft)	309			1905	2865	1522	255	772	3228	597	2629	994	769	1104	9808	1723	2770	1756	2771	1756	2771		
Sinuosity	1.13			1.04	1.02	1.07	1.01	1.13	1.14	1.05	1.20	1.06	1.06	1.06	1.09	1.14	1.10	1.16	1.16	1.16	1.10		
Water Surface Slope (ft/ft)	0.004			---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---		
Channel Slope (ft/ft)	0.003			0.0066	0.0044	0.0093	0.0042	0.0042	0.004	0.0012	0.004	0.0029	0.008	0.004	0.0011	0.0056	0.0027	0.0063	0.0045	0.0063	0.0045		
Rosgen Classification	E5			G5c	G5c	E5	G5c	E5	C5	E5	C5	F5	E5	C5	E5	E5	E5	E5	E5	E5	E5		

<sup>1</sup> Bankfull stage was estimated using NC Regional Curve equations and existing conditions data

<sup>2</sup> NC Regional Curve equations source: Doll et al. (2003)

<sup>3</sup> NC Regional Curve equations source: Sweet and Geratz (2003)



**Appendix D. Table 11. - Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)**

**Project Name/Number: Best Site/ NCDMS Project # 95353**

	Cross Section 21 (Run)							Cross Section 22 (Pool)							Cross Section 23 (Run)							Cross Section 24 (Pool)							Cross Section 25 (Run)						
Based on fixed baseline bankfull elevation <sup>1</sup>	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	65.1	65.1	65.1	65.1				65.0	65.0	65.0	65.0				62.8	62.8	62.8	62.8				62.5	62.5	62.5	62.5				71.5	71.5	71.5	71.5			
Bankfull Width (ft)	10.9	10.0	9.3	9.7				10.7	10.5	10.4	10.6				9.1	10.3	11.1	10.0				13.2	13.8	19.0	14.1				12.2	11.5	13.1	12.1			
Floodprone Width (ft)	50.0	50.0	50.0	50.0				50.0	50.0	50.0	50.0				50.0	50.0	50.0	50.0				50.0	50.0	50.0	50.0				50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.0	1.0	1.1	1.1				1.3	1.2	1.2	1.3				1.0	0.8	0.8	0.8				1.4	1.0	0.4	0.5				0.3	0.3	0.3	0.3			
Bankfull Max Depth (ft)	1.9	1.9	2.1	2.2				2.4	2.3	2.4	2.5				1.8	1.4	1.4	1.2				2.6	2.1	1.0	0.9				0.8	0.7	0.8	0.8			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	11.1	10.0	10.0	10.4				14.2	12.4	12.4	13.3				8.7	8.1	9.1	7.7				18.3	14.4	7.7	7.2				4.2	3.6	4.4	4.1			
Bankfull Width/Depth Ratio	10.7	9.9	8.6	9.1				8.1	8.8	8.7	8.4				9.4	13.1	13.5	13.0				9.5	13.3	47.0	27.6				35.5	36.6	39.0	36.1			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2				>2.2	>2.2	>2.2	N/A				>2.2	>2.2	>2.2	>2.2				>2.2	>2.2	>2.2	N/A				>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0				1.0	1.0	1.0	N/A				1.0	1.0	1.0	1.0				1.0	1.0	1.0	N/A				1.0	1.0	1.0	1.0			
	Cross Section 26 (Run)							Cross Section 27 (Riffle)							Cross Section 28 (Run)							Cross Section 29 (Pool)							Cross Section 30 (Run)						
Based on fixed baseline bankfull elevation <sup>1</sup>	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	67.9	67.9	67.9	67.9				69.9	69.9	69.9	69.9				69.2	69.2	69.2	69.2				65.3	65.3	65.3	65.3				63.7	63.7	63.7	63.7			
Bankfull Width (ft)	5.6	5.3	6.1	5.7				7.2	6.7	6.5	5.7				5.7	5.3	5.6	5.2				8.7	3.3	8.3	6.3				6.4	6.7	5.6	5.3			
Floodprone Width (ft)	50.0	50.0	50.0	50.0				50.0	50.0	50.0	13.2				50.0	15.0	16.8	9.3				50.0	20.0	13.7	15.8				50.0	20.0	19.3	16.4			
Bankfull Mean Depth (ft)	0.6	0.5	0.8	0.9				0.7	0.6	0.8	0.8				0.5	0.5	0.4	0.4				0.4	0.4	0.3	0.3				0.9	0.8	0.9	0.7			
Bankfull Max Depth (ft)	1.0	0.9	1.6	1.7				1.1	1.0	1.3	1.2				0.9	0.8	0.8	0.6				0.9	0.8	0.6	0.4				1.3	1.5	1.6	1.0			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.1	2.7	5.1	5.1				4.7	4.1	4.9	4.5				3.1	2.4	2.5	1.9				3.8	3.3	2.1	1.8				5.7	5.6	5.1	4.0			
Bankfull Width/Depth Ratio	10.2	10.2	7.4	6.5				10.8	11.0	8.5	7.1				10.4	11.4	12.5	14.5				19.9	22.1	32.7	22.4				7.1	7.9	6.3	7.2			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2				>2.2	>2.2	>2.2	>2.2				>2.2	>2.2	>2.2	1.8				>2.2	1.9	1.6	N/A				>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0				1.0	1.0	1.0	0.9				1.0	1.0	1.0	2.7				1.0	1.0	1.0	N/A				1.0	1.0	1.0	1.2			
	Cross Section 31 (Riffle)							Cross Section 32 (Run)							Cross Section 33 (Pool)							Cross Section 34 (Run)													
Based on fixed baseline bankfull elevation <sup>1</sup>	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	63.0	63.0	63.0	63.0																															
Bankfull Width (ft)	7.7	8.5	3.4	4.0																															
Floodprone Width (ft)	50.0	15.0	14.2	13.4																															
Bankfull Mean Depth (ft)	0.4	0.2	0.3	0.3																															
Bankfull Max Depth (ft)	0.7	0.5	0.5	0.4																															
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.0	2.1	0.9	1.1																															
Bankfull Width/Depth Ratio	19.5	34.5	13.2	14.9																															
Bankfull Entrenchment Ratio	>2.2	1.7	>2.2	>2.2																															
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.7																															
	Cross Section 35 (Run)							Cross Section 36 (Pool)							Cross Section 37 (Run)							Cross Section 38 (Pool)													
Based on fixed baseline bankfull elevation <sup>1</sup>	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>																																			
Bankfull Width (ft)																																			
Floodprone Width (ft)																																			
Bankfull Mean Depth (ft)																																			
Bankfull Max Depth (ft)																																			
Bankfull Cross Sectional Area (ft <sup>2</sup> )																																			
Bankfull Width/Depth Ratio																																			
Bankfull Entrenchment Ratio																																			
Bankfull Bank Height Ratio																																			

1 = Widths and depths for annual measurements will be based on the baseline bankfull datum regardless of dimensional/depositional development. Input the elevation used as the datum, which should be consistent and based on the baseline datum established. If the performer has inherited the project and cannot acquire the datum used for prior years this must be discussed with EEP. If this cannot be resolved in time for a given years report submission a footnote in this should be included that states: "It is uncertain if the monitoring datum has been consistent over the monitoring history, which may influence calculated values. Additional data from a prior performer is being acquired to provide confirmation. Values will be recalculated in a future submission based on a consistent datum if determined to be necessary."  
 Note: Starting in MY3, BHR was calculated on riffles using the baseline bankfull elevation. This method was used because the dimension of the channels has not changed enough to alter the bankfull elevation.

**Table 12. Best Stream and Wetland Restoration Site Bank Pin Array Summary**

<b>Cross Section</b>	<b>Location</b>	<b>Position</b>	<b>Year 1 Reading</b>	<b>Year 2 Reading</b>	<b>Year 3 Reading</b>
XS 1 @ Sta. 1+00 - UT1	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
XS 4 @ Sta. 4+25 - UT1	US	Top	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
XS 5 @ Sta. 6+25 - UT1	US	Top	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
XS 8 @ Sta. 9+90 - UT1	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
XS 11 @ Sta. 15+90 - UT1	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	6"	0.0	0.0
		Bottom	24"	0.0	0.0
XS 13 @ Sta. 5+75 - UT2	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
XS 22 @ Sta. 23+55 - UT2	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
XS 24 @ Sta. 28+45 - UT2	US	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0

Notes:

US – Upstream from cross section


DS – Downstream from cross section



Upstream



Downstream

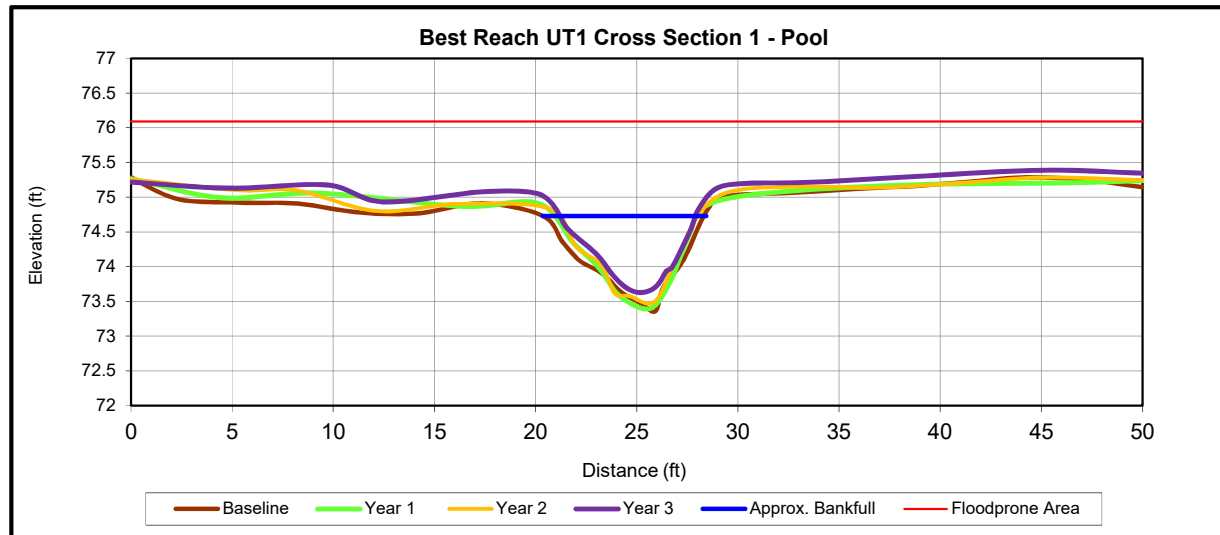


	Cross Section 1 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	74.7	74.7	74.7	74.7			
Bankfull Width (ft)	8.0	6.7	7.7	8.9			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.8	0.7	0.8	0.8			
Bankfull Max Depth (ft)	1.4	1.2	1.3	1.4			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	6.0	4.5	5.9	7.0			
Bankfull Width/Depth Ratio	10.5	10.0	9.9	11.4			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

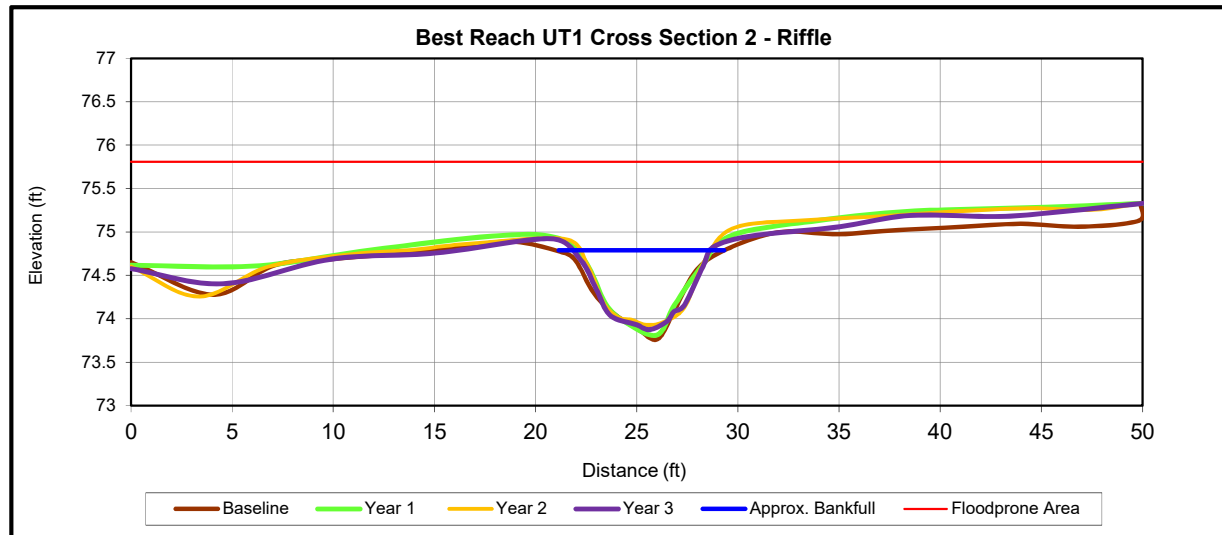

	<b>Cross Section 2 (Riffle)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	74.8	74.8	74.8	74.8			
Bankfull Width (ft)	8.2	7.2	7.8	7.4			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.5	0.5	0.6	0.6			
Bankfull Max Depth (ft)	1.0	1.0	1.0	0.9			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.2	3.9	4.8	4.3			
Bankfull Width/Depth Ratio	15.9	13.5	12.7	12.8			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			






Upstream



Downstream

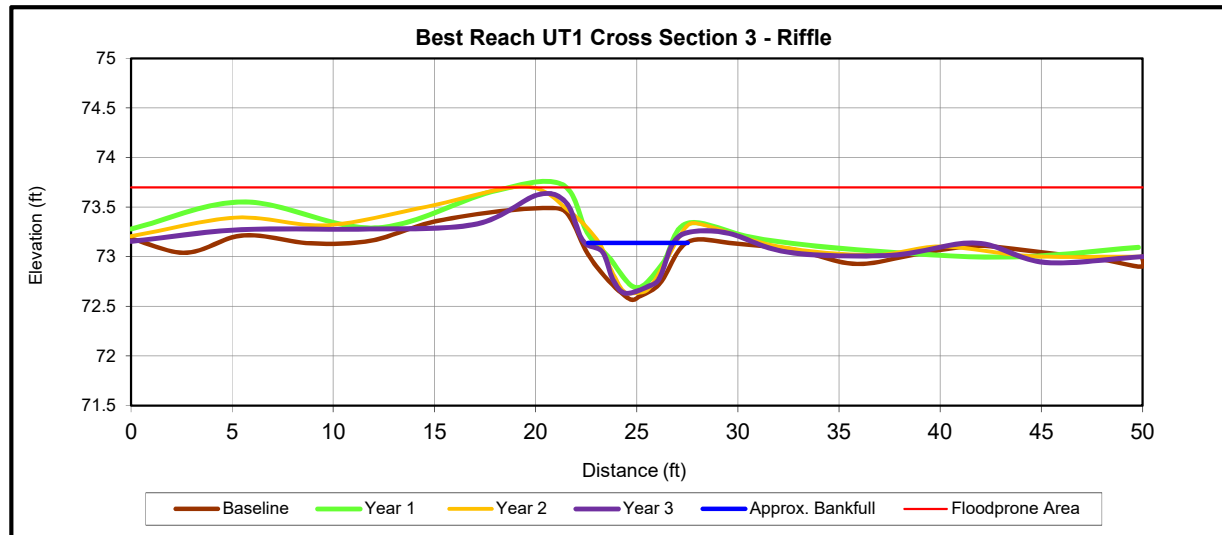


	<b>Cross Section 3 (Riffle)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	73.1	73.1	73.1	73.1			
Bankfull Width (ft)	5.2	3.9	5.6	5.6			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.3	0.2	0.4	0.3			
Bankfull Max Depth (ft)	0.6	0.5	0.7	0.6			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	1.8	0.9	2.1	1.8			
Bankfull Width/Depth Ratio	15.1	16.2	14.7	16.9			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

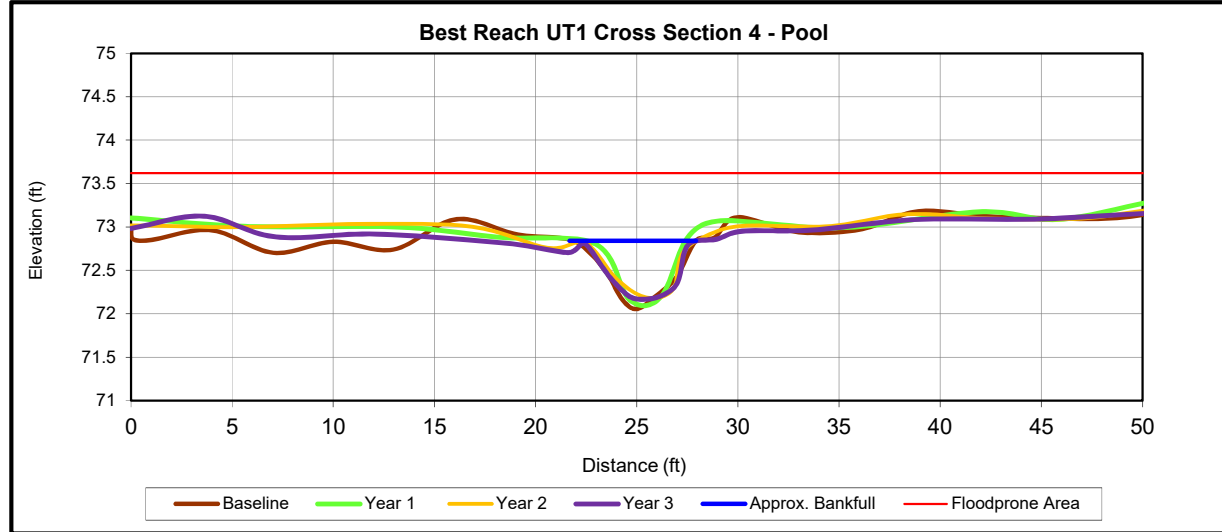


	<b>Cross Section 4 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	72.8	72.8	72.8	72.8			
Bankfull Width (ft)	6.1	4.5	5.9	5.2			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.4	0.5	0.4	0.4			
Bankfull Max Depth (ft)	0.8	0.7	0.7	0.6			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	2.6	2.0	2.2	2.2			
Bankfull Width/Depth Ratio	14.5	9.9	16.2	12.3			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

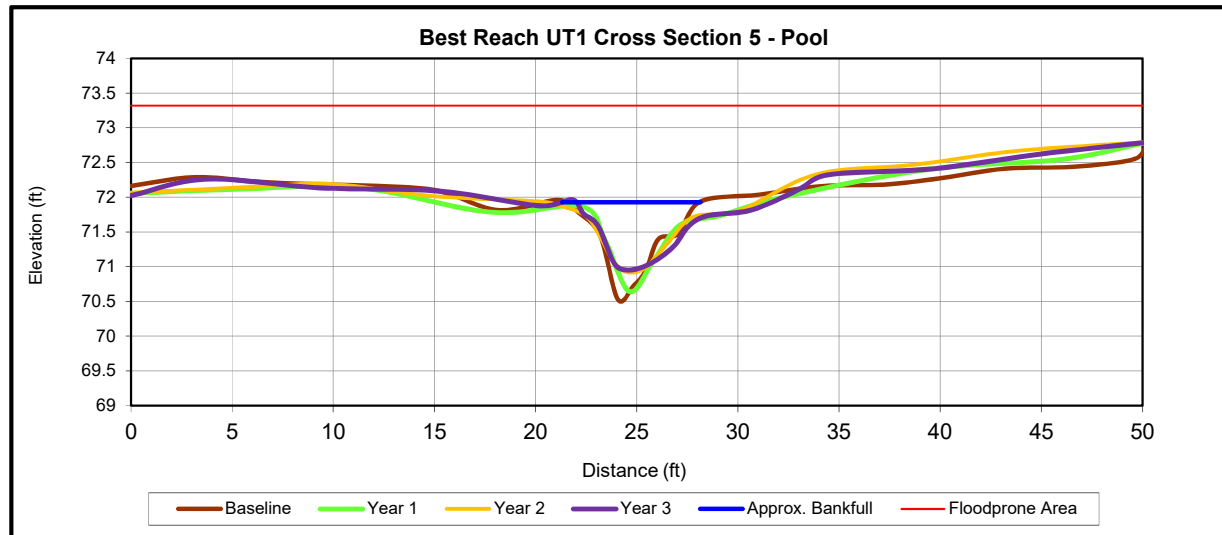


	<b>Cross Section 5 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	71.9	71.9	71.9	71.9			
Bankfull Width (ft)	6.8	6.8	9.5	9.3			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.6	0.6	0.4	0.4			
Bankfull Max Depth (ft)	1.4	1.3	0.9	0.9			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.1	4.0	3.8	4.0			
Bankfull Width/Depth Ratio	11.4	11.7	23.4	21.6			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

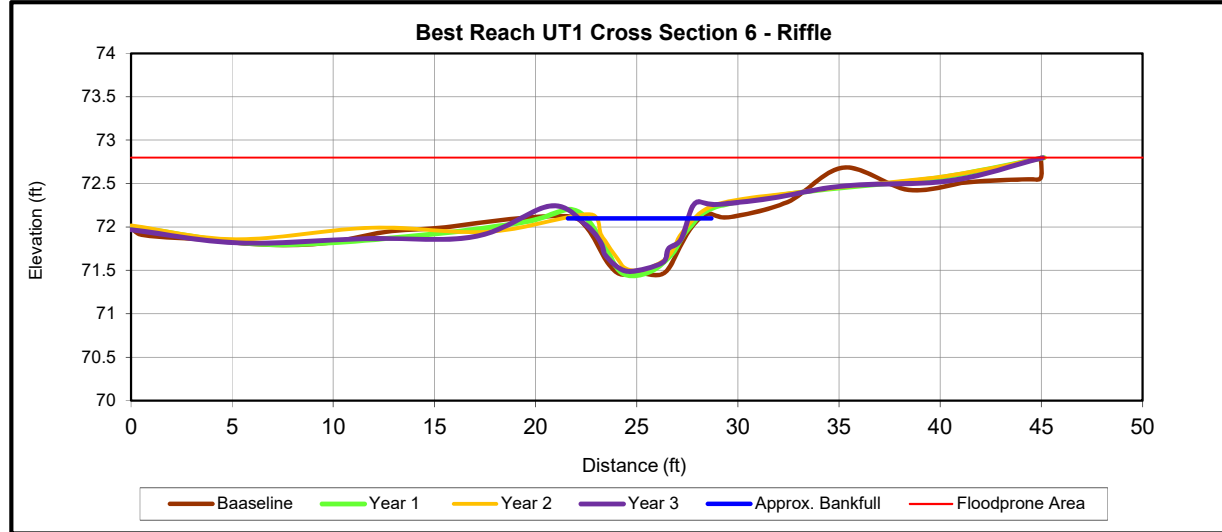


	Cross Section 6 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	72.1	72.1	72.1	72.1			
Bankfull Width (ft)	7.1	6.1	5.5	6.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.4	0.4	0.4	0.4			
Bankfull Max Depth (ft)	0.7	0.6	0.6	0.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	2.8	2.4	2.1	2.8			
Bankfull Width/Depth Ratio	18.0	16.0	14.4	16.0			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.1			



Upstream



Downstream

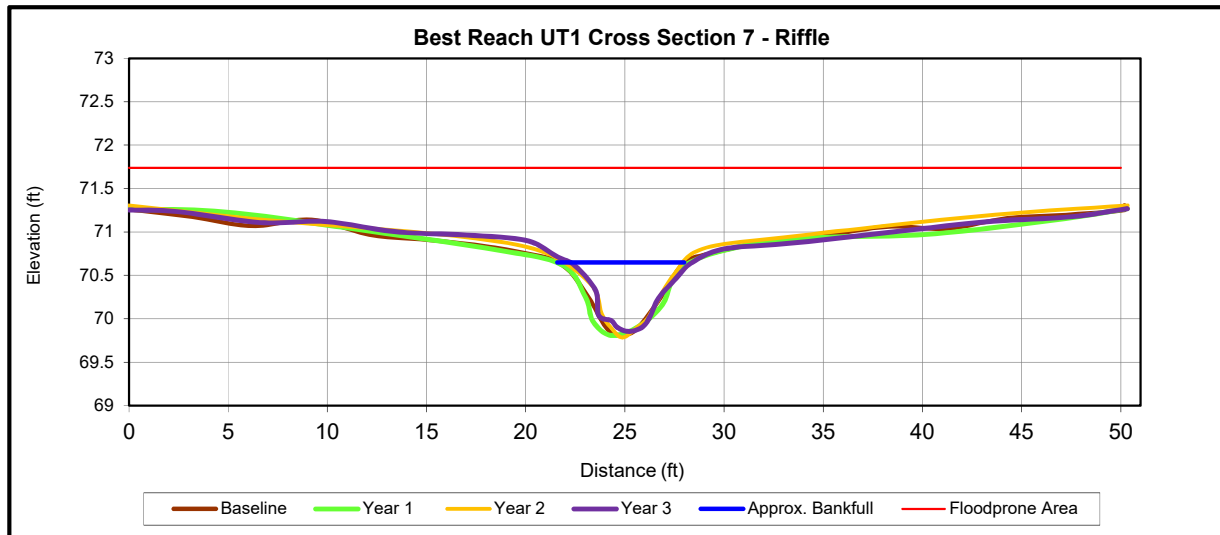


	<b>Cross Section 7 (Riffle)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bank full elevation</b>							
<b>Record elevation (datum) used</b>	70.7	70.7	70.7	70.7			
Bankfull Width (ft)	6.4	7.1	6.4	6.2			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4			
Bankfull Max Depth (ft)	0.8	0.8	0.9	0.8			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.0	3.3	2.7	2.7			
Bankfull Width/Depth Ratio	14.0	15.2	15.0	14.5			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

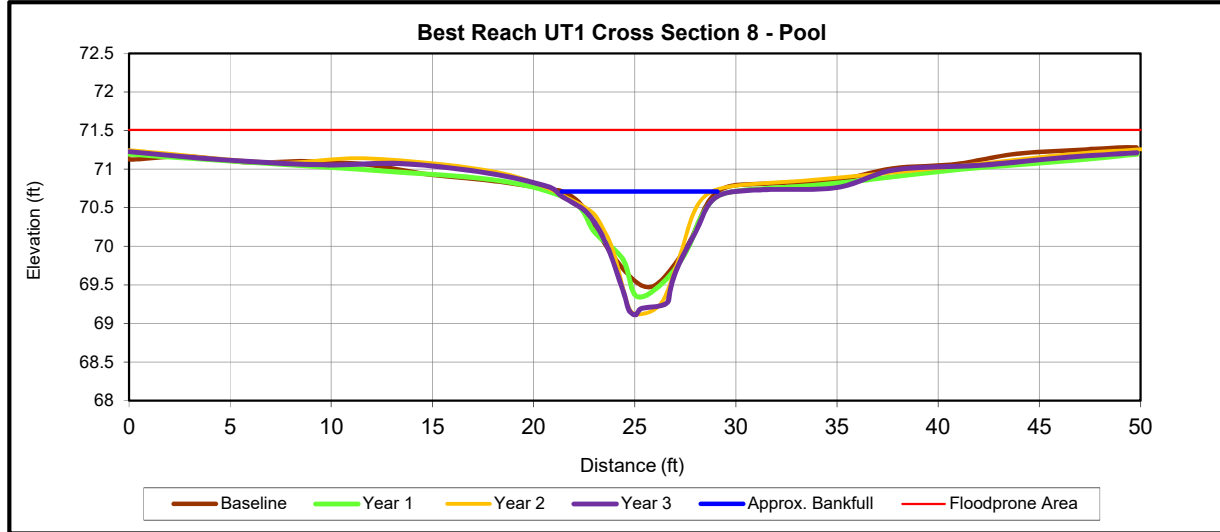


	<b>Cross Section 8 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	70.7	70.7	70.7	70.7			
Bankfull Width (ft)	7.7	10.1	8.4	8.5			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.7	0.6	0.7	0.7			
Bankfull Max Depth (ft)	1.2	1.4	1.6	1.6			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	5.2	5.6	5.7	6.3			
Bankfull Width/Depth Ratio	11.3	18.2	12.5	11.3			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

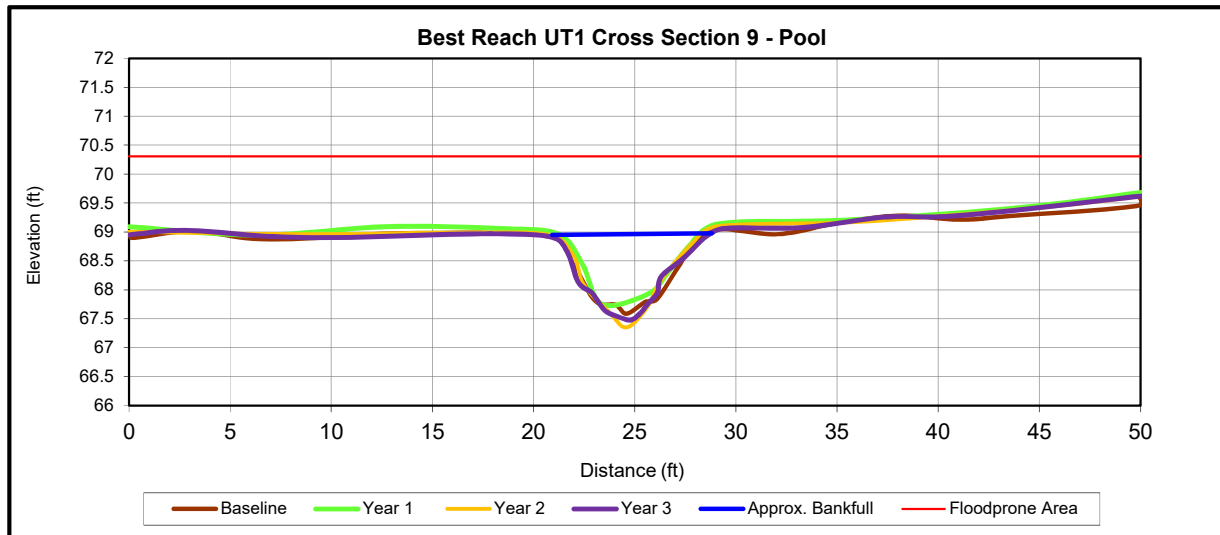


	<b>Cross Section 9 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	69.0	69.0	69.0	69.0			
Bankfull Width (ft)	7.7	7.1	7.6	7.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.8	0.7	0.8	0.8			
Bankfull Max Depth (ft)	1.4	1.2	1.6	1.5			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	6.1	5.0	6.1	6.2			
Bankfull Width/Depth Ratio	9.9	10.3	9.6	9.4			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

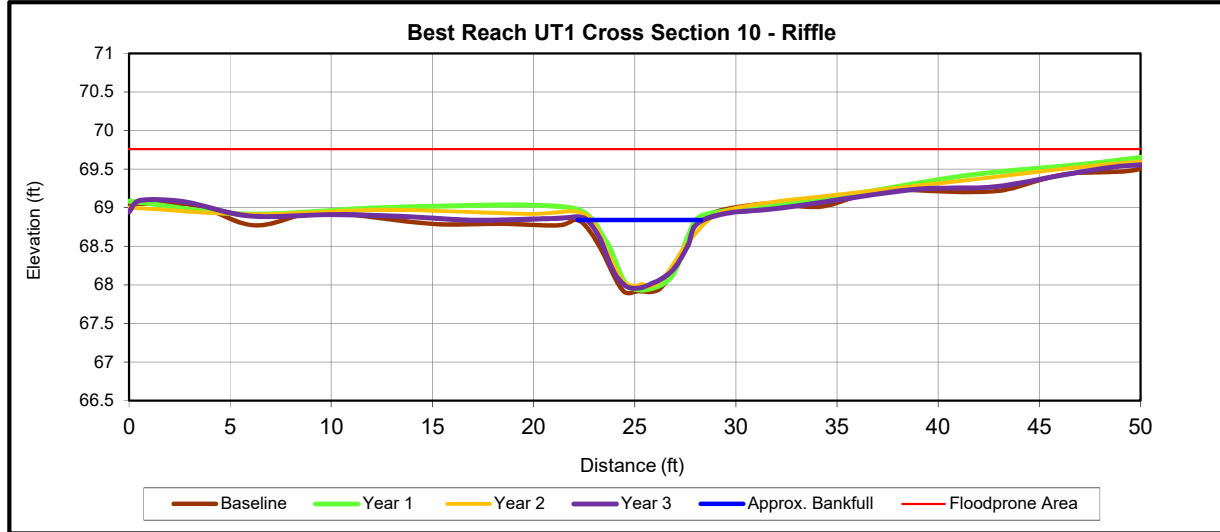

	<b>Cross Section 10 (Riffle)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	68.8	68.8	68.8	68.8			
Bankfull Width (ft)	6.1	5.7	6.3	6.0			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.6	0.5	0.5	0.5			
Bankfull Max Depth (ft)	0.9	0.9	0.9	0.9			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.5	2.9	3.1	3.2			
Bankfull Width/Depth Ratio	10.4	11.3	12.7	11.4			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	0.9			






Upstream



Downstream

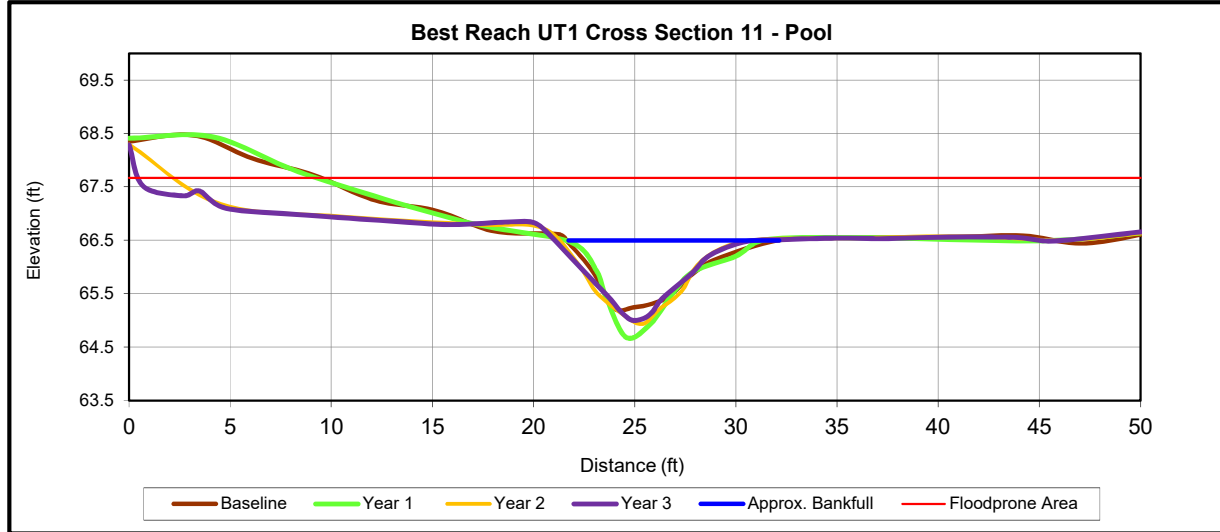


	<b>Cross Section 11 (Pool)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	66.5	66.5	66.5	66.5			
Bankfull Width (ft)	10.4	10.0	10.6	10.6			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.6	0.8	0.7	0.7			
Bankfull Max Depth (ft)	1.3	1.8	1.6	1.5			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	6.7	7.6	7.4	6.9			
Bankfull Width/Depth Ratio	16.0	13.2	15.3	16.2			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

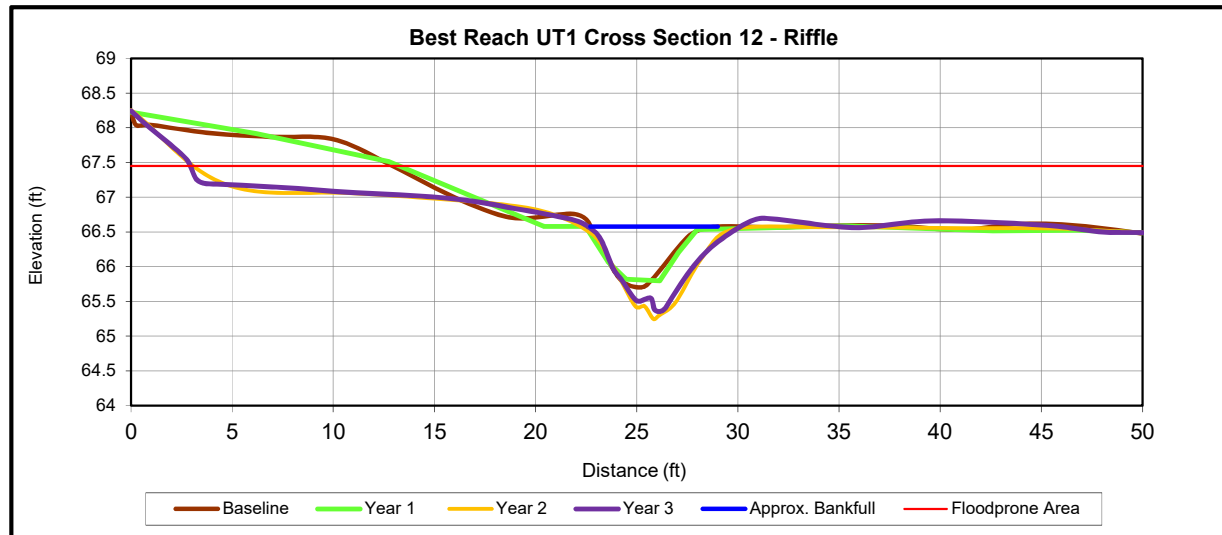


	<b>Cross Section 12 (Riffle)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	66.6	66.6	66.6	66.6			
Bankfull Width (ft)	6.5	5.5	7.9	7.6			
Floodprone Width (ft)	37.0	37.0	37.0	37.0			
Bankfull Mean Depth (ft)	0.4	0.5	0.7	0.6			
Bankfull Max Depth (ft)	0.9	0.8	1.3	1.2			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	2.8	2.9	5.2	4.7			
Bankfull Width/Depth Ratio	15.1	10.7	12.0	12.5			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

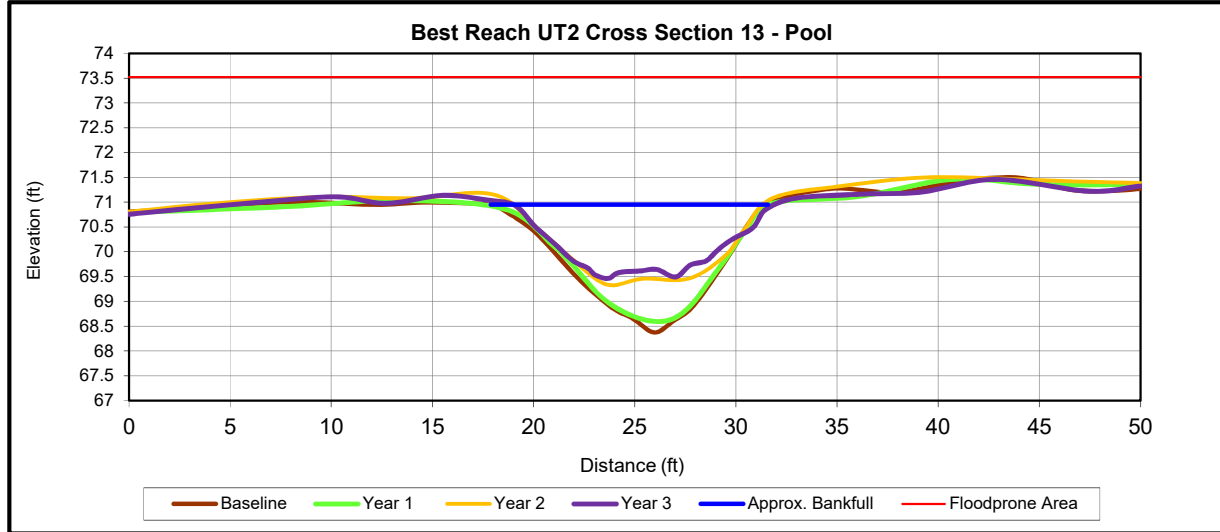


	Cross Section 13 (Pool)						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
Record elevation (datum) used	71.0	71.0	71.0	71.0			
Bankfull Width (ft)	13.7	13.1	12.8	13.2			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.4	1.3	1.0	0.9			
Bankfull Max Depth (ft)	2.6	2.3	1.6	1.5			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	18.6	17.6	13.4	12.4			
Bankfull Width/Depth Ratio	10.1	9.0	12.3	14.0			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

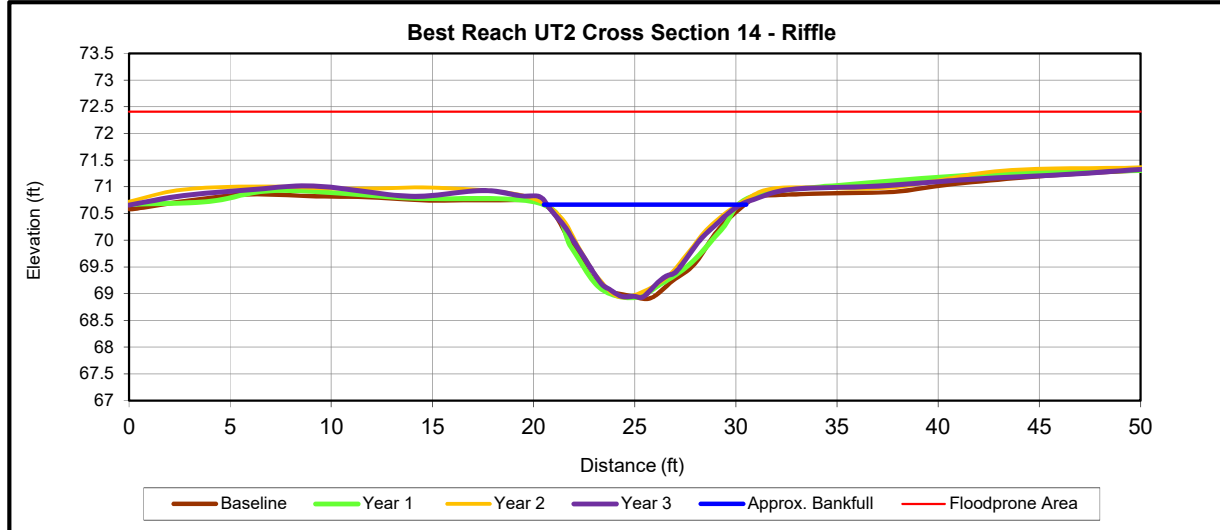


	Cross Section 14 (Run/Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	70.7	70.7	70.7	70.7			
Bankfull Width (ft)	10.0	10.0	9.9	9.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.1	1.1	0.9	1.0			
Bankfull Max Depth (ft)	1.7	1.7	1.7	1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	10.7	10.6	9.1	9.5			
Bankfull Width/Depth Ratio	9.3	9.6	10.7	9.9			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

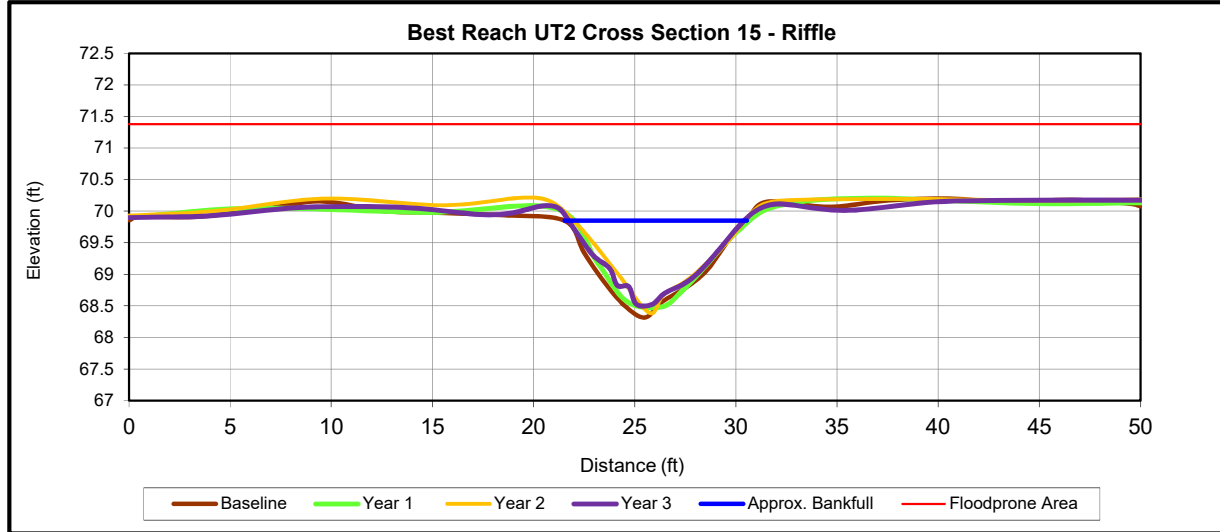


<b>Cross Section 15 (Riffle)</b>							
<b>Based on fixed baseline bankfull elevation</b>	Base	MY1	MY2	MY3	MY5	MY7	MY+
Record elevation (datum) used	69.9	69.9	69.9	69.9			
Bankfull Width (ft)	9.0	9.4	8.6	8.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.9	0.8	0.7	0.8			
Bankfull Max Depth (ft)	1.5	1.4	1.5	1.3			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	7.8	7.3	6.3	6.6			
Bankfull Width/Depth Ratio	10.3	12.0	11.7	11.5			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.1			



Upstream



Downstream

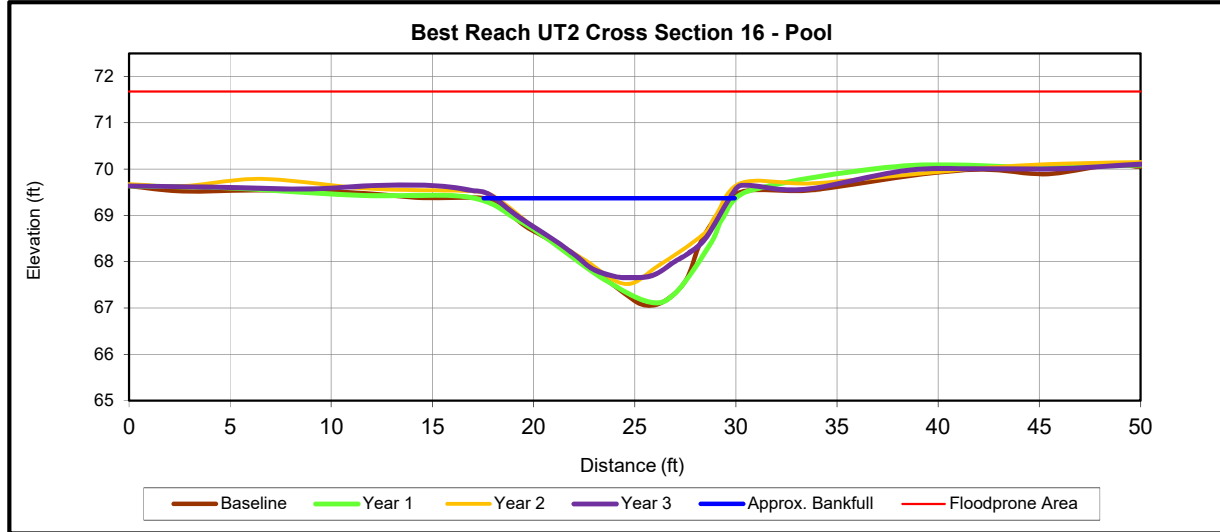


	<b>Cross Section 16 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	69.4	69.4	69.4	69.4			
Bankfull Width (ft)	12.4	13.3	12.0	12.6			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.2	1.2	1.1	1.1			
Bankfull Max Depth (ft)	2.3	2.2	2.0	1.8			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	15.1	15.7	13.4	14.1			
Bankfull Width/Depth Ratio	10.2	11.3	10.7	11.2			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

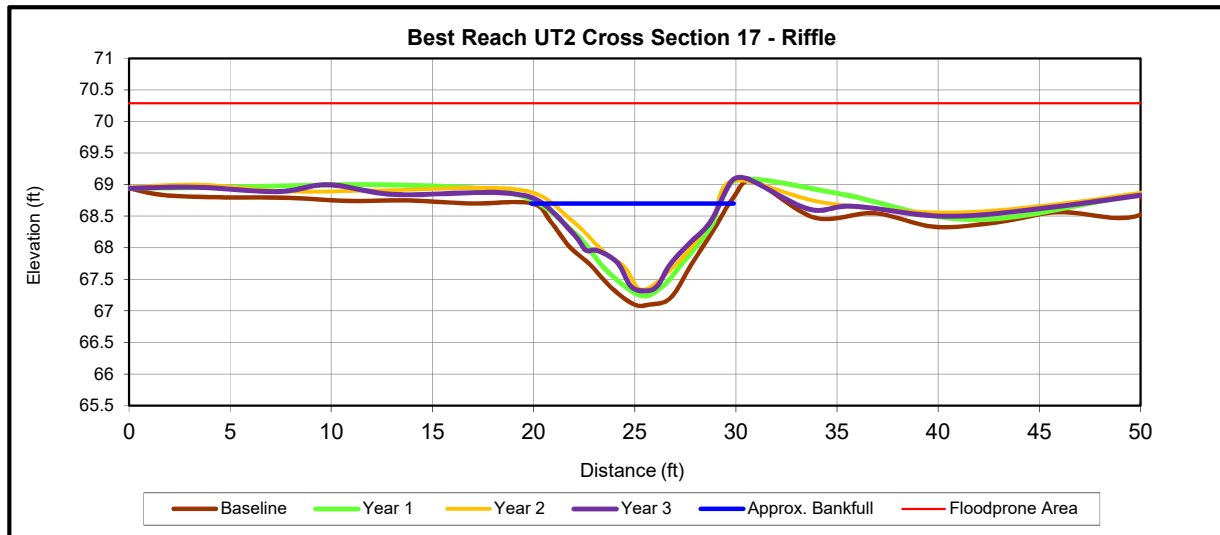


	<b>Cross Section 17 (Riffle)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	68.7	68.7	68.7	68.7			
Bankfull Width (ft)	9.8	9.6	10.2	9.1			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.9	0.8	0.8	0.8			
Bankfull Max Depth (ft)	1.6	1.5	1.5	1.4			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	9.3	7.5	8.0	6.9			
Bankfull Width/Depth Ratio	10.3	12.3	12.9	12.0			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

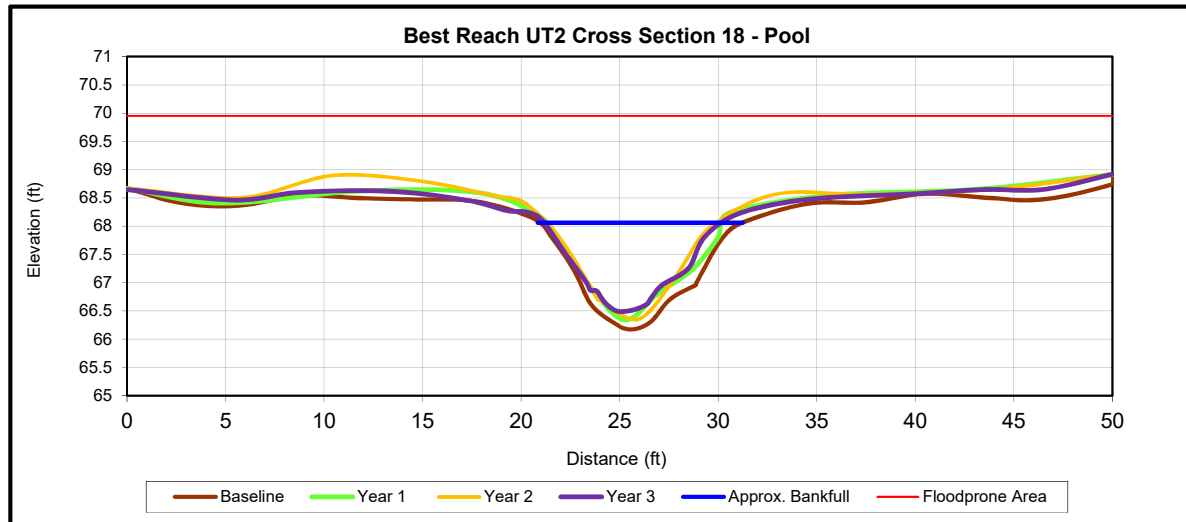

	<b>Cross Section 18 (Pool)</b>						
<b>Based on fixed baseline bankfull elevation</b>	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	68.1	68.1	68.1	68.1			
Bankfull Width (ft)	10.4	9.2	11.6	10.8			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.1	1.0	1.0	0.9			
Bankfull Max Depth (ft)	1.9	1.7	2.1	1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	11.2	8.8	11.6	10.2			
Bankfull Width/Depth Ratio	9.7	9.6	11.5	11.6			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			






Upstream



Downstream

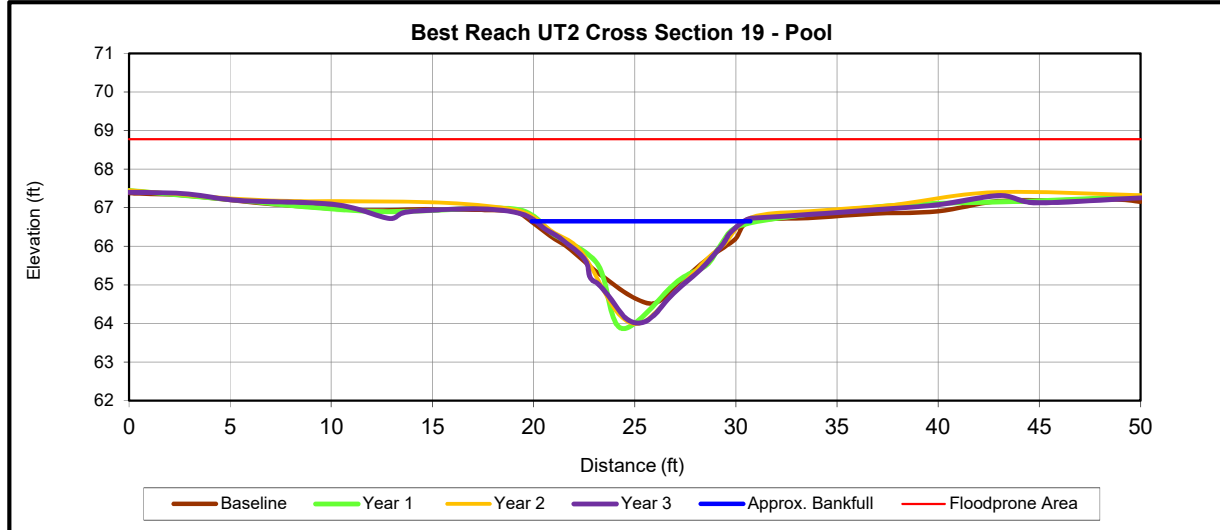


	<b>Cross Section 19 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	66.7	66.7	66.7	66.7			
Bankfull Width (ft)	10.8	11.4	10.7	10.8			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.2	1.1	1.3	1.3			
Bankfull Max Depth (ft)	2.1	2.8	2.7	2.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	12.5	11.4	14.1	14.4			
Bankfull Width/Depth Ratio	9.4	10.0	8.2	8.0			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

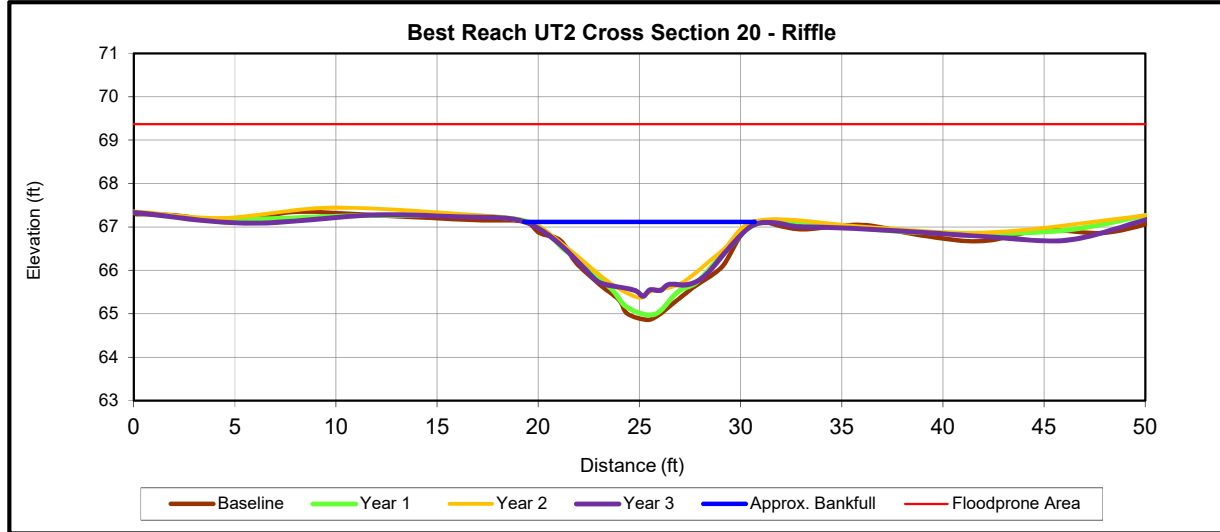


	Cross Section 20 (Run/Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	67.1	67.1	67.1	67.1			
Bankfull Width (ft)	11.4	12.1	11.5	12.4			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.2	1.1	1.0	0.9			
Bankfull Max Depth (ft)	2.3	2.1	1.8	1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	13.8	13.0	10.9	11.4			
Bankfull Width/Depth Ratio	9.4	11.2	12.0	13.4			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

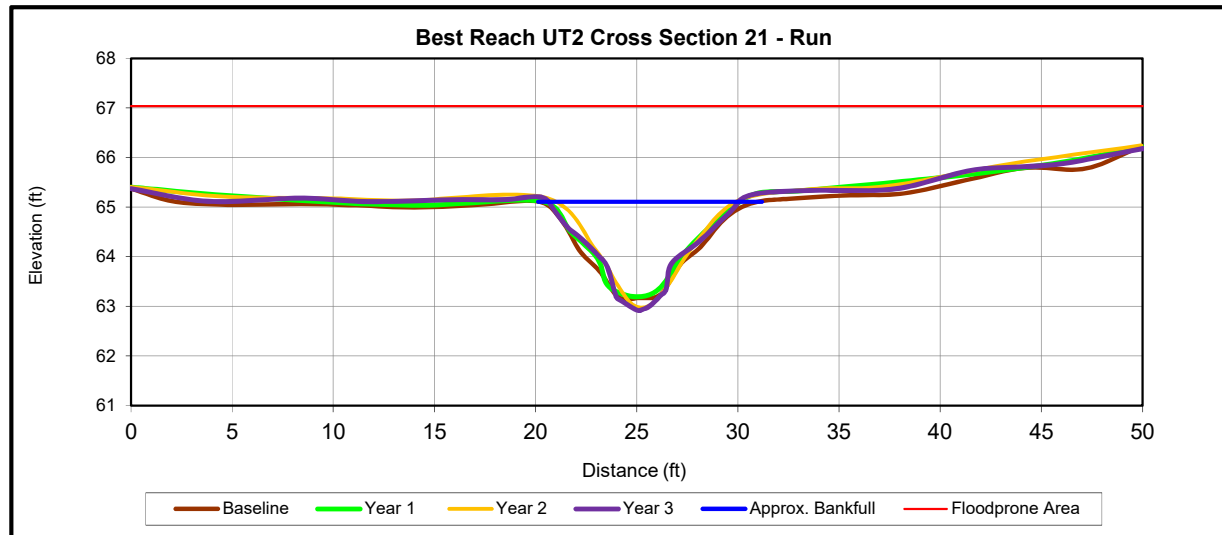


	<b>Cross Section 21 (Run)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
Record elevation (datum) used	65.1	65.1	65.1	65.1			
Bankfull Width (ft)	10.9	10.0	9.3	9.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.0	1.0	1.1	1.1			
Bankfull Max Depth (ft)	1.9	1.9	2.1	2.2			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	11.1	10.0	10.0	10.4			
Bankfull Width/Depth Ratio	10.7	9.9	8.6	9.1			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

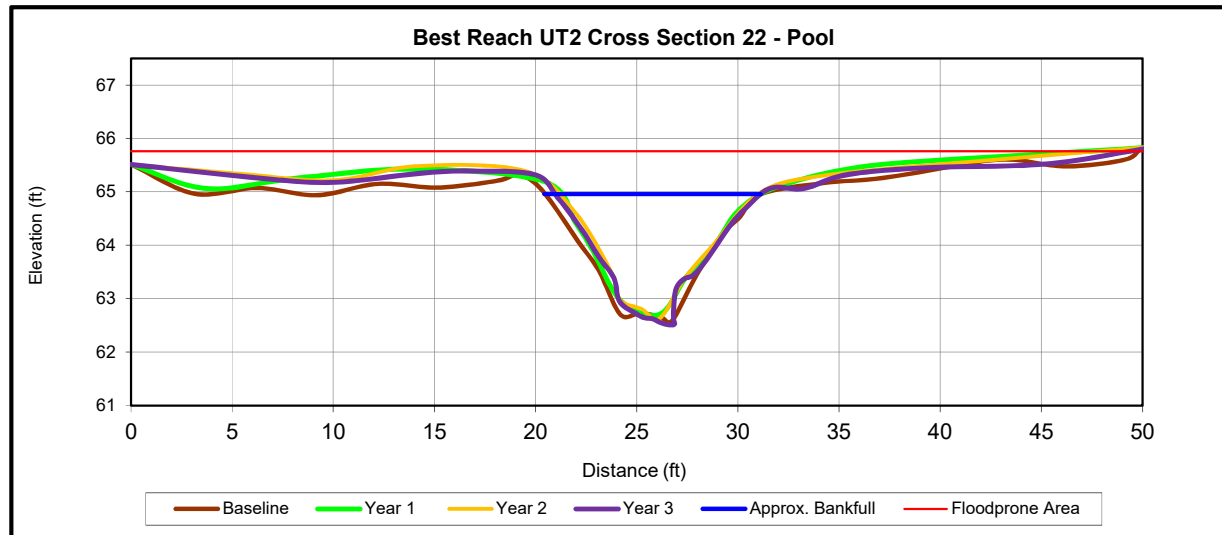


	<b>Cross Section 22 (Pool)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	65.0	65.0	65.0	65.0			
Bankfull Width (ft)	10.7	10.5	10.4	10.6			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.3	1.2	1.2	1.3			
Bankfull Max Depth (ft)	2.4	2.3	2.4	2.5			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	14.2	12.4	12.4	13.3			
Bankfull Width/Depth Ratio	8.1	8.8	8.7	8.4			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

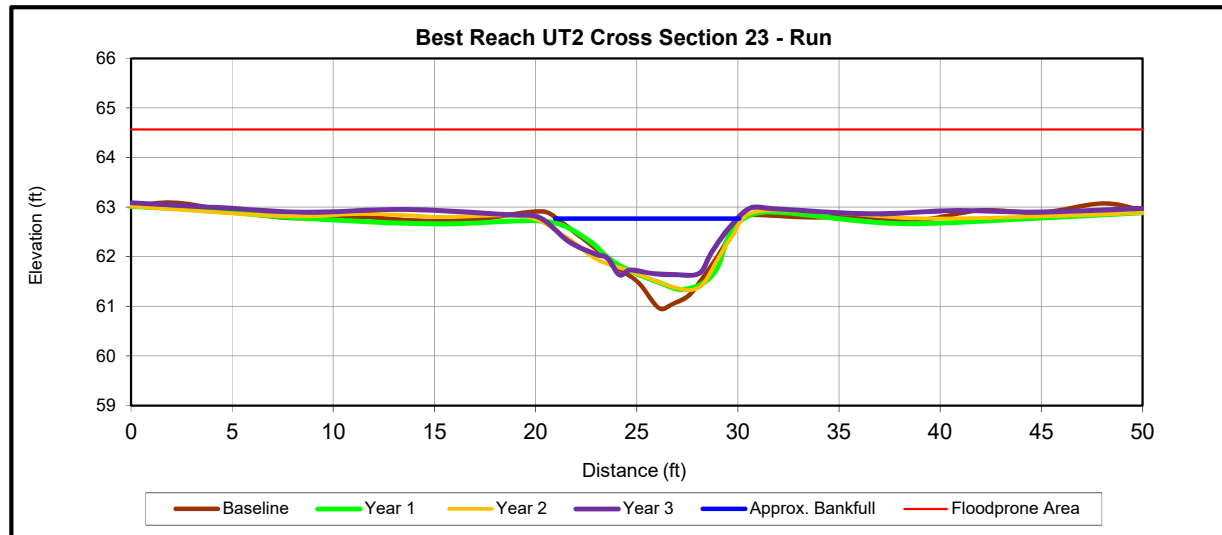


	<b>Cross Section 23 (Run)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	62.8	62.8	62.8	62.8			
Bankfull Width (ft)	9.1	10.3	11.1	10.0			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.0	0.8	0.8	0.8			
Bankfull Max Depth (ft)	1.8	1.4	1.4	1.2			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.7	8.1	9.1	7.7			
Bankfull Width/Depth Ratio	9.4	13.1	13.5	13.0			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

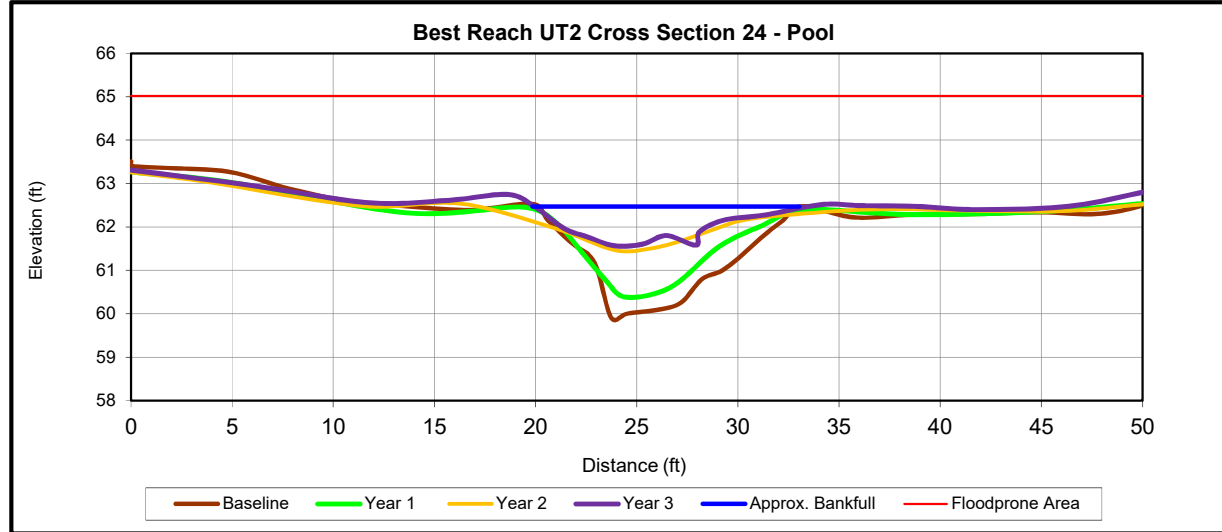


	<b>Cross Section 24 (Pool)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
Record elevation (datum) used	62.5	62.5	62.5	62.5			
Bankfull Width (ft)	13.2	13.8	19.0	14.1			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	1.4	1.0	0.4	0.5			
Bankfull Max Depth (ft)	2.6	2.1	1.0	0.9			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	18.3	14.4	7.7	7.2			
Bankfull Width/Depth Ratio	9.5	13.3	47.0	27.6			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

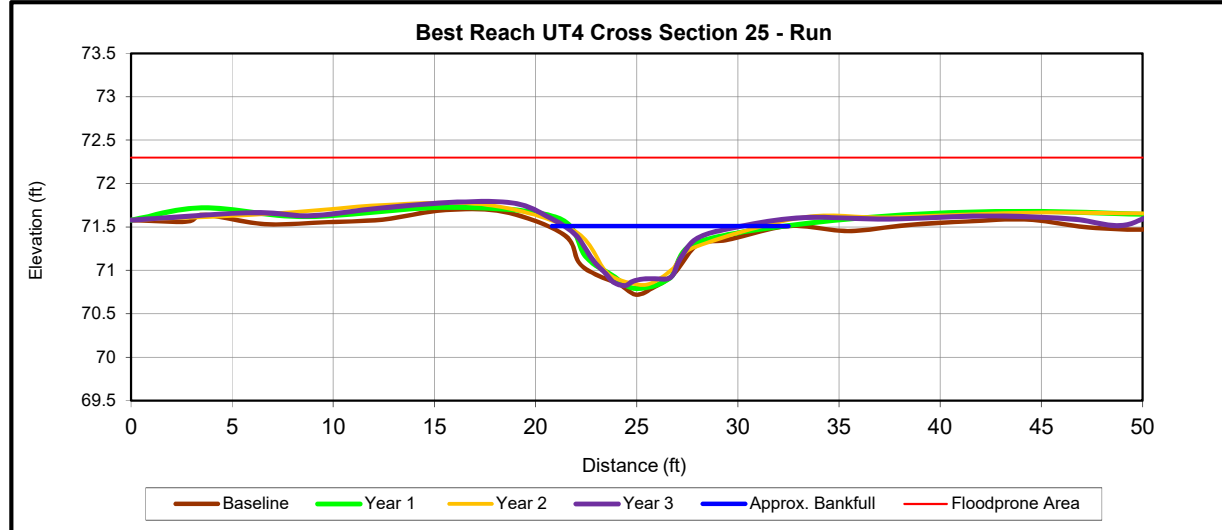


	<b>Cross Section 25 (Run)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
Record elevation (datum) used	71.5	71.5	71.5	71.5			
Bankfull Width (ft)	12.2	11.5	13.1	12.1			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.3	0.3	0.3	0.3			
Bankfull Max Depth (ft)	0.8	0.7	0.8	0.8			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.2	3.6	4.4	4.1			
Bankfull Width/Depth Ratio	35.5	36.6	39.0	36.1			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			



Upstream



Downstream

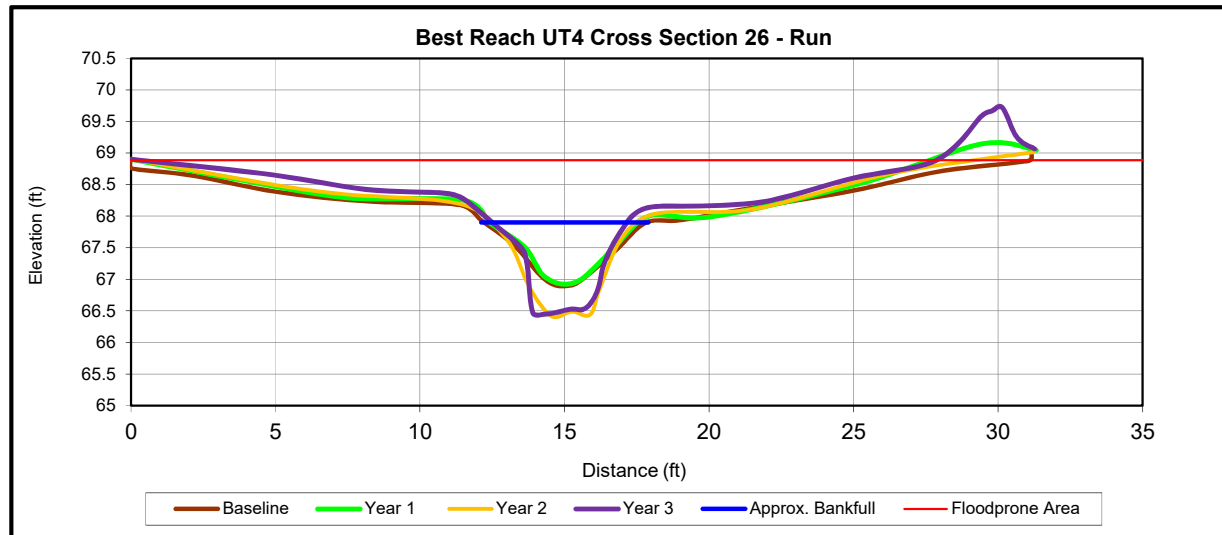

	Cross Section 26 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
Record elevation (datum) used	67.9	67.9	67.9	67.9			
Bankfull Width (ft)	5.6	5.3	6.1	5.7			
Floodprone Width (ft)	50.0	50.0	50.0	50.0			
Bankfull Mean Depth (ft)	0.6	0.5	0.8	0.9			
Bankfull Max Depth (ft)	1.0	0.9	1.6	1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.1	2.7	5.1	5.1			
Bankfull Width/Depth Ratio	10.2	10.2	7.4	6.5			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.0			






Upstream



Downstream

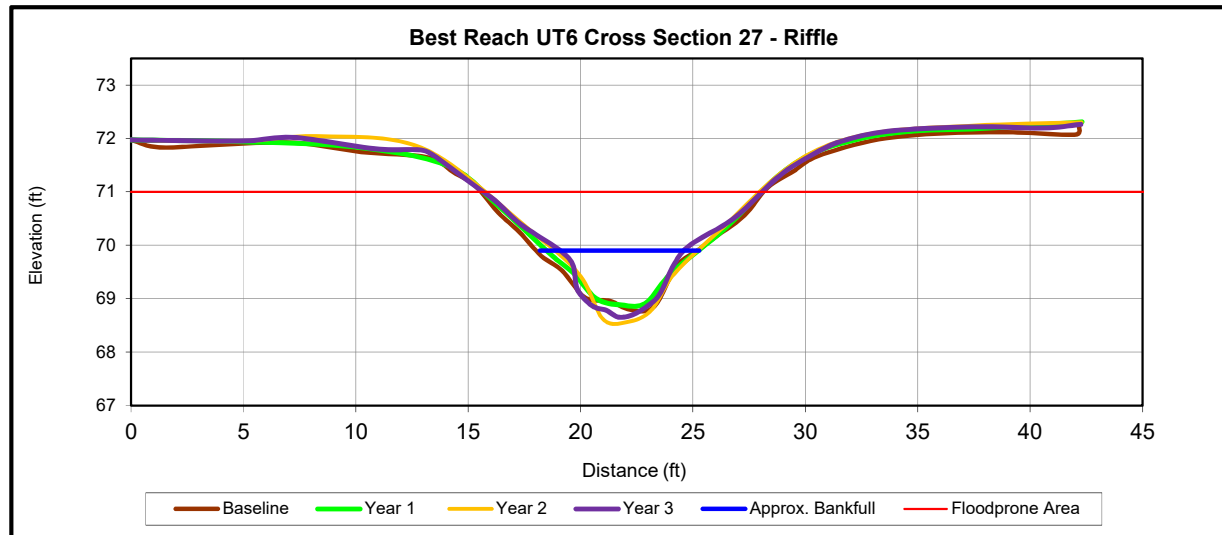


	Cross Section 27 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	69.9	69.9	69.9	69.9			
Bankfull Width (ft)	7.2	6.7	6.5	5.7			
Floodprone Width (ft)	50.0	50.0	50.0	13.2			
Bankfull Mean Depth (ft)	0.7	0.6	0.8	0.8			
Bankfull Max Depth (ft)	1.1	1.0	1.3	1.2			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	4.7	4.1	4.9	4.5			
Bankfull Width/Depth Ratio	10.8	11.0	8.5	7.1			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	0.9			



Upstream



Downstream

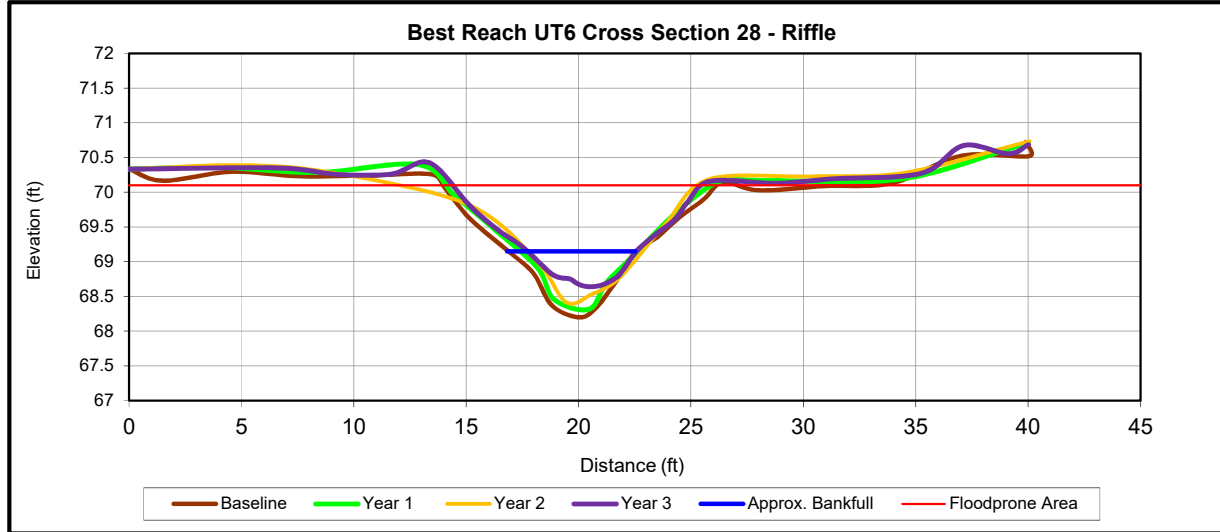


	<b>Cross Section 28 (Run)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	69.2	69.2	69.2	69.2			
Bankfull Width (ft)	5.7	5.3	5.6	5.2			
Floodprone Width (ft)	50.0	15.0	16.8	9.3			
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4			
Bankfull Max Depth (ft)	0.9	0.8	0.8	0.6			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.1	2.4	2.5	1.9			
Bankfull Width/Depth Ratio	10.4	11.4	12.5	14.5			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	1.8			
Bankfull Bank Height Ratio	1.0	1.0	1.0	2.7			



Upstream



Downstream

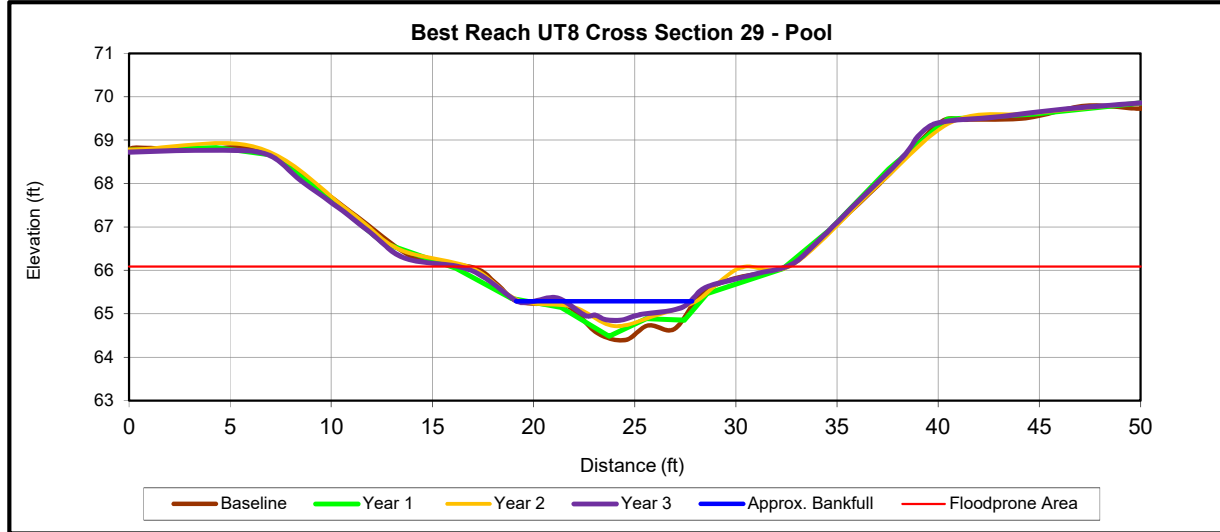


	<b>Cross Section 29 (Pool)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	65.3	65.3	65.3	65.3			
Bankfull Width (ft)	8.7	3.3	8.3	6.3			
Floodprone Width (ft)	50.0	20.0	13.7	15.8			
Bankfull Mean Depth (ft)	0.4	0.4	0.3	0.3			
Bankfull Max Depth (ft)	0.9	0.8	0.6	0.4			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.8	3.3	2.1	1.8			
Bankfull Width/Depth Ratio	19.9	22.1	32.7	22.4			
Bankfull Entrenchment Ratio	>2.2	1.9	1.6	N/A			
Bankfull Bank Height Ratio	1.0	1.0	1.0	N/A			



Upstream



Downstream

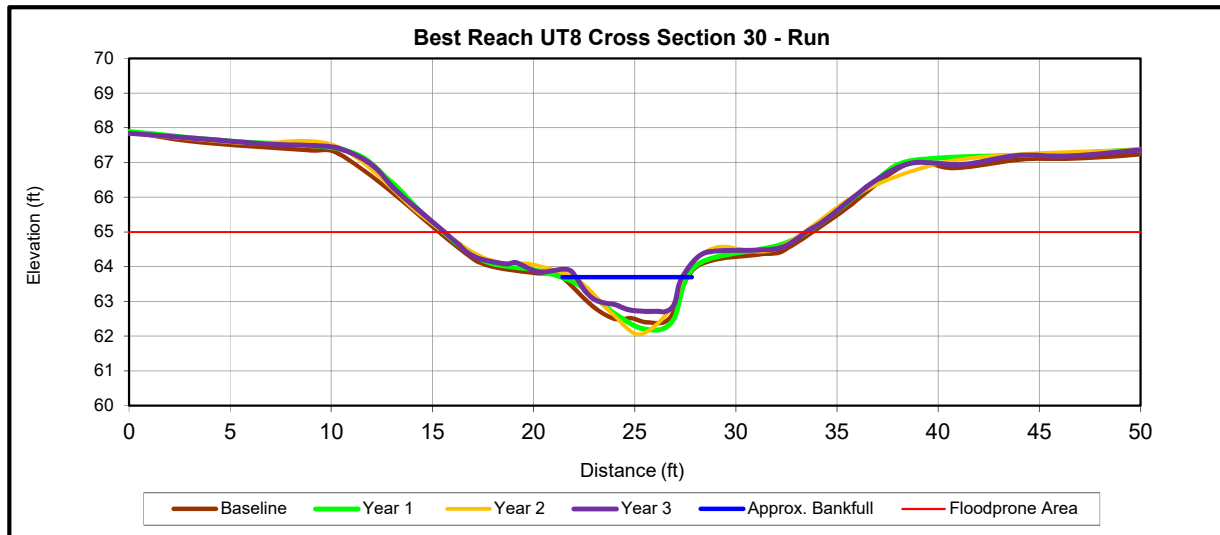


	<b>Cross Section 30 (Run)</b>						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Based on fixed baseline bankfull elevation</b>							
<b>Record elevation (datum) used</b>	63.7	63.7	63.7	63.7			
Bankfull Width (ft)	6.4	6.7	5.6	5.3			
Floodprone Width (ft)	50.0	20.0	19.3	16.4			
Bankfull Mean Depth (ft)	0.9	0.8	0.9	0.7			
Bankfull Max Depth (ft)	1.3	1.5	1.6	1.0			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	5.7	5.6	5.1	4.0			
Bankfull Width/Depth Ratio	7.1	7.9	6.3	7.2			
Bankfull Entrenchment Ratio	>2.2	>2.2	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.2			



Upstream



Downstream

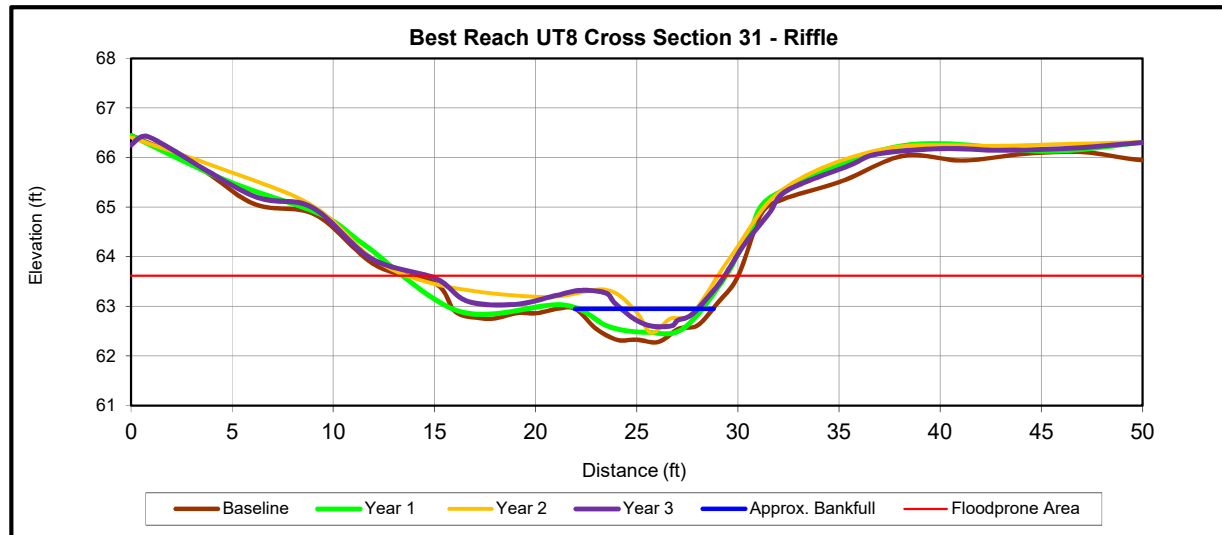

	<b>Cross Section 31 (Riffle)</b>						
Based on fixed baseline bankfull elevation	Base	MY1	MY2	MY3	MY5	MY7	MY+
<b>Record elevation (datum) used</b>	63.0	63.0	63.0	63.0			
Bankfull Width (ft)	7.7	8.5	3.4	4.0			
Floodprone Width (ft)	50.0	15.0	14.2	13.4			
Bankfull Mean Depth (ft)	0.4	0.2	0.3	0.3			
Bankfull Max Depth (ft)	0.7	0.5	0.5	0.4			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	3.0	2.1	0.9	1.1			
Bankfull Width/Depth Ratio	19.5	34.5	13.2	14.9			
Bankfull Entrenchment Ratio	>2.2	1.7	>2.2	>2.2			
Bankfull Bank Height Ratio	1.0	1.0	1.0	1.7			

# **Appendix E**

## **Hydrology Data**

Table 13. Documentation of Geomorphologically Significant Flow Events

Table 14. Rainfall Summary

Table 15a. Wetland Hydrology Criteria Attainment

Table 15b. MY1-MY3 Wetland Hydrology Summary

Chart 1. 2017 Precipitation Data for Best Site

Chart 2. 2017 Groundwater Monitoring Gauge Hydrographs

Figure 8. Crest Gauge Verification Photos

**Table 13. Documentation of Geomorphologically Significant Flow Events**

Crest Gauge	Stream Reach	Number of Bankfull Events	Date of Highest Bankfull Event	Maximum Bankfull Height (ft.)	Photo Number
Crest Gauge 1	UT-1	6	9/21/2017	0.25	1
Crest Gauge 2	UT-2	22	9/21/2017	1.19	2
Crest Gauge 3	UT-3	9	8/13/2017	0.55	3
Crest Gauge 4	UT-4	0	N/A	N/A	4
Crest Gauge 5	UT-6	7	8/13/2017	1.2	5
Crest Gauge 6	UT-8	13	8/13/2017	2.15	6

**Table 14. 2017 Rainfall Summary**

Month	Average	Normal Limits		Albert Ellis Airport Station Precipitation	On-Site Auto Rain Gauge
		30 Percent	70 Percent		
January	4.33	3.32	5.03	4.34	4.47
February	3.23	2.14	3.87	1.54	2.21
March	4.50	3.23	5.32	2.59	2.65
April	3.16	1.70	3.85	6.20	10.04
May	3.68	2.69	4.34	4.88	3.44
June	4.49	3.11	5.34	3.06	2.82
July	6.06	4.16	7.22	5.58	2.54*
August	5.40	3.12	6.56	8.01	---
September	5.00	2.04	6.07	3.11	---
October	3.21	1.62	3.92	2.40	---
November	2.89	1.83	3.49	---	---
December	3.24	2.14	3.88	---	---
Total	49.19	31.10	58.89	41.73	25.63

\* On-Site Auto Rain Gauge data missing July 10, 2017-November 14, 2017

**Table 15a. 2017 Wetland Hydrology Criteria Attainment**

<b>2017 Max Hydroperiod (Growing Season 17-Mar through 14-Nov, 242 days)</b>					
<b>Success Criterion 9% = 22 Consecutive Days</b>					
<b>Gauge</b>	<b>Consecutive</b>		<b>Cumulative</b>		<b>Occurrences</b>
	<b>Days</b>	<b>Percent of growing Season</b>	<b>Days</b>	<b>Percent of growing Season</b>	
<b>AW1</b>	53	22	156	64	11
<b>AW2</b>	49	20	114	47	12
<b>AW3</b>	118	49	225	93	6
<b>AW4</b>	117	48	217	89	7
<b>AW5</b>	120	49	214	88	6
<b>AW6</b>	55	23	167	69	13
<b>AW7</b>	13	5	87	36	21
<b>AW8</b>	16*	7	94*	39	20
<b>AW9</b>	14*	6	74*	31	20
<b>RAW1</b>	71	29	182	75	9
<b>RAW2</b>	24	10	51	21	14
<b>RAW3</b>	45	19	135	56	13

\*AW8 and AW9 missing data for March 17, 2017 - May 3, 2017 = 48 days


**Table 15b. MY1, MY2, MY3 Wetland Hydrology Gauge Summary**

<b>Gauge</b>	<b>MY1 - 2015</b>		<b>MY2 - 2016</b>		<b>MY3 - 2017</b>	
	<b>Consecutive</b>		<b>Consecutive</b>		<b>Consecutive</b>	
	<b>Days</b>	<b>Percent of growing Season</b>	<b>Days</b>	<b>Percent of growing Season</b>	<b>Days</b>	<b>Percent of growing Season</b>
<b>AW1</b>	49	20	53	22	53	22
<b>AW2</b>	18	7	18	7	49	20
<b>AW3</b>	88	36	99	41	118	49
<b>AW4</b>	88	36	97	40	117	48
<b>AW5</b>	51	21	103	43	120	49
<b>AW6</b>	28	12	42	17	55	23
<b>AW7</b>	22	9	17	7	13	5
<b>AW8</b>	24	10	32	13	16*	7
<b>AW9</b>	24	10	18	7	14*	6
<b>RAW1</b>	52	21	34	14	71	29
<b>RAW2</b>	46	19	10	4	24	10
<b>RAW3</b>	29	12	32	13	45	19

\*AW8 and AW9 missing data for March 17, 2017 - May 3, 2017 = 48 days




Chart 1. 2017 Precipitation Data for Best Site

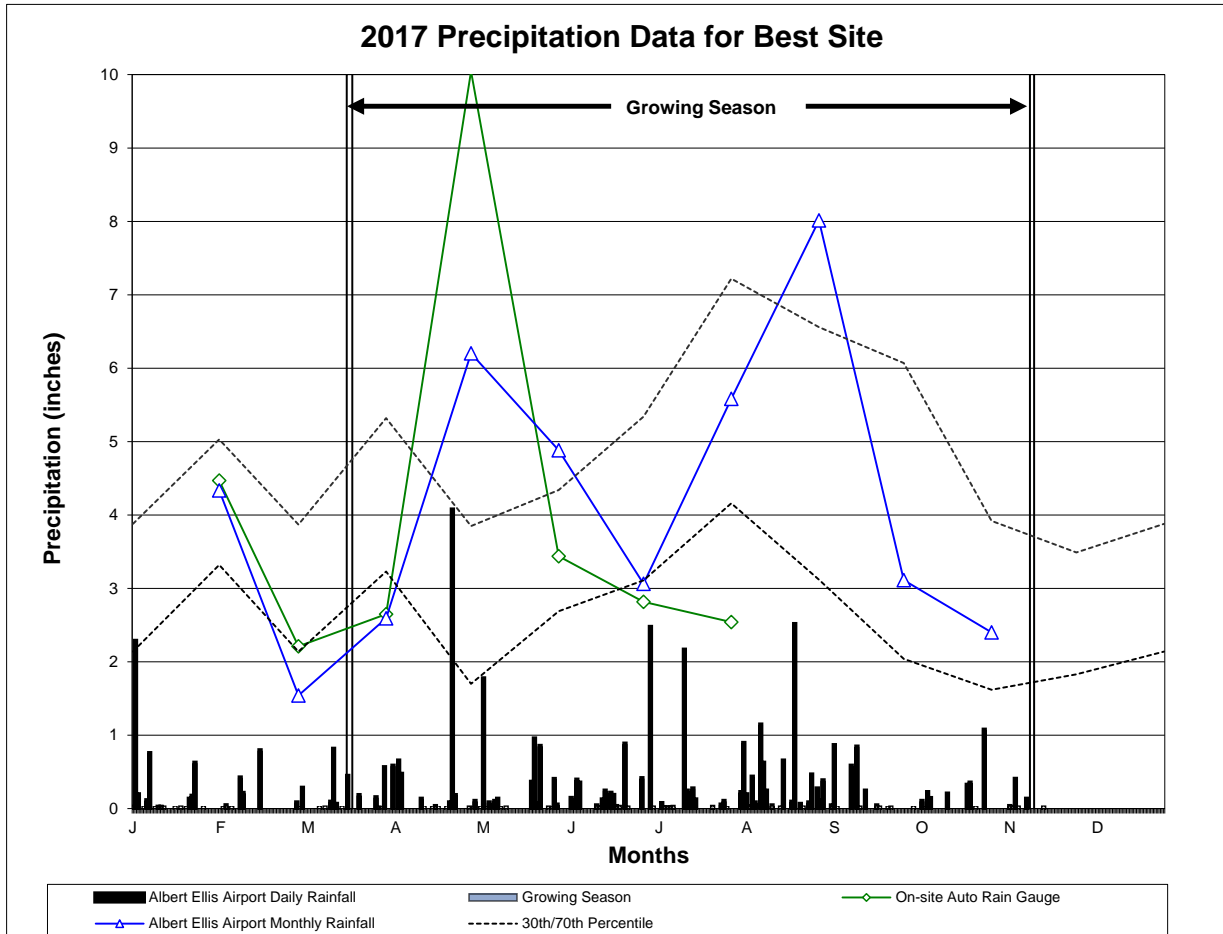


\*On-Site Auto Rain Gauge data missing July 10, 2017-November 14, 2017


Chart 2. 2017 Best Site Groundwater Monitoring Gauge Hydrographs

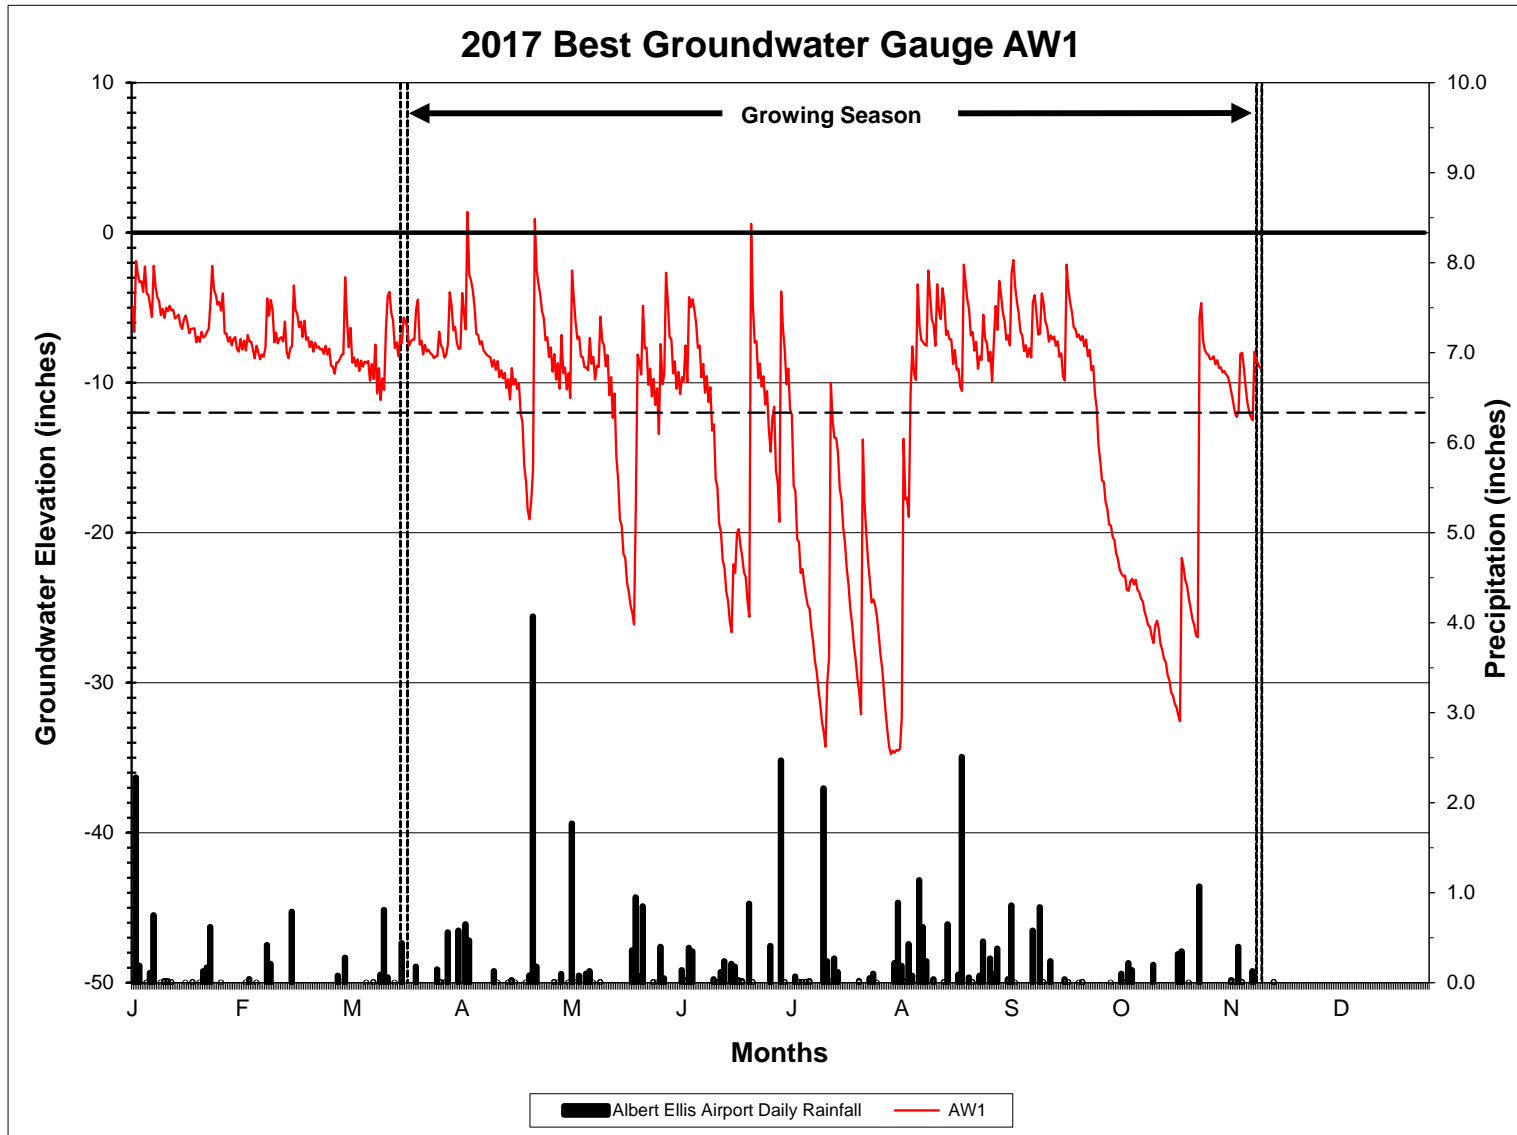


Appendix E – Crest Gauge Verification Photos

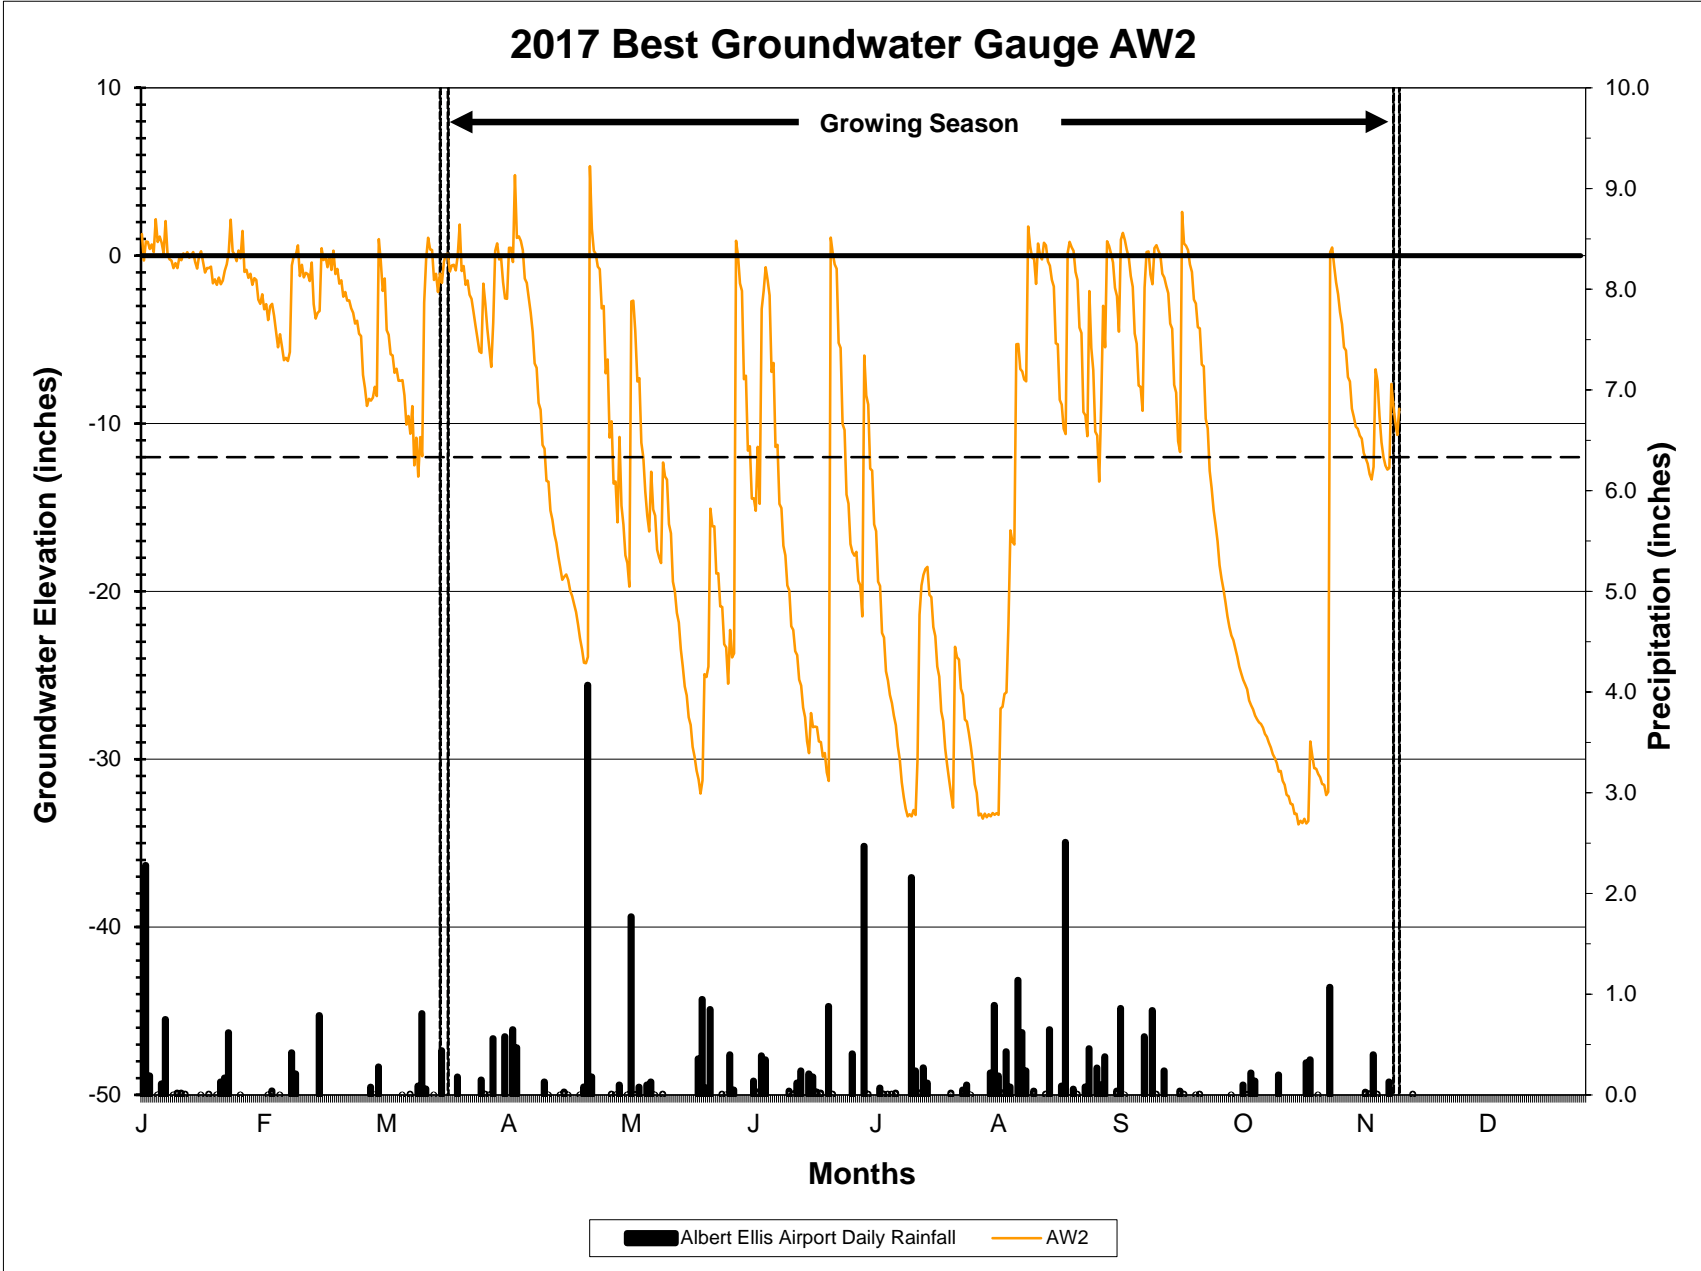


Appendix E – Crest Gauge Verification Photos

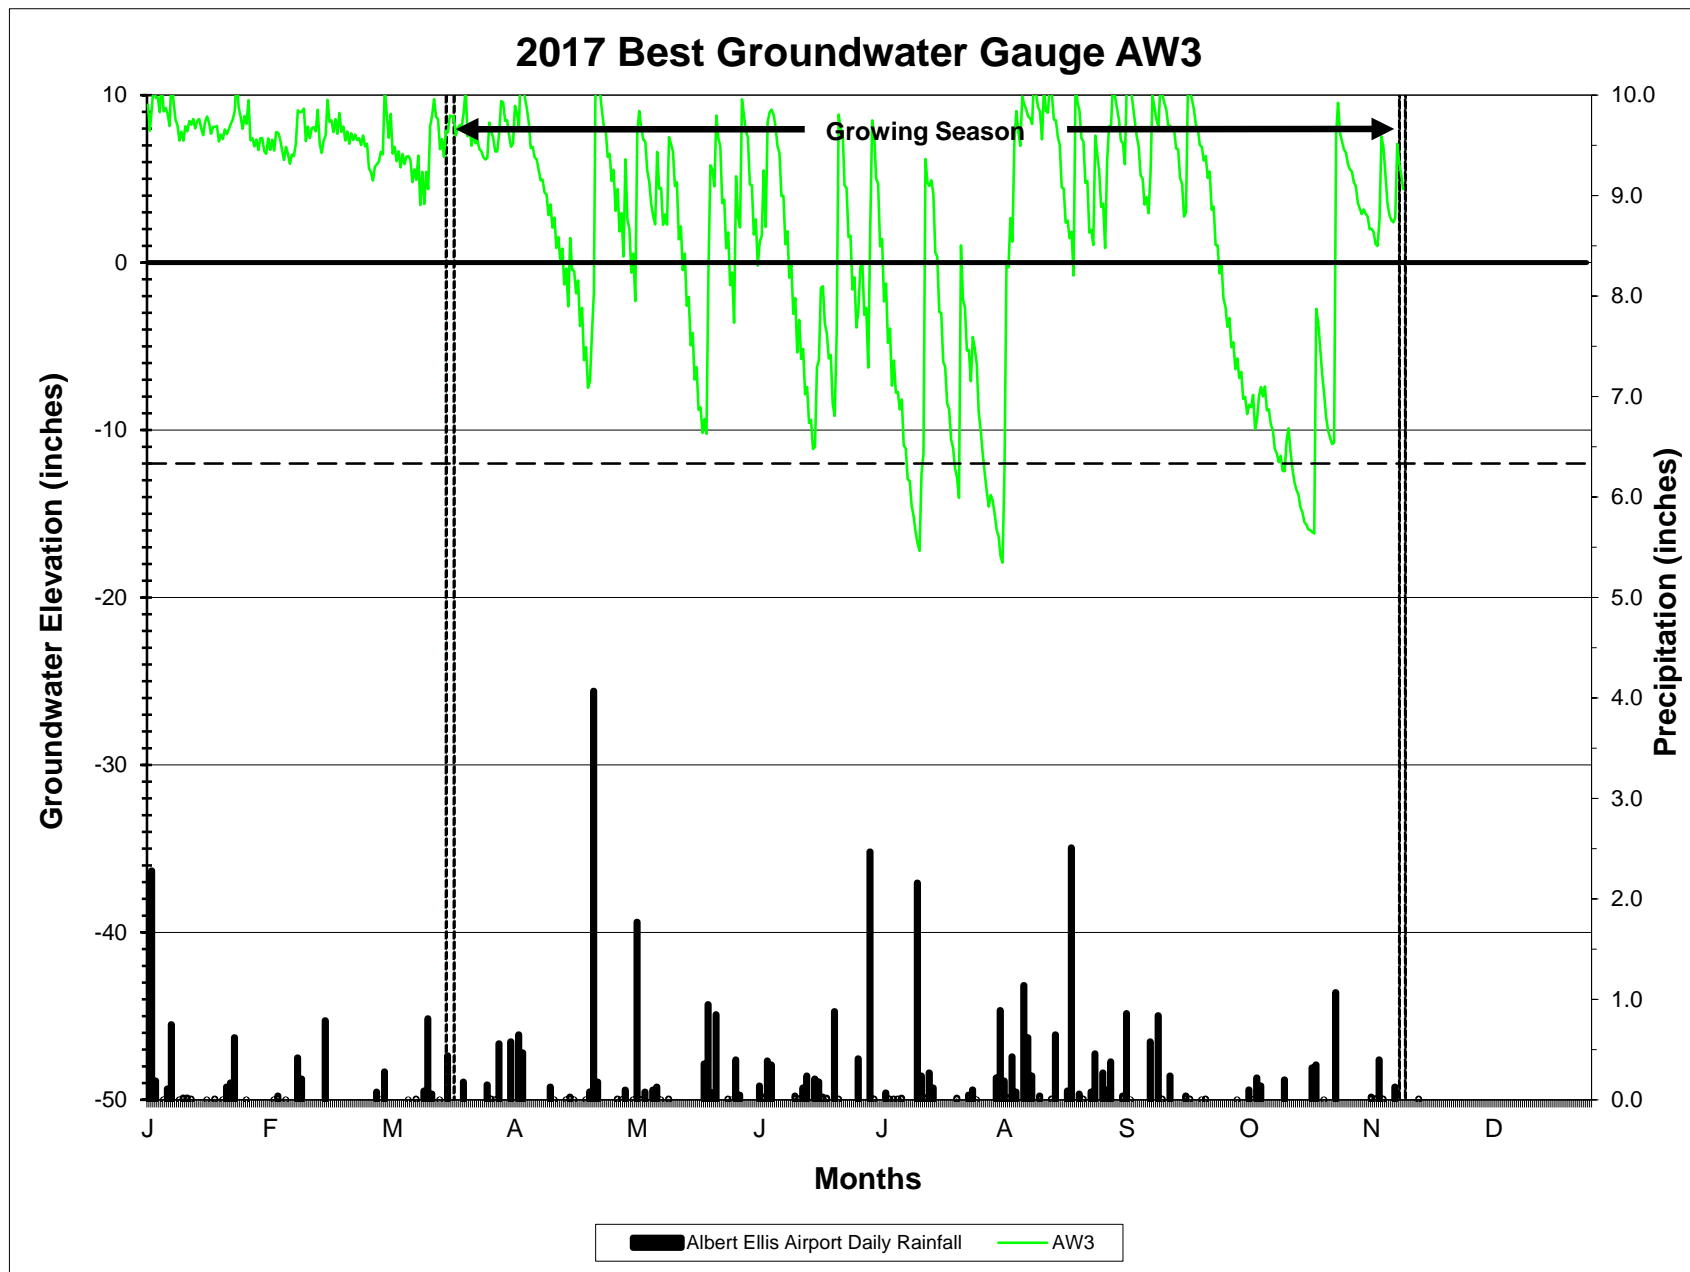


Appendix E – Crest Gauge Verification Photos

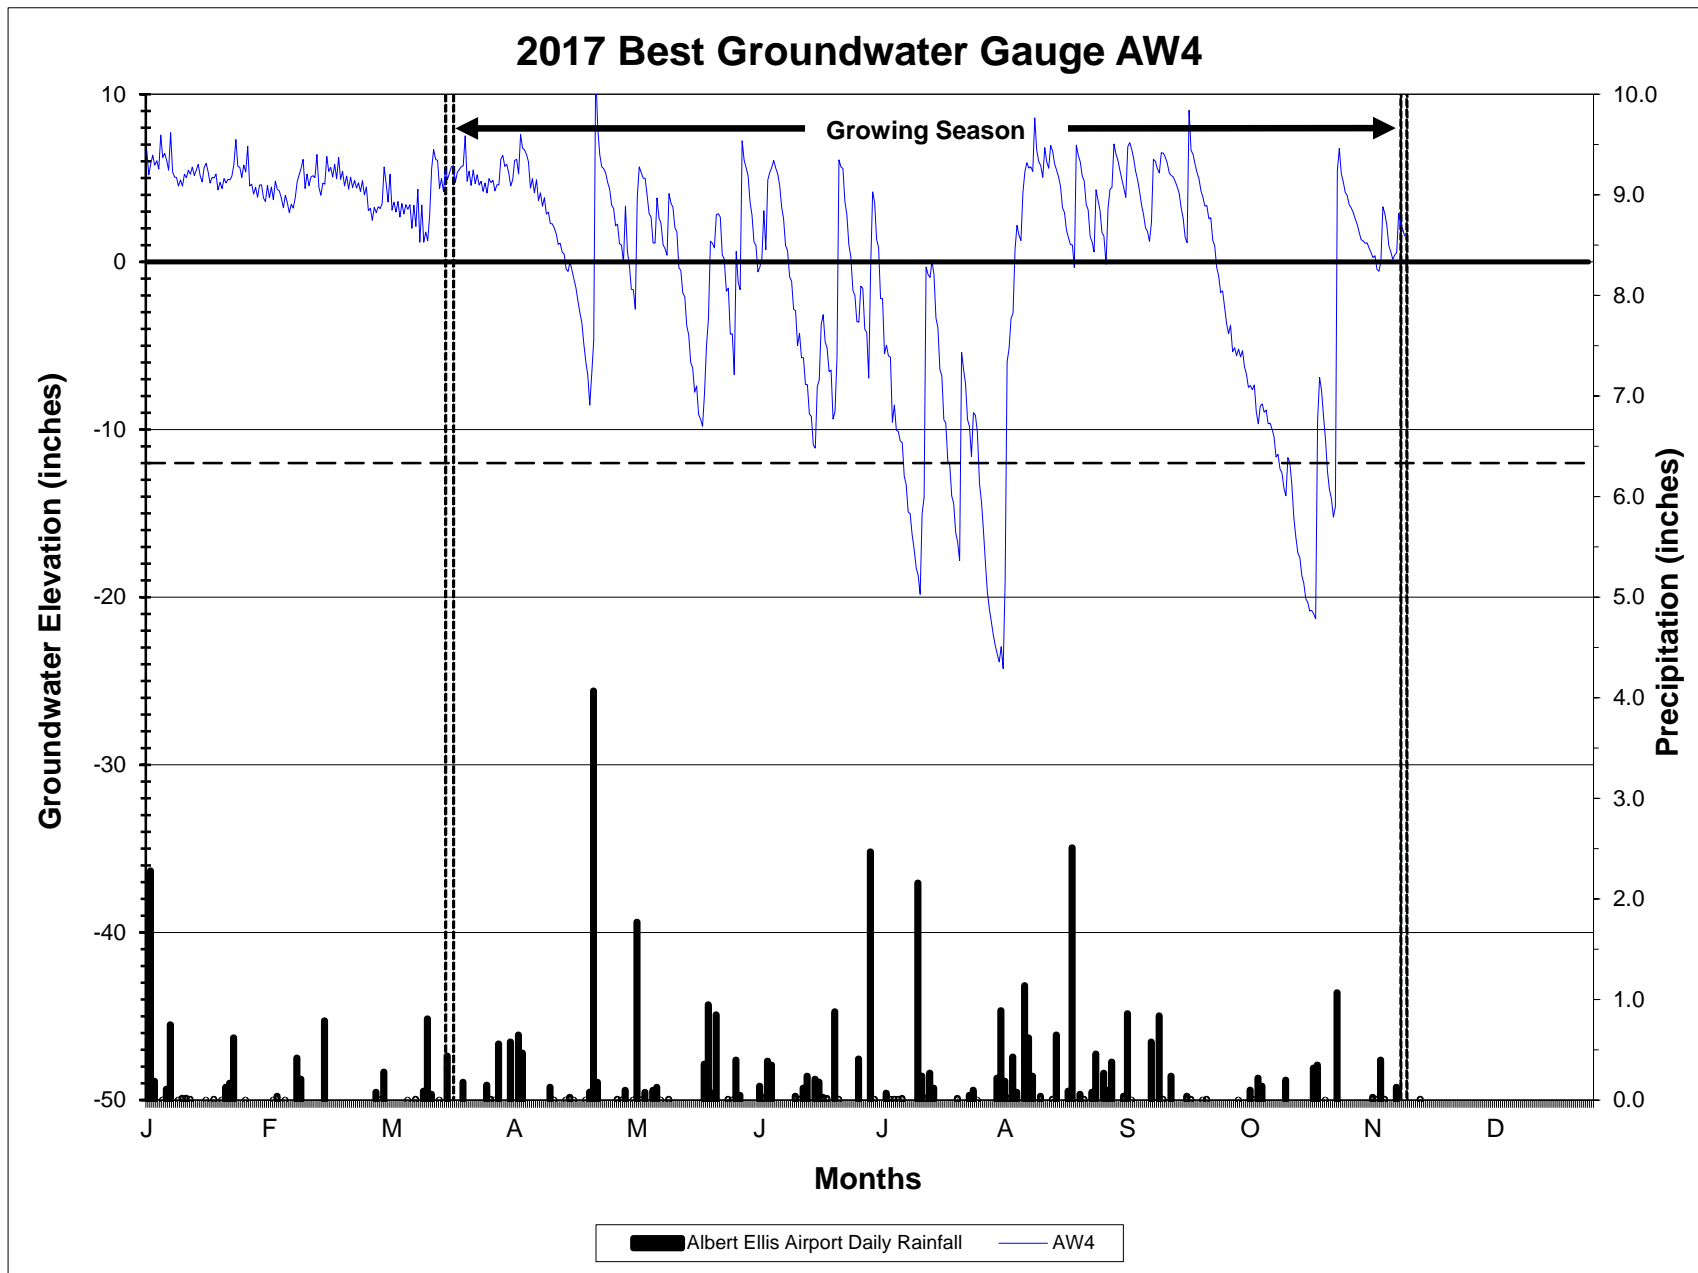


Appendix E – Crest Gauge Verification Photos

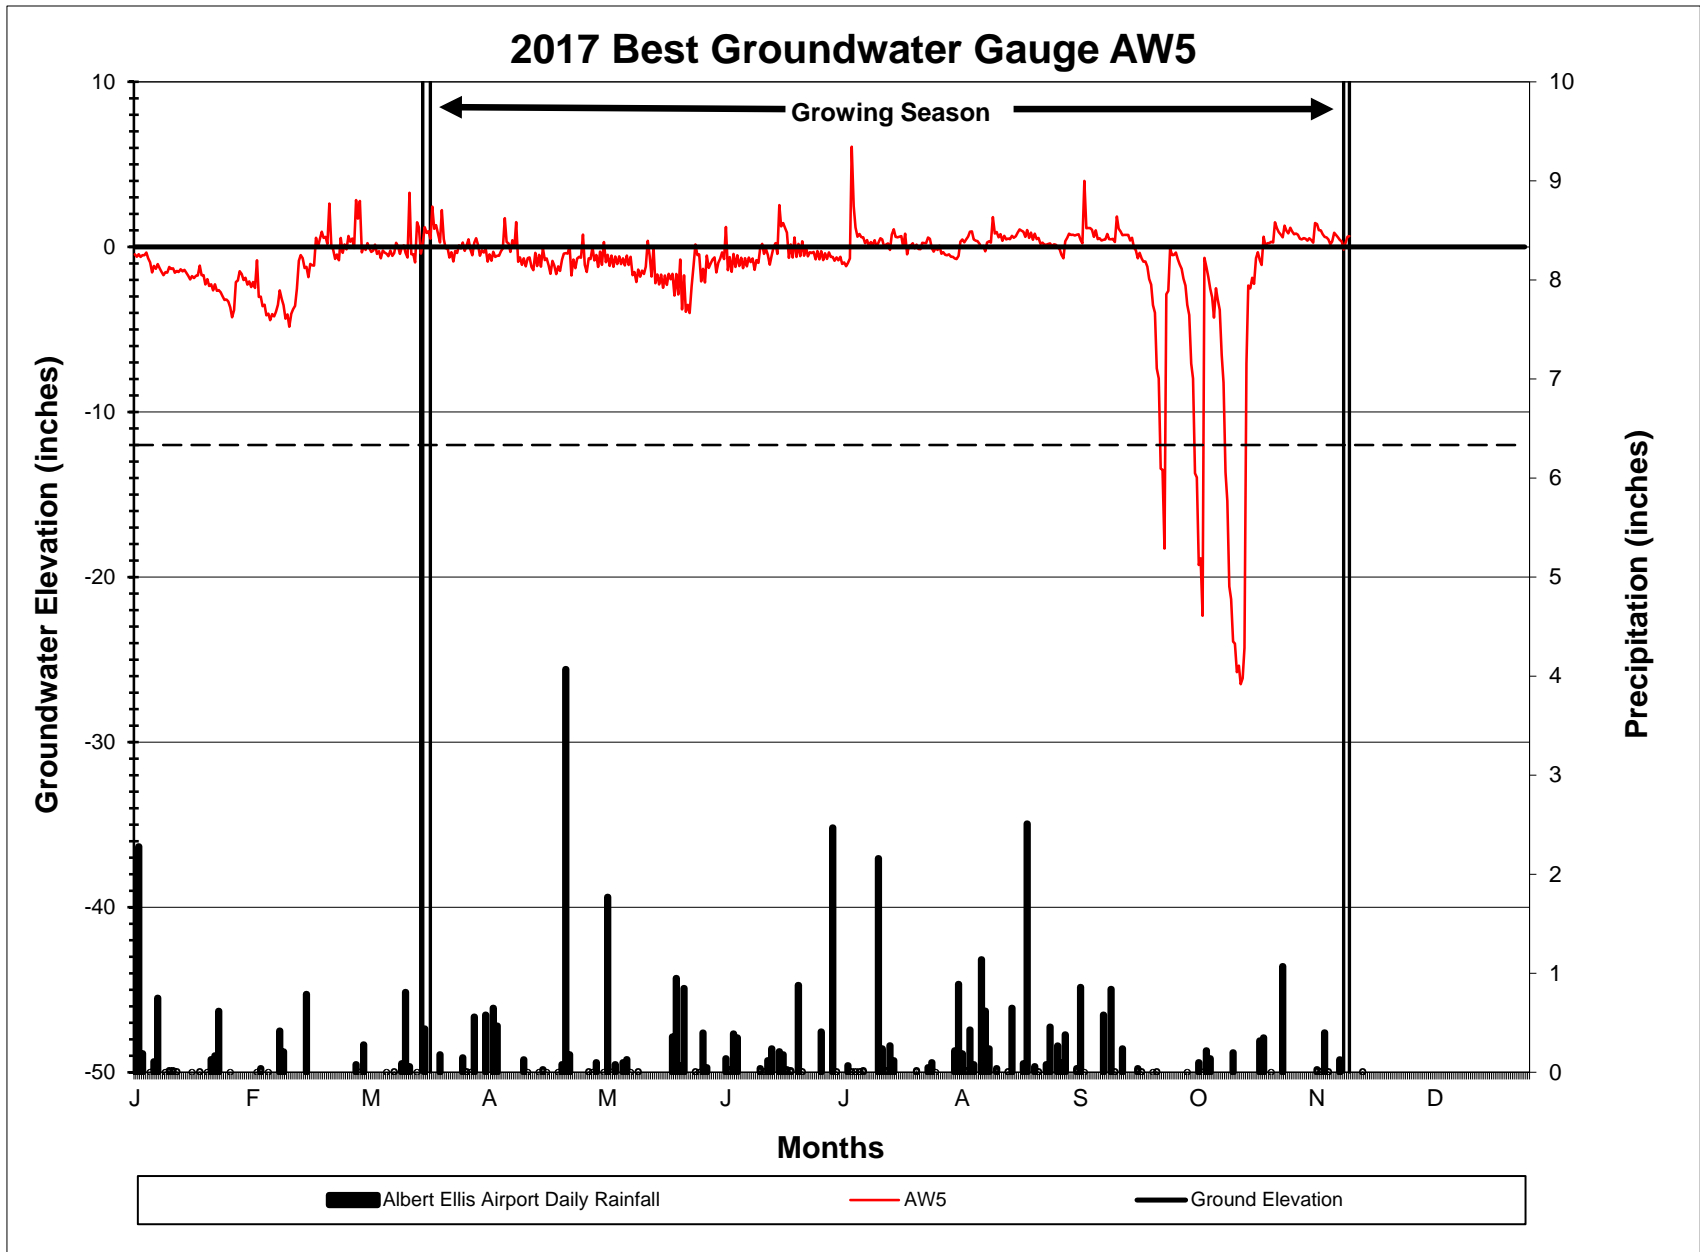

Appendix E – Crest Gauge Verification Photos

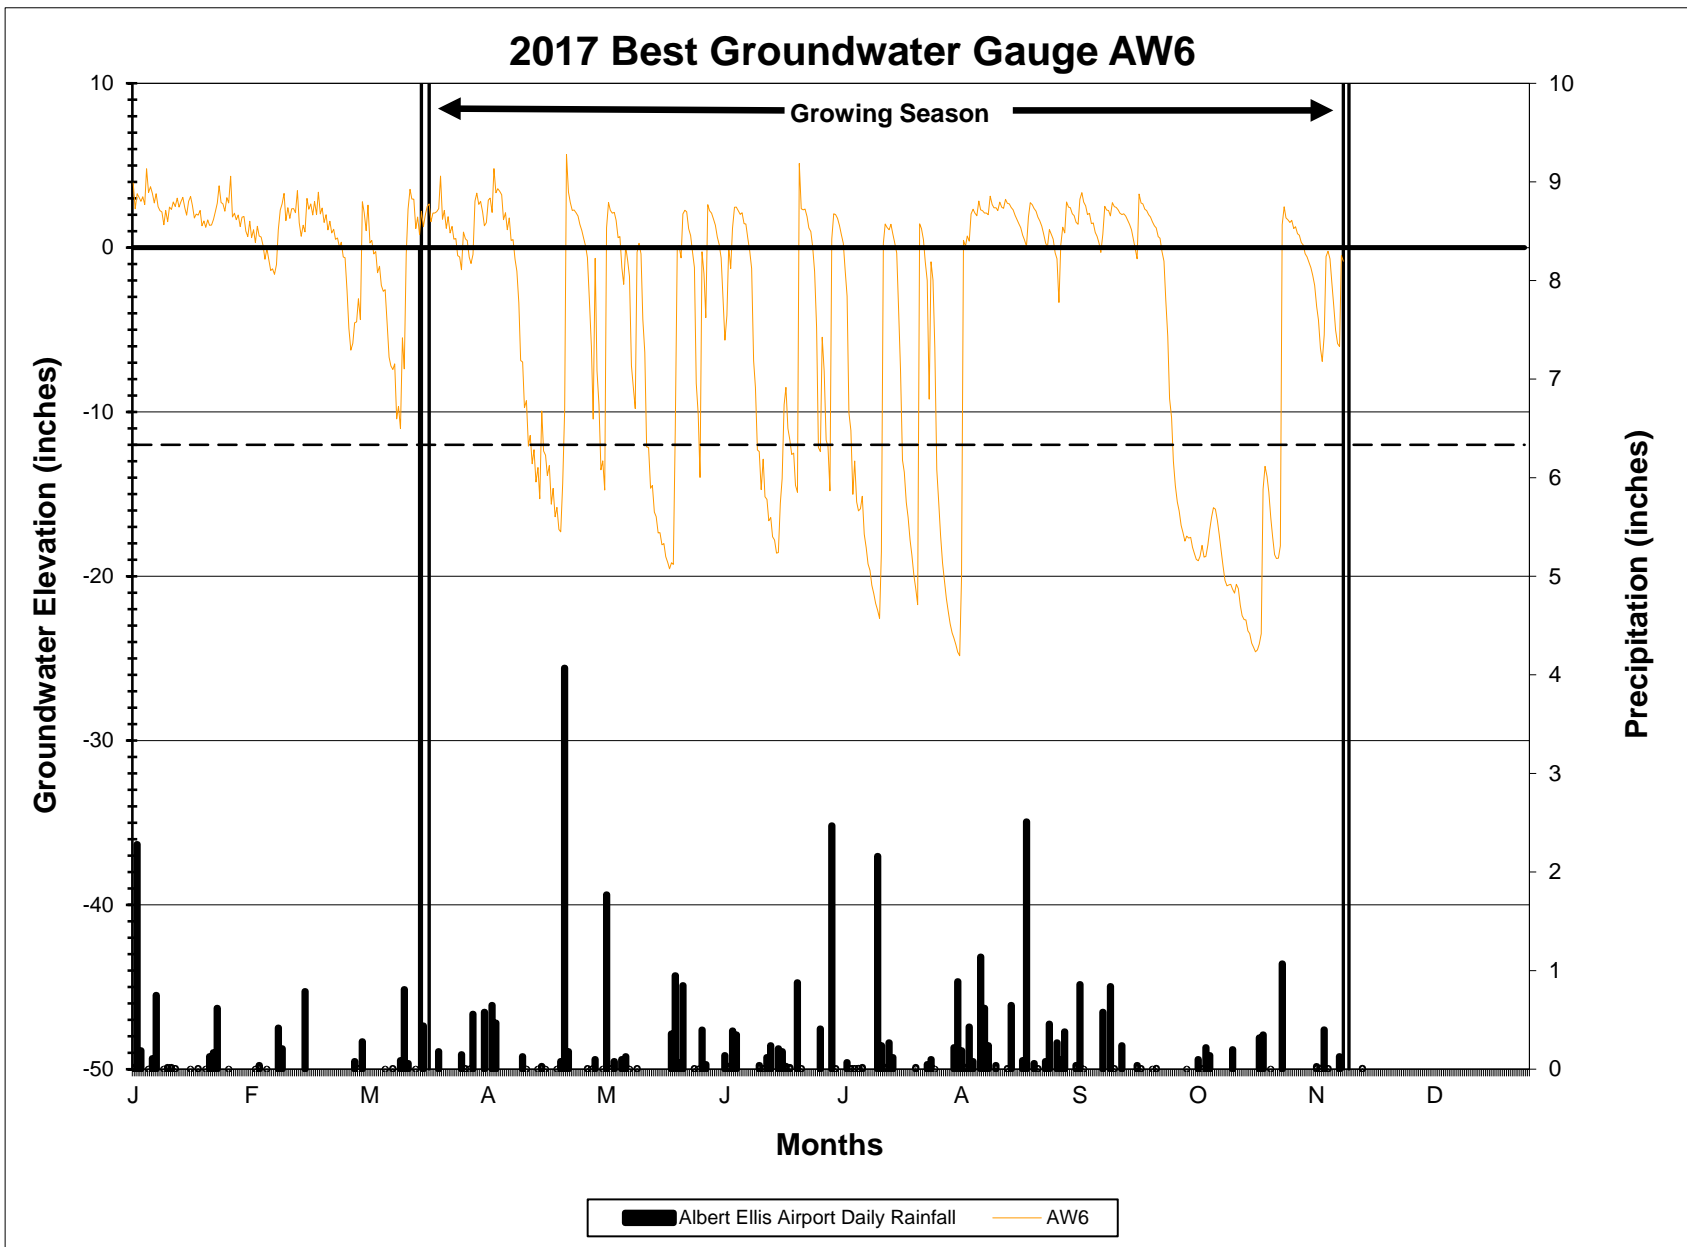


Appendix E – Crest Gauge Verification Photos

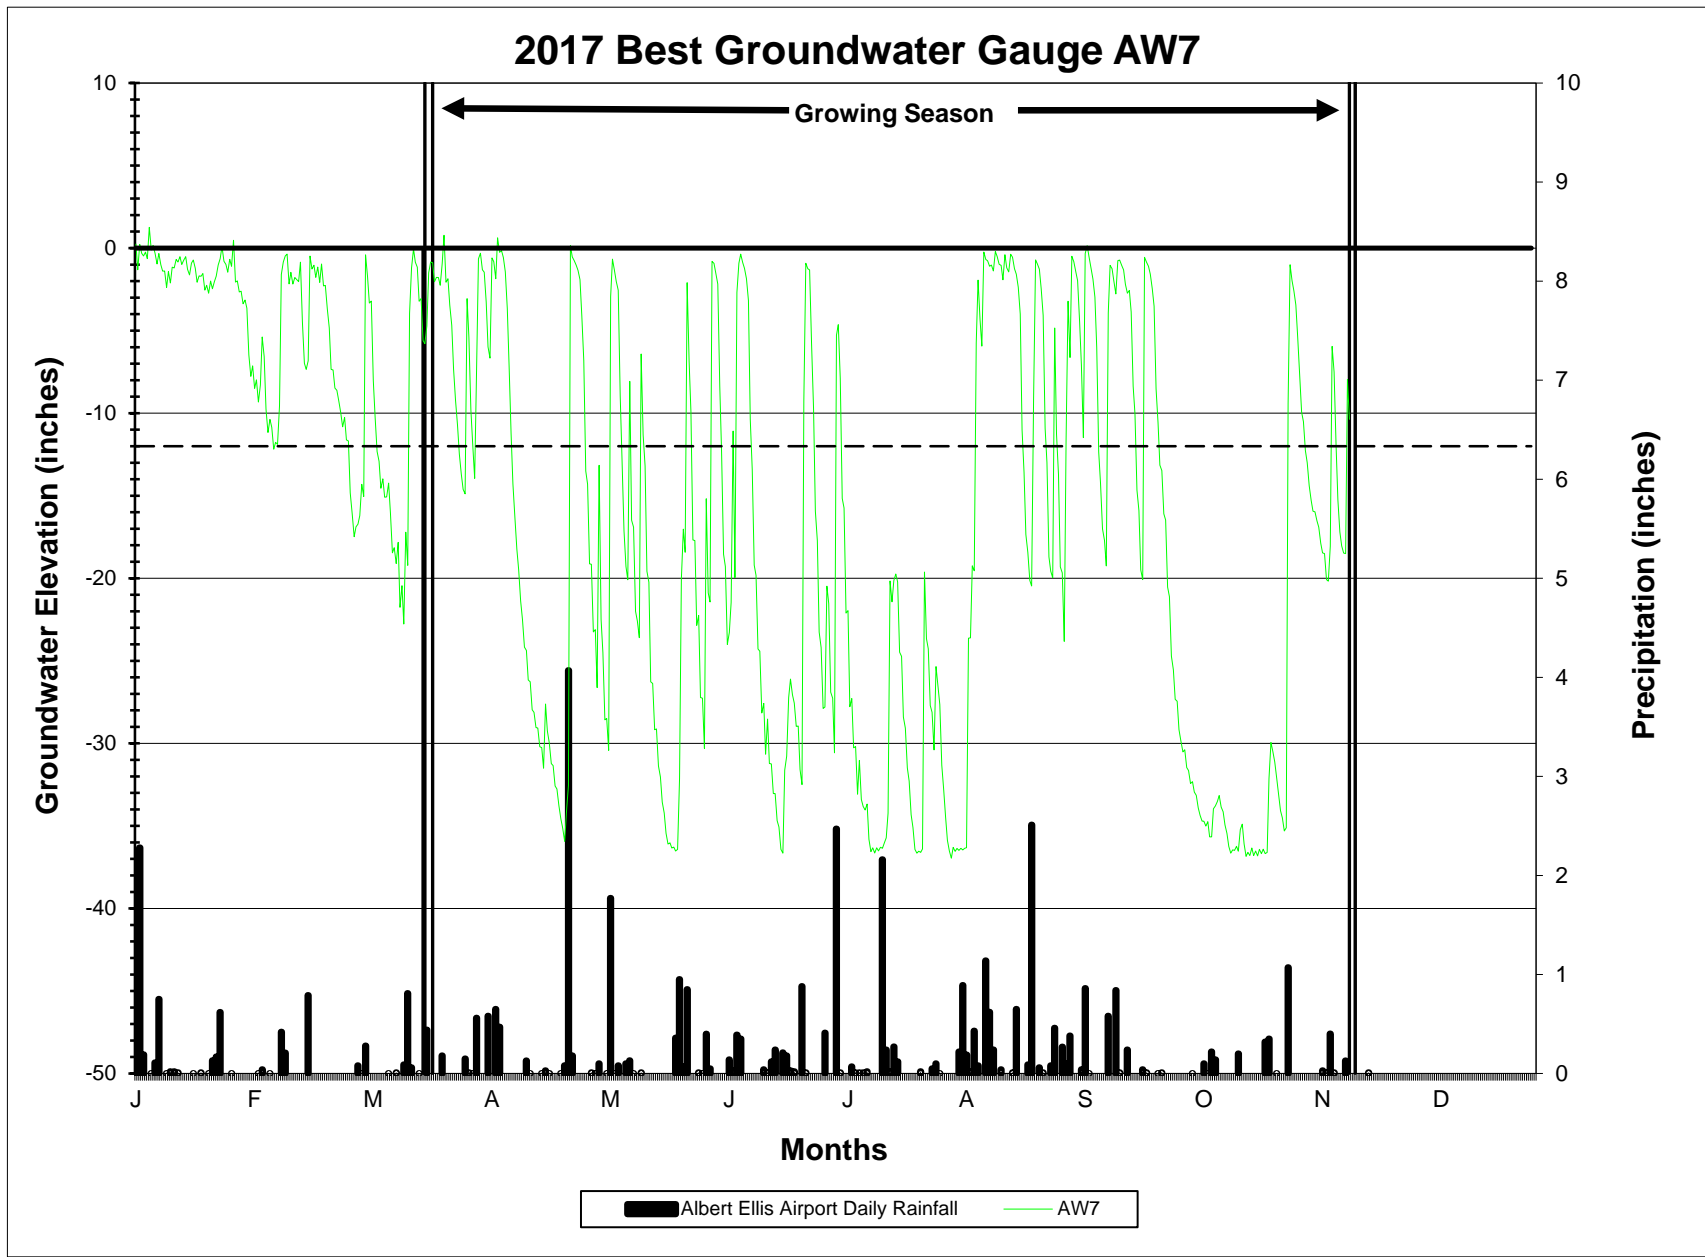




Appendix E – Crest Gauge Verification Photos

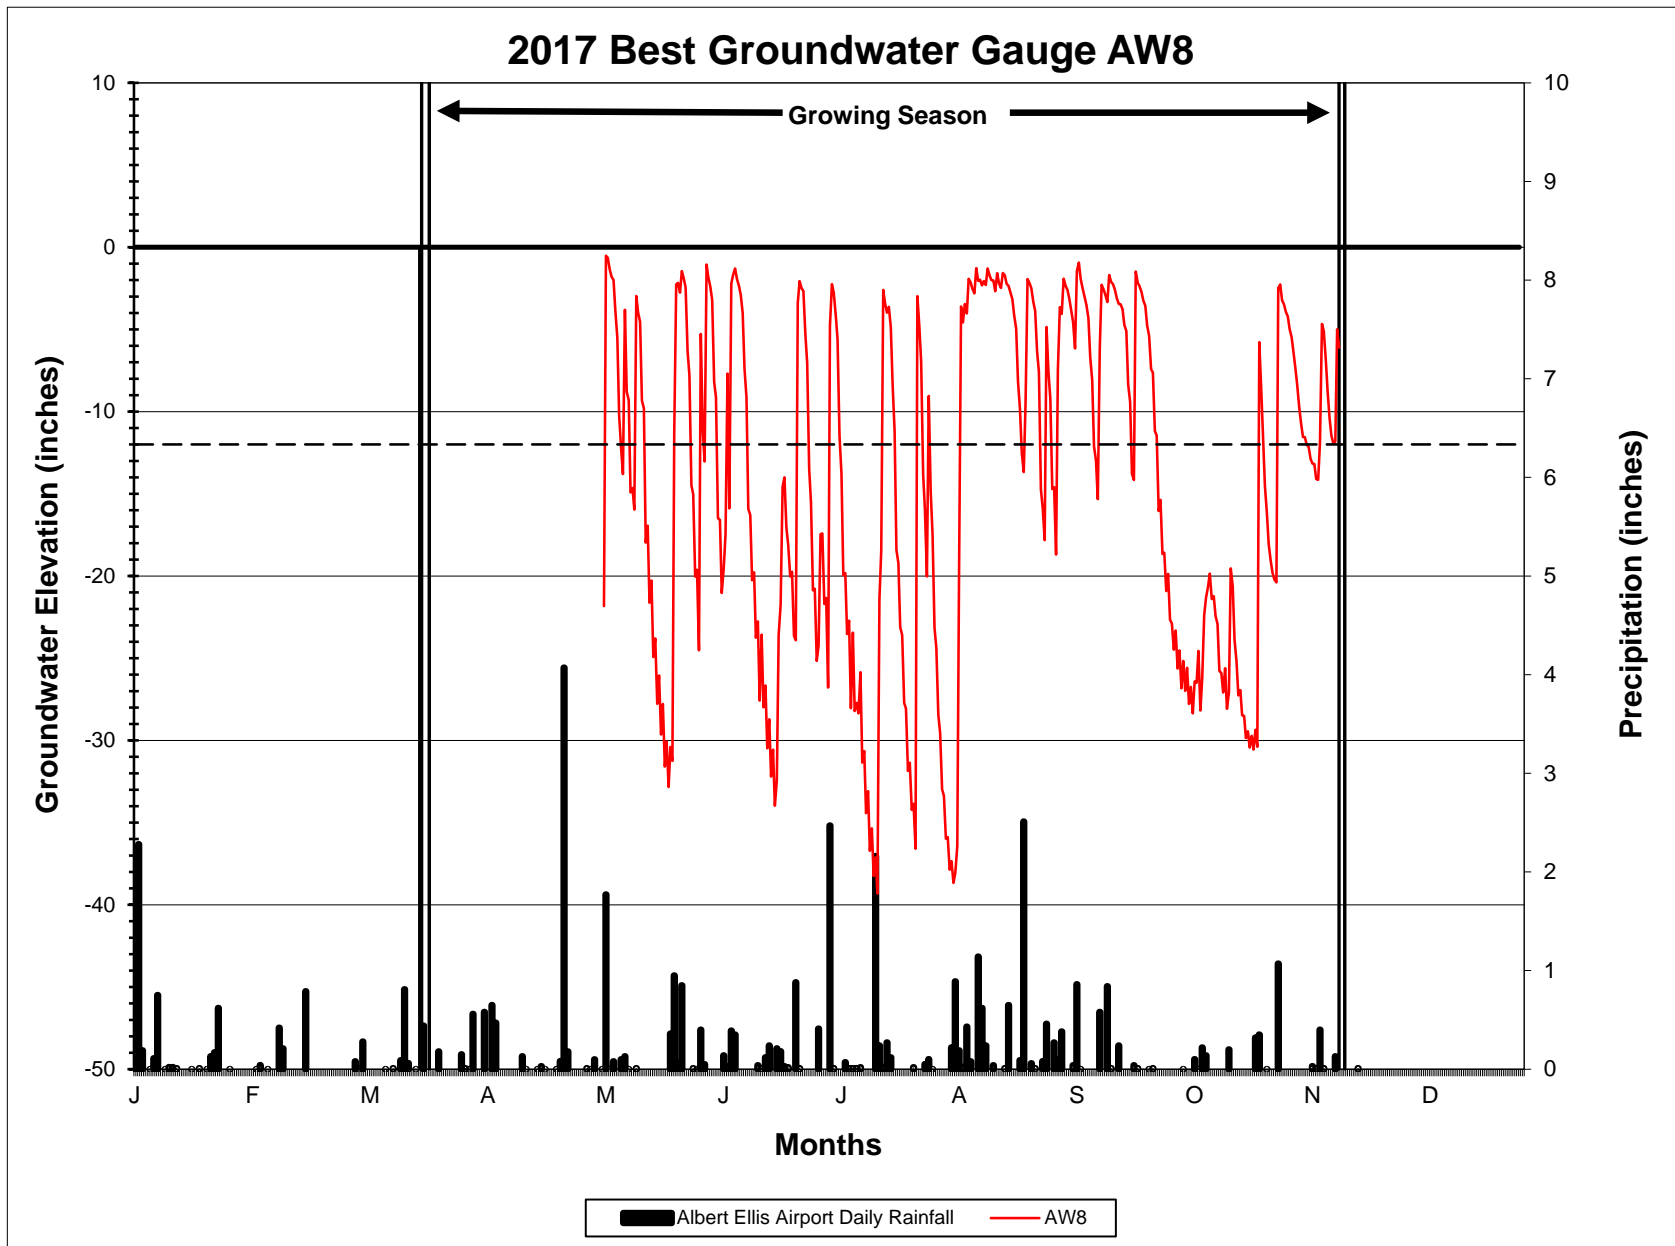


\*Well data missing before May 4, 2017

Appendix E – Crest Gauge Verification Photos

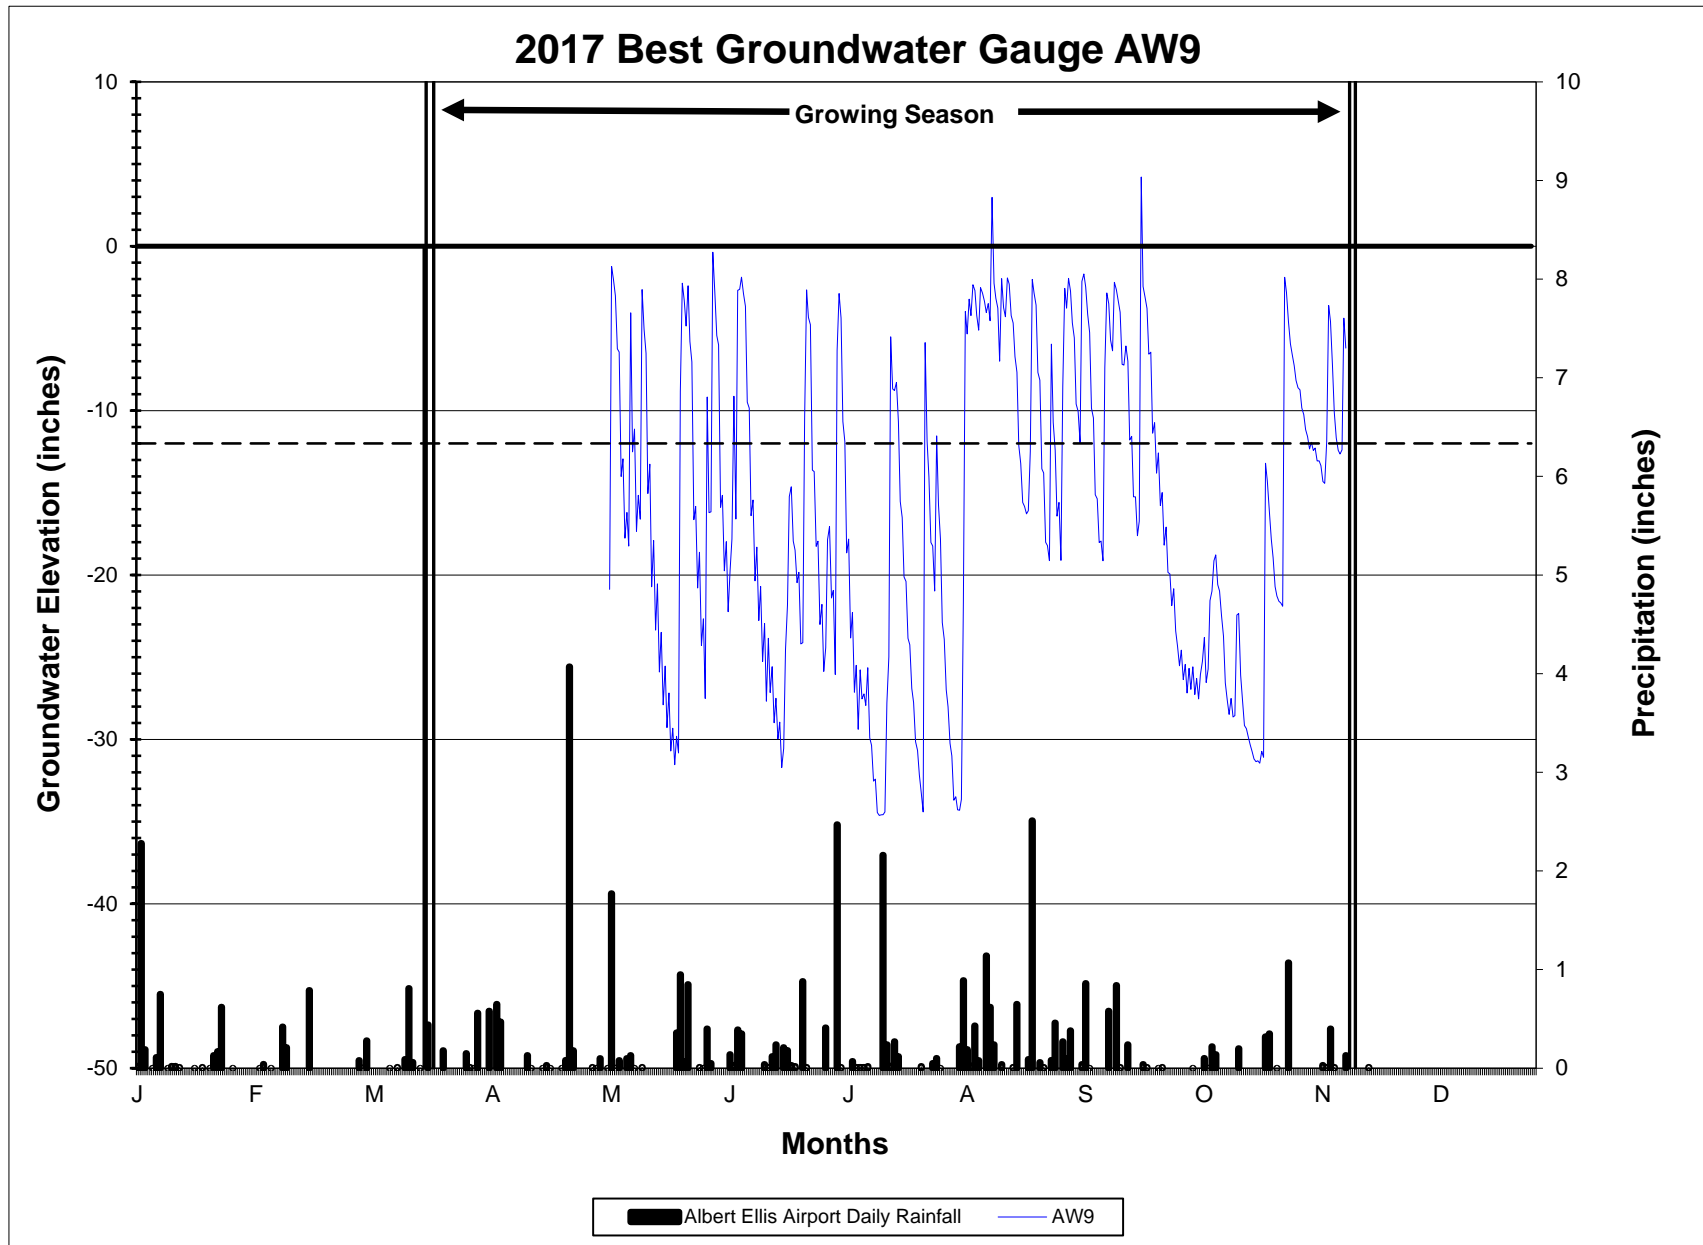


\*Well data missing before May 4, 2017


Appendix E – Crest Gauge Verification Photos

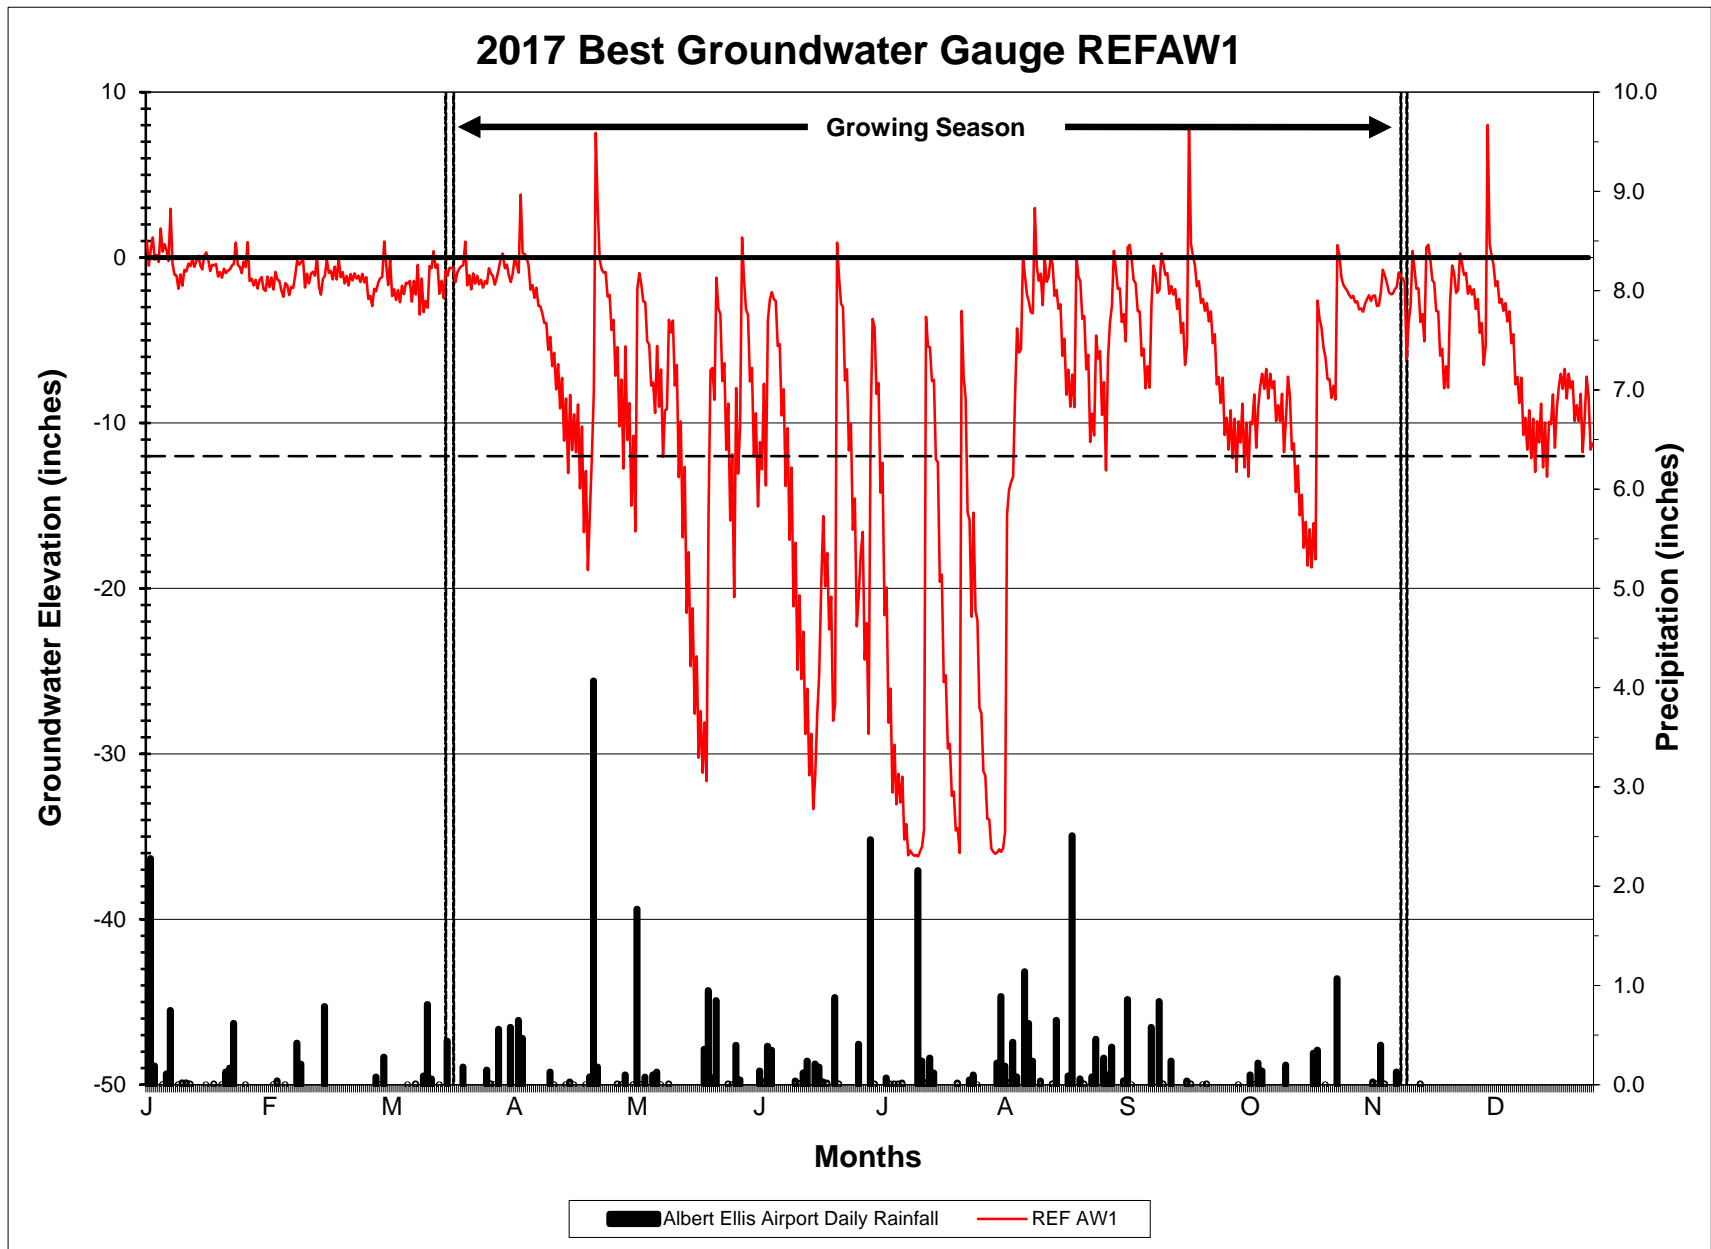

Appendix E – Crest Gauge Verification Photos

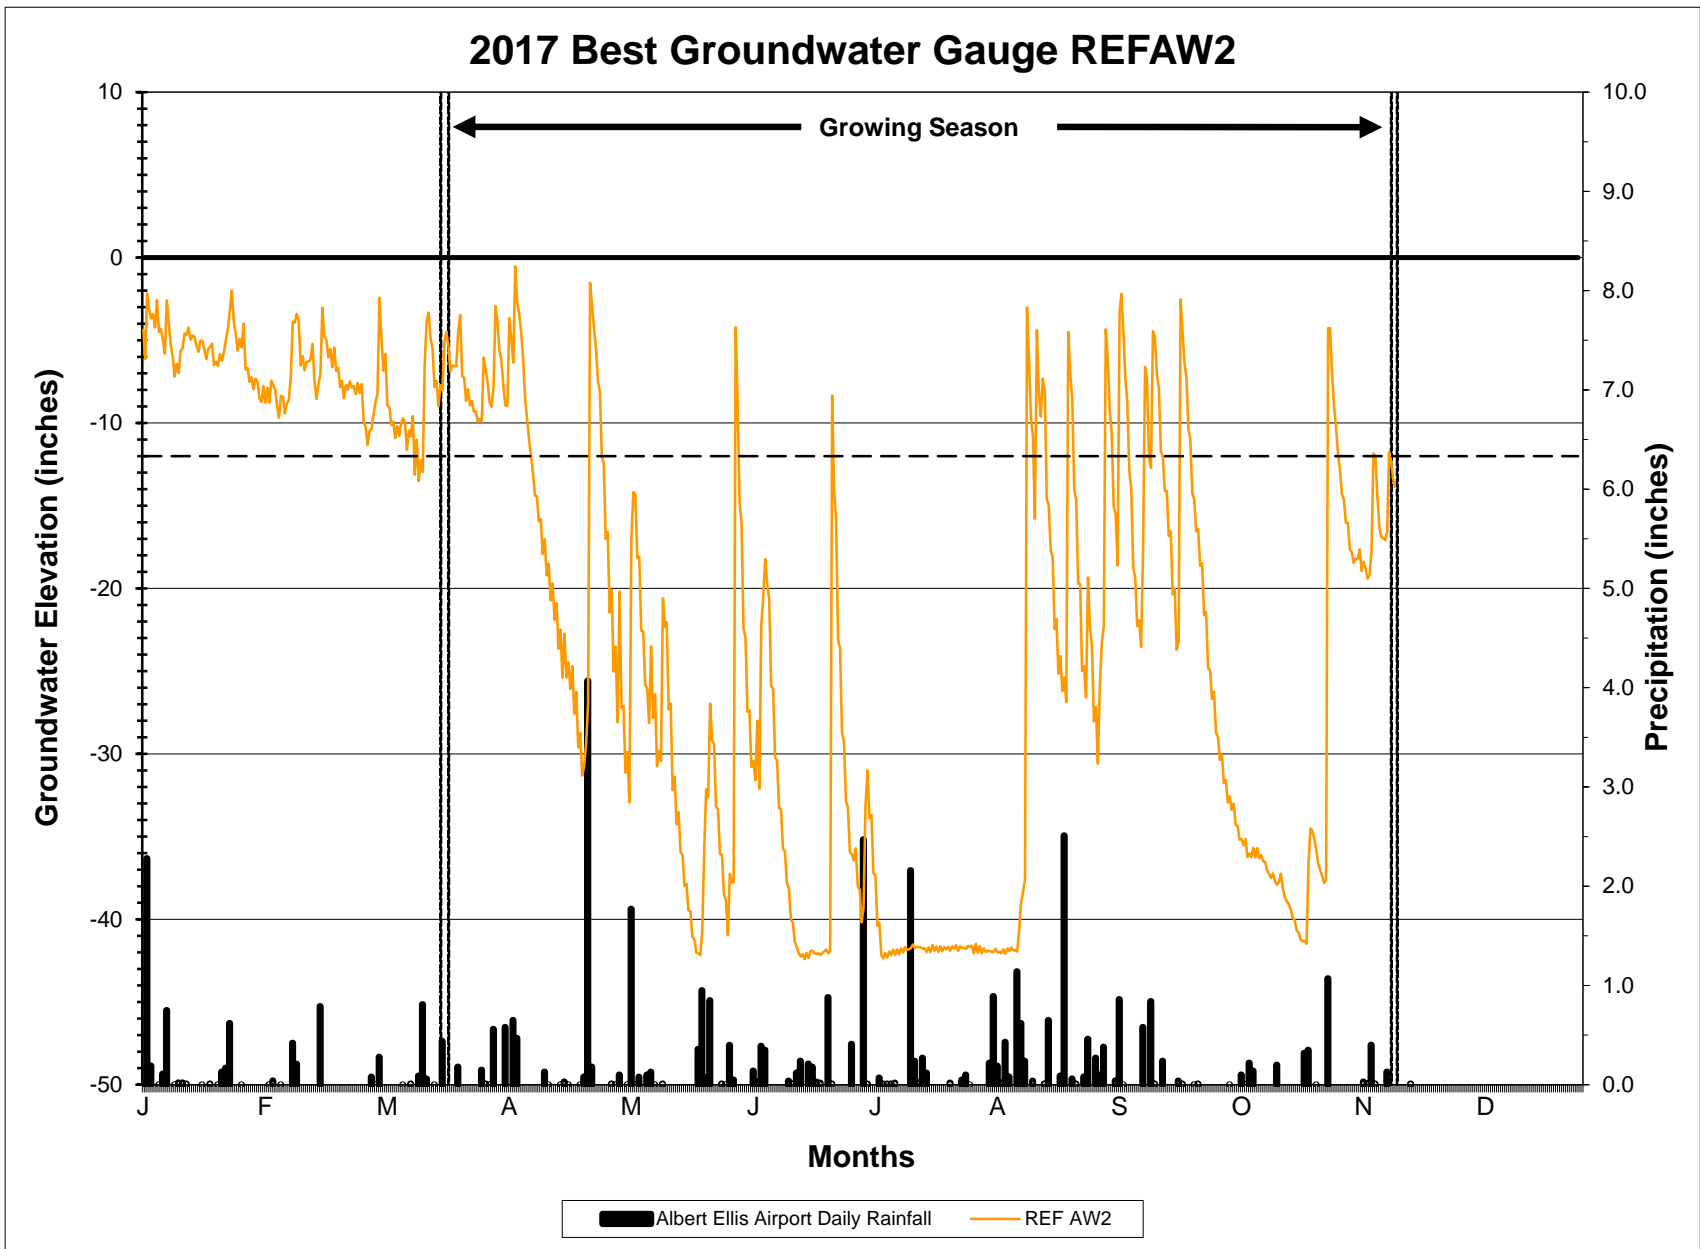

Appendix E – Crest Gauge Verification Photos

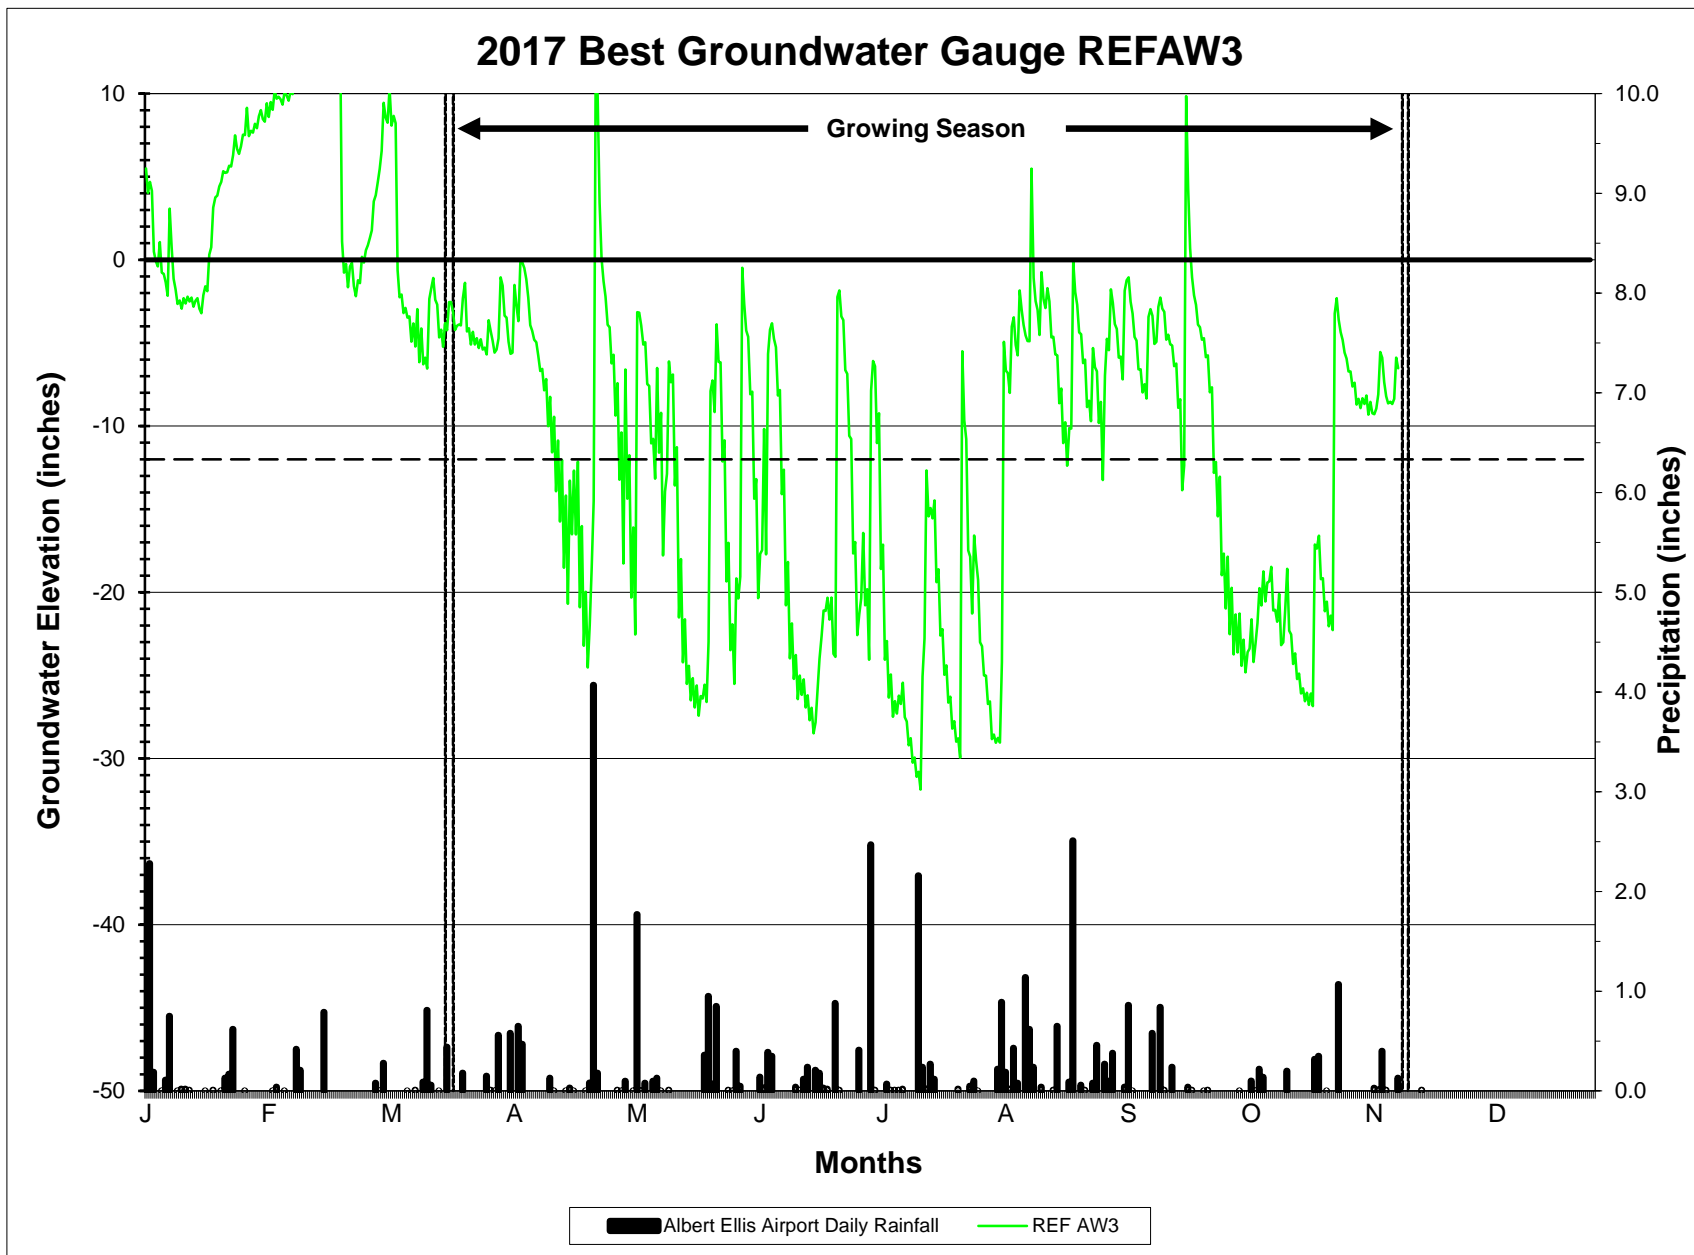

**Figure 8. Crest Gauge Verification Photos**



Crest Gauge 1 Reading 0.25' (9/21/2017)



Crest Gauge 2 Reading 1.19' (9/21/2017)



Crest Gauge 3 Reading 0.55' (8/13/2017)



Crest Gauge 4 Reading 0' (11/16/2017)



Crest Gauge 5 Reading 1.2' (8/13/2017)



Crest Gauge 6 Reading 2.15' (8/13/2017)

### MY3 2017 Best Crest Gauge ACG4

