

**BEST STREAM AND WETLAND RESTORATION PROJECT
MONITORING REPORT
MONITORING YEAR 6
FINAL**

DUPLIN COUNTY, NORTH CAROLINA
CONTRACT No. 004631 - PROJECT No. 95353
USACE Action ID No. 2012-01384 -NCDWR Project No. 13-0865



Prepared for:

Division of Mitigation Services
North Carolina Department of Environment and Natural Resources
1652 Mail Service Center
Raleigh, NC 27699-1652

January 2021

**Best
Duplin County, North Carolina
DMS Project ID 95353**

**Cape Fear River Basin
HUC 03030007060010**

Prepared by:



**Resource Environmental Solutions, LLC
3600 Glenwood Ave, Suite 100
Raleigh, NC 27612
919-209-1061**



3600 Glenwood Avenue, Suite 100
Raleigh, NC 27612

Corporate Headquarters
6575 W Loop S #300
Bellaire, TX 77401
Main: 713.520.5400

February 8, 2021

Jeremiah Dow
NC DEQ Division of Mitigation Services
217 West Jones Street
Raleigh, NC 27604

RE: Best Stream and Wetland Restoration Site: MY6 Monitoring Report (NCDMS ID 95353)

Listed below are comments provided by DMS on December 14, 2020 regarding the Best Stream and Wetland Restoration Site: Year 6 Monitoring Report and RES' responses.

1. Section 5.1.5: a. When discussing AW7 and possible loss of wetland credit, please edit language to say that the credit loss area could be up to 0.39 acres and that RES will perform a wetland delineation and investigation of soil development (since the area may delineate as a jurisdictional wetland) to further refine the exact extent of the area that may potentially be removed from credit if the gauge fails to meet success criteria in MY7.

[Done.](#)

2. Appendix B

a. Please show a polygon on the CCPV for the 0.39 acres of wetland credit at risk.

[Done.](#)

b. Please show gauge ACG4 on the CCPV.

[The symbol for ACG4 was hidden behind the XS26 label. This error has been corrected.](#)

c. Table 5 should reflect the piping identified on UT4 and UT6.

[The piping structures were repaired in October 2020 and are functioning properly, therefore RES does not feel it is appropriate to add them to Table 5.](#)



3. Electronic Files a. DMS identified features that did not match reported asset lengths or areas in MY5. Mitigation plan shapefiles were submitted, but these shapefiles did not address all of the discrepancies. The remaining discrepancies are detailed below, reported as feature length vs. Table 1 reported length. If possible, please submit features that accurately represent these creditable lengths/areas.

[The correct Mitigation Plan shapefile has been provided to DMS via email.](#)

TABLE OF CONTENTS

1	PROJECT GOALS, BACKGROUND AND ATTRIBUTES.....	3
1.1	Location and Setting.....	3
1.2	Project Goals and Objectives.....	3
1.3	Project Structure.....	5
1.3.1	Restoration Type and Approach.....	5
1.4	Project History, Contacts and Attribute Data.....	11
1.4.1	Project History.....	11
1.4.2	Project Watersheds.....	11
2	Success Criteria.....	11
2.1	Stream Restoration.....	11
2.1.1	Bankfull Events.....	11
2.1.2	Cross Sections.....	12
2.1.3	Bank Pin Arrays.....	12
2.1.4	Digital Image Stations.....	12
2.2	Wetland Restoration.....	12
2.3	Vegetation Success Criteria.....	13
2.4	Scheduling/Reporting.....	13
3	MONITORING PLAN.....	13
3.1	Stream Restoration.....	13
3.1.1	As-Built Survey.....	13
3.1.2	Bankfull Events.....	13
3.1.3	Cross Sections.....	14
3.1.4	Digital Image Stations.....	14
3.1.5	Bank Pin Arrays.....	14
3.1.6	Visual Assessment Monitoring.....	14
3.1.7	Surface Flow.....	14
3.2	Wetland Hydrology.....	15
3.3	Vegetation.....	15
4	Maintenance and Contingency plan.....	15
4.1	Stream.....	15
4.2	Wetlands.....	15
4.3	Vegetation.....	15
5	Year 6 Monitoring Conditions (MY6).....	16
5.1	Year 6 Monitoring Data Collection.....	16
5.1.1	Morphological State of the Channel (MY5).....	16
5.1.2	Vegetation.....	16
5.1.3	Photo Documentation.....	17
5.1.4	Stream Hydrology.....	17
5.1.5	Wetland Hydrology.....	17
6	REFERENCES.....	18

Appendices

Appendix A. General Tables and Figures

- Table 1. Project Components and Mitigation Credits
- Table 2. Project Activity and Reporting History
- Table 3. Project Contacts
- Table 4. Project Information Summary
- Figure 1. Project Vicinity Map
- Figure 2. Project USGS Map

Appendix B. Visual Assessment Data

- Figure 3a,3b,3c. Current Conditions Plan View Map (CCPV)
- Table 5. Visual Stream Morphology Stability Assessment
- Table 6. Vegetation Condition Assessment
- Table 7. Stream Problem Areas
- Table 8. Vegetation Problem Areas
- Figure 4. Vegetation Plot Photos
- Figure 5. Stream Problem Photos
- Figure 6. Vegetation Problem Photos

Appendix C. Vegetation Plot Data

- Table 9a. Vegetation Plot Criteria Attainment Summary
- Table 9b. Planted and Total Stem Counts (Species by Plot)

Appendix D. Stream Geomorphology Data (MY5 2019)

- Table 10. Morphological Parameters Summary Data
- Table 11. Dimensional Morphology Summary – Cross Sections Data
- Table 12. Bank Pin Array Summary Data
- Figure 7. Cross Section Plots

Appendix E. Hydrology Data

- Table 13. Documentation of Geomorphologically Significant Flow Events
- Table 14. Rainfall Summary
- Table 15a. Wetland Hydrology Criteria Attainment
- Table 15b. Wetland Hydrology Summary
- 2020 Groundwater Monitoring Gauge Hydrographs
- Figure 8. Crest Gauge Verification Photos
- Figure 9. Headwater Valley Restoration Flow Chart

1 PROJECT GOALS, BACKGROUND AND ATTRIBUTES

1.1 Location and Setting

The Best Stream and Wetland Site is located in Duplin County approximately two miles east of Beulaville, NC (**Figure 1**). To access the downstream end of the site from the town of Beulaville, travel 0.6 miles east on NC HWY 24, take a right onto Lyman Road (SR 1801), and continue 1.6 miles southeast to the crossing with Muddy Creek. Reaches UT7, UT8, UT9, UT10 and the lower end of Muddy Creek may all be accessed from Lyman Road. Reaches UT5 and UT6 are located just south of NC HWY 24, approximately 1.9 miles east of Beulaville. The upstream portion of the site may be accessed from two locations. Reaches UT1, UT2 and Muddy Creek are located to the south of NC HWY 24, opposite of the intersection of NC HWY 24 and Penny Road (SR 1720), approximately 2.8 miles east of Beulaville. To access reaches UT3, UT4 and Muddy Creek, travel 3.2 miles east on NC HWY 24 from Beulaville to Edwards Road (SR 1835), continue south for approximately 1.0 mile, turn right onto Put Lane, and follow the road down to Reaches UT3 and UT4.

1.2 Project Goals and Objectives

The Best stream and wetland mitigation project will provide numerous ecological and water quality benefits within the Cape Fear River Basin. While many of these benefits are limited to the project area, others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Expected improvements to water quality, hydrology, and habitat are outlined below.

Design Goals and Objectives

Benefits Related to Water Quality	
Nutrient removal	Benefit will be achieved through filtering of runoff from adjacent CAFOs through buffer areas, the conversion of active farm fields to forested buffers, improved denitrification and nutrient uptake through buffer zones, and installation of BMPs at the headwaters of selected reaches and ditch outlets.
Sediment removal	Benefit will be achieved through the stabilization of eroding stream banks and reduction of sediment loss from field areas due to lack of vegetative cover. Channel velocities will also be decreased through a reduction in slope, therefore decreasing erosive forces.
Increase dissolved oxygen concentration	Benefit will be achieved through the construction of instream structures to increase turbulence and dissolved oxygen concentrations and lower water temperature to increase dissolved oxygen capacity.
Runoff filtration	Benefit will be achieved through the restoration of buffer areas that will receive and filter runoff, thereby reducing nutrients and sediment concentrations reaching water bodies downstream.
Benefits to Flood Attenuation	
Water storage	Benefit will be achieved through the restoration of buffer areas which will infiltrate more water during precipitation events than under current site conditions.
Improved groundwater recharge	Benefit will be achieved through the increased storage of precipitation in buffer areas, ephemeral depressions, and reconnection of existing floodplain. Greater storage of water will lead to improved infiltration and groundwater recharge.
Improved/restored hydrologic connections	Benefit will be achieved by restoring the stream to a natural meandering pattern with an appropriately sized channel, such that the channel's floodplain will be flooded more frequently at flows greater than the bankfull stage.
Benefits Related to Ecological Processes	
Restoration of habitats	Benefit will be achieved by restoring riparian buffer habitat to appropriate bottomland hardwood ecosystem.

Improved substrate and instream cover	Benefit will be achieved through the construction of instream structures designed to improve bedform diversity and to trap detritus. Substrate will become coarser as a result of the stabilization of stream banks and an overall decrease in the amount of fine materials deposited in the stream.
Addition of large woody debris	Benefit will be achieved through the addition of wood structures as part of the restoration design. Such structures may include log vanes, root wads, and log weirs.
Reduced temperature of water due to shading	Benefit will be achieved through the restoration of canopy tree species to the stream buffer areas.
Restoration of terrestrial habitat	Benefit will be achieved through the restoration of riparian buffer bottomland hardwood habitats.

The North Carolina Division of Mitigation Services (NCDMS) develops River Basin Restoration Priorities (RBRP) to guide its restoration activities within each of the state’s 54 cataloging units. RBRPs delineate specific watersheds that exhibit both the need and opportunity for wetland, stream and riparian buffer restoration. These TLWs receive priority for DMS planning and restoration project funds. Currently, no Local Watershed Plan (LWP) is available for the project area.

The 2009 Cape Fear River Basin River Basin Restoration Priorities (RPRP) identified HUC 03030007060010 as a Targeted Local Watershed (TLW). The watershed is characterized by 52 percent agricultural land use area with Muddy Creek identified as Impaired for aquatic life because of a Fair benthic community rating. The Best Stream and Wetland Restoration Project was identified as a stream and wetland opportunity to improve water quality, habitat, and hydrology within the TLW.

The project goals address stressors identified in the TLW and include the following:

- Nutrient removal,
- Sediment removal,
- Reducing runoff from animal operations,
- Filtration of runoff, and
- Improved aquatic and terrestrial habitat.

The project goals will be addressed through the following project objectives:

- Establishing riparian buffer areas adjacent to CAFOs,
- Converting active farm field to forested buffers,
- Stabilization of eroding stream banks,
- Improving and protecting portions of headwater systems that discharge to a 303d listed stream,
- Reduction in stream bank slope,
- Restoration of riparian buffer bottomland hardwood habitats, and
- Construction of in-stream structures designed to improve bedform diversity and trap detritus.

The Best stream and wetland mitigation project is located within the northern (upstream) portion of the TLW and includes sections of Muddy Creek (303d listed) and headwater streams that discharge into Muddy Creek. Due to its location and improvements, the project provides numerous ecological and water quality benefits within the Cape Fear River Basin. While many of these benefits are limited to the project area, others, such as pollutant removal and improved aquatic and terrestrial habitat, have more far-reaching effects. Many of the project design goals and objectives, including restoration of riparian buffers to filter runoff from agricultural operations and improve terrestrial habitat, and construction of in-stream structures to improve habitat diversity, addresses the degraded water quality and nutrient input from farming that were identified as major watershed stressors in the 2009 Cape Fear RBRP.

1.3 Project Structure

Following 2016 monitoring the NCIRT requested a review of the differential between the Approved Mitigation Plan and Baseline Monitoring Report. RES does not plan on submitting an asset revision and will revert to the Approved Mitigation Plan assets. The assets under the “Proposed SMUs” and “Proposed WMUs” are the Approved Mitigation Plan assets.

Reach	Mitigation Type*	Proposed Length (LF)	Mitigation Ratio	Proposed SMUs	Baseline SMUs
UT1	P1 Restoration	1,723	1:1	1,723	1,757
UT1	SP & BE	303	1:5	61	56
UT2	P1 Restoration	2,770	1:1	2,770	2,772
UT2	SP & BE	309	1:5	62	66
UT3	Enhancement II	812	1:2.5	325	325
UT3	SP & BE	64	1:5	13	13
UT4	HV Restoration	510	1:1	510	494
UT4	SP & BE	655	1:5	131	129
UT5	SP & BE	4,043	1:5	809	809
UT6	Enhancement I	538	1:1.5	359	359
UT7	SP & BE	3,183	1:5	637	637
UT8	Enhancement I	825	1:1.5	550	510
UT8	SP & BE	313	1:5	63	63
UT9	SP & BE	1,171	1:5	234	221
UT10	SP & BE	768	1:5	154	154
Muddy Creek	SP & BE	9,073	1:5	1,815	1,815
Total		27,060		10,213	10,178

*P1=Priority 1, SP & BE= Stream Preservation and Buffer Enhancement, HV= Headwater Valley

**The contracted amount of credits for this Site is 10,133 SMUs

Wetland	Mitigation Type	Mitigation Area (ac)	Mitigation Ratio	Proposed WMUs	Baseline WMUs
W1	Restoration	3.66	1:1	3.66	3.77
W2	Restoration	0.29	1:1	0.29	0.31
W3A	Restoration	0.58	1:1	0.58	0.58
W3B	Restoration	0.59	1:1	0.59	0.59
Total		5.12		5.12	5.25

*The contracted amount of credits for this Site is 4.40 WMUs

1.3.1 Restoration Type and Approach

UT1

Priority Level 1 restoration was completed for UT1 to address all existing impairments, particularly the greatly oversized channel and lack of bedform diversity. The design approach included meandering the channel within the natural valley and backfilling the existing stream. A minimum 50 foot buffer was established and planted with native riparian vegetation. Because the pre-existing buffer was devoid of significant woody vegetation, woody debris was installed along the bed to

improve in-stream habitat. Livestock was excluded with fencing installed along the easement boundary. An existing CMP culvert located along the middle of the reach was removed and replaced downstream at station 13+75 to allow the landowner access to both sides of the property. Stream Preservation and Buffer Enhancement was completed for the downstream section of the channel where it flows through a forested buffer down to the confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT2

Similar to UT1, Priority 1 restoration was completed for UT2 to address historic straightening and channel enlargement. The existing channel was backfilled, and the restored channel was relocated such that it meanders within the existing valley. A diffuse flow structure was installed at the ditch adjacent to the proposed crossing. The structure was placed such that flows from the existing ditch will be attenuated to establish sheet flow as the water enters the restored channel. All areas within the minimum 50 foot buffer were planted with native riparian vegetation. An existing 60" CMP culvert located at station 20+25 of the reach was removed and replaced with a 48" HDPE culvert to allow the landowner access to the entire property. Additionally, the existing culvert at the upstream end of UT2 was upgraded to a 48" HDPE culvert and reset to more effectively transition the existing channel upstream into the project stream. Priority Level I restoration was appropriate for this channel because it was the only mitigation approach that would address bed and bank instability, establish a forested riparian buffer, and significantly enhance aquatic habitat. Stream Preservation and Buffer Enhancement was completed for the most downstream section, where the channel enters the existing forested buffer, down to its confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT3

Enhancement Level II was completed on Reach UT3 due to the channel's stability and appropriate size. The design approach on this reach focused on improving the riparian buffer. The existing hog lagoon located within buffer on the west side of the reach has remained in place, preventing the generation of stream credits for approximately 600 linear feet. Through this section, the left buffer was extended out to a minimum of 75 feet along the left bank, and the right buffer was extended just past top of bank. The existing crossing located at station 8+50 was replaced and upgraded with a 30" HDPE pipe, allowing the landowner continued access across his property. Additional bank grading

and stabilization was included in the culvert replacement. The grading of pools and the installation of woody debris structures was performed along the reach to improve aquatic habitat. Upstream of the crossing, a 75-foot buffer was restored along the east bank where the channel currently flowed through an active pasture. A 100-foot buffer was implemented for the headwater origin point to further protect water quality from cattle access. Cattle have been excluded with fencing. All areas within the buffer were planted with native riparian vegetation. Stream Preservation and Buffer Enhancement was implemented along the downstream end where the channel enters the Muddy Creek floodplain. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT4

Headwater valley restoration was completed for the upper section of UT4. The existing channel was backfilled, and flow was directed from its current position east back to the historic valley location. A minor amount of earthwork was completed in the headwater valley restoration apart from ditch plugging to tie the existing ditch back to the natural valley. Areas within the 100 foot buffer that were disturbed or lacked riparian vegetation were planted. Cattle were excluded from the buffer through the installation of fencing. An existing 15" CPP culvert crossing located at station 8+50 of the reach was removed and replaced with triple 18" HDPE culverts. This crossing was relocated to the low spot in the valley to allow the landowner continued access to an agricultural field west of the channel. Downstream of the crossing, a smaller low flow channel was constructed within the natural valley. This segment now connects the upstream headwater valley section to the existing channel approximately 230 feet below the crossing. Due to the stable nature of the buffer along the downstream reach of UT4, Stream Preservation and Buffer Enhancement was implemented from just downstream of the crossing to the confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT5

Stream Preservation and Buffer Enhancement was completed on UT5. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional

treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT6

Enhancement Level I was completed on UT6. The mitigation approach on this reach focused on bank stabilization, bedform diversity, and improving the riparian buffer. The existing channel was impaired by channelization, vertical un-vegetated banks, and a dense privet understory within the buffer. The grading of pools, grade control structures, and the installation of woody debris structures were implemented along the reach to improve aquatic habitat. All disturbed areas within the riparian buffer were planted with native riparian vegetation.

UT7

Stream Preservation and Buffer Enhancement was completed on UT7. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT8

Enhancement Level I was completed on UT8. The mitigation approach on this reach focused on bank stabilization, bedform diversity, and riparian buffer restoration. The existing channel was impaired by channelization, localized bank instability, and cleared agricultural land in the buffer. Stabilization activities included grading a floodplain bench, installing grade control structures, and installing woody debris structures to improve hydraulic efficiency and aquatic habitat. All disturbed areas within the riparian buffer were planted with native riparian vegetation. Stream Preservation and Buffer Enhancement was completed on 313 linear feet where the channel enters the existing forested buffer, down to its confluence with Muddy Creek. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT9

Stream Preservation and Buffer Enhancement was completed on UT9. The stream is channelized, but stable throughout the easement. The active channel is meandering within the larger excavated channel bottom. The riparian buffer is intact hardwood forest with localized areas of privet. The easement boundary extends a minimum of 50 feet outward from the stream channel, or to the limit of adjacent riparian wetlands, whichever is wider. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

UT10

Stream Preservation and Buffer Enhancement was completed on UT10. The channel is stable throughout the easement and provides a variety of aquatic habitats. The easement boundary extends a minimum of 50 feet outward from the stream channel, or the limit of adjacent riparian wetlands, whichever is wider. The riparian buffer is an intact hardwood forest with localized areas of privet. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

Muddy Creek

Stream Preservation and Buffer Enhancement was completed for the majority of Muddy Creek. The buffer was restored and increased to a width of 75 feet along the south side. Buffer enhancement activities included the treatment of invasive exotic species by herbicide applications and/or mechanical control as well as planting bare root seedlings in sparsely vegetated areas. RES will continue to conduct invasive species treatments on an as needed basis. Additional treatments will be dependent on monitoring results and regulatory agency guidance. These treatments will be timed in accordance with specific invasive exotic plant phenology for the most effective control. Considering such factors as the influence of established invasive exotics on adjacent land, it is not feasible to expect complete eradication of the targeted invasive species. However, RES does expect to achieve significant reduction of targeted invasive exotic species through this control plan. The goal of the treatment program is control of invasive exotic species such that the target natural communities are present and on a positive trajectory at project closeout.

Wetland W1

Wetland W1 is located at the headwater of UT1 and has a natural constriction at the outlet. The soil is a sandy loam/loamy sandy underlain by clayey textured subsoil that forms an effective restrictive

layer to groundwater loss. This area receives runoff from NC HWY 24. Based upon soil and landscape position, it is likely this area has a seasonal seepage along the upper boundary.

Site modifications included removal of dredged and excavated materials, plugging the ditch, and raising the streambed elevation to bring the water table closer to the ground surface. Additional temporal habitat was constructed to eliminate surface leveling and smoothing for agricultural use. The temporal habitat is variable to mimic sloughs, oxbows, root-tips and other shallow natural features. During monitoring, beaver activity will be controlled to allow the site to stabilize and vegetative community to establish. After the monitoring period, the site is designed to promote and tolerate beaver activity. No hydrologic trespass is anticipated due to beaver activity in this wetland. These modifications will increase storage and eliminate the rapid loss of surface water. This area may receive limited overbank flows due to location in the headwater of UT1. Subsoil ripping and roughing of the soil surface were performed to ameliorate soil compaction and create an uneven surface more conducive for surface water retention, infiltration, and increase storage that would be present in natural wetland systems.

Wetland W2

Wetland W2 is located at the toe slope along Muddy Creek and UT2. The soil is a sandy loam/loamy sandy underlain by sandy clay loam and sandy clay. This site is at a low elevation and is influenced by the water table on the floodplain of Muddy Creek. It is unlikely that groundwater loss is significant during most of the year. This area has a small watershed, but flooding from UT2 and Muddy Creek will increase hydrologic storage.

Hydrology was restored by removing dredge material along the channel and raising the streambed elevation, bringing the water table closer to the ground surface. Site modifications included subsoil ripping, crown removal, and surface roughing of the area. Additional temporal habitat was constructed to eliminate the surface leveling and smoothing for agricultural use. The temporal habitat is variable to mimic sloughs, root-tips and other shallow natural features. This ameliorates past soil leveling and compaction and creates an uneven surface more conducive of infiltration and storage that would be present in natural wetland systems.

Wetland W3

Wetland W3 is composed of two similar area (W3a and W3b) located at the toe slope along Muddy Creek. A low finger of soil separates them. The soil in these areas is a loamy sand/sandy loam. The surrounding upland is underlain by clayey subsoil that forms an effective restrictive layer that lateral flow rides provide additional hydrological input. A ditch is located upslope of these areas and alongside W3a that drains to Muddy Creek.

The soil is a sandy loam/loamy sand. The surrounding upland has a sandy clay loam and sandy clay that form an effective restrictive layer that lateral flow rides provide additional hydrological input. Both areas have small watersheds, but W3b receives groundwater seepage along the toe of slope diverted by the upslope ditch.

Hydrology was restored by filling ditches and enhancing the concave topography by removing soil material where cultivation had filled low features and leveled the surface to facilitate cultivation. Additional groundwater seepage diverted by the ditch was restored to these wetlands. Temporal habitat was constructed to eliminate the surface leveling and smoothing for agricultural use. Subsoil ripping and surface roughing of the area was performed to ameliorate soil compaction and create an uneven surface more conducive of infiltration and storage that would be present in natural wetland systems.

1.4 Project History, Contacts and Attribute Data

1.4.1 Project History

The Best Stream and Wetland Restoration Site was restored by Resource Environmental Solutions, LLC (RES) through a full-delivery contract awarded by NCDMS in 2012. **Tables 2, 3, and 4 in Appendix A** provide a time sequence and information pertaining to the project activities, history, contacts, and baseline information.

1.4.2 Project Watersheds

The easement totals 142.7 acres and the project streams include ten unnamed tributaries to Muddy Creek and a portion of Muddy Creek extending from approximately 0.3 miles west of Edwards Road to 0.4 miles past Lyman Road. The total drainage area at the downstream limits of the project is 2,928 acres (4.58 mi²). The land use in the project watershed is approximately 47 percent cultivated cropland, 21 percent evergreen and deciduous forest, 13 percent shrub/scrub, ten percent bottomland forest/hardwood swamp, three percent developed, and six percent managed herbaceous cover and pasture.

UT1 has a drainage area of 0.06 square miles (41 acres), and flows in a southerly direction to the confluence with Muddy Creek. UT2 flows south to its confluence with Muddy Creek and has a drainage area of 0.23 square miles (146 acres). UT3 is located to the south of Muddy Creek, opposite of UT2, and flows to the north and into Muddy Creek. This reach has a drainage area of 0.09 square miles (56 acres). UT4 is located to the west of UT3 and discharges to Muddy Creek. This reach has a drainage area of 0.13 square miles (82 acres). UT5 flows in a southerly direction from NC HWY 24 to Muddy Creek and has a drainage area of 0.59 square miles (380 acres). UT6 flows southeast to its confluence with UT5 and has a drainage area of 0.12 square miles (79 acres). UT7 flows in a southerly direction east of Lyman Road down to its confluence with UT5 before discharging to Muddy Creek. UT7 has a drainage area of 0.60 square miles (387 acres). UT8 has a drainage area of 0.09 square miles (56 acres), and flows in an easterly direction through a cultivated field east of Lyman Road down to the confluence with UT7. UT9 flows southeast to its confluence with Muddy Creek and has a drainage area of 0.06 square miles (36 acres). UT10 is the downstream-most tributary within the Best Site and flows in a westerly direction from a farm crossing west of Lyman Road down to Muddy Creek. UT10 has a drainage area of 0.48 square miles (306 acres). Muddy Creek is a stable swamp stream system with intact hardwood forest floodplain, extending from approximately 0.3 miles west of Edwards Road to 0.5 miles south of Lyman Road. Muddy Creek has a drainage area of 4.6 square miles (2,930 acres) at the downstream limits and has an existing length of 9,214 linear feet.

2 Success Criteria

The success criteria for the Best Site will follow accepted and approved success criteria presented in the USACE Stream Mitigation Guidelines and subsequent NCDMS and agency guidance. Specific success criteria components are presented below.

2.1 Stream Restoration

2.1.1 Bankfull Events

Two bankfull flow events must be documented within the seven-year monitoring period. The two bankfull events must occur in separate years. Otherwise, the stream monitoring will continue until

two bankfull events have been documented in separate years. Bankfull events will be documented using crest gauges, auto-logging crest gauges, photographs, and visual assessments for evidence of debris rack lines.

2.1.2 Cross Sections

There should be little change in as-built cross-sections. If changes do take place, they should be evaluated to determine if they represent a movement toward a less stable condition (for example down-cutting or erosion), or are minor changes that represent an increase in stability (for example settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). Starting in MY3, BHR was calculated on riffles using the baseline bankfull elevation. This method was used because the dimension of the channels has not changed enough to alter the bankfull elevation. Starting in MY5, BHR was calculated according to the Industry Technical Workgroup memorandum. None of the restoration riffle cross sections exceeded a 1.2 BHR. Two cross sections on Enhancement I reaches did exceed 1.2 but both have baseline bankfull elevations below top of bank. Cross-sections are classified using the Rosgen stream classification method, and all monitored cross-sections should fall within the quantitative parameters defined for channels of the design stream type.

2.1.3 Bank Pin Arrays

Bank pin arrays will be used as a supplemental method to monitor erosion on selected meander bends where there is not a cross section. Bank pin arrays will be installed along the outer bend of the meander. Bank pins will be installed just above the water surface and every two feet above the lowest pin. Bank pin exposure will be recorded at each monitoring event, and the exposed pin will be driven flush with the bank, there should be little change in as-built cross-sections. If changes do take place, they should be evaluated to determine if they represent a movement toward a less stable condition (for example down-cutting or erosion), or are minor changes that represent an increase in stability (for example settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). Cross-sections shall be classified using the Rosgen stream classification method, and all monitored cross-sections should fall within the quantitative parameters defined for channels of the design stream type.

2.1.4 Digital Image Stations

Digital images are used to subjectively evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, and effectiveness of erosion control measures. Longitudinal images should not indicate the absence of developing bars within the channel or an excessive increase in channel depth. Lateral images should not indicate excessive erosion or continuing degradation of the banks over time. A series of images over time should indicate successional maturation of riparian vegetation.

2.2 Wetland Restoration

Success criteria and monitoring for wetland hydrology within the wetland restoration areas on the site follows NCDMS Guidance dated 7 November 2011. The target minimum wetland hydroperiod is 9 percent of the growing season. Stream hydrology and water balance calculations indicate the wetland area will meet jurisdictional criteria (5 percent hydroperiod). However, due to immature vegetation and reduced PET, a longer success criterion is appropriate. Auto recording gauges are used to measure daily groundwater elevations throughout the Sampson County growing season in all 7 years of monitoring.

If a hydrology gauge location fails to meet these success criteria in the seven-year monitoring period then monitoring may be extended, remedial actions may be undertaken, or groundwater modeling

may be used to demonstrate the limits of wetland restoration.

2.3 Vegetation Success Criteria

Specific and measurable success criteria for plant density within the wetland restoration and riparian buffers on the site will follow NCDMS Guidance dated 7 November 2011. Vegetation monitoring plots are a minimum of 0.02 acres in size, and cover a minimum of two percent of the planted area. The following data is recorded for all trees in the plots: species, height, planting date (or volunteer), and grid location. Monitoring occurs in the fall of Years 1, 2, 3, 5, and 7. The interim measures of vegetative success for the site is the survival of at least 320 three-year old planted trees per acre at the end of Year 3, and 260 planted trees per acre at the end of Year 5. The final vegetative success criteria is the survival of 210 planted trees per acre at the end of Year 7 of the monitoring period.

Invasive and noxious species will be monitored and controlled so that none become dominant or alter the desired community structure of the site. If necessary, RES will develop a species-specific control plan.

2.4 Scheduling/Reporting

The monitoring program will be implemented to document system development and progress toward achieving the success criteria. The restored stream morphology is assessed to determine the success of the mitigation. The monitoring program will be undertaken for seven years or until the final success criteria are achieved, whichever is longer.

Monitoring reports will be prepared in the fall of each year of monitoring and submitted to NCDMS. The monitoring reports will include all information, and be in the format required by NCDMS in Version 2.0 of the NCDMS Monitoring Report Template (Oct. 2010).

3 MONITORING PLAN

Annual monitoring data will be reported using the DMS monitoring template. Annual monitoring shall be conducted for stream, wetland, and vegetation monitoring parameters as noted below.

3.1 Stream Restoration

3.1.1 As-Built Survey

An as-built survey was conducted following construction to document channel size, condition, and location. The survey includes a complete profile of thalweg, water surface, bankfull, and top of bank to compare with future geomorphic data. Longitudinal profiles will not be required in annual monitoring reports unless requested by NCDMS or USACE.

3.1.2 Bankfull Events

Six sets of manual and auto-logging crest gauges were installed on the site, one along UT1, UT2, UT3, UT4, UT6, and one along UT8. The auto logging crest gauges were installed within the channel and will continuously record flow conditions at an hourly interval. Manual crest gauges were installed on the bank at bankfull elevation. Crest gauges will be checked during each site visit to determine if a bankfull event has occurred since the last site visit. Crest gauge readings and debris rack lines will be photographed to document evidence of bankfull events. Flow days will be reported on headwater valley restoration reaches.

3.1.3 Cross Sections

A total of 31 permanent cross sections were installed to monitor channel dimensions and stability. Twelve cross sections were installed along UT1 where Priority 1 restoration was performed. Twelve cross sections (six pools and six shallows) were installed along UT2 also. UT4 has a total of two cross sections installed throughout its length. Stream segment UT6 has two cross sections installed along its length where enhancement activities were performed. On the UT8 side of the project, a total of three cross sections were installed. Cross sections were typically located at representative riffle and pool sections along each stream reach. Each cross section was permanently marked with 3/8 rebar pin to establish a monument location at each end. A marker pole was also installed at both ends of each cross section to allow ease locating during monitoring activities. Cross section surveys will be performed once a year during annual monitoring years 1, 2, 3, 5, and 7 and will include all breaks in slope including top of bank, bottom of bank, streambed, edge of water, and thalweg.

3.1.4 Digital Image Stations

Digital photographs will be taken at least once a year to visually document stream and vegetation conditions. This monitoring practice will continue for seven years following construction and planting. Permanent photo point locations at cross sections and vegetation plots have been established so that the same directional view and location may be repeated each monitoring year. Monitoring photographs will also be used to document any stream and vegetation problematic areas such as erosion, stream and bank instability, easement encroachment and vegetation damage.

3.1.5 Bank Pin Arrays

Eight bank pin array sets have been installed at pool cross sections located along UT1 and UT2. These bank pin arrays were installed along the upstream and downstream third of the meander. Bank pins are a minimum of three feet long, and have been installed just above the water surface and every two feet above the lowest pin. Bank pin exposure will be recorded at each monitoring event, and the exposed pin will be driven flush with the bank.

3.1.6 Visual Assessment Monitoring

Visual monitoring of all mitigation areas is conducted a minimum of twice per monitoring year by qualified individuals. The visual assessments include vegetation density, vigor, invasive species, and easement encroachments. Visual assessments of stream stability include a complete stream walk and structure inspection. Digital images are taken at fixed representative locations to record each monitoring event as well as any noted problem areas or areas of concern. Results of visual monitoring are presented in a plan view exhibit with a brief description of problem areas and digital images. Photographs will be used to subjectively evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, and effectiveness of erosion control measures. Longitudinal photos should indicate the absence of developing bars within the channel or an excessive increase in channel depth. Lateral photos should not indicate excessive erosion or continuing degradation of the banks over time. A series of photos over time should indicate successional maturation of riparian vegetation.

3.1.7 Surface Flow

The headwater valley restoration area on UT4 will be monitored to document intermittent or seasonal surface flow. This will be accomplished through direct observation, photo documentation of dye tests, and continuous flow monitoring devices (pressure transducers). An auto logging crest gauge has been installed within the headwater valley channel and will continuously record flow conditions at an hourly interval. This gauge will be downloaded during each site visit to determine if intermittent or seasonal flows conditions are present.

3.2 Wetland Hydrology

Wetland hydrology will be monitored to document hydric conditions in the wetland restoration areas. This will be accomplished with automatic recording pressure transducer gauges installed in representative locations across the restoration areas and reference wetland areas. A total of twelve automatic recording pressure transducers (Auto-Wells) have been installed on the site. Nine auto-wells have been installed within the wetland restoration area and three within reference areas. The gauges will be downloaded quarterly and wetland hydroperiods will be calculated during the growing season. Gauge installation followed current regulatory and DMS guidance. Visual observations of primary and secondary wetland hydrology indicators will also be recorded during quarterly site visits.

3.3 Vegetation

A total of 23 vegetation plots were randomly established within the planted stream riparian buffer easement. Vegetation plots measure 10 meters by 10 meters or 5 meters by 20 meters (0.02 acres) and have all four corners marked with metal posts. Planted woody vegetation was assessed within each plot to establish a baseline dataset. Within each vegetation plot, each planted stem was identified for species, “X” and “Y” origin located, and measured for height. Reference digital photographs were also captured to document baseline conditions. Species composition, density, growth patterns, damaged stems, and survival ratios will be measured and reported on an annual basis. Vegetation plot data will be reported for each plot as well as an overall site average.

4 MAINTENANCE AND CONTINGENCY PLAN

All identified problematic areas or areas of concern such as stream bank erosion/instability, aggradation/degradation, lack of targeted vegetation, and invasive/exotic species which prevent the site from meeting performance success criteria will be evaluated on a case by case basis. These areas will be documented and remedial actions will be discussed amongst NCDMS staff to determine a plan of action. If it is determined remedial action is required, a plan will be provided.

4.1 Stream

Two minor stream problem areas were found and repaired in October 2020. The first was a piping log sill on UT4 and the second was a piping log sill on UT6. These areas are called out on **Figure 3** and photos are in **Table 8**.

4.2 Wetlands

One wetland problem area was noted during the Year 5 monitoring period. AW7 did not meet success for the fourth time in six years, however this year it fell only one percent short. This area, about 0.39 acres, has been considered as at-risk credits. If this well does not meet success again in MY7, RES will perform a wetland delineation and soil development investigation to refine and remove the unsuccessful area from crediting.

4.3 Vegetation

One vegetation problem was identified during the Year 6 monitoring period. This vegetation problem area is documented (**Table 6** and **Table 8**) and mapped on the CCPV (**Figure 3**) as part of the annual monitoring report. This area consists of a low stem density area (0.28 acres) in and around Vegetation Plot 18. The problem area is described in Section 5.1.2 and will be replanted this dormant season. RES treated a number of invasive species areas in September and October 2020. The main areas were at the top of UT1 and along UT6.

5 YEAR 6 MONITORING CONDITIONS (MY6)

The Best Site Year 6 Monitoring activities were completed in October 2020. All Year 6 monitoring data is present below and in the appendices.

5.1 Year 6 Monitoring Data Collection

5.1.1 Morphological State of the Channel (MY5)

Per the Approved Mitigation Plan, cross section data was not collected in MY6. Data from MY5, however, is discussed below and included in the appendices for reference. All morphological stream data for the MY5 dimensions were collected during the annual monitoring survey performed during July 2019. **Appendix D** includes summary data tables, morphological parameters, and stream photographs.

Profile

The baseline (MY-0) profiles closely matched the proposed design profiles. The plotted longitudinal profiles can be found on the As-Built Drawings. Longitudinal profiles will not be performed in annual monitoring reports unless requested by NCDMS or USACE. Morphological summary data tables can be found in **Table 10**.

Dimension

The Year 5 (MY5) cross sectional dimensions closely match the baseline and MY3 cross section parameters. Minimal changes were noted during Year 5 cross section surveys resulting from stable bed and bank conditions. Cross Section 26 shows a slight shift in dimension from the previous years which was most likely caused by a middle channel bar that formed on the flow gauge directly upstream of this cross section. All cross-section plots and data tables can be found in **Table 11 and Figure 7**.

Sediment Transport

The Year 5 conditions show that shear stress and velocities have been reduced for all six restoration reaches. Pre-construction conditions documented all six reaches as sand bed channels and remain classified as sand bed channels post-construction. Visual assessments (**Table 5**) show the channels are transporting sediment as designed and will continue to be monitored for aggradation and degradation.

Bank Pin Arrays

Eight pool cross section locations with bank pin arrays were observed and measured for bank erosion located on the outside meander bends. If bank pin exposure was noticeable, it was measured, recorded, photographed, and then driven flush with the bank at each monitoring location. No bank pin array readings were recorded during the Year 5 monitoring season. Bank pin array data tables can be found in **Table 12**.

5.1.2 Vegetation

The Year 6 monitoring (MY6) vegetation survey was completed in October 2020 and resulted in an average of 734 planted stems per acre, well above the interim survival density of 210 stems per acre at the end of Year 7 monitoring. The average stems per vegetation plot was 18 planted stems. The minimum planted stem per acre was 81 and the maximum was 1,214. Vegetation Plot 18 fell below the interim success criteria. Vegetation Plot 18 showed signs of heavy browsing and is located in a forested area. RES plans to plant some shade tolerant container trees in this area this dormant season. Vegetation Plot 2 met success in MY6 after finding planted stems from previous years as they grew

taller than the blackberry. Volunteers were noted in a few vegetation plots on the site and were recorded within the CVS-EEP Data entry tool. The average planted stem height was 12.8 feet. Vegetation summary data tables can be found in **Table 9** and vegetation plot photos in **Figure 4**.

5.1.3 Photo Documentation

Permanent photo point locations have been established at cross sections, vegetation plots, stream crossings, and stream structures by RES staff. Any additional problem areas or areas of concern will also be documented with a digital photograph during monitoring activities. Stream digital photographs can be found in **Figure 5 and 7** and **Figures 4 and 6** for vegetation photos.

5.1.4 Stream Hydrology

Six sets of manual and auto-logging crest gauges were installed on the site, one along UT1, UT2, UT3, UT4, UT6, and one along UT8. The auto logging crest gauges were installed within the channel and continuously record flow conditions at an hourly interval. Three of five crest gauges recorded bankfull events during the Year 6 monitoring period (**Table 13; Figure 8**). The HOBOS in Crest Gauge 3 and 5 failed in MY6 and will be replaced in early MY7. All crest gauges with a bankfull standard have met the success criteria. Crest Gauge 4 is located on a headwater valley restoration reach and the success criteria is to document 30 days of continuous flow. In Year 6, this reach recorded 135 consecutive days of flow.

5.1.5 Wetland Hydrology

A total of 12 wetland hydrology gauges are installed at the Best Site, nine in areas of wetland restoration and three as reference gauges in existing on-site wetland. Seven of the nine wetland restoration gauges achieved the success criteria by remaining continuously within the 12 inches of the soil surface for at least nine percent of the growing season. Groundwater gauge data indicate the hydroperiods being responsive to rainfall events; however, AW7 did not meet the nine percent success criteria in MY6. This is the fourth time in six years (MY2, MY3, MY5, MY6) that this wetland hydrology gauge did not meet success. However, the hydroperiod was only one percent short of success this year. This area, about 0.39 acres, has been considered as at-risk credits. If this well does not meet success again in MY7, RES will perform a wetland delineation and soil development investigation to refine the area to be potentially removed from credit. The HOBOS in AW3 failed in MY6 therefore recorded no data. This HOBOS will be replaced before the MY7 growing season. Rainfall data reported by CRONOS station Williamsdale Field Lab indicated rainfall was below average during the months of January, March, June, July, and October. All three reference gauges met the nine percent success criteria. Wetland gauge and rainfall data is presented in **Appendix E**.

6 REFERENCES

Chow, Ven Te. 1959. Open-Channel Hydraulics, McGraw-Hill, New York.

Cowardin, L.M., V. Carter, F.C. Golet and E.T. LaRoe. 1979. Classification of Wetlands and DDMSwater Habitats of the United States. U.S. Fish and Wildlife Service, Office of Biological Services, FWS/OBS-79/31. U.S. Department of the Interior, Washington, DC.

Environmental Banc & Exchange (2013). The Best Stream and Wetland Restoration Project Final Mitigation Plan. North Carolina Ecosystems Enhancement Program, Raleigh, NC.

Horton, J. Wright Jr. and Victor A. Zullo. 1991. The Geology of the Carolinas, Carolina Geological Society Fiftieth Anniversary Volume. The University of Tennessee Press. Knoxville, TN.

Johnson PA. 2006. Assessing stream channel stability at bridges in physiographic regions. U.S. Department of Transportation. Federal Highway Administration. Report Number FHWA-HRT-05-072.

Lee, Michael T., R.K. Peet, S.S. Roberts, and T.R. Wentworth. 2008. CVS-EEP Protocol for Recording Vegetation, Version 4.2 (<http://cvs.bio.unc.edu/methods.htm>)

Natural Resources Conservation Service (NRCS). 2007. Stream Restoration Design Handbook (NEH 654), USDA

NCDENR. "Water Quality Stream Classifications for Streams in North Carolina." Water Quality Section. <http://h2o.enr.state.nc.us/wqhome/html> (June 2005).

Radford, A.E., H.E. Ahles and F.R. Bell. 1968. Manual of the Vascular Flora of the Carolinas. The University of North Carolina Press, Chapel Hill, North Carolina.

Schafale, M.P. and A.S. Weakley. 1990. Classification of the Natural Communities of North Carolina, Third Approximation. North Carolina Natural Heritage Program, Division of Parks and Recreation, NCDENR, Raleigh, NC.

Appendix A

Project Background History and Maps

**Table 1. Project Components and Mitigation Credits
Best Stream and Wetland Restoration Project/DMS Project # 95353**

Mitigation Credits									
Type	Stream		Riparian Wetland		Non-riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset
	R	RE	R	RE	R	RE			
Totals	5,003	5,210	5,12*	N/A	N/A	N/A	N/A	N/A	N/A

Project Components							
Project Component -or- Reach ID	Approved Mitigation Plan Stationing/Location (LF)	Existing Footage/Acreage	Approach (PI, PII etc.)	Restoration - or- Restoration Equivalent	Mitigation Plan Restoration Footage or Acreage	Mitigation Ratio	SMUs/ WMUs
UT1	0+47 to 18+00	1,551	PI	R	1,723	1 : 1.0	1,723
UT1	18+00 to 21+03	303	Preservation & BE	RE	303	1 : 5.0	61
UT2	2+30 to 30+30	2,552	PI	R	2,770	1 : 1.0	2,770
UT2	30+30 to 33+39	309	Preservation & BE	RE	309	1 : 5.0	62
UT3	0+00 to 8+42	1,458	EII	RE	812	1 : 2.5	325
UT3	14+58 to 15+22	64	Preservation & BE	RE	64	1 : 5.0	13
UT4	5+63 to 11+03	534	HV Restoration	R	510	1 : 1.0	510
UT4	11+03 to 17+58	655	Preservation & BE	RE	655	1 : 5.0	131
UT5	0+00 to 40+86	4,086	Preservation & BE	RE	4,043	1 : 5.0	809
UT6	0+62 to 6+00	538	EI	RE	538	1 : 1.5	359
UT7	0+44 to 32+27	3,183	Preservation & BE	RE	3,183	1 : 5.0	637
UT8	0+75 to 9+00	825	EI	RE	825	1 : 1.5	550
UT8	9+00 to 12+13	313	Preservation & BE	RE	313	1 : 5.0	63
UT9	0+64 to 11+71	1,171	Preservation & BE	RE	1,171	1 : 5.0	234
UT10	3+37 to 11+05	768	Preservation & BE	RE	768	1 : 5.0	154
Muddy Creek	0+35 to 92+49	9,214	Preservation & BE	RE	9,073	1 : 5.0	1,815
Wetland 1	---	3.66	Restoration	RE	3.66	1 : 1.0	3.66
Wetland 2	---	0.29	Restoration	RE	0.29	1 : 1.0	0.29
Wetland 3A	---	0.58	Restoration	RE	0.58	1 : 1.0	0.58
Wetland 3B	---	0.59	Restoration	RE	0.59	1 : 1.0	0.59*

*0.39 acres of wetland area at-risk for credit due to unsuccessful hydrology data from AW7

Component Summation						
Restoration Level	Stream (linear feet)	Riparian Wetland (acres)		Non-riparian Wetland (acres)	Buffer (square feet)	Upland (acres)
		Riverine	Non-Riverine			
Restoration	4,493	5.12				
Headwater Valley	510					
Enhancement I	1,363					
Enhancement II	812					
Creation						
Preservation	19,882					
High Quality Preservation						

BMP Elements			
Element	Location	Purpose/Function	Notes
---	---	---	---
---	---	---	---
---	---	---	---

BMP Elements
BR = Bioretention Cell; SF = Sand Filter; SW = Stormwater Wetland; WDP = Wet Detention Pond; DDP = Dry Detention Pond; FS = Filter Strip; S = Grassed, Swale; LS = Level Spreader; NI = Natural Infiltration Area; FB = Forested Buffer

Note: Credit calculations were originally calculated along the as-built thalweg. For Monitoring Year 3 forward, credits were updated to match the Approved Mitigation Plan stream centerlines per the April 3, 2017 Credit Release Meeting.

Project Activity and Reporting History

Best Stream and Wetland Restoration Project / DMS Project #95353

Activity or Report	Data Collection Complete	Completion or Delivery
Mitigation Plan	NA	Oct-13
Final Design – Construction Plans	NA	Nov-14
Construction Completed	Sep-13	May-15
Site Planting Completed	May-15	May-15
Baseline Monitoring Document (Year 0 Monitoring – baseline)	Jul-15	Oct-15
Year 1 Monitoring	Dec-15	Mar-16
Year 2 Supplemental Replant/Repair Work	---	Apr-16
Year 2 Monitoring	Nov-16	Jan-17
Year 3 Monitoring	Nov-17	Feb-18
Year 4 Supplemental Planting	---	Jan-18
Year 4 Monitoring	Oct-18	Jan-19
Year 4 Supplemental Planting and Repair Work	---	Dec-18
Year 5 Monitoring	Stream: July-19 Vegetation: Oct-19	Feb-20
Year 4 Invasive Species Treatment (UT1)	---	Sep-20
Year 4 Invasive Species Treatment (UT6)	---	Sep-20
Year 4 Log Sill Repair Work	---	Oct-20
Year 6 Monitoring	Vegetation: Oct-20	Nov-20
Year 7 Monitoring		

Table 3. Project Contacts Table

Best Stream and Wetland Restoration Project /DMS Project # 95353

Designer	WK Dickson and Co., Inc. 720 Corporate Center Drive Raleigh, NC 27607 (919) 782-0495 Frasier Mullen, PE
Construction Contractor	Wright Contracting PO Box 545 Siler City, NC 27344 (919) 663-0810 Joseph Wright
Planting Contractor	0+47 to 18+00 18+00 to 21+03 2+30 to 30+30 30+30 to 33+39 David Godley
Seeding Contractor	5+63 to 11+03 11+03 to 17+58 Siler City, NC 27344 (919) 663-0810 Joseph Wright
Seed Mix Sources	Green Resource
Nursery Stock Suppliers	Arbogen, NC Forestry Services Nursery
Full Delivery Provider	Resource Environmental Solutions, LLC 302 Jefferson Street, Suite 110 Raleigh, NC 27605
Project Manager:	Brad Breslow
Monitoring Performers	Resource Environmental Solutions, LLC 3600 Glenwood Avenue, Suite 100 Raleigh, NC 27612
Project Manager:	Ryan Medric

Project Information	
Project Name	Best Stream and Wetland Restoration Project
County	Duplin
Project Area (acres)	142.7
Project Coordinates (latitude and longitude)	34° 54' 44.011" N 77° 44' 57.344" W

Project Watershed Summary Information	
Physiographic Province	5003
River Basin	Cape Fear
USGS Hydrologic Unit 8-digit	3030007
USGS Hydrologic Unit 14-digit	3.03001E+12
DWQ Sub-basin	3/6/2022
Project Drainage Area (acres)	2,928 acres
Project Drainage Area Percentage of Impervious Area	6%
CGIA Land Use Classification	Woody wetlands, emergent herbaceous wetlands, cultivated crops, evergreen forest


Reach Summary Information (As-Built Conditions)	
	2+30 to 30+30
	30+30 to 33+39

Parameters	UT1	UT2	UT3	UT4	UT5	UT6
Length of reach (linear feet)	2,036	3,103	876	1,140	4,043	538
Valley Classification	X	5+83 to 11+03	X	X	X	X
Drainage area (acres)	41	11+03 to 17+58	56	82	380	79
NCDWQ stream identification score	32.5	31.5	33	33.75	36.75	30.5
NCDWQ Water Quality Classification	N/A	C Sw	N/A	N/A	C Sw	N/A
Morphological Description (stream type)	G5c	G5c	E5	G5c/E5	C5	E5
Evolutionary trend	Stage II	Stage II	Stage VI	Stage II/VI	Stage I	Stage II
Underlying mapped soils	GoA MkA NbB RaA	AuB McC MkA NbA NbB	McC MkA NbB	McC MkA NbB	MkA NbB	NbA NbB
Drainage class	well; mod; well; poorly	well; poorly	well; poorly	well; poorly	well; poorly	well
Soil Hydric status	Hydric	Hydric	Hydric	Hydric	Hydric	Not hydric
Slope	0.66%	0.44%	0.93%	0.42%	0.40%	0.12%
FEMA classification	N/A	N/A	N/A	N/A	AE (high risk)	N/A
Native vegetation community	pasture, cultivated	pasture	mixed hardwood forest	mixed hardwood forest	mixed hardwood forest	mixed hardwood forest
Percent composition of exotic invasive vegetation	0	0	5	5	<40	<25

Reach Summary Information (continued)					
Parameters	4493				Muddy Creek
Length of reach (linear feet)	510				9,214
Valley Classification	1363				X
Drainage area (acres)	812				2930
NCDWQ stream identification score	38.5	30.5	32	34	43.25
NCDWQ Water Quality Classification	19882				C Sw
Morphological Description (stream type)	C5	F5	E5	C5	E5
Evolutionary trend	Stage I	Stage II	Stage VI	Stage VI	Stage VI
Underlying mapped soils	McC MkA NbB	McC NbA NbB	McC MkA	McC MkA	McC MkA
Drainage class	well; poorly	well	well; poorly	well; poorly	well; poorly
Soil Hydric status	Hydric	Hydric	Hydric	Hydric	Hydric
Slope	0.40%	0.29%	0.80%	0.40%	0.11%
FEMA classification	AE (high risk)	N/A	AE (high risk)	AE (high risk)	AE (high risk)
Native vegetation community	mixed hardwood forest	cultivated	mixed hardwood forest	mixed hardwood forest	mixed hardwood forest
Percent composition of exotic invasive vegetation	<40	<5	<15	<20	<45

Wetland Summary Information				
Parameters	Wetland 1	Wetland 2	Wetland 3A	Wetland 3B
Size of Wetland (acres)	3.77	0.31	0.58	0.59
Wetland Type (non-riparian, riparian riverine or riparian non-riverine)	Riparian	Riparian	Riparian	Riparian
Mapped Soil Series	Rains, Goldston	Noboco, Auryville, Marvyn, Grincey	Marvyn, Grincey, Muckalee loam	Marvyn, Grincey, Muckalee loam
Drainage class	Poorly	Mod. Well, Poorly	Poorly, Well	Poorly, Well
Soil Hydric Status	Yes	Hydric with Hydric Inclusions	Hydric with Hydric Inclusions	Hydric with Hydric Inclusions
Source of Hydrology	Runoff/Groundwater Discharge	Runoff/Groundwater Discharge	Runoff, Flooding, Groundwater Discharge	Runoff, Flooding, Groundwater Discharge
Hydrologic Impairment	Grazing Cattle and Incised Channel	Incised Channel	Ditched	Ditched
Native vegetation community	Forested	Cultivated	Cultivated	Cultivated
Percent composition of exotic invasive vegetation	0	0	0	0

Regulatory Considerations			
Regulation	Applicable	Resolved	Supporting Documentation
Waters of the United States - Section 404	Yes	Yes	SAW-2012-01384
Waters of the United States - Section 401	Yes	Yes	DWR # 13-0865
Endangered Species Act	Yes	Yes	USFWS (Corr. Letter)
Historic Preservation Act	Yes	Yes	SHPO (Corr. Letter)
Coastal Zone Management Act (CZMA)/Coastal Area Management Act (CAMA)	No	NA	N/A
FEMA Floodplain Compliance	Yes	Yes	EFP Floodplain Requirements Checklist
Essential Fisheries Habitat	No	NA	N/A

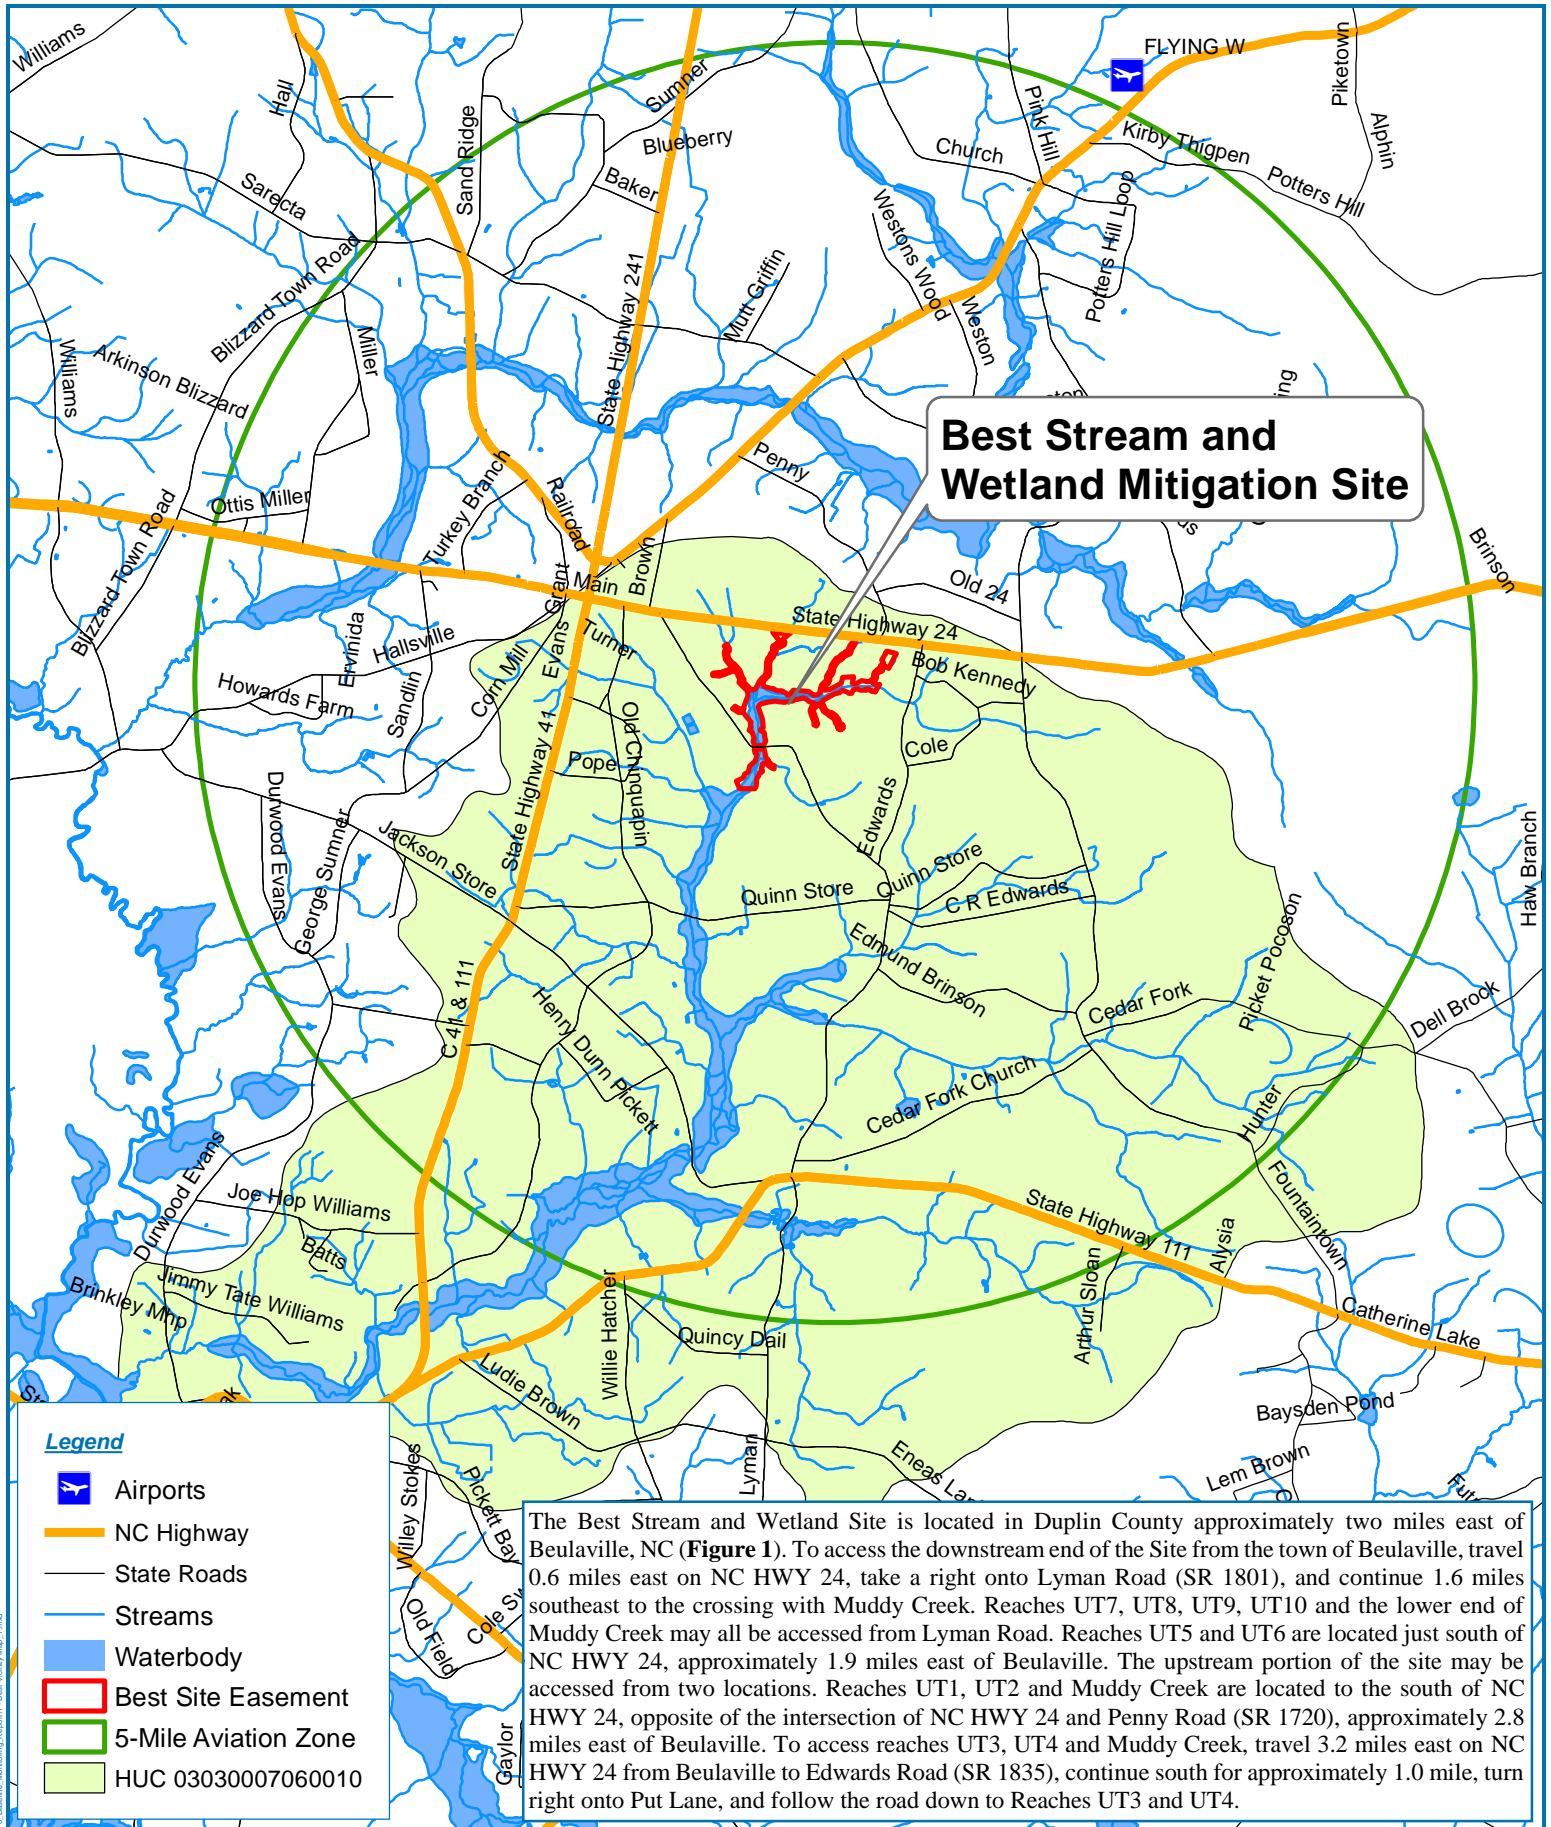


Best Stream and Wetland Mitigation Site

Legend

- Airports
- NC Highway
- State Roads
- Streams
- Waterbody
- Best Site Easement
- 5-Mile Aviation Zone
- HUC 03030007060010

The Best Stream and Wetland Site is located in Duplin County approximately two miles east of Beulaville, NC (**Figure 1**). To access the downstream end of the Site from the town of Beulaville, travel 0.6 miles east on NC HWY 24, take a right onto Lyman Road (SR 1801), and continue 1.6 miles southeast to the crossing with Muddy Creek. Reaches UT7, UT8, UT9, UT10 and the lower end of Muddy Creek may all be accessed from Lyman Road. Reaches UT5 and UT6 are located just south of NC HWY 24, approximately 1.9 miles east of Beulaville. The upstream portion of the site may be accessed from two locations. Reaches UT1, UT2 and Muddy Creek are located to the south of NC HWY 24, opposite of the intersection of NC HWY 24 and Penny Road (SR 1720), approximately 2.8 miles east of Beulaville. To access reaches UT3, UT4 and Muddy Creek, travel 3.2 miles east on NC HWY 24 from Beulaville to Edwards Road (SR 1835), continue south for approximately 1.0 mile, turn right onto Put Lane, and follow the road down to Reaches UT3 and UT4.

Figure 1
Project Vicinity Map
Best Stream and Wetland Restoration Site
Duplin County, North Carolina



Date: 9/15/2015

Drawn by: BSH



Document Path: E:\RES_Plan\BestCAD\03030007060010_Best_Stream_Mitigation_Site.mxd

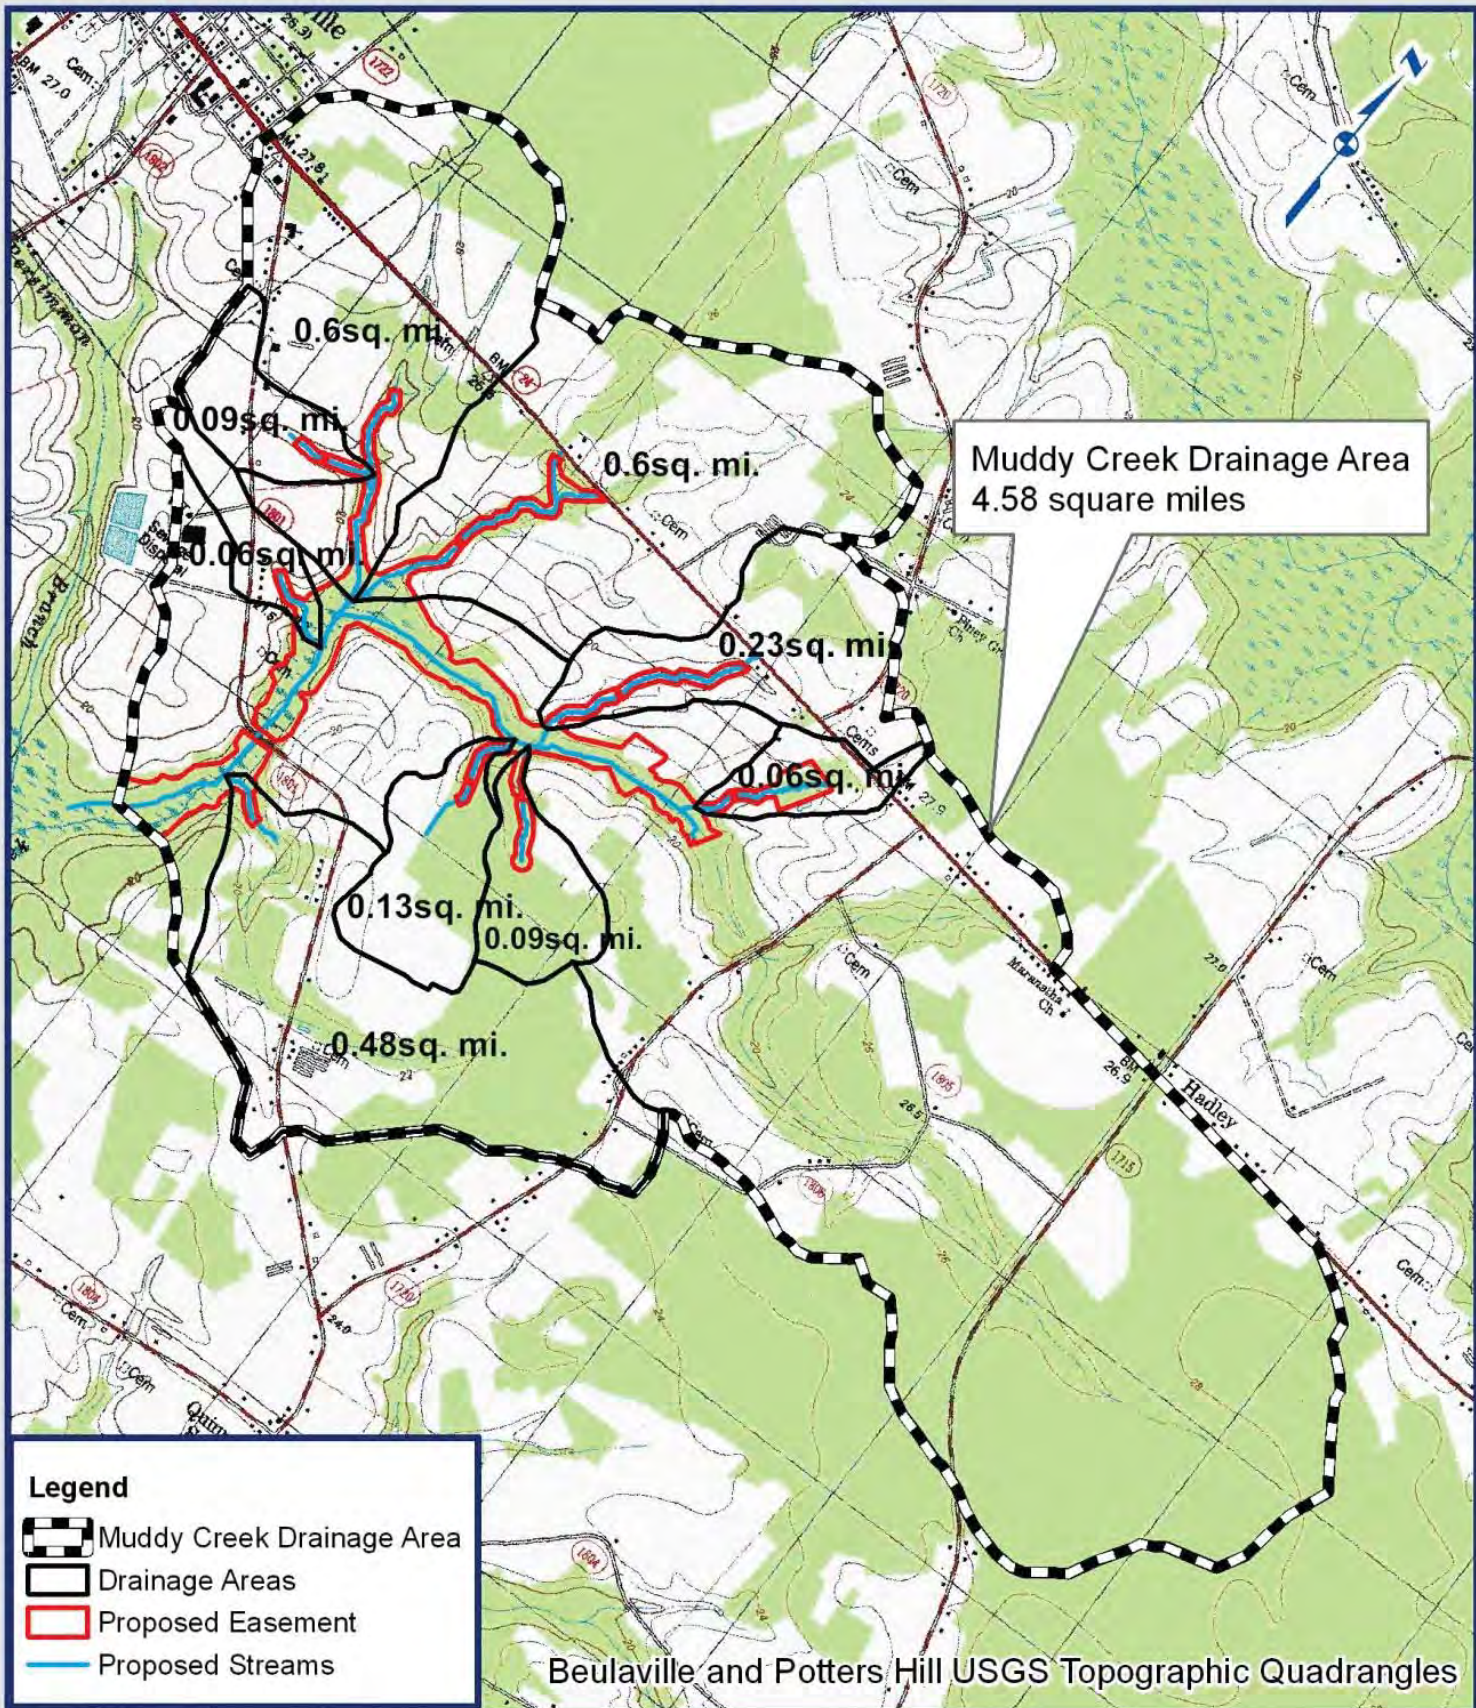


Figure 2.
 USGS Map
 Best Stream and Wetland Mitigation Site

0 1,500 3,000 6,000 Feet

1 inch = 3,000 feet



Appendix B

Visual Assessment Data




Figure 3a

Best Stream and Wetland Restoration Project

Current Conditions Plan View

MY6 2020

Date: 1/14/2021

Drawn by: RTM

1 inch = 250 feet


Review by: BBP

Legend

- Conservation Easement
- Wetland Restoration Area
- Wetland Credit At Risk
- Vegetation Plot**
- >260 stems/acre
- <260 stems/acre
- Cross Sections
- P1 Restoration
- Headwater Valley Rest.
- Enhancement I
- Enhancement II
- BE & Preservation
- ★ Crest Gauge/RG Locations
- Wetland Hydroperiod**
- >9%
- 5-8%
- ⊗ Not Available

Vegetation Condition Assessment

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill	No Fill	No Fill
Present	No Fill	No Fill	No Fill

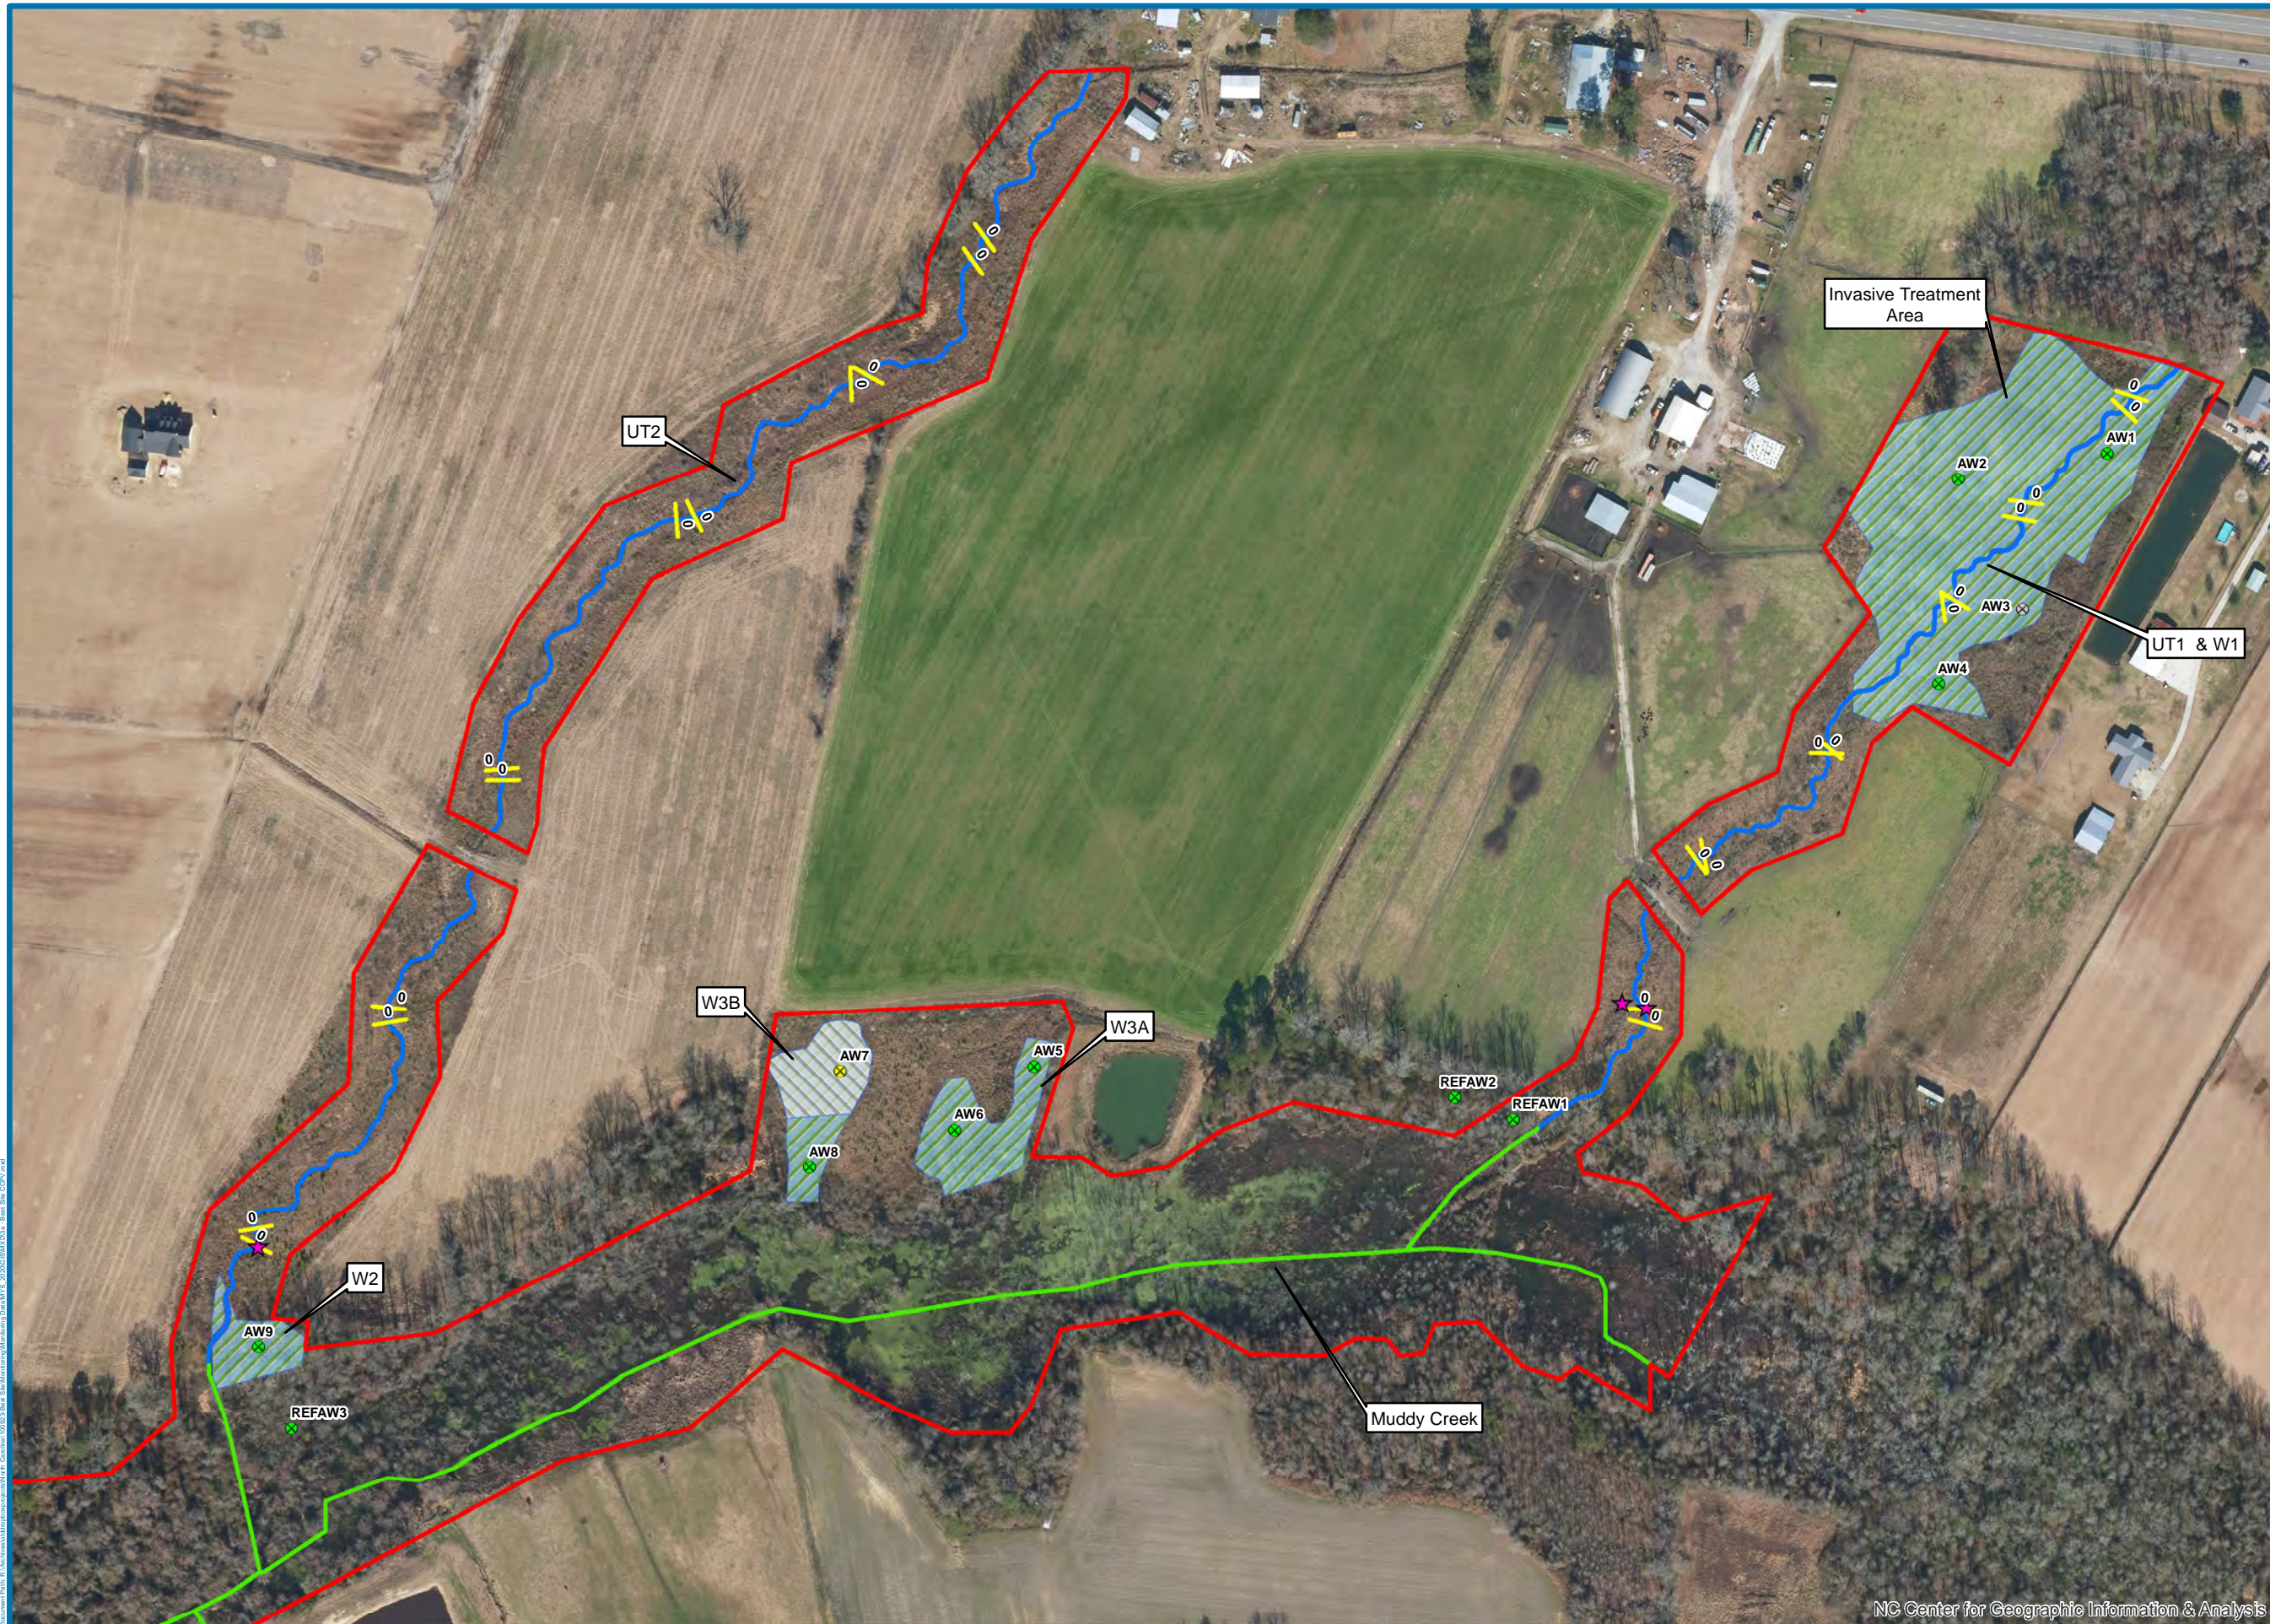




Figure 3b
Best Stream and Wetland Restoration Project
Current Conditions
Plan View
MY6 2020

Date: 1/14/2021 Drawn by: RTM
 1 inch = 150 feet Review by: BPB

Legend

- Conservation Easement
- Wetland Restoration Area
- Vegetation Plot**
- >210 stems/acre
- <210 stems/acre
- Cross Sections
- Stream Mitigation**
- P1 Restoration
- Headwater Valley Rest.
- Enhancement I
- Enhancement II
- BE & Preservation
- No Credit
- ★ Crest Gauge/RG Locations

Vegetation Condition Assessment

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			



Document Path: R:\arcgis\workspace\arcgis\workspace\GIS\Projects\10003_Site_Evaluation\Map_Series\Draft\10003_Site_Evaluation\10003_Site_Evaluation.mxd
 Date: 1/14/2021 10:03:00 AM
 User: RTM




Figure 3c
Best Stream and Wetland Restoration Project
Current Conditions
Plan View
MY6 2020

Date: 11/9/2020 Drawn by: RTM
 1 inch = 400 feet Review by: BPB

Legend

- Conservation Easement
- Vegetation Plot**
- >260 stems/acre
- <260 stems/acre
- ★ Crest Gauge/RG Locations
- Cross Sections
- Stream Mitigation**
- P1 Restoration
- Headwater Valley Rest.
- Enhancement I
- Enhancement II
- BE & Preservation
- Wetland Restoration Area

Vegetation Condition Assessment

Invasive Species	Target Community		
	Present	Marginal	Absent
Absent	No Fill		
Present			

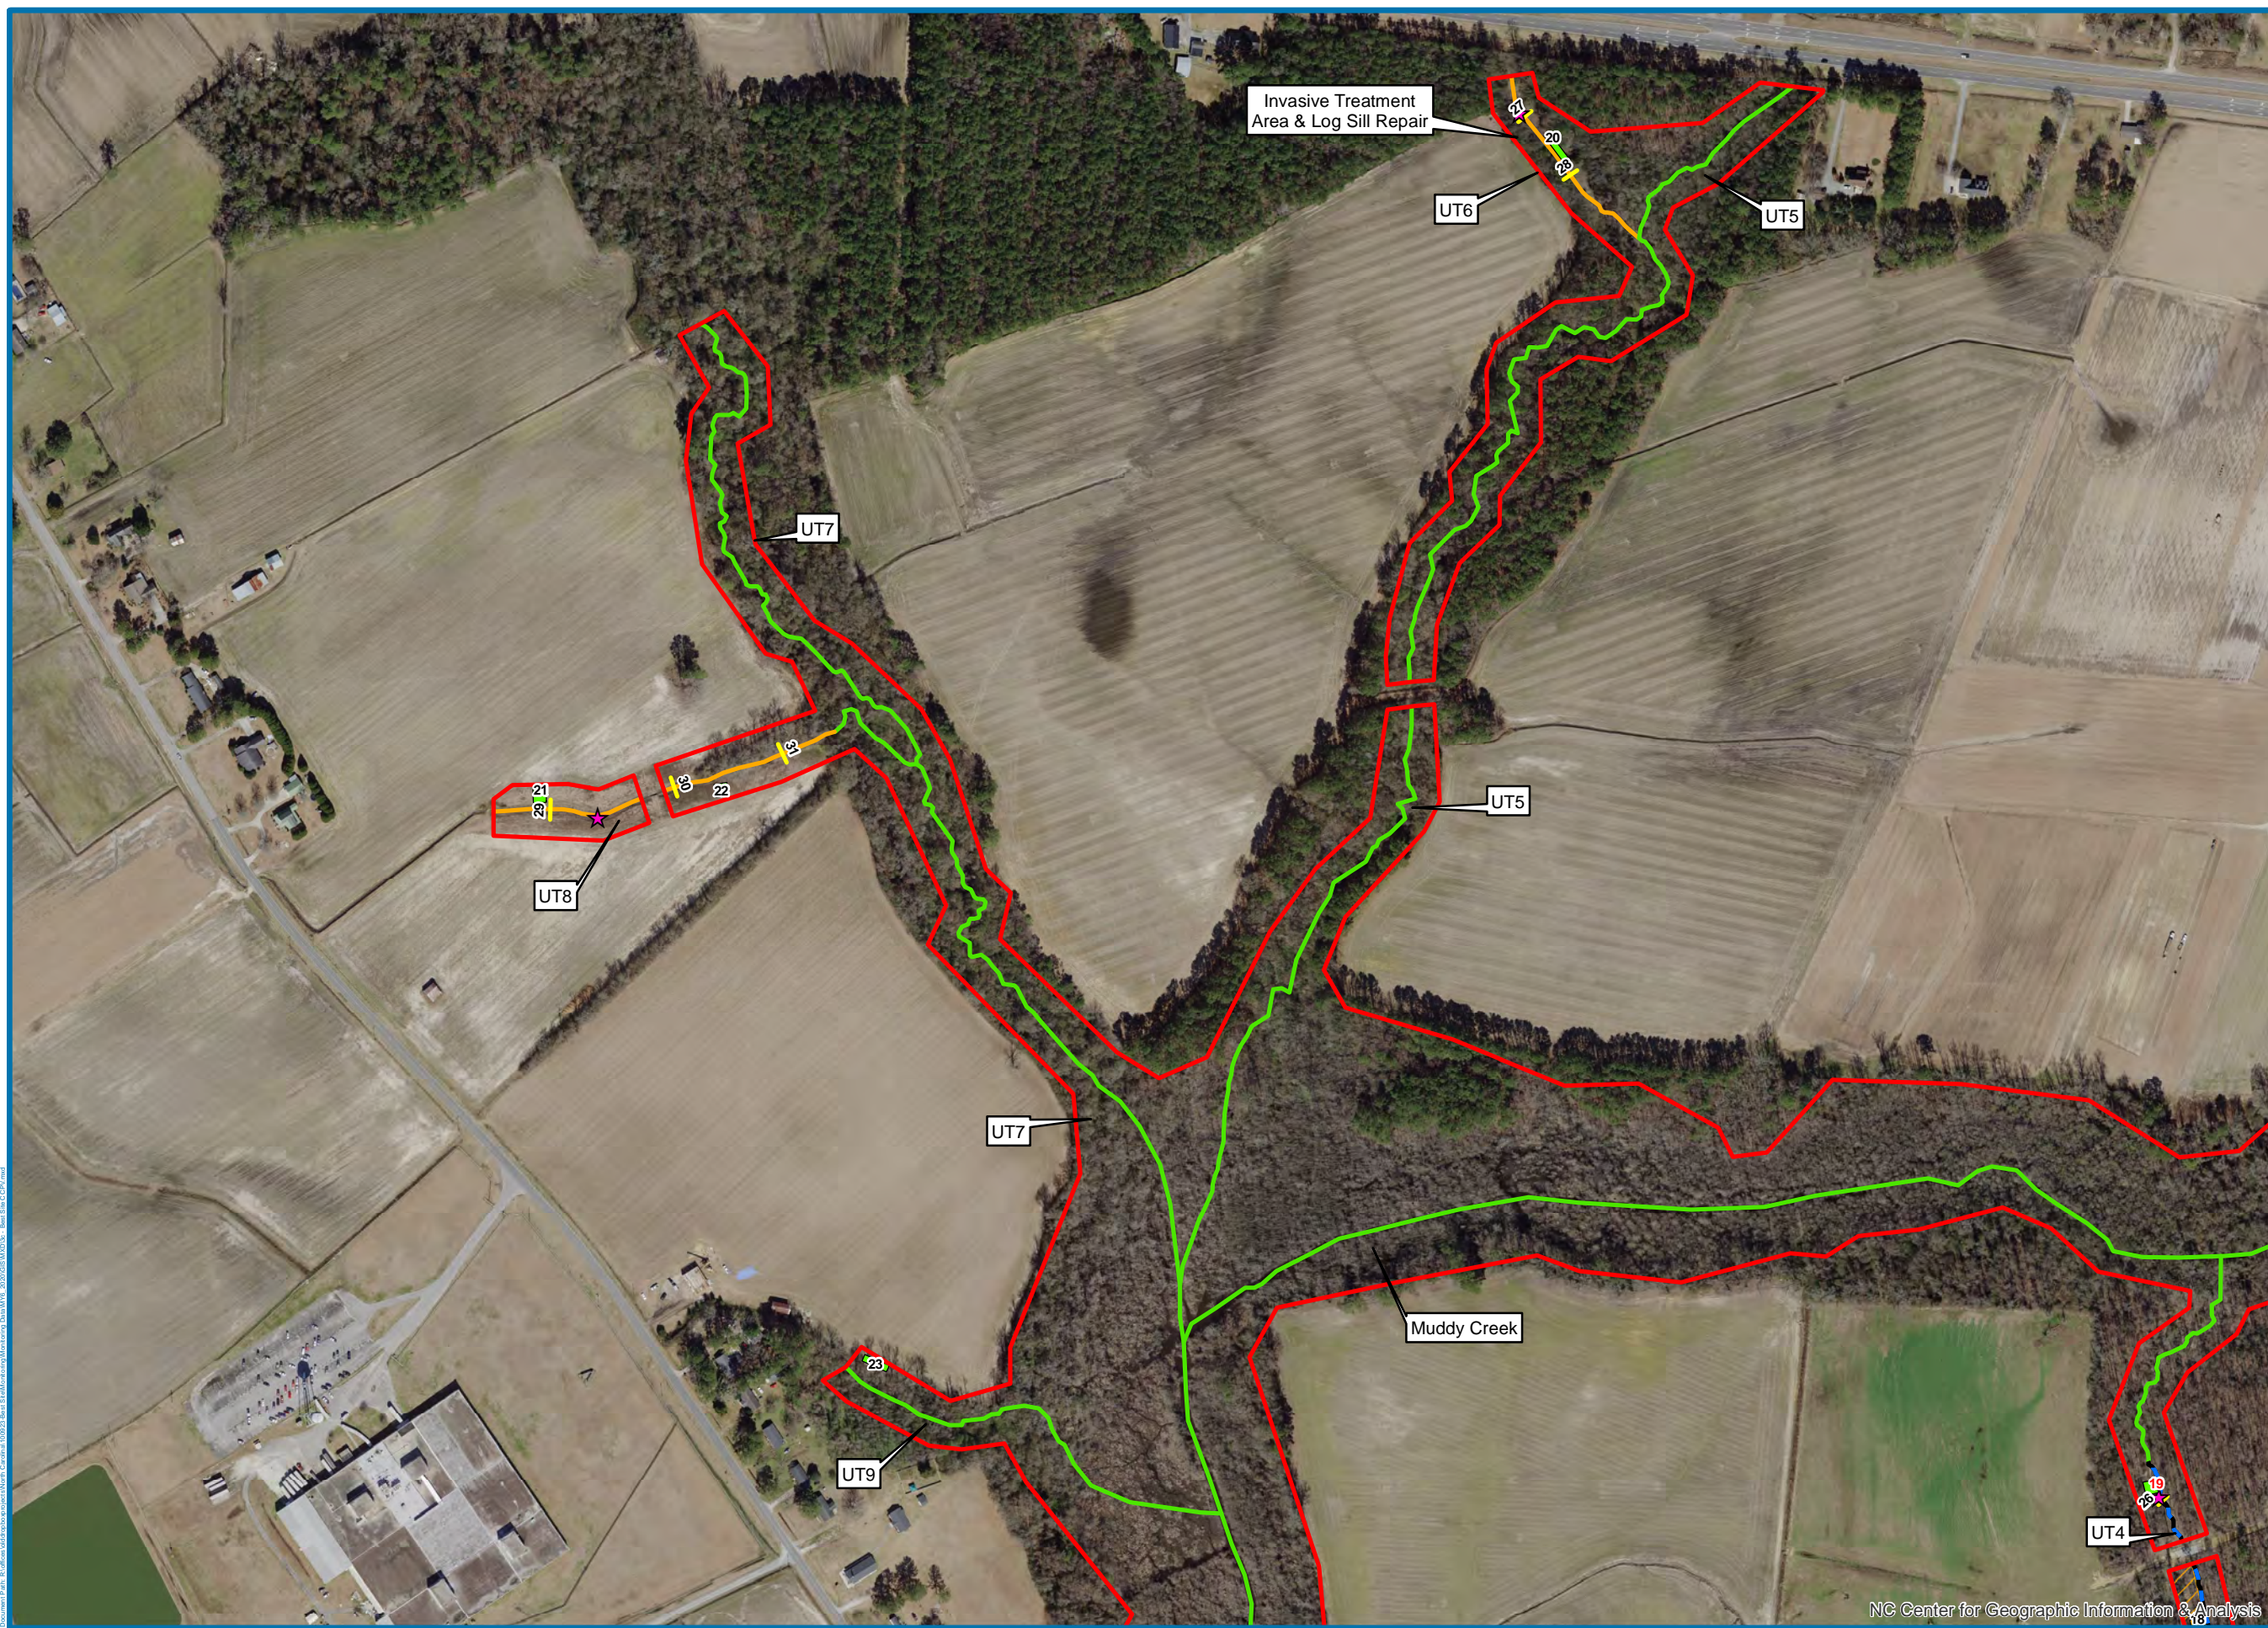


Table 5 **Visual Stream Morphology Stability Assessment**
 Reach ID UT1
 Assessed Length 2036

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	19	19			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	19	19			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	19	19			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	19	19			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio ≥ 1.6 Rootwads/logs providing some cover at base-flow.	19	19			100%			

Table 5 **Visual Stream Morphology Stability Assessment**
 Reach ID UT2
 Assessed Length 3103

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	23	23			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	23	23			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	23	23			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence doesnot exceed 15%. (See guidance for this table in EEP monitoring guidance document)	23	23			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio ≥ 1.6 Rootwads/logs providing some cover at base-flow.	23	23			100%			

Table 5 Visual Stream Morphology Stability Assessment
 Reach ID UT3
 Assessed Length 876

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	1	1			100%			

Table 5 **Visual Stream Morphology Stability Assessment**
 Reach ID UT4
 Assessed Length 1140

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	6	6			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	6	6			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	6	6			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	6	6			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	6	6			100%			

Table 5 Visual Stream Morphology Stability Assessment
 Reach ID UT6
 Assessed Length 538

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	3	3			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio ≥ 1.6 Rootwads/logs providing some cover at base-flow.	3	3			100%			

Table 5 Visual Stream Morphology Stability Assessment
 Reach ID UT8
 Assessed Length 765

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
	Totals				0	0	100%	0	0	100%
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	3	3			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	3	3			100%			

Table 6 **Vegetation Condition Assessment**

Planted Acreage¹ **24.5**

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	0.1 acres	Red Lines	0	0.00	0.0%
2. Low Stem Density Areas	Woody stem densities clearly below target levels.	0.1 acres	Orange Lines	1	0.28	1.1%
Total				1	0.28	1.1%
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 acres	Orange Lines	0	0.00	0.0%
Cumulative Total				1	0.28	1.1%

Easement Acreage² **37.6**

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern⁴	Areas or points (if too small to render as polygons at map scale).	1000 SF	Cross Hatch	0	0.00	0.0%
5. Easement Encroachment Areas³	Areas or points (if too small to render as polygons at map scale).	none	Red Lines	0	0.00	0.0%

¹ = Enter the planted acreage within the easement. This number is calculated as the easement acreage minus any existing mature tree stands that were not subject to supplemental planting of the understory, the channel acreage, crossings or any other elements not directly planted as part of the project effort.

² = The acreage within the easement boundaries.

³ = Encroachment may occur within or outside of planted areas and will therefore be calculated against the overall easement acreage. In the event a polygon is cataloged into items 1, 2 or 3 in the table and is the result of encroachment, the associated acreage should be tallied in the relevant item (i.e., item 1, 2 or 3) as well as a parallel tally in item 5.

⁴ = Invasives may occur in or out of planted areas, but still within the easement and will therefore be calculated against the overall easement acreage. Invasives of concern/interest are listed below. The list of high concern species are those with the potential to directly outcompete native, young, woody stems in the short-term (e.g. monitoring period or shortly thereafter) or affect the community structure for existing, more established tree/shrub stands over timeframes that are slightly longer (e.g. 1-2 decades). The low/moderate concern group are those species that generally do not have this capacity over the timeframes discussed and therefore are not expected to be mapped with regularity, but can be mapped, if in the judgement of the observer their coverage, density or distribution is suppressing the viability, density, or growth of planted woody stems. Decisions as to whether remediation will be needed are based on the integration of risk factors by EEP such as species present, their coverage, distribution relative to native biomass, and the practicality of treatment. For example, even modest amounts of Kudzu or Japanese Knotweed early in the projects history will warrant control, but potentially large coverages of Microstegium in the herb layer will not likely trigger control because of the limited capacities to impact tree/shrub layers within the timeframes discussed and the potential impacts of treating extensive amounts of ground cover. Those species with the "watch list" designator in gray shade are of interest as well, but have yet to be observed across the state with any frequency. Those in *red italics* are of particular interest given their extreme risk/threat level for mapping as points where *isolated* specimens are found, particularly early in a projects monitoring history. However, areas of discreet, dense patches will of course be mapped as polygons. The symbology scheme below was one that was found to be helpful for symbolizing invasives polygons, particularly for situations where the condition for an area is somewhere between isolated specimens and dense, discreet patches. In any case, the point or polygon/area feature can be symbolized to describe things like high or low concern and species can be listed as a map inset, in legend items if the number of species are limited or in the narrative section of the executive summary.

Table 7. Stream Problem Areas

Best Stream and Wetland Restoration Project - Project # 95353

Feature Issue	Station # / Range	Suspected Cause; Repair	Photo Number
Piping Log Sill	UT4	Inproper installation; October 2020	1
Piping Log Sill	UT6	Inproper installation; October 2020	2

Table 8. Vegetation Problem Areas

Best Stream and Wetland Restoration Project - Project # 95353

Feature Category	Station Numbers	Suspected Cause; Repair	Photo Number
Low Stem Density	UT4 (0.28 acres)	Located in full canopy; replant with shade tolerant container trees	VP 18

Figure 4. Vegetation Plot Photos



Vegetation Plot 1



Vegetation Plot 2



Vegetation Plot 3



Vegetation Plot 4



Vegetation Plot 5



Vegetation Plot 6



Vegetation Plot 7



Vegetation Plot 8



Vegetation Plot 9



Vegetation Plot 10



Vegetation Plot 11



Vegetation Plot 12



Vegetation Plot 13



Vegetation Plot 14



Vegetation Plot 15



Vegetation Plot 16



Vegetation Plot 17



Vegetation Plot 18



Vegetation Plot 19



Vegetation Plot 20



Vegetation Plot 21



Vegetation Plot 22



Vegetation Plot 23

Figure 5. MY6 Stream Problem Area Photos



Photo 1 – Piping Log Sill UT4 (Repaired October 2020)



Photo 2 – Piping Log Sill UT6 (Repaired October 2020)

Figure 6. Vegetation Problem Area Photos



VP18 – Low Stem Density Area UT4 (0.28 acres)

Appendix C

Vegetation Plot Data

Table 9a. Vegetation Plot Criteria Attainment

Plot #	Planted Stems/Acre	Volunteer Stems/Acre	Total Stems/Acre	Success Criteria Met?	Average Planted Stem Height (ft)
1	445	0	445	Yes	16.9
2	607	324	931	Yes	12.1
3	364	0	364	Yes	12.5
4	1093	0	1093	Yes	17.2
5	567	40	607	Yes	9.7
6	1214	324	1538	Yes	12.7
7	607	607	1214	Yes	9.2
8	688	162	850	Yes	14.8
9	1174	0	1174	Yes	14.0
10	809	40	850	Yes	14.3
11	1255	486	1740	Yes	7.0
12	1093	647	1740	Yes	15.8
13	931	0	931	Yes	6.7
14	971	2833	3804	Yes	15.2
15	647	0	647	Yes	11.9
16	647	4856	5504	Yes	13.5
17	364	0	364	Yes	9.7
18	81	121	202	No	1.7
19	243	0	283	Yes	8.5
20	890	0	890	Yes	20.0
21	931	0	931	Yes	17.1
22	647	81	728	Yes	10.0
23	567	4047	4613	Yes	6.7
Project Avg	734	633	1367	Yes	12.8

Appendix D

Stream Geomorphology Data

Table 10. Best Site Morphological Parameters

Feature	Reference Reach			Existing ¹												Design				As-Built/Baseline			
	Pool	Run	Shallow	UT1	UT2	UT3	UT4 (US)	UT4 (DS)	UT5	UT6	UT7	UT8	UT9	UT10	Muddy Creek	UT1		UT2		UT1		UT2	
				Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Shallow	Pool	Shallow	Pool	Shallow	Pool	Shallow
Drainage Area (ac)	286			41	146	59	82	82	380	79	387	56	36	306	2930	41		146		41		146	
Drainage Area (mi ²)	0.45			0.06	0.23	0.09	0.13	0.13	0.59	0.12	0.60	0.09	0.06	0.48	4.58	0.06		0		0.06		0	
NC Regional Curve Discharge (cfs) ²	---	---	9.3	2.3	5.7	3.0	3.8	3.8	11.4	3.7	11.5	2.9	2.1	9.7	49.5	2.3		6		2.3		6	
NC Regional Curve Discharge (cfs) ³	---	---	4.8	1.1	2.9	1.4	1.8	1.8	5.9	1.8	6.0	1.4	1.0	5.0	27.9	1.1		3		1.1		3	
Design/Calculated Discharge (cfs)	---	---	13	---	---	---	---	---	---	---	---	---	---	---	---	---		---		---		---	
Dimension																							
BF Width (ft)	10.9	8.9	7.0	5.1	4.8	9.8	6.4	7.5	11.0	5.1	10.1	9.5	6.5	13.7	15.7	6.2	7.1	9.4	10.8	6.6	7.8	10.0	11.9
Floodprone Width (ft)	100	100	100	9	9	22	10	>50	>100	>50	>50	12	>50	84	>50	>50	>50	>50	>50	>50	>50	>50	>50
BF Cross Sectional Area (ft ²)	11.4	8.4	5.0	3.2	4.6	8.1	6.4	6.2	6.0	4.3	6.1	4.9	3.6	7.8	21.2	3.9	6.1	8.9	14.2	3.0	5.1	10.2	15.0
BF Mean Depth (ft)	1.0	0.9	0.8	0.6	1.0	0.8	0.9	0.8	0.5	0.8	0.6	0.5	0.6	0.6	1.4	0.6	0.9	1.0	1.3	0.5	0.7	1.0	1.3
BF Max Depth (ft)	2.1	1.7	1.3	1.1	1.3	1.2	1.1	1.2	1.0	1.2	1.1	0.7	1.1	0.9	2.3	1.0	1.4	1.5	2.2	0.8	1.3	1.8	2.3
Width/Depth Ratio	10.4	9.5	8.8	8.1	5.0	11.8	8.4	9.1	20.2	6.2	16.7	18.2	11.8	24.0	11.6	9.9	8.3	9.9	8.2	14.8	12.3	9.9	9.5
Entrenchment Ratio	9.2	11.2	15.1	1.8	1.9	2.2	1.4	>2.2	>2.2	>2.2	>2.2	1.3	>2.2	6.1	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2
Wetted Perimeter (ft)	12.8	9.7	7.4	5.8	6.3	10.8	8.1	8.3	11.3	6.0	10.5	9.8	7.2	13.9	17.0	6.6	7.7	10.0	11.8	6.8	8.3	10.8	13.0
Hydraulic Radius (ft)	0.9	0.9	0.7	0.6	0.7	0.8	0.8	0.8	0.5	0.7	0.6	0.5	0.5	0.6	1.2	0.6	0.8	0.9	1.2	0.4	0.6	0.9	1.2
Substrate																							
	Fine Sand			Fine Sand												Fine Sand		Fine Sand		Fine Sand		Fine Sand	
Pattern																							
	Min	Max	Med	---	---	---	---	---	---	---	---	---	---	---	---	Min	Max	Min	Max	Min	Max	Min	Max
Channel Beltwidth (ft)	13.6	31.8	23.1	---	---	---	---	---	---	---	---	---	---	---	---	11	28	20	41	13	33	21	48
Radius of Curvature (ft)	11.0	27.6	17.6	---	---	---	---	---	---	---	---	---	---	---	---	9	27	17	37	9	34	14	44
Radius of Curvature Ratio	1.5	3.7	2.3	---	---	---	---	---	---	---	---	---	---	---	---	1.5	4.4	1.8	3.9	1.4	5.1	1.4	4.4
Meander Wavelength (ft)	34.9	68.3	54.5	---	---	---	---	---	---	---	---	---	---	---	---	32	71	44	106	31	67	35	108
Meander Width Ratio	1.8	4.2	3.1	---	---	---	---	---	---	---	---	---	---	---	---	1.8	4.5	2.1	4.4	1.9	5.0	2.1	4.8
Profile																							
Shallow Length (ft)	3.1	30.7	12.6	---	---	---	---	---	---	---	---	---	---	---	---	4	23	6	41	5	26	8	45
Run Length (ft)	2.2	33.2	11.3	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
Pool Length (ft)	4.2	9.5	5.8	---	---	---	---	---	---	---	---	---	---	---	---	3	10	7	12	5	14	8	15
Pool -to-Pool Spacing (ft)	17.5	59.8	36.3	---	---	---	---	---	---	---	---	---	---	---	---	16	49	25	68	18	55	30	74
Additional Reach Parameters																							
Valley Length (ft)	274			1826	2818	1417	253	686	2843	567	2192	942	725	1042	9021	1510	2529	1510	2529				
Channel Length (ft)	309			1905	2865	1522	255	772	3228	597	2629	994	769	1104	9808	1723	2770	1756	2771				
Sinuosity	1.13			1.04	1.02	1.07	1.01	1.13	1.14	1.05	1.20	1.06	1.06	1.06	1.09	1.14	1.10	1.16	1.10				
Water Surface Slope (ft/ft)	0.004			---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---				
Channel Slope (ft/ft)	0.003			0.0066	0.0044	0.0093	0.0042	0.0042	0.004	0.0012	0.004	0.0029	0.008	0.004	0.0011	0.0056	0.0027	0.0063	0.0045				
Rosgen Classification	E5			G5c	G5c	E5	G5c	E5	C5	E5	C5	F5	E5	C5	E5	E5	E5	E5	E5				

¹ Bankfull stage was estimated using NC Regional Curve equations and existing conditions data

² NC Regional Curve equations source: Doll et al. (2003)

³ NC Regional Curve equations source: Sweet and Geratz (2003)

Appendix D. Table 11. - Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)

Project Name/Number: Best Site/ NCDMS Project # 95353

Dimension	Cross Section 1 (Pool)							Cross Section 2 (Riffle)							Cross Section 3 (Riffle)							Cross Section 4 (Pool)							Cross Section 5 (Pool)							
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	
Bankfull Elevation (ft) - Based on AB-XSA ¹	74.7	74.7	74.7	74.7	75.0			74.8	74.8	74.8	74.8	74.9			73.1	73.1	73.1	73.1	73.3			72.8	72.8	72.8	72.8	72.8			71.9	71.9	71.9	71.9	71.9			
Bankfull Width (ft) ¹	8.0	6.7	7.7	8.9	8.1			8.2	7.2	7.8	7.4	7.5			5.2	3.9	5.6	5.6	5.7			6.1	4.5	5.9	5.2	8.9			6.8	6.8	9.5	9.3	10.2			
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.2			50.0	50.0	50.0	50.0	50.0			50.0	50.0	50.0	50.0	50.1			50.0	50.0	50.0	50.0	50.3			50.0	50.0	50.0	50.0	50.4			
Bankfull Mean Depth (ft)	0.8	0.7	0.8	0.8	-			0.5	0.5	0.6	0.6	-			0.3	0.2	0.4	0.3	-			0.4	0.5	0.4	0.4	-			0.6	0.6	0.4	0.4	-			
Bankfull Max Depth (ft) ²	1.4	1.2	1.3	1.4	1.3			1.0	1.0	1.0	0.9	1.1			0.6	0.5	0.7	0.6	0.6			0.8	0.7	0.7	0.6	0.4			1.4	1.3	0.9	0.9	0.7			
Low Bank Elevation (ft)	-	-	-	-	75.0			-	-	-	-	75.0			-	-	-	-	73.3			-	-	-	-	72.7			-	-	-	-	71.7			
Bankfull Cross Sectional Area (ft ²) ²	6.0	4.5	5.9	7.0	5.9			4.2	3.9	4.8	4.3	4.7			1.8	0.9	2.1	1.8	1.8			2.6	2.0	2.2	2.2	1.5			4.1	4.0	3.8	4.0	2.4			
Bankfull Width/Depth Ratio	10.5	10.0	9.9	11.4	-			15.9	13.5	12.7	12.8	-			15.1	16.2	14.7	16.9	-			14.5	9.9	16.2	12.3	-			11.4	11.7	23.4	21.6	-			
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>6.7			>2.2	>2.2	>2.2	>2.2	>8.9			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	N/A	N/A			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	1.1			1.0	1.0	1.0	1.0	1.0	1.1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	N/A	N/A		
Dimension	Cross Section 6 (Riffle)							Cross Section 7 (Riffle)							Cross Section 8 (Pool)							Cross Section 9 (Pool)							Cross Section 10 (Riffle)							
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	
Bankfull Elevation (ft) - Based on AB-XSA ¹	72.1	72.1	72.1	72.1	72.3			70.7	70.7	70.7	70.7	70.7			70.7	70.7	70.7	70.7	70.6			69.0	69.0	69.0	69.0	69.0			68.8	68.8	68.8	68.8	69.0			
Bankfull Width (ft) ¹	7.1	6.1	5.5	6.7	6.3			6.4	7.1	6.4	6.2	6.7			7.7	10.1	8.4	8.5	6.4			7.7	7.1	7.6	7.7	8.9			6.1	5.7	6.3	6.0	7.2			
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	45.2			50.0	50.0	50.0	50.0	50.3			50.0	50.0	50.0	50.0	49.8			50.0	50.0	50.0	50.0	50.1			50.0	50.0	50.0	50.0	50.6			
Bankfull Mean Depth (ft)	0.4	0.4	0.4	0.4	-			0.5	0.5	0.4	0.4	-			0.7	0.6	0.7	0.7	-			0.8	0.7	0.8	0.8	-			0.6	0.5	0.5	0.5	-			
Bankfull Max Depth (ft) ²	0.7	0.6	0.6	0.7	0.6			0.8	0.8	0.9	0.8	0.9			1.2	1.4	1.6	1.6	1.3			1.4	1.2	1.6	1.5	1.3			0.9	0.9	0.9	0.9	0.9			
Low Bank Elevation (ft)	-	-	-	-	72.2			-	-	-	-	70.8			-	-	-	-	70.5			-	-	-	-	68.9			-	-	-	-	69.0			
Bankfull Cross Sectional Area (ft ²) ²	2.8	2.4	2.1	2.8	2.3			3.0	3.3	2.7	2.7	3.5			5.2	5.6	5.7	6.3	4.9			6.1	5.0	6.1	6.2	5.5			3.5	2.9	3.1	3.2	3.6			
Bankfull Width/Depth Ratio	18.0	16.0	14.4	16.0	-			14.0	15.2	15.0	14.5	-			11.3	18.2	12.5	11.3	-			9.9	10.3	9.6	9.4	-			10.4	11.3	12.7	11.4	14.9			
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>7.2			>2.2	>2.2	>2.2	>2.2	>7.5			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>7.0			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.1	<1			1.0	1.0	1.0	1.0	1.1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	0.9	1.0			
Dimension	Cross Section 11 (Pool)							Cross Section 12 (Riffle)							Cross Section 13 (Pool)							Cross Section 14 (Run/Riffle)							Cross Section 15 (Riffle)							
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	
Bankfull Elevation (ft) - Based on AB-XSA ¹	66.5	66.5	66.5	66.5	66.5			66.6	66.6	66.6	66.6	66.3			71.0	71.0	71.0	71.0	71.4			70.7	70.7	70.7	70.7	70.8			69.9	69.9	69.9	69.9	70.1			
Bankfull Width (ft) ¹	10.4	10.0	10.6	10.6	9.5			6.5	5.5	7.9	7.6	5.1			13.7	13.1	12.8	13.2	18.0			10.0	10.0	9.9	9.7	10.4			9.0	9.4	8.6	8.7	10.1			
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.2			37.0	37.0	37.0	37.0	42.4			50.0	50.0	50.0	50.0	>50			50.0	50.0	50.0	50.0	>50			50.0	50.0	50.0	50.0	>50			
Bankfull Mean Depth (ft)	0.6	0.8	0.7	0.7	-			0.4	0.5	0.7	0.6	-			1.4	1.3	1.0	0.9	-			1.1	1.1	0.9	1.0	-			0.9	0.8	0.7	0.8	-			
Bankfull Max Depth (ft) ²	1.3	1.8	1.6	1.5	1.2			0.9	0.8	1.3	1.2	1.3			2.6	2.3	1.6	1.5	1.7			1.7	1.7	1.7	1.7	1.8			1.5	1.4	1.5	1.3	1.6			
Low Bank Elevation (ft)	-	-	-	-	66.3			-	-	-	-	66.7			-	-	-	-	71.2			-	-	-	-	70.7			-	-	-	-	70.1			
Bankfull Cross Sectional Area (ft ²) ²	6.7	7.6	7.4	6.9	5.0			2.8	2.9	5.2	4.7	5.5			18.6	17.6	13.4	12.4	13.8			10.7	10.6	9.1	9.5	9.6			7.8	7.3	6.3	6.6	8.6			
Bankfull Width/Depth Ratio	16.0	13.2	15.3	16.2	13.4			15.1	10.7	12.0	12.5	9.4			10.1	9.0	12.3	14.0	-			9.3	9.6	10.7	9.9	-			10.3	12.0	11.7	11.5	-			
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	8.3			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>4.8			>2.2	>2.2	>2.2	>2.2	>5			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	1.5			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	<1			1.0	1.0	1.0	1.1	1.0			
Dimension	Cross Section 16 (Pool)							Cross Section 17 (Riffle)							Cross Section 18 (Pool)							Cross Section 19 (Pool)							Cross Section 20 (Run/Riffle)							
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.4	69.4	69.4	69.4	69.7			68.7	68.7	68.7	68.7	69.1			68.1	68.1	68.1	68.1	68.4			66.7	66.7	66.7	66.7	66.6			67.1	67.1	67.1	67.1	67.4			
Bankfull Width (ft) ¹	12.4	13.3	12.0	12.6	15.2			9.8	9.6	10.2	9.1	12.6			10.4	9.2	11.6	10.8	12.0			10.8	11.4	10.7	10.8	9.7			11.4	12.1	11.5	12.4	13.1			
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50			50.0	50.0	50.0	50.0	>50			50.0	50.0	50.0	50.0	>50			50.0	50.0	50.0	50.0	50.1			50.0	50.0	50.0	50.0	50.3			
Bankfull Mean Depth (ft)	1.2	1.2	1.1	1.1	-			0.9	0.8	0.8	0.8	-			1.1	1.0	1.0	0.9	-			1.2	1.1	1.3	1.3	-			1.2	1.1	1.0	0.9	-			
Bankfull Max Depth (ft) ²	2.3	2.2	2.0	1.8	1.7			1.6	1.5	1.5	1.4	1.3			1.9	1.7	2.1	1.7	1.6			2.1	2.8	2.7	2.7	2.4			2.3	2.1	1.8	1.7	1.8			
Low Bank Elevation (ft)	-	-	-	-	69.7			-	-	-	-	68.9			-	-	-	-	68.4			-	-	-	-	66.8			-	-	-	-	67.1			
Bankfull Cross Sectional Area (ft ²) ²	15.1	15.7	13.4	14.1	14.1			9.3	7.5	8.0	6.9	6.8			11.2	8.8	11.6	10.2	11.1			12.5	11.4	14.1	14.4	14.9			13.8	13.0	10.9	11.4	10.8			
Bankfull Width/Depth Ratio	10.2	11.3	10.7	11.2	-			10.3	12.3	12.9	12.0	-			9.7	9.6	11.5	11.6	-			9.4	10.0	8.2	8.0	-			9.4	11.2	12.0	13.4	-			
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>4			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>3.9			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	<1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	N/A	N/A			1.0							

Appendix D. Table 11. - Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)

Project Name/Number: Best Site/ NCDMS Project # 95353

Dimension	Cross Section 21 (Run)							Cross Section 22 (Pool)							Cross Section 23 (Run)							Cross Section 24 (Pool)							Cross Section 25 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	65.1	65.1	65.1	65.1	65.2			65.0	65.0	65.0	65.0	65.1			62.8	62.8	62.8	62.8	63.0			62.5	62.5	62.5	62.5	63.3			71.5	71.5	71.5	71.5	71.6		
Bankfull Width (ft) ¹	10.9	10.0	9.3	9.7	11.2			10.7	10.5	10.4	10.6	11.5			9.1	10.3	11.1	10.0	11.8			13.2	13.8	19.0	14.1	14.4			12.2	11.5	13.1	12.1	10.6		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.0			50.0	50.0	50.0	50.0	50.1			50.0	50.0	50.0	50.0	50.2			50.0	50.0	50.0	50.0	50.3			50.0	50.0	50.0	50.0	>50.3		
Bankfull Mean Depth (ft)	1.0	1.0	1.1	1.1	-			1.3	1.2	1.2	1.3	-			1.0	0.8	0.8	0.8	-			1.4	1.0	0.4	0.5	-			0.3	0.3	0.3	0.3	-		
Bankfull Max Depth (ft) ²	1.9	1.9	2.1	2.2	1.8			2.4	2.3	2.4	2.5	2.4			1.8	1.4	1.4	1.2	0.9			2.6	2.1	1.0	0.9	1.2			0.8	0.7	0.8	0.8	0.8		
Low Bank Elevation (ft)	-	-	-	-	64.8			-	-	-	-	65.0			-	-	-	-	62.7			-	-	-	-	62.3			-	-	-	-	71.4		
Bankfull Cross Sectional Area (ft ²) ²	11.1	10.0	10.0	10.4	7.3			14.2	12.4	12.4	13.3	13.2			8.7	8.1	9.1	7.7	5.2			18.3	14.4	7.7	7.2	5.7			4.2	3.6	4.4	4.1	2.7		
Bankfull Width/Depth Ratio	10.7	9.9	8.6	9.1	-			8.1	8.8	8.7	8.4	-			9.4	13.1	13.5	13.0	-			9.5	13.3	47.0	27.6	11.4			35.5	36.6	39.0	36.1	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4.4			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>4.3			>2.2	>2.2	>2.2	N/A	N/A			>2.2	>2.2	>2.2	>2.2	>4.8		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	<1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.0	<1		
Dimension	Cross Section 26 (Run)							Cross Section 27* (Riffle)							Cross Section 28* (Run)							Cross Section 29* (Pool)							Cross Section 30* (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	67.9	67.9	67.9	67.9	67.8			69.9	69.9	69.9	69.9	69.7			69.2	69.2	69.2	69.2	69.2			65.3	65.3	65.3	65.3	65.7			63.7	63.7	63.7	63.7	63.9		
Bankfull Width (ft) ¹	5.6	5.3	6.1	5.7	3.9			7.2	6.7	6.5	5.7	5.3			5.7	5.3	5.6	5.2	5.3			8.7	3.3	8.3	6.3	10.5			6.4	6.7	5.6	5.3	6.2		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	25.4			50.0	50.0	50.0	13.2	11.7			50.0	15.0	16.8	9.3	11.5			50.0	20.0	13.7	15.8	19.6			50.0	20.0	19.3	16.4	18.5		
Bankfull Mean Depth (ft)	0.6	0.5	0.8	0.9	-			0.7	0.6	0.8	0.8	-			0.5	0.5	0.4	0.4	-			0.4	0.4	0.3	0.3	-			0.9	0.8	0.9	0.7	-		
Bankfull Max Depth (ft) ²	1.0	0.9	1.6	1.7	1.7			1.1	1.0	1.3	1.2	3.3			0.9	0.8	0.8	0.6	1.9			0.9	0.8	0.6	0.4	1.1			1.3	1.5	1.6	1.0	1.5		
Low Bank Elevation (ft)	-	-	-	-	68.2			-	-	-	-	71.8			-	-	-	-	70.2			-	-	-	-	66.0			-	-	-	-	64.0		
Bankfull Cross Sectional Area (ft ²) ²	3.1	2.7	5.1	5.1	5.3			4.7	4.1	4.9	4.5	25.9			3.1	2.4	2.5	1.9	11.2			3.8	3.3	2.1	1.8	7.7			5.7	5.6	5.1	4.0	6.4		
Bankfull Width/Depth Ratio	10.2	10.2	7.4	6.5	-			10.8	11.0	8.5	7.1	-			10.4	11.4	12.5	14.5	-			19.9	22.1	32.7	22.4	-			7.1	7.9	6.3	7.2	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	6.5			>2.2	>2.2	>2.2	>2.2	2.2			>2.2	>2.2	>2.2	1.8	2.2			>2.2	1.9	1.6	N/A	N/A			>2.2	>2.2	>2.2	>2.2	3.0		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.4			1.0	1.0	1.0	0.9	2.6			1.0	1.0	1.0	2.7	2.1			1.0	1.0	1.0	N/A	N/A			1.0	1.0	1.0	1.2	1.1		
Dimension	Cross Section 31* (Riffle)																																		
	Base	MY1	MY2	MY3	MY5	MY7	MY+																												
Bankfull Elevation (ft) - Based on AB-XSA ¹	63.0	63.0	63.0	63.0	63.5																														
Bankfull Width (ft) ¹	7.7	8.5	3.4	4.0	6.3																														
Floodprone Width (ft) ¹	50.0	15.0	14.2	13.4	18.4																														
Bankfull Mean Depth (ft)	0.4	0.2	0.3	0.3	-																														
Bankfull Max Depth (ft) ²	0.7	0.5	0.5	0.4	2.8																														
Low Bank Elevation (ft)	-	-	-	-	65.5																														
Bankfull Cross Sectional Area (ft ²) ²	3.0	2.1	0.9	1.1	20.5																														
Bankfull Width/Depth Ratio	19.5	34.5	13.2	14.9	-																														
Bankfull Entrenchment Ratio ¹	>2.2	1.7	>2.2	>2.2	2.9																														
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.7	3.7																														

Note: In MY3, BHR was calculated on riffles using the baseline bankfull elevation. This method was used because the dimension of the channels has not changed enough to alter the bankfull elevation. None of the riffle cross sections exceeded a 1.2 BHR.

Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull elevation. These changes reflect the 2018 guidance that arose from the mitigation technical workgroup consisting of DMS, the IRT, and industry mitigation providers.

*Enhancement I cross sections are subject to higher BHR because they are not built with bankfull elevations equal to the top of bank like the restoration reaches.

Table 12. Bank Pin Array Summary Data


Cross Section	Location	Position	Year 1 Reading	Year 2 Reading	Year 3 Reading	Year 5 Reading
XS 1 @ Sta. 1+00 - UT1	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
XS 4 @ Sta. 4+25 - UT1	US	Top	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
XS 5 @ Sta. 6+25 - UT1	US	Top	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
XS 8 @ Sta. 9+90 - UT1	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
XS 11 @ Sta. 15+90 - UT1	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	6"	0.0	0.0	0.0
		Bottom	24"	0.0	0.0	0.0
XS 13 @ Sta. 5+75 - UT2	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
XS 22 @ Sta. 23+55 - UT2	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
XS 24 @ Sta. 28+45 - UT2	US	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0
	DS	Top	0.0	0.0	0.0	0.0
		Bottom	0.0	0.0	0.0	0.0



Upstream



Downstream

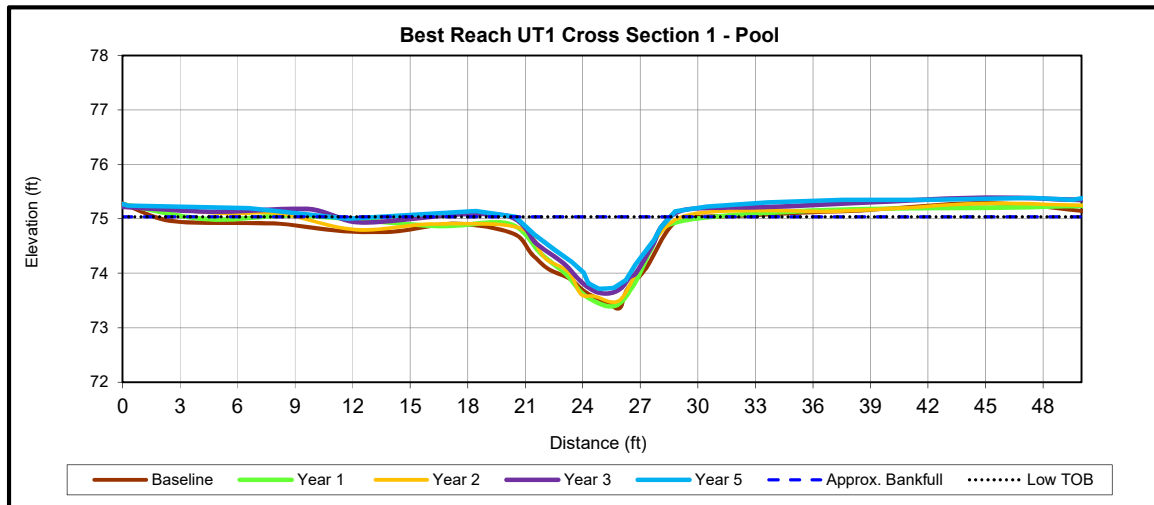

Dimension	Cross Section 1 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	74.7	74.7	74.7	74.7	75.0		
Bankfull Width (ft) ¹	8.0	6.7	7.7	8.9	8.1		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.2		
Bankfull Mean Depth (ft)	0.8	0.7	0.8	0.8	-		
Bankfull Max Depth (ft) ²	1.4	1.2	1.3	1.4	1.3		
Low Bank Elevation (ft)	-	-	-	-	75.0		
Bankfull Cross Sectional Area (ft ²) ²	6.0	4.5	5.9	7.0	5.9		
Bankfull Width/Depth Ratio	10.5	10.0	9.9	11.4	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

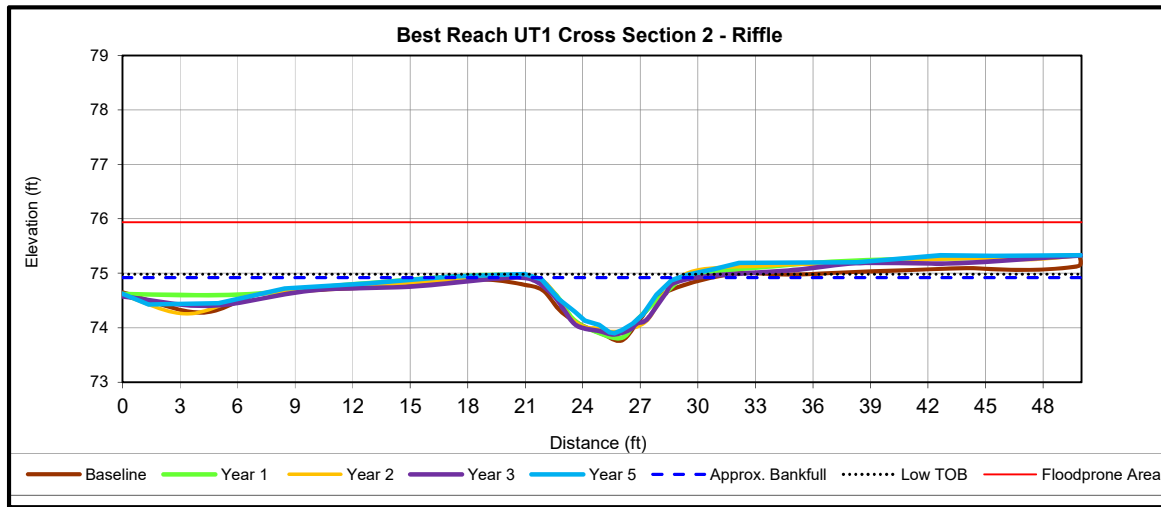

Dimension	Cross Section 2 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	74.8	74.8	74.8	74.8	74.9		
Bankfull Width (ft) ¹	8.2	7.2	7.8	7.4	7.5		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.0		
Bankfull Mean Depth (ft)	0.5	0.5	0.6	0.6	-		
Bankfull Max Depth (ft) ²	1.0	1.0	1.0	0.9	1.1		
Low Bank Elevation (ft)	-	-	-	-	75.0		
Bankfull Cross Sectional Area (ft ²) ²	4.2	3.9	4.8	4.3	4.7		
Bankfull Width/Depth Ratio	15.9	13.5	12.7	12.8	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>6.7		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

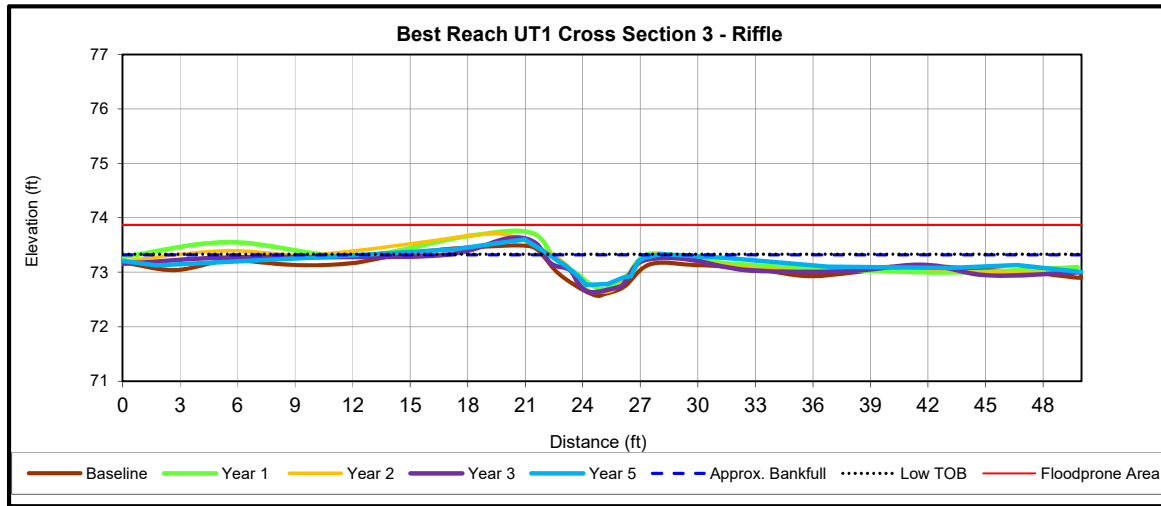

Dimension	Cross Section 3 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	73.1	73.1	73.1	73.1	73.3		
Bankfull Width (ft) ¹	5.2	3.9	5.6	5.6	5.7		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.1		
Bankfull Mean Depth (ft)	0.3	0.2	0.4	0.3	-		
Bankfull Max Depth (ft) ²	0.6	0.5	0.7	0.6	0.6		
Low Bank Elevation (ft)	-	-	-	-	73.3		
Bankfull Cross Sectional Area (ft ²) ²	1.8	0.9	2.1	1.8	1.8		
Bankfull Width/Depth Ratio	15.1	16.2	14.7	16.9	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>8.9		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.0		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

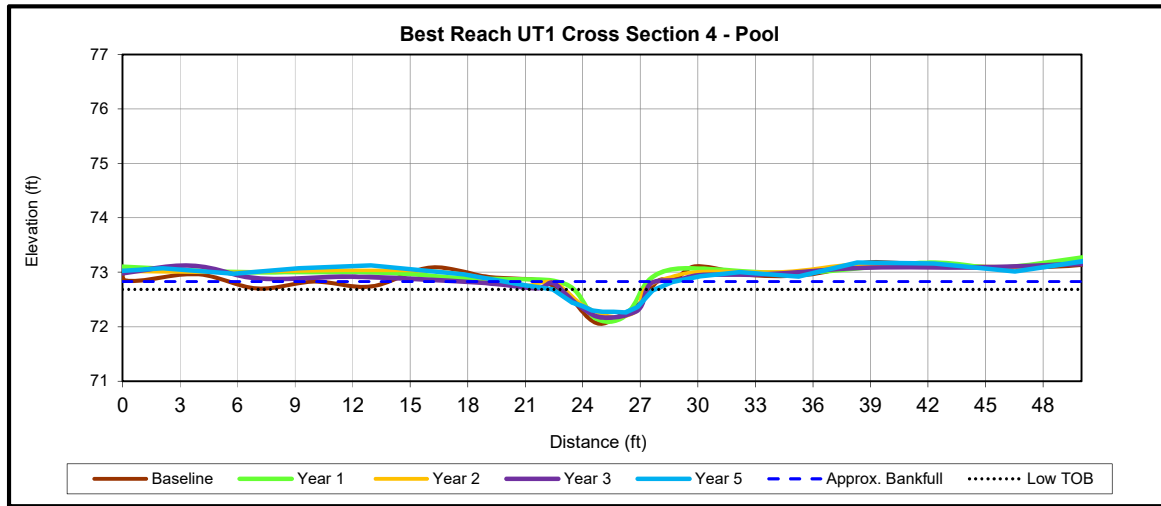

Dimension	Cross Section 4 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	72.8	72.8	72.8	72.8	72.8		
Bankfull Width (ft) ¹	6.1	4.5	5.9	5.2	8.9		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.3		
Bankfull Mean Depth (ft)	0.4	0.5	0.4	0.4	-		
Bankfull Max Depth (ft) ²	0.8	0.7	0.7	0.6	0.4		
Low Bank Elevation (ft)	-	-	-	-	72.7		
Bankfull Cross Sectional Area (ft ²) ²	2.6	2.0	2.2	2.2	1.5		
Bankfull Width/Depth Ratio	14.5	9.9	16.2	12.3	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

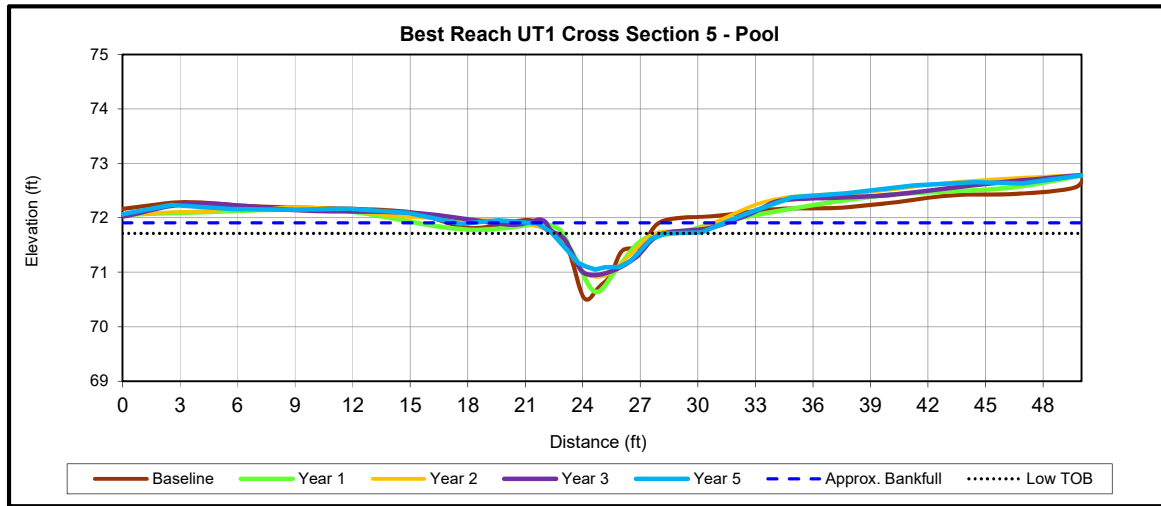

Dimension	Cross Section 5 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	71.9	71.9	71.9	71.9	71.9		
Bankfull Width (ft) ¹	6.8	6.8	9.5	9.3	10.2		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.4		
Bankfull Mean Depth (ft)	0.6	0.6	0.4	0.4	-		
Bankfull Max Depth (ft) ²	1.4	1.3	0.9	0.9	0.7		
Low Bank Elevation (ft)	-	-	-	-	71.7		
Bankfull Cross Sectional Area (ft ²) ²	4.1	4.0	3.8	4.0	2.4		
Bankfull Width/Depth Ratio	11.4	11.7	23.4	21.6	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

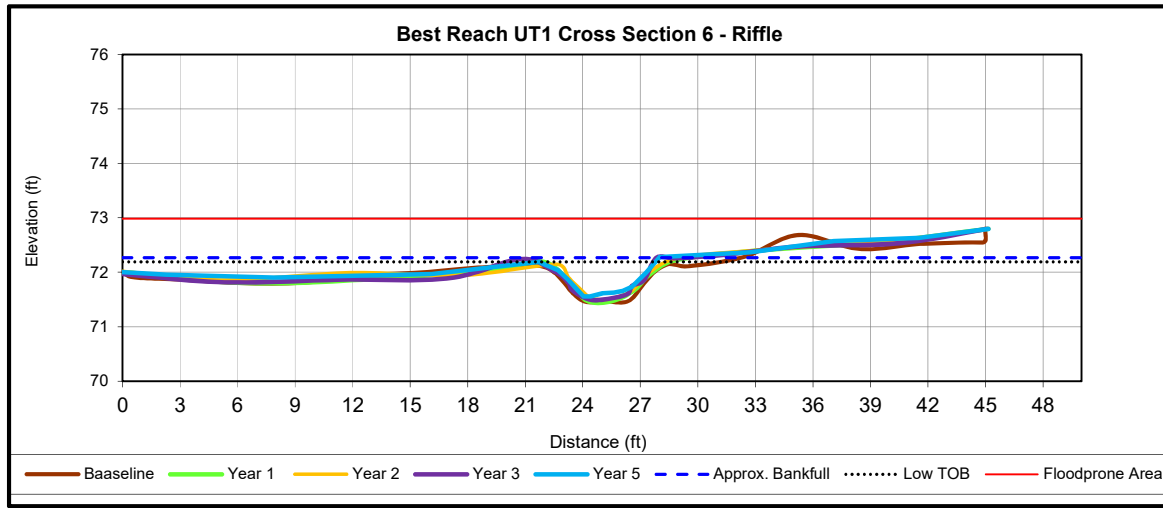

Dimension	Cross Section 6 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	72.1	72.1	72.1	72.1	72.3		
Bankfull Width (ft) ¹	7.1	6.1	5.5	6.7	6.3		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	45.2		
Bankfull Mean Depth (ft)	0.4	0.4	0.4	0.4	-		
Bankfull Max Depth (ft) ²	0.7	0.6	0.6	0.7	0.6		
Low Bank Elevation (ft)	-	-	-	-	72.2		
Bankfull Cross Sectional Area (ft ²) ²	2.8	2.4	2.1	2.8	2.3		
Bankfull Width/Depth Ratio	18.0	16.0	14.4	16.0	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>7.2		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.1	<1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

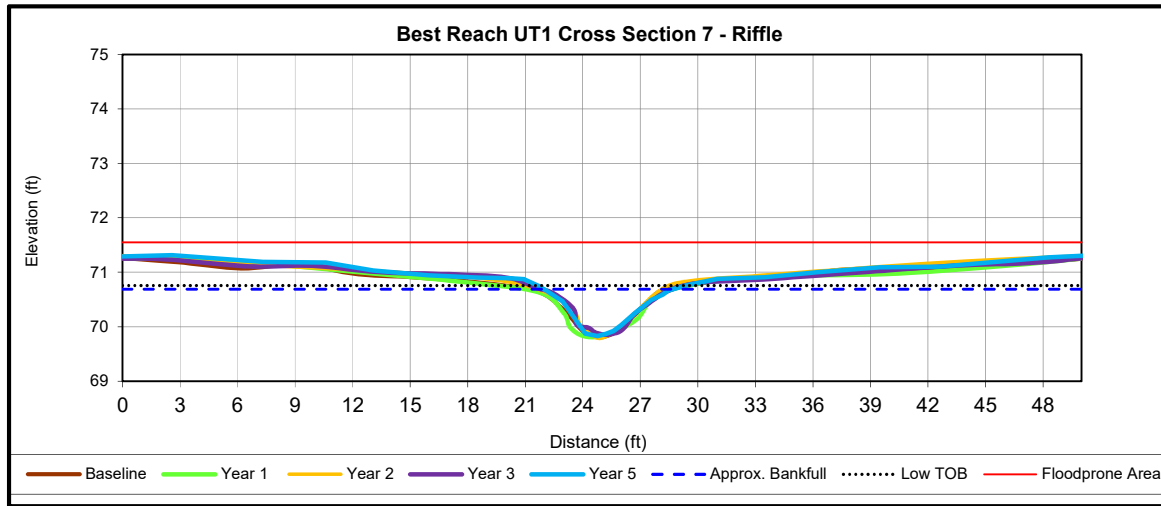

Dimension	Cross Section 7 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	70.7	70.7	70.7	70.7	70.7		
Bankfull Width (ft) ¹	6.4	7.1	6.4	6.2	6.7		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.3		
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4	-		
Bankfull Max Depth (ft) ²	0.8	0.8	0.9	0.8	0.9		
Low Bank Elevation (ft)	-	-	-	-	70.8		
Bankfull Cross Sectional Area (ft ²) ²	3.0	3.3	2.7	2.7	3.5		
Bankfull Width/Depth Ratio	14.0	15.2	15.0	14.5	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>7.5		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

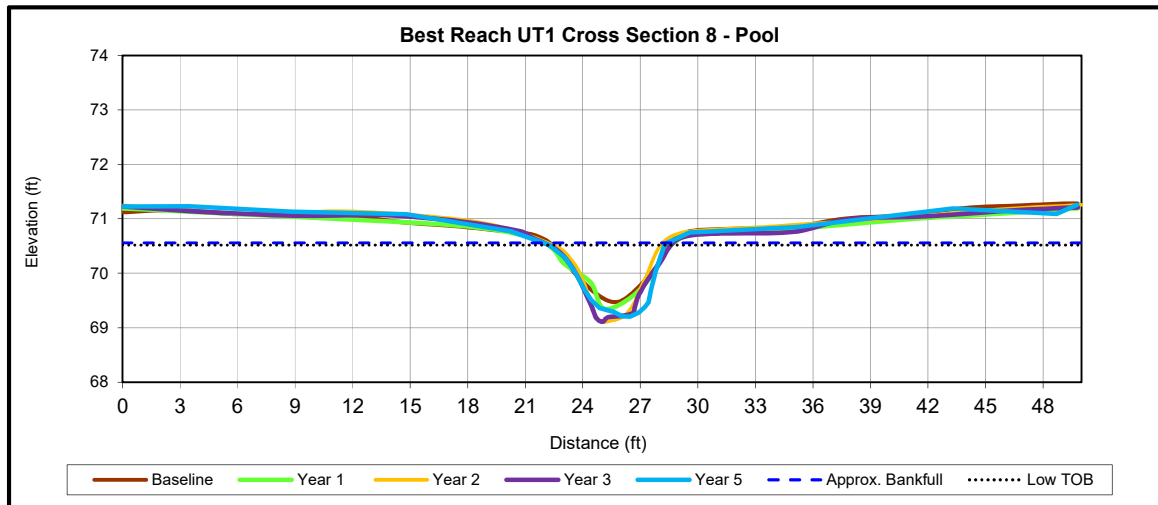

Dimension	Cross Section 8 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	70.7	70.7	70.7	70.7	70.6		
Bankfull Width (ft) ¹	7.7	10.1	8.4	8.5	6.4		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	49.8		
Bankfull Mean Depth (ft)	0.7	0.6	0.7	0.7	-		
Bankfull Max Depth (ft) ²	1.2	1.4	1.6	1.6	1.3		
Low Bank Elevation (ft)	-	-	-	-	70.5		
Bankfull Cross Sectional Area (ft ²) ²	5.2	5.6	5.7	6.3	4.9		
Bankfull Width/Depth Ratio	11.3	18.2	12.5	11.3	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

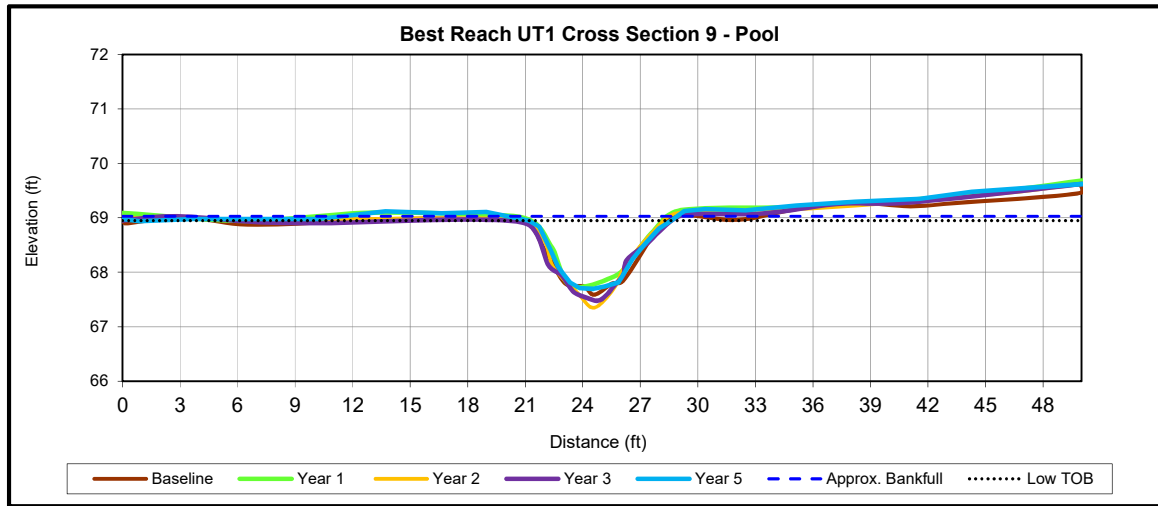

Dimension	Cross Section 9 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.0	69.0	69.0	69.0	69.0		
Bankfull Width (ft) ¹	7.7	7.1	7.6	7.7	8.9		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.1		
Bankfull Mean Depth (ft)	0.8	0.7	0.8	0.8	-		
Bankfull Max Depth (ft) ²	1.4	1.2	1.6	1.5	1.3		
Low Bank Elevation (ft)	-	-	-	-	68.9		
Bankfull Cross Sectional Area (ft ²) ²	6.1	5.0	6.1	6.2	5.5		
Bankfull Width/Depth Ratio	9.9	10.3	9.6	9.4	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

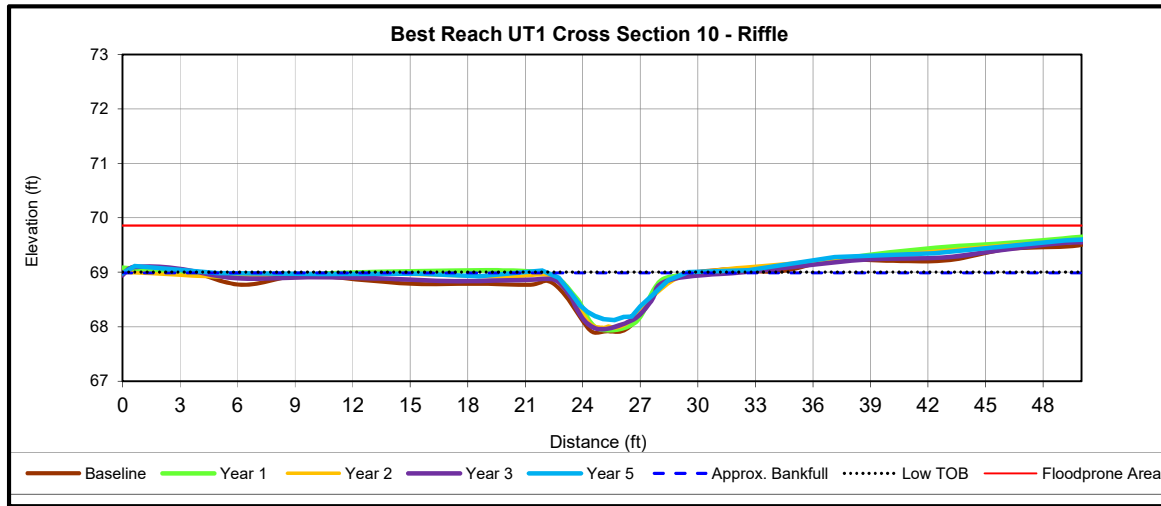

Dimension	Cross Section 10 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	68.8	68.8	68.8	68.8	69.0		
Bankfull Width (ft) ¹	6.1	5.7	6.3	6.0	7.2		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.6		
Bankfull Mean Depth (ft)	0.6	0.5	0.5	0.5	-		
Bankfull Max Depth (ft) ²	0.9	0.9	0.9	0.9	0.9		
Low Bank Elevation (ft)	-	-	-	-	69.0		
Bankfull Cross Sectional Area (ft ²) ²	3.5	2.9	3.1	3.2	3.6		
Bankfull Width/Depth Ratio	10.4	11.3	12.7	11.4	14.9		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>7.0		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	0.9	1.0		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

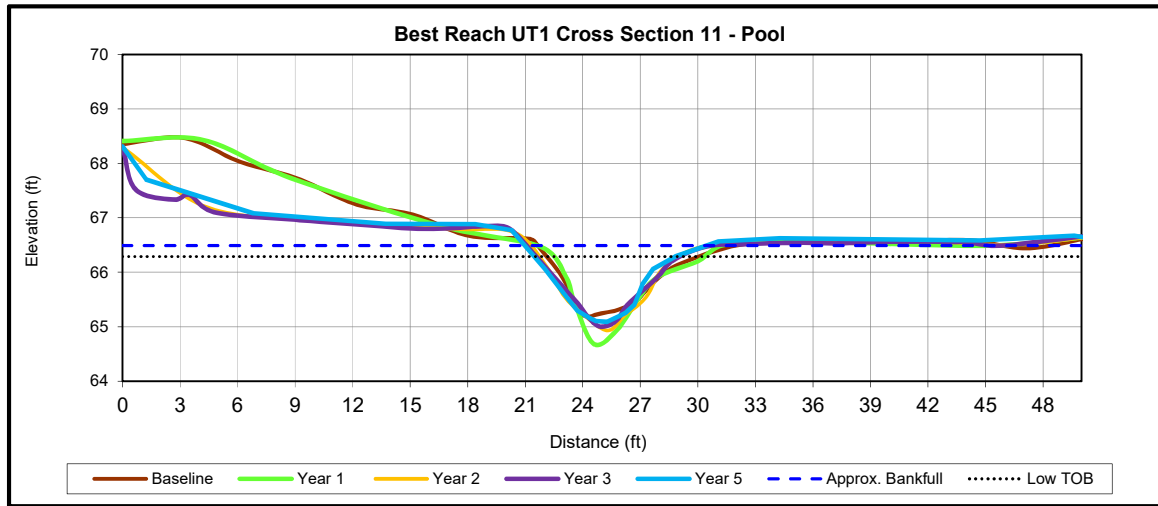

Dimension	Cross Section 11 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	66.5	66.5	66.5	66.5	66.5		
Bankfull Width (ft) ¹	10.4	10.0	10.6	10.6	9.5		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.2		
Bankfull Mean Depth (ft)	0.6	0.8	0.7	0.7	-		
Bankfull Max Depth (ft) ²	1.3	1.8	1.6	1.5	1.2		
Low Bank Elevation (ft)	-	-	-	-	66.3		
Bankfull Cross Sectional Area (ft ²) ²	6.7	7.6	7.4	6.9	5.0		
Bankfull Width/Depth Ratio	16.0	13.2	15.3	16.2	13.4		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

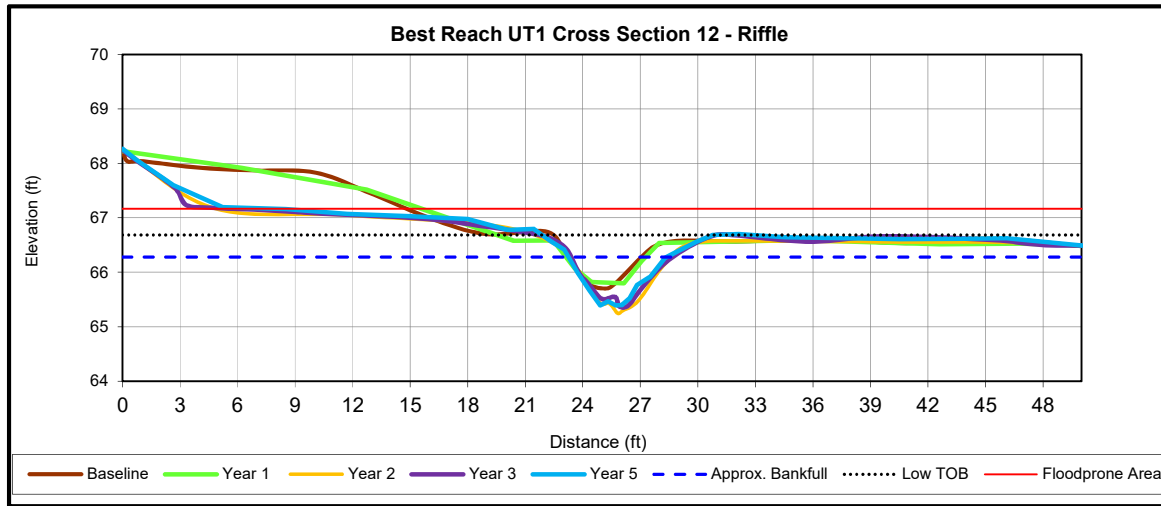

Dimension	Cross Section 12 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	66.6	66.6	66.6	66.6	66.3		
Bankfull Width (ft) ¹	6.5	5.5	7.9	7.6	5.1		
Floodprone Width (ft) ¹	37.0	37.0	37.0	37.0	42.4		
Bankfull Mean Depth (ft)	0.4	0.5	0.7	0.6	-		
Bankfull Max Depth (ft) ²	0.9	0.8	1.3	1.2	1.3		
Low Bank Elevation (ft)	-	-	-	-	66.7		
Bankfull Cross Sectional Area (ft ²) ²	2.8	2.9	5.2	4.7	5.5		
Bankfull Width/Depth Ratio	15.1	10.7	12.0	12.5	9.4		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	8.3		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.5		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

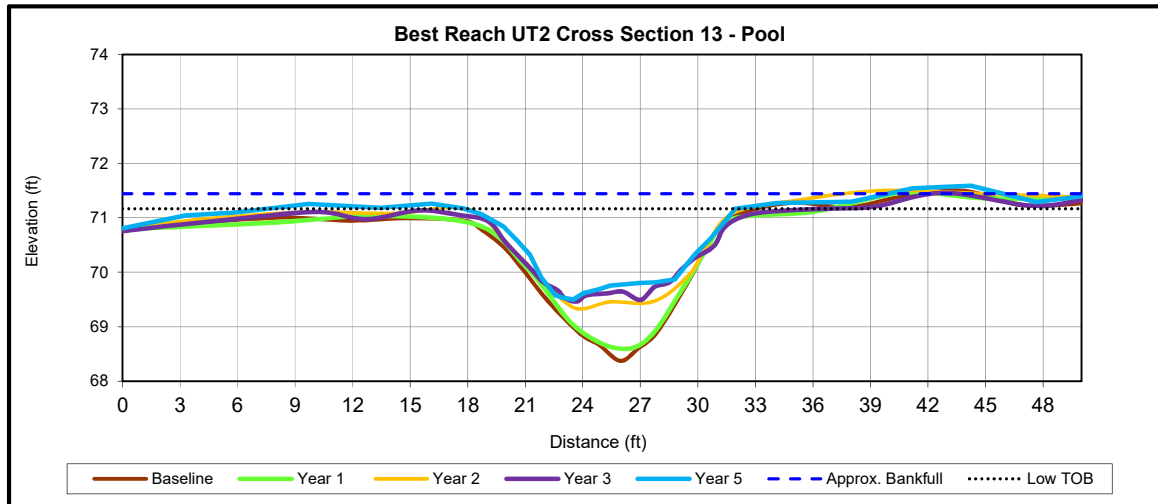

Dimension	Cross Section 13 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	71.0	71.0	71.0	71.0	71.4		
Bankfull Width (ft) ¹	13.7	13.1	12.8	13.2	18.0		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	1.4	1.3	1.0	0.9	-		
Bankfull Max Depth (ft) ²	2.6	2.3	1.6	1.5	1.7		
Low Bank Elevation (ft)	-	-	-	-	71.2		
Bankfull Cross Sectional Area (ft ²) ²	18.6	17.6	13.4	12.4	13.8		
Bankfull Width/Depth Ratio	10.1	9.0	12.3	14.0	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

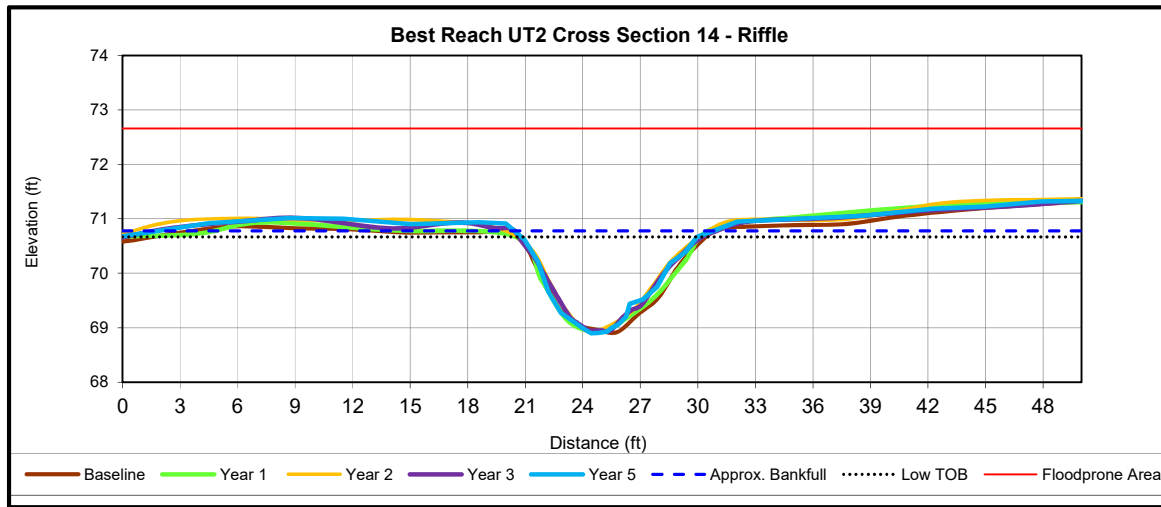

Dimension	Cross Section 14 (Run/Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	70.7	70.7	70.7	70.7	70.8		
Bankfull Width (ft) ¹	10.0	10.0	9.9	9.7	10.4		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	1.1	1.1	0.9	1.0	-		
Bankfull Max Depth (ft) ²	1.7	1.7	1.7	1.7	1.8		
Low Bank Elevation (ft)	-	-	-	-	70.7		
Bankfull Cross Sectional Area (ft ²) ²	10.7	10.6	9.1	9.5	9.6		
Bankfull Width/Depth Ratio	9.3	9.6	10.7	9.9	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4.8		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

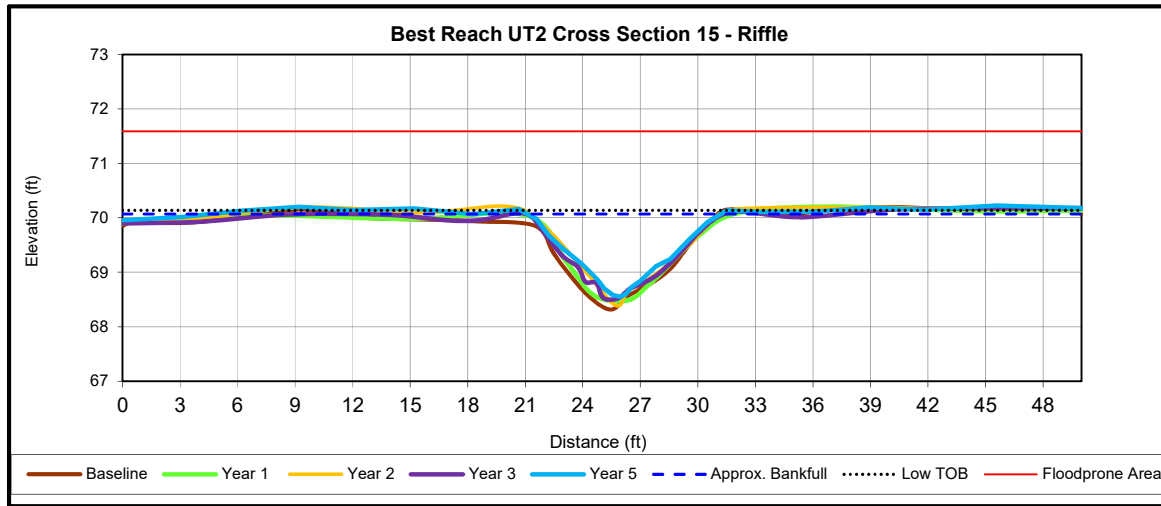

Dimension	Cross Section 15 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.9	69.9	69.9	69.9	70.1		
Bankfull Width (ft) ¹	9.0	9.4	8.6	8.7	10.1		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	0.9	0.8	0.7	0.8	-		
Bankfull Max Depth (ft) ²	1.5	1.4	1.5	1.3	1.6		
Low Bank Elevation (ft)	-	-	-	-	70.1		
Bankfull Cross Sectional Area (ft ²) ²	7.8	7.3	6.3	6.6	8.6		
Bankfull Width/Depth Ratio	10.3	12.0	11.7	11.5	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>5		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.1	1.0		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

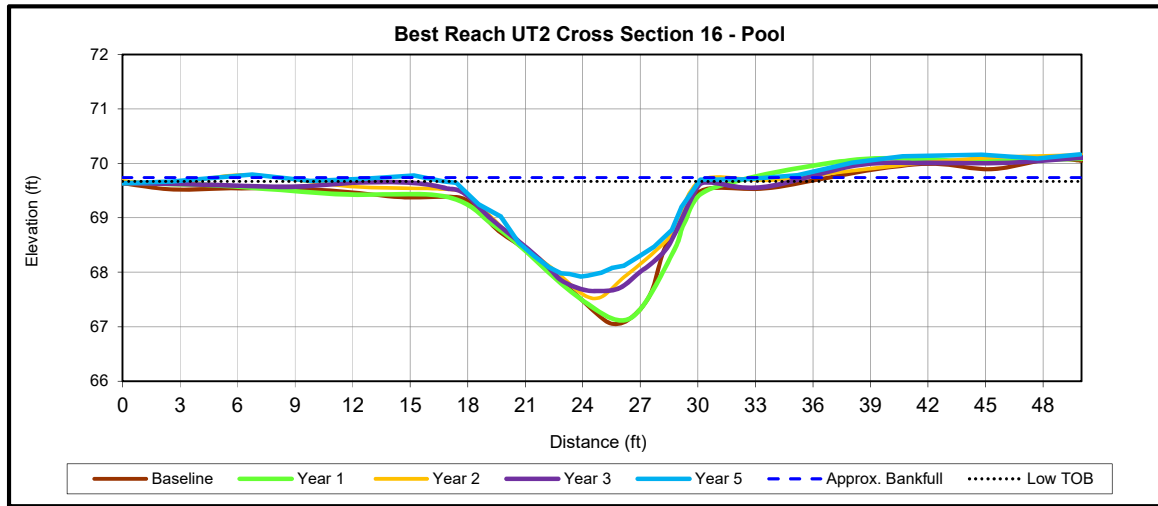

Dimension	Cross Section 16 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.4	69.4	69.4	69.4	69.7		
Bankfull Width (ft) ¹	12.4	13.3	12.0	12.6	15.2		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	1.2	1.2	1.1	1.1	-		
Bankfull Max Depth (ft) ²	2.3	2.2	2.0	1.8	1.7		
Low Bank Elevation (ft)	-	-	-	-	69.7		
Bankfull Cross Sectional Area (ft ²) ²	15.1	15.7	13.4	14.1	14.1		
Bankfull Width/Depth Ratio	10.2	11.3	10.7	11.2	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

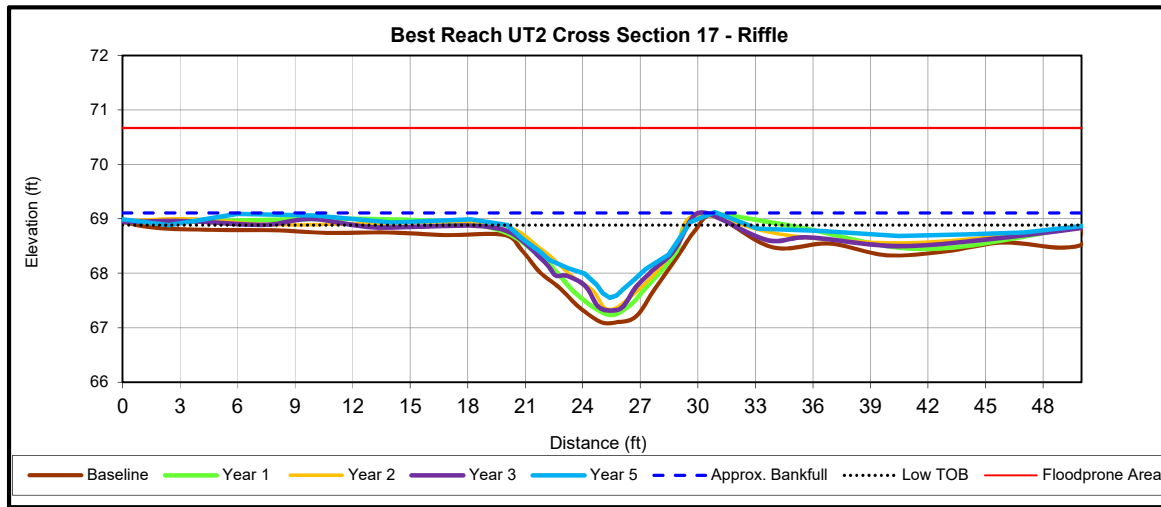

Dimension	Cross Section 17 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	68.7	68.7	68.7	68.7	69.1		
Bankfull Width (ft) ¹	9.8	9.6	10.2	9.1	12.6		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	0.9	0.8	0.8	0.8	-		
Bankfull Max Depth (ft) ²	1.6	1.5	1.5	1.4	1.3		
Low Bank Elevation (ft)	-	-	-	-	68.9		
Bankfull Cross Sectional Area (ft ²) ²	9.3	7.5	8.0	6.9	6.8		
Bankfull Width/Depth Ratio	10.3	12.3	12.9	12.0	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

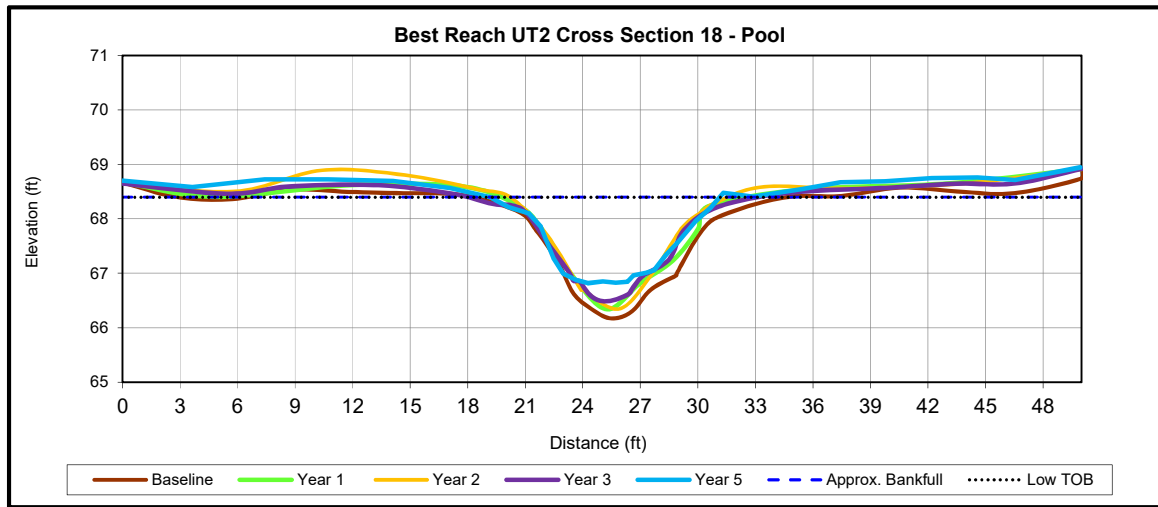

Dimension	Cross Section 18 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	68.1	68.1	68.1	68.1	68.4		
Bankfull Width (ft) ¹	10.4	9.2	11.6	10.8	12.0		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50		
Bankfull Mean Depth (ft)	1.1	1.0	1.0	0.9	-		
Bankfull Max Depth (ft) ²	1.9	1.7	2.1	1.7	1.6		
Low Bank Elevation (ft)	-	-	-	-	68.4		
Bankfull Cross Sectional Area (ft ²) ²	11.2	8.8	11.6	10.2	11.1		
Bankfull Width/Depth Ratio	9.7	9.6	11.5	11.6	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

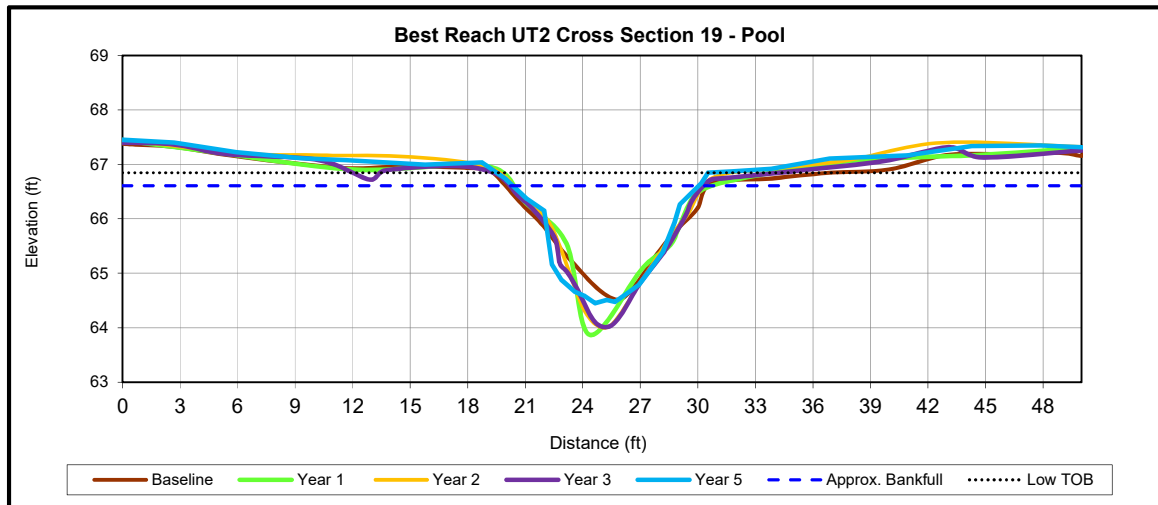

Dimension	Cross Section 19 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	66.7	66.7	66.7	66.7	66.6		
Bankfull Width (ft) ¹	10.8	11.4	10.7	10.8	9.7		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.1		
Bankfull Mean Depth (ft)	1.2	1.1	1.3	1.3	-		
Bankfull Max Depth (ft) ²	2.1	2.8	2.7	2.7	2.4		
Low Bank Elevation (ft)	-	-	-	-	66.8		
Bankfull Cross Sectional Area (ft ²) ²	12.5	11.4	14.1	14.4	14.9		
Bankfull Width/Depth Ratio	9.4	10.0	8.2	8.0	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

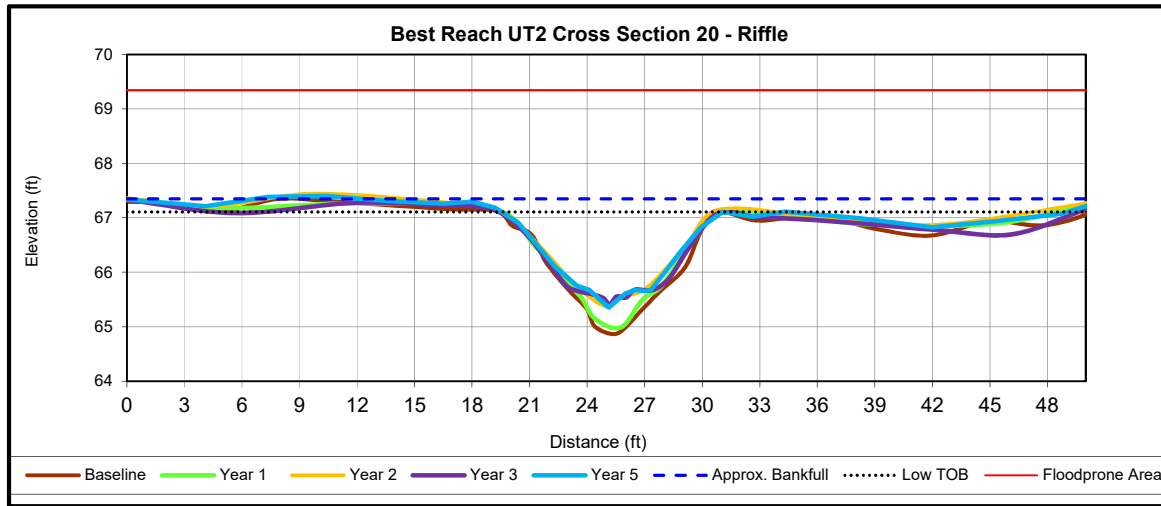

Dimension	Cross Section 20 (Run/Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bank full Elevation (ft) - Based on AB-XSA ¹	67.1	67.1	67.1	67.1	67.4		
Bankfull Width (ft) ¹	11.4	12.1	11.5	12.4	13.1		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.3		
Bankfull Mean Depth (ft)	1.2	1.1	1.0	0.9	-		
Bankfull Max Depth (ft) ²	2.3	2.1	1.8	1.7	1.8		
Low Bank Elevation (ft)	-	-	-	-	67.1		
Bankfull Cross Sectional Area (ft ²) ²	13.8	13.0	10.9	11.4	10.8		
Bankfull Width/Depth Ratio	9.4	11.2	12.0	13.4	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>3.9		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

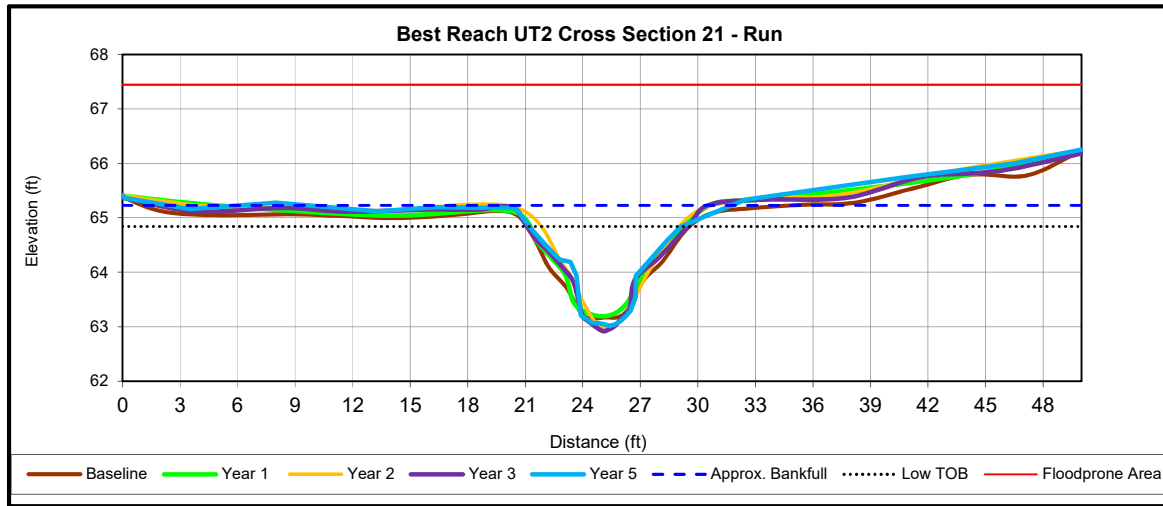

Dimension	Cross Section 21 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	65.1	65.1	65.1	65.1	65.2		
Bankfull Width (ft) ¹	10.9	10.0	9.3	9.7	11.2		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.0		
Bankfull Mean Depth (ft)	1.0	1.0	1.1	1.1	-		
Bankfull Max Depth (ft) ²	1.9	1.9	2.1	2.2	1.8		
Low Bank Elevation (ft)	-	-	-	-	64.8		
Bankfull Cross Sectional Area (ft ²) ²	11.1	10.0	10.0	10.4	7.3		
Bankfull Width/Depth Ratio	10.7	9.9	8.6	9.1	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4.4		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

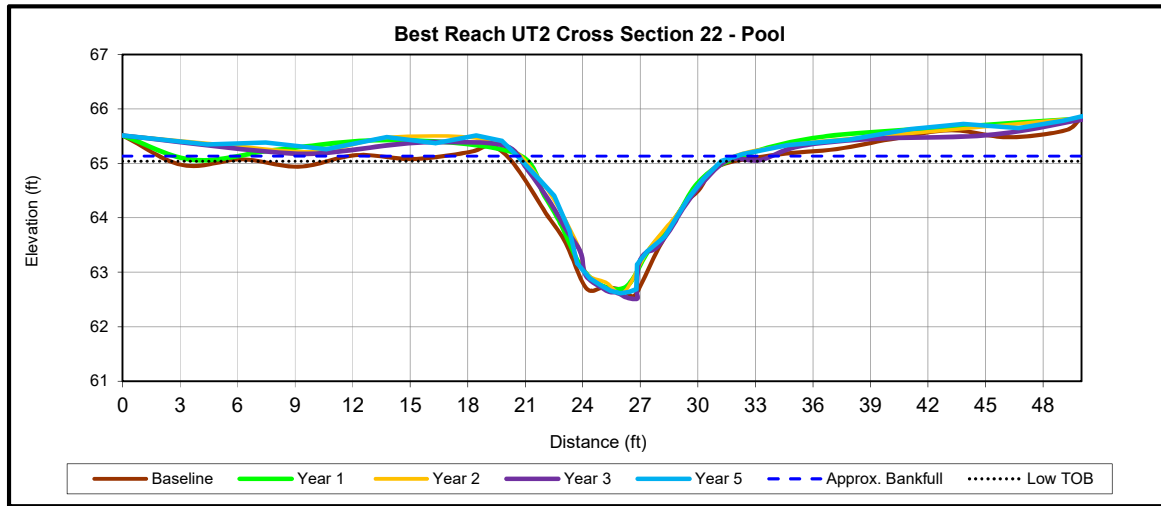

Dimension	Cross Section 22 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	65.0	65.0	65.0	65.0	65.1		
Bankfull Width (ft) ¹	10.7	10.5	10.4	10.6	11.5		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.1		
Bankfull Mean Depth (ft)	1.3	1.2	1.2	1.3	-		
Bankfull Max Depth (ft) ²	2.4	2.3	2.4	2.5	2.4		
Low Bank Elevation (ft)	-	-	-	-	65.0		
Bankfull Cross Sectional Area (ft ²) ²	14.2	12.4	12.4	13.3	13.2		
Bankfull Width/Depth Ratio	8.1	8.8	8.7	8.4	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

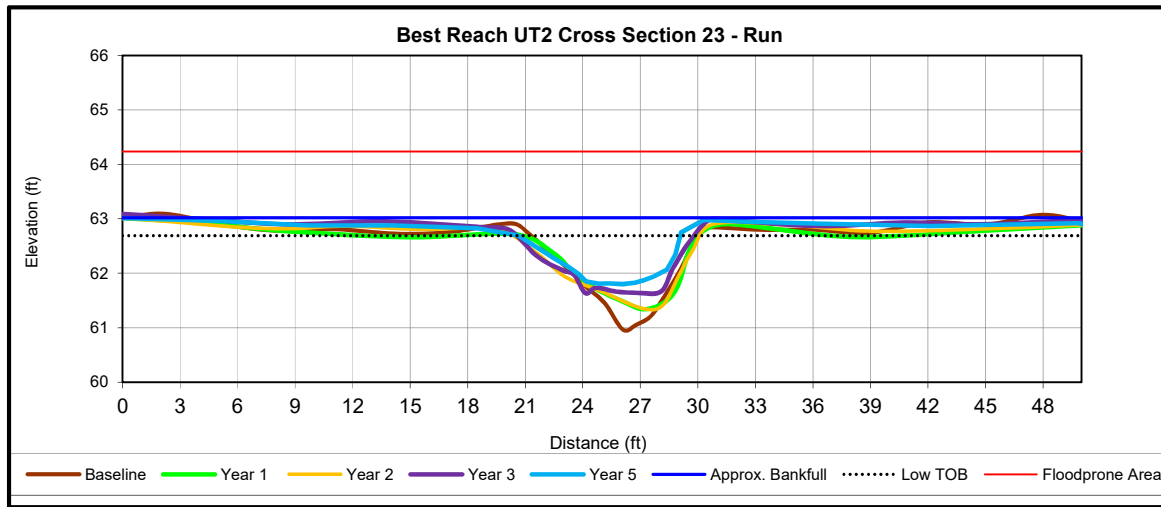

Dimension	Cross Section 23 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	62.8	62.8	62.8	62.8	63.0		
Bankfull Width (ft) ¹	9.1	10.3	11.1	10.0	11.8		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.2		
Bankfull Mean Depth (ft)	1.0	0.8	0.8	0.8	-		
Bankfull Max Depth (ft) ²	1.8	1.4	1.4	1.2	0.9		
Low Bank Elevation (ft)	-	-	-	-	62.7		
Bankfull Cross Sectional Area (ft ²) ²	8.7	8.1	9.1	7.7	5.2		
Bankfull Width/Depth Ratio	9.4	13.1	13.5	13.0	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4.3		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MYS, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

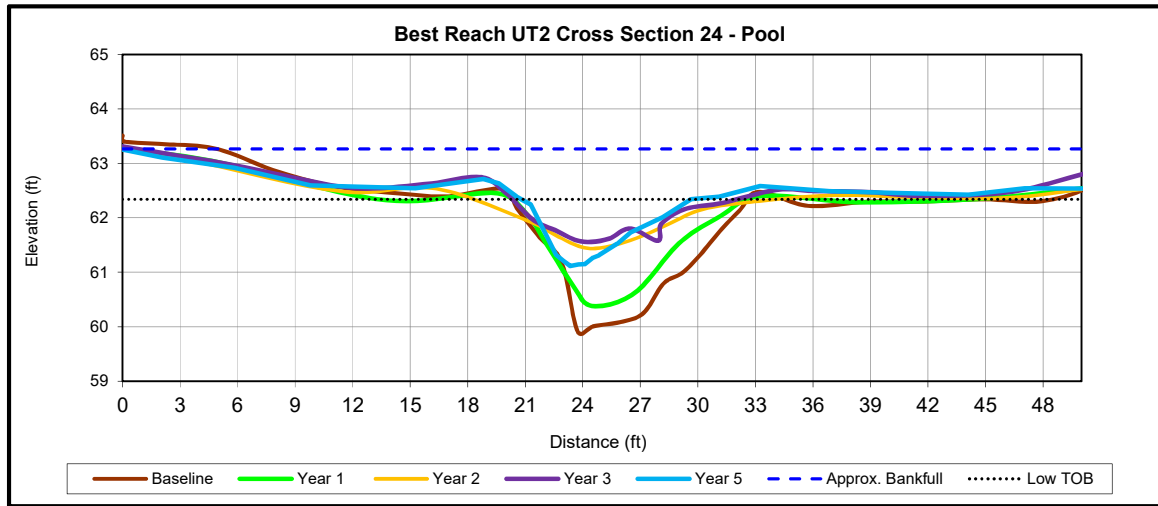

Dimension	Cross Section 24 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	62.5	62.5	62.5	62.5	63.3		
Bankfull Width (ft) ¹	13.2	13.8	19.0	14.1	14.4		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	50.3		
Bankfull Mean Depth (ft)	1.4	1.0	0.4	0.5	-		
Bankfull Max Depth (ft) ²	2.6	2.1	1.0	0.9	1.2		
Low Bank Elevation (ft)	-	-	-	-	62.3		
Bankfull Cross Sectional Area (ft ²) ²	18.3	14.4	7.7	7.2	5.7		
Bankfull Width/Depth Ratio	9.5	13.3	47.0	27.6	11.4		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

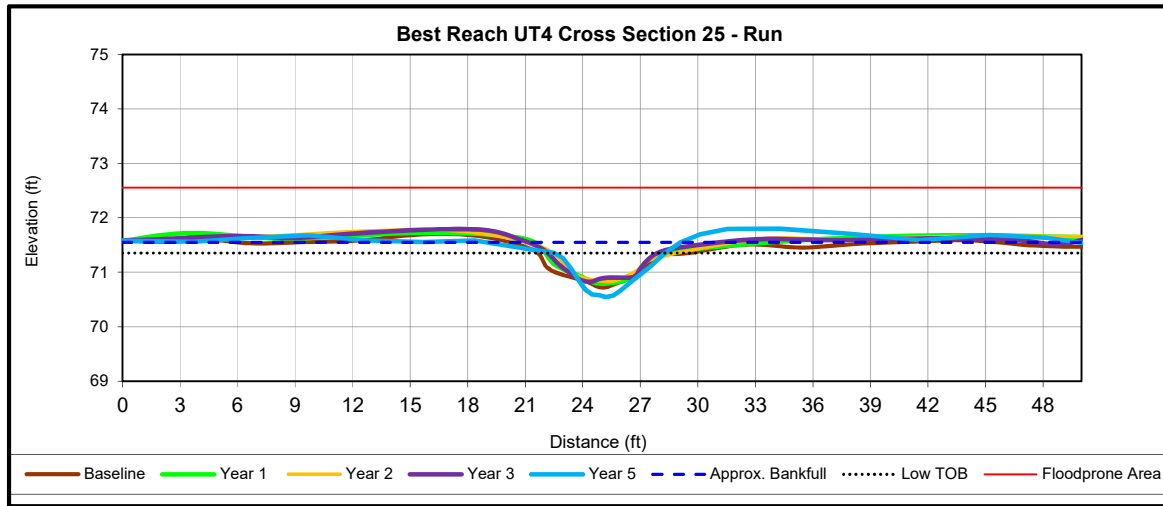

Dimension	Cross Section 25 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	71.5	71.5	71.5	71.5	71.6		
Bankfull Width (ft) ¹	12.2	11.5	13.1	12.1	10.6		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	>50.3		
Bankfull Mean Depth (ft)	0.3	0.3	0.3	0.3	-		
Bankfull Max Depth (ft) ²	0.8	0.7	0.8	0.8	0.8		
Low Bank Elevation (ft)	-	-	-	-	71.4		
Bankfull Cross Sectional Area (ft ²) ²	4.2	3.6	4.4	4.1	2.7		
Bankfull Width/Depth Ratio	35.5	36.6	39.0	36.1	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	>4.8		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	<1		


Note: Starting in MYS, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

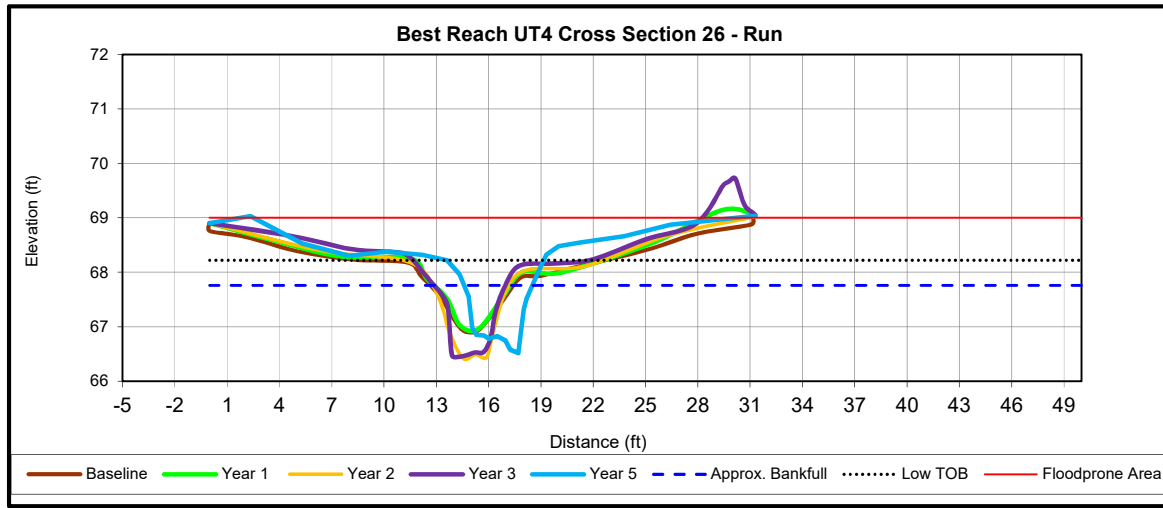

Dimension	Cross Section 26 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	67.9	67.9	67.9	67.9	67.8		
Bankfull Width (ft) ¹	5.6	5.3	6.1	5.7	3.9		
Floodprone Width (ft) ¹	50.0	50.0	50.0	50.0	25.4		
Bankfull Mean Depth (ft)	0.6	0.5	0.8	0.9	-		
Bankfull Max Depth (ft) ²	1.0	0.9	1.6	1.7	1.7		
Low Bank Elevation (ft)	-	-	-	-	68.2		
Bankfull Cross Sectional Area (ft ²) ²	3.1	2.7	5.1	5.1	5.3		
Bankfull Width/Depth Ratio	10.2	10.2	7.4	6.5	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	6.5		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0	1.4		


Note: Starting in MYS, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

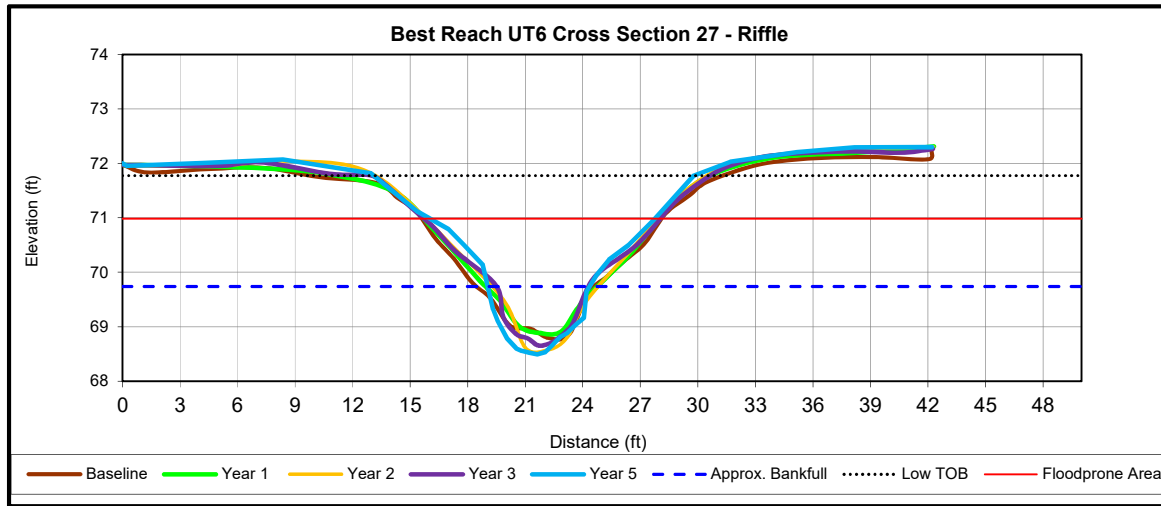

Dimension	Cross Section 27 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.9	69.9	69.9	69.9	69.7		
Bankfull Width (ft) ¹	7.2	6.7	6.5	5.7	5.3		
Floodprone Width (ft) ¹	50.0	50.0	50.0	13.2	11.7		
Bankfull Mean Depth (ft)	0.7	0.6	0.8	0.8	-		
Bankfull Max Depth (ft) ²	1.1	1.0	1.3	1.2	3.3		
Low Bank Elevation (ft)	-	-	-	-	71.8		
Bankfull Cross Sectional Area (ft ²) ²	4.7	4.1	4.9	4.5	25.9		
Bankfull Width/Depth Ratio	10.8	11.0	8.5	7.1	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	2.2		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	0.9	2.6		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

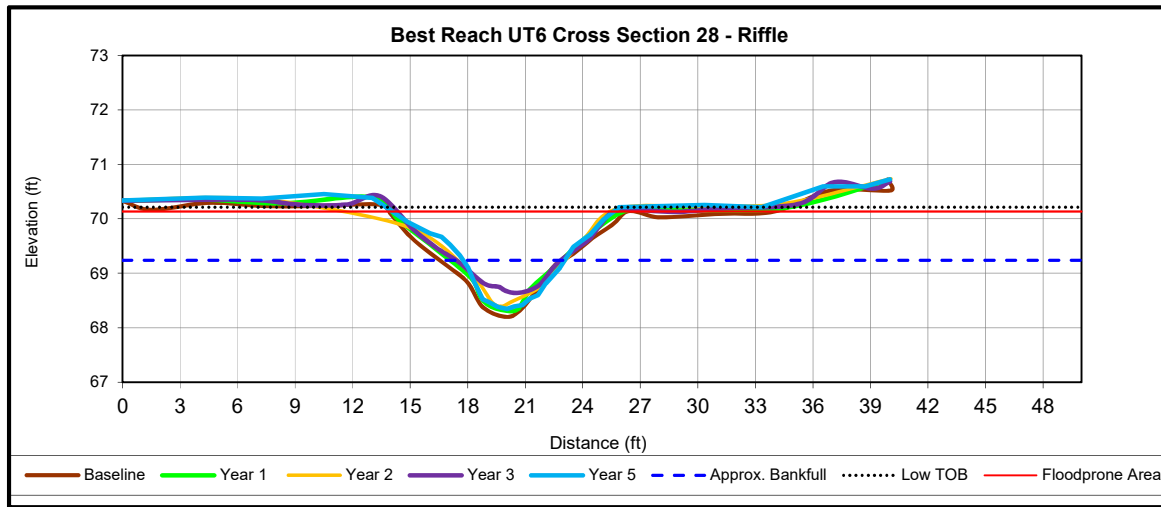

Dimension	Cross Section 28 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	69.2	69.2	69.2	69.2	69.2		
Bankfull Width (ft) ¹	5.7	5.3	5.6	5.2	5.3		
Floodprone Width (ft) ¹	50.0	15.0	16.8	9.3	11.5		
Bankfull Mean Depth (ft)	0.5	0.5	0.4	0.4	-		
Bankfull Max Depth (ft) ²	0.9	0.8	0.8	0.6	1.9		
Low Bank Elevation (ft)	-	-	-	-	70.2		
Bankfull Cross Sectional Area (ft ²) ²	3.1	2.4	2.5	1.9	11.2		
Bankfull Width/Depth Ratio	10.4	11.4	12.5	14.5	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	1.8	2.2		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	2.7	2.1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

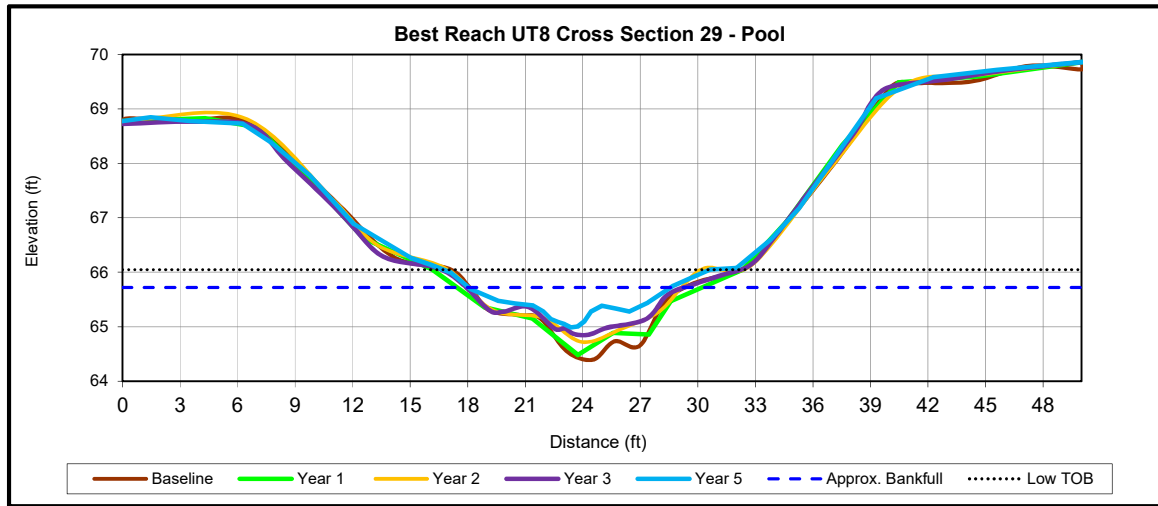

Dimension	Cross Section 29 (Pool)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	65.3	65.3	65.3	65.3	65.7		
Bankfull Width (ft) ¹	8.7	3.3	8.3	6.3	10.5		
Floodprone Width (ft) ¹	50.0	20.0	13.7	15.8	19.6		
Bankfull Mean Depth (ft)	0.4	0.4	0.3	0.3	-		
Bankfull Max Depth (ft) ²	0.9	0.8	0.6	0.4	1.1		
Low Bank Elevation (ft)	-	-	-	-	66.0		
Bankfull Cross Sectional Area (ft ²) ²	3.8	3.3	2.1	1.8	7.7		
Bankfull Width/Depth Ratio	19.9	22.1	32.7	22.4	-		
Bankfull Entrenchment Ratio ¹	>2.2	1.9	1.6	N/A	N/A		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	N/A	N/A		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

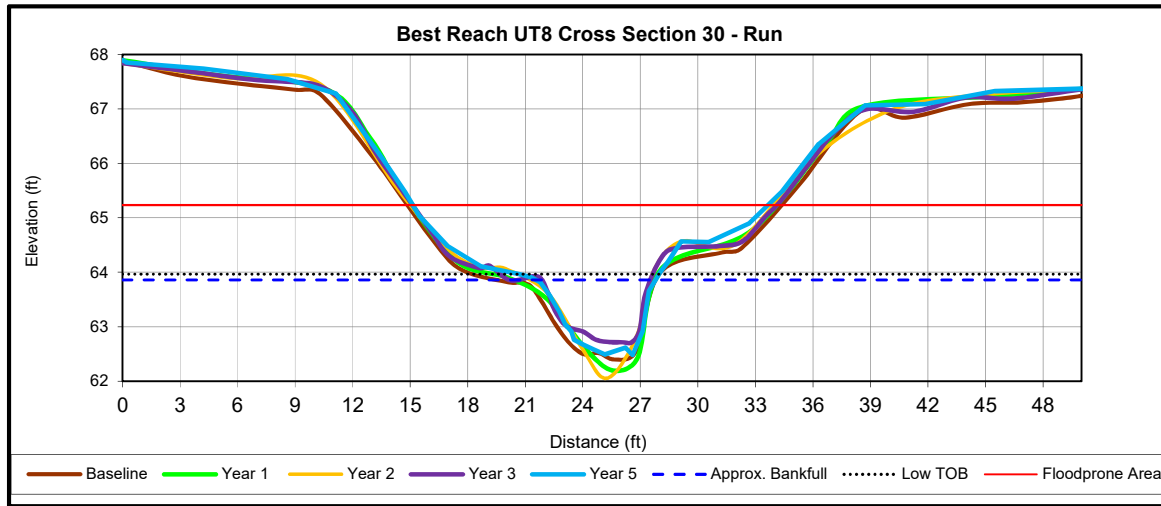

Dimension	Cross Section 30 (Run)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	63.7	63.7	63.7	63.7	63.9		
Bankfull Width (ft) ¹	6.4	6.7	5.6	5.3	6.2		
Floodprone Width (ft) ¹	50.0	20.0	19.3	16.4	18.5		
Bankfull Mean Depth (ft)	0.9	0.8	0.9	0.7	-		
Bankfull Max Depth (ft) ²	1.3	1.5	1.6	1.0	1.5		
Low Bank Elevation (ft)	-	-	-	-	64.0		
Bankfull Cross Sectional Area (ft ²) ²	5.7	5.6	5.1	4.0	6.4		
Bankfull Width/Depth Ratio	7.1	7.9	6.3	7.2	-		
Bankfull Entrenchment Ratio ¹	>2.2	>2.2	>2.2	>2.2	3.0		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.2	1.1		


Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.



Upstream



Downstream

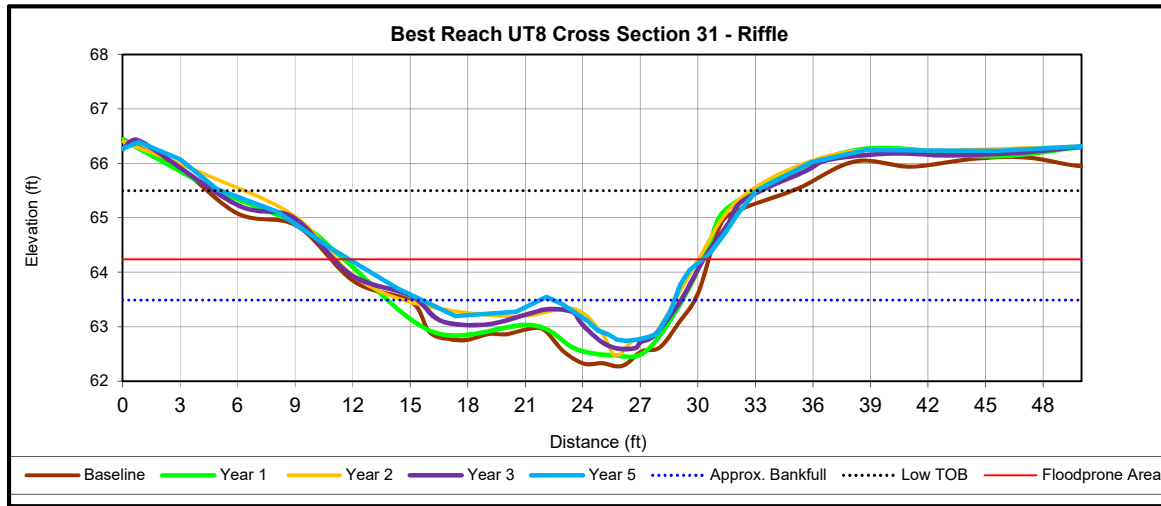

Dimension	Cross Section 31 (Riffle)						
	Base	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA ¹	63.0	63.0	63.0	63.0	63.5		
Bankfull Width (ft) ¹	7.7	8.5	3.4	4.0	6.3		
Floodprone Width (ft) ¹	50.0	15.0	14.2	13.4	18.4		
Bankfull Mean Depth (ft)	0.4	0.2	0.3	0.3	-		
Bankfull Max Depth (ft) ²	0.7	0.5	0.5	0.4	2.8		
Low Bank Elevation (ft)	-	-	-	-	65.5		
Bankfull Cross Sectional Area (ft ²) ²	3.0	2.1	0.9	1.1	20.5		
Bankfull Width/Depth Ratio	19.5	34.5	13.2	14.9	-		
Bankfull Entrenchment Ratio ¹	>2.2	1.7	>2.2	>2.2	2.9		
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.7	3.7		

Note: Starting in MY5, the parameters denoted with ¹ were calculated using the as-built cross sectional area as the basis for adjusting the bankfull elevation and the parameters denoted with ² were calculated using the current years low top of bank as the bankfull.

Appendix E

Hydrology Data

Table 13. Documentation of Geomorphologically Significant Flow Events

Crest Gauge	Flow Events	Maximum Consecutive Flow Days	Cumulative Flow Days
Crest Gauge 4 (HWV UT-4)			
MY4	1	282	282
MY5	1	270	270
MY6	7	135	228

Crest Gauge	Number of Bankfull Events	Maximum Bankfull Height (ft.)
Crest Gauge 1 (UT-1)		
MY1	2	0.3
MY2	2	0.5
MY3	6	0.25
MY4	7	0.95
MY5	1	0.14
MY6	11	0.8
Crest Gauge 2 (UT-2)		
MY1	11	1.3
MY2	18	1.95
MY3	22	1.19
MY4	21	2.91
MY5	16	1.42
MY6	25	1.46
Crest Gauge 3 (UT-3)		
MY1	2	0.8
MY2	4	0.6
MY3	9	0.55
MY4	12	3.03
MY5	2	0.83
MY6	NA	NA
Crest Gauge 5 (UT6)		
MY1	3	1.1
MY2	4	1.1
MY3	7	1.2
MY4	1	1.25
MY5	1	0.5
MY6	NA	NA
Crest Gauge 6 (UT8)		
MY1	8	1.9
MY2	7	2.2
MY3	13	2.15
MY4	16	3
MY5	18	1.8
MY6	12	1.03

NA = Not Available due to HOBO failure

Table 14. 2020 Rainfall Summary

Month	Average	Normal Limits		Williamsdale Station Precipitation
		30 Percent	70 Percent	
January	4.33	3.32	5.03	4.16
February	3.23	2.14	3.87	6.10
March	4.50	3.23	5.32	4.02
April	3.16	1.70	3.85	3.34
May	3.68	2.69	4.34	10.68
June	4.49	3.11	5.34	4.03
July	6.06	4.16	7.22	4.70
August	5.40	3.12	6.56	6.36
September	5.00	2.04	6.07	7.17
October	3.21	1.62	3.92	2.62
November	2.89	1.83	3.49	0.36
December	3.24	2.14	3.88	---
Total	49.19	31.10	58.89	53.54


Table 15a.

2020 Max Hydroperiod (Growing Season 17-Mar through 14-Nov, 242 days)					
Success Criterion 9% = 22 Consecutive Days					
Gauge	Consecutive		Cumulative		Occurrences
	Days	Percent of growing Season	Days	Percent of growing Season	
AW1	43	18	141	58	7
AW2	41	17	125	51	8
AW3	NA	NA	NA	NA	NA
AW4	108	44	179	74	5
AW5	115	47	191	79	4
AW6	44	18	158	65	8
AW7	20	8	107	44	17
AW8	56	23	154	63	8
AW9	42	17	143	59	10
RAW1	56	23	158	65	4
RAW2	26	11	107	44	17
RAW3	109	45	191	79	5


Appendix E. Hydrology Data

Gauge	MY1 - 2015		MY2 - 2016		MY3 - 2017		MY4 - 2018		MY5 - 2019		MY6 - 2020	
	Consecutive		Consecutive		Consecutive		Consecutive		Consecutive		Consecutive	
	Days	Percent of growing Season	Days	Percent of growing Season	Days	Percent of growing Season	Days	Percent of growing Season	Days	Percent of growing Season	Days	Percent of growing Season
AW1	49	20	53	22	53	22	57	23	43	18	43	18
AW2	18	7	18	7	49	20	46	19	31	13	41	17
AW3	88	36	99	41	118	49	105	43	53	22	NA	NA
AW4	88	36	97	40	117	48	106	44	52	21	108	44
AW5	51	21	103	43	120	49	58	24	54	22	115	47
AW6	28	12	42	17	55	23	47	19	42	17	44	18
AW7	22	9	17	7	13	5	31	13	9	4	20	8
AW8	24	10	32	13	16	7	46	19	42	17	56	23
AW9	24	10	18	7	14	6	36	15	31	13	42	17
RAW1	52	21	34	14	71	29	57	23	45	18	56	23
RAW2	46	19	10	4	24	10	34	14	31	13	26	11
RAW3	29	12	32	13	45	19	48	20	41	17	109	45

NA = Not Available due to HOBO failure




2020 Best Groundwater Gauge AW1

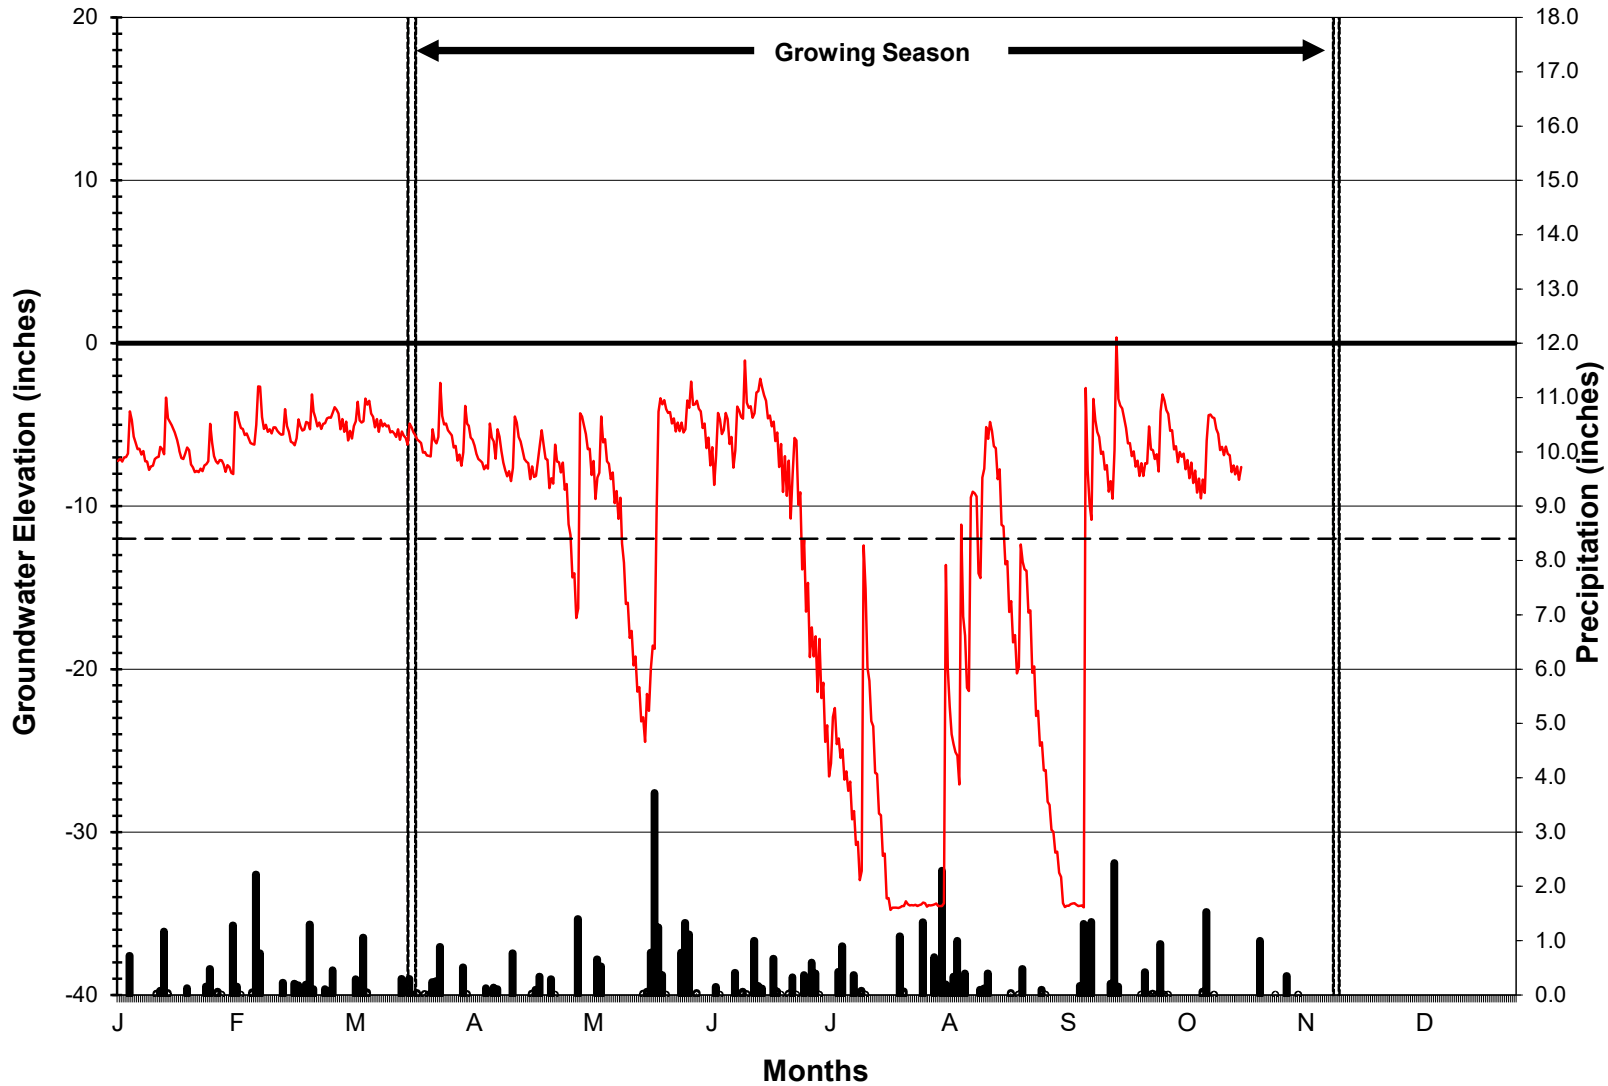


Williamsdale Daily Rainfall AW1

2020 Best Groundwater Gauge AW2

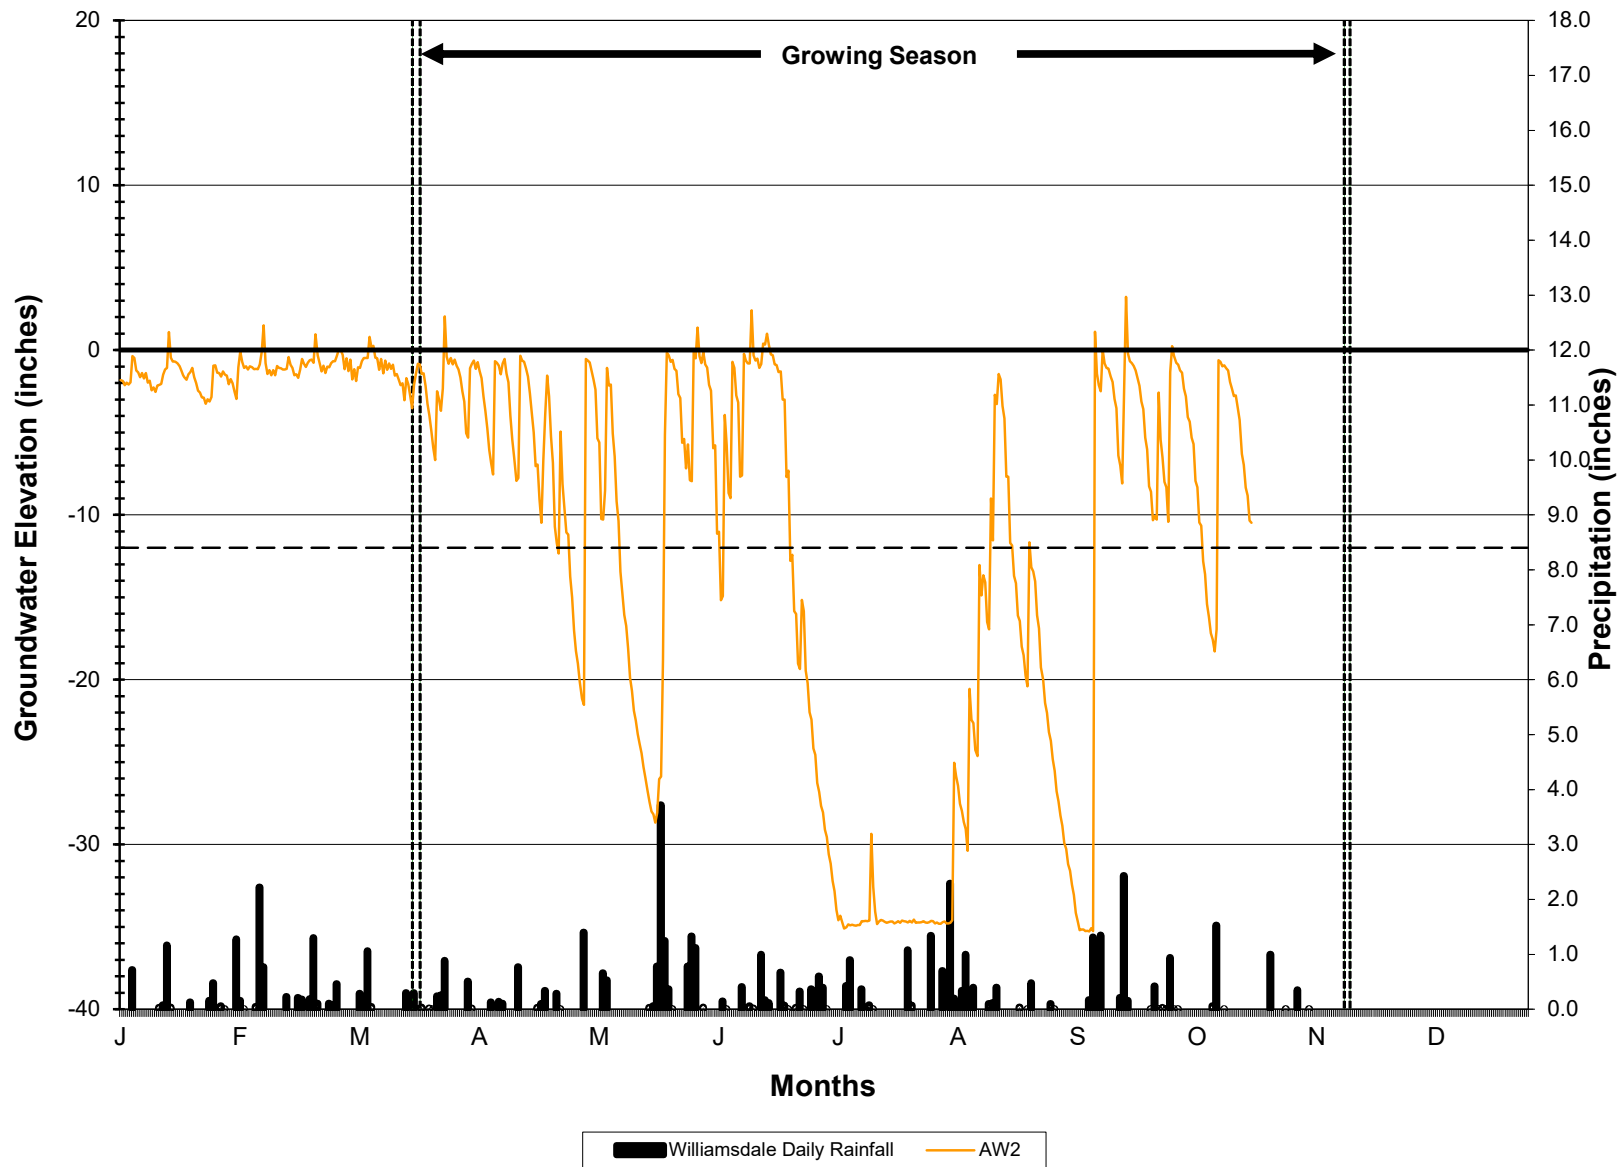


2020 Best Groundwater Gauge AW3 (HOBO failed MY6 2020)

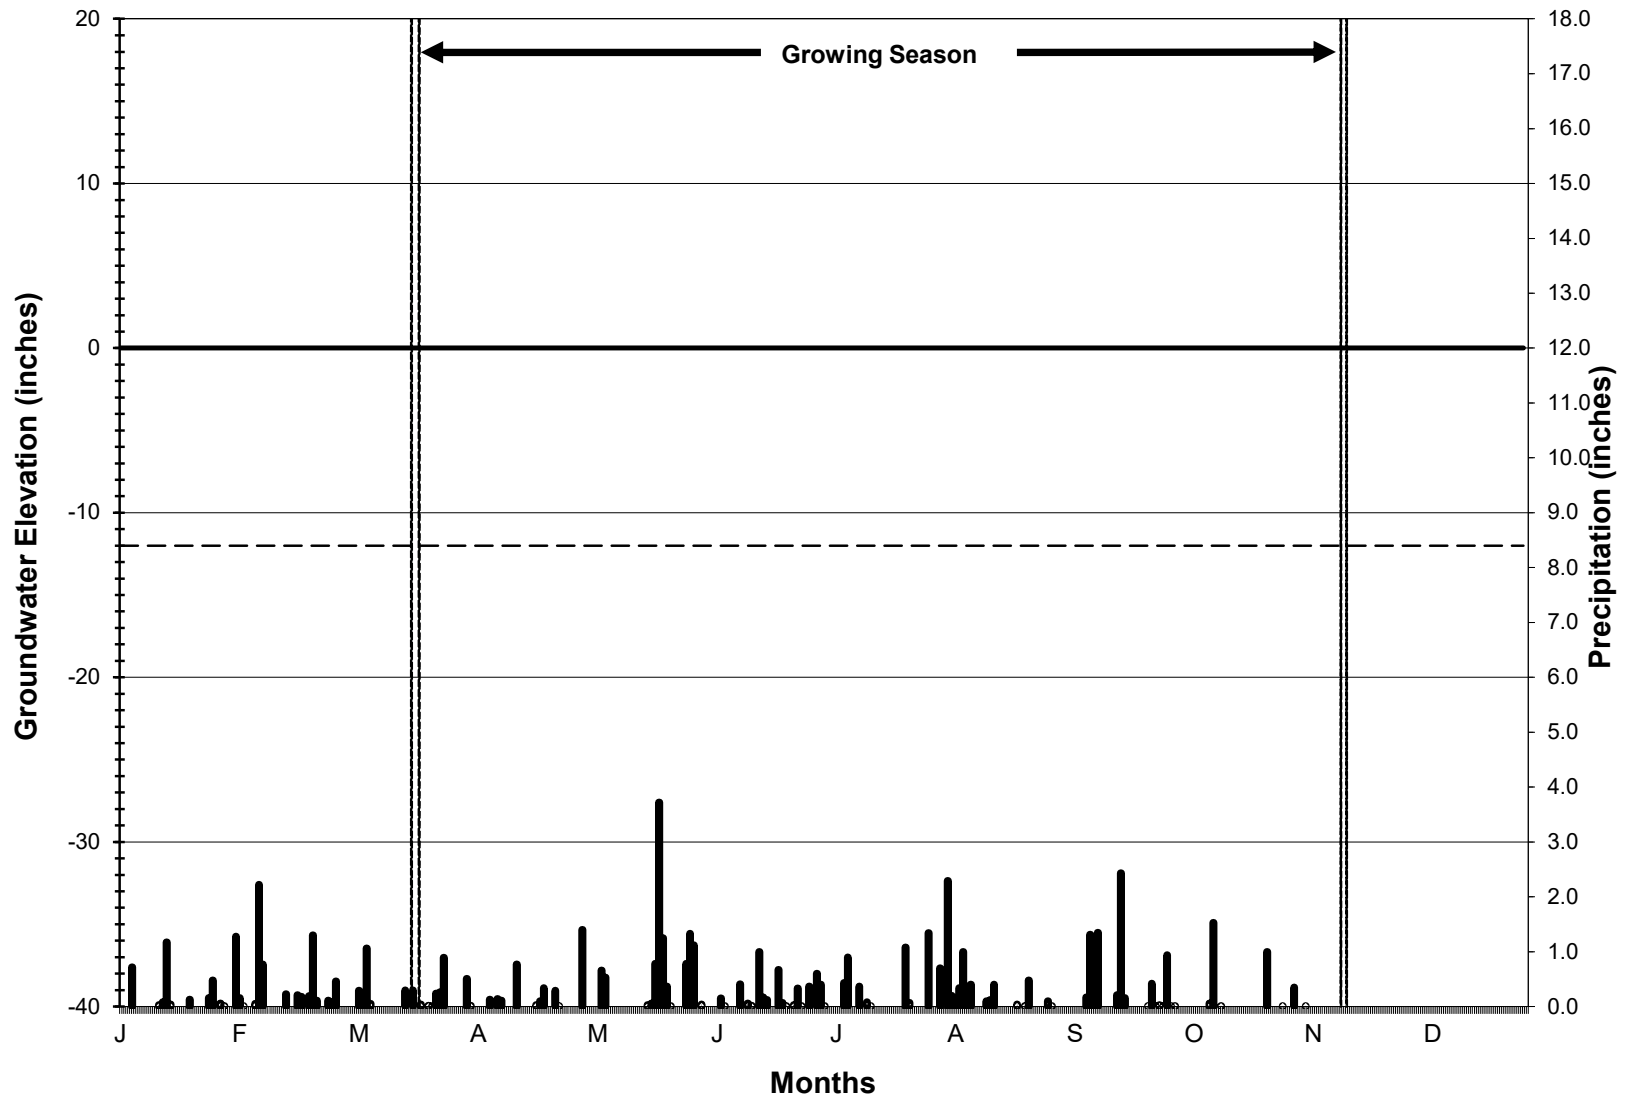


Williamsdale Daily Rainfall AW3

2020 Best Groundwater Gauge AW4

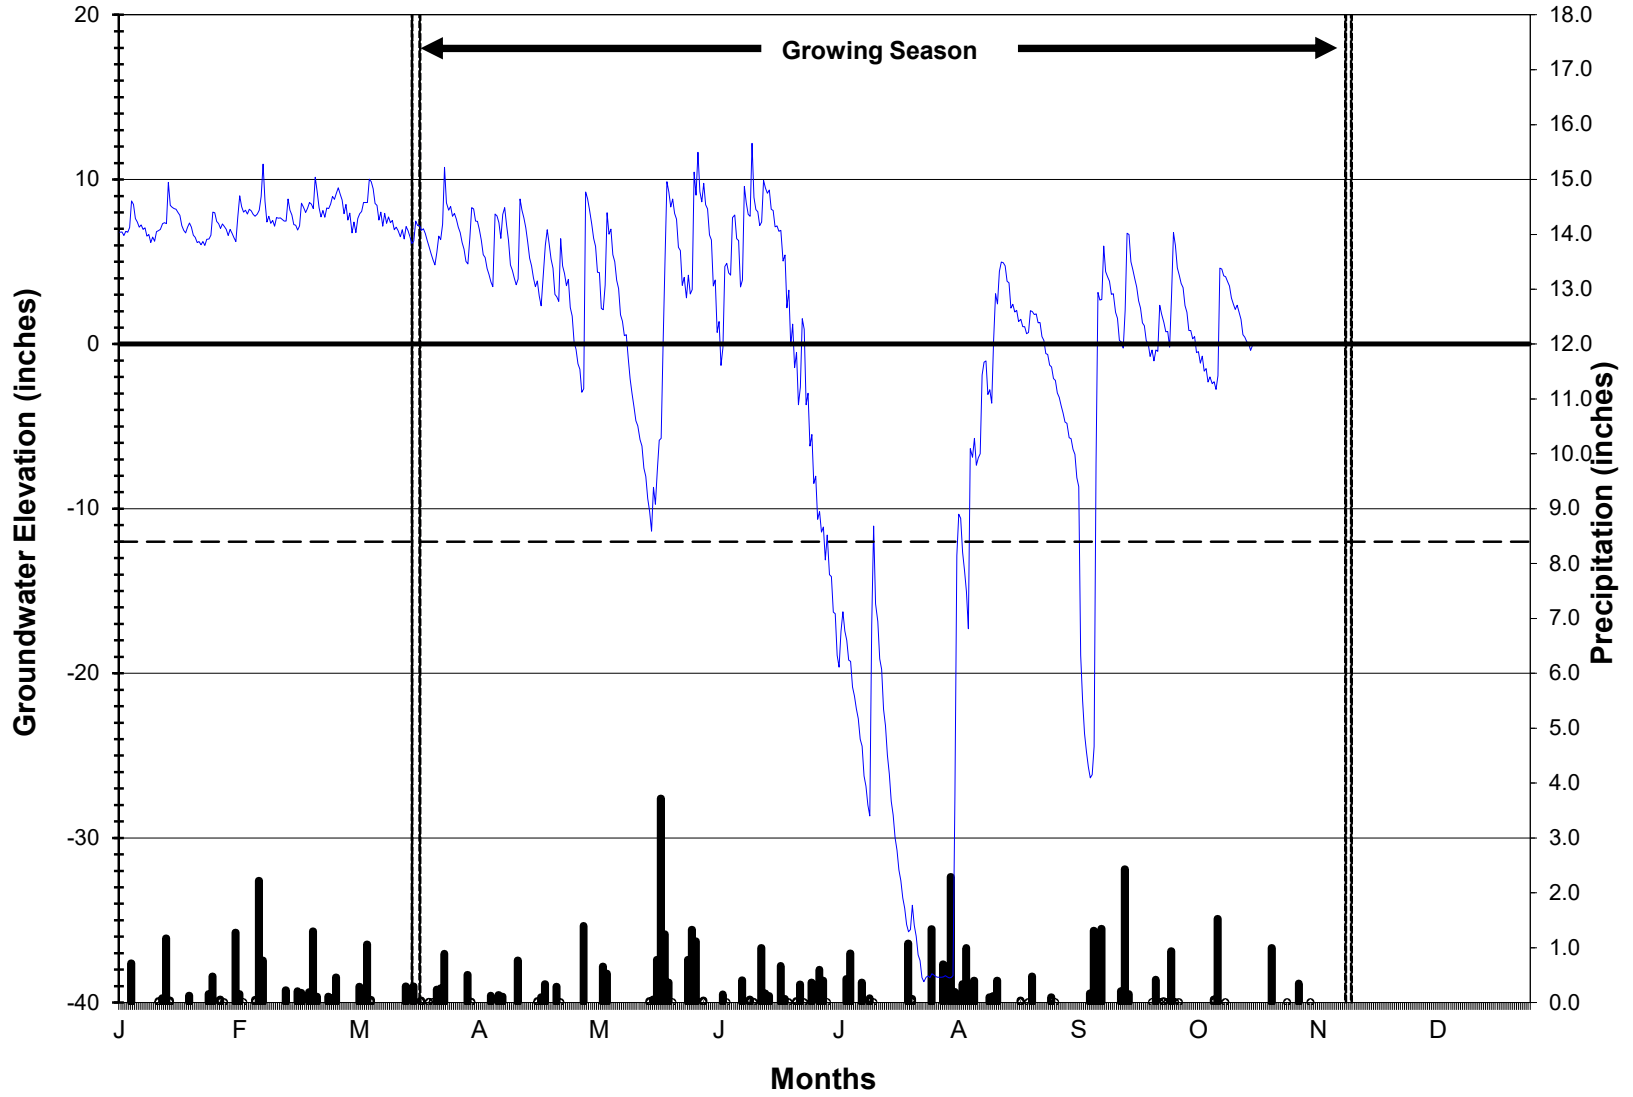


Williamsdale Daily Rainfall AW4


2020 Best Groundwater Gauge AW5

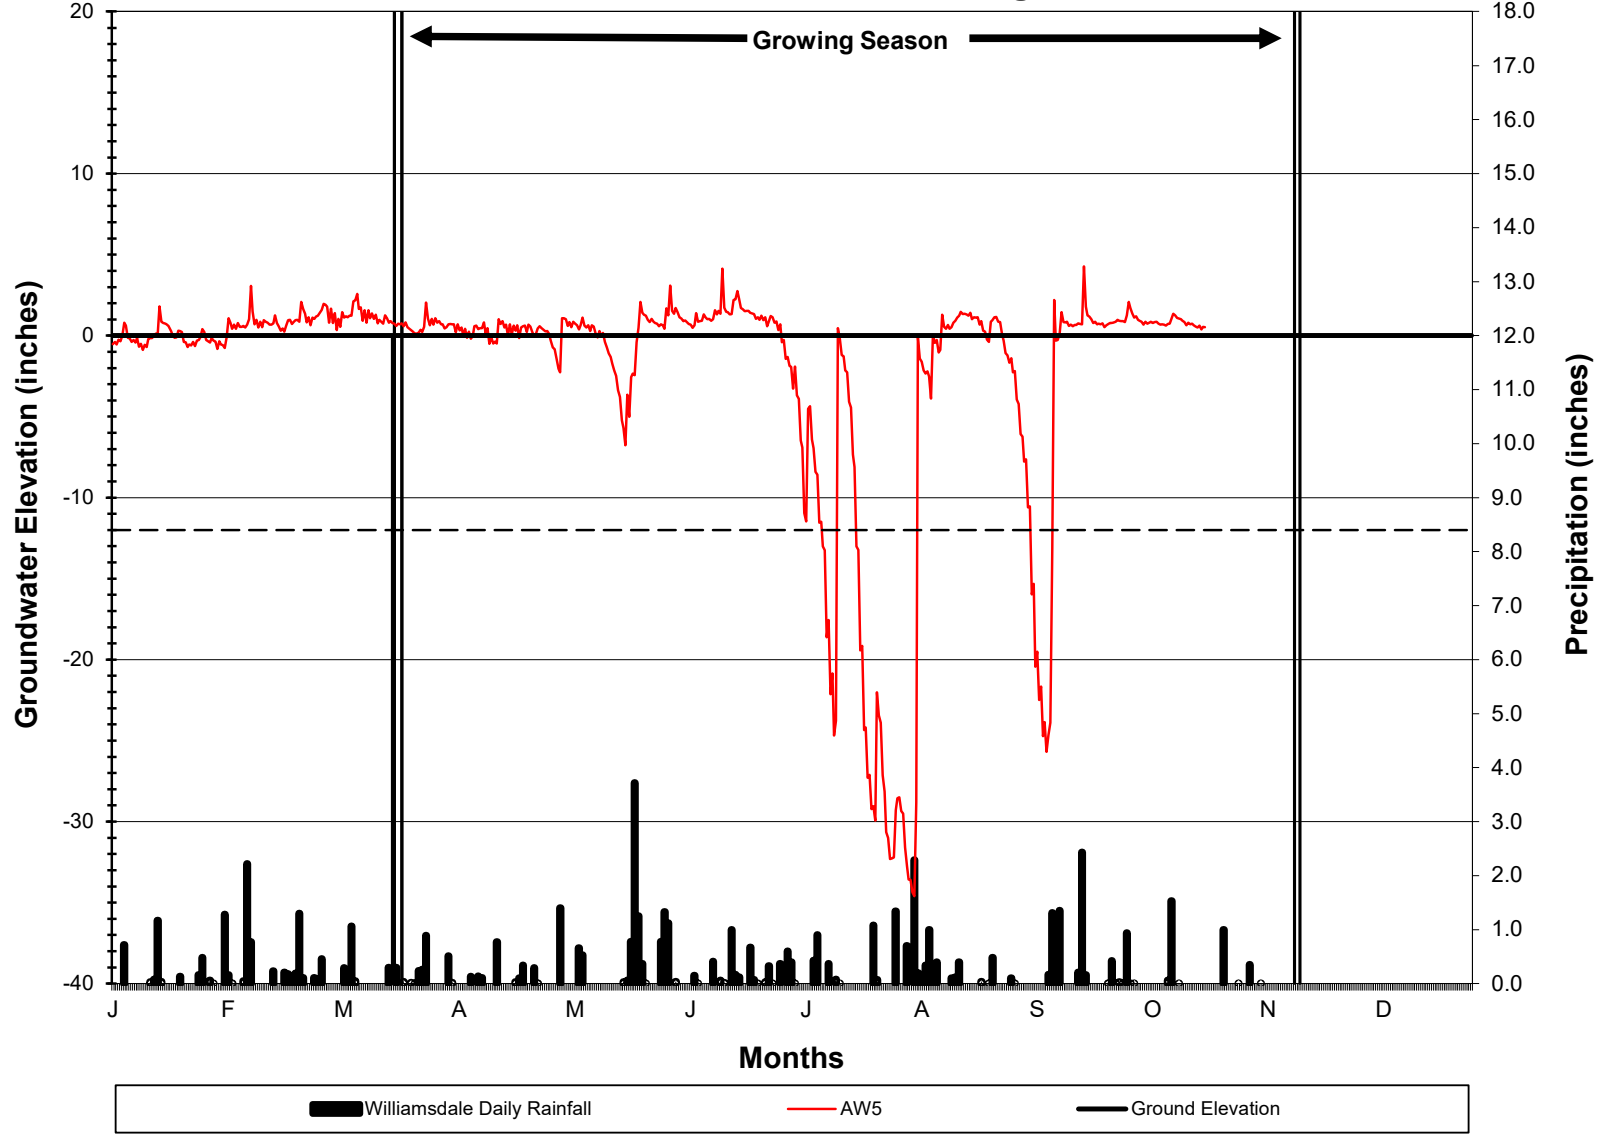


2020 Best Groundwater Gauge AW6

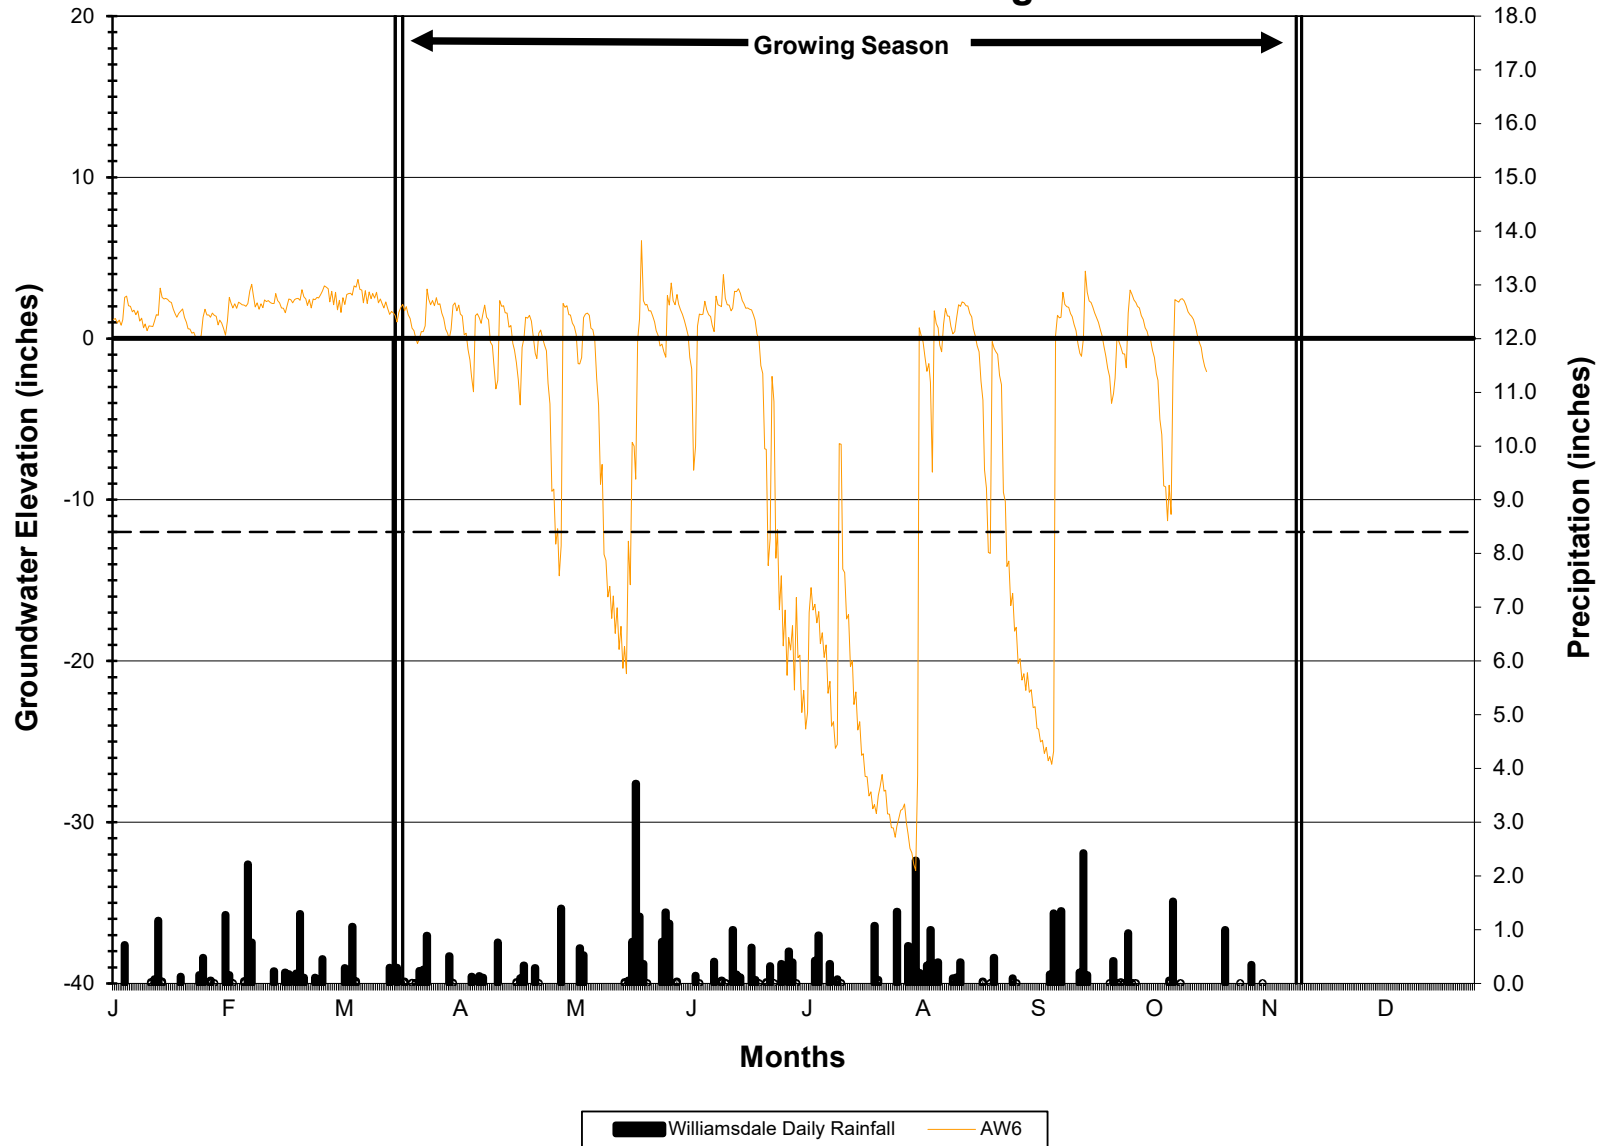

2020 Best Groundwater Gauge AW7

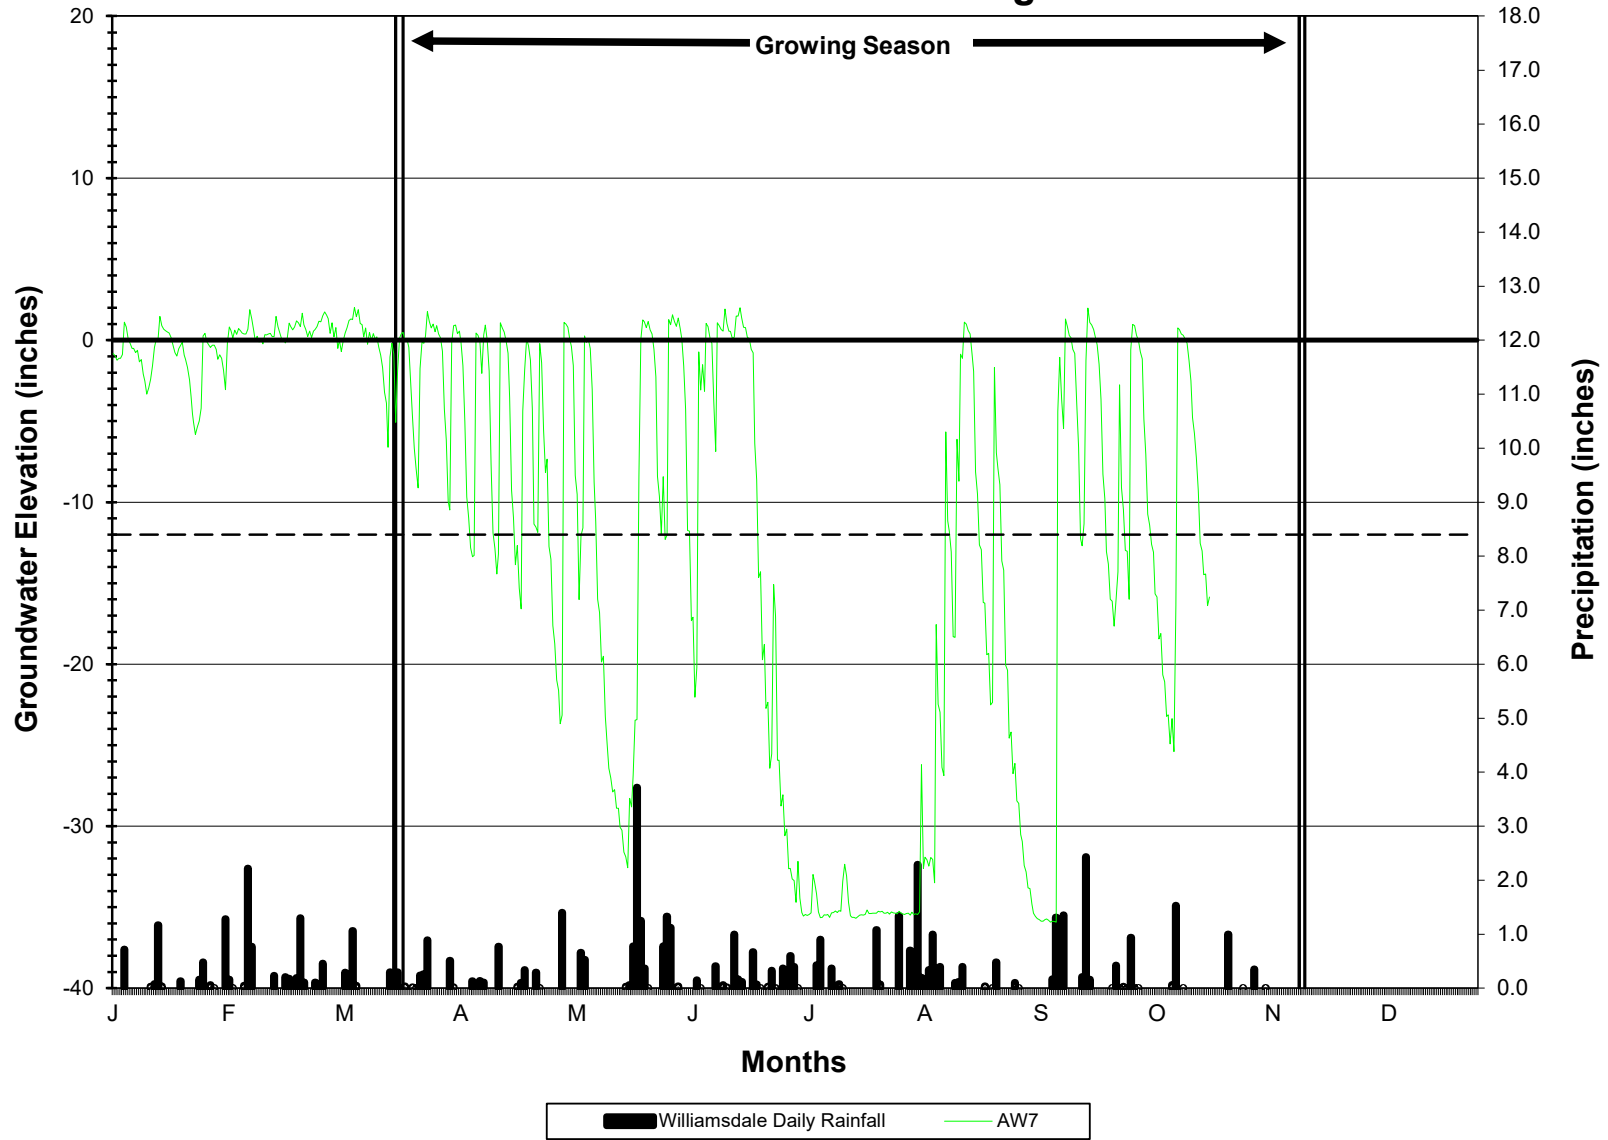


2020 Best Groundwater Gauge AW8

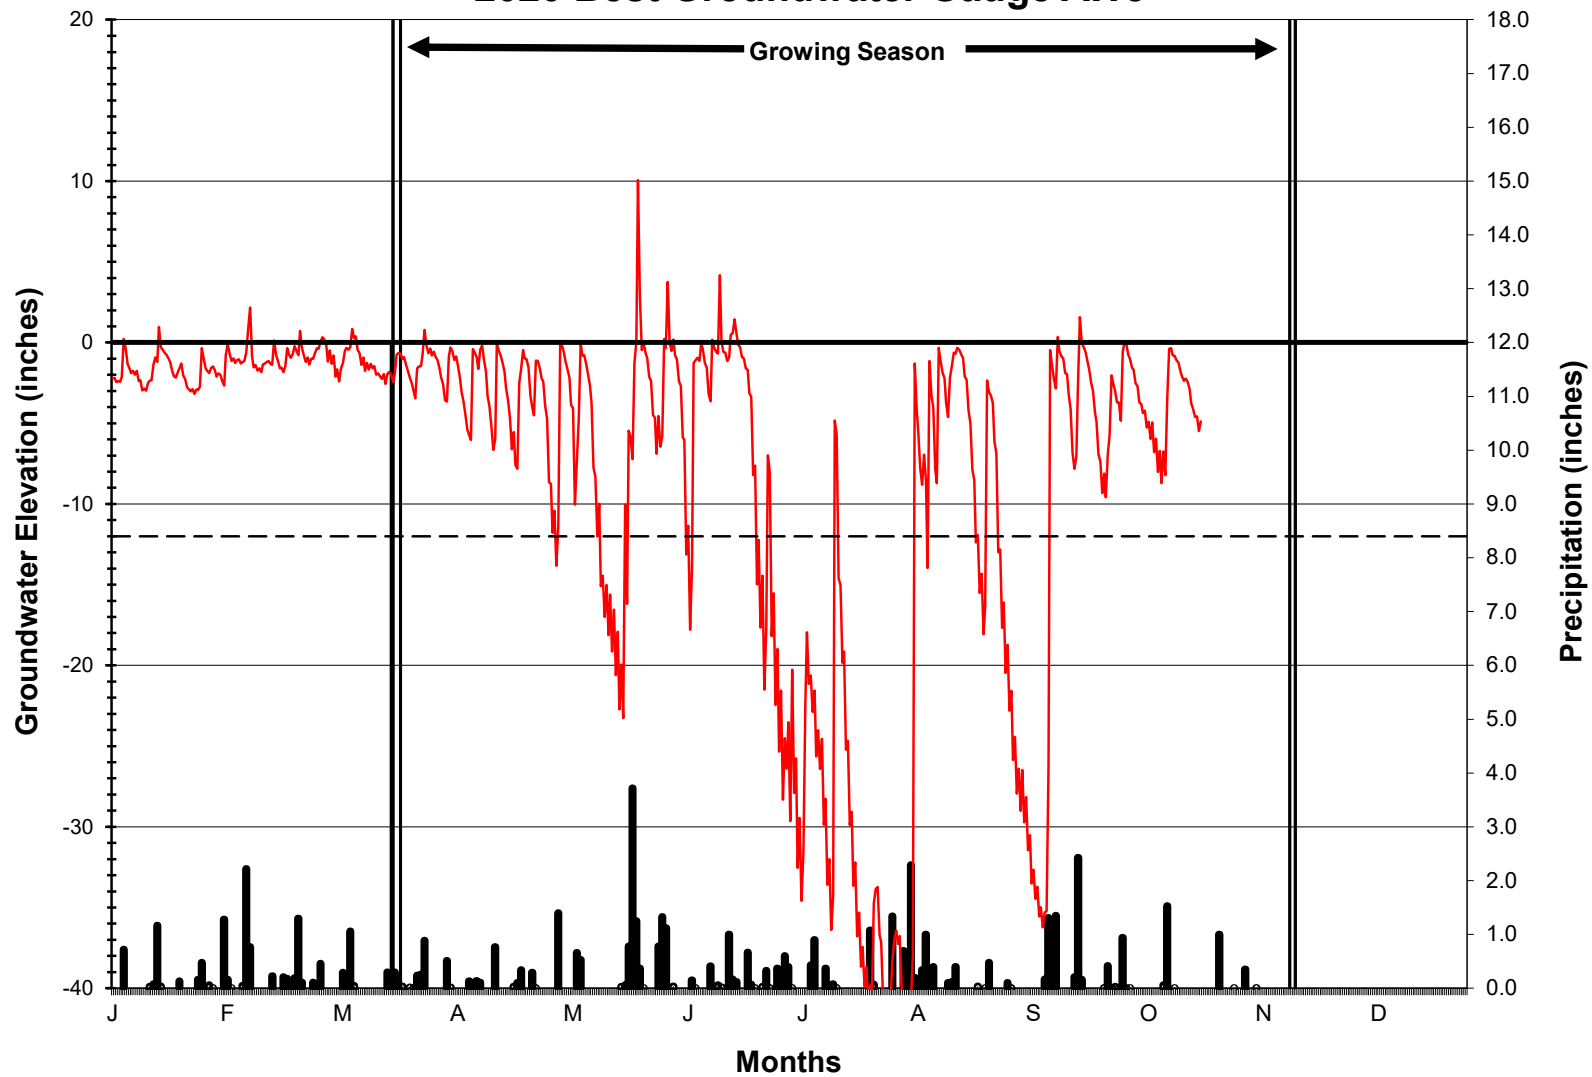


Williamsdale Daily Rainfall AW8


2020 Best Groundwater Gauge AW9

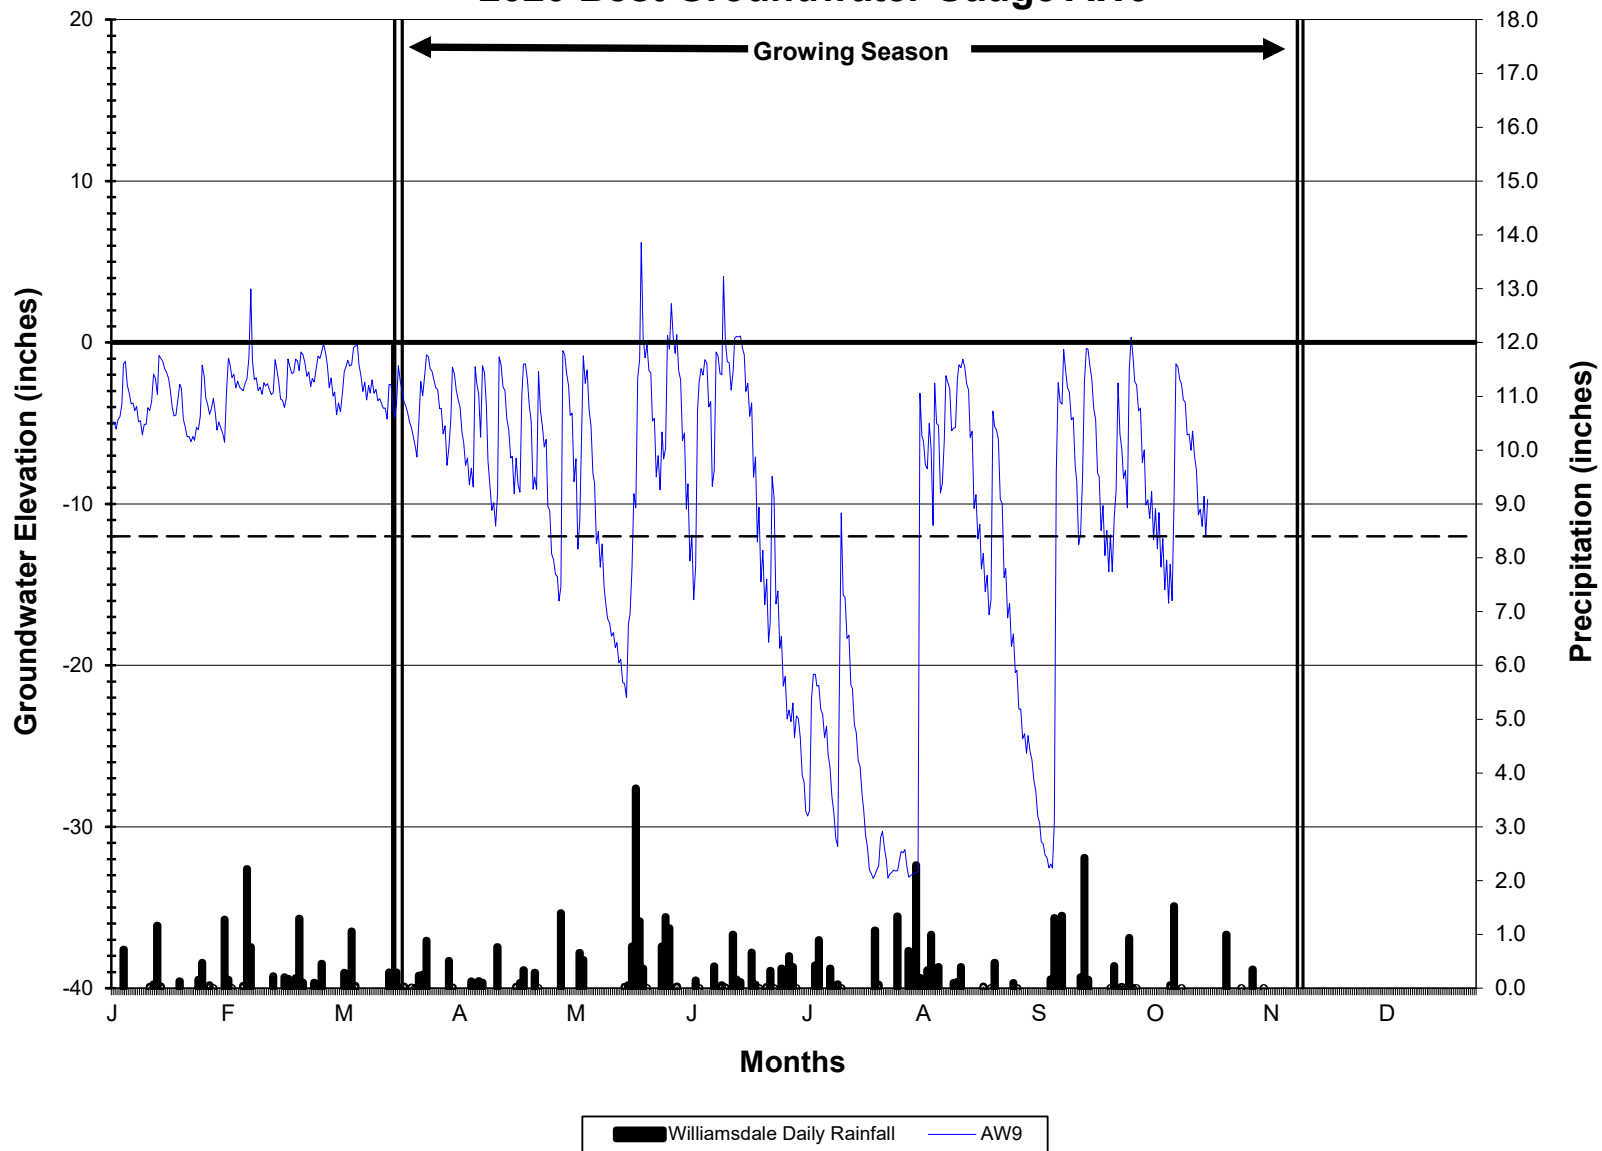


2020 Best Groundwater Gauge REFAW1

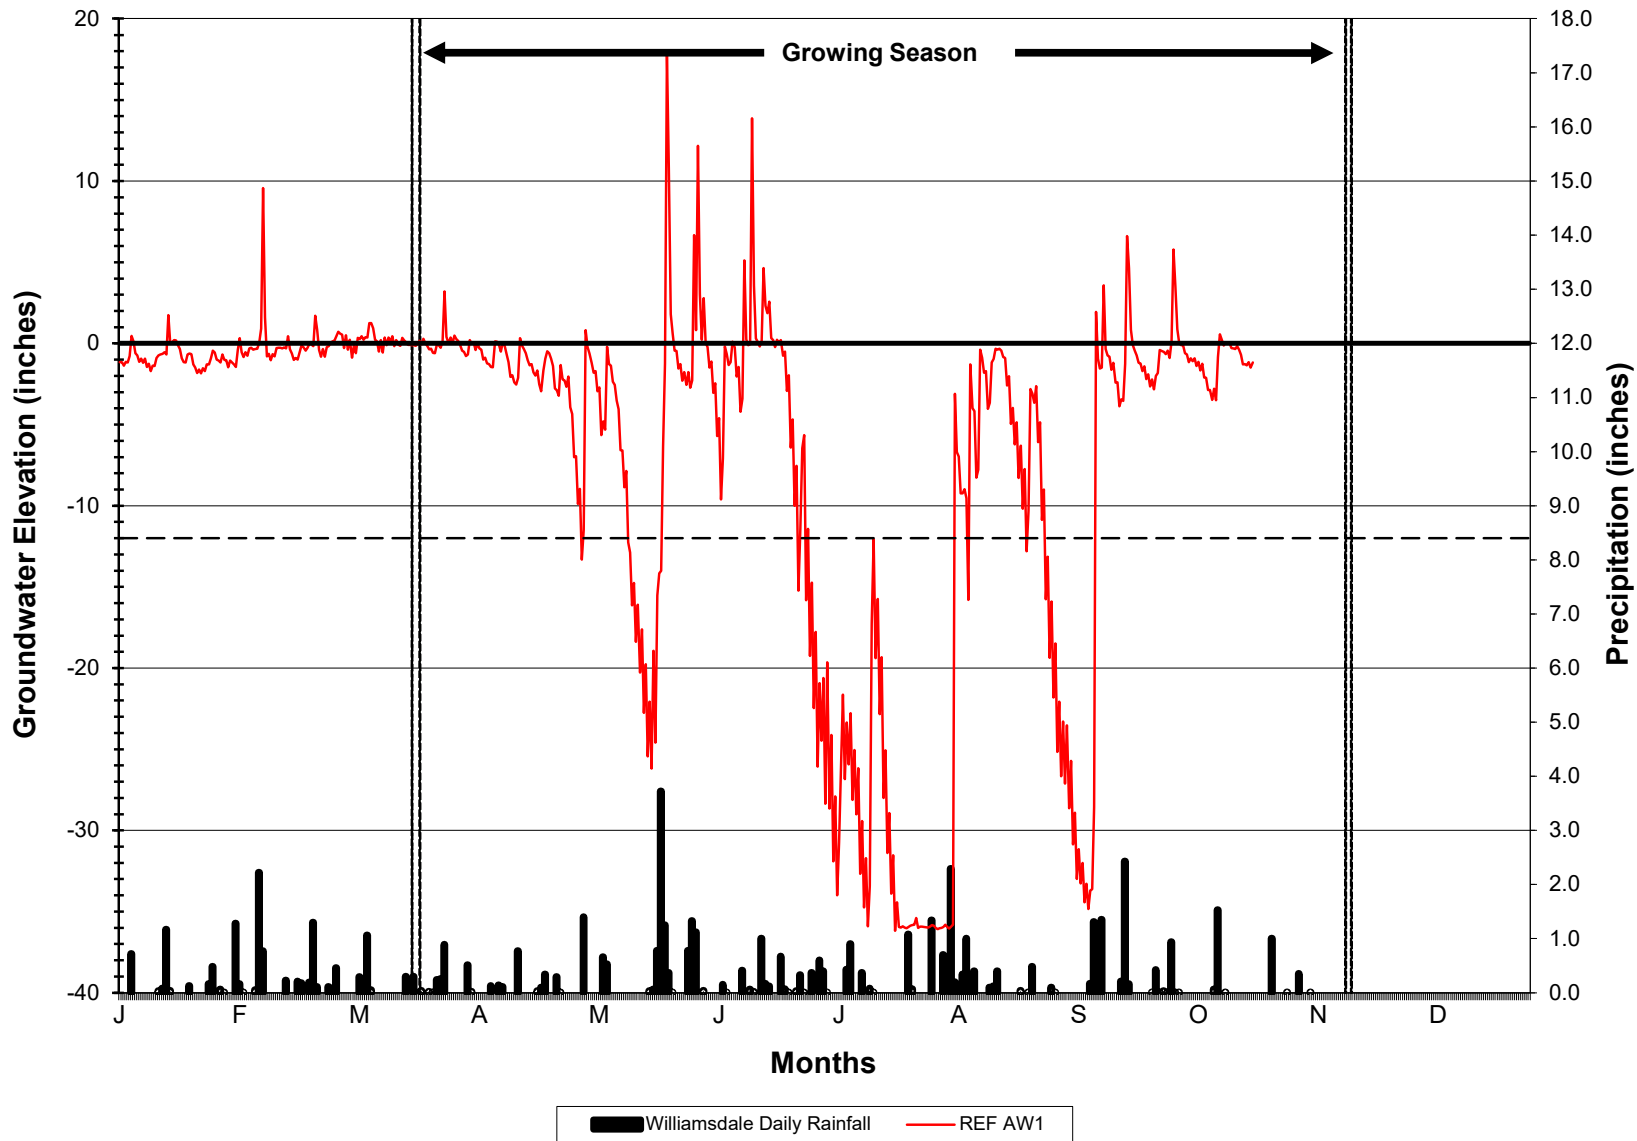

2020 Best Groundwater Gauge REFAW2

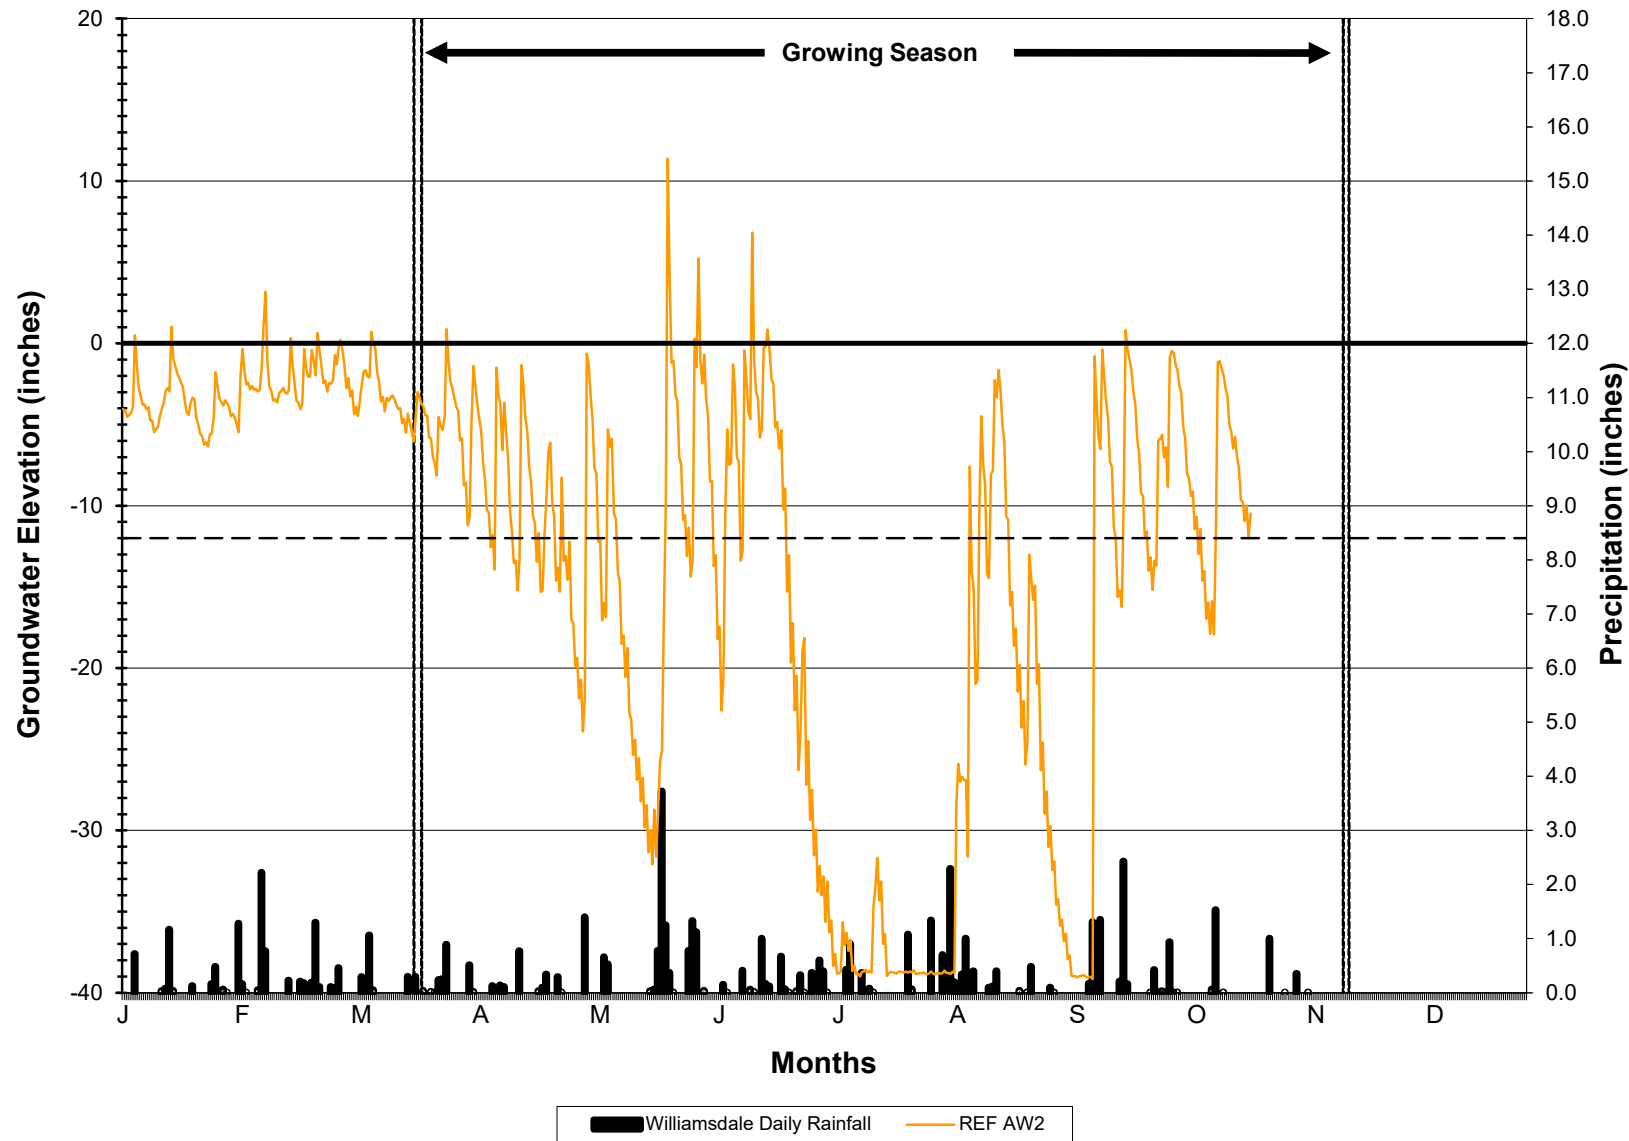

2020 Best Groundwater Gauge REFAW3

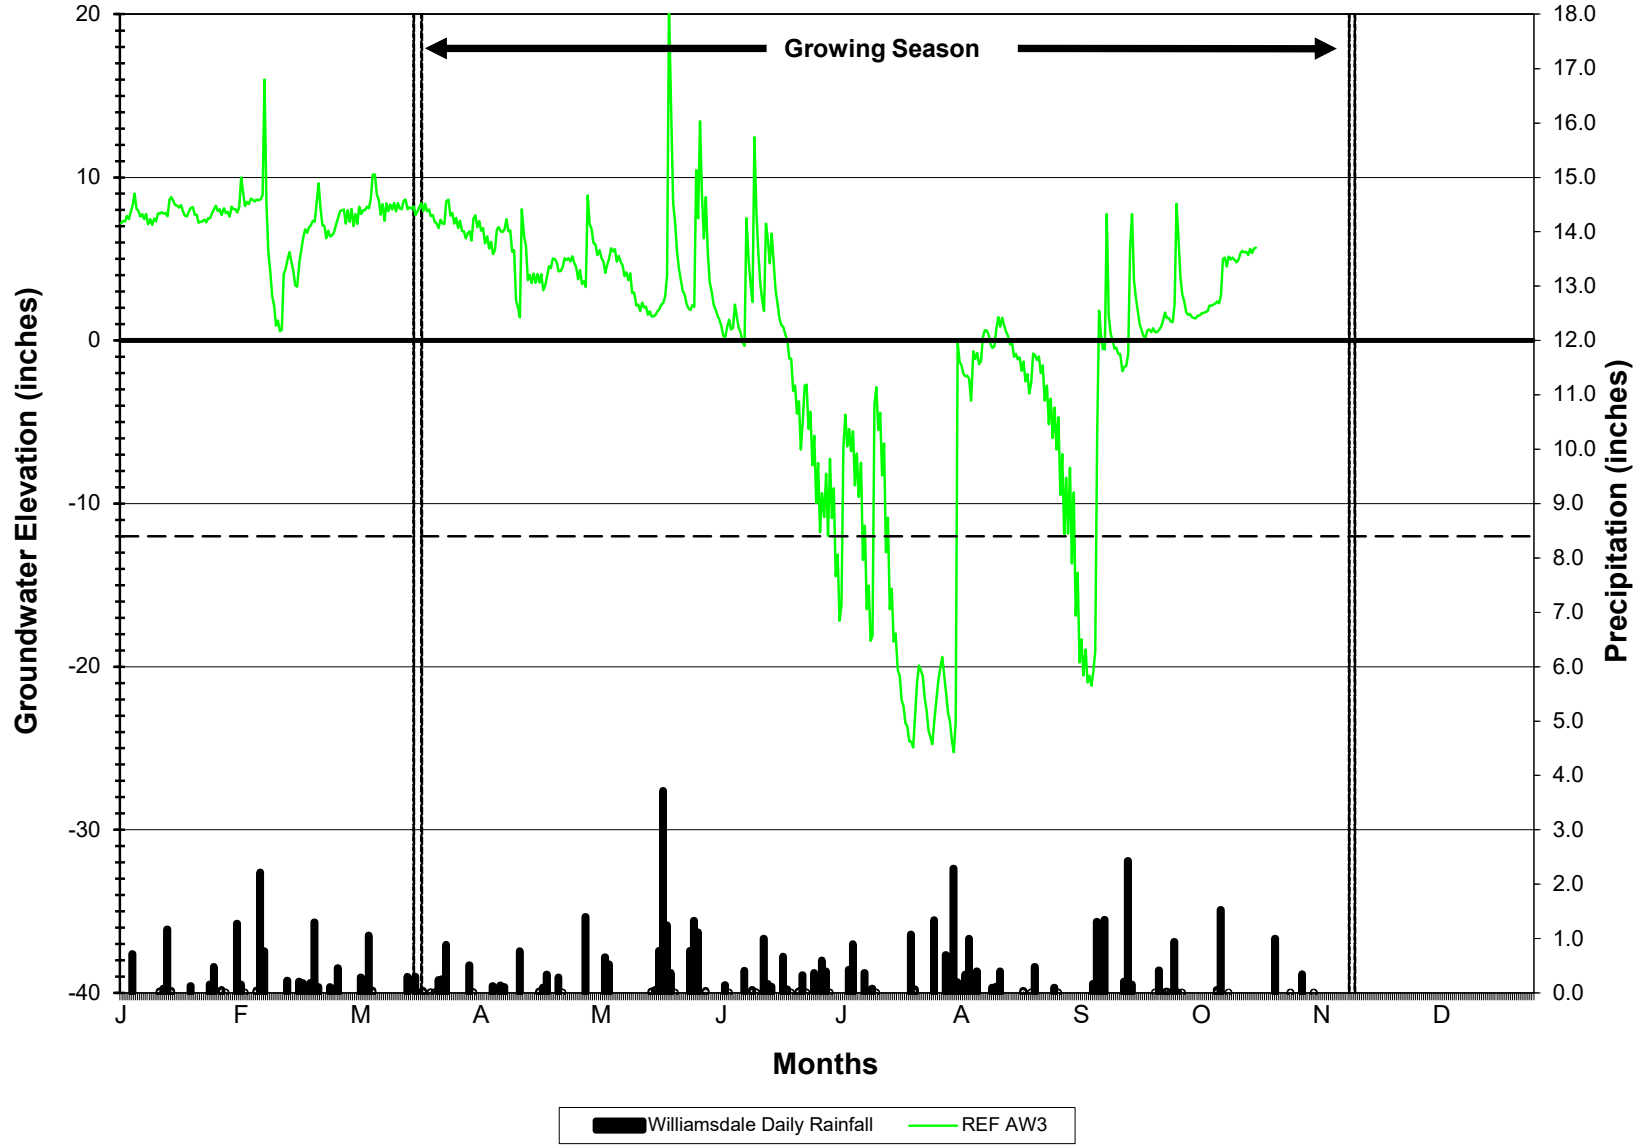

MY6 2020 Best Crest Gauge ACG4

