

Elk Branch Restoration Project

Year 3 Monitoring Report

Mitchell County, North Carolina



Monitoring Firm: Michael Baker Engineering, Inc. (Baker)

Monitoring Firm POC: Micky Clemmons

Prepared for: North Carolina Ecosystem Enhancement Program (NCEEP)



NCEEP Project Manager: Matthew Reid

Report Prepared By: Michael Baker Engineering, Inc., NC Professional Engineering License #F-1084

797 Haywood Road, Suite 201

Asheville, NC 28806

Contract Number: D06125-C, EEP Project Number: 92665

Project Construction: 2011

Data Collection Period: November-December 2015

Date Submitted: February 2015

Table of Contents

| | |
|---|-----------|
| EXECUTIVE SUMMARY | 1 |
| 1.0 PROJECT BACKGROUND..... | 2 |
| 1.1 LOCATION AND SETTING..... | 2 |
| 1.2 MITIGATION STRUCTURE AND OBJECTIVES | 2 |
| 1.3 PROJECT HISTORY AND BACKGROUND | 5 |
| 1.4 MONITORING PLAN VIEW | 8 |
| 2.0 PROJECT CONDITION AND MONITORING RESULTS | 10 |
| 2.1 VEGETATION ASSESSMENT | 10 |
| 2.1.1 <i>Vegetation</i> | 10 |
| 2.1.2 <i>Soil Data</i> | 12 |
| 2.1.3 <i>Vegetative Problem Areas</i> | 12 |
| 2.1.4 <i>Stem Counts</i> | 12 |
| 2.2 STREAM ASSESSMENT..... | 13 |
| 2.2.1 <i>Morphologic Parameters and Channel Stability</i> | 13 |
| 2.2.2 <i>Hydrology</i> | 15 |
| 2.2.3 <i>Photographic Documentation of Site</i> | 15 |
| 2.2.4 <i>Stream Stability Assessment</i> | 16 |
| 2.3 AREAS OF CONCERN | 16 |

Tables and Exhibits

| | |
|-----------------|---|
| Figure 1 | Project Location Map |
| Table 1 | Project Mitigation Structure and Objectives Table |
| Table 2 | Project Activity and Reporting History |
| Table 3 | Project Contact Table |
| Table 4 | Project Background Table |
| Figure 2 | Project Approach Map |
| Table 5 | Riparian Buffer Planting List |
| Table 6 | Preliminary Soil Data |

Appendix A

| | |
|-----------------|---|
| Table 7 | Stem Count Arranged by Plot - Year 4 (Species Survival Rates) |
| Table 7b | Stem Count Arranged by Plot - Year 4 (Planted Vs. Total) |
| Table 8 | Vegetative Problem Areas |
| Exhibit | Sink Hole Creek: Vegetation Plot Photo Points (Year 4) |

Appendix B

| | |
|-----------------|---------------------------------------|
| Table 9 | Hydrological (Bankfull) Verifications |
| Table 10 | Stream Problem Areas |

| | |
|-----------------|---|
| Exhibit | Graphs of mainstem and UT stream cross-sections |
| Exhibit | Graphs of mainstem and UT stream profiles |
| Table 11 | Categorical Stream Feature Visual Stability Assessment |
| Table 12 | Visual Morphological Stability Assessment |
| Table 13 | Stream Reach Morphology and Hydraulic Data |
| Table 14 | Cross-section Morphology and Hydraulic Data |
| Exhibit | Riffle Pebble Count Size Class Distribution (Sink Hole Reach 1) |
| Exhibit | Reference Photo Points on mainstem and UTs |

EXECUTIVE SUMMARY

The Elk Branch site was restored through a full delivery contract with the North Carolina Ecosystem Enhancement Program (NCEEP). This report presents Year 3 monitoring data as part of the five-year monitoring period. The goals for the restoration project are as follows:

- Restore or enhance headwater tributaries to Cane Creek and the French Broad Basin;
- Reduce sediment and nutrient loading through restoration of riparian areas and streambanks;
- Improve and restore hydrologic connections between the project streams and the floodplain;
- Create geomorphically stable conditions on the Elk Branch project site; and
- Improve aquatic and terrestrial habitat along the project corridor.

To accomplish these goals, the following objectives were implemented:

- Restore the existing trampled, straightened and relocated streams by creating stable channels with adequate grade control and access to the floodplain;
- Establish buffers for nutrient removal from runoff and stabilization of streambanks to reduce bank erosion;
- Improve in-stream habitat by reducing fine sediment loading from the watershed, provide a more diverse bedform with riffles and pools, create deeper pools, develop areas that increase oxygenation, provide woody debris for habitat, and reduce bank erosion; and
- Improve terrestrial habitat by planting riparian areas with native vegetation and protect these areas with a permanent conservation easement and fencing, so that the riparian area will increase storm water runoff filtering capacity, improve bank stability, provide shading to decrease water temperature and improve wildlife habitat.

A total of six vegetation monitoring plots 100 square meters (m²) (10m x 10m) in size were installed to evaluate survival of the woody vegetation planted on-site. The Year 3 vegetation monitoring indicated an average survival rate of 357 planted stems per acre, no volunteers were observed. The data shows that the Site has met the interim stem survival criteria for Year 3 (320 stems per acre) and may meet the final success criteria of 260 trees per acre by the end of Year 5. However, due to the low survival of trees in half the plots which represent areas of the riparian zone that may be experiencing low survival, Baker is pursuing additional plantings within the buffer area near these plots.

The design proposed for the Elk Branch mitigation project involved Restoration (Priority 1 & 2) and Enhancement approaches and this was completed as described in the baseline monitoring report for this site. The project should ultimately result in having stable Cb and Eb-type channels for Elk Branch, UT1 and UT2. Longitudinal profile and cross-section data indicate that the project streams have remained stable since baseline monitoring data were collected in 2011. Additionally, as the photo logs included in this report show, herbaceous cover at the project site is dense, and in conjunction with other erosion control measures like matting, is promoting bank stability on-site while planted, woody vegetation becomes more established. Based on data collected and presented in this report, this site is currently on track to meet the other success criteria specified in the Elk Branch Mitigation Plan.

Summary information and data related to the occurrence of items such as beaver impacts or encroachment, and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Site conditions were evaluated in comparison to project success criteria; there are no project issues or concerns to report at this time. During the Year-3 monitoring period surface flows were found throughout UT2, which is in contrast with previous monitoring periods. In Year-1 103 linear feet of UT2 was observed to experience subsurface flow and in Year-2 the total subsurface flow had dropped to 20 linear feet in UT2. Baker will continue to monitor the status of continuous flow in this channel. Narrative background and supporting information can be found in previous reports that are available on EEP's website. All raw data supporting the tables and figures in the appendices is available from EEP upon request.

1.0 PROJECT BACKGROUND

The Elk Branch mitigation site is situated in the French Broad River Basin, within North Carolina Division of Water Quality (NCDWQ) sub-basin 04-03-06 and United States Geologic Survey (USGS) hydrologic unit 06010108040010. The watershed in which the Elk Branch mitigation project is located is dominated by forested land, but also contains pastures and residences. Slightly less than two-thirds of the watershed is in forested cover, leaving about one-third of the drainage in some form of pasture land or other agricultural or residential use. Elk Branch and its tributaries have been impaired by historical and recent land management practices that include timber harvesting, pasture conversion, channelization, and livestock grazing. Prior to restoration, stream channelization and dredging were evident through much of the project site, as were the impacts of open stream access by cattle and horses. A significant loss of woody streambank vegetation also occurred during the development of the land for agricultural use. Over time, these practices have contributed excessive sediment and nutrients to Elk Branch, Cane Creek and ultimately to the North Toe River, home to the endangered Appalachian elktoe mussel.


The project involved restoration or enhancement of 3,159 linear feet (LF) of channel, primarily along three on-site streams: Elk Branch and two unnamed tributaries (UT1 and UT2). In addition, a third tributary (UT3) segment was also restored by day-lighting the tributary from the easement boundary to its confluence with Elk Branch. UT3 was impounded sometime in the past to create a small pond which flowed to the easement boundary through a pipe. Elk Branch is shown as a solid blue-line stream while spring-fed tributaries UT1 and UT2 are apparent from the topography, but are not displayed on the USGS topographic quadrangle map for the site. Elk Branch, UT1 and UT2 were confirmed as being perennial and UT3 was considered intermittent based on field evaluations using the NCDWQ stream assessment protocol.

1.1 Location and Setting

The Elk Branch project site is located about one mile northeast of Bakersville in Mitchell County, North Carolina (Figure 1). To reach the project site, follow I-26 North from Asheville for approximately 20 miles and take U.S. Highway 19N Exit 9, towards Burnsville and Spruce Pine. Continue along U.S. Highway 19 (which becomes 19-E), for 25 miles. Turn left onto N.C. Highway 226 and continue until you reach the Town of Bakersville. Once in Bakersville, turn right (northeast) onto North Mitchell Avenue and after approximately a half mile, North Mitchell Avenue becomes Cane Creek Road. Continue on Cane Creek Road another 0.7 miles, then turn left off of Cane Creek Road onto Nora Lane (SR 1219). Continue on Nora Lane for .65 miles where Nora Lane ends in a turn around with a private drive continuing north onto the Wylie property (and the upstream point of the project) and to the west of the turnaround Annies Cove (a dead end) diverges. The Hall property (UT1 is on the Hall property) is accessed from Annies Cove. The project site begins just below a spring head at the top of the valley on the Wylie property, approximately 1,500 feet beyond the end of Nora Road (unpaved) and the project along the mainstem ends where it crosses under Annies Cove.

1.2 Mitigation Structure and Objectives

Table 1 summarizes project data for each reach and restoration approach used. The design proposed for the Elk Branch mitigation project involved Restoration (Priority 1 & 2) and Enhancement approaches. Beyond a few minor changes, restoration and enhancement were completed in accordance with the approved design approach provided in the mitigation plan for this site. Field changes made were implemented in order to minimize impacts to existing resources and adapt to unmapped or changed field conditions including micro-topography, vegetation, and existing in-stream grade control. The project should ultimately result in stable Cb and Eb-type channels for Elk Branch, UT1 and UT2.

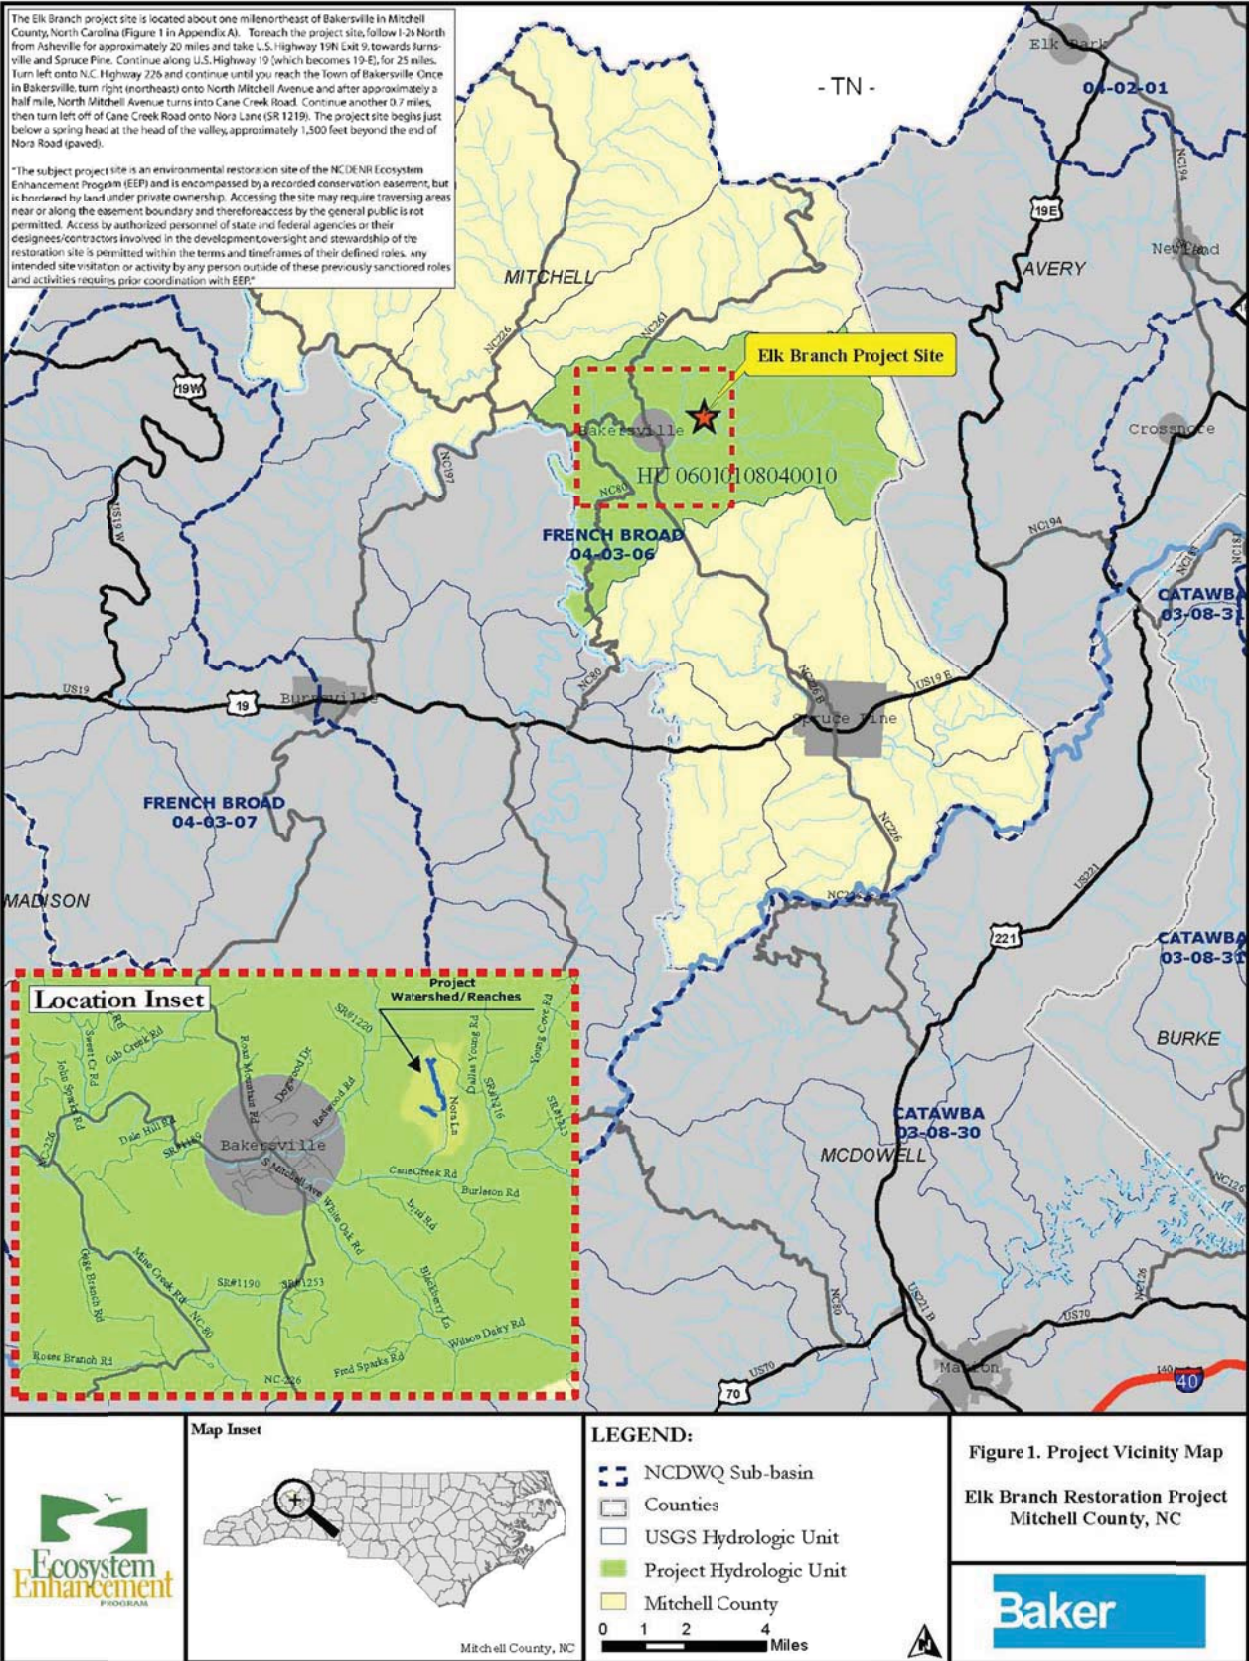

| Table 1. Project Mitigation Structure and Objectives Elk Branch Mitigation Project-NCEEP Project #92665 | | | | | | | | | |
|--|-------------------------|-----------------|----------|--------------------|--------------------|------------------|------------------|----------------|--|
| Project Segment or Reach ID | Existing Feet/ Acres | Mitigation Type | Approach | Target Stream Type | Footage or Acreage | Mitigation Ratio | Mitigation Units | Stationing | Comment |
| Elk Branch | | | | | | | | | |
| Reach 1 | 2,020 LF | R | PI | Cb4 | 951 LF | 1:1 | 951 | 0+76 to 10+50 | Adjust pattern, improve dimension by removal of vertical banks and increased floodplain connectivity, and restore step-pool channel via grade control and constructed riffles. |
| Reach A | | E | LI | | 592 LF | 1.5:1 | 395 | 10+50 to 16+42 | Restore stable dimension to halt erosion and add grade control to improve pools. Grade control structures will provide long-term channel stability and improve in-stream habitat. |
| Reach B | | R | P1/2 | | 403 LF | 1:1 | 403 | 16+42 to 20+60 | Adjust pattern, improve dimension by removal of vertical banks and increased floodplain connectivity, and restore step-pool channel via grade control and constructed riffles. |
| Reach 2 | 279 LF | E | LI | | 279 LF | 1.5:1 | 186 | 20+60 to 23+39 | Restore stable dimension to halt erosion and add grade control to improve pools. Grade control structures will provide long-term channel stability and improve in-stream habitat. |
| UT 1 | | | | | | | | | |
| Reach 1 | 685 LF | R | P1 | Cb4 | 656 LF | 1:1 | 656 | 0+06 to 6+83 | Restore channel-floodplain connectivity of previously channelized tributary. Adjustments also made to pattern and profile to eliminate eroding streambanks and improve habitat diversity. Invasive vegetation also removed; riparian buffer restored. |
| UT 2 | | | | | | | | | |
| Reach 1 | 279 LF | R | PI | Eb4 | 242 LF | 1:1 | 242 | 0+92 to 3+34 | Excavate previously buried section of UT2. New channel constructed with stable dimension, pattern, and profile. Priority 1 approach also applied to existing segment of UT2 to improve channel and bank stability, as well as increased access to the floodplain. Trash and debris were removed. *buried portion not included in existing length |
| UT 3 (New component, not in restoration plan) | | | | | | | | | |
| Reach 1 | 0 LF | R | PI | Cb4 | 36 LF | 1:1 | 36 | 0+00 to 0+36 | Minor pattern adjustment, extensive improvements to dimension by removal of vertical banks and increased floodplain connectivity, and restore profile via multiple grade control structures and constructed riffles. |

| Mitigation Unit Summations | | | | | |
|---|------------------------|---------------------------|---------------------|--------------|---------|
| Stream (SMU) | Riparian Wetland (WMU) | Nonriparian Wetland (WMU) | Total Wetland (WMU) | Buffer (BMU) | Comment |
| 2,869 | NA | NA | NA | | |
| Notes: | | | | | |
| 1. Elk Branch R1 was broken into smaller reaches subsequent to the submittal and approval of the restoration plan, following regulatory comments. | | | | | |
| 2. Mitigation units have been calculated by excluding easement exception on Elk Branch Reach I, Elk Branch Reach B and UT1. | | | | | |

In accordance with the approved mitigation plan for the site, construction activities began in May 2011. Project activity on Elk Branch Reach 1, Reach B, UT1, UT2, and UT3 consisted of making adjustments to channel dimension, pattern, and profile typically using a Priority 1 Restoration approach. A Level I Enhancement approach was used on Elk Branch Reaches A and 2 to re-establish a stable channel cross-section that provides floodplain access, while recreating a stable channel profile and bedform using a step-pool restoration approach that features grade control structures and constructed riffles.

The creation of a step-pool channel profile was used to achieve vertical stability and eliminate self-propagating headcuts previously found within the site. This was the primary method for promoting improved stability, water quality, and habitat goals. In-stream structures (constructed riffles, boulder steps, log vanes, log drops, and log rollers) were used to control streambed grade, reduce stresses on streambanks, and promote diversity of bedform and habitat. Structures were spaced at a distance that replicated natural pool to pool spacing and allowed downstream headers to protect the upstream structure footer to create long term vertical stability.

Channel dimensions were adjusted to eliminate vertical banks and erosion resulting from excessive shear stress and lack of floodplain relief. Streambanks were stabilized using a combination of erosion control matting, bare-root planting, transplants, and live staking. Transplants will provide living root mass quickly to increase streambank stability and create shaded holding areas for fish and aquatic biota. Where feasible, plan form adjustments were made to correct prior channelization by making slight adjustments to channel pattern (step-pool channels have a low sinuosity). These modifications will allow flows larger than bankfull to spread onto the restored floodplain, dissipating flow energies and reducing streambank stress. The entire mitigation site is protected through a permanent conservation easement and native vegetation was planted throughout the easement area.

1.3 Project History and Background

The chronology of the Elk Branch mitigation project is presented in Table 2 while the contact information for designers, contractors and plant material suppliers is presented in Table 3. Relevant project background information is presented in Table 4. The total as-built stream length across the project is 3,159 LF.

| Activity or Report | Data Collection Complete | Completion or Delivery |
|--|--------------------------|------------------------|
| Restoration Plan | | December 2009 |
| Final Design-90% | | December 2009 |
| Construction | | June 2011 |
| Temporary S&E mix applied to entire project area | | June 2011 |
| Permanent seed mix applied to project site | | June 2011 |
| Installation of crest gauges | | July 2011 |
| Plantings set out | January 2012 | January 2012 |

| Table 2. Project Activity and Reporting History Elk Branch Mitigation Project-NCEEP Project #92665 | | |
|---|-------------------------|---------------|
| Mitigation Plan / As-built (Year 0 Monitoring – baseline) | July 2011/January 2012 | April 2012 |
| Year 1 Monitoring | October 2012 | December 2012 |
| Year 2 Monitoring | November 2013 | February 2014 |
| Easement boundary was marked by EEP. | | October 2014 |
| Year 3 Monitoring | November /December 2014 | February 2015 |
| Year 4 Monitoring | | |
| Year 5 Monitoring | | |

| Table 3. Project Contacts Elk Branch Mitigation Project-NCEEP Project #92665 | |
|---|--|
| Principal-In-Charge | |
| Michael Baker Engineering, Inc. | 797 Haywood Rd Suite 201, Asheville, NC 28806 <u>Contact:</u> Micky Clemmons, Tel. 828.350.1408 x2002 |
| Designer | |
| Michael Baker Engineering, Inc. | 797 Haywood Rd Suite 201, Asheville, NC 28806 <u>Contact:</u> Micky Clemmons, Tel. 828.350.1408 x2002 |
| Construction Contractor | |
| River Works, Inc. | 6105 Chapel Hill Road; Raleigh, NC 27607 <u>Contact:</u> Bill Wright, Tel. 919.818.6686 |
| Planting & Seeding Contractor | |
| River Works, Inc. | 6105 Chapel Hill Road; Raleigh, NC 27607 <u>Contact:</u> George Morris, Tel. 919.459.9001 |
| Seed Mix Sources | Green Resources |
| Nursery Stock Suppliers | Arborgen and Hillis Nursery |
| Monitoring | |
| Michael Baker Engineering, Inc. | 797 Haywood Rd Suite 201, Asheville, NC 28806 <u>Contact:</u> Micky Clemmons, Tel. 828.350.1408 x2002 |


| Table 4. Project Attribute Elk Branch Mitigation Project-NCEEP Project #92665 | |
|--|--|
| Project County | Mitchell County, NC |
| Physiographic Region | Blue Ridge |
| Ecoregion | Blue Ridge Mountains-Southern Crystalline Ridges and Mountains |
| Project River Basin | French Broad |
| USGS HUC for Project | 6010108040010 |
| NCDWQ Sub-basin for Project | 04-03-06 |
| Within extent of EEP Watershed Plan? | In a TLW (French Broad River Basin Priorities Report-2009) |
| WRC Class | Cold |

| Table 4. Project Attribute Elk Branch Mitigation Project-NCEEP Project #92665 | |
|--|---|
| % of Project Easement Fenced or Demarcated | 100% (~60% fenced, 40% demarcated) |
| Beaver Activity Observed During Design Phase? | No |
| Drainage Area (Square Miles) | |
| Elk Branch Reach 1 | .07 mi ² |
| Reach A | |
| Reach B | |
| Elk Branch Reach 2 | .14 mi ² |
| UT1 | .06 mi ² |
| UT2 | .01 mi ² |
| Stream Order | Elk Branch-1 st , UT1-Zero, UT2-Zero, UT3-Zero |
| Restored Length | |
| Elk Branch Reach 1 | 951 LF |
| Reach A | 592 LF |
| Reach B | 403 LF |
| Elk Branch Reach 2 | 279 LF |
| UT1 | 656 LF |
| UT2 | 242 LF |
| UT3 | 36 LF |
| Perennial or Intermittent | Perennial |
| Watershed Type | Rural (Predominantly Forested) |
| Watershed LULC Distribution (Percent area) | |
| Forest | 57% |
| Shrub | 6% |
| Pasture/Crops | 33% |
| Developed Open Space | 4% |
| Drainage Impervious Cover Estimate (%) | <10% |
| NCDWQ AU/Index # | 7-2-59-8 |
| 303d Listed | No |
| Upstream of 303d Listed Segment | No |
| Reasons for 303d Listing or Stressor | - |
| Total Acreage of Easement | 9.46 |
| Total Vegetated Acreage w/in Easement | Easement vegetated with exception of stream channel and a ford crossings within an easement break |
| Total Planted Acreage within the Easement | ~4 Acres (remainder already forested) |
| Rosgen Classification (Pre-existing) | |
| Elk Branch | Cb/B/G/Eb |
| UT1 | Fb |
| UT2 | B |
| UT3 | Piped |
| Rosgen Classification of As-built | |
| Elk Branch-Reach 1 | Cb4 |

| Table 4. Project Attribute Elk Branch Mitigation Project-NCEEP Project #92665 | |
|--|---|
| Reach A | Cb4 |
| Reach B | Cb4 |
| Elk Branch-Reach 2 | Cb4 |
| UT1 | Cb4 |
| UT2 | Eb4 |
| UT3 | Cb4 |
| Valley Type | II |
| Valley Slope | .03 (Elk Branch), .04 (UT1), .04 (UT2) |
| Valley Side Slope Range | n/a |
| Valley Toe Slope Range | n/a |
| Trout Waters Designation | Yes (Elk Branch is a tributary to designated trout waters) |
| Species of Concern | No |


1.4 Monitoring Plan View

The current conditions plan view depicts the monitoring features for the Elk Branch mitigation project. The plan set will also be used to identify locations where stream and vegetation problem areas are present. At this time, no problems areas are present. Figure 2 illustrates the project as it is delineated by reach.

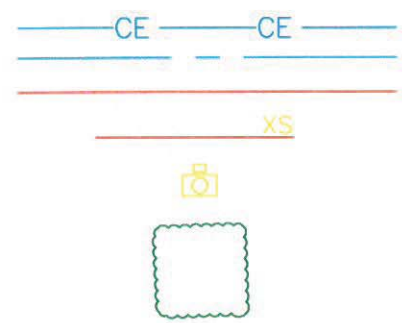


CONSERVATION EASEMENT
 ASBUILT CENTERLINE
 ASBUILT TOP OF BANK
 CROSS SECTION
 PHOTO ID POINT
 VEGETATION PLOT

VEGETATION PLOT MEETING CRITERIA
 VEGETATION PLOT NOT MEETING CRITERIA
 STREAM PROBLEM AREA (NO AREAS EXHIBITING PROBLEM)

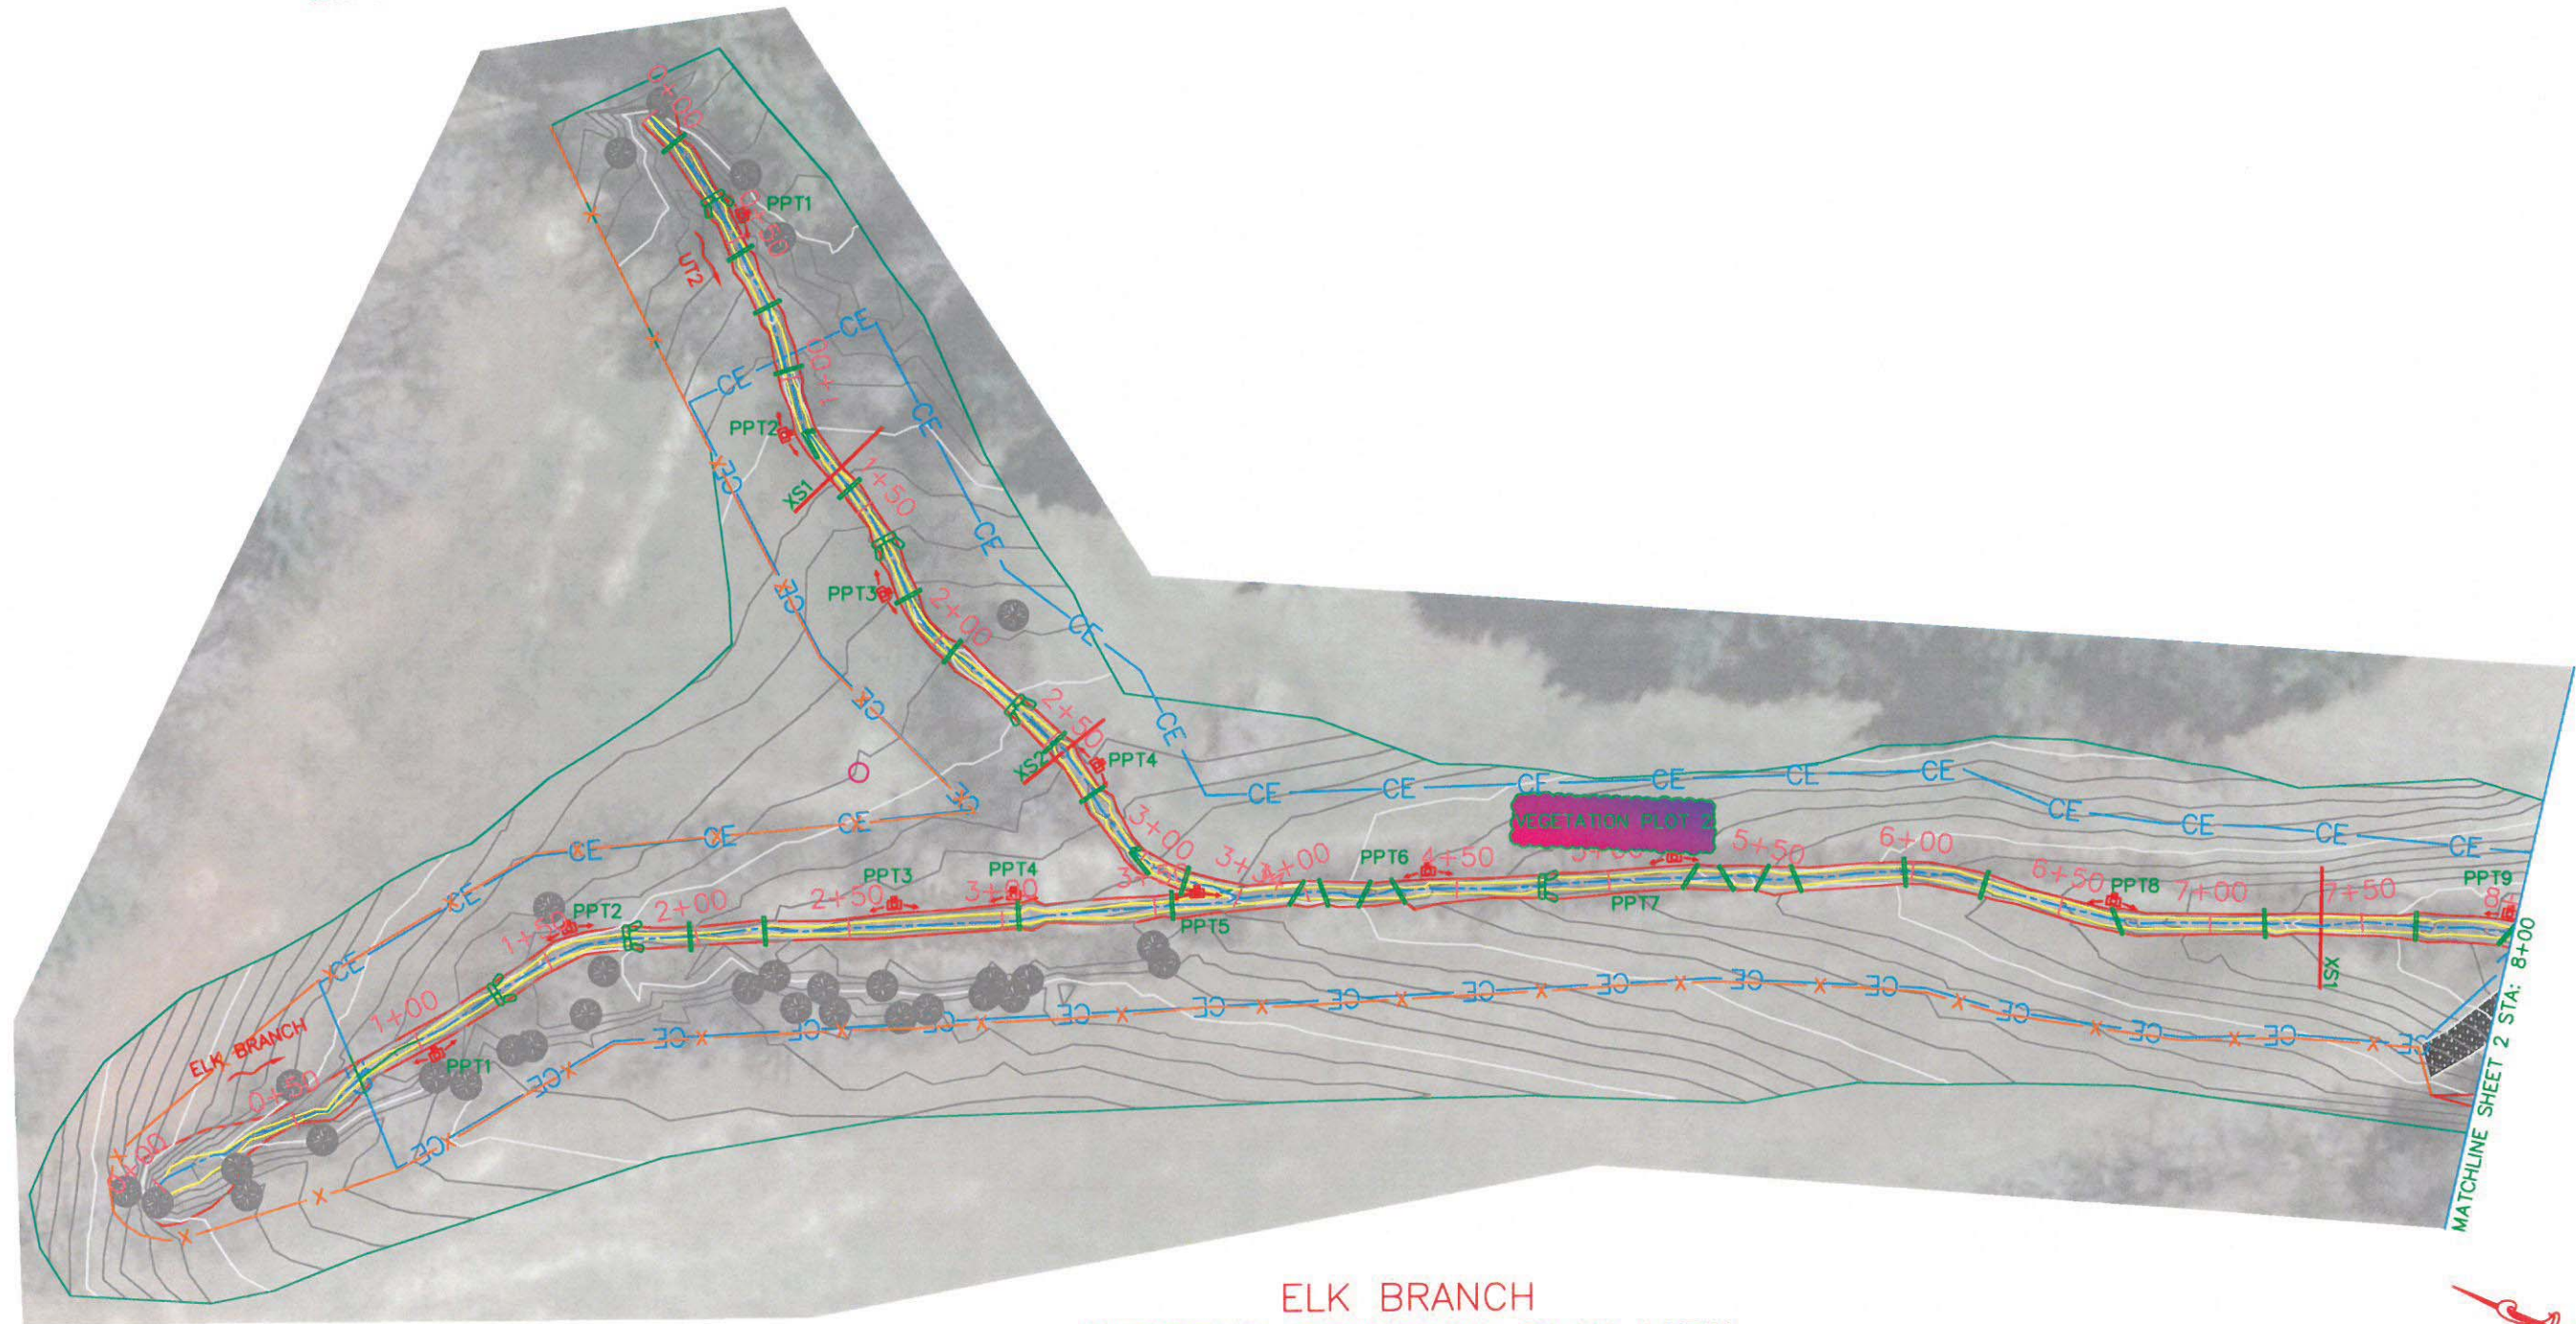

ELK BRANCH
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING
 STA. 0+00-8+00



Michael Baker Engineering Inc.
 NC Engineering License F-1084
 797 Haywood Road, Suite 201
 Asheville, North Carolina 28806
 Phone: 828.350.1408
 Fax: 828.350.1409


Baker


ELK BRANCH RESTORATION PROJECT
 MITCHELL COUNTY, NORTH CAROLINA
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING




Prepared for:
 Ecosystem Enhancement Program
 2728 Capital Blvd., Suite 1103
 Raleigh, NC 27604
 Phone 919-715-0476
 Fax 919-715-2216

| | |
|-------------------|-----------|
| EEP Project No. | 92665 |
| Baker Project No. | 111085 |
| Date: | 2/11/2015 |
| DESIGNED: | JPM |
| DRAWN: | MCR |
| APPROVED: | MMC |
| Monitoring Year: | 3 of 5 |
| Sheet: | 1 of 4 |

— CE — CE — CONSERVATION EASEMENT
 — — — ASBUILT CENTERLINE
 — — — ASBUILT TOP OF BANK
 — XS — CROSS SECTION
 PHOTO ID POINT

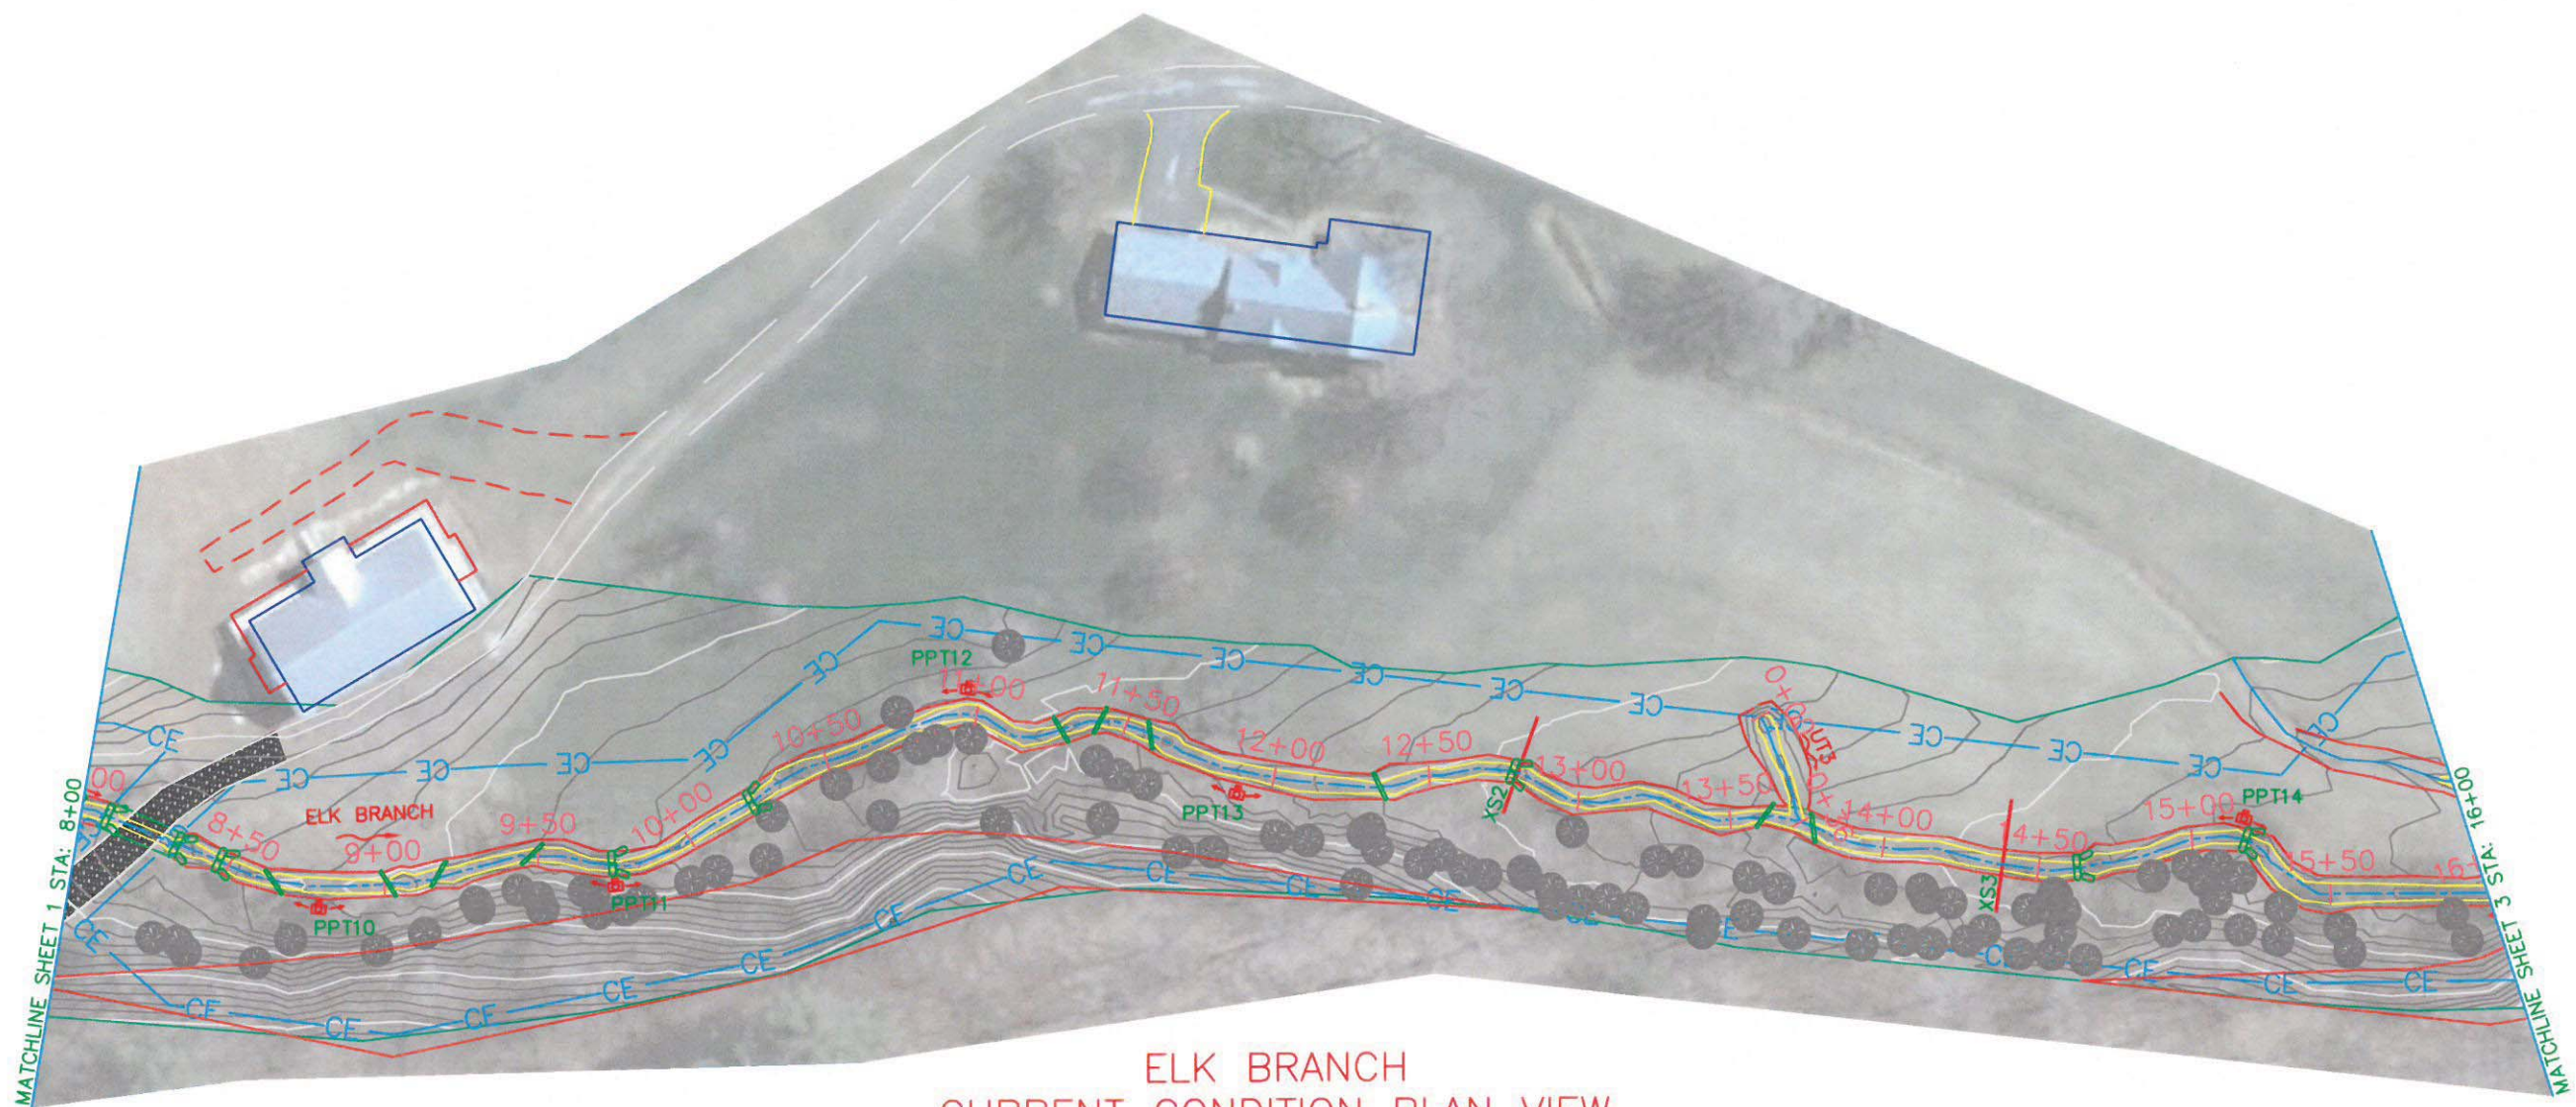

ELK BRANCH
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING
 STA. 8+00-16+00



Michael Baker Engineering Inc.
 NC Engineering License F-1084
 797 Haywood Road, Suite 201
 Asheville, North Carolina 28806
 Phone: 828.350.1408
 Fax: 828.350.1409




Baker

ELK BRANCH RESTORATION PROJECT
 MITCHELL COUNTY, NORTH CAROLINA
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING




Prepared for
 Ecosystem Enhancement Program
 2728 Capital Blvd. Suite 11 103
 Raleigh, NC 27604
 Phone 919-715-0476
 Fax 919-715-2219

| | |
|-------------------|-----------|
| EEP Project No. | 92665 |
| Baker Project No. | 111085 |
| Date: | 2/11/2015 |
| DESIGNED: | JEM |
| DRAWN: | MDE |
| APPROVED: | MMC |
| Monitoring Year: | 3 of 5 |
| Sheet: | 2 of 4 |

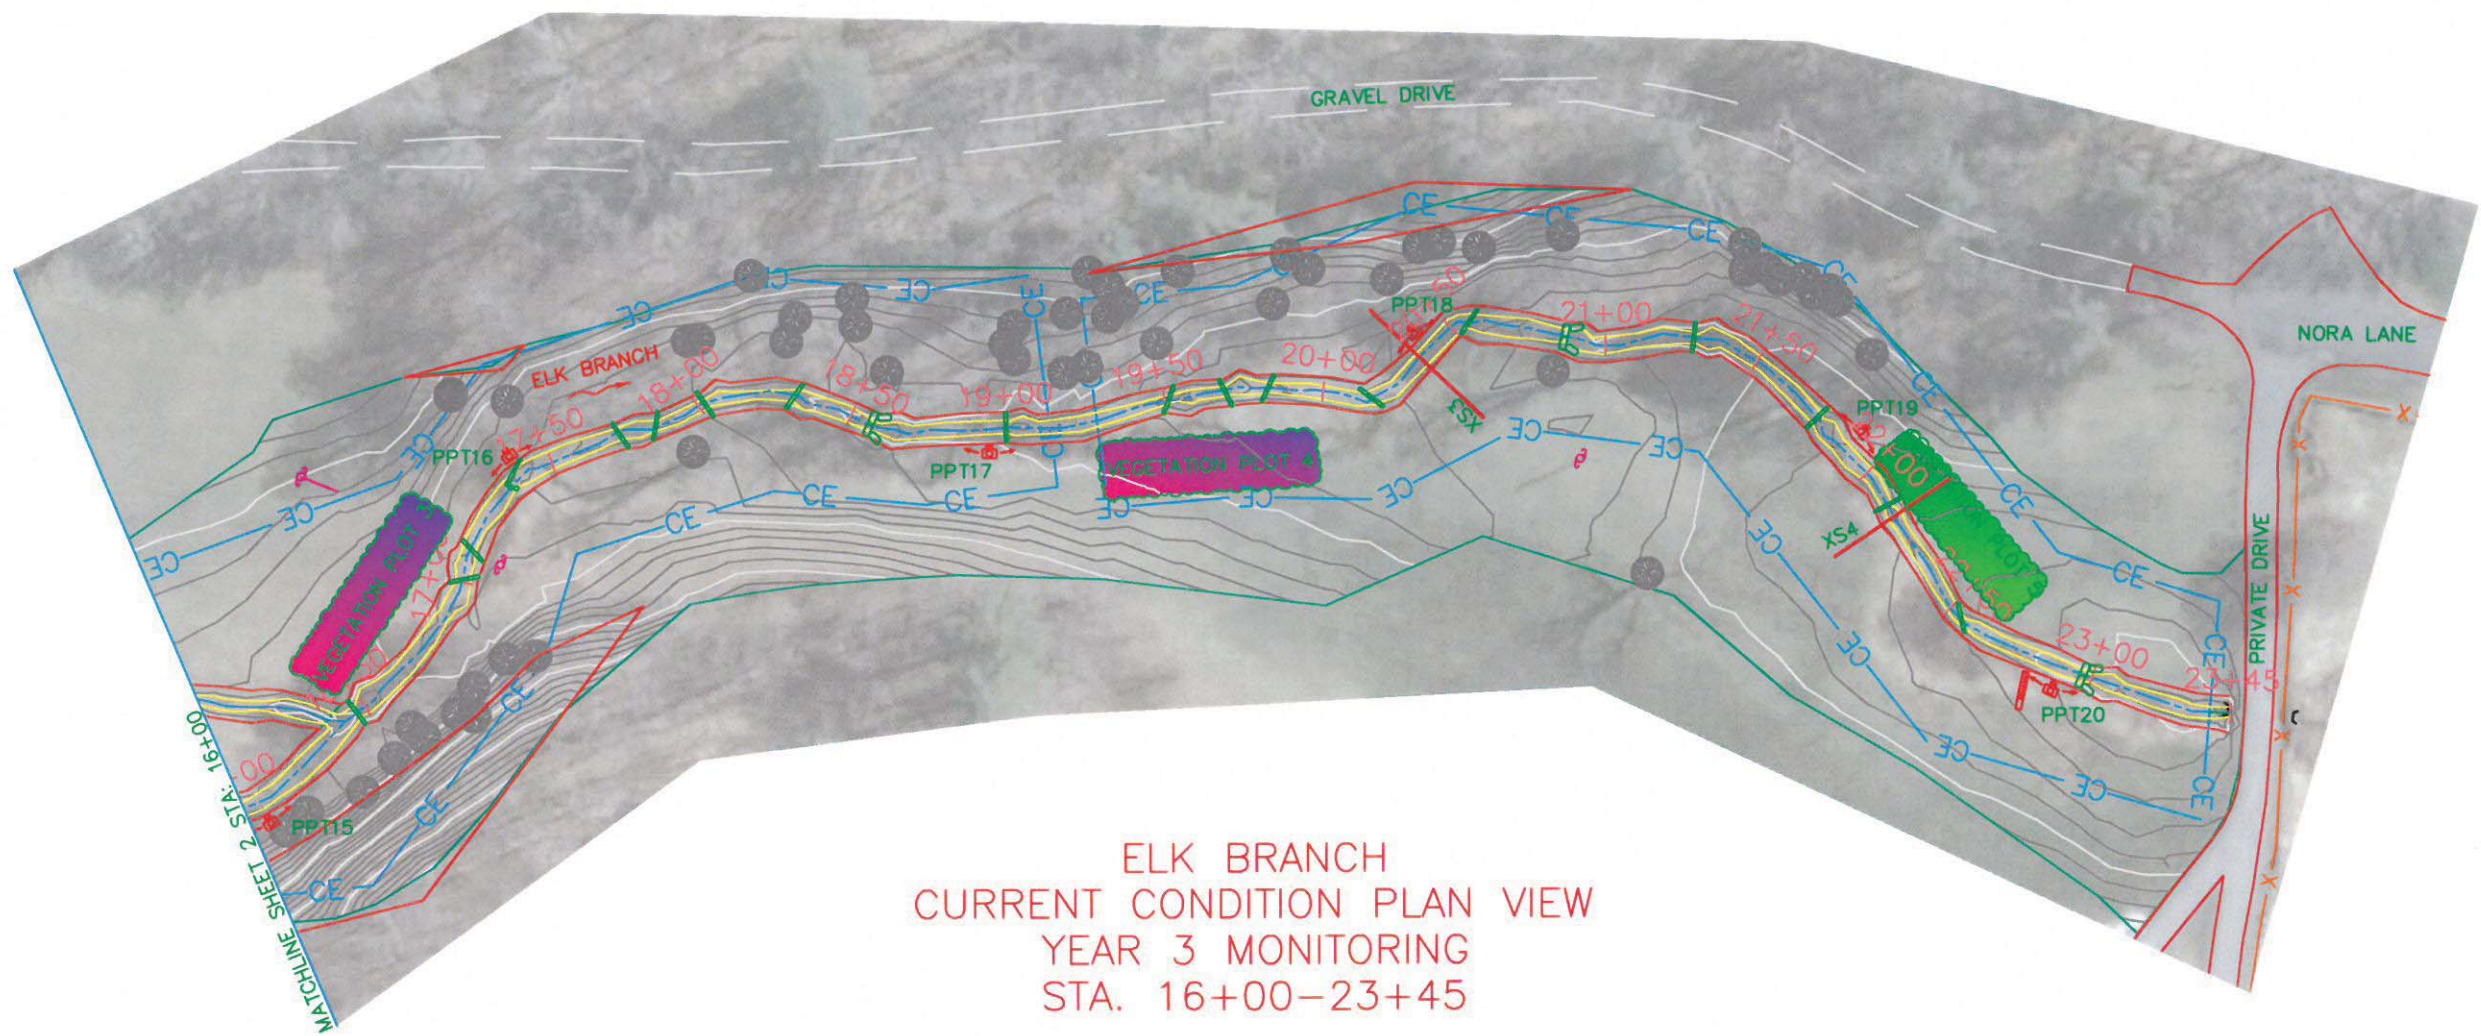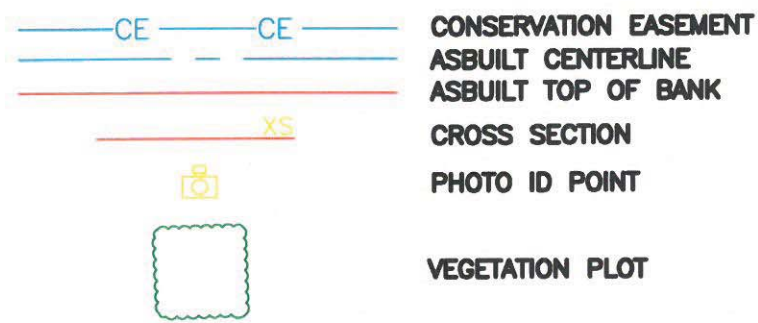

ELK BRANCH
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING
 STA. 16+00-23+45



Michael Baker Engineering Inc.
 NC Engineering License E-1084
 797 Haywood Road, Suite 201
 Asheville, North Carolina 28806
 Phone: 828.350.1408
 Fax: 828.350.1409




Baker

ELK BRANCH RESTORATION PROJECT
 MITCHELL COUNTY, NORTH CAROLINA
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING




Prepared for:
 Ecosystem Enhancement Program
 2728 Capital Blvd., Suite 1103
 Raleigh, NC 27604
 Phone 919-715-0076
 Fax 919-715-2219

| | |
|-------------------|-----------|
| EEP Project No. | 92665 |
| Baker Project No. | 111085 |
| Date: | 2/11/2015 |
| DESIGNED: | JEM |
| DRAWN: | MDE |
| APPROVED: | MMC |
| Monitoring Year: | 3 of 5 |
| Sheet: | 3 of 4 |

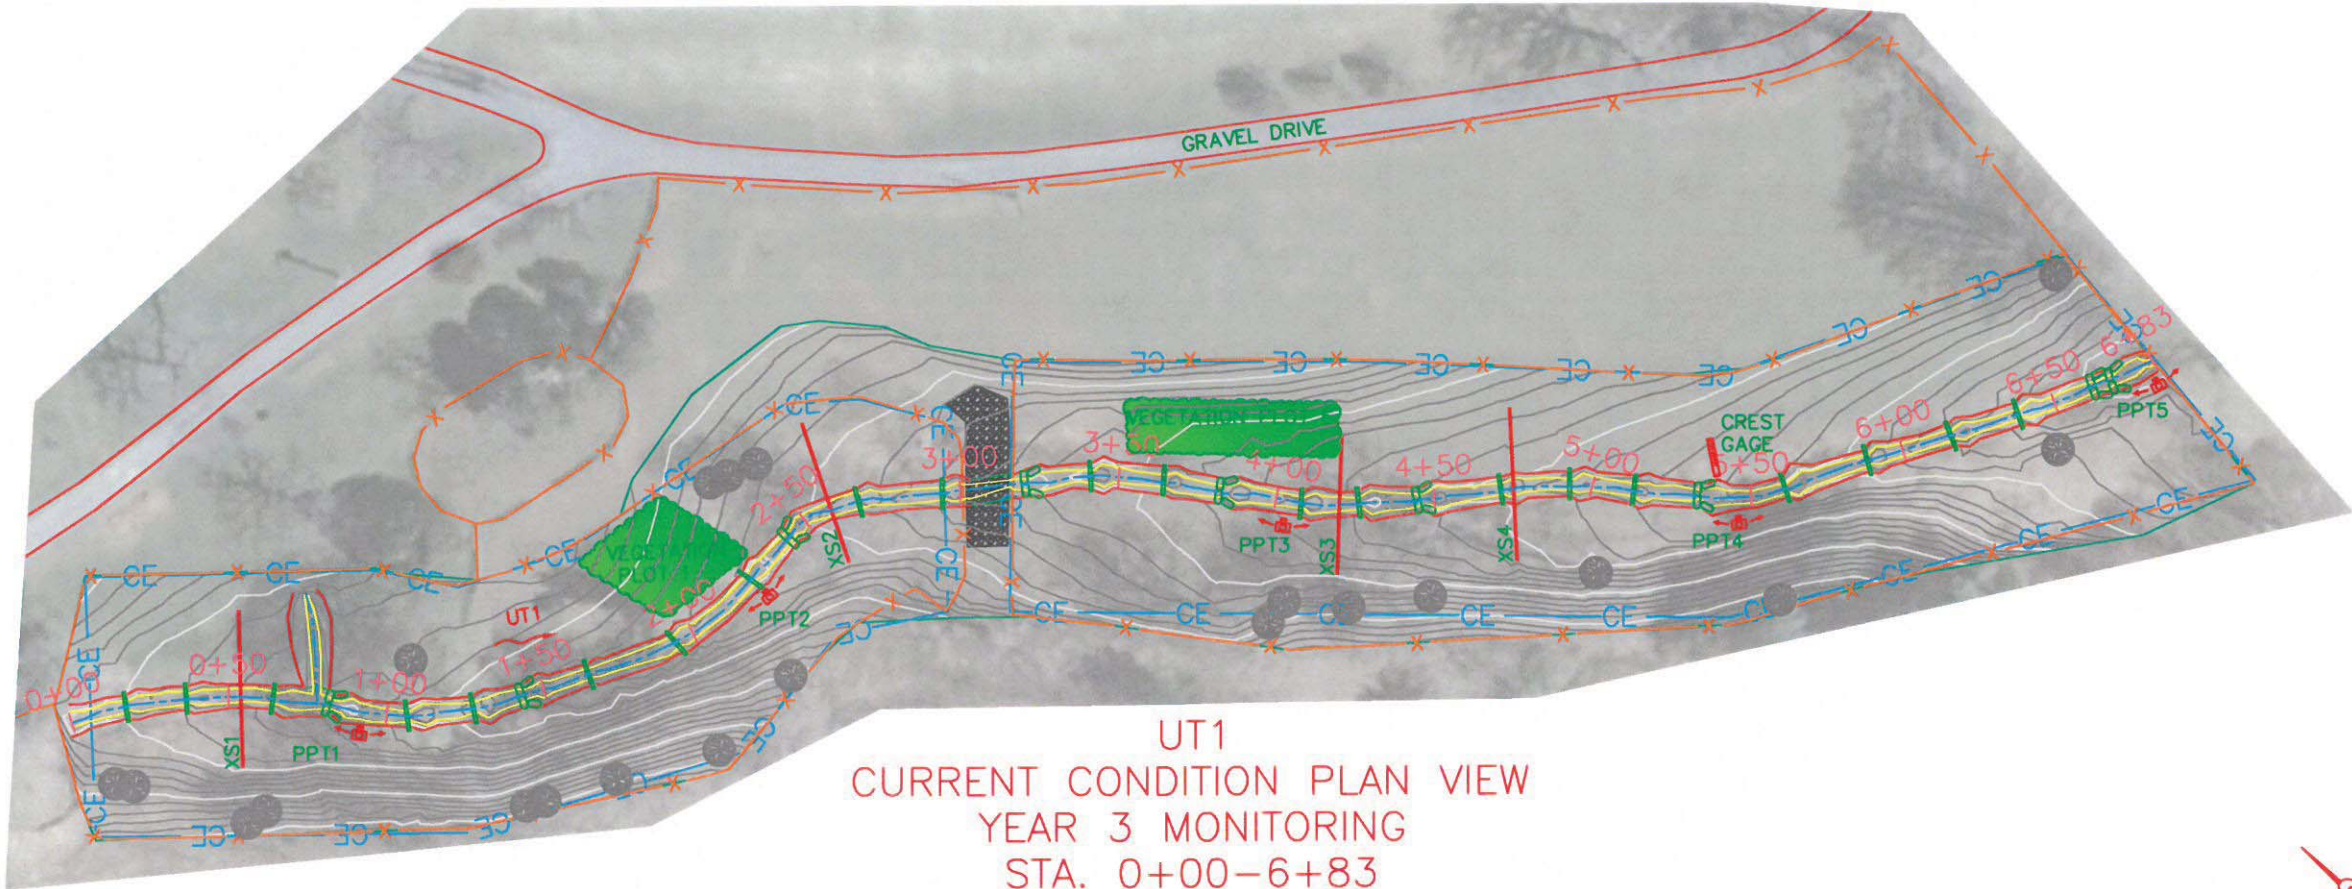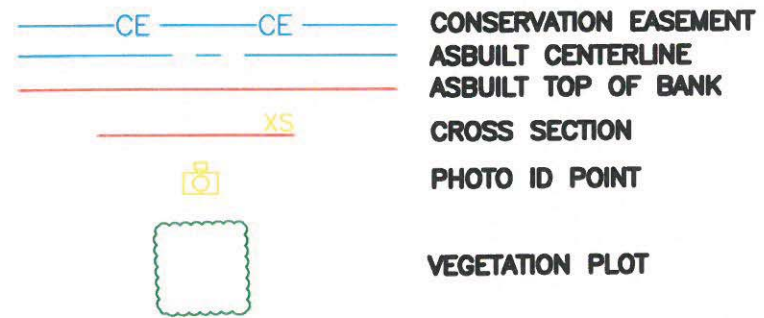

UT1
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING
 STA. 0+00-6+83



Michael Baker Engineering Inc.
 NC Engineering License F-1084
 797 Haywood Road, Suite 201
 Asheville, North Carolina 28806
 Phone: 828.350.1408
 Fax: 828.350.1409




ELK BRANCH RESTORATION PROJECT
 MITCHELL COUNTY, NORTH CAROLINA
 CURRENT CONDITION PLAN VIEW
 YEAR 3 MONITORING



Prepared for:
 Ecosystem Enhancement Program
 2728 Capital Blvd., Suite H 103
 Raleigh, NC 27604
 Phone: 919-716-0476
 Fax: 919-716-2219

| | |
|-------------------|-----------|
| EEP Project No. | 92665 |
| Baker Project No. | 111085 |
| Date: | 2/11/2015 |
| DESIGNED: | JEM |
| DRAWN: | MJR |
| APPROVED: | MMC |
| Monitoring Year: | 3 of 5 |
| Sheet: | 4 of 4 |

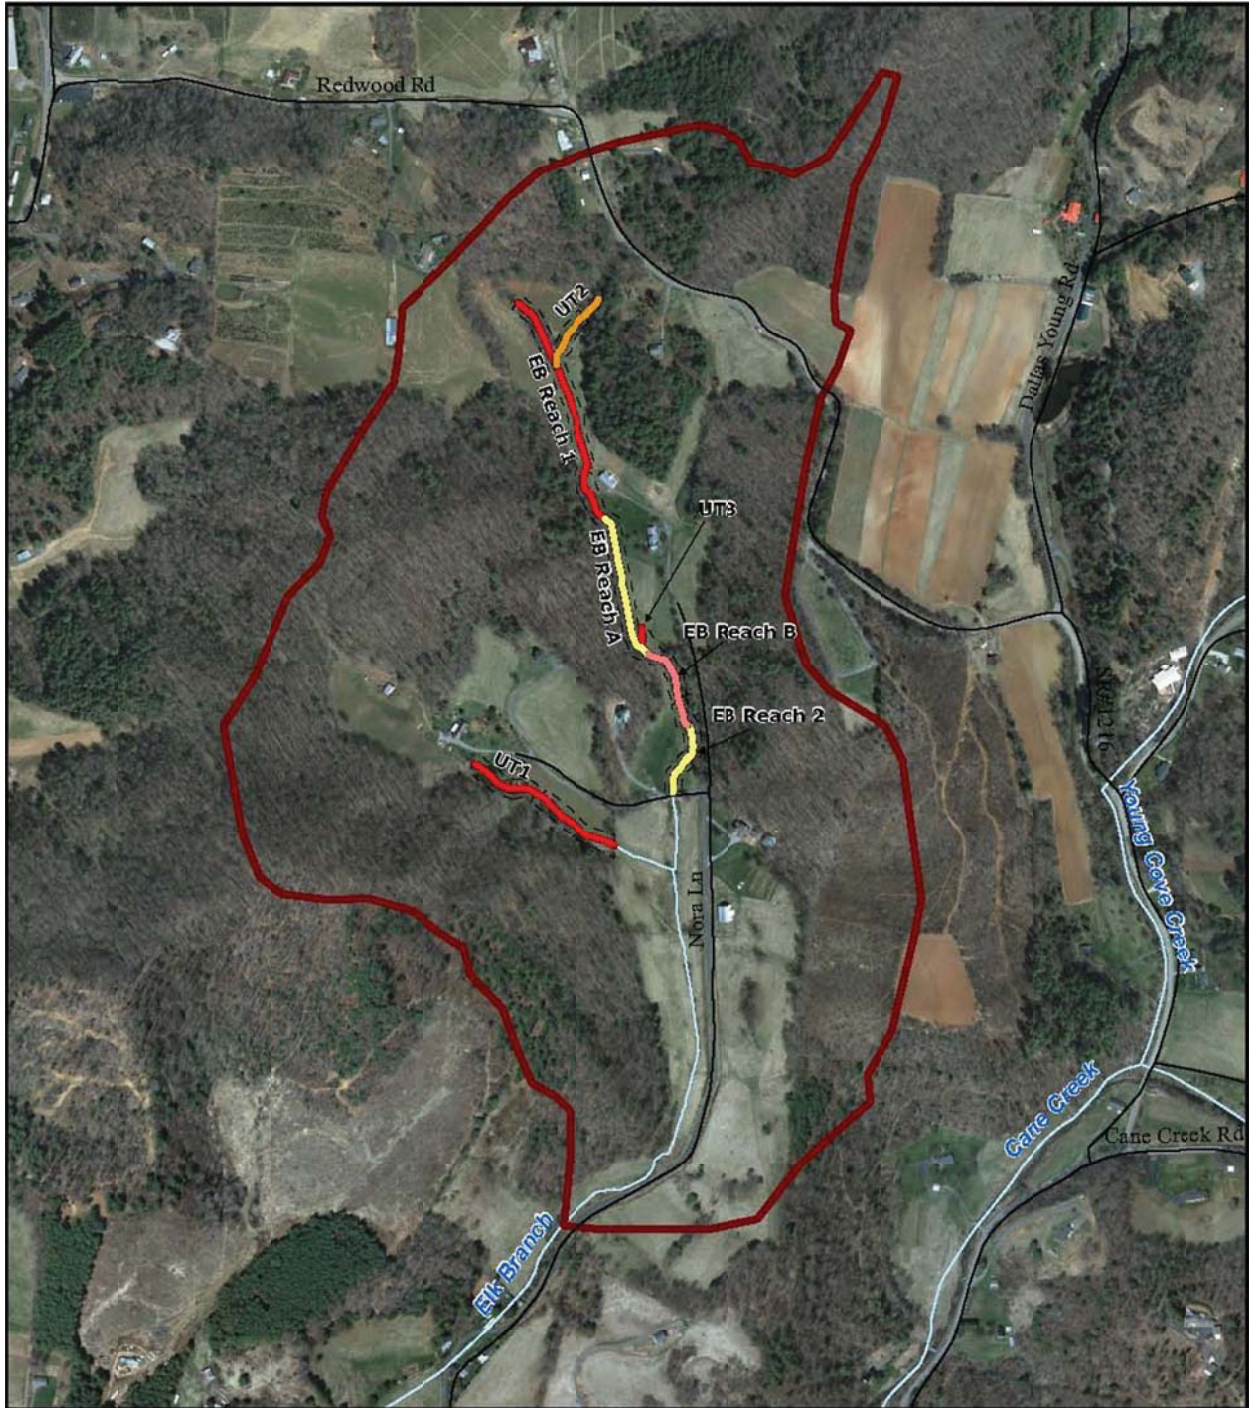

LEGEND:

- Proposed Project Component
- Enhancement 1
 - Priority 1 Restoration
 - Priority 2 Restoration
 - Priority I & 2 Restoration

- Proposed Easement Boundary
- Streams
- Watershed Boundary

0 200 400 800 Feet



Figure 2. Project Approach

Elk Branch Restoration Project
Mitchell County, NC



2.0 PROJECT CONDITION AND MONITORING RESULTS

The five-year monitoring plan for the Elk Branch mitigation project includes criteria to evaluate the success of the vegetation and channel components of the project. The specific locations of vegetation plots, permanent cross-sections, reference photo stations and crest gauges are shown on the Year 3 Current Condition Plan View shown above.

2.1 Vegetation Assessment

2.1.1 Vegetation

Successful restoration of the vegetation on a site is dependent upon hydrologic restoration, active planting of preferred canopy species, and volunteer regeneration of the native plant community. In order to determine if the criteria are achieved, six vegetation monitoring quadrants were installed across the restoration site. The size of individual quadrants vary from 100 square meters for tree species to 1 square meter for herbaceous vegetation. Individual quadrant data provided during subsequent monitoring events will include diameter, height, density, and coverage quantities. Individual seedlings will be marked to ensure that they can be found in succeeding monitoring years. Survival will be determined from the difference between the previous year's living, planted seedlings and the current year's living, planted seedlings.

Photographs are used to visually document vegetation success in sample plots. Reference photos of tree and herbaceous plots are taken at least once per year to indicate vegetation condition within the plots. Photos of the plots are included in Appendix A of this report.

The interim measure of vegetative success for the site is the survival of at least 320, 3-year old, planted trees per acre at the end of the Year 3 monitoring period. The final vegetative success criteria is the survival of 260, 5-year old, planted trees per acre at the end of the Year 5 monitoring period. If the measurement of vegetative density proves to be inadequate for assessing plant community health, additional plant community indices may be incorporated into the vegetation monitoring plan as requested by the NCEEP.

Temporary seeding applied to streambanks beneath the erosion matting sprouted within two weeks of application and has provided excellent ground coverage. Live stakes and bare root trees planted are also providing streambank stability. Bare-root trees were planted throughout the conservation easement. A minimum 60-foot-wide conservation easement was established along the project streams during initial design (this is in addition to the stream width). After final design, a buffer width of 30 feet on either side of the stream was achieved in most areas. In some areas, regulatory comments or ultimate field design changes resulted in varying buffer widths. In general, bare-root vegetation was planted at a target density of 537 stems per acre, in a 9-foot by 9-foot grid pattern. Planting of bare-root trees was completed in January 2012. Species planted are listed below.

Table 5. Riparian Buffer Plantings
Elk Branch Mitigation Project- NCEEP Project #92665

| Common Name | Scientific Name | % Planted by Species | Planting Totals | Wetness Tolerance |
|---|--------------------------------|----------------------|-----------------|-------------------|
| <u>Riparian Buffer Plantings</u> | | | | |
| Trees | | | | |
| Red Maple | <i>Acer rubrum</i> | 5 | 100 | FAC |
| River Birch | <i>Betula nigra</i> | 5 | 100 | FACW |
| Shagbark hickory | <i>Carya ovata</i> | 5 | 100 | FACU |
| Persimmon | <i>Diospyros virginiana</i> | 5 | 100 | FAC |
| Tulip Poplar | <i>Liriodendron tulipifera</i> | 5 | 100 | FAC |
| Black gum | <i>Nyssa sylvatica</i> | 5 | 100 | FAC |
| Sycamore | <i>Platanus occidentalis</i> | 5 | 100 | FACW- |
| White Oak | <i>Quercus alba</i> | 5 | 100 | FACU |
| Northern Red Oak | <i>Quercus rubra</i> | 5 | 100 | FACU |
| Shrubs | | | | |
| Tag Alder | <i>Alnus serrulata</i> | 10 | 200 | OBL |
| Sweet shrub | <i>Calycanthus floridus</i> | 10 | 300 | FACU |
| Ironwood | <i>Carpinus caroliniana</i> | 5 | 300 | FAC |
| Flowering Dogwood | <i>Cornus florida</i> | 5 | 400 | FACU |
| Hazelnut | <i>Corylus americana</i> | 5 | 50 | FACU |
| Witch Hazel | <i>Hamamelis virginiana</i> | 5 | 400 | FACU |
| Spicebush | <i>Lindera benzoin</i> | 5 | 100 | FACW |
| Elderberry | <i>Sambucus canadensis</i> | 5 | 200 | FAC |
| Highbush Blueberry | <i>Vaccinium sp</i> | 5 | 200 | FACU |
| <u>Riparian Livestake Plantings</u> | | | | |
| Ninebark | <i>Physocarpus opulifolius</i> | 10 | | FAC- |
| Elderberry | <i>Sambucus canadensis</i> | 20 | | FACW- |
| Black Willow | <i>Salix nigra</i> | 10 or less | | OBL |
| Silky Willow | <i>Salix sericea</i> | 35 | | OBL |
| Silky Dogwood | <i>Cornus amomum</i> | 25 | | FACW+ |
| *Note: In previous mitigation reports (As-Built to YR2) this table indicated those species that were requested to be planted; however, with this report we have corrected this table to indicate what was actually planted. Total numbers of livestock installed was not recorded by the planter. | | | | |

2.1.2 Soil Data

| Table 6. Preliminary Soil Data Elk Branch Mitigation Project-NCEEP Project #92665 | | | | | |
|---|---|-------------------|------------------|----------|------|
| Dominant Soil Series and Characteristics | Bandana/ Fannin/Saunook - Thunder/Saunook | | | | |
| | Depth (in.) | % Clay | K Factor | T Factor | % OM |
| Elk Branch Reach 1 | >60" | 7-20/12-27, 5-35 | .24/.05, .32 | 5 | 4-10 |
| Reach A | >60" | 7-20/12-27, 5-35 | .24/.05, .32 | 5 | 0-10 |
| Reach B | >60" | 7-20/12-27, 5-35 | .24/.05, .32 | 5 | 4-10 |
| Elk Branch Reach 2 | >60" | 7-20/12-27, 10-20 | .24/.05, .2 | 5,4 | 4-10 |
| UT1 | >60" | 7-20/12-27 | .24/.05 | 5 | 0-10 |
| UT2 | >60" | 7-20/12-27, 12-35 | .24/.05, .15-.32 | 5 | 4-10 |

2.1.3 Vegetative Problem Areas

Currently, there are no vegetative problem areas.

2.1.4 Stem Counts

The mitigation plan for the Elk Branch Site specifies that the number of quadrants required will be based on the species/area curve method, as described in NCEEP monitoring guidance documents. The size of individual quadrants is 100 square meters for woody tree species, and 1 square meter for herbaceous vegetation. A total of six vegetation plots, each 10 by 10 meters or 5 by 20 meters in size, were established across the restored site.

2.1.4.1 Results

Table 7 in Appendix A presents information on the stem counts for each of the vegetation monitoring plots. Data from Year 3 monitoring showed a range of 202-526 planted stems per acre, with approximately 90% of the stems showing no signs of damage. The average density of planted bare root or livestake stems, based on data collected from the six monitoring plots during Year 3 monitoring, is 357 stems per acre which indicates that the Site has met the minimum interim success criteria of 320 trees per acre at the end of Year 3 and is on track to meet the final success criteria of 260 trees per acre by the end of Year 5. The locations of the vegetation plots are shown on the Year 3 Current Condition Plan View.

As shown in Table 8 (Appendix A), no woody or herbaceous vegetation problem areas were identified during Year 3 monitoring. Although the density of herbaceous cover varies across the site, conditions observed during the Year 3 monitoring survey found ground cover in the easement area to be sufficient for providing site stabilization. Based on the plot data collected, plots 2, 3 and 4 are not currently meeting the success criteria with 202, 243 and 243 trees per acre respectively. The lower density recorded may be attributed to the orientation of the plots and planted trees, in which bare roots were planted in relation to the layout of these 5x20' vegetation plots, and the measurement of stem offsets (9'x9') as described in the Baseline Monitoring Document. Wet conditions from ground water on or near the surface may also be the cause of vegetation mortality in these plots. In other instances, lower densities can be attributed to damage brought about by animals and competition with dense herbaceous cover. Survival rates of planted woody stems in the vegetation plots indicate that plantings across the easement area are of sufficient density to meet regulatory requirements, as well as the site stabilization and habitat

enhancement goals originally set forth in the mitigation plan. The eventual onset of volunteer trees will further aid in site stabilization and habitat improvements. Additional trees were not planted at this site in the fall 2014. However, due to the low survival of trees in half the plots during this monitoring year, which represent areas of the riparian zone that may be experiencing low survival, Baker is pursuing additional plantings within the buffer area near these plots. A photo log of the vegetation plots is provided in Appendix A.

2.2 Stream Assessment

2.2.1 Morphologic Parameters and Channel Stability

Geomorphic monitoring of restored stream reaches is being conducted over a five year period to evaluate the effectiveness of the restoration practices installed. Monitored stream parameters include channel dimension (cross-sections), profile (longitudinal survey), pattern, bed composition, bank stability, bankfull flows, and stability of reference sites documented by photographs. Crest gauges, as well as high flow marks, will be used to document the occurrence of bankfull events. The methods used and any related success criteria are described below for each parameter. To monitor stream success criteria, eleven permanent cross-sections, six longitudinal profile sections and two crest gauges were installed.

2.2.1.1 Dimension

Eleven permanent cross-sections were installed to help evaluate the success of the mitigation project; data and graphics are provided in Appendix B. Permanent cross-sections were established throughout the project site as follows: five cross-sections were located on Elk Branch, four cross-sections were located on UT1 and two cross-sections were located on UT2. Cross-sections selected for monitoring were located in representative riffle and pool reaches, and each cross-section was marked on both banks with permanent pins to establish the exact transect to be used year-to-year. A common horizontal and vertical reference is used for cross-sections and consistently referenced to facilitate comparison of year-to-year data. The cross-sectional surveys include points measured at all breaks in slope, including top of bank, bankfull, inner berm, edge of water, and thalweg, if the features are discernible. Riffle cross-sections are classified using the Rosgen Stream Classification System.

Although minor changes are not uncommon, there should not be any significant changes in the as-built cross-sections. If changes do take place, they will be evaluated to determine if they represent a movement toward a more unstable condition (e.g., down-cutting or erosion) or a movement toward increased stability (e.g., settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). At this time, cross-sectional measurements do not indicate any streambank or channel stability issues.

2.2.1.1.1 Results

As-built cross-section monitoring data for stream stability was collected in July 2011. The eleven permanent cross-sections along the restored channels were resurveyed in November and December of 2014 to document stream dimension for Monitoring Year 3. Cross-sectional data is presented in Appendix B and the location of cross-sections is shown on the Year 3 Current Condition Plan View submitted with this report.

The cross-sections show that there has been little adjustment to stream dimension across the project reaches since construction. What adjustment that has occurred has primarily been observed in riffle cross-sections that are exhibiting signs of narrowing, or depending of flow for the year, deepening of pools may be observed. Based on field observation, the narrowing can

be attributed to thick herbaceous vegetation becoming well established. At this time, cross-sectional measurements do not indicate any streambank or channel stability issues.

2.2.1.2 Pattern and Longitudinal Profile

Longitudinal profiles for Year 3 were surveyed during November and December 2014; profiles of the various project reaches are provided in Appendix B. A longitudinal profile was completed for the entire project length of Elk Branch, UT1 and UT2 to evaluate changes in channel bed conditions since the as-built survey was completed. Longitudinal profiles will be replicated annually during the five year monitoring period.

Measurements taken during longitudinal profiles include thalweg, water surface, and top of low bank. The pools should remain relatively deep with flat water surface slopes, and the riffles should remain steeper and shallower than the pools. Bed form observations should be consistent with those observed for channels of the design stream type. Profile data collected reflect stable channel bedform and a diverse range of riffle and pool complexes.

All measurements were taken at the head of each feature (e.g., riffle, run, pool, or glide) and at the maximum pool depth. Elevations of grade control structures were also included in longitudinal profiles surveyed. Surveys were tied to permanent horizontal and vertical control. Thick herbaceous vegetation made it difficult to locate some grade control structures during 2014. The longitudinal profiles show that the bed features are stable. Where the channel slopes are steeper, closely-spaced grade control structures should help maintain the overall profile desired and there was no significant bank erosion observed as a result of the channel profile adjustments.

Although pattern adjustments were made, Elk Branch and its tributaries are primarily Cb-type streams characterized by step-pool sequences, and increased sinuosity is not a design goal, nor a typical characteristic of this channel type. Pattern information is not provided in Appendix B, as this information is generally only provided for meandering, alluvial channels. Nevertheless, as the site is monitored, reaches will be evaluated for significant changes in pattern and any changes warranting repair work will be discussed in future monitoring reports.

2.2.1.2.1 Results

The longitudinal profiles show that the bed features are stable across the project site. As noted in the Stream Reach Morphology Data Tables in Appendix B (Tables 13 and 14), riffle and pool characteristics do not appear to have changed much and are acceptable when compared to reference reach and design data provided for the project reaches. Last year it was noted that pool depth had increased in many of the pools shown on the profile, due to high flow conditions during the year. While 2014 has had a number of high water events, some of the pools have decreased in depth during this year as sediment moving within the system has reduced pool depth to a minor degree. Given the location of these project reaches in the valley and the spacing of structures in these streams, it is expected that the profiles will display little significant change over the course of the monitoring period.

It was noted in the Year 1 monitoring survey data that UT2 had subsurface flow for 103 linear feet. In Year 2 this subsurface flow decreased to one section where the flow was subsurface for 20 linear feet. This 3rd year of sampling did not indicate any areas of subsurface flow. As indicated last year high flows within the channel during 2013 and 2014 moved sediment and fines through the system. This may have helped seal any areas within the bed or around structures where water was discovering a subsurface path to follow. No areas of instability were noted in the project area during Year 3 monitoring.

2.2.1.3 Substrate and Sediment Transport

Bed material analysis consists of conducting a pebble count in the same constructed riffle during annual geomorphic surveys of the project site. This sample will reveal changes in sediment gradation that occur over time as the stream adjusts to upstream sediment loading and transport out of the study reaches. Significant changes in sediment gradation will be evaluated with respect to stream stability and watershed changes.

2.2.1.3.1 Results

For this project, a pebble count was collected in Reach A of Elk Branch. As noted in the pebble count exhibit in Appendix B, the pebble count for Reach A of Elk Branch indicates a general coarsening of the bedload. Visual observations of Elk Branch and its tributaries and a review of pebble count data collected did not yield any signs that sediment transport functions have been hampered by the mitigation project; specifically, no significant areas of aggradation or degradation within the project area were observed during the Year 3 monitoring survey.

2.2.2 Hydrology

2.2.2.1 Streams

The occurrence of bankfull events within the monitoring period is being documented by the use of crest gauges and photographs. Crest gauges were installed on the floodplain at bankfull elevation. One crest gauge was placed near the end of Reach 2 of Elk Branch while another gauge was set up near the end of the project area on UT1 to Elk Branch. The crest gauges will record the highest watermark between site visits and will be checked at each site visit to determine if a bankfull event has occurred. Photographs will be used to document the occurrence of debris lines and sediment deposition on the floodplain during monitoring site visits.

Two bankfull flow events must be documented on each crest gauge within the 5-year monitoring period. The two bankfull events must occur in separate years; otherwise, the stream monitoring will continue until two bankfull events have been documented in separate years.

2.2.2.1.1 Results

Since the time of the As-built survey, the Site was found to have had at least two bankfull events, during different years based on crest gauge readings obtained on the mainstem and UT1. Information on these events is provided in Table 9 of Appendix B.

2.2.3 Photographic Documentation of Site

Photographs will be used to document restoration success visually. Reference stations were photographed during the as-built survey; this will be repeated for at least five years following construction. Reference photos are taken once a year, from a height of approximately five to six feet. Permanent markers will ensure that the same locations (and view directions) are utilized during each monitoring period. Selected site photographs are shown in Appendix B.

2.2.3.1 Lateral Reference Photos

Reference photo transects were taken of the right and left banks at each permanent cross-section. A survey tape was captured in most photographs which represents the cross-section line located perpendicular to the channel flow. The water line was located in the lower edge of the frame in order to document bank and riparian conditions. Photographers will make an effort to consistently maintain the same area in each photo over time.

2.2.3.2 Structure Photos

Photographs of primary grade control structures (i.e. vanes and weirs), along the restored streams are included within the photographs taken at reference photo stations. Photographers will make every effort to consistently maintain the same area in each photo over time.

Lateral and structure photographs are used to evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, structure function and stability, and a subjective judgment of the effectiveness of erosion control measures. Lateral photos should not indicate excessive erosion or degradation of the banks. A series of photos over time should indicate successive maturation of riparian vegetation and consistent structure function.

2.2.3.2.1 Results

Photographs of the restoration project were taken in November and December 2014. The photographs illustrate stable conditions across the project site. Vegetative growth along the streambanks and riparian buffers has become dense and has improved since construction was completed in 2011. Structures are functioning as designed. While the same photo stations have been maintained, the ability to observe structures is limited at this site due to the thick herbaceous vegetation that overhangs the channel and most of the structures.

2.2.4 Stream Stability Assessment

In-stream structures installed within the restored streams included constructed riffles, log drops, log sequences, and boulder steps. The Year 3 visual observations of these structures indicate that little or no changes have occurred since the baseline survey was performed; structures are functioning as designed and are holding their elevation and grade. Frequent spacing of log drops, log sequences and boulder drops have greatly enhanced bedform diversity as well as promoting more stable C and B-type channels. The Categorical Stream Feature Visual Stability Assessment and Visual Morphological Stability Assessment tables in Appendix B (Tables 11 and 12), summarize the condition of project structures.

Quantitative reference reach and design data used to determine the restoration approach, as built data, as well as Year 3 monitoring data are summarized in Tables 13 and 14 of Appendix B.

2.3 Areas of Concern

At this time, there are no areas of concern. As previously noted in the As-built report, additional planting is proposed because of our concern that stem density may be insufficient to meet vegetation success criteria at some locations within the project site. Based on Year 3 monitoring data, increasing stem density by planting additional trees is unnecessary based on the guidelines; however, we desire to exceed the guideline density at closeout. Because wet conditions appear to me the main issue we will do supplemental planting with more wet tolerant species in the areas showing a need.

APPENDIX A

VEGETATION RAW DATA

- 1. VEGETATION SURVEY DATA TABLES**
- 2. VEGETATION MONITORING PLOT PHOTOS**

| Table 7b. Stem Count Arranged by Plot (Planted vs. Total) Elk Branch Mitigation Project-#92665 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|---|--------------------|--------------|------------------------------|-------|-------|----------------|-------|-------|----------------|-------|-------|----------------|-------|-------|----------------|-------|-------|----------------|-------|------|--------------|-------|------|------------|-------|------|------------|-------|------|------------|-------|-----|---|
| Scientific Name | Common Name | Species Type | Current Plot Data (MY3 2014) | | | | | | | | | | | | | | | | | | Annual Means | | | | | | | | | | | | |
| | | | E92665-01-0001 | | | E92665-01-0002 | | | E92665-01-0003 | | | E92665-01-0004 | | | E92665-01-0005 | | | E92665-01-0006 | | | MY3 (2014) | | | MY2 (2013) | | | MY1 (2012) | | | MY0 (2011) | | | |
| | | | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | PnoLS | P-all | T | |
| <i>Acer rubrum</i> | red maple | Tree | 6 | 6 | 6 | 3 | 3 | 3 | 1 | 1 | 1 | 1 | 1 | 1 | | | | 6 | 6 | 6 | 17 | 17 | 17 | 17 | 17 | 17 | 19 | 19 | 19 | 19 | 19 | 19 | |
| <i>Alnus serrulata</i> | hazel alder | Tree | | | | | | | 3 | 3 | 3 | | | | 3 | 3 | 3 | 1 | 1 | 1 | 7 | 7 | 7 | 7 | 7 | 7 | 7 | 7 | 7 | 7 | 7 | | |
| <i>Betula nigra</i> | river birch | Tree | 2 | 2 | 2 | | | | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | | | | 5 | 5 | 5 | 5 | 5 | 5 | 5 | 5 | 5 | 3 | 3 | 3 | |
| <i>Carya ovata</i> | shagbark hickory | Tree | 3 | 3 | 3 | | | | 1 | 1 | 1 | | | | | | | 3 | 3 | 3 | 7 | 7 | 7 | 11 | 11 | 11 | 15 | 15 | 15 | 16 | 16 | 16 | |
| <i>Catalpa ovata</i> | Chinese catalpa | Tree | | | | | | | | | | | | | | | | | | | | | | | | | | | | 1 | 1 | 1 | |
| <i>Corylus americana</i> | American hazelnut | Tree | | | | | | | | | | | | | | | | | | | | | | | | | | | 1 | 1 | 1 | | |
| <i>Diospyros virginiana</i> | common persimmon | Tree | 1 | 1 | 1 | 1 | 1 | 1 | | | | | | | 1 | 1 | 1 | | | | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | 3 | |
| <i>Juglans nigra</i> | black walnut | Tree | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <i>Lindera benzoin</i> | northern spicebush | Shrub | | | | | | | | | | | | 2 | 2 | 2 | | | | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 4 | 4 | 4 | |
| <i>Liriodendron tulipifera</i> | tuliptree | Tree | 1 | 1 | 1 | | | | | | | | | 1 | 1 | 1 | | | | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 4 | 4 | 4 | | |
| <i>Platanus occidentalis</i> | American sycamore | Tree | | | | | | | | | | 4 | 4 | 4 | | | | 1 | 1 | 1 | 6 | 6 | 6 | 6 | 6 | 6 | 7 | 7 | 7 | 8 | 8 | 8 | |
| <i>Quercus rubra</i> | northern red oak | Tree | | | | | | | | | | | | 2 | 2 | 2 | | | | 2 | 2 | 2 | 4 | 4 | 4 | 5 | 5 | 5 | 5 | 5 | 5 | | |
| <i>Salix nigra</i> | black willow | Tree | | | | 1 | 1 | 1 | | | | | | 1 | 1 | 1 | | | | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | 2 | | |
| <i>Vaccinium</i> | blueberry | Shrub | | | | | | | | | | | | | | | | | | | | | | | | | | | 1 | 1 | 1 | 1 | 1 |
| | Stem count | | 13 | 13 | 13 | 5 | 5 | 5 | 6 | 6 | 6 | 6 | 6 | 12 | 12 | 12 | 11 | 11 | 11 | 53 | 53 | 53 | 60 | 60 | 60 | 69 | 69 | 69 | 65 | 65 | 65 | | |
| | size (ares) | | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | 6 | |
| | size (ACRES) | | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.025 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | 0.15 | | |
| | Species count | | 5 | 5 | 5 | 3 | 3 | 3 | 4 | 4 | 4 | 3 | 3 | 3 | 8 | 8 | 8 | 4 | 4 | 4 | 10 | 10 | 10 | 11 | 11 | 11 | 12 | 12 | 12 | 11 | 11 | 11 | |
| | Stems per ACRE | | 526 | 526 | 526 | 202 | 202 | 202 | 243 | 243 | 243 | 243 | 243 | 243 | 486 | 486 | 486 | 445 | 445 | 445 | 357 | 357 | 357 | 405 | 405 | 405 | 465 | 465 | 465 | 438 | 438 | 438 | |

Table 7b. Elk Branch Stem Count Arranged by Plot (Planted vs. Total)

| Table 8. Vegetation Problem Areas | | | |
|--|-------------|-----------------|--------------|
| Elk Branch Mitigation Project: Project No. 92665 | | | |
| Elk Branch Reach 1 (951 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| Elk Branch Reach A (592 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| Elk Branch Reach B (403 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| Elk Branch Reach 2 (279 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| UT1 to Elk Branch (656 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| UT2 to Elk Branch (242 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |
| UT3 to Elk Branch (36 LF) | | | |
| Feature Issue | Station No. | Suspected Cause | Photo Number |
| Other | N/A | N/A | N/A |
| Bare Bank | N/A | N/A | N/A |
| Bare Bench | N/A | N/A | N/A |
| Bare Flood Plain | N/A | N/A | N/A |
| Invasive/Exotic Populations | N/A | N/A | N/A |

Elk Branch Mitigation Projects

Photo Log – Vegetation Plot Photo Points (Year 3)

Notes: Photos for Elk Branch vegetation plots were taken November 22, 2014

1. Vegetation plots marked by t-posts at corners; herbaceous plot marked by stake within larger plot.
2. Planted vegetation flagged and tagged for future identification.



Photo 1: Veg. Plot 1



Photo 2: Veg Plot 1, Herbaceous Plot



Photo 3: Veg Plot 2



Photo 4: Veg Plot 2: Herbaceous Plot



Photo 5: Veg Plot 3



Photo 6: Veg Plot 3: Herbaceous Plot



Photo 7: Veg Plot 4



Photo 8: Veg Plot 4: Herbaceous Plot



Photo 9: Veg Plot 5



Photo 10: Veg Plot 5: Herbaceous Plot



Photo 11: Veg Plot 6



Photo 12: Veg Plot 6: Herbaceous Plot

APPENDIX B

- 1. HYDROLOGICAL (BANKFULL) VERIFICATIONS (TABLE 9)**
- 2. STREAM PROBLEM AREAS (TABLE 10)**
- 3. CROSS-SECTION PLOTS WITH ANNUAL OVERLAYS**
- 4. LONGITUDINAL PROFILES WITH ANNUAL OVERLAYS**
- 5. CATEGORICAL STREAM FEATURE VISUAL STABILITY ASSESSMENT (TABLE 11)**
- 6. VISUAL MORPHOLOGICAL STABILITY ASSESSMENT (TABLE 12)**
- 7. STREAM REACH MORPHOLOGY AND HYDRAULIC DATA (TABLE 13)**
- 8. CROSS-SECTION MORPHOLOGY AND HYDRAULIC DATA (TABLE 14)**
- 9. RIFFLE PEBBLE COUNT SIZE CLASS DISTRIBUTIONS**
- 10. STREAM REFERENCE STATION PHOTO LOGS**

| Table 9. Hydrological (Bankfull) Verifications | | | | |
|---|--------------------------------|---------------------------|---------------------------------|--------|
| Elk Branch Mitigation Project-#92665 | | | | |
| Date of Data Collection | Date of Event | Method of Data Collection | Gauge Watermark Height (inches) | |
| | | | Elk Branch Reach 2 | UT1 |
| 10/25/2012 | Between July 2011 and 10/25/12 | Gauge measurement. | 6", 2.4" | 3" |
| 11/27/2013 | Between 10/25/12 and 11/27/13 | Gauge measurement. | 1.6" | 4.12" |
| 11/25/2014 | Between 11/27/13 and 11/25/14 | Gauge measurement. | 1.5" | 25.5"* |

*Cork in the crest gauge was this high on staff but we question accuracy, do believe a banfull flow was recorded.

| Table 10. Stream Problem Areas | | | | |
|---------------------------------------|-------------------------------|-------------|--|--------------|
| Elk Branch Mitigation Project-#92665 | | | | |
| MY | Feature Issue | Station No. | Suspected Cause | Photo Number |
| 1 | Lack of continuous flow (UT2) | 1+07-1+19 | Survey conducted in summer during time with lack of significant rainfall | --- |
| | | 1+25-1+42 | | --- |
| | | 1+48-2+06 | | --- |
| | | 2+16-2+32 | | --- |
| 2 | Lack of continuous flow (UT2) | 1+43-1+63 | Structure may not be completely sealed on upstream end | --- |
| 3 | NONE | | | --- |

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|-----|----------|----------|
| Riffle | Cb | 3.1 | 6.4 | 0.49 | 0.88 | 13.04 | 1 | 4.8 | 2620.47 | 2620.47 |

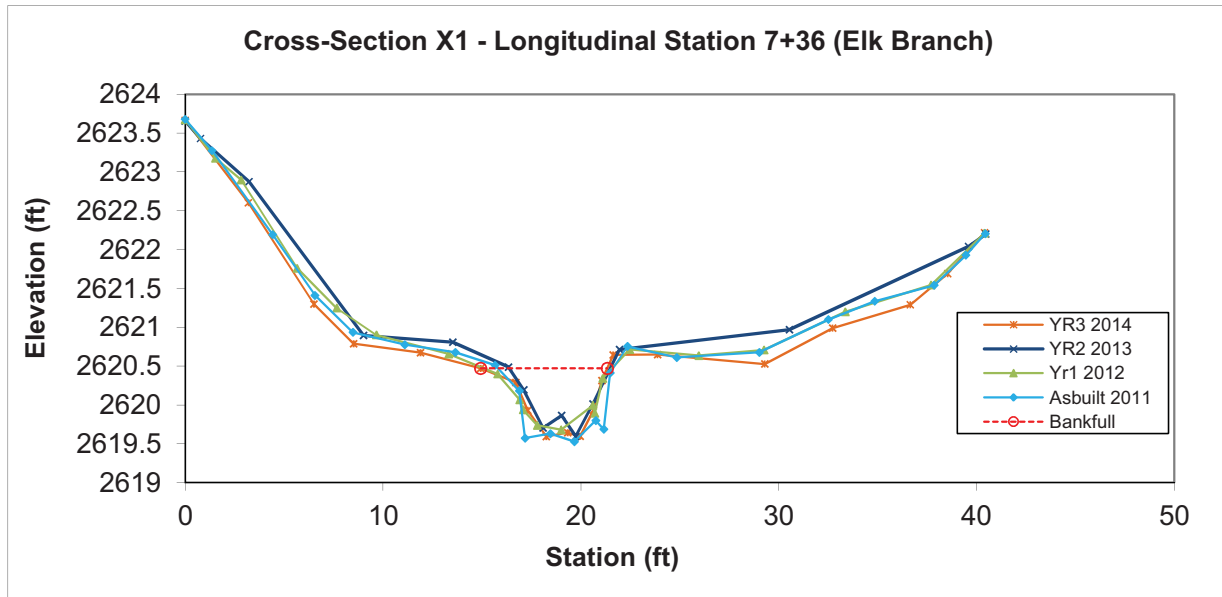


Photo 1: XS-1 facing right bank



Photo 2: XS-1 facing left bank

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|------|----------|-----|----------|----------|
| Pool | | 6.4 | 6.68 | 0.96 | 1.94 | 6.94 | 1.1 | 4.9 | 2604.35 | 2604.51 |

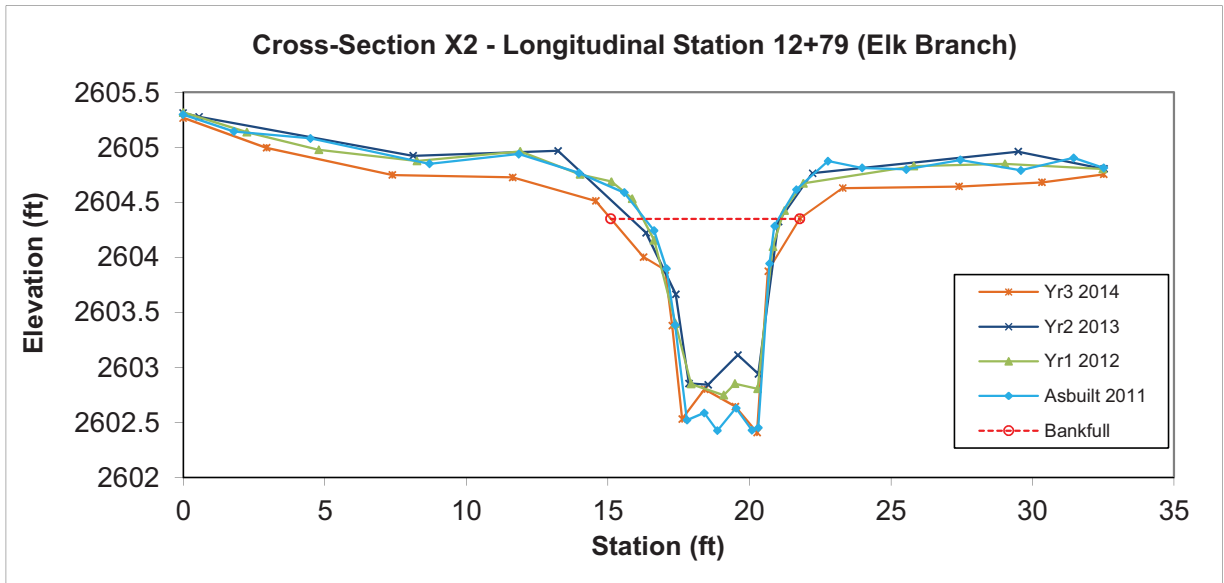


Photo 3: XS-2 facing right bank



Photo 4: XS-2 facing right bank at the channel



Photo 5: XS-2 facing left bank



Photo 6: XS-2 facing left bank at the channel

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|-----|----------|----------|
| Riffle | Cb | 2.7 | 7.87 | 0.34 | 0.77 | 22.84 | 1 | 3.9 | 2599.16 | 2599.16 |

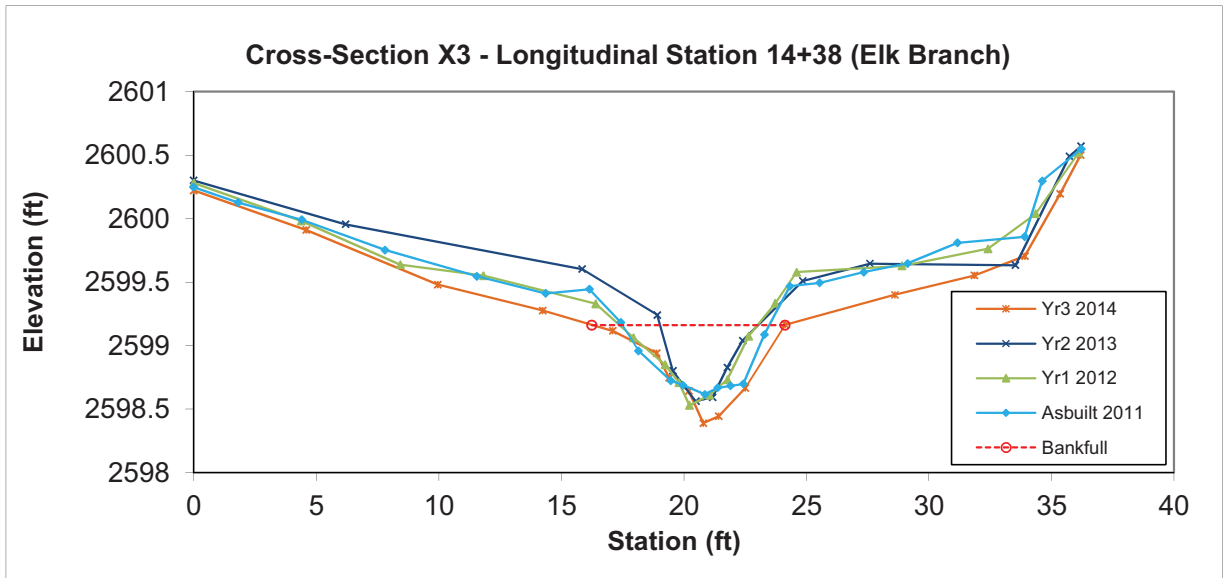


Photo 7: XS-3 facing right bank



Photo 8: XS-3 facing right bank at the channel



Photo 9: XS-3 facing left bank



Photo 10: XS-3 facing downstream

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|-----|----------|----------|
| Riffle | Cb | 5.1 | 12.64 | 0.4 | 0.93 | 31.27 | 1 | 3.5 | 2587.5 | 2587.51 |

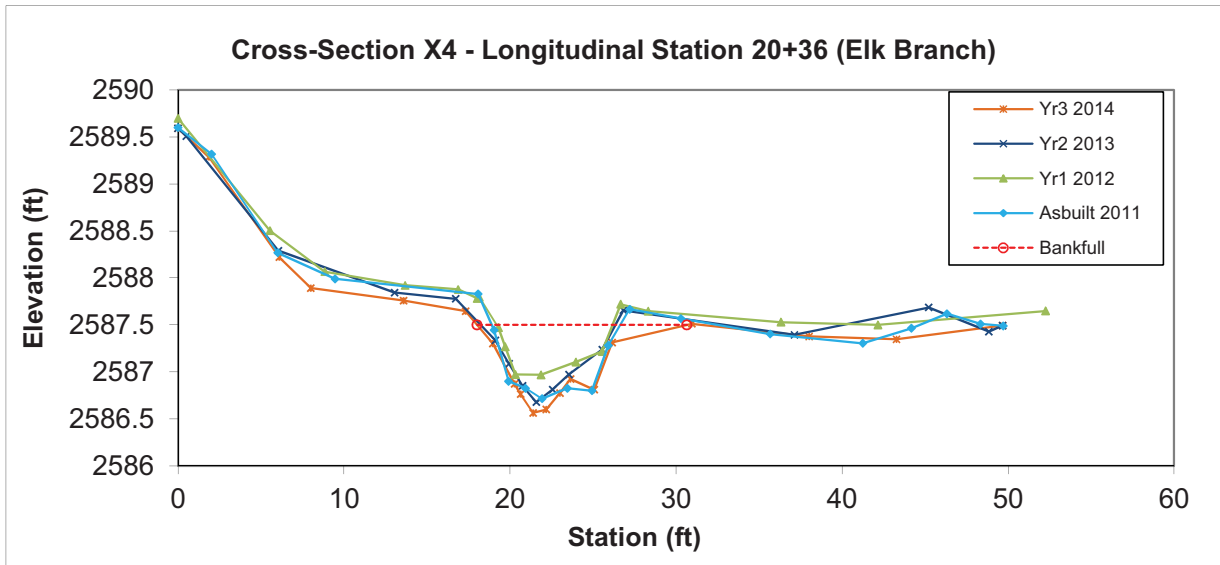


Photo 11: XS-4 facing right bank



Photo 12: XS-4 facing right bank at the channel



Photo 13: XS-4 facing left bank



Photo 14: XS-4 facing left bank at the channel

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|-----|----------|----------|
| Pool | | 9.4 | 12.9 | 0.73 | 2.21 | 17.67 | 1 | 3.4 | 2583.13 | 2583.14 |

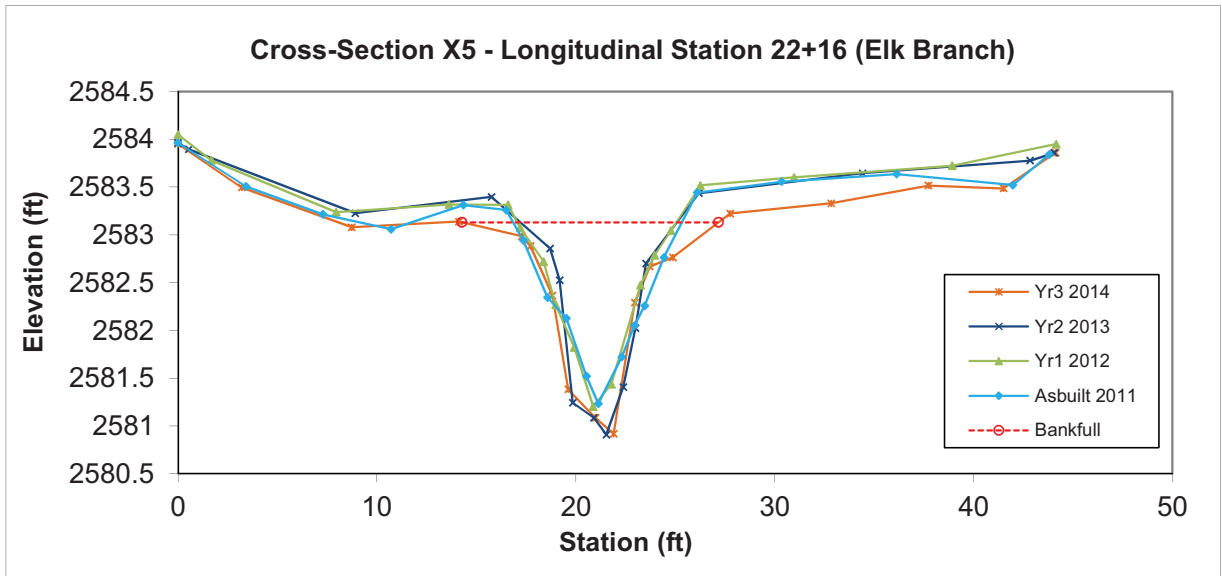


Photo 15: XS-5 facing left bank



Photo 16: XS-5 facing left bank at the channel



Photo 17: XS-5 facing right bank



Photo 18: XS-5 facing right bank at the channel

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|------|----------|-----|----------|----------|
| Riffle | | 2.1 | 6.7 | 0.32 | 0.67 | 21.1 | 1 | 5.1 | 2607.93 | 2607.93 |

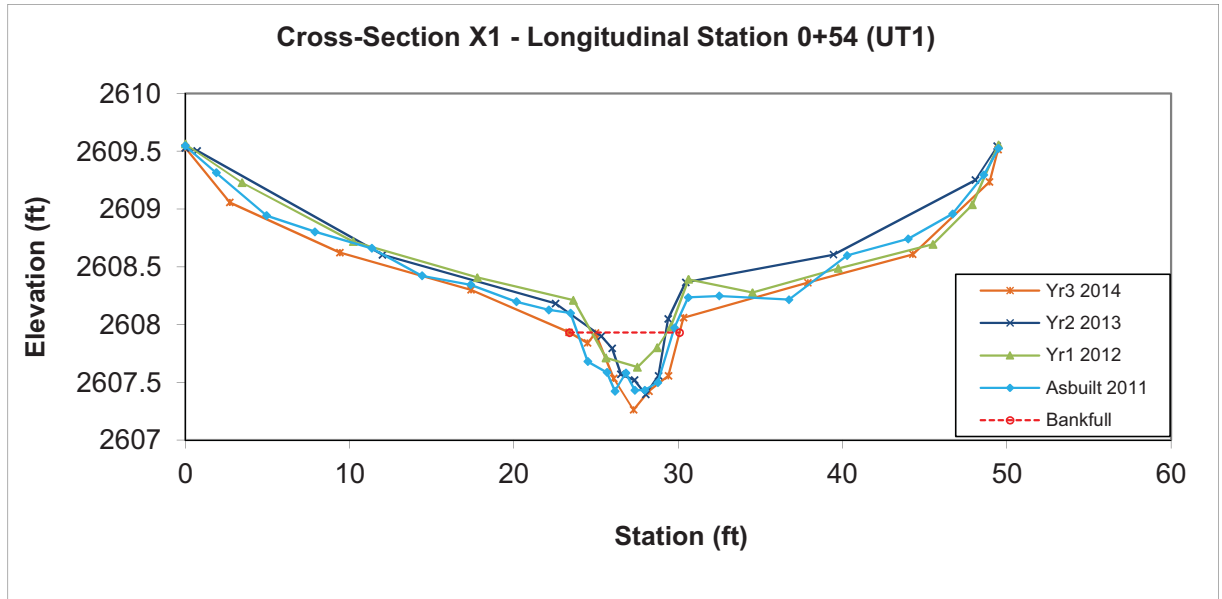


Photo 1: XS-1 facing left bank, showing fallen willow tree laying across transect, storm damage.



Photo 2: XS-1 facing the right bank, showing fallen willow tree laying across transect, storm damage.

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|------|----------|-----|----------|----------|
| Riffle | | 4.7 | 7.95 | 0.59 | 1.18 | 13.4 | 1 | 5.6 | 2599.9 | 2599.91 |

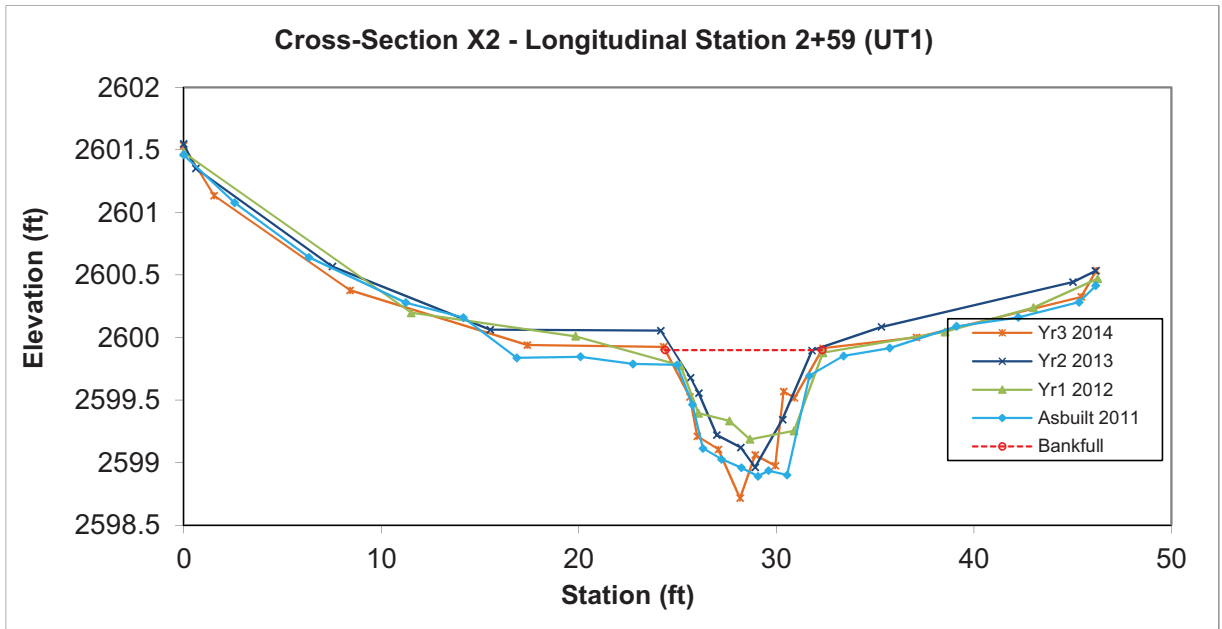


Photo 3: XS-2 facing right bank



Photo 4: XS-2 facing left bank

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|----|----------|----------|
| Riffle | Cb | 5 | 9.83 | 0.5 | 1.33 | 19.47 | 1 | 4 | 2592.19 | 2592.19 |

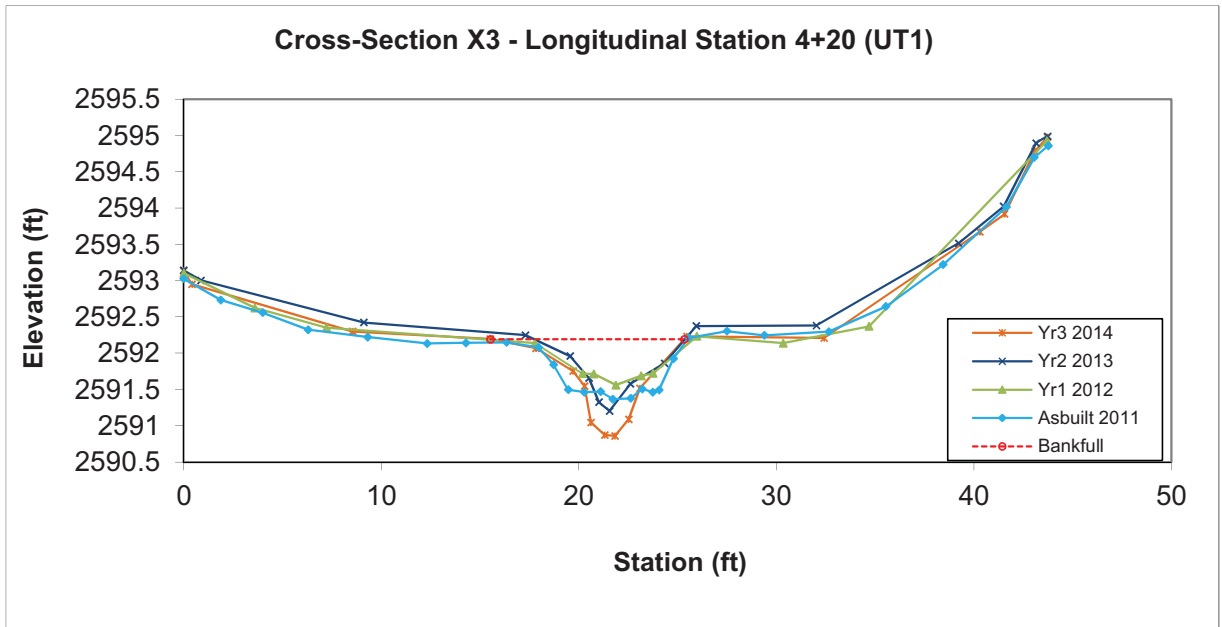


Photo 5: XS-3 facing left bank



Photo 6: XS-3 facing right bank

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|------|----------|-----|----------|----------|
| Pool | | 10.7 | 9.53 | 1.12 | 2.51 | 8.49 | 1 | 4.9 | 2589.9 | 2589.91 |

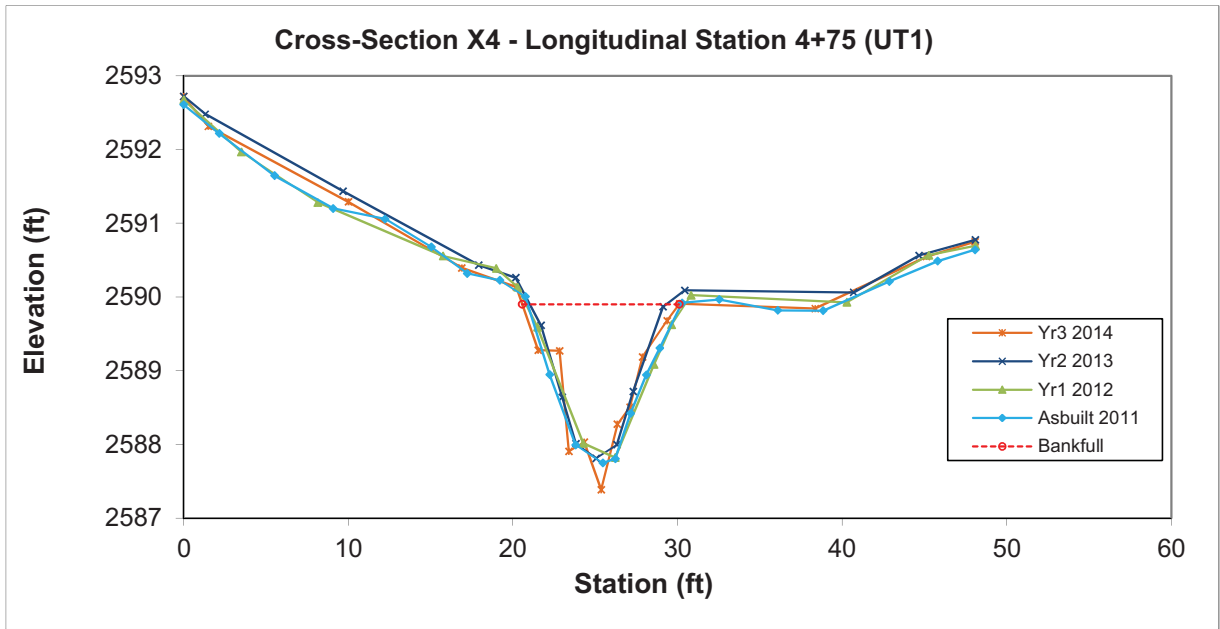


Photo 7: XS-4 facing right bank



Photo 8: XS-4 facing left bank

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|------|----------|-----|----------|----------|
| Riffle | Eb | 2.8 | 5.77 | 0.49 | 0.88 | 11.9 | 1 | 6.7 | 2639.18 | 2639.2 |

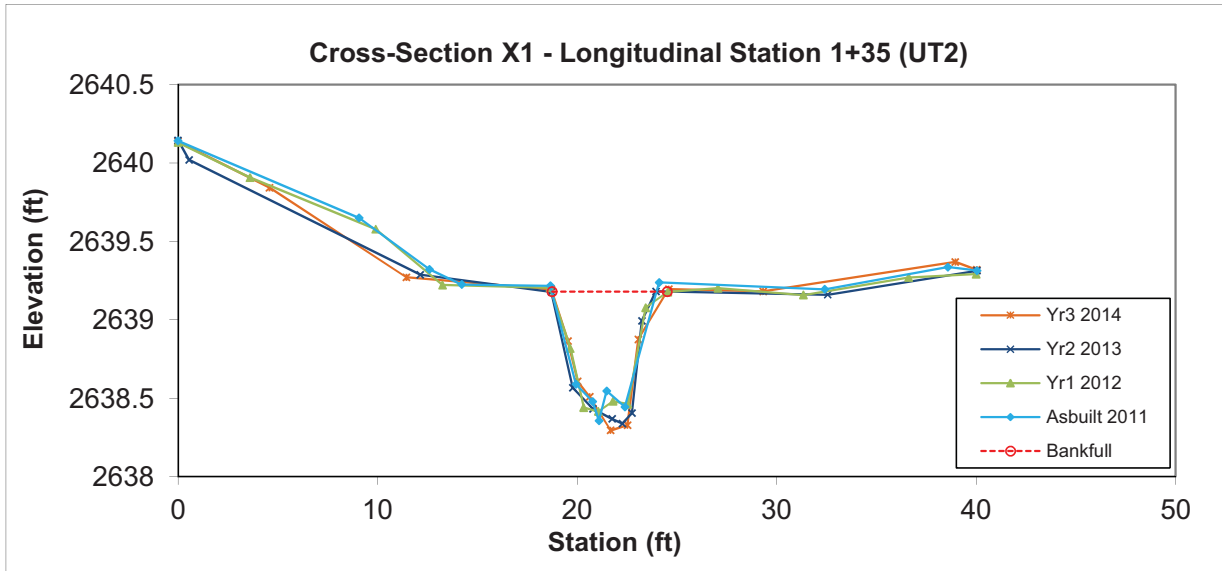


Photo 1: XS-1 facing right bank



Photo 2: XS-1 facing left bank

| Feature | Stream Type | BKF Area | BKF Width | BKF Depth | Max BKF Depth | W/D | BH Ratio | ER | BKF Elev | TOB Elev |
|---------|-------------|----------|-----------|-----------|---------------|-------|----------|----|----------|----------|
| Pool | | 4.6 | 6.84 | 0.67 | 1.23 | 10.23 | 1 | 5 | 2633.9 | 2633.93 |

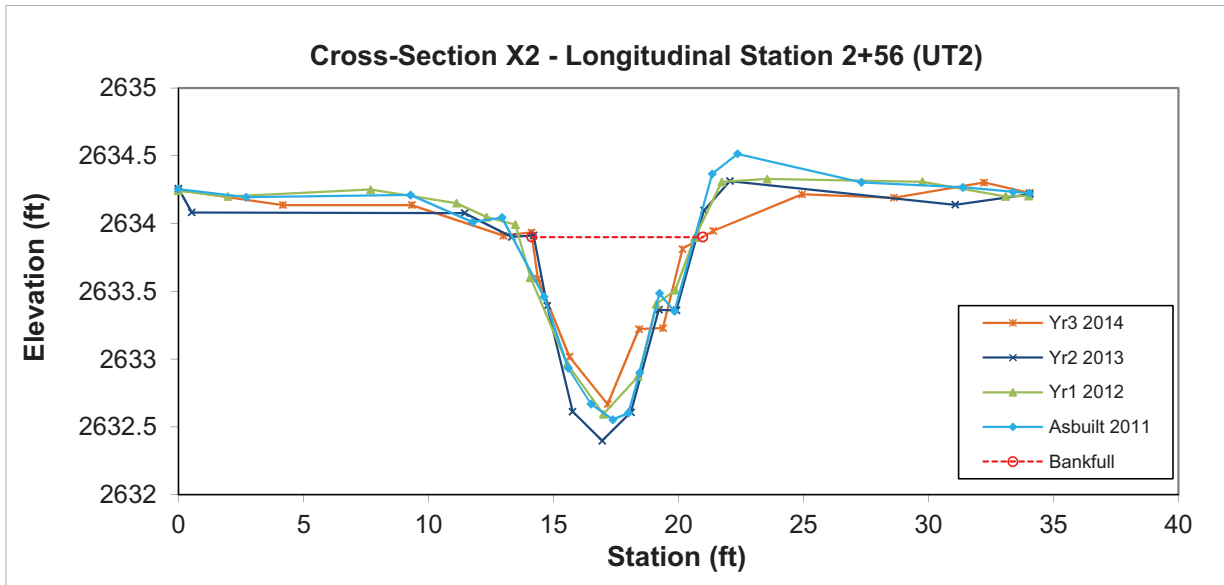


Photo 3: XS-2 facing right bank



Photo 4: XS-2 facing right bank at channel

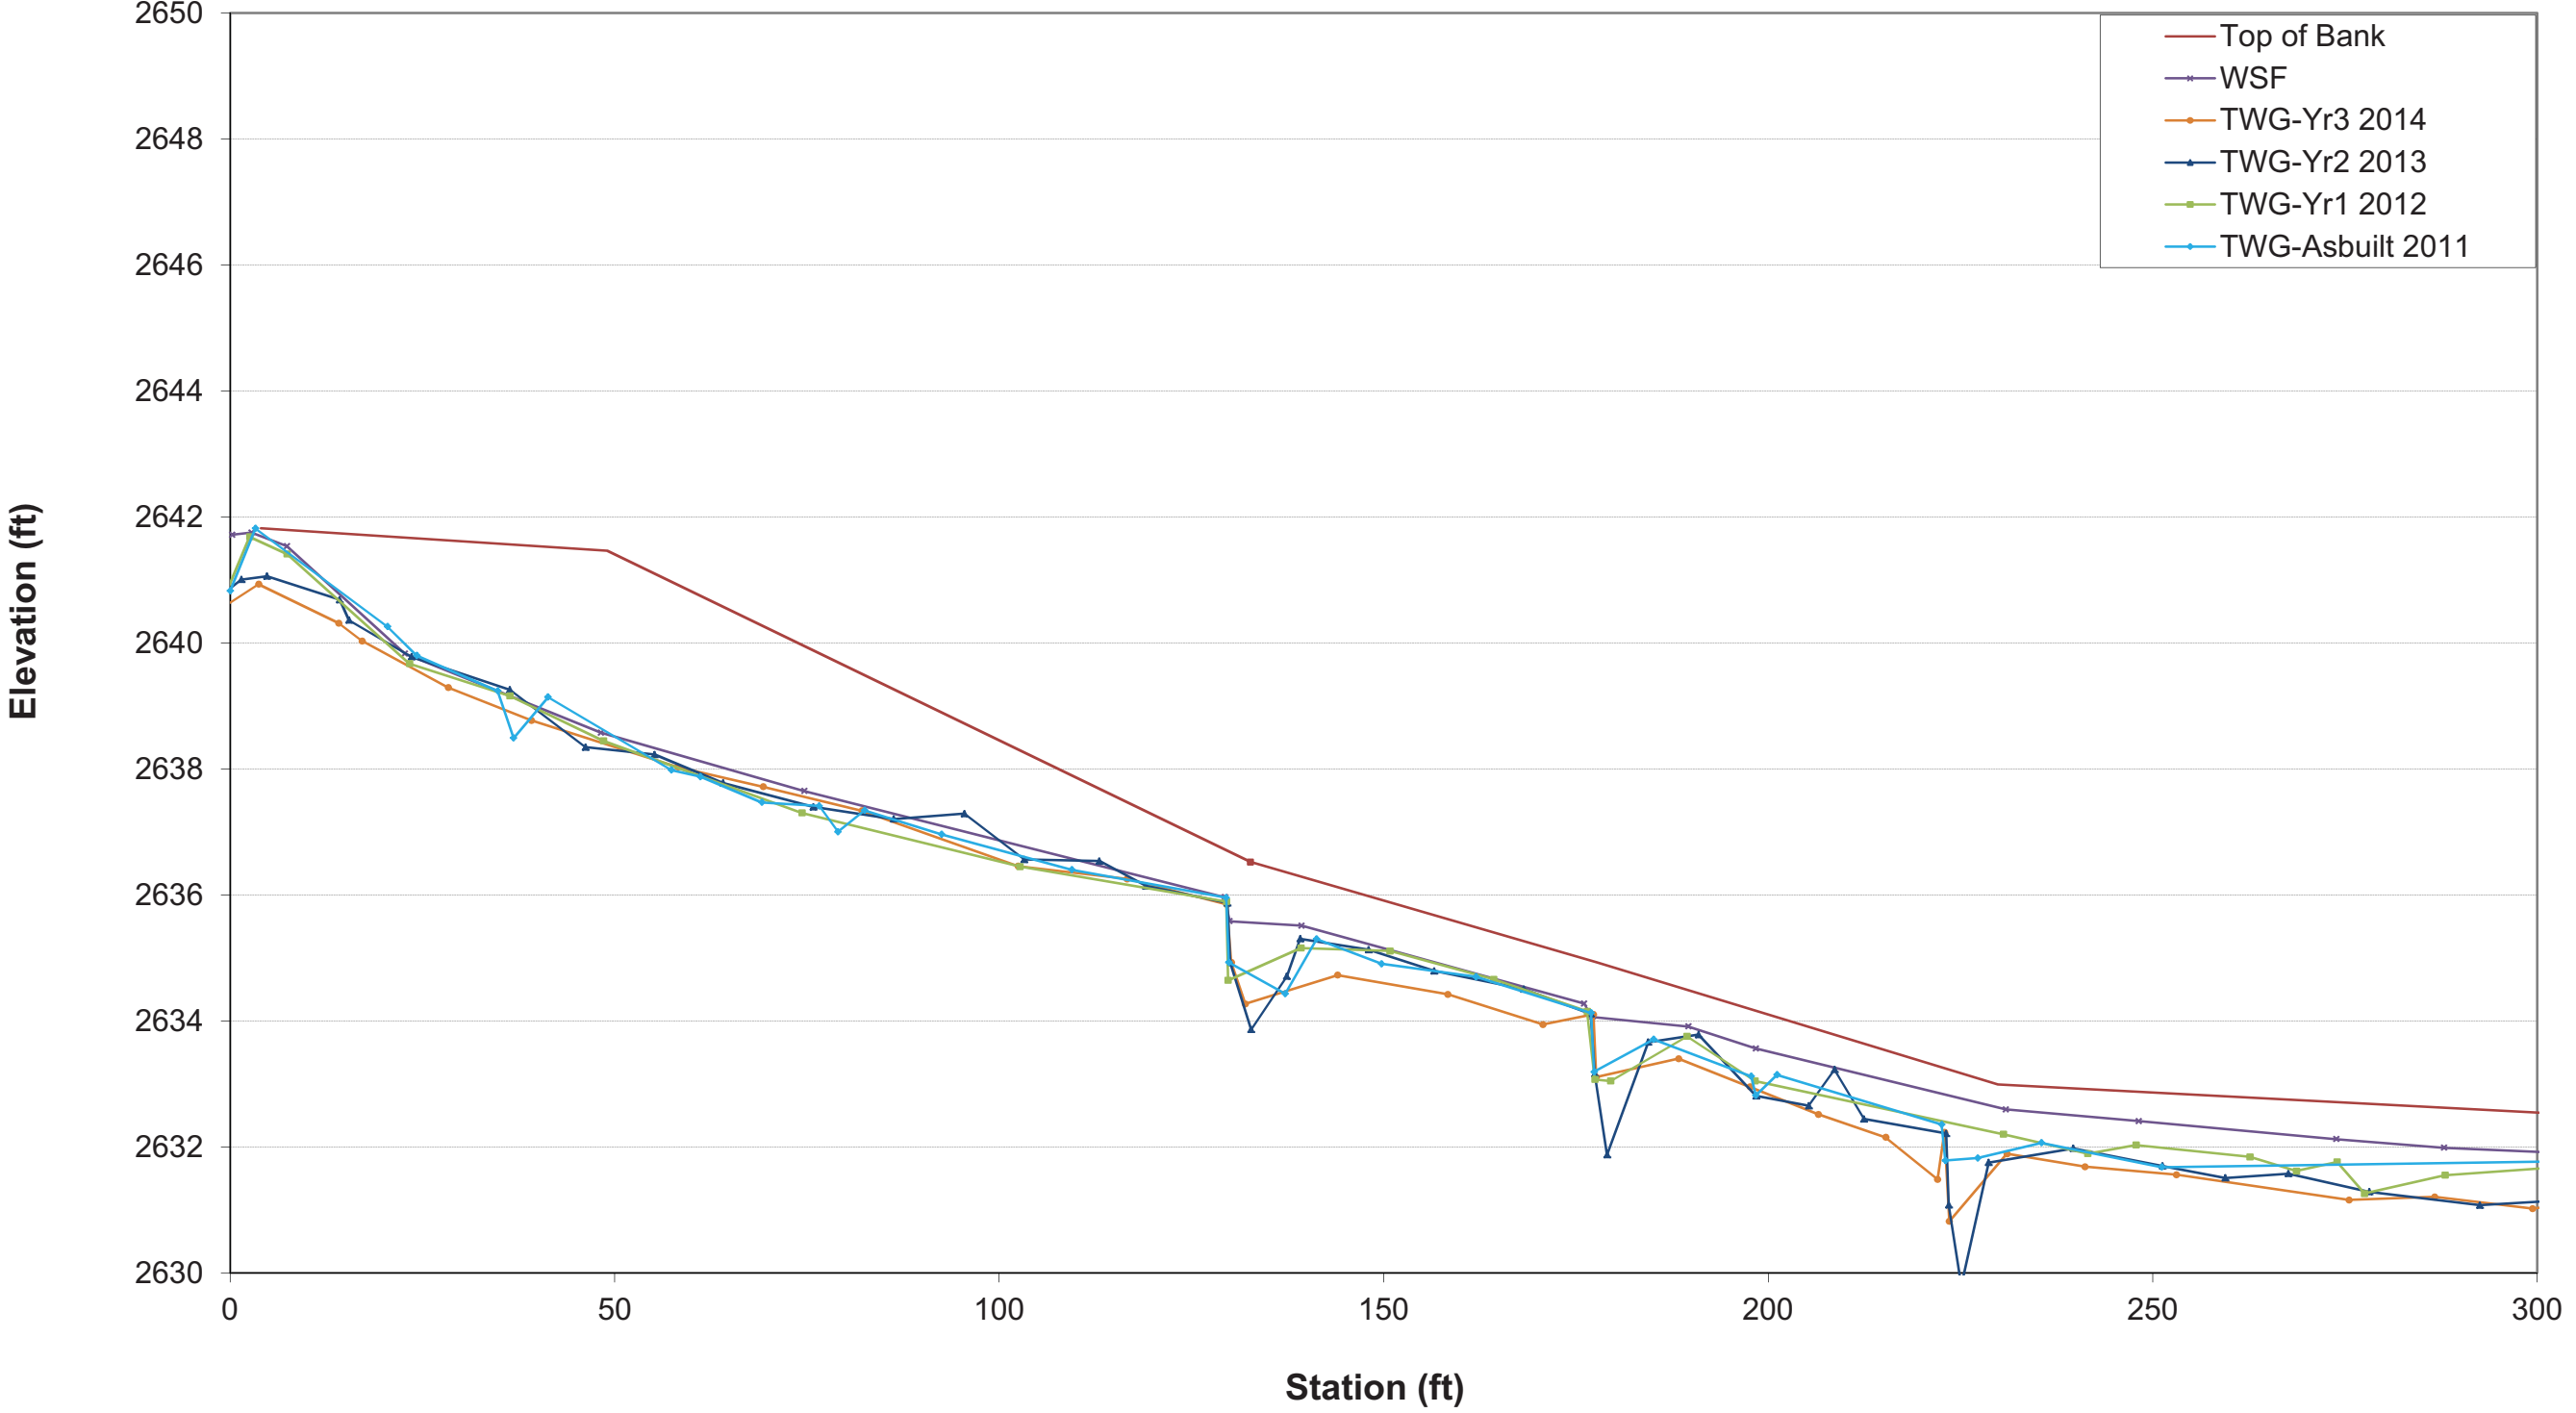


Photo 5: XS-2 facing left bank

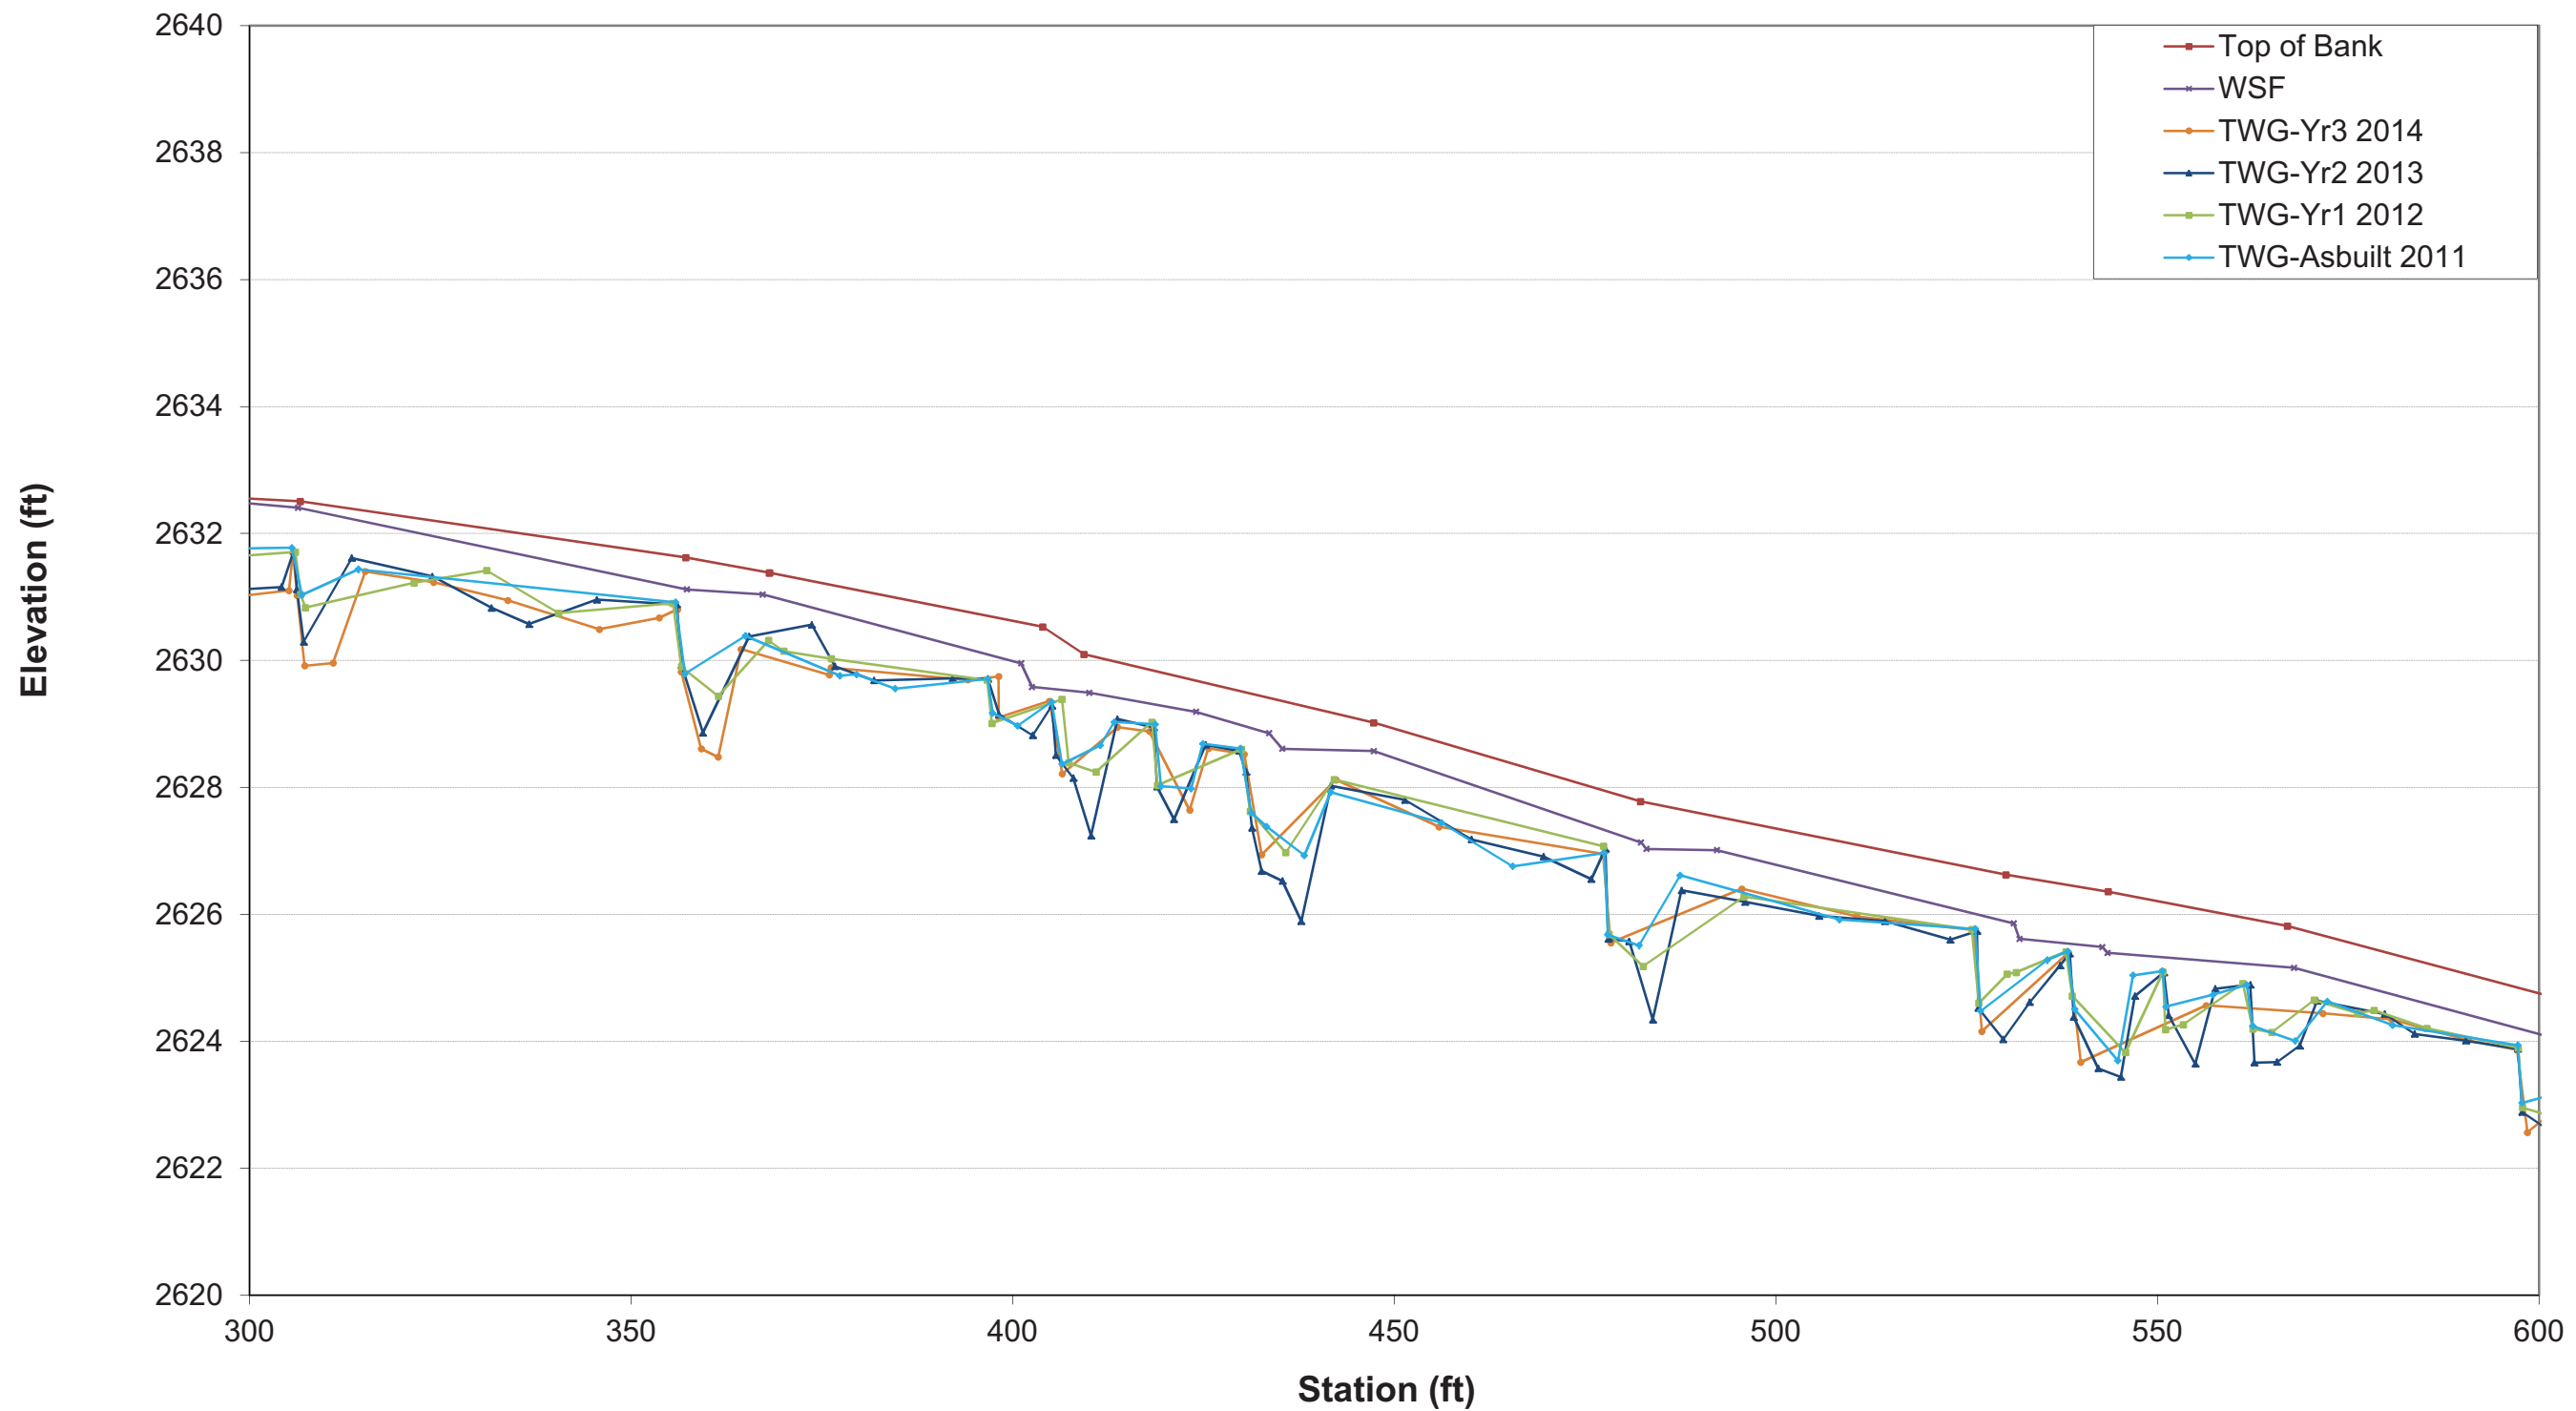


Photo 6: XS-2 facing left bank at channel


Longitudinal Thalweg Profile - Elk Branch for All Years
0+00 to 3+00




Longitudinal Thalweg Profile - Elk Branch for All Years 3+00 to 6+00




Longitudinal Thalweg Profile - Elk Branch for All Years
6+00 to 9+00

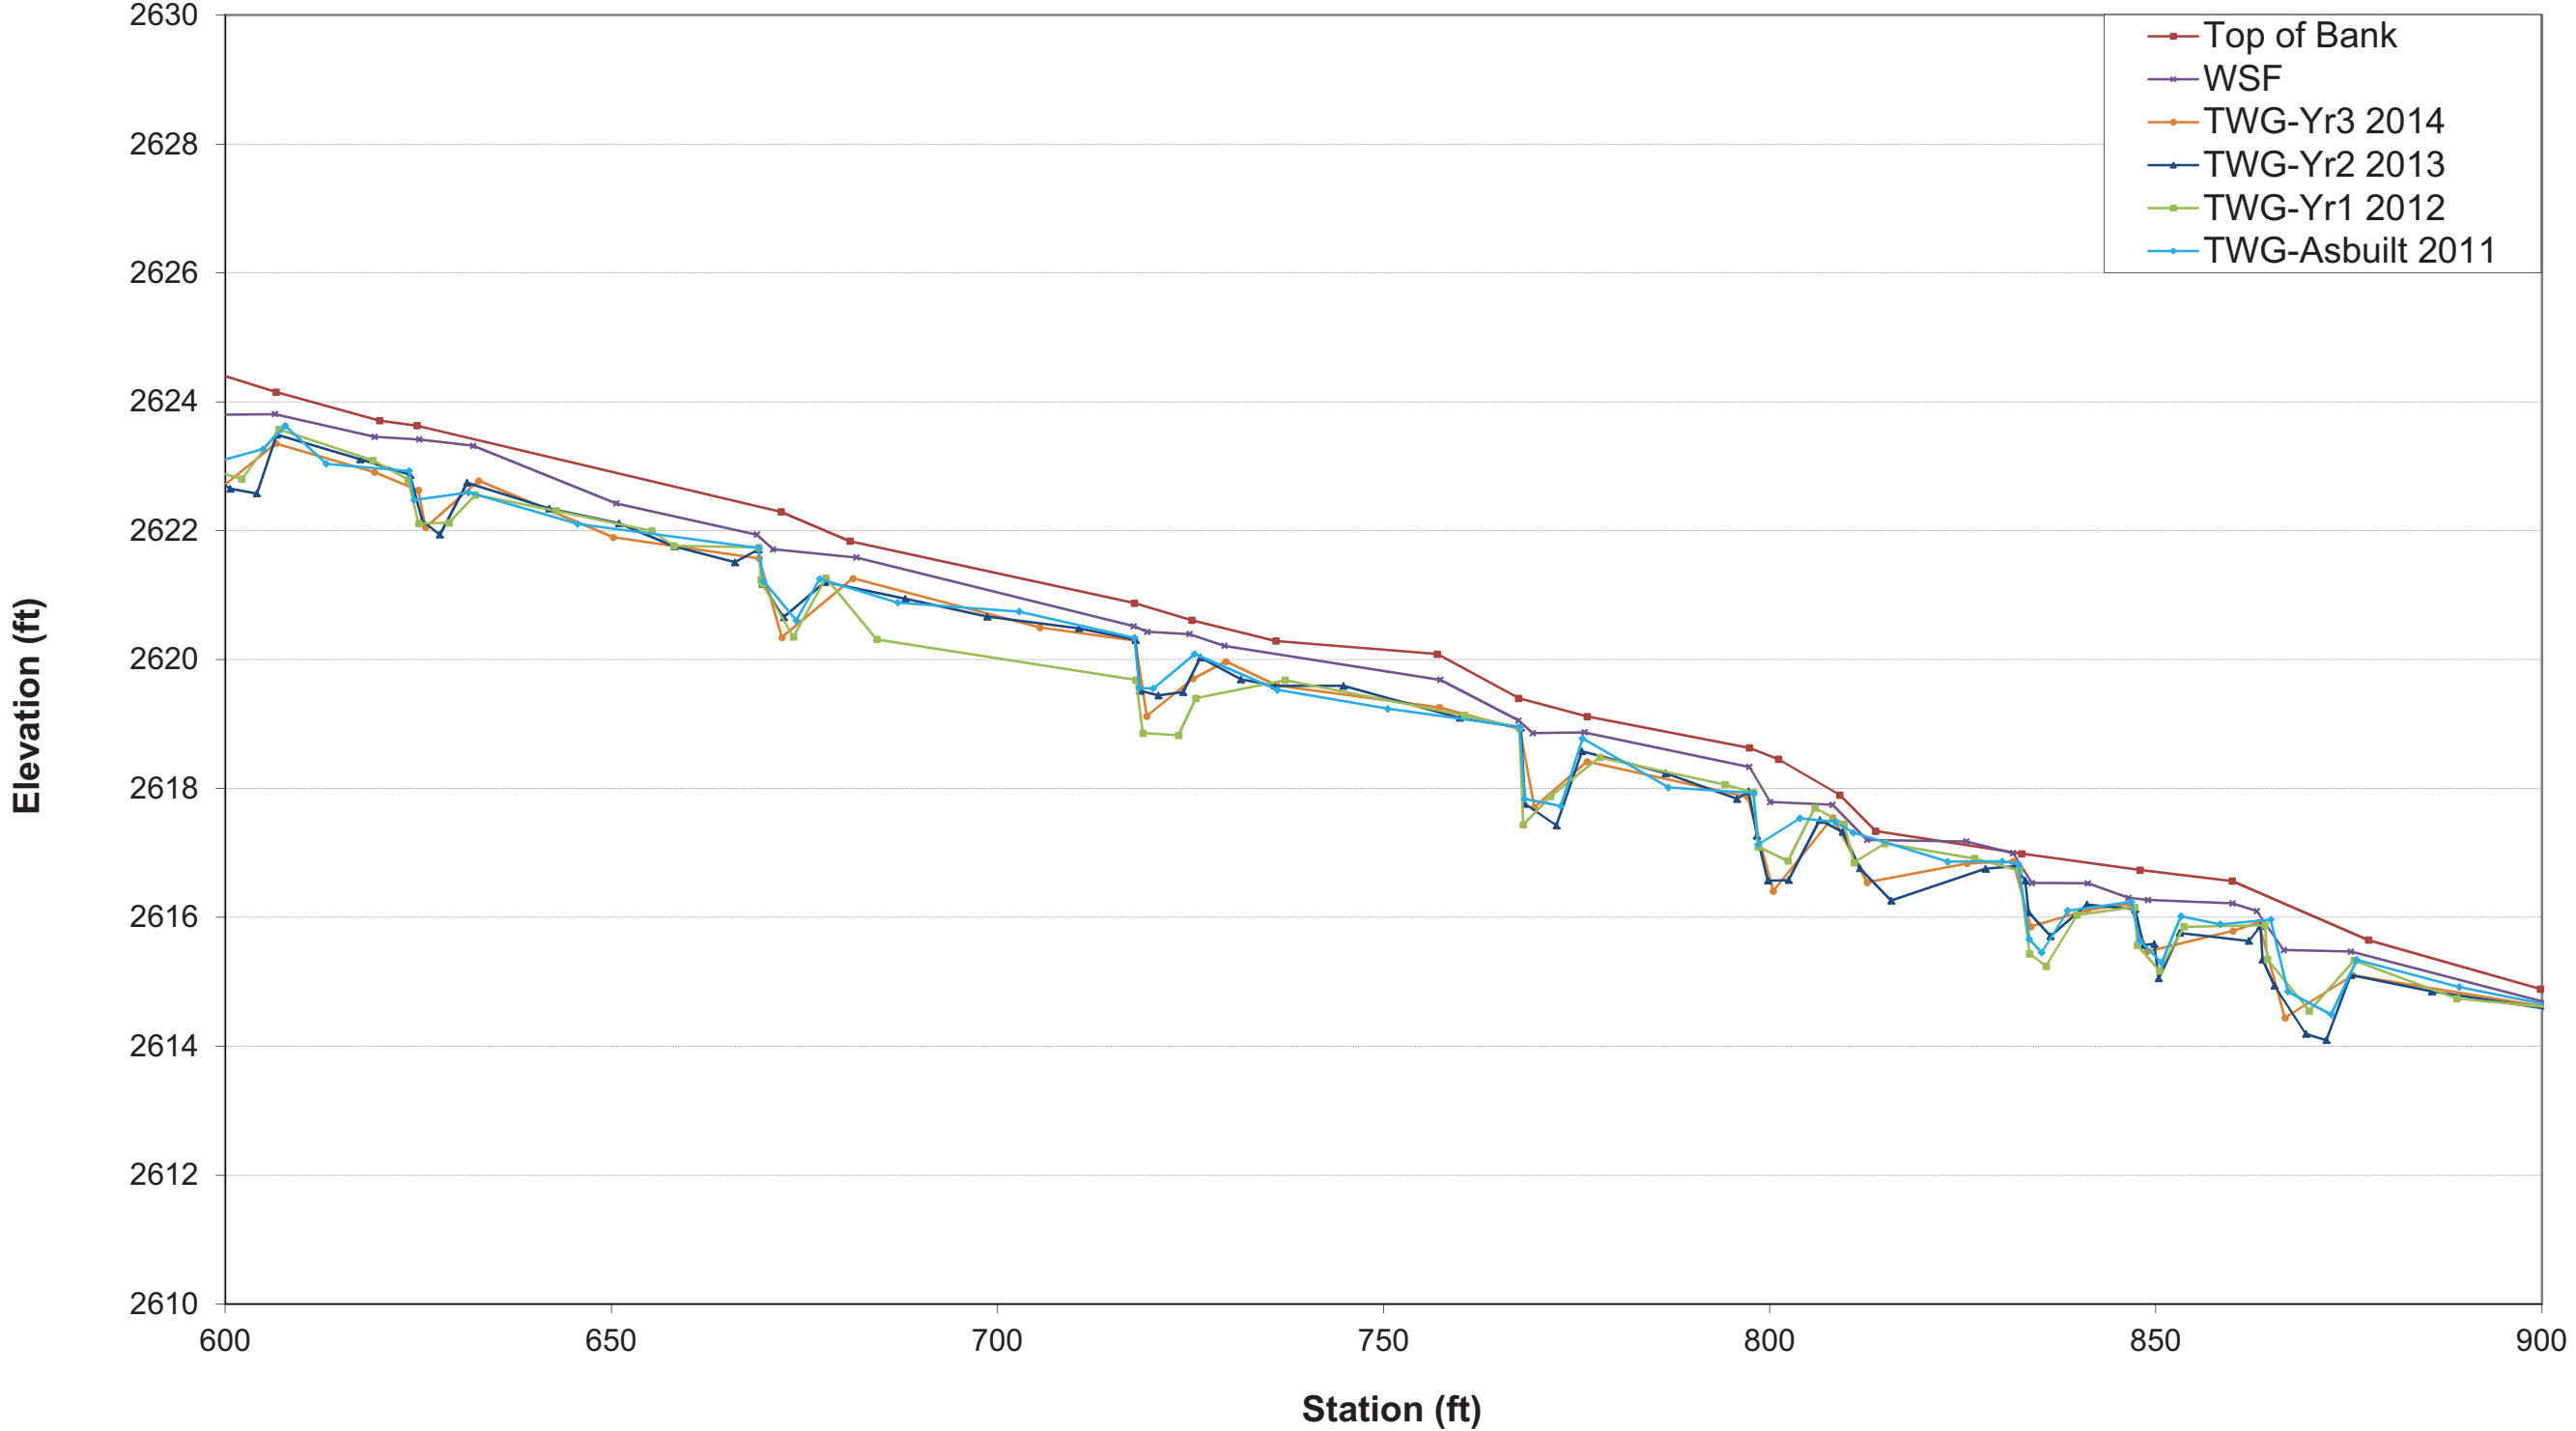


Longitudinal Thalweg Profile - Elk Branch for All Years
9+00 to 12+00

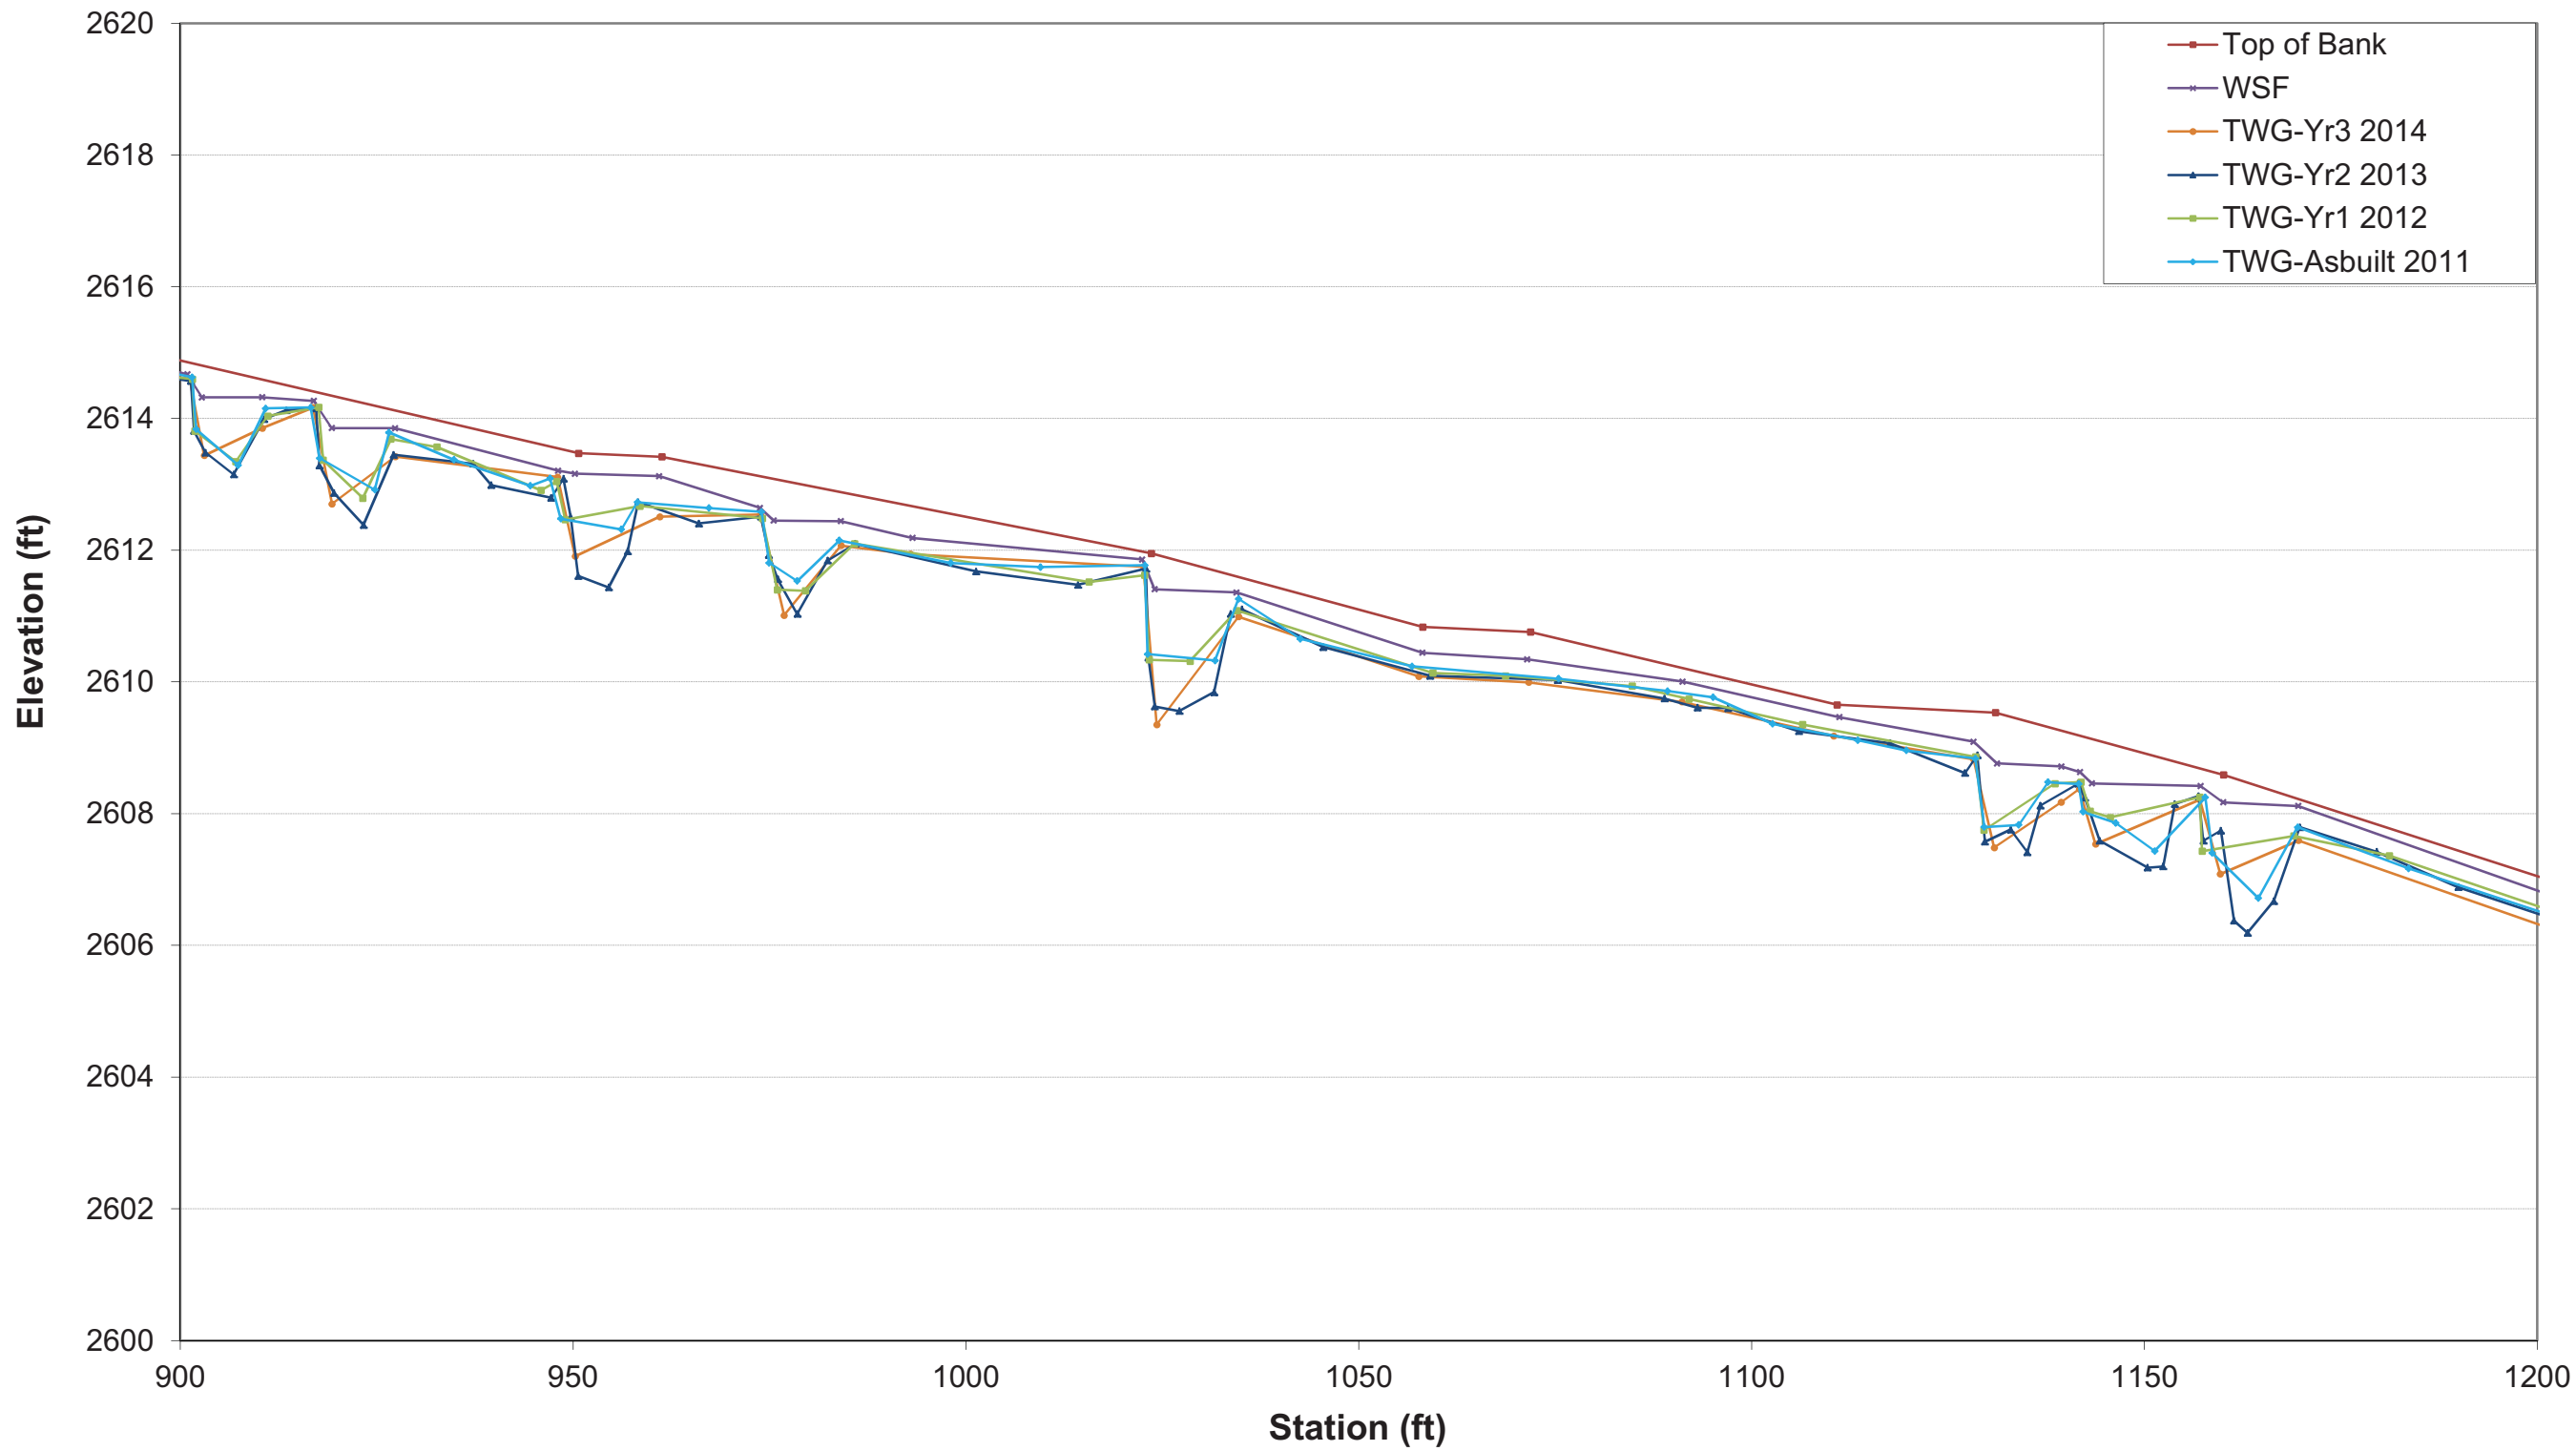


Longitudinal Thalweg Profile - Elk Branch for All Years
12+00 to 15+00

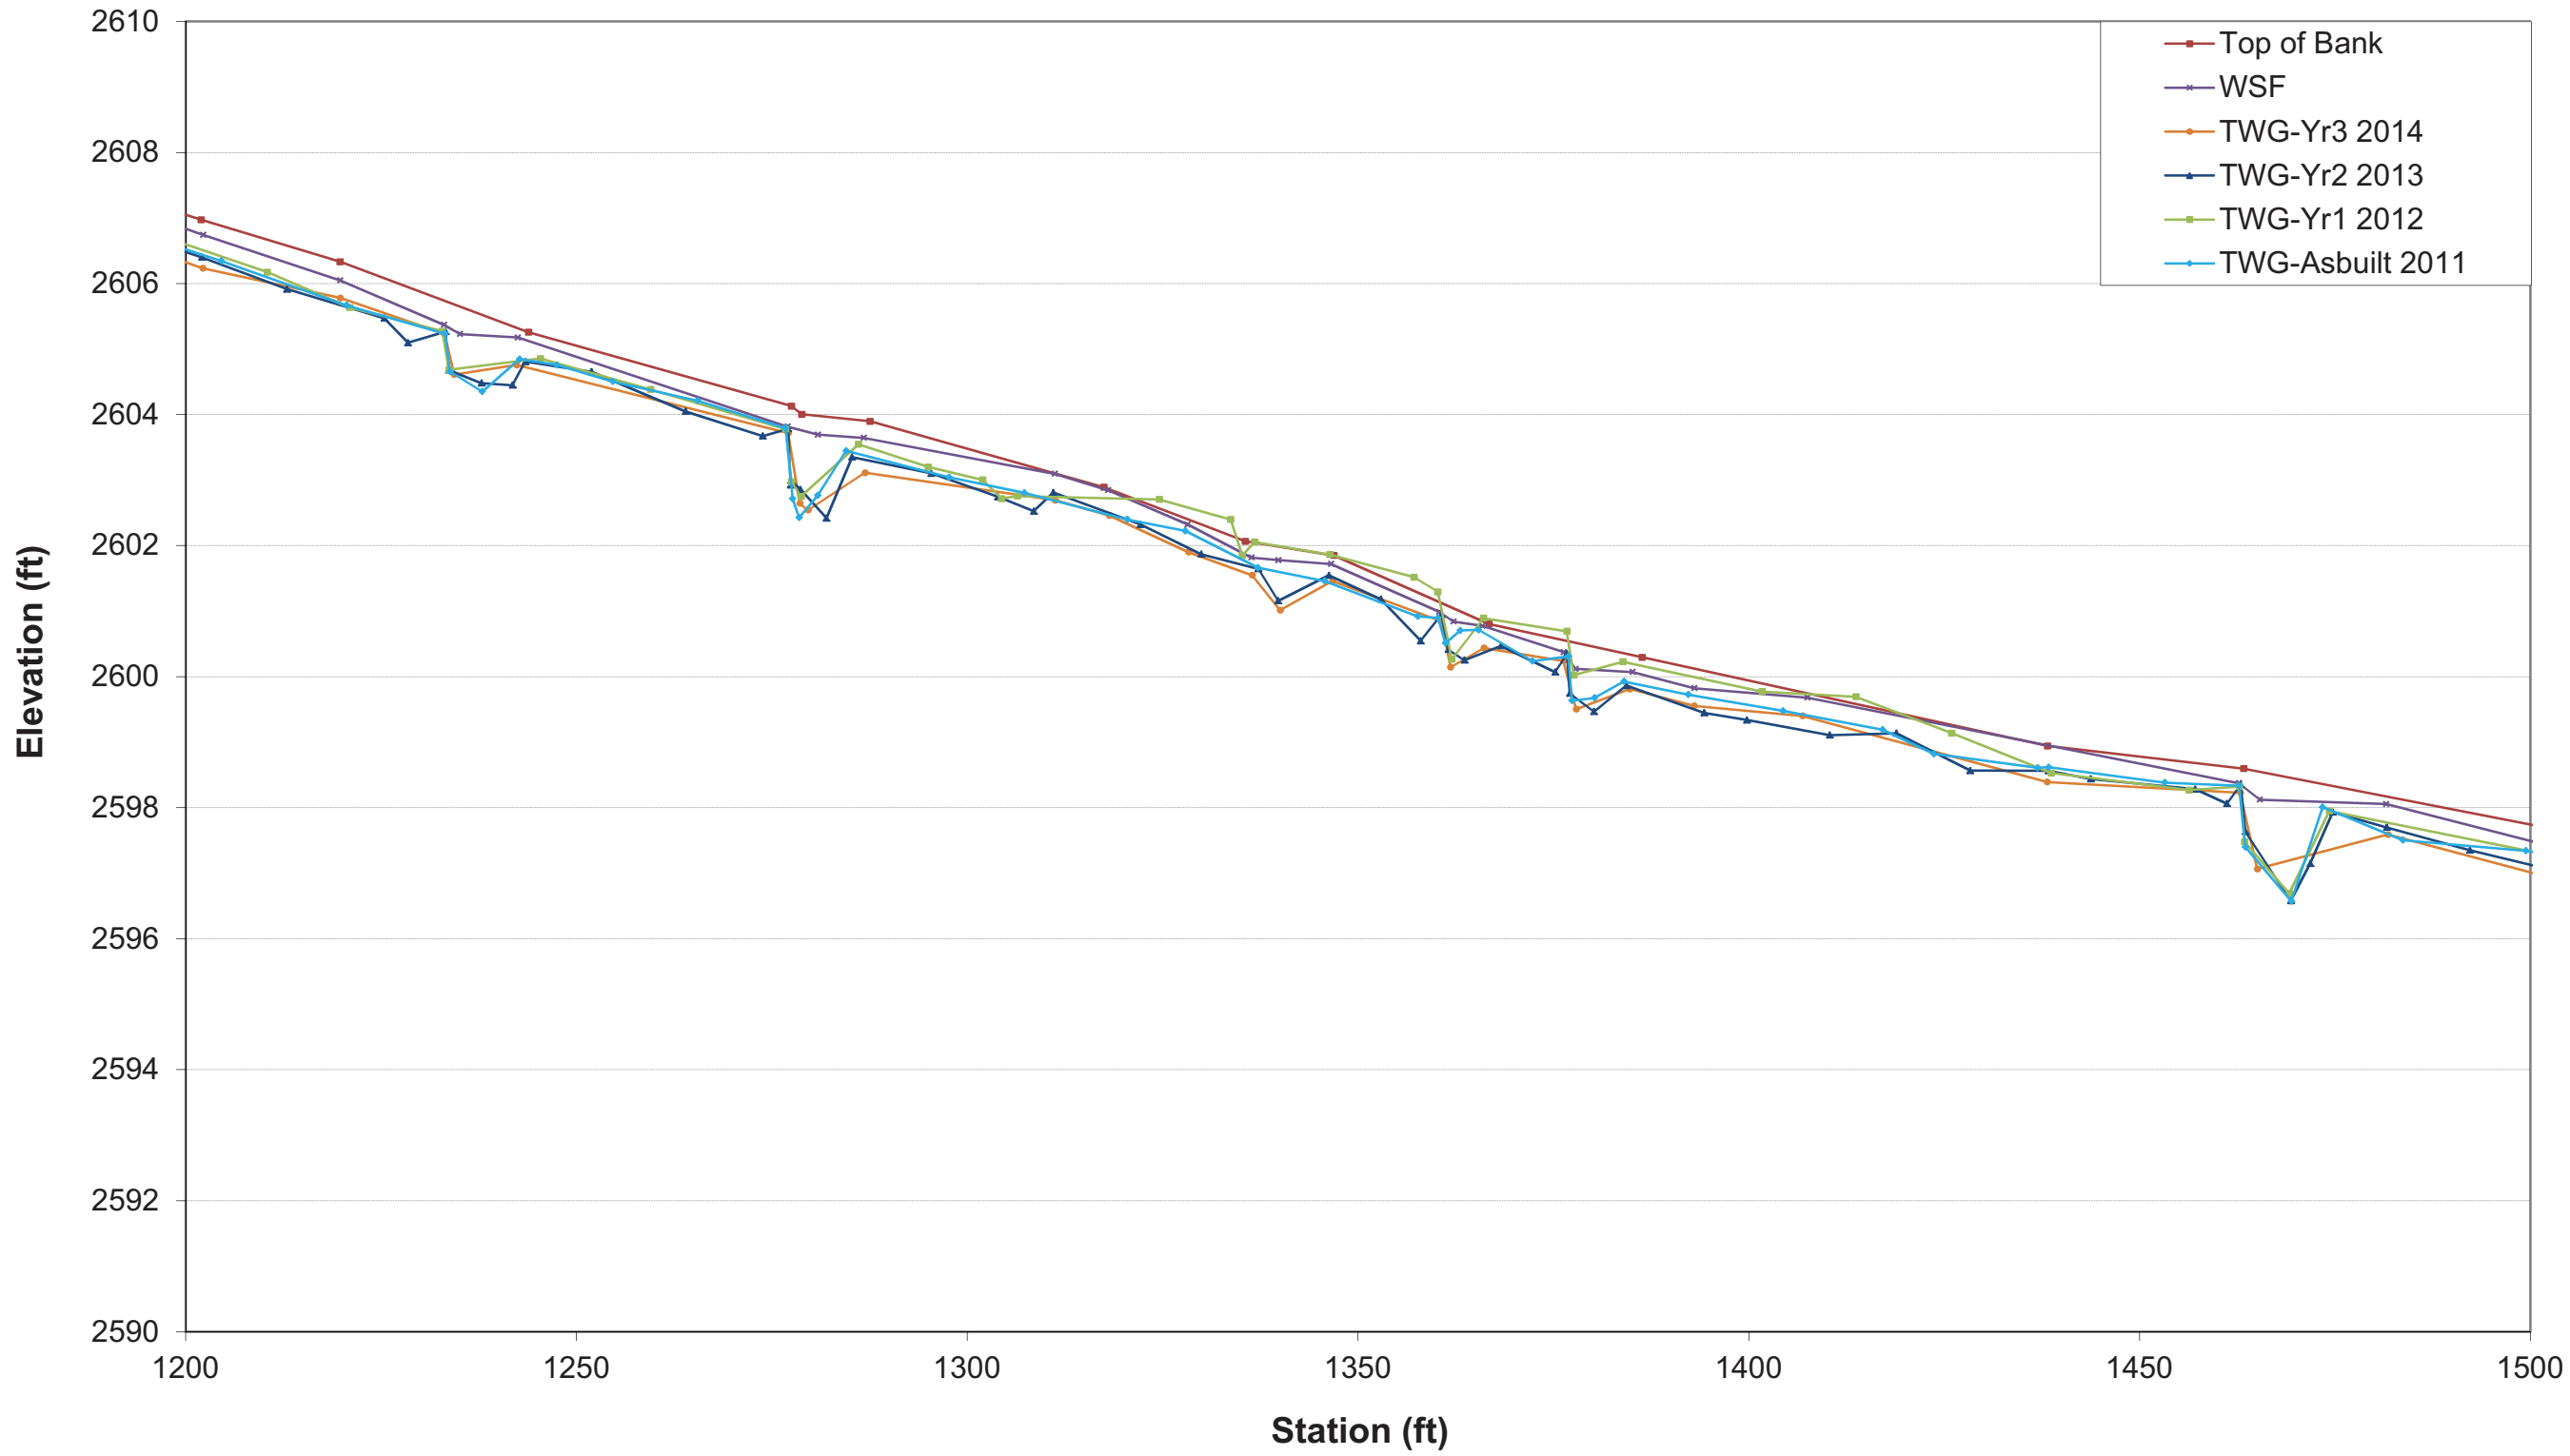


Longitudinal Thalweg Profile - Elk Branch for All Years
15+00 to 18+00

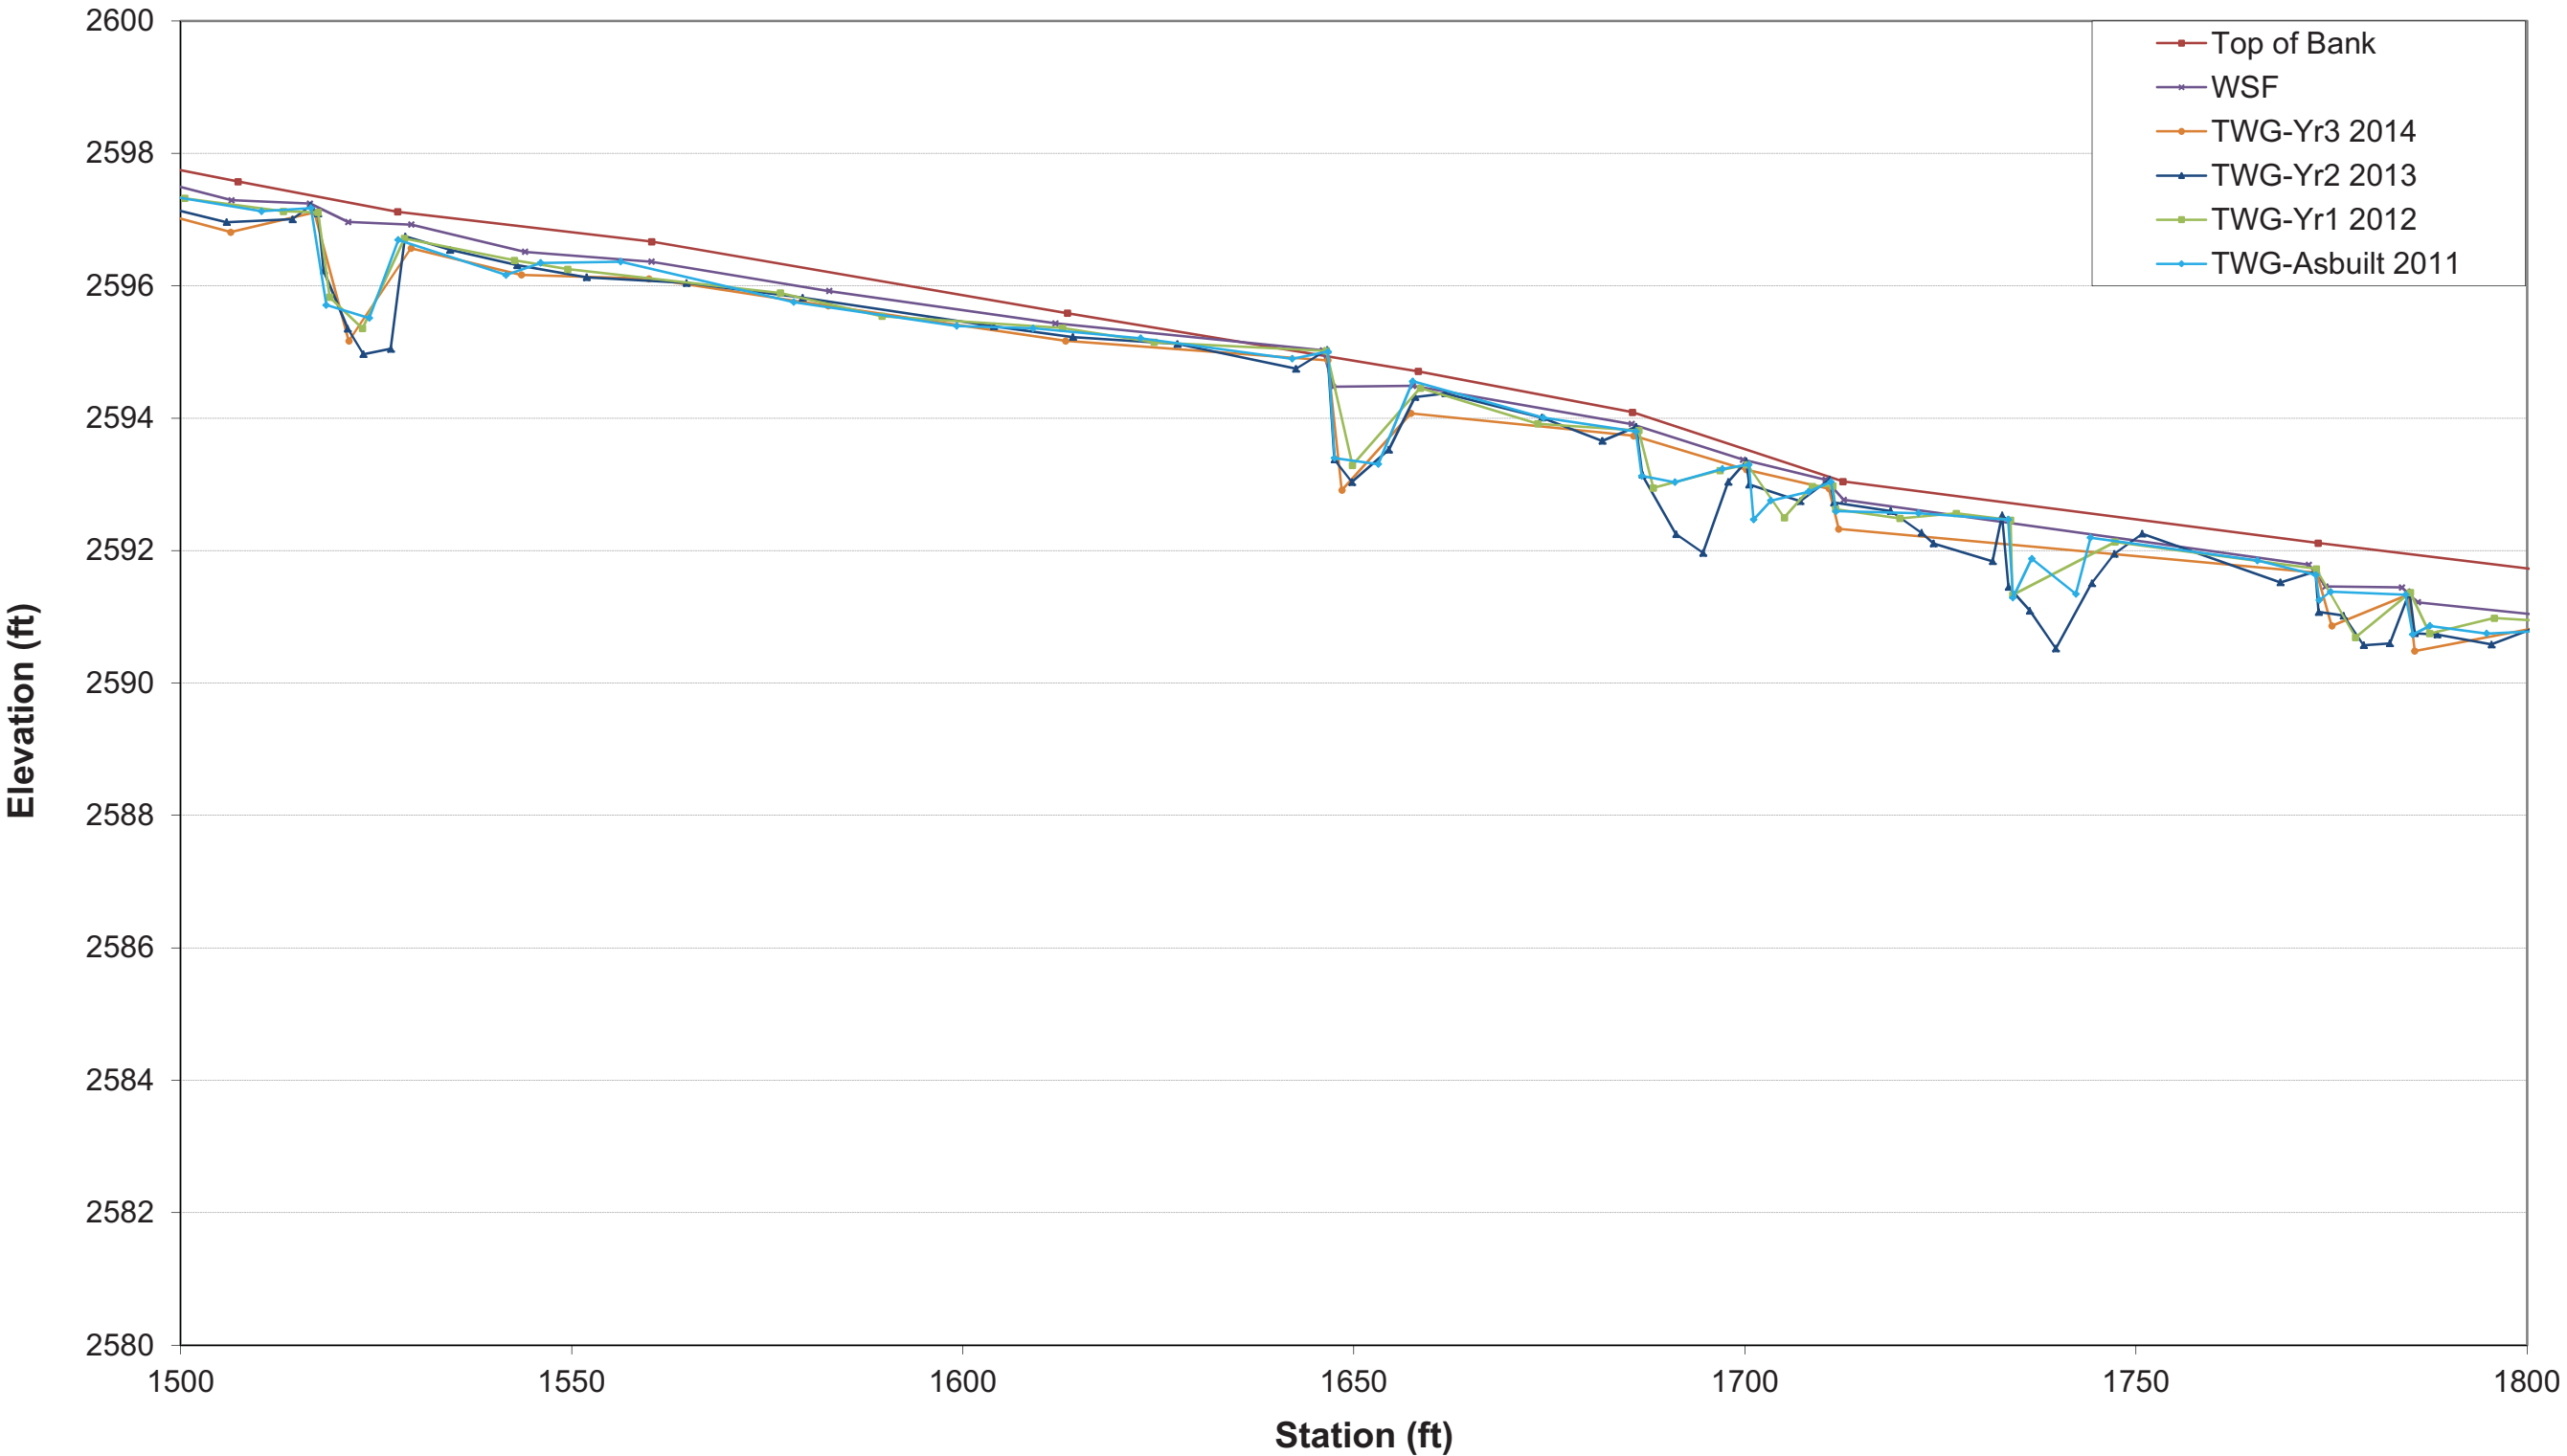


Longitudinal Thalweg Profile - Elk Branch for All Years 18+00 to 21+00

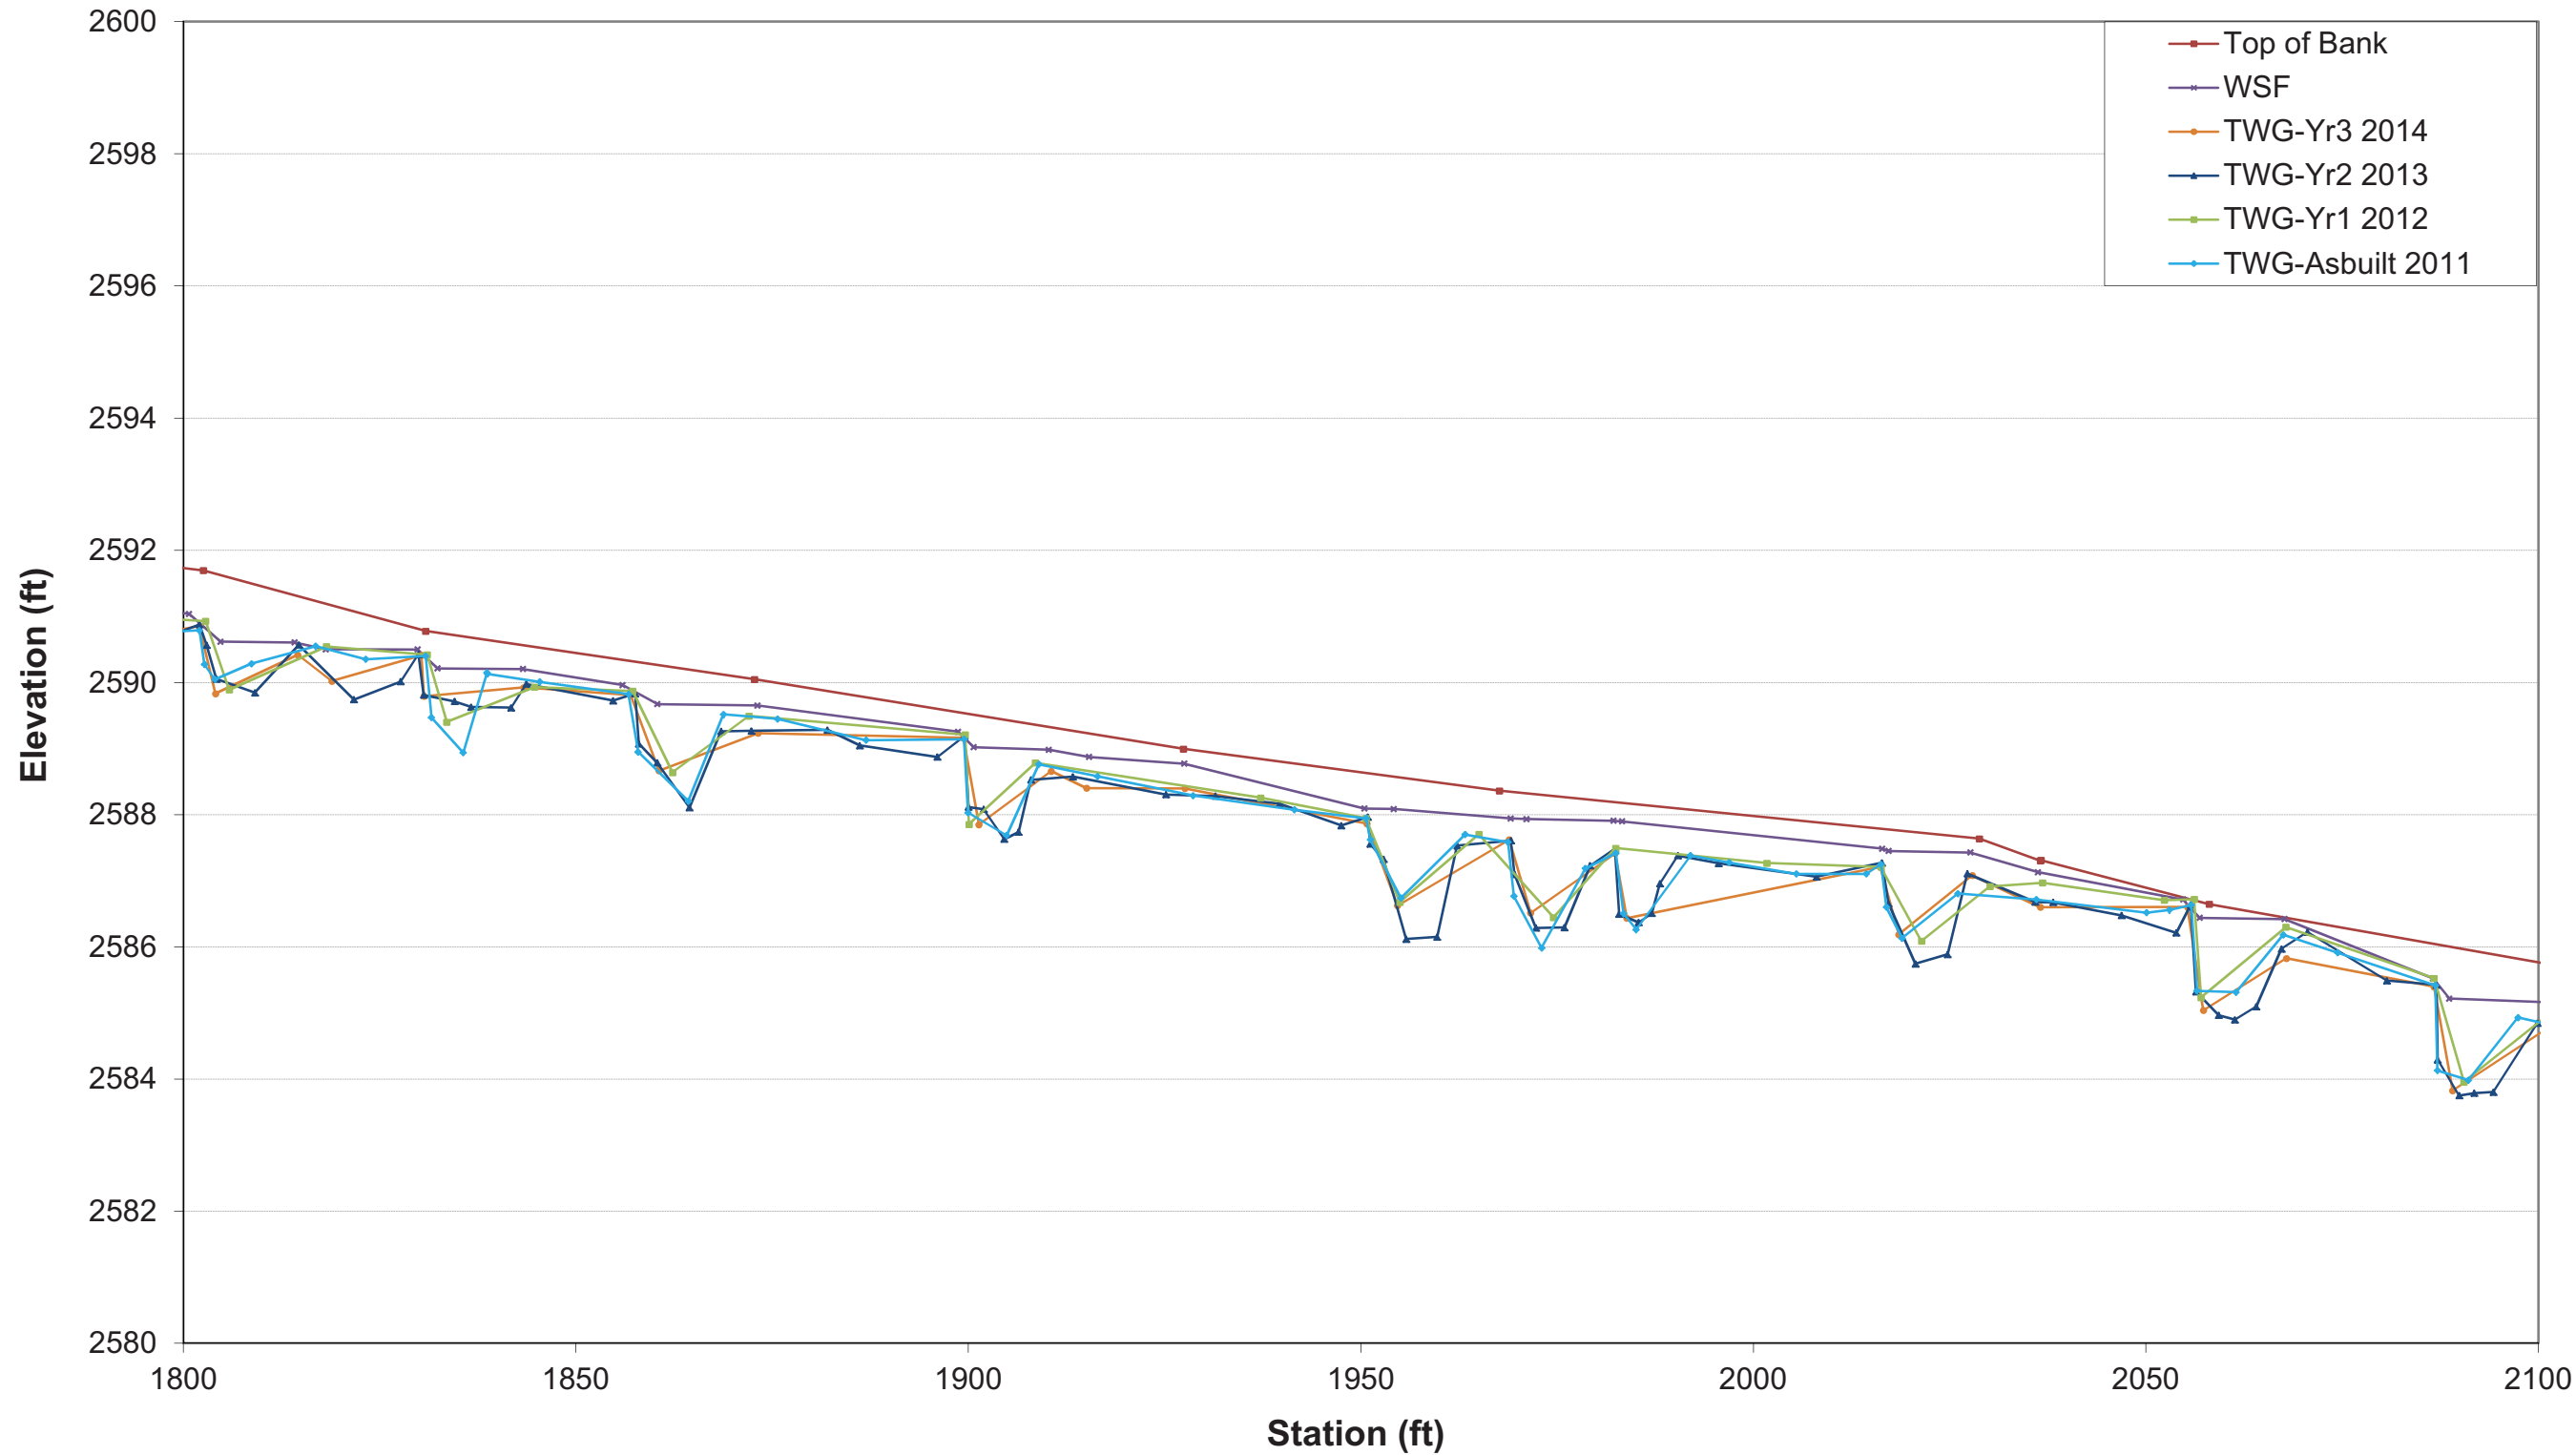


Longitudinal Thalweg Profile - Elk Branch for All Years 21+00 to 24+00

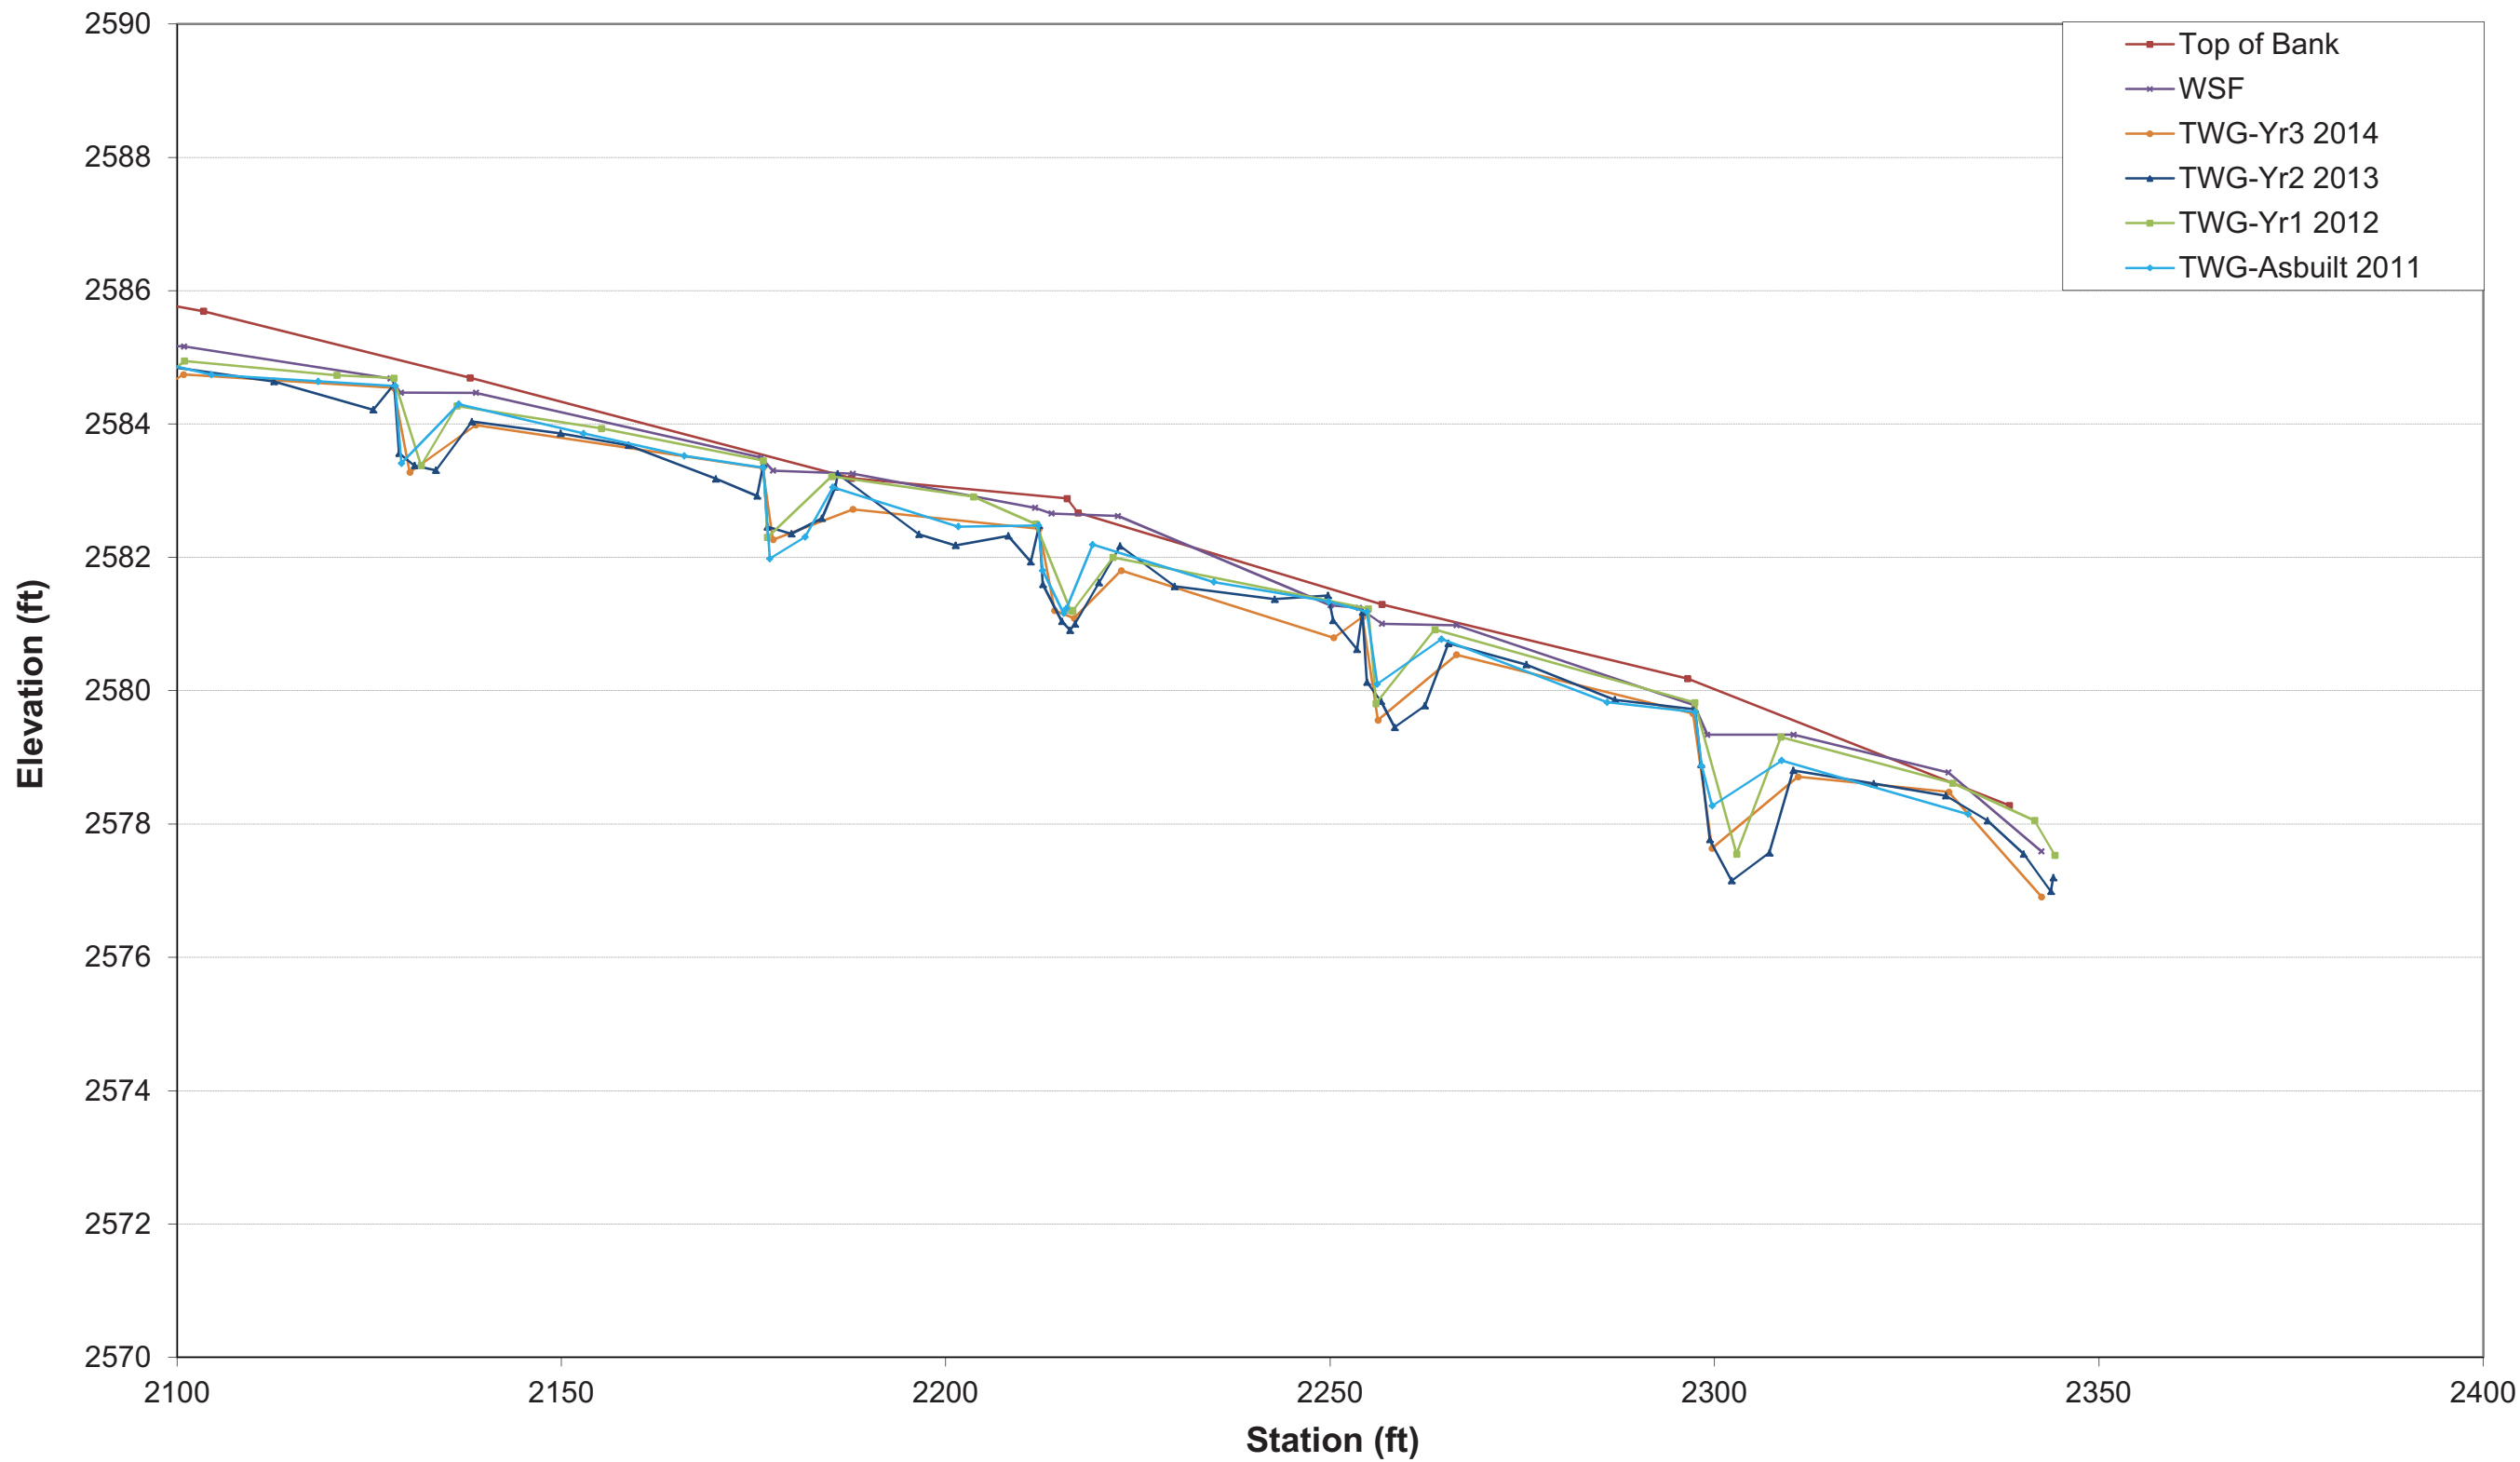


Longitudinal Profile - UT1 for Year 3 Monitoring 0+00 to 3+50

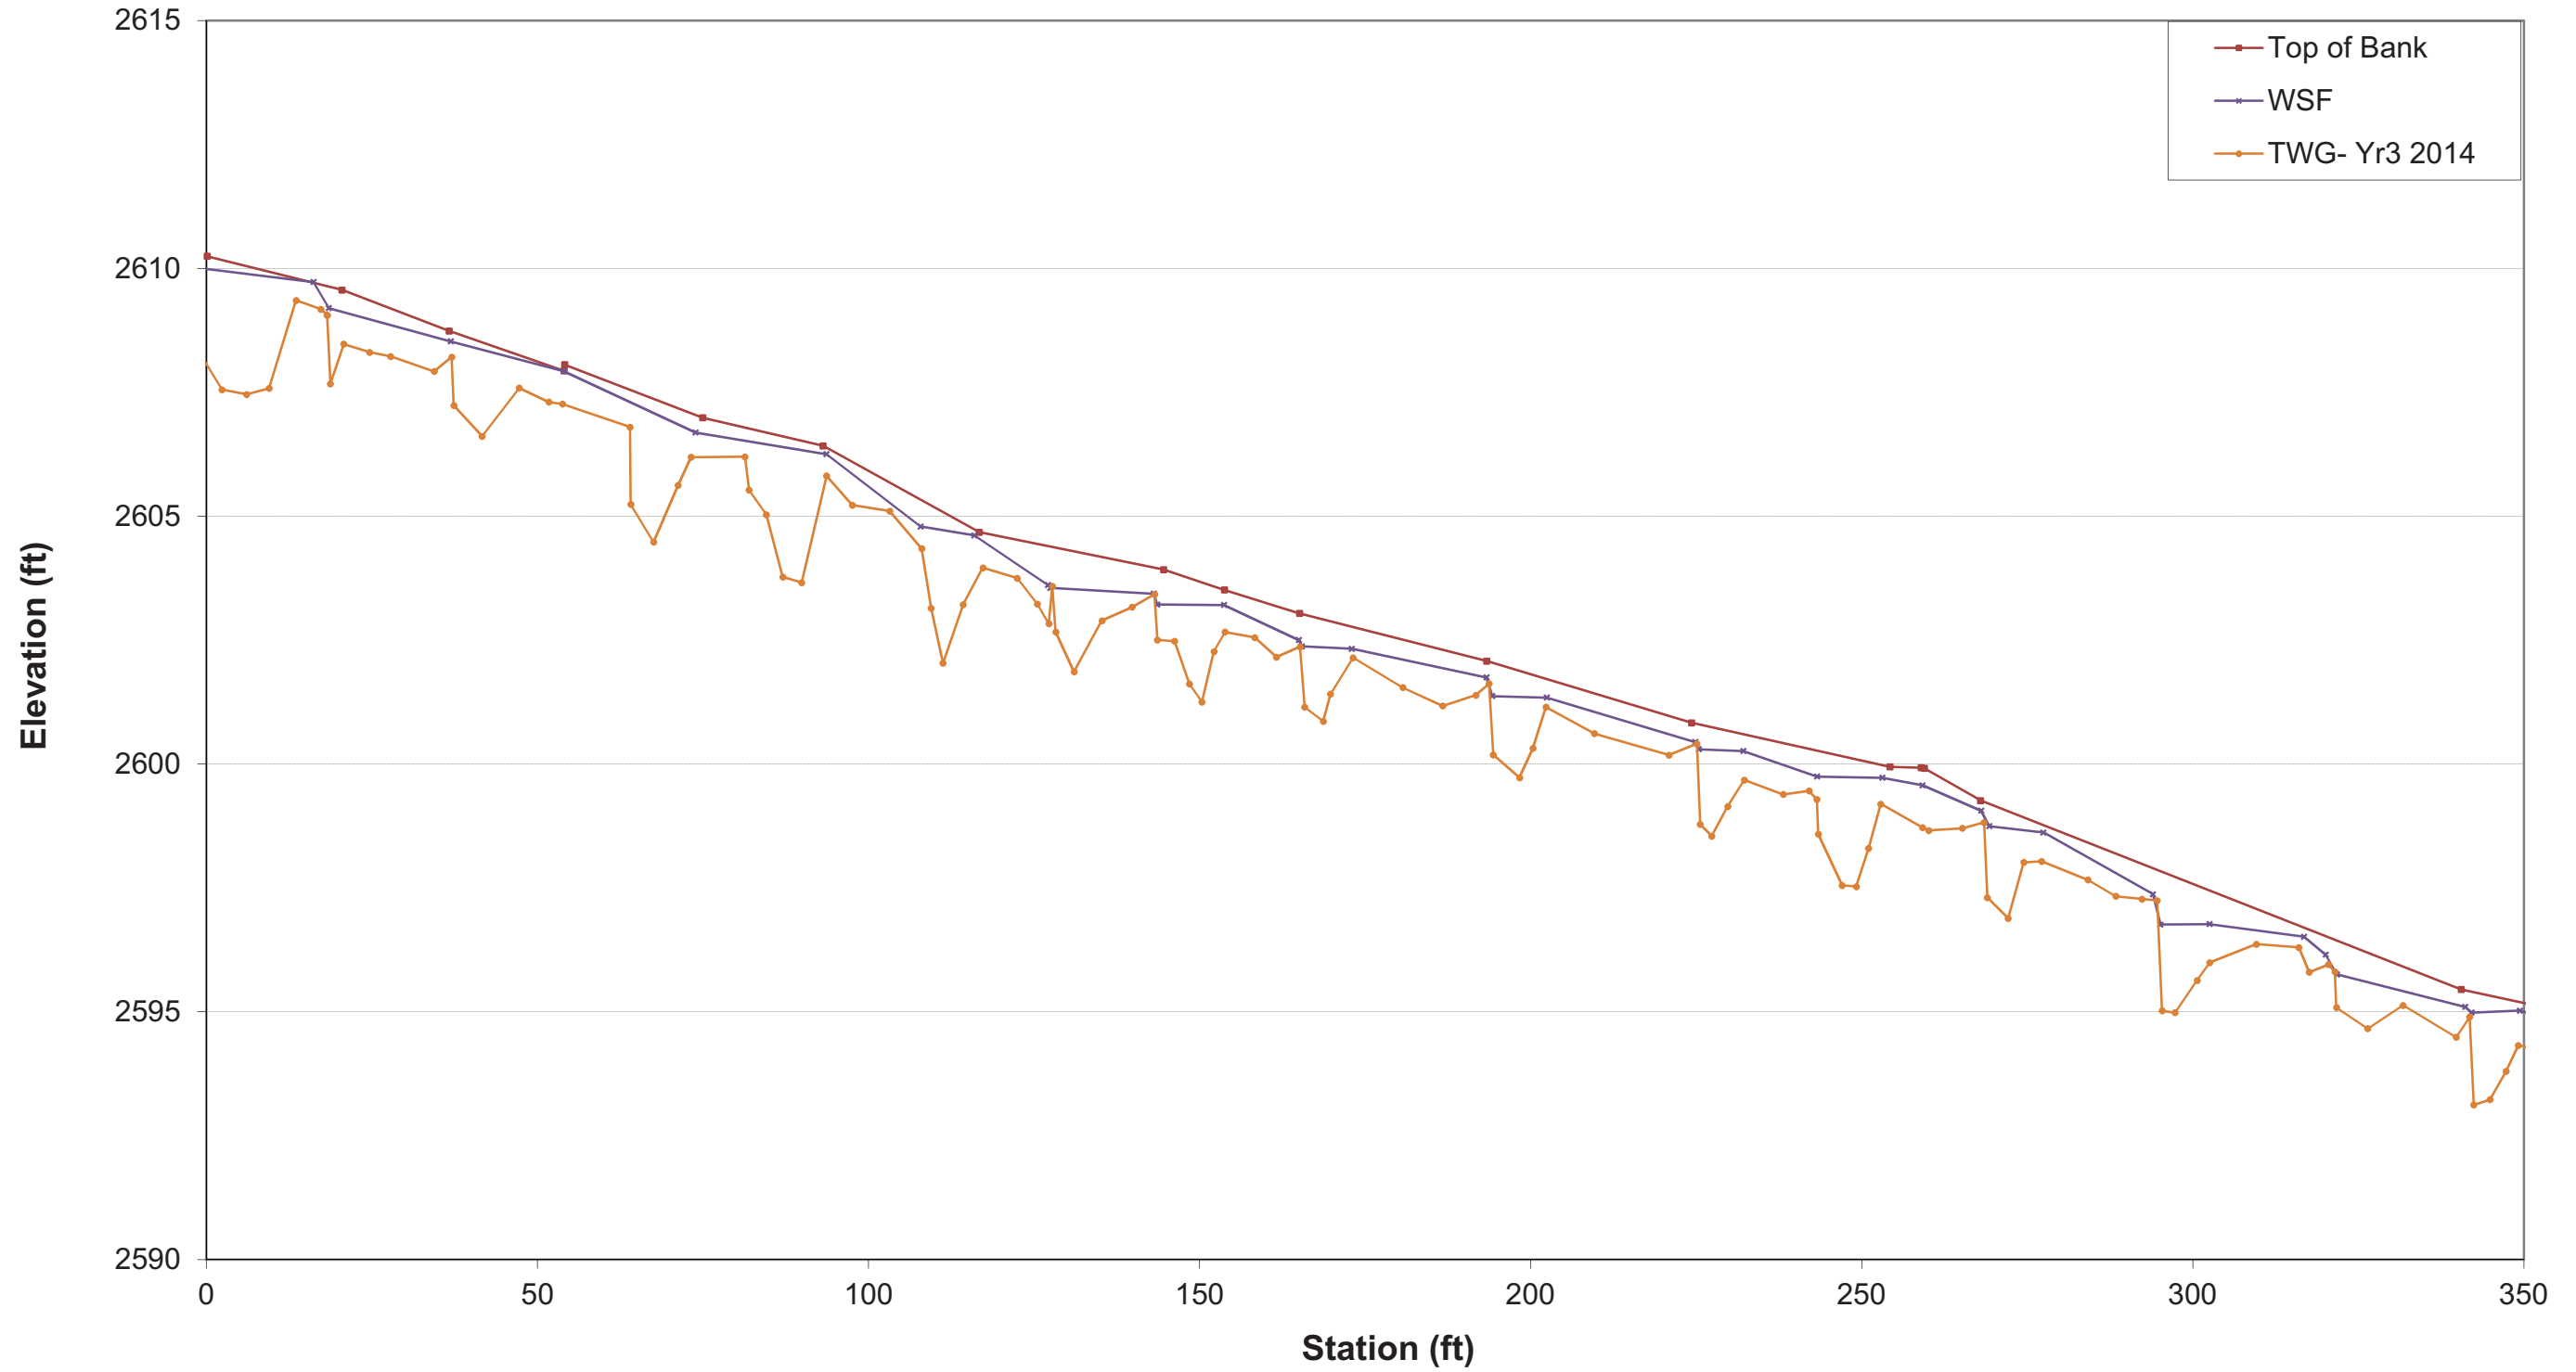


Longitudinal Profile - UT1 for All Years
0+00 to 3+50

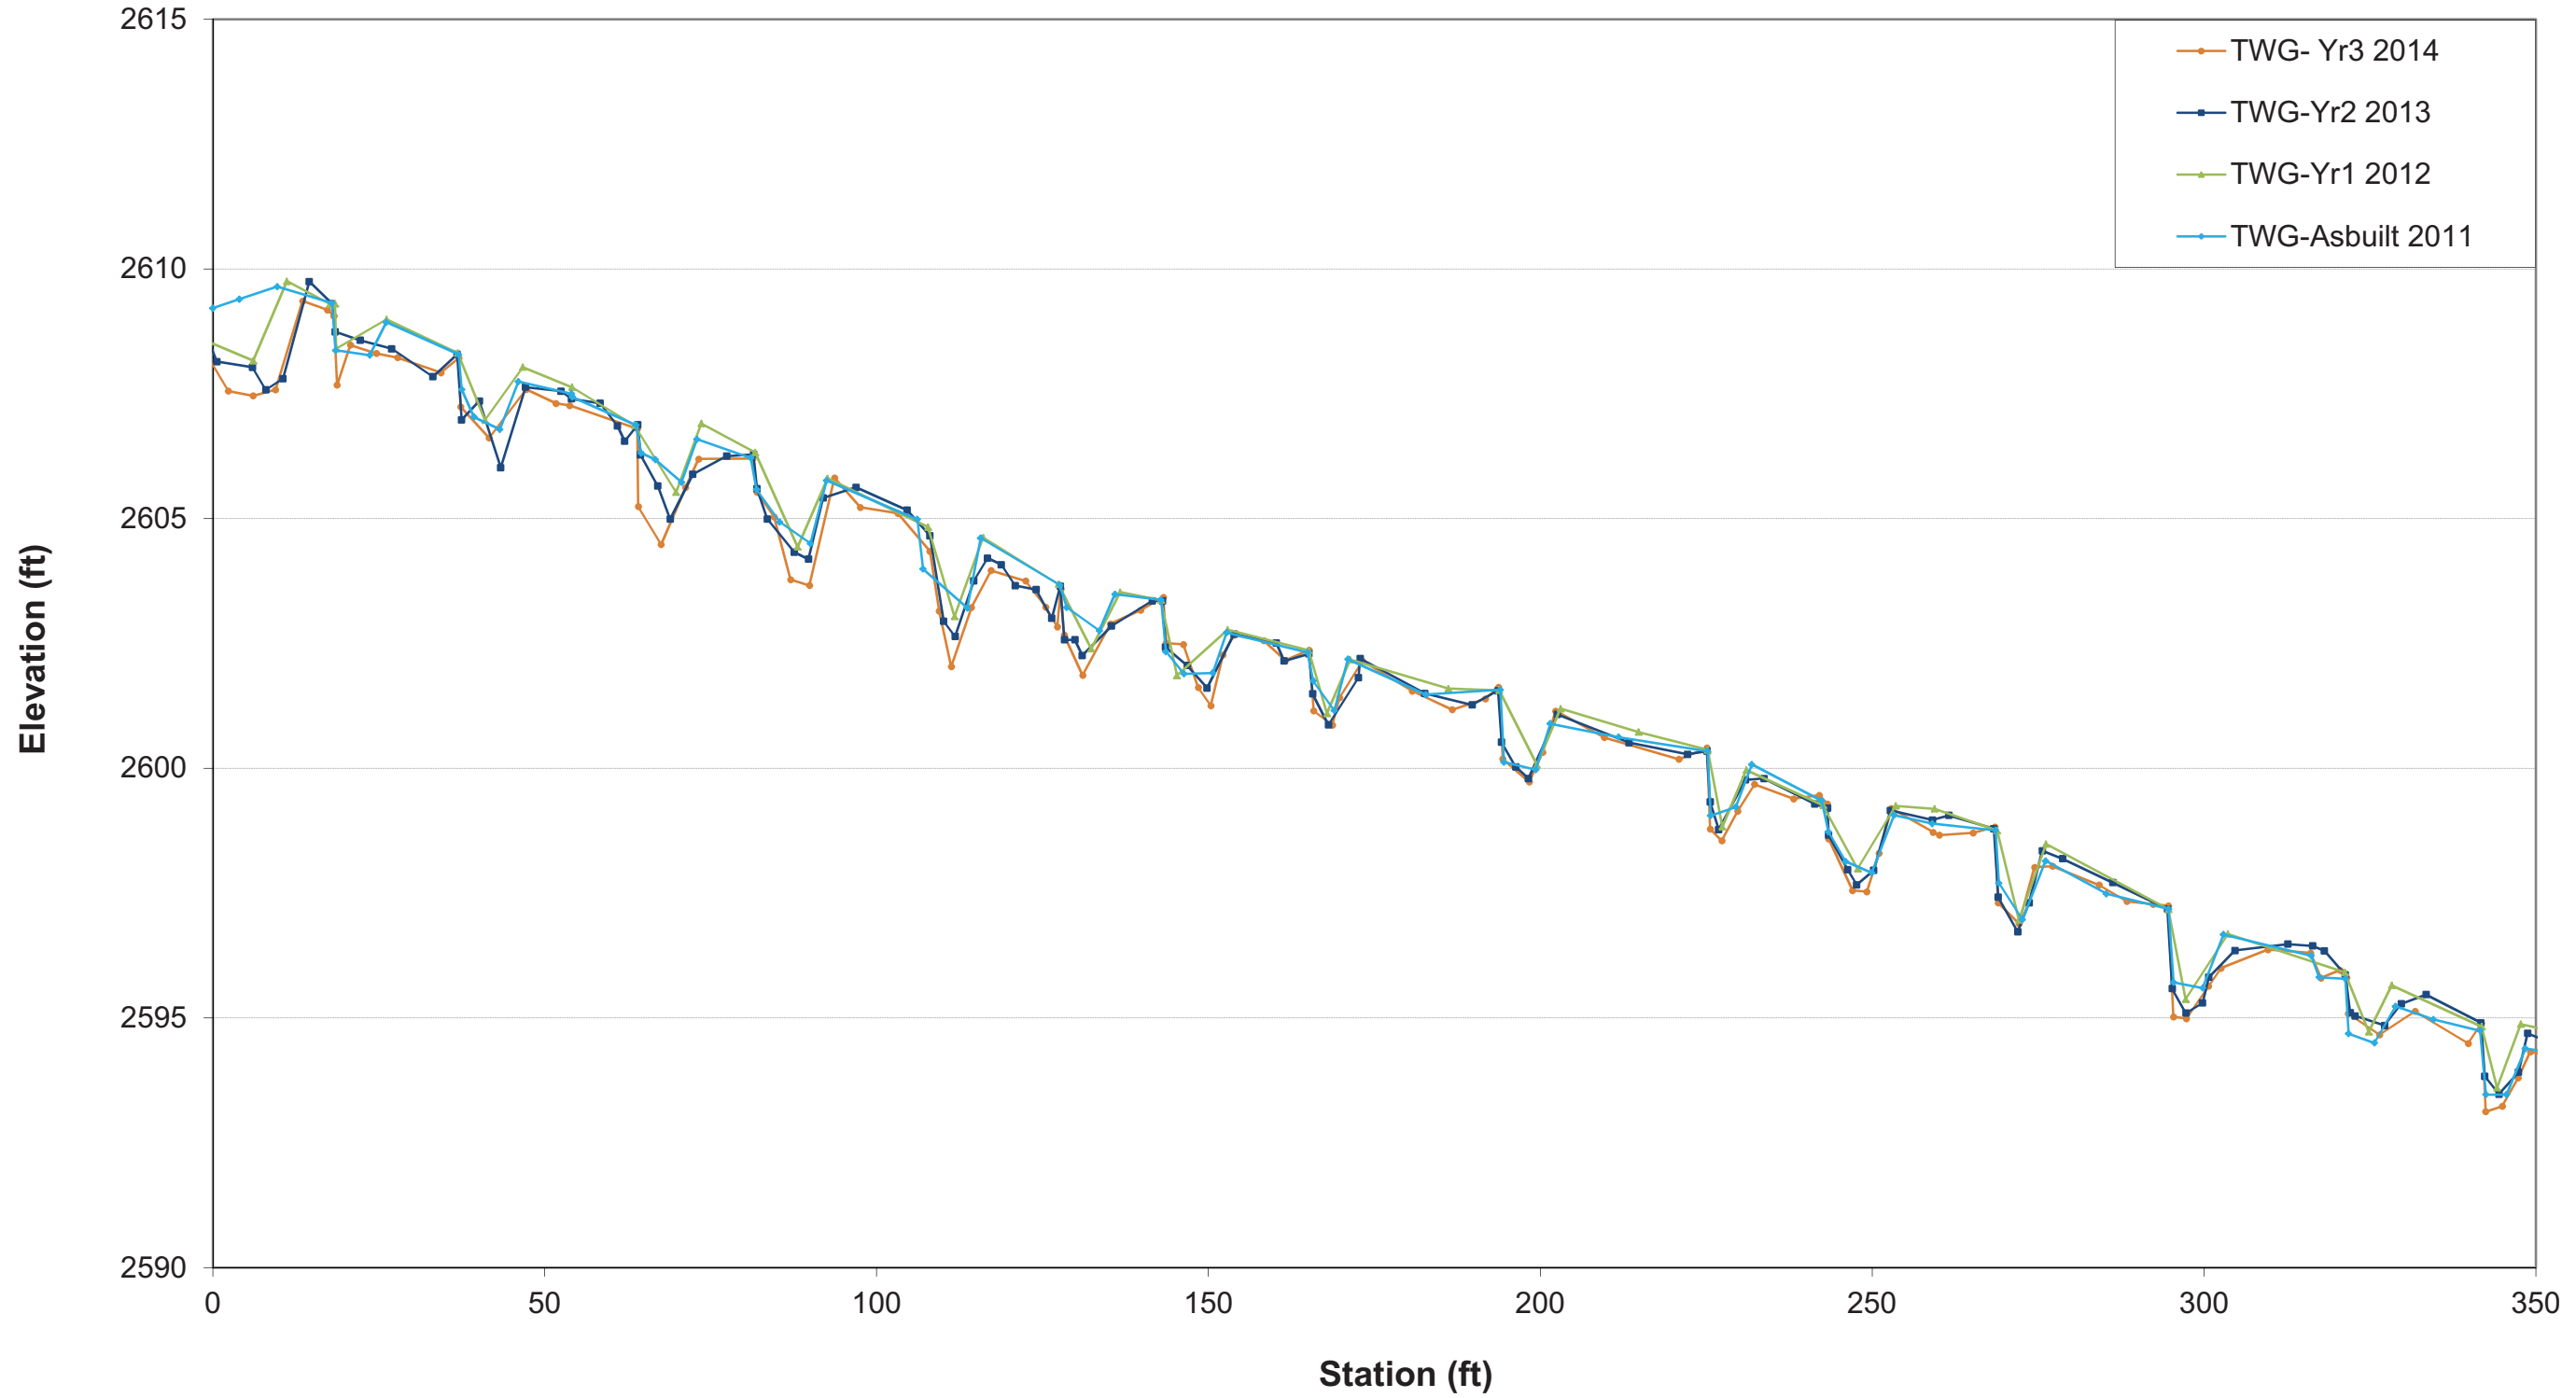


Longitudinal Profile - UT1 for Year 3 Monitoring 3+50 to 7+00

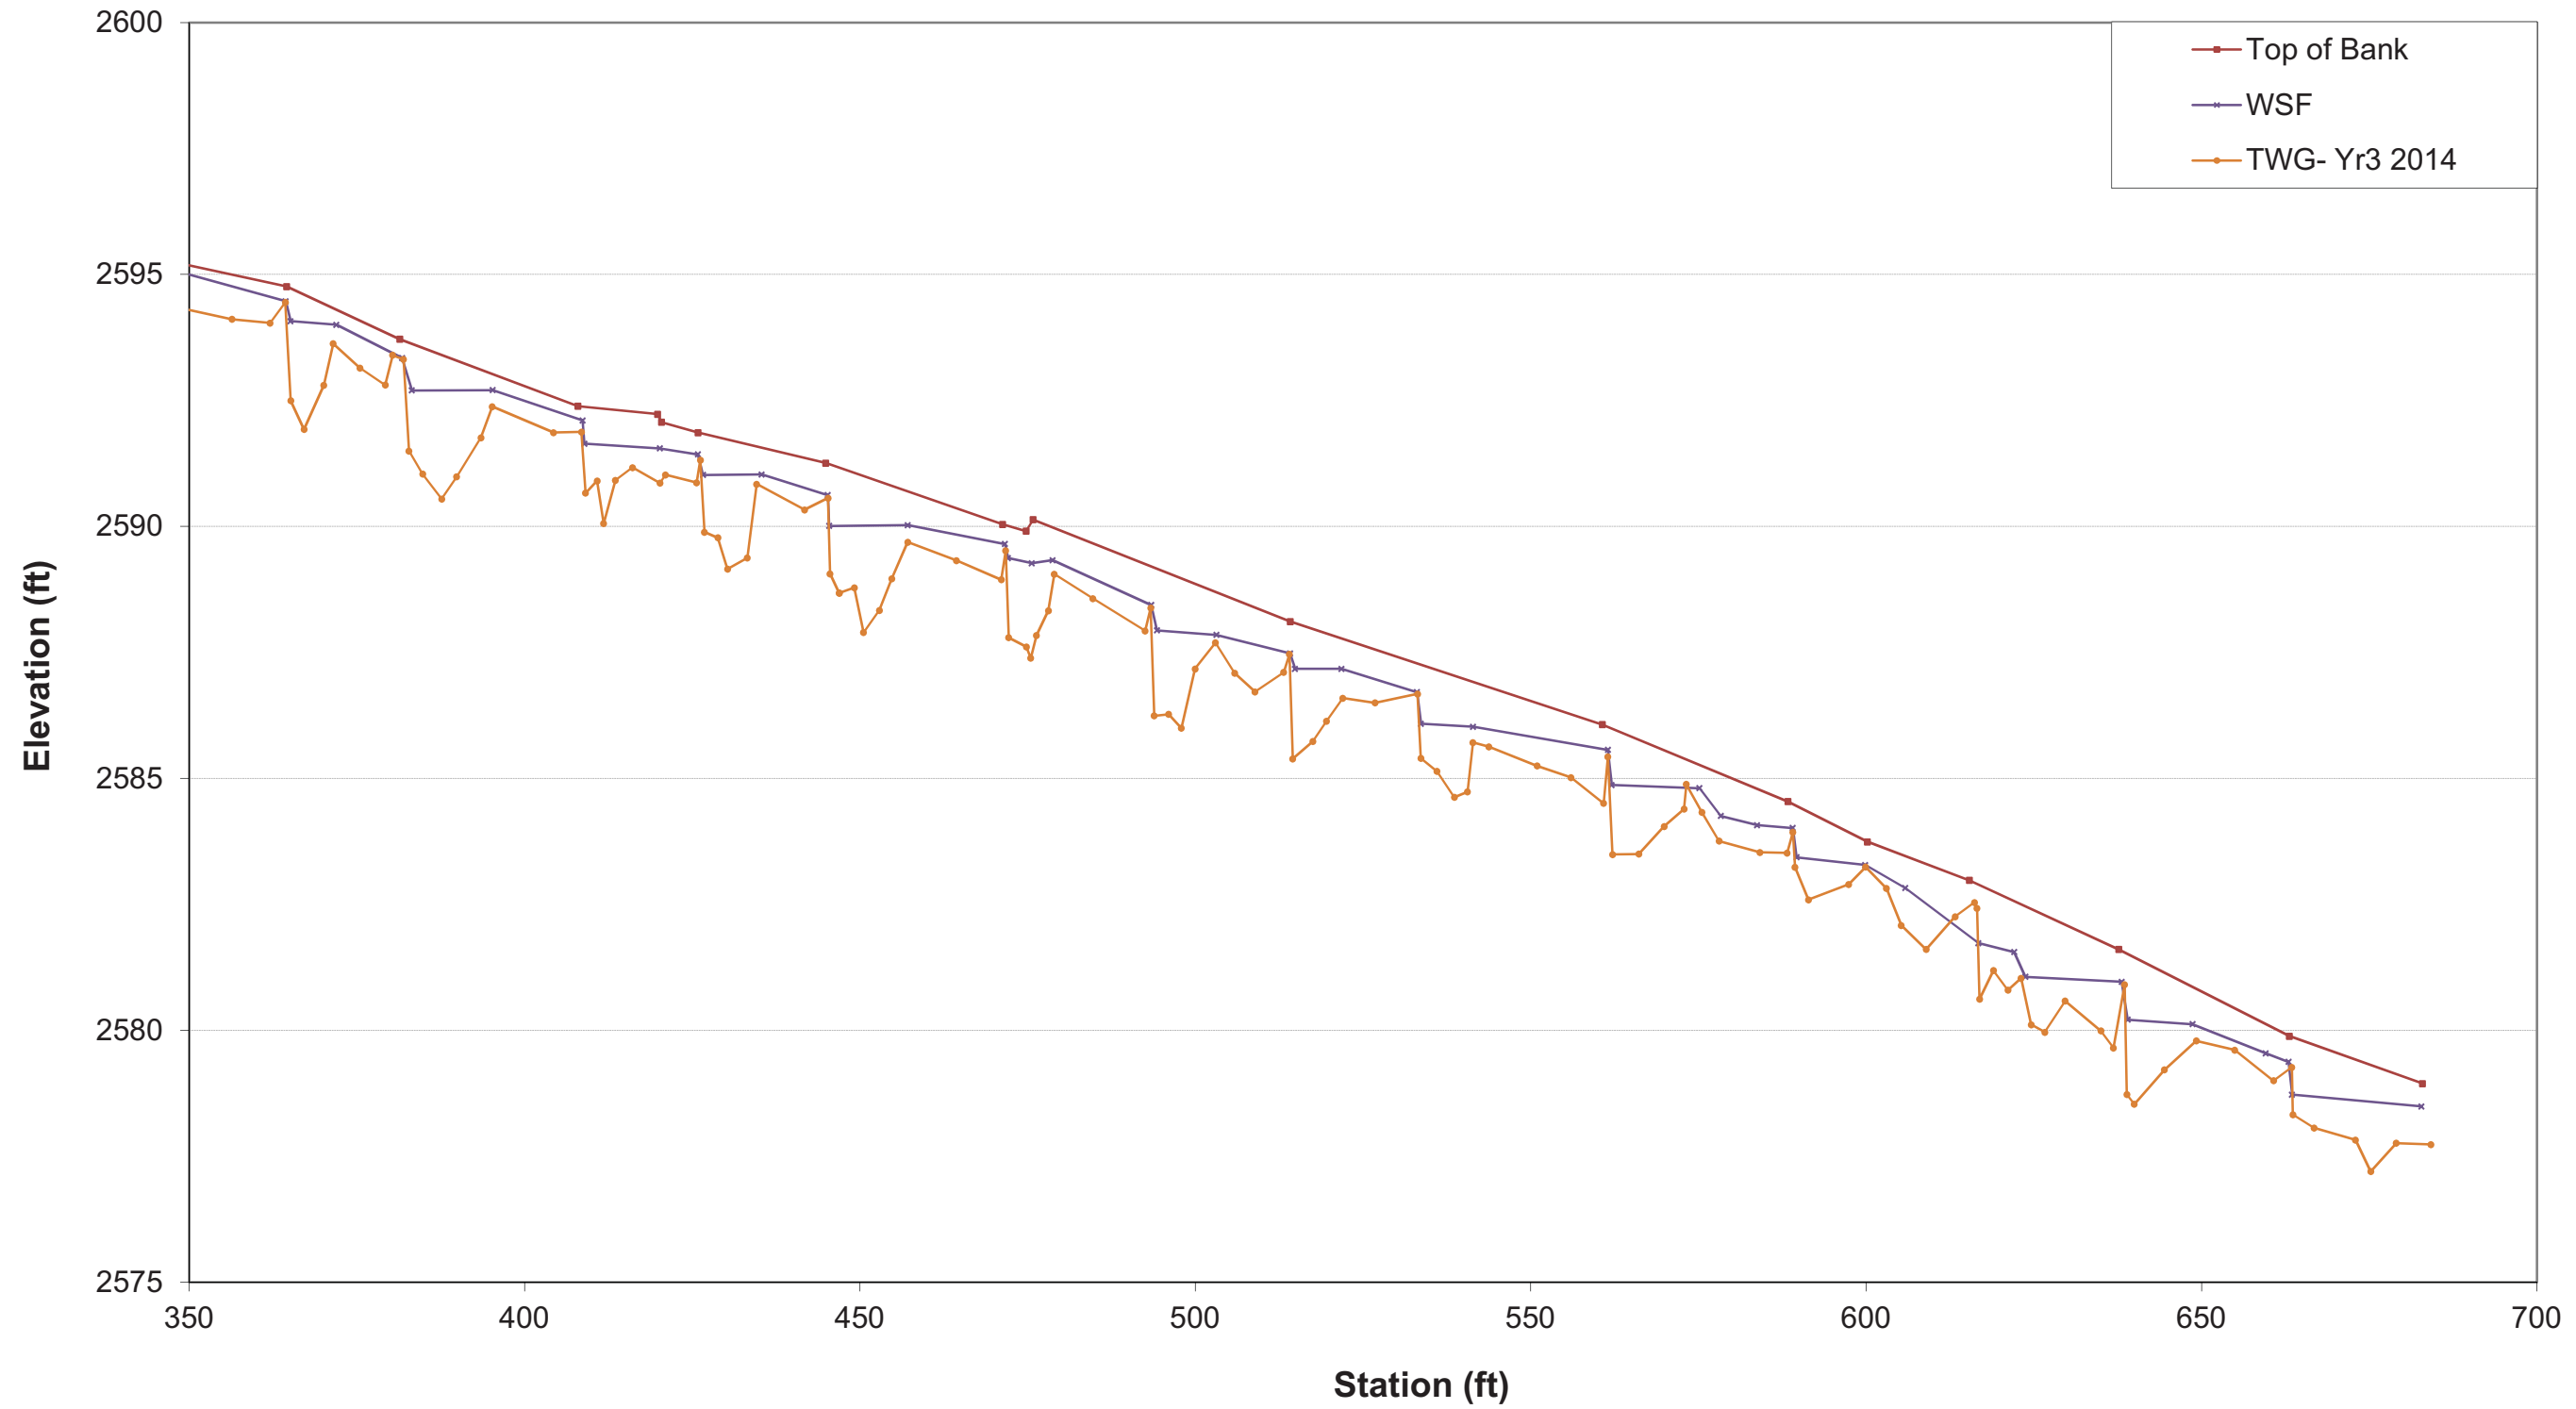


Longitudinal Profile - UT1 for All Years 3+50 to 7+00

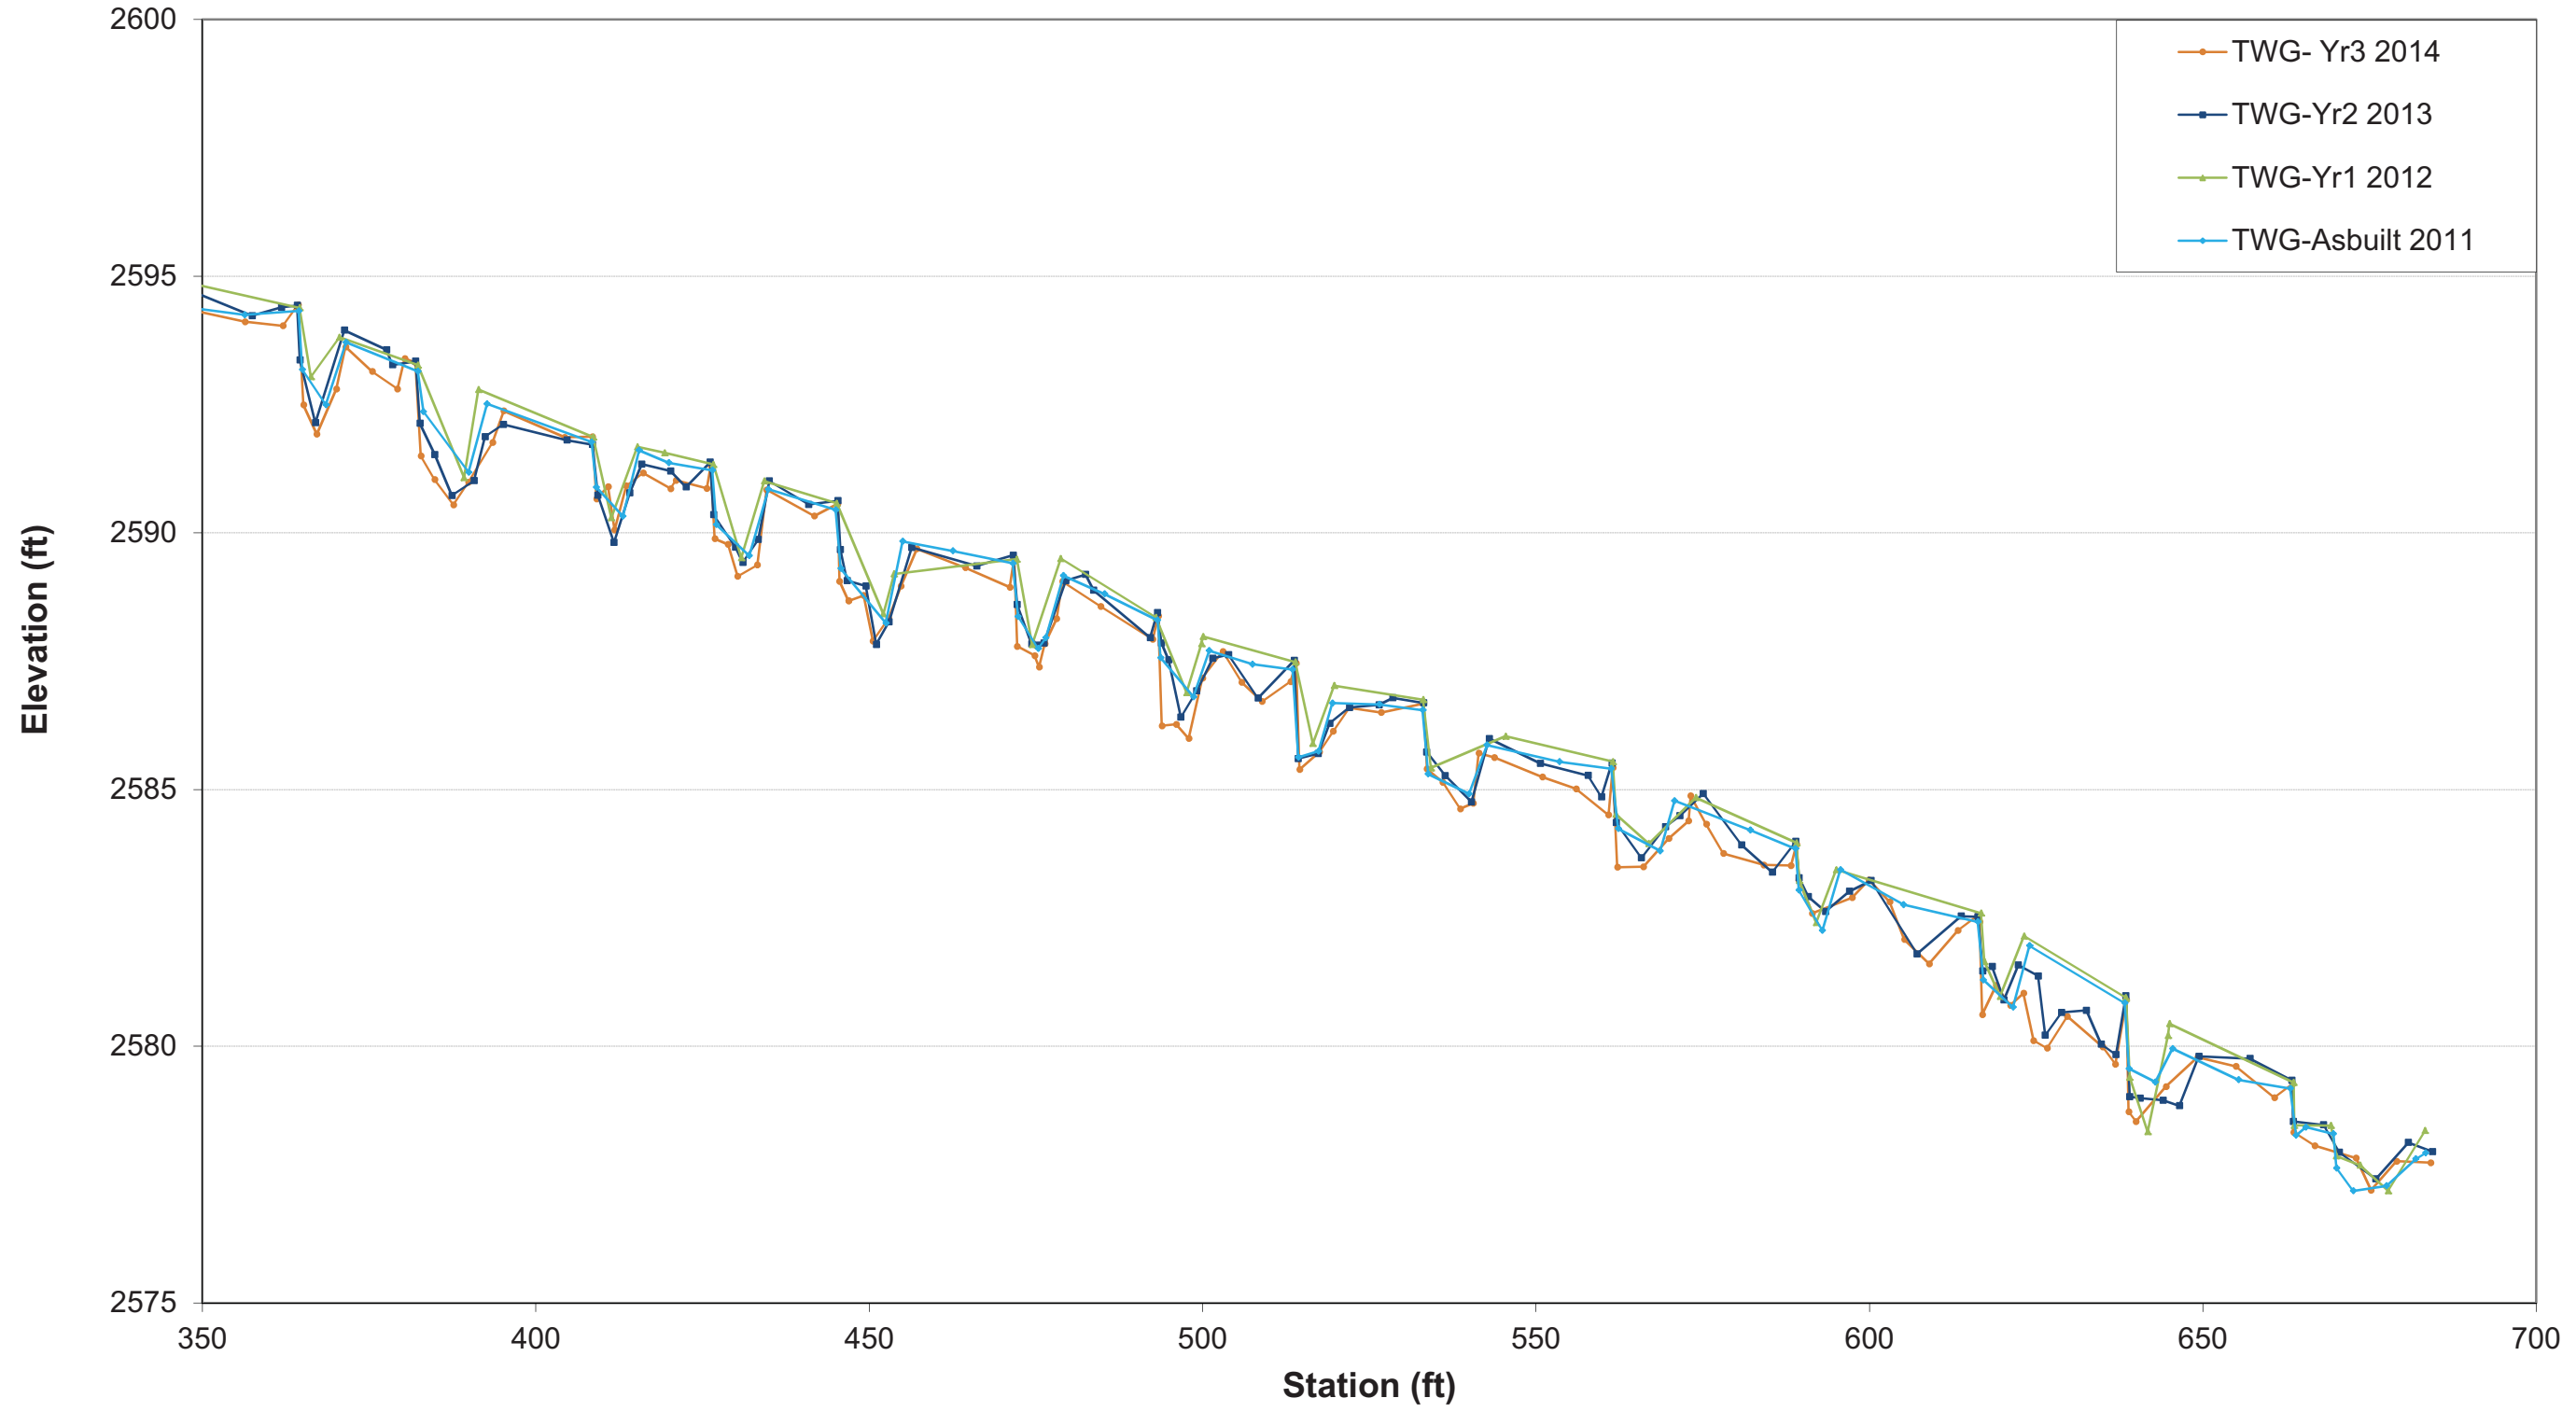

Longitudinal Profile - UT2 for Year 3 Monitoring

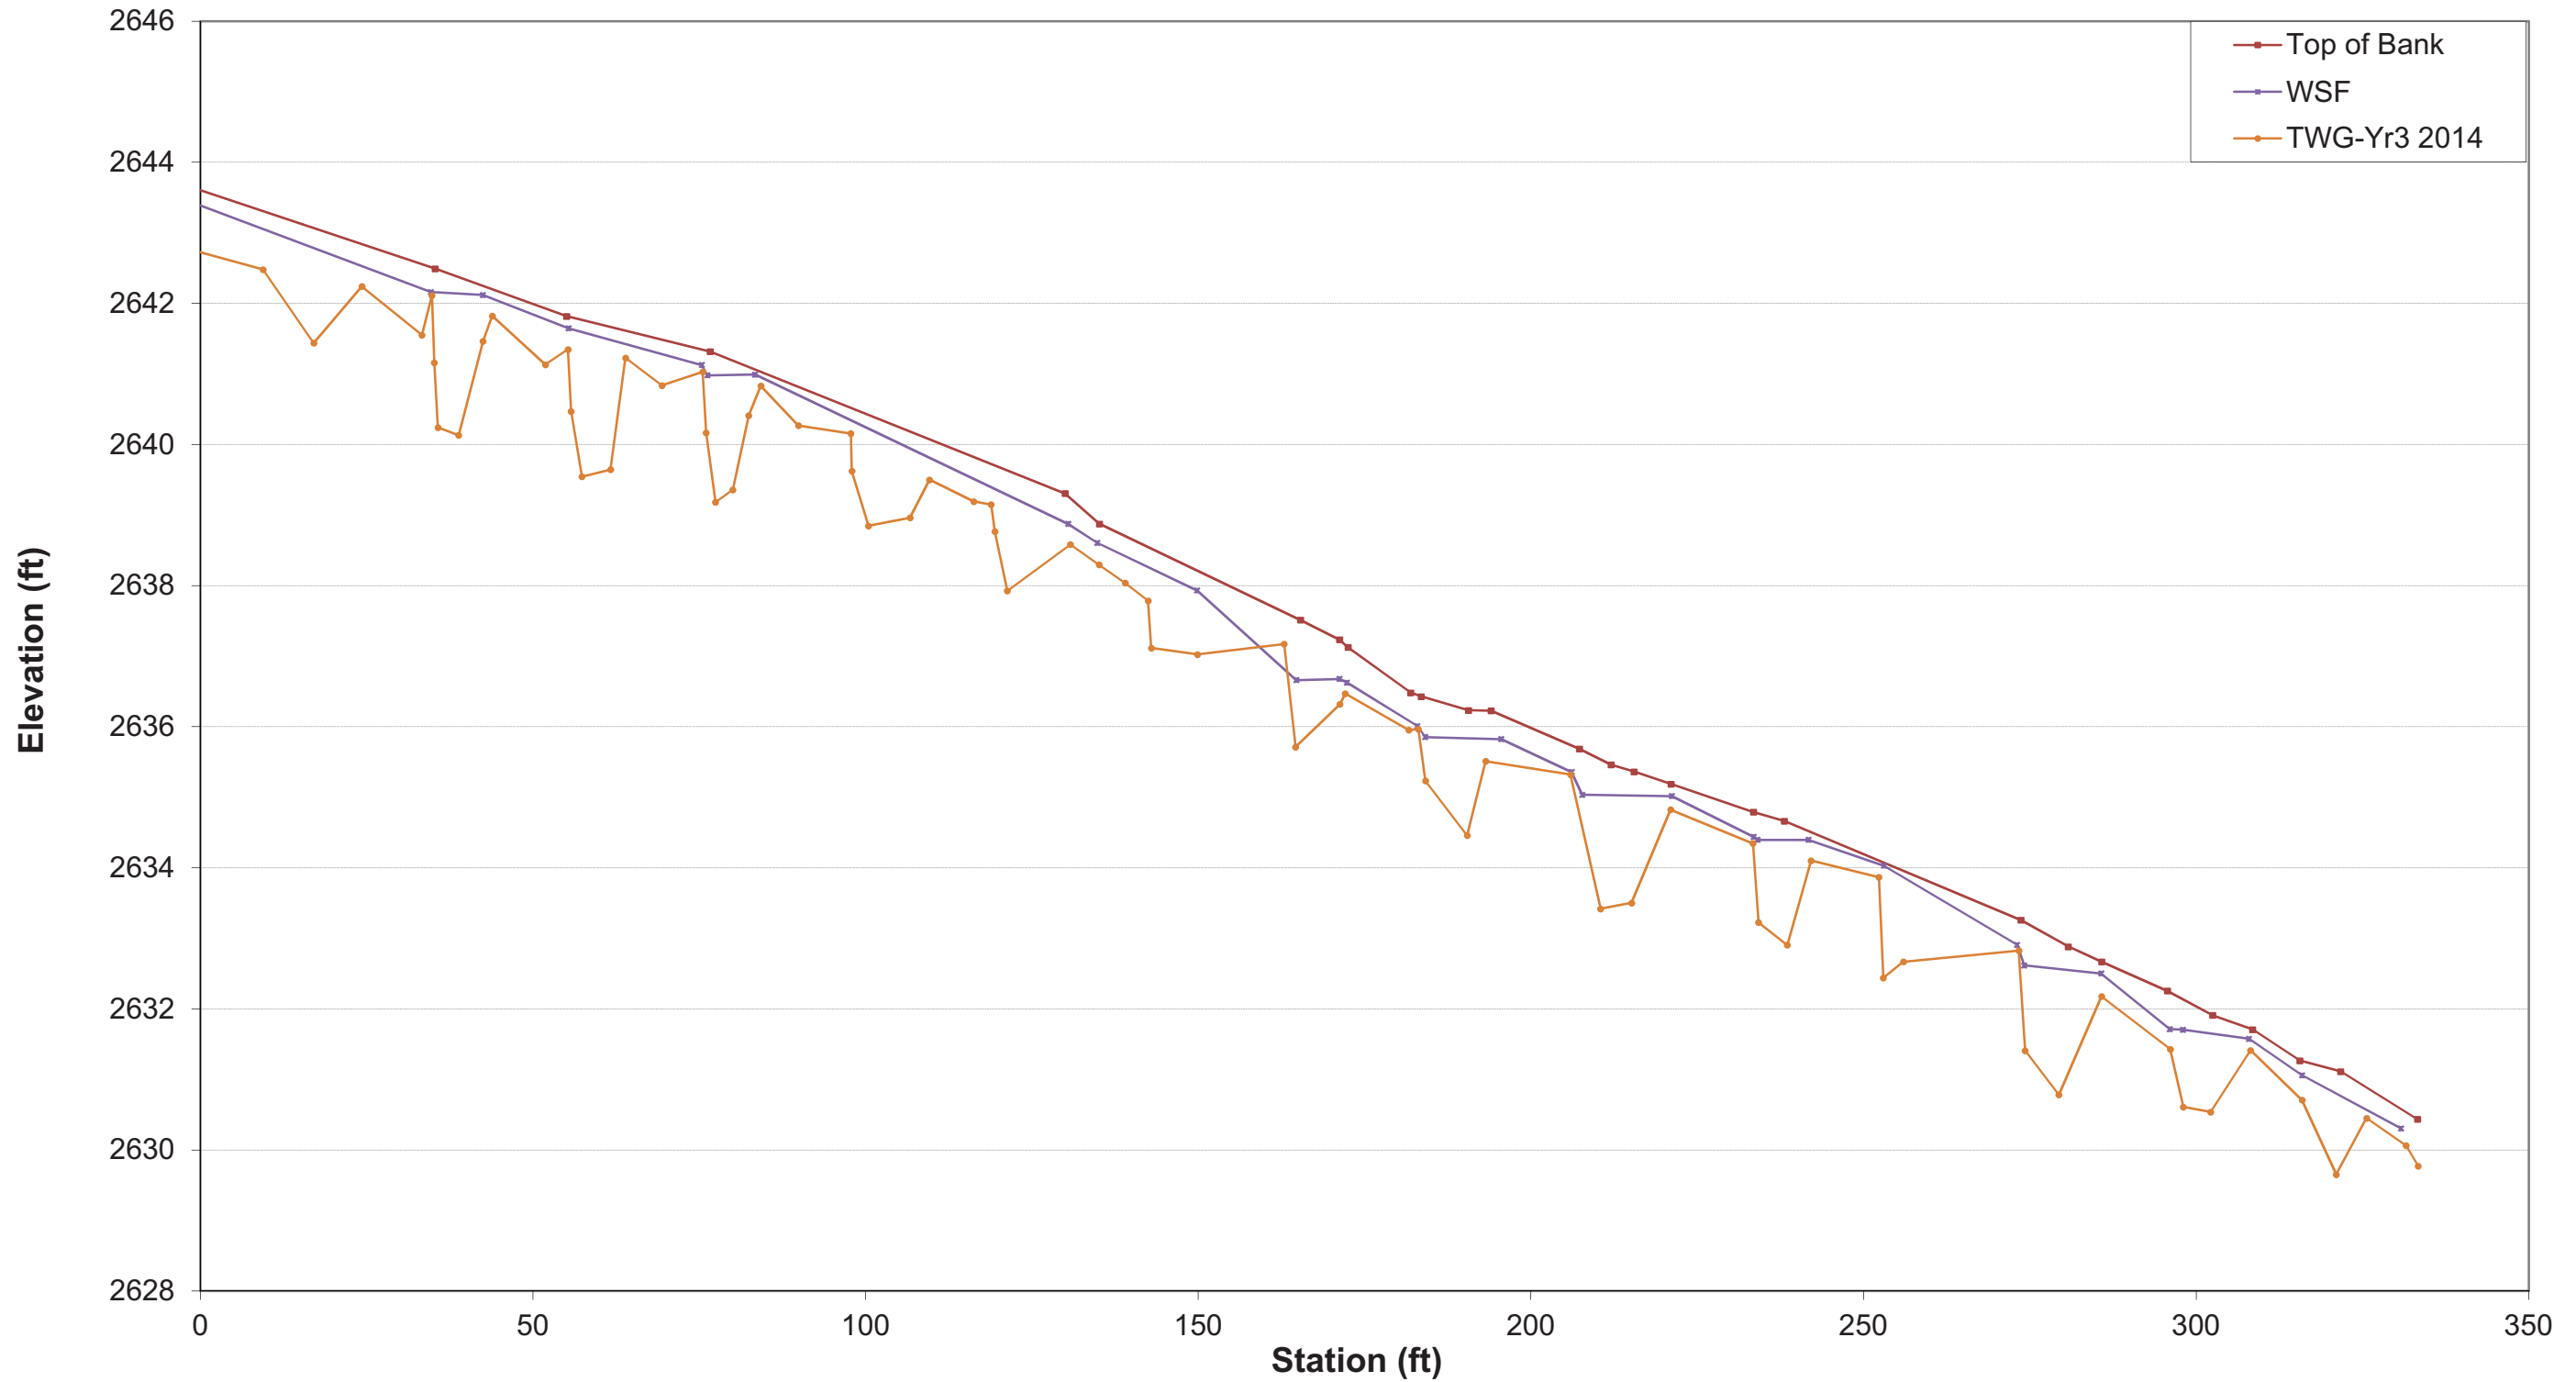

Longitudinal Thalweg Profile on UT2 for All Years

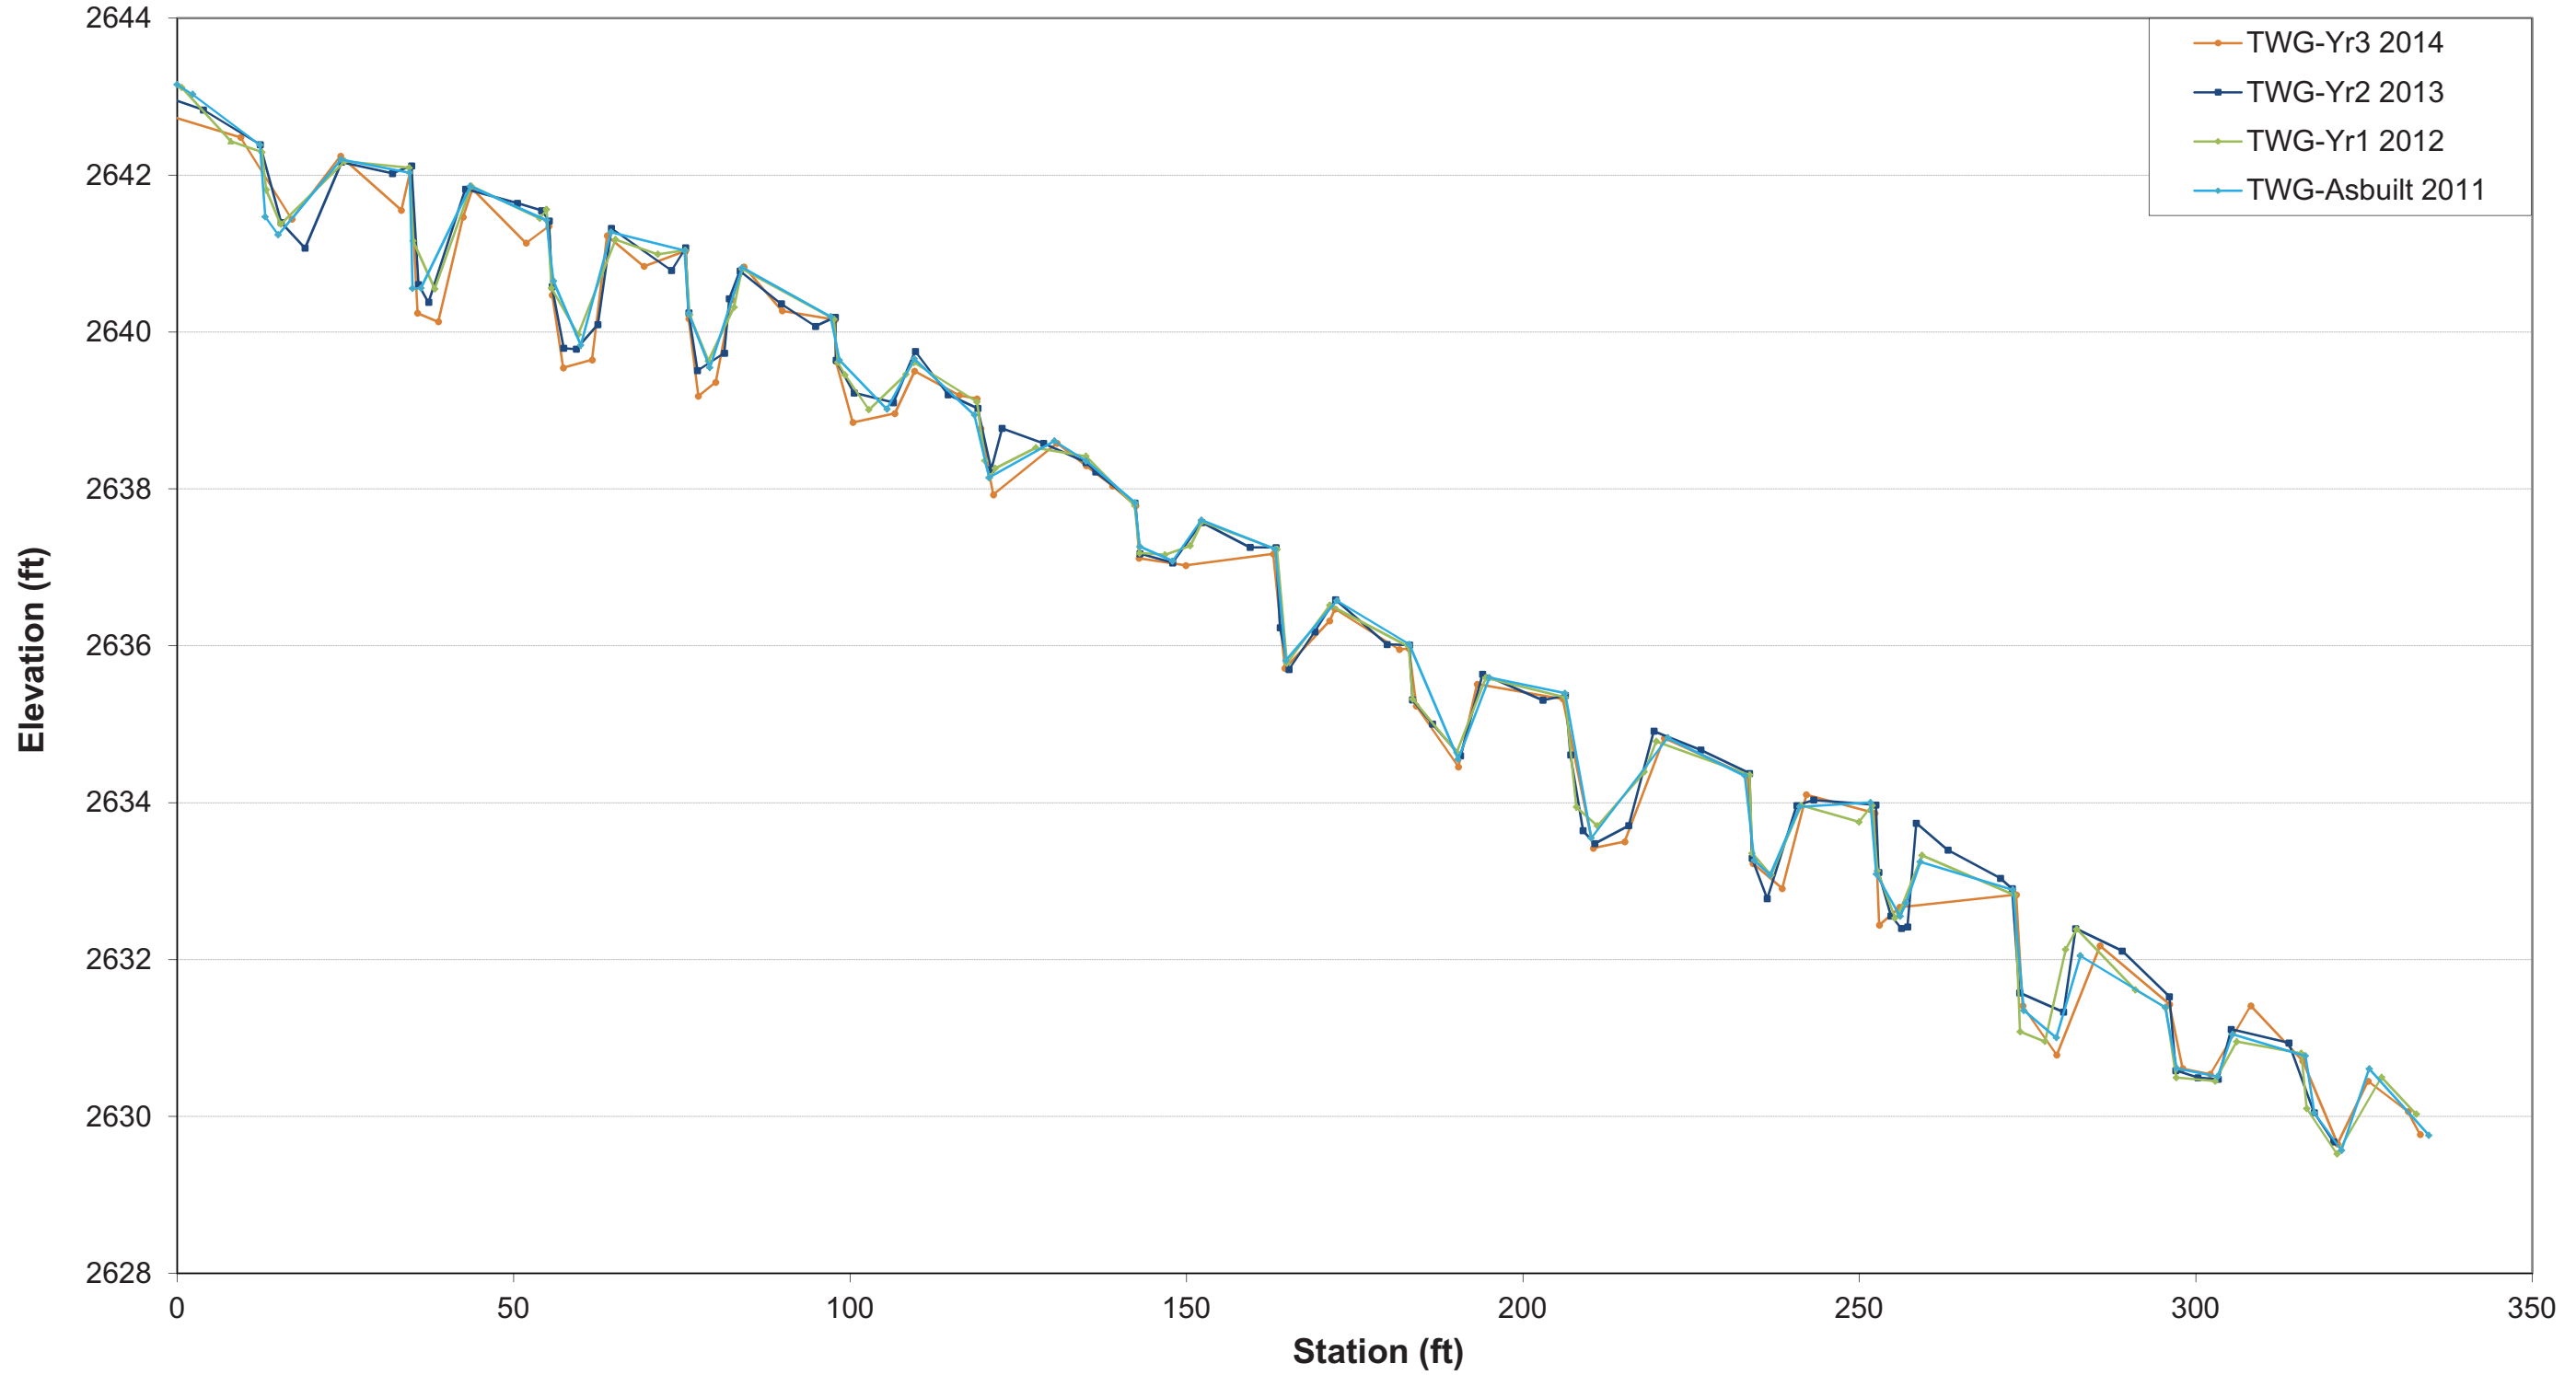

UT2 Longitudinal Thalweg Profile
0+00 to 3+50 All Years

| Table 11. Categorical Visual Morphological Stability Assessment | | | | | | |
|--|----------------|--------------|--------------|--------------|--------------|--------------|
| Elk Branch Mitigation Project - Project No. 92665 | | | | | | |
| Elk Branch Reach 1 (951 LF) | | | | | | |
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 100% | 100% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 100% | 100% | 100% | | |
| Vanes / J Hooks etc. | ----- | ----- | ----- | ----- | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |
| Elk Branch Reach A (592 LF) | | | | | | |
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 100% | 100% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 100% | 100% | 100% | | |
| Vanes / J Hooks etc. | ----- | ----- | ----- | ----- | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |
| Elk Branch Reach B (403 LF) | | | | | | |
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 100% | 100% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 100% | 100% | 100% | | |
| Vanes / J Hooks etc. | 100% | 100% | 100% | 100% | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |
| Elk Branch Reach 2 (186 LF) | | | | | | |
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 100% | 100% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 100% | 100% | 100% | | |
| Vanes / J Hooks etc. | ----- | ----- | ----- | ----- | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |

| UT1 (656LF) | | | | | | |
|----------------------|----------------|--------------|--------------|--------------|--------------|--------------|
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 94% | 100% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 99% | 100% | 100% | | |
| Vanes / J Hooks etc. | ----- | ----- | ----- | ----- | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |
| UT2 (242 LF) | | | | | | |
| Feature | Initial | MY-01 | MY-02 | MY-03 | MY-04 | MY-05 |
| Riffles | 100% | 100% | 100% | 100% | | |
| Pools | 100% | 100% | 100% | 100% | | |
| Thalweg | 100% | 100% | 100% | 100% | | |
| Meanders | ----- | ----- | ----- | ----- | | |
| Bed General | 100% | 79% | 96% | 100% | | |
| Bank Condition | 100% | 100% | 100% | 100% | | |
| Rock/Log Drops | 100% | 100% | 98% | 100% | | |
| Vanes / J Hooks etc. | 100% | 100% | 100% | 100% | | |
| Wads and Boulders | ----- | ----- | ----- | ----- | | |

Table 12. Visual Morphological Stability Assessment
Elk Branch Mitigation Project -Project No. 92665

| Elk Branch Reach 1 (951 LF) | | | | | | |
|------------------------------------|--|--|---------------------------|---------------------------------------|----------------------------------|-----------------------------------|
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 23 | 23 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 23 | 23 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 23 | 23 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 23 | 23 | 0/0 | 100 | |
| | 5. Length appropriate? | 23 | 23 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 30 | 30 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 30 | 30 | 0/0 | 100 | |
| | 3. Length appropriate? | 30 | 30 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General | 1. General channel bed aggradation areas (bar formation) | 951 | 951 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 951 | 951 | 0/0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 30 | 30 | 0/0 | 100 | |
| | 2. Height appropriate? | 30 | 30 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 30 | 30 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 30 | 30 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| Elk Branch Reach A (592 LF) | | | | | | |
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 15 | 15 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 15 | 15 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 15 | 15 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 15 | 15 | 0/0 | 100 | |
| | 5. Length appropriate? | 15 | 15 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 15 | 15 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 15 | 15 | 0/0 | 100 | |
| | 3. Length appropriate? | 15 | 15 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General | 1. General channel bed aggradation areas (bar formation) | 592 | 592 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 592 | 592 | 0/0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 9 | 9 | 0/0 | 100 | |
| | 2. Height appropriate? | 9 | 9 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 9 | 9 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 9 | 9 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| Elk Branch Reach B (403 LF) | | | | | | |
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 14 | 14 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 14 | 14 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 14 | 14 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 14 | 14 | 0/0 | 100 | |
| | 5. Length appropriate? | 14 | 14 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 14 | 14 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 14 | 14 | 0/0 | 100 | |
| | 3. Length appropriate? | 14 | 14 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |

| | | | | | | |
|------------------------------------|--|--|---------------------------|---------------------------------------|----------------------------------|-----------------------------------|
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General | 1. General channel bed aggradation areas (bar formation) | 403 | 403 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 403 | 403 | 0/0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 14 | 14 | 0/0 | 100 | |
| | 2. Height appropriate? | 14 | 14 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 14 | 14 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 14 | 14 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| Elk Branch Reach 2 (279 LF) | | | | | | |
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 7 | 7 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 7 | 7 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 7 | 7 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 7 | 7 | 0/0 | 100 | |
| | 5. Length appropriate? | 7 | 7 | 0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 7 | 7 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 7 | 7 | 0/0 | 100 | |
| | 3. Length appropriate? | 7 | 7 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General | 1. General channel bed aggradation areas (bar formation) | 279 | 279 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 279 | 279 | 0/0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 7 | 7 | 0/0 | 100 | |
| | 2. Height appropriate? | 7 | 7 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 7 | 7 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 7 | 7 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| UT1 (656 LF) | | | | | | |
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 29 | 29 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 29 | 29 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 29 | 29 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 29 | 29 | 0/0 | 100 | |
| | 5. Length appropriate? | 29 | 29 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 30 | 30 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 30 | 30 | 0/0 | 100 | |
| | 3. Length appropriate? | 30 | 30 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General ⁴ | 1. General channel bed aggradation areas (bar formation) | 656 | 656 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 656 | 656 | 0/0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 29 | 29 | 0/0 | 100 | |
| | 2. Height appropriate? | 29 | 29 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 29 | 29 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 29 | 29 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |

| UT2 (242 LF) | | | | | | |
|---|--|--|---------------------------|---------------------------------------|----------------------------------|-----------------------------------|
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 10 | 10 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 10 | 10 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 10 | 10 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 10 | 10 | 0/0 | 100 | |
| | 5. Length appropriate? | 10 | 10 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 10 | 10 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 10 | 10 | 0/0 | 100 | |
| | 3. Length appropriate? | 10 | 10 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General ⁴ | 1. General channel bed aggradation areas (bar formation) | 242 | 242 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 242 | 242 | 0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 11 | 11 | 0/0 | 100 | |
| | 2. Height appropriate? | 11 | 11 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 11 | 11 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 10 | 11 | 0/0 | 91 | 98% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| UT3 (36 LF) | | | | | | |
| Feature Category | Metric (per As-Built and reference baselines) | (# Stable) Number Performing as Intended | Total number per As-Built | Total Number / feet in unstable state | % Performing in Stable Condition | Feature Performance Mean or Total |
| A. Riffles | 1. Present? | 3 | 3 | 0/0 | 100 | |
| | 2. Armor stable (e.g. no displacement)? | 3 | 3 | 0/0 | 100 | |
| | 3. Facet grades appears stable? | 3 | 3 | 0/0 | 100 | |
| | 4. Minimal evidence of embedding/fining? | 3 | 3 | 0/0 | 100 | |
| | 5. Length appropriate? | 3 | 3 | 0/0 | 100 | 100% |
| B. Pools | 1. Present? (e.g. not subject to severe aggradation or migration?) | 2 | 2 | 0/0 | 100 | |
| | 2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?) | 2 | 2 | 0/0 | 100 | |
| | 3. Length appropriate? | 2 | 2 | 0/0 | 100 | 100% |
| C. Thalweg ¹ | 1. Upstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | |
| | 2. Downstream of pool (structure) centering? | 1 | 1 | 0/0 | 100 | 100% ² |
| D. Meanders | 1. Outer bend in state of limited/controlled erosion? | 0 | 0 | 0/0 | N/A | |
| | 2. Of those eroding, # w/concomitant point bar formation? | 0 | 0 | 0/0 | N/A | |
| | 3. Apparent Rc within spec? | 0 | 0 | 0/0 | N/A | |
| | 4. Sufficient floodplain access and relief? | 0 | 0 | 0/0 | N/A | N/A ³ |
| E. Bed General | 1. General channel bed aggradation areas (bar formation) | 36 | 36 | 0/0 | 100 | |
| | 2. Channel bed degradation - areas of increasing down-cutting or head cutting? | 36 | 36 | 0 | 100 | 100% |
| F. Vanes, Rock/Log Drop Structures | 1. Free of back or arm scour? | 2 | 2 | 0/0 | 100 | |
| | 2. Height appropriate? | 2 | 2 | 0/0 | 100 | |
| | 3. Angle and geometry appear appropriate? | 2 | 2 | 0/0 | 100 | |
| | 4. Free of piping or other structural failures? | 2 | 2 | 0/0 | 100 | 100% |
| G. Wads/Boulders | 1. Free of scour? | N/A | N/A | N/A | N/A | |
| | 2. Footing stable? | N/A | N/A | N/A | N/A | N/A |
| ¹ Thalweg feature is scored according to the centering of the thalweg over inverts of drop structures above pools and through the constructed riffle below pools since this reach is a step-pool channel without meander bends. It should be noted that this was difficult to access as thick stands of herbaceous vegetation was covering the channel and even the drop structures were located by feeling along the bottom. ² 100% of the structures and riffles had a centered thalweg. ³ Given the stream types present within the project area, stream flow energy was primarily managed vertically through drop control structures. Pattern adjustments were not designed to increase sinuosity on-site. As a result, the features addressed in Section D. 1-3 are not as common to the project site as they are on C or E type channels in more gently sloping terrain. Pattern adjustments were limited to maintaining channel in low point of the valley. | | | | | | |

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary Elk Branch: Reach 1 | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|----------------|------|----------------------------|-------|-------|--------------------------------|-------|-------|------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | (As-Built) | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| Dimension - Riffle | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max |
| Bankfull Width (ft) | 6.3-9.3 | 3.9 | 5.9 | 7.8 | 11.7 | 19.7 | 27.6 | 4.0 | 7.3 | 10.5 | ---- | 6.1 | ---- | ---- | 5.5 | ---- | ---- | 5.2 | ---- | ---- | 6.4 | ---- |
| Floodprone Width (ft) | ---- | 5.2 | 30.1 | 55.0 | 20.0 | ---- | 41.0 | 9.0 | 44.5 | 80.0 | ---- | 30.9 | ---- | ---- | 24.3 | ---- | ---- | 26.4 | ---- | ---- | 30.5 | ---- |
| Bankfull Mean Depth (ft) | .44-.61 | 0.48 | 0.80 | 1.12 | 0.60 | 0.85 | 1.10 | 0.40 | 0.58 | 0.75 | ---- | 0.67 | ---- | ---- | 0.46 | ---- | ---- | 0.51 | ---- | ---- | 0.5 | ---- |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.50 | 0.75 | 1.00 | ---- | 0.98 | ---- | ---- | 0.72 | ---- | ---- | 0.89 | ---- | ---- | 0.9 | ---- |
| Bankfull Cross Sectional Area (ft2) | 3.6-6.8 | 2.9 | 8.7 | 14.5 | 10.2 | 21.6 | 33.0 | 3.0 | 5.0 | 7.0 | ---- | 4.1 | ---- | ---- | 2.6 | ---- | ---- | 2.7 | ---- | ---- | 3.1 | ---- |
| Width/Depth Ratio | ---- | 5.0 | 9.5 | 14.0 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | ---- | 9.0 | ---- | ---- | 12.0 | ---- | ---- | 10.1 | ---- | ---- | 13.0 | ---- |
| Entrenchment Ratio | ---- | 1.6 | 4.3 | 7.0 | 1.3 | 2.3 | 3.2 | 3.0 | 5.3 | 7.6 | ---- | 5.1 | ---- | ---- | 4.4 | ---- | ---- | 5.1 | ---- | ---- | 4.8 | ---- |
| Bank Height Ratio | ---- | 1.4 | 2.3 | 3.1 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.3 | ---- | ---- | 1.3 | ---- |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | ---- | 2.6 | ---- | ---- | 4.1 | ---- | ---- | 3.9 | ---- | ---- | 3.4 | ---- |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | 2 | 3 | 4 | 16 | 36 | 55 | 11 | 45 | 80 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | 2 | 4 | 7 | 28 | 38 | 47 | 5 | 15 | 25 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | 9 | 23 | 38 | 70 | 165 | 260 | 21 | 52 | 82 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | 0.4 | 0.6 | 0.8 | 1.1 | 2.6 | 4.1 | 3.5 | 5.8 | 8.0 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 18.0 | 33.6 | 50.7 | 21.1 | 29.2 | 37.2 | 20.4 | 30.8 | 38.0 | 12.8 | 38.3 | 93.6 |
| Riffle Slope (ft/ft) | ---- | 0.02 | 0.03 | 0.03 | 0.200 | 0.480 | 0.760 | 0.022 | 0.037 | 0.051 | 0.021 | 0.029 | 0.045 | 0.017 | 0.026 | 0.031 | 0.018 | 0.026 | 0.034 | 0.011 | 0.024 | 0.039 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13 | 15 | 16 | ---- | ---- | ---- | 2.5 | 6.4 | 9.5 | 2.3 | 7.5 | 13.2 | 8.6 | 10.2 | 13.4 | 7.5 | 11.7 | 18.2 |
| Pool Spacing (ft) | ---- | 42 | ---- | 157 | 42.0 | 136.5 | 231.0 | 9.0 | 29.5 | 50.0 | 17.1 | 39.6 | 54.6 | 14.7 | 39.2 | 54.1 | 17.2 | 39.9 | 52.7 | 26.5 | 49.9 | 106.6 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | 1.2/6.6/13/65/130 | | | 1-6/14/31-39/51-88/110-210 | | | .6-1.5/2-7/6.2-19/19-65/26-130 | | | --- | | | --- | | | --- | | | --- | | |
| Reach Shear Stress (competency) lb/f2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.0 | ---- | ---- | ---- | 0.7 | ---- | ---- | 0.7 | ---- | ---- | 0.7 | ---- |
| Stream Power (transport capacity) W/m2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.6 | ---- | ---- | ---- | 2.8 | ---- | ---- | 2.6 | ---- | ---- | 2.3 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 901 | ---- | ---- | 901 | ---- | ---- | 901 | ---- | ---- | 901 | ---- | ---- | 901 | ---- |
| Drainage Area (SM) | ---- | 0.03 | 0.05 | 0.07 | 0.45 | 1.03 | 1.60 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 |
| Rosgen Classification | ---- | ---- | Cb/B/G /Eb4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 7-13 | ---- | ---- | ---- | ---- | ---- | ---- | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | 1.02 | 1.07 | 1.11 | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.033 | ---- | ---- | 0.032 | ---- | ---- | 0.029 | ---- | ---- | 0.027 | ---- |

Table 13. Stream Reach Morphology and Hydraulic Data Elk Branch Reach 1

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary Elk Branch: Reach A | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|----------------|------|----------------------------|-------|-------|--------------------------------|-------|-------|-----------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | (As-Built) | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| Dimension - Riffle | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max |
| Bankfull Width (ft) | 6.3-9.3 | 3.9 | 5.9 | 7.8 | 11.7 | 19.7 | 27.6 | 4.0 | 7.3 | 10.5 | ---- | 8.1 | ---- | ---- | 7.3 | ---- | ---- | 8.2 | ---- | ---- | 7.9 | ---- |
| Floodprone Width (ft) | ---- | 5.2 | 30.1 | 55.0 | 20.0 | ---- | 41.0 | 9.0 | 44.5 | 80.0 | ---- | 34.6 | ---- | ---- | 32.5 | ---- | ---- | 35.6 | ---- | ---- | 32.7 | ---- |
| Bankfull Mean Depth (ft) | .44-.61 | 0.48 | 0.80 | 1.12 | 0.60 | 0.85 | 1.10 | 0.40 | 0.58 | 0.75 | ---- | 0.51 | ---- | ---- | 0.40 | ---- | ---- | 0.42 | ---- | ---- | 0.3 | ---- |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.50 | 0.75 | 1.00 | ---- | 0.83 | ---- | ---- | 0.80 | ---- | ---- | 0.95 | ---- | ---- | 0.8 | ---- |
| Bankfull Cross Sectional Area (ft2) | 3.6-6.8 | 2.9 | 8.7 | 14.5 | 10.2 | 21.6 | 33.0 | 3.0 | 5.0 | 7.0 | ---- | 4.2 | ---- | ---- | 2.9 | ---- | ---- | 3.4 | ---- | ---- | 2.7 | ---- |
| Width/Depth Ratio | ---- | 5.0 | 9.5 | 14.0 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | ---- | 15.8 | ---- | ---- | 18.4 | ---- | ---- | 19.6 | ---- | ---- | 22.8 | ---- |
| Entrenchment Ratio | ---- | 1.6 | 4.3 | 7.0 | 1.3 | 2.3 | 3.2 | 3.0 | 5.3 | 7.6 | ---- | 4.3 | ---- | ---- | 4.4 | ---- | ---- | 4.3 | ---- | ---- | 3.9 | ---- |
| Bank Height Ratio | ---- | 1.4 | 2.3 | 3.1 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | ---- | 2.5 | ---- | ---- | 3.6 | ---- | ---- | 3.1 | ---- | ---- | 3.9 | ---- |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | 2 | 3 | 4 | 16 | 36 | 55 | 11 | 45 | 80 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | 2 | 4 | 7 | 28 | 38 | 47 | 5 | 15 | 25 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | 9 | 23 | 38 | 70 | 165 | 260 | 21 | 52 | 82 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | 0.40 | 0.60 | 0.80 | 1.10 | 2.60 | 4.10 | 3.50 | 5.75 | 8.00 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 34.0 | 45.0 | 63.7 | 31.4 | 43.9 | 63.8 | 35.0 | 44.0 | 64.0 | 20.5 | 52.2 | 107.2 |
| Riffle Slope (ft/ft) | ---- | 0.02 | 0.03 | 0.03 | 0.200 | 0.480 | 0.760 | 0.022 | 0.037 | 0.051 | 0.010 | 0.025 | 0.040 | 0.013 | 0.026 | 0.037 | 0.008 | 0.022 | 0.039 | 0.010 | 0.022 | 0.038 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13 | 15 | 16 | ---- | ---- | ---- | 4.0 | 4.9 | 6.0 | 5.1 | 9.0 | 11.7 | 9.0 | 12.0 | 14.0 | 8.5 | 11.7 | 18.9 |
| Pool Spacing (ft) | ---- | 42 | ---- | 157 | 42 | 137 | 231 | 9.0 | 29.5 | 50.0 | 21.7 | 43.4 | 56.7 | 27.8 | 44.0 | 54.1 | 21.0 | 41.0 | 55.0 | 16.0 | 61.1 | 127.0 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | 1.2/6.6/13/65/130 | | | 1-6/14/31-39/51-88/110-210 | | | .6-1.5/2-7/6.2-19/19-65/26-130 | | | 3.2/12/17/37/69 | | | 0.2/17/27/69/117 | | | 9.4/24/30/72/152 | | | 18/28/37/82/123 | | |
| Reach Shear Stress (competency) lb/f2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.7 | ---- | ---- | 0.7 | ---- | ---- | 0.7 | ---- | ---- | 0.7 | ---- |
| Stream Power (transport capacity) W/m2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.7 | ---- | ---- | 2.5 | ---- | ---- | 2.1 | ---- | ---- | 2.6 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 642 | ---- | ---- | 642 | ---- | ---- | 642 | ---- | ---- | 642 | ---- | ---- | 642 | ---- |
| Drainage Area (SM) | ---- | ---- | .03-.07 | ---- | 0.45 | 1.03 | 1.60 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 |
| Rosgen Classification | ---- | ---- | Cb/B/G /Eb4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 7-13 | ---- | ---- | ---- | ---- | ---- | ---- | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.027 | ---- | ---- | 0.028 | ---- | ---- | 0.028 | ---- | ---- | 0.027 | ---- |

Table 13. Stream Reach Morphology and Hydraulic Data Elk Branch Reach A

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary Elk Branch: Reach B | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|-------------|-------|--------------------------|-------|-------|--------------------------------|-------|-------|------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | (As-Built) | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| Dimension - Riffle | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max |
| Bankfull Width (ft) | 6.3-9.3 | 3.9 | 5.9 | 7.8 | 11.7 | 19.7 | 27.6 | 4.0 | 7.3 | 10.5 | ---- | 8.7 | ---- | ---- | 8.3 | ---- | ---- | 9.4 | ---- | ---- | 12.6 | ---- |
| Floodprone Width (ft) | ---- | 5.2 | 30.1 | 55.0 | 20.0 | ---- | 41.0 | 9.0 | 44.5 | 80.0 | ---- | 45.0 | ---- | ---- | 46.5 | ---- | ---- | 45.2 | ---- | ---- | 44.4 | ---- |
| Bankfull Mean Depth (ft) | .44-.61 | 0.48 | 0.80 | 1.12 | 0.60 | 0.85 | 1.10 | 0.40 | 0.58 | 0.75 | ---- | 0.65 | ---- | ---- | 0.53 | ---- | ---- | 0.52 | ---- | ---- | 0.4 | ---- |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.50 | 0.75 | 1.00 | ---- | 0.95 | ---- | ---- | 0.75 | ---- | ---- | 0.98 | ---- | ---- | 0.9 | ---- |
| Bankfull Cross Sectional Area (ft ²) | 3.6-6.8 | 2.9 | 8.7 | 14.5 | 10.2 | 21.6 | 33.0 | 3.0 | 5.0 | 7.0 | ---- | 5.7 | ---- | ---- | 4.4 | ---- | ---- | 4.9 | ---- | ---- | 5.1 | ---- |
| Width/Depth Ratio | ---- | 5.0 | 9.5 | 14.0 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | ---- | 13.3 | ---- | ---- | 15.6 | ---- | ---- | 18.0 | ---- | ---- | 31.3 | ---- |
| Entrenchment Ratio | ---- | 1.6 | 4.3 | 7.0 | 1.3 | 2.3 | 3.2 | 3.0 | 5.3 | 7.6 | ---- | 5.2 | ---- | ---- | 5.6 | ---- | ---- | 4.8 | ---- | ---- | 3.5 | ---- |
| Bank Height Ratio | ---- | 1.4 | 2.3 | 3.1 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | ---- | 1.8 | ---- | ---- | 2.4 | ---- | ---- | 2.1 | ---- | ---- | 2.1 | ---- |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | 2 | 3 | 4 | 16 | 36 | 55 | 11 | 45 | 80 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | 2 | 4 | 7 | 28 | 38 | 47 | 5 | 15 | 25 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | 9 | 23 | 38 | 70 | 165 | 260 | 21 | 52 | 82 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | 0.40 | 0.60 | 0.80 | 1.10 | 2.60 | 4.10 | 3.50 | 5.75 | 8.00 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 5.5 | 22.6 | 41.7 | 12.5 | 25.4 | 42.1 | 11.0 | 24.0 | 40.0 | 13.7 | 32.2 | 53.4 |
| Riffle Slope (ft/ft) | ---- | 0.02 | 0.03 | 0.03 | 0.200 | 0.480 | 0.760 | 0.022 | 0.037 | 0.051 | 0.018 | 0.025 | 0.039 | 0.005 | 0.021 | 0.041 | 0.017 | 0.018 | 0.022 | 0.003 | 0.014 | 0.022 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13.0 | 14.5 | 16.0 | ---- | ---- | ---- | 4.1 | 7.6 | 13.6 | 7.9 | 9.3 | 11.2 | 8.1 | 11.2 | 13.0 | 10.6 | 16.4 | 33.8 |
| Pool Spacing (ft) | ---- | 42.0 | ---- | 156.5 | 42.0 | 136.5 | 231.0 | 9.0 | 29.5 | 50.0 | 10.4 | 29.0 | 50.2 | 16.7 | 31.1 | 54.9 | 17.0 | 33.0 | 56.0 | 29.2 | 44.1 | 63.5 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | 1.2/6.6/13/65/130 | | | 6/14/31-39/51-88/110-2' | | | .6-1.5/2-7/6.2-19/19-65/26-130 | | | --- | | | --- | | | --- | | | --- | | |
| Reach Shear Stress (competency) lb/f ² | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.0 | ---- | ---- | 0.9 | ---- | ---- | 0.9 | ---- | ---- | 0.9 | ---- |
| Stream Power (transport capacity) W/m ² | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.9 | ---- | ---- | 2.0 | ---- | ---- | 1.8 | ---- | ---- | 1.8 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 403 | ---- | ---- | 403 | ---- | ---- | 403 | ---- | ---- | 403 | ---- | ---- | 403 | ---- |
| Drainage Area (SM) | ---- | ---- | .03-.07 | ---- | 0.45 | 1.03 | 1.60 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 |
| Rosgen Classification | ---- | ---- | Cb/B/G /Eb4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 7-13 | ---- | ---- | ---- | ---- | ---- | ---- | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.021 | ---- | ---- | 0.023 | ---- | ---- | 0.021 | ---- | ---- | 0.020 | ---- |

Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Reach B

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary Elk Branch: Reach 2 | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|-------------|-------|----------------------------|-------|-------|--------------------------------|-------|-------|------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | (As-Built) | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| Dimension - Riffle* | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max |
| Bankfull Width (ft) | 9.30 | 3.9 | 5.9 | 7.8 | 11.7 | 19.7 | 27.6 | 4.0 | 7.3 | 10.5 | ---- | 9.2 | ---- | ---- | 9.0 | ---- | ---- | 10.3 | ---- | ---- | 12.9 | ---- |
| Floodprone Width (ft) | ---- | 5.2 | 30.1 | 55.0 | 20.0 | ---- | 41.0 | 9.0 | 44.5 | 80.0 | ---- | 43.8 | ---- | ---- | 44.2 | ---- | ---- | 44.1 | ---- | ---- | >44.0 | ---- |
| Bankfull Mean Depth (ft) | 0.61 | 0.48 | 0.80 | 1.12 | 0.60 | 0.85 | 1.10 | 0.40 | 0.58 | 0.75 | ---- | 0.98 | ---- | ---- | 0.96 | ---- | ---- | 1.01 | ---- | ---- | 0.7 | ---- |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.50 | 0.75 | 1.00 | ---- | 2.02 | ---- | ---- | 2.11 | ---- | ---- | 2.49 | ---- | ---- | 2.2 | ---- |
| Bankfull Cross Sectional Area (ft2) | 6.80 | 2.9 | 8.7 | 14.5 | 10.2 | 21.6 | 33.0 | 3.0 | 5.0 | 7.0 | ---- | 9.0 | ---- | ---- | 8.7 | ---- | ---- | 10.4 | ---- | ---- | 9.4 | ---- |
| Width/Depth Ratio | ---- | 5.0 | 9.5 | 14.0 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | ---- | 9.3 | ---- | ---- | 9.4 | ---- | ---- | 10.2 | ---- | ---- | 17.7 | ---- |
| Entrenchment Ratio | ---- | 1.6 | 4.3 | 7.0 | 1.3 | 2.3 | 3.2 | 3.0 | 5.3 | 7.6 | ---- | 4.8 | ---- | ---- | 4.9 | ---- | ---- | 4.3 | ---- | ---- | 3.4 | ---- |
| Bank Height Ratio | ---- | 1.4 | 2.3 | 3.1 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | ---- | 1.2 | ---- | ---- | 1.2 | ---- | ---- | 1.0 | ---- | ---- | 1.1 | ---- |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | 2 | 3 | 4 | 16 | 36 | 55 | 11 | 45 | 80 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | 2 | 4 | 7 | 28 | 38 | 47 | 5 | 15 | 25 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | 9 | 23 | 38 | 70 | 165 | 260 | 21 | 52 | 82 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | 0.40 | 0.60 | 0.80 | 1.10 | 2.60 | 4.10 | 3.50 | 5.75 | 8.00 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 19.4 | 30.4 | 39.6 | 18.9 | 29.6 | 39.9 | 17.0 | 27.0 | 38.0 | 18.8 | 26.5 | 38.2 |
| Riffle Slope (ft/ft) | ---- | 0.02 | 0.03 | 0.03 | 0.200 | 0.480 | 0.760 | 0.022 | 0.037 | 0.051 | 0.021 | 0.028 | 0.039 | 0.021 | 0.028 | 0.041 | 0.018 | 0.029 | 0.049 | 0.007 | 0.016 | 0.026 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13.0 | 14.5 | 16.0 | ---- | ---- | ---- | 7.4 | 9.2 | 11.0 | 4.6 | 9.4 | 14.0 | 9.0 | 10.0 | 12.0 | 10.7 | 12.8 | 15.9 |
| Pool Spacing (ft) | ---- | 42.0 | ---- | 156.5 | 42.0 | 136.5 | 231.0 | 9.0 | 29.5 | 50.0 | 30.6 | 39.4 | 47.9 | 33.5 | 39.4 | 45.0 | 39.0 | 43.0 | 48.0 | 31.8 | 40.7 | 47.2 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | 1.2/6.6/13/65/130 | | | 1-6/14/31-39/51-88/110-210 | | | .6-1.5/2-7/6.2-19/19-65/26-130 | | | --- | | | --- | | | --- | | | --- | | |
| Reach Shear Stress (competency) lb/f2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.3 | ---- | ---- | 1.4 | ---- | ---- | 1.4 | ---- | ---- | 1.4 | ---- |
| Stream Power (transport capacity) W/m2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.6 | ---- | ---- | 1.7 | ---- | ---- | 1.4 | ---- | ---- | 1.6 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 279 | ---- | ---- | 279 | ---- | ---- | 279 | ---- | ---- | 279 | ---- | ---- | 279 | ---- |
| Drainage Area (SM) | ---- | 0.07 | ---- | 0.14 | 0.45 | 1.03 | 1.60 | 0.07 | 0.11 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 | 0.05 | 0.10 | 0.14 |
| Rosgen Classification | ---- | ---- | Cb/B/G /Eb4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 13-23 | ---- | ---- | ---- | ---- | ---- | ---- | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 | 7 | 11 | 14 |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- | ---- | 1.09 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.024 | ---- | ---- | 0.023 | ---- | ---- | 0.023 | ---- | ---- | 0.026 | ---- |

Note: Dimension information based on pool cross-section

Table 13. Stream Reach Morphology and Hydraulic Data Elk Branch Reach 2

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary UT1 to Elk Branch | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|-------|-------|--------------------------|-------|-------|--------|-------|-------|----------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | As-Built | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| | | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean |
| Dimension - Riffle | | | | | | | | | | | | | | | | | | | | | | |
| Bankfull Width (ft) | 6.90 | 3.5 | 7.7 | 11.9 | 11.7 | 19.7 | 27.6 | 3.0 | 6.9 | 8.4 | 6.5 | 6.9 | 7.3 | 6.5 | 7.2 | 7.8 | 7.0 | 7.7 | 8.3 | 6.4 | 9.0 | 12.6 |
| Floodprone Width (ft) | ---- | 6.8 | 29.4 | 52.0 | 20.0 | 30.5 | 41.0 | 9.0 | 17.0 | 25.0 | 34.8 | 36.3 | 37.9 | 33.0 | 35.0 | 36.9 | 36.9 | 38.9 | 40.9 | 30.5 | 35.9 | 44.4 |
| Bankfull Mean Depth (ft) | 0.47 | 0.34 | 0.53 | 0.72 | 0.60 | 0.85 | 1.10 | 0.30 | 0.45 | 0.60 | 0.46 | 0.53 | 0.59 | 0.34 | 0.38 | 0.42 | 0.37 | 0.4 | 0.52 | 0.3 | 0.4 | 0.5 |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.40 | 0.70 | 1.00 | 0.68 | 0.74 | 0.80 | 0.58 | 0.59 | 0.59 | 0.79 | 0.9 | 1.04 | 0.8 | 0.9 | 0.9 |
| Bankfull Cross Sectional Area (ft ²) | 4.10 | 5.5 | 7.7 | 9.9 | 10.2 | 21.6 | 33.0 | 3.0 | 4.5 | 6.0 | 3.1 | 3.5 | 3.8 | 2.4* | 2.6* | 2.9 | 2.7 | 3.3* | 3.7 | 2.7 | 3.6 | 5.1 |
| Width/Depth Ratio | ---- | 2.1 | 5.1 | 8.1 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | 11.0 | 12.8 | 14.5 | 16.7 | 20.0 | 23.2 | 13.6 | 16.7 | 19.7 | 13.0 | 22.4 | 31.3 |
| Entrenchment Ratio | ---- | 1.9 | 4.8 | 7.7 | 1.3 | 2.3 | 3.2 | ---- | 3.0 | ---- | 4.8 | 5.3 | 5.8 | 4.2 | 5.0 | 5.7 | 4.6 | 5.2 | 5.8 | 3.5 | 4.1 | 4.8 |
| Bank Height Ratio | ---- | 1.0 | 1.5 | 1.9 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 | 1.0 |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | 2.6 | 2.9 | 3.2 | 3.4 | 3.8 | 4.2* | 3.7 | 2.8* | 2.7 | 2.0 | 3.0 | 3.7 |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | ---- | ---- | ---- | 16 | 36 | 55 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | ---- | ---- | ---- | 28 | 38 | 47 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | ---- | ---- | ---- | 70 | 165 | 260 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | ---- | ---- | ---- | 1.10 | 2.60 | 4.10 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 11 | 17 | 24 | 11 | 15 | 22 | 11 | 15 | 19 | 10 | 15 | 23 |
| Riffle Slope (ft/ft) | ---- | 0.022 | 0.030 | 0.038 | 0.200 | 0.138 | 0.076 | 0.023 | 0.042 | 0.061 | 0.018 | 0.066 | 0.104 | 0.037 | 0.061 | 0.080 | 0.022 | 0.042 | 0.063 | 0.015 | 0.038 | 0.126 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13 | 15 | 16 | ---- | ---- | ---- | 2 | 4 | 6 | 2 | 5 | 8 | 7 | 9 | 11 | 6 | 10 | 15 |
| Pool Spacing (ft) | ---- | ---- | ---- | ---- | 42 | 137 | 231 | 9 | 13 | 17 | 20 | 23 | 26 | 18 | 21 | 24 | 19 | 23 | 24 | 8 | 22 | 31 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | ---- | ---- | ---- | -6/14/31-39/51-88/110-21 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Reach Shear Stress (competency) lb/f ² | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.53 | ---- | ---- | 0.53 | ---- | ---- | 0.53 | ---- | ---- | 0.53 | ---- |
| Stream Power (transport capacity) W/m ² | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.54 | ---- | ---- | 2.00 | ---- | ---- | 1.48 | ---- | ---- | 1.58 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | 685 | ---- | ---- | ---- | ---- | ---- | 654 | ---- | ---- | 656 | ---- | ---- | 656 | ---- | ---- | 656 | ---- | ---- | 656 | ---- |
| Drainage Area (SM) | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- | ---- | 0.06 | ---- |
| Rosgen Classification | ---- | ---- | B4/G | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 10-12 | ---- | ---- | ---- | ---- | ---- | ---- | 3 | 7 | 10 | ---- | 10 | ---- | ---- | 10 | ---- | ---- | 10 | ---- | ---- | 10 | ---- |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.046 | ---- | ---- | 0.046 | ---- | ---- | 0.048 | ---- | ---- | 0.046 | ---- |

*These datum have been corrected and should be used rather than data shown in previous monitoring reports.

Table 13. Stream Reach Morphology and Hydraulic Data UT1 to Elk Branch

**Table 13. Stream Reach Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Stream Reach Data Summary UT2 to Elk Branch | | | | | | | | | | | | | | | | | | | | | | |
|--|-------------------------|------------------------|------|------|--------------------------|-------|-------|--------|-------|-------|----------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|-------------------|-------|-------|
| Parameter | Regional Curve Equation | Pre-Existing Condition | | | Reference Reach(es) Data | | | Design | | | As-Built | | | Monitoring Year 1 | | | Monitoring Year 2 | | | Monitoring Year 3 | | |
| Dimension - Riffle | Eq. | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max | Min | Mean | Max |
| Bankfull Width (ft) | 3.70 | 3.5 | 7.7 | 11.9 | 11.7 | 19.7 | 27.6 | 3.0 | 5.7 | 8.4 | ---- | 5.4 | ---- | ---- | 5.8 | ---- | ---- | 5.2 | ---- | ---- | 5.8 | ---- |
| Floodprone Width (ft) | ---- | 6.8 | 29.4 | 52.0 | 20.0 | 30.5 | 41.0 | 9.0 | 17.0 | 25.0 | ---- | 38.9 | ---- | ---- | 36.9 | ---- | ---- | 39.5 | ---- | ---- | 38.9 | ---- |
| Bankfull Mean Depth (ft) | 0.28 | 0.34 | 0.53 | 0.72 | 0.60 | 0.85 | 1.10 | 0.30 | 0.45 | 0.60 | ---- | 0.52 | ---- | ---- | 0.44 | ---- | ---- | 0.55 | ---- | ---- | 0.49 | ---- |
| Bankfull Max Depth (ft) | ---- | 0.90 | 1.30 | 1.70 | 0.90 | 1.70 | 2.50 | 0.40 | 0.70 | 1.00 | ---- | 0.86 | ---- | ---- | 0.76 | ---- | ---- | 0.84 | ---- | ---- | 0.88 | ---- |
| Bankfull Cross Sectional Area (ft2) | 1.50 | 5.5 | 7.7 | 9.9 | 10.2 | 21.6 | 33.0 | 3.0 | 4.5 | 6.0 | ---- | 2.8 | ---- | ---- | 2.6 | ---- | ---- | 2.9 | ---- | ---- | 2.8 | ---- |
| Width/Depth Ratio | ---- | 2.1 | 5.1 | 8.1 | 10.7 | 18.9 | 27.0 | 10.0 | 12.0 | 14.0 | ---- | 10.3 | ---- | ---- | 13.3 | ---- | ---- | 9.5 | ---- | ---- | 11.9 | ---- |
| Entrenchment Ratio | ---- | 1.9 | 4.8 | 7.7 | 1.3 | 2.3 | 3.2 | ---- | 3.0 | ---- | ---- | 7.2 | ---- | ---- | 6.3 | ---- | ---- | 7.6 | ---- | ---- | 6.7 | ---- |
| Bank Height Ratio | ---- | 1.0 | 1.5 | 1.9 | 1.0 | 1.0 | 1.0 | 1.0 | 1.1 | 1.1 | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- | ---- | 1.0 | ---- |
| Bankfull Velocity (fps) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.0 | 4.0 | 6.0 | ---- | 2.1 | ---- | ---- | 2.3 | ---- | ---- | 2.1 | ---- | ---- | 2.1 | ---- |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | ---- | ---- | ---- | ---- | 16 | 36 | 55 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Radius of Curvature (ft) | ---- | ---- | ---- | ---- | 28 | 38 | 47 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Wavelength (ft) | ---- | ---- | ---- | ---- | 70 | 165 | 260 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Meander Width Ratio | ---- | ---- | ---- | ---- | 1.1 | 2.6 | 4.1 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| Riffle Length (ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 9.0 | 12.0 | 13.8 | 9.0 | 13.1 | 14.9 | 10.0 | 13.0 | 15.0 | 5.9 | 10.5 | 13.6 |
| Riffle Slope (ft/ft) | ---- | ---- | ---- | ---- | 0.190 | 0.475 | 0.760 | 0.023 | 0.042 | 0.061 | 0.026 | 0.050 | 0.080 | 0.038 | 0.048 | 0.056 | 0.042 | 0.054 | 0.065 | 0.016 | 0.048 | 0.091 |
| Pool Length (ft) | ---- | ---- | ---- | ---- | 13.0 | 14.5 | 16.0 | ---- | ---- | ---- | 3.0 | 6.6 | 11.4 | 4.1 | 6.8 | 9.4 | 8.0 | 10.0 | 12.0 | 8.6 | 11.1 | 15.1 |
| Pool Spacing (ft) | ---- | ---- | ---- | ---- | 42.0 | 136.5 | 231.0 | 9.0 | 25.5 | 42.0 | 15.2 | 22.2 | 27.3 | 17.8 | 21.0 | 23.5 | 19.0 | 21.0 | 23.0 | 14.5 | 21.3 | 28.0 |
| Substrate and Transport Parameters | | | | | | | | | | | | | | | | | | | | | | |
| d16 / d35 / d50 / d84 / d95 | ---- | ---- | ---- | ---- | 1-6/14/31-39/51-88/110 | | | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- |
| Reach Shear Stress (competency) lb/f2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 1.1 | ---- | ---- | 0.9 | ---- | ---- | 0.9 | ---- | ---- | 0.9 | ---- |
| Stream Power (transport capacity) W/m2 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 2.3 | ---- | ---- | 2.1 | ---- | ---- | 1.9 | ---- | ---- | 2.0 | ---- |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| Channel length (ft) | ---- | ---- | 185 | ---- | ---- | ---- | ---- | ---- | 244 | ---- | ---- | 241 | ---- | ---- | 241 | ---- | ---- | 241 | ---- | ---- | 241 | ---- |
| Drainage Area (SM) | ---- | ---- | 0.01 | ---- | 0.45 | 1.025 | 1.60 | ---- | 0.01 | ---- | ---- | 0.01 | ---- | ---- | 0.01 | ---- | ---- | 0.01 | ---- | ---- | 0.01 | ---- |
| Rosgen Classification | ---- | ---- | B4/G | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- | ---- | B4 | ---- |
| Bankfull Discharge (cfs) | 2-3 | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 6 | ---- | ---- | 6 | ---- | ---- | 6 | ---- | ---- | 6 | ---- | ---- | 6 | ---- |
| Sinuosity | ---- | 1.02 | 1.06 | 1.10 | 1.10 | 1.15 | 1.19 | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- |
| BF slope (ft/ft) | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | ---- | 0.039 | ---- | ---- | 0.039 | ---- | ---- | 0.040 | ---- | ---- | 0.041 | ---- |

Table 13. Stream Reach Morphology and Hydraulic Data
UT2 to Elk Branch

**Table 14. Cross-Section Morphology and Hydraulic Data
Elk Branch Mitigation Project #92665**

| Parameter | Elk Branch - Reach 1 | | | | | | Elk Branch - Reach A | | | | | | | | | | | |
|--|-----------------------------|-------|-------|-------------|-------|-------|-------------------------|-------|-------|-------------|-------|-------|---------------------------|-------|------|-------------|-----|-----|
| | Cross Section 1 Riffle | | | | | | Cross Section 2 Pool | | | | | | Cross Section 3 Riffle | | | | | |
| | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 |
| Dimension | | | | | | | | | | | | | | | | | | |
| BF Width (ft) | 6.1 | 5.5 | 5.2 | 6.4 | | | 6.0 | 5.7 | 5.1 | 6.7 | | | 8.1 | 7.3 | 8.2 | 7.9 | | |
| Floodprone Width (ft) | 30.9 | 24.3 | 26.4 | 30.5 | | | 32.5 | 32.5 | 32.5 | 32.5 | | | 34.6 | 32.5 | 35.6 | 32.7 | | |
| BF Cross Sectional Area (ft ²) | 4.1 | 2.6 | 2.7 | 3.1 | | | 7.3 | 6.3 | 4.8 | 6.4 | | | 4.2 | 2.9 | 3.4 | 2.7 | | |
| BF Mean Depth (ft) | 0.7 | 0.5 | 0.5 | 0.5 | | | 1.2 | 1.1 | 0.9 | 1.0 | | | 0.5 | 0.4 | 0.4 | 0.3 | | |
| BF Max Depth (ft) | 1.0 | 0.7 | 0.9 | 0.9 | | | 2.2 | 1.8 | 1.5 | 1.9 | | | 0.8 | 0.8 | 1.0 | 0.8 | | |
| Width/Depth Ratio | 9.0 | 12.0 | 10.1 | 13.0 | | | 4.9 | 5.1 | 5.5 | 6.9 | | | 15.8 | 18.4 | 19.6 | 22.8 | | |
| Entrenchment Ratio | 5.1 | 4.4 | 5.1 | 4.8 | | | 5.4 | 5.7 | 6.4 | 4.9 | | | 4.3 | 4.4 | 4.3 | 3.9 | | |
| Wetted Perimeter (ft) | 7.4 | 6.5 | 6.2 | 7.4 | | | 8.5 | 7.9 | 7.0 | 8.6 | | | 9.1 | 8.1 | 9.1 | 8.6 | | |
| Hydraulic Radius (ft) | 0.6 | 0.4 | 0.4 | 0.4 | | | 0.9 | 0.8 | 0.7 | 0.7 | | | 0.5 | 0.4 | 0.4 | 0.3 | | |
| Substrate | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | | | | | | | | | | | | | | | | | |
| d84 (mm) | | | | | | | | | | | | | | | | | | |
| | Elk Branch - Reach B | | | | | | | | | | | | | | | | | |
| | Cross Section 4 Riffle | | | | | | | | | | | | | | | | | |
| | AB | MY1 | MY2 | MY3 | MY4 | MY5 | | | | | | | | | | | | |
| Dimension | | | | | | | | | | | | | | | | | | |
| BF Width (ft) | 8.7 | 8.3 | 9.4 | 12.6 | | | | | | | | | | | | | | |
| Floodprone Width (ft) | 45.0 | 46.5 | 45.2 | 44.4 | | | | | | | | | | | | | | |
| BF Cross Sectional Area (ft ²) | 5.7 | 4.4 | 4.9 | 5.1 | | | | | | | | | | | | | | |
| BF Mean Depth (ft) | 0.7 | 0.5 | 0.5 | 0.4 | | | | | | | | | | | | | | |
| BF Max Depth (ft) | 1.0 | 0.8 | 1.0 | 0.9 | | | | | | | | | | | | | | |
| Width/Depth Ratio | 13.3 | 15.6 | 18.0 | 31.3 | | | | | | | | | | | | | | |
| Entrenchment Ratio | 5.2 | 5.6 | 4.8 | 3.5 | | | | | | | | | | | | | | |
| Wetted Perimeter (ft) | 10.0 | 9.3 | 10.5 | 13.4 | | | | | | | | | | | | | | |
| Hydraulic Radius (ft) | 0.6 | 0.5 | 0.5 | 0.4 | | | | | | | | | | | | | | |
| | AB (2011) | | | MY-1 (2012) | | | MY-2 (2013) | | | MY-3 (2014) | | | MY-4 (2015) | | | MY-5 (2016) | | |
| | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med |
| Pattern | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | | | | | | | | | | | | | | | | | | |
| Radius of Curvature (ft) | | | | | | | | | | | | | | | | | | |
| Meander Wavelength (ft) | | | | | | | | | | | | | | | | | | |
| Meander Width Ratio | | | | | | | | | | | | | | | | | | |
| Profile | | | | | | | | | | | | | | | | | | |
| Riffle length (ft) | 5.5 | 63.7 | 35.7 | 12.5 | 63.8 | 28.6 | 11.0 | 63.6 | 33.8 | 12.8 | 107.2 | 32.9 | | | | | | |
| Riffle Slope (ft/ft) | 0.010 | 0.045 | 0.025 | 0.005 | 0.041 | 0.027 | 0.008 | 0.039 | 0.021 | 0.011 | 0.039 | 0.023 | | | | | | |
| Pool Length (ft) | 2.5 | 13.6 | 7.1 | 2.3 | 13.2 | 8.7 | 8.1 | 13.8 | 11.8 | 7.5 | 33.8 | 12.1 | | | | | | |
| Pool Spacing (ft) | 10.4 | 56.7 | 44.4 | 14.7 | 54.9 | 44.7 | 16.6 | 56.2 | 43.9 | 26.5 | 127.0 | 47.3 | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | 17 | | | | | | 27 | | | 30 | | | 37 | | | | |
| d84 (mm) | | 38 | | | | | | 69 | | | 72 | | | 82 | | | | |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | |
| Valley Length (ft) | | 2121 | | | | | | 2121 | | | 2121 | | | 2121 | | | | |
| Channel Length (ft) | | 1946 | | | | | | 1946 | | | 1946 | | | 1946 | | | | |
| Sinuosity | | 1.09 | | | | | | 1.09 | | | 1.09 | | | 1.09 | | | | |
| Water Surface Slope (ft/ft) | | 0.027 | | | | | | 0.027 | | | 0.029 | | | 0.029 | | | | |
| BF Slope (ft/ft) | 0.021 | 0.033 | 0.027 | 0.023 | 0.032 | 0.028 | 0.021 | 0.029 | 0.025 | 0.020 | 0.027 | 0.027 | | | | | | |
| Rosgen Classification | | B4 | | | | | | B4 | | | B4 | | | B4 | | | | |

Table 14. Cross-Section Morphology and Hydraulic Data, Elk Branch Reach 1, A, & B.

**Table 14. Cross-Section Morphology and Hydraulic Data
Elk Branch Mitigation Project #D06125-B**

| | | Elk Branch - Reach 2 | | | | | | | | | | | | | | | | | | | | |
|------------------------------------|--|-------------------------|--------|-------|-------------|--------|-------|-------------|--------|-------|-------------|--------|-------|-------------|-----|-----|-------------|-----|-----|--|--|--|
| Parameter | | Cross Section 5 Pool | | | | | | | | | | | | | | | | | | | | |
| | | AB | MY1 | MY2 | MY3 | MY4 | MY5 | | | | | | | | | | | | | | | |
| Dimension | | | | | | | | | | | | | | | | | | | | | | |
| | BF Width (ft) | 9.2 | 9.0 | 10.3 | 12.9 | | | | | | | | | | | | | | | | | |
| | Floodprone Width (ft) | 43.8 | 44.2 | 44.1 | >44.0 | | | | | | | | | | | | | | | | | |
| | BF Cross Sectional Area (ft ²) | 9.0 | 8.7 | 10.4 | 9.4 | | | | | | | | | | | | | | | | | |
| | BF Mean Depth (ft) | 1.0 | 1.0 | 1.0 | 0.7 | | | | | | | | | | | | | | | | | |
| | BF Max Depth (ft) | 2.0 | 2.1 | 2.5 | 2.2 | | | | | | | | | | | | | | | | | |
| | Width/Depth Ratio | 9.3 | 9.4 | 10.2 | 17.7 | | | | | | | | | | | | | | | | | |
| | Entrenchment Ratio | 4.8 | 4.9 | 4.3 | 3.4 | | | | | | | | | | | | | | | | | |
| | Wetted Perimeter (ft) | 11.1 | 11.0 | 12.3 | 14.4 | | | | | | | | | | | | | | | | | |
| | Hydraulic Radius (ft) | 0.8 | 0.8 | 0.8 | 0.7 | | | | | | | | | | | | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | | | | | |
| | d50 (mm) | | | | | | | | | | | | | | | | | | | | | |
| | d84 (mm) | | | | | | | | | | | | | | | | | | | | | |
| Parameter | | AB (2011) | | | MY-1 (2012) | | | MY-2 (2013) | | | MY-3 (2014) | | | MY-4 (2015) | | | MY-5 (2016) | | | | | |
| | | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | | | |
| Pattern | | | | | | | | | | | | | | | | | | | | | | |
| | Channel Beltwidth (ft) | | | | | | | | | | | | | | | | | | | | | |
| | Radius of Curvature (ft) | | | | | | | | | | | | | | | | | | | | | |
| | Meander Wavelength (ft) | | | | | | | | | | | | | | | | | | | | | |
| | Meander Width Ratio | | | | | | | | | | | | | | | | | | | | | |
| Profile | | | | | | | | | | | | | | | | | | | | | | |
| | Riffle length (ft) | 19.4 | 39.6 | 31.2 | 18.9 | 39.9 | 29.9 | 16.5 | 38.0 | 27.0 | 18.8 | 38.2 | 25.8 | | | | | | | | | |
| | Riffle Slope (ft/ft) | 0.021 | 0.039 | 0.026 | 0.021 | 0.041 | 0.025 | 0.018 | 0.049 | 0.024 | 0.007 | 0.026 | 0.015 | | | | | | | | | |
| | Pool Length (ft) | 7 | 11 | 9 | 5 | 14 | 10 | 9 | 12 | 11 | 11 | 16 | 13 | | | | | | | | | |
| | Pool Spacing (ft) | 31 | 48 | 40 | 33 | 45 | 40 | 39 | 48 | 42 | 32 | 47 | 42 | | | | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | | | | | |
| | d50 (mm) | | --- | | | --- | | | --- | | | --- | | | | | | | | | | |
| | d84 (mm) | | --- | | | --- | | | --- | | | --- | | | | | | | | | | |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | |
| | Valley Length (ft) | | 304 | | | 304 | | | 304 | | | 304 | | | | | | | | | | |
| | Channel Length (ft) | | 279 | | | 279 | | | 279 | | | 279 | | | | | | | | | | |
| | Sinuosity | | 1.09 | | | 1.09 | | | 1.09 | | | 1.09 | | | | | | | | | | |
| | Water Surface Slope (ft/ft) | | 0.027 | | | 0.027 | | | 0.028 | | | 0.029 | | | | | | | | | | |
| | BF Slope (ft/ft) | 0.017 | 0.024 | 0.021 | | 0.023 | | | 0.023 | | | 0.027 | | | | | | | | | | |
| | Rosgen Classification | | B4/Eb4 | | | B4/Eb4 | | | B4/Eb4 | | | B4/Eb4 | | | | | | | | | | |

Table 14. Cross-Section Morphology and Hydraulic Data, Elk Branch Reach 2

| Table 14. Cross-Section Morphology and Hydraulic Data Elk Branch Mitigation Project #D06125-B | | | | | | | | | | | | | | | | | | | | | | | | | |
|--|---------------------------|-------|-------|-------------|-------|-------|---------------------------|-------|-------|-------------|-------|-------|---------------------------|-------|------|-------------|------|-----|-------------------------|-------|------|------|-----|-----|--|
| UT1 | | | | | | | | | | | | | | | | | | | | | | | | | |
| Parameter | Cross Section 1 Riffle | | | | | | Cross Section 2 Riffle | | | | | | Cross Section 3 Riffle | | | | | | Cross Section 4 Pool | | | | | | |
| | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 | |
| Dimension | | | | | | | | | | | | | | | | | | | | | | | | | |
| BF Width (ft) | 6.7 | 6.5 | 7.3 | 6.7 | | | 6.5 | 6.96 | 7.0 | 8.0 | | | 7.3 | 7.79 | 8.3 | 9.8 | | | 9.4 | 10.3 | 9.9 | 9.5 | | | |
| Floodprone Width (ft) | 35.7 | 36.89 | 36.9 | 34.1 | | | 37.6 | 34.75 | 40.9 | 45.0 | | | 34.8 | 33.03 | 37.8 | 39.6 | | | 45.2 | 45.88 | 45.9 | 46.9 | | | |
| BF Cross Sectional Area (ft ²) | 3.1 | 2.45 | 2.7 | 2.1 | | | 3.8 | 2.91 | 3.6 | 4.7 | | | 3.6 | 2.61 | 3.7 | 5.0 | | | 11.9 | 12.36 | 11.7 | 10.7 | | | |
| BF Mean Depth (ft) | 0.46 | 0.38 | 0.37 | 0.32 | | | 0.59 | 0.42 | 0.52 | 0.59 | | | 0.5 | 0.34 | 0.45 | 0.50 | | | 1.3 | 1.2 | 1.2 | 1.12 | | | |
| BF Max Depth (ft) | 0.68 | 0.58 | 0.79 | 0.67 | | | 0.8 | 0.59 | 0.93 | 1.18 | | | 0.71 | 0.91 | 1.04 | 1.33 | | | 2.2 | 2.2 | 2.3 | 2.51 | | | |
| Width/Depth Ratio | 14.7 | 17.3 | 19.7 | 21.1 | | | 11.0 | 16.67 | 13.6 | 13.4 | | | 14.5 | 23.2 | 18.3 | 19.5 | | | 7.5 | 8.58 | 8.3 | 8.5 | | | |
| Entrenchment Ratio | 5.3 | 5.7 | 5.1 | 5.1 | | | 5.8 | 5.0 | 5.8 | 5.6 | | | 4.8 | 4.2 | 4.6 | 4.0 | | | 4.8 | 4.45 | 4.7 | 4.9 | | | |
| Wetted Perimeter (ft) | 7.7 | 7.3 | 8.0 | 7.3 | | | 7.7 | 7.8 | 8.1 | 9.1 | | | 8.3 | 8.5 | 9.2 | 10.8 | | | 11.9 | 12.7 | 12.2 | 11.8 | | | |
| Hydraulic Radius (ft) | 0.41 | 0.34 | 0.34 | 0.29 | | | 0.50 | 0.37 | 0.45 | 0.51 | | | 0.44 | 0.31 | 0.40 | 0.46 | | | 1.00 | 0.97 | 0.96 | 0.91 | | | |
| Substrate | | | | | | | | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | | | | | | | | | | | | | | | | | | | | | | | | |
| d84 (mm) | | | | | | | | | | | | | | | | | | | | | | | | | |
| Parameter | AB (2011) | | | MY-1 (2012) | | | MY-2 (2013) | | | MY-3 (2014) | | | MY-4 (2015) | | | MY-5 (2016) | | | | | | | | | |
| | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | | | | | | | |
| Pattern | | | | | | | | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | | | | | | | | | | | | | | | | | | | | | | | | | |
| Radius of Curvature (ft) | | | | | | | | | | | | | | | | | | | | | | | | | |
| Meander Wavelength (ft) | | | | | | | | | | | | | | | | | | | | | | | | | |
| Meander Width Ratio | | | | | | | | | | | | | | | | | | | | | | | | | |
| Profile | | | | | | | | | | | | | | | | | | | | | | | | | |
| Riffle length (ft) | 11 | 24 | 15 | 11 | 22 | 14 | 11 | 19 | 16 | 9.7 | 22.8 | 14.3 | | | | | | | | | | | | | |
| Riffle Slope (ft/ft) | 0.018 | 0.104 | 0.080 | 0.037 | 0.080 | 0.063 | 0.022 | 0.064 | 0.044 | 0.015 | 0.126 | 0.031 | | | | | | | | | | | | | |
| Pool Length (ft) | 2.4 | 6.4 | 3.8 | 2.2 | 7.7 | 4.6 | 6.7 | 10.9 | 9.6 | 6.0 | 15.40 | 9.50 | | | | | | | | | | | | | |
| Pool Spacing (ft) | 30.6 | 25.6 | 23.2 | 17.7 | 23.6 | 22.1 | 19.1 | 24.3 | 23.3 | 8.0 | 31.0 | 22.4 | | | | | | | | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | | | | | | |
| d84 (mm) | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | | | | | | |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | | | | | | | | |
| Valley Length (ft) | | 662 | | | 662 | | | 662 | | | 662 | | | 662 | | | | | | | | | | | |
| Channel Length (ft) | | 683 | | | 683 | | | 683 | | | 683 | | | 683 | | | | | | | | | | | |
| Sinuosity | | 1.04 | | | 1.04 | | | 1.04 | | | 1.04 | | | 1.04 | | | | | | | | | | | |
| Water Surface Slope (ft/ft) | | 0.049 | | | 0.046 | | | 0.046 | | | 0.047 | | | | | | | | | | | | | | |
| BF Slope (ft/ft) | | 0.046 | | | 0.046 | | | 0.048 | | | 0.046 | | | | | | | | | | | | | | |
| Rosgen Classification | | B | | | B | | | B | | | B | | | | | | | | | | | | | | |

Table 14. Cross-Section Morphology and Hydraulic Data, Elk Branch - UT1

**Table 14. Cross-Section Morphology and Hydraulic Data
Elk Branch Mitigation Project #D06125-B**

| UT2 | | | | | | | | | | | | | | | | | | |
|--|---------------------------|-------|-------|-------------|-------|-------|-------------------------|-------|-------|-------------|-------|-------|-------------|------|-----|-------------|------|-----|
| Parameter | Cross Section 1 Riffle | | | | | | Cross Section 2 Pool | | | | | | | | | | | |
| | AB | MY1 | MY2 | MY3 | MY4 | MY5 | AB | MY1 | MY2 | MY3 | MY4 | MY5 | | | | | | |
| Dimension | | | | | | | | | | | | | | | | | | |
| BF Width (ft) | 5.4 | 5.8 | 5.2 | 5.8 | | | 7.9 | 7.4 | 6.5 | 6.8 | | | | | | | | |
| Floodprone Width (ft) | 38.9 | 36.9 | 39.5 | 38.9 | | | 34.0 | 34.0 | 34.1 | 34.0 | | | | | | | | |
| BF Cross Sectional Area (ft ²) | 2.8 | 2.6 | 2.9 | 2.8 | | | 6.6 | 5.9 | 5.9 | 4.6 | | | | | | | | |
| BF Mean Depth (ft) | 0.52 | 0.44 | 0.55 | 0.49 | | | 0.83 | 0.80 | 0.91 | 0.67 | | | | | | | | |
| BF Max Depth (ft) | 0.86 | 0.76 | 0.84 | 0.88 | | | 1.49 | 1.40 | 1.50 | 1.23 | | | | | | | | |
| Width/Depth Ratio | 10.3 | 13.3 | 9.5 | 11.9 | | | 9.5 | 9.3 | 7.2 | 10.2 | | | | | | | | |
| Entrenchment Ratio | 7.2 | 6.3 | 7.6 | 6.7 | | | 4.3 | 4.6 | 5.2 | 5.0 | | | | | | | | |
| Wetted Perimeter (ft) | 6.4 | 6.7 | 6.3 | 6.8 | | | 9.6 | 9.0 | 8.3 | 8.2 | | | | | | | | |
| Hydraulic Radius (ft) | 0.4 | 0.4 | 0.5 | 0.4 | | | 0.7 | 0.7 | 0.7 | 0.6 | | | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | | | | | | | | | | | | | | | | | |
| d84 (mm) | | | | | | | | | | | | | | | | | | |
| Parameter | AB (2011) | | | MY-1 (2012) | | | MY-2 (2013) | | | MY-3 (2014) | | | MY-4 (2015) | | | MY-5 (2016) | | |
| | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med | Min | Max | Med |
| Pattern | | | | | | | | | | | | | | | | | | |
| Channel Beltwidth (ft) | | | | | | | | | | | | | | | | | | |
| Radius of Curvature (ft) | | | | | | | | | | | | | | | | | | |
| Meander Wavelength (ft) | | | | | | | | | | | | | | | | | | |
| Meander Width Ratio | | | | | | | | | | | | | | | | | | |
| Profile | | | | | | | | | | | | | | | | | | |
| Riffle length (ft) | 9.0 | 13.8 | 12.6 | 9.0 | 14.9 | 13.4 | 10.0 | 14.9 | 14.2 | 5.9 | 13.6 | 10.9 | | | | | | |
| Riffle Slope (ft/ft) | 0.026 | 0.080 | 0.047 | 0.038 | 0.056 | 0.050 | 0.042 | 0.065 | 0.054 | 0.016 | 0.091 | 0.044 | | | | | | |
| Pool Length (ft) | 3 | 11 | 5 | 4 | 9 | 7 | 8 | 12 | 9 | 8.6 | 15.1 | 11.6 | | | | | | |
| Pool Spacing (ft) | 15 | 27 | 23 | 18 | 24 | 22 | 19 | 23 | 20 | 14.5 | 28.0 | 21.3 | | | | | | |
| Substrate | | | | | | | | | | | | | | | | | | |
| d50 (mm) | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | |
| d84 (mm) | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | | | ---- | |
| Additional Reach Parameters | | | | | | | | | | | | | | | | | | |
| Valley Length (ft) | | 320 | | | 320 | | | 320 | | | 320 | | | | | | | |
| Channel Length (ft) | | 241 | | | 241 | | | 241 | | | 241 | | | | | | | |
| Sinuosity | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | ---- | 1.04 | ---- | | | | | | |
| Water Surface Slope (ft/ft) | ---- | 0.038 | ---- | ---- | 0.038 | ---- | ---- | 0.039 | ---- | | 0.040 | | | | | | | |
| BF Slope (ft/ft) | 0.039 | 0.049 | 0.044 | | 0.039 | | | 0.040 | | | 0.041 | | | | | | | |
| Rosgen Classification | | B4 | | | B4 | | | B4 | | | B4 | | | | | | | |



Table 14. Cross-Section Morphology and Hydraulic Data, Elk Branch - UT2

Figure B1. Elk Branch Pebble Count
Elk Branch Mitigation Project, EEP# 92665

| | |
|------------------|------------------------------|
| SITE OR PROJECT: | Elk Branch |
| REACH/LOCATION: | Mainstem, Riffle below PPT16 |
| FEATURE: | Riffle |

| | | | 2014 | | |
|------------------------------|------------------|-------------|-------|---------|-------|
| MATERIAL | PARTICLE | SIZE (mm) | Total | Class % | % Cum |
| Silt / Clay | Silt / Clay | < .063 | | | 0% |
| Sand | Very Fine | .063 - .125 | | | 0% |
| | Fine | .125 - .25 | | | 0% |
| | Medium | .25 - .50 | | | 0% |
| | Coarse | .50 - 1.0 | | | 0% |
| | Very Coarse | 1.0 - 2.0 | | | 0% |
| Gravel | Very Fine | 2.0 - 2.8 | | | 0% |
| | Very Fine | 2.8 - 4.0 | | | 0% |
| | Fine | 4.0 - 5.6 | | | 0% |
| | Fine | 5.6 - 8.0 | 2 | 2% | 2% |
| | Medium | 8.0 - 11.0 | 5 | 5% | 7% |
| | Medium | 11.0 - 16.0 | 6 | 6% | 13% |
| | Coarse | 16 - 22.6 | 11 | 11% | 24% |
| | Coarse | 22.6 - 32 | 20 | 20% | 43% |
| | Very Coarse | 32 - 45 | 18 | 18% | 61% |
| | Very Coarse | 45 - 64 | 15 | 15% | 75% |
| Cobble | Small | 64 - 90 | 12 | 12% | 87% |
| | Small | 90 - 128 | 9 | 9% | 96% |
| | Large | 128 - 180 | 3 | 3% | 99% |
| | Large | 180 - 256 | 1 | 1% | 100% |
| Boulder | Small | 256 - 362 | | | 100% |
| | Small | 362 - 512 | | | 100% |
| | Medium | 512 - 1024 | | | 100% |
| | Large-Very Large | 1024 - 2048 | | | 100% |
| Bedrock | Bedrock | > 2048 | | | 100% |
| Total% of Whole Count | | | 102 | 100% | |

| Summary Data | |
|--------------------|---------|
| Channel Materials | |
| D ₁₆ = | 17.76 |
| D ₃₅ = | 27.70 |
| D ₅₀ = | 36.54 |
| D ₈₄ = | 81.90 |
| D ₉₅ = | 122.61 |
| D ₁₀₀ = | 180-256 |

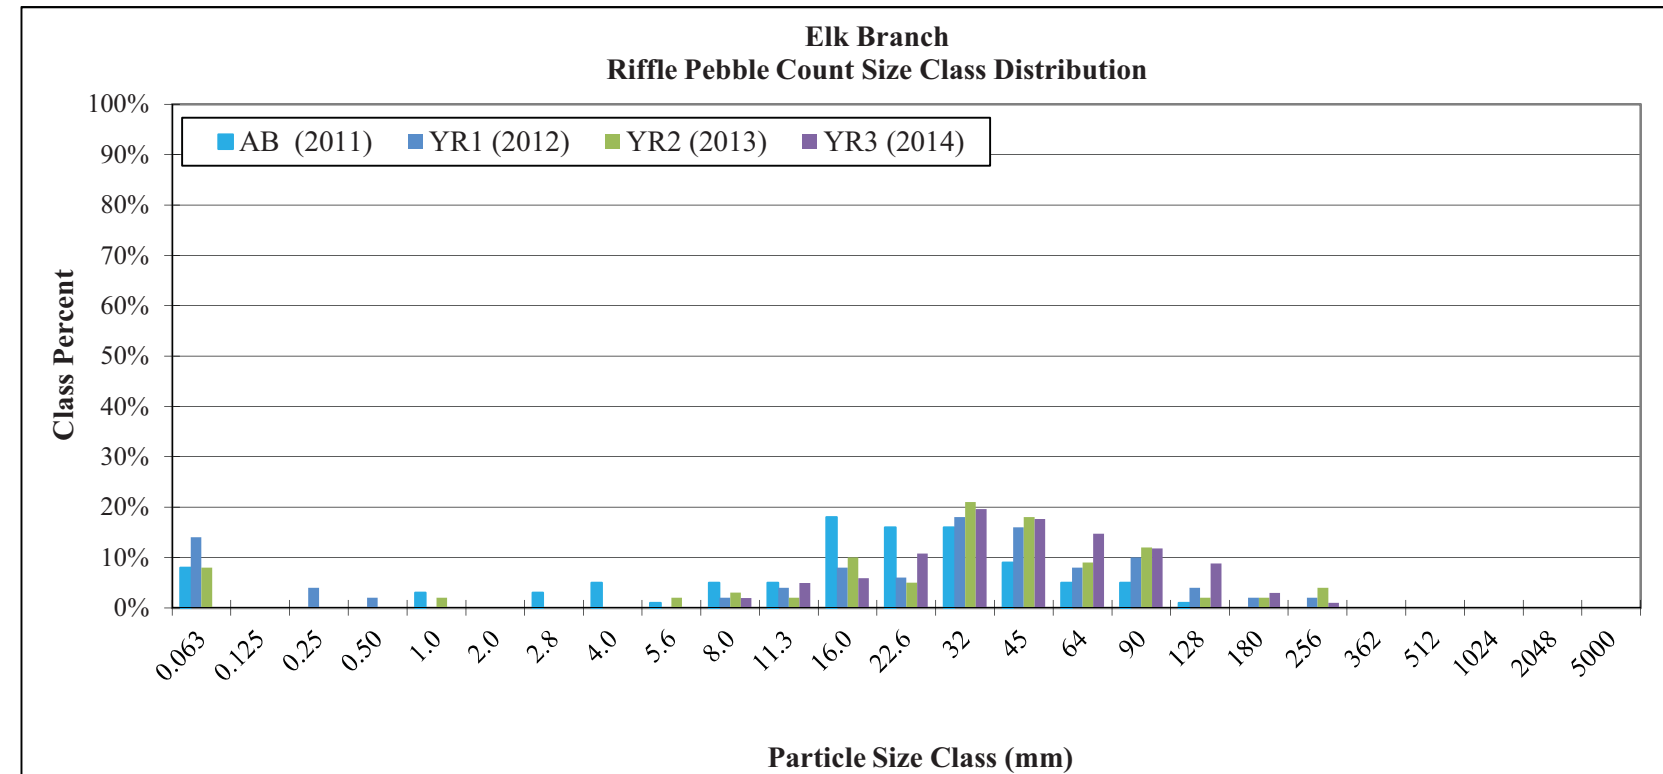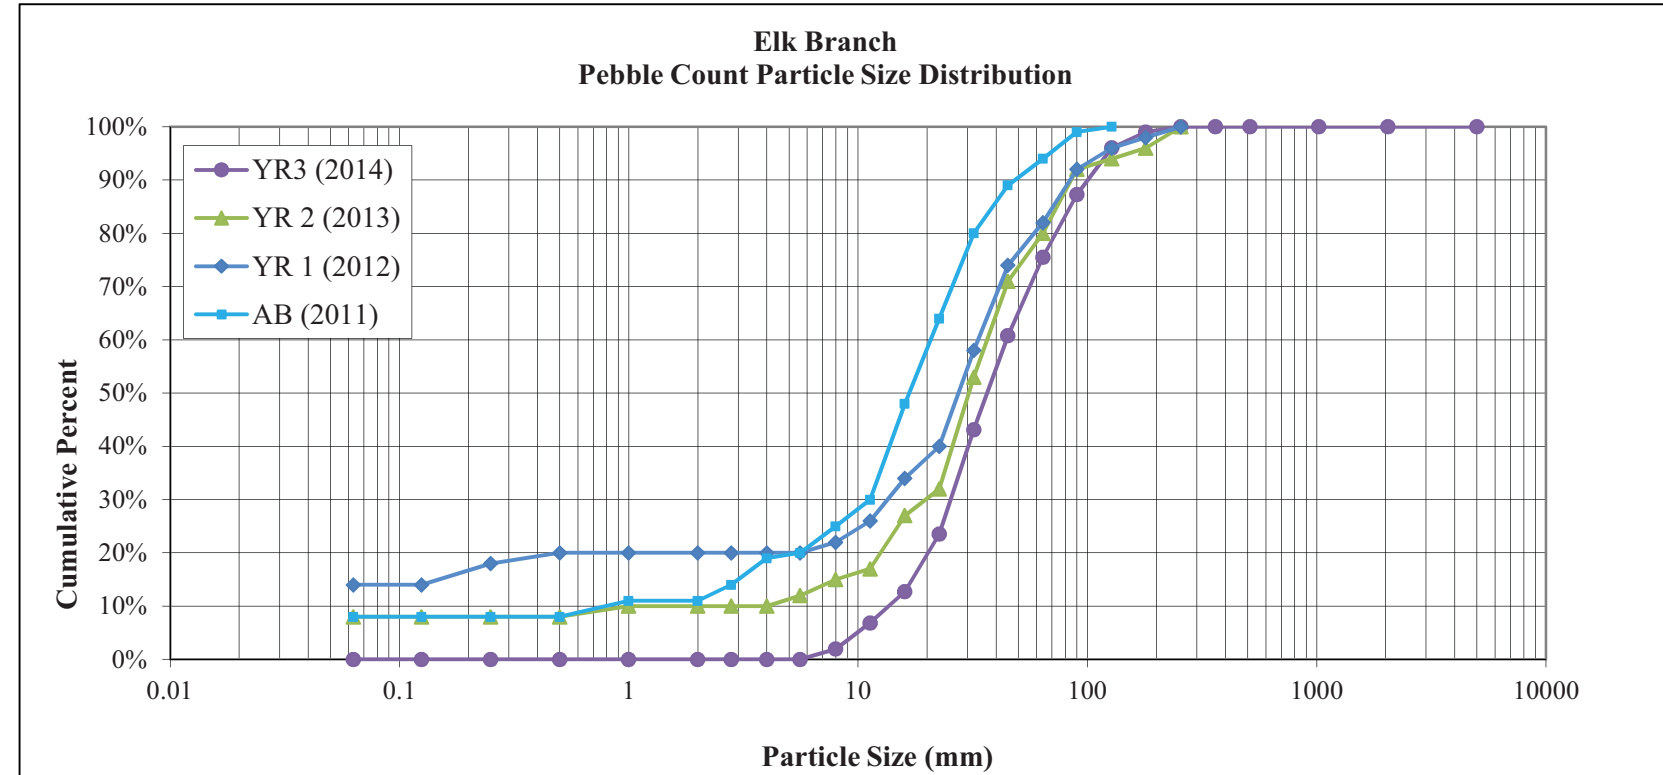

Riffle Pebble Count Size Class Distribution (Sink Hole Reach 1)

Elk Branch

Photo Log - Reference Photo Points

Notes: Photos for Elk Branch were taken November 22, 2014.

1. Photo point locations are shown on the plan views in the actual location the picture was taken.
2. All points are marked with a wooden stake and flagging tape. For channel points, the stake is set up on an adjacent bank.



Photo Point 1: looking upstream



Photo Point 1: looking downstream



Photo Point 2: looking upstream



Photo Point 2: looking downstream



Photo Point 3: looking upstream



Photo Point 3: looking downstream



Photo Point 4: looking upstream



Photo Point 4: looking downstream



Photo Point 5: looking upstream



Photo Point 5: looking downstream



Photo Point 6: looking upstream



Photo Point 6: looking downstream



Photo Point 7: looking upstream



Photo Point 7: looking downstream



Photo Point 8: looking upstream



Photo Point 8: looking downstream



Photo Point 9: looking upstream



Photo Point 9: looking downstream



Photo Point 10: looking upstream



Photo Point 10: looking downstream



Photo Point 11: looking upstream



Photo Point 11: looking downstream



Photo Point 12: looking upstream



Photo Point 12: looking downstream



Photo Point 13: looking upstream



Photo Point 13: looking downstream



Photo Point 14: looking upstream



Photo Point 14: looking downstream



Photo Point 15: looking upstream



Photo Point 15: looking downstream



Photo Point 16: looking upstream



Photo Point 16: looking downstream



Photo Point 17: looking upstream



Photo Point 17: looking downstream



Photo Point 18: looking upstream



Photo Point 18: looking downstream



Photo Point 19: looking upstream



Photo Point 19: looking downstream



Photo Point 20: looking upstream



Photo Point 20: looking downstream

UT1 to Elk Branch Photo Log - Reference Photo Points

Notes: Photos for UT1 to Elk Branch were taken November 22, 2014

1. Photo point locations are shown on the plan views in the actual location the picture was taken.
2. All points are marked with a wooden stake and flagging tape. For channel points, the stake is set up on an adjacent bank.



Photo Point 1: looking upstream, willow tree blown down in wind storm blocking normal photo point.



Photo Point 1: looking downstream, willow tree blown down in wind storm blocking normal photo point.



Photo Point 2: looking upstream



Photo Point 2: looking downstream



Photo Point 3: looking upstream



Photo Point 3: looking downstream



Photo Point 4: looking upstream



Photo Point 4: looking downstream



Photo Point 5: looking upstream

UT2 to Elk Branch Photo Log - Reference Photo Points

Notes: Photos for UT2 to Elk Branch were taken November 22, 2014.

1. Photo point locations are shown on the plan views in the actual location the picture was taken.
2. All points are marked with a wooden stake and flagging tape. For channel points, the stake is set up on an adjacent bank.



Photo Point 1: looking upstream



Photo Point 1: looking downstream



Photo Point 2: looking upstream



Photo Point 2: looking downstream



Photo Point 3: looking upstream



Photo Point 3: looking downstream



Photo Point 4: looking upstream



Photo Point 4: looking downstream



Photo Point 5: looking upstream
