



FINAL MONITORING REPORT (MY7) / CLOSEOUT REPORT

Final

HOPEWELL STREAM MITIGATION SITE

Randolph County, NC

DEQ Contract No. 004642

DMS Project No. 95352

USACE Action ID Number 2012-01111

NCDWR Project Number 13-0933

Data Collection Period: June – September 2021

Final Submission Date: January 6, 2022

PREPARED FOR:



NC Department of Environmental Quality

Division of Mitigation Services

1652 Mail Service Center

Raleigh, NC 27699-1652

PREPARED BY:



1430 South Mint Street, Suite 104
Charlotte, NC 28203

Phone: 704.332.7754
Fax: 704.332.3306



January 6, 2022

Mr. Harry Tsomides
Project Manager
Division of Mitigation Services
5 Ravenscroft Dr., Suite 102
Asheville, NC 28801

RE: Final Monitoring Report (MY7) / Closeout Report – Final Submittal
Hopewell Stream Mitigation Site
DMS Project No. 95352
DEQ Contract No. 004642

Dear Mr. Tsomides:

Wildlands Engineering, Inc. (Wildlands) has reviewed the Division of Mitigation Services' (DMS) comments from the Draft Monitoring Year (MY) 7 / Closeout Report for the Hopewell Stream Mitigation Site. The following Wildlands' responses to DMS' report comments are noted in italic lettering.

DMS' comment: For clarity, please provide an overall assets summary table as follows:

Overall Assets Summary	
Asset Category	Overall Credits
Stream (warm)	7,412.133
Wetland	NA

Wildlands' Response: An overall assets summary table has been added to Appendix 1 (Table 1B).

DMS' comment: In Appendix 7 please provide a map showing the sweetgum-treated area and include a table indicating quantities and species planted.

Wildlands' Response: A map depicting the sweetgum treatment area has been inserted into Appendix 7. A table with species, container size, and quantities for the supplemental plantings in the sweetgum treatment area and captured easement along UT1B R1 has been to Appendix 7. The table was inadvertently left out of the MY7 draft submittal.

DMS' comment: Please follow up and respond via email to the miscellaneous minor property close out issues sent via email on 11/8/2021, following that field visit.

Wildlands' Response: Wildlands responded to Harry Tsomides, DMS PM, via email on 1/5/2021 regarding the miscellaneous items including boundary marking and debris removal.



DMS' Digital File Comment: Please address the minor issues (scattered invasives, loose fencing etc.) identified with DMS during the 12/8/2021 site meeting and follow up with me prior to close out).

Wildlands' Response: Wildlands will address the minor issues in January 2022 and notify DMS when work is complete.

Two (2) hard copies of the Final Monitoring Report (MY7) / Closeout Report and a full electronic submittal has been mailed to the DMS Western Field Office. Please contact me at 704-332-7754 x110 if you have any questions.

Sincerely,

A handwritten signature in blue ink that reads 'Kristi Suggs'. The signature is fluid and cursive, with the first letters of 'Kristi' and 'Suggs' being capitalized and prominent.

Kristi Suggs
Senior Environmental Scientist
ksuggs@wildlandseng.com

EXECUTIVE SUMMARY

Wildlands Engineering, Inc. (Wildlands) completed a full delivery project at the Hopewell Mitigation Site (Site) for the North Carolina Division of Mitigation Services (DMS) to restore, enhance, and preserve a total of 12,308 linear feet (LF) of perennial and intermittent streams in Randolph County, NC. The Site is expected to generate 7,412.133 stream mitigation units (SMUs) by closeout. The Site is located near the town of Asheboro in the Yadkin-Pee Dee River Basin. The eight-digit Cataloging Unit (CU) is 03040104 and the 14-digit Hydrologic Unit Code (HUC) is 03040104030010 (Figure 1). The project streams consist of the Little River and five unnamed tributaries (UTs) to the Little River (Figure 2). The Little River eventually flows into the Pee Dee River near the town of Ingram in Richmond County, while the five unnamed streams are small headwater tributaries to the Little River. The project watershed consists primarily of pastureland and forest.

The Site is in the Little River watershed, which was designated as a Targeted Local Watershed (TLW) in the 2009 Lower Yadkin Pee-Dee River Basin Restoration Priorities (RBRP) plan. The RBRP plan does not specifically identify stressors or project goals in this TLW, but states that continuing watershed improvements will increase ecological uplift. The intent of this project is to help meet the goals for the watershed outlined in the RBRP and provide numerous ecological benefits within the Yadkin-Pee Dee River Basin.

The project goals established in the Mitigation Plan (Wildlands, 2013) were established with careful consideration of goals and objectives that were described in the RBRP and to meet DMS mitigation needs while maximizing the ecological and water quality uplift within the watershed. The following project goals established include:

- Restoring a degraded stream impacted by cattle to create and improve aquatic habitat, reduce sediment inputs from streambank erosion, and reduce agricultural runoff pollution; and
- Restoring a riparian buffer along stream corridors for additional terrestrial and aquatic habitat, nutrient input reduction, and water quality benefits.

The Site construction, planting, and as-built surveys were completed between July 2014 and January 2015. Annual monitoring activities have been conducted since 2015 with an anticipated closeout date in 2022. A conservation easement is in place on 35.4 acres of the riparian corridors to protect them in perpetuity.

This is the seventh and final monitoring report (MY7) as established in the in the Mitigation Plan (Wildlands, 2013) and will also serve as the closeout report. The Site has met the required geomorphic, vegetation, and hydrologic success criteria for the seven years of post-construction monitoring. Geomorphically, each restored and enhanced stream has remained stable with cross-sectional dimensions falling within the range of parameters for the appropriate Rosgen stream type (Rosgen, 1996). Visual stream assessments indicate channel bed, banks, and engineered structures are functioning as designed with little to no instability. The overall average stem density for the Site is 423 stems per acre which exceeds the final density criteria of 210 stems per acres. Hydrological success criteria in the form of two or more bankfull events occurring within separate years has been documented at all stream gages.



HOPEWELL STREAM MITIGATION SITE
Final Monitoring Report (MY7) / Closeout Report

TABLE OF CONTENTS

Section 1: PROJECT OVERVIEW 1-3

 1.1 Project Goals and Objectives 1-3

 1.2 Monitoring Year 7 Data Assessment..... 1-4

 1.2.1 Vegetative Assessment 1-5

 1.2.2 Stream Assessment 1-5

 1.2.3 Areas of Concern/Adaptive Management Plan 1-6

 1.2.4 Hydrology Assessment..... 1-6

 1.3 Monitoring Year 7 Summary 1-6

Section 2: METHODOLOGY 2-1

Section 3: REFERENCES 3-1

APPENDICES

Appendix 1	General Figures and Tables
Figure 1	Vicinity Map
Figure 2	Project Component Map
Table 1A	Project Components and Mitigation Credits
Table 1B	Overall Assets Summary
Table 2	Project Activity and Reporting History
Table 3	Project Contacts Table
Table 4	Project Information and Attributes
Appendix 2	Visual Assessment Data
Figure 3.0-3.7	Integrated Current Condition Plan View
Table 5a-f	Visual Stream Morphology Stability Assessment Table
Table 6	Vegetation Condition Assessment Table
	Stream Photographs & Vegetation Photographs
Appendix 3	Vegetation Plot Data
Table 7	Vegetation Plot Criteria Attainment Table
Table 8	CVS Vegetation Tables - Metadata
Table 9a-g	Planted and Total Stem Counts (Species by Plot with Annual Means)
	Stems Per Plot Across All Years
Appendix 4	Morphological Summary Data and Plots
Table 10a-d	Baseline Stream Data Summary
Table 11a-b	Morphology and Hydraulic Summary (Dimensional Parameters – Cross Section)
Table 12a-g	Monitoring Data – Stream Reach Data Summary
	Cross Section Plots
	Reachwide and Cross Section Pebble Count Plots
Appendix 5	Hydrology Summary Data
Table 13a-e	Verification of Bankfull Events
	Monthly Rainfall Plot
Appendix 6	IRT MY4 Credit Release Site Walk Meeting Minutes
Appendix 7	MY6 Sweetgum Treatment & Supplemental Planting
	UT1B Reach 1 Photographs
	Sweetgum Treatment Figure
	MY6 Supplemental Planting – UT1B Reach 1 Summary Table

Section 1: PROJECT OVERVIEW

The Site is in central Randolph County within the Yadkin-Pee Dee River Basin (USGS Hydrologic Unit 03040104) near the town of Asheboro, North Carolina. The Site is located along Hopewell Friends Road, Mack Road, and Pisgah Covered Bridge Road, just west of Interstate 74/73. The Site is in the Carolina Slate Belt of the Piedmont Physiographic Province (USGS, 1998). The project watershed consists primarily of agricultural and wooded land. The only significant development in the watershed is within the northern extent which includes portions of the City of Asheboro. The drainage area for the western portion of the project site is 429 acres (0.67 square miles). The drainage area for the eastern portion of the project site, which includes a reach on the Little River, is 4,517 acres (7.06 square miles).

The project streams consist of the Little River and five unnamed tributaries (UTs) to the Little River. Mitigation work within the Site included restoration, enhancement, and preservation of 12,308 linear feet (LF) of perennial and intermittent stream channel. Stream restoration reaches include UT2 Reach 1 and 2, UT2A Reach 2, UT2B Reach 2, and UT2C Reach 2 and 3. Stream enhancement I (EI) include UT1B Reach 1 and UT2A Reach 1. Stream enhancement II (EII) reaches include Little River Reach 2, UT1A Reach 1, UT1B Reach 2 and 3, UT2B Reach 1, and UT2C Reach 1. Preservation reaches on the Site include Little River Reach 1 and UT1A Reach 2.

The riparian areas were planted with native vegetation to improve habitat and protect water quality. Construction activities were completed by Terry's Plumbing and Land Mechanics Designs, Inc. in November 2014. Planting and seeding activities were completed by Bruton Natural Systems, Inc., and Terry's Plumbing in January 2015. A conservation easement has been recorded and is in place along the stream riparian corridors to protect them in perpetuity. Baseline monitoring (MY0) was conducted between December 2014 and January 2015. Annual monitoring was conducted for seven years, and now that success criteria have been met, close out is anticipated to commence in 2022. The conservation easement includes 35.954 acres (Deed Book 2371, Page 108-122) within a tract owned by Double T Farms of Randolph, LLC. The project provides 7,412.133 stream mitigation units (SMU's). Appendix 1 provides more detailed project activity, history, contact information, and watershed/site background information for this project.

Directions and a map of the Site are provided in Figure 1 and project components are illustrated for the Site in Figure 2.

1.1 Project Goals and Objectives

Prior to construction activities, many of the streams on the Site, especially those that were accessed less by cattle, exhibited relative stability. However, other project reaches appeared incised and had been severely trampled by cattle resulting in unstable banks, and the bed morphologies were often destroyed. Table 4 in Appendix 1 and Tables 10a through 10d in Appendix 4 present the pre-restoration conditions in detail.

The Site will help meet the goals for the watershed outlined in the RBRP and provide numerous ecological benefits within the Yadkin-Pee Dee River Basin. While many of these benefits are limited to the Hopewell project area, others, such as pollutant removal, reduced sediment loading, and improved aquatic and terrestrial habitat, have a more extensive impact. Expected improvements to water quality and ecological processes are outlined below as project goals and objectives. These project goals were established with careful consideration of goals and objectives that were described in the RBRP and to meet DMS mitigation needs while maximizing the ecological and water quality uplift within the watershed.



The RBRP describes the goals for the 8-digit HUC as the following:

- Continuation of watershed improvement efforts already on-going,
- Protection of valuable natural resources, and
- Development of local partnerships that will work together to implement management strategies for stormwater impacts.

The following project-specific goals were established in the Mitigation Plan (Wildlands, 2013) to contribute to meeting management goals as described above for the Yadkin-Pee Dee Catalog Unit 03040104 and the Little River Target Local Watershed (TLW):

- Restoring a degraded stream impacted by cattle to create and improve aquatic habitat, reduce sediment inputs from streambank erosion, and reduce agricultural runoff pollution; and
- Restoring a riparian buffer along stream corridors for additional terrestrial and aquatic habitat, nutrient input reduction, and water quality benefits.

The project goals were addressed through the following project objectives as stated in the Mitigation Plan:

- On-site nutrient inputs will be decreased by removing cattle from streams and filtering on-site runoff through buffer zones. Off-site nutrient inputs will be absorbed on-site by filtering flood flows through restored floodplain areas, where flood flow will spread through native vegetation;
- Restored buffers and exclusion of livestock to streams will significantly reduce inputs of livestock wastes to streams. This will eliminate a major source of fecal coliform pollution;
- Streambank erosion which contributes sediment load to the creek will be greatly reduced, if not eliminated, in the project area. Eroding stream banks will be stabilized using bioengineering, natural channel design techniques, and grading to reduce bank angles and bank height. Storm flow containing fine sediment will be filtered through restored floodplain areas, where flow will spread through native vegetation. Spreading flood flows will also reduce stream velocity and allow sediment to settle out. Sediment transport capacity of restored reaches will be improved so that capacity balances more closely with load;
- Restored riffle/pool sequences will promote aeration of water and create deep water zones, helping to lower water temperature. Establishment and maintenance of riparian buffers will create long-term shading of the channel to minimize thermal heating. Lower water temperatures will help maintain dissolved oxygen concentrations;
- In-stream structures will be constructed to improve habitat diversity and trap detritus. Wood habitat structures will be included in the stream as part of the restoration design. Such structures may include log drops and riffle structures that incorporate woody debris;
- Adjacent buffer and riparian habitats will be restored with native vegetation as part of the project. Native vegetation will provide cover and food for terrestrial wildlife. Native plant species will be planted and invasive species will be treated. Eroding and unstable areas will also be stabilized with vegetation as part of this project; and
- The restored land will be protected in perpetuity through a conservation easement.

The design streams were restored to the appropriate type based on the surrounding landscape, climate, and natural vegetation communities, but also with strong consideration to existing watershed conditions and trajectory.

1.2 Monitoring Year 7 Data Assessment

Annual monitoring and site visits were conducted during MY7 to assess the condition of the project. The stream and vegetation success criteria for the Site follows the approved success criteria presented in the



Hopewell Stream Mitigation Plan (Wildlands, 2013). The MY7 vegetation and stream surveys were completed in September 2021.

1.2.1 Vegetative Assessment

A total of 31 vegetation plots were established during baseline monitoring within the project easement areas. All of the plots were installed using a standard 10 meter by 10 meter plot. The final vegetative success criteria will be the survival of 210 planted stems per acre in the riparian corridor along restored and enhanced reaches at the end of the MY7. Planted vegetation must average 10 feet in height in each plot at the end of the seventh year of monitoring.

In MY7, all vegetation plots exceeded the final stem density success criteria (210 stems/acre) for planted stems. Individual plot density ranged between 243 stems/acre to 607 stems/acre with an overall average stem density of 423 stems/acre. Stem heights averaged 17.2 feet in MY7 which is a 29% increase in height compared to the MY6 stem height average of 13.4 feet. Most vegetation plots (26 of 31) exceed the final average stem height requirement of 10 feet at the end of MY7. Five plots have average stem heights slightly below the final success criteria and range from 7.7 to 9.0 feet. Most planted woody stems (94%) within the plots had a vigor rating of 3 or more. Refer to Appendix 2 for vegetation plot photographs and the vegetation condition assessment table, and Appendix 3 for vegetation data tables.

Significant efforts were implemented during construction to control the invasive species within the Site, and follow up treatments have continued throughout the seven years of post-construction monitoring. Invasive species treatments have primarily focused on Chinese privet (*Lingustrum sinense*) and to a lesser extent, tree of heaven (*Ailanthus altissima*). Based on visual assessments, treatments have reduced invasive species from approximately 23% of the overall easement acreage in MY1 to less than 1% in MY6 and MY7. During September 2021, small pockets of Chinese privet and tree of heaven (*Ailanthus altissima*) were treated across the site.

Pockets of dense sweetgum (*Liquidambar styraciflua*) volunteers were treated in late 2019 and early 2020 in the upper section of UT1B Reach 1 and UT2C Reach 2. In February 2020, 75 containerized trees were planted in the larger sweetgum treatment area on UT1B Reach 1 as discussed during the IRT/DMS site meeting in May 2019. A follow up sweetgum treatment was performed in September 2021 to areas with resprouts on the upper section of UT1B Reach 1. Refer to Appendix 6 for IRT/DMS meeting minutes and Appendix 7 for photographs of sweetgum treatment and containerized tree planting areas taken in May 2020. Refer to Appendix 2 for the vegetation condition assessment table and the Integrated Current Condition Plan View (CCPV) Maps.

A small portion of fencing along UT1B Reach 1 that deviated from the conservation easement was realigned to match the easement boundary during MY6. Thirty containerized trees were planted within the newly captured easement area in April 2020. Refer to Appendix 6 for list of the types and number of planted trees, as well as their container size, and Appendix 7 for photographic documentation of MY6 plantings taken in May 2020.

1.2.2 Stream Assessment

All streams within the Site appear stable and have met the final geomorphic success criteria. Riffle cross-sections generally show little change in the bankfull area, maximum depth ratio, and width-to-depth ratio and fell within the appropriate Rosgen stream type parameters (Rosgen, 1996). Minor channel adjustments documented during MY7 include deposition at cross-sections 1 (UT2A Reach 1), cross-sections 14 and 15 (UT1B), and cross-sections 16 and 17 (UT2C). Subtle cross-section changes are expected and do not indicate instability. No instability was observed during MY7 field assessments.

In-stream structures used to restore and enhance channel habitat and stability are functioning as designed. Per the Mitigation Plan (Wildlands 2013), pattern data would only be completed if annual monitoring data indicated vertical and lateral instability. No changes were observed in pattern data (radius of curvature or channel belt width); therefore, no pattern data was collected in MY7.

In general, substrate materials in the restoration and enhancement reaches indicated coarser materials in the riffles and finer particles in the pools and distributions are indicative of cyclic changes in sediment transport.

Refer to Appendix 2 for the visual stability assessment table, CCPV maps, and reference photographs. Refer to Appendix 4 for the morphological data and plots.

1.2.3 Areas of Concern/Adaptive Management Plan

Wildlands will continue to monitor and implement invasive treatments through closeout to reduce and control the extent of invasive species at the Site.

1.2.4 Hydrology Assessment

At the end of the seven-year monitoring period, two or more bankfull events must have occurred in separate years within the restoration and enhancement reaches. The hydrology success criteria were met for the seven-year monitoring period after MY2. During MY7, bankfull events were recorded on all automated gages except for UT2B Reach 2; however, evidence of a bankfull event was recorded with the use of the manual crest gage on this reach. Refer to Appendix 5 for hydrologic data.

1.3 Monitoring Year 7 Summary

Overall, the Site has met the final geomorphic, vegetation, and hydrologic success criteria. Stream surveys indicate the channel dimensions are stable and functioning as designed. Visual assessments reveal little to no signs of instability within bed, bank, or engineered structures. The average planted stem density for the Site (423 stems per acre) exceeds the final MY7 success density criteria (210 stems per acre). Most vegetation plots (26 of 31) exceed the average stem height per plot success criteria of 10 feet. The five plots below the threshold are trending towards the 10-foot criteria. Multiple bankfull events have been documented at all stream gages across the Site in separate monitoring years which satisfies the final hydrology success criteria. MY7 is the final year of monitoring, and the Site will be presented to the IRT for regulatory closeout in 2022.

Summary information and data related to the performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Mitigation Plan documents available on DMS's website. All raw data supporting the tables and figures in the appendices are available from DMS upon request.



Section 2: METHODOLOGY


Geomorphic data were collected following the standards outlined in The Stream Channel Reference Site: An Illustrated Guide to Field Techniques (Harrelson et al., 1994) and in the Stream Restoration: A Natural Channel Design Handbook (Doll et al., 2003). All Integrated Current Condition Mapping was recorded using a Trimble handheld GPS with sub-meter accuracy and processed using Pathfinder and ArcGIS. Crest gages and pressure transducers were installed in surveyed riffle cross sections and monitored quarterly to document bankfull events. Hydrologic monitoring instrument installation and monitoring methods are in accordance with the United States Army Corps of Engineers (USACE, 2003) standards. Vegetation monitoring protocols followed the Carolina Vegetation Survey-EEP Level 2 Protocol (Lee et al., 2008).



Section 3: REFERENCES

- Doll, B.A., Grabow, G.L., Hall, K.A., Halley, J., Harman, W.A., Jennings, G.D., and Wise, D.E. 2003. Stream Restoration A Natural Channel Design Handbook.
- Harrelson, C.C., Rawlins, C.L., Potyondy, J.P. 1994. *Stream Channel Reference Sites: An Illustrated Guide to Field Technique*. Gen. Tech. Rep. RM-245. Fort Collins, CO: U.S. Department of Agriculture, Forest Service, Rocky Mountain Forest and Range Experiment Station. 61 p.
- Lee, M.T., Peet, R.K., S.D., Wentworth, T.R. 2008. CVS-EEP Protocol for Recording Vegetation Version 4.2. Retrieved from <http://cvs.bio.unc.edu/protocol/cvs-eep-protocol-v4.2-lev1-5.pdf>.
- North Carolina Division of Mitigation Services and Interagency Review Team Technical Workgroup. 2018. Standard Measurement of the BHR Monitoring Parameter. Raleigh, NC.
- Rosgen, D.L. 1994. A classification of natural rivers. *Catena* 22:169-199.
- Rosgen, D.L. 1996. Applied River Morphology. Pagosa Springs, CO: Wildland Hydrology Books.
- Rosgen, D.L. 1997. A Geomorphological Approach to Restoration of Incised Rivers. Proceedings of the Conference on Management of Landscapes Disturbed by Channel Incision. Center For Computational Hydroscience and Bioengineering, Oxford Campus, University of Mississippi, Pages 12-22.
- United States Army Corps of Engineers. 2003. Stream Mitigation Guidelines. USACE, NCDENR-DWQ, USEPA, NCWRC.
- United States Geological Survey. 1998. North Carolina Geology. <http://www.geology.enr.state.nc.us/usgs/carolina.htm>
- Wildlands Engineering, Inc. 2013. Hopewell Stream Mitigation Site Mitigation Plan. NCEEP, Raleigh, NC.
- Wildlands Engineering, Inc. 2015. Hopewell Stream Mitigation Site Baseline Monitoring Document and As-Built Baseline Report. NCEEP, Raleigh, NC.

APPENDIX 1. General Figures and Tables

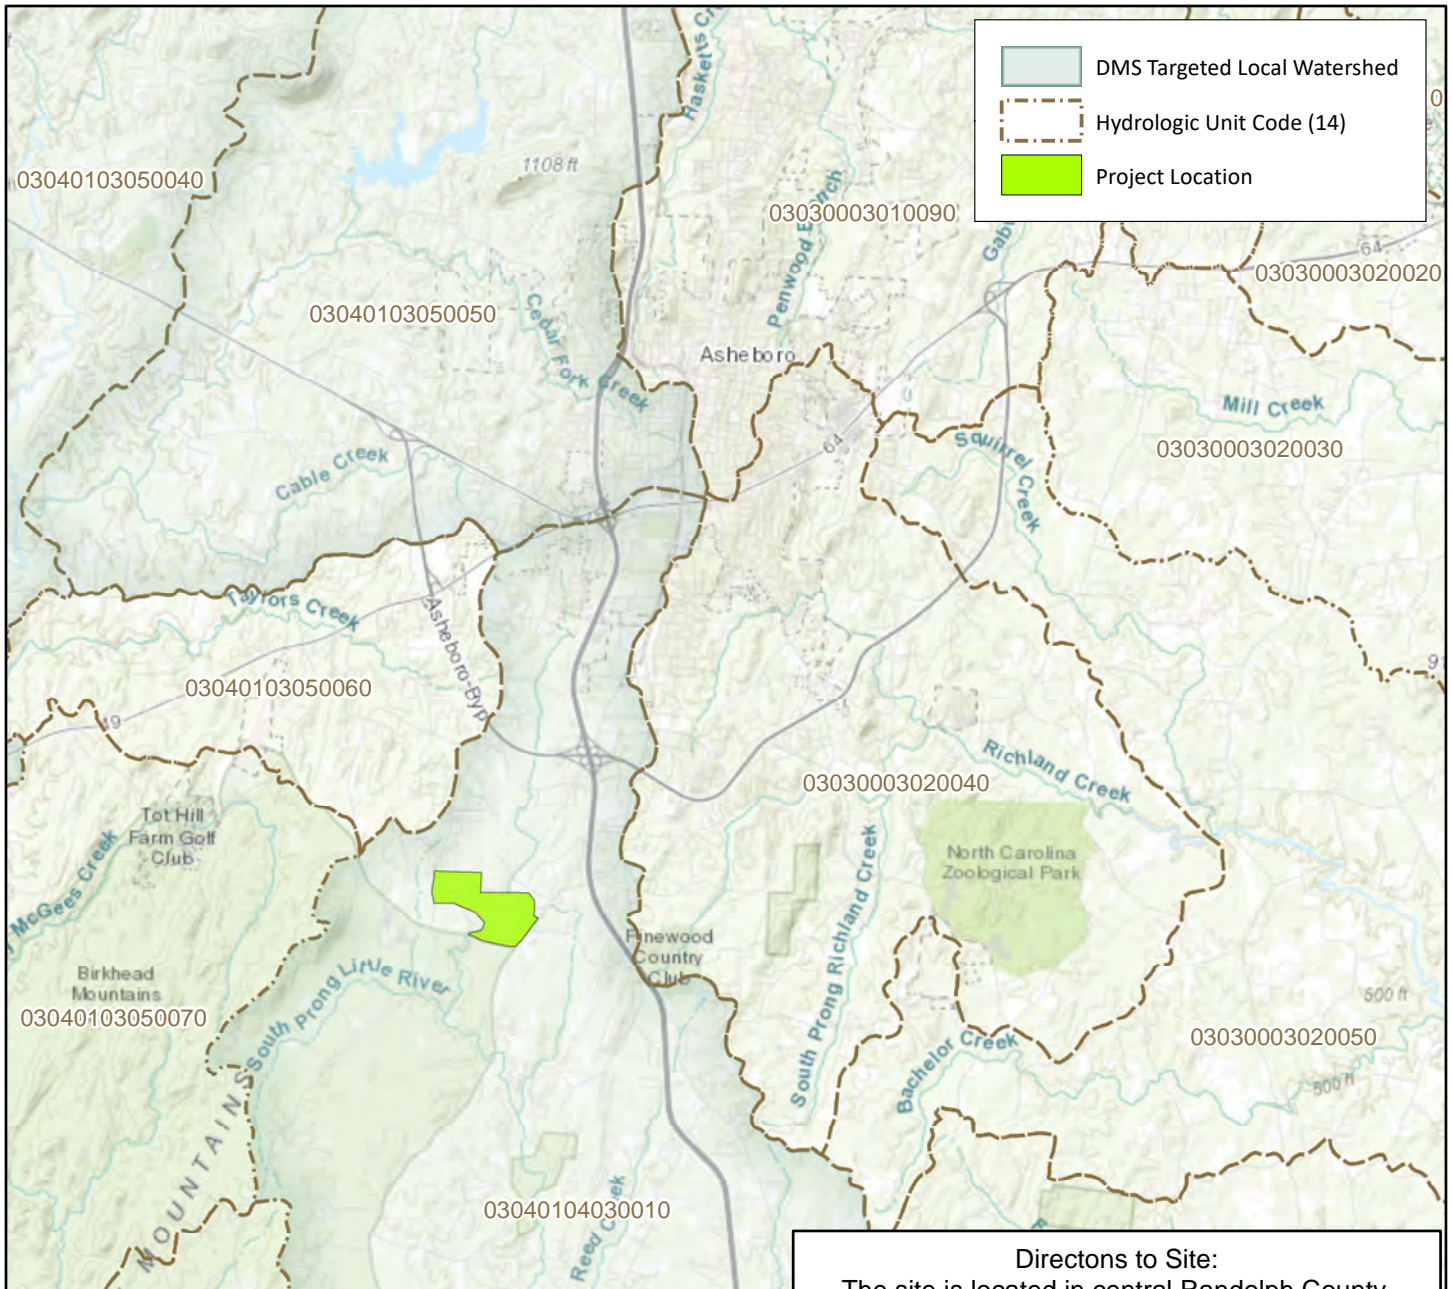

The subject project site is an environmental restoration site of the Department of Environmental Quality (DEQ) Division of Mitigation Services (DMS) and is encompassed by a recorded conservation easement, but is bordered by land under private ownership. Accessing the site may require traversing areas near or along the easement boundary and therefore access by the general public is not permitted. Access by authorized personnel of state and federal agencies or their designees/contractors involved in the development, oversight, and stewardship of the restoration site is permitted within the terms and timeframes of their defined roles. Any intended site visitation or activity by any person outside of these previously sanctioned roles and activities requires prior coordination with DMS.

Directions to Site:
 The site is located in central Randolph County, southwest of Asheboro. From Route 64 in Asheboro, take Route 220 south 4.6 miles. Take Exit 68 for Dawson Miller Road. Turn right onto Dawson Miller Road and travel 1.2 miles. Turn left onto Pisgah Covered Bridge Road and travel 0.2 miles. The main entrance to the site is on the right. A second entrance offering easy access to the western side of the site also exists. To reach this entrance continue on Pisgah Covered Bridge Road for an additional 90 feet past the main entrance and turn right onto Hopewell Friends Road. Travel 0.9 miles and turn right onto Mack Road. Travel 0.5 miles and entrance will be on the right.




Figure 1 Vicinity Map
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County, NC


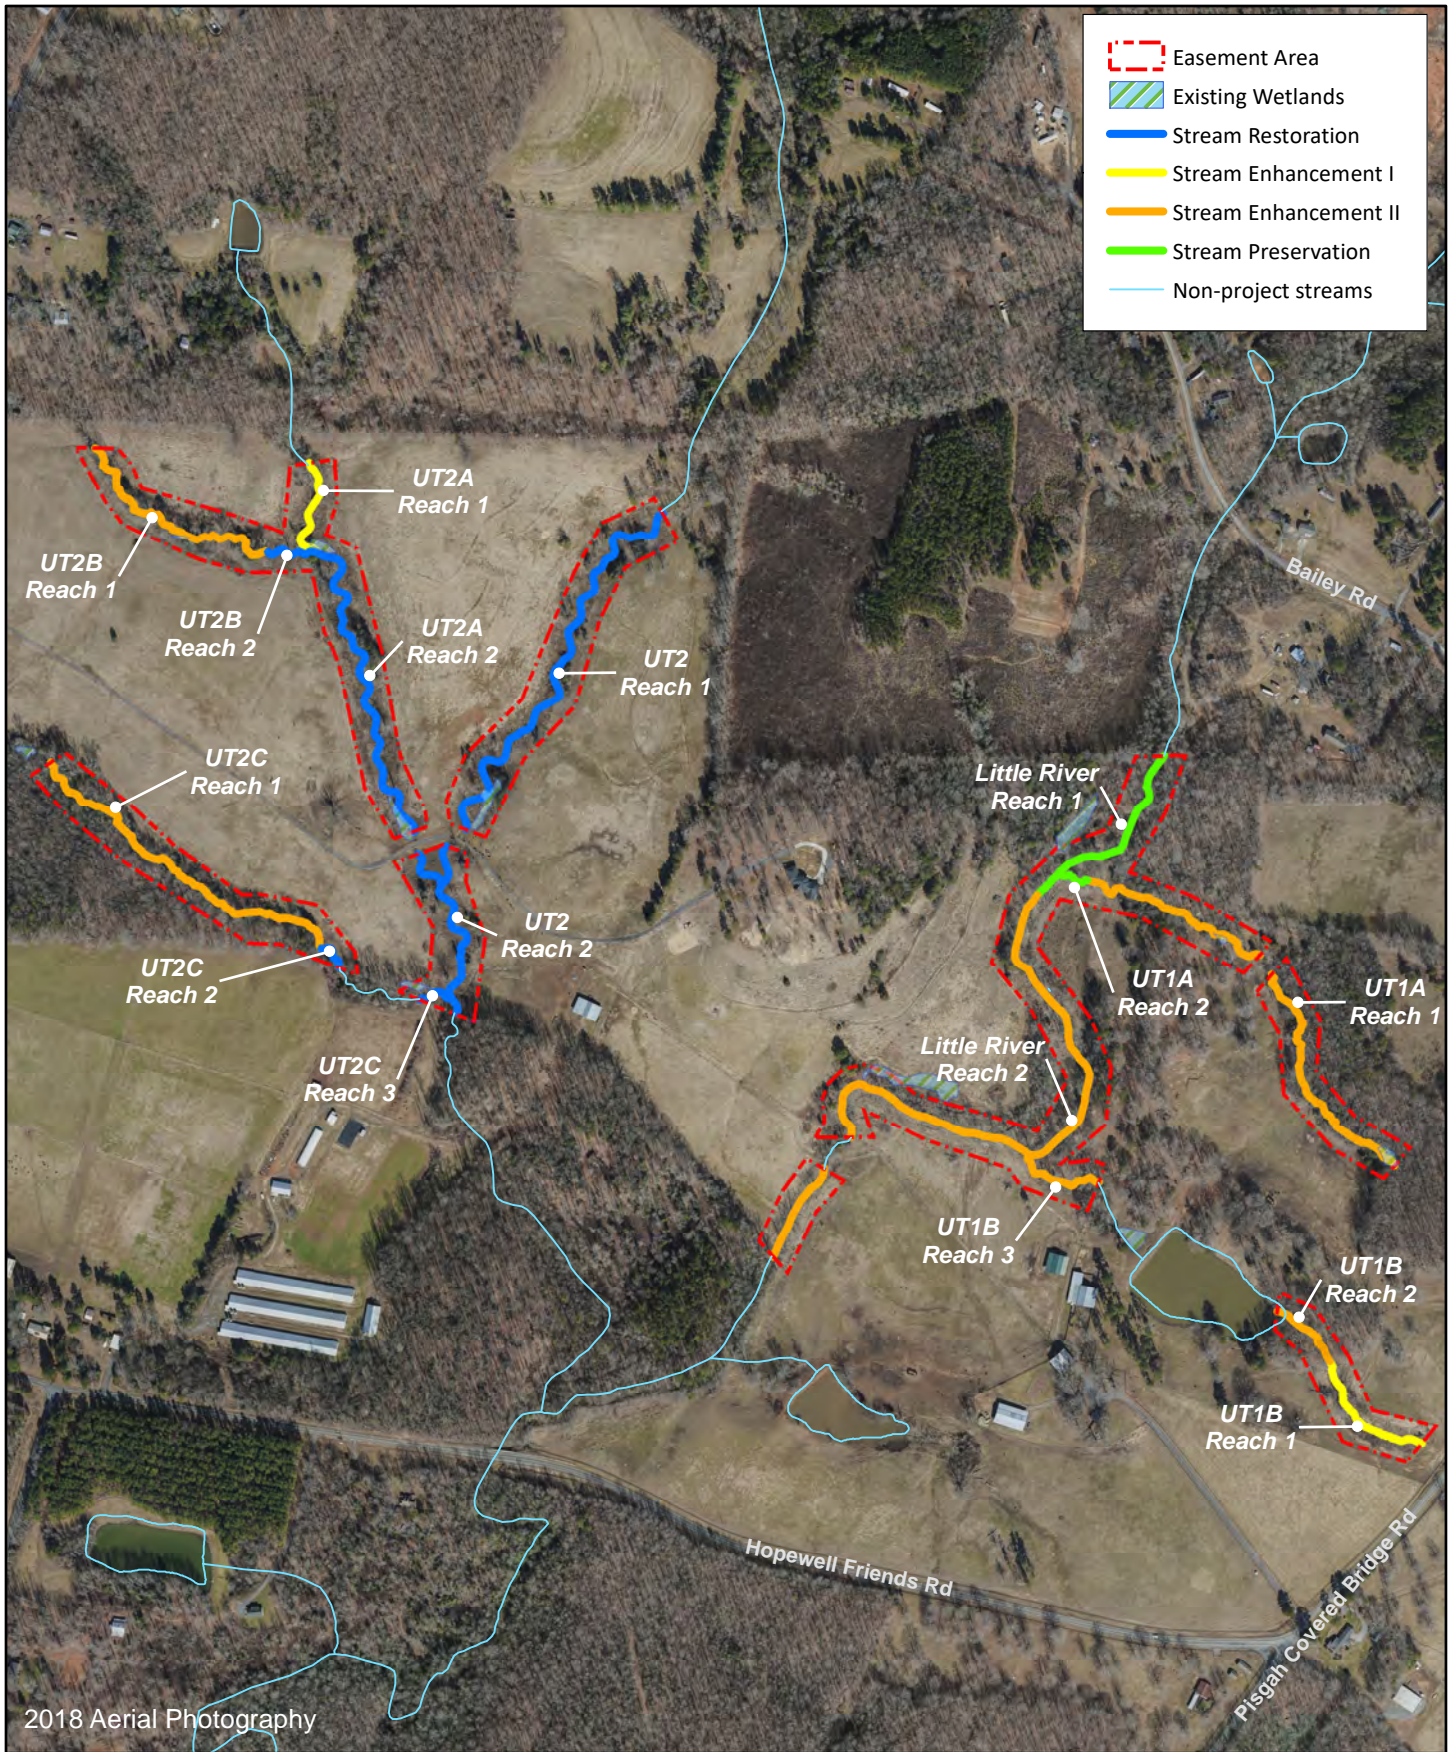


Figure 2 Project Component Map
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County, NC

Table 1A. Project Components and Mitigation Credits

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Mitigation Credits									
	Stream		Riparian Wetland		Non-Riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset
Type	R	RE	R	RE	R	RE			
Totals	7,247.933	164.200	N/A	N/A	N/A	N/A	N/A	N/A	N/A
Project Components									
Reach ID	As-Built Stationing / Location	Existing Footage / Acreage	Approach	Restoration or Restoration Equivalent	Restoration Footage / Acreage	Mitigation Ratio	Credits (SMU / WMU)		
STREAMS									
Little River Reach 1	100+00 - 107+04	704	Preservation	P	704	5:1	140.800		
Little River Reach 2	107+04 - 126+53 128+06 - 131+57	2,374	Fencing / Invasives Control	EII	2,300	2.5:1	920.000		
UT1A Reach 1	200+00 - 208+95 209+84 - 217+00	1,611	Fencing / Invasives Control	EII	1,611	2.5:1	644.400		
UT1A Reach 2	217+00 - 218+17	117	Preservation	P	117	5:1	23.400		
UT1B Reach 1	300+87 - 305+67	475	Fencing / Invasives Control	EI	480	1.5:1	320.000		
UT1B Reach 2 & 3	305+67 - 308+25 350+00 - 353+17	580	Fencing / Invasives Control	EII	575	2.5:1	230.000		
UT2 Reach 1 & 2	400+00 - 415+47 416+35 - 423+16	2,419	Priority 1	Restoration	2,228	1:1	2,228.000		
UT2A Reach 1	500+39 - 504+25	386	Fencing / Invasives Control	EI	386	1.5:1	257.333		
UT2A Reach 2	504+25 - 516+21 517+00 - 518+68	1,368	Priority 1	Restoration	1,364	1:1	1,364.000		
UT2B Reach 1	600+00 - 608+48	848	Fencing / Invasives Control	EII	848	2.5:1	339.200		
UT2B Reach 2	608+48 - 610+46	114	Priority 1	Restoration	198	1:1	198.000		
UT2C Reach 1	700+00 - 712+50	1,215	Fencing / Invasives Control	EII	1,250	2.5:1	500.000		
UT2C Reach 2	712+50 - 713+60	326	Priority 1	Restoration	110	1:1	110.000		
UT2C Reach 3	800+00 - 801+37		Priority 1	Restoration	137	1:1	137.000		

Component Summation						
Restoration Level	Stream (LF)	Riparian Wetland (acres)		Non-Riparian (acres)	Buffer (square)	Upland (acres)
		Riverine	Non-Riverine			
Restoration	4,037	-	-	-	-	-
Enhancement		-	-	-	-	-
Enhancement I	866					
Enhancement II	6,584					
Preservation	821	-	-	-	-	-
High Quality Preservation	-	-	-	-	-	-

Table 1B. Overall Assets Summary
Hopewell Stream Mitigation Site
DMS Project No. 95352
Monitoring Year 7 - 2021

Overall Asset Summary	
Asset Category	Overall Credits
Stream (warm)	7412.133
Wetland	N/A

Table 2. Project Activity and Reporting History

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Activity or Report	Data Collection Complete	Completion or Scheduled Delivery
Mitigation Plan	January 2013	November 2013
Final Design - Construction Plans	January 2013	March 2014
Construction	July 2014-November 2014	November 2014
Temporary S&E mix applied to entire project area ¹	November 2014	November 2014
Permanent seed mix applied to reach/segments	November 2014	November 2014
Bare root and live stake plantings for reach/segments	January 2015	January 2015
Baseline Monitoring Document (Year 0)	December 2014-January 2015	February 2015
Year 1 Monitoring	Stream Survey	December 2015
	Vegetation Survey	
Invasive Plant Control	April 2016	
Bare Areas (UT2A) Limed/Fertilized/Seeded	April 2016	
Year 2 Monitoring	Stream Survey	December 2016
	Vegetation Survey	
Invasive Plant Control	February 2017	
Year 3 Monitoring	Stream Survey	December 2017
	Vegetation Survey	
Invasive Plant Control	October 2017	
Year 4 Monitoring	Stream Survey	December 2018
	Vegetation Survey	
Invasive Plant Control	October 2018	
Year 5 Monitoring	Stream Survey	November 2019
	Vegetation Survey	
Sweetgum Monoculture Treatment	October - December 2019	
Invasive Plant Control	November - December 2019	
Sweetgum Monoculture Treatment (follow up treatment)	February 2020	
Containerized Tree Planting - UT1B Reach 1 (Sweetgum treatment area)	February 2020	
Containerized Tree Planting - UT1B Reach 1 (Newly captured easement)	April 2020	
Year 6 Monitoring	Stream Survey	November 2020
	Vegetation Survey	
Sweetgum Monoculture Treatment	September 2021	
Invasive Plant Control	September 2021	
Year 7 Monitoring	Stream Survey	November 2021
	Vegetation Survey	

¹Seed and mulch is added as each section of construction is completed.**Table 3. Project Contact Table**

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Designer Jeff Keaton, PE	Wildlands Engineering, Inc. 1430 South Mint Street, Suite 104 Charlotte, NC 28203 704.332.7754
Construction Contractor	Terry's Plumbing 465 Lewallen Road Asheboro, NC 27205
	Land Mechanics Designs, Inc. 126 Circle G Lane Willow Spring, NC 27592
Planting Contractor	Bruton Natural Systems, Inc P.O. Box 1197 Fremont, NC 27830
Seeding Contractor	Terry's Plumbing 465 Lewallen Road Asheboro, NC 27205
Seed Mix Sources	Green Resource, LLC
Nursery Stock Suppliers Bare Roots Live Stakes	Dykes and Son Nursery Bruton Natural Systems, Inc
Monitoring Performers	Wildlands Engineering, Inc.
Monitoring, POC	Kristi Suggs 704.332.7754, ext. 110

Table 4. Project Information and Attributes

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Project Information										
Project Name	Hopewell Stream Mitigation Site									
County	Randolph county									
Project Area (acres)	35.4									
Project Coordinates (latitude and longitude)	35°37'37.32" N, 79° 51'13.27" W									
Project Watershed Summary Information										
Physiographic Province	Carolina Slate Belt of the Piedmont Physiographic Province									
River Basin	Yadkin-Pee Dee									
USGS Hydrologic Unit 8-digit	03040104									
USGS Hydrologic Unit 14-digit	03040104030010									
DWR Sub-basin	03-07-15									
Project Drainage Area (acres)	4,083									
Project Drainage Area Percentage of Impervious Area	2%									
CGIA Land Use Classification	2.01.03 – Hay and Pasture Land; 2.99.05 - Farm Ponds; 4 – Forest Land; 1 - Urban and Developed Land									
Reach Summary Information										
Parameters	Little River	UT1A	UT1B Reach 1	UT1B Reach 2 & 3	UT2 Reach 1	UT2 Reach 2	UT2A Reach 1	UT2A Reach 2	UT2B	UT2C
Length of reach (linear feet) - Post-Restoration	3,911	597	480	575	1,547	681	386	1,364	1,046	247
Drainage area (acres)	4,083	38	19	45	246	378	64	102	22	51
NCDWR stream identification score	43.5	22.5	24.5	30	35.5	35.5	27	35	23.7	31
NCDWR Water Quality Classification	C									
Morphological Description (stream type)	P	I	I	P	P	P	I	P	I	P
Evolutionary trend (Simon's Model) - Pre- Restoration	I/II	I	III	I	III/IV	IV	III	III/IV	III	III
Underlying mapped soils	Badin-Tarrus Complex, Chewacla Loam, Georgeville silt loam, Georgeville silty clay loam, Mecklenburg clay loam, Riverview sandy loam									
Drainage class	---	---	---	---	---	---	---	---	---	---
Soil hydric status	---	---	---	---	---	---	---	---	---	---
Slope	0.0051	0.0389	0.03	0.0583	0.0093	0.0075	0.0102	0.011	0.0259	0.0154
FEMA classification	AE*									
Native vegetation community	Piedmont Bottomland Forest / Mixed Mesic Hardwood Forest									
Percent composition exotic invasive vegetation-Post-Restoration	0%									
Regulatory Considerations										
Regulation	Applicable?			Resolved?			Supporting Documentation			
Waters of the United States - Section 404	X			X			USACE Nationwide Permit No.27 and DWQ 401 Water Quality Certification No. 3885.			
Waters of the United States - Section 401	X			X						
Division of Land Quality (Dam Safety)	N/A			N/A			N/A			
Endangered Species Act	X			X			Hopewell Mitigation Plan; Wildlands determined "no effect" on Randolph County listed endangered species. (Letter from USFWS dated July 27, 2012)			
Historic Preservation Act	X			X			No historic resources were found to be impacted (letter from SHPO dated 7/13/2012).			
Coastal Zone Management Act (CZMA)/Coastal Area Management Act (CAMA)	N/A			N/A			N/A			
FEMA Floodplain Compliance	X			X			Little River is a mapped Zone AE floodplain with defined base flood elevations. A floodway has not been delineated but non-encroachment widths have been defined; (FEMA Zone AE, FIRM panel 7648).			
Essential Fisheries Habitat	N/A			N/A			N/A			

APPENDIX 2. Visual Assessment Data





2018 Aerial Photography





Figure 3.1 Integrated Current Condition Plan View (Sheet 1 of 7)
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County

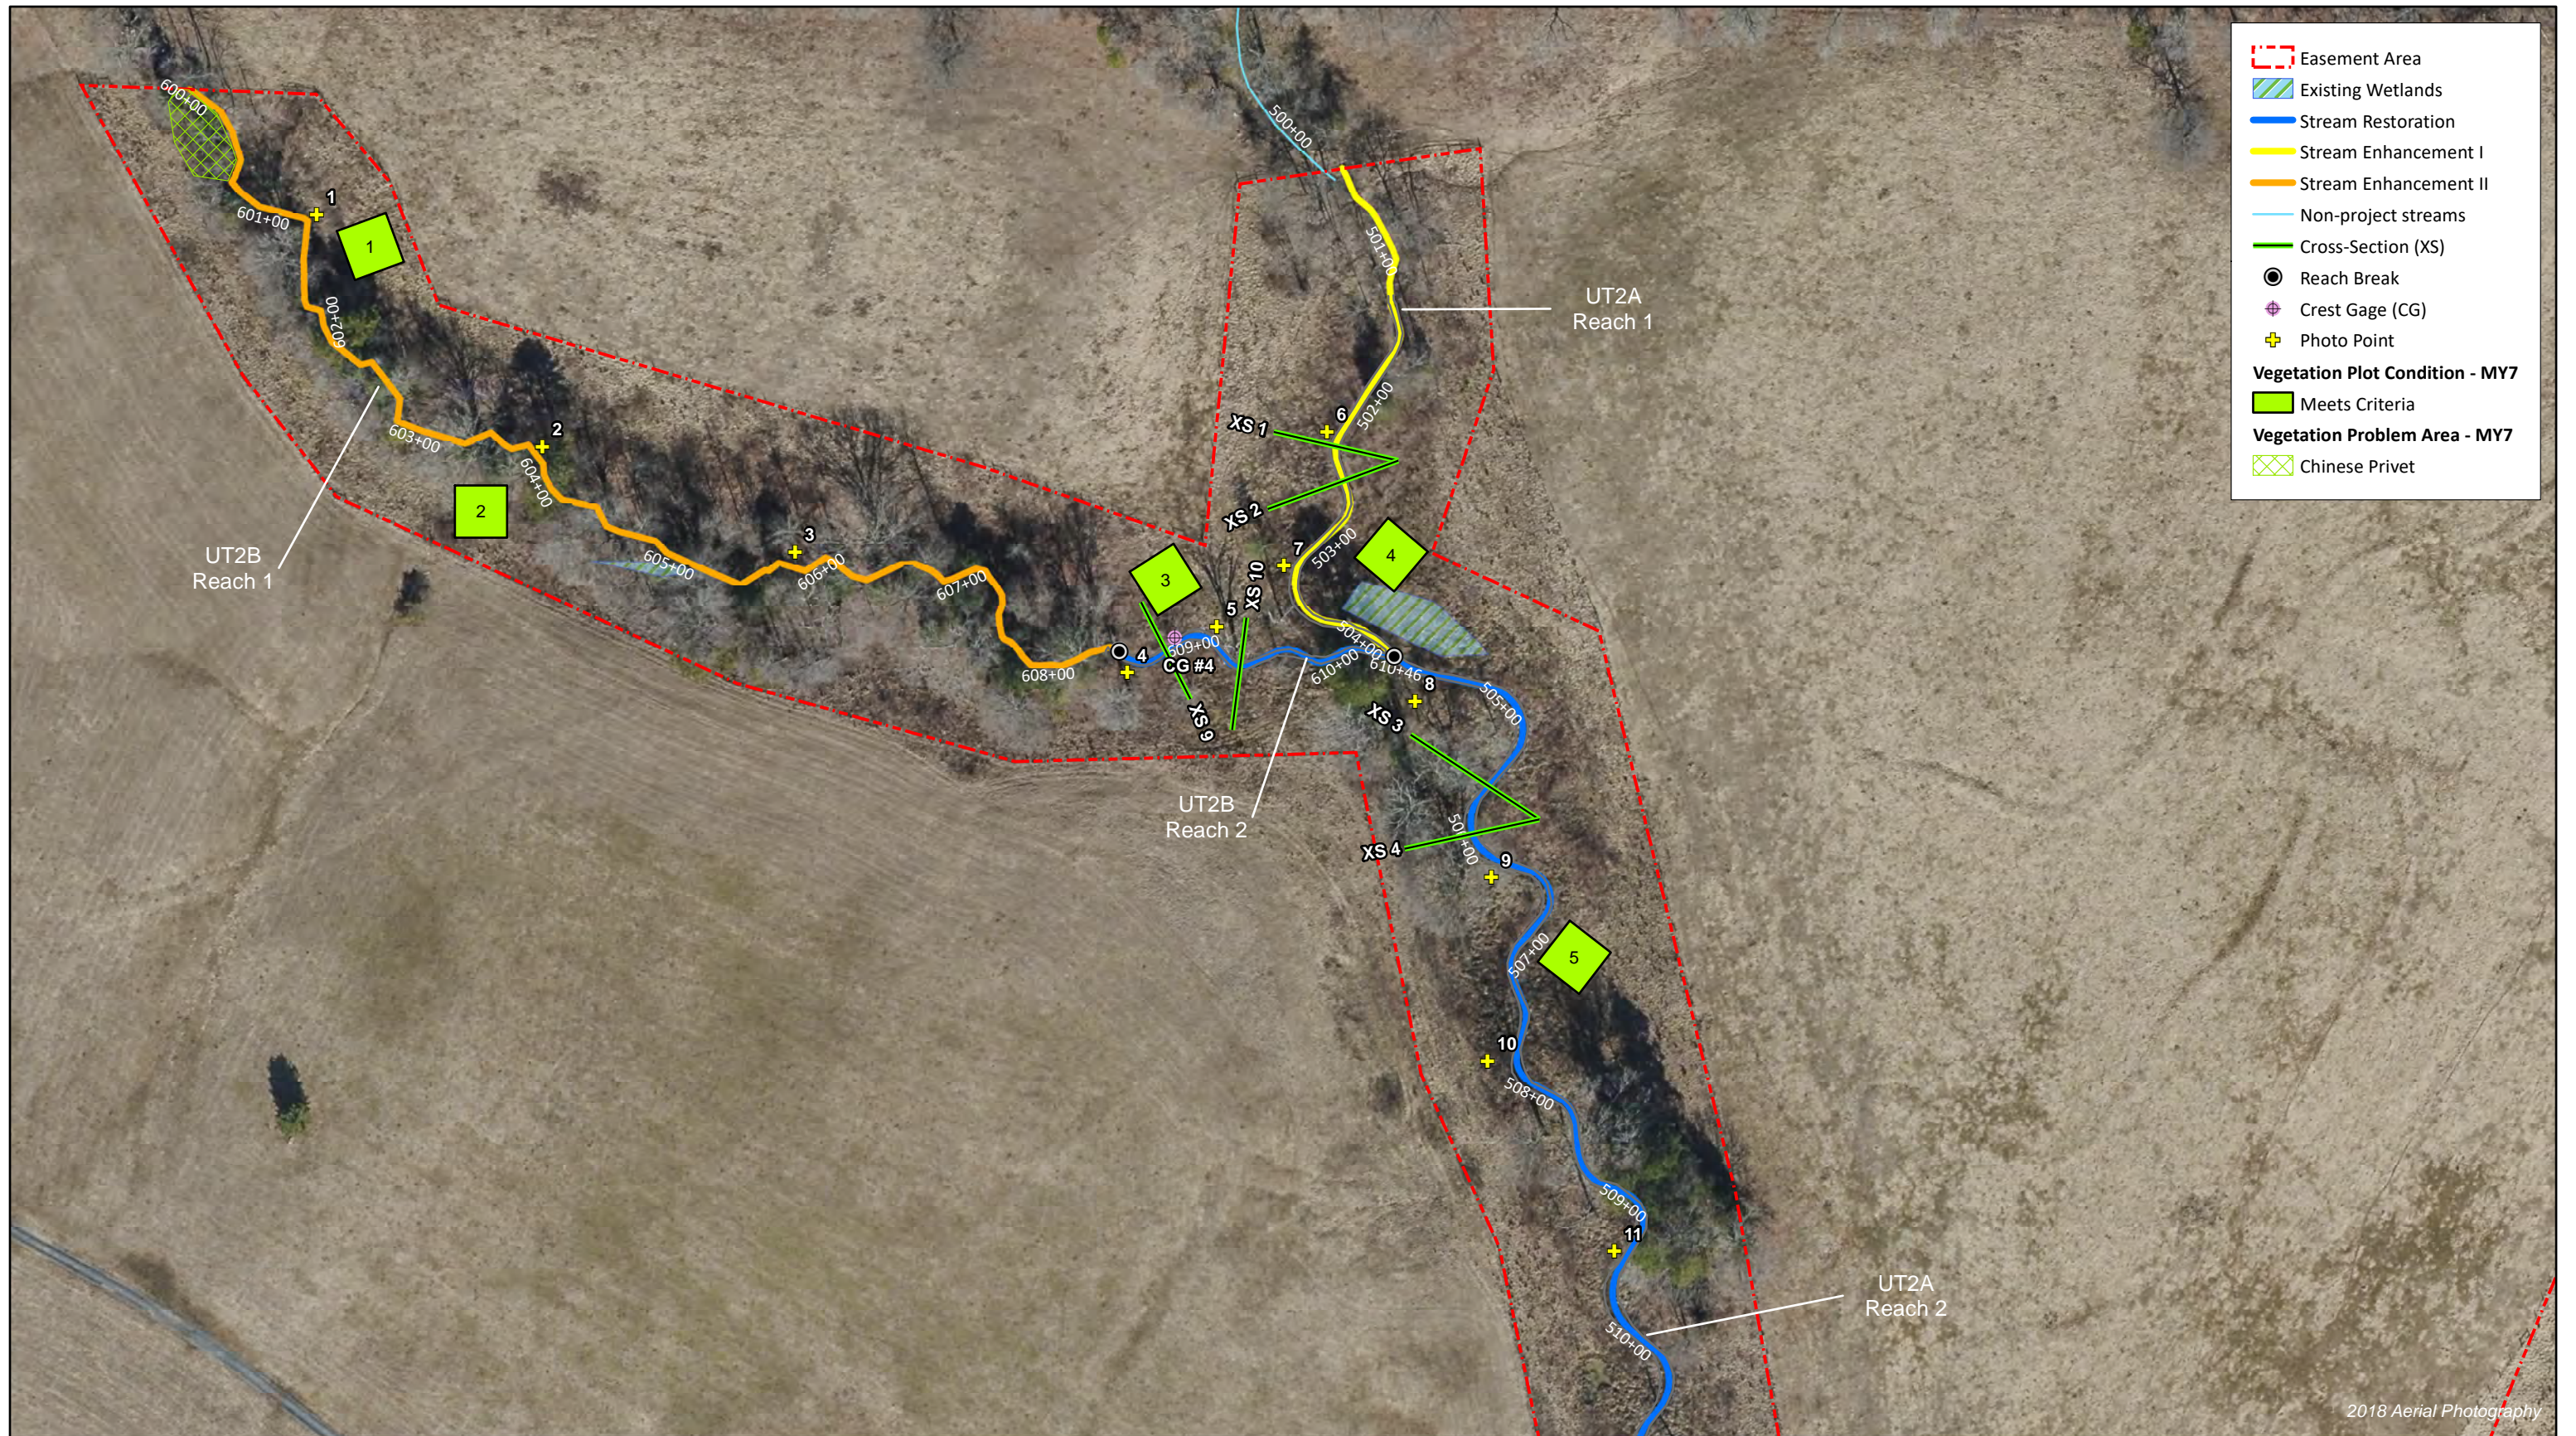

2018 Aerial Photography





Figure 3.2 Integrated Current Condition Plan View (Sheet 2 of 7)
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County

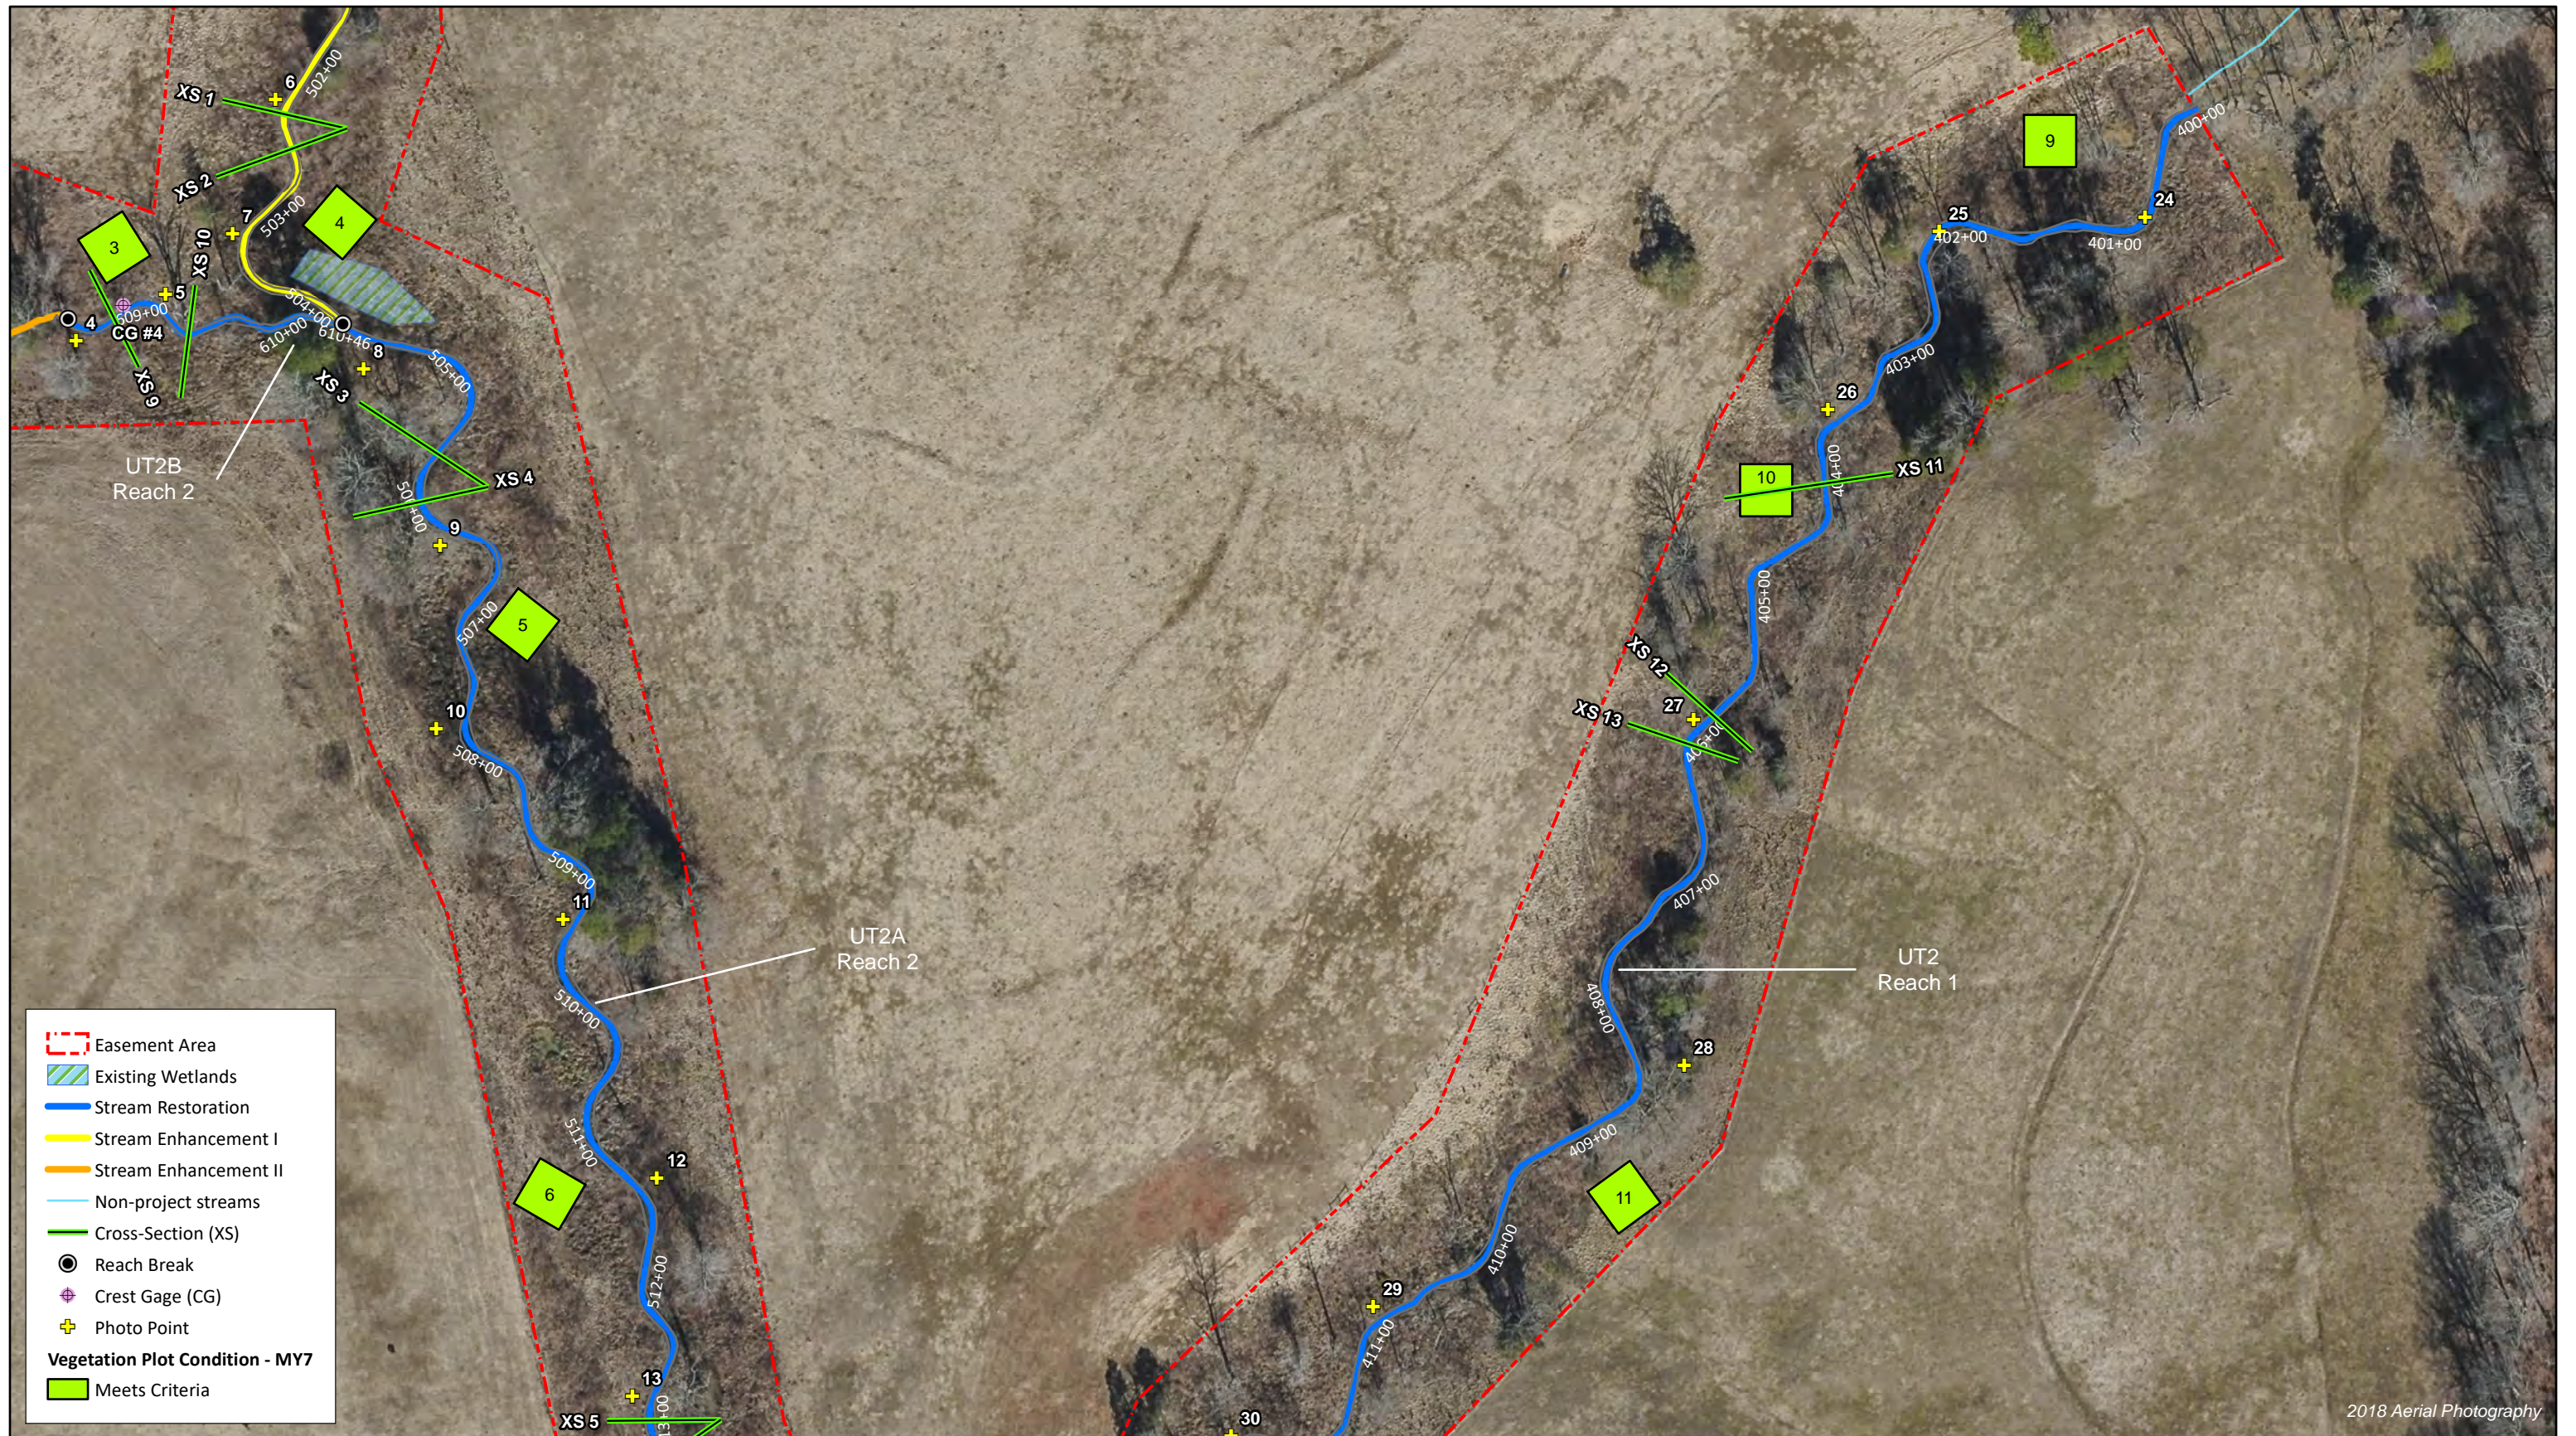

2018 Aerial Photography




Figure 3.3 Integrated Current Condition Plan View (Sheet 3 of 7)
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County









2018 Aerial Photography




Figure 3.7 Integrated Current Condition Plan View (Sheet 7 of 7)
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County

Table 5a. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT1B Reach 1 (480 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	8	8			100%			
	3. Meander Pool Condition	Depth Sufficient	8	8			100%			
		Length Appropriate	8	8			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	8	8			100%			
		Thalweg centering at downstream of meander bend (Glide)	8	8			100%			
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	n/a	n/a			n/a			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	n/a	n/a			n/a			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	n/a	n/a			n/a			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	n/a	n/a			n/a			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	n/a	n/a			n/a			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 5b. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT2 Reach 1 & 2 (2,228 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	30	30			100%			
	3. Meander Pool Condition	Depth Sufficient	29	29			100%			
		Length Appropriate	29	29			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	29	29			100%			
		Thalweg centering at downstream of meander bend (Glide)	29	29			100%			
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	32	32			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	13	13			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	13	13			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	20	20			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	20	20			100%			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 5c. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT2A Reach 1 & 2 (1,750 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	31	31		100%				
	3. Meander Pool Condition	Depth Sufficient	31	31		100%				
		Length Appropriate	31	31		100%				
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	31	31		100%				
		Thalweg centering at downstream of meander bend (Glide)	31	31		100%				
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	32	32			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	2	2			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	2	2			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	21	21			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	20	20			100%			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 5d. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT2B Reach 2 (198 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	7	7		100%				
	3. Meander Pool Condition	Depth Sufficient	6	6		100%				
		Length Appropriate	6	6		100%				
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	6	6		100%				
		Thalweg centering at downstream of meander bend (Glide)	6	6		100%				
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	6	6			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	n/a	n/a			n/a			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	n/a	n/a			n/a			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	6	6			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	6	6			100%			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 5e. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT2C Reach 2 (110 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	5	5		100%				
	3. Meander Pool Condition	Depth Sufficient	4	4		100%				
		Length Appropriate	4	4		100%				
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	4	4		100%				
		Thalweg centering at downstream of meander bend (Glide)	4	4		100%				
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	4	4			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	n/a	n/a			n/a			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	n/a	n/a			n/a			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	4	4			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	4	4			100%			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 5f. Visual Stream Morphology Stability Assessment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

UT2C Reach 3 (137 LF) / Assessment Date 9/30/2021

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-Built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjust % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Shallow and Run units)	Aggradation			0	0	100%			
		Degradation			0	0	100%			
	2. Riffle Condition	Texture/Substrate	3	3			100%			
	3. Meander Pool Condition	Depth Sufficient	2	2			100%			
		Length Appropriate	2	2			100%			
	4. Thalweg Position	Thalweg centering at upstream of meander bend (Run)	2	2			100%			
		Thalweg centering at downstream of meander bend (Glide)	2	2			100%			
2. Bank	1. Scoured/Eroded	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	n/a	n/a	n/a
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	n/a	n/a	n/a
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	n/a	n/a	n/a
Totals					0	0	100%	n/a	n/a	n/a
3. Engineered Structures ¹	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	n/a	n/a			n/a			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	n/a	n/a			n/a			
	3. Bank Protection	Bank erosion within the structures extent of influence does not exceed 15%.	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~Max Pool Depth : Bankfull Depth ≥ 1.6 Rootwads/logs providing some cover at baseflow.	1	1			100%			

¹Excludes constructed shallows since they are evaluated in section 1.

Table 6. Vegetation Condition Assessment Table Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021 / Assessment Dates 9/27 -9/30/2021

Planted Acreage 24

Vegetation Category	Definitions	Mapping Threshold (Ac)	Number of Polygons	Combined Acreage	% of Planted Acreage
Bare Areas	Very limited cover of both woody and herbaceous material	0.1	0	0	0.0%
Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1	0	0.0	0.0%
Total			0	0.0	0.0%
Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 Ac	0	0	0%
Cumulative Total			0	0.0	0.0%

Easement Acreage 35

Vegetation Category	Definitions	Mapping Threshold (SF)	Number of Polygons	Combined Acreage	% of Easement Acreage
Invasive Areas of Concern	Areas of points (if too small to render as polygons at map scale).	1,000	4	0.14	0.4%
Easement Encroachment Areas	Areas of points (if too small to render as polygons at map scale).	none	0	0	0%

**Stream Photographs
Monitoring Year 7**



UT2B R1 – Photo Point 1 looking upstream (06/03/2021)



UT2B R1 – Photo Point 1 looking downstream (06/03/2021)



UT2B R1 – Photo Point 2 looking upstream (06/03/2021)



UT2B R1 – Photo Point 2 looking downstream (06/03/2021)



UT2B R1 – Photo Point 3 looking upstream (06/03/2021)



UT2B R1 – Photo Point 3 looking downstream (06/03/2021)



UT2B R1 – Photo Point 4 looking upstream (06/03/2021)



UT2B R1 – Photo Point 4 looking downstream (06/03/2021)



UT2B R1 – Photo Point 5 looking upstream (06/03/2021)



UT2B R1 – Photo Point 5 looking downstream (06/03/2021)



UT2A R1 – Photo Point 6 looking upstream (06/03/2021)



UT2A R1 – Photo Point 6 looking downstream (06/03/2021)



UT2A R1 – Photo Point 7 looking upstream (06/03/2021)



UT2A R1 – Photo Point 7 looking downstream (06/03/2021)



UT2A R2 – Photo Point 8 looking upstream (06/03/2021)



UT2A R2 – Photo Point 8 looking downstream (06/03/2021)



UT2A R2 – Photo Point 9 looking upstream (06/03/2021)



UT2A R2 – Photo Point 9 looking downstream (06/03/2021)



UT2A R2 – Photo Point 10 looking upstream (06/03/2021)



UT2A R2 – Photo Point 10 looking downstream (06/03/2021)



UT2A R2 – Photo Point 11 looking upstream (06/03/2021)



UT2A R2 – Photo Point 11 looking downstream (06/03/2021)



UT2A R2 – Photo Point 12 looking upstream (06/03/2021)



UT2A R2 – Photo Point 12 looking downstream (06/03/2021)



UT2A R2 – Photo Point 13 looking upstream (06/03/2021)



UT2A R2 – Photo Point 13 looking downstream (06/03/2021)



UT2A R2 – Photo Point 14 looking upstream (06/03/2021)



UT2A R2 – Photo Point 14 looking downstream (06/03/2021)



UT2A R2 – Photo Point 15 looking upstream (06/03/2021)



UT2A R2 – Photo Point 15 looking downstream (06/03/2021)



UT2C R1 – Photo Point 16 looking upstream (06/03/2021)



UT2C R1 – Photo Point 16 looking downstream (06/03/2021)



UT2C R1 – Photo Point 17 looking upstream (06/03/2021)



UT2C R1 – Photo Point 17 looking downstream (06/03/2021)



UT2C R1 – Photo Point 18 looking upstream (06/03/2021)



UT2C R1 – Photo Point 18 looking downstream (06/03/2021)



UT2C R1 – Photo Point 19 looking upstream (06/03/2021)



UT2C R1 – Photo Point 19 looking downstream (06/03/2021)



UT2C R1 – Photo Point 20 looking upstream (06/03/2021)



UT2C R1 – Photo Point 20 looking downstream (06/03/2021)



UT2C R1 – Photo Point 21 looking upstream (06/03/2021)



UT2C R1 – Photo Point 21 looking downstream (06/03/2021)



UT2C R2 – Photo Point 22 looking upstream (06/03/2021)



UT2C R2 – Photo Point 22 looking downstream (06/03/2021)



UT2C R3 – Photo Point 23 looking upstream (06/03/2021)



UT2C R3 – Photo Point 23 looking downstream (06/03/2021)



UT2 R1 – Photo Point 24 looking upstream (06/03/2021)



UT2 R1 – Photo Point 24 looking downstream (06/03/2021)



UT2 R1 – Photo Point 25 looking upstream (06/03/2021)



UT2 R1 – Photo Point 25 looking downstream (06/03/2021)



UT2 R1 – Photo Point 26 looking upstream (06/03/2021)



UT2 R1 – Photo Point 26 looking downstream (06/03/2021)



UT2 R1 – Photo Point 27 looking upstream (06/03/2021)



UT2 R1 – Photo Point 27 looking downstream (06/03/2021)



UT2 R1 – Photo Point 28 looking upstream (06/03/2021)



UT2 R1 – Photo Point 28 looking downstream (06/03/2021)



UT2 R1 – Photo Point 29 looking upstream (06/03/2021)



UT2 R1 – Photo Point 29 looking downstream (06/03/2021)



UT2 R1 – Photo Point 30 looking upstream (06/03/2021)



UT2 R1 – Photo Point 30 looking downstream (06/03/2021)



UT2 R1 – Photo Point 31 looking upstream (06/03/2021)



UT2 R1 – Photo Point 31 looking downstream (06/03/2021)



UT2 R1 – Photo Point 32 looking upstream (06/03/2021)



UT2 R1 – Photo Point 32 looking downstream (06/03/2021)



UT2 R2 – Photo Point 33 looking upstream (06/03/2021)



UT2 R2 – Photo Point 33 looking downstream (06/03/2021)



UT2 R2 – Photo Point 34 looking upstream (06/03/2021)



UT2 R2 – Photo Point 34 looking downstream (06/03/2021)



UT2 R2 – Photo Point 35 looking upstream (06/03/2021)



UT2 R2 – Photo Point 35 looking downstream (06/03/2021)



Little River R1 – Photo Point 36 looking upstream (09/29/2021)



Little River R1–Photo Point 36 looking downstream (09/29/2021)



Little River R1 – Photo Point 37 looking upstream (09/29/2021)



Little River R1–Photo Point 37 looking downstream (09/29/2021)



Little River R1 – Photo Point 38 looking upstream (09/29/2021)



Little River R1–Photo Point 38 looking downstream (09/29/2021)



Little River R2 – Photo Point 39 looking upstream (09/29/2021)



Little River R2–Photo Point 39 looking downstream (09/29/2021)



Little River R2 – Photo Point 40 looking upstream (09/29/2021)



Little River R2-Photo Point 40 looking downstream (09/29/2021)



Little River R2 – Photo Point 41 looking upstream (09/29/2021)



Little River R2-Photo Point 41 looking downstream (09/29/2021)



Little River R2 – Photo Point 42 looking upstream (09/29/2021)



Little River R2-Photo Point 42 looking downstream (09/29/2021)



Little River R2 – Photo Point 43 looking upstream (09/29/2021)



Little River R2–Photo Point 43 looking downstream (09/29/2021)



Little River R2 – Photo Point 44 looking upstream (09/29/2021)



Little River R2–Photo Point 44 looking downstream (09/29/2021)



Little River R2 – Photo Point 45 looking upstream (09/29/2021)



Little River R2–Photo Point 45 looking downstream (09/03/2021)



Little River R2 – Photo Point 46 looking upstream (09/29/2021)



Little River R2–Photo Point 46 looking downstream (09/29/2021)



Little River R2 – Photo Point 47 looking upstream (09/29/2021)



Little River R2–Photo Point 47 looking downstream (09/29/2021)



UT1A R1 – Photo Point 48 looking upstream (06/03/2021)



UT1A R1 – Photo Point 48 looking downstream (06/03/2021)



UT1A R1 – Photo Point 49 looking upstream (06/03/2021)



UT1A R1 – Photo Point 49 looking downstream (06/03/2021)



UT1A R1 – Photo Point 50 looking upstream (06/03/2021)



UT1A R1 – Photo Point 50 looking downstream (06/03/2021)



UT1A R1 – Photo Point 51 looking upstream (06/03/2021)



UT1A R1 – Photo Point 51 looking downstream (06/03/2021)



UT1A R1 – Photo Point 52 looking upstream (06/03/2021)



UT1A R1 – Photo Point 52 looking downstream (06/03/2021)



UT1A R1 – Photo Point 53 looking upstream (06/03/2021)



UT1A R1 – Photo Point 53 looking downstream (06/03/2021)



UT1A R1 – Photo Point 54 looking upstream (06/03/2021)



UT1A R1 – Photo Point 54 looking downstream (06/03/2021)



UT1A R1 – Photo Point 55 looking upstream (06/03/2021)



UT1A R1 – Photo Point 55 looking downstream (06/03/2021)



UT1A R1 – Photo Point 56 looking upstream (06/03/2021)



UT1A R1 – Photo Point 56 looking downstream (06/03/2021)



UT1B R1 – Photo Point 57 looking upstream (06/03/2021)



UT1B R1 – Photo Point 57 looking downstream (06/03/2021)



UT1B R1 – Photo Point 58 looking upstream (06/03/2021)



UT1B R1 – Photo Point 58 looking downstream (06/03/2021)



UT1B R1 – Photo Point 59 looking upstream (06/03/2021)



UT1B R1 – Photo Point 59 looking downstream (06/03/2021)



UT1B R1 – Photo Point 60 looking upstream (06/03/2021)



UT1B R1 – Photo Point 60 looking downstream (06/03/2021)



UT1B R2 – Photo Point 61 looking upstream (06/03/2021)



UT1B R2 – Photo Point 61 looking downstream (06/03/2021)



UT1B R2 – Photo Point 62 looking upstream (06/03/2021)



UT1B R2 – Photo Point 62 looking downstream (06/03/2021)



UT1B R3 – Photo Point 63 looking upstream (06/03/2021)



UT1B R3 – Photo Point 63 looking downstream (06/03/2021)



UT1B R3 – Photo Point 64 looking upstream (06/03/2021)



UT1B R3 – Photo Point 64 looking downstream (06/03/2021)

**Vegetation Photographs
Monitoring Year 7**



Vegetation Plot 1 – (09/27/2021)



Vegetation Plot 2 – (09/27/2021)



Vegetation Plot 3 – (09/27/2021)



Vegetation Plot 4 – (09/27/2021)



Vegetation Plot 5 – (09/27/2021)



Vegetation Plot 6 – (09/27/2021)



Vegetation Plot 7 – (09/27/2021)




Vegetation Plot 8 – (09/27/2021)



Vegetation Plot 9 – (09/27/2021)



Vegetation Plot 10 – (09/27/2021)

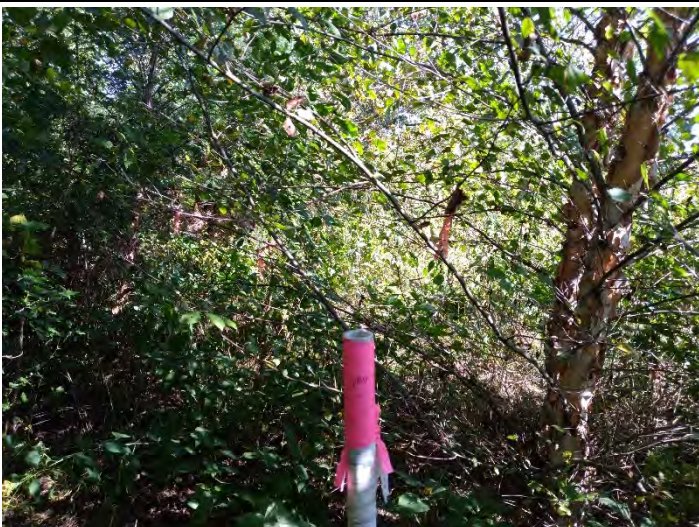

Vegetation Plot 11 – (09/27/2021)



Vegetation Plot 12 – (09/27/2021)



Vegetation Plot 13 – (09/27/2021)



Vegetation Plot 14 – (09/27/2021)



Vegetation Plot 15 – (09/27/2021)



Vegetation Plot 16 – (09/27/2021)



Vegetation Plot 17 – (09/27/2021)



Vegetation Plot 18 – (09/28/2021)



Vegetation Plot 19 – (09/28/2021)



Vegetation Plot 20 – (09/28/2021)



Vegetation Plot 21 – (09/28/2021)



Vegetation Plot 22 – (09/28/2021)



Vegetation Plot 23– (09/28/2021)



Vegetation Plot 24 – (09/28/2021)



Vegetation Plot 25 – (09/28/2021)



Vegetation Plot 26 – (09/28/2021)



Vegetation Plot 27 – (09/28/2021)



Vegetation Plot 28 – (09/28/2021)



Vegetation Plot 29 – (09/28/2021)



Vegetation Plot 30 – (09/28/2021)



Vegetation Plot 31 – (09/28/2021)

APPENDIX 3. Vegetation Plot Data

Table 7. Vegetation Plot Criteria Attainment Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Plot	MYS Success Criteria Met (Y/N)	Tract Mean
1	Y	100%
2	Y	
3	Y	
4	Y	
5	Y	
6	Y	
7	Y	
8	Y	
9	Y	
10	Y	
11	Y	
12	Y	
13	Y	
14	Y	
15	Y	
16	Y	
17	Y	
18	Y	
19	Y	
20	Y	
21	Y	
22	Y	
23	Y	
24	Y	
25	Y	
26	Y	
27	Y	
28	Y	
29	Y	
30	Y	
31	Y	

Table 8. CVS Vegetation Tables - Metadata

Hopewell Stream Mitigation Site
DMS Project No. 95352
Monitoring Year 7 - 2021

Report Prepared By	Ian Eckardt
Date Prepared	11/16/2021 17:54
Database Name	cvs-eep-entrytool-v2.5.0 Hopewell MY7.mdb
Database Location	\\192.168.3.7\projects\ActiveProjects\005-02133 Hopewell Mitigation FDP\Monitoring\Monitoring Year 7 (2021)\Vegetation Assessment
Computer Name	IAN
File Size	53575680
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Project Planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Project Total Stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and Spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY-----	
Project Code	95352
Project Name	Hopewell Stream Mitigation Site
Area (sq m)	128285.35
Required Plots (calculated)	22
Sampled Plots	31

Table 9a. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Scientific Name	Common Name	Species Type	Current Plot Data (MY7 2021)															
			Vegetation Plot 1			Vegetation Plot 2			Vegetation Plot 3			Vegetation Plot 4			Vegetation Plot 5			
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	
<i>Acer negundo</i>	Box elder	Tree										10						
<i>Acer rubrum</i>	Red maple	Tree																
<i>Alnus serrulata</i>	Hazel alder	Shrub																
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub																
<i>Betula nigra</i>	River birch	Tree				1	1	1					1	1	1			
<i>Carya</i>	Hickory	Tree																
<i>Cedrus</i>	Cedar	Tree																
<i>Celtis laevigata</i>	Sugarberry	Tree																
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree																
<i>Crataegus</i>	Hawthorn	Tree																
<i>Diospyros virginiana</i>	Common persimmon	Tree																
<i>Fraxinus pennsylvanica</i>	Green ash	Tree							6	6	6		5	5	5			
<i>Gleditsia triacanthos</i>	Honey locust	Tree																
<i>Ilex opaca</i>	American holly	Tree																
<i>Juglans nigra</i>	Black walnut	Tree																
<i>Juniperus</i>	Juniper	Tree																
<i>Juniperus communis</i>	Common juniper	Tree																
<i>Juniperus virginiana</i>	Eastern redcedar	Tree																
<i>Liquidambar styraciflua</i>	Sweetgum	Tree			5						85			43				7
<i>Liriodendron tulipifera</i>	Tuliptree	Tree						2								1	1	1
<i>Nyssa biflora</i>	Swamp tupelo	Tree																
<i>Nyssa sylvatica</i>	Blackgum	Tree																
<i>Pinus</i>	Pine	Tree										11			15			3
<i>Pinus palustris</i>	Longleaf pine	Tree																
<i>Pinus rigida</i>	Pitch pine	Tree																
<i>Pinus serotina</i>	Pond pine	Tree																
<i>Pinus taeda</i>	Loblolly pine	Tree																
<i>Pinus virginiana</i>	Virginia Pine	Tree																
<i>Platanus occidentalis</i>	American sycamore	Tree	2	2	2	1	1	6				7	7	14	2	2	2	
<i>Prunus serotina</i>	Black cherry	Tree																
<i>Quercus</i>	Oak	Tree																
<i>Quercus accutissima</i>	Sawtooth oak	Tree																
<i>Quercus alba</i>	White oak	Tree																
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree	4	4	4	3	3	3	2	2	2				3	3	3	
<i>Quercus pagoda</i>	Cherrybark oak	Tree																
<i>Quercus phellos</i>	Willow oak	Tree	2	2	2				4	4	4				3	3	3	
<i>Quercus rubra</i>	Northern red oak	Tree	2	2	2	2	2	2							2	2	2	
<i>Rhus</i>	Sumac	Shrub																
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub																
<i>Rhus glabra</i>	Smooth sumac	Shrub																
<i>Rhus typhina</i>	Staghorn sumac	Shrub																
<i>Robinia pseudoacacia</i>	Black locust	Tree																
<i>Salix nigra</i>	Black willow	Tree																
<i>Salix sericea</i>	Silky willow	Shrub																
<i>Sambucus canadensis</i>	Common elderberry	Shrub																
<i>Taxodium distichum</i>	Bald cypress	Tree																
<i>Ulmus alata</i>	Winged elm	Tree			1			5						2				7
<i>Ulmus americana</i>	American elm	Tree																
	Stem count		10	10	16	7	7	19	12	12	118	13	13	80	11	11	28	
	Size (ares)			1			1			1			1			1		
	Size (acres)			0.0247			0.0247			0.0247			0.0247			0.0247		
	Species count		4	4	6	4	4	6	3	3	6	3	3	6	5	5	8	
	Stems per acre		405	405	647	283	283	769	486	486	4,775	526	526	3,237	445	445	1,133	

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9b. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

			Current Plot Data (MY7 2021)														
Scientific Name	Common Name	Species Type	Vegetation Plot 6			Vegetation Plot 7			Vegetation Plot 8			Vegetation Plot 9			Vegetation Plot 10		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer negundo L.</i>	Boxelder	Tree															
<i>Acer rubrum</i>	Red maple	Tree															
<i>Alnus serrulata</i>	Hazel alder	Shrub															
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub															
<i>Betula nigra</i>	River birch	Tree							3	3	3	2	2	2	1	1	1
<i>Carya</i>	Hickory	Tree															
<i>Cedrus</i>	Cedar	Tree															
<i>Celtis laevigata</i>	Sugarberry	Tree															
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree															
<i>Crataegus</i>	Hawthorn	Tree															
<i>Diospyros virginiana</i>	Common persimmon	Tree			11			4									
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	3	3	3	1	1	1				1	1	12	2	2	5
<i>Gleditsia triacanthos</i>	Honey locust	Tree															
<i>Ilex opaca</i>	American holly	Tree															
<i>Juglans nigra</i>	Black walnut	Tree												1			1
<i>Juniperus</i>	Juniper	Tree						1						3			2
<i>Juniperus communis</i>	Common juniper	Tree															
<i>Juniperus virginiana</i>	Eastern redcedar	Tree															
<i>Liquidambar styraciflua</i>	Sweetgum	Tree			6			4									
<i>Liriodendron tulipifera</i>	Tuliptree	Tree	1	1	5	1	1	1						2	4	4	7
<i>Nyssa biflora</i>	Swamp tupelo	Tree															
<i>Nyssa sylvatica</i>	Blackgum	Tree															
<i>Pinus</i>	Pine	Tree												5			
<i>Pinus palustris</i>	Longleaf pine	Tree															
<i>Pinus rigida</i>	Pitch pine	Tree															
<i>Pinus serotina</i>	Pond pine	Tree															
<i>Pinus taeda</i>	Loblolly pine	Tree															
<i>Pinus virginiana</i>	Virginia pine	Tree															
<i>Platanus occidentalis</i>	American sycamore	Tree	1	1	1	8	8	8	5	5	5	7	7	7	2	2	3
<i>Prunus serotina</i>	Black cherry	Tree															1
<i>Quercus</i>	Oak	Tree															
<i>Quercus acutissima</i>	Sawtooth oak	Tree															
<i>Quercus alba</i>	White Oak	Tree															
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree	4	4	4	3	3	3	1	1	1	1	1	1			
<i>Quercus pagoda</i>	Cherrybark oak	Tree															
<i>Quercus phellos</i>	Willow oak	Tree										1	1	1	1	1	1
<i>Quercus rubra</i>	Northern red oak	Tree							1	1	1	1	1	1	5	5	5
<i>Rhus</i>	Sumac	Shrub															
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub															
<i>Rhus glabra</i>	Smooth sumac	Shrub															
<i>Rhus typhina</i>	Staghorn sumac	Shrub															
<i>Robinia pseudoacacia</i>	Black locust	Tree															
<i>Salix nigra</i>	Black willow	Tree									1						
<i>Salix sericea</i>	Silky willow	Shrub															
<i>Sambucus canadensis</i>	Common elderberry	Shrub															
<i>Taxodium distichum</i>	Bald cypress	Tree															
<i>Ulmus alata</i>	Winged elm	Tree						1									
<i>Ulmus americana</i>	American elm	Tree												9			4
Stem count			9	9	30	13	13	23	10	10	11	13	13	44	15	15	30
Size (ares)			1			1			1			1			1		
Size (acres)			0.0247			0.0247			0.0247			0.0247			0.0247		
Species count			4	4	6	4	4	8	4	4	5	6	6	11	6	6	10
Stems per acre			364	364	1,214	526	526	931	405	405	445	526	526	1,781	607	607	1,214

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9c. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

			Current Plot Data (MY7 2021)														
Scientific Name	Common Name	Species Type	Vegetation Plot 11			Vegetation Plot 12			Vegetation Plot 13			Vegetation Plot 14			Vegetation Plot 15		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer negundo</i> L.	Boxelder	Tree															
<i>Acer rubrum</i>	Red maple	Tree															
<i>Alnus serrulata</i>	Hazel alder	Shrub															
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub															
<i>Betula nigra</i>	River birch	Tree	3	3	3	2	2	2				1	1	1	1	1	1
<i>Carya</i>	Hickory	Tree															
<i>Cedrus</i>	Cedar	Tree															
<i>Celtis laevigata</i>	Sugarberry	Tree															
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree															
<i>Crataegus</i>	Hawthorn	Tree															
<i>Diospyros virginiana</i>	Common persimmon	Tree						1			7						15
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	3	3	3	3	3	3	2	2	3	1	1	1	2	2	3
<i>Gleditsia triacanthos</i>	Honey locust	Tree															
<i>Ilex opaca</i>	American holly	Tree											1				
<i>Juglans nigra</i>	Black walnut	Tree			1			2									
<i>Juniperus</i>	Juniper	Tree															
<i>Juniperus communis</i>	Common juniper	Tree															
<i>Juniperus virginiana</i>	Eastern redcedar	Tree															
<i>Liquidambar styraciflua</i>	Sweetgum	Tree			1			1						1			5
<i>Liriodendron tulipifera</i>	Tuliptree	Tree			1	2	2	3			1	3	3	46			1
<i>Nyssa biflora</i>	Swamp tupelo	Tree															
<i>Nyssa sylvatica</i>	Blackgum	Tree															
<i>Pinus</i>	Pine	Tree			1									1			
<i>Pinus palustris</i>	Longleaf pine	Tree															
<i>Pinus rigida</i>	Pitch pine	Tree															
<i>Pinus serotina</i>	Pond pine	Tree															
<i>Pinus taeda</i>	Loblolly pine	Tree															
<i>Pinus virginiana</i>	Virginia pine	Tree															
<i>Platanus occidentalis</i>	American sycamore	Tree	1	1	1	4	4	4	9	9	12			3	9	9	9
<i>Prunus serotina</i>	Black cherry	Tree												3			
<i>Quercus</i>	Oak	Tree															
<i>Quercus acutissima</i>	Sawtooth oak	Tree															
<i>Quercus alba</i>	White Oak	Tree															
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree	2	2	2	1	1	1				4	4	4	1	1	1
<i>Quercus pagoda</i>	Cherrybark oak	Tree															
<i>Quercus phellos</i>	Willow oak	Tree										1	1	1			
<i>Quercus rubra</i>	Northern red oak	Tree				1	1	1	1	1	1	1	1	2	2	2	2
<i>Rhus</i>	Sumac	Shrub															
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub															
<i>Rhus glabra</i>	Smooth sumac	Shrub															
<i>Rhus typhina</i>	Staghorn sumac	Shrub															
<i>Robinia pseudoacacia</i>	Black locust	Tree															
<i>Salix nigra</i>	Black willow	Tree															
<i>Salix sericea</i>	Silky willow	Shrub															
<i>Sambucus canadensis</i>	Common elderberry	Shrub															
<i>Taxodium distichum</i>	Bald cypress	Tree															
<i>Ulmus alata</i>	Winged elm	Tree						5									
<i>Ulmus americana</i>	American elm	Tree															
Stem count			9	9	13	13	13	23	12	12	24	11	11	64	15	15	37
Size (ares)			1			1			1			1			1		
Size (acres)			0.0247			0.0247			0.0247			0.0247			0.0247		
Species count			4	4	8	6	6	10	3	3	5	6	6	11	5	5	8
Stems per acre			364	364	526	526	526	931	486	486	971	445	445	2,590	607	607	1,497

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9d. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

			Current Plot Data (MY7 2021)														
Scientific Name	Common Name	Species Type	Vegetation Plot 16			Vegetation Plot 17			Vegetation Plot 18			Vegetation Plot 19			Vegetation Plot 20		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer negundo L.</i>	Boxelder	Tree															
<i>Acer rubrum</i>	Red maple	Tree															
<i>Alnus serrulata</i>	Hazel alder	Shrub															
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub															
<i>Betula nigra</i>	River birch	Tree	1	1	1	3	3	3	2	2	2	1	1	1	4	4	4
<i>Carya</i>	Hickory	Tree															
<i>Cedrus</i>	Cedar	Tree															
<i>Celtis laevigata</i>	Sugarberry	Tree															
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree															
<i>Crataegus</i>	Hawthorn	Tree															
<i>Diospyros virginiana</i>	Common persimmon	Tree									1						
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	4	4	4	4	4	4	2	2	2	5	5	6	5	5	12
<i>Gleditsia triacanthos</i>	Honey locust	Tree									1						
<i>Ilex opaca</i>	American holly	Tree															
<i>Juglans nigra</i>	Black walnut	Tree			1						3						
<i>Juniperus</i>	Juniper	Tree															
<i>Juniperus communis</i>	Common juniper	Tree						2									
<i>Juniperus virginiana</i>	Eastern redcedar	Tree															1
<i>Liquidambar styraciflua</i>	Sweetgum	Tree						300			116			5			2
<i>Liriodendron tulipifera</i>	Tuliptree	Tree				1	1	13									
<i>Nyssa biflora</i>	Swamp tupelo	Tree															
<i>Nyssa sylvatica</i>	Blackgum	Tree															
<i>Pinus</i>	Pine	Tree															
<i>Pinus palustris</i>	Longleaf pine	Tree															
<i>Pinus rigida</i>	Pitch pine	Tree															
<i>Pinus serotina</i>	Pond pine	Tree															
<i>Pinus taeda</i>	Loblolly pine	Tree															
<i>Pinus virginiana</i>	Virginia pine	Tree															
<i>Platanus occidentalis</i>	American sycamore	Tree	6	6	6	4	4	9	2	2	2	4	4	4	1	1	1
<i>Prunus serotina</i>	Black cherry	Tree															
<i>Quercus</i>	Oak	Tree															
<i>Quercus acutissima</i>	Sawtooth oak	Tree															
<i>Quercus alba</i>	White Oak	Tree												1			1
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree	2	2	2	1	1	1									
<i>Quercus pagoda</i>	Cherrybark oak	Tree															
<i>Quercus phellos</i>	Willow oak	Tree															2
<i>Quercus rubra</i>	Northern red oak	Tree				1	1	1	1	1	1				4	4	4
<i>Rhus</i>	Sumac	Shrub															
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub															
<i>Rhus glabra</i>	Smooth sumac	Shrub															
<i>Rhus typhina</i>	Staghorn sumac	Shrub															
<i>Robinia pseudoacacia</i>	Black locust	Tree															
<i>Salix nigra</i>	Black willow	Tree															
<i>Salix sericea</i>	Silky willow	Shrub															
<i>Sambucus canadensis</i>	Common elderberry	Shrub															
<i>Taxodium distichum</i>	Bald cypress	Tree															
<i>Ulmus alata</i>	Winged elm	Tree												2			4
<i>Ulmus americana</i>	American elm	Tree															
Stem count			13	13	14	14	14	333	7	7	128	10	10	19	14	14	31
Size (ares)			1			1			1			1			1		
Size (acres)			0.0247			0.0247			0.0247			0.0247			0.0247		
Species count			4	4	5	6	6	8	4	4	8	3	3	6	4	4	9
Stems per acre			526	526	567	567	567	13,476	283	283	5,180	405	405	769	567	567	1,255

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%
- Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9e. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

			Current Plot Data (MY7 2021)														
Scientific Name	Common Name	Species Type	Vegetation Plot 21			Vegetation Plot 22			Vegetation Plot 23			Vegetation Plot 24			Vegetation Plot 25		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer negundo</i> L.	Boxelder	Tree															
<i>Acer rubrum</i>	Red maple	Tree															
<i>Alnus serrulata</i>	Hazel alder	Shrub															
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub															
<i>Betula nigra</i>	River birch	Tree	1	1	1	2	2	2	1	1	1				1	1	1
<i>Carya</i>	Hickory	Tree															
<i>Cedrus</i>	Cedar	Tree															
<i>Celtis laevigata</i>	Sugarberry	Tree															
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree															
<i>Crataegus</i>	Hawthorn	Tree															
<i>Diospyros virginiana</i>	Common persimmon	Tree			1			5									1
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	1	1	1	3	3	3			4	1	1	2	1	1	1
<i>Gleditsia triacanthos</i>	Honey locust	Tree															
<i>Ilex opaca</i>	American holly	Tree															
<i>Juglans nigra</i>	Black walnut	Tree															
<i>Juniperus</i>	Juniper	Tree															
<i>Juniperus communis</i>	Common juniper	Tree															
<i>Juniperus virginiana</i>	Eastern redcedar	Tree						5									
<i>Liquidambar styraciflua</i>	Sweetgum	Tree			8			4					1				1
<i>Liriodendron tulipifera</i>	Tuliptree	Tree	1	1	2			1					1				
<i>Nyssa biflora</i>	Swamp tupelo	Tree															
<i>Nyssa sylvatica</i>	Blackgum	Tree															
<i>Pinus</i>	Pine	Tree															
<i>Pinus palustris</i>	Longleaf pine	Tree															
<i>Pinus rigida</i>	Pitch pine	Tree															
<i>Pinus serotina</i>	Pond pine	Tree															
<i>Pinus taeda</i>	Loblolly pine	Tree															
<i>Pinus virginiana</i>	Virginia pine	Tree															
<i>Platanus occidentalis</i>	American sycamore	Tree	2	2	2	1	1	1	7	7	7	4	4	7	4	4	10
<i>Prunus serotina</i>	Black cherry	Tree															
<i>Quercus</i>	Oak	Tree															
<i>Quercus accutissima</i>	Sawtooth oak	Tree															
<i>Quercus alba</i>	White Oak	Tree															
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree			1	3	3	3									
<i>Quercus pagoda</i>	Cherrybark oak	Tree						3									
<i>Quercus phellos</i>	Willow oak	Tree	2	2	2												
<i>Quercus rubra</i>	Northern red oak	Tree	3	3	3							1	1	1	1	1	1
<i>Rhus</i>	Sumac	Shrub															
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub															
<i>Rhus glabra</i>	Smooth sumac	Shrub															
<i>Rhus typhina</i>	Staghorn sumac	Shrub															
<i>Robinia pseudoacacia</i>	Black locust	Tree															
<i>Salix nigra</i>	Black willow	Tree															
<i>Salix sericea</i>	Silky willow	Shrub															
<i>Sambucus canadensis</i>	Common elderberry	Shrub															
<i>Taxodium distichum</i>	Bald cypress	Tree															
<i>Ulmus alata</i>	Winged elm	Tree			6			8			3						
<i>Ulmus americana</i>	American elm	Tree															
Stem count			10	10	27	9	9	35	8	8	15	6	6	12	7	7	15
Size (ares)			1			1			1			1			1		
Size (acres)			0.0247			0.0247			0.0247			0.0247			0.0247		
Species count			6	6	10	4	4	10	2	2	4	3	3	5	4	4	6
Stems per acre			405	405	1,093	364	364	1,416	324	324	607	243	243	486	283	283	607

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9f. Planted and Total Stems (Species by Plot with Annual Means)

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Scientific Name	Common Name	Species Type	Current Plot Data (MY7 2021)																	
			Vegetation Plot 26			Vegetation Plot 27			Vegetation Plot 28			Vegetation Plot 29			Vegetation Plot 30			Vegetation Plot 31		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer negundo L.</i>	Boxelder	Tree																		
<i>Acer rubrum</i>	Red maple	Tree																		
<i>Alnus serrulata</i>	Hazel alder	Shrub																		
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub																		
<i>Betula nigra</i>	River birch	Tree	1	1	1							2	2	2	1	1	2			
<i>Carya</i>	Hickory	Tree																		
<i>Cedrus</i>	Cedar	Tree																		
<i>Celtis laevigata</i>	Sugarberry	Tree																1	1	
<i>Chamaecyparis thyoides</i>	Atlantic white cedar	Tree																	1	
<i>Crataegus</i>	Hawthorn	Tree																		
<i>Diospyros virginiana</i>	Common persimmon	Tree																		
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	2	2	2	4	4	9	4	4	4	2	2	2	4	4	4	5	5	
<i>Gleditsia triacanthos</i>	Honey locust	Tree																		
<i>Ilex opaca</i>	American holly	Tree																		
<i>Juglans nigra</i>	Black walnut	Tree															7		3	
<i>Juniperus</i>	Juniper	Tree																		
<i>Juniperus communis</i>	Common juniper	Tree																		
<i>Juniperus virginiana</i>	Eastern redcedar	Tree															1			
<i>Liquidambar styraciflua</i>	Sweetgum	Tree						1						11			1			
<i>Liriodendron tulipifera</i>	Tuliptree	Tree				1	1	1			1	1	1	4			3		12	
<i>Nyssa biflora</i>	Swamp tupelo	Tree									1	1	1				1	1	2	
<i>Nyssa sylvatica</i>	Blackgum	Tree																		
<i>Pinus</i>	Pine	Tree																		
<i>Pinus palustris</i>	Longleaf pine	Tree																		
<i>Pinus rigida</i>	Pitch pine	Tree																		
<i>Pinus serotina</i>	Pond pine	Tree																		
<i>Pinus taeda</i>	Loblolly pine	Tree																		
<i>Pinus virginiana</i>	Virginia pine	Tree																		
<i>Platanus occidentalis</i>	American sycamore	Tree	1	1	1	4	4	4	4	4	4	1	1	12					1	
<i>Prunus serotina</i>	Black cherry	Tree																		
<i>Quercus</i>	Oak	Tree																		
<i>Quercus acutissima</i>	Sawtooth oak	Tree																		
<i>Quercus alba</i>	White Oak	Tree																		
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree				3	3	3												
<i>Quercus pagoda</i>	Cherrybark oak	Tree																		
<i>Quercus phellos</i>	Willow oak	Tree	1	1	1	1	1	1				1	1	1			1			
<i>Quercus rubra</i>	Northern red oak	Tree	1	1	1							2	2	2	4	4	5	3	6	
<i>Rhus</i>	Sumac	Shrub																		
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub																		
<i>Rhus glabra</i>	Smooth sumac	Shrub																		
<i>Rhus typhina</i>	Staghorn sumac	Shrub																		
<i>Robinia pseudoacacia</i>	Black locust	Tree																		
<i>Salix nigra</i>	Black willow	Tree																		
<i>Salix sericea</i>	Silky willow	Shrub																		
<i>Sambucus canadensis</i>	Common elderberry	Shrub																		
<i>Taxodium distichum</i>	Bald cypress	Tree																		
<i>Ulmus alata</i>	Winged elm	Tree																		
<i>Ulmus americana</i>	American elm	Tree																		
	Stem count		6	6	6	13	13	19	8	8	9	9	9	34	9	9	24	10	30	
	Size (ares)		1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	
	Size (acres)		0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	0.0247	
	Species count		5	5	5	5	5	6	2	2	3	6	6	7	3	3	8	4	7	
	Stems per acre		243	243	243	526	526	769	324	324	364	364	364	1,376	364	364	971	405	1,214	

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

PnoLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Table 9g. Planted and Total Stems (Species by Plot with Annual Means)
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Scientific Name	Common Name	Species Type	Annual Means																							
			MY7 (2021)			MY6 (2020)			MY5 (2019)			MY4 (2018)			MY3 (2017)			MY2 (2016)			MY1 (2015)			MY0 (2015)		
			P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T	P-noLS	P-all	T
<i>Acer negundo</i>	Boxelder	Tree			10			55						1												
<i>Acer rubrum</i>	Red maple	Tree					15			27			50			45						2				
<i>Alnus serrulata</i>	Hazel alder	Shrub					1								1				1							
<i>Baccharis angustifolia</i>	Saltwater false willow	Shrub					3																			
<i>Betula nigra</i>	River birch	Tree	35	35	36	34	34	36	34	34	38	38	38	46	37	37	47	37	37	42	44	44	51	53	53	
<i>Carya</i>	Hickory	Tree																					1			
<i>Cedrus</i>	Cedar	Tree																								
<i>Celtis laevigata</i>	Sugarberry	Tree	1	1	1	1	1	1	1	1	1	1	1	1	1	2	1	1	1							
<i>Chamaecyparis thuyoides</i>	Atlantic white cedar	Tree																					1			
<i>Crataegus</i>	Hawthorn	Tree																								
<i>Diospyros virginiana</i>	Common persimmon	Tree			46			36			65			74			93					51				
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	76	76	110	76	76	127	79	79	139	80	80	174	79	79	113	86	86	133	85	85	116	92	92	
<i>Ilex opaca</i>	American holly	Tree			1																					
<i>Gleditsia triacanthos</i>	Honey locust	Tree			1			4																		
<i>Juglans nigra</i>	Black walnut	Tree			19			14			18			13			13			14						
<i>Juniperus</i>	Juniper	Tree			6																					
<i>Juniperus communis</i>	Common juniper	Tree			2																					
<i>Juniperus virginiana</i>	Eastern redcedar	Tree			7			4			3						4					1				
<i>Liquidambar styraciflua</i>	Sweetgum	Tree			622			878			1192			500			565			261			102			
<i>Liriodendron tulipifera</i>	Tuliptree	Tree	17	17	96	17	17	122	17	17	124	17	17	78	17	17	98	24	24	64	24	24	28	52	52	
<i>Nyssa biflora</i>	Swamp tupelo	Tree						3																		
<i>Nyssa sylvatica</i>	Blackgum	Tree												2			2			1						
<i>Pinus</i>	Pine	Tree			36									24			25									
<i>Pinus palustris</i>	Longleaf pine	Tree									12															
<i>Pinus rigida</i>	Pitch pine	Tree												22			25									
<i>Pinus serotina</i>	Pond pine	Tree						3											1							
<i>Pinus taeda</i>	Loblolly pine	Tree						18			52															
<i>Pinus virginiana</i>	Virginia pine	Tree									3			1												
<i>Platanus occidentalis</i>	American sycamore	Tree	103	103	148	103	103	139	102	102	174	103	103	186	105	105	133	110	110	146	108	108	115	114	114	
<i>Prunus serotina</i>	Black cherry	Tree			4						7									4						
<i>Quercus</i>	Oak	Tree															5			2						
<i>Quercus acutissima</i>	Sawtooth oak	Tree									5															
<i>Quercus alba</i>	White Oak	Tree			2									2												
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree	38	38	39	38	38	38	39	39	39	39	39	39	42	42	42	45	45	45	45	45	45	46	46	
<i>Quercus pagoda</i>	Cherrybark oak	Tree			3																					
<i>Quercus phellos</i>	Willow oak	Tree	17	17	20	16	16	20	15	15	16	17	17	17	20	20	20	34	34	34	36	36	36	71	71	
<i>Quercus rubra</i>	Northern red oak	Tree	39	39	44	40	40	41	44	44	44	48	48	49	52	52	55	58	58	61	60	60	62	69	69	
<i>Rhus</i>	Sumac	Shrub						3																		
<i>Rhus copallinum</i>	Flameleaf sumac	Shrub						1																		
<i>Rhus glabra</i>	Smooth sumac	Shrub												4			7									
<i>Rhus typhina</i>	Staghorn sumac	Shrub												2						1						
<i>Rabinoa pseudoacacia</i>	Black locust	Tree												2												
<i>Salix nigra</i>	Black willow	Tree			1									1												
<i>Salix sericea</i>	Silky willow	Shrub									1						1									
<i>Sambucus canadensis</i>	Common Elderberry	Shrub									2			4					3							
<i>Taxodium distichum</i>	Bald cypress	Tree									17															
<i>Ulmus alata</i>	Winged elm	Tree			44			27			47			33			4						1			
<i>Ulmus americana</i>	American elm	Tree			12			81			1															
Stem count			326	326	1,310	325	325	1,670	331	331	2,034	343	343	1,319	353	353	1,301	395	395	896	402	402	612	497	497	
Size (acres)				0.77			0.77			0.77			0.77			0.77			0.77			0.77			0.77	
Species count			8	8	24	8	8	24	8	8	20	8	8	21	8	8	22	8	8	18	7	7	14	7	7	
Stems per acre			426	426	1,711	424	424	2,181	432	447	2,656	448	448	1,723	461	461	1,699	516	516	1,170	525	525	799	649	649	

Exceeds requirements by 10%
 Exceeds requirements, but by less than 10%
 Fails to meet requirements, by less than 10%
 Fails to meet requirements by more than 10%
 Volunteers included

P-noLS: Number of planted stems excluding live stakes
 P-All: Number of planted stems including live stakes
 T: Total stems

Stems Per Plot Across All Years

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Plot	2021			2020			2019			2018			2017			2016			2015		
	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC	Planted Stems	Total Stems	Total Stems/AC
1	10	16	647	10	19	769	10	19	769	11	40	1,619	10	13	526	11	17	688	11	11	445
2	7	19	769	7	11	445	7	18	728	10	25	1,012	11	16	647	12	13	526	13	13	526
3	12	118	4,775	12	376	15,216	12	132	5,342	11	126	5,099	13	184	7,446	13	63	2,550	14	14	567
4	13	80	3,237	13	351	14,204	13	145	5,868	13	127	5,140	13	86	3,480	14	14	567	14	14	567
5	11	28	1,133	11	117	4,735	11	29	1,174	11	21	850	11	34	1,376	13	14	567	13	13	526
6	9	30	1,214	9	53	2,145	9	48	1,942	9	16	647	11	63	2,550	14	37	1,497	15	15	607
7	13	23	931	13	20	809	13	20	809	14	15	607	14	17	688	15	20	809	15	15	607
8	10	11	445	10	12	486	10	12	486	10	13	526	11	13	526	13	17	688	13	13	526
9	13	44	1,781	13	30	1,214	13	51	2,064	13	56	2,266	14	14	567	14	14	567	13	13	526
10	15	30	1,214	15	17	688	15	28	1,133	15	33	1,335	15	18	728	15	18	728	15	15	607
11	9	13	526	9	12	486	9	10	405	9	15	607	10	13	526	12	12	486	13	13	526
12	13	23	931	13	19	769	13	21	850	14	32	1,295	14	20	809	14	17	688	14	14	567
13	12	24	971	12	26	1,052	12	24	971	12	41	1,659	12	44	1,781	12	46	1,862	12	12	486
14	11	64	2,590	11	58	2,347	11	31	1,255	12	33	1,335	13	29	1,174	14	22	890	14	14	567
15	15	37	1,497	15	44	1,781	15	45	1,821	15	51	2,064	15	30	1,214	15	31	1,255	15	15	607
16	13	14	567	13	13	526	13	14	567	13	14	567	13	14	567	14	14	567	13	13	526
17	14	333	13,476	14	69	2,792	14	174	7,042	14	103	4,168	15	95	3,845	15	115	4,654	15	15	607
18	7	128	5,180	7	34	1,376	7	38	1,538	8	55	2,226	9	63	2,550	13	41	1,659	13	13	526
19	10	19	769	10	21	850	10	23	931	10	38	1,538	11	20	809	12	31	1,255	12	12	486
20	14	31	1,255	14	49	1,983	14	45	1,821	14	26	1,052	14	31	1,255	15	15	607	15	15	607
21	10	27	1,093	10	31	1,255	11	41	1,659	12	43	1,740	12	27	1,093	12	12	486	12	12	486
22	9	35	1,416	9	21	850	9	25	1,012	9	33	1,335	9	31	1,255	11	29	1,174	11	11	445
23	8	15	607	8	45	1,821	9	36	1,457	10	49	1,983	10	52	2,104	14	58	2,347	15	15	607
24	6	12	486	6	14	567	7	12	486	7	16	647	6	10	405	10	20	809	13	13	526
25	7	15	607	7	13	526	8	13	526	8	16	647	8	10	405	10	17	688	12	12	486
26	6	6	243	7	8	324	8	10	405	8	10	405	8	8	324	10	10	405	11	11	445
27	13	19	769	13	22	890	13	27	1,093	13	35	1,416	13	17	688	13	17	688	13	13	526
28	8	9	364	8	8	324	9	10	405	9	10	405	10	10	405	12	12	486	13	13	526
29	7	32	1,295	7	46	1,862	7	95	3,845	9	75	3,035	10	82	3,318	11	32	1,295	11	11	445
30	9	24	971	9	74	2,995	9	614	24,848	10	95	3,845	9	166	6,718	10	65	2,630	9	9	364
31	10	30	1,214	10	37	1,497	10	218	8,822	10	57	2,307	9	71	2,873	12	53	2,145	11	11	445

APPENDIX 4. Morphological Summary Data and Plots

Table 10a. Baseline Stream Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2 Reaches 1 and 2

Parameter	Gage	Pre-Restoration Condition				Reference Reach Data						Design				As-Built/Baseline							
		UT2 Reach 1		UT2 Reach 2		Dutchman's Creek		UT to Rocky Creek		Spencer Creek Reach 1		Spencer Creek Reach 2		Spencer Creek Reach 3		UT2 Reach 1		UT2 Reach 2		UT2 Reach 1		UT2 Reach 2	
		Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																							
Bankfull Width (ft)	N/A	7.9	10.9	10.7	23.0	32.0	12.2	8.7	2.1	2.6	1.0	1.2	12.5	14.0	10.6	14.2	15.3						
Floodprone Width (ft)		12	18	14	61	69	72	229	60	>114	14	125	50	125	50	125	>68	101	>55				
Bankfull Mean Depth		1.0	1.4	1.4	1.1	1.4	1.3	1.2	1.6	1.8	0.8	1.0	1.0	1.0	0.8	0.9	1.0						
Bankfull Max Depth		1.4	1.8	2.0	1.9	2.1	1.8	1.9	2.1	2.6	1.0	1.2	1.5	1.5	1.3	1.7	1.5						
Bankfull Cross-sectional Area (ft ²)		11.1	11.4	14.9	32.9	36.1	16.3	10.6	17.8	19.7	6.6	8.7	12.0	14.3	8.4	12.7	14.8						
Width/Depth Ratio		5.7	10.4	7.7	16.4	28.9	9.1	7.3	5.8	7.1	7.9	9.3	13.0	14.0	13.2	15.8	15.8						
Entrenchment Ratio		1.5	1.7	1.3	2.2	2.6	6.0	26.3	5.5	10.2	1.7	4.3	4.0	10.0	3.6	8.9	>7	7.1	>4				
Bank Height Ratio		1.4	1.9	2.1	---	---	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.0						
D50 (mm)		0.100		12.5											24.2	28.0	45.8						
Pattern																							
Riffle Length (ft)	N/A				---	---	---	---	---	---	---	---	---	---	11	120	24	36					
Riffle Slope (ft/ft)		---	---	---	---	---	0.0606	0.0892	0.01	0.067	0.013	0.0184	0.0343	0.0105	0.0225	0.0154	0.033	0.0033	0.0227	0.0104	0.0386		
Pool Length (ft)					---	---	---	---	---	---	---	---	---	---	17	66	41	105					
Pool Max Depth (ft)		2.0	2.2	2.2	---	---	2.2	6.7	2.5	3.3	1.2	1.8	1.8	2.4	1.9	2.5	1.7	3.6	3.2	5.0			
Pool Spacing (ft)		---	---	---	---	---	26	81	13	47	71	9	46	19	81	21	91	20	108	65	132		
Pool Volume (ft ³)																							
Substrate, Bed and Transport Parameters																							
Channel Beltwidth (ft)	N/A	45	79	67	69	84	---	24	52	38	41	10	50	20	75	22	84	5	11	32	79		
Radius of Curvature (ft)		12	28	22	25	---	---	5	22	11	15	12	85	23	38	25	42	13	35	21	24		
Rc:Bankfull Width (ft/ft)		1.5	2.6	2.1	2.3	---	---	0.6	2.5	1.3	1.4	1.9	9.1	1.8	3.0	1.8	3	1.2	2.5	1.4	1.6		
Meander Length (ft)		102	245	125	132	---	---	---	---	---	---	53	178	50	188	56	120	60	171	113	120		
Meander Width Ratio		5.7	7.2	6.3	6.4	---	---	6.0	6.0	#DIV/0!	3.6	1.6	5.4	1.6	6.0	1.6	6.0	0.5	0.8	2.1	5.2		
Additional Reach Parameters																							
Drainage Area (SM)	N/A	0.38	0.59	2.90	1.10	0.50	0.96	0.37	0.38	0.59	0.38	0.59	0.38	0.59	0.38	0.59	0.38	0.59	0.38	0.59	0.38	0.59	
Watershed Impervious Cover Estimate (%)		1%	1%	---	---	---	---	---	1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	1%	
Rosgen Classification		G5/4	G4	B/C	E4b	E4/C4	E4	E4	C4	C4	C4	C4	C4	C4	C4	C4	C4	C4	C4	C4	C4	C4	
Bankfull Velocity (fps)		3.7	4.0	3.9	---	5.5	---	4.9	5.4	5.6	3.1	3.9	2.7	3.0	3.8								
Bankfull Discharge (cfs)		45	58	203	85	---	97	35	40	54	23	38	56										
Q-NFF regression (2-yr)		85	112	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-USGS extrapolation (1.2-yr)		46	62	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Q-Mannings		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Valley Length (ft)		1,465	428	---	---	---	---	---	1,465	428	1,465	428	1,465	428	1,465	428	1,465	428	1,465	428	1,465	428	
Channel Thalweg Length (ft)		1,527	704	---	---	---	---	---	1,715	732	1,787	529	---	---	---	---	---	---	---	---	---	---	
Sinuosity		1.3	1.1	---	1.1	1.1	1.3	1.0	1.3	1.0	1.2	1.0	1.2	1.0	1.2	1.0	1.2	1.2	1.2	1.2	1.2	1.2	
Water Surface Slope (ft/ft) ²		---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	
Bankfull Slope (ft/ft) ²		0.0083	0.0082	0.019	0.0235	0.132	0.0047	0.019	0.022	0.0083	0.0108	0.0085	0.0086	0.0103	0.0107								

SC: Silt/Clay <0.062 mm diameter particles

(---): Data was not provided

N/A: Not Applicable

Table 10b. Baseline Stream Data Summary

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Hopewell-UT2A Reaches 1 and 2

Parameter	Gage	Pre-Restoration Condition				Reference Reach Data	Design				As-Built/Baseline					
		UT2A Reach 1		UT2A Reach 2			UT2A Reach 1		UT2A Reach 2		UT2A Reach 1		UT2A Reach 2			
		Min	Max	Min	Max		Min	Max	Min	Max	Min	Max	Min	Max		
Dimension and Substrate - Riffle																
Bankfull Width (ft)	N/A	6.2	6.0	7.9	See Table 10a.	9.0	10.0	10.3	9.8	10.9						
Floodprone Width (ft)		40	6	10		50	125	50	125	>87	63	>88				
Bankfull Mean Depth		1.0	0.8	1.0		0.6	0.7	0.8	0.7	0.8	0.7					
Bankfull Max Depth		2.0	1.1	1.5		0.9	0.8	1.1	1.1	1.6	1.1	1.2				
Bankfull Cross-sectional Area (ft ²)		6.2	6.1	6.2		5.7	7.0	8.0	7.0	8.0	6.8	8.0				
Width/Depth Ratio		6.2	5.9	10.0		14.0	14.0	13.3	14.0	13.3	14.0	14.9				
Entrenchment Ratio		6.5	0.8	1.7		5.6	13.9	5	12.5	>8	5.7	>9				
Bank Height Ratio		1.4	2.3	2.9		1.0	1.0	1.0	1.0	1.0	1.0					
D50 (mm)		0.1	0.1							30.9	34.3	39.8				
Profile																
Riffle Length (ft)	N/A				See Table 10a.	---	---	18	54	10	67					
Riffle Slope (ft/ft)		---	---	---		0.119	0.0255	0.013	0.028	0.0032	0.0210	0.0034	0.0330			
Pool Length (ft)						---	---	18	54	14	55					
Pool Max Depth (ft)		2.3	1.9	2.7		1.2	1.5	1.4	1.7	1.4	2.9	1.5	4.1			
Pool Spacing (ft)		---	---	---		14	59	15	65	40	67	27	88			
Pool Volume (ft ³)																
Pattern																
Channel Beltwidth (ft)	N/A	18	22	26	72	See Table 10a.	14	54	16	60	20	38	15	42		
Radius of Curvature (ft)		8	31	6	28		16	27	18	30	16	25	18	30		
Rc:Bankfull Width (ft/ft)		1.3	5.0	1.0	3.5		1.8	3.0	1.8	3.0	0.5	2.4	1.8	2.8		
Meander Length (ft)		54	61	102	173		36	135	40	150	76	116	64	147		
Meander Width Ratio		2.9	3.6	4.3	9.1		1.6	6.0	1.6	6.0	1.9	3.7	1.5	3.9		
Substrate, Bed and Transport Parameters																
Ri%/Ru%/P%/G%/S%	N/A				See Table 10a.											
SC%/Sa%/G%/C%/B%/Be%																
d16/d35/d50/d84/d95/d100		SC/SC/0.1/3/7	SC/SC/0.1/3/7							SC/2/18/57/87/180	SC/2/18/57/87/180					
Reach Shear Stress (Competency) lb/ft ²		---	---				0.3	0.36		0.25	0.44	0.45				
Max part size (mm) mobilized at bankfull																
Stream Power (Capacity) W/m ²																
Additional Reach Parameters																
Drainage Area (SM)	N/A	0.10	0.16		See Table 10a.	0.10	0.16	0.10	0.16							
Watershed Impervious Cover Estimate (%)		<1%	<1%			<1%	<1%	<1%	<1%	<1%	<1%					
Rosgen Classification		E/G5/4	E/G5/4			C4	C4	C4	C4							
Bankfull Velocity (fps)		3.0	2.7	3.1		2.6	3.0	2.2	2.8							
Bankfull Discharge (cfs)		19	19			15	21	18	19	25						
Q-NFF regression (2-yr)		35	48													
Q-USGS extrapolation (1.2-yr)		18	25													
Q-Mannings		---	---													
Valley Length (ft)		283	1,198			283	1,198	283	1,198							
Channel Thalweg Length (ft)		368	1,368			386	1,311	386	1,443							
Sinuosity		1.3	1.2			1.0	1.2	1.3	1.2							
Water Surface Slope (ft/ft) ²		---	---			---	---	0.006	0.0108							
Bankfull Slope (ft/ft)		0.0082	0.0086			0.0102	0.0110	0.0084	0.0092	0.0107	0.0109					

SC: Silt/Clay <0.062 mm diameter particles
 (---): Data was not provided
 N/A: Not Applicable

Table 10c. Baseline Stream Data Summary

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Hopewell-UT2B Reach 2 and UT2C Reaches 2 and 3

Parameter	Gage	Pre-Restoration Condition				Reference Reach Data See Table 10a.	Design				As-Built/Baseline			
		UT2B		UT2C			UT2B Reach 2		UT2C Reach 2 & 3		UT2B Reach 2		UT2C Reach 2 & 3	
		Min	Max	Min	Max		Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle														
Bankfull Width (ft)	N/A	3.4	5.1	4.2	6.4	See Table 10a.	5.0		7.8		5.2		9.9	
Floodprone Width (ft)		4	8	7	53		50	125	50	125	>41	>48		
Bankfull Mean Depth		0.4	0.6	0.6	0.9		0.4	0.6		0.4	0.5			
Bankfull Max Depth		0.7	1.0	0.9	1.4		0.5	0.6	0.7	0.8	0.6		1.1	
Bankfull Cross-sectional Area (ft ²)		2.2	2.3	3.8	4.2		2.1		4.3		2.1		5.3	
Width/Depth Ratio		5.5	11.3	4.6	9.6		12.0		14.0		13.0		18.4	
Entrenchment Ratio		1.2	1.6	1.2	2.6		10.0	25.0	6.4	16.0	>8		>5	
Bank Height Ratio		1.7	4.0	1.0	3.4		1.0		1.0		1.0		1.0	
D50 (mm)		2.1		6.0							25.4		18.4	
Profile														
Riffle Length (ft)	N/A					See Table 10a.	---		---		7	25	6	20
Riffle Slope (ft/ft)		---		---			0.03	0.065	0.0180	0.0380	0.0146	0.0441	0.0051	0.0584
Pool Length (ft)		---		---			---		---		10	21	3	25
Pool Max Depth (ft)		---		1.1	1.2		0.6	1.0	1.1	1.5	1.3	2.8	2.2	3.7
Pool Spacing (ft)		---		---			8	33	12	51	19	36	23	36
Pool Volume (ft ³)		---		---										
Pattern														
Channel Beltwidth (ft)	N/A	25	32	33	46	See Table 10a.	8	30	12	47	8	19	10	25
Radius of Curvature (ft)		20		6	20		9	15	14	23	9	15	14	15
Rc:Bankfull Width (ft/ft)		2.9	3.9	1.4	3.1		1.8	3.0	1.9	3.0	1.7	2.9	1.4	1.5
Meander Length (ft)		23	21	160	165		20	75	31	117	40	62	45	82
Meander Width Ratio		7.4	6.3	7.9	7.2		1.6	6.0	1.6	6.0	1.6	3.6	1.0	2.5
Substrate, Bed and Transport Parameters														
Ri%/Ru%/P%/G%/S%	N/A					See Table 10a.								
SC%/Sa%/G%/C%/B%/Be%														
d16/d35/d50/d84/d95/d100		SC/SC/2.1/18/107		SC/0.8/6/45/78							SC/6/21/55/128/256		SC/SC/9/45/78/128	
Reach Shear Stress (Competency) lb/ft ²		---		---			0.49		0.46	0.72	0.46		0.25	1.11
Max part size (mm) mobilized at bankfull														
Stream Power (Capacity) W/m ²														
Additional Reach Parameters														
Drainage Area (SM)	N/A	0.03		0.08		See Table 10a.	0.03		0.08		0.03		0.08	
Watershed Impervious Cover Estimate (%)		<1%		<1%			<1%		<1%		<1%		<1%	
Rosgen Classification		G4		E/G4			C4		C4		C4b		C4/C4b	
Bankfull Velocity (fps)		3.0	3.2	3.3	3.7		3	2.7	2.7	2.7	2.7		2.1	
Bankfull Discharge (cfs)		7		14			7		13		6		11	
Q-NFF regression (2-yr)		18		31										
Q-USGS extrapolation (1.2-yr)		9		15										
Q-Mannings		---		---										
Valley Length (ft)		183		296			183		229		183		229	
Channel Thalweg Length (ft)		114		326			198		247		198		247	
Sinuosity		1.2		1.1			1.0	1.2	1.0	1.2	1.1		1.1	
Water Surface Slope (ft/ft) ²		---		---			---		---		0.0211		0.0083	0.0365
Bankfull Slope (ft/ft)		0.0250		0.0120			0.0259		0.0154	0.024	0.0207	0.0215	0.0102	0.0459

SC: Silt/Clay <0.062 mm diameter particles

(---): Data was not provided

N/A: Not Applicable

Table 10d. Baseline Stream Data Summary
Hopewell Stream Mitigation Site
DMS Project No. 95352
Monitoring Year 7 - 2021

Hopewell-UT1B Reach 1

Parameter	Gage	Pre-Restoration		Reference Reach Data	Design		As-Built/Baseline	
		UT1B			UT1B Reach 1		UT1B Reach 1	
		Min	Max	See Table 10a.	Min	Max	Min	Max
Dimension and Substrate - Riffle								
Bankfull Width (ft)	N/A	7.1	13.2	See Table 10a.	5.0		4.8	
Floodprone Width (ft)		8	28		10	25	12.4	
Bankfull Mean Depth		0.7	1.1		0.4		0.4	
Bankfull Max Depth		1.2	1.9		0.5		0.6	
Bankfull Cross-sectional Area (ft ²)		8.0	12.0		1.9		1.8	
Width/Depth Ratio		10.1	12.0		13.0		13.3	
Entrenchment Ratio		2.2			10.0	25.0	2.6	
Bank Height Ratio		2.5			1.0		1.0	
D50 (mm)		52.3					56.3	
Profile								
Riffle Length (ft)	N/A			See Table 10a.	---		11	47
Riffle Slope (ft/ft)		---			0.0154	0.033	0.0185	0.0646
Pool Length (ft)					---		20	105
Pool Max Depth (ft)		1.4	2.6		1.9	2.5	1.1	1.6
Pool Spacing (ft)		---			21	91	56	103
Pool Volume (ft ³)								
Pattern								
Channel Beltwidth (ft)	N/A	20	47	See Table 10a.	22	84	---	
Radius of Curvature (ft)		10	84		25	42	---	
Rc:Bankfull Width (ft/ft)		0.9	7.5		1.8	3.0	---	
Meander Length (ft)		68	294		56	210	---	
Meander Width Ratio		1.8	4.2		1.6	6.0	---	
Substrate, Bed and Transport Parameters								
Ri%/Ru%/P%/G%/S%	N/A			See Table 10a.				
SC%/Sa%/G%/C%/B%/Be%								
d16/d35/d50/d84/d95/d100		SC/15.41/52.3/136/172					SC/1/6/128/256/512	
Reach Shear Stress (Competency) lb/ft ²		---			0.61		0.54	
Max part size (mm) mobilized at bankfull								
Stream Power (Capacity) W/m ²								
Additional Reach Parameters								
Drainage Area (SM)	N/A	0.03		See Table 10a.	0.03		0.03	
Watershed Impervious Cover Estimate (%)		<1%			<1%		<1%	
Rosgen Classification		Eb/B4			C4b		C4b	
Bankfull Velocity (fps)		1.7			3.3		2.8	
Bankfull Discharge (cfs)		12			6		5	
Q-NFF regression (2-yr)		15						
Q-USGS extrapolation (1.2-yr)		7						
Q-Mannings		---						
Valley Length (ft)		431			431		431	
Channel Thalweg Length (ft)		475			475		480	
Sinuosity		1.1			1.0	1.2	1.1	
Water Surface Slope (ft/ft) ²		---			---		0.0270	
Bankfull Slope (ft/ft)		0.0369			0.0360		0.0246	0.0260

SC: Silt/Clay <0.062 mm diameter particles

(---): Data was not provided

N/A: Not Applicable

Table 11a. Morphology and Hydraulic Summary (Dimensional Parameters - Cross Section)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Dimension and Substrate	Cross-Section 1, UT2A Reach 1 (Pool)								Cross-Section 2, UT2A Reach 1 (Riffle)							Cross-Section 3, UT2A Reach 2 (Riffle)								
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankfull Elevation (ft)	722.6	722.6	722.6	722.6	722.8	722.8	722.6	722.7	722.4	722.4	722.4	722.4	722.6	722.6	722.6	722.8	719.7	719.7	719.7	719.7	719.7	719.8	719.7	719.7
Low Bank Elevation (ft)	722.6	722.6	722.6	722.6	722.8	722.8	722.6	722.7	722.4	722.4	722.4	722.4	722.6	722.7	722.7	722.9	719.7	719.7	719.7	719.7	719.7	720.0	719.9	720.0
Bankfull Width (ft)	12.1	12.7	12.7	13.1	15.9	14.0	12.8	13.3	10.3	9.7	10.1	10.7	11.9	11.8	11.9	11.1	9.8	10.3	10.2	10.2	10.2	10.4	10.2	11.1
Floodprone Width (ft)	---	---	---	---	---	---	---	---	>87	>88	>88	>88	>87	>87	>87	>87	>88	>87	>92	>75	>89	>93	>93	>95
Bankfull Mean Depth (ft)	1.4	1.3	1.3	1.2	1.0	1.1	1.0	0.9	0.8	0.8	0.8	0.7	0.7	0.7	0.8	0.8	0.7	0.7	0.8	0.5	0.7	0.8	0.8	0.9
Bankfull Max Depth (ft)	2.7	2.5	2.5	2.7	2.4	2.2	1.9	1.8	1.6	1.3	1.4	1.3	1.5	1.6	1.7	1.8	1.1	1.1	1.3	1.0	1.2	1.4	1.4	1.4
Bankfull Cross-Sectional Area (ft ²)	16.8	16.5	16.5	15.1	16.3	15.3	12.7	11.6	8.0	7.6	7.6	7.0	8.0	8.4	9.3	9.2	6.8	6.7	7.7	5.6	6.7	8.0	8.4	9.7
Bankfull Width/Depth Ratio	8.7	9.8	9.8	11.4	15.5	12.8	12.8	15.3	13.3	12.4	13.3	16.3	17.7	16.7	15.3	13.4	14.0	15.8	13.6	18.6	15.4	13.6	12.3	12.7
Bankfull Entrenchment Ratio	---	---	---	---	---	---	---	---	>8	>9	>9	>8	>7	>7	>7	>7	>9	>8	>9	>7	>9	>9	>9	>8
Bankfull Bank Height Ratio ^{1,2}	---	---	---	---	---	---	---	---	1.0	1.0	1.0	1.0	1.0	1.0	1.1	1.1	1.0	1.0	1.0	1.0	1.0	1.1	1.1	1.2
d50 (mm)	---	---	---	---	---	---	---	---	30.9	40.3	27.7	0.3	37.9	11.0	0.3	33.4	39.8	26.3	26.9	43.3	48.3	37.9	33.2	41.6
Dimension and Substrate	Cross-Section 4, UT2A Reach 2 (Pool)								Cross-Section 5, UT2A Reach 2 (Pool)							Cross-Section 6, UT2A Reach 2 (Riffle)								
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankfull Elevation (ft)	719.6	719.6	719.6	719.6	719.6	719.8	719.8	719.9	713.5	713.5	713.5	713.5	713.5	713.4	713.6	713.7	713.4	713.4	713.4	713.4	713.3	713.3	713.4	713.4
Low Bank Elevation (ft)	719.6	719.6	719.6	719.6	719.6	719.8	719.8	719.9	713.5	713.5	713.5	713.5	713.5	713.4	713.6	713.7	713.4	713.4	713.4	713.4	713.3	713.3	713.4	713.4
Bankfull Width (ft)	12.1	12.1	12.7	11.8	12.0	11.9	12.2	11.7	12.7	12.8	12.6	12.6	13.0	11.8	13.4	14.0	10.9	14.0	13.8	10.9	11.3	12.4	10.7	14.2
Floodprone Width (ft)	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	63.0	66.0	69.0	67.0	65.4	66.2	61.3	69.5
Bankfull Mean Depth (ft)	1.4	1.3	1.3	1.3	1.4	1.3	1.3	1.4	1.0	0.9	1.1	1.0	1.0	1.0	1.0	1.0	0.7	0.6	0.7	0.7	0.6	0.6	0.6	0.6
Bankfull Max Depth (ft)	3.0	2.7	2.8	3.1	2.9	2.6	2.6	2.9	1.6	1.7	1.8	1.9	1.9	1.9	2.0	2.2	1.2	1.2	1.4	1.3	1.3	1.3	1.2	1.4
Bankfull Cross-Sectional Area (ft ²)	16.7	15.6	16.7	16.0	16.8	15.6	15.8	16.3	12.3	12.1	11.1	13.0	13.3	11.8	13.4	13.6	8.0	9.0	9.2	8.0	6.9	7.6	6.2	8.7
Bankfull Width/Depth Ratio	8.8	9.4	9.7	8.8	8.6	9.1	9.4	8.4	13.2	13.5	12.4	12.2	12.8	11.8	13.3	14.3	14.9	21.8	20.6	14.8	18.4	20.1	18.5	23.1
Bankfull Entrenchment Ratio	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	5.7	4.7	5.0	6.1	5.8	5.3	5.7	4.9
Bankfull Bank Height Ratio ^{1,2}	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	1.0	1.0	1.0	1.0	1.0	1.0	0.9	1.0
d50 (mm)	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	34.3	41.6	29.1	18.6	62.8	27.5	38.7	45.0
Dimension and Substrate	Cross-Section 7, UT2 Reach 2 (Pool) ³								Cross-Section 8, UT2 Reach 2 (Riffle)							Cross-Section 9, UT2B Reach 2 (Riffle) ⁴								
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankfull Elevation (ft)	705.9	705.9	705.9	705.9	705.6	705.4	705.5	705.5	705.0	705.0	705.0	705.0	705.0	705.1	705.0	704.9	724.8	724.8	724.8	724.8	724.7	724.8	724.7	724.8
Low Bank Elevation (ft)	705.9	705.9	705.9	705.9	705.6	705.4	705.5	705.5	705.0	705.0	705.0	705.0	704.9	704.9	704.9	705.0	724.8	724.8	724.8	724.8	724.7	724.8	724.7	724.9
Bankfull Width (ft)	32.2	32.4	32.8	32.7	18.5	16.6	18.8	20.8	13.1	13.1	13.5	13.9	13.7	13.6	13.7	14.1	7.9	9.6	8.3	8.5	9.2	7.4	7.8	9.6
Floodprone Width (ft)	---	---	---	---	---	---	---	---	>55	>60	>60	>59	>55	>56	>57	>59	>67	>62	>68	>68	>68	>68	>68	>67
Bankfull Mean Depth (ft)	1.2	1.3	1.6	1.5	2.3	2.3	2.2	2.1	1.1	1.2	1.2	1.1	0.9	0.9	1.0	1.1	0.6	0.5	0.6	0.7	0.6	0.6	0.6	0.6
Bankfull Max Depth (ft)	3.8	3.6	5.1	5.1	4.6	4.5	4.7	4.7	1.5	1.8	1.9	1.7	1.5	1.7	1.6	1.8	1.0	0.9	1.1	1.6	1.2	1.1	1.2	1.3
Bankfull Cross-Sectional Area (ft ²)	38.6	41.8	52.1	50.1	41.8	38.1	42.1	42.8	14.6	16.2	16.5	14.4	12.6	12.6	13.3	14.9	4.9	5.0	5.2	6.1	5.5	4.6	5.0	6.1
Bankfull Width/Depth Ratio	26.9	25.1	20.7	21.4	8.2	7.3	8.4	10.1	11.8	10.6	11.1	13.6	15.0	14.7	14.1	13.4	12.8	18.4	13.2	11.8	15.2	11.8	12.2	15.0
Bankfull Entrenchment Ratio	---	---	---	---	---	---	---	---	>4	>5	>5	>4	>4	>4	>4	>4	>8	>7	>8	>8	>7	>9	>8	>7
Bankfull Bank Height Ratio ^{1,2}	---	---	---	---	---	---	---	---	1.0	1.0	1.0	1.0	0.9	0.9	0.9	1.0	1.0	1.0	1.0	1.0	1.1	1.0	1.0	1.1
d50 (mm)	---	---	---	---	---	---	---	---	45.8	25.7	23.4	38.7	23.3	49.1	35.1	92.1	25.4	33.7	11.0	22.6	22.6	17.1	11.6	12.5
Dimension and Substrate	Cross-Section 10, UT2B Reach 2 (Pool)																							
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7																
Bankfull Elevation (ft)	723.4	723.4	723.4	723.4	723.2	723.5	723.4	723.4																
Low Bank Elevation (ft)	723.4	723.4	723.4	723.4	723.2	723.5	723.4	723.4																
Bankfull Width (ft)	10.8	11.3	10.5	10.7	9.1	10.5	9.6	8.2																
Floodprone Width (ft)	---	---	---	---	---	---	---	---																
Bankfull Mean Depth (ft)	0.8	0.8	0.7	0.8	0.8	0.9	0.9	1.1																
Bankfull Max Depth (ft)	1.5	1.5	1.8	1.8	1.8	1.8	1.7	1.8																
Bankfull Cross-Sectional Area (ft ²)	8.3	8.6	7.8	9.0	6.9	9.0	8.8	8.7																
Bankfull Width/Depth Ratio	14.1	14.8	14.0	12.8	11.8	12.2	10.6	7.8																
Bankfull Entrenchment Ratio	---	---	---	---	---	---	---	---																
Bankfull Bank Height Ratio ^{1,2}	---	---	---	---	---	---	---	---																
d50 (mm)	---	---	---	---	---	---	---	---																

¹ Prior to MY4, bankfull dimensions were calculated using a fixed baseline bankfull elevation.

² MY4-MY7 Bank Height Ratio are calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Bankfull elevation was set too high on Cross-Section 7 between MY0 and MY3 which resulted in a wider bankfull width in those years.

⁴ Bankfull dimension calculations were adjusted at Cross-Section 9 between MY0 and MY3 because the baseline bankfull elevation was set low and fell within the active channel.

(---): Data was not provided

Table 11b. Morphology and Hydraulic Summary (Dimensional Parameters - Cross Section)

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Dimension and Substrate	Cross-Section 11, UT2 Reach 1 (Riffle)								Cross-Section 12, UT2 Reach 1 (Riffle)								Cross-Section 13, UT2 Reach 1 (Pool)							Cross-Section 14, UT1B Reach 1 (Pool)								
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankfull Elevation (ft)	719.3	719.3	719.3	719.3	719.3	719.1	719.2	719.0	717.3	717.3	717.3	717.3	717.5	717.4	717.5	717.4	717.4	717.4	717.4	717.4	717.5	717.4	717.3	717.7	764.2	764.2	764.2	764.2	764.7	764.5	764.9	764.9
Low Bank Elevation (ft)	719.3	719.3	719.3	719.3	719.1	719.0	719.0	718.9	717.3	717.3	717.3	717.3	717.5	717.5	717.6	717.6	717.4	717.4	717.4	717.4	717.5	717.4	717.3	717.7	764.7	764.7	764.7	764.7	764.7	764.5	764.9	764.9
Bankfull Width (ft)	14.2	13.7	13.9	13.8	11.4	12.1	11.3	11.3	10.6	10.6	11.2	10.9	12.7	12.4	12.6	11.4	19.6	17.4	17.1	18.2	18.2	16.0	13.8	16.5	5.2	4.9	5.3	5.0	5.1	8.1	9.2	10.3
Floodprone Width (ft)	101	105	104	103	98	100	98	103	>68	>57	>68	>66	>69	>70	>72	>70	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
Bankfull Mean Depth (ft)	0.9	1.0	1.0	0.8	0.9	0.9	0.9	1.0	0.8	0.7	0.7	0.6	0.7	0.7	0.8	0.8	1.2	1.1	1.3	1.1	1.1	1.1	1.2	1.3	0.5	0.2	0.2	0.1	0.4	0.2	0.3	0.3
Bankfull Max Depth (ft)	1.7	1.8	1.9	1.8	1.7	1.7	1.7	1.9	1.3	1.1	1.3	1.2	1.3	1.4	1.6	1.6	2.4	2.0	2.3	2.3	2.4	2.4	2.3	2.7	0.7	0.3	0.4	0.3	0.8	0.3	0.7	0.7
Bankfull Cross-Sectional Area (ft ²)	12.7	14.1	14.0	11.7	10.4	11.3	10.6	11.8	8.4	7.3	7.7	7.1	8.4	8.6	9.6	9.6	23.1	18.5	21.5	19.8	19.5	18.4	16.4	21.8	2.5	1.0	1.2	0.6	2.1	1.8	2.4	2.8
Bankfull Width/Depth Ratio	15.8	13.3	13.8	16.4	12.4	13.0	12.1	10.9	13.2	15.6	16.2	16.9	19.1	17.8	16.5	13.5	16.7	16.4	13.6	16.7	16.9	13.9	11.5	12.6	10.4	23.3	22.5	40.5	12.8	36.6	35.4	36.9
Bankfull Entrenchment Ratio	7.1	7.6	7.4	7.4	8.6	8.2	8.7	9.1	>7	>5	>6	>6	>5	>5	>5	>6	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
Bankfull Bank Height Ratio ^{1,2}	1.0	1.0	1.0	1.0	0.9	0.9	0.9	1.0	1.0	1.0	1.0	1.0	1.0	1.0	1.1	1.1	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
d50 (mm)	28.0	17.4	14.6	74.5	56.2	48.8	18.2	56.9	24.2	22.1	12.8	25.4	25.5	23.6	24.7	70.8	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---	---
Dimension and Substrate	Cross-Section 15, UT1B Reach 1 (Riffle)								Cross-Section 16, UT2C Reach 2 (Riffle)								Cross-Section 17, UT2C Reach 2 (Pool)															
	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7	Base	MY1	MY2	MY3	MY4	MY5	MY6	MY7								
Bankfull Elevation (ft)	761.9	761.9	761.9	761.9	762.1	762.1	762.3	762.4	709.2	709.2	709.2	709.2	709.5	709.5	709.5	709.5	708.3	708.3	708.3	708.3	708.1	708.2	708.4	708.4								
Low Bank Elevation (ft)	761.9	761.9	761.9	761.9	762.0	762.1	762.0	762.2	709.2	709.2	709.2	709.2	709.5	709.5	709.5	709.4	708.3	708.3	708.3	708.3	708.1	708.2	708.4	708.4								
Bankfull Width (ft)	4.8	4.6	5.2	3.6	5.2	6.9	3.2	5.4	9.9	9.0	9.3	8.9	9.3	10.0	10.3	9.8	13.0	12.8	11.8	10.8	4.3	5.4	5.5	5.3								
Floodprone Width (ft)	12	8	10	9	17	19	15	23	>48	>45	>47	>47	>49	>45	>51	>43	---	---	---	---	---	---	---	---								
Bankfull Mean Depth (ft)	0.4	0.2	0.3	0.2	0.3	0.3	0.3	0.2	0.5	0.5	0.5	0.4	0.5	0.5	0.6	0.5	0.9	0.8	0.5	0.5	0.9	0.7	0.6	0.5								
Bankfull Max Depth (ft)	0.6	0.3	0.5	0.4	0.6	0.7	0.6	0.6	1.1	1.0	1.1	1.1	1.3	1.0	1.2	0.9	2.0	2.0	1.2	1.3	1.5	1.1	1.1	0.8								
Bankfull Cross-Sectional Area (ft ²)	1.8	1.0	1.5	0.7	1.5	1.9	1.0	0.9	5.3	4.6	4.9	3.9	5.0	4.9	5.9	4.6	11.2	10.7	5.9	5.7	4.0	3.7	3.4	2.7								
Bankfull Width/Depth Ratio	13.3	22.1	18.8	19.0	18.4	24.4	10.5	22.8	18.4	17.5	17.6	20.3	17.2	20.2	17.9	20.9	15.1	15.3	23.8	20.4	4.7	7.9	8.7	10.6								
Bankfull Entrenchment Ratio	2.6	1.6	1.9	2.4	3.2	2.8	4.8	4.2	>5	>5	>5	>5	>5	>5	>5	>4	---	---	---	---	---	---	---	---								
Bankfull Bank Height Ratio ^{1,2}	1.0	1.0	1.0	1.3	0.8	1.0	0.7	0.8	1.0	1.0	1.0	1.1	1.0	0.9	1.1	0.9	---	---	---	---	---	---	---	---								
d50 (mm)	56.3	69.7	13.3	23.9	11.0	S/C	4.0	18.4	18.4	10.8	8.0	11.5	22.6	24.3	13.9	20.9	---	---	---	---	---	---	---	---								

¹ Prior to MY4, bankfull dimensions were calculated using a fixed baseline bankfull elevation.

² MY4-MY7 Bank Height Ratio are calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

(---): Data was not provided

Table 12a. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021

Hopewell-UT1B Reach 1

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	4.8		4.6		5.2		3.6		5.2		6.9		3.2		5.4	
Floodprone Width (ft)	12.0		8.0		10.0		9.0		16.7		19.2		15.0		23.0	
Bankfull Mean Depth	0.4		0.2		0.3		0.2		0.3		0.3		0.3		0.2	
Bankfull Max Depth	0.6		0.3		0.5		0.4		0.6		0.7		0.6		0.6	
Bankfull Cross Sectional Area (ft ²)	1.8		1.0		1.5		0.7		1.5		1.9		1.0		0.9	
Width/Depth Ratio	13.3		22.1		18.8		19.0		18.4		24.4		10.5		22.8	
Entrenchment Ratio	2.6		1.6		1.9		2.4		3.2		2.8		4.8		4.2	
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.3		0.8		1.0		0.7		0.8	
D50 (mm)	56.3		69.7		13.3		23.9		11.0		Silt/Clay		4.0		18.4	
Profile																
Riffle Length (ft)	11	47														
Riffle Slope (ft/ft)	0.0185	0.0646														
Pool Length (ft)	20	105														
Pool Max Depth (ft)	1.1	1.6														
Pool Spacing (ft)	56	103														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	---															
Radius of Curvature (ft)	---															
Rc:Bankfull Width (ft/ft)	---															
Meander Wave Length (ft)	---															
Meander Width Ratio	---															
Additional Reach Parameters																
Rosgen Classification	C4b															
Channel Thalweg Length (ft)	480															
Sinuosity (ft)	1.1															
Water Surface Slope (ft/ft)	0.0270															
Bankfull Slope (ft/ft)	0.0246	0.0260														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/1/6/128/256/512	SC/0.7/7/139/241/>2048	SC/6/9/23/57/180	SC/SC/1.1/128/1248/2048	SC/SC/3.6/23.9/50.6/90 ³	SC/SC/SC/77/143/>2048	0.14/2/5/73/151/256	SC/4/11/79/148/256								
% of Reach with Eroding Banks	0%	0%	0%	0%	0%	0%	0%	0%								

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12b. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2 Reach 1

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	10.6	14.2	10.6	13.7	11.2	13.9	10.9	13.8	11.4	12.7	12.1	12.4	11.3	12.6	11.3	11.4
Floodprone Width (ft)	>68	101	>57	105	>68	104	>66	103	>69	98.0	>70	100	72.0	98.4	>70	103
Bankfull Mean Depth	0.8	0.9	0.7	1.0	0.7	1.0	0.6	0.8	0.7	0.9	0.7	0.9	0.8	0.9	0.8	1.0
Bankfull Max Depth	1.3	1.7	1.1	1.8	1.3	1.9	1.2	1.8	1.3	1.7	1.4	1.7	1.6	1.7	1.6	1.9
Bankfull Cross Sectional Area (ft ²)	8.4	12.7	7.3	14.1	7.7	14.0	7.1	11.7	8.4	10.4	8.6	11.3	9.6	10.6	9.6	11.8
Width/Depth Ratio	13.2	15.8	13.3	15.6	13.8	16.2	13.6	16.4	12.4	19.1	13.0	17.8	12.1	16.5	10.9	13.5
Entrenchment Ratio	>7	7.1	>5	7.6	>6	7.4	>6	7.4	>5	8.6	>6	8.2	>5	8.7	>6	9.1
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		0.9	1.0	0.9	1.0	0.9	1.1	1.0	1.1
D50 (mm)	24.2	28.0	17.4	22.1	12.8	14.6	25.4	74.5	25.5	56.2	23.6	48.8	18.2	24.7	56.9	70.8
Profile																
Riffle Length (ft)	11	120														
Riffle Slope (ft/ft)	0.0033	0.0227														
Pool Length (ft)	17	66														
Pool Max Depth (ft)	1.7	3.6														
Pool Spacing (ft)	20	108														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	5	11														
Radius of Curvature (ft)	13	36														
Rc:Bankfull Width (ft/ft)	1.2	2.5														
Meander Wave Length (ft)	60	171														
Meander Width Ratio	0.5	0.8														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,787															
Sinuosity (ft)	1.20															
Water Surface Slope (ft/ft)	0.0087															
Bankfull Slope (ft/ft)	0.0085	0.0086														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/1.4/24/73/128/180		SC/5.6/20/112/237/2048		SC/10/17/51/174/2048		SC/SC/25/70/116/180		SC/SC/3.6/23.9/50.6/90 ³		SC/SC/1.8/76/157/256		0.84/10/15/51/107/180		SC/1.4/30/105/171/1024	
% of Reach with Eroding Banks	0%		0%		0%		0%		0%		0%		0%		0%	

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12c. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2 Reach 2

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	15.3		13.1		13.5		13.9		13.7		13.6		13.7		14.1	
Floodprone Width (ft)	>55		>60		>60		>59		>55		>56		>57		>59	
Bankfull Mean Depth	1.0		1.2		1.2		1.0		0.9		0.9		1.0		1.1	
Bankfull Max Depth	1.5		1.8		1.9		1.7		1.5		1.7		1.6		1.8	
Bankfull Cross Sectional Area (ft ²)	14.8		16.2		16.5		14.4		12.6		12.6		13.3		14.9	
Width/Depth Ratio	15.8		10.6		11.1		13.6		15.0		14.7		14.1		13.4	
Entrenchment Ratio	>4		>5		>5		>4		>4		>4		>4		>4	
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		0.9		0.9		0.9		1.0	
D50 (mm)	45.8		25.7		23.4		38.7		23.3		49.1		35.1		92.1	
Profile																
Riffle Length (ft)	24	36														
Riffle Slope (ft/ft)	0.01039	0.03859														
Pool Length (ft)	41	105														
Pool Max Depth (ft)	3.2	5.0														
Pool Spacing (ft)	65	132														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	32	79														
Radius of Curvature (ft)	21	24														
Rc:Bankfull Width (ft/ft)	1.4	1.6														
Meander Wave Length (ft)	113	120														
Meander Width Ratio	2.1	5.2														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	529															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0126															
Bankfull Slope (ft/ft)	0.0103	0.0107														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/1.4/24/73/128/180 ⁴	SC/5.6/20/112/237/2048	SC/10/17/51/174/2048	SC/SC/25/70/116/180 ⁴	SC/SC/3.6/23.9/50.6/90 ³	SC/SC/1.8/76/157/256	0.84/10/15/51/107/180	SC/1.4/30/105/171/1024								
% of Reach with Eroding Banks	0%		0%	0%	0%	0%	0%	0%								

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12d. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2A Reach 1

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	10.3		9.7		10.1		10.7		11.9		11.8		11.9		11.1	
Floodprone Width (ft)	>87		>88		>88		>87		>87		>87		>87		>87	
Bankfull Mean Depth	0.8		0.8		0.8		0.7		0.7		0.7		0.8		0.8	
Bankfull Max Depth	1.6		1.3		1.4		1.3		1.5		1.6		1.7		1.8	
Bankfull Cross Sectional Area (ft ²)	8.0		7.6		7.6		7.0		8.0		8.4		9.3		9.2	
Width/Depth Ratio	13.3		12.4		13.3		16.3		17.7		16.7		15.3		13.4	
Entrenchment Ratio	>8		>9		>9		>8		>7		>7		>7		>7	
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		1.0		1.0		1.1		1.1	
D50 (mm)	30.9		40.3		27.7		0.3		37.9		11.0		0.3		33.4	
Profile																
Riffle Length (ft)	18	54														
Riffle Slope (ft/ft)	0.0032	0.0210														
Pool Length (ft)	18	54														
Pool Max Depth (ft)	1.4	2.9														
Pool Spacing (ft)	40	67														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	20	38														
Radius of Curvature (ft)	16	25														
Rc:Bankfull Width (ft/ft)	0.5	2.4														
Meander Wave Length (ft)	76	116														
Meander Width Ratio	1.9	3.7														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,443															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0108															
Bankfull Slope (ft/ft)	0.0107	0.0109														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/2/18/57/87/180		SC/13/28/128/220/362 ⁴		SC/4/12/78/152/256 ⁴		SC/SC/12/61/110/180 ⁴		SC/SC/3.6/23.9/50.6/90 ³		SC/SC/5.6/58/90/180		SC/SC/0.5/70/113/362		SC/11/33/90/146/180	
% of Reach with Eroding Banks	0%		0%		0%		0%		0%		0%		0%		0%	

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12e. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2A Reach 2

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	9.8	10.9	10.3	14.0	10.2	13.8	10.9	12.6	10.2	11.3	10.4	12.4	10.2	10.7	11.1	14.2
Floodprone Width (ft)	63	>88	66	>87	69	>92	67	>75	65	>89	66	>93	61	>93	70	>95
Bankfull Mean Depth	0.7		0.6	0.7	0.7	0.8	0.5	0.7	0.6	0.7	0.6	0.8	0.6	0.8	0.6	0.9
Bankfull Max Depth	1.1	1.2	1.1	1.2	1.3	1.4	1.0	1.3	1.2	1.3	1.3	1.4	1.2	1.4	1.4	1.4
Bankfull Cross Sectional Area (ft ²)	6.8	8.0	6.7	9.0	7.7	9.2	5.6	8.0	6.7	6.9	7.6	8.0	6.2	8.4	8.7	9.7
Width/Depth Ratio	14.0	14.9	15.8	21.8	13.6	20.6	14.8	18.6	15.4	18.4	13.6	20.1	12.3	18.5	12.7	23.1
Entrenchment Ratio	5.7	>9	4.7	>8	5.0	>9	6.1	>7	5.8	>9	5.3	>9	5.7	>9	4.9	>8
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		1.0	1.0	1.0	1.1	0.9	1.1	1.0	1.2
D50 (mm)	34.3	39.8	26.3	41.6	26.9	29.1	18.6	43.3	48.3	62.8	27.5	37.9	33.2	38.7	41.6	45.0
Profile																
Riffle Length (ft)	10	67														
Riffle Slope (ft/ft)	0.0034	0.0330														
Pool Length (ft)	14	55														
Pool Max Depth (ft)	1.5	4.1														
Pool Spacing (ft)	27	88														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	15	42														
Radius of Curvature (ft)	18	30														
Rc:Bankfull Width (ft/ft)	1.8	2.8														
Meander Wave Length (ft)	64	147														
Meander Width Ratio	1.5	3.9														
Additional Reach Parameters																
Rosgen Classification	C4															
Channel Thalweg Length (ft)	1,443															
Sinuosity (ft)	1.2															
Water Surface Slope (ft/ft)	0.0108															
Bankfull Slope (ft/ft)	0.0107	0.0109														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/2/18/57/87/180		SC/13/28/128/220/362		SC/4/12/78/152/256		SC/SC/12/61/110/180		SC/SC/3.6/23.9/50.6/90 ³		SC/SC/5.6/58/90/180		SC/SC/0.5/70/113/362		SC/11/33/90/146/180	
% of Reach with Eroding Banks	0%		0%		0%		0%		0%		0%		0%		0%	

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12f. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2B Reach 2

Parameter	As-Built/Baseline ⁴		MY1		MY2		MY3		MY4		MY5		MY6		MY7	
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max
Dimension and Substrate - Riffle																
Bankfull Width (ft)	7.9		9.6		8.3		8.5		9.2		7.4		7.8		9.6	
Floodprone Width (ft)	>67		>62		>68		>68		>68		>68		>68		>67	
Bankfull Mean Depth	0.6		0.5		0.6		0.7		0.6		0.6		0.6		0.6	
Bankfull Max Depth	1.0		0.9		1.1		1.6		1.2		1.1		1.2		1.3	
Bankfull Cross Sectional Area (ft ²)	4.9		5.0		5.2		6.1		5.5		4.6		5.0		6.1	
Width/Depth Ratio	12.8		18.4		13.2		11.8		15.2		11.8		12.2		15	
Entrenchment Ratio	>8		>7		>8		>8		>7		>9		>8		>7	
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		1.1		1.0		1.0		1.1	
D50 (mm)	25.4		33.7		11.0		22.6		22.6		17.1		11.6		12.5	
Profile																
Riffle Length (ft)	7	25														
Riffle Slope (ft/ft)	0.0146	0.0441														
Pool Length (ft)	10	21														
Pool Max Depth (ft)	1.3	2.8														
Pool Spacing (ft)	19	36														
Pool Volume (ft ³)	---															
Pattern																
Channel Beltwidth (ft)	8	19														
Radius of Curvature (ft)	9	15														
Rc:Bankfull Width (ft/ft)	1.1	1.9														
Meander Wave Length (ft)	40	62														
Meander Width Ratio	1.1	2.4														
Additional Reach Parameters																
Rosgen Classification	C4b															
Channel Thalweg Length (ft)	198															
Sinuosity (ft)	1.1															
Water Surface Slope (ft/ft)	0.0211															
Bankfull Slope (ft/ft)	0.0207	0.0215														
Ri%/Ru%/P%/G%/S%	---															
SC%/Sa%/G%/C%/B%/Be%	---															
d16/d35/d50/d84/d95/d100	SC/6/21/55/128/256		SC/4/9/38/83/180		2.2/7/19/54/82/180		SC/SC/1.7/41/76/180		SC/SC/3.6/23.9/50.6/90 ³		SC/SC/0.8/67/110/180		SC/SC/0.4/15/71/180		SC/0.4/8/80/124/180	
% of Reach with Eroding Banks	0%		0%		0%		0%		0%		0%		0%		0%	

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.

Table 12g. Monitoring Data - Stream Reach Data Summary

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Hopewell-UT2C Reach 2

Parameter	As-Built/Baseline		MY1		MY2		MY3		MY4		MY5		MY6		MY7		
	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	Min	Max	
Dimension and Substrate - Riffle																	
Bankfull Width (ft)	9.9		9.0		9.3		8.9		9.3		10.0		10.3		9.8		
Floodprone Width (ft)	>48		>45		>47		>47		>49		>45		>51		>43		
Bankfull Mean Depth	0.5		0.5		0.5		0.4		0.5		0.5		0.6		0.5		
Bankfull Max Depth	1.1		1.0		1.1		1.1		1.3		1.0		1.2		0.9		
Bankfull Cross Sectional Area (ft ²)	5.3		4.6		4.9		3.9		5.0		4.9		5.9		4.6		
Width/Depth Ratio	18.4		17.5		17.6		20.3		17.2		20.2		17.9		20.9		
Entrenchment Ratio	>5		>5		>5		>5		>5		>5		>5		>4		
Bank Height Ratio ^{1,2}	1.0		1.0		1.0		1.0		1.0		0.9		1.1		0.9		
D50 (mm)	18.4		10.8		8.0		11.5		22.6		24.3		13.9		20.9		
Profile																	
Riffle Length (ft)	6	20															
Riffle Slope (ft/ft)	0.0051	0.0584															
Pool Length (ft)	3	25															
Pool Max Depth (ft)	2.2	3.7															
Pool Spacing (ft)	23	36															
Pool Volume (ft ³)	---																
Pattern																	
Channel Beltwidth (ft)	10	25															
Radius of Curvature (ft)	14	15															
Rc:Bankfull Width (ft/ft)	1.4	1.5															
Meander Wave Length (ft)	45	82															
Meander Width Ratio	1.0	2.6															
Additional Reach Parameters																	
Rosgen Classification	C4/C4b																
Channel Thalweg Length (ft)	247																
Sinuosity (ft)	1.1																
Water Surface Slope (ft/ft)	0.0083	0.0365															
Bankfull Slope (ft/ft)	0.0102	0.0459															
Ri%/Ru%/P%/G%/S%	---																
SC%/Sa%/G%/C%/B%/Be%	---																
d16/d35/d50/d84/d95/d100	SC/SC/9/45/78/128		SC/0.2/6/73/124/256	0.2/0.5/1.3/9/45/128	0.28/1.3/3.5/17/30/90	SC/SC/3.6/23.9/50.6/90 ³	SC/SC/0.6/14/32/362	0.2/3/12/31/44/180	0.2/1/15/71/147/256								
% of Reach with Eroding Banks	0%		0%	0%	0%	0%	0%	0%	0%								

(---): Data was not provided

¹ Prior to MY4, bankfull dimensions were calculated using a fixed bankfull elevation

² MY4-MY7 Bank Height Ratio was calculated based on the As-built (MY0) cross-sectional area as described in the Standard Measurement of the BHR Monitoring Parameter document provided by the NCIRT (9/2018). The remainder of the cross-section dimension parameters were calculated based on the current year's low bank height.

³ Reachwide sediment results were incorrectly reported in MY4. This data has been updated to reflect the correct results.


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 1, UT2A Reach 1

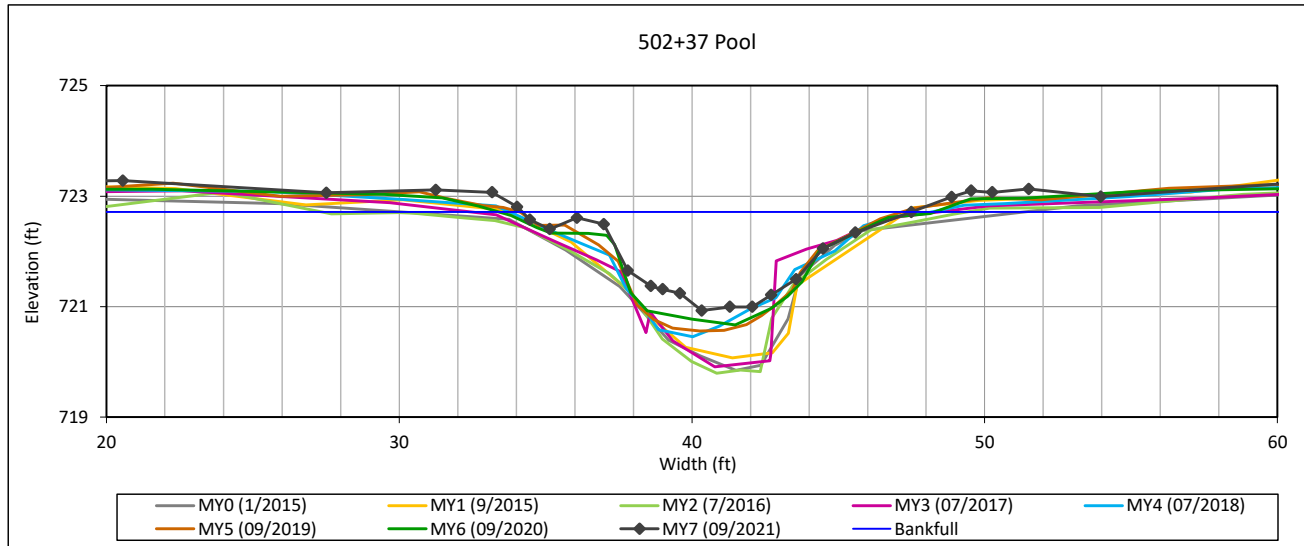

Bankfull Dimensions

11.6	x-section area (m.sq.)
13.3	width (m)
0.9	mean depth (m)
1.8	max depth (m)
14.2	wetted parimeter (m)
0.8	hyd radi (m)
15.3	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross- Section 2, UT2A Reach 1

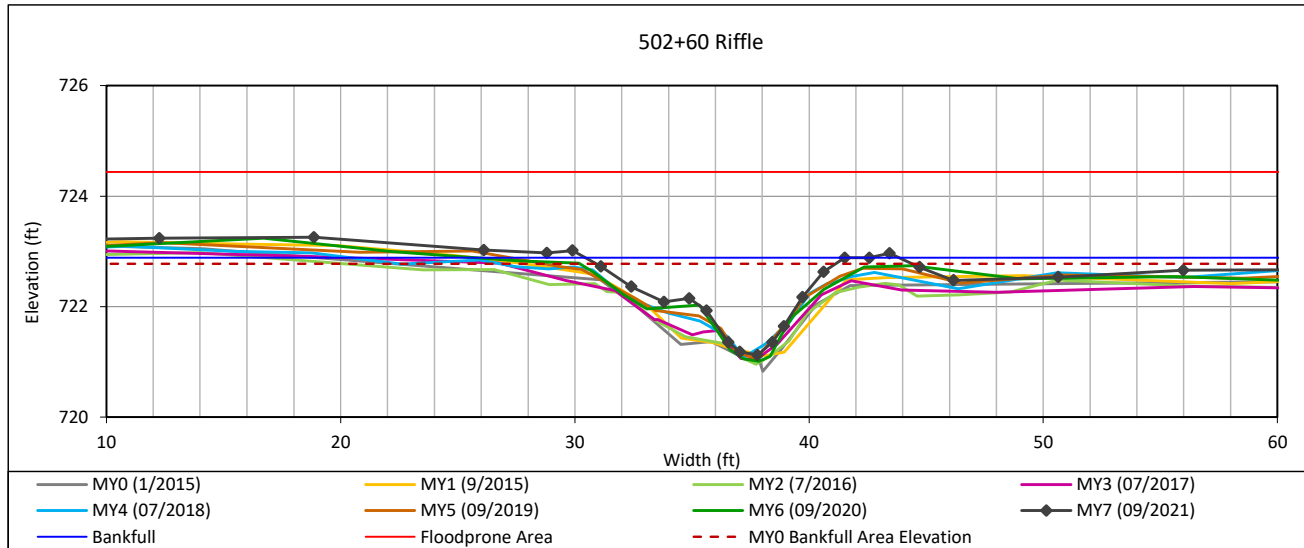

Bankfull Dimensions

9.2	x-section area (m.sq.)
11.1	width (m)
0.8	mean depth (m)
1.8	max depth (m)
11.8	wetted perimeter (m)
0.8	hyd radi (m)
13.4	width-depth ratio
87.4	W flood prone area (ft)
7.9	entrenchment ratio
1.1	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 3, UT2A Reach 2

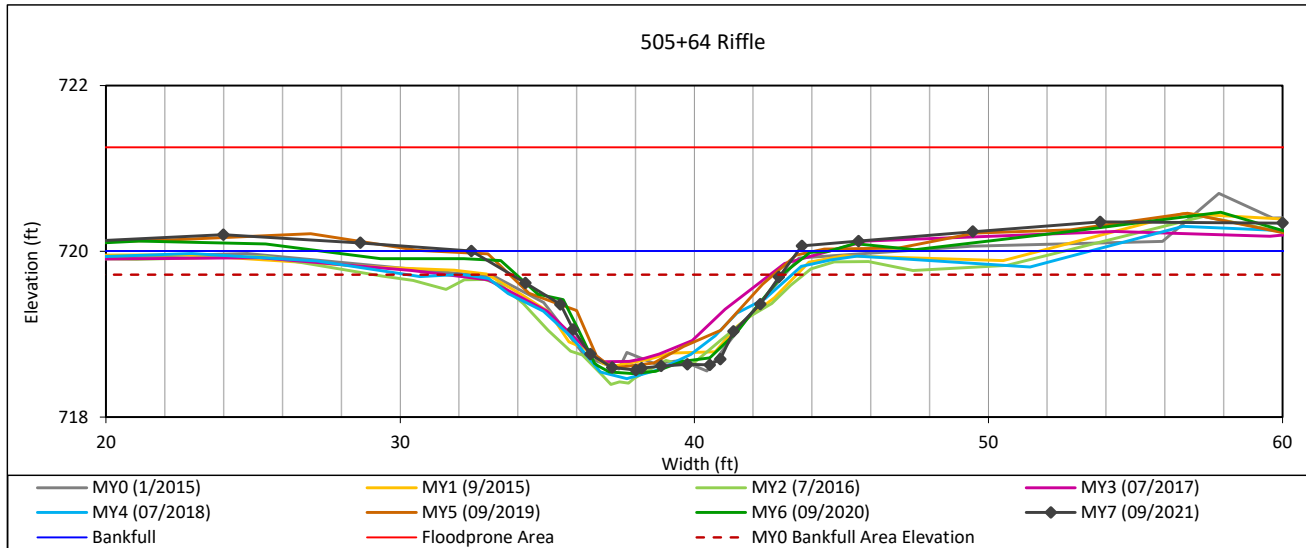

Bankfull Dimensions

9.7	x-section area (m.sq.)
11.1	width (m)
0.9	mean depth (m)
1.4	max depth (m)
11.7	wetted perimeter (m)
0.8	hyd radi (m)
12.7	width-depth ratio
95.2	W flood prone area (ft)
8.6	entrenchment ratio
1.2	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 4, UT2A Reach 2

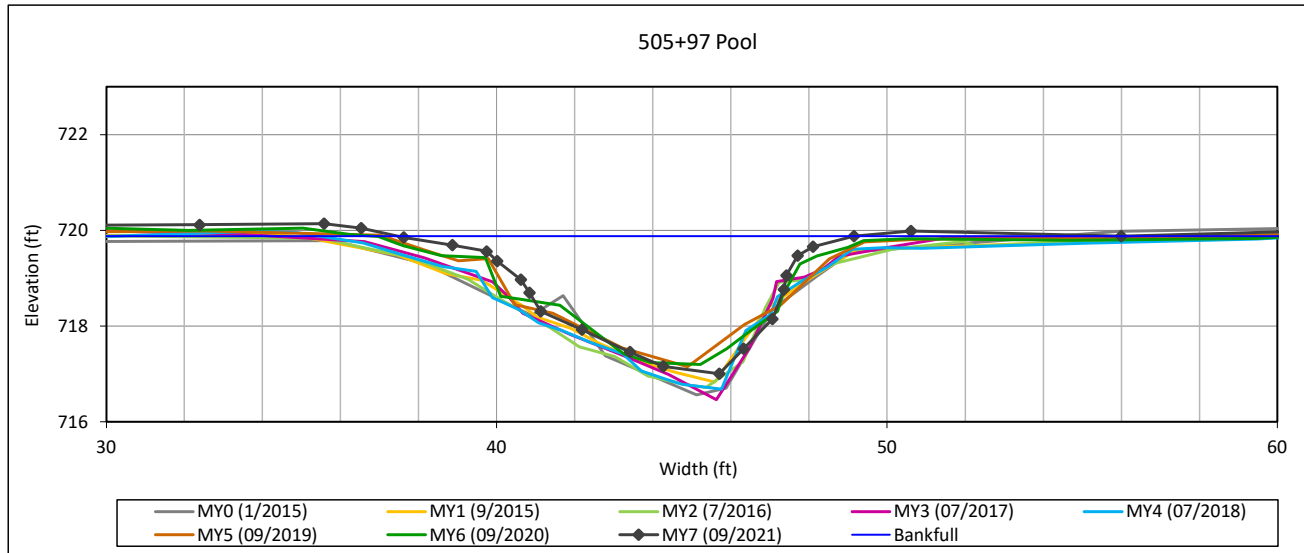

Bankfull Dimensions

16.3	x-section area (m.sq.)
11.7	width (m)
1.4	mean depth (m)
2.9	max depth (m)
13.7	wetted perimeter (m)
1.2	hyd radi (m)
8.4	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 5, UT2A Reach 2

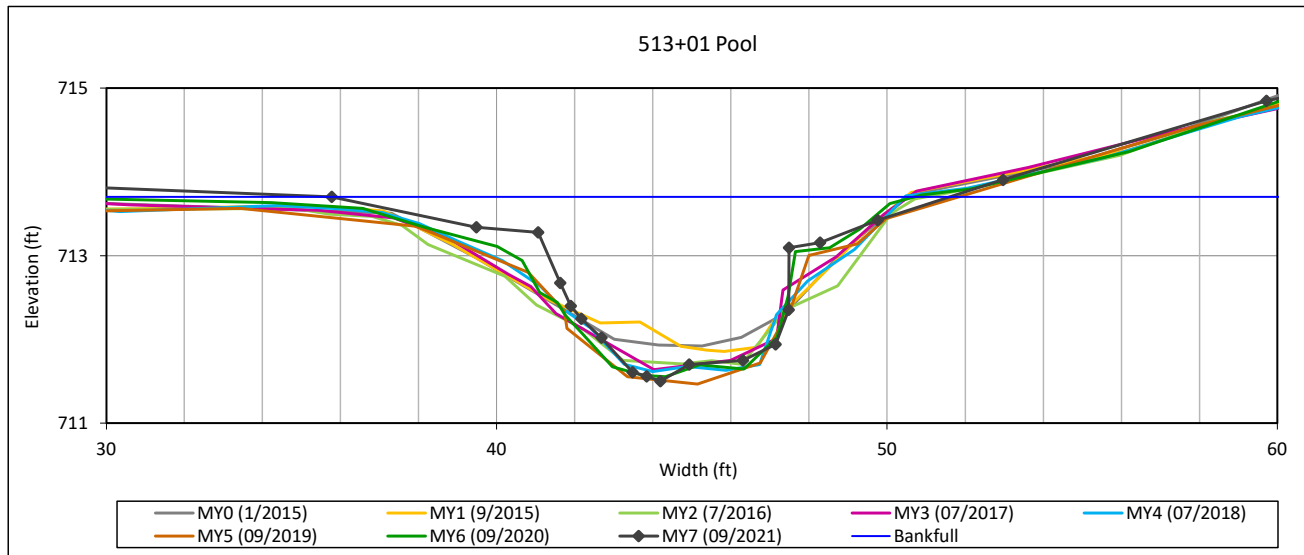

Bankfull Dimensions

13.6	x-section area (m.sq.)
14.0	width (m)
1.0	mean depth (m)
2.2	max depth (m)
15.6	wetted perimeter (m)
0.9	hyd radi (m)
14.3	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 6, UT2A R2

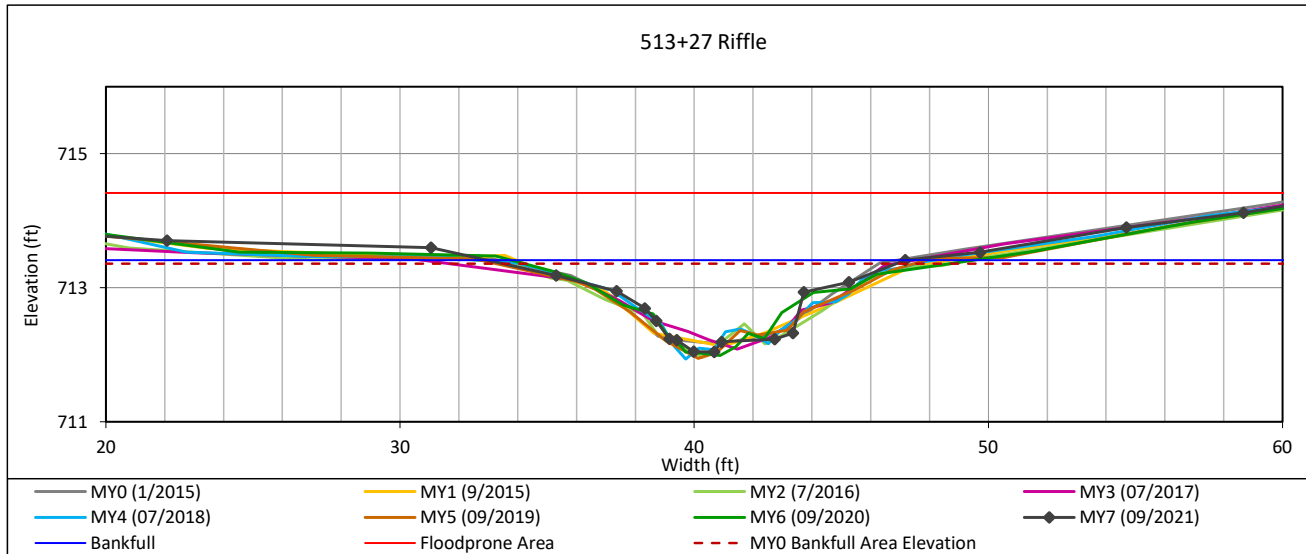

Bankfull Dimensions

8.7	x-section area (m.sq.)
14.2	width (m)
0.6	mean depth (m)
1.4	max depth (m)
14.8	wetted perimeter (m)
0.6	hyd radi (m)
23.1	width-depth ratio
69.5	W flood prone area (ft)
4.9	entrenchment ratio
1.0	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 7, UT2 R2

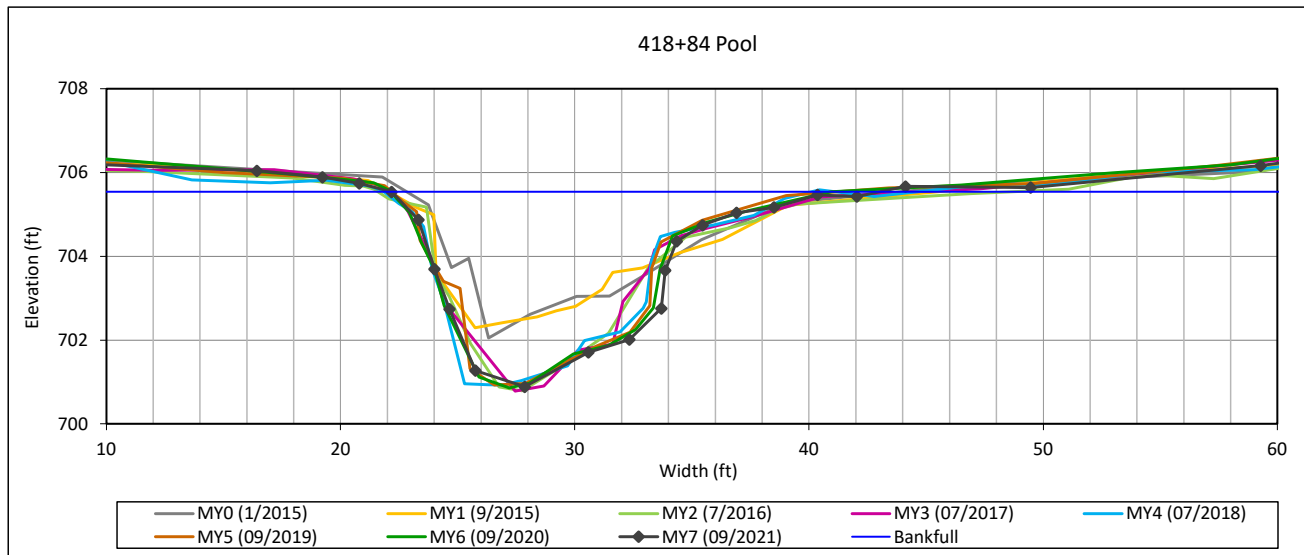

Bankfull Dimensions

42.8	x-section area (m.sq.)
20.8	width (m)
2.1	mean depth (m)
4.7	max depth (m)
24.5	wetted perimeter (m)
1.7	hyd radi (m)
10.1	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 8, UT2 R2

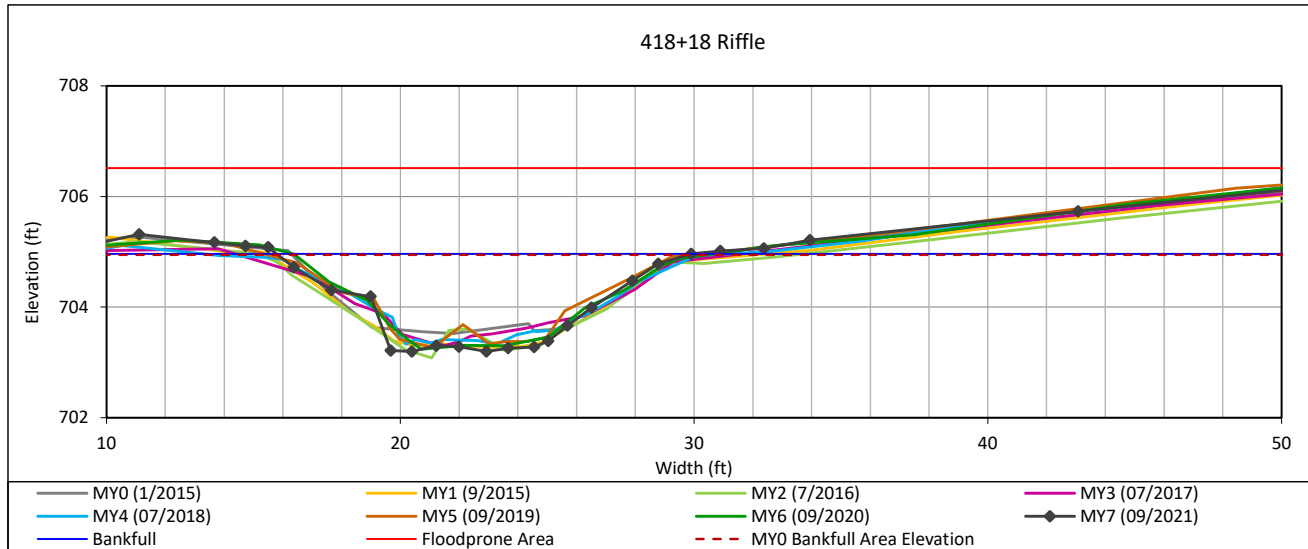

Bankfull Dimensions

14.9	x-section area (m.sq.)
14.1	width (m)
1.1	mean depth (m)
1.8	max depth (m)
15.0	wetted perimeter (m)
1.0	hyd radi (m)
13.4	width-depth ratio
59.8	W flood prone area (ft)
4.2	entrenchment ratio
1.0	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 9, UT2B R2

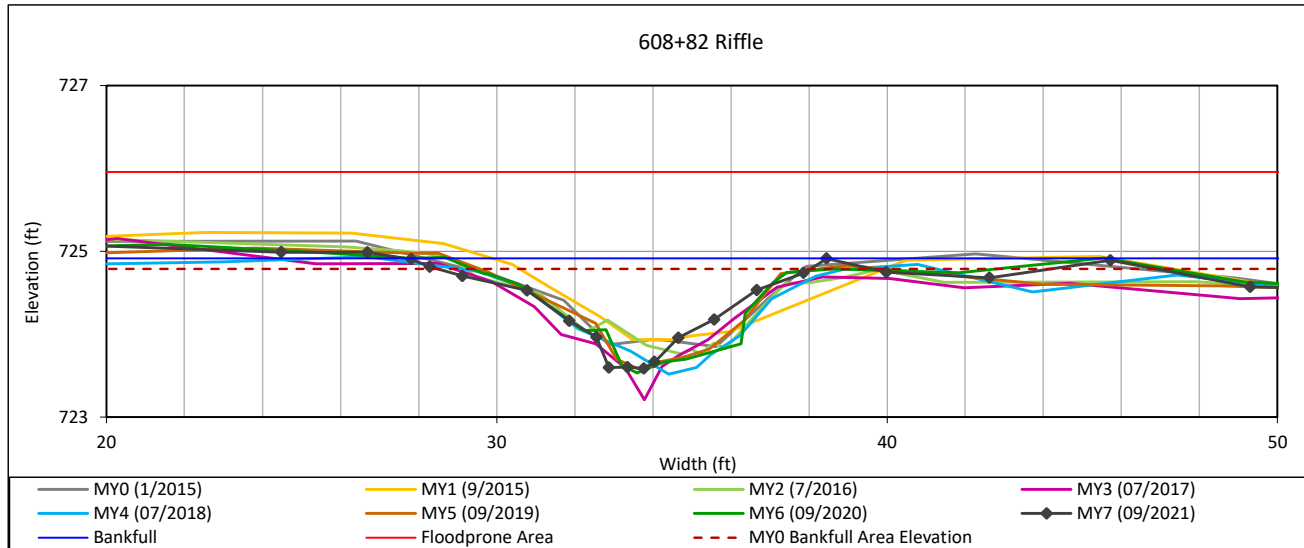

Bankfull Dimensions

6.1	x-section area (m.sq.)
9.6	width (m)
0.6	mean depth (m)
1.3	max depth (m)
10.0	wetted perimeter (m)
0.6	hyd radi (m)
15.0	width-depth ratio
67.8	W flood prone area (ft)
7.1	entrenchment ratio
1.1	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 10, UT2B R2

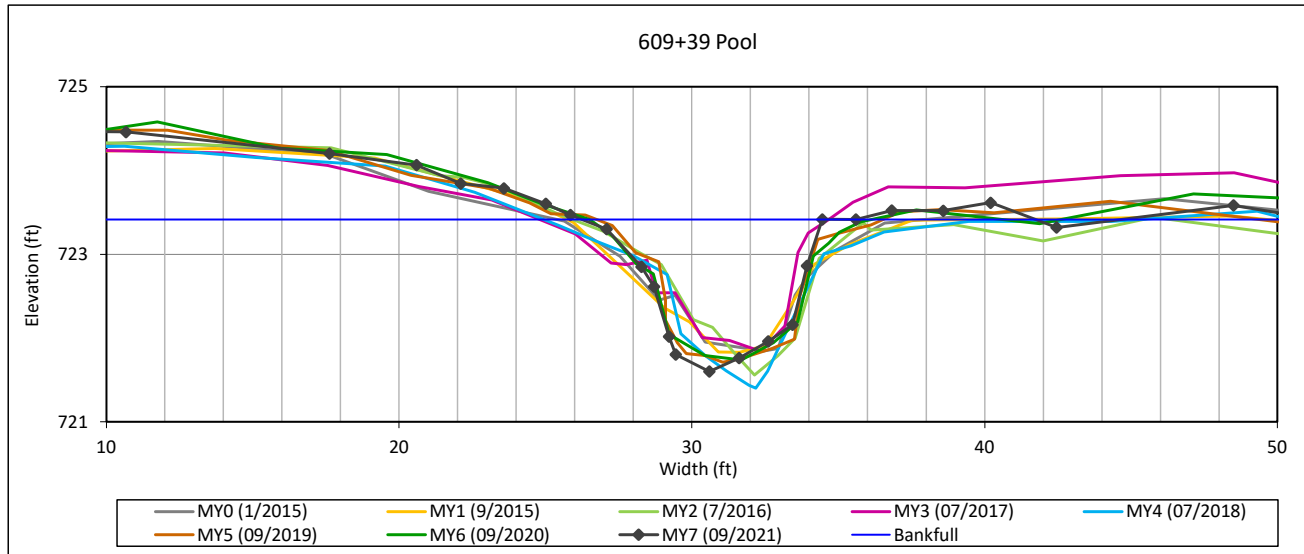

Bankfull Dimensions

8.7	x-section area (m.sq.)
8.2	width (m)
1.1	mean depth (m)
1.8	max depth (m)
9.4	wetted perimeter (m)
0.9	hyd radi (m)
7.8	width-depth ratio

Survey Date: 9/2021
Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 11, UT2 R1

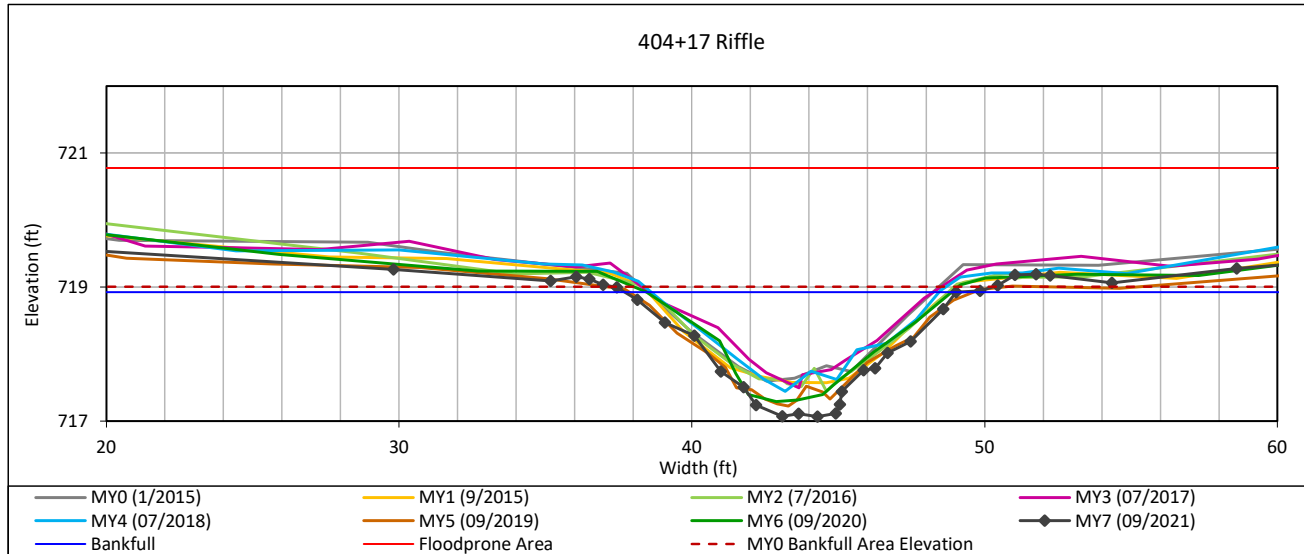

Bankfull Dimensions

11.8	x-section area (m.sq.)
11.3	width (m)
1.0	mean depth (m)
1.9	max depth (m)
12.2	wetted parimeter (m)
1.0	hyd radi (m)
10.9	width-depth ratio
102.5	W flood prone area (ft)
9.1	entrenchment ratio
1.0	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 12, UT2 R1

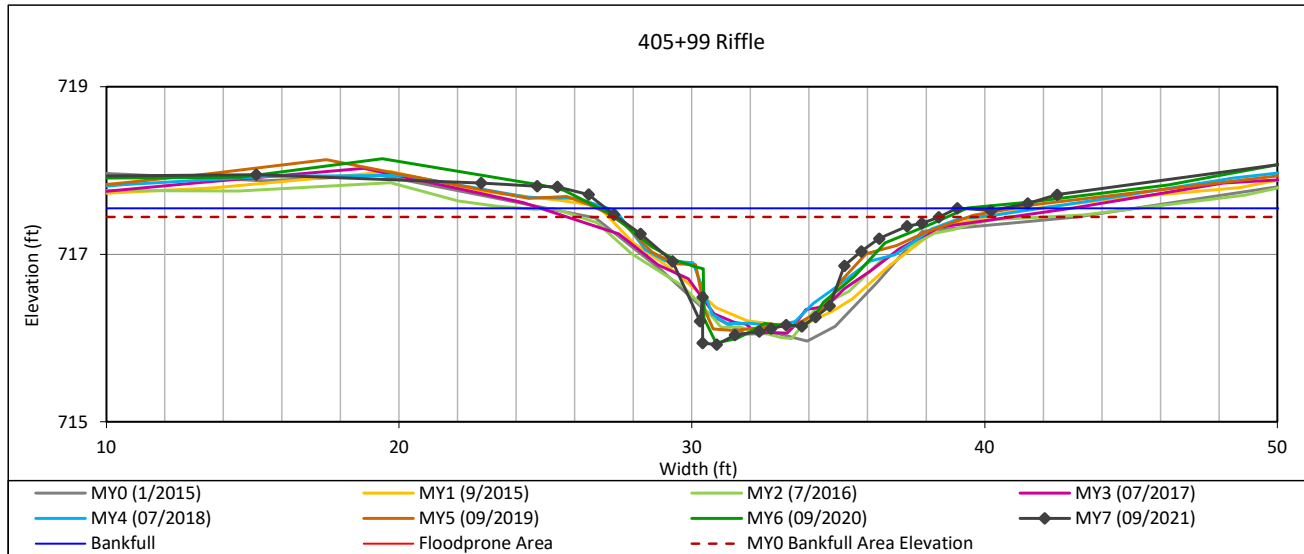

Bankfull Dimensions

9.6	x-section area (m.sq.)
11.4	width (m)
0.8	mean depth (m)
1.6	max depth (m)
12.8	wetted parimeter (m)
0.8	hyd radi (m)
13.5	width-depth ratio
70.6	W flood prone area (ft)
6.2	entrenchment ratio
1.1	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 13, UT2 R1

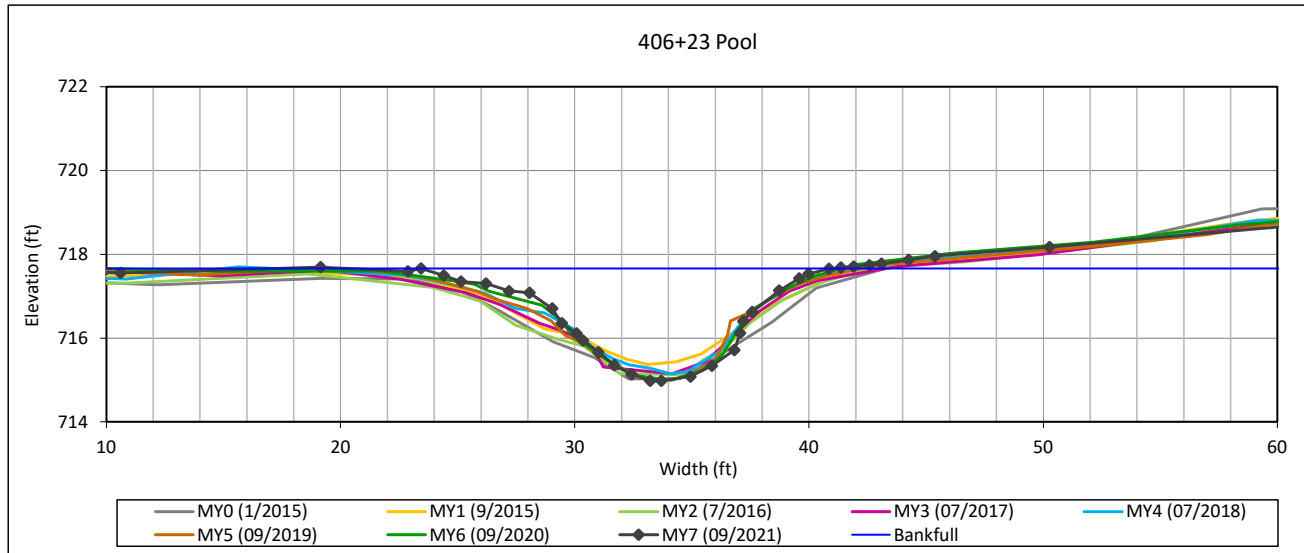

Bankfull Dimensions

21.8	x-section area (m.sq.)
16.5	width (m)
1.3	mean depth (m)
2.7	max depth (m)
17.8	wetted parimeter (m)
1.2	hyd radi (m)
12.6	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 14, UT1B R1

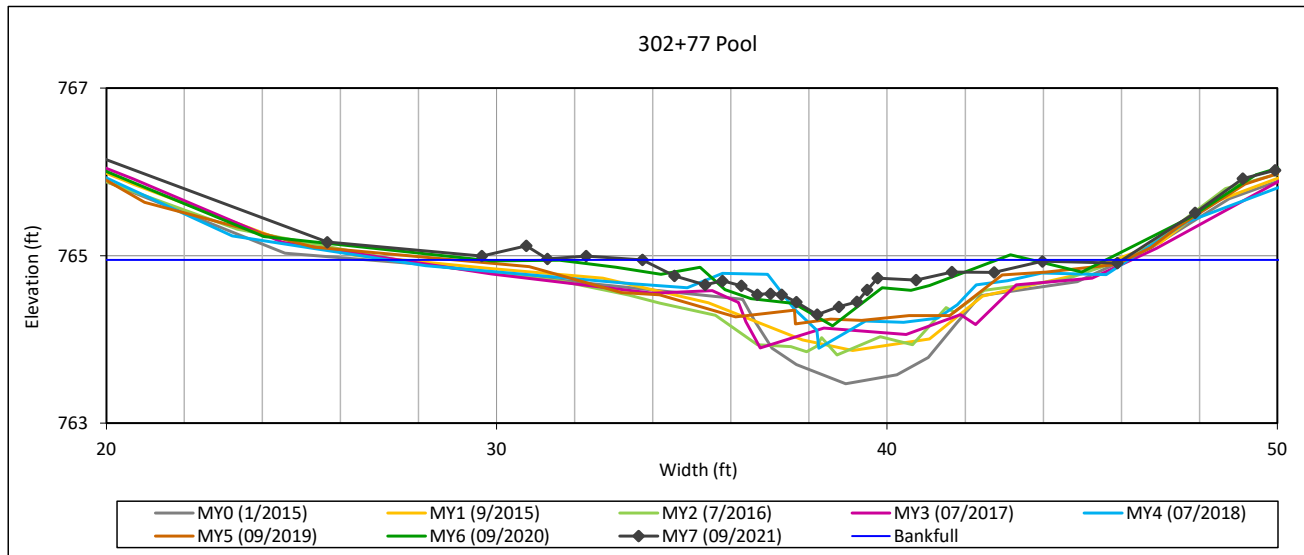

Bankfull Dimensions

2.8	x-section area (m.sq.)
10.3	width (m)
0.3	mean depth (m)
0.7	max depth (m)
10.4	wetted perimeter (m)
0.3	hyd radi (m)
36.9	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 15, UT1B R1

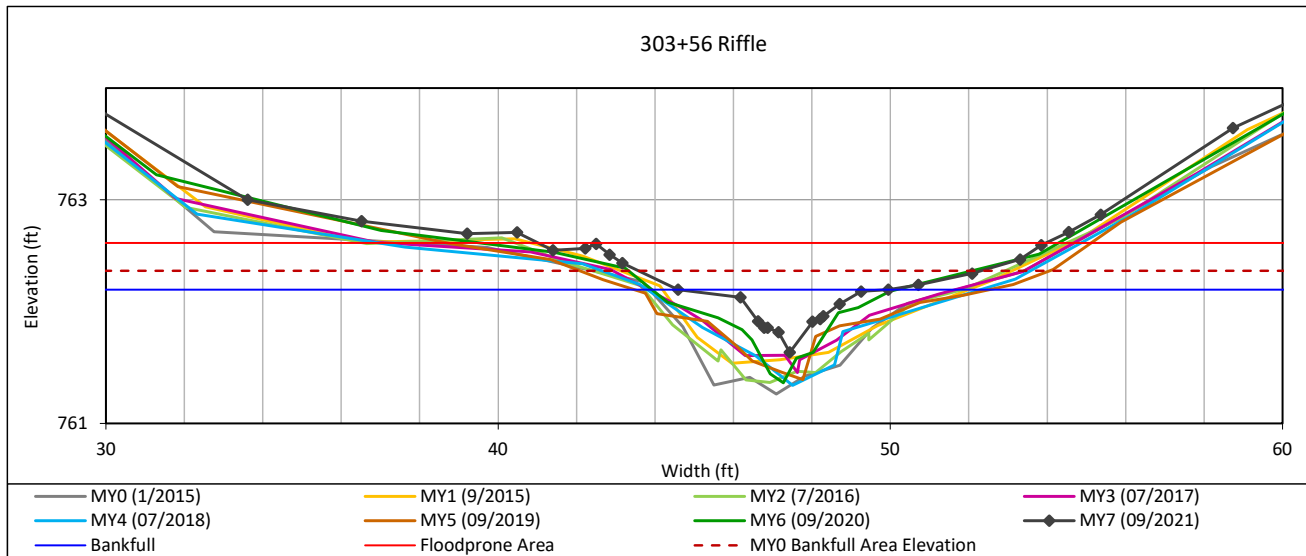

Bankfull Dimensions

0.9	x-section area (m.sq.)
5.4	width (m)
0.2	mean depth (m)
0.6	max depth (m)
5.6	wetted perimeter (m)
0.2	hyd radi (m)
32.3	width-depth ratio
22.8	W flood prone area (ft)
4.2	entrenchment ratio
0.8	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 16, UT2C R2

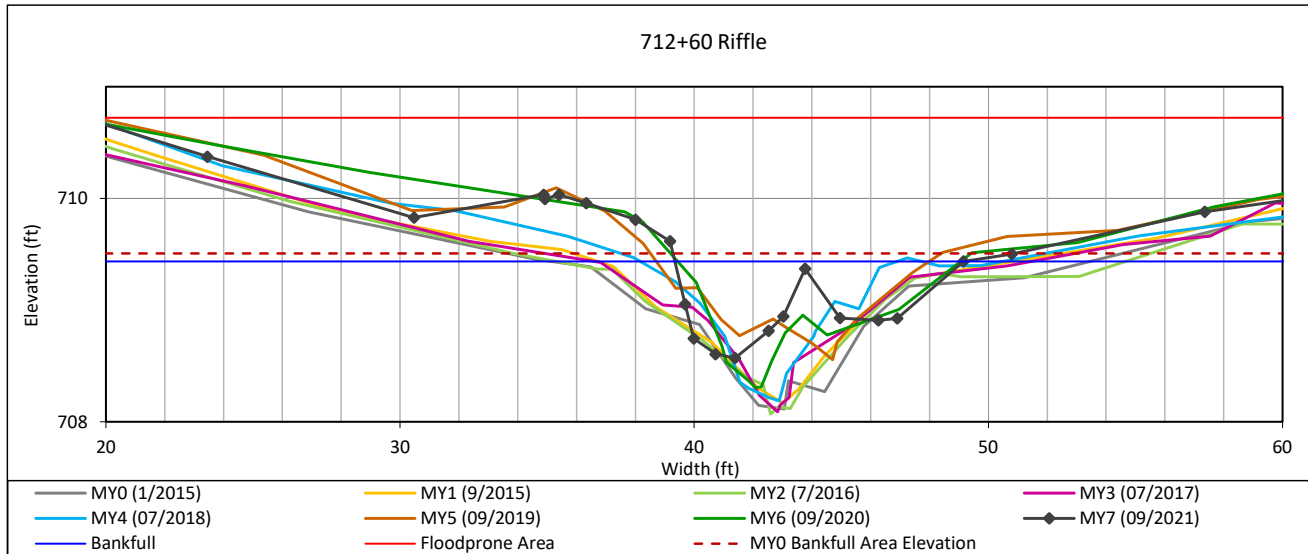

Bankfull Dimensions

4.6	x-section area (m.sq.)
9.8	width (m)
0.5	mean depth (m)
0.9	max depth (m)
10.4	wetted perimeter (m)
0.4	hyd radi (m)
20.9	width-depth ratio
43.9	W flood prone area (ft)
4.5	entrenchment ratio
0.9	low bank height ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream


Cross-Section Plots

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Cross-Section 17, UT2C R2

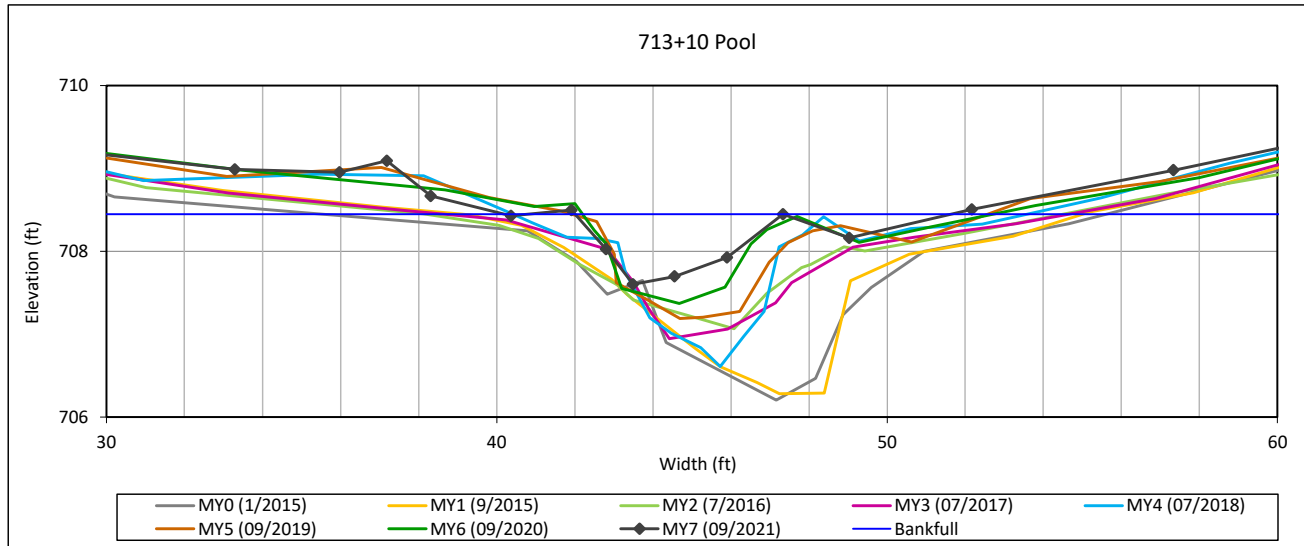

Bankfull Dimensions

2.7	x-section area (m.sq.)
5.3	width (m)
0.5	mean depth (m)
0.8	max depth (m)
5.7	wetted perimeter (m)
0.5	hyd radi (m)
10.6	width-depth ratio

Survey Date: 9/2021

Field Crew: Wildlands Engineering



View Downstream

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2A, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062		23	23	23	23
SAND	Very fine	0.062	0.125		1	1	1	24
	Fine	0.125	0.250					24
	Medium	0.25	0.50		2	2	2	26
	Coarse	0.5	1.0					26
	Very Coarse	1.0	2.0		2	2	2	28
GRAVEL	Very Fine	2.0	2.8					28
	Very Fine	2.8	4.0					28
	Fine	4.0	5.6		1	1	1	29
	Fine	5.6	8.0		3	3	3	32
	Medium	8.0	11.0		3	3	3	35
	Medium	11.0	16.0		3	3	3	38
	Coarse	16.0	22.6	1	3	4	4	42
	Coarse	22.6	32	5	2	7	7	49
	Very Coarse	32	45	9		9	9	58
	Very Coarse	45	64	7	3	10	10	68
COBBLE	Small	64	90	15	1	16	16	84
	Small	90	128	6	2	8	8	92
	Large	128	180	7	1	8	8	100
BOULDER	Large	180	256					100
	Small	256	362					100
BOULDER	Small	362	512					100
	Medium	512	1024					100
BOULDER	Large/Very Large	1024	2048					100
	Bedrock	2048	>2048					100
Total				50	50	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	11.0
D ₅₀ =	33.2
D ₈₄ =	90.0
D ₉₅ =	145.5
D ₁₀₀ =	180.0

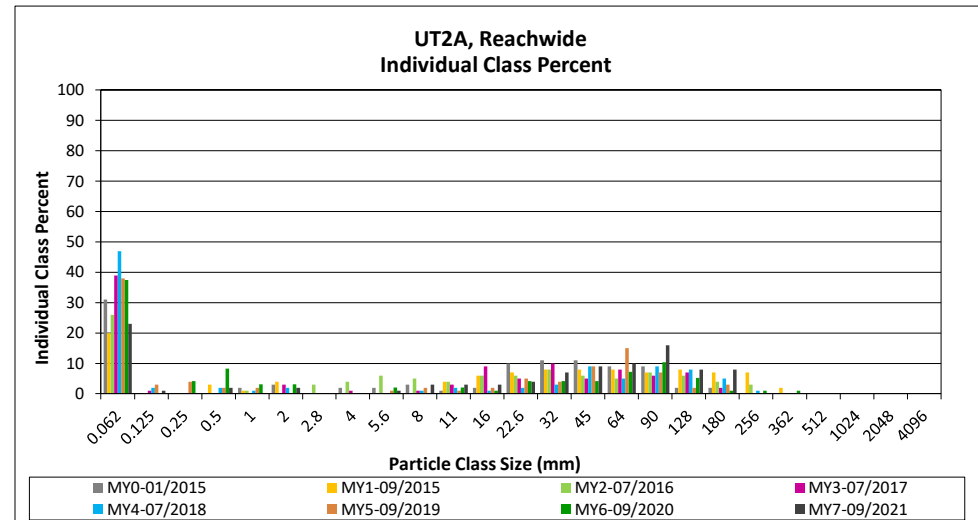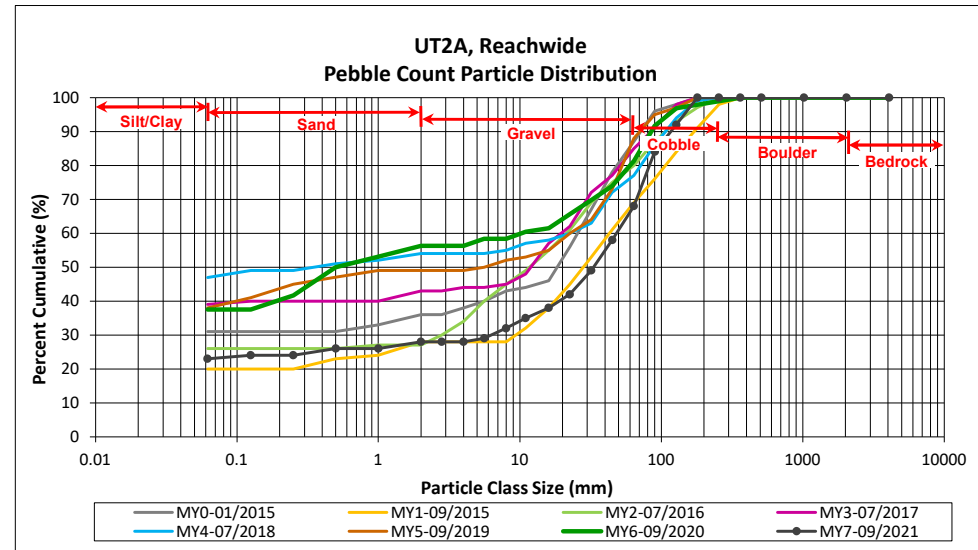

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2A-R1, Cross-Section 2

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	11	11	11
SAND	Very fine	0.062	0.125			11
	Fine	0.125	0.250			11
	Medium	0.25	0.50			11
	Coarse	0.5	1.0			11
	Very Coarse	1.0	2.0	3	3	14
GRAVEL	Very Fine	2.0	2.8			14
	Very Fine	2.8	4.0			14
	Fine	4.0	5.6			14
	Fine	5.6	8.0			14
	Medium	8.0	11.0	4	4	18
	Medium	11.0	16.0	5	5	23
	Coarse	16.0	22.6	8	8	31
	Coarse	22.6	32	17	17	48
	Very Coarse	32	45	16	16	64
COBBLE	Small	64	90	13	13	90
	Small	90	128	6	6	96
	Large	128	180	4	4	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 2 Channel materials (mm)	
D ₁₆ =	9.4
D ₃₅ =	24.5
D ₅₀ =	33.4
D ₈₄ =	76.9
D ₉₅ =	120.7
D ₁₀₀ =	180.0

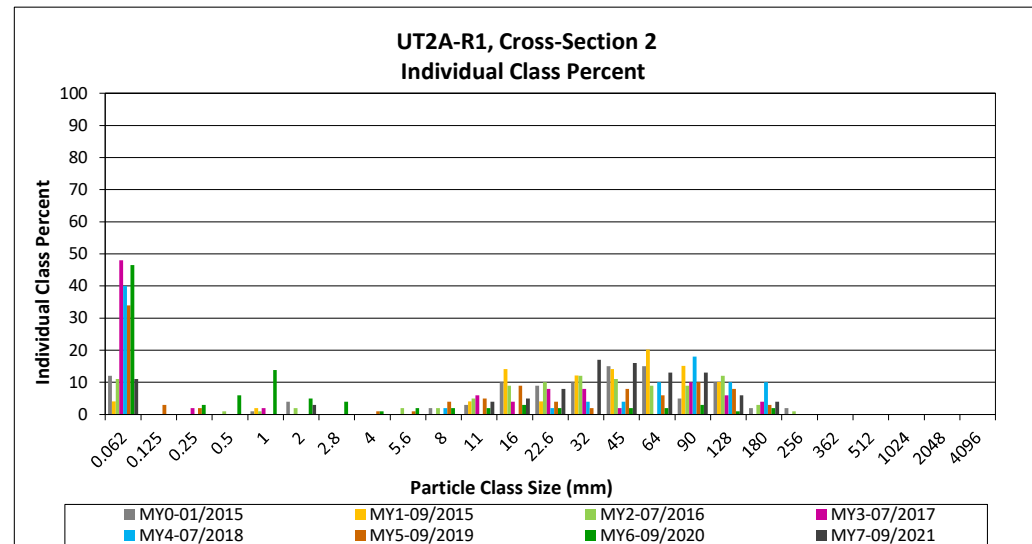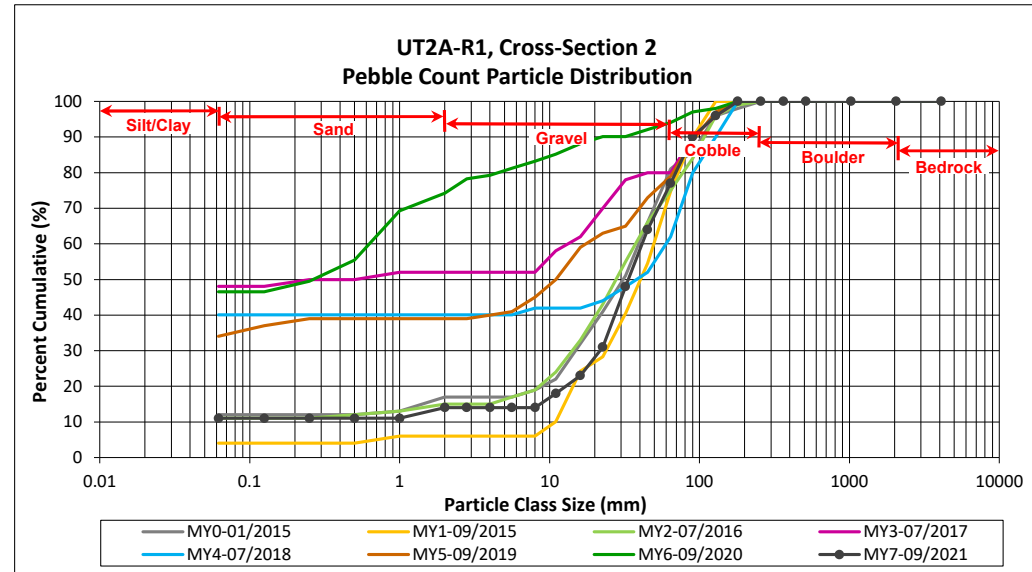

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2A-R2, Cross-Section 3

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	2	2	2
SAND	Very fine	0.062	0.125	1	1	3
	Fine	0.125	0.250	1	1	4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	2	2	6
GRAVEL	Very Fine	2.0	2.8			6
	Very Fine	2.8	4.0			6
	Fine	4.0	5.6			6
	Fine	5.6	8.0	2	2	8
	Medium	8.0	11.0	5	5	13
	Medium	11.0	16.0	11	11	24
	Coarse	16.0	22.6	12	12	36
	Coarse	22.6	32	4	4	40
	Very Coarse	32	45	13	13	53
	Very Coarse	45	64	10	10	63
COBBLE	Small	64	90	18	18	81
	Small	90	128	10	10	91
	Large	128	180	9	9	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 3 Channel materials (mm)	
D ₁₆ =	12.2
D ₃₅ =	22.0
D ₅₀ =	41.6
D ₈₄ =	100.0
D ₉₅ =	148.9
D ₁₀₀ =	180.0

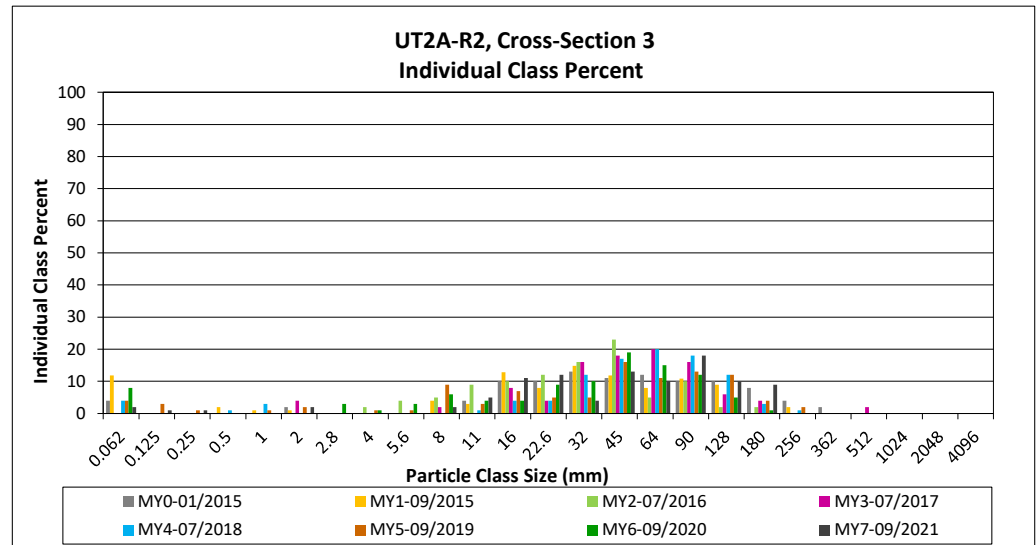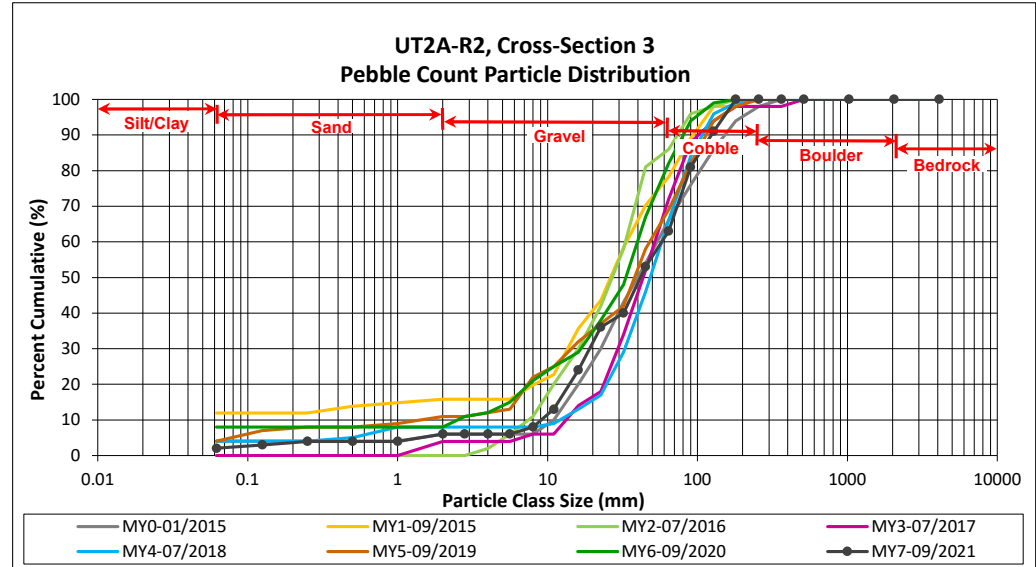

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2A-R2, Cross-Section 6

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062			0
SAND	Very fine	0.062	0.125			0
	Fine	0.125	0.250			0
	Medium	0.25	0.50			0
	Coarse	0.5	1.0			0
	Very Coarse	1.0	2.0			0
GRAVEL	Very Fine	2.0	2.8			0
	Very Fine	2.8	4.0			0
	Fine	4.0	5.6	2	2	2
	Fine	5.6	8.0			2
	Medium	8.0	11.0	2	2	4
	Medium	11.0	16.0	6	6	10
	Coarse	16.0	22.6	13	13	23
	Coarse	22.6	32	12	12	35
	Very Coarse	32	45	15	15	50
COBBLE	Small	64	90	16	16	79
	Small	90	128	9	9	88
	Large	128	180	9	9	97
	Large	180	256	2	2	99
BOULDER	Small	256	362	1	1	100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 6 Channel materials (mm)	
D ₁₆ =	18.8
D ₃₅ =	32.0
D ₅₀ =	45.0
D ₈₄ =	109.5
D ₉₅ =	166.9
D ₁₀₀ =	362.0

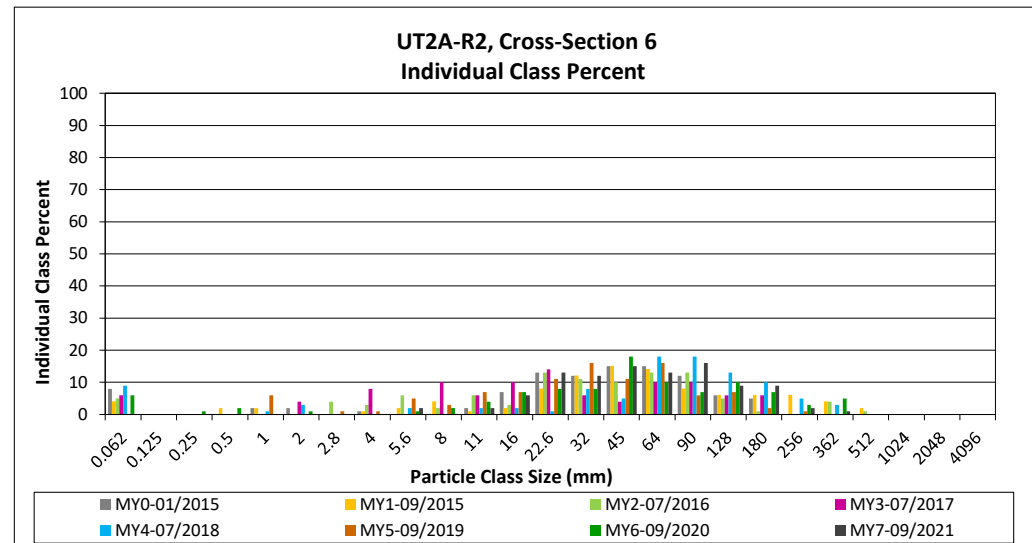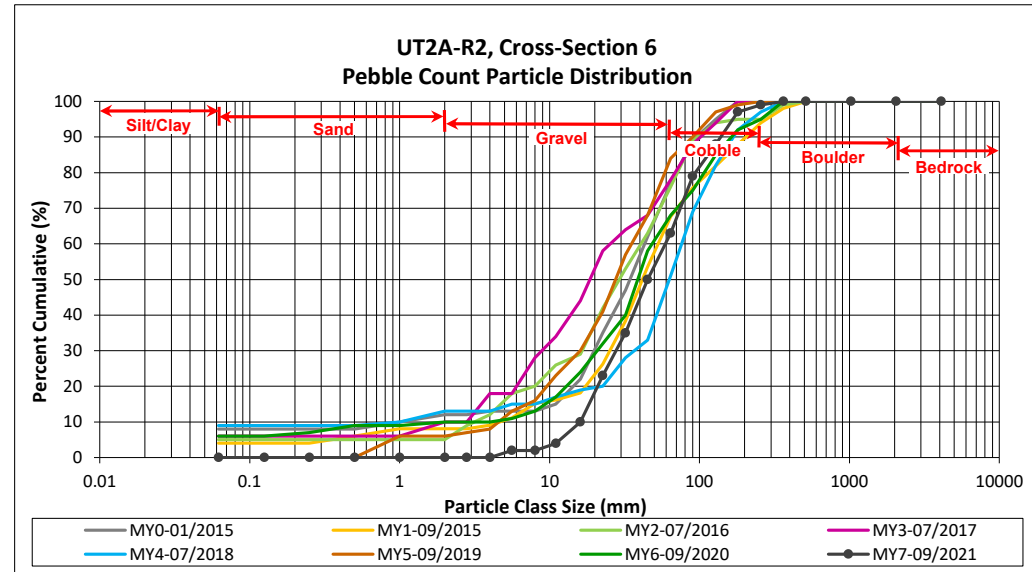

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2-R2, Cross-Section 8

Particle Class		Diameter (mm)		Rifle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	2	2	6
GRAVEL	Very Fine	2.0	2.8			6
	Very Fine	2.8	4.0			6
	Fine	4.0	5.6			6
	Fine	5.6	8.0			6
	Medium	8.0	11.0			6
	Medium	11.0	16.0			6
	Coarse	16.0	22.6			6
	Coarse	22.6	32	4	4	10
	Very Coarse	32	45	6	6	16
	Very Coarse	45	64	16	16	32
COBBLE	Small	64	90	16	16	48
	Small	90	128	30	30	78
	Large	128	180	12	12	90
	Large	180	256	4	4	94
BOULDER	Small	256	362	6	6	100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 8 Channel materials (mm)	
D ₁₆ =	45.0
D ₃₅ =	68.2
D ₅₀ =	92.1
D ₈₄ =	151.8
D ₉₅ =	271.2
D ₁₀₀ =	362.0

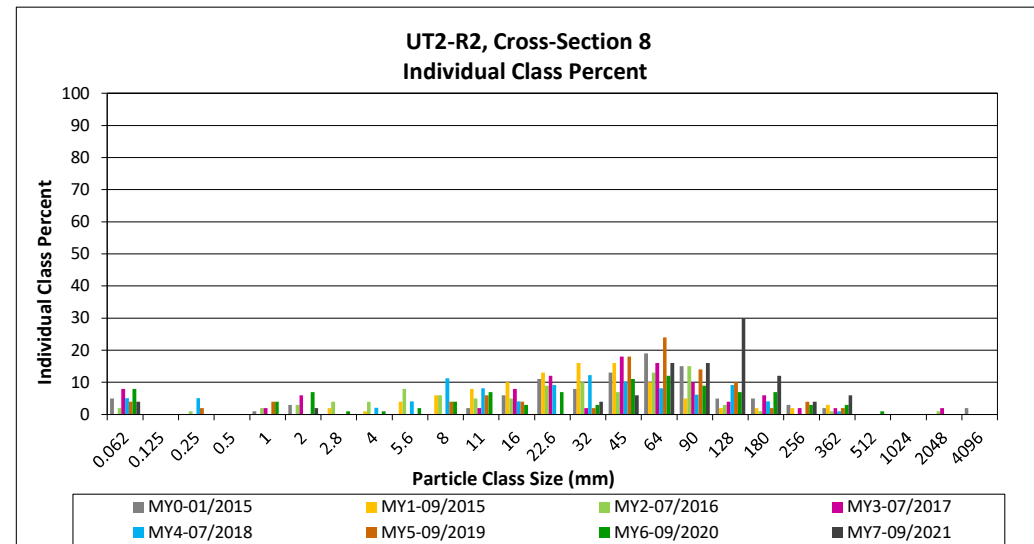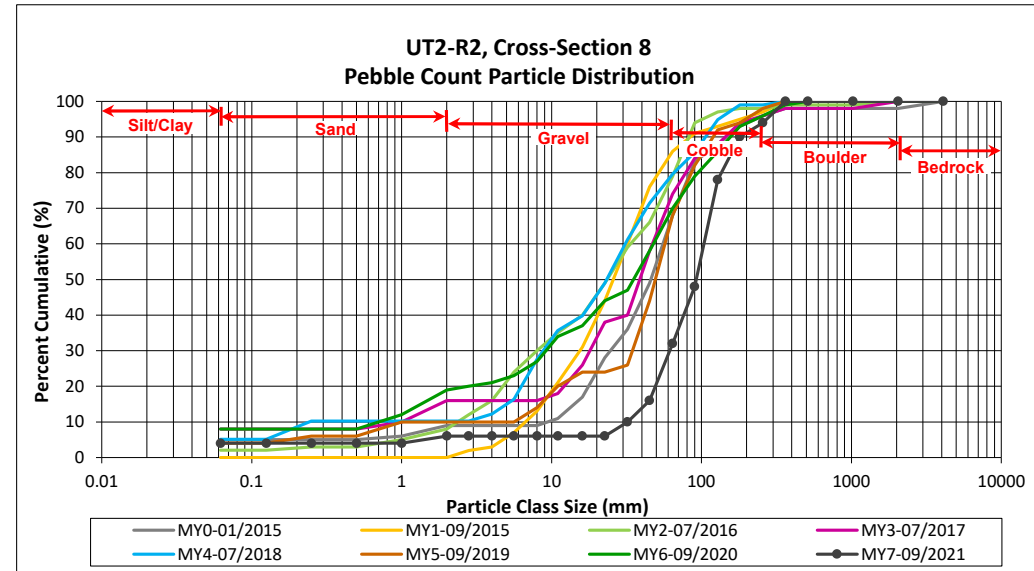

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2B-R2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	5	24	29	29	29
SAND	Very fine	0.062	0.125					29
	Fine	0.125	0.250		3	3	3	32
	Medium	0.25	0.50	1	3	4	4	36
	Coarse	0.5	1.0		2	2	2	38
	Very Coarse	1.0	2.0	3	2	5	5	43
GRAVEL	Very Fine	2.0	2.8					43
	Very Fine	2.8	4.0		1	1	1	44
	Fine	4.0	5.6		1	1	1	45
	Fine	5.6	8.0	2	3	5	5	50
	Medium	8.0	11.0		6	6	6	56
	Medium	11.0	16.0	3	2	5	5	61
	Coarse	16.0	22.6	2	2	4	4	65
	Coarse	22.6	32	6		6	6	71
	Very Coarse	32	45	3		3	3	74
	Very Coarse	45	64	6		6	6	80
COBBLE	Small	64	90	6		6	6	86
	Small	90	128	10		10	10	96
	Large	128	180	3	1	4	4	100
	Large	180	256					100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
BEDROCK	Large/Very Large	1024	2048					100
	Bedrock	2048	>2048					100
Total				50	50	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	0.4
D ₅₀ =	8.0
D ₈₄ =	80.3
D ₉₅ =	123.6
D ₁₀₀ =	180.0

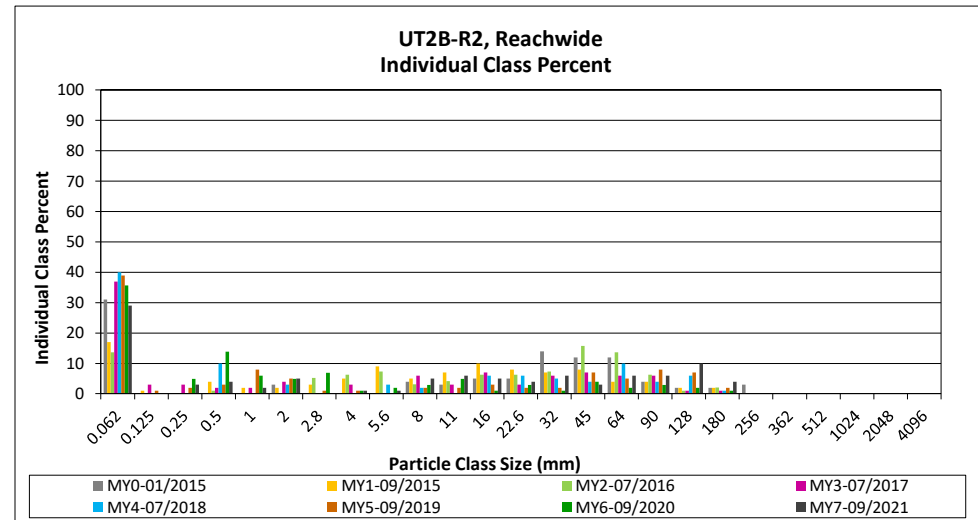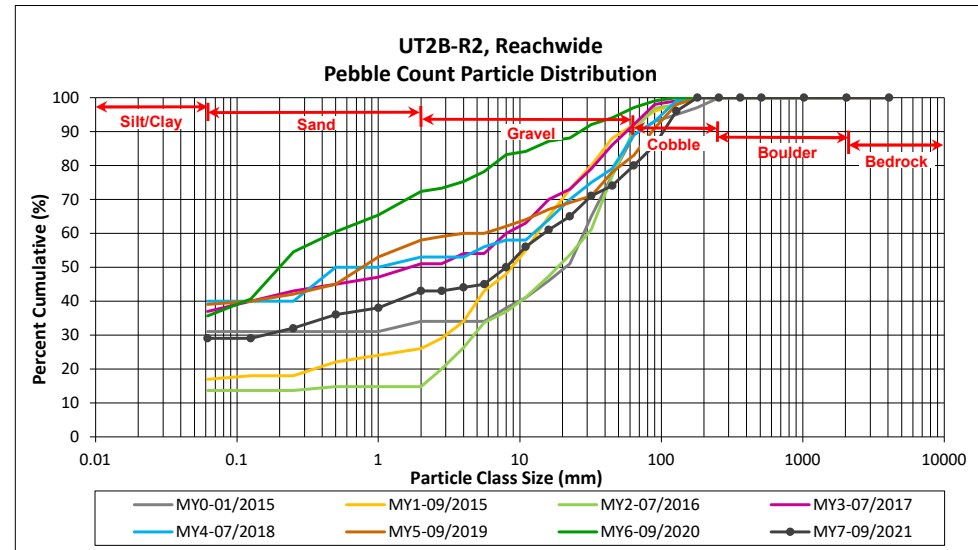

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2B-R2, Cross-Section 9

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	5	5	9
GRAVEL	Very Fine	2.0	2.8	4	4	13
	Very Fine	2.8	4.0	9	9	22
	Fine	4.0	5.6	11	11	33
	Fine	5.6	8.0	8	8	41
	Medium	8.0	11.0	4	4	45
	Medium	11.0	16.0	15	15	60
	Coarse	16.0	22.6	7	7	67
	Coarse	22.6	32	6	6	73
	Very Coarse	32	45	5	5	78
	Very Coarse	45	64	7	7	85
COBBLE	Small	64	90	9	9	94
	Small	90	128	5	5	99
	Large	128	180	1	1	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 9 Channel materials (mm)	
D ₁₆ =	3.2
D ₃₅ =	6.1
D ₅₀ =	12.5
D ₈₄ =	60.9
D ₉₅ =	96.6
D ₁₀₀ =	180.0

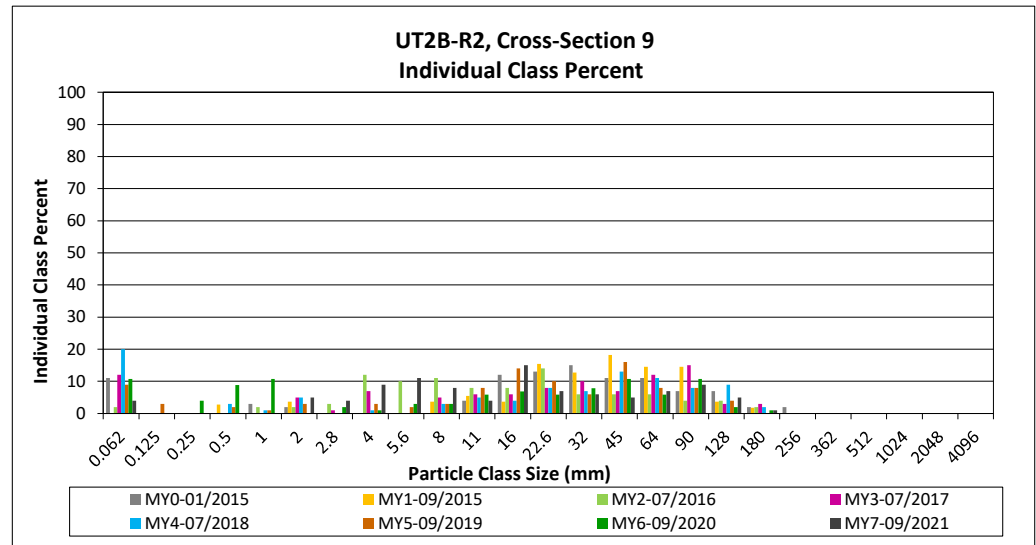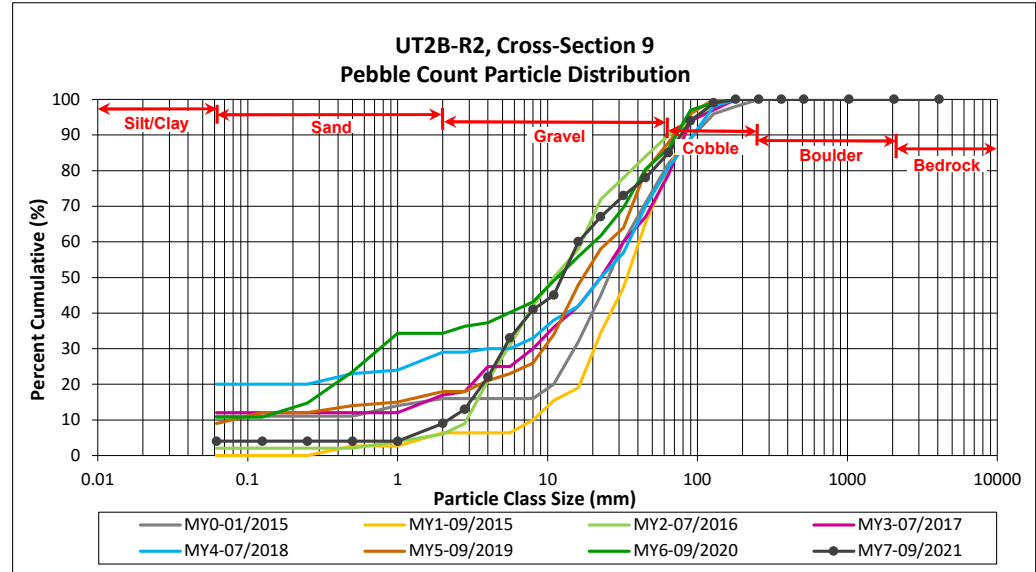

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	3	16	19	19	19
SAND	Very fine	0.062	0.125		2	2	2	21
	Fine	0.125	0.250					21
	Medium	0.25	0.50	1	3	4	4	25
	Coarse	0.5	1.0		6	6	6	31
	Very Coarse	1.0	2.0	2	7	9	9	40
GRAVEL	Very Fine	2.0	2.8					40
	Very Fine	2.8	4.0					40
	Fine	4.0	5.6					40
	Fine	5.6	8.0		1	1	1	41
	Medium	8.0	11.0		1	1	1	42
	Medium	11.0	16.0	1		1	1	43
	Coarse	16.0	22.6	2	1	3	3	46
	Coarse	22.6	32	3	2	5	5	51
	Very Coarse	32	45	3	5	8	8	59
	Very Coarse	45	64	7	3	10	10	69
COBBLE	Small	64	90	10	1	11	11	80
	Small	90	128	8	1	9	9	89
	Large	128	180	6	1	7	7	96
	Large	180	256	2		2	2	98
BOULDER	Small	256	362	1		1	1	99
	Small	362	512					99
	Medium	512	1024	1		1	1	100
BEDROCK	Bedrock	1024	2048					100
Total				50	50	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	1.4
D ₅₀ =	29.8
D ₈₄ =	105.3
D ₉₅ =	171.4
D ₁₀₀ =	1024.0

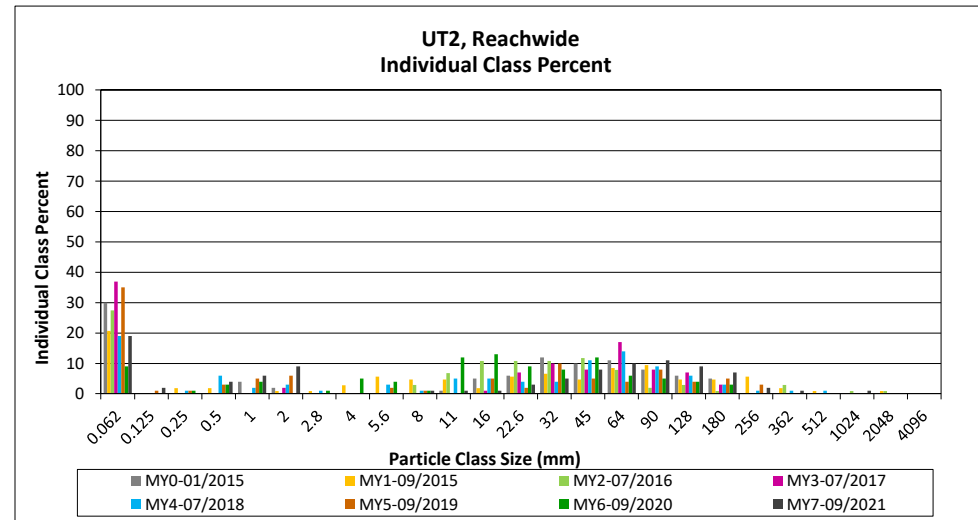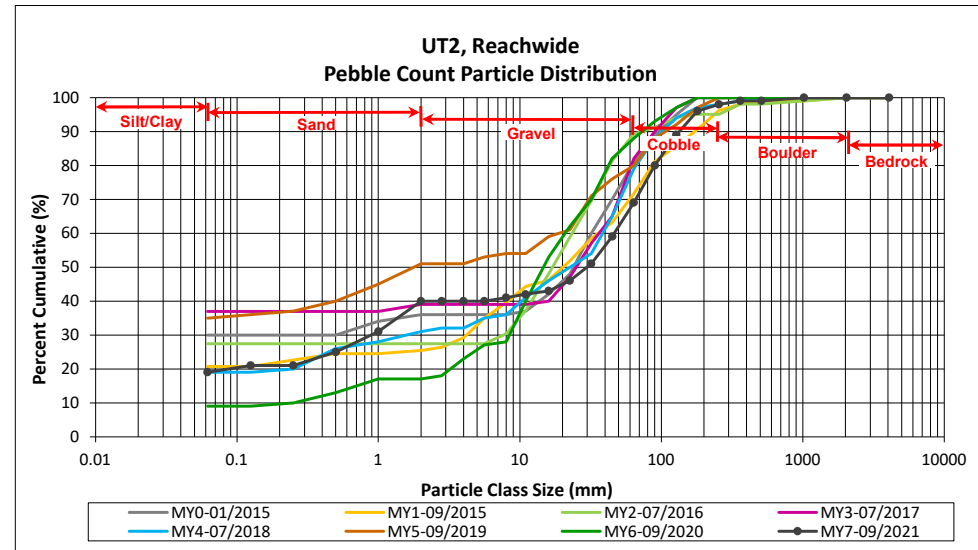

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2-R1, Cross-Section 11

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	10	10	10
SAND	Very fine	0.062	0.125			10
	Fine	0.125	0.250			10
	Medium	0.25	0.50			10
	Coarse	0.5	1.0	2	2	12
	Very Coarse	1.0	2.0	6	6	18
GRAVEL	Very Fine	2.0	2.8			18
	Very Fine	2.8	4.0			18
	Fine	4.0	5.6	4	4	22
	Fine	5.6	8.0	2	2	24
	Medium	8.0	11.0	2	2	26
	Medium	11.0	16.0	2	2	28
	Coarse	16.0	22.6	4	4	32
	Coarse	22.6	32	4	4	36
	Very Coarse	32	45	6	6	42
	Very Coarse	45	64	12	12	54
COBBLE	Small	64	90	26	26	80
	Small	90	128	8	8	88
	Large	128	180	8	8	96
	Large	180	256	4	4	100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 11 Channel materials (mm)	
D ₁₆ =	1.6
D ₃₅ =	29.3
D ₅₀ =	56.9
D ₈₄ =	107.3
D ₉₅ =	172.5
D ₁₀₀ =	256.0

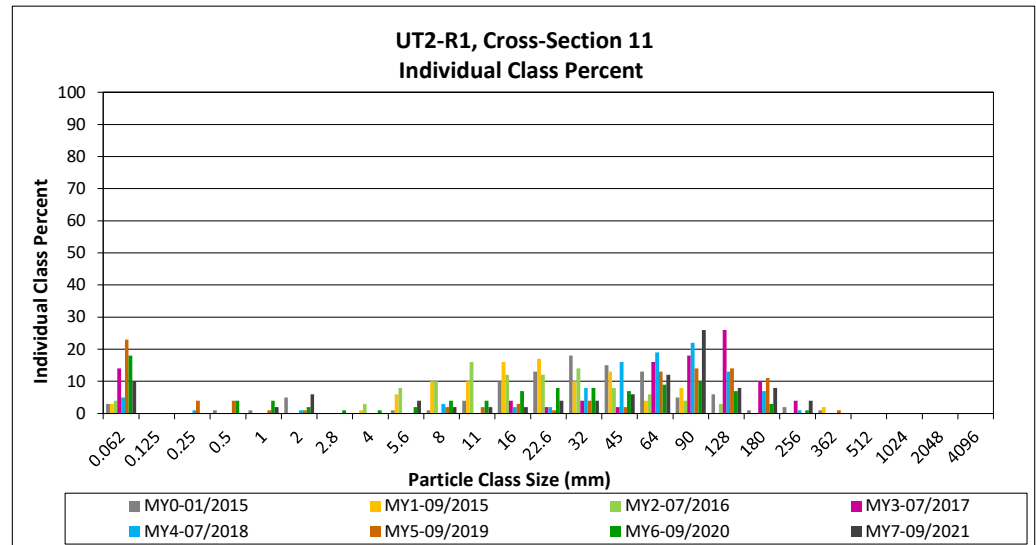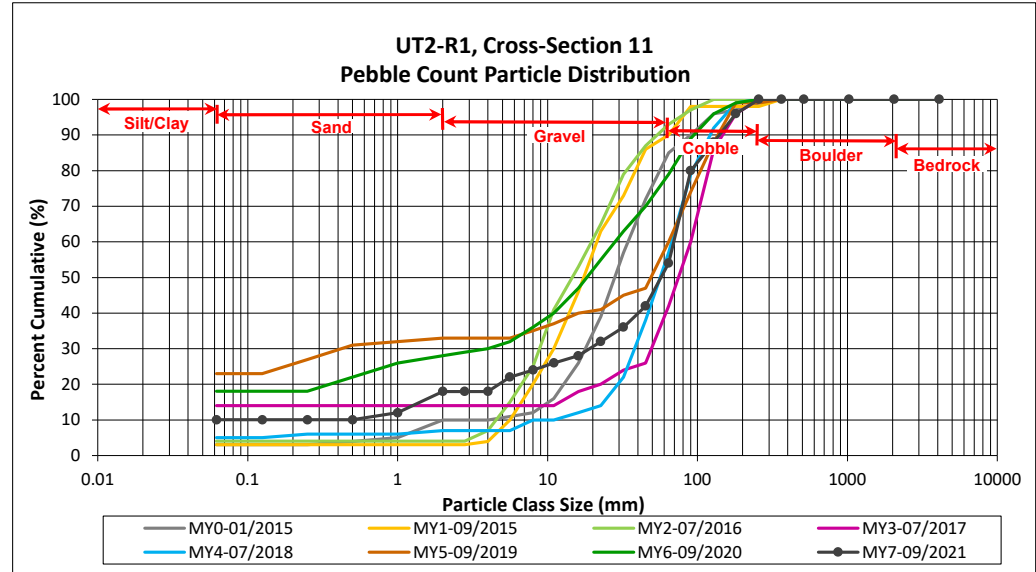

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2-R1, Cross-Section 12

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	4	4	8
GRAVEL	Very Fine	2.0	2.8			8
	Very Fine	2.8	4.0			8
	Fine	4.0	5.6			8
	Fine	5.6	8.0			8
	Medium	8.0	11.0			8
	Medium	11.0	16.0	4	4	12
	Coarse	16.0	22.6	6	6	18
	Coarse	22.6	32	4	4	22
	Very Coarse	32	45	4	4	26
	Very Coarse	45	64	14	14	40
COBBLE	Small	64	90	34	34	74
	Small	90	128	20	20	94
	Large	128	180	6	6	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 12 Channel materials (mm)	
D ₁₆ =	20.1
D ₃₅ =	56.4
D ₅₀ =	70.8
D ₈₄ =	107.3
D ₉₅ =	135.5
D ₁₀₀ =	180.0

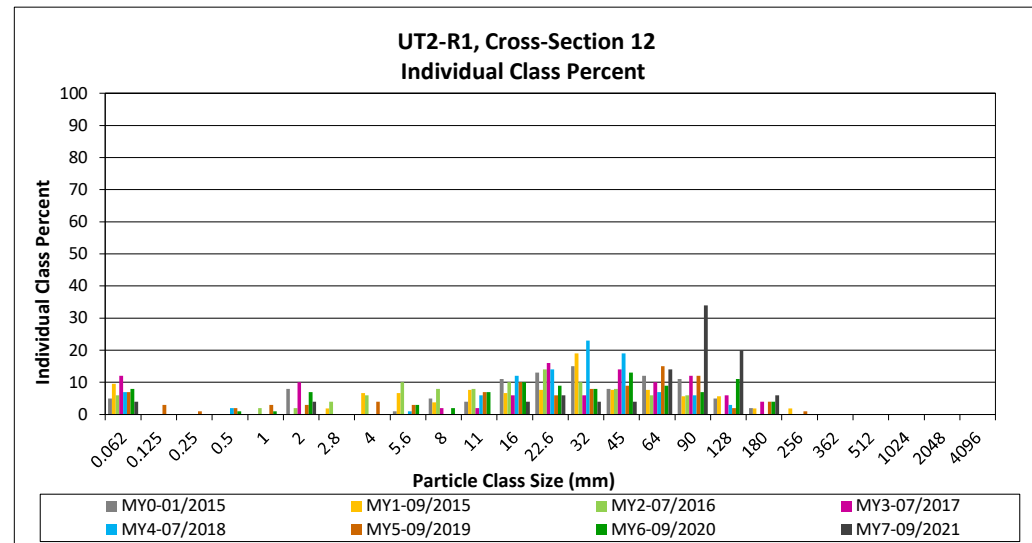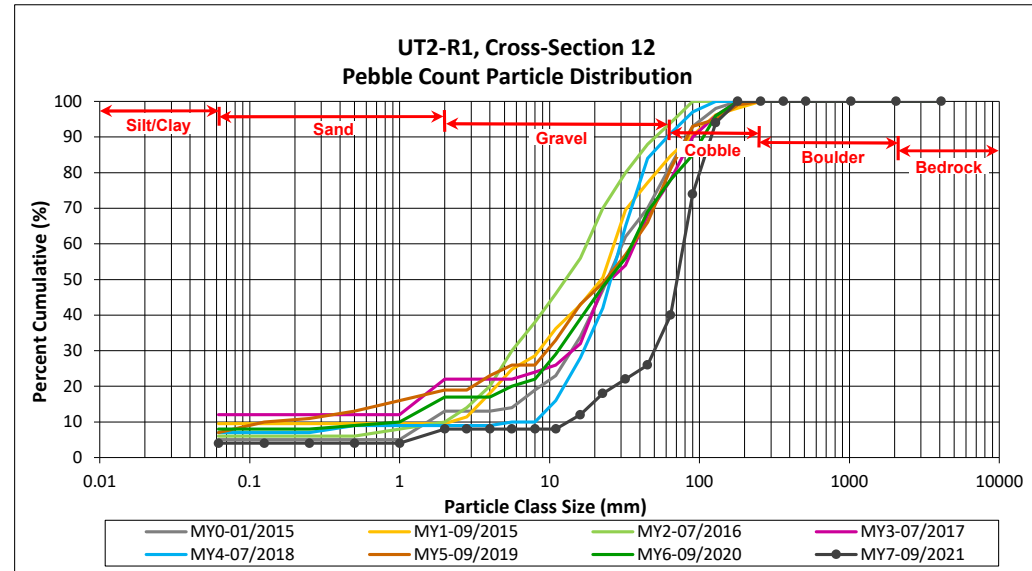

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT1B, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	7	21	28	28	28
SAND	Very fine	0.062	0.125					28
	Fine	0.125	0.250					28
	Medium	0.25	0.50					28
	Coarse	0.5	1.0					28
	Very Coarse	1.0	2.0	1	3	4	4	32
GRAVEL	Very Fine	2.0	2.8		1	1	1	33
	Very Fine	2.8	4.0		2	2	2	35
	Fine	4.0	5.6		4	4	4	39
	Fine	5.6	8.0		6	6	6	45
	Medium	8.0	11.0	1	4	5	5	50
	Medium	11.0	16.0	2	5	7	7	57
	Coarse	16.0	22.6	3	1	4	4	61
	Coarse	22.6	32	10	1	11	11	72
	Very Coarse	32	45	4	2	6	6	78
	Very Coarse	45	64	3		3	3	81
COBBLE	Small	64	90	5		5	5	86
	Small	90	128	6		6	6	92
	Large	128	180	7		7	7	99
	Large	180	256	1		1	1	100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
BEDROCK	Large/Very Large	1024	2048					100
	Bedrock	2048	>2048					100
Total				50	50	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	Silt/Clay
D ₃₅ =	4.0
D ₅₀ =	11.0
D ₈₄ =	78.5
D ₉₅ =	148.1
D ₁₀₀ =	256.0

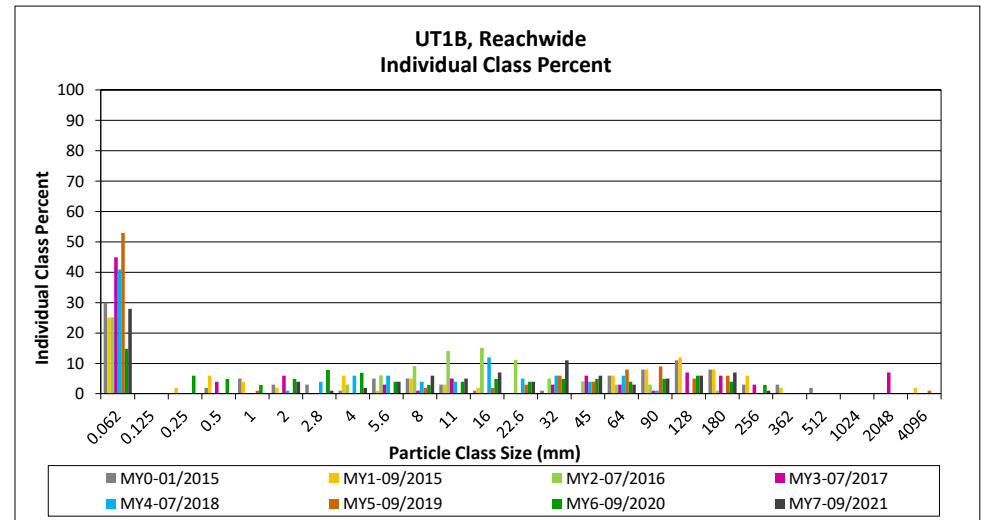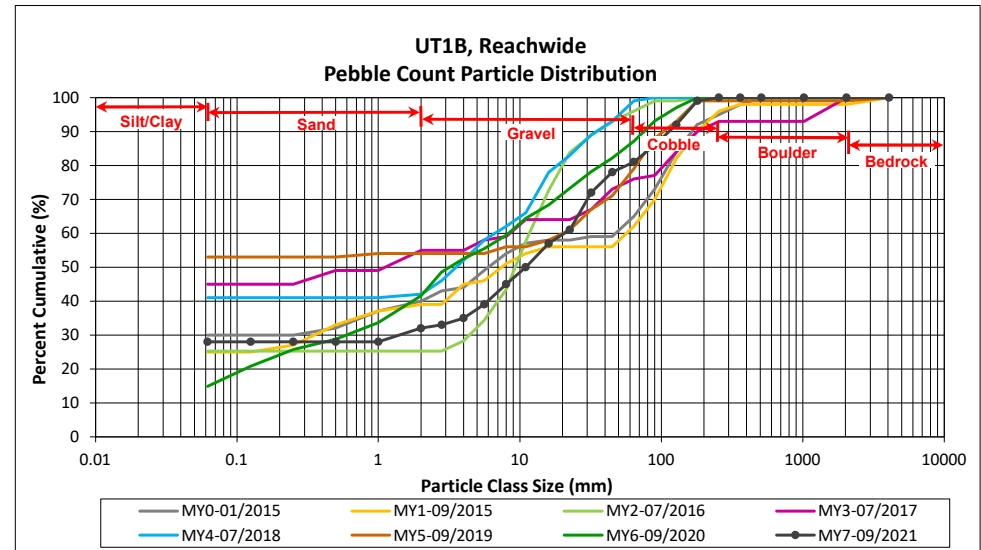

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT1B-R1, Cross-Section 15

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	5	5	5
SAND	Very fine	0.062	0.125			5
	Fine	0.125	0.250			5
	Medium	0.25	0.50			5
	Coarse	0.5	1.0			5
	Very Coarse	1.0	2.0	1	1	6
GRAVEL	Very Fine	2.0	2.8	4	4	10
	Very Fine	2.8	4.0			10
	Fine	4.0	5.6	5	5	15
	Fine	5.6	8.0	7	7	22
	Medium	8.0	11.0	11	11	33
	Medium	11.0	16.0	13	13	46
	Coarse	16.0	22.6	10	10	56
	Coarse	22.6	32	2	2	58
	Very Coarse	32	45	3	3	61
	Very Coarse	45	64	5	5	66
COBBLE	Small	64	90	10	10	76
	Small	90	128	10	10	86
	Large	128	180	11	11	97
	Large	180	256	2	2	99
BOULDER	Small	256	362	1	1	100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 15 Channel materials (mm)	
D ₁₆ =	5.9
D ₃₅ =	11.7
D ₅₀ =	18.4
D ₈₄ =	119.3
D ₉₅ =	169.2
D ₁₀₀ =	362.0

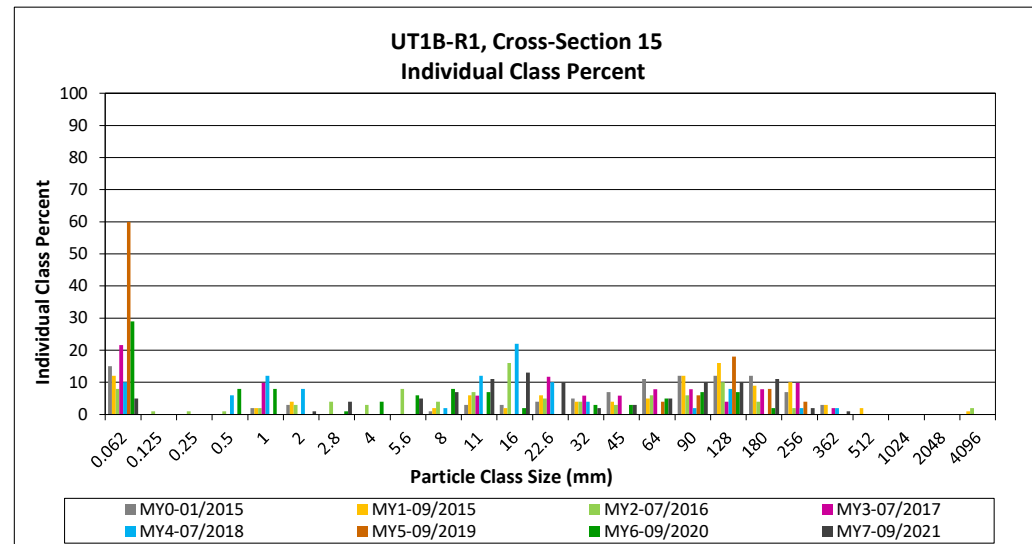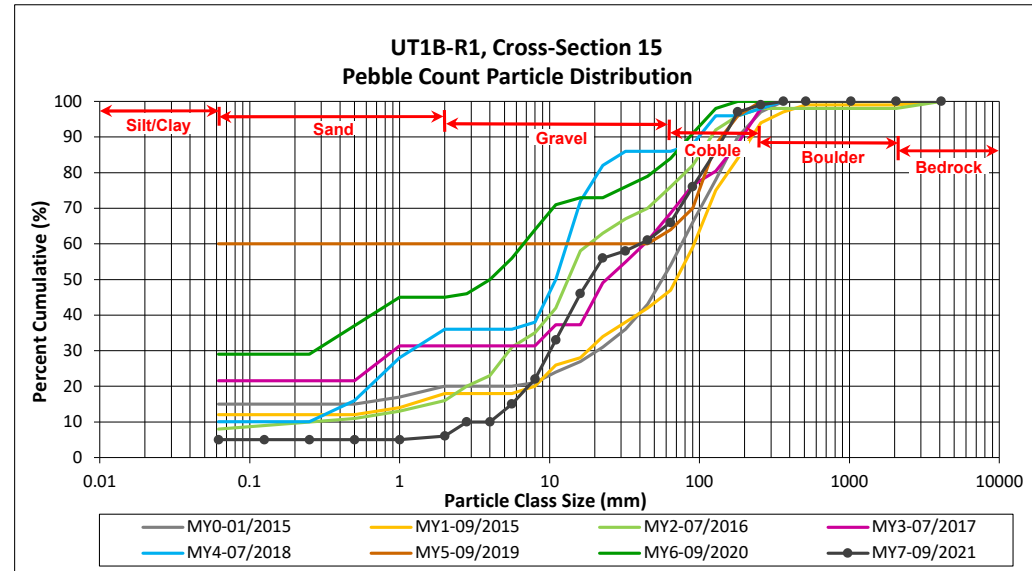

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2C-R2, Reachwide

Particle Class		Diameter (mm)		Particle Count			Reach Summary	
		min	max	Riffle	Pool	Total	Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	1	7	8	8	8
SAND	Very fine	0.062	0.125		2	2	2	10
	Fine	0.125	0.250		9	9	9	19
	Medium	0.25	0.50	2	5	7	7	26
	Coarse	0.5	1.0	1	6	7	7	33
	Very Coarse	1.0	2.0	1	5	6	6	39
GRAVEL	Very Fine	2.0	2.8					39
	Very Fine	2.8	4.0					39
	Fine	4.0	5.6					39
	Fine	5.6	8.0		1	1	1	40
	Medium	8.0	11.0	1	3	4	4	44
	Medium	11.0	16.0	3	4	7	7	51
	Coarse	16.0	22.6	3	3	6	6	57
	Coarse	22.6	32	9	1	10	10	67
	Very Coarse	32	45	5	1	6	6	73
	Very Coarse	45	64	9		9	9	82
COBBLE	Small	64	90	7		7	7	89
	Small	90	128	1	3	4	4	93
	Large	128	180	5		5	5	98
	Large	180	256	2		2	2	100
BOULDER	Small	256	362					100
	Small	362	512					100
	Medium	512	1024					100
BEDROCK	Large/Very Large	1024	2048					100
	Bedrock	2048	>2048					100
Total				50	50	100	100	100

Reachwide Channel materials (mm)	
D ₁₆ =	0.2
D ₃₅ =	1.3
D ₅₀ =	15.2
D ₈₄ =	70.5
D ₉₅ =	146.7
D ₁₀₀ =	256.0

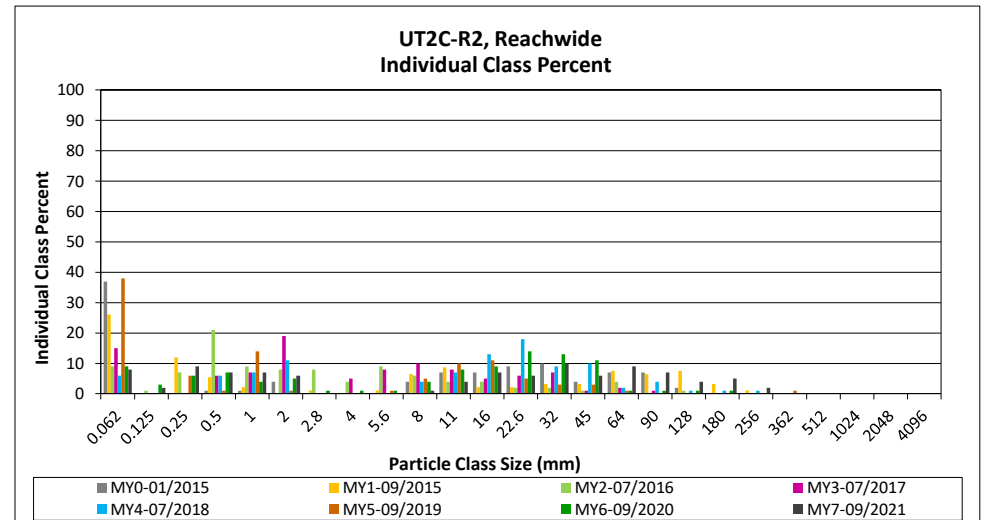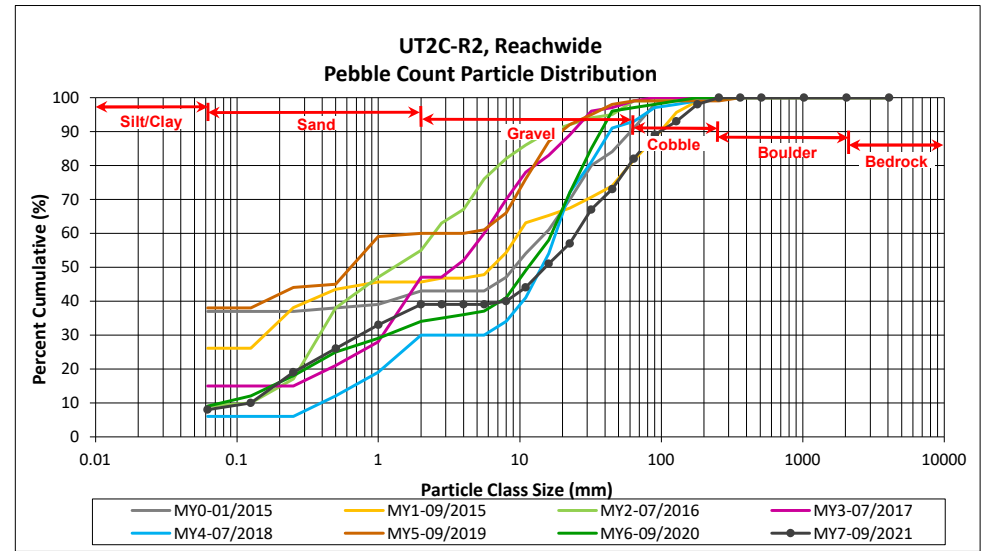

Reachwide and Cross-Section Pebble Count Plots

Hopewell Stream Mitigation Site



DMS Project No. 95352

Monitoring Year 7 - 2021

UT2C-R2, Cross-Section 16

Particle Class		Diameter (mm)		Riffle 100-Count	Summary	
		min	max		Class Percentage	Percent Cumulative
SILT/CLAY	Silt/Clay	0.000	0.062	4	4	4
SAND	Very fine	0.062	0.125			4
	Fine	0.125	0.250			4
	Medium	0.25	0.50			4
	Coarse	0.5	1.0			4
	Very Coarse	1.0	2.0	4	4	8
GRAVEL	Very Fine	2.0	2.8			8
	Very Fine	2.8	4.0			8
	Fine	4.0	5.6	2	2	10
	Fine	5.6	8.0	6	6	16
	Medium	8.0	11.0	8	8	24
	Medium	11.0	16.0	12	12	36
	Coarse	16.0	22.6	18	18	54
	Coarse	22.6	32	16	16	70
	Very Coarse	32	45	16	16	86
	Very Coarse	45	64	4	4	90
COBBLE	Small	64	90	8	8	98
	Small	90	128			98
	Large	128	180	2	2	100
	Large	180	256			100
BOULDER	Small	256	362			100
	Small	362	512			100
	Medium	512	1024			100
BEDROCK	Large/Very Large	1024	2048			100
	Bedrock	2048	>2048			100
Total				100	100	100

Cross-Section 16 Channel materials (mm)	
D ₁₆ =	8.0
D ₃₅ =	15.5
D ₅₀ =	20.9
D ₈₄ =	43.1
D ₉₅ =	79.2
D ₁₀₀ =	180.0

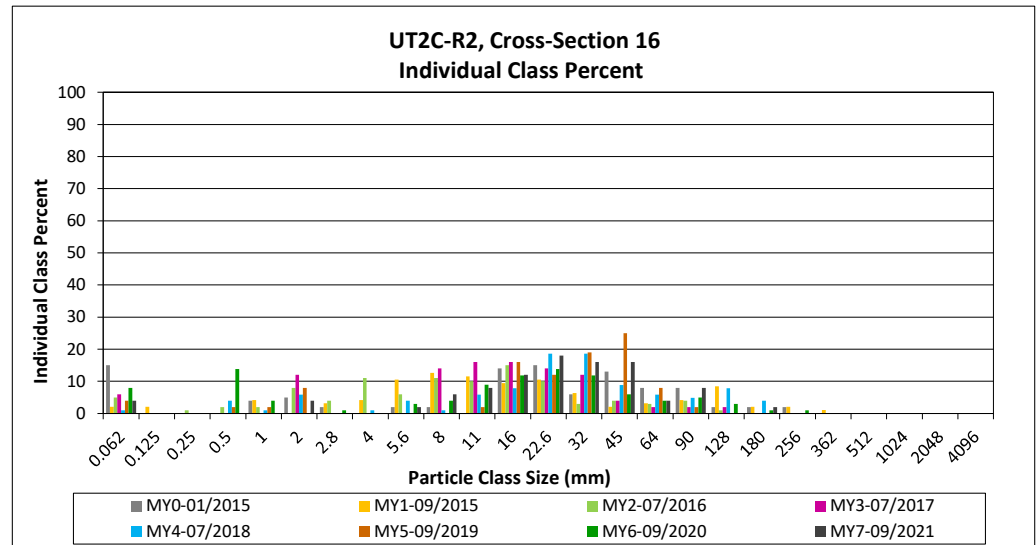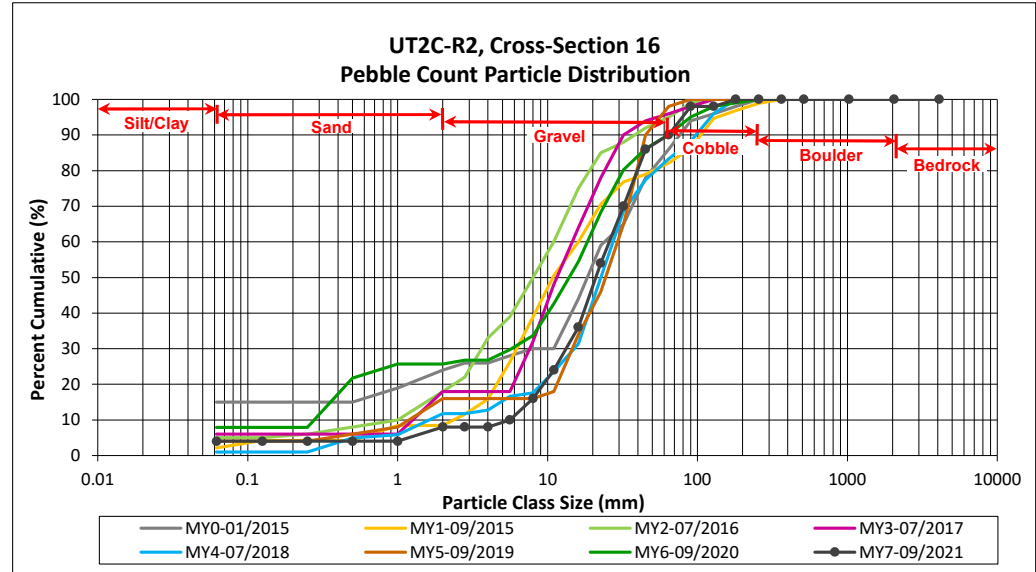

APPENDIX 5. Hydrology Summary Data

Table 13a. Verification of Bankfull Events

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Reach	Monitoring Year	Date of Data Collection	Date of Occurrence	Method
UT1B Reach 1	MY1	3/25/2015	Unknown	Crest Gage
		7/9/2015	Unknown	Crest Gage
		8/6/2015	8/6/2015	Stream Gage
		10/3/2015	10/3/2015	Stream Gage
		11/5/2015	11/2/2015	Crest/Stream Gage
	MY2	2/16/2016	2/16/2016	Stream Gage
		4/19/2016	Unknown	Crest Gage
	MY3	1/2/2017	1/2/2017	Stream Gage
		4/6/2017	4/6/2017	Stream Gage
		4/24/2017	4/24/2017	Stream Gage
		5/5/2017	5/5/2017	Stream Gage
		5/24/2017	5/24/2017	Stream Gage
		6/21/2017	6/21/2017	Stream Gage
		7/8/2017	7/8/2017	Stream Gage
	MY4	9/1/2017	9/1/2017	Stream Gage
		7/23/2018	7/23/2018	Stream Gage
		8/3/2018	8/3/2018	Stream Gage
		8/20/2018	8/20/2018	Stream Gage
		8/31/2018	8/31/2018	Stream Gage
		9/15/2018	9/15/2018	Stream Gage
		9/16/2018 ¹	9/16/2018	Stream Gage
	9/27/2018	9/27/2018	Stream Gage	
	MY5	10/11/2018	10/11/2018	Stream Gage
		1/11/2019	1/11/2019	Stream Gage
		1/19/2019	1/19/2019	Stream Gage
		1/21/2019	1/21/2019	Stream Gage
		2/16/2019	2/16/2019	Stream Gage
		2/21/2019	2/21/2019	Stream Gage
		2/22/2019	2/22/2019	Stream Gage
		3/3/2019	3/3/2019	Stream Gage
		4/5/2019	4/5/2019	Stream Gage
		4/8/2019	4/8/2019	Stream Gage
		4/13/2019	4/13/2019	Stream Gage
		6/9/2019	6/9/2019	Stream Gage
		9/9/2019	Unknown	Crest/Stream Gage
	MY6	1/3/2020	1/3/2020	Stream Gage
		1/24/2020	1/24/2020	Stream Gage
		2/6/2020 ²	2/6/2020	Stream Gage
		2/7/2020	2/7/2020	Stream Gage
		2/13/2020	2/13/2020	Stream Gage
		3/25/2020	3/25/2020	Stream Gage
		4/13/2020	4/13/2020	Stream Gage
		4/30/2020	4/13/2020	Stream Gage
		5/19/2020	5/19/2020	Stream Gage
		5/20/2020	5/20/2020	Stream Gage
		5/21/2020 ²	5/21/2020	Stream Gage
		5/24/2020	5/24/2020	Stream Gage
5/27/2020		5/27/2020	Stream Gage	
5/28/2020		5/28/2020	Stream Gage	
5/29/2020	5/29/2020	Stream Gage		
7/23/2020	7/23/2020	Stream Gage		
9/18/2020	9/18/2020	Crest/Stream Gage		

¹ Two bankfull events were documented on UT1B R1 during heavy rainfall related to the remnants of Hurricane Florence on 9/16/18.

² Two bankfull events were documented on 2/6/20 and 5/21/2020.

Table 13b. Verification of Bankfull Events

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Reach	Monitoring Year	Date of Data Collection	Date of Occurrence	Method
UT1B Reach 1	MY7	1/1/2021	1/2/2021	Stream Gage
		1/2/2021	1/2/2021	Stream Gage
		1/8/2021	1/8/2021	Stream Gage
		1/26/2021	1/26/2021	Stream Gage
		1/27/2021	1/27/2021	Stream Gage
		1/31/2021	1/31/2021	Stream Gage
		2/7/2021	2/7/2021	Stream Gage
		2/11/2021	2/11/2021	Stream Gage
		2/13/2021	2/13/2021	Stream Gage
		2/14/2021	2/14/2021	Stream Gage
		2/15/2021	2/15/2021	Stream Gage
		2/16/2021	2/16/2021	Stream Gage
		2/18/2021	2/18/2021	Stream Gage
		2/19/2021 ¹	2/19/2021	Stream Gage
		2/22/2021	2/22/2021	Stream Gage
		2/26/2021	2/26/2021	Stream Gage
		3/1/2021	3/1/2021	Stream Gage
		3/16/2021	3/16/2021	Stream Gage
		3/19/2021	3/19/2021	Stream Gage
		3/27/2021	3/27/2021	Stream Gage
		3/28/2021 ¹	3/28/2021	Stream Gage
		3/31/2021	3/31/2021	Stream Gage
		5/10/2021	5/10/2021	Stream Gage
		5/29/2021	5/29/2021	Stream Gage
		6/3/2021	6/3/2021	Crest/Stream Gage
		6/10/2021	6/10/2021	Stream Gage
6/22/2021	6/22/2021	Stream Gage		
7/8/2021	7/8/2021	Stream Gage		
8/7/2021	8/7/2021	Stream Gage		
8/18/2021	8/18/2021	Stream Gage		
9/22/2021 ¹	9/22/2021	Stream Gage		

¹ Two bankfull events were documented on 2/19/21, 3/28/2021, and 9/22/2021.

Table 13c. Verification of Bankfull Events

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Reach	Monitoring Year	Date of Data Collection	Date of Occurrence	Method
UT2 Reach 2	MY1	7/9/2015	Unknown	Crest Gage
		10/3/2015	10/3/2015	Stream Gage
		11/5/2015	11/2/2015	Crest/Stream Gage
	MY2	1/6/2016	1/6/2016	Stream Gage
		2/3/2016	2/3/2016	Stream Gage
		2/10/2016	2/10/2016	Stream Gage
		2/16/2016	2/16/2016	Stream Gage
		3/27/2016	3/27/2016	Stream Gage
		4/19/2016	Unknown	Crest Gage
		6/15/2016	6/15/2016	Stream Gage
	MY3	4/24/2017	4/24/2017	Stream Gage
		5/5/2017	5/5/2017	Stream Gage
		6/5/2017	6/5/2017	Stream Gage
		9/1/2017	9/1/2017	Stream Gage
	MY4	7/23/2018	7/23/2018	Stream Gage
		7/25/2018	7/25/2018	Stream Gage
		8/20/2018	8/20/2018	Stream Gage
		8/31/2018	8/31/2018	Stream Gage
		9/16/2018	9/16/2018	Stream Gage
		10/11/2018	10/11/2018	Stream Gage
	MY5	1/11/2019	1/11/2019	Stream Gage
		1/21/2019	1/21/2019	Stream Gage
		3/18/2019	Unknown	Crest Gage
		4/13/2019	4/13/2019	Stream Gage
		9/9/2019	Unknown	Crest Gage
	MY6	1/24/2020	1/24/2020	Stream Gage
		2/6/2020	2/26/2020	Stream Gage
		4/30/2020	4/30/2020	Stream Gage
	MY7	6/3/2021	6/3/2021	Crest Gage
		6/11/2021	6/11/2021	Stream Gage
8/18/2021		8/18/2021	Stream Gage	
10/1/2021		Unknown	Crest Gage	

Table 13d. Verification of Bankfull Events

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

Reach	Monitoring Year	Date of Data Collection	Date of Occurrence	Method
UT2A Reach 2	MY1	3/25/2015	Unknown	Crest Gage
		10/3/2015	10/3/2015	Stream Gage
		11/5/2015	11/2/2015	Crest Gage
	MY2	1/20/2016	1/20/2016	Stream Gage
		6/15/2016	6/15/2016	Stream Gage
	MY3	1/9/2017	1/9/2017	Stream Gage
		5/5/2017	5/5/2017	Stream Gage
		6/21/2017	6/21/2017	Stream Gage
		7/8/2017	7/8/2017	Stream Gage
	MY4	9/1/2017	9/1/2017	Stream Gage
		7/23/2018	7/23/2018	Stream Gage
		8/20/2018	8/20/2018	Stream Gage
		8/31/2018	8/31/2018	Stream Gage
	MY5	9/16/2018	9/16/2018	Stream Gage
		1/11/2019	1/11/2019	Stream Gage
		1/21/2019	1/21/2019	Stream Gage
		3/18/2019	Unknown	Crest Gage
	MY6	4/13/2019	4/13/2019	Stream Gage
		1/21/2020	1/21/2020	Stream Gage
		1/22/2020 ¹	1/22/2020	Stream Gage
		1/24/2020	1/24/2020	Stream Gage
		2/6/2020	2/6/2020	Stream Gage
		2/28/2020	2/28/2020	Stream Gage
		2/29/2020	2/29/2020	Stream Gage
		3/1/2020	3/1/2020	Stream Gage
		3/8/2020	3/8/2020	Stream Gage
		4/13/2020	4/13/2020	Stream Gage
		5/24/2020	5/24/2020	Stream Gage
	MY7	5/28/2020	5/28/2020	Stream Gage
		5/29/2020	5/29/2020	Stream Gage
		1/3/2021	1/3/2021	Stream Gage
		1/10/2021	1/10/2021	Stream Gage
		1/29/2021	1/29/2021	Stream Gage
2/3/2021		2/3/2021	Stream Gage	
2/8/2021		2/8/2021	Stream Gage	
2/15/2021		2/15/2021	Stream Gage	
2/20/2021		2/20/2021	Stream Gage	
3/31/2021		3/31/2021	Stream Gage	
6/3/2021	6/3/2021	Crest/Stream Gage		
6/11/2021	6/11/2021	Stream Gage		
8/18/2021	8/18/2021	Stream Gage		

¹ Two bankfull events were documented on 1/22/2020.

Table 13e. Verification of Bankfull Events

Hopewell Stream Mitigation Site
 DMS Project No. 95352
Monitoring Year 7 - 2021


Reach	Monitoring Year	Date of Data Collection	Date of Occurrence	Method
UT2B Reach 2	MY1	3/25/2015	Unknown	Crest Gage
		7/9/2015	Unknown	Crest Gage
		10/3/2015	10/3/2015	Stream Gage
	MY2	1/25/2016	1/25/2016	Stream Gage
		2/16/2016	2/16/2016	Stream Gage
		4/19/2016	Unknown	Crest Gage
	MY3	4/6/2017	4/6/2017	Stream Gage
		4/24/2017	4/24/2017	Stream Gage
		5/5/2017	5/5/2017	Stream Gage
		5/24/2017	5/24/2017	Stream Gage
	6/21/2017	6/21/2017	Stream Gage	
	MY4	9/16/2018	9/16/2018	Stream Gage
	MY5	1/11/2019	1/11/2019	Stream Gage
		1/21/2019	1/21/2019	Stream Gage
3/18/2019	Unknown	Crest Gage		
MY7	6/3/2021	Unknown	Crest Gage	
UT2C Reach 2	MY1	10/3/2015	10/3/2015	Stream Gage
		11/5/2015	11/2/2015	Crest Gage
	MY2	1/6/2016	1/7/2016	Stream Gage
		1/20/2016	1/20/2016	Stream Gage
		2/14/2016	2/15/2016	Stream Gage
		4/19/2016	Unknown	Crest Gage
	MY3	1/9/2017	1/9/2017	Stream Gage
	MY5	1/11/2019	1/11/2019	Stream Gage
		1/21/2019	1/21/2019	Stream Gage
		2/21/2019	2/21/2019	Stream Gage
		3/18/2019	Unknown	Crest Gage
		4/13/2019	4/14/2019	Stream Gage
	9/9/2019	Unknown	Crest Gage	
	MY6	5/29/2020	5/29/2020	Stream Gage
MY7	3/31/2021	3/31/2021	Stream Gage	
	6/3/2021	Unknown	Crest Gage	
	6/10/2021	6/10/2021	Stream Gage	

Monthly Rainfall Plot

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 7 - 2021

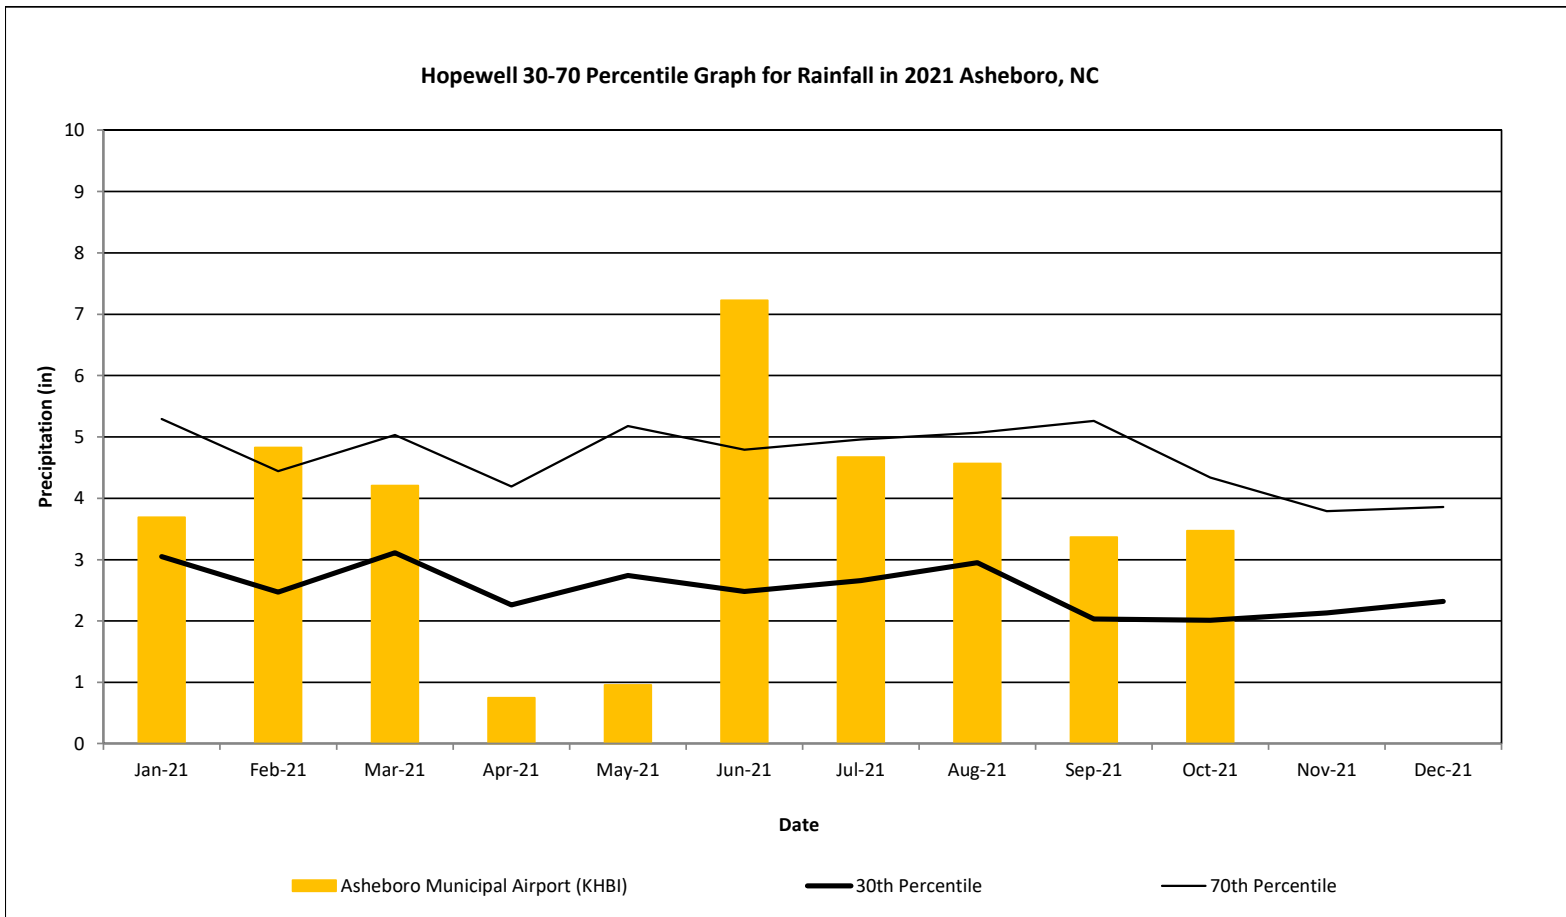

30th and 70th percentile rainfall data collected from weather station Asheboro 2 W, in Asheboro, NC (USDA, 2000).

APPENDIX 6. IRT MY4 Credit Release Site Walk Meeting Minutes



MEETING NOTES

MEETING: IRT MY4 Credit Release Site Walk
Hopewell Mitigation Site
Yadkin 03040104; Randolph County, NC
DEQ Contract No. 4642
DMS Project No. 95352
Wildlands Project No. 005-02133

DATE: Wednesday, May 29, 2019

LOCATION: Pisgah Covered Bridge Road
Asheboro, NC

Attendees

Todd Tugwell, USACE	Melonie Allen, DMS	Shawn Wilkerson, Wildlands
Kim Browning, USACE	Paul Wiesner, DMS	Jeff Keaton, Wildlands
Mac Haupt, DWR	Harry Tsomides, DMS	Kristi Suggs, Wildlands
Erin Davis, DWR	Joe Famularo, DMS	Ian Eckardt, Wildlands

Materials

Wildlands Engineering Hopewell Mitigation Site MY4 Monitoring Report dated December 13, 2018.

Meeting Notes

The purpose of the tour was to present the site to a group of IRT members and to get input into the condition of the site at this point in the monitoring period. Jeff Keaton of Wildlands Engineering, Inc. (Wildlands or WEI) began the meeting by giving the IRT members an overview of the project site. Then, portions of each of the project reaches were walked and discussed by the group.

1. UT2C

The tour began with Reaches 1 and 2 of UT2C. Jeff pointed out that the stream is spring fed and consistently has good flow. Reach 2 is a short reach where restoration was performed. The group only looked at a short section of this reach. Reach 1 is an enhancement reach. Todd Tugwell asked what work was done on the reach. Jeff and Shawn Wilkerson explained that the work consisted of fencing out cattle, planting trees in the left floodplain buffer zone, and treating privet. Todd noted several small privet trees, mostly in the right buffer area. Jeff explained that Wildlands has been treating privet every fall but not necessarily every location every year.

At this point, Erin Davis of DWR asked about the status of the issues with the fencing on the project. Jeff explained that there were a few spots where the fence was incorrectly installed inside the easement in short sections or a post was placed right on an easement corner. There was also an area on Little River where cows

were able to get into the easement and into the river. Jeff explained that the fencing issues have been corrected except for one small area on UT1 B where the landowner has refused to allow the fence to be moved.

Shawn explained that Wildlands has discussed this area with the landowner multiple times. Wildlands attempted to modify the easement, so that the existing fence would be outside of it, but DMS would not allow it. Shawn stated the next and last step would be for Wildlands to send a letter explaining that if the fence is not relocated outside of the easement, that State would further pursue the issue and legally require the fence to be moved. Shawn said that the letter would go out within a few of weeks after the completion of the site visit.

2. UT2A Reach 2

The tour continued with UT2A Reach 2. The stream was difficult to access due to vegetation growth within the easement. A short section was walked. The group seemed to agree that the stream looked stable and that the tree growth was good. Shawn mentioned that this small stream has always had flow.

3. UT2B

Next, the group walked the lower section of UT2B. Todd was interested to see how much privet remained along this reach. Many dead privet plants that had been treated the previous fall were observed but a few plants remained.

4. UT2A Reach 1

The group walked a portion of UT2A next. Jeff explained that this Enhancement I reach was constructed by adding a series of riffles to raise the bed of the stream. Portions of the reach were completely reconstructed. It was noted that there was previously a lot of privet in this area too, but that it has been successfully treated.

5. UT2 Reach 1

The group walked a short section of this reach. It was difficult to access due to dense vegetation growth within the easement. It was noted that the stream looked stable.

6. UT1B Reach 1

At this point, the group drove to the east side of the property. The first area visited on the east side of the site was UT1B Reach 1. There was discussion about this area because the planted vegetation is not performing as well as the rest of the site and sweetgums and pines have proliferated in the last couple of years. Jeff explained that, due to the cut in this area, the soils were not as good for growing the planted trees. Todd stated that this area is not meeting the intent of the mitigation plan or the success criteria for vegetation. It was also noted that the stream channel has a lot of herbaceous growth, probably due to the open canopy.

Todd and Mac suggested that Wildlands should remove the sweetgums and some of the pines and replant the trees specified in the planting plan, possibly as containerized plants rather than bare roots. Shawn indicated that he agreed, and Wildlands would conduct the activities during the next planting season. There was also an agreement that no work, such as removing in-stream vegetation or sediment by raking, hand digging, or other mechanical means, should be conducted in the channel. Instead, the planting of some of the proposed container plants, closer to the stream's top of bank, would be implemented in order to shade out the in-stream wetland vegetation.

The group also looked at the area where the landowner would not allow the fence to be moved (previously referenced in Section 1. UT2C). During this discussion, Kristi Suggs said she believed the corner fence post was about 32 feet inside the easement. Jeff stated that the buffer width in this area is still at least 50 feet. Shawn



reiterated his earlier statement from when the group was walking UT2C. The IRT also felt that the fence line should be moved out to the easement, reiterating Wildlands' and DMS' position.

Wildlands indicated that they will send the landowner a letter, within the next few weeks, asking the property owner once again to allow the fence line to be moved, in order to be easement-compliant, or the matter will be turned over to the State for possible legal action. Wildlands will let DMS look at the WEI letter before it is sent to the landowner. The letter will explain to the landowner that the fence needs to be moved into alignment with the easement and will give a timeline (60 days) for completion.

7. UT1A Reach 1

The group then walked to UT1A. There have been questions about the possibility that this stream is ephemeral. During the site visit the stream was flowing. Jeff and Ian Eckardt explained that Wildlands had installed a trail cam and had about 6 months of data indicating that the stream had flow continuously through that period. Todd asked what work had been done on this reach. Jeff stated that cows had been fenced out and supplemental planting had been done outside the woods line on the left floodplain.

8. Little River

The group walked a short portion of Little River. Shawn pointed out how successful the privet removal had been in this area. A large debris jam in the river was noted.

9. UT1B Reach 3

The last reach the group looked at was UT1B Reach 3. There have been some concerns that this reach, which is below the pond dam, would have issues with maintaining adequate flow frequencies. The stream was flowing on this day, and Wildlands indicated that flow frequencies have not been of issue on the reach.

10. Summary Discussion

Back at the vehicles, the group briefly discussed the overall site. Todd stated that the main issues are the vegetation problems on UT1B Reach 1, the remaining fencing issue on that reach, and on-going privet treatment throughout the site. The IRT agreed to release MY4 credits per the credit release schedule established in the approved Mitigation Plan.

These meeting minutes were prepared by Jeff Keaton and Kristi Suggs on June 6, 2019 and reviewed by Shawn Wilkerson on June 7, 2019 and represent the authors' interpretation of events. The minutes were subsequently revised on 6/14/2019 to incorporate comments received in an email from Harry Tsmoides with DMS on 6/12/2019.



APPENDIX 7. MY6 Sweetgum Treatment & Supplemental Planting
UT1B Reach 1 Photographs
Sweetgum Treatment Figure
MY6 Supplemental Planting – UT1 Reach 1 Summary Table



Right hillside at Station 303+00 – sweetgum treatment / plantings (05/13/2020)



Right hillside at Station 303+50 – sweetgum treatment / plantings (05/13/2020)



Left hillside at Station 303+50 – sweetgum treatment / plantings (05/13/2020)



Left hillside at Station 303+50 – looking upstream (05/13/2020)




Left easement corner at Station 303+50 – new fencing / plantings (05/13/2020)



Left easement corner at Station 303+50 – new fencing / plantings (05/13/2020)



2018 Aerial Photography



Sweetgum Treatments
 Hopewell Stream Mitigation Site
 DMS Project No. 95352
 Monitoring Year 7 - 2021
 Randolph County

MY6 Supplemental Planting - UT1B Reach 1 Summary Table

Hopewell Stream Mitigation Site

DMS Project No. 95352

Monitoring Year 6 - 2020

Scientific Name	Common Name	Size	Quantity
<i>Betula nigra</i>	River birch	3-gallon	18
<i>Quercus michauxii</i>	Swamp chestnut oak	3-gallon	9
		5-gallon	11
<i>Quercus phellos</i>	Willow oak	3-gallon	9
		5-gallon	11
<i>Quercus rubra</i>	Northern red oak	3-gallon	9
<i>Platanus occidentalis</i>	Sycamore	1-gallon	4
		3-gallon	9
		Total	80
