

Year 3 Monitoring Report

FINAL

MOCKINGBIRD SITE

NCDMS Project # 100021 (Contract # 7185)

USACE Action ID: SAW-2017-01505

DWR Project #20171040

Davie County, North Carolina

Yadkin River Basin

HUC 03040101



Prepared By:



Resource Environmental Solutions, LLC
For Environmental Banc & Exchange, LLC

Prepared For:

NC Department of Environmental Quality
Division of Mitigation Services

January 2024



3600 Glenwood Avenue, Suite 100
Raleigh, NC 27612

Corporate Headquarters
6575 W Loop S #300
Bellaire, TX 77401
Main: 713.520.5400

January 12, 2024

Harry Tsomides
NC DEQ Division of Mitigation Services
5 Ravenscroft Drive, Suite 102
Asheville, NC 28801

RE: Mockingbird Site: Year 3 Monitoring Report (NCDMS ID 100021)

Listed below are comments provided by DMS on January 3, 2024 regarding the Mockingbird Site: Year 3 Report and RES' responses.

Comments:

- Goals table (Pages 9-10) – If possible can RES add a column for Cumulative Monitoring Results to bring it up to the current reporting standard (see October 2020 Monitoring Table guidance on the DMS website)?
[The monitoring summary and parameters table in section 1.3 has been updated with the projects cumulative monitoring results.](#)
- In the Project Summary Section, please indicate that RES and DMS met onsite for a boundary inspection in September 2023, that DMS sent the inspection results by email on 9/15/2023, and that RES has either resolved or is actively working on resolving the identified boundary and potential stewardship transfer issues. Thank you for mapping those areas of boundary concern as well.
[The first paragraph of section 1.7 has been updated to reflect the language DMS has requested. RES will keep DMS updated as potential easement boundary issues are resolved.](#)
- When the site is treated for scattered invasives in 2024, please remember to map the treated areas in the MY4 (2024) report.
[RES will include the treated invasive polygons in the MY4 CCPV figure.](#)
- Thank you for providing the GW gauge data and graph as requested at the 2023 Credit Release meeting.
[Thank you.](#)

Table of Contents

1.0 Project Summary	6
1.1 Project Location and Description	6
1.2 Project Goals and Objectives	6
1.3 Project Success Criteria	7
Stream Restoration Success Criteria	8
Vegetation Success Criteria.....	8
1.4 Project Components.....	9
1.5 Stream Design/Approach	9
1.6 Construction and As-Built Conditions	13
1.7 Year 3 Monitoring Performance (MY3)	13
Vegetation	13
Stream Geomorphology.....	14
Stream Hydrology.....	14
Wetland Hydrology	14
2.0 Methods	15
3.0 References	16

Appendix A: Background Tables

Table 1: Project Mitigation Components
Table 2: Project Activity and Reporting History
Table 3: Project Contacts Table
Table 4: Project Background Information Table
Figure 1: Site Location Map

Appendix B: Visual Assessment Data

Figure 2: Current Conditions Plan View
Table 5. Visual Stream Morphology Stability Assessment
Table 6. Vegetation Condition Assessment
Vegetation Plot Photos
Monitoring Device Photos
Crossing Photos

Appendix C: Vegetation Plot Data

Table 7: Planted Species Summary
Table 8: Vegetation Plot Mitigation Success Summary
Table 9. Stem Count Total and Planted by Plot Species

Appendix D: Stream Measurement and Geomorphology Data

Table 10. Baseline Stream Data Summary
Table 11. Cross Section Morphology Data Table
Cross Section Overlay Plots

Appendix E: Hydrology Data

Table 12. 2023 Rainfall Summary
Table 13. Documentation of Geomorphically Significant Flow Events
Stream Flow Hydrographs
Table 14. 2023 Max Hydroperiod
Table 15. Summary of Groundwater Monitoring Results
Groundwater Hydrographs

1.0 Project Summary

1.1 Project Location and Description

The Mockingbird Site (the "Project") is located in Davie County, North Carolina, approximately eight miles west of Clemmons and five miles northwest of Bermuda Run. Water quality stressors affecting the Project included livestock production, agricultural production, and lack of riparian buffer. The Project presents 8,998 linear feet of stream restoration, enhancement, and preservation generating 6,427.833 Warm Stream Mitigation Units (SMU) along Hauser Creek and eight unnamed tributaries.

The Project's total easement area is 27.46 acres within the overall drainage area of 1,540 acres. The Project has two separate portions along Hauser Creek and in between those portions is the Scout Mitigation Bank. While each site could be developed independently of the other, the combined easements result in greater continuity of protected corridors along the main stem of Hauser Creek. The downstream end of the Project connects to the DMS Hauser Creek Mitigation Site, which closed out in 2017 and is now in NCDEQ stewardship. All easements combined total approximately 49.33 acres and 14,605 linear feet of stream that are protected in perpetuity. Approximately 10,400 LF of Hauser Creek is protected by these three projects and this is 60% of Hauser Creek's total length (Figure 1).

The stream design approach for the Project was to combine the analog method of natural channel design with analytical methods to evaluate stream flows and hydraulic performance of the channel and floodplain. The analog method involved the use of a reference reach, or "template" stream, adjacent to, nearby, or previously in the same location as the design reach. The template parameters of the analog reach were replicated to create the features of the design reach. The analog approach is useful when watershed and boundary conditions are similar between the design and analog reaches (Skidmore et al., 2001). Hydraulic geometry was developed using analytical methods to identify the design discharge.

The Project has been constructed and planted and will be monitored on a regular basis throughout the seven-year post-construction monitoring period, or until performance standards are met. The Project will be transferred to the NCDEQ Stewardship Program. This party shall serve as conservation easement holder and long-term steward for the property and will conduct periodic inspection of the site to ensure that restrictions required in the conservation easement are upheld. Funding will be supplied by the responsible party on a yearly basis until such time an endowment is established.

1.2 Project Goals and Objectives

Through the comprehensive analysis of the Project's maximum functional uplift using the Stream Functions Pyramid Framework, specific, attainable goals and objectives were realized by the Project. These goals clearly address the degraded water quality and nutrient input from farming that were identified as major watershed stressors in the 2009 Upper Yadkin Pee-Dee River RBRP.

The Project goals are:

- Improve water transport from watershed to the channel in a non-erosive manner in a stable channel;
- Improve flood flow attenuation on site and downstream by allowing for overbanks flows and connection to the active floodplain;
- Improve instream habitat;
- Restore and enhance native floodplain vegetation;
- Indirectly support the goals of the 2009 Upper Yadkin Pee-Dee RBRP to improve water quality and to reduce sediment and nutrient loads; and
- Protect Water Supply Watersheds (WSW).

The Project objectives to address the goals are:

- Designed and reconstructed stream channels sized to convey bankfull flows that maintain a stable dimension, profile, and planform based on modeling watershed conditions, and reference reach conditions;
- Permanently excluded livestock from stream channels and their associated buffers;
- Added in-stream structures and bank stabilization measures to protect restored and enhanced streams;
- Installed habitat features such as brush toes, constructed riffles, woody materials, and pools of varying depths to restored and enhanced streams;
- Reduced bank height ratios and increased entrenchment ratios to reference reach conditions;
- Increased forested riparian buffers to at least 50 feet on both sides of the channel along the Project reaches with a hardwood riparian plant community;
- Implemented two sediment traps in order to limit inputs of sediment, nutrients, and fecal coliform to streams from surrounding farming operations;
- Treated exotic invasive species; and
- Established a permanent conservation easement on the Project.

Functional uplift, benefits, and improvements within the Project area, as based on the Function Based Framework, are outlined in the Mitigation Plan.

1.3 Project Success Criteria

The success criteria for the Project follows the 2016 USACE Wilmington District Stream and Wetland Compensatory Mitigation Update, the Mockingbird Site Final Mitigation Plan (November 2018), and subsequent agency guidance. Cross section and vegetation plot monitoring takes place in Years 0, 1, 2, 3, 5, and 7. Hydrology and visual monitoring takes place annually. Specific success criteria components are presented below.

Stream Restoration Success Criteria

Four bankfull flow events must be documented within the seven-year monitoring period. The bankfull events must occur in separate years. Otherwise, the stream monitoring will continue until four bankfull events have been documented in separate years. *Stage recorders were installed on the bottom of Reach HC1 and Reach NM2 to document bankfull events.*

There should be little change in as-built cross sections. If changes do take place, they should be evaluated to determine if they represent a movement toward a less stable condition (for example down-cutting or erosion), or are minor changes that represent an increase in stability (for example settling, vegetative changes, deposition along the banks, or decrease in width/depth ratio). Cross sections shall be classified using the Rosgen stream classification method, and all monitored cross sections should fall within the quantitative parameters defined for channels of the design stream type. For C/E channels, bank height ratio shall not exceed 1.2, and the entrenchment ratio shall be no less than 2.2 within restored reaches. For B channels, bank height ratio shall not exceed 1.2, and the entrenchment ratio shall be no less than 1.4 within restored reaches. Channel stability should be demonstrated through a minimum of four bankfull events documented in the seven-year monitoring period.

Digital images are used to subjectively evaluate channel aggradation or degradation, bank erosion, success of riparian vegetation, and effectiveness of erosion control measures. Longitudinal images should not indicate the absence of developing bars within the channel or an excessive increase in channel depth. Lateral images should not indicate excessive erosion or continuing degradation of the banks over time. A series of images over time should indicate successional maturation of riparian vegetation.

Stream restoration reaches will be monitored to document intermittent or seasonal surface flow. This will be accomplished through direct observation and the use of hydraulic pressure transducers with data loggers. Intermittent reaches must demonstrate a minimum of 30 consecutive days of flow. Flow gauges were installed on Reaches NM1, NM4, TP2 and TP3.

Vegetation Success Criteria

Specific and measurable success criteria for plant density within the riparian buffers on the Project follow IRT Guidance. The interim measures of vegetative success for the Project is the survival of at least 320 planted three-year old trees per acre at the end of Year 3, 260 trees per acre with an average of seven feet in height at the end of Year 5, and the final vegetative success criteria is 210 trees per acre with an average height of ten feet at the end of Year 7 (USACE, 2016). Volunteer trees are counted, identified to species, and included in the yearly monitoring reports, but are not counted towards the success criteria of total planted stems. Moreover, any single species can only account for up to 50 percent of the required number of stems within any vegetation plot. Any stems in excess of 50 percent will be shown in the monitoring table but will not be used to demonstrate success.

Level	Function	Goal	Functional Parameter	Existing Rating/Projected Rating (Reach)	Objective	Measurement Method	Cumulative Monitoring Results
1	Hydrology Transport of water from the watershed to the channel	to transport water from the watershed to the channel in a non-erosive manner and maintain a stable water table in riparian wetlands	Channel-Forming Discharge Catchment Hydrology Precipitation/Runoff Relationship Reach Runoff Flow Duration Baseflow Alteration Flood Frequency	F/HF (All Reaches)	Convert land-use of streams and their headwaters from pasture to riparian forest Install one agricultural runoff attenuation structure to regulate upstream runoff coming into reach	Percent Project drainage area converted to riparian forest (indirect measurement) Visually monitor integrity of runoff attenuation structure	469 flow days - MY0/1 830 flow days - MY1 822 flow days - MY2 873 flow days - MY3
2	Hydraulic Transport of water in the channel, on the floodplain, and through the sediments	to transport water in a stable non-erosive manner	Flood Bank Connectivity Flow Dynamics Groundwater/Surface water exchange	NF/HF (HC1, NM2, NM3, NM4, NM5, TP2) FAR/HF (NM1, HC2-B, HC2-C, TP3) F/HF (HC2-A, HC2-D, TP1)	Improve flood bank connectivity by reducing bank height ratios and increase entrenchment ratios	Cross sections Crest gauges Bank Height Ratio Entrenchment Ratio	14 BF Events - MY0/1 5 BF Events - MY1 7 BF Events - MY2 6 BF Events - MY3
3	Geomorphology Transport of wood and sediment to create diverse bedforms and dynamic equilibrium	to create a diverse bedform to achieve dynamic equilibrium	Sediment Transport Large Woody Debris Transport & Storage Lateral Stability Channel Evolution Channel Sinuosity Bedform Diversity Bed Material Riparian Buffer	NF/HF (HC1, NM2, NM3, NM4, NM5, TP2) FAR/HF (NM1, HC2-B, HC2-C, TP3) F/HF (HC2-A, HC2-D, TP1)	Reduce erosion rates and channel stability to reference reach conditions Improve bedform diversity (pool spacing, percent riffles, etc) Increase buffer width to 50 feet	As-built stream profile Cross sections Visual monitoring Stream walks Vegetation plots	21/21 with BHR<1.2 - MY0 20/21 with BHR<1.2 - MY1 21/21 with BHR<1.2 - MY2 21/21 with BHR<1.2 - MY3
4	Physiochemical ^o Temperature and oxygen regulation; processing of organic matter and nutrients	to achieve appropriate levels for water temperature, dissolved oxygen concentration, and other important nutrients including but not limited to Nitrogen and Phosphorus	Water Temperature Nutrient load Organic Carbon Bacteria Water Quality	NF/HF (HC1, NM2, NM3, NM4, NM5, TP2) FAR/HF (NM1, HC2-B, HC2-C, TP3) F/HF (HC2-A, HC2-D, TP1)	Improve stream temperature regulation through introduction of canopy Decrease nutrient loading through filtration of planted riparian buffer, and removing livestock from the riparian areas	Vegetation plots (indirect measurement) Established fencing and perpetual conservation easement (indirect measurement)	NA
5	Biology [*] Biodiversity and life histories of aquatic life histories and riparian life	to achieve functionality in levels 1-4 to support the life histories of aquatic and riparian plants and animals	Microbial Communities Macrophyte Communities Benthic Macroinvertebrate Communities Fish Communities Landscape Connectivity	NF/HF (HC1, NM2, NM3, NM4, NM5, TP2) FAR/HF (NM1, HC2-B, HC2-C, TP3) F/HF (HC2-A, HC2-D, TP1)	Improve aquatic habitat through the installation of habitat features, construction of pools at varying depths, and planting the riparian buffer	Vegetation plots (indirect measurement)	15/15 passed - MY0 15/15 passed - MY1 15/15 passed - MY2 15/15 passed - MY3

Not Measured (NM); Not Functioning (NF); Functioning-at-risk (FAR); Functioning (F); Highly Functioning (HF)
^o These categories are measured indirectly; ^{*} These categories are not quantifiably measured

1.4 Project Components

The restoration reaches were significantly impacted by livestock production, agricultural practices, and a lack of riparian buffer. Improvements to the Project help meet the river basin needs expressed in the 2009 Upper Yadkin Pee-Dee River Basin Restoration Priorities (RBRP) as well as ecological improvements to riparian corridor within the easement.

Through stream restoration, enhancement, and preservation, the Project presents 8,998 LF of stream, generating 6,427.833 Warm Stream Mitigation Units (SMU) (**Table 1**) as established in the Approved Mitigation Plan. Changes made between mitigation plan approval and construction are detailed in **Section 1.6**.

Mitigation Approach	Linear Feet	Ratio	Warm SMU
Restoration	4,849	1.00000	4,849.000
Enhancement I	155	1.50000	103.333
Enhancement II	3,587	2.50000	1,434.800
Preservation	407	10.00000	40.700
Total	8,998		6,427.833

1.5 Stream Design/Approach

The Project includes Priority I Restoration, Priority II Restoration, Enhancement Levels I and II, and Preservation. Stream restoration incorporates the design of a single thread meandering channel, with parameters based on data taken from reference sites, published empirical relationships, regional curves developed from existing project streams, and NC Regional Curves. Analytical design techniques were also a crucial element of the project and were used to determine the design discharge and to verify the design as a whole.

The Project is broken into the following reaches:

Reach HC1 – Reach HC1 begins at the upstream end of the northern portion of the project and at the downstream limits of the Scout Mitigation Bank Project. There is a 40-foot easement break between the two projects that coincides with a culvert crossing and includes 24 LF of 48-inch double barrel RCP. The reach totals 2,083 LF of Priority I Restoration to address historic channelization and livestock impacts. Priority I Restoration provided higher functional uplift and less risk of failure when connected to the restoration on upstream Reach HC3. The left bank was crop land while the right bank was active pasture, which contributed to significant disturbance on both banks. Restoration activities included constructing a new channel within the natural valley with appropriate dimensions and pattern, adding channel plugs where necessary and backfilling the abandoned channel. Backfilling the abandoned stream channel created wetlands in the ephemeral pool areas. In-stream structures such as log sills, brush toes, rock cross vanes, and rock/wood constructed riffles were installed for channel stability and to improve habitat. A minimum 50-foot buffer was implemented along each side of the channel. Buffer activities will improve riparian areas that will filter runoff from adjacent pastures, thereby reducing nutrient and sediment loads to the channel.

Reach NM1 – Historically channelized reach NM1 begins at the ephemeral/intermittent break on the right bank near the top of HC1 and flows west to a confluence with HC1. Active pasture previously surrounded this reach. The reach totals 229 LF of Enhancement II, and enhancement activities includes buffer plantings and the treatment of invasive species. This reach treatment ends at the farm path.

Reach NM2 – Reach NM2 begins on the west side of Reach HC1 and flows east to the confluence with HC1 near it's midpoint. The reach totals 637 LF of Priority I Restoration and 731 LF of Priority II Restoration. Due to elevation and slope constraints, Priority II Restoration was utilized at the top of the reach, blending into Priority I as it nears the HC1 floodplain. Active crop land previously surrounded this reach as well as limited cattle exposure. There is a 40-foot easement break for a culvert crossing where an existing 72-inch CMP was removed and replaced with 24 LF of a double barrel 48-inch RCP. Restoration activities included constructing a new channel within the natural valley with appropriate dimensions and pattern, adding channel plugs where necessary and backfilling the abandoned channel. In-stream structures such as log sills, brush toes, log cross vanes, and rock/wood constructed riffles were installed for channel stability and to improve habitat. A minimum 50-foot buffer was maintained along on each side of the channel. Buffer activities improve riparian areas that filter runoff from adjacent fields, thereby reducing nutrient and sediment loads to the channel.

Reach NM3 – Reach NM3 begins at a culvert on the west side of Reach HC1, near the downstream end of the Project, and flows east to a confluence with HC1. The reach totals 280 LF of Priority I Restoration to address historic channelization and excess deposition due to agricultural practices. The incised reach was surrounded by fields of row crops and lacked a protective buffer. Restoration activities included constructing a new channel with appropriate dimensions and pattern, adding channel plugs where necessary and backfilling the abandoned channel. In-stream structures such as log sills, brush toes, rock cross vanes, and constructed riffles were installed for channel stability and to improve habitat. A minimum of 50 feet of buffer on each side of the channel was implemented. Buffer activities will improve riparian areas that will filter runoff from adjacent fields, reducing nutrient and sediment loads to the channel.

Reach NM4 – NM4 is a headwater reach that forms from the hills on the east side of HC1 near the downstream portion of the Project. Active pasture previously surrounded this reach. This reach totals 253 LF of Enhancement II. Treatment included removing an existing crossing at a 15-inch RCP, establishing a minimum 50-foot riparian buffer, and instream structures such as rock cross vanes and log sills to provide channel stability.

Reach NM5 – NM5 is a headwater reach that forms within the eastern floodplain of Reach HC1, just upstream of Reach NM4, and flows west to a confluence with HC1. Realignment of Reach HC1 will displace the majority of NM5 due to plugging this channel at its confluence with the existing HC1 and filling in that abandoned channel. A small portion of intermittent channel is protected within the easement but does not receive credit. Active pasture previously surrounded this reach.

Reach JS1 – Reach JS1 begins in a previously active pasture, north of Spillman Road, and flows east into the existing DMS Hauser Creek Mitigation Site that exists downstream from the Project. This reach totals 523 LF of Priority I Restoration to address historic channelization, livestock impacts and erosion. Restoration activities included removing an existing ford, constructing a new channel within the natural valley, backfilling the abandoned channel, and reconnecting to the floodplain for frequent inundation. In-stream structures such as log sills, brush toes, log cross vanes, rock cross vanes, and constructed riffles were installed for channel stability and to improve habitat. A minimum of 50 feet of buffer on each side of the channel was implemented. Buffer activities improve riparian areas that filter runoff from adjacent pastures, thereby reducing nutrient and sediment loads to the channel. The channel ties back into the existing location in order to connect to the 72-inch CMP under the landowner’s gravel driveway.

Reach HC2-A – Reach HC2-A begins at the upstream end of the Project (the southern portion of the project), and flows north to Reach HC2-B. The reach totals 2,018 LF of Enhancement II. Agricultural fields and bottomland hardwood forests are located adjacent to the reach. Enhancement activities included the re-establishment of a riparian buffer along the channel (buffers extended a minimum of 50 feet from the top of each bank) and invasive species treatment as needed. Buffer improvements filter runoff from adjacent pastures, thereby reducing nutrient and sediment loads to the channel. Additional habitat improvements were gained through

livestock exclusion. There is a 31-foot easement break to maintain an existing ford crossing within the bottom third of this reach.

Reach HC2-B – Reach HC2-B begins immediately downstream of Reach HC2-A and flows north to Reach HC2-C. The reach totals 595 LF of Priority I Restoration to address historic channelization and cattle exposure. The reach was surrounded by active pasture and the downstream portion is surrounded by disturbed bottomland hardwood forests and riparian wetlands. Restoration activities included constructing a new channel within the natural valley with appropriate dimensions and pattern, adding channel plugs where necessary and backfilling the abandoned channel. In-stream structures such as log sills, brush toes, cross vanes, rock A-vanes, and constructed riffles were installed for channel stability and to improve habitat. A minimum of 50 feet of buffer on each side of the channel was implemented. Buffer activities improve riparian areas that will filter runoff from adjacent pastures, thereby reducing nutrient and sediment loads to the channel. Reach TP3 ties into HC2-B prior to a proposed 35-foot easement break and ford crossing, before transitioning into Reach HC2-C. Also, the reach was built through part of a jurisdictional wetland that is on the right bank floodplain and was degraded from cattle access and pasture-use. While this project is not claiming any wetland credit, the raised channel bed enhanced the wetlands' hydrology by reconnecting the floodplain wetlands to the stream. Also, backfilling the abandoned stream channel created additional wetlands in the ephemeral pool areas. A gauge was installed on the right floodplain to monitor the wetland hydrology and will be reported annually.

Reach HC2-C – This reach begins at the downstream end of HC2-B and flows north from a ford crossing to the upstream end of HC2-D. Although cattle have been historically excluded from this reach, upstream pasture activity and travel across the existing ford previously resulted in bed and bank erosion and sedimentation. The reach totals 155 LF of Enhancement I, and enhancement activities included laying back and/or benching the left bank and installing coir matting and live stakes to provide channel stabilization. Bottomland hardwoods are located adjacent to the reach.

Reach HC2-D – Reach begins immediately downstream of Reach HC2-C and flows north to the downstream boundary of the southern portion of the easement. The reach totals 407 LF of preservation with minimum 50-foot buffers. Bottomland hardwoods surround this reach.

Reach TP1 – Reach TP1 begins on the east side of Reach HC2-A in headwater Piedmont forest and flows west to a confluence with Reach HC1-A. Lightly disturbed forest surrounds this reach. The reach totals 146 LF of Enhancement II, where cattle exclusion and supplemental planting of the riparian buffer occurred. This reach treatment ends at the fence line.

Reach TP2 - This reach begins on the east side of Reach HC2-A, just downstream of the confluence of TP1 with HC2-A and flows southwest to a confluence with Hauser Creek. The reach totals 471 LF of Enhancement II. The reach was surrounded by active pasture and a small wetland occurs near the stream origin. Enhancement activities included reestablishing the riparian buffer with native vegetation and cattle exclusion. A sediment trap was installed upstream of

ephemeral/intermittent stream break to provide sediment and nutrient control from upland agricultural practices.

Reach TP3 – This reach begins to the east of Reach HC2-B and flows southwest to a confluence with HC2-B upstream of an easement break. The reach totals 470 LF of Enhancement II. The reach was surrounded by active pasture and forms out of a headwater wetland. A sediment trap (made from woody debris and livestakes) was installed at the upper end of the reach to provide sediment and nutrient control from upland agricultural practices.

1.6 Construction and As-Built Conditions

Stream construction and planting was completed in June 2020. Overall, the Site was built to design plans and guidelines. However, there were two changes that were made between the time of Final Mitigation Plan approval and site construction that reduced the project linear footage by 88 feet. The first was an error on the stationing for TP2. The crediting was mistakenly shown starting above the ESP structure, where the channel was non-jurisdictional. The crediting should begin below the ESP, shortening the reach from 471 to 441. The second was a design change on NM1 that reduced the linear footage from 229 to 171. Both changes are shown on the redline survey and on **Table 1**, however the project credits remain as established in the Final Mitigation Plan. The as-built survey (including a redlined version) is included in the As-Built Baseline Report.

Planting plan changes are outlined on Table 7, **Appendix C**. Planting plan changes were based on bare root availability. Monitoring devices had minor shifts in locations, however the quantities of devices remained the same as proposed for vegetation plots (15), flow gauges (4), stage recorders (2), and wetland gauges (1). Cross sections were installed in all the proposed locations where stream work was completed and removed from reaches (preservation and EII) where stream work was not completed. The total number of cross sections was reduced from 26 to 21.

1.7 Year 3 Monitoring Performance (MY3)

The Mockingbird MY3 activities were performed in June and October of 2023. All Year 3 Monitoring data is present below and in the appendices. NCDMS and RES met onsite for a boundary inspection in September 2023. Inspection results were sent by email on 9/15/2023, and RES has either resolved or is actively working on resolving all identified boundary and potential stewardship transfer issues. The Site is on track to meeting vegetation and stream interim success criteria.

Vegetation

Monitoring of the 10 fixed vegetation plots and five random vegetation plots was completed in October 2023. MY3 monitoring data indicates that all plots are exceeding the interim success criteria of 320 planted stems per acre. Planted stem densities ranged from 445 to 809 planted stems per acre with a mean of 650 planted stems per acre across all the plots. Volunteer species were noted in all of the fixed vegetation plots. The average stem height in the plots was 5.3 feet.

A total of 15 species were documented within the plots. Vegetation data is located in **Appendix C**, associated photos are in **Appendix B**, and plot locations are in **Appendix B**.

Visual assessment of vegetation outside of the monitoring plots indicates that the herbaceous vegetation is becoming well established throughout the project. A small scattering of Chinese privet, autumn olive, and multiflora rose was observed throughout the easement, these areas will be treated in 2024. No polygons of invasive species greater than 1000 ft² were found on site. Several areas around the easement have insufficient boundary marking however only a few small areas of easement encroachment are located around the site (< 0.1 acres), these areas are called out in **Figure 2** of **Appendix B**. RES is working currently to solve all easement issues found on the site and will remain in contact with NCDMS to rectify the situation. Photos of crossings can be found in **Appendix B** and appear to be functioning as designed.

Stream Geomorphology

Cross section and geomorphology data collection for MY3 was collected in June 2023. Summary tables and cross section plots are in **Appendix D**. Overall the MY3 cross sections relatively match the baseline cross sections. Cross section five shows signs of light degradation from previous years profiles however appears to have returned to baseline conditions. The as-built conditions indicate that shear stress and velocities have been reduced for all restoration/enhancement reaches. All reaches were designed as gravel bed channels and remain classified as gravel bed channels post-construction.

Visual assessment of the stream channel was performed to document signs of instability, such as eroding banks, structural instability, or excessive sedimentation. The channel is transporting sediment as designed and will continue to be monitored for aggradation and degradation.

Stream Hydrology

Two stage recorders and four flow gauges were installed in June 2020: one stage recorder on HC1, one stage recorder on NM2 and flow gauges on NM1, NM4, TP2, and TP3. The stage recorders are in place to document bankfull events and the flow gauge to document at least intermittent flow. The stage recorder on HC1 recorded seven bankfull events in MY3 with the highest reading being 1.133 feet above top of bank. The stage recorder on NM2 recorded two bankfull events during M3, the highest event being 0.27 feet out of bank. The flow gauges on NM1, NM4, TP2, and TP3 recorded between one and nine flow events lasting between 55 and 282 consecutive days. The flow gage on NM1 is missing data this year from June on due to some data corruption, we have contacted technical support to restore any lost data and will include it future reports if recovered. Despite the missing data, NM1 still recorded 55 days of flow. All recorded streams are on track to pass hydrology metrics. Stream hydrology data is included in the **Appendix E**. Gauge locations can be found on **Figure 2** and photos are in **Appendix B**.

Wetland Hydrology

One groundwater well (GW1) was installed in April 2020. The goal of the groundwater well is to track the hydrology in the jurisdictional wetlands on site post-construction. There is no hydroperiod success criteria for this groundwater well. In MY3, GW1 recorded a consecutive hydroperiod of 22 percent of the growing season. Wetland hydrology data is included in **Appendix E**. The groundwater well location can be found on **Figure 2**.

2.0 Methods

Stream monitoring was conducted using a Topcon GTS-312 Total Station. Three-dimensional coordinates associated with cross-section data were collected in the field (NAD83 State Plane feet FIPS 3200). Morphological data were collected at 21 cross-sections. Survey data were imported into CAD, ArcGIS®, and Microsoft Excel® for data processing and analysis. The stage recorders include an automatic pressure transducer placed in PVC casing in a pool. The elevation of the bed and top of bank at each stage recorder are used to detect bankfull events. The flow gauge was also installed in a pool and records flow conditions at an hourly interval. Water level data from the flow gauge is corrected using the height of the downstream riffle to detect stream flow events.

Vegetation success is being monitored at ten permanent monitoring plots and five random monitoring plots. Vegetation plot monitoring follows the CVS-EEP Level 2 Protocol for Recording Vegetation, version 4.2 (Lee et al. 2008) and includes analysis of species composition and density of planted species. Data are processed using the CVS data entry tool. In the field, the four corners of each plot were permanently marked with PVC at the origin and metal conduit at the other corners. Photos of each plot are taken from the origin each monitoring year. The random plots are collected in locations where there are no permanent vegetation plots. Random plots will most likely be collected in the form of 100 square meter belt transects with variable dimensions. Tree species and height were recorded for each planted stem and the transects will be mapped and new locations will be monitored in subsequent years.

Wetland hydrology is monitored to document maintenance of jurisdictional groundwater levels in the stream restoration area (as requested by NCIRT). This is accomplished with an automatic pressure transducer gauge (located in a groundwater well) that records the daily groundwater level. One automatic pressure transducer is installed above ground for use as a barometric reference. Gauges are downloaded quarterly and wetland hydroperiods are calculated during the growing season. Gauge installation followed current regulatory guidance. Visual observations of primary and secondary wetland hydrology indicators are also recorded during quarterly site visits.

3.0 References

- Griffith, G.E., J.M.Omernik, J.A. Comstock, M.P. Schafale, W.H.McNab, D.R.Lenat, T.F.MacPherson, J.B. Glover, and V.B. Shelburne. (2002). Ecoregions of North Carolina and South Carolina, (color Poster with map, descriptive text, summary tables, and photographs): Reston, Virginia, U.S. Geological Survey (map scale 1:1,500,000).
- Lee Michael T., Peet Robert K., Roberts Steven D., and Wentworth Thomas R., 2008. *CVS-EEP Protocol for Recording Vegetation Level*. Version 4.2
- Peet, R.K., Wentworth, T.S., and White, P.S. (1998), *A flexible, multipurpose method for recording vegetation composition and structure*. *Castanea* 63:262-274
- Resource Environmental Solutions (2018). Mockingbird Site Final Mitigation Plan.
- Schafale, M.P. 2012. Classification of the Natural Communities of North Carolina, Third Approximation. North Carolina Natural Heritage Program, Division of Parks and Recreation, NCDENR, Raleigh, NC.
- USACE. (2016). Wilmington District Stream and Wetland Compensatory Mitigation Update. NC: Interagency Review Team (IRT).

Appendix A

Background Tables

The Mockingbird Site - Mitigation Components									
Reach	Existing Footage	Mitigation Plan Footage	Mitigation Category	Restoration Level	Priority Level	Mitigation Ratio (X:1)	Mitigation Plan Credit	As-Built Footage	Notes
HC2-A	1,345	1345	Warm	EII	N/A	2.50000	538,000	1345	Riparian and supplemental planting, livestock exclusion, invasives treatment
HC2-A	673	673	Warm	EII	N/A	2.50000	269,200	673	Riparian and supplemental planting, livestock exclusion, invasives treatment
HC2-B	568	595	Warm	R	1	1.00000	595,000	595	Channel restoration, riparian planting, livestock exclusion
HC2-C	155	155	Warm	EI	3	1.50000	103,333	155	Bank grading and stabilization, supplemental planting, conservation easement
HC2-D	408	407	Warm	P	N/A	10.00000	40,700	407	Conservation Easement
HC1	2,135	2083	Warm	R	1	1.00000	2083,000	2,083	Channel restoration, riparian planting, livestock exclusion
TP1	157	146	Warm	EII	N/A	2.50000	58,400	146	Riparian planting, livestock exclusion
TP2*	450	471	Warm	EII	N/A	2.50000	188,400	441	Riparian planting, livestock exclusion
TP3	525	470	Warm	EII	N/A	2.50000	188,000	470	Riparian planting, livestock exclusion
NM1*	229	229	Warm	EII	N/A	2.50000	91,600	171	Riparian planting, livestock exclusion
NM2	889	997	Warm	R	1 & 2	1.00000	997,000	997	Channel restoration, riparian planting, livestock exclusion
NM2	330	371	Warm	R	1	1.00000	371,000	371	Channel restoration, riparian planting, livestock exclusion
NM3	197	280	Warm	R	1	1.00000	280,000	280	Channel restoration, riparian planting
NM4	286	253	Warm	EII	N/A	2.50000	101,200	253	Riparian planting, livestock exclusion
JS1	465	523	Warm	R	1	1.00000	523,000	523	Channel restoration, riparian planting, livestock exclusion

*Stream length changed at as-built

Project Credits

Restoration Level	Stream	Riparian Wetland		Non-riparian Wetland
		Riverine	Non-Riverine	
Restoration	4,849,000			
Enhancement I	103,333			
Enhancement II	1,434,800			
Creation				
Preservation	40,700			
High Quality Pres				
Total	6,427,833			

**Table 2. Project Activity and Reporting History
Mockingbird Mitigation Site**

Elapsed Time Since grading complete: 3 year 2 months

Elapsed Time Since planting complete: 3 year 2 months

Number of reporting Years¹: 3

Activity or Deliverable	Data Collection Complete	Completion or Delivery
Restoration Plan	NA	Nov-19
Final Design – Construction Plans	NA	Sep-19
Stream Construction	NA	Jun-20
Site Planting	NA	Jun-20
As-built (Year 0 Monitoring – baseline)	Jun-20	Oct-20
HC1 Hand Repair	NA	Jan-21
Supplemental Planting (VP 6 and 7)	NA	Jan-21
Year 1 Monitoring	XS: Jul-21 VP: Oct-21	Jan-22
Year 2 Monitoring	XS: Jun-22 VP: Oct-22	Nov-22
Year 3 Monitoring	XS: Jun-23 VP: Oct-23	Dec-23
Year 4 Monitoring		
Year 5 Monitoring		
Year 6 Monitoring		
Year 7 Monitoring		

¹ = The number of reports or data points produced excluding the baseline

**Table 3. Project Contacts Table
Mockingbird Mitigation Site**

Designer	RES / 3600 Glenwood Ave., Suite 100, Raleigh, NC 27612
Primary project design POC	Frasier Mullen
Construction Contractor	KBS Earthwork Inc. / 5616 Coble Church Rd., Julian, NC 27283
Construction contractor POC	Kory Strader
Survey Contractor	Matrix East, PLLC / 906 N. Queen St., Suite A, Kinston, NC 28501
Survey contractor POC	Chris Paderick, PLS
Planting Contractor	H&J Forestry
Planting contractor POC	Matt Hitch
Monitoring Performers	RES / 401 Charles Ave, Charlotte NC, 29605
Stream Monitoring POC	Daniel Dixon 864.567.7761
Vegetation Monitoring POC	Daniel Dixon 864.567.7761



Table 4. Project Background Information

Table 4. Project Background Information			
Project Name		Mockingbird	
County		Davie	
Project Area (acres)		27.46	
Project Coordinates (latitude and longitude)		Northern portion: Latitude: 36.038433 Longitude: - 80.516410	
		Southern Portion: Latitude: 36.028029 Longitude: - 80.502333	
Planted Acreage (Acres of Woody Stems Planted)		23.2	
Project Watershed Summary Information			
Physiographic Province		Southern Outer Piedmont	
River Basin		Yadkin Pee-Dee	
USGS Hydrologic Unit 8-digit	03040101	USGS Hydrologic Unit 14-digit	3040101160010
DWR Sub-basin		3/7/2002	
Project Drainage Area (Acres and Square Miles)		1,540 ac (2.406 sqmi)	
Project Drainage Area Percentage of Impervious Area		2%	
CGIA Land Use Classification		Managed Herbaceous Cover and Mixed Upland Hardwoods	
Regulatory Considerations			
Parameters	Applicable?	Resolved?	Supporting
Water of the United States - Section 404	Yes	Yes	Mit Plan
Water of the United States - Section 401	Yes	Yes	Mit Plan
Endangered Species Act	Yes	Yes	Mit Plan
Historic Preservation Act	Yes	Yes	Mit Plan
Coastal Zone Management Act (CZMA or CAMA)	No	N/A	N/A
FEMA Floodplain Compliance	Yes	No	Mit Plan
Essential Fisheries Habitat	No	N/A	N/A

Reach Summary Information

Parameters	HC1	HC2-A	HC2-B	HC2-C	HC2-D	JS1	NM1	NM2	NM3	NM4	NM5	TP1	TP2	TP3
Length of reach (linear feet)	2,135	2018	568	563	563	465	229	1219	197	286	101	157	450	525
Valley confinement (Confined, moderately confined, unconfined)														
Drainage area (Acres and Square Miles)	1,319 ac	55 ac	151 ac	194 ac	207 ac	221 ac	20 ac	330 ac	74 ac	27 ac	24 ac	45 ac	20 ac	20 ac
Perennial, Intermittent, Ephemeral	P	P	P	P	P	P	I	P	P	I	I	P	I	I
NCDWR Water Quality Classification														
Stream Classification (existing)	E5	B3c	F3/C3	C3	C3	E5	E4	E4	E6b	E6b	E6b	B3c	C6b	B6
Stream Classification (proposed)	E3/E4		E3/E4			E4/E5		E4/E5	E3/E4					

Targeted Local Watershed
Turner & Hauser Creek
03040101160010

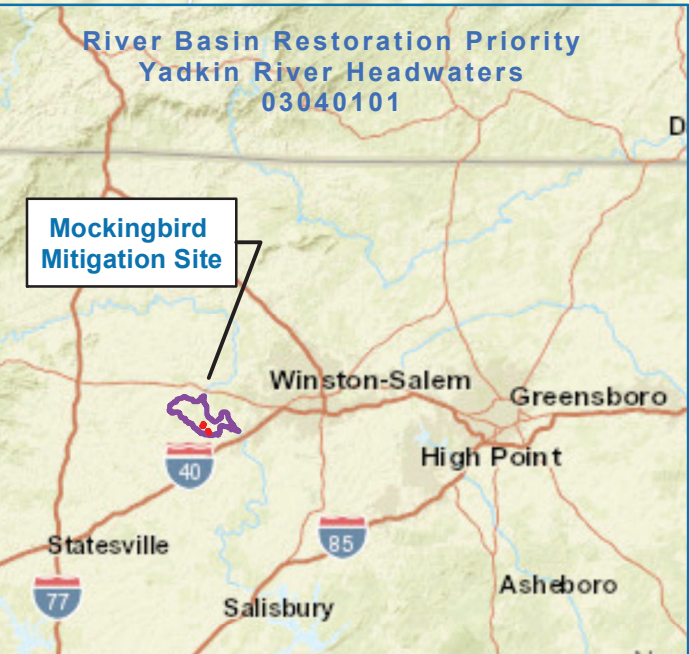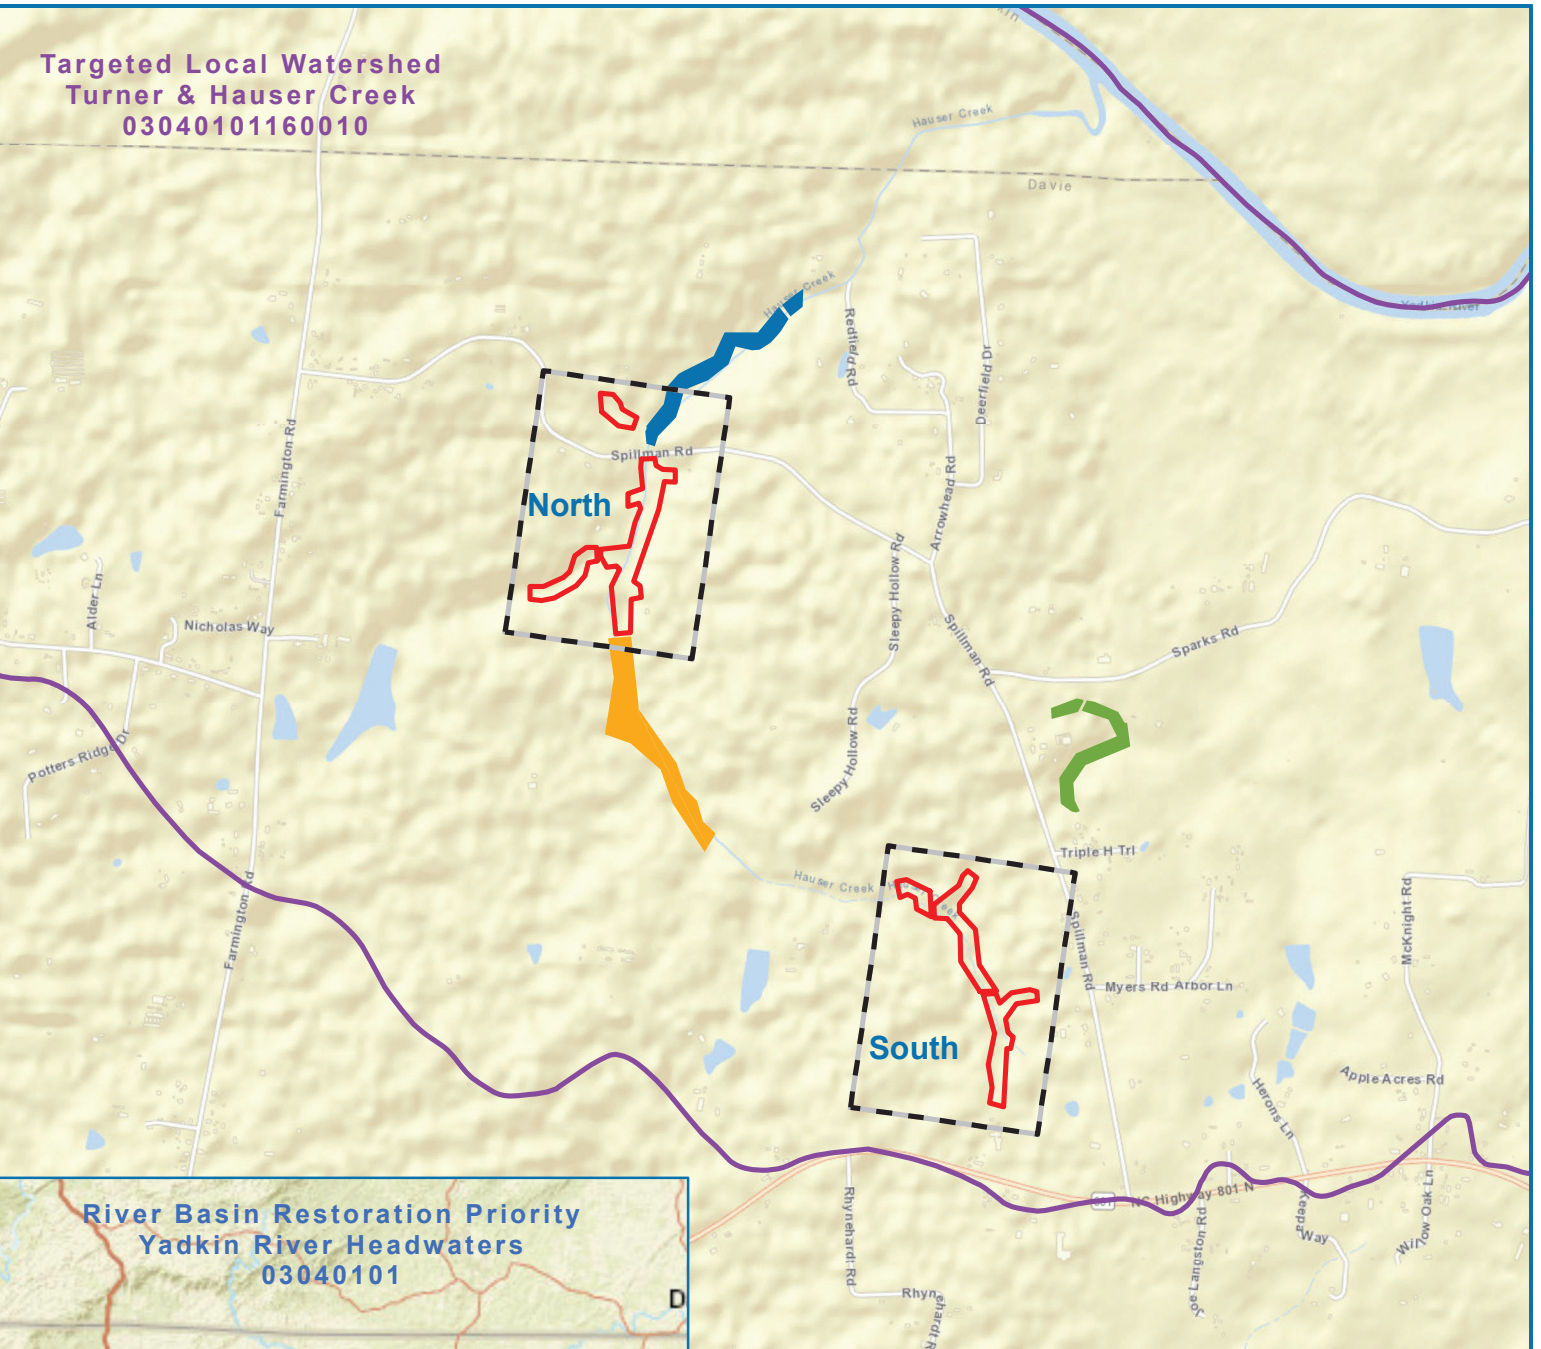

- Legend**
- Conservation Easement (Red outline)
 - Scout Easement (Orange fill)
 - Catbird Easement (Green fill)
 - Hauser Creek Easement (Blue fill)
 - HUC - 03040101 (Blue outline)
 - TLW - 03040101160010 (Purple outline)
 - CCPV Index Sheets (Dashed black outline)



Figure 1 - Site Location Map
Mockingbird Mitigation Site
Davie County, North Carolina

Date: 6/22/2020

Drawn by: HKH

Checked By: RTM

1 inch = 2,000 feet



Appendix B

Visual Assessment Data



Restoring a resilient earth for a modern world





Figure 2 - CCPV MY3

Mockingbird Mitigation Project

Davie County, North Carolina

Date: 12/5/2023
 1 in = 208 feet
 Drawn by: HG
 Checked by: DD

- Conservation
- Easement
- Encroachment
- Existing
- Insufficient Signage
- Fixed
- >320 stems/acre
- RVP MY3 Mockingbird
- > 320 Stems/Acre
- Enhancement
- Enhancement
- No
- Cross
- Flow Gauge
- Stage
- Wetland
- Gauge/Ambient

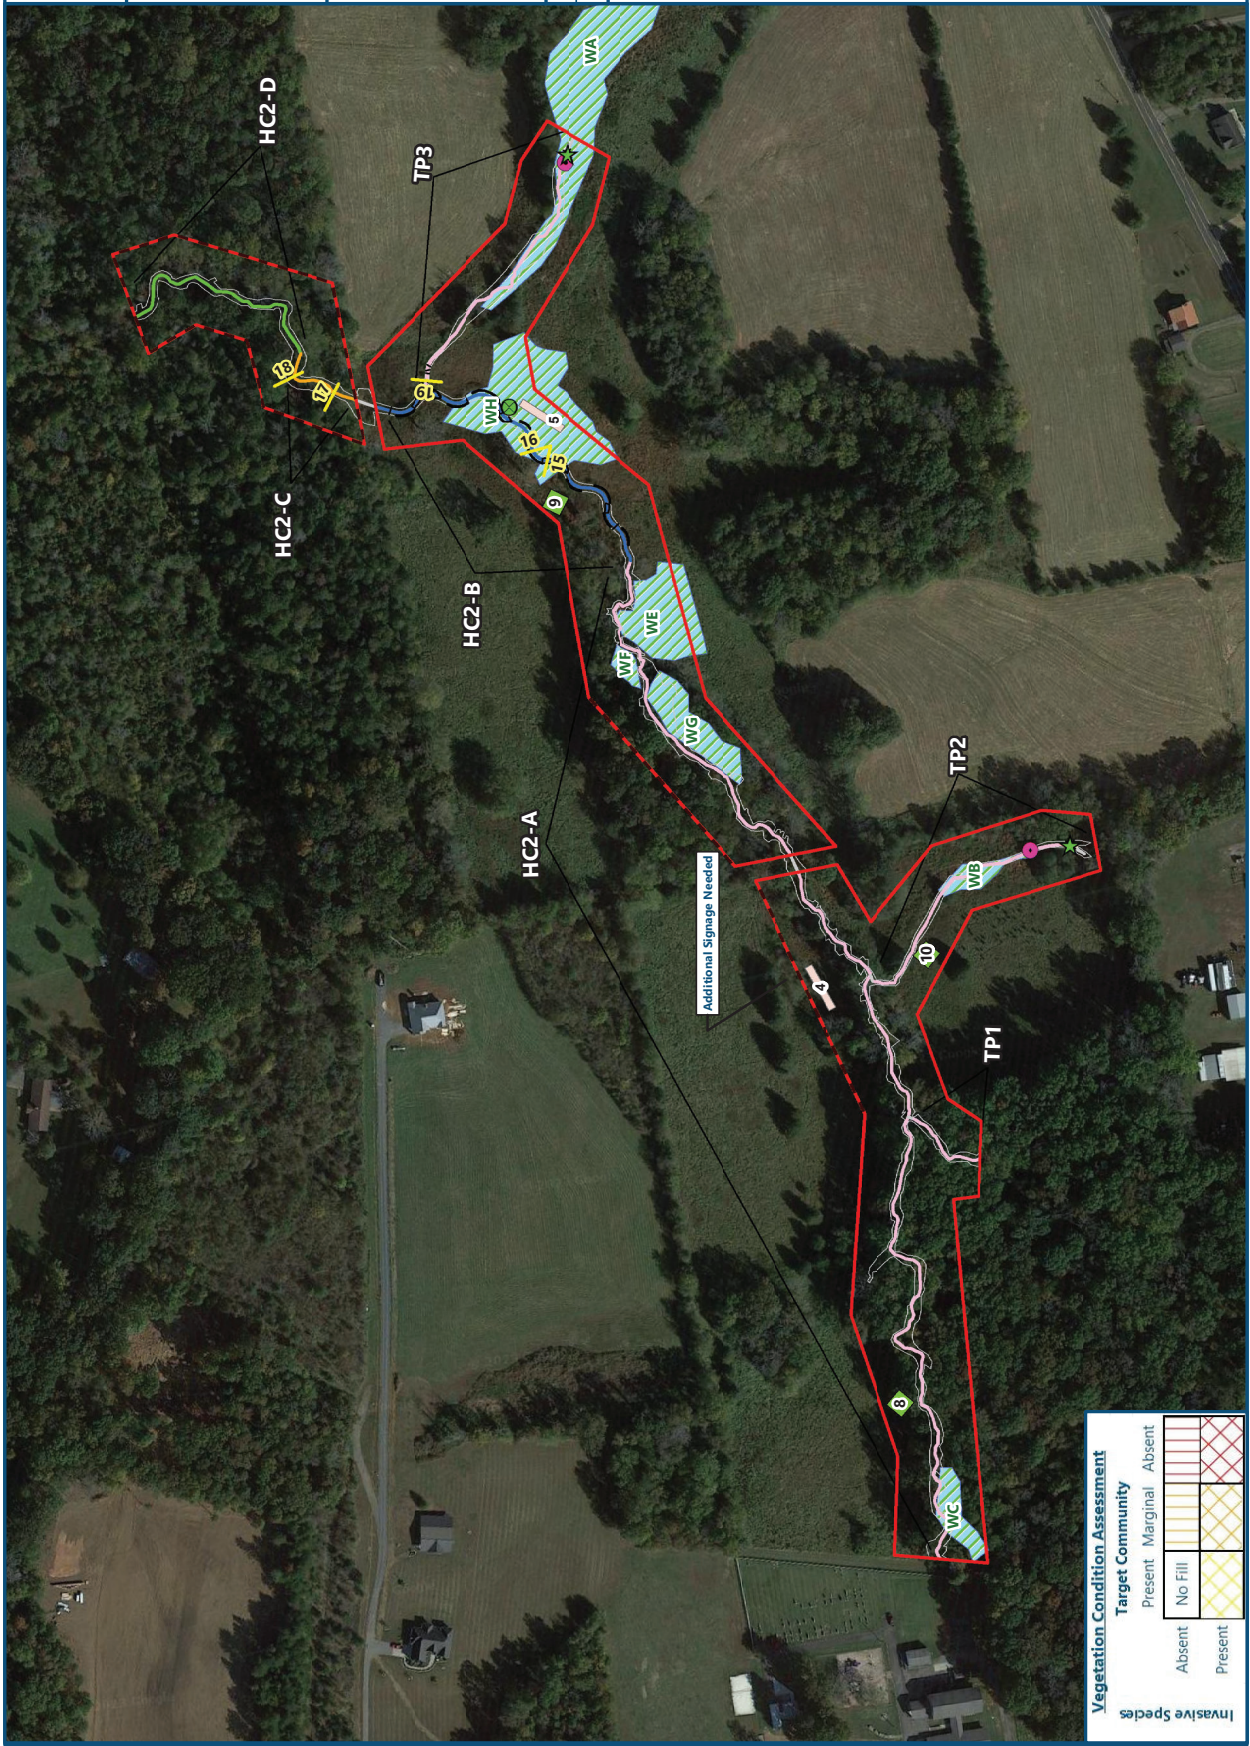

Additional Signage Needed

Vegetation Condition Assessment	
Invasive Species	Present
	Absent
Target Community	Present
	Marginal
Target Community	Marginal
	Absent
Target Community	No Fill
	Present

Small text at the bottom of the page, likely a scale or reference note.



Restoring a resilient earth for a modern world




Figure 2 - CCPV MY3


Mockingbird Mitigation Project

Davie County, North Carolina

Date: 12/5/2023 Drawn by: HG

1 in = 200 feet Checked by: DD

- Conservation
- Easement
- Encroachment
- Existing
- Insufficient Signage
- Fixed
- >320 stems/acre
- RVP MY3 Mockingbird
- > 320 Stems/Acre
- Enhancement
- Enhancement
- No
- Cross
- Flow Gauge
- Stage
- Wetland
- Gauge/Ambient

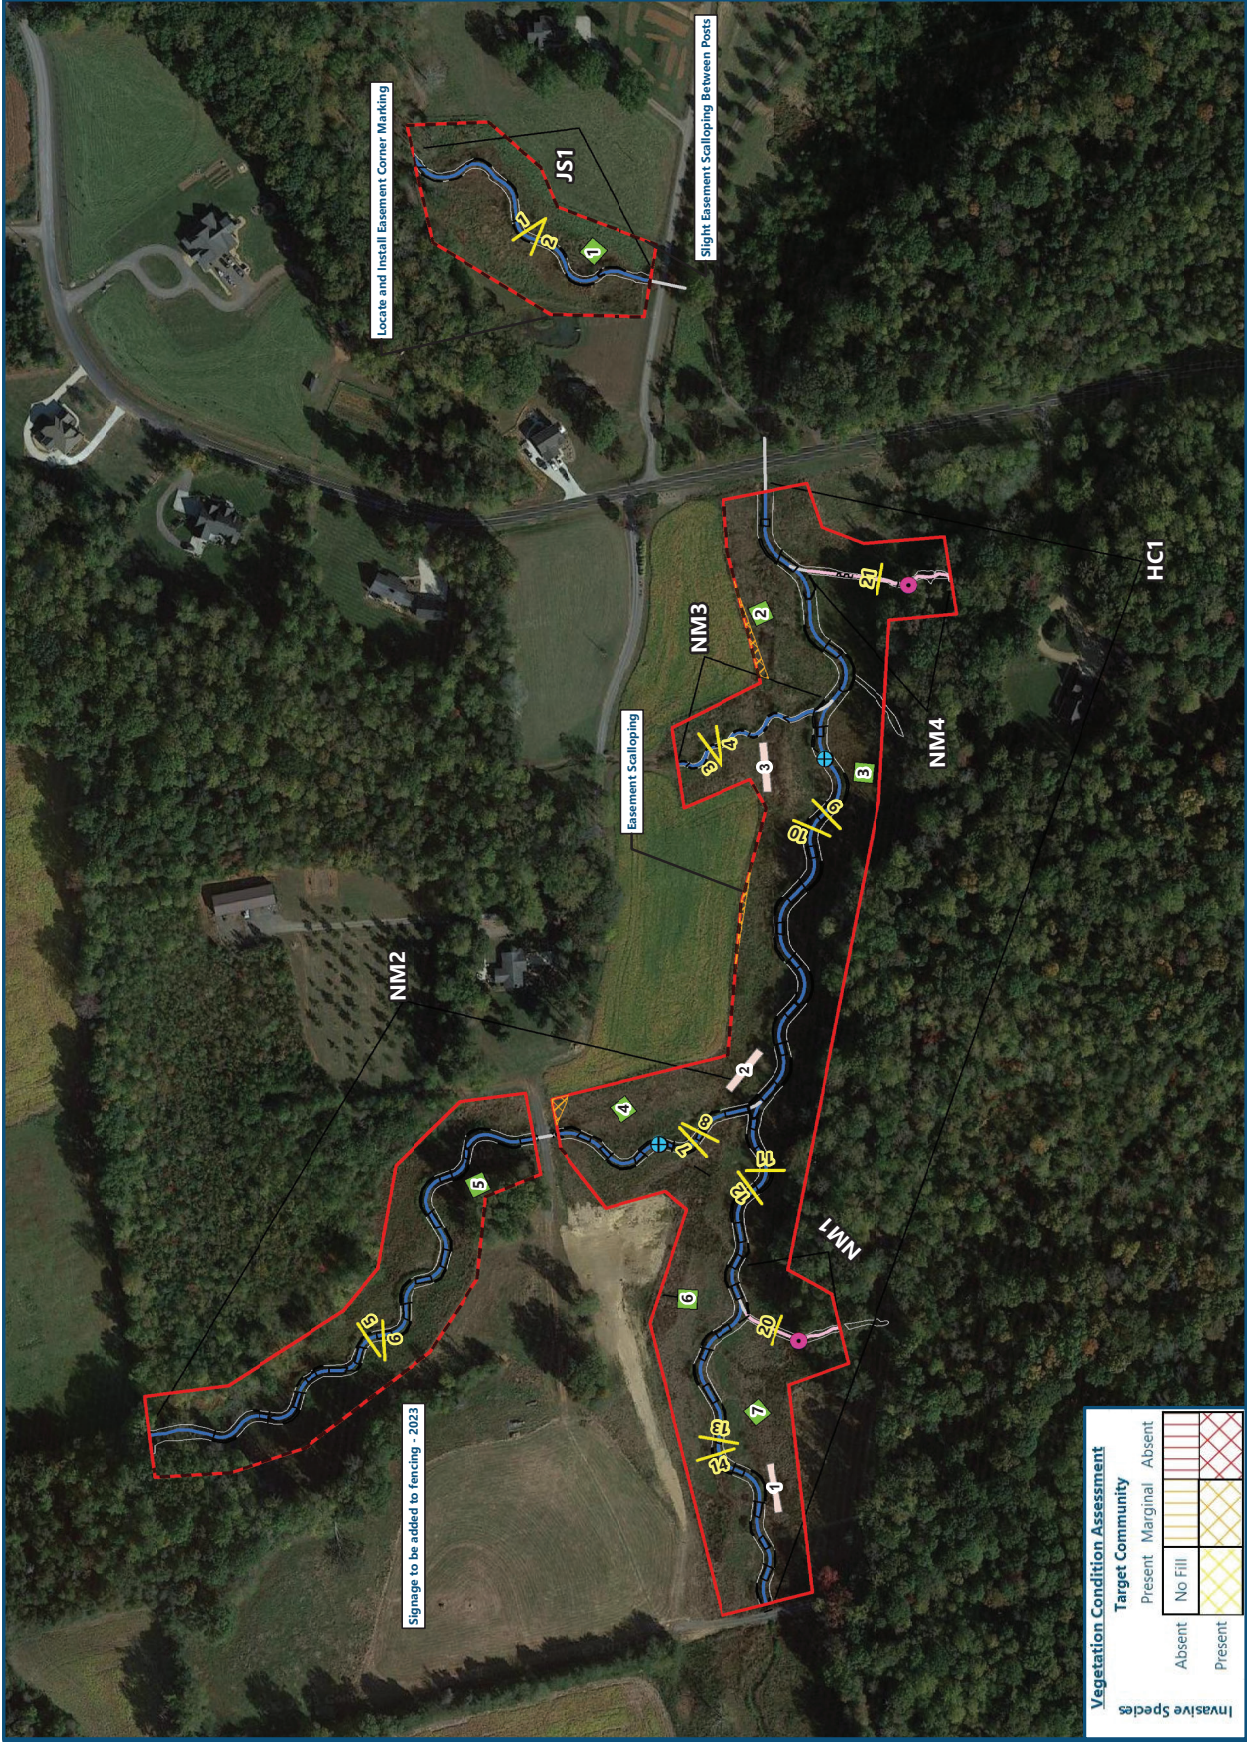

Vegetation Condition Assessment

Target Community		Invasive Species	
Present	Absent	No Fill	Present
Present	Marginal	Absent	Absent
Present	Marginal	Present	Present

Table 5. Visual Stream Morphology Stability Assessment
Mockingbird Site - NM2
Assessed Length 1,368 feet

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Rifle and Run Units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars).			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting.			0	0	100%			
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate.	22	22			100%			
		1. <u>Depth Sufficient</u> (Max Pool Depth : Mean Bankfull Depth ≥ 1.6).	20	20			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle).	20	20			100%			
2. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
		Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
		Bank slumping, calving, or collapse.			0	0	100%	0	0	100%
	Totals			0	0	100%	0	0	100%	
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	34	34			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill	34	34			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	34	34			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	34	34			100%			
	4. Habitat	Pool forming structures maintaining* Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	34	34			100%			

Date of last site inspection - 10/10/2023

Table 5 Cont'd. Visual Stream Morphology Stability Assessment
Mockingbird Site - NM3
Assessed Length 280 feet

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Rifle and Run Units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars).			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting.			0	0	100%			
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate.	10	10			100%			
		1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth± 1.6).	11	11			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle).	11	11			100%			
	2. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0
Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.					0	0	100%	0	0	100%
Bank slumping, calving, or collapse.					0	0	100%	0	0	100%
3. Mass Wasting						100%				
3. Engineered Structures	1. Overall Integrity		13	13			100%			
		Structures physically intact with no dislodged boulders or logs.								
	2. Grade Control		13	13			100%			
		Grade control structures exhibiting maintenance of grade across the sill.								
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	13	13			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does NOT exceed 15%.	13	13			100%			
Pool forming structures maintaining~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.		13	13			100%				
4. Habitat										
			Totals							

Date of last site inspection - 10/10/2023

Table 5 Cont'd. Visual Stream Morphology, Stability Assessment
Mockingbird Site - HCI
Assessed Length 2,083 feet

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Rifle and Run Units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars).			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting.			0	0	100%			
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate.	30	30			100%			
		1. <u>Depth Sufficient</u> (Max Pool Depth : Mean Bankfull Depth± 1.6).	28	28			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle).	28	28			100%			
	2. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0
Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.					0	0	100%	0	0	100%
Bank slumping, calving, or collapse.					0	0	100%	0	0	100%
3. Mass Wasting				0	0	100%	0	0	100%	
3. Engineered Structures	Totals									
	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	47	47			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	47	47			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	47	47			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does NOT exceed 15%.	47	47			100%			
4. Habitat	Pool forming structures maintaining~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	47	47			100%				

Date of last site inspection - 10/10/2023

Table 5 Cont'd. Visual Stream Morphology Stability Assessment

Mockingbird Site - HC2-B

Assessed Length **595** feet

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Rifle and Run Units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars).			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting.			0	0	100%			
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate.	14	14			100%			
		1. <u>Depth Sufficient</u> (Max Pool Depth : Mean Bankfull Depth± 1.6).	13	13			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle).	13	13			100%			
	2. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0
Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.					0	0	100%	0	0	100%
Bank slumping, calving, or collapse.					0	0	100%	0	0	100%
3. Mass Wasting				0	0	100%	0	0	100%	
Totals			19	19			100%			100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	19	19			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	19	19			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	19	19			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does NOT exceed 15%.	19	19			100%			
4. Habitat	Pool forming structures maintaining~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	19	19			100%				

Date of last site inspection - 10/10/2023

Table 5 Cont'd. Visual Stream Morphology, Stability Assessment

Mockingbird Site - JS1
Assessed Length 523 feet

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Rifle and Run Units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars).			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting.			0	0	100%			
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate.	7	7			100%			
		1. <u>Depth Sufficient</u> (Max Pool Depth : Mean Bankfull Depth± 1.6).	7	7			100%			
	3. Meander Pool Condition	2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle).	7	7			100%			
2. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
		Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
		Bank slumping, calving, or collapse.			0	0	100%	0	0	100%
	3. Mass Wasting			0	0	100%	0	0	100%	
Totals			13	13			100%			100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	13	13			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	13	13			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	13	13			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does NOT exceed 15%.	13	13			100%			
4. Habitat	Pool forming structures maintaining~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	13	13			100%				

Date of last site inspection - 10/10/2023

Vegetation Condition Assessment

18.6

Table 6
Planted Acreage¹

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	0.1 acres	Red Simple Hatch	0	0.00	0.0%
2. Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1 acres	Orange Simple Hatch	0	0.00	0.0%
Total						
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 acres	Orange Simple Hatch	0	0.00	0.0%
Cumulative Total						
						0.0%

Easement Acreage²

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern⁴	Areas or points (if too small to render as polygons at map scale).	1000 SF	Yellow Crosshatch	0	0.00	0.0%
5. Easement Encroachment Areas³	Areas or points (if too small to render as polygons at map scale).	none	Red Simple Hatch	3	0.02	0.1%

Date of last site inspection - 10/10/2023


¹ = Enter the planted acreage within the easement. This number is calculated as the easement acreage minus any existing mature tree stands that were not subject to supplemental planting of the understory, the channel acreage, crossings or any other elements not directly planted as part of the project effort.

² = The acreage within the easement boundaries.

³ = Encroachment may occur within or outside of planted areas and will therefore be calculated against the overall easement acreage. In the event a polygon is cataloged into items 1, 2 or 3 in the table and is the result of encroachment, the associated acreage should be tallied in the relevant item (i.e., item 1, 2 or 3) as well as a parallel tally in item 5.

⁴ = Invasives may occur in or out of planted areas, but still within the easement and will therefore be calculated against the overall easement acreage. Invasives of concern/interest are listed below. The list of high concern species are those with the potential to directly outcompete native, young, woody stems in the short-term (e.g. monitoring period or shortly thereafter) or affect the community structure for existing, more established tree/shrub stands over timeframes that are slightly longer (e.g. 1-2 decades). The low/moderate concern group are those species that generally do not have this capacity over the timeframes discussed and therefore are not expected to be mapped with regularity, but can be mapped, if in the judgment of the observer their coverage, density or distribution is suppressing the viability, density, or growth of planted woody stems. Decisions as to whether remediation will be needed are based on the integration of risk factors by EEP such as species present, their coverage, distribution relative to native biomass, and the practicality of treatment. For example, even modest amounts of Kudzu or Japanese Knotweed early in the projects history will warrant control, but potentially large coverages of Microstegium in the herb layer will not likely trigger control because of the limited capacities to impact tree/shrub layers within the timeframes discussed and the potential impacts of treating extensive amounts of ground cover. Those species with the "watch list" designator in gray shade are of interest as well, but have yet to be observed across the state with any frequency. Those in *red italics* are of particular interest given their extreme risk/threat level for mapping as points where isolated specimens are found, particularly early in a projects monitoring history. However, areas of discreet, dense patches will of course be mapped as polygons. The symbology scheme below was one that was found to be helpful for symbolizing invasives polygons, particularly for situations where the condition for an area is somewhere between isolated specimens and dense, discreet patches. In any case, the point or polygon/area feature can be symbolized to describe things like high or low concern and species can be listed as a map inset, in legend items if the number of species are limited or in the narrative section of the executive summary.

Mockingbird MY3 Vegetation Monitoring Plot Photos 10/10/2023

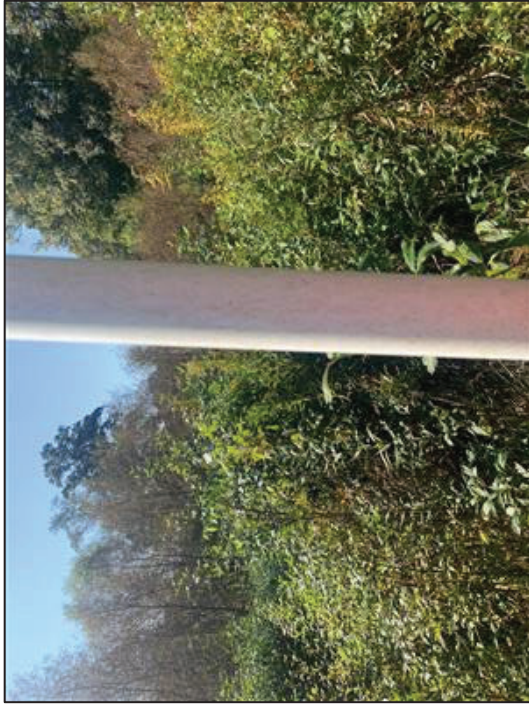

Vegetation Plot 1



Vegetation Plot 2



Vegetation Plot 3



Vegetation Plot 4



Vegetation Plot 6



Vegetation Plot 8



Vegetation Plot 5



Vegetation Plot 7



Vegetation Plot 9



Vegetation Plot 10

Mockingbird MY3 Random Vegetation Monitoring Plot Photos (10/10/2023)



Random Plot 1



Random Plot 2



Random Plot 3




Random Plot 4



Random Plot 5

Mockingbird Monitoring Device Photos 2023

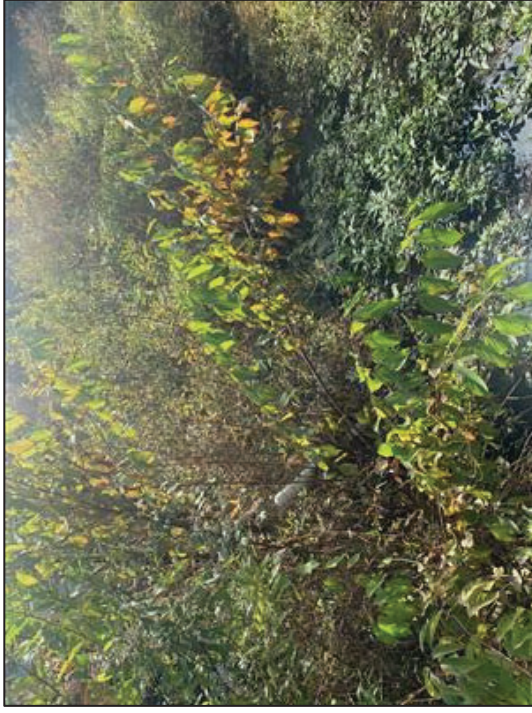

Stage Recorder HC1 (10/10/2023)



Stage Recorder NM2 (10/10/2023)



Flow Gauge NM1 (10/10/2023)



Flow Gauge NM4 (10/10/2023)

Mockingbird Monitoring Device Photos



Flow Gauge TP2 (10/10/2023)



Flow Gauge TP3 (10/10/2023)



Groundwater Well 1 (10/10/2023)

Mockingbird Culvert Crossing Photos 2023



Downstream HC1 (06/01/2023)



Upstream HC1 (10/08/2023)



Downstream NM2 (06/06/2023)



Upstream NM2 (06/06/2023)

Appendix C

Vegetation Plot Data

Table 7. Planted Species Summary

Common Name	Scientific Name	Mitigation Plan %	As-Built %	Total Stems Planted
Water Oak	<i>Quercus nigra</i>	15	14	4,000
Willow Oak	<i>Quercus phellos</i>	15	12	3,500
River Birch	<i>Betula nigra</i>	15	12	3,500
Sycamore	<i>Platanus occidnetalis</i>	15	12	3,400
Northern Red Oak	<i>Quercus rubra</i>	10	11	3,300
Persimmon	<i>Diospyros virginiana</i>	5	11	3,200
Yellow Poplar	<i>Liriodendron tulipifera</i>	10	11	3,200
Green Ash	<i>Fraxinus pennsylvanica</i>	10	5	1,500
Crab Apple	<i>Malus angustifolia</i>	0	3	900
Eastern Redbud	<i>Cercis canadensis</i>	0	3	800
Black Walnut	<i>Juglans nigra</i>	0	2	700
Elderberry	<i>Sambucus candadensis</i>	0	1	500
Silky Dogwood	<i>Cornus amomum</i>	0	1	400
Sugarberry	<i>Celtis laevigata</i>	0	1	350
American Plum	<i>Prunus americana</i>	0	1	300
Blackgum	<i>Nyssa sylvatica</i>	5	0	0
Total				29,550
Planted Area				18.6
As-built Planted Stems/Acre				1,589

Table 8. Vegetation Plot Mitigation Success Summary

Wetland/Stream Vegetation Totals
(per acre)

Plot #	Planted Stems/Acre	Volunteer Stems/Acre	Total Stems/Acre	Average Stem Height (ft)	Success Criteria Met?
1	567	40	607	3.6	Yes
2	647	40	688	3.8	Yes
3	607	445	1052	1.7	Yes
4	728	40	769	9.0	Yes
5	809	243	1052	7.5	Yes
6	445	40	486	3.8	Yes
7	486	40	526	5.9	Yes
8	728	1295	2023	6.2	Yes
9	809	121	931	6.5	Yes
10	728	1416	2145	7.3	Yes
RV1	567	0	567	4.1	Yes
RV2	607	0	607	6.6	Yes
RV3	688	0	688	4.4	Yes
RV4	688	0	688	4.1	Yes
RV5	647	0	647	5.5	Yes
Project Avg	650	372	898	5.3	Yes

Table 9. Stem Count Total and Planted by Plot Species

Scientific Name	Common Name	Species Type	Current Plot Data (MY3 2023)																										
			100021-01-0001	100021-01-0002	100021-01-0003	100021-01-0004	100021-01-0005	100021-01-0006	100021-01-0007	100021-01-0008	100021-01-0009	100021-01-0010																	
			P	N	S	P	N	S	P	N	S	P	N	S	P	N	S	P	N	S	P	N	S						
Betula nigra	river birch	Tree	1	1	2				11	11	11	3	3	3				3	3	3	17	17	17	7	7	7	10	10	10
Celtis laevigata	sugarberry	Tree																											
Celtis occidentalis	common hackberry	Tree										6	6	6															
Cephalanthus occidentalis	common buttonbush	Shrub																											
Cercis canadensis	eastern redbud	Tree																											
Diospyros virginiana	common persimmon	Tree				1	1	1	1	1	1	3	3	3	2	2	2	6	6	6	7	7	7						
Fraxinus pennsylvanica	green ash	Tree																											
Hamamelis virginiana	American witchhazel	Tree																											
Juglans nigra	black walnut	Tree																											
Liquidambar styraciflua	sweetgum	Tree																											
Liriodendron tulipifera	tuliptree	Tree				1	1	1																1	1	1			
Morus rubra	red mulberry	Tree																											
Nyssa biflora	swamp tupelo	Tree							2	2	2																		
Platanus occidentalis	American sycamore	Tree	1	1	1				2	3	3	5	5	8	5	5	5										1	1	1
Prunus americana	American plum	Tree																											
Quercus alba	white oak	Tree				5	5	5																					
Quercus nigra	water oak	Tree										1	1	1										1	1	1			
Quercus phellos	willow oak	Tree				5	5	5	4	4	4	4	4	4	4	4	4	2	2	2	2	2	2	2	2	2	2	2	2
Quercus rubra	northern red oak	Tree	12	12	12	4	4	4	2	2	2	2	2	2	2	2	2							6	6	6	6	6	6
Salix nigra	black willow	Tree																											
Ulmus alata	winged elm	Tree																											
Ulmus americana	American elm	Tree																											
		Stem count	14	14	15	16	16	17	18	18	19	20	20	26	11	11	12	12	12	13	18	18	18	20	20	23	18	18	53
		size (ares)	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1	1
		size (ACRES)	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02	0.02
		Species count	3	3	3	5	5	6	4	4	5	6	6	7	3	3	4	4	4	4	4	4	4	4	4	6	4	4	4
		Stems per ACRE	567	567	607	647	647	688	607	607	728	809	809	1052	445	445	486	486	486	526	728	728	728	809	809	931	728	728	2145

Scientific Name	Common Name	Species Type	Current Plot Data (MY3 2023)												Annual Means												
			RVP1		RVP2		RVP3		RVP4		RVP5		MY3 (2023)		MY2 (2022)		MY1 (2021)		MY0 (2020)								
			P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T	P-noLS	T							
<i>Betula nigra</i>	river birch	Tree	2	2	2	6	6	6	1	1	1	2	2	2	1	1	64	64	65	53	53	51	51	51	54	54	
<i>Celtis laevigata</i>	sugarberry	Tree																				1	1	1			
<i>Celtis occidentalis</i>	common hackberry	Tree																									
<i>Cephalanthus occidentalis</i>	common buttonbush	Shrub	4	4	4																						
<i>Cercis canadensis</i>	eastern redbud	Tree																									
<i>Diospyros virginiana</i>	common persimmon	Tree	6	6	6	2	2	2																			
<i>Fraxinus pennsylvanica</i>	green ash	Tree							4	4	4	4	4	4	1	1	10	5	72	5	5	5	5	5	122	5	5
<i>Hamamelis virginiana</i>	American witchhazel	Tree																2									
<i>Juglans nigra</i>	black walnut	Tree																									
<i>Liquidambar styraciflua</i>	sweetgum	Tree																									
<i>Liriodendron tulipifera</i>	tuliptree	Tree																									
<i>Morus rubra</i>	red mulberry	Tree																									
<i>Nyssa biflora</i>	swamp tupelo	Tree				2	2	2																			
<i>Platanus occidentalis</i>	American sycamore	Tree				3	3	3																			
<i>Prunus americana</i>	American plum	Tree																									
<i>Quercus alba</i>	white oak	Tree				1	1	10	10	10																	
<i>Quercus nigra</i>	water oak	Tree	1	1	1	1	1	3	3	3																	
<i>Quercus phellos</i>	willow oak	Tree	1	1	1																						
<i>Quercus rubra</i>	northern red oak	Tree																									
<i>Salix nigra</i>	black willow	Tree																									
<i>Ulmus alata</i>	winged elm	Tree																									
<i>Ulmus americana</i>	American elm	Tree																									
	Stem count		14	14	14	15	15	15	17	17	17	17	17	17	16	16	241	206	331	167	167	159	159	308	297	297	
	size (ares)		1			1			1						1		15			15		15			15		
	size (ACRES)		0.02			0.02			0.02						0.02		0.37			0.37		0.37			0.37		
	Species count		5	5	5	6	6	6	4	4	4	5	5	5	6	6	11	11	15	11	11	11	11	13	14		
	Stems per ACRE		567	567	567	607	607	607	688	688	688	688	688	688	647	647	650	556	893	631	645	645	656	1049	1202		

Appendix D

Stream Measurement and Geomorphology Data

**Table 10. Baseline Stream Data Summary
Mockingbird Mitigation Site - Reach NM2**

Parameter	Gauge ²				Regional Curve				Pre-Existing Condition								Reference Reach(es) Data				Design				Monitoring Baseline				
	LL	UL	Eq.		Min	Mean	Med	Max	SD ³	n	Min	Mean	Med	Max	SD ³	n	Min	Mean	Med	Max	SD ³	n	Min	Mean	Med	Max	SD ³	n	
Dimension and Substrate - Rifle Only																													
Bankfull Width (ft)				9.3	13.7	15.0	15.0	15.0	2	13.7	15.0	15.0	15.0	2	13.7	15.0	15.0	15.0	15.0	2	13.7	15.0	15.0	15.0	15.0	15.0	15.0	15.0	2
Floodprone Width (ft)				20.7	>30	>30	>30	>30	2	>30	>30	>30	>30	2	>30	>30	>30	>30	>30	>30	2	>30	>30	>30	>30	>30	>30	>30	2
Bankfull Mean Depth (ft)				1.8	2.5	2.5	2.5	2.5	2	2.5	2.5	2.5	2.5	2	2.5	2.5	2.5	2.5	2.5	2	2.5	2.5	2.5	2.5	2.5	2.5	2.5	2	
Bankfull Max Depth (ft)				2.6	4.0	4.0	4.0	4.0	2	4.0	4.0	4.0	4.0	2	4.0	4.0	4.0	4.0	4.0	2	4.0	4.0	4.0	4.0	4.0	4.0	4.0	2	
Bankfull Cross Sectional Area (ft ²)				17.8	23.0	23.0	23.0	23.0	2	23.0	23.0	23.0	23.0	2	23.0	23.0	23.0	23.0	23.0	2	23.0	23.0	23.0	23.0	23.0	23.0	23.0	2	
Width:Depth Ratio				3.8	5.6	5.6	5.6	5.6	2	5.6	5.6	5.6	5.6	2	5.6	5.6	5.6	5.6	5.6	2	5.6	5.6	5.6	5.6	5.6	5.6	5.6	2	
Enrichment Ratio				2.1	>2.2	>2.2	>2.2	>2.2	2	>2.2	>2.2	>2.2	>2.2	2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	>2.2	2
Bank Height Ratio				1.1	2.2	2.2	2.2	2.2	2	2.2	2.2	2.2	2.2	2	2.2	2.2	2.2	2.2	2.2	2	2.2	2.2	2.2	2.2	2.2	2.2	2.2	2	
Profile																													
Rifle Length (ft)										4																			
Rifle Slope (ft/ft)																													
Pool Length (ft)										3																			
Pool Max depth (ft)																													
Pool Spacing (ft)										12																			
Pattern																													
Channel Beltwidth (ft)										15																			
Radius of Curvature (ft)										6																			
Rc:Bankfull width (ft/ft)										1																			
Meander Wavelength (ft)										23																			
Meander Width Ratio										4.4																			
Transport parameters																													
Reach Shear Stress (competency) lb/ft ²																													
Max part size (mm) mobilized at bankfull																													
Stream Power (transport capacity) W/m ²																													
Additional Reach Parameters																													
Resgen Classification																													
Bankfull Velocity (fps)																													
Bankfull Discharge (cfs)																													
Valley length (ft)																													
Channel Thalweg length (ft)																													
Sinuosity (ft)																													
Water Surface Slope (Channel) (ft/ft)																													
Channel slope (ft/ft)																													
Bankfull Floodplain Area (acres)																													
% of Reach with Eroding Banks																													
Channel Stability or Habitat Metric																													
Biological or Other																													

1 = The distribution for these parameters varies include information from both the cross-section measurements and the longitudinal profiles. 2 = For projects with a proximal USGS gauge is file with the project reach (add the bankfull verification - mss). 3 = Utilizing X3 measurement data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riserslope. 4 = Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data. 5. 0/ value needed only if the n exceeds 3. 6 = Seek details release that these will typically use the file file.

Table 10. Baseline Stream Data Summary (continued)
Mockingbird Mitigation Site - Reach NM3

Parameter	Gauge ²				Regional Curve				Pre-Existing Condition					Reference Reach(es) Data					Design					Monitoring Baseline				
	LL	UL	Eq.		Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n
Dimension and Substrate - Rifle Only																												
Bankfull Width (ft)						6.7	21.9			1	5.2	13.7			2	6.4												
Floodprone Width (ft)										1	>30				2	30.0												
Bankfull Mean Depth (ft)						0.6	1.4			1	0.6				2	0.7												
Bankfull Max Depth (ft)						1.4				1	0.8				2	1.0												
Bankfull Cross Sectional Area (ft ²)						3.9	11.4			1	3.0				2	4.7												
Width/Depth Ratio						3.3				1	>2.2				2	8.7												
Enrichment Ratio						0.8				1	>2.2				2	4.7												
Bank Height Ratio						1.0				1	1.0				2	1.0												
Profile																												
Rifle Length (ft)											4				22	4.4												
Rifle Slope (ft/ft)															43	0.5												
Pool Length (ft)											3				12	6												
Pool Max depth (ft)															43	16												
Pool Spacing (ft)											12				15													
Pattern																												
Channel Beltwidth (ft)											15				18													
Radius of Curvature (ft)											6				7													
Rc:Bankfull width (ft/ft)											1				1.1													
Meander Wavelength (ft)											23				28													
Meander Width Ratio											3.6				4													
Transport parameters																												
Reach Shear Stress (competency) lb/ft ²																												
Max part size (mm) mobilized at bankfull																												
Stream Power (transport capacity) W/m ²																												
Additional Reach Parameters																												
Resgen Classification																												
Bankfull Velocity (fps)																												
Bankfull Discharge (cfs)																												
Valley length (ft)																												
Channel Thalweg length (ft)																												
Sinuosity (ft)																												
Water Surface Slope (Channel) (ft/ft)																												
Channel slope (ft/ft)																												
Bankfull Floodplain Area (acres)																												
% of Reach with Eroding Banks																												
Channel Stability or Habitat Metric																												
Biological or Other																												

Skewed distributions will typically use the fitted distribution.

1 - The distribution for these parameters varies significantly from both the cross-section measurements and the longitudinal profiles. 2 - For projects with a proximal USGS gauge in-line with the project reach (add the bankfull verification - map).

3 - Utilizing XS measurement data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riser/slope.

4 - Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data. 5 - Of value needed only if the n exceeds 3.

Table 10. Baseline Stream Data Summary (continued)
Mockingbird Mitigation Site - Reach HC1

Parameter	Gauge ²				Regional Curve				Pre-Existing Condition								Reference Reach(es) Data								Design								Monitoring Baseline							
	LL	UL	Eq.		Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Med	Max		Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n								
Dimension and Substrate - Rifle Only																																								
Bankfull Width (ft)					11.9	15.4	20.0	27.4	3.0	3	5.2	13.7	21.8	33.3	2	19.6	20.6	22.2	22.2	1.4	3					19.6	20.6	20.0	22.2	1.4	3									
Floodprone Width (ft)					27.4	30.0	50.0	>50	3	>30					2	65.0	65.0	65.0	65.0	0.0	3					65.0	65.0	65.0	65.0	0.0	3									
Bankfull Mean Depth (ft)					1.9	2.0	2.5	3.8	3	0.8					2	2.2	2.5	2.4	2.8	0.3	3					2.3	2.5	2.4	2.8	0.3	3									
Bankfull Max Depth (ft)					3.2	3.7	3.8	4.0	3	3.0					2	47.0	47.0	45.6	45.6	7.1	3					33.3	37.4	33.4	45.6	7.1	3									
Bankfull Cross Sectional Area (ft ²)					23.0	38.0	40.0	10.1	3	8.9					2	10.1	10.1	10.1	10.1	0.0	3					2.9	3.2	3.3	3.3	0.2	3									
Width:Depth Ratio					6.1	6.2	10.1	>4	3	>2.2					2	2.3	2.3	2.3	2.3	0.2	3					2.9	3.2	3.3	3.3	0.2	3									
Enrichment Ratio					1.4	1.8	1.8	1.8	3	1.2					2	1.0	1.0	1.0	1.0	0.0	3					1.0	1.0	1.0	1.0	0.0	3									
Bank Height Ratio					1.8	1.8	1.8	1.8	3	1.2					2	1.0	1.0	1.0	1.0	0.0	3					1.0	1.0	1.0	1.0	0.0	3									
Profile																																								
Rifle Length (ft)										4						29	8	24	22	93	15	30					29	8	24	22	93	15	30							
Rifle Slope (ft/ft)																10	0.01	1.0	0.8	2.4	0.7	30					0.01	1.0	0.8	2.4	0.7	30								
Pool Length (ft)										3						8	17	47	50	65	12	28					67	17	47	50	65	12	28							
Pool Max depth (ft)																																								
Pool Spacing (ft)										12						29	46	73	70	163	22	27					103	46	73	70	163	22	27							
Pattern																																								
Channel Beltwidth (ft)										15						45	82	45	82	103	103						82	45	82	103	103									
Radius of Curvature (ft)										6						38	38	38	38	4.4	4.4						103	38	38	38	38									
Re-Bankfull width (ft/ft)										1						1.7	1.7	1.7	1.7	4.4	4.4						4.4	1.7	1.7	1.7	1.7									
Meander Wavelength (ft)										23						95	95	95	95	123	123						123	95	95	95	95									
Meander Width Ratio										3.6						2.1	2.1	2.1	2.1	3.5	3.5						3.5	2.1	2.1	2.1	2.1									
Transport parameters																																								
Reach Shear Stress (competency) lb/ft ²																55.5	55.5	55.5	55.5	82	82						82	45	82	103	103									
Max part size (mm) mobilized at bankfull																103.3	103.3	103.3	103.3	103	103						103	38	38	38	38									
Stream Power (transport capacity) W/m ²																6.9	6.9	6.9	6.9	4.4	4.4						4.4	1.7	1.7	1.7	1.7									
Additional Reach Parameters																																								
Resegen Classification																																								
Bankfull Velocity (fps)																E5	E4	E4	E4	E3/E4	E3/E4						E3/E4	E4	E4	E4	E3/E4									
Bankfull Discharge (cfs)																1925	1925	1925	1925	2083	2083						1925	2083	2083	2083	2083									
Valley length (ft)																2135	2135	2135	2135	108	108						2083	108	108	108	108									
Channel Thalweg length (ft)																1.11	1.11	1.11	1.11	0.003	0.003						1.08	0.003	0.003	0.003	0.003									
Channel Sinuosity (ft)																0.0051	0.0051	0.0051	0.0051	0.003	0.003						0.003	0.003	0.003	0.003	0.003									
Water Surface Slope (Channel) (ft/ft)																0.0028	0.0028	0.0028	0.0028	0.003	0.003						0.003	0.003	0.003	0.003	0.003									
Channel slope (ft/ft)																																								
Bankfull Floodplain Area (acres)																																								
% of Reach with Eroding Banks																																								
Channel Stability or Habitat Metric																																								
Biological or Other																																								

1 - The distribution for these parameters varies include information from both the cross-section measurements and the longitudinal profile. 2 - For projects with a proximal USGS gauge is file with the project reach (add the bankfull verification - mes).
 3 - Utilizing XS measurement data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riser/slope.
 4 - Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data. 5 - Of value needed only if the n exceeds 3.
 Shaded cells indicate that these will typically not be filled in.

Table 10. Baseline Stream Data Summary (continued)
Mockingbird Mitigation Site - Reach HC2-B

Parameter	Gauge ²				Regional Curve				Pre-Existing Condition				Reference Reach(es) Data				Design				Monitoring Baseline			
	LL	UL	Eq.	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Med	Max	Min	Mean	Med	Max	SD ⁵	n
Dimension and Substrate - Rifle Only																								
Bankfull Width (ft)					11.7	15.0	17.7	13.7	2	5.2	11.7	15.0	17.7	13.7	2	12.6	12.0	12.0	7	15	12	54	12	14
Floodprone Width (ft)					15.0	15.0	15.0	15.0	1	>30	15.0	15.0	15.0	15.0	1	50.0	>50	>50	2	32	33	43	10	13
Bankfull Mean Depth (ft)					1.0	1.0	1.0	1.0	1	0.6	1.0	1.0	1.0	1.0	2	1.3	1.6	1.6	2	4.4	4.4	4.4	1.2	14
Bankfull Max Depth (ft)					1.2	1.2	1.2	1.2	1	0.8	1.2	1.2	1.2	1.2	2	1.8	1.8	1.8	2	10	10	10	4	12
Bankfull Cross Sectional Area (ft ²)					11.9	11.9	11.9	11.9	1	3.0	11.9	11.9	11.9	11.9	2	18.1	18.4	18.4	2	3.5	4	4	4	12
Width/Depth Ratio					11.6	11.6	11.6	11.6	1	8.9	11.6	11.6	11.6	11.6	2	9.7	9.7	9.7	2	17	17	17	4	12
Enrichment Ratio					1.3	1.3	1.3	1.3	1	>2.2	1.3	1.3	1.3	1.3	2	4.0	4.0	4.0	2	3.5	4	4	4	12
'Bank Height Ratio					2.0	2.0	2.0	2.0	1	1.0	2.0	2.0	2.0	2.0	2	1.0	1.0	1.0	2	3.5	4	4	4	12
Profile																								
Rifle Length (ft)										4									6	17	15	12	54	12
Rifle Slope (ft/ft)																				0.1	1.6	1.4	4.4	1.2
Pool Length (ft)										3									5	39	32	33	43	10
Pool Max depth (ft)																								
Pool Spacing (ft)										12									17	59	43	45	55	12
Pattern																								
Channel Belwidth (ft)										15									26	47	26	47	59	14
Radius of Curvature (ft)										6									22	59	22	59	59	14
Rc:Bankfull width (ft/ft)										1									1.7	4.4	1.7	4.4	4.4	14
Meander Wavelength (ft)										23									55	71	55	71	71	14
Meander Width Ratio										3.6									3.5	4	3.5	4	4	12
Transport parameters																								
Reach Shear Stress (competency) lb/ft ²																								
Max part size (mm) mobilized at bankfull																								
Stream Power (transport capacity) W/m ²																								
Additional Reach Parameters																								
Resgen Classification																								
Bankfull Velocity (fps)																								
Bankfull Discharge (cfs)																								
Valley length (ft)																								
Channel Thalweg length (ft)																								
Sinuosity (ft)																								
Water Surface Slope (Channel) (ft/ft)																								
Channel slope (ft/ft)																								
Bankfull Floodplain Area (acres)																								
% of Reach with Eroding Banks																								
Channel Stability or Habitat Metric																								
Biological or Other																								

1 - The distribution for these parameters varies include information from both the cross-section measurements and the longitudinal profiles. 2 - For projects with a proximal USGS gauge is file with the project reach (add the bankfull verification - map).
3 - Utilizing XS measurement data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riserslope.
4 - Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data. 5 - Of values needed only if the n exceeds 3.
Skewed distributions that skew will typically use the file file.

**Table 10. Baseline Stream Data Summary (continued)
Mockingbird Mitigation Site - Reach JS1**

Parameter	Gauge ²				Regional Curve				Pre-Existing Condition							Reference Reach(es) Data							Design							Monitoring Baseline						
	LL	UL	Eq.	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Med	Max	SD ⁵	n	Min	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n					
Dimension and Substrate - <u>Rifle Only</u>																																				
Bankfull Width (ft)																																				
Floodprone Width (ft)																																				
Bankfull Mean Depth (ft)																																				
Bankfull Max Depth (ft)																																				
Bankfull Cross Sectional Area (ft ²)																																				
Width:Depth Ratio																																				
Enrichment Ratio																																				
'Bank Height Ratio																																				
Profile																																				
Rifle Length (ft)																																				
Rifle Slope (ft/ft)																																				
Pool Length (ft)																																				
Pool Max depth (ft)																																				
Pool Spacing (ft)																																				
Pattern																																				
Channel Beltwidth (ft)																																				
Radius of Curvature (ft)																																				
Re-Bankfull width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
Transport parameters																																				
Reach Shear Stress (competency) lb/ft ²																																				
Max part size (mm) mobilized at bankfull																																				
Stream Power (transport capacity) W/m ²																																				
Additional Reach Parameters																																				
Respin Classification																																				
Bankfull Velocity (fps)																																				
Bankfull Discharge (cfs)																																				
Valley length (ft)																																				
Channel Thalweg length (ft)																																				
Sinuosity (ft)																																				
Water Surface Slope (Channel) (ft/ft)																																				
Channel slope (ft/ft)																																				
Bankfull Floodplain Area (acres)																																				
% of Reach with Eroding Banks																																				
Channel Stability or Habitat Metric																																				
Biological or Other																																				
Statistical tests that were used will typically use the first 40																																				

1 = The distribution for these parameters can include information from both the cross-section measurements and the longitudinal profile. 2 = For projects with a proximal USGS gauge in-line with the project reach (add the bankfull verification - nos). 3 = Utilizing X3 measurement data produces an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riserslope. 4 = Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data. 5. 0/ value needed only if the n exceed 3.

Statistical tests that were used will typically use the first 40

Appendix D, Table 11 - Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)

		Project Name/Number: Mockingbird #100021																																		
		Cross Section 1 (Pool)			Cross Section 2 (Riffle)			Cross Section 3 (Pool)			Cross Section 4 (Riffle)			Cross Section 5 (Pool)																						
Bankfull Elevation (ft) - Based on AB-XSA	Bankfull Width (ft)	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+	Base	MY1	MY2	MY3	MY5	MY7	MY+							
				709.5	709.6	709.7	709.6				709.5	709.7	709.8	709.8	709.8			711.2	711.5	711.5	711.6				711.1	711.3	711.4	711.4			717.9	718.3	718.2	718.1		
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
		1.6	2.1	2.3	2.4				1.8	2.0	2.1	2.0			1.3	1.2	1.2	1.0				1.2	1.0	1.0	0.9			3.1	2.0	2.3	3.0					
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
		15.1	15.2	15.6	15.6				17.0	16.4	14.0	14.6			4.5	4.3	3.6	3.5				4.3	3.6	3.8	3.5			25.8	19.3	19.8	20.4					
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
		1.0	0.8	0.9	0.9				1.0	1.0	0.9	0.9			1.0	1.0	0.9	0.9				1.0	0.9	0.9	0.9			-	-	-	-	-	-	-	-	
Bankfull Elevation (ft) - Based on AB-XSA		Cross Section 6 (Riffle)																																		
		Cross Section 7 (Pool)			Cross Section 8 (Riffle)			Cross Section 9 (Riffle)			Cross Section 10 (Pool)																									
		718.0	718.1	718.2	718.2				713.5	713.6	713.4	713.6			710.6	710.7	710.7	710.8				710.6	710.7	710.7	710.8			710.5	710.5	710.5	710.6					
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
		16.3	17.3	17.3	17.3				15.4	17.5	15.3	16.1			22.2	24.4	22.2	22.2				22.2	24.4	22.2	22.2			-	-	-	-	-	-	-	-	
		2.0	1.6	1.9	2.1				3.0	3.1	3.1	2.2			2.8	2.9	2.9	2.9				2.8	2.9	2.9	2.9			3.9	4.0	2.1	3.9			-		
		718.0	717.7	717.9	718.0				714.0	714.2	714.0				710.6	710.6	710.8	710.6				710.6	710.6	710.8	710.6			-	710.7	710.6	710.4			-		
		23.2	14.7	19.3	20.7				27.6	29.0	29.2	28.7			45.6	43.6	46.6	39.6				45.6	43.6	46.6	39.6			50.7	38.5	32.9	47.2			-		
		1.0	0.8	0.9	0.9				1.0	1.0	1.1	1.0			1.0	1.0	1.0	1.0				1.0	1.0	1.0	1.0			-	-	-	-	-	-	-	-	
Bankfull Elevation (ft) - Based on AB-XSA		Cross Section 11 (Pool)																																		
		Cross Section 12 (Riffle)			Cross Section 13 (Riffle)			Cross Section 14 (Pool)			Cross Section 15 (Riffle)																									
		713.2	713.3	713.1	713.4				713.6	713.5	713.2	713.6			714.9	714.9	715.0	715.0				715.1	715.1	715.0	715.0			758.0	758.0	758.0	758.1			-		
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
		4.3	4.0	4.4	4.0				2.4	2.3	2.5	2.4			3.3	2.9	3.0	3.0				4.0	4.3	4.2	4.2			1.6	1.7	1.8	1.7			-		
		46.3	40.9	47.1	41.3				33.3	29.3	36.0	33.0			33.3	34.4	33.8	32.9				47.7	47.8	48.9	46.2			14.0	12.7	16.0	12.7			-		
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
		1.0	0.8	0.9	0.9				1.0	1.0	1.1	1.0			1.0	1.0	1.0	1.0				1.0	1.0	1.0	1.0			-	-	-	-	-	-	-	-	
Bankfull Elevation (ft) - Based on AB-XSA		Cross Section 16 (Pool)																																		
		Cross Section 17 (Riffle)			Cross Section 18 (Pool)			Cross Section 19 (Riffle)			Cross Section 20 (Riffle)			Cross Section 21 (Riffle)																						
		757.9	757.9	758.0	758.0				751.9	751.5	751.5	751.6			751.8	751.9	752.0	751.9				754.9	754.9	755.0	755.0			715.0	714.9	715.2	715.0			-		
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
		2.9	2.9	3.0	2.7				1.3	1.8	1.7	1.8			2.8	1.9	2.5				1.2	1.1	1.1	1.1			1.2	1.0	1.3	1.3			-			
		23.2	23.5	22.4	19.7				8.9	12.8	11.3	12.0			26.8	28.3	34.3	25.7				5.8	4.8	5.2	4.6			7.5	5.1	8.5	8.8			-		
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
		1.0	0.8	0.9	0.9				1.0	1.0	1.1	1.0			1.0	1.0	1.0	1.0				1.0	1.0	1.0	1.0			-	-	-	-	-	-	-	-	
Bankfull Elevation (ft) - Based on AB-XSA		Cross Section 21 (Riffle) EII																																		
		Cross Section 21 (Riffle) EII																																		
		712.4	712.4	712.5	712.6				712.4	712.5	712.5	712.6			712.4	712.5	712.6				712.4	712.5	712.5	712.6			712.4	712.5	712.6							
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
		24.7	6.1	31.0	33.4				24.7	6.1	31.0	33.4			24.7	6.1	31.0	33.4			24.7	6.1	31.0	33.4			24.7	6.1	31.0	33.4						
		0.7	1.1	0.9	0.9				0.7	1.1	0.9	0.9			0.7	1.1	0.9	0.9			0.7	1.1	0.9	0.9			0.7	1.1	0.9	0.9						
		712.40	712.6	712.5	712.6				712.40	712.6	712.5	712.6			712.40	712.6	712.5	712.6			712.40	712.6	712.5	712.6			712.40	712.6	712.5	712.6						
		2.6	4.2	2.7	2.4				2.6	4.2	2.7	2.4			2.6	4.2	2.7	2.4			2.6	4.2	2.7	2.4			2.6	4.2	2.7	2.4						
		4.5	4.5	5.2	5.4				4.5	4.5	5.2	5.4			4.5	4.5	5.2	5.4			4.5	4.5	5.2	5.4			4.5	4.5	5.2	5.4						
		1.0	1.3	1.0	1.0				1.0	1.3	1.0	1.0			1.0	1.3	1.0	1.0			1.0	1.3	1.0	1.0			1.0	1.3	1.0	1.0						

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

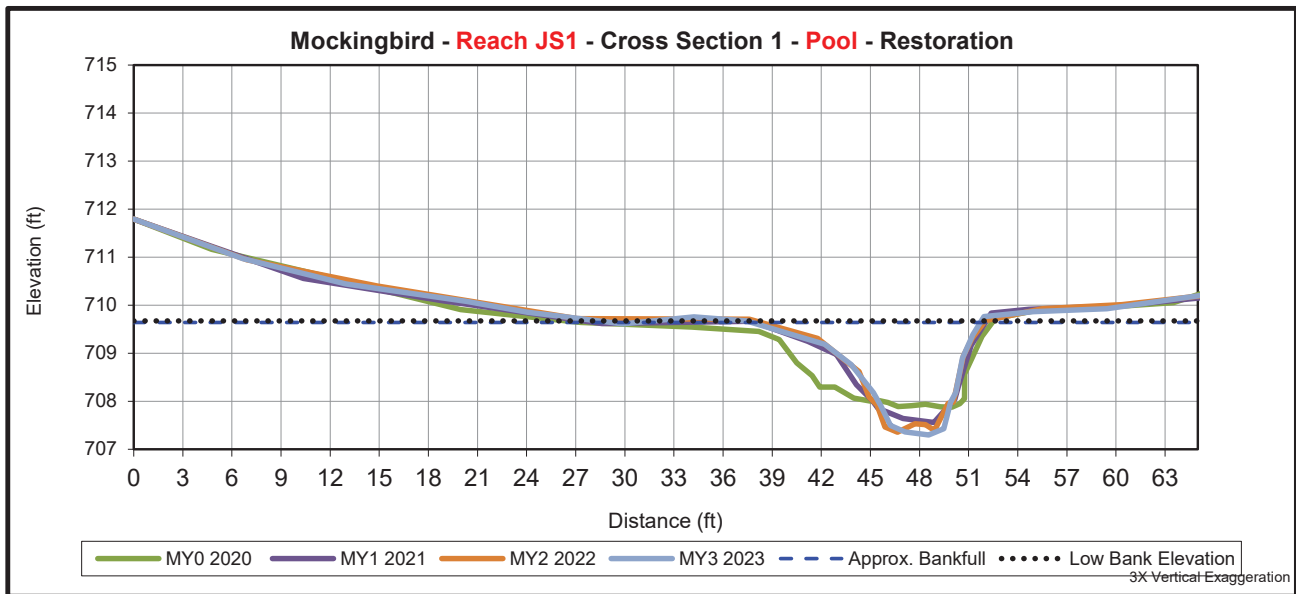

	Cross Section 1 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA	709.45	709.6	709.7	709.6			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	1.6	2.1	2.3	2.4			
Low Bank Elevation (ft)	-	709.7	709.7	709.7			
Bankfull Cross Sectional Area (ft ²) ²	15.1	15.5	15.2	15.6			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

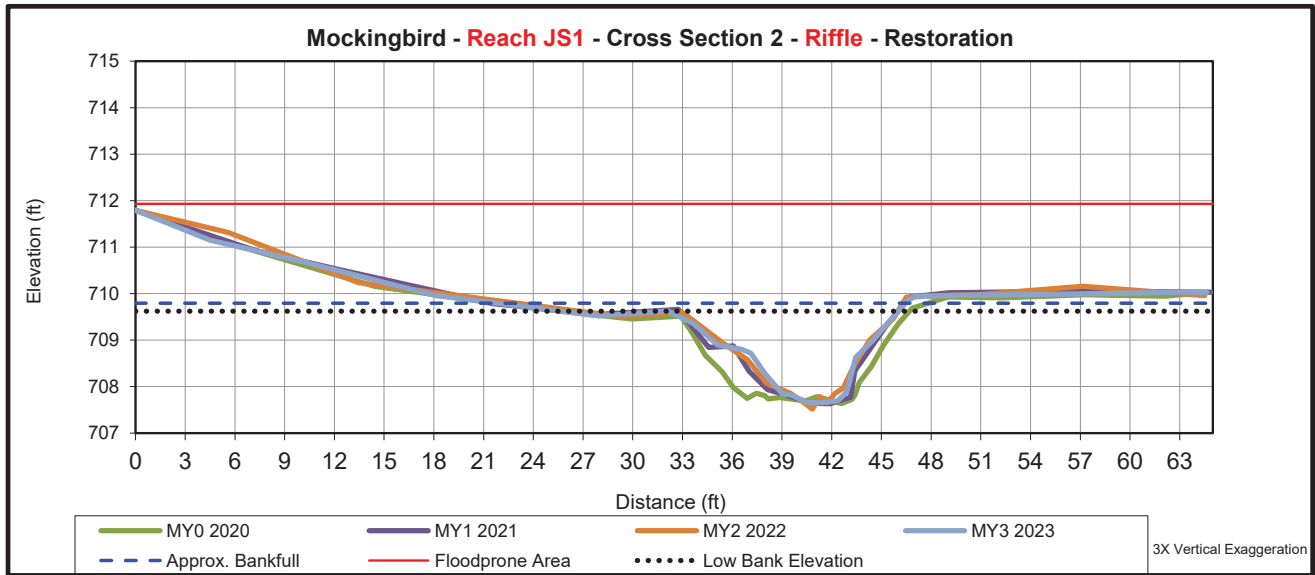

	Cross Section 2 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	709.46	709.7	709.8	709.8			
Bankfull Width (ft) ¹	13.3	13.4	13.3	14.3			
Floodprone Width (ft) ¹	>60.8	>64.1	>64.5	>64.6			
Bankfull Max Depth (ft) ²	1.8	2.0	2.1	2.0			
Low Bank Elevation (ft)	709.46	709.7	709.6	709.6			
Bankfull Cross Sectional Area (ft ²) ²	17.0	16.4	14.0	14.6			
Bankfull Entrenchment Ratio ¹	>4.6	>4.8	>4.8	>4.5			
Bankfull Bank Height Ratio ¹	1.0	1.0	0.9	0.9			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

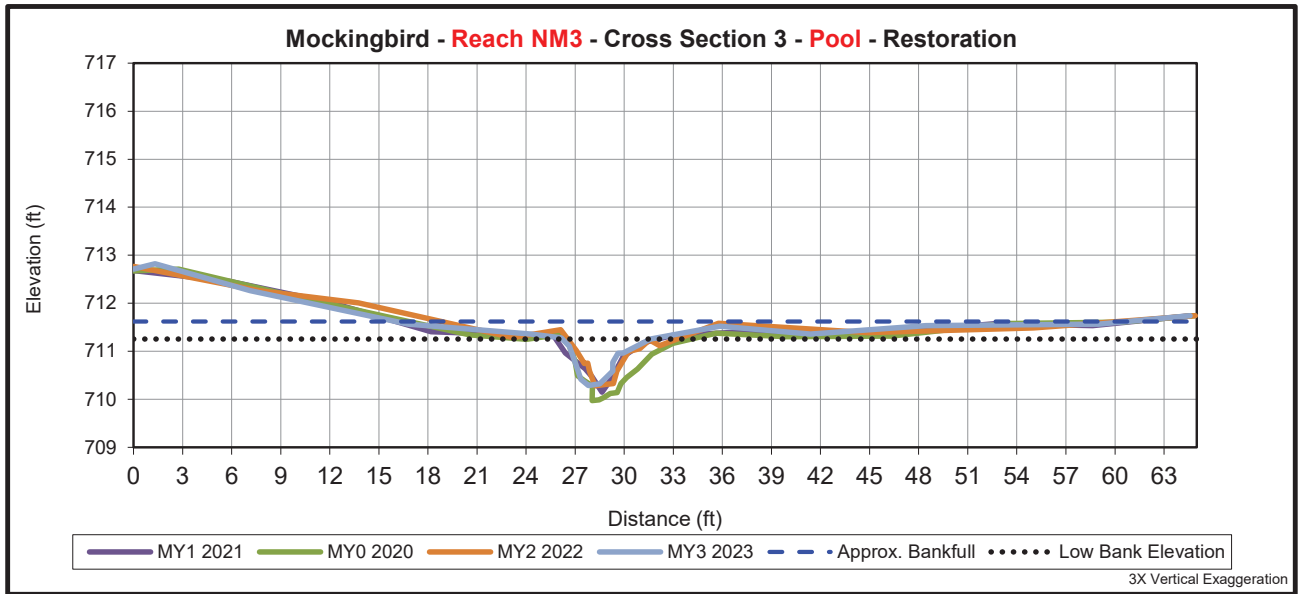

	Cross Section 3 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	711.25	711.5	711.5	711.6			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	1.3	1.2	1.2	1.0			
Low Bank Elevation (ft)	-	711.3	711.4	711.3			
Bankfull Cross Sectional Area (ft ²) ²	4.5	3.3	3.7	2.5			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream




Downstream

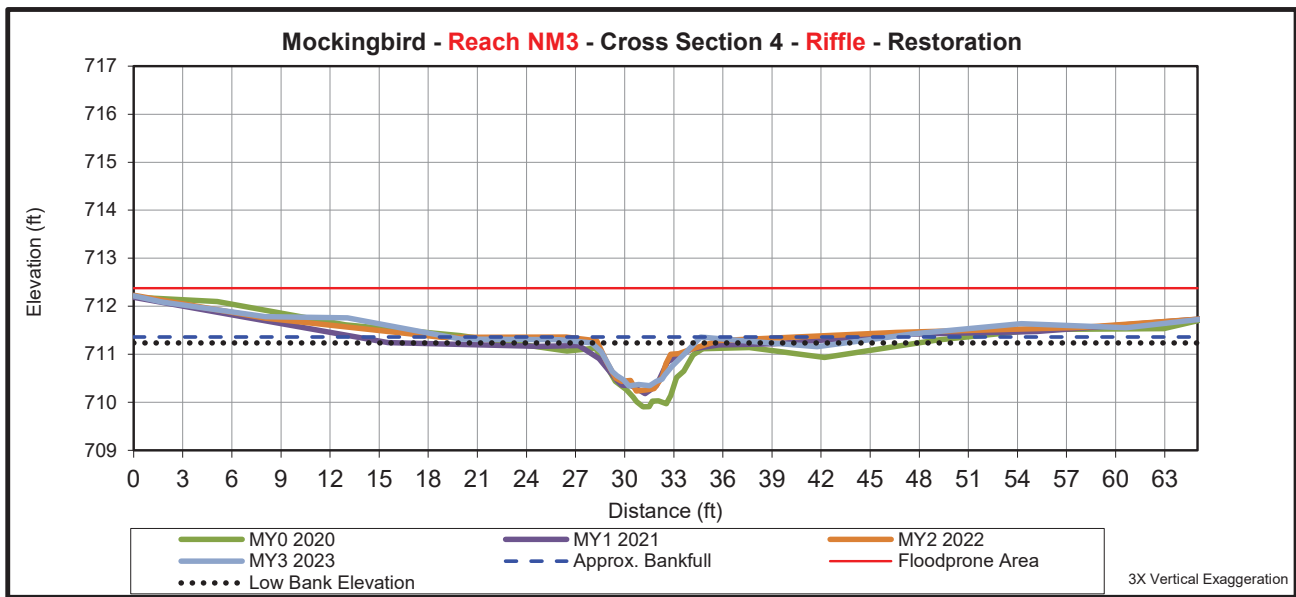

	Cross Section 4 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	711.07	711.3	711.4	711.4			
Bankfull Width (ft) ¹	6.2	8.6	7.5	6.7			
Floodprone Width (ft) ¹	>65	>65.5	>65.4	>65.5			
Bankfull Max Depth (ft) ²	1.2	1.0	1.0	0.9			
Low Bank Elevation (ft)	711.07	711.2	711.3	711.2			
Bankfull Cross Sectional Area (ft ²) ²	4.3	3.6	3.8	3.5			
Bankfull Entrenchment Ratio ¹	>10.6	>7.7	>8.7	>9.8			
Bankfull Bank Height Ratio ¹	1.0	0.9	0.9	0.9			


1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation

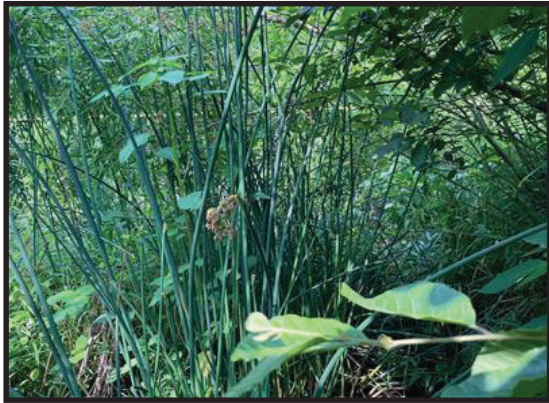

Upstream



Downstream

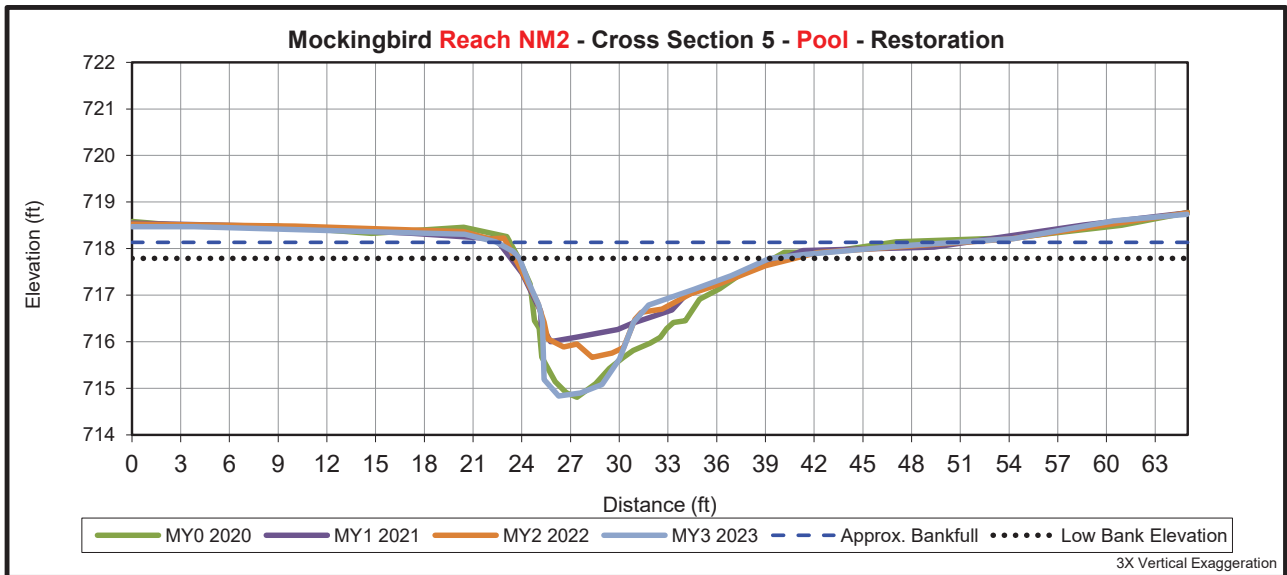

	Cross Section 5 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	717.92	718.3	718.2	718.1			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	3.1	2.0	2.3	3.0			
Low Bank Elevation (ft)	-	718.0	717.9	717.8			
Bankfull Cross Sectional Area (ft ²) ²	25.8	19.3	19.8	20.4			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			


- 1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
- 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

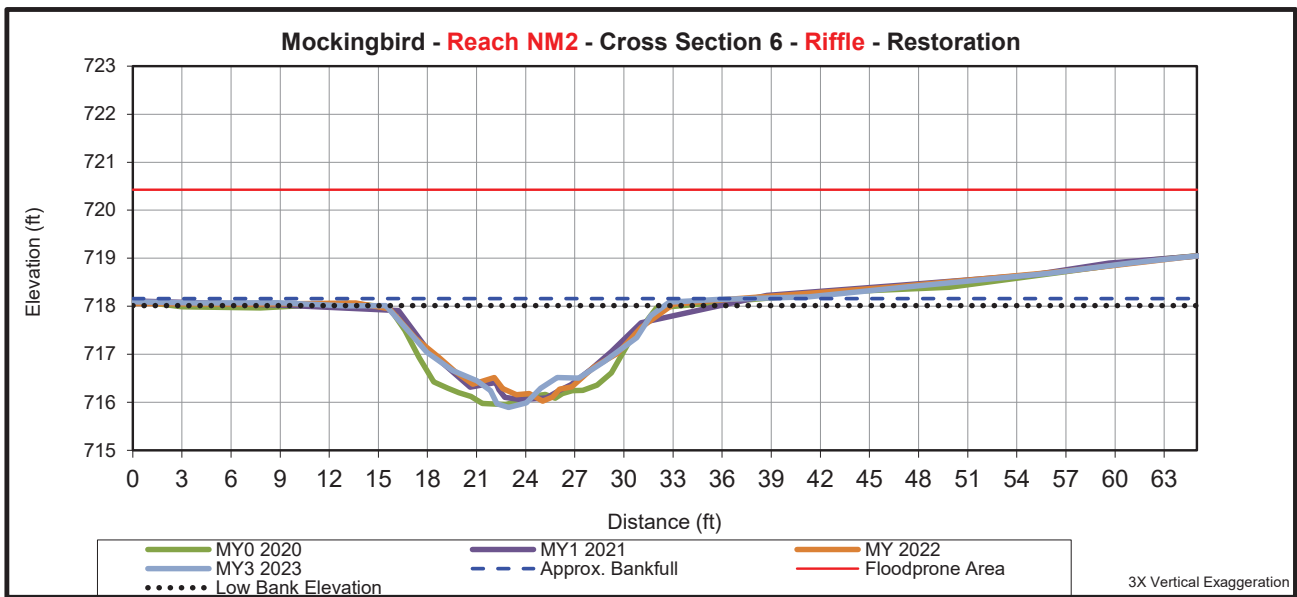

	Cross Section 6 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	717.96	718.1	718.2	718.2			
Bankfull Width (ft) ¹	16.3	21.3	17.3	17.3			
Floodprone Width (ft) ¹	>65	>65.2	>65	>65			
Bankfull Max Depth (ft) ²	2.0	1.6	1.9	2.1			
Low Bank Elevation (ft)	717.96	717.7	717.9	718.0			
Bankfull Cross Sectional Area (ft ²) ²	23.2	14.7	19.3	20.7			
Bankfull Entrenchment Ratio ¹	>4	>3.1	>3.7	>3.8			
Bankfull Bank Height Ratio ¹	1.0	0.8	0.9	0.9			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

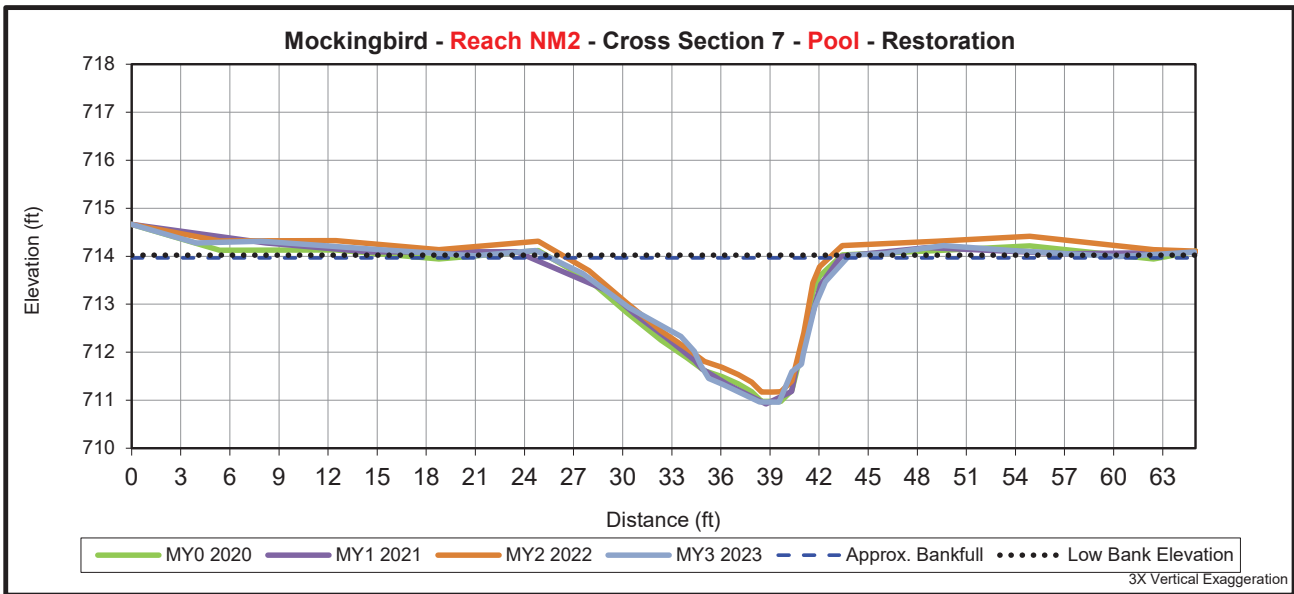

	Cross Section 7 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	713.94	713.9	714.1	714.0			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	3.0	3.1	3.1	3.1			
Low Bank Elevation (ft)	-	714.0	714.2	714.0			
Bankfull Cross Sectional Area (ft ²) ²	27.6	29.0	29.2	28.7			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

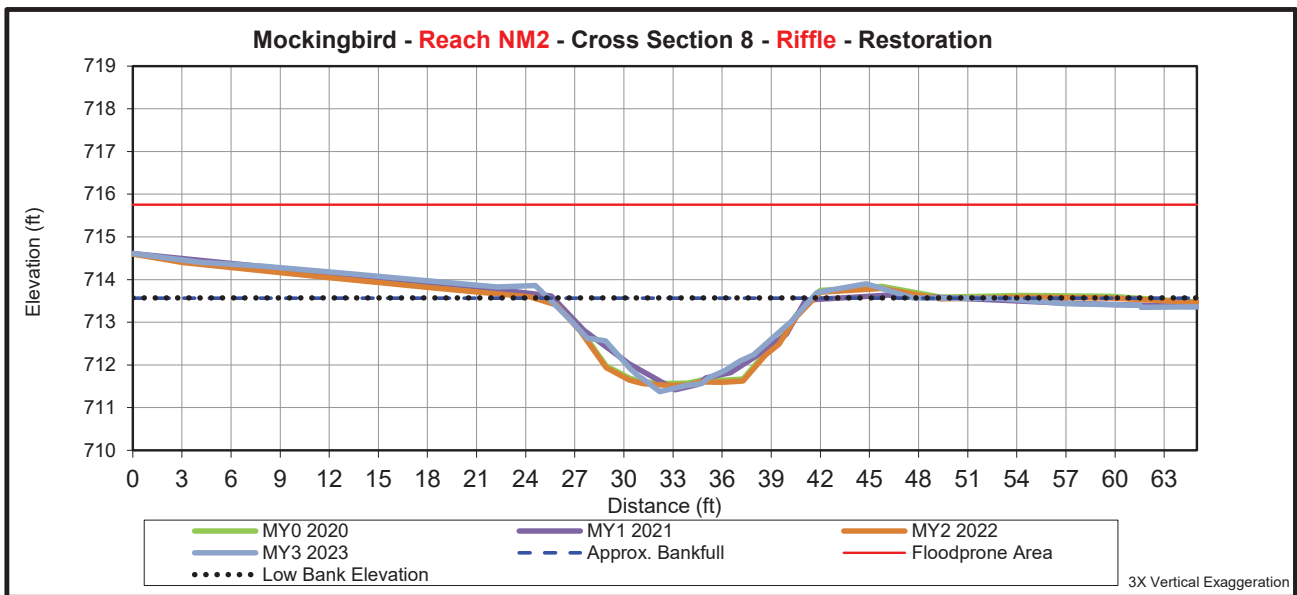

	Cross Section 8 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	713.45	713.6	713.4	713.6			
Bankfull Width (ft) ¹	15.4	17.5	15.3	16.1			
Floodprone Width (ft) ¹	>65	>65.1	>65.1	>65			
Bankfull Max Depth (ft) ²	1.9	2.1	2.1	2.2			
Low Bank Elevation (ft)	713.45	713.5	713.6	713.6			
Bankfull Cross Sectional Area (ft ²) ²	20.7	19.9	23.8	20.8			
Bankfull Entrenchment Ratio ¹	>4.2	>3.7	>4.2	>4.0			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.1	1.0			


1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

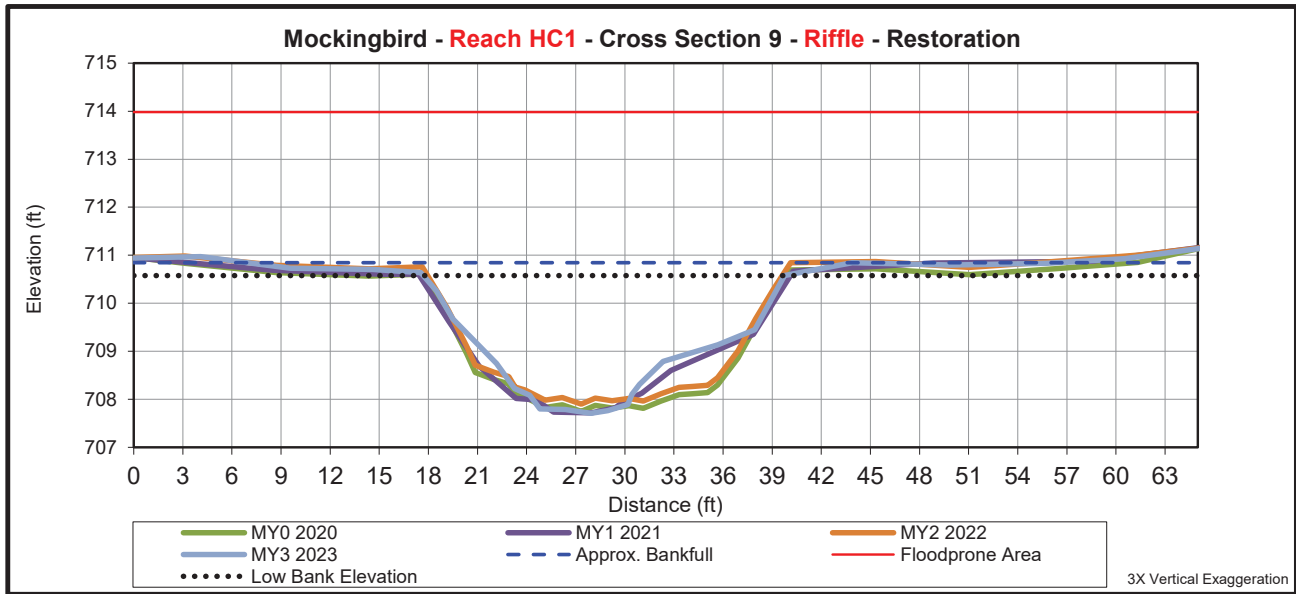

	Cross Section 9 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	710.56	710.7	710.7	710.8			
Bankfull Width (ft) ¹	22.2	24.4	22.2	22.2			
Floodprone Width (ft) ¹	>65	>65.4	>65.3	>65.5			
Bankfull Max Depth (ft) ²	2.8	2.9	2.9	2.9			
Low Bank Elevation (ft)	710.56	710.6	710.8	710.6			
Bankfull Cross Sectional Area (ft ²) ²	45.6	43.6	46.6	39.6			
Bankfull Entrenchment Ratio ¹	>2.9	>2.7	>2.9	>2.9			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	0.9			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

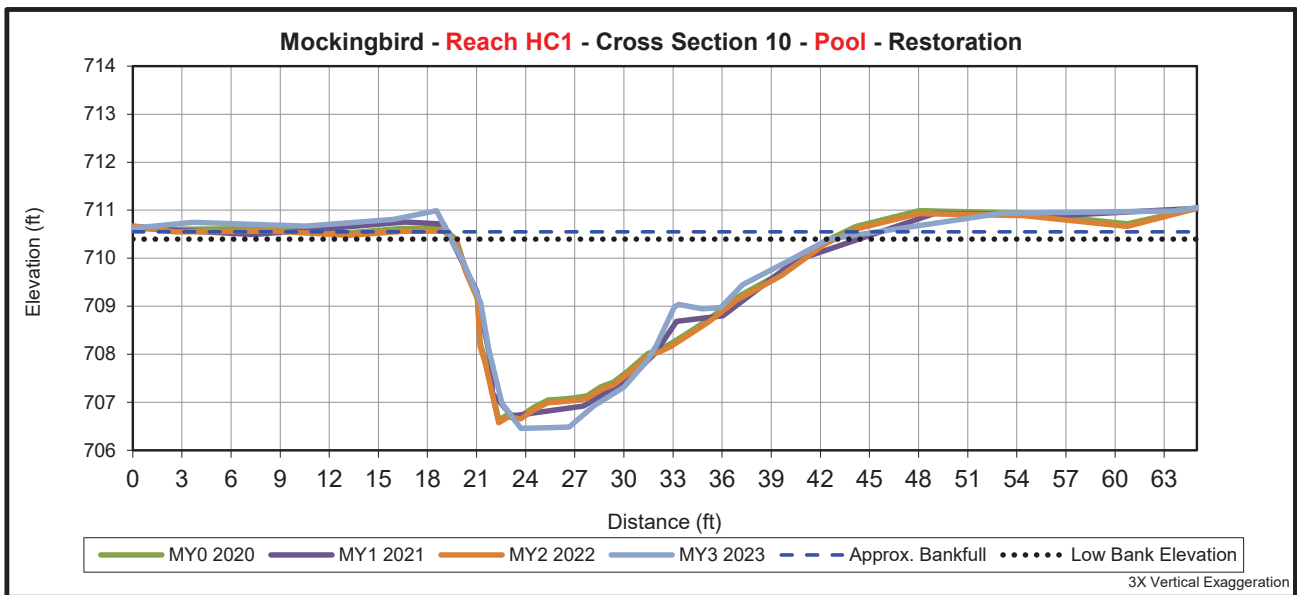

	Cross Section 10 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	710.53	710.5	710.5	710.6			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	3.9	4.0	2.1	3.9			
Low Bank Elevation (ft)	-	710.7	710.6	710.4			
Bankfull Cross Sectional Area (ft ²) ²	50.7	58.5	52.9	47.2			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			


1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

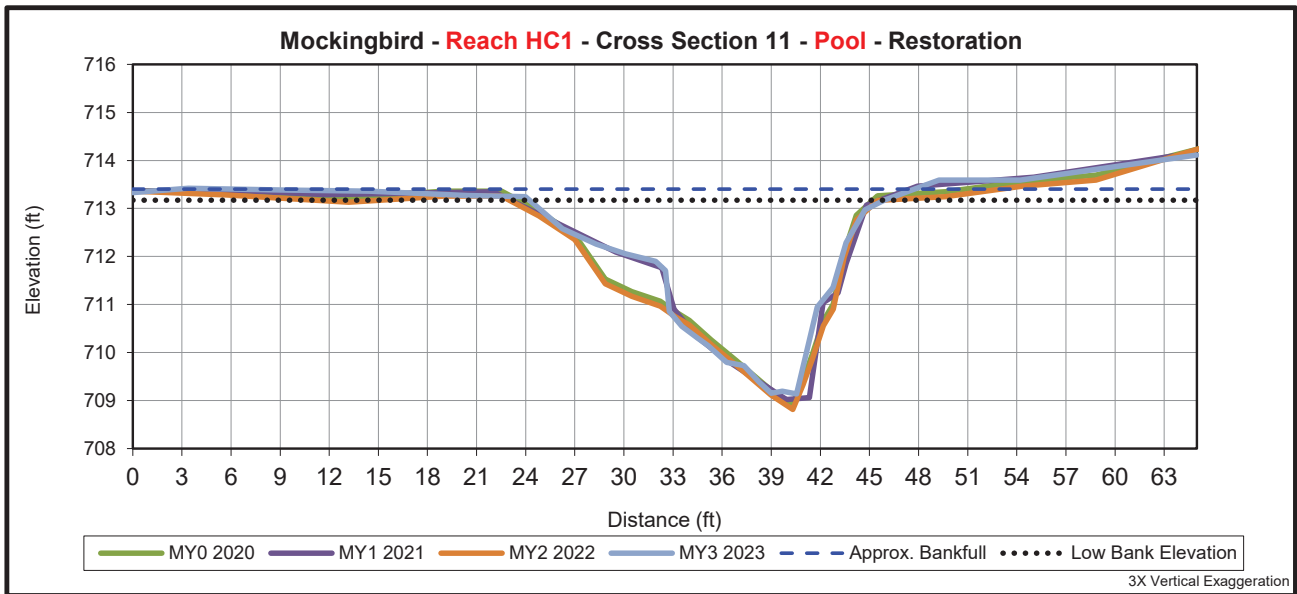

	Cross Section 11 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	713.23	713.3	713.1	713.4			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	4.3	4.0	4.4	4.0			
Low Bank Elevation (ft)	-	713.1	713.2	713.2			
Bankfull Cross Sectional Area (ft ²) ²	46.3	40.9	47.1	41.3			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			


1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

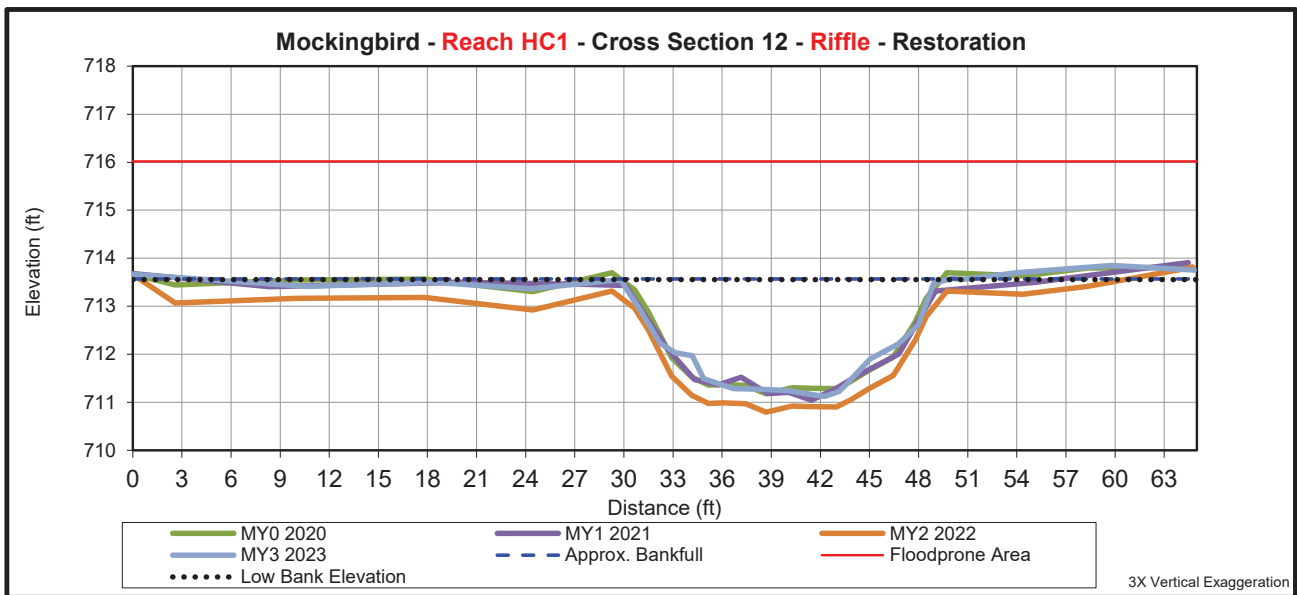

	Cross Section 12 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	713.56	713.5	713.2	713.6			
Bankfull Width (ft) ¹	19.6	25.0	19.6	20.2			
Floodprone Width (ft) ¹	>65	>64.5	>64.8	>64.8			
Bankfull Max Depth (ft) ²	2.4	2.3	2.5	2.4			
Low Bank Elevation (ft)	713.56	713.3	713.3	713.6			
Bankfull Cross Sectional Area (ft ²) ²	33.3	29.3	36.0	33.0			
Bankfull Entrenchment Ratio ¹	>3.3	>2.6	>3.3	>3.2			
Bankfull Bank Height Ratio ¹	1.0	0.9	1.1	1.0			


1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

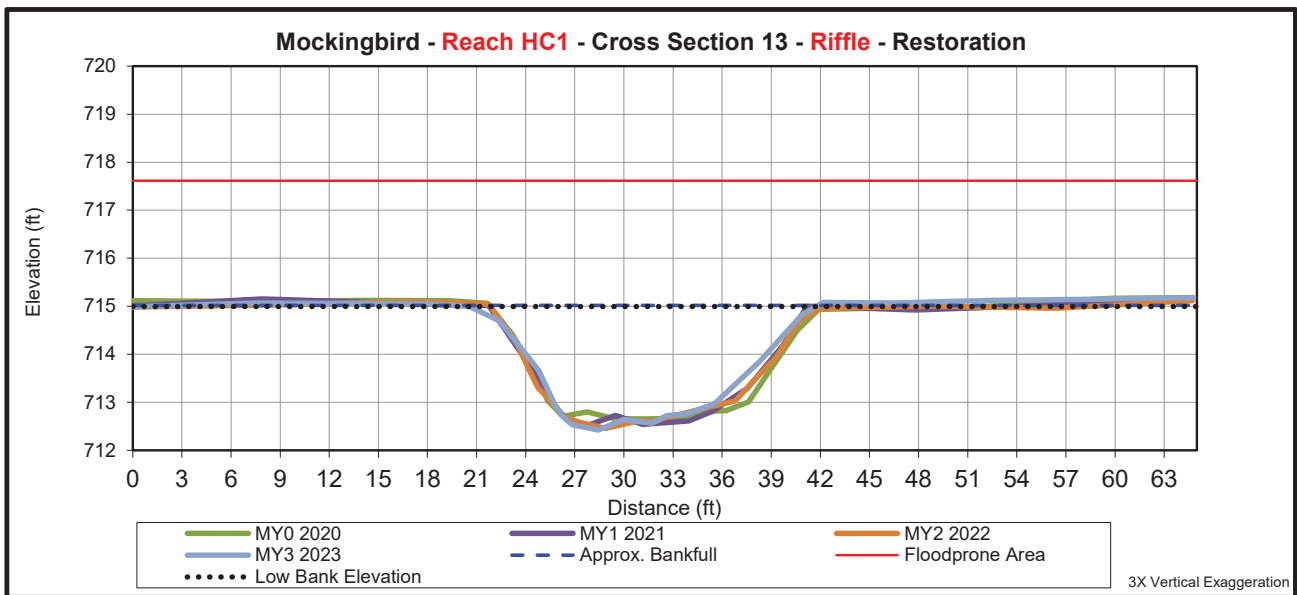

	Cross Section 13 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	714.94	714.9	714.9	715.0			
Bankfull Width (ft) ¹	20.0	19.2	20.0	21.3			
Floodprone Width (ft) ¹	>65	>64.8	>64.7	>64.8			
Bankfull Max Depth (ft) ²	2.3	2.5	2.5	2.6			
Low Bank Elevation (ft)	714.94	715.0	715.0	715.0			
Bankfull Cross Sectional Area (ft ²) ²	33.4	34.4	33.8	32.9			
Bankfull Entrenchment Ratio ¹	>3.3	>3.4	>3.2	>3.0			
Bankfull Bank Height Ratio ¹	1.0	1.0	1.0	1.0			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

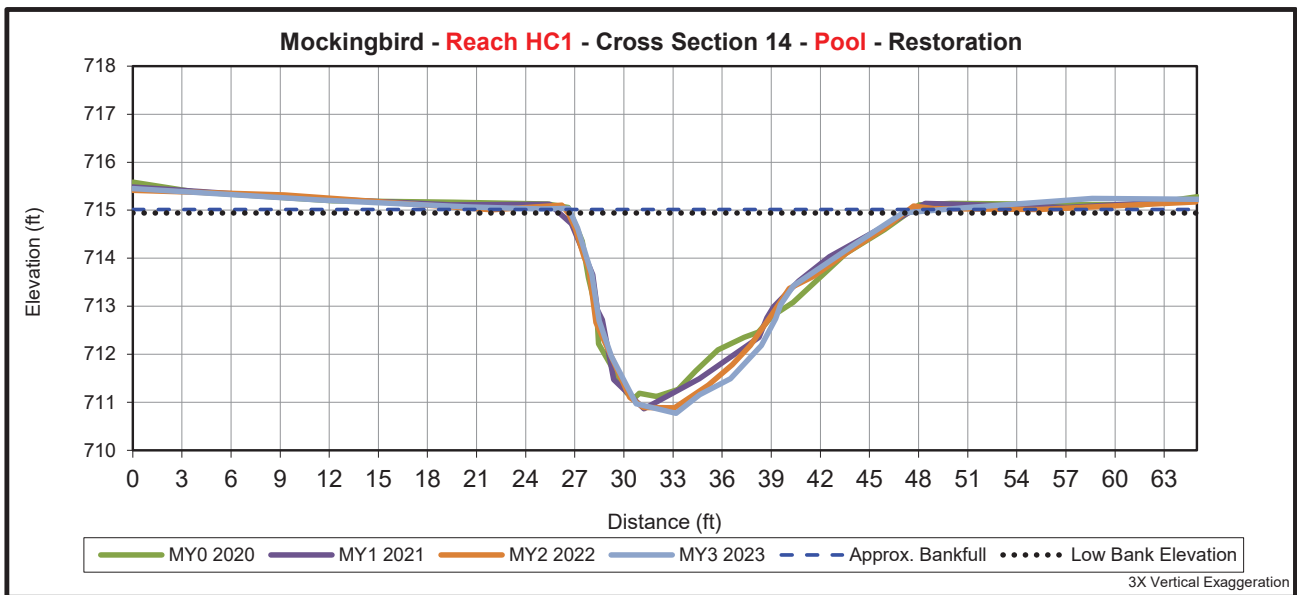

	Cross Section 14 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	715.11	715.1	715.0	715.0			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	4.0	4.3	4.2	4.2			
Low Bank Elevation (ft)	-	715.1	715.1	714.9			
Bankfull Cross Sectional Area (ft ²) ²	47.7	47.8	48.9	46.2			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

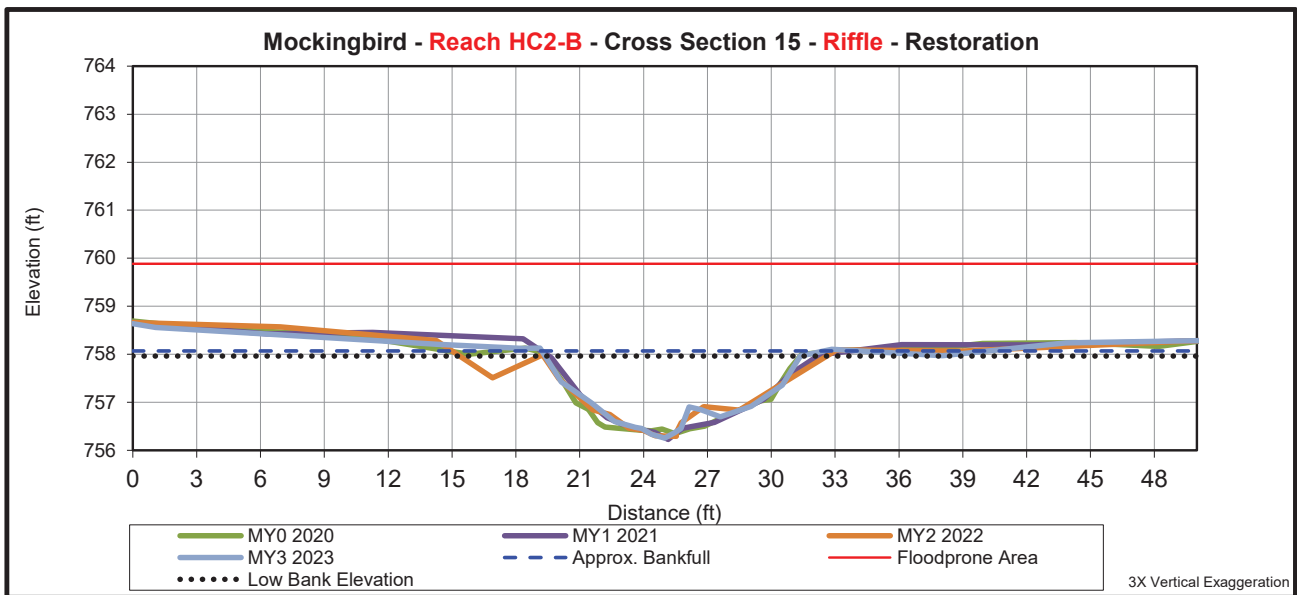

	Cross Section 15 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	757.99	758.0	758.0	758.1			
Bankfull Width (ft) ¹	12.0	13.5	17.2	12.1			
Floodprone Width (ft) ¹	>50	>50.4	>50.1	>50.4			
Bankfull Max Depth (ft) ²	1.6	1.7	1.8	1.7			
Low Bank Elevation (ft)	757.99	757.9	758.1	758.0			
Bankfull Cross Sectional Area (ft ²) ²	14.0	12.7	16.0	12.7			
Bankfull Entrenchment Ratio ¹	>4.2	>3.7	>2.9	>4.1			
Bankfull Bank Height Ratio ¹	1.0	0.9	1.1	0.9			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

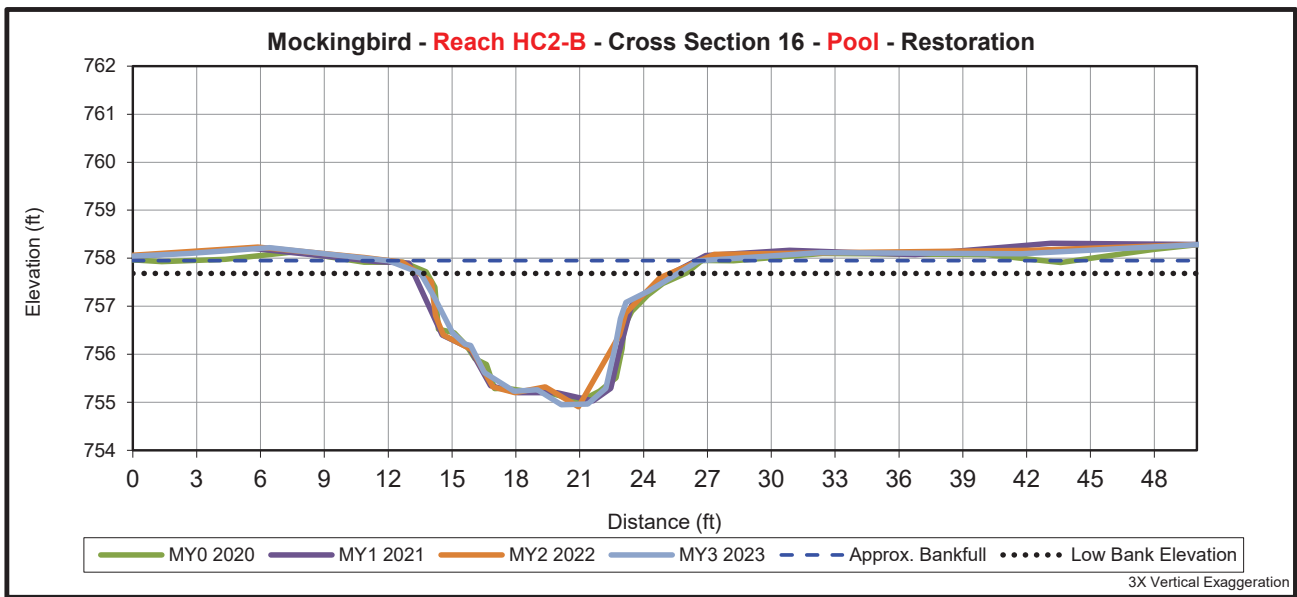

	Cross Section 16 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	757.91	757.9	758.0	758.0			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	2.9	2.9	3.0	2.7			
Low Bank Elevation (ft)	-	757.9	757.9	757.7			
Bankfull Cross Sectional Area (ft ²) ²	23.2	23.5	22.4	19.7			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

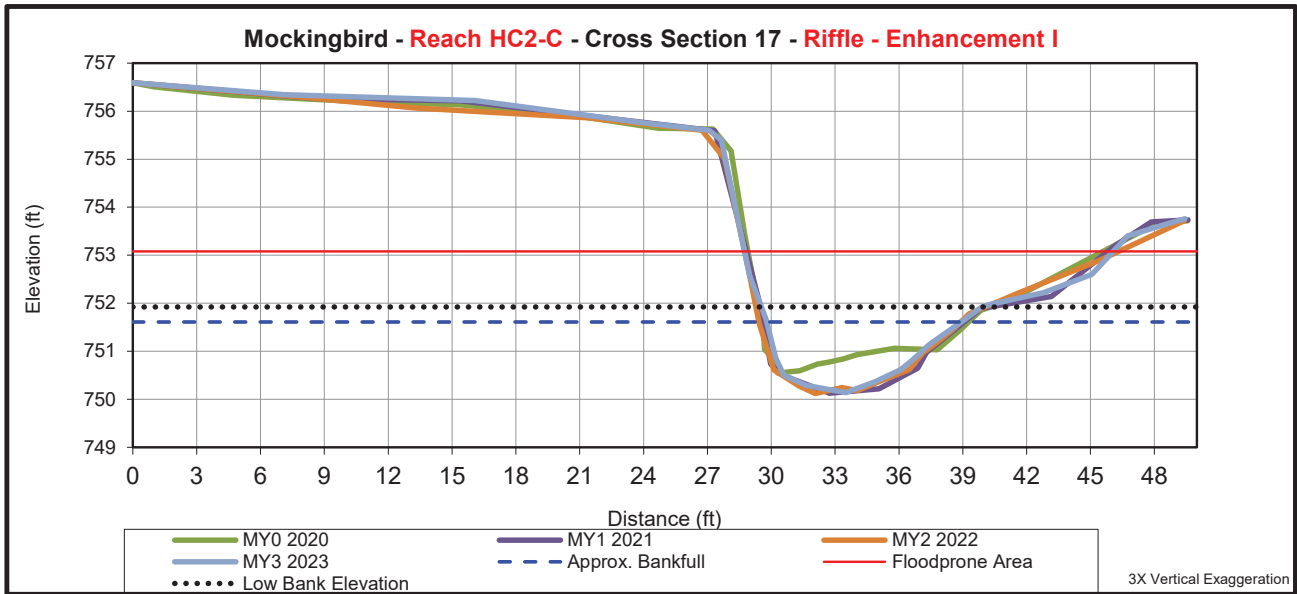

	Cross Section 17 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	751.86	751.5	751.5	751.6			
Bankfull Width (ft) ¹	10.3	9.1	9.2	9.1			
Floodprone Width (ft) ¹	17.1	16.3	16.8	17.3			
Bankfull Max Depth (ft) ²	1.3	1.8	1.7	1.8			
Low Bank Elevation (ft)	751.86	751.9	751.8	751.9			
Bankfull Cross Sectional Area (ft ²) ²	8.9	12.8	11.3	12.0			
Bankfull Entrenchment Ratio ¹	1.7	1.8	1.8	1.9			
Bankfull Bank Height Ratio ¹	1.0	1.3	1.2	1.2			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

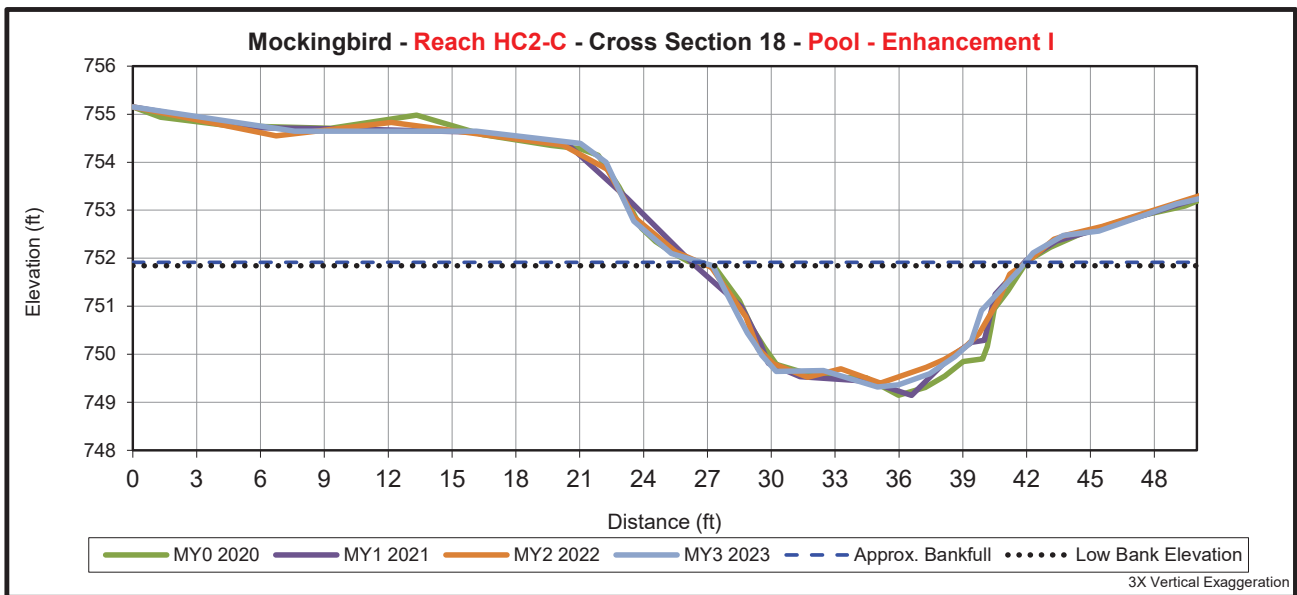

	Cross Section 18 (Pool)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	751.83	751.9	752.0	751.9			
Bankfull Width (ft) ¹	-	-	-	-			
Floodprone Width (ft) ¹	-	-	-	-			
Bankfull Max Depth (ft) ²	2.7	2.8	1.9	2.5			
Low Bank Elevation (ft)	751.83	752.0	752.4	751.8			
Bankfull Cross Sectional Area (ft ²) ²	26.8	28.3	34.3	25.7			
Bankfull Entrenchment Ratio ¹	-	-	-	-			
Bankfull Bank Height Ratio ¹	-	-	-	-			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

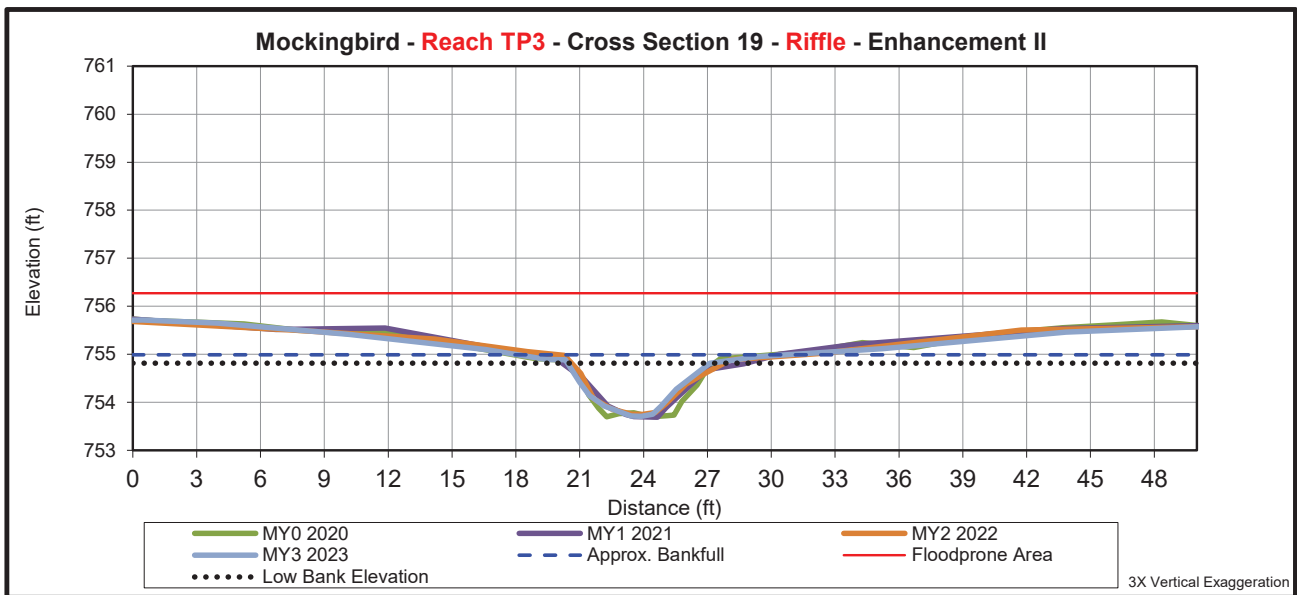

	Cross Section 19 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	754.87	754.9	755.0	755.0			
Bankfull Width (ft) ¹	7.1	9.7	10.2	6.8			
Floodprone Width (ft) ¹	>50.5	>50.5	>50.4	>50.3			
Bankfull Max Depth (ft) ²	1.2	1.1	1.1	1.1			
Low Bank Elevation (ft)	754.87	754.8	754.9	754.8			
Bankfull Cross Sectional Area (ft ²) ²	5.8	4.8	5.2	4.6			
Bankfull Entrenchment Ratio ¹	>7.1	>5.2	>4.9	>7.4			
Bankfull Bank Height Ratio ¹	1.0	0.9	0.9	0.9			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

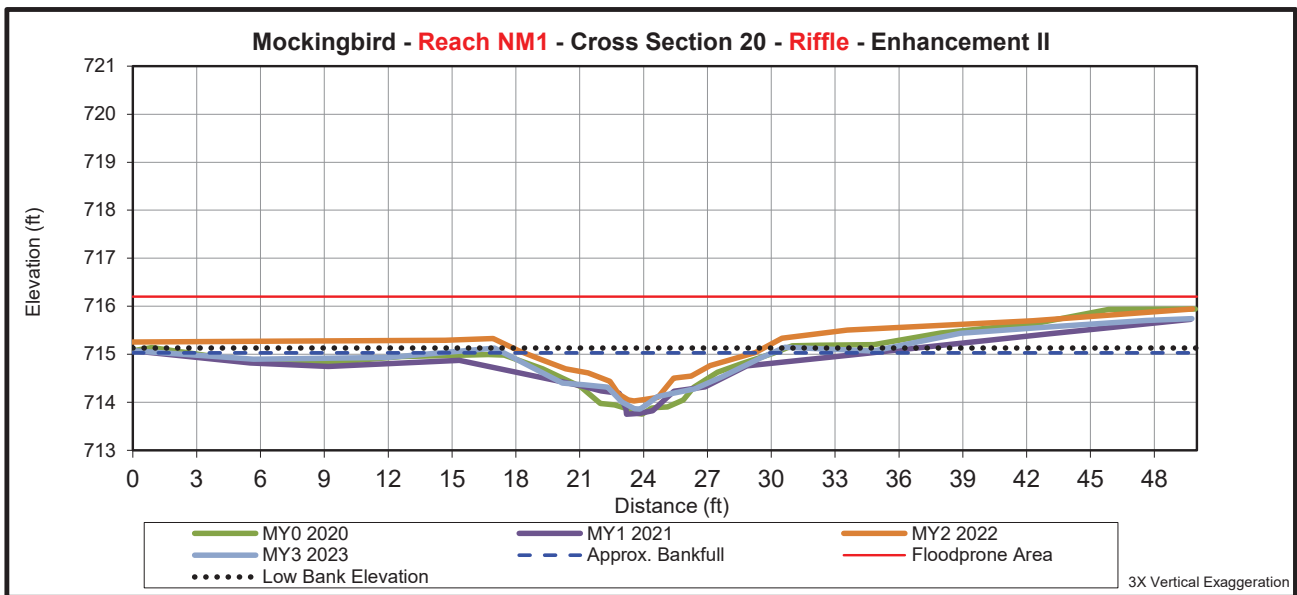

	Cross Section 20 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	714.99	714.9	715.2	715.0			
Bankfull Width (ft) ¹	12.4	16.9	12.6	12.6			
Floodprone Width (ft) ¹	>49.9	>49.7	>49.8	>49.8			
Bankfull Max Depth (ft) ²	1.2	1.0	1.3	1.3			
Low Bank Elevation (ft)	714.99	714.8	715.3	715.1			
Bankfull Cross Sectional Area (ft ²) ²	7.5	5.1	8.5	8.8			
Bankfull Entrenchment Ratio ¹	>4.0	>2.9	>3.9	>4.0			
Bankfull Bank Height Ratio ¹	1.0	0.9	1.1	1.1			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation


2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation



Upstream



Downstream

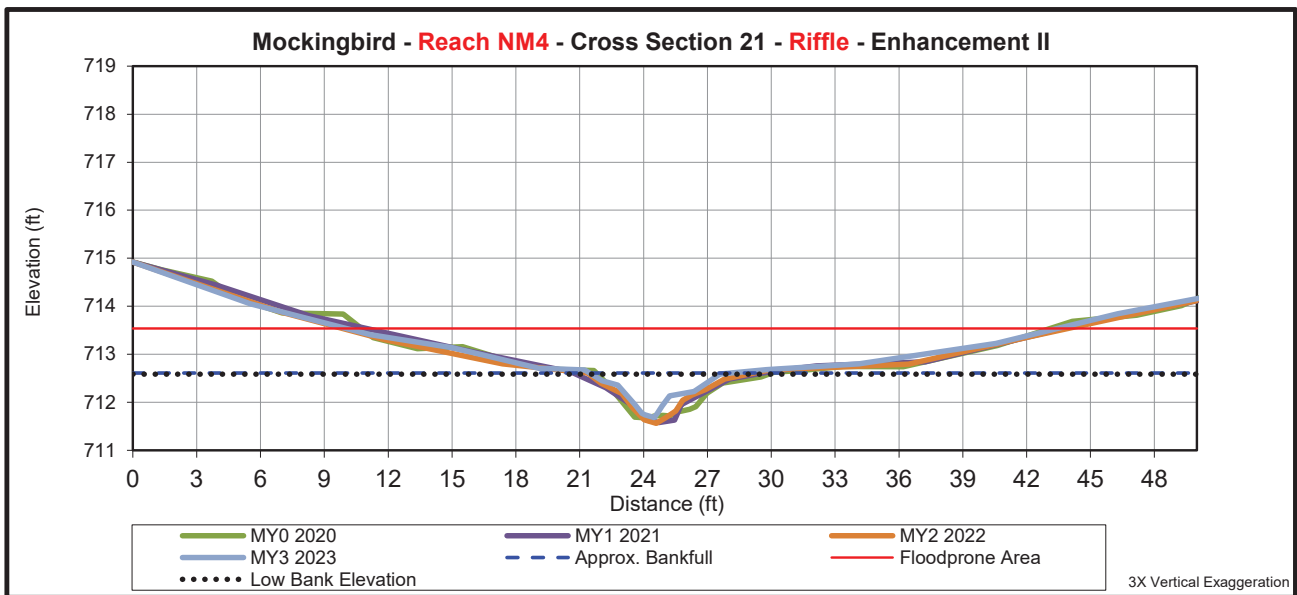

	Cross Section 21 (Riffle)						
	MY0	MY1	MY2	MY3	MY5	MY7	MY+
Bankfull Elevation (ft) - Based on AB-XSA¹	712.40	712.4	712.5	712.6			
Bankfull Width (ft) ¹	5.5	6.1	6.0	6.1			
Floodprone Width (ft) ¹	24.7	6.1	31.0	33.4			
Bankfull Max Depth (ft) ²	0.7	1.1	0.9	0.9			
Low Bank Elevation (ft)	712.40	712.6	712.5	712.6			
Bankfull Cross Sectional Area (ft ²) ²	2.6	4.2	2.7	2.4			
Bankfull Entrenchment Ratio ¹	4.5	4.5	5.2	5.4			
Bankfull Bank Height Ratio ¹	1.0	1.3	1.0	1.0			

1 - Uses the as-built cross sectional area as the basis for adjusting each subsequent years bankfull elevation
 2 - Uses the current years low top of bank as the basis for adjusting each subsequent years bankfull elevation

Appendix E

Hydrology Data

Table 12. Rainfall Summary 2023

Month	Average	Normal Limits		Project Location Precipitation*
		30 Percent	70 Percent	
November (2022)	3.18	1.71	3.89	4.37
December (2022)	3.72	2.55	4.44	4.41
January	3.64	2.62	4.30	4.55
February	3.32	2.35	3.93	3.42
March	3.83	2.64	4.56	2.60
April	3.96	2.52	4.77	5.63
May	3.89	2.55	4.68	2.89
June	4.27	3.13	5.01	6.78
July	4.90	3.51	5.79	3.80
August	4.44	3.09	5.28	3.57
September	4.32	2.73	5.21	1.51
October	3.27	1.96	3.94	1.04
Total Annual **	45.64	41.65	49.09	44.57
Above Normal Limits	Below Normal Limits			

WETS Station: Yadkinville, NC. Approximately 13 miles from the site.

*Project Location Precipitation is a location-weighted average of surrounding gauged data retrieved by the USACE Antecedent Precipitation Tool. Gauges used include Elkin, King, Yadkinville 6 E.

**Total Annual represents the average total precipitation, annually, as calculated by the 30-year period.

Table 13. Documentation of Geomorphically Significant Flow Events

Year	Number of Bankfull Events	Maximum Bankfull Height (ft)	Date of Maximum Bankfull Event	
Stage Recorder HC1				
MY0/1 2020	10	3.447	11/11/2020	
MY1 2021	4	1.257	5/3/2021	
MY2 2022	6	0.612	2/23/2022	
MY3 2023	5	1.33	4/8/2023	
Stage Recorder NM2				
MY0/1 2020	4	1.04	11/11/2020	
MY1 2021	1	0.13	8/18/2021	
MY2 2022	1	N/A	12/22/2022	
MY3 2023	1	0.28	6/26/2023	
Year	Number of Flow Events	Maximum Consecutive Flow Days	Maximum Cumulative Flow Days	Maximum Consecutive Flow Date Range
Flow Gauge NM1				
MY0/1 2020	2	51	54	11/11/2020 - 12/31/2021
MY1 2021	5	97	132	7/1/2021 - 10/6/2021
MY2 2022	10	34	148	7/7/2022 - 8/10/2022
MY3 2023	9	55	77	04/02/2023 - 06/01/2023
Flow Gauge NM4				
MY0/1 2020	2	165	169	6/19/2020 - 12/1/2020
MY1 2021	2	156	159	5/3/2021 - 10/6/2021
MY2 2022	2	171	276	1/1/2022 - 6/21/2022
MY3 2023	1	282	282	1/1/2023 - 10/10/2023
Flow Gauge TP2				
MY0/1 2020	2	168	246	7/16/2020 - 12/31/2020
MY1 2021	5	210	260	1/1/2021 - 7/29/2021
MY2 2022	6	138	183	1/1/2022 - 5/18/2022
MY3 2023	1	232	232	1/1/2023 - 8/21/2023
Flow Gauge TP3				
MY0/1 2020	1	247	247	4/28/2020 - 12/31/2020
MY1 2021	1	279	279	1/1/2021 - 10/6/2021
MY2 2022	11	68	215	2/2/2022 - 4/11/2022
MY3 2023	1	282	282	1/1/2023 - 10/10/2023


Table 14.

2023 Max Hydroperiod (Growing Season 18-Mar through 15-Nov, 242 days)					
Well ID	Consecutive		Cumulative		Occurrences
	Days	Hydroperiod (%)	Days	Hydroperiod (%)	
GW1	54	22	111	46	15

Table 15.

Summary of Groundwater Monitoring Results									
Mockingbird									
Well ID	Wetland ID	Ground Elevation (ft)	Hydroperiod (%)						
			Year 1 (2021)	Year 2 (2022)	Year 3 (2023)	Year 4 (2024)	Year 5 (2025)	Year 6 (2026)	Year 7 (2027)
GW1	WA	765.00	8	22	22				


2023 Mockingbird GW1

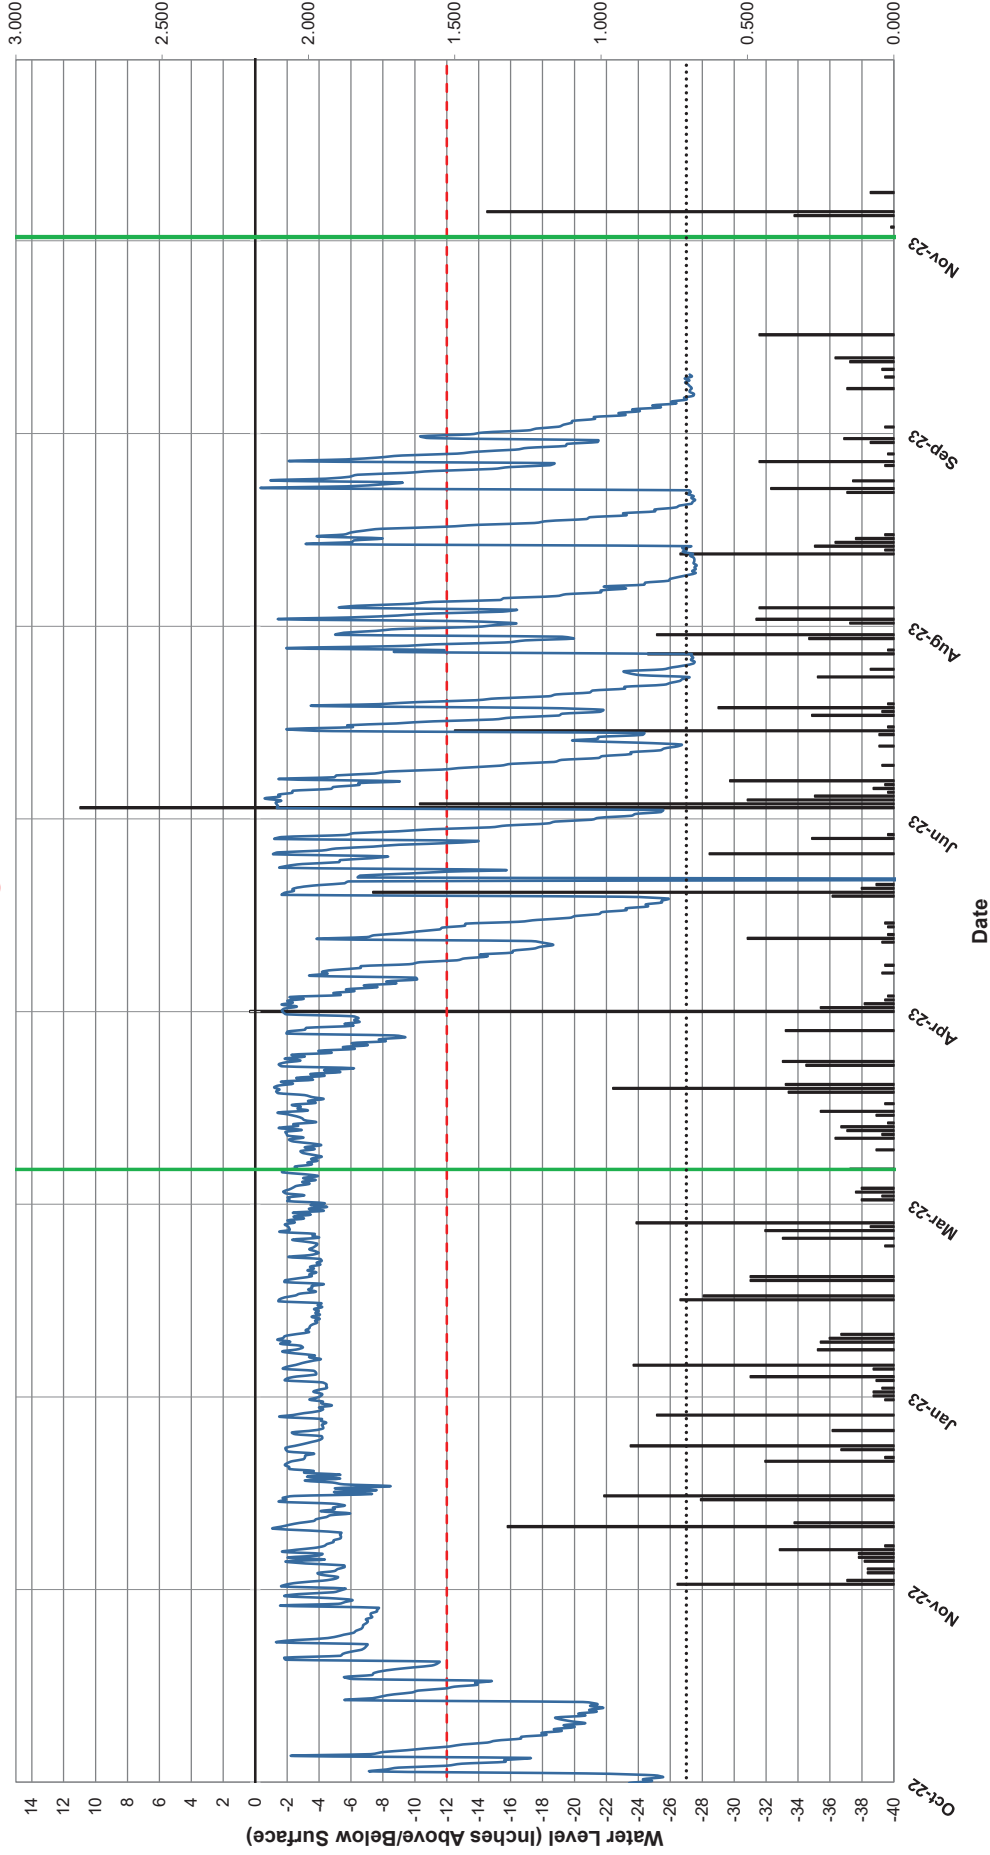


33 Consecutive Days of Hydrology
03/18/2023 - 06/01/2023




2023 Mockingbird HC1 Stage Recorder Graph

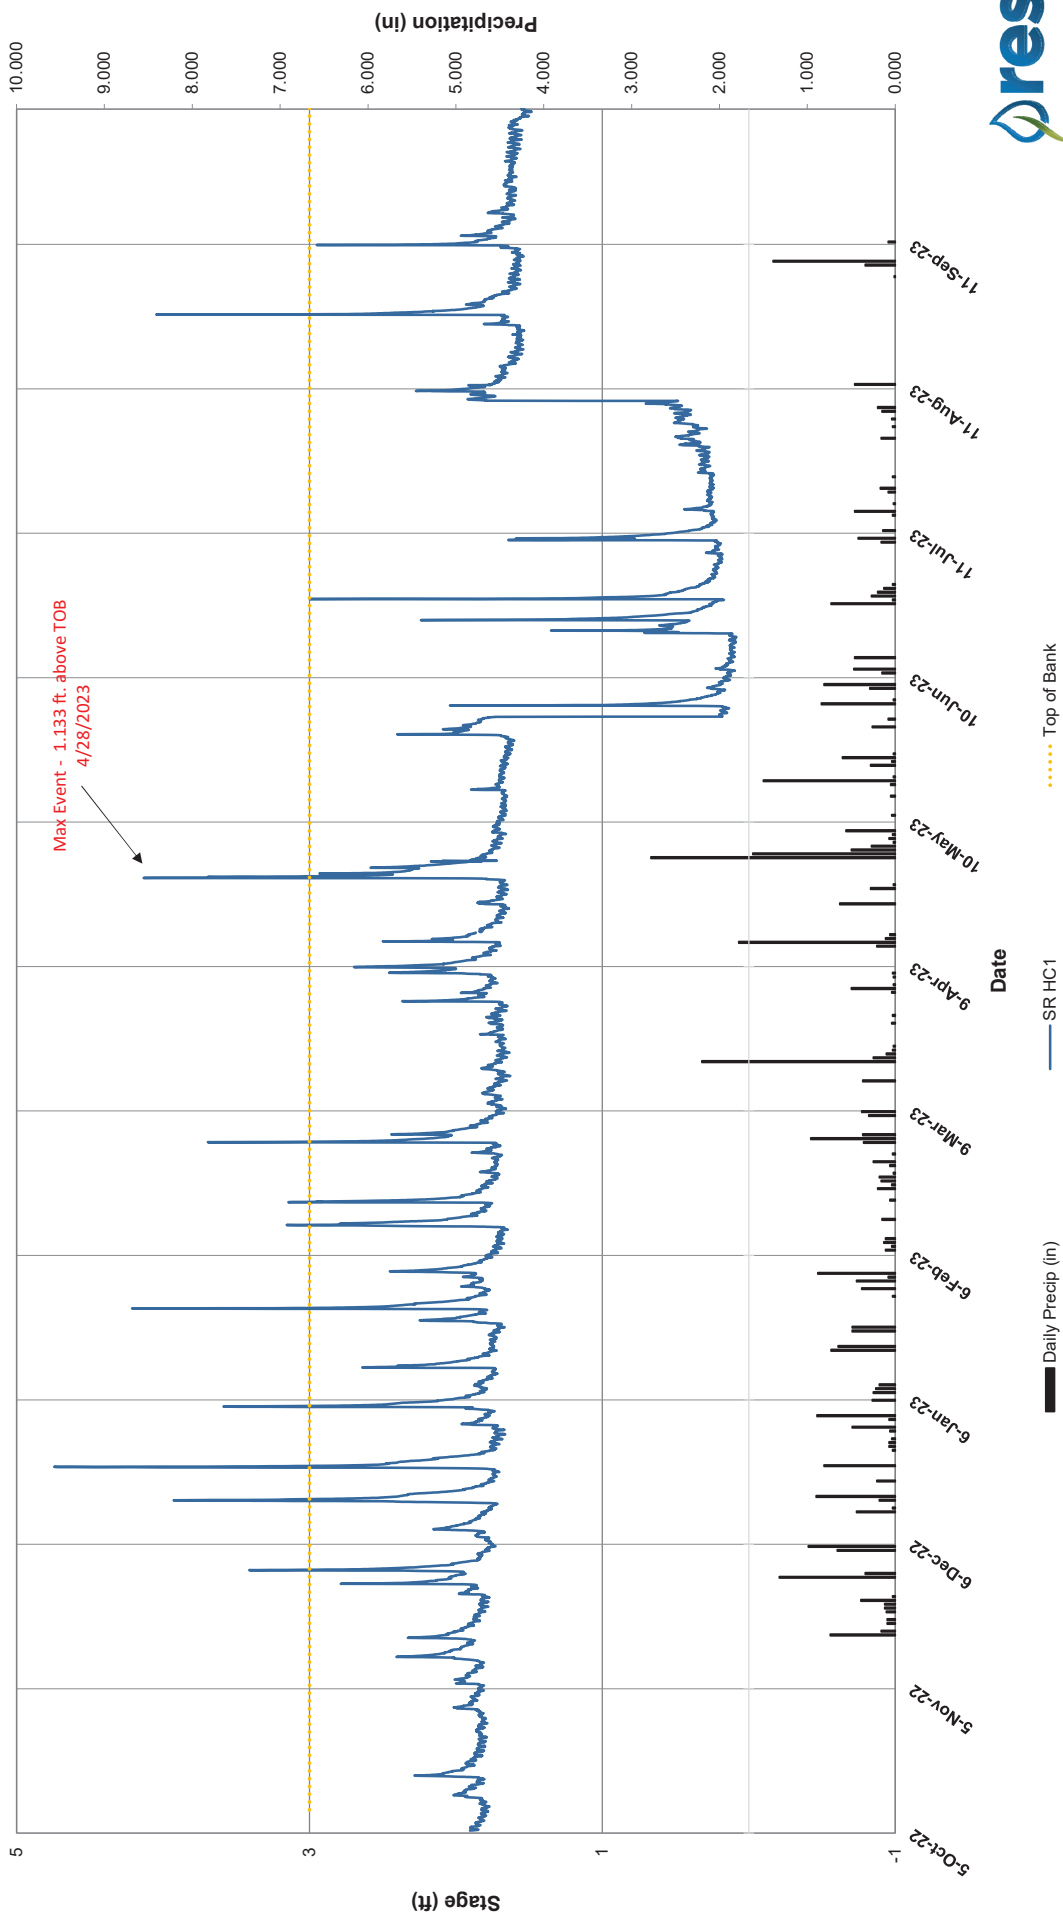

2023 Mockingbird NM2 Stage Recorder Graph

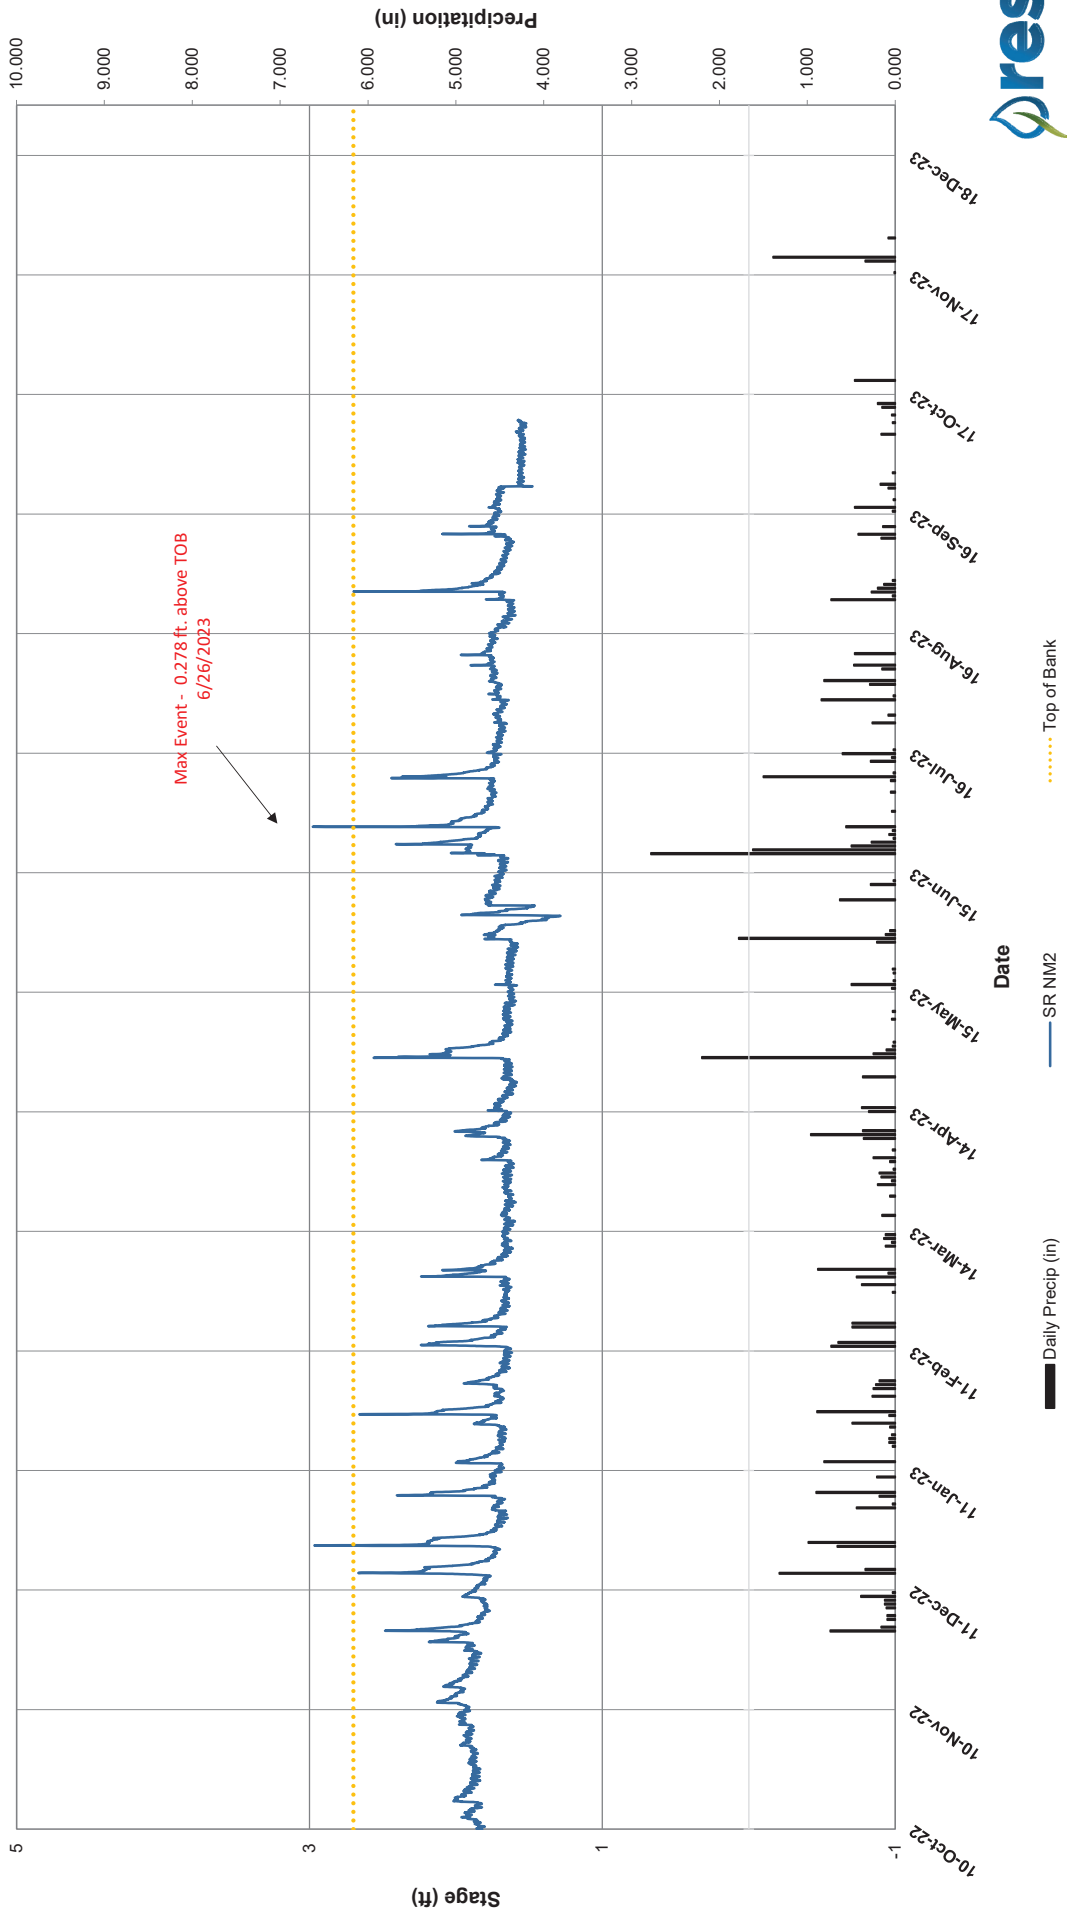


2023 Mockingbird NM1 Flow Gauge Graph

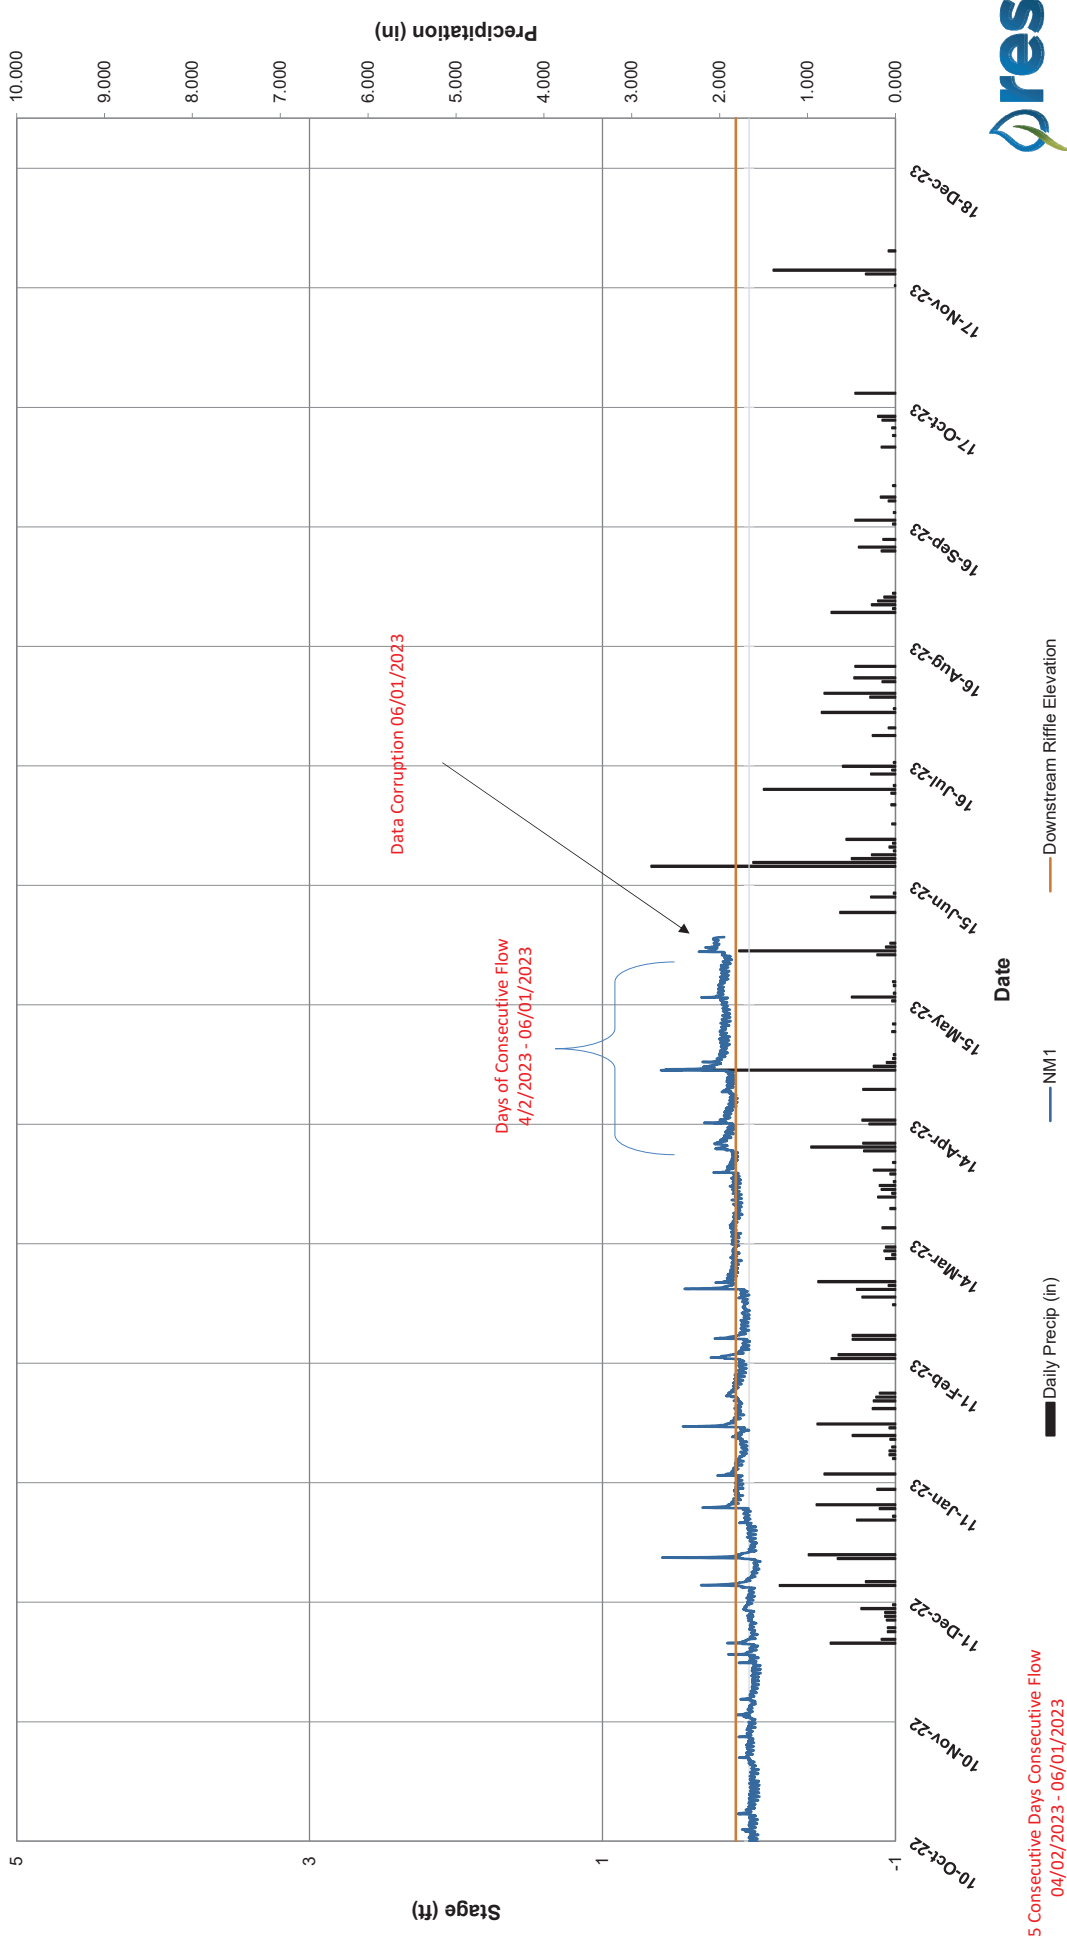

55 Consecutive Days Consecutive Flow
04/02/2023 - 06/01/2023

2023 Mockingbird NM4 Flow Gauge Graph

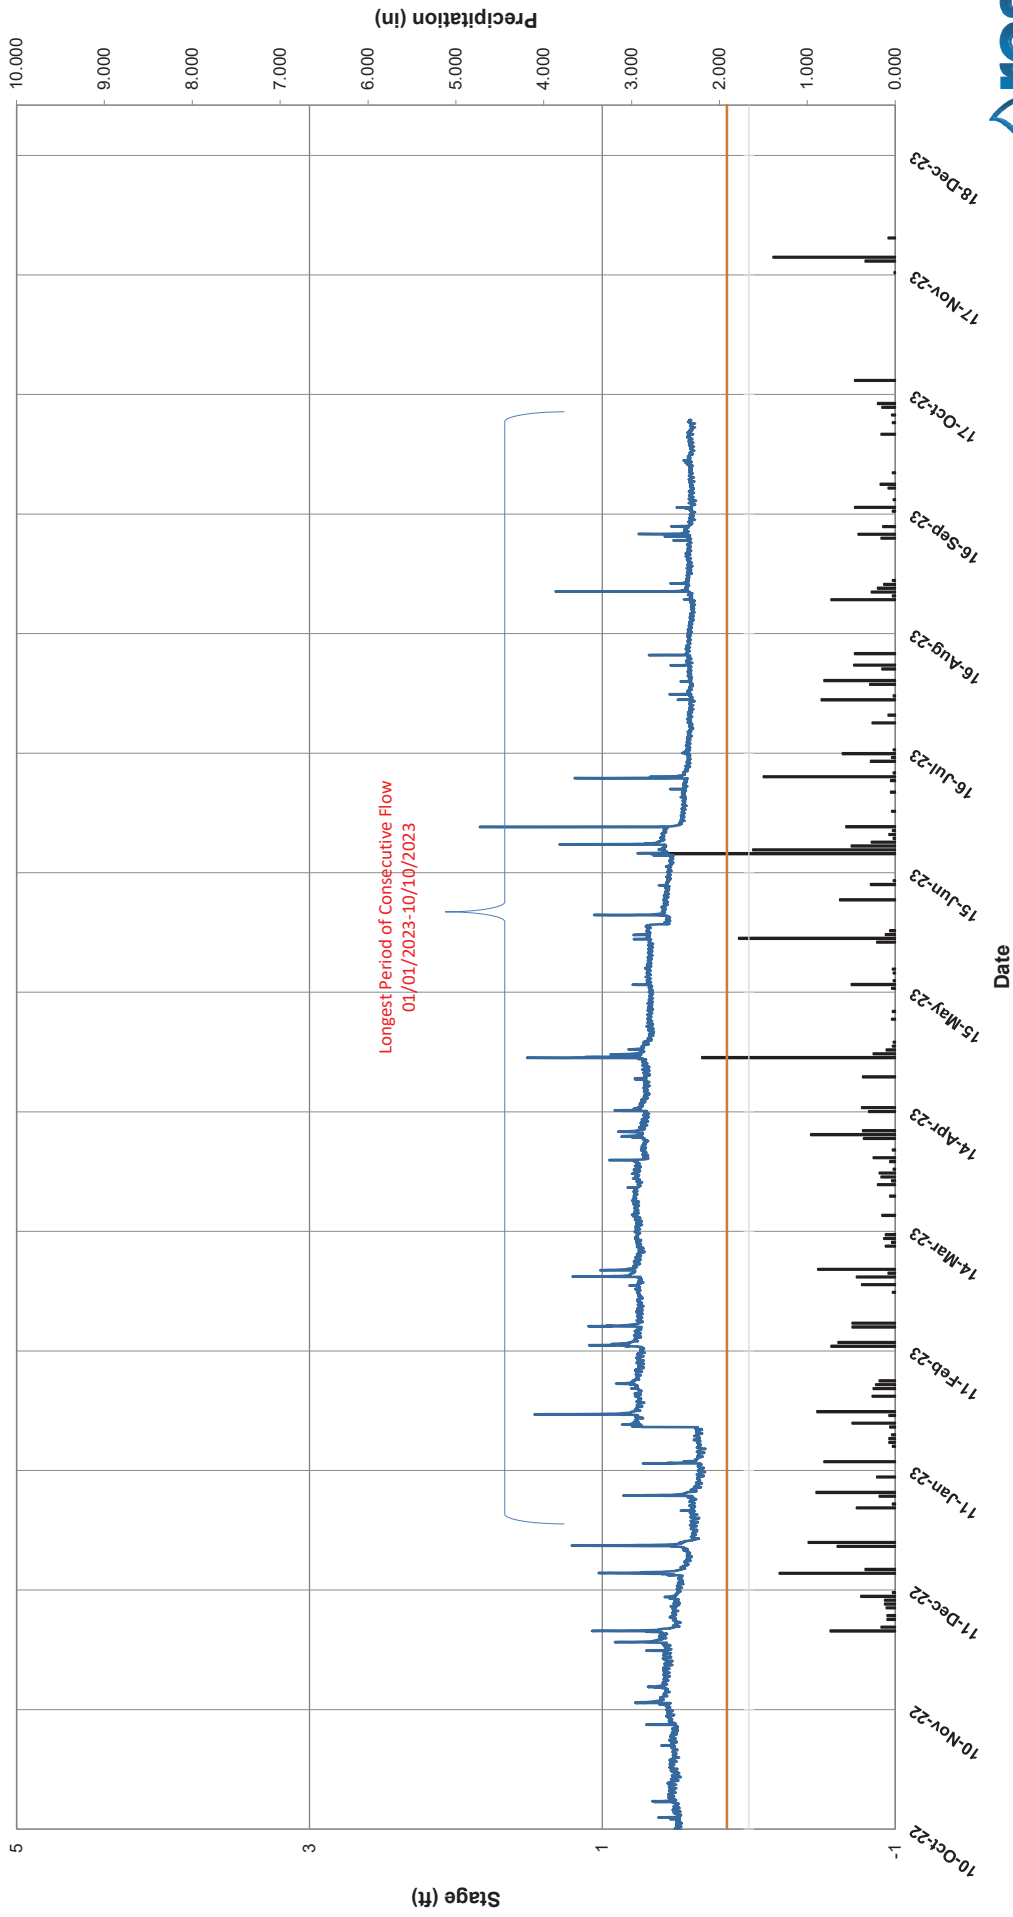


282 Consecutive Days of Hydrology
01/01/2023 - 10/10/2023

Downstream Rifle Elevation

NM4


Daily Precip (in)

2023 Mockingbird TP2 Flow Gauge Graph

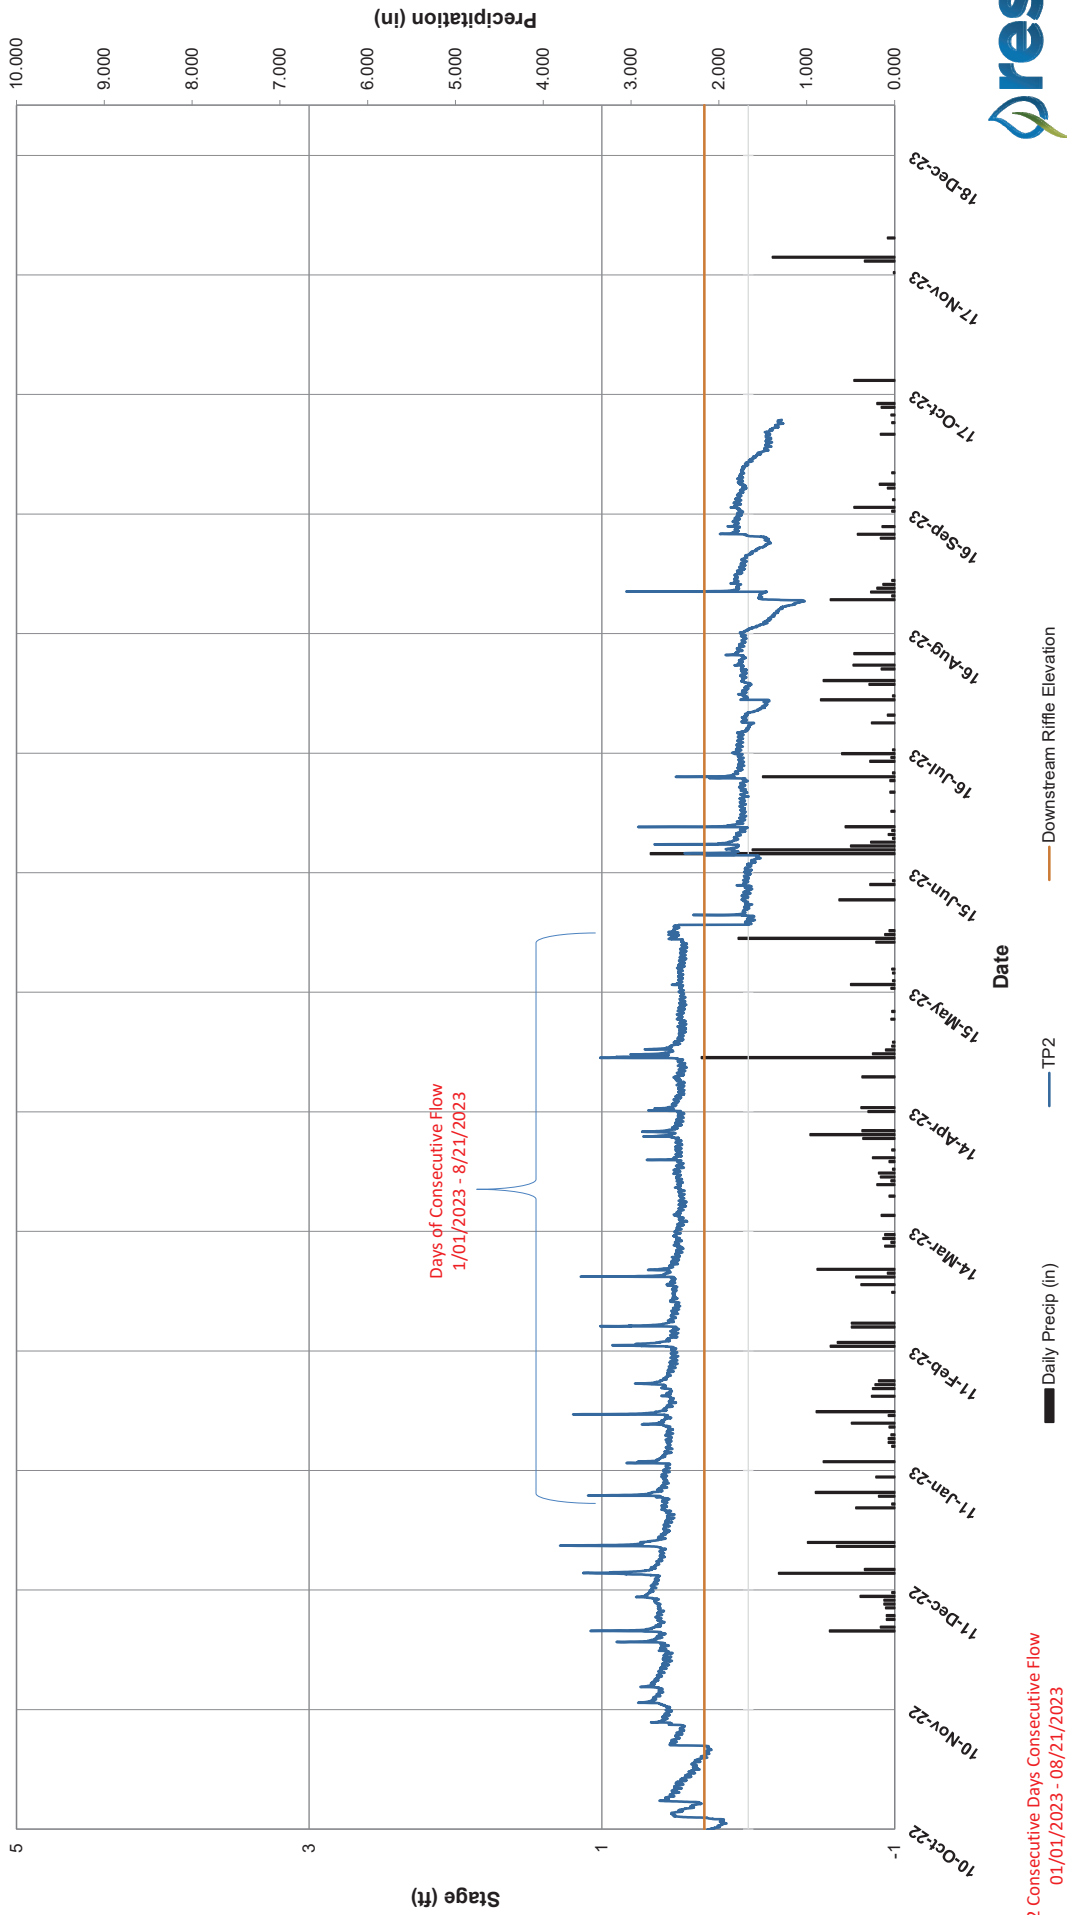

232 Consecutive Days Consecutive Flow
01/01/2023 - 08/21/2023

2023 Mockingbird TP3 Flow Gauge Graph

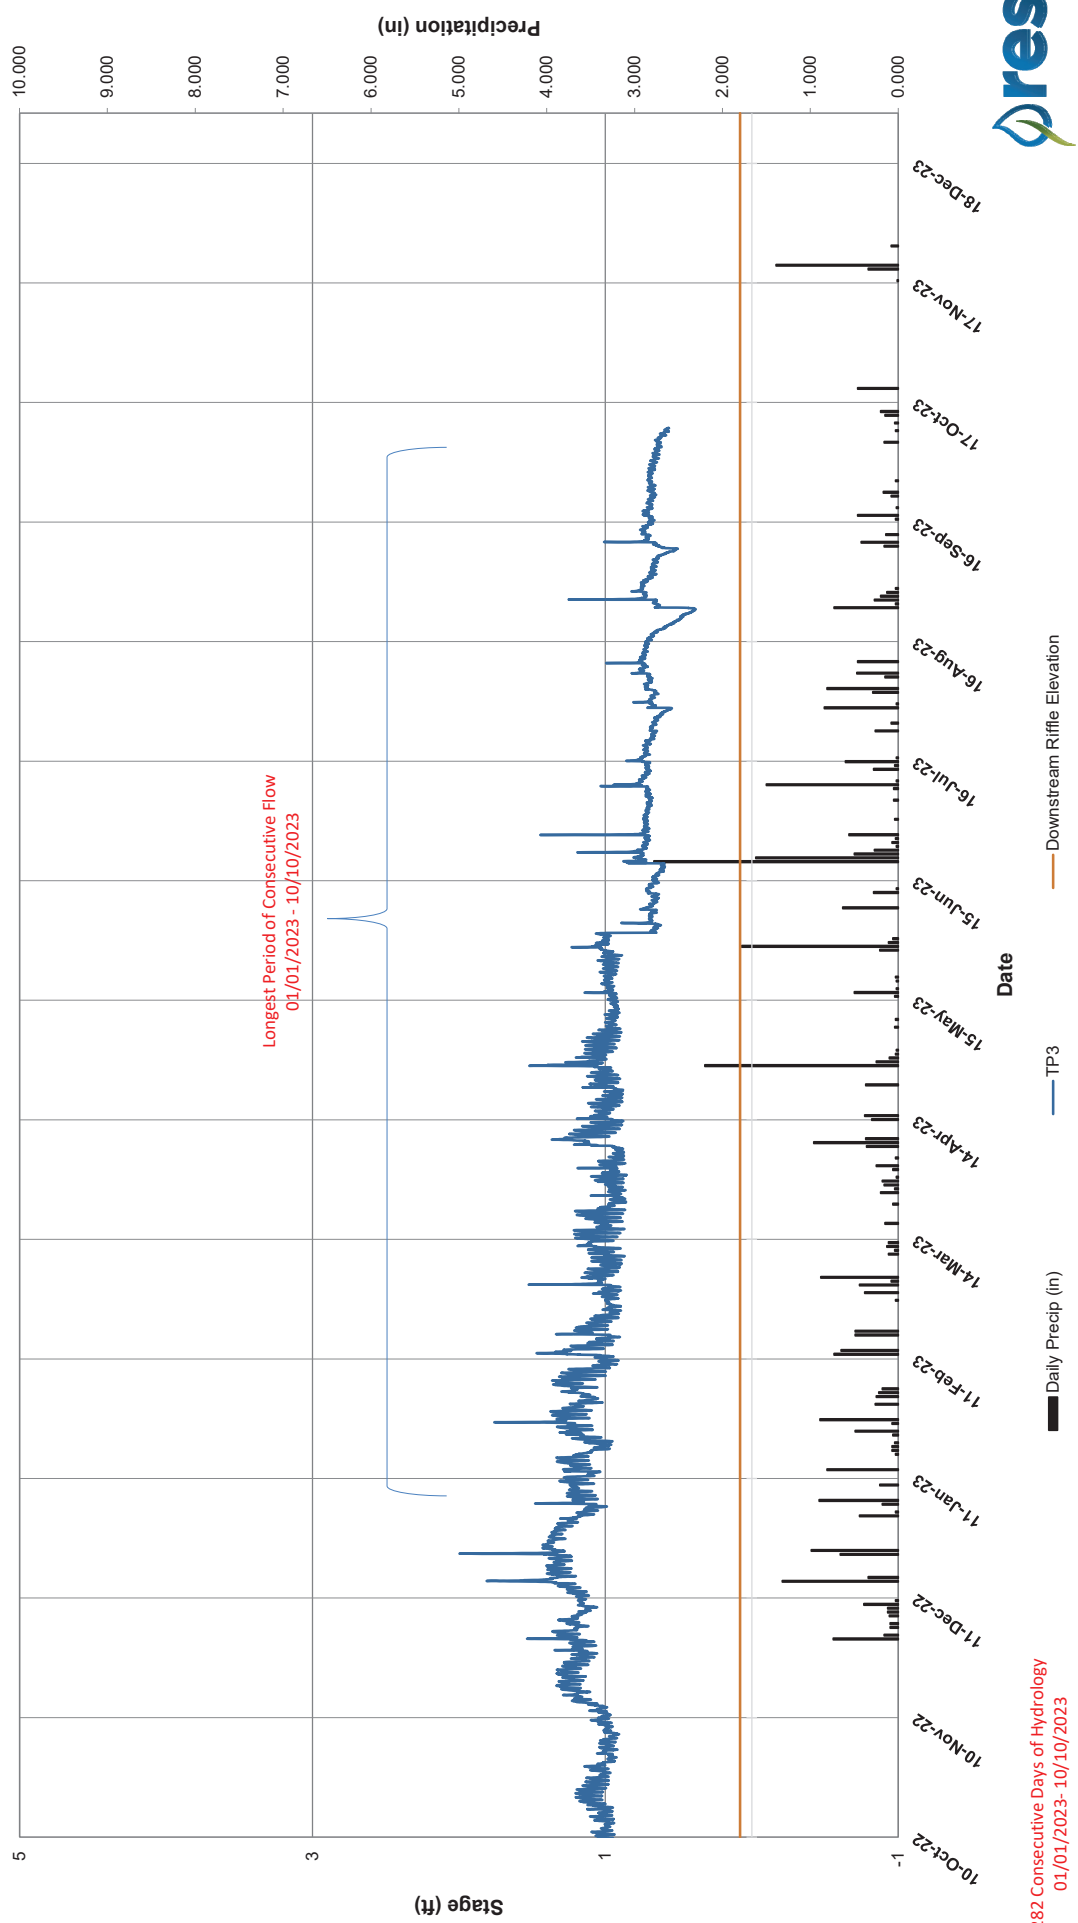

282 Consecutive Days of Hydrology
01/01/2023- 10/10/2023
