

Shadrick Creek Restoration Project

Annual Monitoring Report

Monitoring Year 1 of 5

FINAL

Shadrick Creek Stream Restoration Project

NCDMS Contract No. 7343

NCDMS Project No. 92916

DWR# 10-04065

USACE Action ID: 2010-00764

McDowell County, North Carolina

Data Collected: June 5th, 2018 – November 8th, 2018

Date Submitted: November 12th, 2018



Submitted to:

NCDEQ-Division of Mitigation Services
1652 Mail Service Center Raleigh N C 27699-1652

Page Intentionally Left Blank

November 28, 2018

Matthew Reid
Project Manager
DENR Division of Mitigation Services
5 Ravenscroft Dr., #102
Asheville, NC 28801

Subject: Revisions to Shadrick Creek Monitoring Year 1 Report; NCDMS Project #92916

Dear Mr. Reid,

The North Carolina Division of Mitigation Services contracted the services of Equinox to compile and report on the MY1 conditions of the Shadrick Creek Restoration Project. Comments provided by NCDMS on November 28, 2018 are listed below with red text indicating how each was addressed:

Cross Section and Table 11a:

- Please confirm that the MY1 (2018) BHRs have been calculated based on the attached DMS technical guidance. Please add a note on the table that beginning in MY3, the bankfull elevation and channel cross section dimensions are calculated using a fixed Abkf as described in the Standard Measurement of the BHR Monitoring Parameter provided by NCIRT and NCDMS (9/2018). **BHRs have been calculated according to the guidance starting in MY1. A note has been added to the bottom of Table 11a**
- Please review Cross Section 18. Both the graph and entry in Tabl1 11a are using different Abkf from the baseline measurement. **Cross section 18 graph and Table 11a have been updated to show the new calculations using the fixed Abkf from baseline conditions.**

General Comment:

- As Equinox has done in the past, please include a response to the comment letter and how/ where the comments were addressed. Please insert this letter directly behind the cover page in the final deliverables (printed and electronic). The IRT requested that we include this letter with final deliverables. The response letter will need to be included with all future monitoring deliverables. **This letter has been added behind the cover page of both the printed and electronic versions of this report.**



EQUINOX

balance through proper planning

The Equinox project manager for this project is Mr. Drew Alderman. His contact is as follows:

Natural Resource Specialist
Equinox
37 Haywood Street
Asheville, NC 28801
Office: 828-253-6856 ext. 213
Fax: 828-253-8256

Sincerely,

Drew Alderman

Prepared by:



EQUINOX

balance through proper planning

37 Haywood Street, Suite 100
Asheville, NC 28801

Page Intentionally Left Blank

Table of Contents

1.0	Project Summary.....	1
1.1.	Project Setting and Background.....	1
1.2.	Project Goals and Objectives	1
1.3.	Project Success Criteria	2
1.4.	Mitigation Components.....	3
1.5.	Project Performance.....	3
2.0	Methods.....	5
3.0	References.....	6
	Appendix A Project Background Data and Maps	8
	Appendix B Visual Assessment Data.....	14
	Appendix C Vegetation Plot Data	67
	Appendix D Stream Measurement and Geomorphology Data	73
	Appendix E Hydrologic Data	121

Page Intentionally Left Blank

1.0 PROJECT SUMMARY

1.1. Project Setting and Background

The Shadrick Creek Restoration Project (Shadrick) is located in the Catawba River Basin (CU 03050101). The Shadrick Creek site is also located within the Muddy Creek (Upper Catawba) Local Watershed (LWP) area. The Shadrick Creek site watershed also includes the Hydrologic Code (HUC) 0305010103006, which is identified as a Targeted Local Watershed (TLW) in the Ecosystem Enhancement Program's (EEP) 2009 Upper Catawba River Basin Restoration Priority (RBRP) Plan. Project work at the Shadrick site was completed in April 2017, and included construction, planting, invasive treatment, and fence installation. Through the project work, a total of 1,353 linear feet were restored, 6,966 linear feet were enhanced through Enhancement I, 215 linear feet were enhanced through Enhancement II, 2,895 linear feet were preserved, and 0.54 acre of wetlands were enhanced. The site generated a total of 6,662 SMU's, 0.27 WMU, and 527,000 SF of Buffer. Refer to Table 1 for the project components and mitigation credit information and Figure 2 for the project asset map.

The Shadrick site has a history of unrestricted livestock access, leading to bank erosion, compaction, and discontinuity between the stream and its associated floodplain. Historic agricultural practices, including recent tree farming, and removal of the vegetative buffer have caused loss of plant diversity, stream incision, and failing banks. The completed project will reduce sediment inputs from the failing banks, reduce nutrients and bacteria entering the stream from livestock, and will enhance the forested corridor along the stream floodplain.

This project is protected by a 54.6 acre conservation easement and is located approximately 5.5 miles east of Nebo, NC in McDowell County at 35.720410° N, 81.901405° W. The Shadrick Creek site is bounded to the north by the Norfolk Southern Railroad and agricultural and forest land to the south, east, and west.

1.2. Project Goals and Objectives

The project goals address stressors identified in the TLW and priority subwatershed, as outline in the Final Mitigation Plan, and include:

- Improve water quality by repairing eroding stream banks, establishing riparian buffers and implementing agricultural best management practices;
- Improve the community structures of the buffers;
- Improve stream function and habitat by re-establishing stream-to-flood connections;
- Restore long-term stability through the restoration on channel dimensions, pattern, and profile;
- Improve in-stream habitat using in-stream structures; and
- Remove exotic invasive plant species.

The following objectives are proposed for accomplishing the above listed goals as outlined in the Final Mitigation Plan:

- Restoration and enhancement of approximately 5,276 LF of Shadrick Creek;
- Restoration and enhancement of 3,179 LF of UT's 1, 5, 9, and 10;
- Preservation of 3,835 LF of UT's 2, 5, 6, 7, and 8;
- Enhancement of 0.53 acre of wetland by improving hydrologic connections and vegetation communities;

- Installing over 8,000 LF of livestock fence, three wells and six watering tanks; and
- Establishment of riparian buffers by removing exotic invasive plants and installing a variety of native vegetation.

1.3. Project Success Criteria

The stream restoration success criteria for the project will follow accepted and approved criteria based on the Mitigation Plan for Shadrick Creek Stream Restoration (2010). The Shadrick Creek Mitigation Plan references the Stream Mitigation Guidelines issued in April 2003 by the USACE and NCDWQ.

Specific success criteria are presented below.

1.3.1. Streams

The stream geometry will be considered successful if the cross section geometry, profile, and sinuosity are stable or reach a dynamic equilibrium. It is expected that there will be changes in the designed cross sections, profile, and/or substrate composition. Any changes that occur during the monitoring period will be evaluated to determine whether they represent a trend toward a less stable condition (e.g., down cutting, erosion, etc.) or simply an increase in stability (e.g., settling, vegetative changes, coarsening of bed material, etc.) or move toward quasi-equilibrium.

An initial, though not exclusive, indicator of success will be the stream's adherence to design or reference ratios of stream geometry found in the morphological table in Appendix D or in a comparable, stable reference system. The channel may not adhere to design or reference ratios of stream geometry, but can be considered stable if the following key indicators are present:

- **Stream Type:** Maintenance of the design stream type or progression toward/conversion to a stable stream type such as C or E will indicate stability.
- **Bank Height Ratio:** Bank height ratio between 1.0 and 1.2 will indicate that flood flows have access to the active floodplain and that higher flows do not apply excessive stresses to stream banks.

Determination of true bankfull may be difficult to determine until the stream has experienced adequate flooding events to create strong bankfull indicators. Stream bank erosion upstream of the project site will persistently contribute sediment to the project reaches due to unstable upstream banks. Excess sediment will be routed through the project area or deposited in target areas such as point bars and the floodplain. Minor sedimentation of pools and glides may occur. The pools are designed to be over-dug to account for some sedimentation in pools and glides. If a large storm event occurs before the woody vegetation has established, isolated bank erosion may occur in sections where the flood-prone area has been restricted by topography or easements. Areas of bank erosion will be repaired as necessary.

1.3.2. Vegetation

The success of riparian vegetation planting will be gauged by stem counts of planted species. Stem counts of more than 320 trees per acre after three years, and 260 trees per acre after five years will be considered successful. Photos taken at established photo points should indicate maturation of riparian vegetation.

1.4. Mitigation Components

The Shadrick Creek Restoration Project generated 6,662 SMUs, 0.27 WMU, and 527,000 Square Feet. Buffer Credits. Refer to Figure 2 for the project component/ asset map for a visual description of the project assets and Table 1 for project components and mitigation credit information for the Shadrick Creek Restoration Project. These credits are based on stream lengths surveyed during the as-built baseline survey and account for the breaks in the easement.

The total number of SMU's generated from the Shadrick Creek Restoration Project are 164 SMUs lower than what was outlined in the Shadrick Creek Restoration Project Mitigation Plan Addendum (2015). This discrepancy is due mostly to the Mitigation Plan Addendum calculating the total linear feet of stream preservation as 3,835 while the as-built report total indicates that the total linear feet of preservation equals 2,895 (difference of 940 LF). It is believed that this discrepancy is attributed to UT3 and UT4 being determined as non-jurisdictional streams. Other deviations from the Mitigation Plan exist based on data taken from the centerline survey for the As-Built survey. Please refer to Table 1 for these numbers.

1.5. Project Performance

Monitoring Year 1 (MY1) data was collected from June to November 2018. Monitoring activities included visual assessment of all reaches and the surrounding easement, collection of images at 31 permanent photo stations, inventory of 16 permanent vegetation monitoring plots, surveying of 18 cross-sections, conducting 6 pebble counts, and collection of longitudinal profile survey data for approximately 1,354 linear feet of stream channel.

Summary information/data related to the occurrence of items such as beaver or encroachment and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report (formerly Mitigation Plan) and in the Mitigation Plan (formerly Restoration Plan) documents available on the NCDMS website (<http://portal.NCDEQ.org/web/eep>). All raw data supporting the tables and figures in the appendices is available from DMS upon request.

1.5.1. Vegetation

Visual assessment of vegetation outside of the monitoring plots (Appendix B – Table 6) indicates that the herbaceous vegetation is becoming established throughout the project. Shadrick Creek proper has some areas of bare, rocky ground, located primarily along the bankfull bench, This is to be expected in the first few years following construction and will be monitored in future site visits.

Monitoring of the permanent vegetation plots (n = 16; VP) was completed in September 2018. Summary tables and photographs associated with MY1 vegetation monitoring are located in Appendix B and Appendix C. MY1 monitoring data indicates that all vegetation plots are on track to meet the MY3 interim success criteria of 320 planted stems per acre. Planted stem densities among plots ranged from 324 to 688 planted stems per acre with an annual mean of 584 planted stems per acre across all plots. A total of 7 species of planted were documented within the plots. When volunteer stems are included, the mean annual total stems per acre rose to 800 and ranged between 324 and 1,214 stems per acre.

With regard to invasive-exotic species, multiple areas (n=15) of invasive-exotic vegetation were noted in small densities (0.67 acre) throughout the easement (Table 6). The species documented at the Shadrick Creek Site include Japanese honeysuckle (*Lonicera japonica*), Privet spp. (*Ligustrum sinense*), and kudzu (*Pueraria montana*). Two main infestations of kudzu occur on UT-1 and UT-9 Reach 1. Both of these areas were treated during MY1 with a foliar spray of a 1% clopyralid solution during July of 2018. Both of these infestation have been greatly reduced after an initial treatment and will be treated again during MY2. Herbicide treatments and mechanical control of the remaining invasive-exotic populations are also scheduled for MY2.

1.5.2. Stream Geomorphology

Visual assessment of the stream channel was performed to document signs of instability, such as eroding banks, structural instability, or excessive sedimentation. A few small areas of bank scour were noted on Shadrick Creek Reach 1, Shadrick Creek Reach 3 and UT-1 (Table 5, Figure 2 CCPV). The first area on Shadrick Creek Reach 1 is located at the top of the Project near STA 11+00. Here the left descending bank (LDB) has scoured out due to an uprooted tree. A large scour pocket has formed where the tree had previously been rooted. This area has been monitored since baseline conditions and has not worsened during MY1. Further downstream on Shadrick Reach 1 at STA 37+50, the right descending bank (RDB) is scouring just downstream of the log sill structure. At high flows the thalweg is directed directly at this portion of the bank and has scoured out approximately 20 feet of bank downstream from the structure. Just downstream of that from there, another area of instability was noted at STA 39+00 where the LDB has been scoured approximately 20 feet just downstream of the two log structure. While both of these areas of instability are associated with log structures, both structures are intact and the scour appears to be a result of high flows coupled with bare banks after construction. Two areas of bank scour were also noted on Shadrick Creek Reach 3. The first is located at STA 107+75, where again high flows with the lack of a vegetated buffer have scoured out the RDB of the inside bend approximately 20 feet. The other area of bank scour located on Shadrick Creek Reach 3 is located at the bottom of the reach at STA 116+00. This area also lacks vegetation and located along the LDB of a bend. High flows and increased velocity coming out of a very straight portion of the reach have scoured out this area approximately 15 feet. Lastly, a small area of scour was documented at the bottom end of UT-1 at STA 29+50. Increased velocities coming out of a culvert has scoured out the RDB about 20 feet. All of these areas will continue to be monitored in future site visits for further signs of instability.

Geomorphic data for MY1 was collected during October 2018. Summary tables and cross-section data plots related to stream morphology are located in Appendix D. Cross-sectional dimensions remained relatively stable between baseline conditions and MY1 monitoring efforts. The most substantial changes took place at cross-sections 1, 13, and 17. Cross-section 1 had the bankfull width decrease by 1.0 foot and the width/ depth ratio decreased by 2.8. Cross-sections 13 and 17 had the bankfull width increase by 1.4 feet and 1.6 feet and the width/ depth ratio increase by 6.7 and 1.5 respectively (Appendix D, Table 11a). Riffle dimensions for each reach also remained relatively similar between baseline conditions and MY1 monitoring. The most notable changes took place within UT-9 Reach 2, and UT-10. UT-9 Reach 2 saw a decrease in the bankfull width by 0.5 foot and the width/ depth ratio decreased by 2.8. Bankfull width on UT-10 increased by 1.5 feet due to a slight bit of scour along the bankfull bench (Appendix D, Table 11b).

Generally, longitudinal profile data (Appendix B, Table 11b) indicated relatively little change in riffle and pool dimensions between baseline conditions and MY1 monitoring. Profile data from Shadrick

Creek Reach 3 indicates that the stream has remained stable since baseline conditions. Riffle slopes and water surface slopes have remained almost the same since baseline. Mean riffle lengths have decreased by 7.3 feet and mean pool lengths have increased by 10.9 feet. UT-9 Reach 2 dimensions have also indicated that mean riffle lengths are shortening and mean pool lengths are increasing by 5.4 feet and 2.8 feet respectively. These changes are to be expected in the first couple years after baseline completion as the stream channel adjusts. Longitudinal profile data will continue to be collected and analyzed in future monitoring years for unhealthy trends.

Substrate monitoring was performed during MY1. Pebble count D_{50} fell into the coarse gravel range for Shadrick Creek Reach 1, coarse gravel for Shadrick Creek Reach 3, and silt/clay for UT-9 Reach 2. The channel substrate will be monitored in future years for shifts in particle size distributions

1.5.3. Stream Hydrology

Since project completion in late 2017, three bankfull events have been documented at the Shadrick Creek Site. Based on precipitation data, the suspected dates are January 12nd 2018, May 18th 2018, and October 18th 2018 (Table 12, Appendix E).

2.0 METHODS

The visual assessment of the project was performed at the beginning and end of each monitoring year. Permanent photo station photos were taken during the initial visual assessment when leaf-off conditions exist. Additional photos of vegetation or stream problem areas were taken as needed.

Geomorphic measurements were taken during low flow conditions using a Nikon[®] NPR 332 Total Station. Three-dimensional coordinates associated with cross-section and profile data were collected in the field and geo-referenced (NAD83 State Plane feet FIPS 3200). Morphological data were collected at 19 cross-sections. Survey data was imported into CAD, ArcGIS[®], and Microsoft Excel[®] for data processing and analysis. Channel substrate was characterized using a Wolman Pebble Count as outlined in Harrelson et al. (1994) and processed using Microsoft Excel.

Vegetation success is being monitored at 16 permanent monitoring plots. Vegetation monitoring follows the CVS-EEP Level 2 Protocol for Recording Vegetation, version 4.2 (Lee et al. 2008) and includes analysis of species composition and density of planted species. Data is processed using the CVS data entry tool. In the field, the four corners of each plot were permanently marked with metal t-posts and photos of each plot are taken from the origin each monitoring year.

Precipitation data was reported from the NCCRONOS station in Marion, NC. Bankfull events were documented with two crest gauges, one located on Shadrick Creek Reach 1 and another on Shadrick Creek Reach 3. Crest gauges will be monitored semi-annually. The height of the corklines was recorded and cross-referenced with known bankfull elevations at each crest gauge.

3.0 REFERENCES

Ben Patton Land Surveying. 2017. As-Built Survey of Shadrick Creek Restoration Project. Prepared for N.C. Division of Mitigation Services.

Confluence Engineering. 2015. Mitigation Plan Addendum – Final, Shadrick Creek Restoration Project. . Prepared for North Carolina Department of Environment and Natural Resources, Ecosystem Enhancement Program. Mitigation Plan Addendum – Final, Shadrick Creek Restoration Project. EEP Project No. 92916.

Kimley-Horn and Associates, Inc. 2010. Mitigation Plan for Shadrick Creek Stream Restoration. Prepared for North Carolina Department of Environment and Natural Resources, Ecosystem Enhancement Program. Final Mitigation Plan, Shadrick Creek Stream Restoration, McDowell County. EEP Project No: 92916.

Lee, Michael T., R.K. Peet, S.D. Roberts, and T.R. Wentworth. 2008. CVS-EEP Protocol for Recording Vegetation, Version 4.2 (<http://cvs.bio.unc.edu/methods.htm>)

Page Intentionally Left Blank

Appendix A
Project Background Data and Maps

Driving Directions: From Asheville drive east on I-40 and take exit 90. Turn right onto Harmony Grove Road, after 0.6 miles turn right to stay on Harmony Grove Road. After 2.2 miles continue onto State Road 1536. After 0.4 miles turn right on NC-126 E. Follow NC-126 E for approximately 2.5 miles then turn right onto a dirt road across from Lake James State Park. The Shadrick Creek Mitigation Site will be on the right after about 0.25 mile.

The subject project site in an environmental restoration site of the NCDMS and encompassed by a recorded conservation easement, but is bordered by land with private ownership. Accessing the site may require traversing areas near or along the easement boundary and therefore access to the general public is not permitted. Access by authorized personnel of state and federal agencies or their designee/contractors involved in the development, oversight, and stewardship of the restoration site is permitted within the terms and timeframes of their defined role. Any intended site visitation or activity by any person outside of these previously sanctioned roles and activities requires prior coordination with NCDMS.

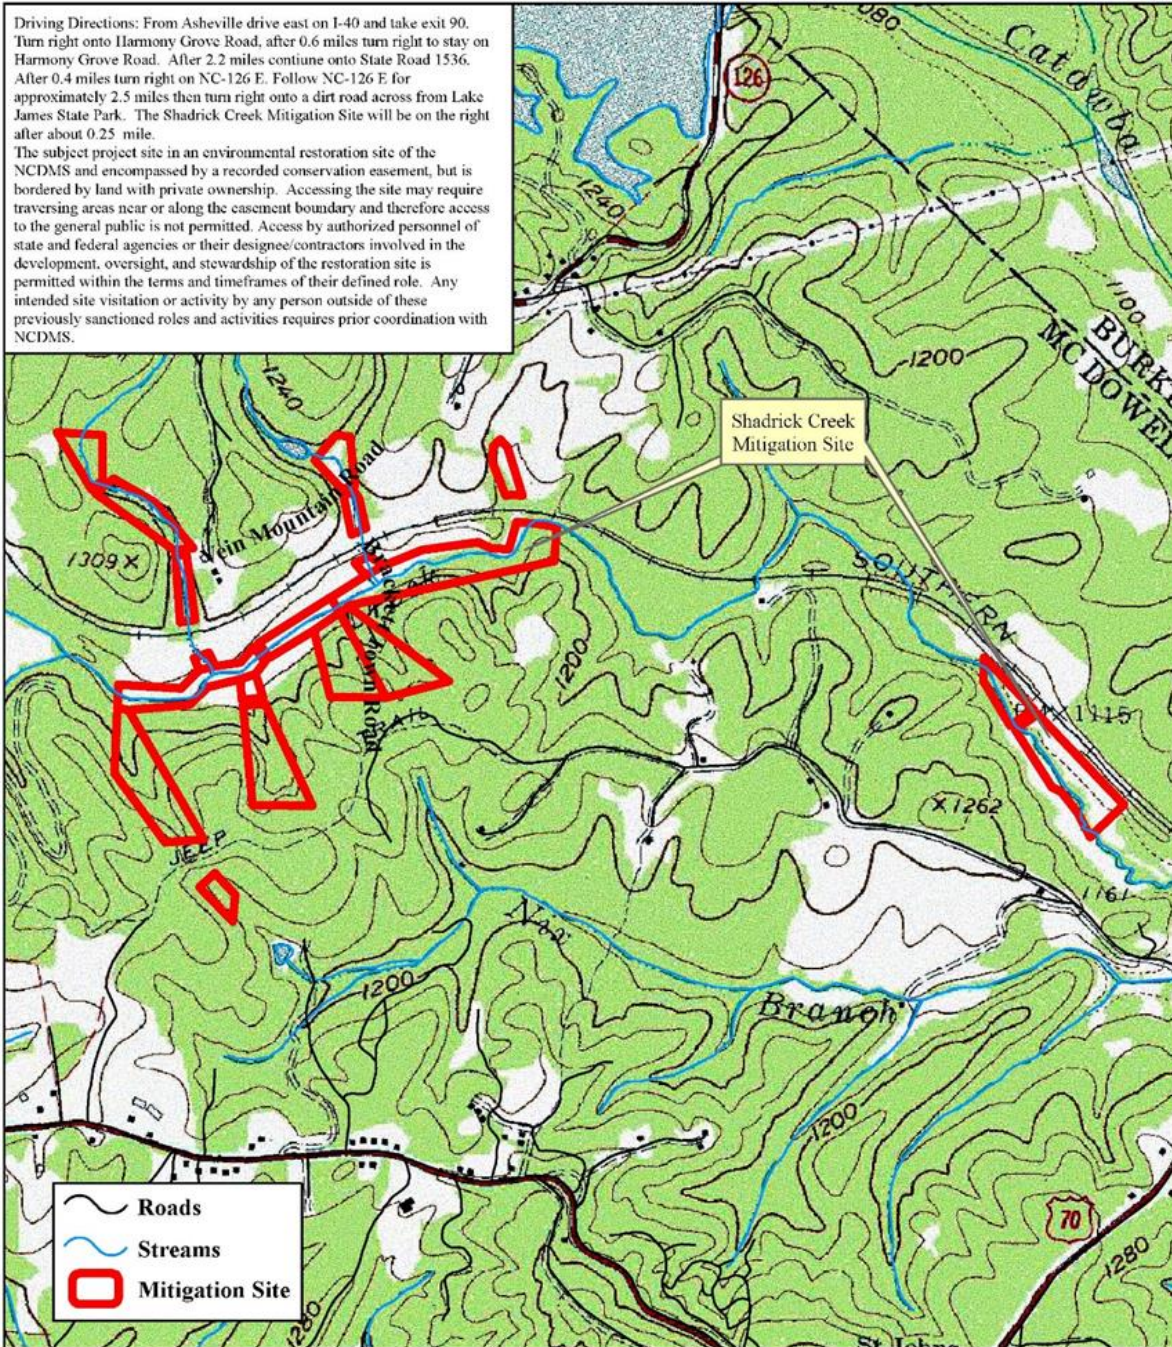


Figure 1
Shadrick Mitigation Site
Vicinity Map




Table 1. Project Mitigation Components and Summation									
Shadrick Creek Stream Restoration Project									
Mitigation Credits*									
	Stream SMUs				Wetland WMUs	Buffer SF			
Type	R	EI	EII	P	E	527,000			
Totals	1,353	4,644	86	579	0.27				
Project Components									
Project Component -or- Reach ID	Stationing/Location	Existing Footage/Acreage	Restoration Footage or Acreage*	Restoration Footage/Acreage Discrepancy from Mitigation Plan	Restoration - or- Restoration Equivalent	Approach	Mitigation Ratio	Mitigation Credits*	Buffer SF
						(PI, PII etc.)			
Shadrick Reach 1	10+06 - 46+84	3,686	3,632	-6	EI	P3	1.5:1	2,421	199,000
Shadrick Reach 2	100+04 - 105+77	595	573	-2	EI	P3	1.5:1	382	226,000
Shadrick Reach 3	105+77 - 117+26	1,168	1,104	-4	R	P2	1:1	1,104	
UT-1	10+00 - 30+57	1,637	1,651	14	EI	P3	1.5:1	1,101	46,000
UT-5	6+64 - 8+79	228	215	-13	EII	Buffer	2.5:1	86	Incl. in Shadrick R1
UT's 2, 5, 6, 7 & 8	-	3,835	2,895	-940	P	Preservation	5:1	579	-
UT-9 Reach 1	9+90 - 17+42	678	706	28	EI	P3	1.5:1	471	34,000
UT-9 Reach 2	19+59 - 22+08	237	249	3	R	P2	1:1	249	
UT-10	9+92 - 13+96	391	404	13	EI	P3	1.5:1	269	24,000
Wetland A	UT1	0.44	0.44	0	E	Stab./Buffer	2:1	0.22	-
Wetland B	Shadrick Reach 1	0.09	0.09	0	E	Buffer	2:1	0.05	-
Component Summation									
Restoration Level	Stream	Riparian Wetland		Non-riparian Wetland	Buffer	Upland			
	(linear feet)	(acres)		(acres)	(square feet)	(acres)			
		Riverine	Non-Riverine	-	-	-			
Restoration	1,353	-	-	-	-	-			
Enhancement	-	0.53	-	-	-	-			
Enhancement I	6,966	-	-	-	-	-			
Enhancement II	215	-	-	-	-	-			
Preservation	2,895	-	-	-	527,000 SF	-			
High Quality Preservation	-	-	-	-	-	-			
BMP Elements									
Element	Location	Purpose/Function		Notes					
FB	Entire Site	Protect Stream Channel							
BMP Elements									
BR = Bioretention Cell; SF = Sand Filter; SW = Stormwater Wetland; WDP = Wet Detention Pond; DDP = Dry Detention Pond; FS = Filter Strip; S = Grassed Swale; LS = Level Spreader; NI = Natural Infiltration Area; FB = Forested Buffer									
* Mitigation credits and stream lengths account for breaks in conservation easements									

**Table 2. Project Activity and Reporting History
Shadrick Creek Restoration Project**

Activity or Report	Data Collection Complete	Completion or Delivery
Mitigation Plan	-	May 2010
Mitigation Plan Addendum	-	Feb 2015
Final Design - Construction Plans	-	Feb 2015
Construction	Oct 2016 - Jun 2017	Jun 2017
Temporary S&E Mix Applied	Oct 2016 - Jun 2017	Jun 2017
Permanent Seed Mix Applied	Oct 2016 - Jun 2017	Jun 2017
Bare Root and Live Stake Plantings	Dec 2016 - Apr 2017	Apr 2017
Baseline Monitoring Document (Year 0 Monitoring - Baseline)	Sep 2017 - Dec 2017	Feb 2018
Stream Assessment	Dec 2017	Feb 2018
Vegetation Assessment	Sep 2017	
Year 1 Monitoring		
Invasive-Exotic Treatment	-	July 2018
Year 1 Vegetation Monitoring	Sept 2018	-
Year 1 Geomorphology Monitoring	Oct 2018	-
Year 2 Monitoring		
Year 3 Monitoring		
Year 4 Monitoring		
Year 5 Monitoring		


Table 3. Project Contacts	
Shadrick Creek Restoration Project	
Prime Contractor	North Carolina Division of Mitigation Services 217 W Jones Street Suite 3000a Raleigh, North Carolina 27603 Matthew Reid (828) 231-7812
Designer	Wildlands Engineering 167B Haywood Road Asheville, North Carolina 28806 Andrew Bick (828) 774-5547
Construction Contractor	Baker Construction 1000 Bat Cave Road Old Fort, NC 28762 Charles Baker (828) 668-5060
Seeding Contractor	Baker Construction 1000 Bat Cave Road Old Fort, NC 28762 Charles Baker (828) 668-5060
Planting Contractor	Equinox 37 Haywood St. Asheville, North Carolina 28801 Owen Carson (828) 253-6856
As-built Surveys	Ben Patton Land Surveying 259 Daves Farm Dr. Marion, NC 28752 Ben Patton (828) 768-1625
Seeding Mix Source	Green Resource 5204 Highgreen Court Colfax, North Carolina 27235 (336) 855-6363
Live Stakes	Foggy Mountain Nursery 797 Helton Creek Road Lansing, North Carolina (336) 384-5323
Monitoring Performers (Y0-Y1) 2017 - 2018	Equinox Environmental 37 Haywood St. Asheville, North Carolina 28801 Drew Alderman (828) 253-6856

Table 4. Project Baseline Information and Attributes							
Project Information							
Project Name	Shadrick Creek						
County	McDowell						
Project Area (acres)	54.6						
Project Coordinates (latitude and longitude)	35.720410° N, -81.901405° W						
Project Watershed Summary Information							
Physiographic Province	Blue Ridge						
River Basin	Catawba River						
USGS Hydrologic Unit 8-digit	3050101	USGS Hydrologic Unit 14-digit				0305010103006	
DWR Sub-basin	03-08-30						
Project Drainage Area (acres)	2,093						
Project Drainage Area Percentage of Impervious Area	> 1%						
CGIA Land Use Classification	Agricultural						
Reach Summary Information							
Parameters	Shadrick Creek Reach 1	Shadrick Creek Reach 2	Shadrick Creek Reach 3	UT-1	UT-9 Reach 1	UT-9 Reach 2	UT-10
Length of reach (linear feet)*	3,632	573	1,104	1,651	706	249	404
Valley Confinement (Rosgen)	VIII	VIII	VIII	II	II	VIII	II
Drainage area (miles ²)	2.80	3.30	3.30	0.10	0.10	0.10	0.05
Perennial, Intermittent, Ephemeral	Perennial	Perennial	Perennial	Perennial	Perennial	Perennial	Perennial
NCDWR Water Quality Classification	C	C	C	C	C	C	C
Stream Classification (existing)	E4	E4	E4	G4	B4, G4	B4, G4	F4
Stream Classification (proposed)	C4	C4	C4	B4	B4	E4	B4
Evolutionary Trend (Rosgen)	V	V	V	V	VI	VI	VI
FEMA classification	-	-	-	-	-	-	-
Wetland Summary Information							
Parameters	Wetland A			Wetland B			
Size of Wetland (acres)	0.44			0.09			
Wetland Type (non-riparian, riparian riverine or riparian non-riverine)	Riparian			Riparian			
Mapped Soil Series	HeD			EwE			
Drainage class	well-drained			well-drained			
Soil Hydric Status	Hydric			Hydric			
Source of Hydrology	Spring			Spring			
Hydrologic Impairment	Logging			Stream Incision, Cattle Grazing			
Native vegetation community	Piedmont/ Low Mountain Alluvial Forest			Piedmont/ Low Mountain Alluvial Forest			
Percent composition of exotic invasive vegetation	0%			0%			
Regulatory Considerations							
Regulation	Applicable?	Resolved?				Supporting Documentation	
Waters of the United States – Section 404	Yes	Yes				Jurisdictional Determination	
Waters of the United States – Section 401	Yes	Yes				Jurisdictional Determination	
Endangered Species Act	No	N/A				ERTR	
Historic Preservation Act	No	N/A				ERTR	
Coastal Zone Management Act (CZMA)/ Coastal Area Management Act (CAMA)	No	N/A					
FEMA Floodplain Compliance	Yes	Yes				Yes	
Essential Fisheries Habitat	No	N/A				-	

*Accounts for breaks in conservation easements

Appendix B
Visual Assessment Data

Figure 2 Current Condition Plan View.

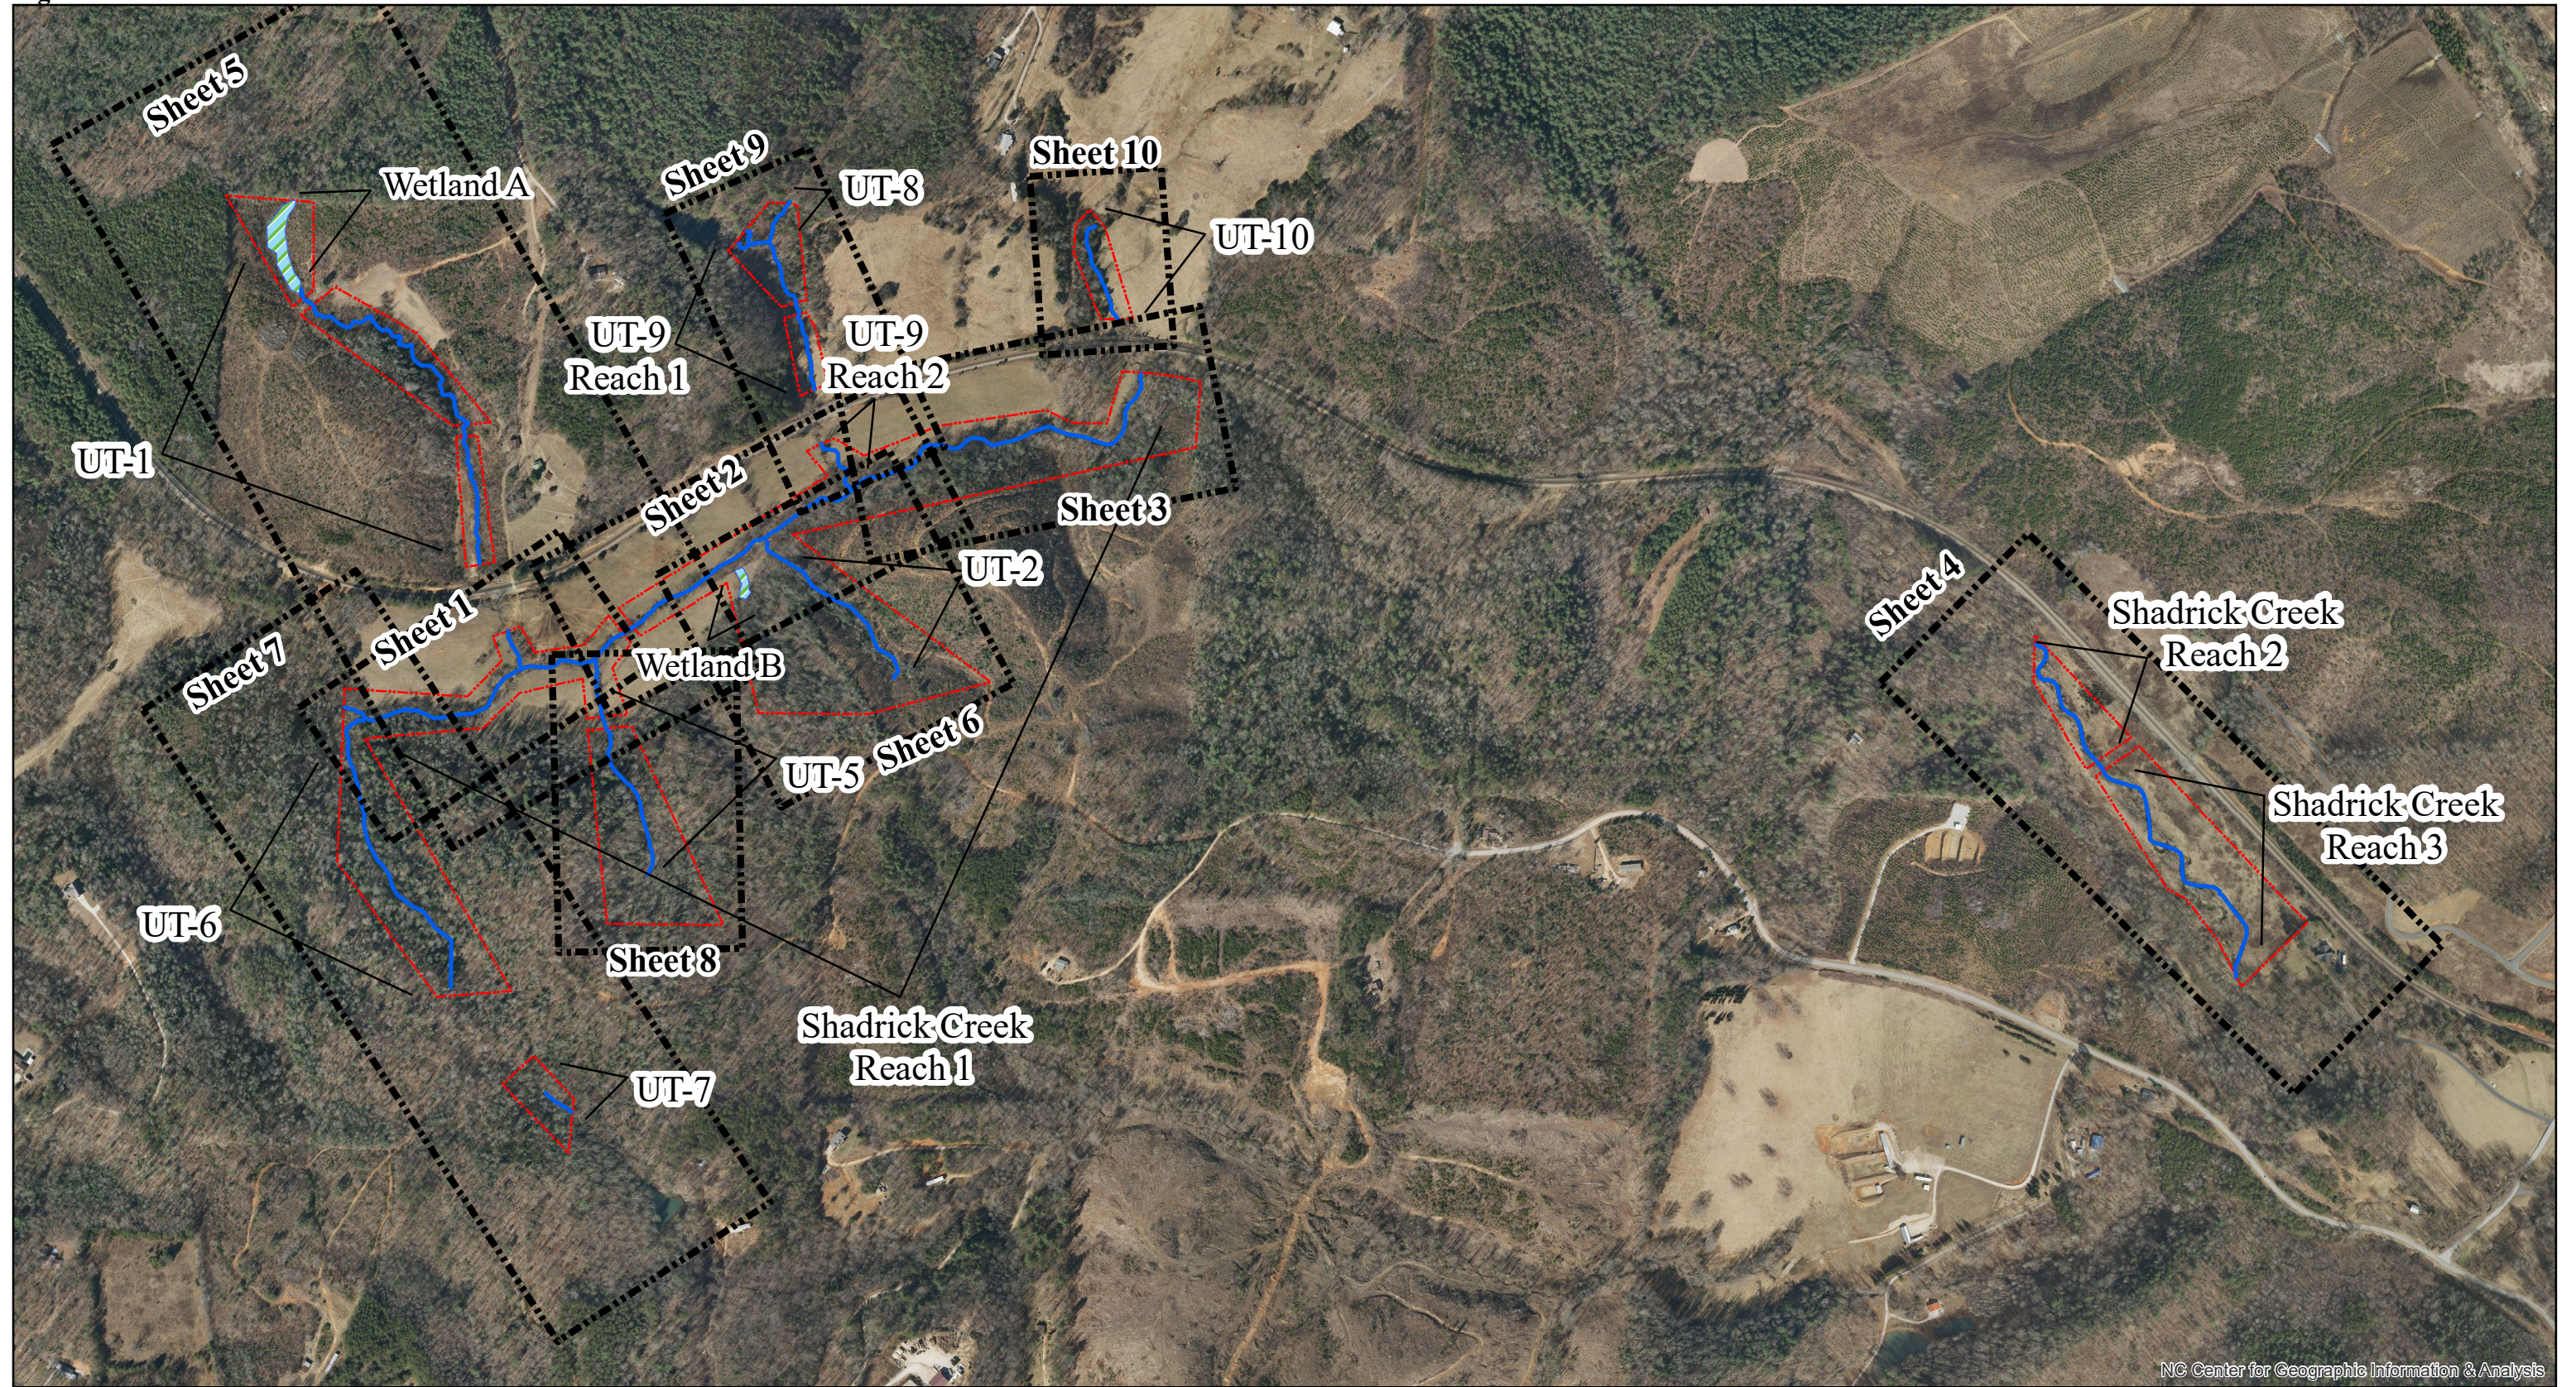

NC Center for Geographic Information & Analysis



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Overview Map






-  Thalweg
-  Wetland Enhancement
-  Easement
-  Sheet



Figure 2 Current Condition Plan View.



Prepared for:

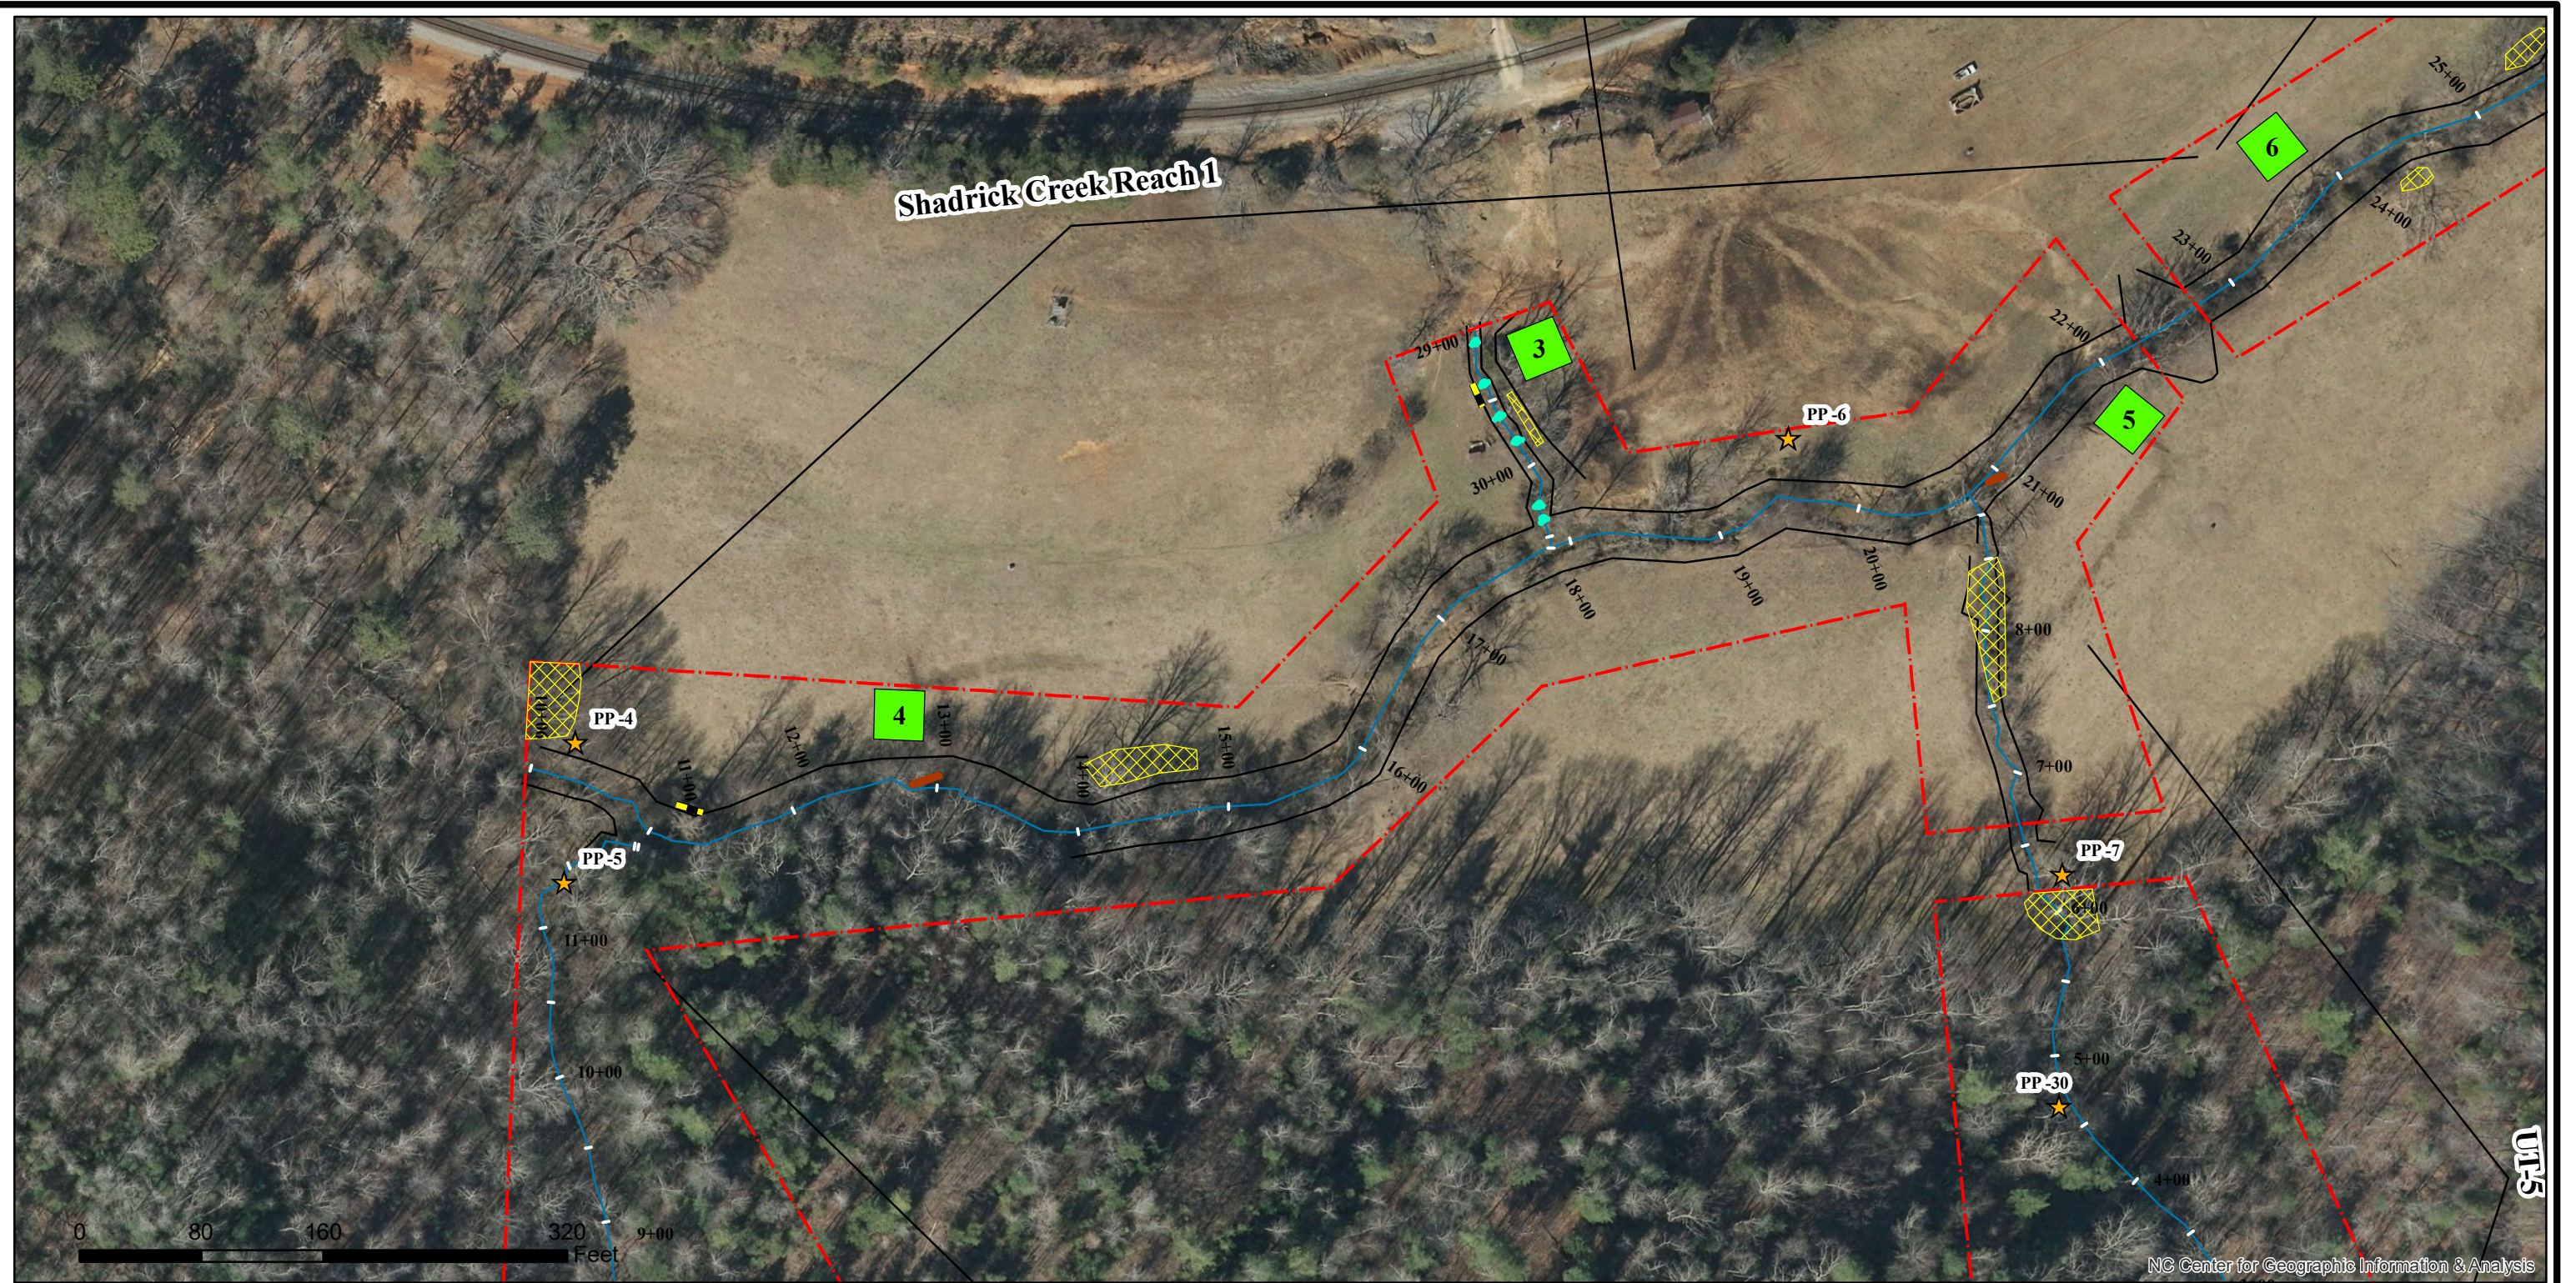

Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 1 of 10

- | | | | |
|---|-------------------|---|-------------------------|
| ★ | Photo Point | ■ | Vegetation Plot |
| — | Easement | ■ | Success Criteria Met |
| — | Top of Bank | — | Stream Problem Areas |
| — | Thalweg | — | Bank Erosion |
| — | Log Vane | — | Invasive-Exotic Species |
| — | Boulder Structure | ■ | Present |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 2 of 10

- | | | | | | |
|--|-------------|--|---------------------|--|----------------------|
| | Crest Gauge | | Cross-Section | | Success Criteria Met |
| | Photo Point | | Log Vane | | Treated |
| | Easement | | Wetland Enhancement | | Present |
| | Top of Bank | | | | |
| | Thalweg | | | | |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



NC Center for Geographic Information & Analysis

Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 3 of 10

- | | | |
|---------------|-----------------------------------|------------------------|
| ★ Photo Point | —+— Cross-Section | Vegetation Plot |
| ⬡ Easement | — Log Vane | ⬡ Success Criteria Met |
| — Top of Bank | — Bank Erosion | Stream Problem Areas |
| — Thalweg | — Invasive-Exotic Species Present | |


Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.

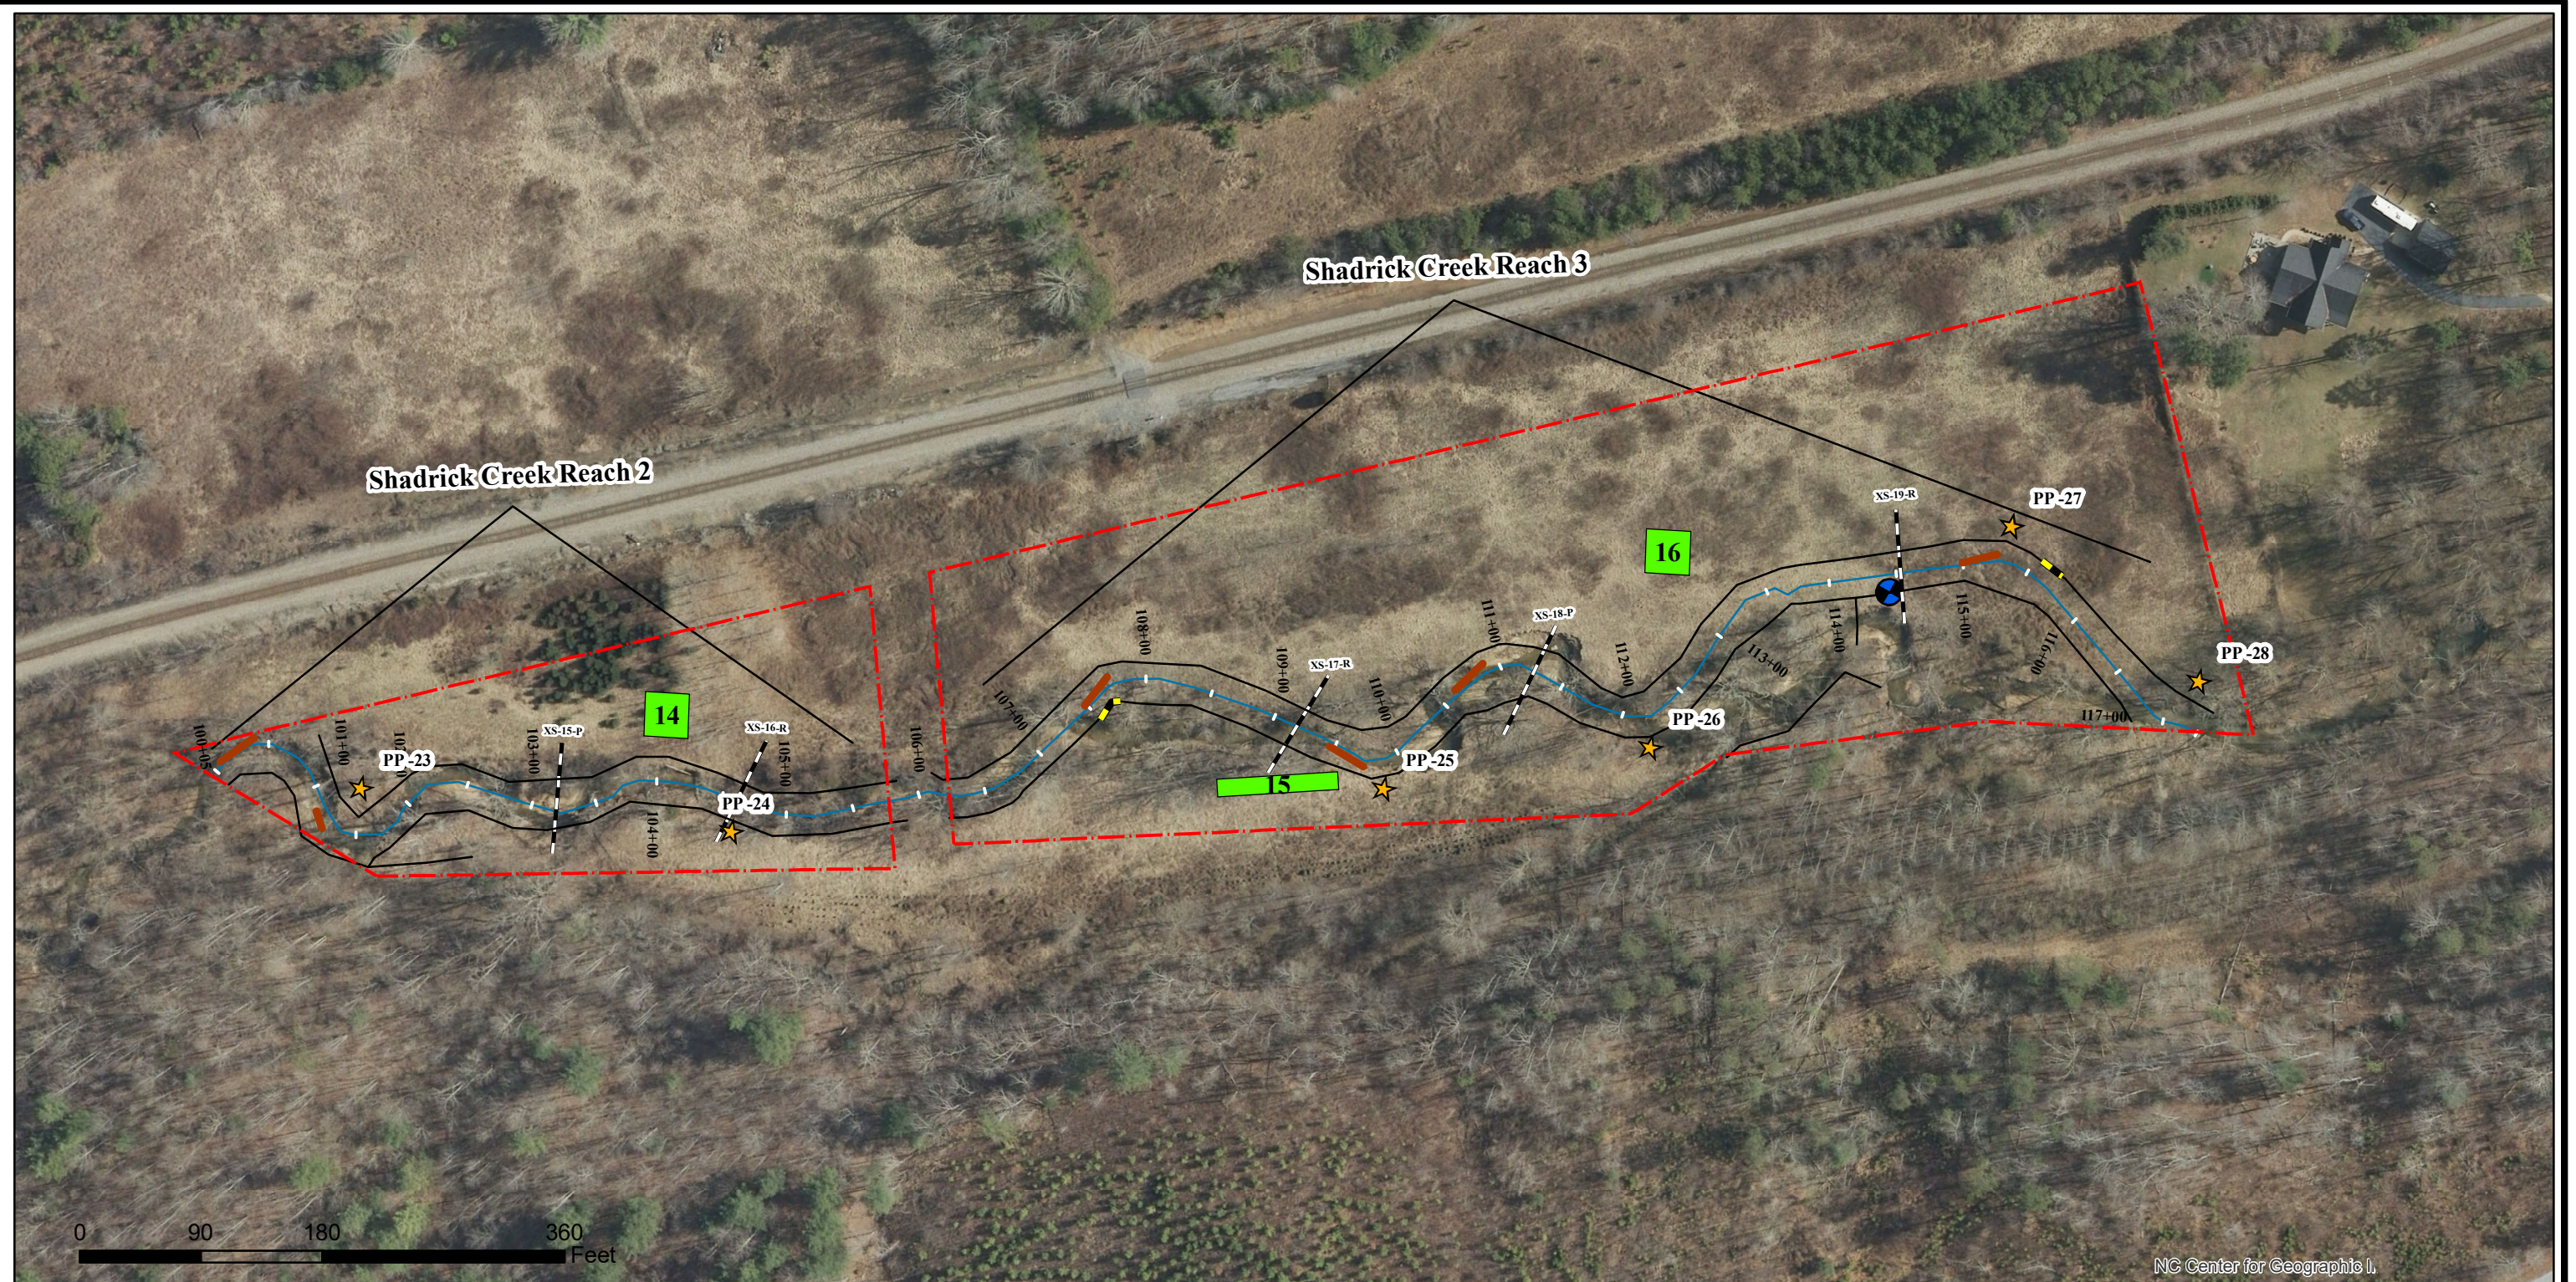

NC Center for Geographic I.

Prepared for:



Shadrick Creek Restoration Site
Monitoring Year 1
McDowell County, NC

NCDMS Contract No.: 00006783

NCDMS Project No.: 92916

Sheet November 2018

- | | | | | | |
|--|-------------|--|----------------------|--|----------------------|
| | Crest Gauge | | Cross-Section | | Vegetation Plot |
| | Photo Point | | Log Vane | | Success Criteria Met |
| | Easement | | Stream Problem Areas | | Bank Erosion |
| | Top of Bank | | Thalweg | | |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



NC Center for Geographic I.

Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 5 of 10

- | | | |
|---------------|-----------------------|---------------------------|
| ★ Photo Point | —+— Cross-Section | ■ Success Criteria Met |
| ⬡ Easement | — Log Vane | ■ Stream Problem Areas |
| — Top of Bank | —+— Boulder Structure | ▨ Bank Erosion |
| — Thalweg | ▨ Wetland Enhancement | ▨ Invasive-Exotic Species |
| | | ▨ Treated |
| | | ▨ Present |


Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.

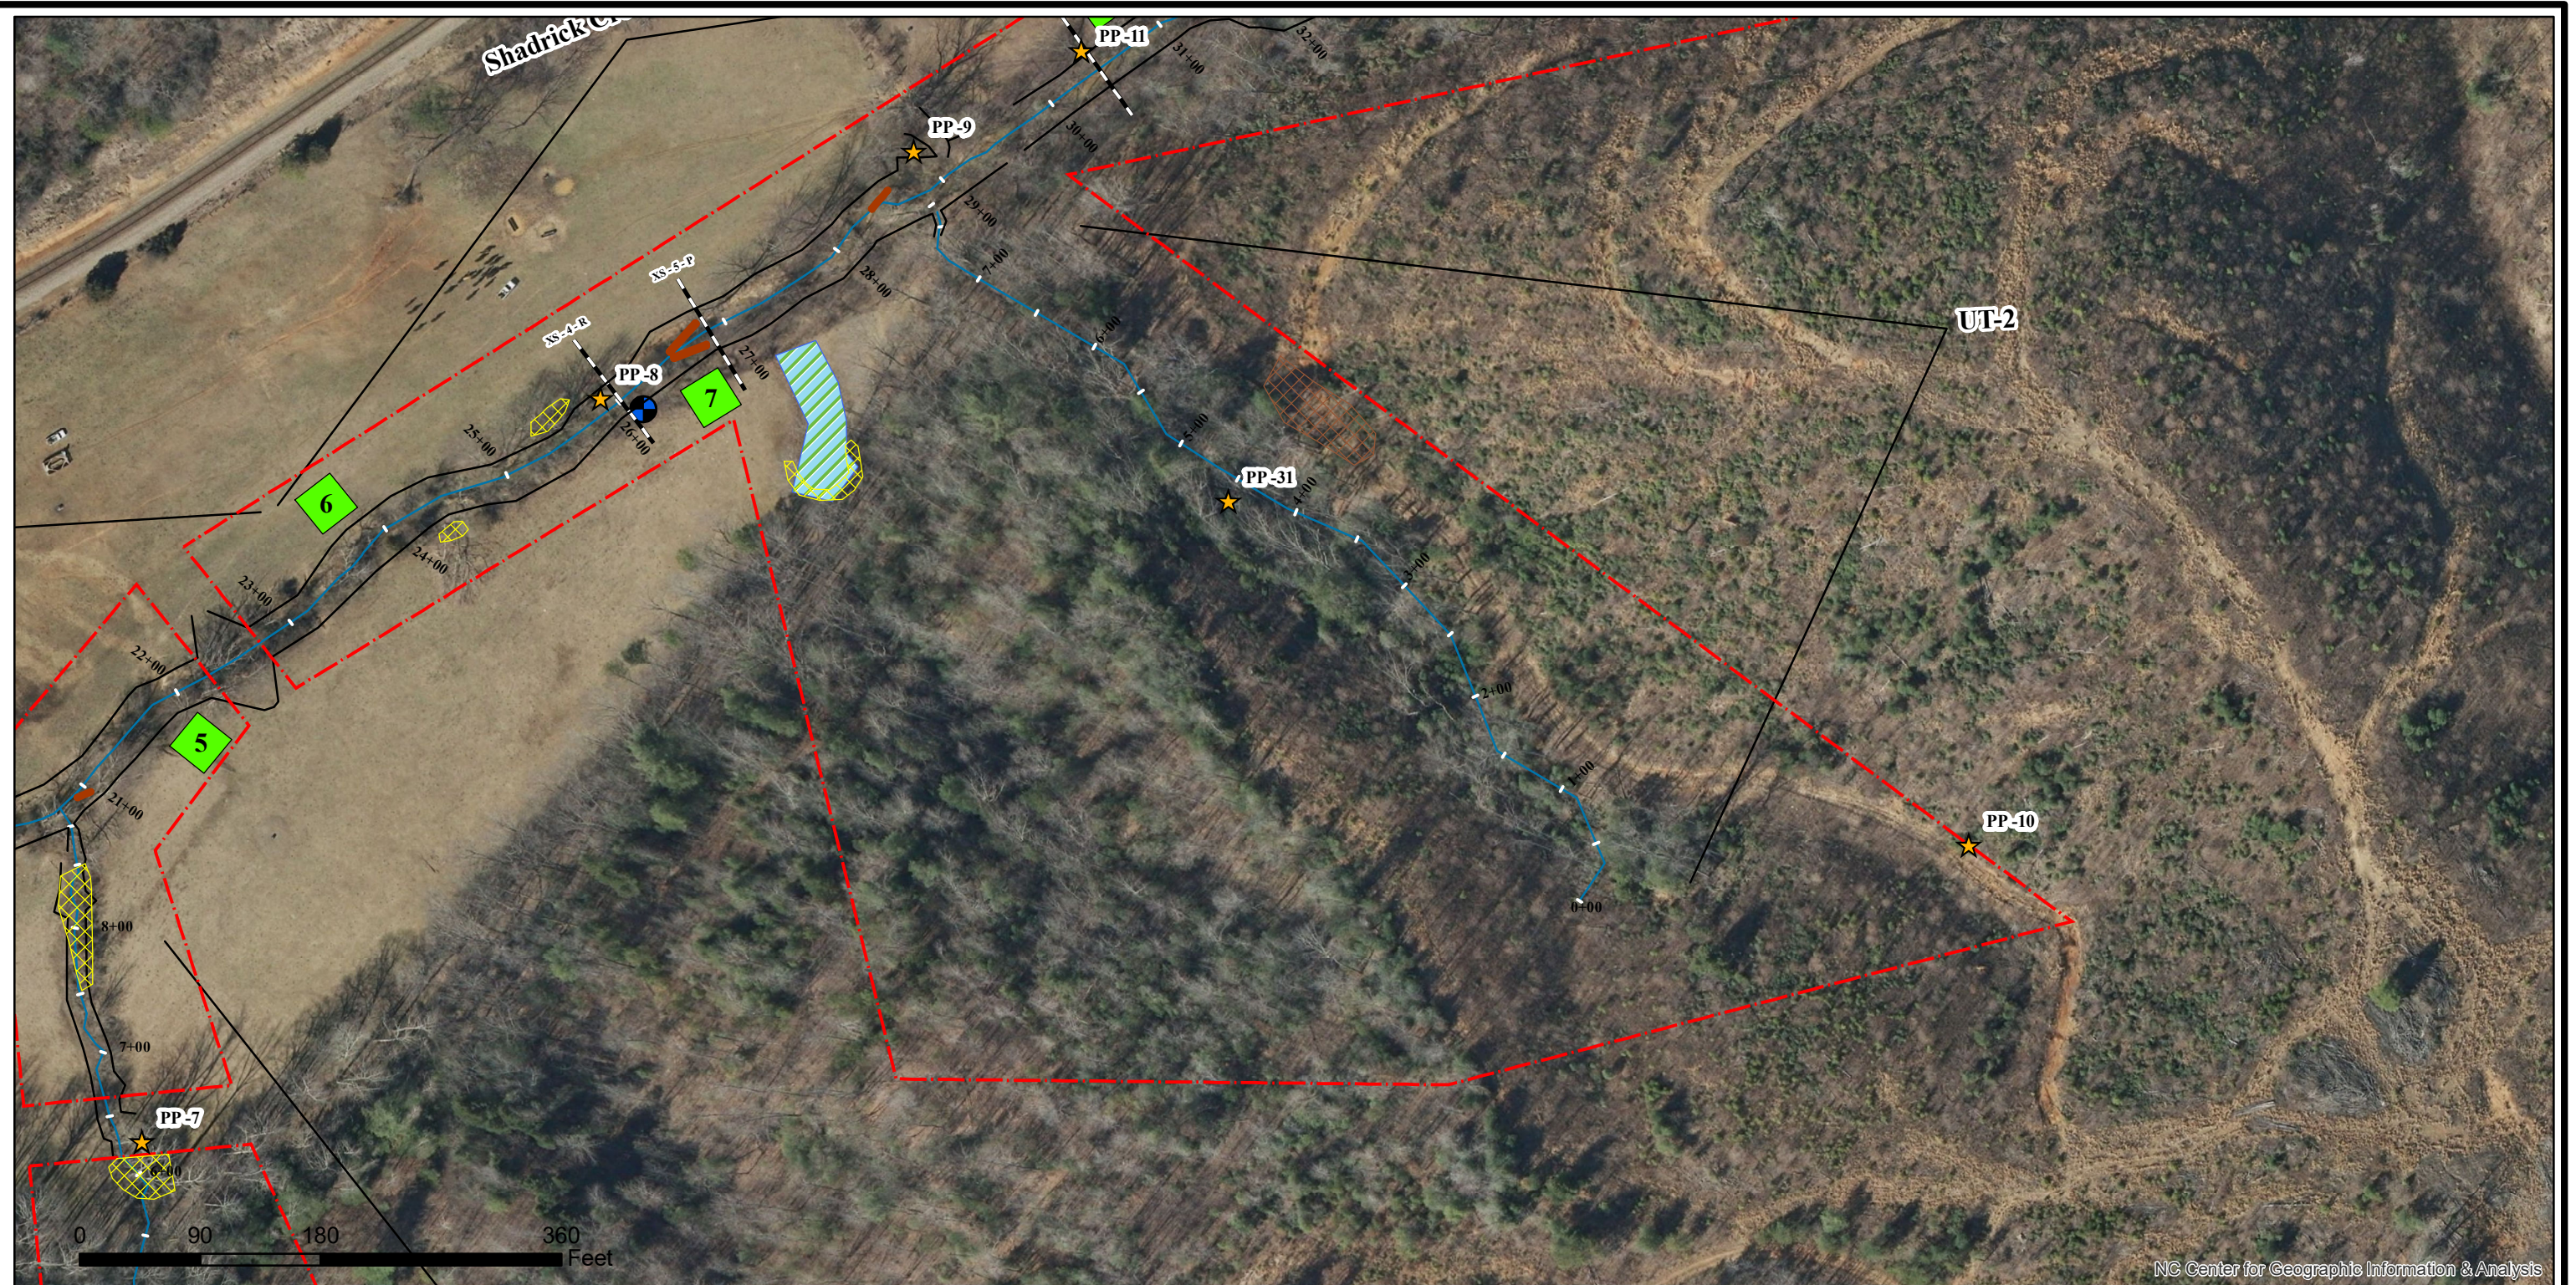

NC Center for Geographic Information & Analysis

Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 6 of 10

- | | | | | | |
|--|-------------|--|---------------------|--|-------------------------|
| | Crest Gauge | | Cross-Section | | Vegetation Plot |
| | Photo Point | | Log Vane | | Success Criteria Met |
| | Easement | | Wetland Enhancement | | Invasive-Exotic Species |
| | Top of Bank | | | | Treated |
| | Thalweg | | | | Present |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 7 of 10

- | | | |
|----------------|-------------|-------------------------|
| ★ | Photo Point | Vegetation Plot |
| ⬜ (dashed red) | Easement | Success Criteria Met |
| — (black) | Top of Bank | Stream Problem Areas |
| — (blue) | Thalweg | Bank Erosion |
| — (brown) | Log Vane | Invasive-Exotic Species |
| | | Present |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 8 of 10

- ★ Photo Point
- ⎓ Easement
- Top of Bank
- Thalweg
- Invasive-Exotic Species
- ▨ Present

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 9 of 10

- | | | | | | |
|---|-------------|-----|-------------------------|---|----------------------|
| ★ | Photo Point | —+— | Cross-Section | ■ | Vegetation Plot |
| — | Easement | — | Log Vane | ■ | Success Criteria Met |
| — | Top of Bank | — | Invasive-Exotic Species | ■ | Treated |
| — | Thalweg | | | | |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Figure 2 Current Condition Plan View.



Prepared for:



Shadrick Creek Restoration Site
 Monitoring Year 1
 McDowell County, NC
 NCDMS Contract No.: 00006783
 NCDMS Project No.: 92916
 November 2018
 Sheet 10 of 10

- | | | | | |
|-------|-------------|-------|---------------|-------------------------|
| ★ | Photo Point | — — — | Cross-Section | Vegetation Plot |
| — — — | Easement | — | Log Vane | Success Criteria Met |
| — | Top of Bank | ■ | | Invasive-Exotic Species |
| — | Thalweg | ▨ | | Present |

Notes:

1) Baseline Data Provided by Patton Land Surveying

Prepared by



Page Intentionally Left Blank

**Table 5. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - Shadrick Creek Reach 1 - Enhancement I
Assessed Length 3,631 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			3	66	99%	0	0	99%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					3	66	99%	N/A	N/A	N/A
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	15	15			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	15	15			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	15	15			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	15	15			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	15	15			100%			

- Information Unavailable

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - Shadrick Creek Reach 2 - Enhancement I
Assessed Length 573 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					0	0	100%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	2	2			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	2	2			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	2	2			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	2	2			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	2	2			100%			

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - Shadrick Creek Reach 3 - Restoration
Assessed Length 1,104 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			2	41	98%	0	0	98%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					2	41	98%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	3			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	3	3			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	3			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	3	3			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio \geq 1.6. Rootwads/logs providing some cover at base-flow.	3	3			100%			

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - UT1 - Enhancement 1
Assessed Length 1,651 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			1	18	99%	0	0	99%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					1	18	99%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	14	14			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	14	14			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	14	14			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	14	14			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio \geq 1.6. Rootwads/logs providing some cover at base-flow.	14	14			100%			

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - UT9 Reach 1 - Enhancement 1
Assessed Length 706 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					0	0	100%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	2	2			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	2	2			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	2	2			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	2	2			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	2	2			100%			

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - UT9 Reach 2 - Restoration
Assessed Length 238 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					0	0	100%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio \geq 1.6. Rootwads/logs providing some cover at base-flow.	1	1			100%			

N/A - Item does not apply.

**Table 5 cont'd. Visual Stream Morphology Stability Assessment
Shadrick Creek Restoration Site - UT10 - Enhancement I
Assessed Length 404 feet**

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bank	1. Scoured / Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion.			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
	3. Mass Wasting	Bank slumping, calving, or collapse.			0	0	100%	N/A	N/A	N/A
Totals					0	0	100%	N/A	N/A	N/A
2. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>NOT</u> exceed 15%.	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth Ratio ≥ 1.6. Rootwads/logs providing some cover at base-flow.	1	1			100%			

N/A - Item does not apply.

**Table 6. Vegetation Condition Assessment
Shadrick Creek Restoration Site**

Planted Acreage : 8.68					
Vegetation Category	Definitions	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	Brown Stipple	0	0.00	0%
2. Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	Red Stipple	0	0.00	0%
Totals			0	0.00	0%
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	N/A	0	0.00	0%
Cumulative Totals			0	0.00	0%
Easement Acreage : 54.59					
Vegetation Category	Definitions	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern	Areas or points (if too small to render as polygons at map scale).	Cross Hatch (Red - Dense/Yellow - Present)	15	0.67	1%
5. Easement Encroachment Areas	Areas or points (if too small to render as polygons at map scale).	N/A	0	0.00	0%

N/A - Item does not apply.

Permanent Photo Stations



UT-1 – Permanent Photo Station 1
Looking Upstream



UT-1 – Permanent Photo Station 1
Looking Downstream



UT-1 – Permanent Photo Station 2
Looking Upstream



UT-1 – Permanent Photo Station 2
Looking Downstream



UT-1 – Permanent Photo Station 3
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 4
Looking Downstream



UT-6 – Permanent Photo Station 5
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 6
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 6
Looking Downstream



UT-7 – Permanent Photo Station 7
Looking Upstream from Crossing



UT-7 – Permanent Photo Station 7
Looking Downstream from Crossing



Shadrick Creek Reach 1 – Permanent Photo Station 8
Looking Upstream from Cross-Section 4



Shadrick Creek Reach 1 – Permanent Photo Station 8
Looking Downstream from Cross-Section 4



Shadrick Creek Reach 1 – Permanent Photo Station 9
Looking Upstream at UT-2



UT-2 - Permanent Photo Station 10
Looking Downstream at Easement



Shadrick Creek Reach 1 – Permanent Photo Station 11
Looking Upstream from Cross-Section 6



Shadrick Creek Reach 1 – Permanent Photo Station 11
Looking Downstream from Cross-Section 6



Shadrick Creek Reach 1 – Permanent Photo Station 12
Looking Upstream Shadrick Creek from confluence of UT-9 Reach 2



Shadrick Creek Reach 1 – Permanent Photo Station 12
Looking Downstream Shadrick Creek from confluence of UT-9 Reach 2



Shadrick Creek Reach 1 – Permanent Photo Station 12
Looking Upstream UT-9 Reach 2 from the confluence with Shadrick Creek



Shadrick Creek Reach 1 – Permanent Photo Station 13
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 13
Looking Downstream



Shadrick Creek Reach 1 – Permanent Photo Station 14
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 14
Looking Downstream



Shadrick Creek Reach 1 – Permanent Photo Station 15
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 16
Looking Upstream



Shadrick Creek Reach 1 – Permanent Photo Station 16
Looking Downstream



UT-9 Reach 1 – Permanent Photo Station 17
Looking Upstream



UT-9 Reach 1 – Permanent Photo Station 17
Looking Downstream



UT-8– Permanent Photo Station 17
Looking Upstream



UT-9 Reach 1 – Permanent Photo Station 18
Looking Downstream



UT-9 Reach 1 – Permanent Photo Station 19
Looking Upstream



UT-9 Reach 2 – Permanent Photo Station 20
Looking Downstream



UT-10 – Permanent Photo Station 21
Looking Downstream



UT-10 – Permanent Photo Station 22
Looking Upstream



Shadrick Creek Reach 2 – Permanent Photo Station 23
Looking Upstream



Shadrick Creek Reach 2 – Permanent Photo Station 23
Looking Downstream



Shadrick Creek Reach 2 – Permanent Photo Station 24
Looking Upstream



Shadrick Creek Reach 2 – Permanent Photo Station 24
Looking Downstream



Shadrick Creek Reach 3 – Permanent Photo Station 25
Looking Upstream



Shadrick Creek Reach 3 – Permanent Photo Station 25
Looking Downstream



Shadrick Creek Reach 3 – Permanent Photo Station 26
Looking Upstream



Shadrick Creek Reach 3 – Permanent Photo Station 26
Looking Downstream



Shadrick Creek Reach 3 – Permanent Photo Station 27
Looking Upstream



Shadrick Creek Reach 3 – Permanent Photo Station 28
Looking Upstream



UT-7 – Permanent Photo Station 29
Looking Downstream



UT5 – Permanent Photo Station 30
Looking Upstream



UT-2 – Permanent Photo Station 31
Looking Downstream

Vegetation Plot Photos



Vegetation Monitoring Plot 1



Vegetation Monitoring Plot 2



Vegetation Monitoring Plot 3



Vegetation Monitoring Plot 4



Vegetation Monitoring Plot 5



Vegetation Monitoring Plot 6



Vegetation Monitoring Plot 7



Vegetation Monitoring Plot 8



Vegetation Monitoring Plot 9



Vegetation Monitoring Plot 10



Vegetation Monitoring Plot 11



Vegetation Monitoring Plot 12



Vegetation Monitoring Plot 13



Vegetation Monitoring Plot 14



Vegetation Monitoring Plot 15



Vegetation Monitoring Plot 16

Appendix C

Vegetation Plot Data

Page Intentionally Left Blank

Table 7. Current Plot Data (MY1) 2018 Shadrick Creek Restoration Project																																	
Scientific Name	Common Name	Species Type	Current Plot Data (MY1 2018)																														
			Plot 1			Plot 2			Plot 3			Plot 4			Plot 5			Plot 6			Plot 7			Plot 8			Plot 9			Plot 10			
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	
<i>Acer rubrum</i>	Red Maple	Tree	2	2	2	3	3	3	1	1	1	2	2	2				4	4	4	1	1	1				1	1	1				
<i>Alnus serrulata</i>	Tag Alder, Smooth Alder, Hazel Alder	Shrub Tree						4					1			8					14			1									
<i>Betula nigra</i>	River Birch, Red Birch	Tree							1	1	1					9	2	2	2	2	2	2	2	2	2	2	2	2	2	7	7	7	
<i>Cercis canadensis</i>	Red bud	Shrub Tree							1	1	1														5	5	5	3	3	3			
<i>Diospyros virginiana</i>	American Persimmon, Possumwood	Tree										1																					
<i>Fraxinus pennsylvanica</i>	Green Ash, Red Ash	Tree	12	12	12	5	5	5	7	7	7	1	1	1	3	3	3	3	3	3	4	4	4	8	8	8	4	4	4				
<i>Hamamelis virginiana</i>	Witch-hazel	Shrub Tree																															
<i>Liriodendron tulipifera</i>	Tulip Poplar	Tree																											6				
<i>Platanus occidentalis</i>	Sycamore, Plane-tree	Tree				3	3	3				5	5	5	1	1	1	2	2	2	3	3	8			9	9	13					
<i>Populus deltoides</i>	Cottonwood	Tree				1	1	1				4	4	4	5	5	5	2	2	2									1	1	1		
<i>Rhus copallinum</i>	Sumac	Shrub Tree																		2													
<i>Salix nigra</i>	Black Willow	Tree						1																	1								
Stem count			14	14	14	12	12	17	10	10	10	12	12	14	9	9	26	13	13	15	10	10	30	15	15	17	17	17	27	8	8	8	
size (ares)			1			1			1			1			1			1			1			1			1			1			
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			
Species count			2	2	2	4	4	6	4	4	4	4	4	6	3	3	5	5	5	6	4	4	6	3	3	5	4	4	5	2	2	2	
Stems per ACRE			567	567	567	486	486	688	405	405	405	486	486	567	364	364	1052	526	526	607	405	405	1214	607	607	688	688	1093	324	324	324		

Table 7. Current Plot Data (MY1) 2018 Shadrick Creek Restoration Project																														
Scientific Name	Common Name	Species Type	Current Plot Data (MY1 2018)																											
			Plot 10			Plot 11			Plot 12			Plot 13			Plot 14			Plot 15			Plot 16			MY1 (2018)			MY0 (2017)			
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS
<i>Acer rubrum</i>	Red Maple	Tree				2	2	2	2	2	2	3	3	5	1	1	1				2	2	2	24	24	26	25	25	25	
<i>Alnus serrulata</i>	Tag Alder, Smooth Alder, Hazel Alder	Shrub Tree																												
<i>Betula nigra</i>	River Birch, Red Birch	Tree	7	7	7	2	2	2							1	1	1	1	1	1	3	3	3	21	21	30	24	24	24	
<i>Cercis canadensis</i>	Red bud	Shrub Tree				1	1	1															10	10	10	10	10	10		
<i>Diospyros virginiana</i>	American Persimmon, Possumwood	Tree																												
<i>Fraxinus pennsylvanica</i>	Green Ash, Red Ash	Tree				2	2	2	7	7	7	3	3	3	1	1	1	4	4	4	2	2	2	66	66	66	67	67	67	
<i>Hamamelis virginiana</i>	Witch-hazel	Shrub Tree										1	1	1	2	2	2	2	2	2	1	1	1	6	6	6	8	8	8	
<i>Liriodendron tulipifera</i>	Tulip Poplar	Tree																												
<i>Platanus occidentalis</i>	Sycamore, Plane-tree	Tree							2	2	2	2	2	6	3	3	3	1	1	1	2	2	2	33	33	46	36	36	36	
<i>Populus deltoides</i>	Cottonwood	Tree	1	1	1	4	4	4				2	2	2	3	3	3	3	3	3	2	2	2	27	27	27	28	28	28	
<i>Rhus copallinum</i>	Sumac	Shrub Tree																												
<i>Salix nigra</i>	Black Willow	Tree																												
Stem count			8	8	8	11	11	11	11	11	11	11	11	17	11	11	11	11	11	16	12	12	12	187	187	256	198	198	198	
size (ares)			1			1			1			1			1			1			1			16			3			
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.32			0.32			
Species count			2	2	2	5	5	5	3	3	3	5	5	5	6	6	6	5	5	8	6	6	6	7	7	12	7	7	7	
Stems per ACRE			324	324	324	445	445	445	445	445	445	445	445	688	445	445	445	445	445	647	486	486	486	584	584	800	619	619	619	

P=Planted, T=Planted & Volunteer

Color for Density

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%

This Page Intentionally Left Blank

Table 8. Vegetation Plot Criteria Attainment Shadrick Creek Restoration Project		
Vegetation Plot ID	Vegetation Survival Threshold Met?	Tract Mean
1	Yes	100%
2	Yes	
3	Yes	
4	Yes	
5	Yes	
6	Yes	
7	Yes	
8	Yes	
9	Yes	
10	Yes	
11	Yes	
12	Yes	
13	Yes	
14	Yes	
15	Yes	
16	Yes	


Table 9. CVS Vegetation Plot Metadata Shadrick Creek Restoration Site	
Report Prepared By	Drew Alderman
Date Prepared	9/27/2018 10:54
database name	DMS_ShadrickCreek_92916_MY1.mdb
database location	Z:\ES\NRI&M\EEP Monitoring\Shadrick Creek\MY1 - 2018\Data\Veg
computer name	FIELD-PC
file size	72011776
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Proj, planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Proj, total stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY-----	
Project Code	92916
project Name	Shadrick Creek
Description	Stream Restoration Project
River Basin	
length(ft)	
stream-to-edge width (ft)	
area (sq m)	
Required Plots (calculated)	
Sampled Plots	16

Appendix D
Stream Measurement and Geomorphology Data

Project Name: Shadrick Creek
Reach Name: UT1

XS Number: 1
XS Type: Pool

Station: 16+05

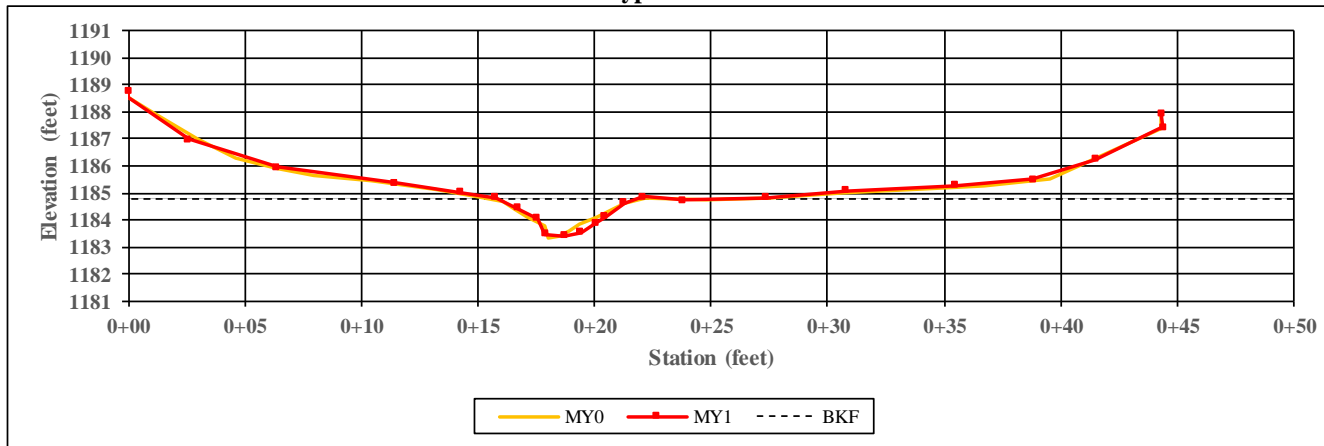

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	7.1	6.1	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.6	0.7	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.5	1.4	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	4.5	4.5	-	-	-	-	-	-
Width/Depth Ratio	11.1	8.3	-	-	-	-	-	-
Entrenchment Ratio	3.4	3.9	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.4						



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT1

XS Number: 2
XS Type: Riffle

Station: 16+29

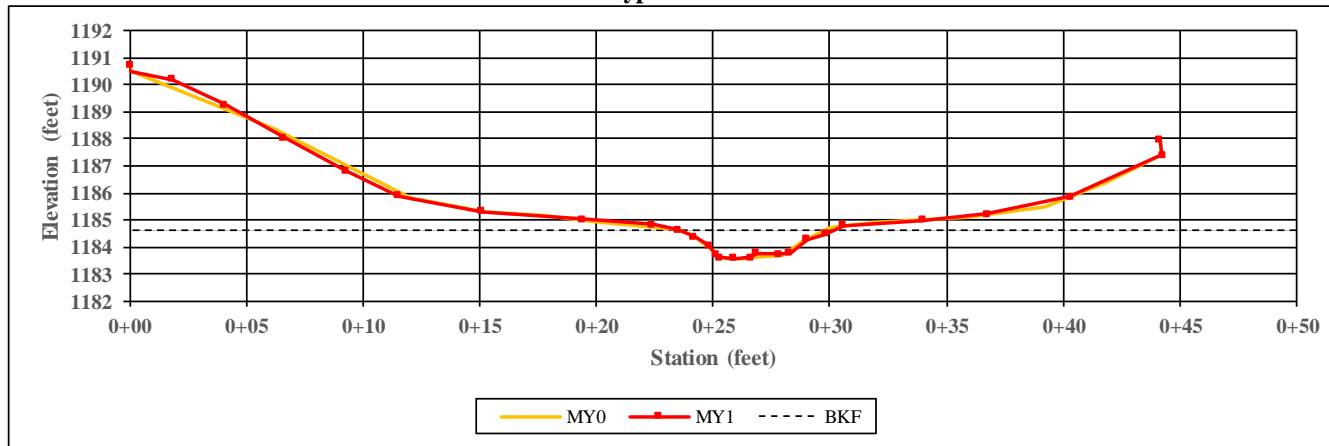

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	6.3	6.7	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.7	0.6	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.1	1.1	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	4.3	4.3	-	-	-	-	-	-
Width/Depth Ratio	9.4	10.4	-	-	-	-	-	-
Entrenchment Ratio	3.8	3.6	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.1	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank


Project Name: Shadrick Creek
Reach Name: UT1

XS Number: 3
XS Type: Riffle

Station: 21+68

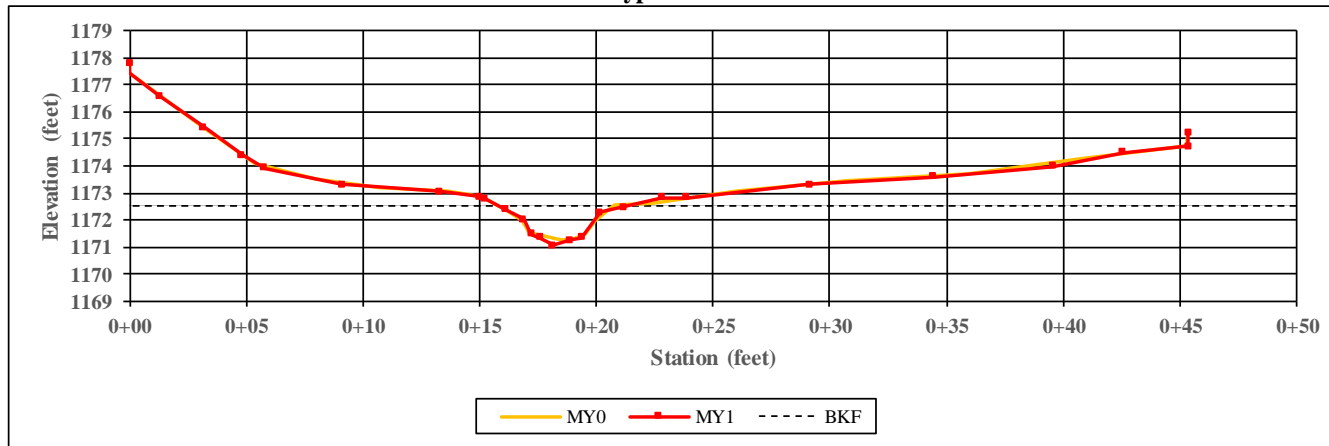

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	5.0	5.6	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.8	0.7	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.3	1.4	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	3.9	3.9	-	-	-	-	-	-
Width/Depth Ratio	6.5	7.9	-	-	-	-	-	-
Entrenchment Ratio	4.8	4.3	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.4	-	-	-	-	-	-

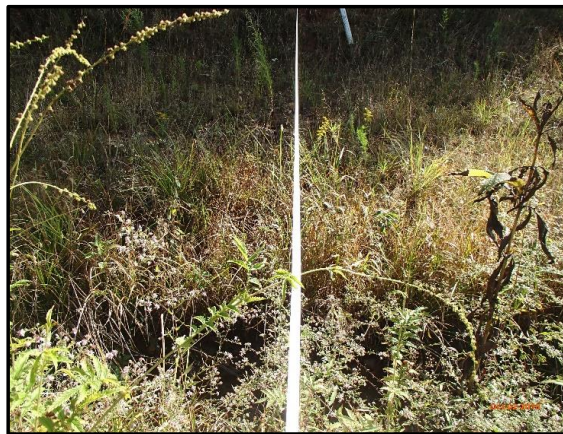

Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 1

XS Number: 4
XS Type: Riffle

Station: 26+02

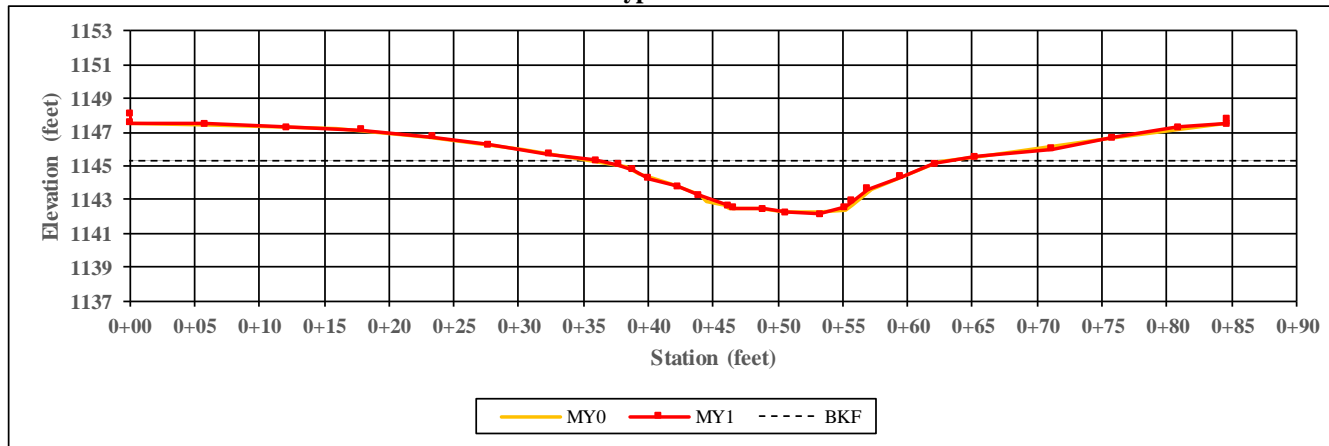

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	26.6	25.9	-	-	-	-	-	-
Floodprone Width (ft)	100.0	100.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	1.8	1.8	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.0	3.1	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	47.0	47.0	-	-	-	-	-	-
Width/Depth Ratio	15.0	14.2	-	-	-	-	-	-
Entrenchment Ratio	3.8	3.9	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	3.0	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 1

XS Number: 5
XS Type: Pool

Station: 26+87

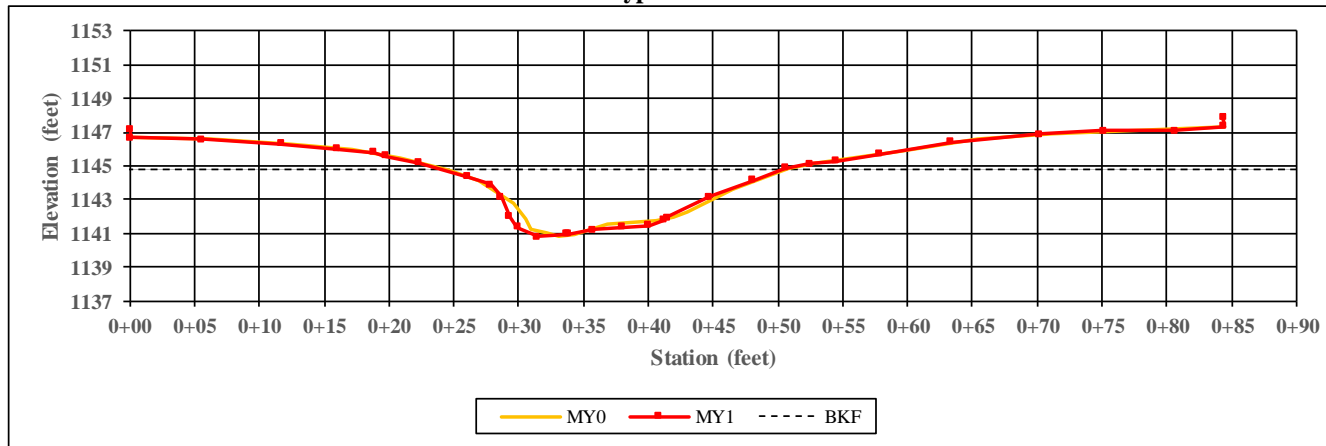

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	26.9	26.4	-	-	-	-	-	-
Floodprone Width (ft)	100.0	100.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.2	2.3	-	-	-	-	-	-
Bankfull Max Depth (ft)	4.0	4.0	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	59.5	59.5	-	-	-	-	-	-
Width/Depth Ratio	12.1	11.7	-	-	-	-	-	-
Entrenchment Ratio	3.7	3.8	-	-	-	-	-	-
Bank Height Ratio	1.0	1.1	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	4.3	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 1

XS Number: 6
XS Type: Riffle

Station: 30+44

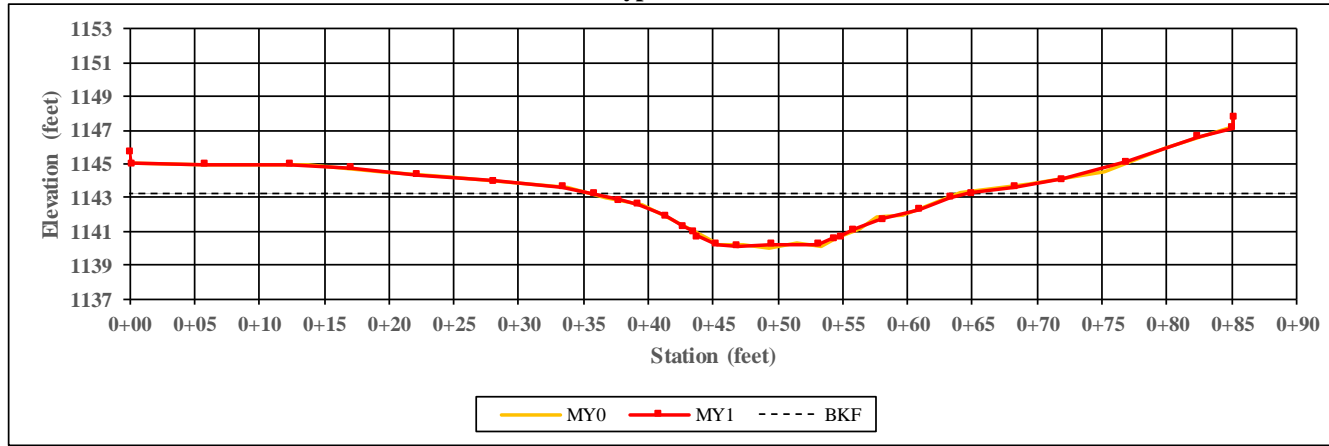

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	28.7	29.1	-	-	-	-	-	-
Floodprone Width (ft)	100.0	100.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	1.8	1.8	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.2	3.1	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	52.0	52.0	-	-	-	-	-	-
Width/Depth Ratio	15.8	16.3	-	-	-	-	-	-
Entrenchment Ratio	3.5	3.4	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	3.1	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 1

XS Number: 7
XS Type: Riffle

Station: 34+64

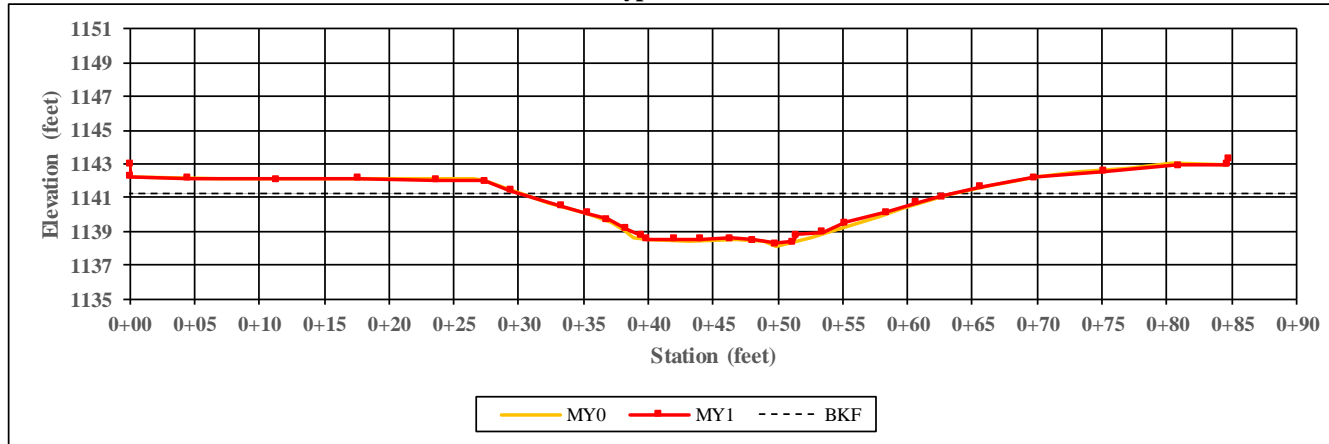

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	32.7	33.6	-	-	-	-	-	-
Floodprone Width (ft)	100.0	100.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	1.8	1.8	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.0	3.0	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	59.3	59.3	-	-	-	-	-	-
Width/Depth Ratio	18.0	19.0	-	-	-	-	-	-
Entrenchment Ratio	3.1	3.0	-	-	-	-	-	-
Bank Height Ratio	1.0	0.9	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	2.8	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 1

XS Number: 8
XS Type: Pool

Station: 37+68

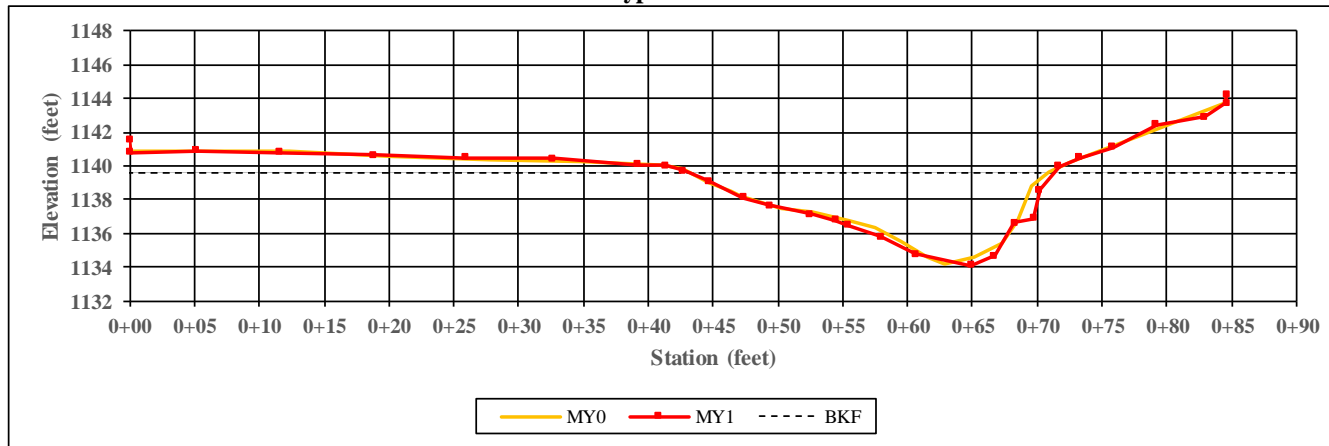

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	28.8	28.2	-	-	-	-	-	-
Floodprone Width (ft)	100.0	100.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.9	3.0	-	-	-	-	-	-
Bankfull Max Depth (ft)	5.6	5.5	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	84.3	84.3	-	-	-	-	-	-
Width/Depth Ratio	9.8	9.4	-	-	-	-	-	-
Entrenchment Ratio	3.5	3.5	-	-	-	-	-	-
Bank Height Ratio	1.0	1.1	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	5.9	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT9 Reach 1

XS Number: 9
XS Type: Riffle

Station: 16+53

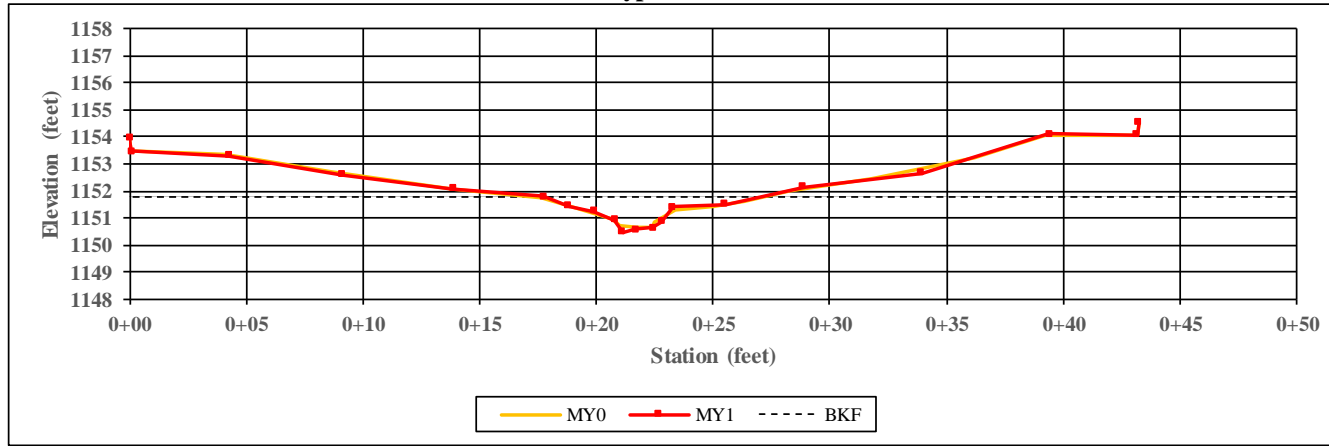

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	9.5	9.2	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.5	0.5	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.1	1.3	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	4.8	4.8	-	-	-	-	-	-
Width/Depth Ratio	18.7	17.6	-	-	-	-	-	-
Entrenchment Ratio	2.5	2.6	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.3	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT9 Reach 1

XS Number: 10
XS Type: Pool

Station: 16+68

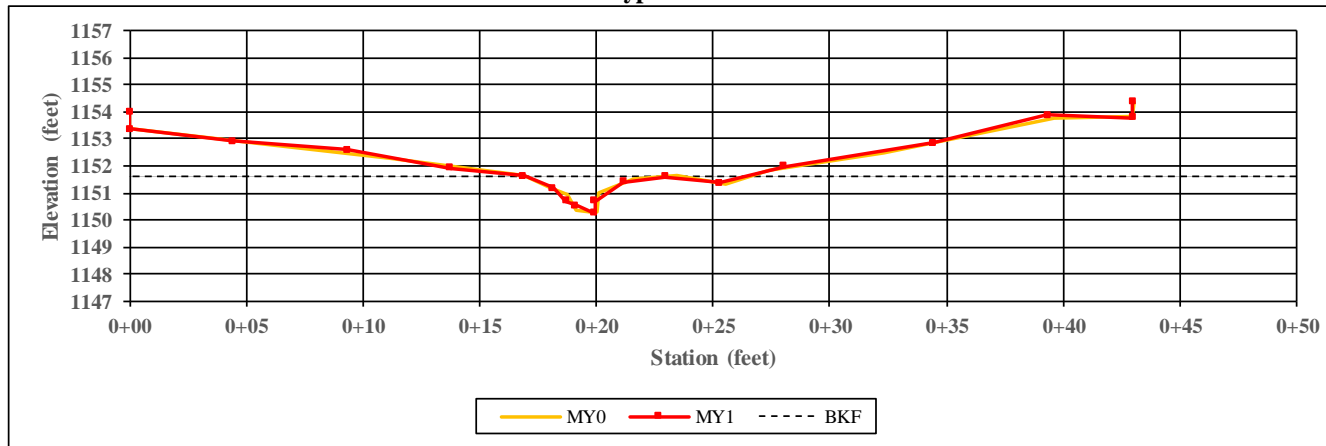

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	6.5	6.1	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.5	0.5	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.3	1.4	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	3.0	3.0	-	-	-	-	-	-
Width/Depth Ratio	14.3	12.1	-	-	-	-	-	-
Entrenchment Ratio	3.7	4.0	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.4	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT9 Reach 2

XS Number: 11
XS Type: Pool

Station: 21+34

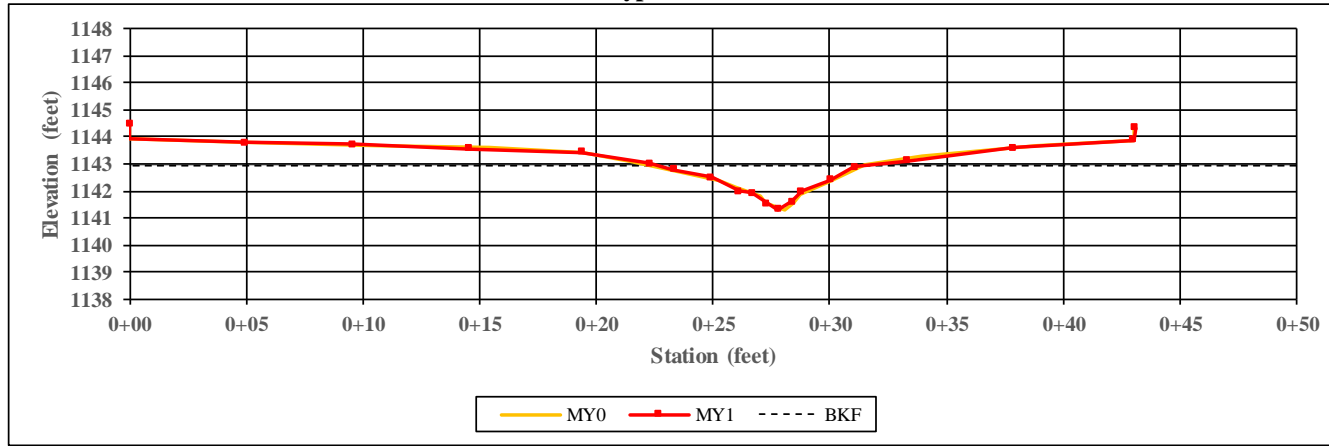

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	8.8	8.6	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.7	0.7	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.6	1.6	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	5.8	5.8	-	-	-	-	-	-
Width/Depth Ratio	13.2	12.8	-	-	-	-	-	-
Entrenchment Ratio	2.7	2.8	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.6	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT9 Reach 2

XS Number: 12
XS Type: Riffle

Station: 21+49

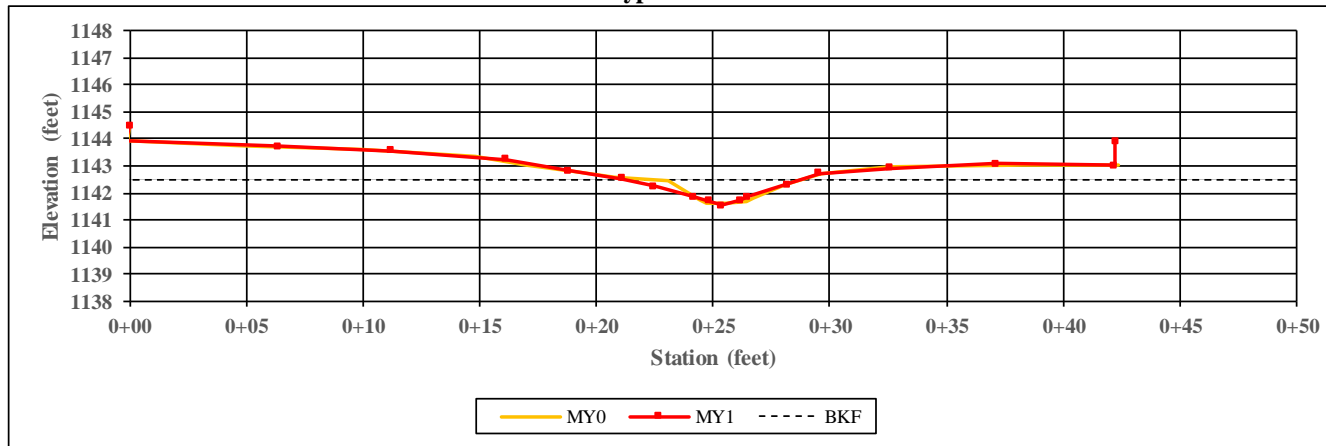

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	8.3	7.7	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.4	0.5	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.0	1.0	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	3.6	3.6	-	-	-	-	-	-
Width/Depth Ratio	19.0	16.2	-	-	-	-	-	-
Entrenchment Ratio	2.9	3.1	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.0	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT10

XS Number: 13
XS Type: Riffle

Station: 13+00

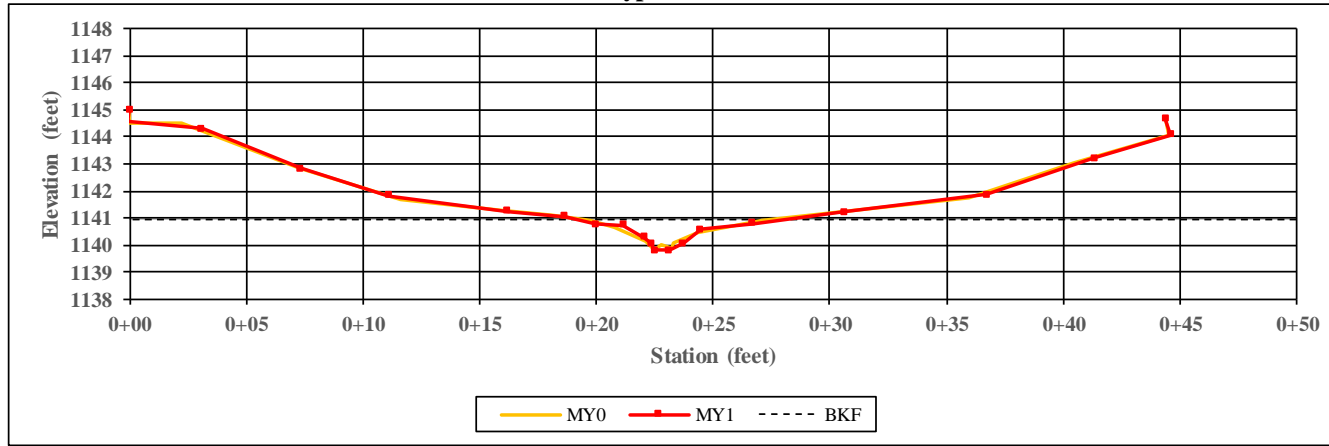

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	7.3	8.7	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.5	0.4	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.1	1.1	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	3.4	3.4	-	-	-	-	-	-
Width/Depth Ratio	15.6	22.3	-	-	-	-	-	-
Entrenchment Ratio	3.3	2.8	-	-	-	-	-	-
Bank Height Ratio	1.0	0.9	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.0	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: UT10

XS Number: 14
XS Type: Pool

Station: 13+13

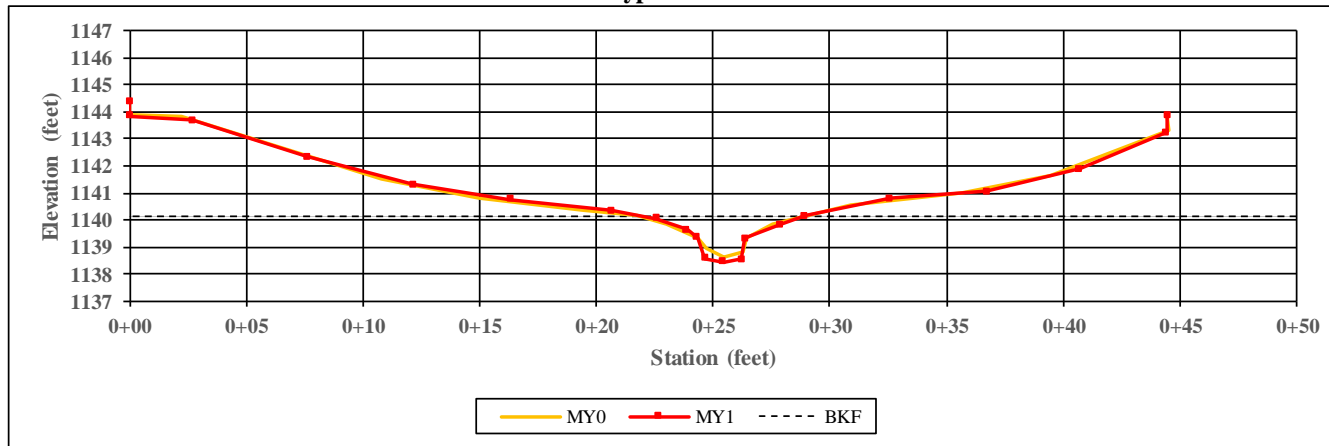

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	7.5	6.9	-	-	-	-	-	-
Floodprone Width (ft)	24.0	24.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	0.6	0.7	-	-	-	-	-	-
Bankfull Max Depth (ft)	1.6	1.7	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	4.8	4.8	-	-	-	-	-	-
Width/Depth Ratio	11.6	9.9	-	-	-	-	-	-
Entrenchment Ratio	3.2	3.5	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	1.6	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 2

XS Number: 15
XS Type: Pool

Station: 103+19

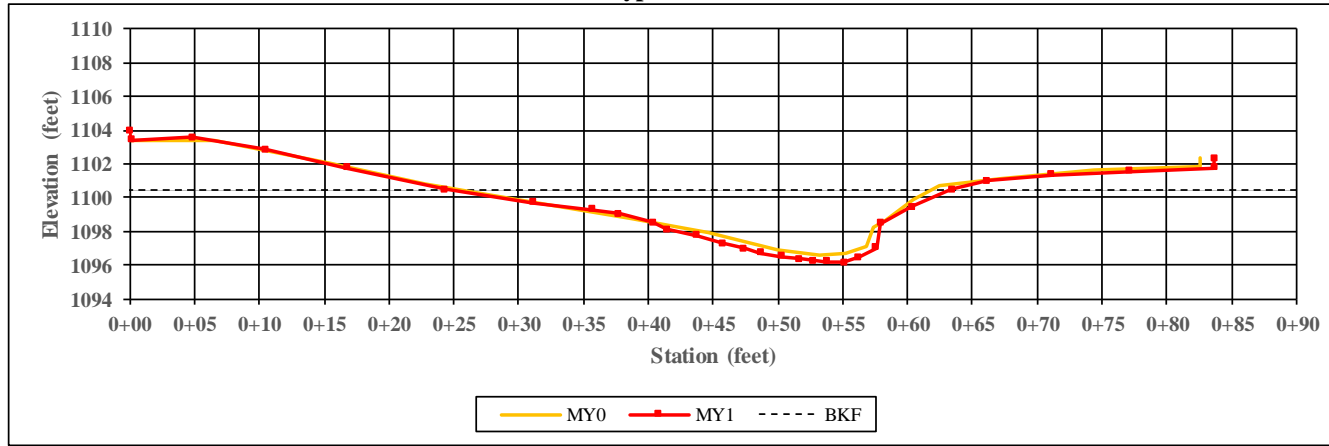

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	38.9	38.8	-	-	-	-	-	-
Floodprone Width (ft)	116.0	116.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.1	2.1	-	-	-	-	-	-
Bankfull Max Depth (ft)	4.1	4.3	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	80.4	80.4	-	-	-	-	-	-
Width/Depth Ratio	18.9	18.7	-	-	-	-	-	-
Entrenchment Ratio	3.0	3.0	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	4.4	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 2

XS Number: 16
XS Type: Riffle

Station: 104+67

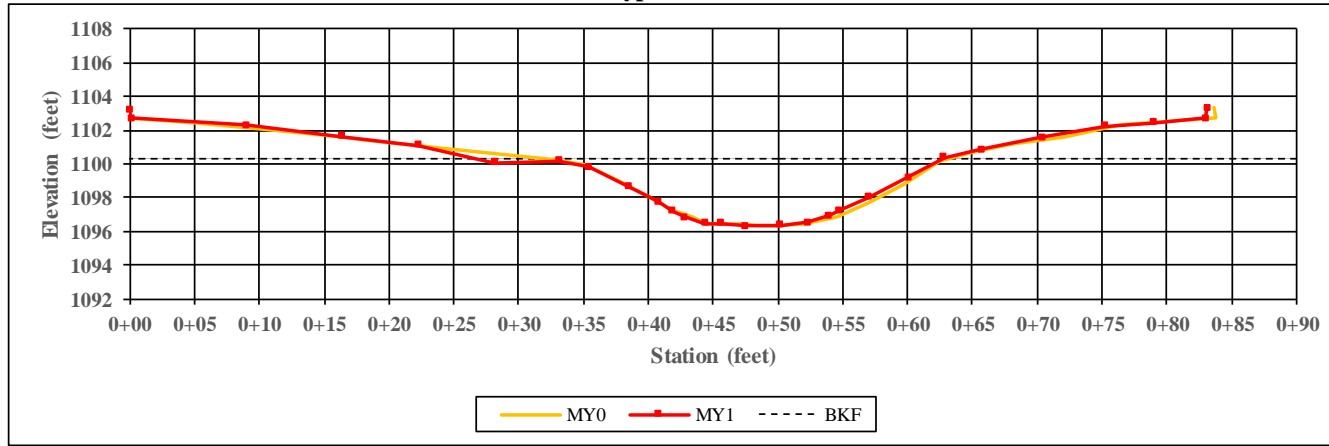

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	29.9	29.5	-	-	-	-	-	-
Floodprone Width (ft)	116.0	116.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.4	2.4	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.9	4.0	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	71.7	71.7	-	-	-	-	-	-
Width/Depth Ratio	12.5	12.1	-	-	-	-	-	-
Entrenchment Ratio	3.9	3.9	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	3.9	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 3

XS Number: 17
XS Type: Riffle

Station: 109+18

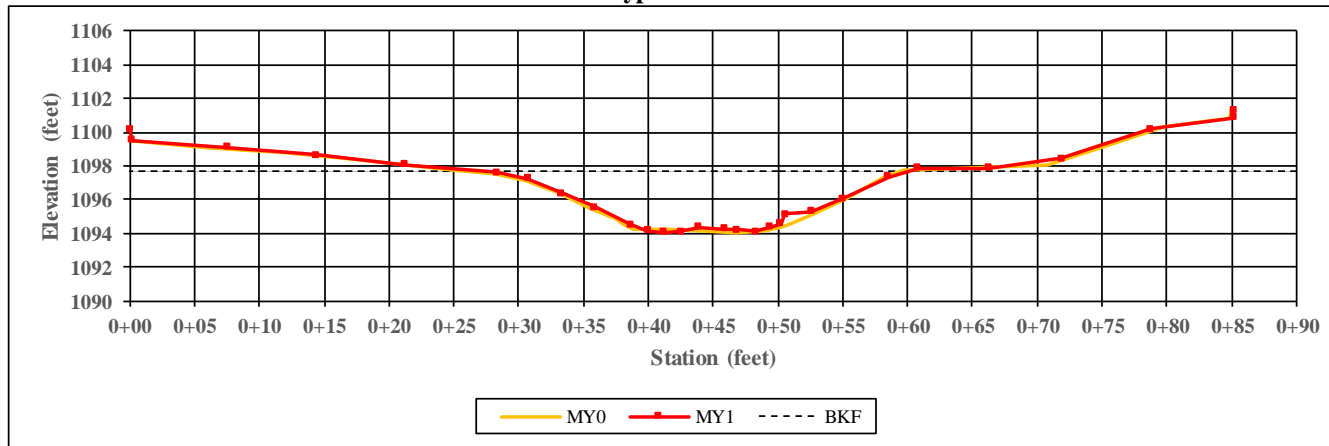

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	31.1	32.7	-	-	-	-	-	-
Floodprone Width (ft)	116.0	116.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.2	2.1	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.5	3.6	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	68.6	68.6	-	-	-	-	-	-
Width/Depth Ratio	14.1	15.6	-	-	-	-	-	-
Entrenchment Ratio	3.7	3.5	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	3.5	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 3

XS Number: 18
XS Type: Pool

Station: 111+27

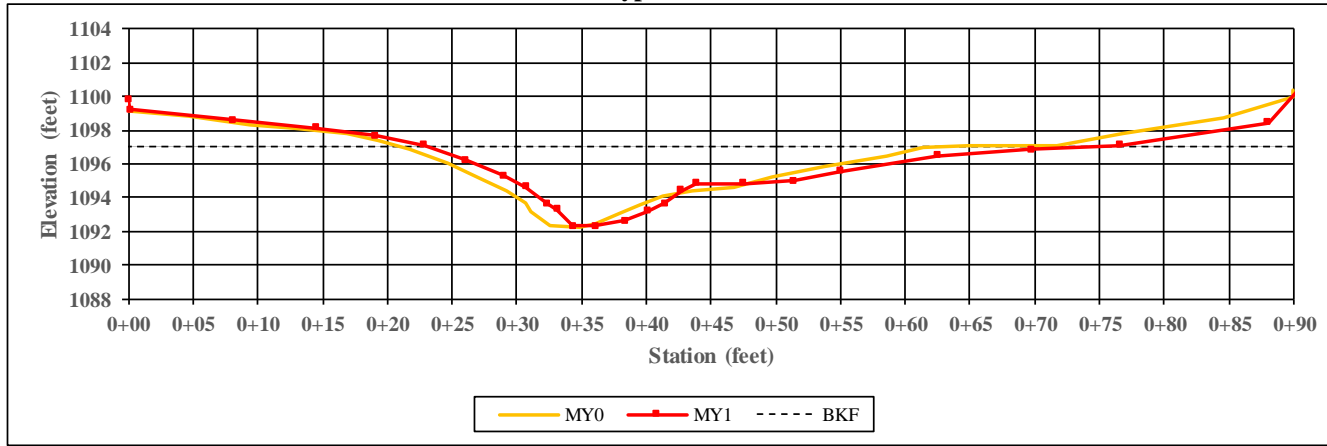

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	40.0	43.7	-	-	-	-	-	-
Floodprone Width (ft)	116.0	116.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.2	2.0	-	-	-	-	-	-
Bankfull Max Depth (ft)	4.7	4.7	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	88.1	88.1	-	-	-	-	-	-
Width/Depth Ratio	18.2	21.6	-	-	-	-	-	-
Entrenchment Ratio	2.9	2.7	-	-	-	-	-	-
Bank Height Ratio	1.0	0.9	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	4.2	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank

Project Name: Shadrick Creek
Reach Name: Shadrick Reach 3

XS Number: 19
XS Type: Riffle

Station: 114+53

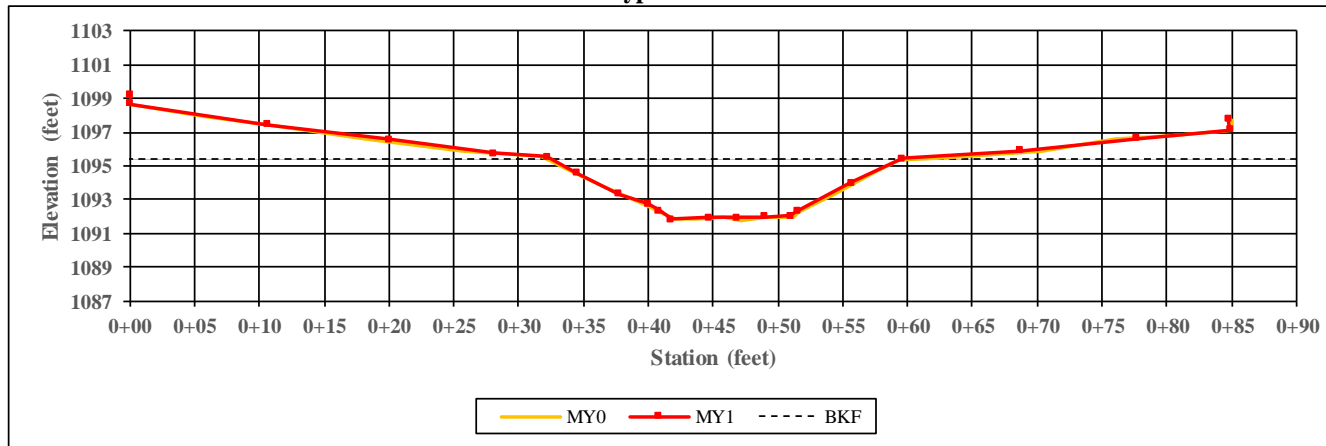

CHANNEL DIMENSIONS SUMMARY	MY0	MY1	MY2	MY3	MY4	MY5	MY6	MY7
Bankful Width (ft)	26.9	26.9	-	-	-	-	-	-
Floodprone Width (ft)	116.0	116.0	-	-	-	-	-	-
Bankfull Mean Depth (ft)	2.3	2.3	-	-	-	-	-	-
Bankfull Max Depth (ft)	3.5	3.5	-	-	-	-	-	-
Bankfull Cross-Sectional Area (ft ²)	61.0	61.0	-	-	-	-	-	-
Width/Depth Ratio	11.9	11.8	-	-	-	-	-	-
Entrenchment Ratio	4.3	4.3	-	-	-	-	-	-
Bank Height Ratio	1.0	1.0	-	-	-	-	-	-
Low Top of Bank Depth (ft)	-	3.6	-	-	-	-	-	-



Left Descending Bank




Right Descending Bank



**Shadrick Creek - Shadrick Reach 3
Longitudinal Profile
Staioning 106+23 to 117+27**





**Shadrick Creek - UT9
Longitudinal Profile
Staioning 19+59 to 22+08**

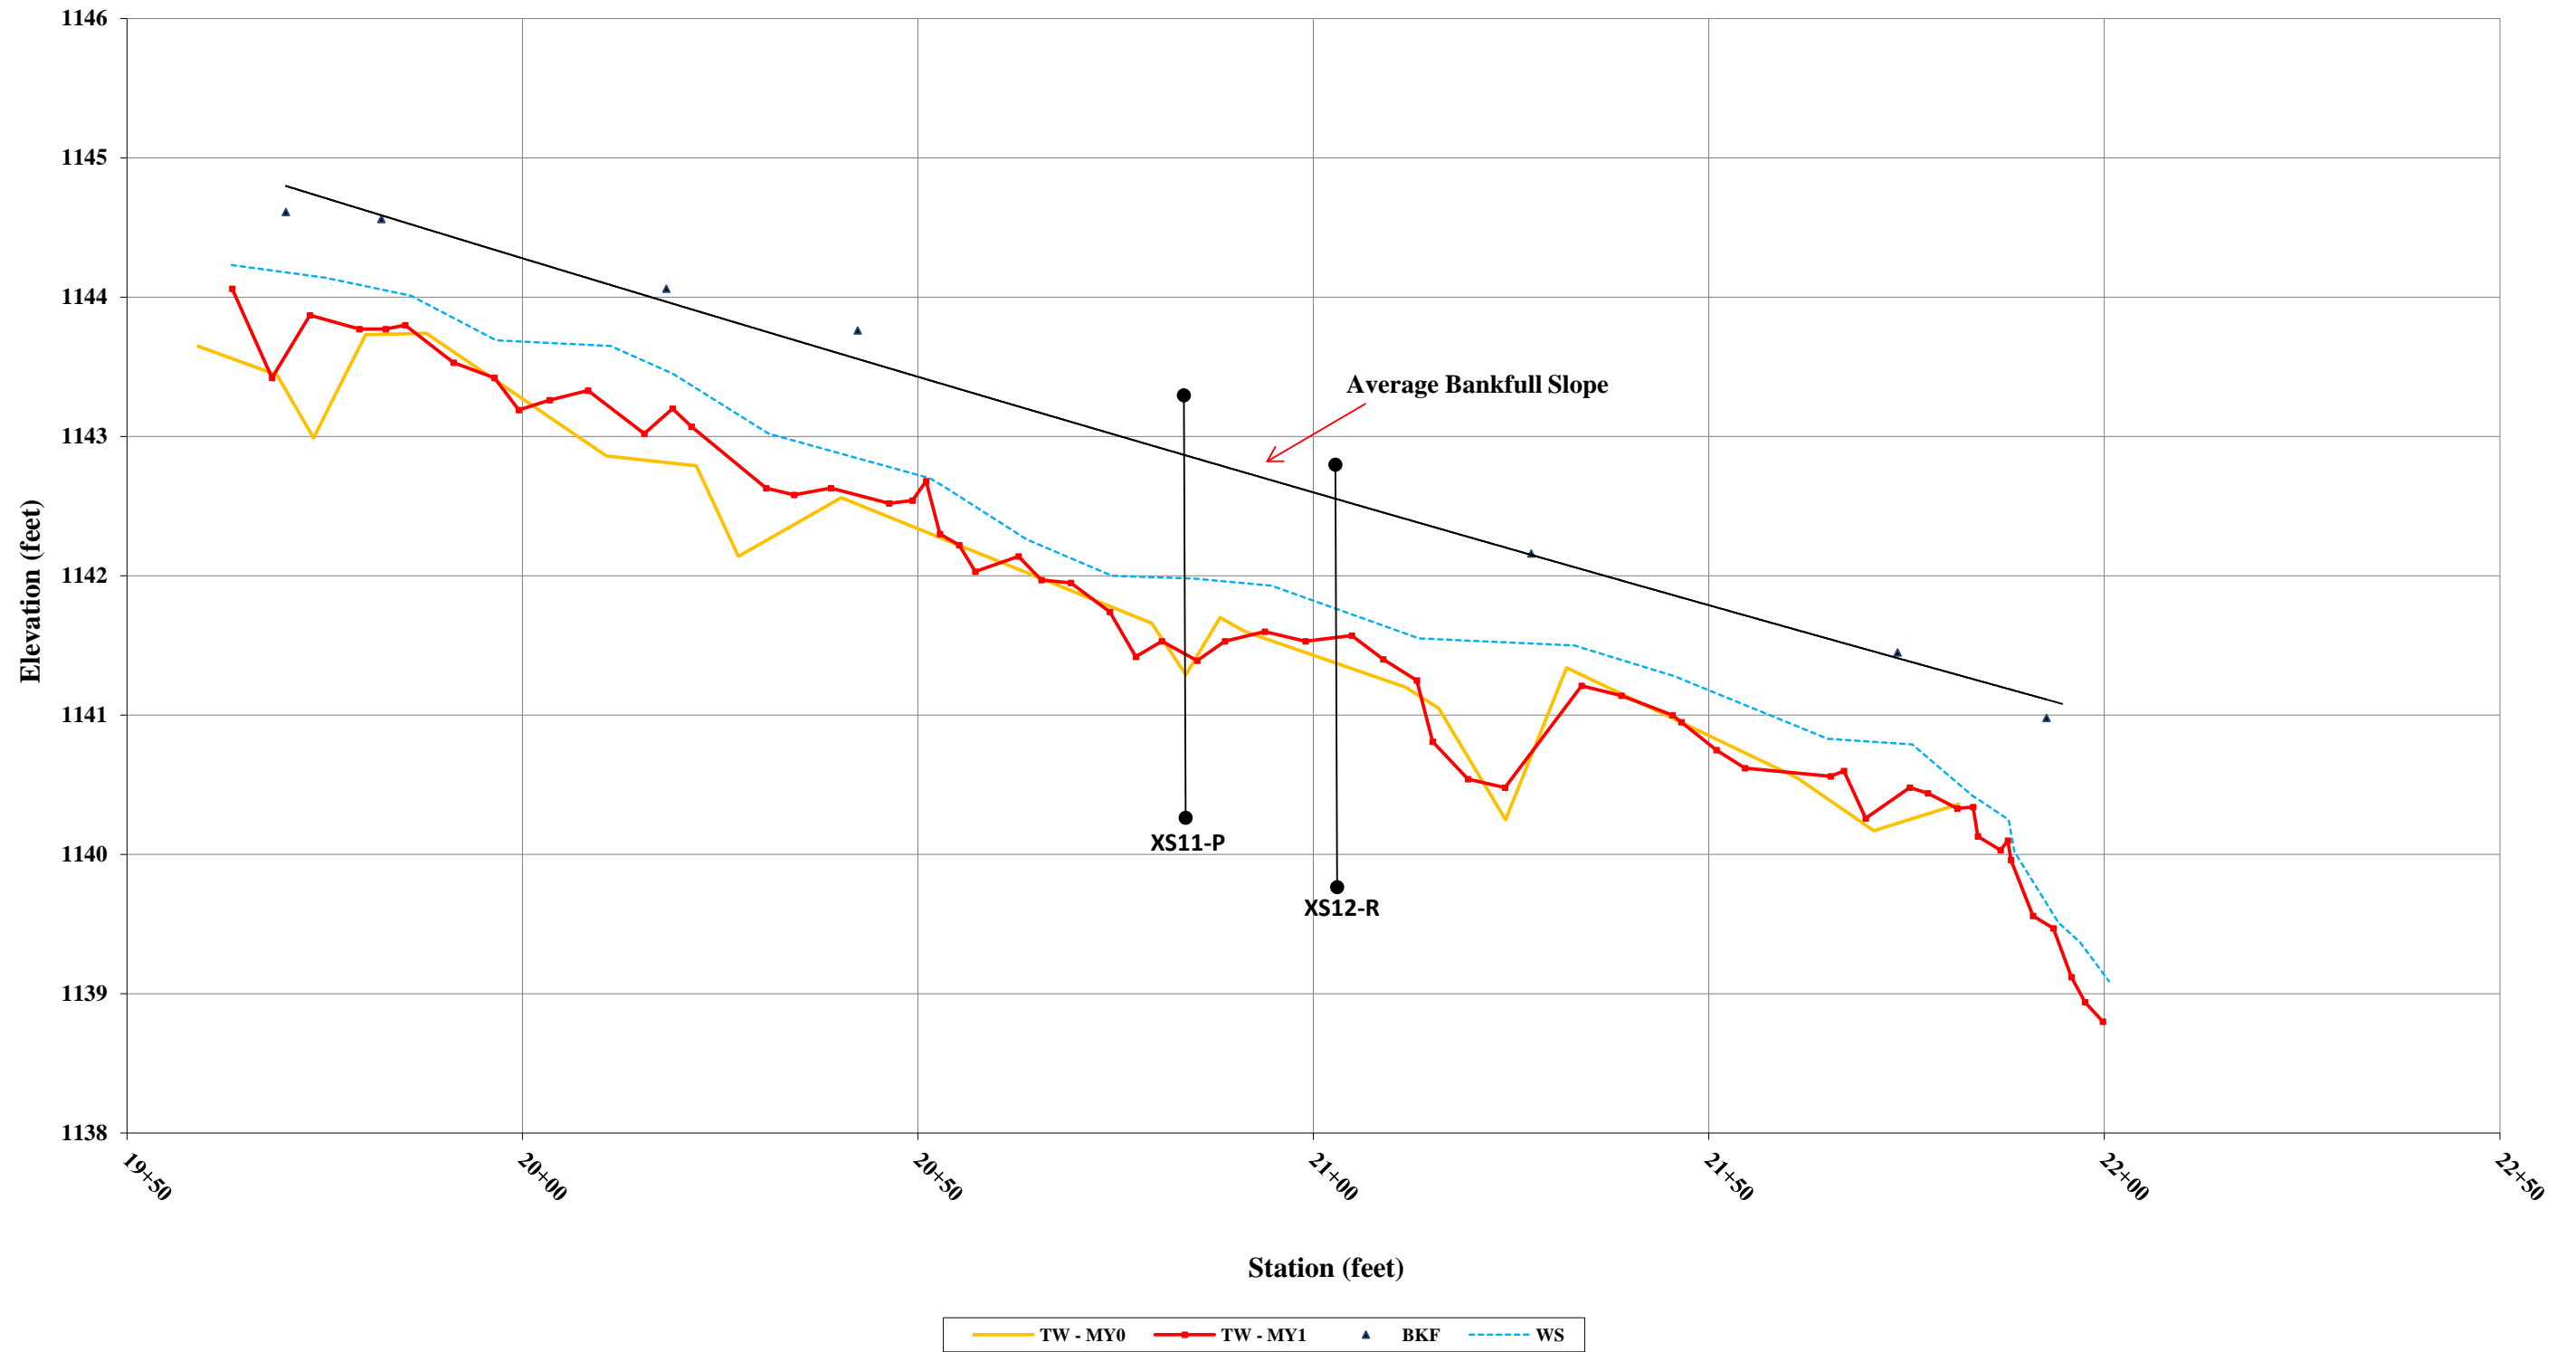



Shadrick Creek Reach 1			
Cross Section 4 - Riffle			
Monitoring Year - 2018; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	0	0.0%	0%
0.062 - 0.125	0	0.0%	0%
0.125 - 0.25	0	0.0%	0%
0.25 - 0.5	0	0.0%	0%
0.5 - 1.0	0	0.0%	0%
1 - 2	5	4.7%	5%
2 - 4	0	0.0%	5%
4 - 8	7	6.5%	11%
8 - 16	12	11.2%	22%
16 - 32	33	30.8%	53%
32 - 64	33	30.8%	84%
64-128	12	11.2%	95%
128-256	4	3.7%	99%
256-512	1	0.9%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	107	100%	100%
		Summary Data	
		D50	30
		D84	64
		D95	120

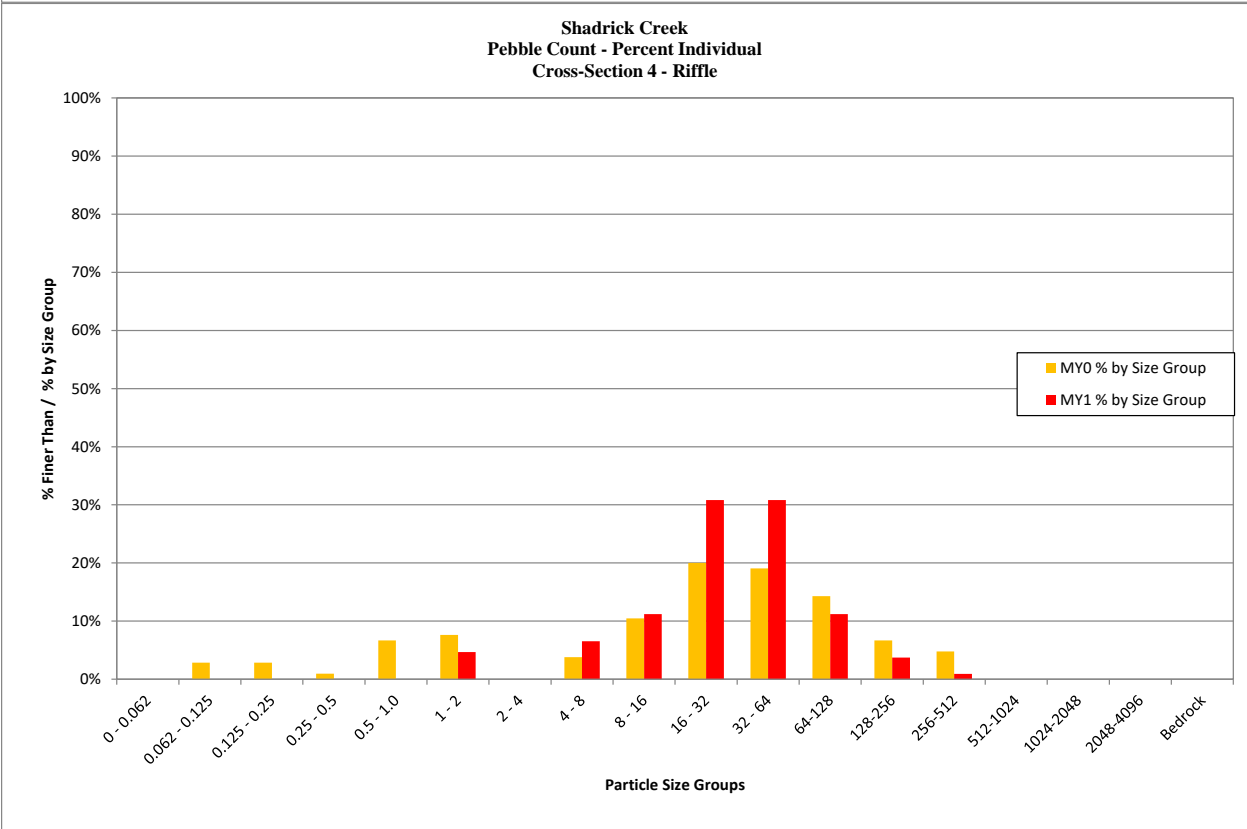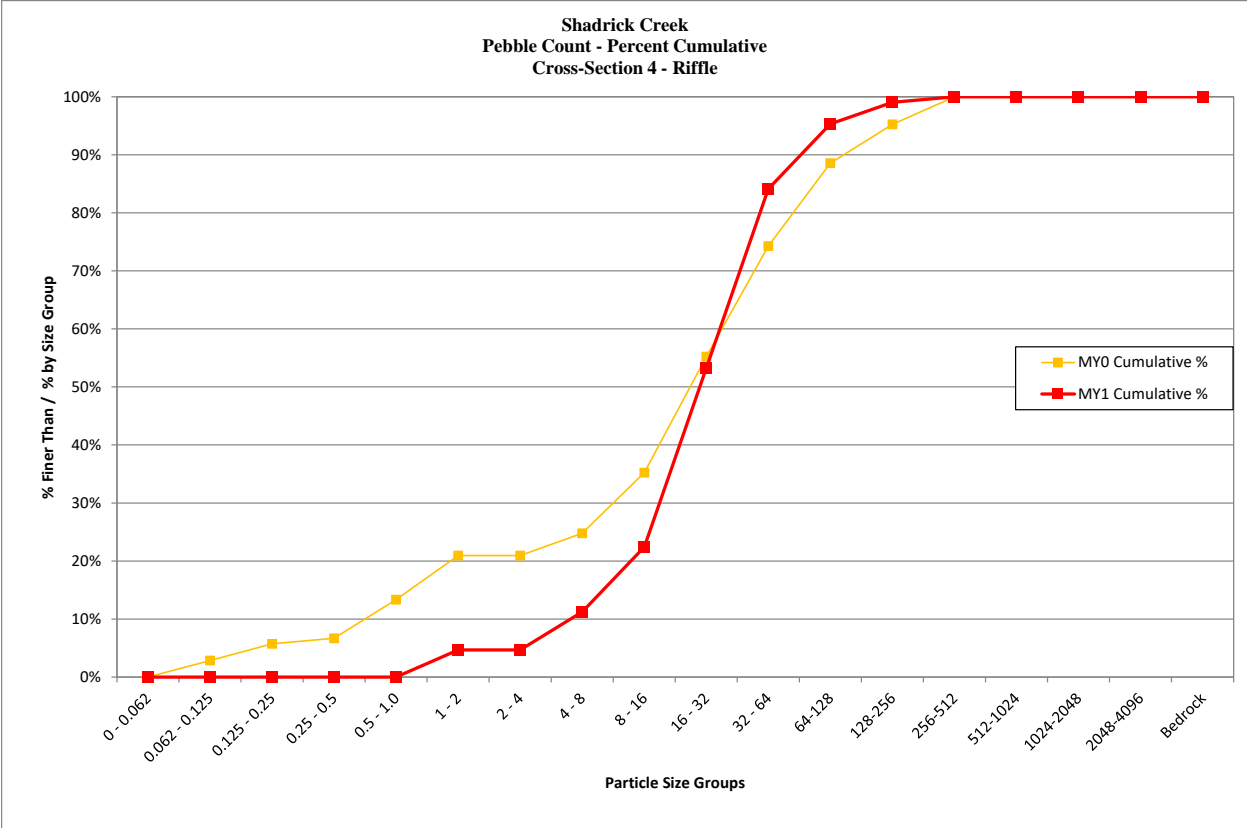



Shadrick Creek Reach 1			
Cross Section 6 - Riffle			
Monitoring Year - 2018; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	0	0.0%	0%
0.062 - 0.125	0	0.0%	0%
0.125 - 0.25	0	0.0%	0%
0.25 - 0.5	0	0.0%	0%
0.5 - 1.0	2	1.9%	2%
1 - 2	4	3.7%	6%
2 - 4	1	0.9%	7%
4 - 8	9	8.4%	15%
8 - 16	21	19.6%	35%
16 - 32	16	15.0%	50%
32 - 64	29	27.1%	77%
64-128	20	18.7%	95%
128-256	5	4.7%	100%
256-512	0	0.0%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	107	100%	100%
		Summary Data	
		D50	32
		D84	86
		D95	130

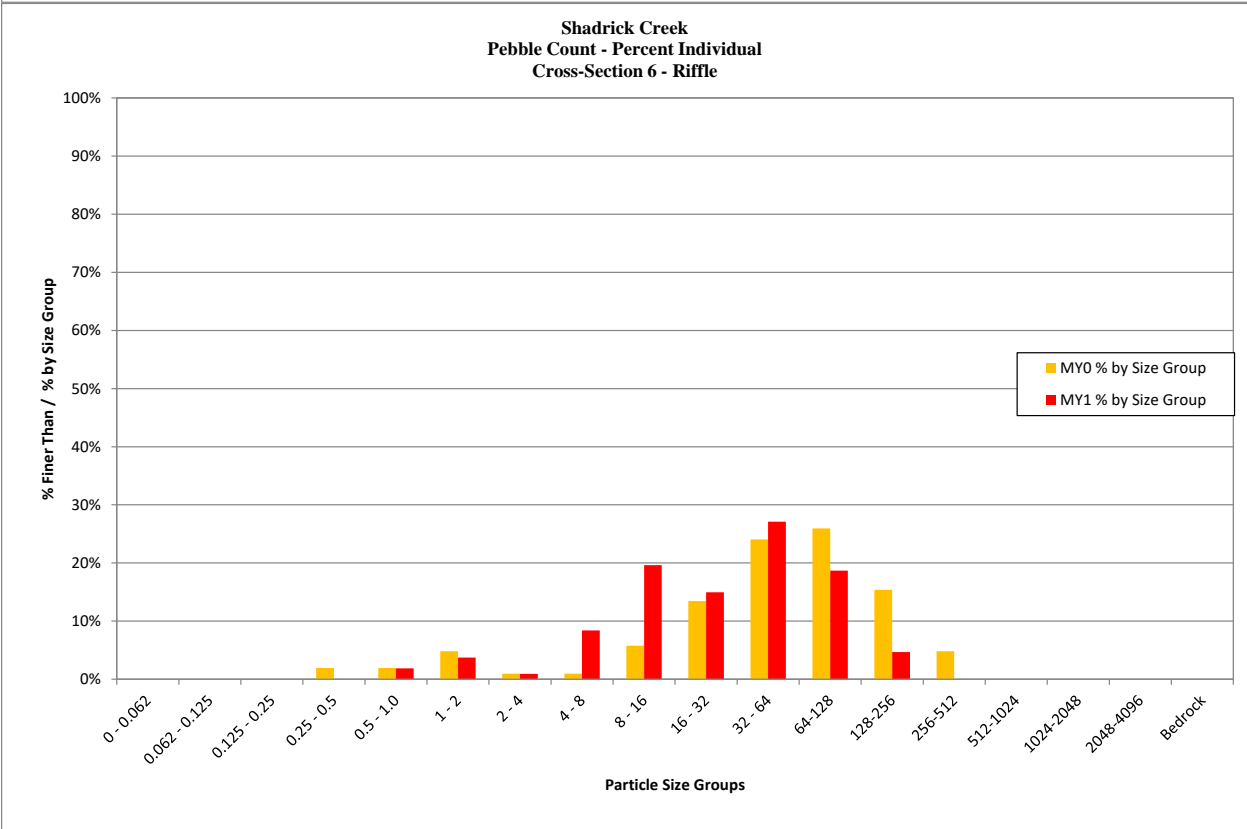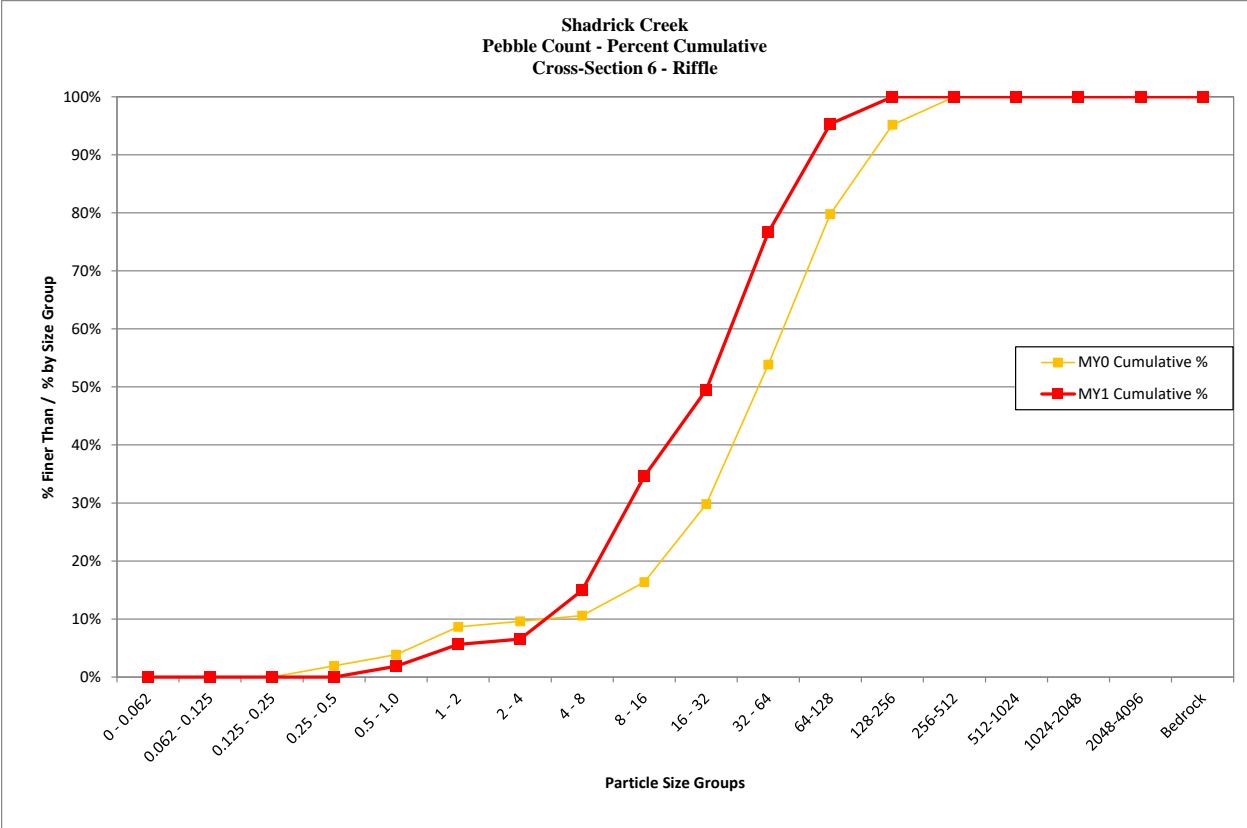



Shadrick Creek Reach 1			
Cross Section 7 - Riffle			
Monitoring Year - 2018; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	0	0.0%	0%
0.062 - 0.125	0	0.0%	0%
0.125 - 0.25	0	0.0%	0%
0.25 - 0.5	0	0.0%	0%
0.5 - 1.0	0	0.0%	0%
1 - 2	1	0.9%	1%
2 - 4	0	0.0%	1%
4 - 8	4	3.8%	5%
8 - 16	27	25.5%	30%
16 - 32	47	44.3%	75%
32 - 64	25	23.6%	98%
64-128	2	1.9%	100%
128-256	0	0.0%	100%
256-512	0	0.0%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	106	100%	100%
Summary Data			
D50		24	
D84		40	
D95		57	

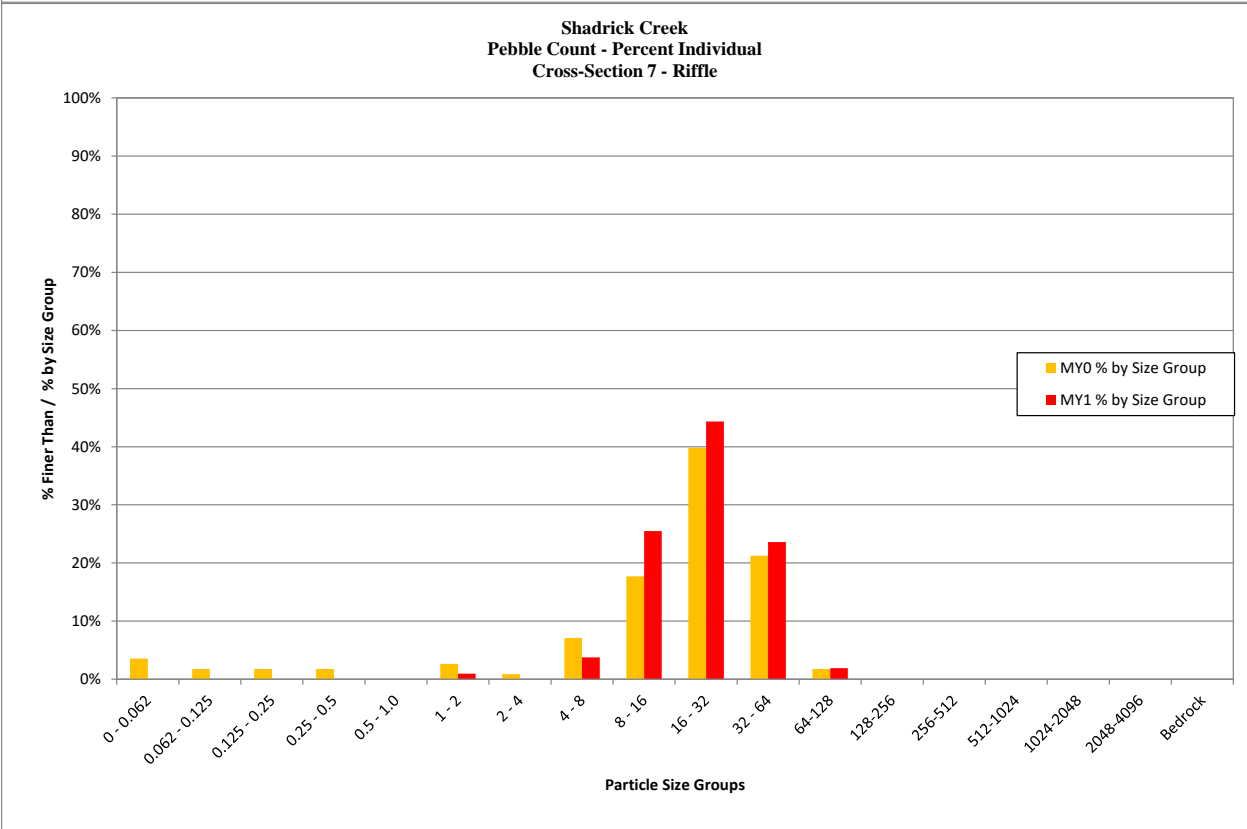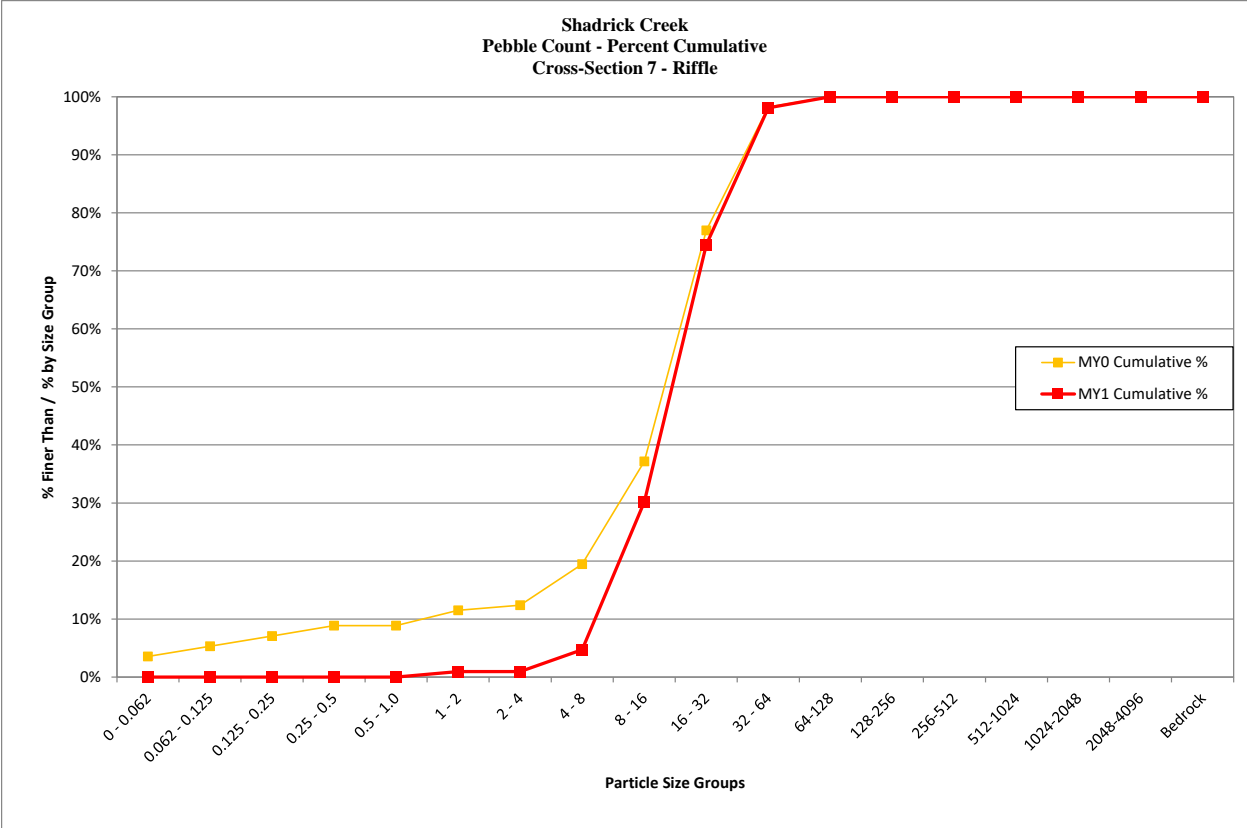

Shadrick Creek UT-9 Reach 2			
Cross Section 12 - Riffle			
Monitoring Year - 2012; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	105	100.0%	100%
0.062 - 0.125	0	0.0%	100%
0.125 - 0.25	0	0.0%	100%
0.25 - 0.5	0	0.0%	100%
0.5 - 1.0	0	0.0%	100%
1 - 2	0	0.0%	100%
2 - 4	0	0.0%	100%
4 - 8	0	0.0%	100%
8 - 16	0	0.0%	100%
16 - 32	0	0.0%	100%
32 - 64	0	0.0%	100%
64-128	0	0.0%	100%
128-256	0	0.0%	100%
256-512	0	0.0%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	105	100%	100%
Summary Data			
D50		0.062	
D84		0.062	
D95		0.062	

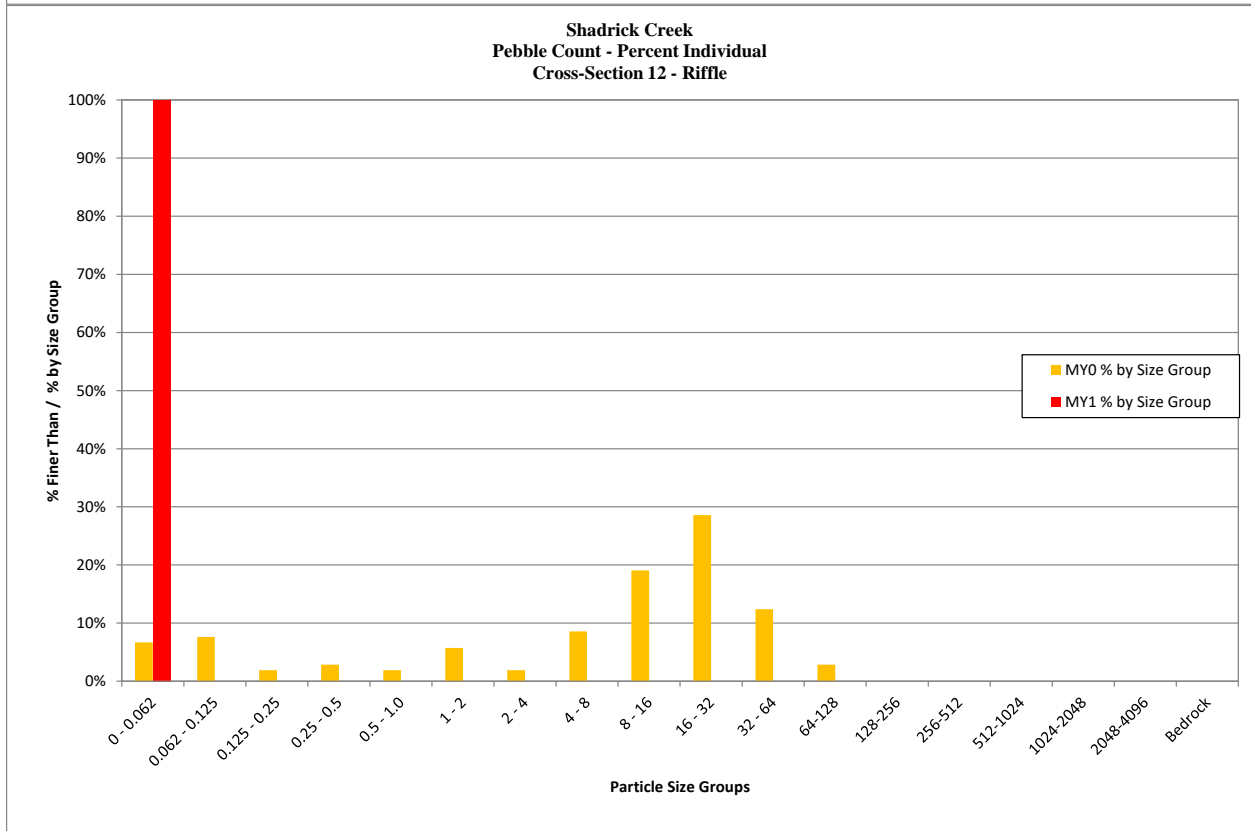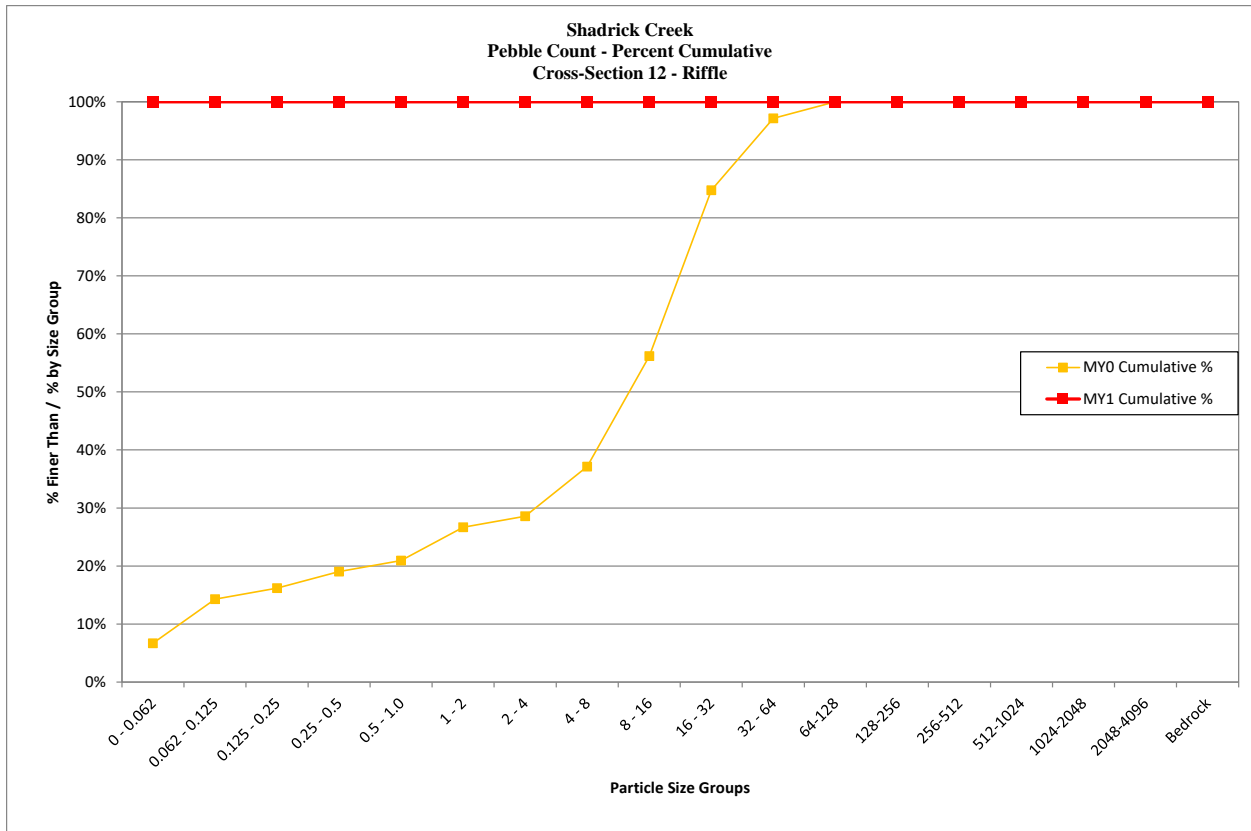

Shadrick Creek Reach 3			
Cross Section 17 - Riffle			
Monitoring Year - 2018; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	0	0.0%	0%
0.062 - 0.125	0	0.0%	0%
0.125 - 0.25	0	0.0%	0%
0.25 - 0.5	0	0.0%	0%
0.5 - 1.0	0	0.0%	0%
1 - 2	0	0.0%	0%
2 - 4	1	1.0%	1%
4 - 8	8	7.6%	9%
8 - 16	19	18.1%	27%
16 - 32	35	33.3%	60%
32 - 64	24	22.9%	83%
64-128	18	17.1%	100%
128-256	0	0.0%	100%
256-512	0	0.0%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	105	100%	100%
		Summary Data	
		D50	27
		D84	66
		D95	94

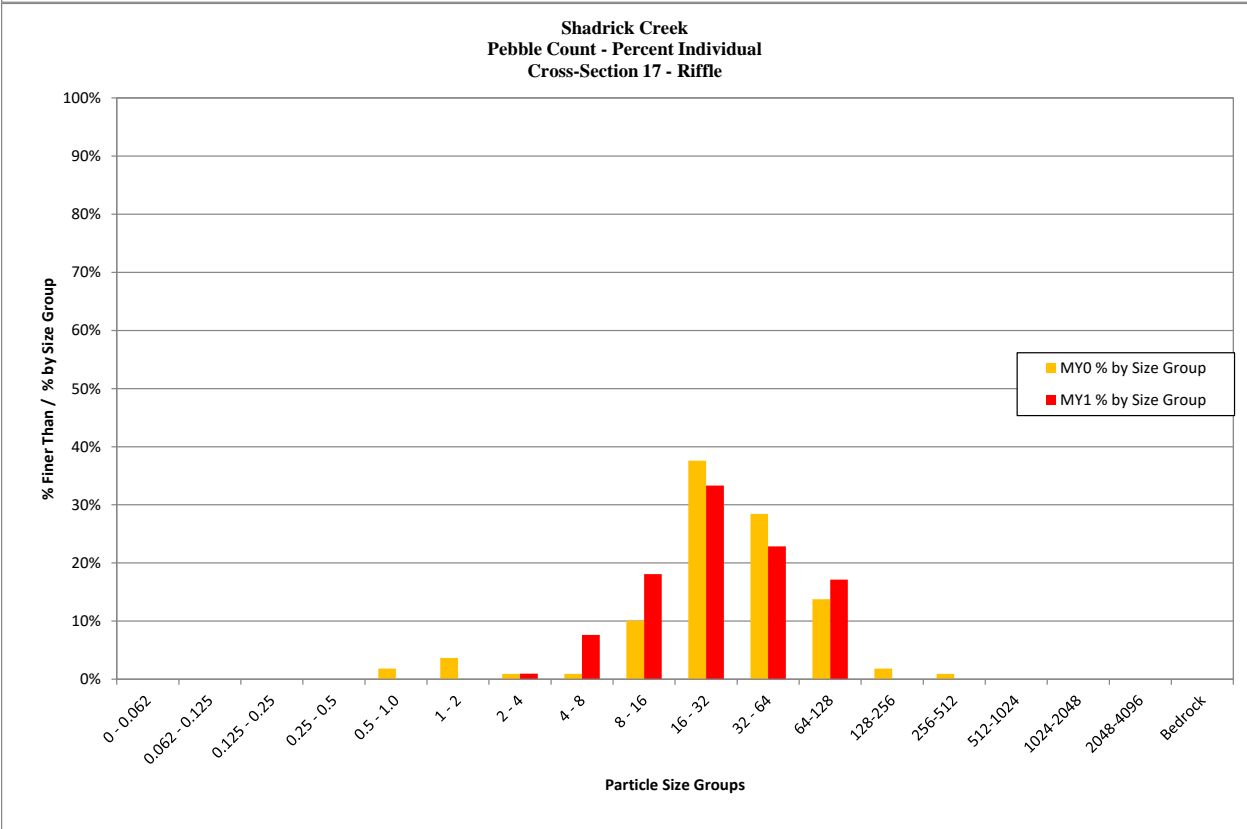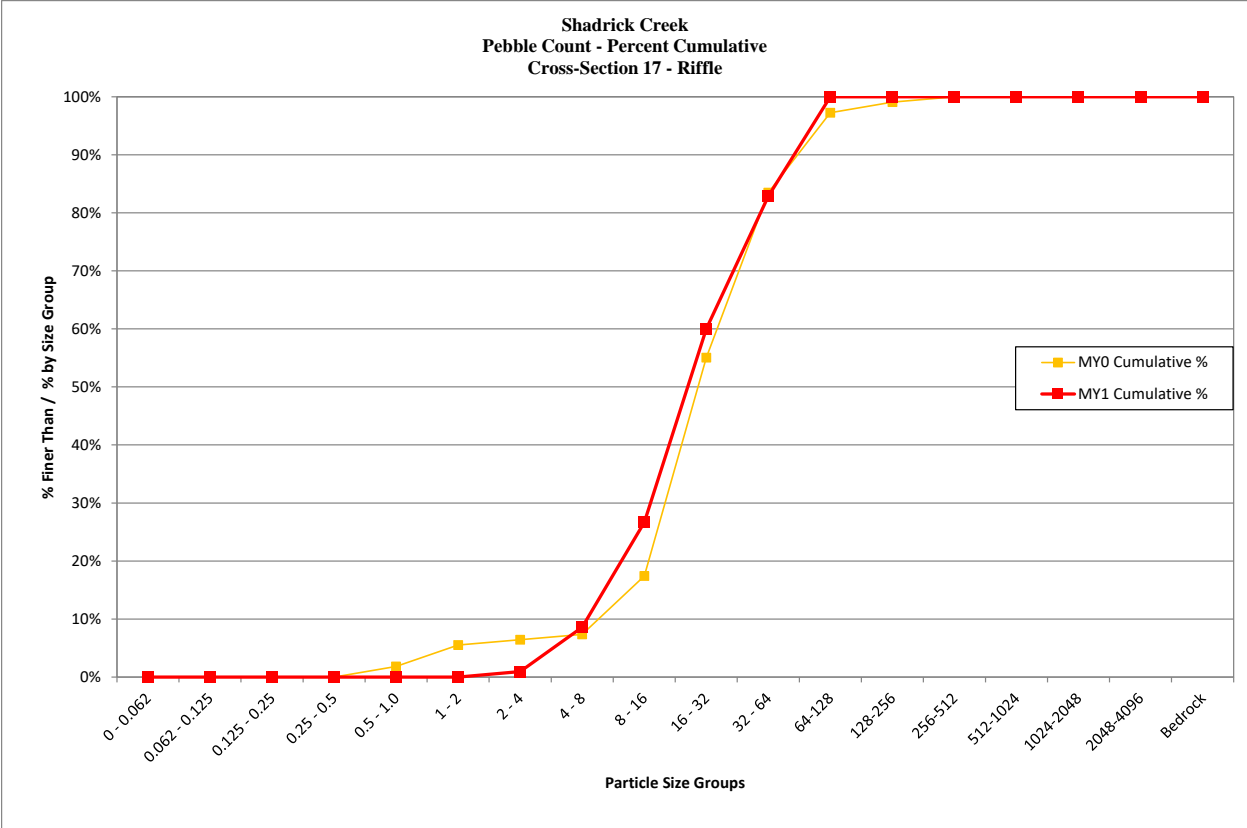

Shadrick Creek Reach 3			
Cross Section 19 - Riffle			
Monitoring Year - 2018; MY1			
Bed Surface Material Particle Size Class (mm)	Number	% Individual	% Cumulative
0 - 0.062	0	0.0%	0%
0.062 - 0.125	0	0.0%	0%
0.125 - 0.25	5	4.5%	5%
0.25 - 0.5	0	0.0%	5%
0.5 - 1.0	0	0.0%	5%
1 - 2	1	0.9%	5%
2 - 4	10	9.1%	15%
4 - 8	9	8.2%	23%
8 - 16	12	10.9%	34%
16 - 32	28	25.5%	59%
32 - 64	16	14.5%	74%
64-128	20	18.2%	92%
128-256	9	8.2%	100%
256-512	0	0.0%	100%
512-1024	0	0.0%	100%
1024-2048	0	0.0%	100%
2048-4096	0	0.0%	100%
Bedrock	0	0.0%	100%
Total	110	100%	100%
Summary Data			
D50		26	
D84		91	
D95		150	

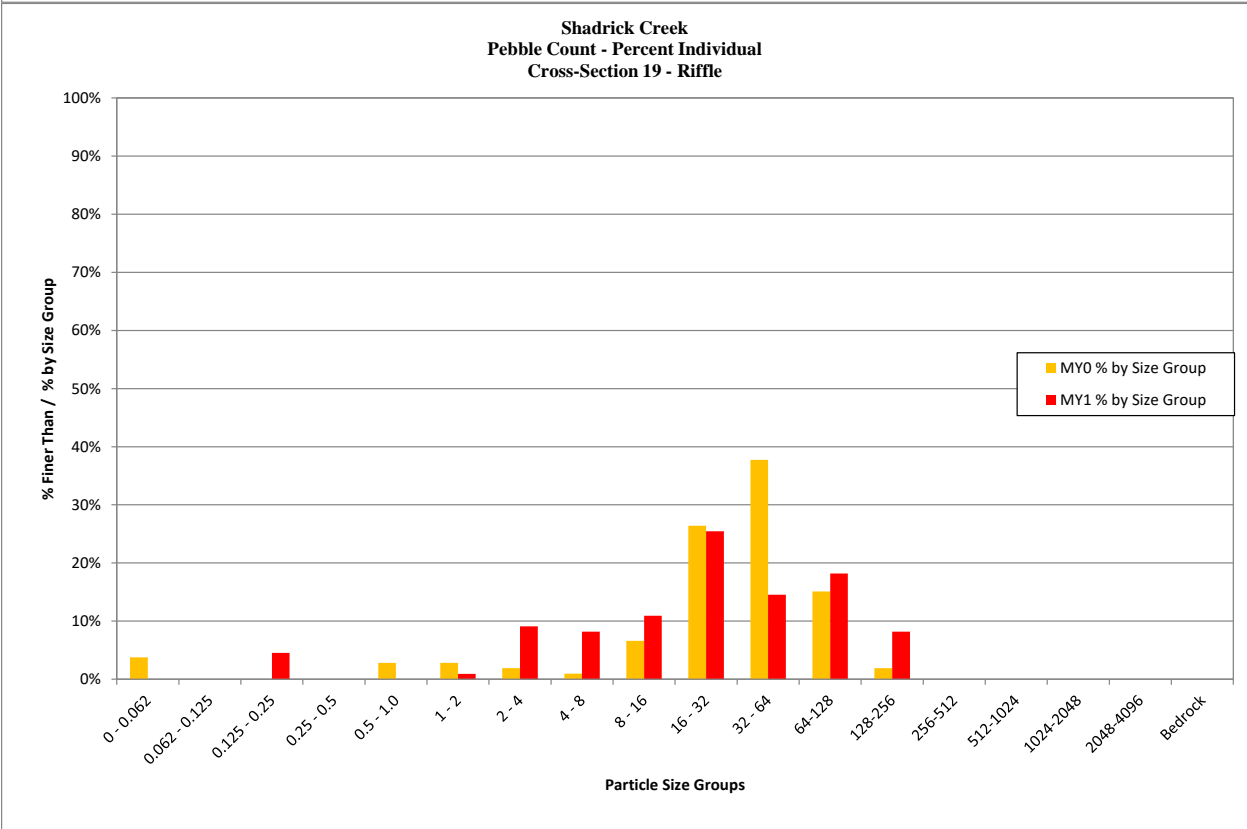
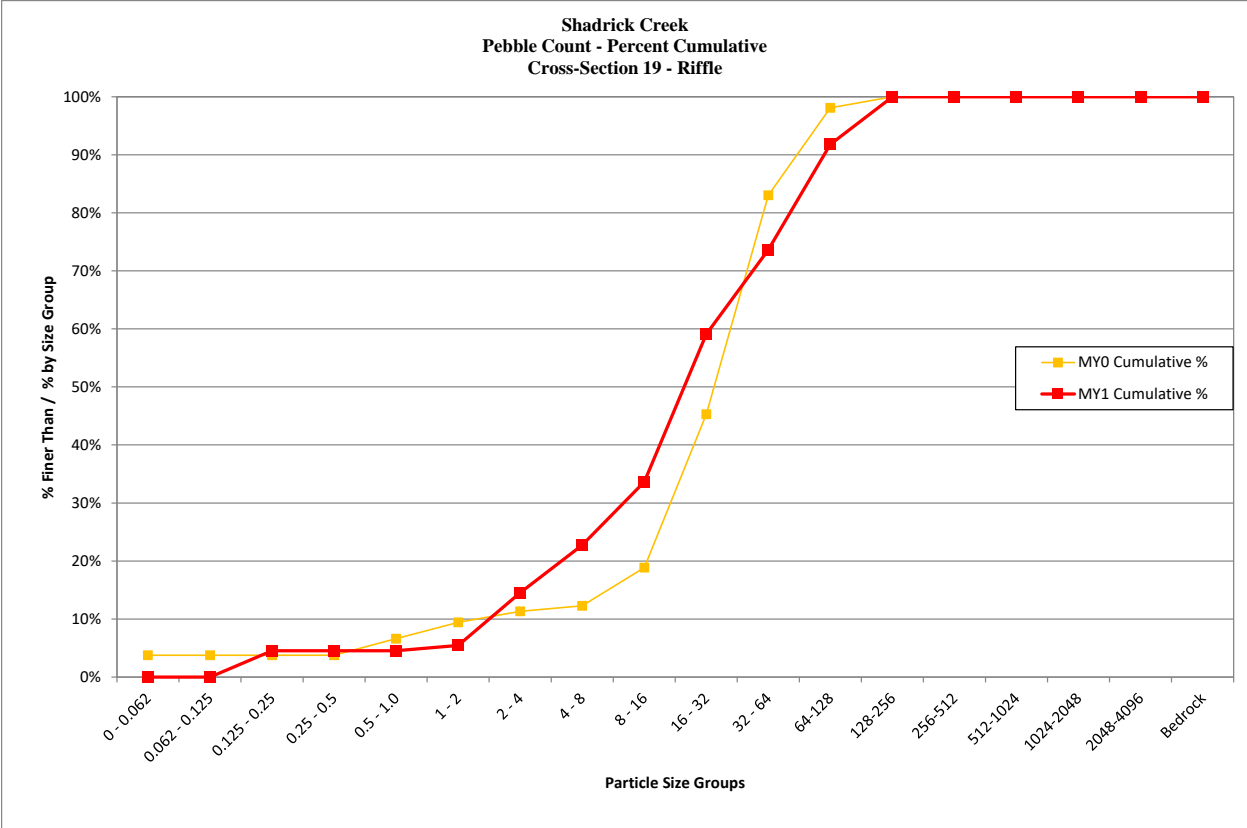


Table 10. Baseline Stream Data Summary																										
Shadrick Creek - Shadrick Creek Reach 1 (3,631 feet)																										
Parameter	Regional Curve			Pre-Existing Condition						Reference Reach Data						Design			As-Built/ Baseline							
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N		
Bankfull Width (ft)	-	-	-	21.0	-	22.0	23.0	-	-	-	-	19	-	-	-	-	27.0	-	26.6	29.3	28.7	32.7	3.1	3		
Floodprone Width (ft)				68.0	-	74.0	80.0	-	-	-	-	32.0	-	-	-	-	100.0	-	100.0	100.0	100.0	100.0	0.0	3		
Bankfull Mean Depth (ft)				2.4	-	2.6	2.8	-	-	-	-	1.8	-	-	-	-	2.2	-	1.8	1.8	1.8	1.8	0.0	3		
Bankfull Max Depth (ft)				3.6	-	3.6	3.7	-	-	-	-	2.1	-	-	-	-	3.0	-	3.0	3.1	3.0	3.2	0.1	3		
Bankfull Cross Sectional Area (ft ²)				51.4	-	57.5	63.5	-	-	-	-	34.5	-	-	-	-	58.4	-	47.0	52.8	52.0	59.3	6.2	3		
Width/Depth Ratio				6.9	-	8.6	10.3	-	-	-	-	10.4	-	-	-	-	12.4	-	15.0	16.3	15.8	18.0	1.5	3		
Entrenchment Ratio				3.0	-	3.4	3.8	-	-	-	-	1.7	-	-	-	-	3.7	-	3.1	3.4	3.5	3.8	0.4	3		
Bank Height Ratio				1.3	-	1.3	1.4	-	-	-	-	-	-	-	-	-	-	-	1.0	1.0	1.0	1.0	0.0	3		
d50 (mm)				23.0	-	25.0	40.0	-	-	-	-	40.0	-	-	-	23.0	25.0	40.0	21.0	35.0	28.0	56.0	18.5	3		
Profile																										
Riffle Length (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Riffle Slope (ft/ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pool Length (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pool Max Depth (ft)				3.9	-	4.4	4.8	-	-	-	-	3.9	-	-	-	-	5.0	-	-	-	-	-	-	-		
Pool Spacing (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pattern																										
Channel Belt Width (ft)				66.0	-	70.0	162.0	-	-	-	-	65.0	-	-	-	66.0	70.0	162.0	-	-	-	-	-	-		
Radius of Curvature (ft)				34.0	-	61.0	149.0	-	-	-	-	60.0	-	-	-	34.0	61.0	149.0	-	-	-	-	-	-		
Rc: Bankfull Width (ft/ft)				1.6	-	2.8	6.5	-	-	-	-	3.2	-	-	-	1.6	2.8	6.5	-	-	-	-	-	-		
Meander Wavelength (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Meander Width Ratio				3.1	-	3.2	7.0	-	-	-	-	3.4	-	-	-	3.1	3.2	7.0	-	-	-	-	-	-		
Substrate, Bed and Transport Parameters																										
Reach Shear Stress (Competency) lb/ft ²							0.75																			
Max Part Size (mm) Mobilized at Bankfull							120.0																			
Stream Power (Transport Capacity) W/m ²							-																			
Additional Reach Parameters																										
Drainage Area (mi ²)							2.8					2.5				2.8										
Rosgen Classification							E4					E4				C4								C4		
Bankfull Velocity (fps)							4.8					3.7				3.9										
Bankfull Discharge (cfs)							273.0					127.0				230.0										
Valley Length (ft)							-					-				-								3,268		
Channel Thalweg Length (ft)							-					-				3,641								3,631		
Sinuosity							1.32					1.80				1.32								1.13		
Water Surface Slope (ft/ft)							0.0053					0.0089				0.0053								-		
Bankfull Slope (ft/ft)							-					-				-								-		
Bankfull Floodplain Area (acres)							-					-														
% of Reach with Eroding Banks							-					-														
Channel Stability or Habitat Metric							-					-														
Biological or Other							-					-														

- Information unavailable.

Non-Applicable.

Table 10 Cont'd. Baseline Stream Data Summary																										
Shadrick Creek - Shadrick Creek Reach 2 (573 feet)																										
Parameter	Regional Curve			Pre-Existing Condition						Reference Reach Data						Design			As-Built/ Baseline							
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N		
Bankfull Width (ft)	-	-	-	19.9	-	20.6	21.3	-	-	-	-	19.7	-	-	-	29.0	-	-	29.9	-	-	-	-	1		
Floodprone Width (ft)	-	-	-	68.0	-	74.0	80.0	-	-	-	-	32.0	-	-	-	100.0	-	-	116.0	-	-	-	-	1		
Bankfull Mean Depth (ft)	-	-	-	2.3	-	2.4	2.5	-	-	-	-	2.1	-	-	-	2.4	-	-	2.4	-	-	-	-	1		
Bankfull Max Depth (ft)	-	-	-	3.4	-	3.7	4.0	-	-	-	-	3.2	-	-	-	3.4	-	-	3.9	-	-	-	-	1		
Bankfull Cross Sectional Area (ft ²)	-	-	-	46.4	-	49.4	52.3	-	-	-	-	41.0	-	-	-	69.7	-	-	71.7	-	-	-	-	1		
Width/Depth Ratio	-	-	-	8.5	-	8.6	8.6	-	-	-	-	9.5	-	-	-	12.1	-	-	12.5	-	-	-	-	1		
Entrenchment Ratio	-	-	-	2.2	-	2.8	3.3	-	-	3.0	-	4.0	5.0	-	-	1.7	-	-	3.9	-	-	-	-	1		
Bank Height Ratio	-	-	-	1.6	-	1.7	1.7	-	-	-	-	1.9	-	-	-	1.0	-	-	1.0	-	-	-	-	1		
d50 (mm)	-	-	-	10.0	-	12.0	32.0	-	-	10.0	-	12.0	32.0	-	-	10.0	12.0	32.0	-	-	-	-	-	-		
Profile																										
Riffle Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Riffle Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pool Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pool Max Depth (ft)	-	-	-	-	-	5.1	-	-	-	-	-	-	-	-	-	5.5	-	-	-	-	-	-	-	-		
Pool Spacing (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Pattern																										
Channel Belt Width (ft)	-	-	-	60.0	-	80.0	100.0	-	-	60.0	-	80.0	100.0	-	-	90.0	116.0	160.0	-	-	-	-	-	-		
Radius of Curvature (ft)	-	-	-	20.0	-	43.0	118.0	-	-	30.0	-	40.0	50.0	-	-	30.0	60.0	75.0	-	-	-	-	-	-		
Rc: Bankfull Width (ft/ft)	-	-	-	1.00	-	21.00	5.50	-	-	1.50	-	2.00	2.50	-	-	1.10	2.10	2.60	-	-	-	-	-	-		
Meander Wavelength (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Meander Width Ratio	-	-	-	3.0	-	3.9	4.7	-	-	3.1	-	4.1	5.1	-	-	3.1	4.0	5.5	-	-	-	-	-	-		
Substrate, Bed and Transport Parameters																										
Reach Shear Stress (Competency) lb/ft ²	-	-	-	-	-	0.84	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Max Part Size (mm) Mobilized at Bankfull	-	-	-	-	-	130.0	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Stream Power (Transport Capacity) W/m ²	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Additional Reach Parameters																										
Drainage Area (mi ²)	-	-	-	-	-	3.3	-	-	-	-	-	3.2	-	-	-	3.3	-	-	-	-	-	-	-	-		
Rosgen Classification	-	-	-	-	-	E4	-	-	-	-	-	E4	-	-	-	C4	-	-	-	-	-	-	-	-		
Bankfull Velocity (fps)	-	-	-	-	-	4.5	-	-	-	-	-	5.3	-	-	-	4.0	-	-	-	-	-	-	-	-		
Bankfull Discharge (cfs)	-	-	-	-	-	225.0	-	-	-	-	-	217.0	-	-	-	280.0	-	-	-	-	-	-	-	-		
Valley Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	499	-		
Channel Thalweg Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	575	-	-	-	-	-	-	573	-		
Sinuosity	-	-	-	-	-	1.26	-	-	-	-	-	1.26	-	-	-	1.31	-	-	-	-	-	-	1.15	-		
Water Surface Slope (ft/ft)	-	-	-	-	-	0.0050	-	-	-	-	-	0.0050	-	-	-	0.0048	-	-	-	-	-	-	-	-		
Bankfull Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Bankfull Floodplain Area (acres)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
% of Reach with Eroding Banks	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Channel Stability or Habitat Metric	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Biological or Other	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		

- Information unavailable.

Non-Applicable.

**Table 10 Cont'd. Baseline Stream Data Summary
Shadrick Creek - Shadrick Creek Reach 3 (1,104 feet)**

Parameter	Regional Curve			Pre-Existing Condition							Reference Reach Data							Design			As-Built/ Baseline					
	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N		
Dimension & Substrate - Riffle																										
Bankfull Width (ft)	-	-	-	19.9	-	20.6	21.3	-	-	-	-	19.7	-	-	-	-	29.0	-	26.9	29.0	29.0	31.1	2.9	2		
Floodprone Width (ft)				68.0	-	74.0	80.0	-	-	-	-	32.0	-	-	-	-	100.0	-	116.0	116.0	116.0	116.0	0.0	2		
Bankfull Mean Depth (ft)	-	-	-	2.3	-	2.4	2.5	-	-	-	-	2.1	-	-	-	-	2.4	-	2.2	2.2	2.2	2.3	0.0	2		
Bankfull Max Depth (ft)				3.4	-	3.7	4.0	-	-	-	-	3.2	-	-	-	-	3.4	-	3.5	3.5	3.5	3.5	0.0	2		
Bankfull Cross Sectional Area (ft ²)				46.4	-	49.4	52.3	-	-	-	-	41.0	-	-	-	-	69.7	-	61.0	64.8	64.8	68.6	5.4	2		
Width/Depth Ratio				8.5	-	8.6	8.6	-	-	-	-	9.5	-	-	-	-	12.1	-	11.9	13.0	13.0	14.1	1.6	2		
Entrenchment Ratio				2.2	-	2.8	3.3	-	-	3.0	-	4.0	5.0	-	-	-	1.7	-	3.7	4.0	4.0	4.3	0.4	2		
Bank Height Ratio				1.6	-	1.7	1.7	-	-	-	-	1.9	-	-	-	-	1.0	-	1.0	1.0	1.0	1.0	0.0	2		
d50 (mm)				10.0	-	12.0	32.0	-	-	10.0	-	12.0	32.0	-	-	10.0	12.0	32.0	29.0	32.0	32.0	35.0	4.2	2		
Profile																										
Riffle Length (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	32.0	69.7	67.8	121.6	34.8	7		
Riffle Slope (ft/ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.004	0.007	0.008	0.011	0.002	7		
Pool Length (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	13.8	42.9	45.0	63.8	15.1	7		
Pool Max Depth (ft)				-	-	5.1	-	-	-	-	-	-	-	-	-	-	-	-	5.5	-	4.3	4.8	4.5	0.5	7	
Pool Spacing (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	87.4	145.2	141.1	196.3	40.1	6		
Pattern																										
Channel Belt Width (ft)				60.0	-	80.0	100.0	-	-	60.0	-	80.0	100.0	-	-	90.0	116.0	160.0	84.7	94.5	95.0	103.5	7.7	4		
Radius of Curvature (ft)				20.0	-	43.0	118.0	-	-	30.0	-	40.0	50.0	-	-	30.0	60.0	75.0	61.6	67.0	66.8	72.9	4.8	4		
Rc: Bankfull Width (ft/ft)				1.00	-	21.00	5.50	-	-	1.50	-	2.00	2.50	-	-	1.10	2.10	2.60	2.12	2.31	2.30	2.51	0.17	3		
Meander Wavelength (ft)				-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	202.5	250.1	248.2	301.6	51.7	4		
Meander Width Ratio				3.0	-	3.9	4.7	-	-	3.1	-	4.1	5.1	-	-	3.1	4.0	5.5	2.1	2.3	2.3	2.5	0.16	4		
Substrate, Bed and Transport Parameters																										
Reach Shear Stress (Competency) lb/ft ²						0.84						-														
Max Part Size (mm) Mobilized at Bankfull						130.0						-														
Stream Power (Transport Capacity) W/m ²						-						-														
Additional Reach Parameters																										
Drainage Area (mi ²)						3.3						3.2						3.3								
Rosgen Classification						E4						E4						C4						C4		
Bankfull Velocity (fps)				-		4.5						5.3						4.0								
Bankfull Discharge (cfs)				-		225.0						217.0						280.0								
Valley Length (ft)						-						-						1,108						1,104		
Channel Thalweg Length (ft)						-						-						-						927		
Sinuosity						1.26						1.26						1.31						1.19		
Water Surface Slope (ft/ft)						0.0050						0.0050						0.0048						0.0043		
Bankfull Slope (ft/ft)						-						-						-						0.0055		
Bankfull Floodplain Area (acres)						-						-						-								
% of Reach with Eroding Banks						-						-						-								
Channel Stability or Habitat Metric						-						-						-								
Biological or Other						-						-						-								

- Information unavailable.

Non-Applicable.

Table 10 Cont'd. Baseline Stream Data Summary																										
Shadrick Creek - UT1 (1,651 feet)																										
Parameter	Regional Curve			Pre-Existing Condition						Reference Reach Data						Design			As-Built/ Baseline							
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N		
Bankfull Width (ft)	-	-	-	3.3	-	3.9	5.3	-	-	5.4	-	6.7	8.0	-	-	8.0	-	5.02	5.68	5.68	6.34	0.93	2			
Floodprone Width (ft)	-	-	-	4.5	-	13.0	21.0	-	-	13.0	-	16.5	20.0	-	-	24.0	-	24	24	24	24	0	2			
Bankfull Mean Depth (ft)	-	-	-	0.3	-	0.7	1.0	-	-	0.6	-	0.6	0.7	-	-	0.7	-	0.68	0.73	0.73	0.77	0.07	2			
Bankfull Max Depth (ft)	-	-	-	0.5	-	0.9	1.2	-	-	1.1	-	1.1	1.2	-	-	1.0	-	1.1	1.19	1.19	1.28	0.12	2			
Bankfull Cross Sectional Area (ft ²)	-	-	-	1.2	-	2.8	4.6	-	-	3.1	-	4.3	5.5	-	-	5.5	-	3.88	4.09	4.09	4.3	0.3	2			
Width/Depth Ratio	-	-	-	4.2	-	6.1	12.6	-	-	9.4	-	10.5	11.6	-	-	11.6	-	6.5	7.93	7.93	9.35	2.02	2			
Entrenchment Ratio	-	-	-	1.1	-	2.8	5.2	-	-	-	-	2.5	-	-	-	3.0	-	3.78	4.28	4.28	4.78	0.7	2			
Bank Height Ratio	-	-	-	1.0	-	1.5	3.0	-	-	-	-	1.0	-	-	-	1.0	-	1.0	1.0	1.0	1.0	0.0	2			
d50 (mm)	-	-	-	3.0	-	6.0	9.0	-	-	3.0	-	6.0	9.0	-	-	3.0	6.0	9.0	-	-	-	-	-			
Profile																										
Riffle Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Riffle Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Pool Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Pool Max Depth (ft)	-	-	-	0.9	-	1.3	1.9	-	-	-	-	1.2	-	-	-	1.6	-	-	-	-	-	-	-			
Pool Spacing (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Pattern																										
Channel Belt Width (ft)	-	-	-	16.0	-	35.0	50.0	-	-	-	-	40.0	-	-	-	16.0	35.0	50.0	-	-	-	-	-			
Radius of Curvature (ft)	-	-	-	7.0	-	20.0	70.0	-	-	21.0	-	22.0	23.0	-	-	7.0	20.0	70.0	-	-	-	-	-			
Rc: Bankfull Width (ft/ft)	-	-	-	2.1	-	5.1	13.2	-	-	3.1	-	3.3	3.4	-	-	2.1	5.1	13.2	-	-	-	-	-			
Meander Wavelength (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Meander Width Ratio	-	-	-	4.8	-	8.9	9.5	-	-	-	-	6.0	-	-	-	4.8	8.9	9.5	-	-	-	-	-			
Substrate, Bed and Transport Parameters																										
Reach Shear Stress (Competency) lb/ft ²				0.95						-						-			-							
Max Part Size (mm) Mobilized at Bankfull				145.0						-						-			-							
Stream Power (Transport Capacity) W/m ²				-						-						-			-							
Additional Reach Parameters																										
Drainage Area (mi ²)				0.10						0.10						0.10										
Rosgen Classification				G4						B4						B4			C4							
Bankfull Velocity (fps)	-			5.5						7.0						4.5										
Bankfull Discharge (cfs)	-			24.0						30.0						25.0										
Valley Length (ft)				-						-						-										
Channel Thalweg Length (ft)				-						-						1,637			1,651							
Sinuosity				1.13						1.13						1.13			1.14							
Water Surface Slope (ft/ft)				0.0230						0.0230						0.0230			-							
Bankfull Slope (ft/ft)				-						-						-			-							
Bankfull Floodplain Area (acres)				-						-						-			-							
% of Reach with Eroding Banks				-						-						-			-							
Channel Stability or Habitat Metric				-						-						-			-							
Biological or Other				-						-						-			-							

- Information unavailable.

Non-Applicable.

Table 10 Cont'd. Baseline Stream Data Summary																									
Shadrick Creek - UT9 Reach 1 (706 feet)																									
Parameter	Regional Curve			Pre-Existing Condition						Reference Reach Data						Design			As-Built/ Baseline						
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N	
Bankfull Width (ft)	-	-	-	4.2	-	5.7	6.0	-	-	5.4	-	6.7	8.0	-	-	-	8.0	-	-	9.5	-	-	-	1	
Floodprone Width (ft)	-	-	-	8.0	-	10.0	11.0	-	-	13.0	-	17.00	20.0	-	-	-	24.0	-	-	24.0	-	-	-	1	
Bankfull Mean Depth (ft)	-	-	-	0.5	-	0.7	1.1	-	-	0.6	-	0.6	0.7	-	-	-	0.7	-	-	0.5	-	-	-	1	
Bankfull Max Depth (ft)	-	-	-	0.6	-	0.9	1.5	-	-	1.1	-	1.1	1.2	-	-	-	1.0	-	-	1.1	-	-	-	1	
Bankfull Cross Sectional Area (ft ²)	-	-	-	2.6	-	2.7	6.3	-	-	3.1	-	4.3	5.5	-	-	-	5.5	-	-	4.8	-	-	-	1	
Width/Depth Ratio	-	-	-	5.7	-	6.3	12.7	-	-	9.4	-	10.5	11.6	-	-	-	11.6	-	-	18.7	-	-	-	1	
Entrenchment Ratio	-	-	-	1.4	-	1.7	2.7	-	-	-	-	2.5	-	-	-	-	3.0	-	-	2.5	-	-	-	1	
Bank Height Ratio	-	-	-	2.3	-	2.7	4.4	-	-	-	-	1.0	-	-	-	-	1.0	-	-	1.0	-	-	-	1	
d50 (mm)	-	-	-	-	-	0.3	-	-	-	3.0	-	6.0	9.0	-	-	-	0.3	-	-	-	-	-	-	-	
Profile																									
Riffle Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Riffle Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pool Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pool Max Depth (ft)	-	-	-	1.0	-	1.2	1.4	-	-	-	-	1.2	-	-	-	-	1.6	-	-	-	-	-	-	-	
Pool Spacing (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pattern																									
Channel Belt Width (ft)	-	-	-	20.0	-	26.0	31.0	-	-	-	-	40.0	-	-	-	20.0	26.0	31.0	-	-	-	-	-	-	
Radius of Curvature (ft)	-	-	-	36.0	-	47.0	62.0	-	-	21.0	-	22.0	23.0	-	-	36.0	47.0	62.0	-	-	-	-	-	-	
Rc: Bankfull Width (ft/ft)	-	-	-	6.0	-	8.2	14.9	-	-	3.1	-	3.3	3.4	-	-	6.0	8.2	14.9	-	-	-	-	-	-	
Meander Wavelength (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Meander Width Ratio	-	-	-	4.5	-	4.8	5.1	-	-	-	-	6.0	-	-	-	4.5	4.8	5.1	-	-	-	-	-	-	
Substrate, Bed and Transport Parameters																									
Reach Shear Stress (Competency) lb/ft ²	-	-	-	-	-	1.44	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Max Part Size (mm) Mobilized at Bankfull	-	-	-	-	-	200.0	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Stream Power (Transport Capacity) W/m ²	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Additional Reach Parameters																									
Drainage Area (mi ²)	-	-	-	-	-	0.1	-	-	-	-	-	0.1	-	-	-	0.1	-	-	-	-	-	-	-	-	
Rosgen Classification	-	-	-	-	-	B4, G4	-	-	-	-	-	B4	-	-	-	B4	-	-	-	-	-	-	-	B4	
Bankfull Velocity (fps)	-	-	-	-	-	10.1	-	-	-	-	-	7.0	-	-	-	4.5	-	-	-	-	-	-	-	-	
Bankfull Discharge (cfs)	-	-	-	-	-	48.0	-	-	-	-	-	30.0	-	-	-	25.0	-	-	-	-	-	-	-	-	
Valley Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	696	-	
Channel Thalweg Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	678	-	-	-	-	-	-	706	-	
Sinuosity	-	-	-	-	-	1.03	-	-	-	-	-	1.13	-	-	-	1.03	-	-	-	-	-	-	1.08	-	
Water Surface Slope (ft/ft)	-	-	-	-	-	0.0350	-	-	-	-	-	0.0230	-	-	-	0.0350	-	-	-	-	-	-	-	-	
Bankfull Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Bankfull Floodplain Area (acres)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
% of Reach with Eroding Banks	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Channel Stability or Habitat Metric	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Biological or Other	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	

- Information unavailable.

Non-Applicable.

Table 10 Cont'd. Baseline Stream Data Summary																										
Shadrick Creek - UT9 Reach 2 (238 feet)																										
Parameter	Regional Curve			Pre-Existing Condition						Reference Reach Data						Design			As-Built/ Baseline							
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Med	Max	SD	N		
Bankfull Width (ft)	-	-	-	4.2	-	5.7	6.0	-	-	5.4	-	6.7	8.0	-	-	-	8.0	-	-	8.3	-	-	-	1		
Floodprone Width (ft)	-	-	-	8.0	-	10.0	11.0	-	-	13.0	-	17	20.0	-	-	-	24.0	-	-	24.0	-	-	-	1		
Bankfull Mean Depth (ft)	-	-	-	0.5	-	0.7	1.1	-	-	0.6	-	0.6	0.7	-	-	-	0.7	-	-	0.4	-	-	-	1		
Bankfull Max Depth (ft)	-	-	-	0.6	-	0.9	1.5	-	-	1.1	-	1.1	1.2	-	-	-	1.0	-	-	1.0	-	-	-	1		
Bankfull Cross Sectional Area (ft ²)	-	-	-	2.6	-	2.7	6.3	-	-	3.1	-	4.3	5.5	-	-	-	5.5	-	-	3.6	-	-	-	1		
Width/Depth Ratio	-	-	-	5.7	-	6.3	12.7	-	-	9.4	-	10.5	11.6	-	-	-	11.6	-	-	19.0	-	-	-	1		
Entrenchment Ratio	-	-	-	1.4	-	1.7	2.7	-	-	-	-	2.5	-	-	-	-	3.0	-	-	2.9	-	-	-	1		
Bank Height Ratio	-	-	-	2.3	-	2.7	4.4	-	-	-	-	1.0	-	-	-	-	1.0	-	-	1.0	-	-	-	1		
d50 (mm)	-	-	-	-	-	0.3	-	-	-	3.0	-	6.0	9.0	-	-	-	0.3	-	-	13.0	-	-	-	1		
Profile																										
Riffle Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	23.3	29.0	27.3	38.4	6.7	4		
Riffle Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.016	0.022	0.020	0.033	0.008	4		
Pool Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	5.6	10.2	11.2	12.6	3.1	4		
Pool Max Depth (ft)	-	-	-	1.0	-	1.2	1.4	-	-	-	-	1.2	-	-	-	-	1.8	-	1.0	1.5	1.5	1.7	0.3	4		
Pool Spacing (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	40.4	47.7	46.4	56.4	8.1	3		
Pattern																										
Channel Belt Width (ft)	-	-	-	20.0	-	26.0	31.0	-	-	-	-	40.0	-	-	-	-	42.0	-	24.5	30.0	29.0	36.6	6.1	3		
Radius of Curvature (ft)	-	-	-	36.0	-	47.0	62.0	-	-	21.0	-	22	23.0	-	-	-	15.0	-	13.3	15.2	15.4	16.9	1.8	3		
Rc: Bankfull Width (ft)	-	-	-	6.0	-	8.2	14.9	-	-	3.1	-	3.3	3.4	-	-	-	1.9	-	2.12	2.31	2.30	2.51	0.17	3		
Meander Wavelength (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	63.7	78.5	79.3	92.5	14.4	3		
Meander Width Ratio	-	-	-	4.5	-	4.8	5.1	-	-	-	-	6.0	-	-	-	-	5.3	-	3.1	3.8	3.6	4.6	0.8	3		
Substrate, Bed and Transport Parameters																										
Reach Shear Stress (Competency) lb/ft ²	-	-	-	-	-	0.58	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Max Part Size (mm) Mobilized at Bankfull	-	-	-	-	-	100.0	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Stream Power (Transport Capacity) W/m ²	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Additional Reach Parameters																										
Drainage Area (mi ²)	-	-	-	-	-	0.10	-	-	-	-	-	0.1	-	-	-	-	0.1	-	-	-	-	-	-	-		
Rosgen Classification	-	-	-	-	-	B4, G4	-	-	-	-	-	B4	-	-	-	-	E4	-	-	-	-	-	-	C5		
Bankfull Velocity (fps)	-	-	-	-	-	10.10	-	-	-	-	-	7.0	-	-	-	-	3.3	-	-	-	-	-	-	-		
Bankfull Discharge (cfs)	-	-	-	-	-	48.00	-	-	-	-	-	30.0	-	-	-	-	18.0	-	-	-	-	-	-	-		
Valley Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	198			
Channel Thalweg Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	245	-	-	-	-	-	238			
Sinuosity	-	-	-	-	-	1.03	-	-	-	-	-	1.13	-	-	-	-	1.71	-	-	-	-	-	1.20			
Water Surface Slope (ft/ft)	-	-	-	-	-	0.04	-	-	-	-	-	0.0230	-	-	-	-	0.0140	-	-	-	-	-	0.0168			
Bankfull Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.0182			
Bankfull Floodplain Area (acres)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
% of Reach with Eroding Banks	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Channel Stability or Habitat Metric	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Biological or Other	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		

- Information unavailable.

Non-Applicable.

Table 10 Cont'd. Baseline Stream Data Summary																											
Shadrick Creek - UT10 (404 feet)																											
Parameter	Regional Curve			Pre-Existing Condition							Reference Reach Data							Design			As-Built/ Baseline						
Dimension & Substrate - Riffle	LL	UL	Eq.	Min	Mean	Med	Max	SD	N	Min	Mean	Med	Max	SD	N	Min	Mean	Max	Min	Mean	Max	Min	Mean	Med	Max	SD	N
Bankfull Width (ft)	-	-	-	-	-	7.0	-	-	-	5.4	-	6.7	8.0	-	-	-	7.0	-	-	7.3	-	-	-	-	-	1	
Floodprone Width (ft)	-	-	-	-	-	9.0	-	-	-	13.0	-	17	20.0	-	-	-	24.0	-	-	24.0	-	-	-	-	-	1	
Bankfull Mean Depth (ft)	-	-	-	-	-	0.5	-	-	-	0.6	-	0.6	0.7	-	-	-	0.6	-	-	0.5	-	-	-	-	-	1	
Bankfull Max Depth (ft)	-	-	-	-	-	0.8	-	-	-	1.1	-	1.1	1.2	-	-	-	0.8	-	-	1.1	-	-	-	-	-	1	
Bankfull Cross Sectional Area (ft ²)	-	-	-	-	-	3.8	-	-	-	3.1	-	4.3	5.5	-	-	-	4.0	-	-	3.4	-	-	-	-	-	1	
Width/Depth Ratio	-	-	-	-	-	13.0	-	-	-	9.4	-	10.5	11.6	-	-	-	12.3	-	-	15.6	-	-	-	-	-	1	
Entrenchment Ratio	-	-	-	-	-	1.3	-	-	-	-	-	2.5	-	-	-	-	3.4	-	-	3.3	-	-	-	-	-	1	
Bank Height Ratio	-	-	-	-	-	2.5	-	-	-	-	-	1.0	-	-	-	-	1.0	-	-	1.0	-	-	-	-	-	1	
d50 (mm)	-	-	-	-	-	0.3	-	-	-	3.0	-	6.0	9.0	-	-	-	0.3	-	-	-	-	-	-	-	-	1	
Profile																											
Riffle Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Riffle Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pool Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pool Max Depth (ft)	-	-	-	-	-	-	-	-	-	-	-	1.2	-	-	-	-	1.3	-	-	-	-	-	-	-	-	-	
Pool Spacing (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Pattern																											
Channel Belt Width (ft)	-	-	-	-	-	30.0	-	-	-	-	-	40	-	-	-	-	30.0	-	-	-	-	-	-	-	-	-	
Radius of Curvature (ft)	-	-	-	-	36.0	-	66.0	67.0	-	-	21.0	-	22	23.0	-	-	66.0	-	-	-	-	-	-	-	-	-	
Rc: Bankfull Width (ft/ft)	-	-	-	-	5.1	-	9.4	9.6	-	-	3.1	-	3.3	3.4	-	-	3.3	-	-	-	-	-	-	-	-	-	
Meander Wavelength (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Meander Width Ratio	-	-	-	-	-	4.3	-	-	-	-	-	6.0	-	-	-	-	4.3	-	-	-	-	-	-	-	-		
Substrate, Bed and Transport Parameters																											
Reach Shear Stress (Competency) lb/ft ²	-	-	-	-	-	0.86	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Max Part Size (mm) Mobilized at Bankfull	-	-	-	-	-	135.0	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Stream Power (Transport Capacity) W/m ²	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Additional Reach Parameters																											
Drainage Area (mi ²)	-	-	-	-	-	0.03	-	-	-	-	-	0.1	-	-	-	-	0.03	-	-	-	-	-	-	-	-	-	
Rosgen Classification	-	-	-	-	-	F4	-	-	-	-	-	B4	-	-	-	-	B4	-	-	-	-	-	-	-	-	-	
Bankfull Velocity (fps)	-	-	-	-	-	1.9	-	-	-	-	-	7	-	-	-	-	7.0	-	-	-	-	-	-	-	-	-	
Bankfull Discharge (cfs)	-	-	-	-	-	7.0	-	-	-	-	-	30.0	-	-	-	-	30.0	-	-	-	-	-	-	-	-	-	
Valley Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	390		
Channel Thalweg Length (ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	391	-	-	-	-	-	-	-	404		
Sinuosity	-	-	-	-	-	1.04	-	-	-	-	-	1.13	-	-	-	-	1.04	-	-	-	-	-	-	-	1.03		
Water Surface Slope (ft/ft)	-	-	-	-	-	0.0249	-	-	-	-	-	0.0230	-	-	-	-	0.0249	-	-	-	-	-	-	-	0.0168		
Bankfull Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.0182		
Bankfull Floodplain Area (acres)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
% of Reach with Eroding Banks	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Channel Stability or Habitat Metric	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Biological or Other	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		

- Information unavailable.

Non-Applicable.

This Page Intentionally Left Blank

Table 11a. Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections) Shadrick Creek Restoration Project																														
Dimension	Cross Section 1 (Pool) UT-1						Cross Section 2 (Riffle) UT-1						Cross Section 3 (Riffle) UT-1						Cross Section 4 (Riffle) Shadrick Reach 1						Cross Section 5 (Pool) Shadrick Reach 1					
	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5
Record Elevation (datum) Used	1184.8	1184.8					1184.6	1184.6					1172.5	1172.5					1145.2	1145.26					1144.9	1144.8				
Low Bank Height Elevation (datum) Used	1184.8	1184.8					1184.6	1184.6					1172.5	1172.5					1145.2	1145.15					1144.9	1145.1				
Bankfull Width (ft)	7.1	6.1					6.3	6.7					5.0	5.6					26.6	25.9					26.9	26.4				
Floodprone Width (ft)	24.0	24.0					24.0	24.0					24.0	24.0					100.0	100.0					100.0	100.0				
Bankfull Mean Depth (ft)	0.6	0.7					0.7	0.6					0.8	0.7					1.8	1.8					2.2	2.3				
Bankfull Max Depth (ft)	1.5	1.4					1.1	1.1					1.3	1.4					3.0	3.1					4.0	4.0				
Bankfull Cross Sectional Area (ft ²)	4.5	4.5					4.3	4.3					3.9	3.9					47.0	47.0					59.5	59.5				
Bankfull Width/Depth Ratio	11.1	8.3					9.4	10.4					6.5	7.9					15.0	14.2					12.1	11.7				
Bankfull Entrenchment Ratio	3.4	3.9					3.8	3.6					4.8	4.3					3.8	3.9					3.7	3.8				
Bankfull Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	1.0					1.0	1.0					1.0	1.1				
Low Top of Bank Depth (ft)	-	1.4					-	1.1					-	1.4					-	3.0					-	4.3				
Dimension	Cross Section 6 (Riffle) Shadrick Reach 1						Cross Section 7 (Riffle) Shadrick Reach 1						Cross Section 8 (Pool) Shadrick Reach 1						Cross Section 9 (Riffle) UT-9 Reach 1						Cross Section 10 (Pool) UT-9 Reach 1					
	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5
Record Elevation (datum) Used	1143.3	1143.2					1141.2	1141.3					1139.8	1139.6					1151.8	1151.8					1151.6	1151.6				
Low Bank Height Elevation (datum) Used	1143.3	1143.2					1141.2	1141.1					1139.8	1140.0					1151.8	1151.8					1151.6	1151.6				
Bankfull Width (ft)	28.7	29.1					32.7	33.6					28.8	28.2					9.5	9.2					6.5	6.1				
Floodprone Width (ft)	100.0	100.0					100.0	100.0					100.0	100.0					24.0	24.0					24.0	24.0				
Bankfull Mean Depth (ft)	1.8	1.8					1.8	1.8					2.9	3.0					0.5	0.5					0.5	0.5				
Bankfull Max Depth (ft)	3.2	3.1					3.0	3.0					5.6	5.5					1.1	1.3					1.3	1.4				
Bankfull Cross Sectional Area (ft ²)	52.0	52.0					59.3	59.3					84.3	84.3					4.8	4.8					3.0	3.0				
Bankfull Width/Depth Ratio	15.8	16.3					18.0	19.0					9.8	9.4					18.7	17.6					14.3	12.1				
Bankfull Entrenchment Ratio	3.5	3.4					3.1	3.0					3.5	3.5					2.5	2.6					3.7	4.0				
Bankfull Bank Height Ratio	1.0	1.0					1.0	0.9					1.0	1.1					1.0	1.0					1.0	1.0				
Low Top of Bank Depth (ft)	-	3.1					-	2.8					-	5.9					-	1.3					-	1.4				
Dimension	Cross Section 11 (Pool) UT-9 Reach 2						Cross Section 12 (Riffle) UT-9 Reach 2						Cross Section 13 (Riffle) UT-10						Cross Section 14 (Pool) UT-10						Cross Section 15 (Pool) Shadrick Reach 2					
	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5
Record Elevation (datum) Used	1142.9	1142.9					1142.5	1142.5					1140.9	1140.9					1140.2	1140.1					1100.7	1100.5				
Low Bank Height Elevation (datum) Used	1142.9	1142.9					1142.5	1142.5					1140.9	1140.8					1140.2	1140.1					1100.7	1100.5				
Bankfull Width (ft)	8.8	8.6					8.3	7.7					7.3	8.7					7.5	6.9					38.9	38.8				
Floodprone Width (ft)	24.0	24.0					24.0	24.0					24.0	24.0					24.0	24.0					116.0	116.0				
Bankfull Mean Depth (ft)	0.7	0.7					0.4	0.5					0.5	0.4					0.6	0.7					2.1	2.1				
Bankfull Max Depth (ft)	1.6	1.6					1.0	1.0					1.1	1.1					1.6	1.7					4.1	4.3				
Bankfull Cross Sectional Area (ft ²)	5.8	5.8					3.6	3.6					3.4	3.4					4.8	4.8					80.4	80.4				
Bankfull Width/Depth Ratio	13.2	12.8					19.0	16.2					15.6	22.3					11.6	9.9					18.9	18.7				
Bankfull Entrenchment Ratio	2.7	2.8					2.9	3.1					3.3	2.8					3.2	3.5					3.0	3.0				
Bankfull Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	0.9					1.0	1.0					1.0	1.0				
Low Top of Bank Depth (ft)	-	1.6					-	1.0					-	1.0					-	1.6					-	4.4				
Dimension	Cross Section 16 (Riffle) Shadrick Reach 2						Cross Section 17 (Riffle) Shadrick Reach 3						Cross Section 18 (Pool) Shadrick Reach 3						Cross Section 19 (Riffle) Shadrick Reach 3											
	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5	Base	MY1	MY2	MY3	MY4	MY5						
Record Elevation (datum) Used	1100.2	1100.3					1097.6	1097.7					1097.0	1097.0					1095.3	1095.4										
Low Bank Height Elevation (datum) Used	1100.2	1100.2					1097.6	1097.6					1097.0	1096.5					1095.3	1095.4										
Bankfull Width (ft)	29.9	29.5					31.1	32.7					40.0	43.7					26.9	26.9										
Floodprone Width (ft)	116.0	116.0					116.0	116.0					116.0	116.0					116.0	116.0										
Bankfull Mean Depth (ft)	2.4	2.4					2.2	2.1					2.2	2.0					2.3	2.3										
Bankfull Max Depth (ft)	3.9	4.0					3.5	3.6					4.7	4.7					3.5	3.5										
Bankfull Cross Sectional Area (ft ²)	71.7	71.7					68.6	68.6					88.1	88.1					61.0	61.0										
Bankfull Width/Depth Ratio	12.5	12.1					14.1	15.6					18.2	21.6					11.9	11.8										
Bankfull Entrenchment Ratio	3.9	3.9					3.7	3.5					2.9	2.7					4.3	4.3										
Bankfull Bank Height Ratio*	1.0	1.0					1.0	1.0					1.0	0.9					1.0	1.0										
Low Top of Bank Depth (ft)	-	3.9					-	3.5					-	4.2					-	3.6										

* Beginning in MY1 (2018), the bankfull elevation and channel cross-section dimensions have been calculated using a fixed Abkf as described in the Standard Measurement of the BHR Monitoring Parameter provided by NCIRT and NCDMS (9/2018)

Table 11b. Monitoring Data - Stream Reach Data Summary Shadrick Creek - Shadrick Creek Reach 1 (3,631 feet)																																				
Parameter	Baseline						MY - 1						MY - 2						MY - 3						MY - 4						MY - 5					
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n
Dimension & Substrate - Riffle																																				
Bankfull Width (ft)	26.6	29.3	28.7	32.7	3.1	3	25.9	29.5	29.1	33.6	3.9	3																								
Floodprone Width (ft)	100.0	100.0	100.0	100.0	0.0	3	100.0	100.0	100.0	100.0	0.0	3																								
Bankfull Mean Depth (ft)	1.8	1.8	1.8	1.8	0.0	3	1.8	1.8	1.8	1.8	0.0	3																								
Bankfull Max Depth (ft)	3.0	3.1	3.0	3.2	0.1	3	3.0	3.1	3.1	3.1	0.1	3																								
Bankfull Cross-Sectional Area (ft ²)	47.0	52.8	52.0	59.3	6.2	3	47.0	52.8	52.0	59.3	6.2	3																								
Width/Depth Ratio	15.0	16.3	15.8	18.0	1.5	3	14.2	16.5	16.3	19.0	2.4	3																								
Entrenchment Ratio	3.1	3.4	3.5	3.8	0.4	3	3.0	3.4	3.4	3.9	0.4	3																								
Bank Height Ratio	1.0	1.0	1.0	1.0	0.0	3	0.9	1.0	1.0	1.0	0.0	3																								
Profile																																				
Riffle Length (ft)																																				
Riffle Slope (ft/ft)																																				
Pool Length (ft)																																				
Pool Max Depth (ft)																																				
Pool Spacing (ft)																																				
Pattern																																				
Channel Belt Width (ft)																																				
Radius of Curvature (ft)																																				
Rc: Bankfull Width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
Additional Reach Parameters																																				
Rosgen Classification																																				
Channel Thalweg Length (ft)																																				
Sinuosity (ft)																																				
Water Surface Slope (Channel) (ft/ft)																																				
Bankfull Slope (ft/ft)																																				
Ri% / Ru% / P% / G% / S%																																				

- Information Unavailable
N/A - Information does not apply.
Ri = Riffle / Ru = Run / P = Pool / G = Glide / S = Step

Table 11b Cont'd. Monitoring Data - Stream Reach Data Summary Shadrick Creek - Shadrick Creek Reach 2 (573 feet)																																				
Parameter	Baseline						MY - 1						MY - 2						MY - 3						MY - 4						MY - 5					
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n
Dimension & Substrate - Riffle																																				
Bankfull Width (ft)	-	29.9	-	-	-	1	-	29.5	-	-	-	1																								
Floodprone Width (ft)	-	116.0	-	-	-	1	-	116.0	-	-	-	1																								
Bankfull Mean Depth (ft)	-	2.4	-	-	-	1	-	2.4	-	-	-	1																								
Bankfull Max Depth (ft)	-	3.9	-	-	-	1	-	4.0	-	-	-	1																								
Bankfull Cross-Sectional Area (ft ²)	-	71.7	-	-	-	1	-	71.7	-	-	-	1																								
Width/Depth Ratio	-	12.5	-	-	-	1	-	12.1	-	-	-	1																								
Entrenchment Ratio	-	3.9	-	-	-	1	-	3.9	-	-	-	1																								
Bank Height Ratio	-	1.0	-	-	-	1	-	1.0	-	-	-	1																								
Profile																																				
Riffle Length (ft)																																				
Riffle Slope (ft/ft)																																				
Pool Length (ft)																																				
Pool Max Depth (ft)																																				
Pool Spacing (ft)																																				
Pattern																																				
Channel Belt Width (ft)																																				
Radius of Curvature (ft)																																				
Rc: Bankfull Width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
Additional Reach Parameters																																				
Rosgen Classification																																				
Channel Thalweg Length (ft)																																				
Sinuosity (ft)																																				
Water Surface Slope (Channel) (ft/ft)																																				
Bankfull Slope (ft/ft)																																				
Ri% / Ru% / P% / G% / S%																																				

- Information Unavailable
N/A - Information does not apply.
Ri = Riffle / Ru = Run / P = Pool / G = Glide / S = Step

Table 11b Cont'd. Monitoring Data - Stream Reach Data Summary																																							
Shadrick Creek - UT9 Reach 1 (706 feet)																																							
Parameter	Baseline						MY - 1						MY - 2						MY - 3						MY - 4						MY - 5								
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n			
Dimension & Substrate - Riffle																																							
Bankfull Width (ft)	-	9.5	-	-	-	1	-	9.2	-	-	-	1																											
Floodprone Width (ft)	-	24.0	-	-	-	1	-	24.0	-	-	-	1																											
Bankfull Mean Depth (ft)	-	0.5	-	-	-	1	-	0.5	-	-	-	1																											
Bankfull Max Depth (ft)	-	1.1	-	-	-	1	-	1.3	-	-	-	1																											
Bankfull Cross-Sectional Area (ft ²)	-	4.8	-	-	-	1	-	4.8	-	-	-	1																											
Width/Depth Ratio	-	18.7	-	-	-	1	-	17.6	-	-	-	1																											
Entrenchment Ratio	-	2.5	-	-	-	1	-	2.6	-	-	-	1																											
Bank Height Ratio	-	1.0	-	-	-	1	-	1.0	-	-	-	1																											
Profile																																							
Riffle Length (ft)																																							
Riffle Slope (ft/ft)																																							
Pool Length (ft)																																							
Pool Max Depth (ft)																																							
Pool Spacing (ft)																																							
Pattern																																							
Channel Belt Width (ft)																																							
Radius of Curvature (ft)																																							
Re: Bankfull Width (ft/ft)																																							
Meander Wavelength (ft)																																							
Meander Width Ratio																																							
Additional Reach Parameters																																							
Rosgen Classification																																							
Channel Thalweg Length (ft)																																							
Sinuosity (ft)																																							
Water Surface Slope (Channel) (ft/ft)																																							
Bankfull Slope (ft/ft)																																							
Ri% / Ru% / P% / G% / S%																																							

- Information Unavailable
 N/A - Information does not apply.
 Ri = Riffle / Ru = Run / P = Pool / G = Glide / S = Step

Table 11b Cont'd. Monitoring Data - Stream Reach Data Summary																																							
Shadrick Creek - UT9 Reach 2 (238 feet)																																							
Parameter	Baseline						MY - 1						MY - 2						MY - 3						MY - 4						MY - 5								
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n			
Dimension & Substrate - Riffle																																							
Bankfull Width (ft)	-	8.3	-	-	-	1	-	7.7	-	-	-	1																											
Floodprone Width (ft)	-	24.0	-	-	-	1	-	24.0	-	-	-	1																											
Bankfull Mean Depth (ft)	-	0.4	-	-	-	1	-	0.5	-	-	-	1																											
Bankfull Max Depth (ft)	-	1.0	-	-	-	1	-	1.0	-	-	-	1																											
Bankfull Cross-Sectional Area (ft ²)	-	3.6	-	-	-	1	-	3.6	-	-	-	1																											
Width/Depth Ratio	-	19.0	-	-	-	1	-	16.2	-	-	-	1																											
Entrenchment Ratio	-	2.9	-	-	-	1	-	3.1	-	-	-	1																											
Bank Height Ratio	-	1.0	-	-	-	1	-	1.0	-	-	-	1																											
Profile																																							
Riffle Length (ft)	23.3	29.0	27.3	38.4	6.7	4	18.8	24.6	24.3	31.0	5.0	4																											
Riffle Slope (ft/ft)	0.016	0.022	0.020	0.033	0.008	4	0.014	0.022	0.021	0.030	0.007	4																											
Pool Length (ft)	5.6	10.2	11.2	12.6	3.1	4	7.1	12.2	11.1	19.3	5.3	4																											
Pool Max Depth (ft)	1.0	1.5	1.5	1.7	0.3	4	1.1	1.4	1.4	1.8	0.3	4																											
Pool Spacing (ft)	40.4	47.7	46.4	56.4	8.1	3	38.7	44.9	45.3	50.6	6.0	3																											
Pattern																																							
Channel Belt Width (ft)	24.5	30.0	29.0	36.6	6.1	3																																	
Radius of Curvature (ft)	13.3	15.2	15.4	16.9	1.8	3																																	
Re: Bankfull Width (ft/ft)	2.1	2.3	2.3	2.5	0.2	3																																	
Meander Wavelength (ft)	63.7	78.5	79.3	92.5	14.4	3																																	
Meander Width Ratio	3.1	3.8	3.6	4.6	0.8	3																																	
Additional Reach Parameters																																							
Rosgen Classification																																							
Channel Thalweg Length (ft)																																							
Sinuosity (ft)																																							
Water Surface Slope (Channel) (ft/ft)																																							
Bankfull Slope (ft/ft)																																							
Ri% / Ru% / P% / G% / S%	60%	13%	21%	6%	0%		51%	15%	25%	9%	0%																												

- Information Unavailable
 N/A - Information does not apply.
 Ri = Riffle / Ru = Run / P = Pool / G = Glide / S = Step

**Table 11b Cont'd. Monitoring Data - Stream Reach Data Summary
Shadrick Creek - UT10 (404 feet)**

Parameter	Baseline						MY - 1						MY - 2						MY - 3						MY - 4						MY - 5					
	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n
Dimension & Substrate - Riffle																																				
Bankfull Width (ft)	-	7.3	-	-	-	1	-	8.7	-	-	-	1																								
Floodprone Width (ft)	-	24.0	-	-	-	1	-	24.0	-	-	-	1																								
Bankfull Mean Depth (ft)	-	0.5	-	-	-	1	-	0.4	-	-	-	1																								
Bankfull Max Depth (ft)	-	1.1	-	-	-	1	-	1.1	-	-	-	1																								
Bankfull Cross-Sectional Area (ft ²)	-	3.4	-	-	-	1	-	3.4	-	-	-	1																								
Width/Depth Ratio	-	15.6	-	-	-	1	-	22.3	-	-	-	1																								
Entrenchment Ratio	-	3.3	-	-	-	1	-	2.8	-	-	-	1																								
Bank Height Ratio	-	1.0	-	-	-	1	-	0.9	-	-	-	1																								
Profile																																				
Riffle Length (ft)																																				
Riffle Slope (ft/ft)																																				
Pool Length (ft)																																				
Pool Max Depth (ft)																																				
Pool Spacing (ft)																																				
Pattern																																				
Channel Belt Width (ft)																																				
Radius of Curvature (ft)																																				
Rc: Bankfull Width (ft/ft)																																				
Meander Wavelength (ft)																																				
Meander Width Ratio																																				
Additional Reach Parameters																																				
Rosgen Classification																																				
Channel Thalweg Length (ft)																																				
Sinuosity (ft)																																				
Water Surface Slope (Channel) (ft/ft)																																				
Bankfull Slope (ft/ft)																																				
Ri% / Ru% / P% / G% / S%																																				

- Information Unavailable
N/A - Information does not apply.
Ri = Riffle / Ru = Run / P = Pool / G = Glide / S = Step

This Page Intentionally Left Blank

Appendix E

Hydrologic Data

This Page Intentionally Left Blank

**Table 12. Verification of Bankfull Events
Shadrick Creek Restoration Project**

Shadrick Reach 1				
Date of Data Collection	Date of Occurrence	Method	Feet Above Bankfull Elevation	Photo # (if available)
6/5/2018	Unknown ¹	Crest Gauge	0.05	1
11/8/2018	Unknown ²	Wrack Lines	Unknown	2
Shadrick Reach 3				
Date of Data Collection	Date of Occurrence	Method	Feet Above Bankfull Elevation	Photo # (if available)
2/5/2018	Unknown ³	Wrack Lines	Unknown	3
11/8/2018	Unknown ²	Crest Gauge	0.6	4

¹ Suspected date is 5/18/2018

² Suspected date is 10/18/2018

³ Suspected date is 1/12/2018

Photo Verification of Bankfull Events



Photo #1 – Shadrick Creek Reach 1 Crest Gauge at 1.2 feet (Recorded bankfull 1.2 feet)

Photo Verification of Bankfull Events



Photo #2 – Shadrick Creek Reach 1 STA 16+00 Wrack Lines



Photo #3 – Shadrick Creek Reach 3 STA 115+50 Wrack Lines

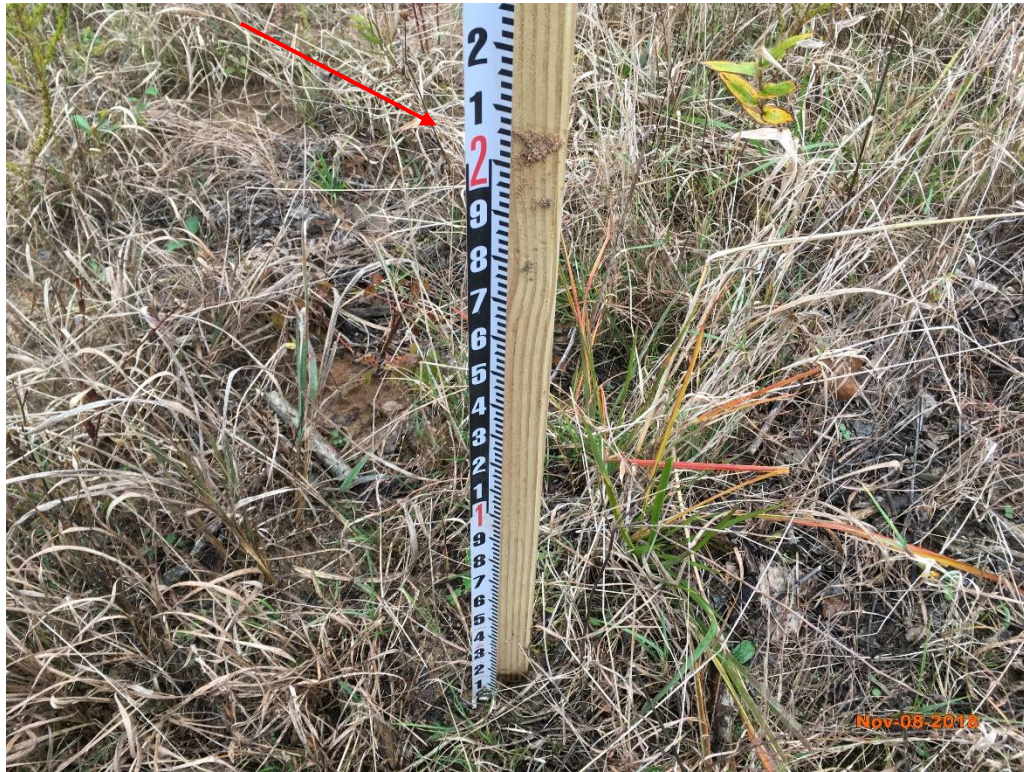


Photo #4 – Shadrick Creek Reach 3 Crest Gauge at 2.05 feet (Recorded bankfull 1.6 feet)

Figure 3. Daily Precipitation Totals for the Shadrick Creek Restoration Site

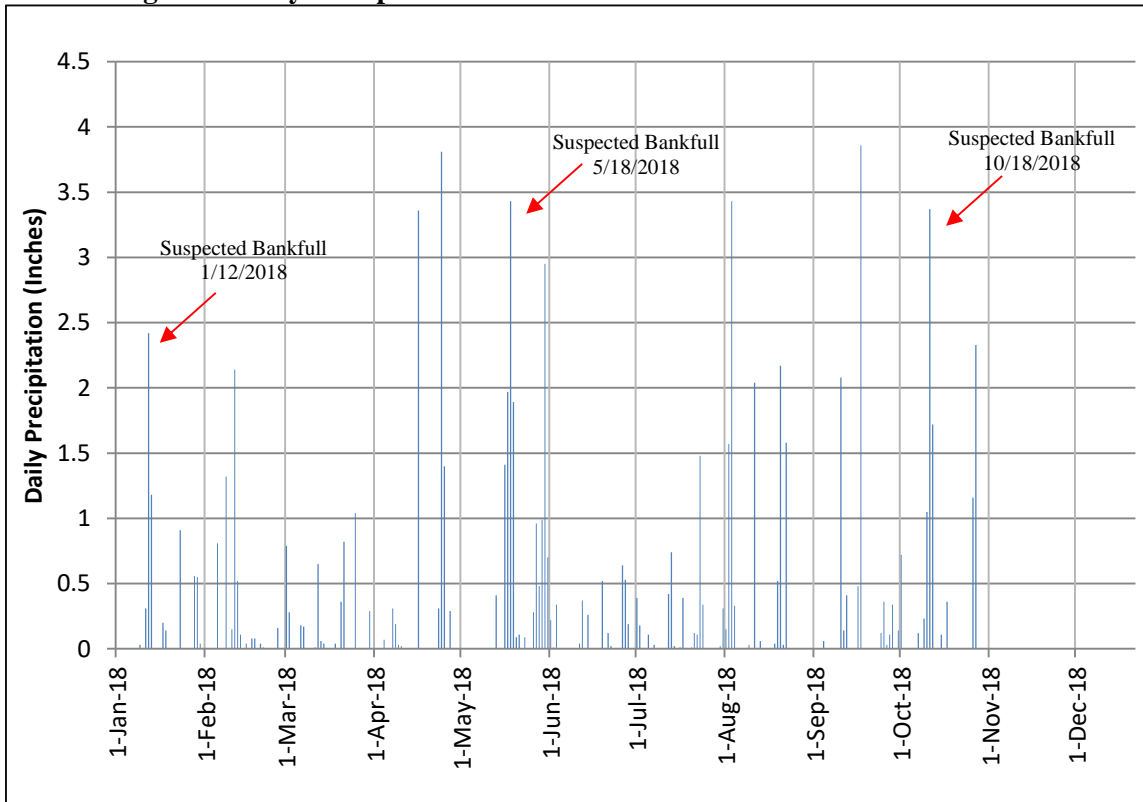


Figure 4. Monthly Precipitation Data Compared to 30th and 70th Percentiles for McDowell County

