

Upper Silver Creek Restoration Project Year 1 Monitoring Report

Burke County, North Carolina

NCDMS Project ID Number – 94645

Catawba River Basin: 03050101-050050



Project Info:

Monitoring Year: 1 of 5

Year of Data Collection: 2015

Year of Completed Construction: 2015

Submission Date: April 2016

Submitted To:

NCDEQ – Division of Mitigation Services

5 Ravenscroft Drive, Suite 102

Asheville, NC 28801

NCDEQ Contract ID No. 003270

Upper Silver Creek Restoration Project Year 1 Monitoring Report

**Burke County, North Carolina
NCDMS Project ID Number – 94645**

Report Prepared and Submitted by Michael Baker Engineering, Inc.
797 Haywood Road, Suite 201
Asheville, NC 28806

NC Professional Engineering License # F-1084



TABLE OF CONTENTS

1.0 EXECUTIVE SUMMARY	1
2.0 METHODOLOGY	3
2.1 <i>Vegetation Assessment</i>	3
2.2 <i>Stream Assessment</i>	3
2.2.1 Morphologic Parameters and Channel Stability	4
2.2.2 Hydrology	4
2.2.3 Photographic Documentation	4
2.3 <i>Wetland Assessment</i>	4
3.0 REFERENCES	5

APPENDICES

Appendix A	<i>Project Vicinity Map and Background Tables</i>
Figure 1	Project Vicinity Map and Directions
Figure 2	Current Conditions Plan View – MY1 Overview Map
Figure 2A	Current Conditions Plan View Monitoring Year 1 Upper Silver Creek Site – North Area
Figure 2B	Current Conditions Plan View Monitoring Year 1 Upper Silver Creek Site – South Area
Appendix B	<i>General Project Tables</i>
Table 1	Project Components and Mitigation Credits
Table 2	Project Activity and Reporting History
Table 3	Project Contacts
Table 4	Project Attributes
Appendix C	<i>Vegetation Assessment Data</i>
Table 5	Vegetation Plot Mitigation Success Summary
Table 6	CVS Vegetation Metadata
Table 7	Stem Count Arranged by Plot and Species
Figure 3	Vegetation Monitoring Plot Photos
Appendix D	<i>Stream Assessment Data</i>
Figure 4	Stream Photos by Channel and Station
Table 8	Visual Morphological Stability Assessment
Table 9	Verification of Bankfull Events
Figure 5	Cross-Sections with Annual Overlays
Figure 6	Longitudinal Profiles with Annual Overlays

Figure	7	Pebble Count Plots with Annual Overlays
Table	10	Monitoring Year 1 Stream Summary
Table	11	Morphology and Hydraulic Monitoring Summary

Appendix E *Hydrologic Data*

Figure	8	Wetland Gauge Graphs
Figure	9	Observed Rainfall versus Historic Average
Table	12	Wetland Gauge Attainment Data
Table	12a	Wetland Area Well Success
Figure	10	Wetland Photo Log

1.0 EXECUTIVE SUMMARY

Michael Baker Engineering, Inc. (Baker) restored or enhanced 5,186 linear feet (LF) of perennial stream channel along Silver Creek and three unnamed tributaries (UT1, UT2, and UT3); and additionally, Baker restored, enhanced or created approximately 9.14 acres of wetlands that had been previously disturbed in Burke County, NC, (Appendix A). The Upper Silver Creek Stream and Wetland Restoration Project (Site) is located southeast of Morganton, NC, approximately 11 miles southeast of the intersection of Highway 64 and I-40 and to the north of the intersection of Highway 64 and Goldmine Road. The Site is located in the NC Division of Water Resources (NCDWR) sub-basin 03-08-31 and the NCDEQ Division of Mitigation Services (NCDMS) Targeted Local Watershed (TLW) 03050101-050050 of the Catawba River Basin. The project involved the restoration and enhancement of a Piedmont/Mountain Mixed Bottomland Hardwood Forest system (NC WAM 2010, Schafale and Weakley 1990) from impairments within the project area due to past agricultural conversion, cattle grazing, gold mining and draining of floodplain wetlands by ditching activities.

The project goals directly addressed stressors identified in the Catawba River Basin Restoration Priority (RBRP) Plan such as degraded riparian conditions, channel modification, and excess sediment and nutrient inputs. The primary restoration goals, as outlined in the approved mitigation plan, are described below:

- Create geomorphically stable stream channels within the Upper Silver Creek project area including headwater tributaries in the Catawba River basin;
- Restore, enhance, and expand wetland functions across the Site;
- Improve and restore hydrologic connections between streams and degraded riparian wetland areas and overall ecosystem functionality;
- Improve water quality within the Upper Silver Creek project area through reduction of bank erosion, improved nutrient and sediment removal, and stabilization of streambanks;
- Improve aquatic and terrestrial habitat.

To accomplish these goals, we recommended the following actions:

- Restore the existing incised, eroding, and channelized stream by creating a stable channel that has access to its floodplain;
- Improve water quality by establishing buffers for nutrient removal from runoff and by stabilizing stream banks to reduce bank erosion;
- Improve in-stream habitat by providing a more diverse bedform with riffles and pools, creating deeper pools, developing areas that increase oxygenation, providing woody debris for habitat, and reducing bank erosion;
- Improve terrestrial habitat by planting riparian areas with native vegetation and protecting these areas with a permanent conservation easement. The riparian area will increase storm water runoff filtering capacity, improve bank stability, provide shading to decrease water temperature and improve habitat.

During Year 1, our monitoring indicated that the planted acreage was functioning well with no banks, benches or flood plain areas having bare areas of a significant size. The only invasive with significant coverage was Chinese privet, which was located in the existing forested area on the right bank of Silver Creek, both upstream and downstream of UT2. Chinese Privet within these areas will be treated with herbicide in the spring of 2016. An additional issue affecting Site vegetation was mowing encroachment. There were six areas along the easement line where the landowner encroached into the easement while attempting to mow outside of the easement line. These areas were pointed out to the landowner and we discussed the need to avoid encroaching

into the easement. The easement line in these areas will be better marked with witness posts before the landowner needs to mow again.

As noted in the Baseline report, we added five additional vegetation monitoring plots at the Site to increase the total from 9 to 14. The location of these new plots can be seen on Figures 2A and 2B, designated 10 through 14. The average density of total planted stems following the Year 1 growing season is 804 stems per acre (n=14). There were no volunteer stems growing at this time. With an average density of 804 stems per acre, the Site is on track to meet the minimum interim success criteria of 320 stems per acre by the end of Year 3, and the final success criteria of 260 stems per acre by the end of Year 5.

Stream geomorphological stability and performance during Year 1 was assessed by surveying sixteen (16) cross-sections (7 on Silver Creek, 2 on UT1, 2 on UT2 and 5 on UT3) and a profile of each channel, evaluating the bed particle size with 5 riffle pebble counts and by observation and replicating channel location photographs. Cross-sections of all the channels indicated that high flows had deposited sediment on the floodplain and decreased cross-sectional area slightly. Deposition was also shown on the profiles of each channel and these indicate that some pools decreased in maximum depth. This observed deposition is not unusual during the first year as pool depth reaches an equilibrium with sediment supply and discharge. The Visual Morphological Stability Assessment indicates that the Site is stable and performing at 100 percent for all parameters on most reaches. We did find that on Reach 2 of Silver Creek, 3 of the 21 structures in this reach were piping water under a vane arm. These structures were repaired on August 27 & 28, 2015. Channel morphology is responding as designed and meeting project goals.

There were no bankfull event recorded on the crest gauge during Year 1 and there was no physical indication of over bank flooding. Stream pebble count data indicated a shift to smaller particle sizes at XS7 on Silver Creek and on UT2. There was an increase in smaller particle sizes for the fraction less than D35 at XS8 of UT3, but the fraction D50 and above was similar to that estimated in the baseline data. Pebble data from XS4 on Silver Creek and on UT1 showed particle sizes were either the same as baseline data or slightly larger. This indicates that the smaller particle sizes of the native bed material are being transported into, and through, the project reaches. This indicates a properly functioning system, as there were no mid-channel bars or other sediment transport issues.

Wetland monitoring during Year 1 demonstrated that four of the twelve groundwater monitoring wells located on the Site met the wetland success criteria as stated in the Site Mitigation Plan. The gauges that met success criteria (USAW1, USAW5, MSAW7 and MSAW9) demonstrated consecutive hydroperiods of 12 percent or greater, these ranged from 17.1 to 38.7 percent of the growing season. The gauges that did not meet success criteria (USAW2, USAW3, USAW4, USAW6, USAW8, USAW10, USAW11 and USAW12) demonstrated consecutive hydroperiods of 12 percent or less, with a range from 1.2 percent to 10.5 percent of the growing season. Baker will continue to monitor the groundwater hydrology of the Site wetlands into Year 2. In December 2015, after an amendment to the Mitigation Plan was approved, one (1) additional well (USAW13) was installed in an area of jurisdictional wetland being enhanced, designated JDW1a (See CCPV). This well was installed to document the groundwater level of this non-riparian wetland area.

To evaluate annual rainfall in the project vicinity we utilized four CRONOS data recording stations that are within close proximity (11.5 to 17.4 miles from the site) to the project site. These stations were all different concerning the "Type of Station", which indicates a difference in data collection methodology. However, in spite of these differences the data collected were very similar and certainly indicate the same pattern in rainfall. These data indicate that 2015 was relatively dry through winter, spring and summer with the exception of April, which was normal or slightly above normal. September through December were exceptionally wet months with rainfall that far exceeded the historic 70th percentile of average rainfall. According to the 2015 rainfall data, a large portion of the year experienced definitively lower than normal amounts of precipitation. Rainfall near the project was determined to be at or below the 30th percentile for seven of the first eight months of the year (exception of April), through the month of August. Therefore, 2015 is considered to be below the normal range

for the growing season. The dry conditions documented in this area are likely the reason that many of our gauges failed to meet the established success criteria.

Summary information/data related to the Site and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report Appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report and in the Mitigation Plan available on the NCDMS website. All raw data supporting the tables and figures in the appendices are available from NCDMS upon request.

2.0 METHODOLOGY

The monitoring plan for the Site includes criteria to evaluate the success of the stream, wetland and vegetation components of the project. The methodology and report template used to evaluate these components adheres to the NCDMS monitoring guidance document dated December 1, 2009 and other mitigation guidance (NCEEP 2009 and USACE 2003), which will continue to serve as the template for subsequent monitoring years. The specific locations of monitoring features: vegetation plots, permanent cross-sections, monitoring wells, flow gauges, and the crest gauge, are shown on the CCPV sheets found in Appendix B.

The Year 1 monitoring data were collected between October and early December 2015. Site photographic data was collected in February 2016.

2.1 Vegetation Assessment

In order to determine if success criteria are achieved, vegetation monitoring quadrants (veg plots) were installed and are monitored across the Site in accordance with the CVS-NCDMS Protocol for Recording Vegetation, Version 4.1 (CVS 2007 and Lee, Peet, Roberts and Wentworth 2007). The vegetation monitoring plots are a minimum of two percent of the planted portion of the Site with 14 plots established randomly within the planted riparian buffer and wetland area, per CVS Monitoring Level 2. No veg plots were established within the undisturbed wooded areas along the right bank of Silver Creek. The sizes of individual quadrants are 100 square meters for woody (tree) species and 1 meter for herbaceous vegetation. Herbaceous vegetation quadrants were established in one corner of the larger woody vegetation plots and are monitored by comparative photographs taken each year.

The existing trees were visually monitored during the annual site visits to document any mortality, due to construction activities or changes to the water table, which could negatively impact existing forest cover or favorable buffer vegetation. Year 1 monitoring found that all vegetation was in good condition. All vegetation monitoring quadrants indicated that vegetation was growing and in good to excellent condition. The average density of planted stems following the Year 1 growing season is 804 stems per acre (n=14). There were no volunteer stems growing at this time. With an average density of 804 stems per acre, the Site is on track to meet the minimum interim success criteria of 320 stems per acre by the end of Year 3, and the final success criteria of 260 stems per acre by the end of Year 5.

Invasive species areas of concern were observed and documented accordingly during Year 1. Monitoring indicated that there were two areas found to contain the invasive species, Chinese privet. To control this invasive species, these areas are scheduled to be treated in 2016 during the appropriate treatment window by use of the herbicide Glyphosate. There were six areas along the easement line where the landowner encroached into the easement while attempting to mow the area outside of the easement line. The easement line in these areas will be better marked with witness posts to make clear the line location.

No other areas of concern regarding the existing vegetation was observed along Silver Creek, UT1, UT2 or UT3. Year 1 vegetation assessment information is provided in Appendix C.

2.2 Stream Assessment

The Upper Silver Creek Site approach for the channels the restoration of a stable morphology that allows for the transport of water and sediment through the Site and allows stream flows larger than bankfull flows to spread onto the floodplain. Stream monitoring efforts focus on visual observations, a crest gauge to document bankfull flooding events, surveying established stream cross-sections and channel profiles to assess channel stability and pebble counts to assess if proper sediment transport is taking place.

Stream survey data was collected to a minimum of Class C Vertical and Class A Horizontal Accuracy using Leica TS06 Total Station and was georeferenced to the NAD83 State Plane Coordinate System, FIPS3200 in US Survey Feet, which was derived from the As-built Survey. This survey system collects point data with an accuracy of less than one tenth of a foot.

2.2.1 Morphologic Parameters and Channel Stability

Cross-sections were classified using the Rosgen Stream Classification System (Rosgen 1994) and all cross-sections were evaluated to determine if they meet design expectations. Cross-sections were also compared to the baseline cross-section plots to evaluate change between construction and the MY1 survey. Morphological survey data is presented in Appendix D.

A longitudinal profile was surveyed for the entire length of each channel to document changes from the as-built baseline conditions during the first year of monitoring. The survey was tied to a permanent benchmark and measurements included thalweg, water surface, and top of low bank. Each of these measurements was taken at the head of each feature (e.g., riffle, pool) and at the maximum pool depth.

2.2.2 Hydrology

Two crest gauge were installed on the floodplain at the bankfull elevation along the left top of bank on Silver Creek approximately at Station 19+00 and on the right bank of UT3 approximately at Station 9+50. No bankfull-flow events were recorded on the two Site crest gauges during the MY1 data collection period, which primarily extended from April 1, 2015 to November 30, 2015. This is commonly a drier time of the year in this part of North Carolina, which was the case during 2015. Crest gauge readings are presented in Appendix D.

2.2.3 Photographic Documentation

Reference transects were photographed at each permanent cross-section. The survey tape was centered in the photograph of the bank. The water line was located in the lower area of the frame, and as much of the bank as possible included in each photograph. Photographs were also taken at specific photo points established along each channel during baseline reporting. Photographs from these points will be replicated each year and used to document changes along the channel. Points were selected to include grade control structures as well as other structural components installed during construction. Annual photographs from the established photo points are shown in Appendix D.

2.3 Wetland Assessment

Thirteen automated groundwater-monitoring stations were installed in the wetland restoration area in order to document the hydrologic conditions during the monitoring period. The installations followed

USACE protocols (USACE 1997). Groundwater data collected during Year 1 monitoring are located in Appendix E.

To meet the hydrologic success criteria, the monitoring gauge data must show that for each normal rainfall year within the monitoring period, the Site has been inundated or saturated for a certain hydroperiod. Success criteria for wetland hydrology will be based on standards for atypical wetland areas (USACE, 2005). Criteria have been met when the wetland is saturated within 12 inches of the soil surface for 12 percent of the growing season when rainfall amounts mimic normal conditions. Alternatively, when dry conditions prevail, we may use the fourteen (14) or more consecutive days during the growing season when antecedent precipitation has been drier than normal for a minimum frequency of 5 years in 10 to 50 percent of the monitoring period (USACE, 1987 and 2005).

Visual monitoring of wetland areas will be conducted annually. Photographs will be used to visually document system performance and identify areas of low stem density, invasive species vegetation, beaver activity, or other areas of concern. Reference stations will be photographed each year for a minimum of five years following construction. Photographs will be taken from a height of approximately five to six feet. Permanent well markers were established and used to ensure that the same locations (and view directions) on the Site are documented in each monitoring period.

3.0 REFERENCES

- Carolina Vegetation Survey (CVS) and NC Ecosystem Enhancement Program (NCEEP). 2007. CVS-NCEEP Data Entry Tool v. 2.3.1. University of North Carolina, Raleigh, NC.
- Lee, M., Peet R., Roberts, S., Wentworth, T. 2007. CVS-NCEEP Protocol for Recording Vegetation, Version 4.1.
- North Carolina Ecosystem Enhancement Program (NCEEP). 2009. Guidance and Content Requirements for EEP Monitoring Reports Version 1.2.1. December 1, 2009.
- Rosgen, D. L. 1994. A Classification of Natural Rivers. *Catena* 22:169-199.
- Schafale, M. P., and A. S. Weakley. 1990. Classification of the natural communities of North Carolina, third approximation. North Carolina Natural Heritage Program. Division of Parks and Recreation, NCDENR. Raleigh, NC.
- United States Army Corps of Engineers (USACE). 1987. Corps of Engineers Wetlands Delineation Manual. Technical Report Y-87-1. Environmental Laboratory. US Army Engineer Waterways Experiment Station. Vicksburg, MS.
- _____. 1997. Corps of Engineers Wetlands Research Program. Technical Note VN-rs-4.1. Environmental Laboratory. U.S. Army Engineer Waterways Experiment Station. Vicksburg, MS.
- _____. 2005. "Technical Standard for Water-Table Monitoring of Potential Wetland Sites," WRAP Technical Notes Collection (ERDC TN-WRAP-05-2), U.S. Army Engineer Research and Development Center. Vicksburg, MS.
- _____. 2003. Stream Mitigation Guidelines, April 2003, U.S. Army Corps of Engineers. Wilmington District.

Appendix A

General Figures and Plan Views

Includes:



Figure 1. Project Vicinity Map and Directions

Figure 2. Current Condition Plan View (CCPV) – Overview
Map

Figure 2A. CCPV North half of Project

Figure 2B. CCPV South half of Project

To reach the project site from Asheville, follow Interstate 40 East and take the NC-226 exit (Exit 86). From the exit, turn left onto NC-226 and continue for 10.5 miles before turning left to take the US-64 ramp. Turn left onto US-64 and continue for 2.5 miles before turning left onto Gold Mine Road. Once on Gold Mine Road, travel for approximately .75 miles and turn right at a gate into the project site. The project site begins where Silver Creek passes under US-64 and continues downstream for approximately 3,000 LF. Unnamed tributaries 1 and 3 flow to the east under Gold Mine Road before converging with Silver Creek. Unnamed tributary 2 enters Silver Creek upstream of the UT1 confluence and flows westward to Silver Creek from a forested area.

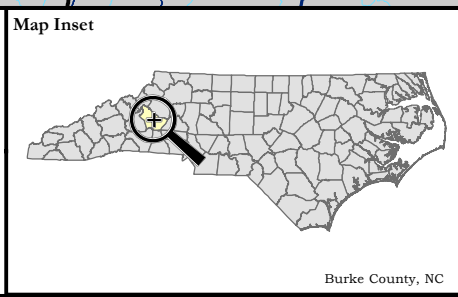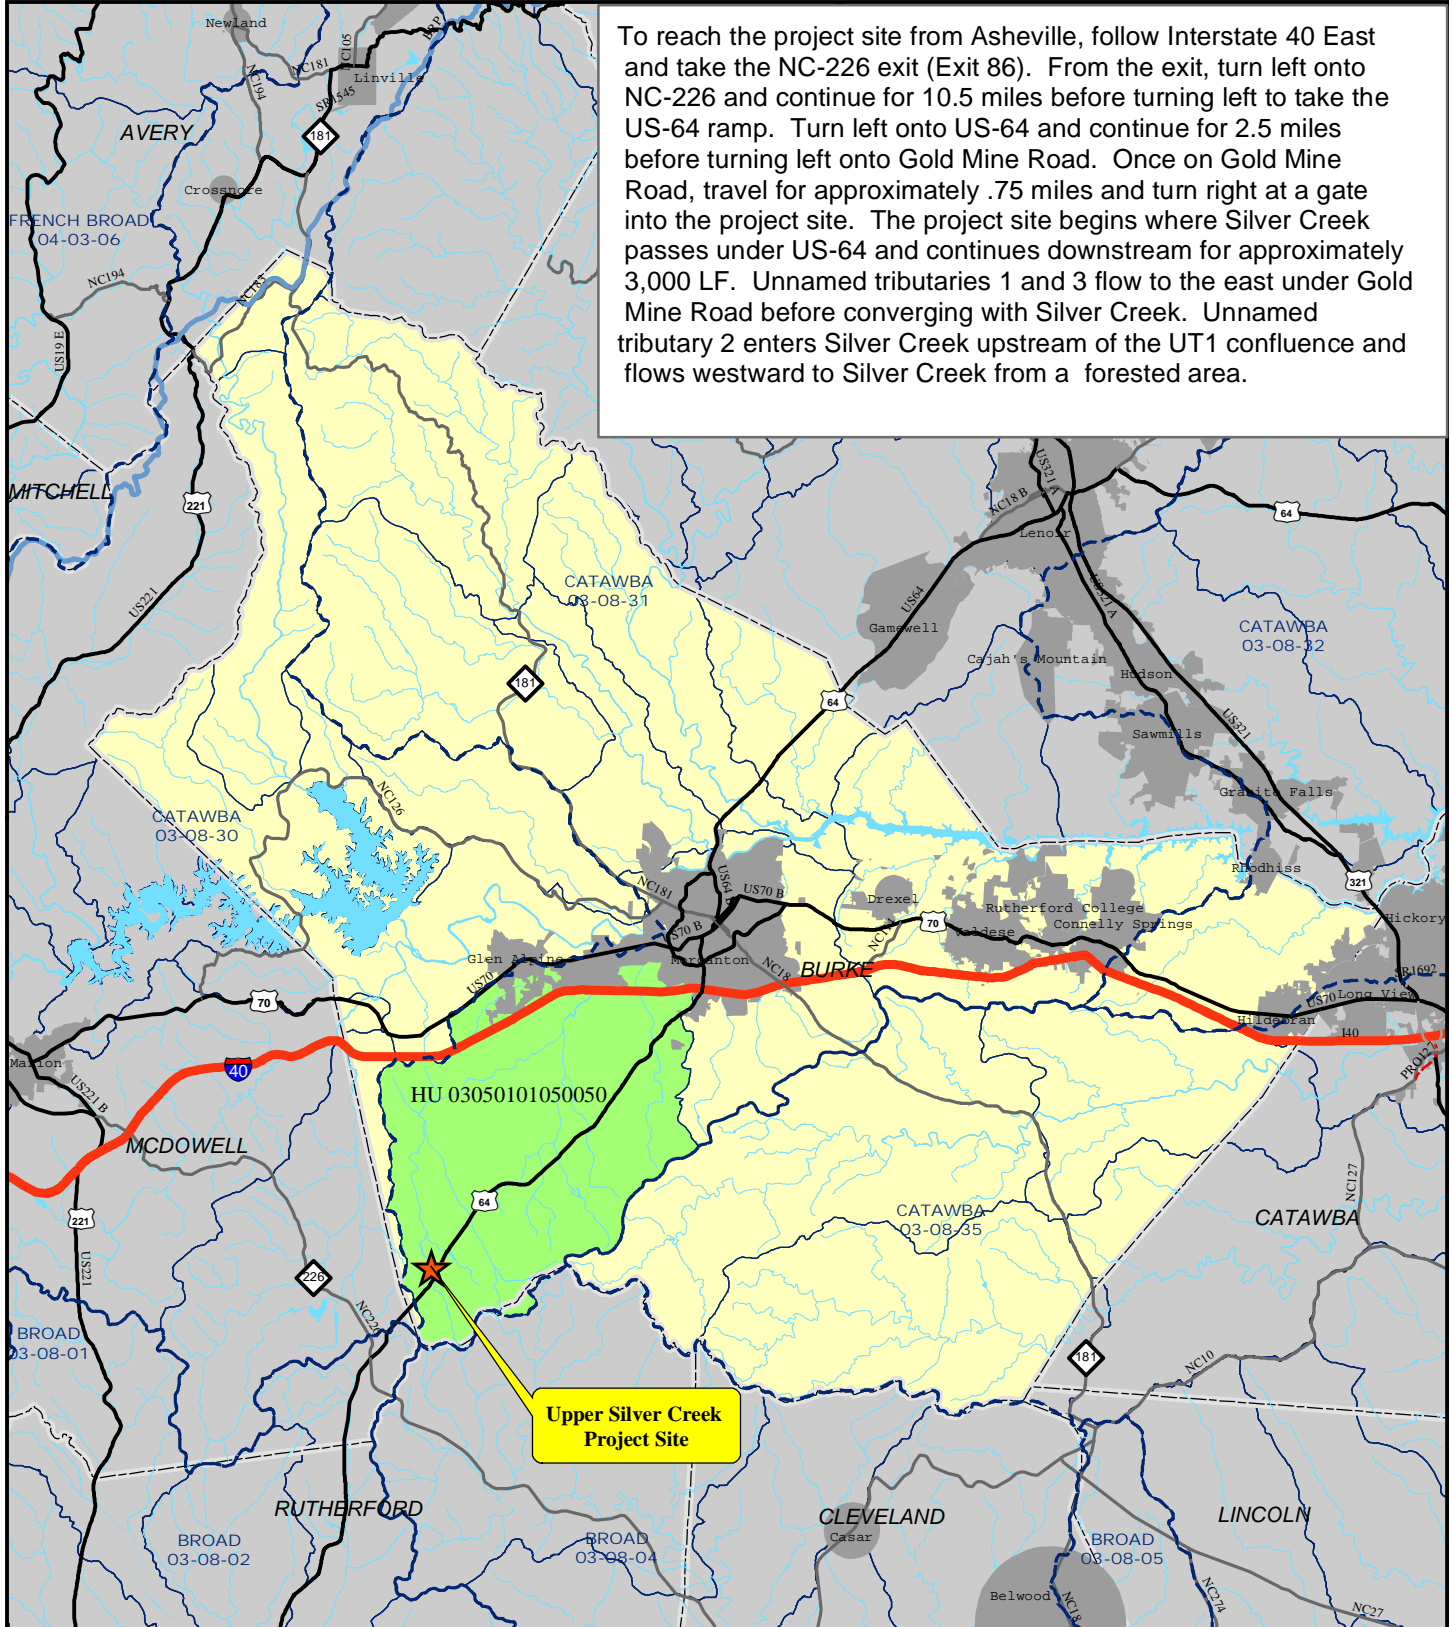

Division of Mitigation Services

LEGEND:

- NCDWR Sub-basin
- Counties
- USGS Hydrologic Unit
- Project Hydrologic Unit
- Burke County

0 1 2 4 Miles

Figure 1. Project Vicinity Map

**Upper Silver Creek
NCDMS Project #94645
Monitoring Year 1 Report
Burke County, NC**

**Michael Baker
INTERNATIONAL**




Fig2A



Fig2B


NC OneMap, NC Center for Geographic Information and Analysis, NC 911 Board

Michael Baker
INTERNATIONAL



DMS Project # 94645

Figure 2
Current Conditions Plan View - MY1
Overview Map
Upper Silver Creek Site

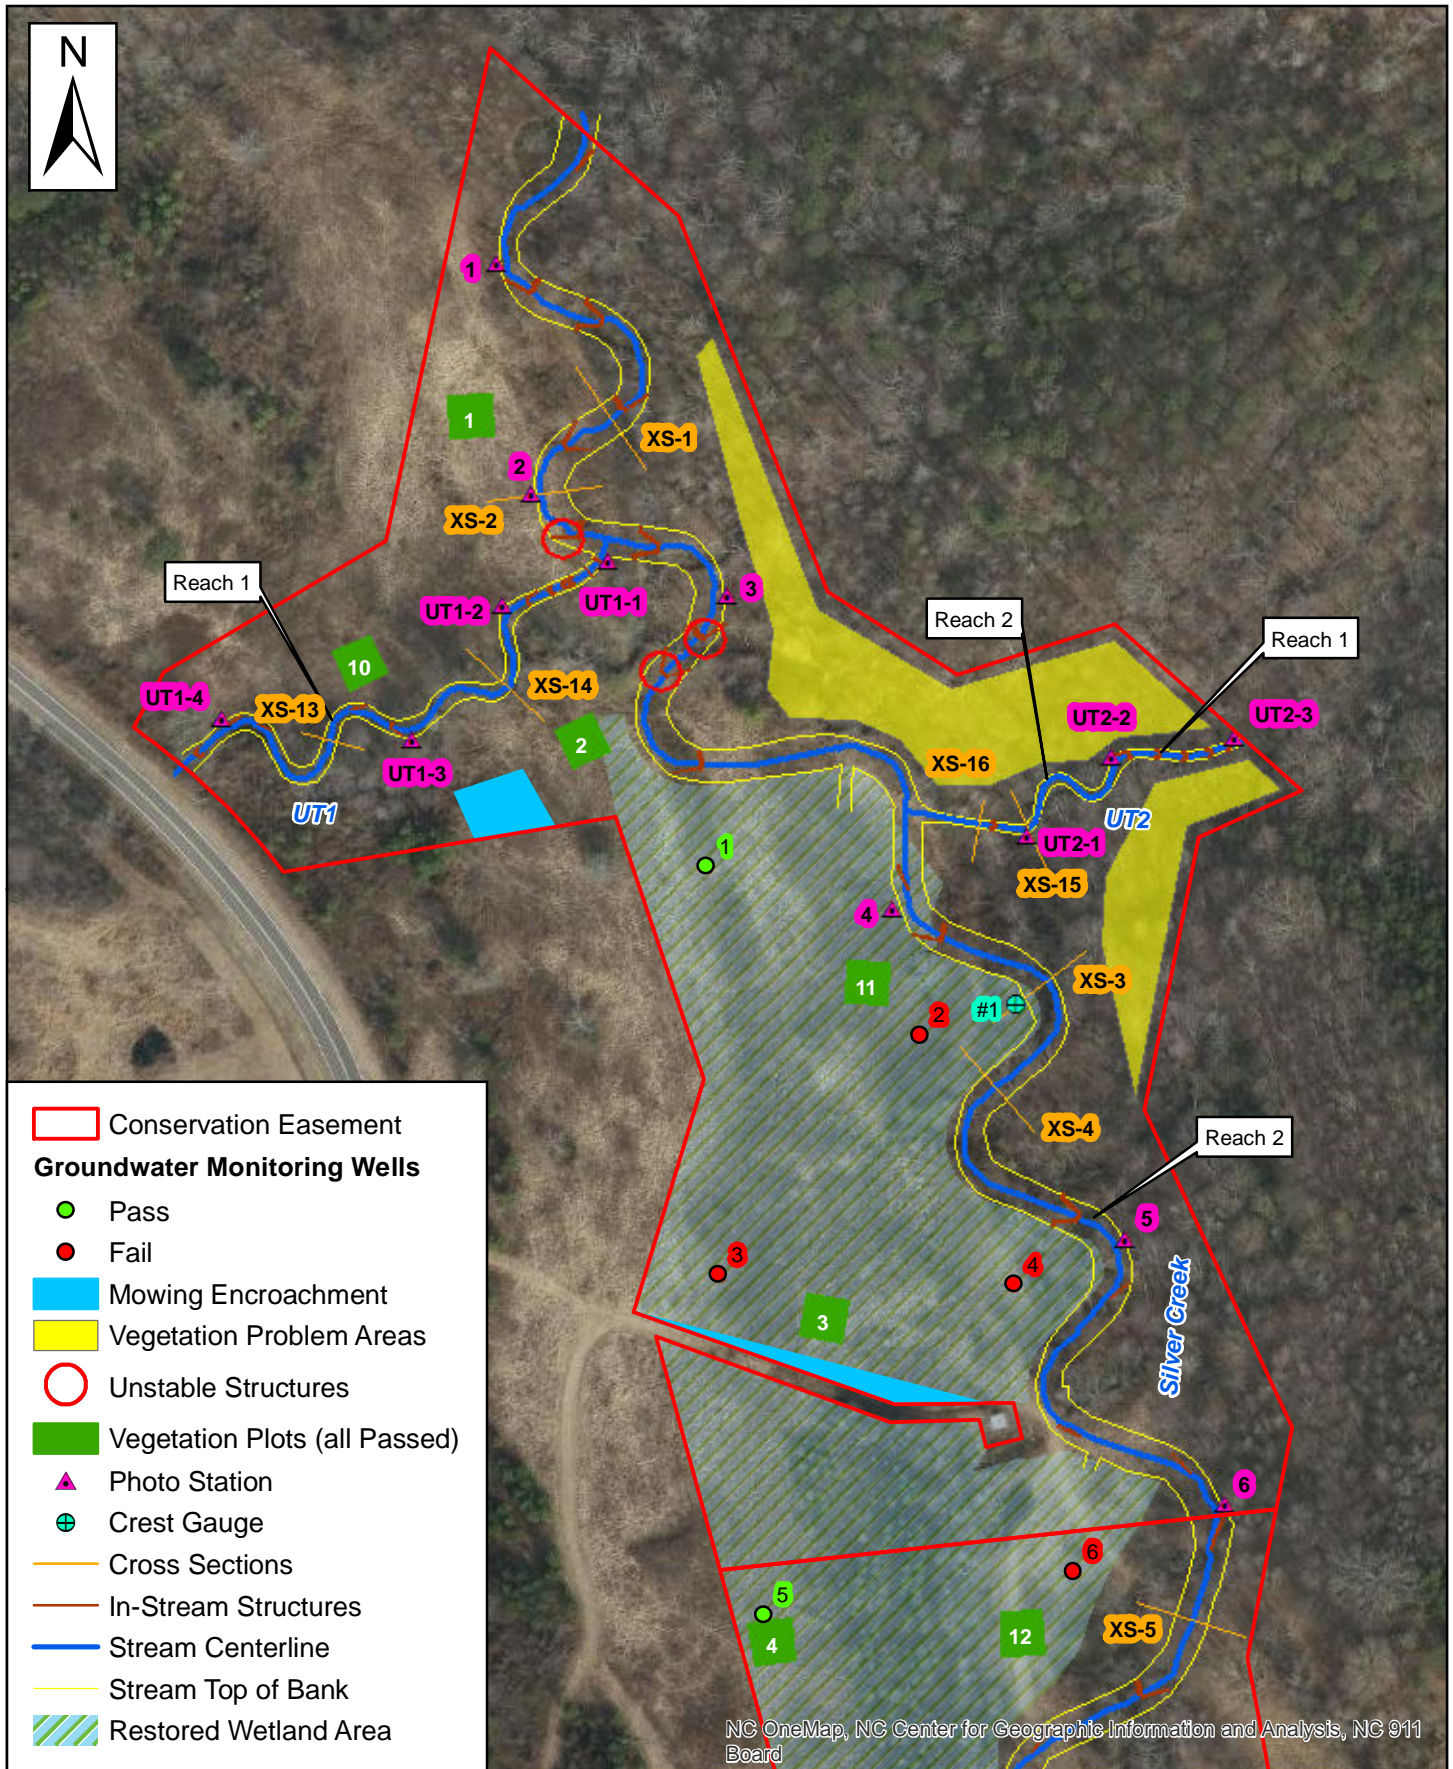

- Conservation Easement
- Groundwater Monitoring Wells**
- Pass
- Fail
- Mowing Encroachment
- Vegetation Problem Areas
- Unstable Structures
- Vegetation Plots (all Passed)
- ▲ Photo Station
- ⊕ Crest Gauge
- Cross Sections
- In-Stream Structures
- Stream Centerline
- Stream Top of Bank
- Restored Wetland Area


NC OneMap, NC Center for Geographic Information and Analysis, NC 911 Board

Michael Baker
INTERNATIONAL



Figure 2A
Current Conditions Plan View
Monitoring Year 1
Upper Silver Creek Site

DMS Project # 94645

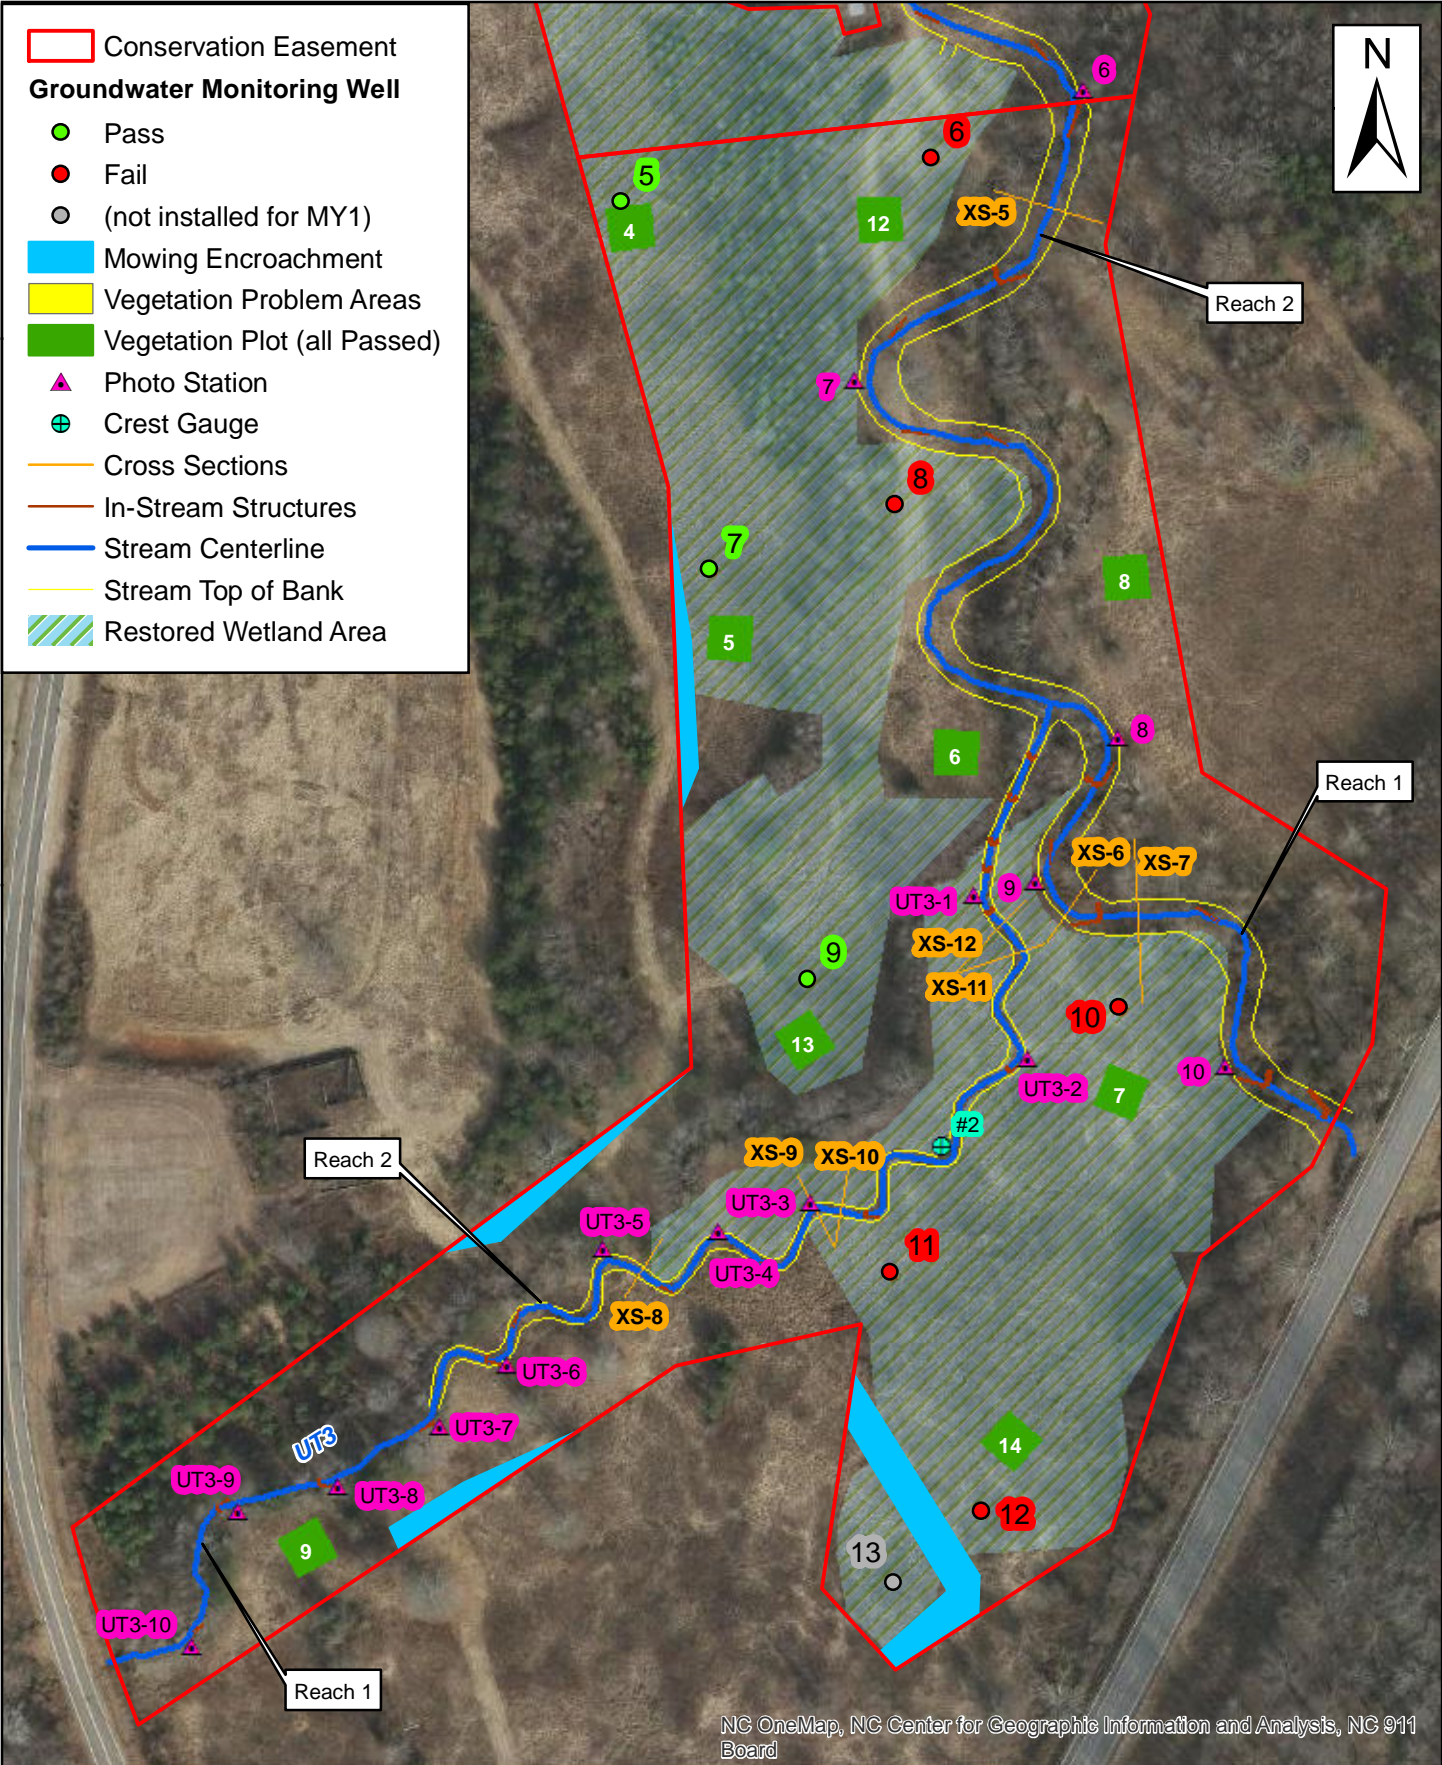

Michael Baker
INTERNATIONAL

DMS Project # 94645

Figure 2B
Current Conditions Plan View
Monitoring Year 1
Upper Silver Creek Site

Appendix B

General Project Tables

Includes:

- Table 1. Project Restoration Components and Mitigation Credits
- Table 2. Project Activity and Reporting History
- Table 3. Project Contacts
- Table 4. Project Attributes

Table 1. Project Components and Mitigation Credits											
Upper Silver Creek Restoration Project: DMS Project ID No. 94645											
Mitigation Credits											
	Stream		Riparian Wetland			Non-riparian Wetland			Buffer	Nitrogen Nutrient Offset	Phosphorus Nutrient Offset
Type	R	EII	R	E	C	R	E	C			
Totals	4,843 SMU	137 SMU	4.67 WMU	1.43 WMU	0.33 WMU	0.21 WMU	0.21 WMU				
Project Components											
Project Component or Reach ID	Stationing/ Location		Existing Footage/ Acreage		Approach	Restoration/ Restoration Equivalent	Restoration Footage or Acreage	Mitigation Ratio			
STREAMS											
Silver Creek											
Reach 1	0+32 to 8+70		2643 LF		Restoration - PII	838 SMU	838 LF	1:1			
Reach 2	8+70 to 30+48				Restoration - PI	2,178 SMU	2178 LF	1:1			
UT1											
Reach 1	0+07 to 5+02		478 LF		Restoration - PI	495 SMU	495 LF	1:1			
UT2											
Reach 1	0+00 to 1+03		187 LF		Restoration - PI	103 SMU	103 LF	1:1			
Reach 2	1+03 to 3+10				Restoration - PI	207 SMU	207 LF	1:1			
UT3											
Reach 1	0+00 to 3+43		1,162 LF		Enhancement I	137 SMU	343 LF	2.5:1			
Reach 2	3+43 to 13+65				Restoration - PI	1,022 SMU	1,022 LF	1:1			
WETLANDS											
See plan sheets											
JDW1a (NR)			0.42 AC		Enhancement	0.21 WMU	0.42 AC	2:1			
JDW1b (Ri)			1.01 AC		Enhancement	0.51 WMU	1.01 AC	2:1			
JDW2 (Ri)			0.51 AC		Enhancement	0.25 WMU	0.51 AC	2:1			
JDW3 (Ri)			0.03 AC		Enhancement	0.02 WMU	0.03 AC	2:1			
JDW4 (Ri)			0.24 AC		Enhancement	0.12 WMU	0.24 AC	2:1			
JDW5 (Ri)			0.81 AC		Enhancement	0.40 WMU	0.81 AC	2:1			
JDW6 (Ri)			0.25 AC		Enhancement	0.13 WMU	0.25 AC	2:1			
R1A (NR)			0		Restoration	0.06 WMU	0.06 AC	1:1			
R1B (NR)			0		Restoration	0.15 WMU	0.15 AC	1:1			
R2 (Ri)			0		Restoration	1.22 WMU	1.22 AC	1:1			
R3 (Ri)			0		Restoration	0.18 WMU	0.18 AC	1:1			
R4 (Ri)			0		Restoration	0.44 WMU	0.44 AC	1:1			
R5 (Ri)			0		Restoration	1.29 WMU	1.29 AC	1:1			
R6 (Ri)			0		Restoration	1.54 WMU	1.54 AC	1:1			
C1 (Ri)			0		Creation	0.33 WMU	0.99 AC	3:1			
Component Summation											
Restoration Level	Stream (LF)		Riparian Wetland (AC)		Non-riparian Wetland (AC)	Buffer (SF)	Upland (AC)				
			Riverine	Non-Riverine							
Restoration	4,843		4.67		0.21						
Enhancement I			2.85		0.42						
Enhancement II	342										
Creation			0.99								
Preservation											
High Quality Preservation											
BMP Elements											
Element	Location	Purpose/Function	Notes								
BMP Elements: BR= Bioretention Cell; SF= Sand Filter; SW= Stormwater Wetland; WDP= Wet Detention Pond; DDP= Dry Detention Pond; FS= Filter Strip; S= Grassed Swale; LS= Level Spreader; NI=Natural Infiltration Area											

Table 2. Project Activity and Reporting History			
Upper Silver Creek Restoration Project: DMS Project ID No. 94645			
Activity or Report	Scheduled Completion	Data Collection Complete	Actual Completion or Delivery
Mitigation Plan Prepared	Jan-13	N/A	Jan-13
Mitigation Plan Amended	Sep-13	N/A	Sep-13
Mitigation Plan Approved	Oct-13	N/A	Oct-13
Final Design – (at least 90% complete)	N/A	N/A	May-14
Construction Begins	N/A	N/A	May-14
Temporary S&E mix applied to entire project area	N/A	N/A	Dec-14
Permanent seed mix applied to entire project area	N/A	N/A	Dec-14
Planting of live stakes	Winter 2015	N/A	Feb-15
Planting of bare root trees	N/A	N/A	Feb-15
End of Construction	N/A	N/A	Dec-14
Survey of As-built conditions (Year 0 Monitoring-baseline)	N/A	Mar-15	Jul-15
Repair of 3 piping structures	N/A	N/A	Aug-15
Mitigation Plan Addendum	N/A	N/A	Dec-15
Year 1 Monitoring	Dec-15	Dec-15	Apr-16
Year 2 Monitoring	Dec-16	N/A	N/A
Year 3 Monitoring	Dec-17	N/A	N/A
Year 4 Monitoring	Dec-18	N/A	N/A
Year 5 Monitoring	Dec-19	N/A	N/A

Table 3. Project Contacts	
Upper Silver Creek Restoration Project: DMS Project ID No. 94645	
Designer	
Michael Baker Engineering, Inc.	797 Haywood Rd Suite 201 Asheville, NC 28806 <u>Contact:</u> Micky Clemmons, Tel. 828-412-6100
Construction Contractor	
River Works, Inc.	6105 Chapel Hill Road Raleigh, NC 27607 <u>Contact:</u> Phillip Todd, Tel. 919-582-3575
Planting Contractor	
River Works, Inc.	6105 Chapel Hill Road Raleigh, NC 27607 <u>Contact:</u> Phillip Todd, Tel. 919-582-3575
Seeding Contractor	
River Works, Inc.	6105 Chapel Hill Road Raleigh, NC 27607 <u>Contact:</u> Phillip Todd, Tel. 919-582-3575
Seed Mix Sources	Green Resources (seed), Tel. 336-855-6363
Nursery Stock Suppliers	Mellow Marsh Farm (trees), 919-742-1200 ArborGen Inc. (trees), 843-528-3204 Dykes and Son (trees), 931-668-8833
Monitoring Performers	
Michael Baker Engineering, Inc.	797 Haywood Rd Suite 201 Asheville, NC 28806 <u>Contact:</u>
Stream Monitoring Point of Contact	Micky Clemmons, Tel. 828-412-6100
Vegetation Monitoring Point of Contact	Micky Clemmons, Tel. 828-412-6100
Wetland Monitoring Point of Contact	Micky Clemmons, Tel. 828-412-6100

Table 4. Project Attributes			
Upper Silver Creek Restoration Project: DMS Project ID No. 94645			
Project Information			
Project Name	Upper Silver Creek Mitigation Project		
County	Burke		
Project Area (acres)	22.0		
Project Coordinates (latitude and longitude)	35.6078 N, -81.81742 W		
Watershed Summary Information			
Physiographic Province	Blue Ridge (borders Piedmont)		
River Basin	Catawba		
USGS Hydrologic Unit 8-digit and 14-digit	03050101 / 03050101050050		
DWR Sub-basin	03-08-31		
Project Drainage Area (AC)	Mainstem 2.7 - 3.3, UT1 0.28, UT2 0.05, UT3 0.17		
Project Drainage Area Percentage of Impervious Area	<2%		
USGA Land Use Classification	Deciduous Forest (64%)	Woody Wetlands (1%)	
	Evergreen Forest (3%)	Developed, Open Space (5%)	
	Shrub/Scrub (5%)	Pasture/Hay (14%)	
	Grassland/Herbaceous (6%)		
NCDMS Land Use Classification for Silver Creek Watershed	Forest (59%)		
	Agriculture (23%)		
	Impervious Cover (2.9%)		
Stream Reach Summary Information			
Parameters	Mainstem - Reach 1	Mainstem - Reach 2	
Length of Reach (LF)	838	2,178	
Valley Classification (Rosgen)	VIII	VIII	
Drainage Area (AC)	1,746	2,147	
NCDWR Stream Identification Score	49.5	49.5	
NCDWR Water Quality Classification	C	C	
Morphological Description (Rosgen stream type)	E	E	
	Incised channel, little connection to floodplain	Incised channel, little connection to floodplain	
Evolutionary Trend	E→G, E→C/F	E→G, E→C/F	
Underlying Mapped Soils	AaA, FnA, UnB	AaA, FnA, UnB	
Drainage Class	Somewhat poorly to well drained	Somewhat poorly to well drained	
Soil Hydric Status	Site-specific	Site-specific	
Average Channel Slope (ft/ft)	0.004	0.004	
FEMA Classification	Zone AE	Zone AE	
Native Vegetation Community	Piedmont/Mtn. Mixed Bottomland Hardwoods	Piedmont/Mtn. Mixed Bottomland Hardwoods	
Percent Composition of Exotic/Invasive Vegetation	10%	5%	
Parameters	UT1 - Reach 1	UT2 - Reach 1	UT2 - Reach 2
Length of Reach (LF)	495	103	207
Valley Classification (Rosgen)	III	III	III
Drainage Area (AC)	177	32	32
NCDWR Stream Identification Score	47.5	45	45
NCDWR Water Quality Classification	C	C	C
Morphological Description (Rosgen stream type)	Gc	channelized B	channelized B
	Incised channel, little connection to floodplain	channelized/ditched channel	channelized/ditched channel
Evolutionary Trend	Gc→F	B→F→C	B→F→C
Underlying Mapped Soils	AaA, FnA	UnB	UnB, FnA
Drainage Class	Somewhat poorly to well drained	Somewhat poorly to well drained	Somewhat poorly to well drained
Soil Hydric Status	Site-specific	Site-specific	Site-specific
Average Channel Slope (ft/ft)	0.016	0.037	0.037
FEMA Classification	N/A	N/A	N/A
Native Vegetation Community	Piedmont Dry-Mesic Oak and Hardwoods to Mixed Bottomland Hardwoods	Piedmont/Mtn. Mixed Bottomland Hardwoods	Piedmont/Mtn. Mixed Bottomland Hardwoods
Percent Composition of Exotic/Invasive Vegetation	5%	2%	2%

Parameters	UT3 - Reach 1		UT3 - Reach 1			
Length of Reach (LF)	342		1,006			
Valley Classification (Rosgen)	III		III			
Drainage Area (AC)	123		123			
NCDWR Stream Identification Score	49.75		49.75			
NCDWR Water Quality Classification	C		C			
Morphological Description (Rosgen stream type)	B/E		E			
	Aggrading at upper end then stable to incising at lower end		Incised channel, little connection to floodplain			
Evolutionary Trend	B/E→G		E→G			
Underlying Mapped Soils	AaA		AaA, FnA			
Drainage Class	Somewhat poorly to well drained		Somewhat poorly to well drained			
Soil Hydric Status	Site-specific		Site-specific			
Average Channel Slope (ft/ft)	0.015		0.015			
FEMA Classification	N/A		N/A			
Native Vegetation Community	Piedmont Dry-Mesic Oak and Hardwoods		Piedmont/Mtn. Mixed Bottomland Hardwoods			
Percent Composition of Exotic/Invasive Vegetation	2%		2%			
Wetland Summary Information						
Parameters	JDW1	JDW2	JDW3	JDW4	JDW5	JDW6
Size of Wetland (AC)	1.43	0.51	0.03	0.24	0.81	0.3
Wetland Type	Riparian	Riparian	Riparian	Riparian	Riparian	Riparian
Mapped Soil Series	FnA	FnA	FnA	FnA	FnA	FnA
Drainage Class	Somewhat poorly to well drained	Somewhat poorly to well drained	Somewhat poorly to well drained	Somewhat poorly to well drained	Somewhat poorly to well drained	Somewhat poorly to well drained
Soil Hydric Status	Site-specific	Site-specific	Site-specific	Site-specific	Site-specific	Site-specific
Source of Hydrology	Hillslope seepage; Baseflow; Overbank Flooding	Hillslope seepage; Baseflow; Overbank Flooding	Hillslope seepage; Baseflow; Overbank Flooding	Hillslope seepage; Baseflow; Overbank Flooding	Hillslope seepage; Baseflow; Overbank Flooding	Hillslope seepage; Baseflow; Overbank Flooding
Hydrologic Impairment	Partially	Yes	No	Partially	Partially	Partially
Native Vegetation Community	Piedmont/Mountain Mixed Bottomland Hardwood Forest. Successional Deciduous Forest Land was once also present near Wetlands 2 & 5.					
Percent Composition of Exotic/Invasive Vegetation	~30%	~55%	~10%	~40%	~55%	~35%
Regulatory Considerations						
Regulation	Applicable	Resolved		Supporting Documentation		
Waters of the United States – Section 404	Yes	Yes		Categorical Exclusion		
Waters of the United States – Section 401	Yes	Yes		Categorical Exclusion		
Endangered Species Act	Yes	Yes		Categorical Exclusion		
Historic Preservation Act	Yes	Yes		Categorical Exclusion		
Coastal Zone Management Act (CZMA)/ Coastal Area Management Act (CAMA)	No	N/A		N/A		
FEMA Floodplain Compliance	Yes	Yes		Categorical Exclusion		
Essential Fisheries Habitat	No	N/A		N/A		
Notes:						
1. See Figure 2.3 of Mitigation Plan for key to soil series symbols.						
2. All wetlands had been disturbed to some degree at the time the project was initiated. As a result, only remnants of native vegetative communities exist in the wetland areas.						
3. Fescue is considered as invasive vegetation; it and other field grasses were the dominant nonnative wetland vegetation observed.						
4. USGS Land Use Data (2001) used rather than CGIA Land Use Classification data which is more outdated (1996).						
5. Source: Upper Catawba River Basin Restoration Priorities (NCEEP 2009) (https://deq.nc.gov/about/divisions/mitigation-services/dms-planning/watershed-planning-documents/catawba-river-basin)						

Appendix C

Vegetation Assessment Data

Includes:

Table 5. Vegetation Plot Mitigation Success Summary

Table 6. CVS Vegetation Metadata Table

Table 7. Stem Count Arranged by Plot and Species

Figure 3. Vegetation Monitoring Plot Photos

**Table 5. Vegetation Plot Mitigation
Success Summary**
(per acre)

Plot #	Stream/ Wetland Stems ²	Volunteers ³	Total ⁴	Success Criteria Met?
1	1457	0	1457	Yes
2	1214	0	1214	Yes
3	688	0	688	Yes
4	850	0	850	Yes
5	850	0	850	Yes
6	647	0	647	Yes
7	647	0	647	Yes
8	647	0	647	Yes
9	647	0	647	Yes
10	688	0	688	Yes
11	769	0	769	Yes
12	769	0	769	Yes
13	688	0	688	Yes
14	688	0	688	Yes
Project Avg	804	0	804	Yes

Stem Class characteristics

¹Buffer Stems Native planted hardwood trees. Does NOT include shrubs. No pines. No vines.

²Stream/
Wetland Stems Native planted woody stems. Includes shrubs, does NOT include live stakes. No vines

³Volunteers Native woody stems. Not planted. No vines.

⁴Total Planted + volunteer native woody stems. Includes live stakes. Excl. exotics. Excl. vines.

Exceeds requirements by 10%

Table 6. Vegetation Metadata

Upper Silver Creek Stream and Wetland Restoration - Project 94645

Report Prepared By	Katie McKeithan
Date Prepared	12/28/2015 14:47
database name	94645_UpperSilver_cvs-eep-entrytool-v2.3.1.mdb
database location	L:\Users\kmckeithan\Silver_Creek
computer name	CARYLSHUNT
file size	60067840
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Proj, planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Proj, total stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY-----	
Project Code	94645
project Name	Upper Silver Creek
Description	Full Delivery stream and wetland restoration site
River Basin	Broad
length(ft)	5,169 feet
stream-to-edge width (ft)	Minimum of 30 feet
area (sq m)	62,321.6 sq.m.
Required Plots (calculated)	14
Sampled Plots	14

Table 7. Stem Count Arranged by Plot
Project: Upper Silver Creek, EEP Project # 94645.

			Current Plot Data (MY1 2015)																				
Scientific Name	Common Name	Species Type	94645-01-0001			94645-01-0002			94645-01-0003			94645-01-0004			94645-01-0005			94645-01-0006			94645-01-0007		
			P	V	T	P	V	T	P	V	T	P	V	T	P	V	T	P	V	T	P	V	T
Acer rubrum	red maple	Tree	1		1	6		6				2		2									
Alnus serrulata	hazel alder	Shrub							1		1												
Betula nigra	river birch	Tree							3		3	1		1				1		1	3		3
Carpinus caroliniana	American hornbeam	Tree	2		2	3		3				1		1	1		1				1		1
Cornus amomum	silky dogwood	Shrub							1		1	3		3	6		6	4		4	2		2
Corylus cornuta	beaked hazelnut	Shrub Tree																1		1			
Diospyros virginiana	common persimmon	Tree	1		1							1		1									
Fraxinus pennsylvanica	green ash	Tree							2		2				8		8	1		1	1		1
Liriodendron tulipifera	tuliptree	Tree	3		3	2		2				1		1									
Platanus occidentalis	American sycamore	Tree	12		12	4		4	6		6	7		7	4		4	3		3	4		4
Quercus sp.	Oak sp.	Tree																					
Quercus michauxii	swamp chestnut oak	Tree				6		6	1		1	2		2	2		2	3		3	4		4
Quercus nigra	water oak	Tree							3		3										1		1
Quercus phellos	willow oak	Tree	2		2	3		3				3		3				3		3			
Unknown		Shrub or Tree				2		2															
Vaccinium corymbosum	highbush blueberry	Shrub				1		1															
Viburnum dentatum	southern arrowwood	Shrub	15		15	3		3															
	Stem count		36		36	30		30	17		17	21		21	21		21	16		16	16		16
	size (ares)		1			1			1			1			1			1			1		
	size (ACRES)		0.02			0.02			0.02			0.02			0.02			0.02			0.02		
	Species count		7		7	9		9	7		7	9		9	5		5	7		7	7		7
	Stems per ACRE		1457		1457	1214		1214	688		688	850		850	850		850	647		647	647		647

P = Planted
V = Volunteer
T = Total

This color indicates that the number includes volunteer stems.
Indicates that the stems per Acre exceeds requirements by 10%
Indicates that the stems per Acre exceeds requirements, but by less than 10%

Table 7. Stem Count Arranged by Plot, continued.
Project: Upper Silver Creek, EEP Project # 94645.

			Current Plot Data (MY1 2015)																				
Scientific Name	Common Name	Species Type	94645-01-0008			94645-01-0009			94645-01-0010			94645-01-0011			94645-01-0012			94645-01-0013			94645-01-0014		
			P	V	T	P	V	T	P	V	T	P	V	T	P	V	T	P	V	T	P	V	T
Acer rubrum	red maple	Tree	3		3									2		2							
Alnus serrulata	hazel alder	Shrub																					
Betula nigra	river birch	Tree										3		3	6		6	3		3	1		1
Carpinus caroliniana	American hornbeam	Tree				1		1							2		2						
Cornus amomum	silky dogwood	Shrub										10		10	3		3	3		3			
Corylus cornuta	beaked hazelnut	Shrub Tree																					
Diospyros virginiana	common persimmon	Tree	1		1																		
Fraxinus pennsylvanica	green ash	Tree										1		1	2		2				4		4
Liriodendron tulipifera	tuliptree	Tree	2		2	2		2	2		2												
Platanus occidentalis	American sycamore	Tree	5		5	3		3	4		4	1		1	2		2	2		2	3		3
Quercus sp.	Oak sp.	Tree													1		1				2		2
Quercus michauxii	swamp chestnut oak	Tree	2		2				1		1	1		1			8		8	3		3	
Quercus nigra	water oak	Tree																					
Quercus phellos	willow oak	Tree				6		6	10		10	2		2	1		1				2		2
Unknown		Shrub or Tree	1		1	3		3				1		1				1		1	2		2
Vaccinium corymbosum	highbush blueberry	Shrub																					
Viburnum dentatum	southern arrowwood	Shrub	2		2	1		1															
	Stem count		16	0	16	16		16	17		17	19		19	19		19	17		17	17		17
	size (ares)		1			1			1			1			1			1			1		
	size (ACRES)		0.02			0.02			0.02			0.02			0.02			0.02			0.02		
	Species count		7		7	6		6	4		4	7		7	8		8	5		5	7		7
	Stems per ACRE		647		647	647		647	688		688	769		769	769		769	688		688	688		688

P = Planted
V = Volunteer
T = Total

This color indicates that the number includes volunteer stems.
Indicates that the stems per Acre exceeds requirements by 10%
Indicates that the stems per Acre exceeds requirements, but by less than 10%

Table 7. Stem Count Arranged by Plot, continued.
Project: Upper Silver Creek, EEP Project # 94645.

Scientific Name	Common Name	Species Type	Annual Means																	
			MY0 (2015)*			MY1 (2015)			MY2 (2016)			MY3 (2017)			MY4 (2018)			MY5 (2019)		
			P	V	T	P	V	T	P	V	T	P	V	T	P	V	T	P	V	T
Acer rubrum	red maple	Tree	12		12	14		14												
Alnus serrulata	hazel alder	Shrub	1		1	1		1												
Betula nigra	river birch	Tree	8		8	21		21												
Carpinus caroliniana	American hornbeam	Tree	9		9	11		11												
Cornus amomum	silky dogwood	Shrub	16		16	32		32												
Corylus comuta	beaked hazelnut	Shrub Tree	1		1	1		1												
Diospyros virginiana	common persimmon	Tree	3		3	3		3												
Fraxinus pennsylvanica	green ash	Tree	12		12	19		19												
Liriodendron tulipifera	tuliptree	Tree	10		10	12		12												
Platanus occidentalis	American sycamore	Tree	47		47	60		60												
Quercus sp.	Oak sp.	Tree			3			3												
Quercus michauxii	swamp chestnut oak	Tree	19		19	33		33												
Quercus nigra	water oak	Tree	4		4	4		4												
Quercus phellos	willow oak	Tree	17		17	32		32												
Unknown		Shrub or Tree	6		6	10		10												
Vaccinium corymbosum	highbush blueberry	Shrub	1		1	1		1												
Viburnum dentatum	southern arrowwood	Shrub	21		21	21		21												
Stem count			187		187	278		278	0		0	0		0	0		0	0		
size (ares)			9			14			9			9			9			9		
size (ACRES)			0.22			0.35			0.22			0.22			0.22			0.22		
Species count			16		16	17		17	0		0	0		0	0		0	0		
Stems per ACRE			841		841	804		804	0		0	0		0	0		0	0		

P = Planted
V = Volunteer
T = Total

This color indicates that the number includes volunteer stems.
Indicates that the stems per Acre exceeds requirements by 10%
Indicates that the stems per Acre exceeds requirements, but by less than 10%

* MY0 included 9 vegetation plots. However upon review it was discovered that we needed to have 14 vegetation plots to meet guidelines. Five additional plots were added in the fall of 2015 and the MY1 and later means include these additional plots.

Figure 3. Upper Silver Creek - Vegetation Plot Photos, DMS Project #94645



Photo 1. Vegetation Plot 1 – Tree photo (taken December 3, 2015).



Photo 2. Vegetation Plot 1 – Herbaceous photo (taken December 3, 2015).

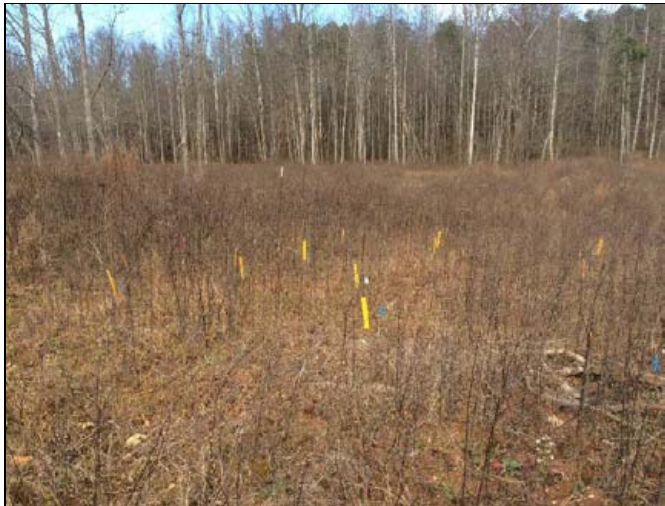


Photo 3. Vegetation Plot 2 – Tree photo (taken December 3, 2015).



Photo 4. Vegetation Plot 2 – Herbaceous photo (taken December 3, 2015).



Photo 5. Vegetation Plot 3 – Tree photo (taken December 3, 2015).



Photo 6. Vegetation Plot 3 – Herbaceous photo (taken December 3, 2015).



Photo 7. Vegetation Plot 4 – Tree photo (taken December 3, 2015).



Photo 8. Vegetation Plot 4 – Herbaceous photo (taken December 3, 2015).



Photo 9. Vegetation Plot 5 – Tree photo (taken December 3, 2015).



Photo Point 10, Vegetation Plot 5 – Herbaceous photo (taken December 3, 2015).



Photo 11. Vegetation Plot 6 – Tree photo (taken December 3, 2015).



Photo 12. Vegetation Plot 6 – Herbaceous photo (taken December 3, 2015).



Photo 13. Vegetation Plot 7 – Tree photo (taken December 3, 2015).



Photo 14. Vegetation Plot 7 – Herbaceous photo (taken December 3, 2015).



Photo 15. Vegetation Plot 8 – Tree photo (taken December 3, 2015).



Photo 16. Vegetation Plot 8 – Herbaceous photo (taken December 3, 2015).



Photo 17. Vegetation Plot 9 – Tree photo (taken December 3, 2015).



Photo 18. Vegetation Plot 9 – Herbaceous photo (taken December 3, 2015).



Photo 19. Vegetation Plot 10 – Tree photo (taken December 3, 2015).



Photo 20. Vegetation Plot 10 – Herbaceous photo (taken December 3, 2015).



Photo 21. Vegetation Plot 11 – Tree photo (taken December 3, 2015).



Photo 22. Vegetation Plot 11 – Herbaceous photo (taken December 3, 2015).



Photo 23. Vegetation Plot 12 – Tree photo (taken December 3, 2015).



Photo 24. Vegetation Plot 12 – Herbaceous photo (taken December 3, 2015).



Photo 25. Vegetation Plot 13 – Tree photo (taken December 3, 2015).



Photo 26. Vegetation Plot 13 – Herbaceous photo (taken December 3, 2015).



Photo 27. Vegetation Plot 14 – Tree photo (taken December 3, 2015).



Photo 28. Vegetation Plot 14 – Herbaceous photo (taken December 3, 2015).

Appendix D

Stream Assessment Data

Includes:

Figure 4. Stream Photos by channel and station

Table 8. Visual Morphological Stability Assessment

Table 9. Verification of Bankfull Events

Figure 5. Cross-Sections with annual overlays

Figure 6. Longitudinal Profiles with annual overlays

Figure 7. Pebble Count plots with annual overlays

Table 10. Stream Summary

Table 11. Morphology and Hydraulic Monitoring Summary

Figure 4. Upper Silver Creek Mainstem Photos – Monitoring Year 1 (2015)



Photo 1. Mainstem Photo Point 1 – Station 29+26 (February 2, 2016) downstream view from left bank.



Photo 2. Mainstem Photo Point 1 – Station 29+26 (February 2, 2016) upstream view from left bank.



Photo 3. Mainstem Photo Point 2 – Station 26+44 (February 2, 2016) downstream view from left bank.



Photo 4. Mainstem Photo Point 2 – Station 26+44 (February 2, 2016) upstream from left bank.



Photo 5. Mainstem Photo Point 3 – Station 24+70 (February 2, 2016) upstream from right bank.



Photo 6. Mainstem Photo Point 3 – Station 24+70 (February 2, 2016) downstream from right bank.



Photo 7. Mainstem Photo Point 4 (PP4) – Station 20+30 (February 2, 2016) downstream from left bank.



Photo 8. Mainstem Photo Point 4 (PP4) – Station 20+30 (February 2, 2016) upstream from left bank.



Photo 9. Mainstem Photo Point 5 – Station 16+03 (February 2, 2016) upstream from right bank.



Photo Point 10, Mainstem Photo Point 5 – Station 16+03 (February 2, 2016) downstream from right bank.



Photo 11. Mainstem Photo Point 6 – Station 13+03 (February 2, 2016) upstream from right bank.



Photo 12. Mainstem Photo Point 5 – Station 13+03 (February 2, 2016) downstream from right bank.



Photo 13. Mainstem Photo Point 7 – Station 10+11
(February 2, 2016) downstream from left bank.



Photo 14. Mainstem Photo Point 7 – Station 10+11
(February 2, 2016) upstream from left bank.



Photo 15. Mainstem Photo Point 8 – Station 5+06
(February 2, 2016) upstream from right bank.



Photo 16. Mainstem Photo Point 8 – Station 5+06
(February 2, 2016) downstream from right bank.



Photo 17. Mainstem Photo Point 9 – Station 3+87
(February 2, 2016) downstream from left bank.



Photo 18. Mainstem Photo Point 9 – Station 3+87
(February 2, 2016) upstream from left bank.



Photo 19. Mainstem Photo Point 10 – Stat. 1+22 (February 2, 2016) downstream from left bank.



Photo 20. Mainstem Photo Point 10 – Stat. 1+22 (February 2, 2016) upstream from left bank.

Unnamed Tributary 1 Photos - Monitoring Year 1



Photo 21. UT1 Photo Point 1 – Station 4+82 (February 2, 2016) upstream from left bank.



Intentionally Left Blank



Photo 22. UT1 Photo Point 2 – Station 4+07 (February 2, 2016) downstream from left bank.



Photo 23. UT1 Photo Point 2 – Station 4+07 (February 2, 2016) upstream from left bank.



Photo 24. UT1 Photo Point 3 – Station 2+55
(February 2, 2016) upstream from right bank.



Photo 25. UT1 Photo Point 3 – Station 2+55
(February 2, 2016) downstream from right bank.



Photo 26. UT1 Photo Point 4 – Station 0+55
(February 2, 2016) downstream from left bank.



Photo 27. UT1 Photo Point 4 – Station 0+55
(February 2, 2016) upstream from left bank.

Unnamed Tributary 2 Photos – Monitoring Year 1



Photo 28. UT2 Photo Point 1 – Station 2+15
(February 2, 2016) downstream from left bank.



Photo 29. UT2 Photo Point 1 – Station 2+15
(February 2, 2016) upstream from left bank.



Photo 30. UT2 Photo Point 2 – Station 0+96 (February 2, 2016) upstream from right bank.



Photo 31. UT2 Photo Point 2 – Station 0+96 (February 2, 2016) downstream from right bank.



Photo 32. UT2 Photo Point 3 – Station 0+02 (February 2, 2016) downstream from right bank.



Photo 33. UT2 Photo Point 3 – Station 0+02 (February 2, 2016) upstream from right bank.

Unnamed Tributary 3 Photos – Monitoring Year 1
Location for photo points on UT3 has been changed to align with the MY1 survey.



Photo 34. UT3 Photo Point 1 – Station 12+10 (February 2, 2016) downstream from left bank.



Photo 35. UT3 Photo Point 1 – Station 12+10 (February 2, 2016) upstream from left bank.



Photo 36. UT3 Photo Point 2 – Station 10+66 (February 2, 2016) upstream from right bank.



Photo 37. UT3 Photo Point 2 – Station 10+66 (February 2, 2016) downstream from right bank.



Photo 38. UT3 Photo Point 3 – Station 8+10 (February 2, 2016) downstream from left bank.



Photo 39. UT3 Photo Point 3 – Station 8+10 (February 2, 2016) upstream from left bank.



Photo 40. UT3 Photo Point 4 – Station 7+05 (February 2, 2016) downstream from left bank.



Photo 41. UT3 Photo Point 4 – Station 7+05 (February 2, 2016) upstream from left bank.



Photo 42. UT3 Photo Point 5 – Station 5+95
(February 2, 2016) downstream from left bank.



Photo 43. UT3 Photo Point 5 – Station 5+95
(February 2, 2016) upstream from left bank.



Photo 44. UT3 Photo Point 6 – Station 4+55
(February 2, 2016) upstream from right bank.



Photo 45. UT3 Photo Point 6 – Station 4+55
(February 2, 2016) downstream from right bank.



Photo 46. UT3 Photo Point 7 – Station 3+60
(February 2, 2016) upstream to structure.



Photo 47. UT3 Photo Point 8 – Station 2+70
(February 2, 2016) upstream to structure.



Photo 48. UT3 Photo Point 9 – Station 1+90
(February 2, 2016) upstream to structure.



Photo 49. UT3 Photo Point 10 – Station 0+60
(February 2, 2016) downstream to structure.

Table 8. Visual Morphological Stability Assessment
Upper Silver Creek Restoration Project: DMS Project ID No. 94645

Silver Creek, Reach 1 (838 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	4	4	0	100	
	2. Armor stable (e.g. no displacement)?	4	4	0	100	
	3. Facet grades appears stable?	4	4	0	100	
	4. Minimal evidence of embedding/fining?	4	4	0	100	
	5. Length appropriate?	4	4	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	4	4	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	4	4	0	100	
	3. Length appropriate?	4	4	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering? (%)	100	100	0	100	
	2. Downstream of pool (structure) centering? (%)	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	4	4	0	100	
	2. Of those eroding, # w/concomitant point bar formation?	4	4	0	100	
	3. Apparent Rc within spec?	4	4	0	100	
	4. Sufficient floodplain access and relief?	4	4	0	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	838	838	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	838	838	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	6	6	0	100	
	2. Height appropriate?	6	6	0	100	
	3. Angle and geometry appear appropriate?	6	6	0	100	
	4. Free of piping or other structural failures?	6	6	0	100	100%
G. Wads/ Boulders	1. Free of scour?	4	4	0	100	
	2. Footing stable?	4	4	0	100	100%
Silver Creek, Reach 2 (2,178 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	17	17	0	100	
	2. Armor stable (e.g. no displacement)?	17	17	0	100	
	3. Facet grades appears stable?	17	17	0	100	
	4. Minimal evidence of embedding/fining?	17	17	0	100	
	5. Length appropriate?	17	17	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	16	16	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	16	16	0	100	
	3. Length appropriate?	16	16	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering? (%)	100	100	0	100	
	2. Downstream of pool (structure) centering? (%)	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	16	16	0	100	
	2. Of those eroding, # w/concomitant point bar formation?	16	16	0	100	
	3. Apparent Rc within spec?	16	16	0	100	
	4. Sufficient floodplain access and relief?	16	16	0	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	2,178	2,178	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	2,178	2,178	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	21	21	0	100	
	2. Height appropriate?	21	21	0	100	
	3. Angle and geometry appear appropriate?	21	21	0	100	
	4. Free of piping or other structural failures?	18	21	3	86	96%
G. Wads/ Boulders	1. Free of scour?	14	14	0	100	
	2. Footing stable?	14	14	0	100	100%
UT1 (502 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	7	7	0	100	
	2. Armor stable (e.g. no displacement)?	7	7	0	100	
	3. Facet grades appears stable?	7	7	0	100	
	4. Minimal evidence of embedding/fining?	7	7	0	100	
	5. Length appropriate?	7	7	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	10	10	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	10	10	0	100	
	3. Length appropriate?	10	10	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering? (%)	100	100	0	100	
	2. Downstream of pool (structure) centering? (%)	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	7	7	0	100	
	2. Of those eroding, # w/concomitant point bar formation?	7	7	0	100	
	3. Apparent Rc within spec?	7	7	0	100	
	4. Sufficient floodplain access and relief?	7	7	0	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	502	502	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	502	502	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	11	11	0	100	
	2. Height appropriate?	11	11	0	100	
	3. Angle and geometry appear appropriate?	11	11	0	100	
	4. Free of piping or other structural failures?	11	11	0	100	100%
G. Wads/ Boulders	1. Free of scour?	N/A	N/A	N/A	N/A	
	2. Footing stable?	N/A	N/A	N/A	N/A	100%

Table 8. Visual Morphological Stability Assessment - Continued
 Upper Silver Creek Restoration Project: DMS Project ID No. 94645

UT2, Reach 1 (103 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	4	4	0	100	
	2. Armor stable (e.g. no displacement)?	4	4	0	100	
	3. Facet grades appears stable?	4	4	0	100	
	4. Minimal evidence of embedding/fining?	4	4	0	100	
	5. Length appropriate?	4	4	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	5	5	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	5	5	0	100	
	3. Length appropriate?	5	5	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering? (%)	100	100	0	100	
	2. Downstream of pool (structure) centering? (%)	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	N/A	N/A	N/A	100	
	2. Of those eroding, # w/concomitant point bar formation?	N/A	N/A	N/A	100	
	3. Apparent Rc within spec?	N/A	N/A	N/A	100	
	4. Sufficient floodplain access and relief?	N/A	N/A	N/A	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	103	103	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	103	103	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	5	5	0	100	
	2. Height appropriate?	5	5	0	100	
	3. Angle and geometry appear appropriate?	5	5	0	100	
	4. Free of piping or other structural failures?	5	5	0	100	100%
G. Wads/Boulders	1. Free of scour?	N/A	N/A	N/A	N/A	
	2. Footing stable?	N/A	N/A	N/A	N/A	N/A
UT2, Reach 2 (207 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	4	4	0	100	
	2. Armor stable (e.g. no displacement)?	4	4	0	100	
	3. Facet grades appears stable?	4	4	0	100	
	4. Minimal evidence of embedding/fining?	4	4	0	100	
	5. Length appropriate?	4	4	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	3	3	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	3	3	0	100	
	3. Length appropriate?	3	3	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering? (%)	100	100	0	100	
	2. Downstream of pool (structure) centering? (%)	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	3	3	0	100	
	2. Of those eroding, # w/concomitant point bar formation?	3	3	0	100	
	3. Apparent Rc within spec?	3	3	0	100	
	4. Sufficient floodplain access and relief?	3	3	0	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	207	207	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	207	207	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	1	1	0	100	
	2. Height appropriate?	1	1	0	100	
	3. Angle and geometry appear appropriate?	1	1	0	100	
	4. Free of piping or other structural failures?	1	1	0	100	100%
G. Wads/Boulders	1. Free of scour?	N/A	N/A	N/A	N/A	
	2. Footing stable?	N/A	N/A	N/A	N/A	N/A

Table 8. Visual Morphological Stability Assessment - Continued
 Upper Silver Creek Restoration Project: DMS Project ID No. 94645

UT3 Reach 1 (343 LF) (Enhancement II reach)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	N/A	N/A	N/A	N/A	
	2. Armor stable (e.g. no displacement)?	N/A	N/A	N/A	N/A	
	3. Facet grades appears stable?	N/A	N/A	N/A	N/A	
	4. Minimal evidence of embedding/fining?	N/A	N/A	N/A	N/A	
	5. Length appropriate?	N/A	N/A	N/A	N/A	N/A
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	N/A	N/A	N/A	N/A	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	N/A	N/A	N/A	N/A	
	3. Length appropriate?	N/A	N/A	N/A	N/A	N/A
C. Thalweg	1. Upstream of pool (structure) centering? (%)	N/A	N/A	N/A	N/A	
	2. Downstream of pool (structure) centering? (%)	N/A	N/A	N/A	N/A	N/A
D. Meanders	1. Outer bend in state of limited/controlled erosion?	N/A	N/A	N/A	N/A	
	2. Of those eroding, # w/concomitant point bar formation?	N/A	N/A	N/A	N/A	
	3. Apparent Rc within spec?	N/A	N/A	N/A	N/A	
	4. Sufficient floodplain access and relief?	N/A	N/A	N/A	N/A	N/A
E. Bed General	1. General channel bed aggradation areas (bar formation)	343	343	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	343	343	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	3	3	0	100	
	2. Height appropriate?	3	3	0	100	
	3. Angle and geometry appear appropriate?	3	3	0	100	
	4. Free of piping or other structural failures?	3	3	0	100	100%
G. Wads/Boulders	1. Free of scour?	N/A	N/A	N/A	N/A	
	2. Footing stable?	N/A	N/A	N/A	N/A	N/A
UT3 Reach 2 (1,022 LF)						
Feature Category	Metric (per As-Built and reference baselines)	(# Stable) Number Performing as Intended	Total number per As-Built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performance Mean or Total
A. Riffles	1. Present?	22	22	0	100	
	2. Armor stable (e.g. no displacement)?	22	22	0	100	
	3. Facet grades appears stable?	22	22	0	100	
	4. Minimal evidence of embedding/fining?	22	22	0	100	
	5. Length appropriate?	22	22	0	100	100%
B. Pools	1. Present? (e.g. not subject to severe aggradation or migration?)	21	21	0	100	
	2. Sufficiently deep (Max Pool D:Mean Bkf >1.6?)	21	21	0	100	
	3. Length appropriate?	21	21	0	100	100%
C. Thalweg	1. Upstream of pool (structure) centering?	100	100	0	100	
	2. Downstream of pool (structure) centering?	100	100	0	100	100%
D. Meanders	1. Outer bend in state of limited/controlled erosion?	17	17	0	100	
	2. Of those eroding, # w/concomitant point bar formation?	17	17	0	100	
	3. Apparent Rc within spec?	17	17	0	100	
	4. Sufficient floodplain access and relief?	17	17	0	100	100%
E. Bed General	1. General channel bed aggradation areas (bar formation)	1,022	1,022	0	100	
	2. Channel bed degradation - areas of increasing down-cutting or head cutting?	1,022	1,022	0	100	100%
F. Vanes, Rock/Log Drop Structures	1. Free of back or arm scour?	15	15	0	100	
	2. Height appropriate?	15	15	0	100	
	3. Angle and geometry appear appropriate?	15	15	0	100	
	4. Free of piping or other structural failures?	15	15	0	100	100%
G. Wads/Boulders	1. Free of scour?	4	4	0	100	
	2. Footing stable?	4	4	0	100	100%

Table 9. Verification of Bankfull or Greater than Bankfull Events				
Upper Silver Creek Restoration Project: DMS Project ID No. 94645				
Date of Data Collection	Date of Event	Method of Data Collection	Gauge Watermark Height (inches)*	
			Silver Creek Station 19+00	UT3 Station 8+10
12/202/2015	N/A	N/A	0	0

* height indicates the highest position of cork shavings on the dowel.

Figure 5. Cross-Sections with Annual Overlays.


Permanent Cross-Section 1
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	45.1	26.22	1.72	2.99	15.23	1	3.7	1197.45	1197.44

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	43.4	24.58	1.76	2.92	13.93	1	3.9	1197.38	1197.44

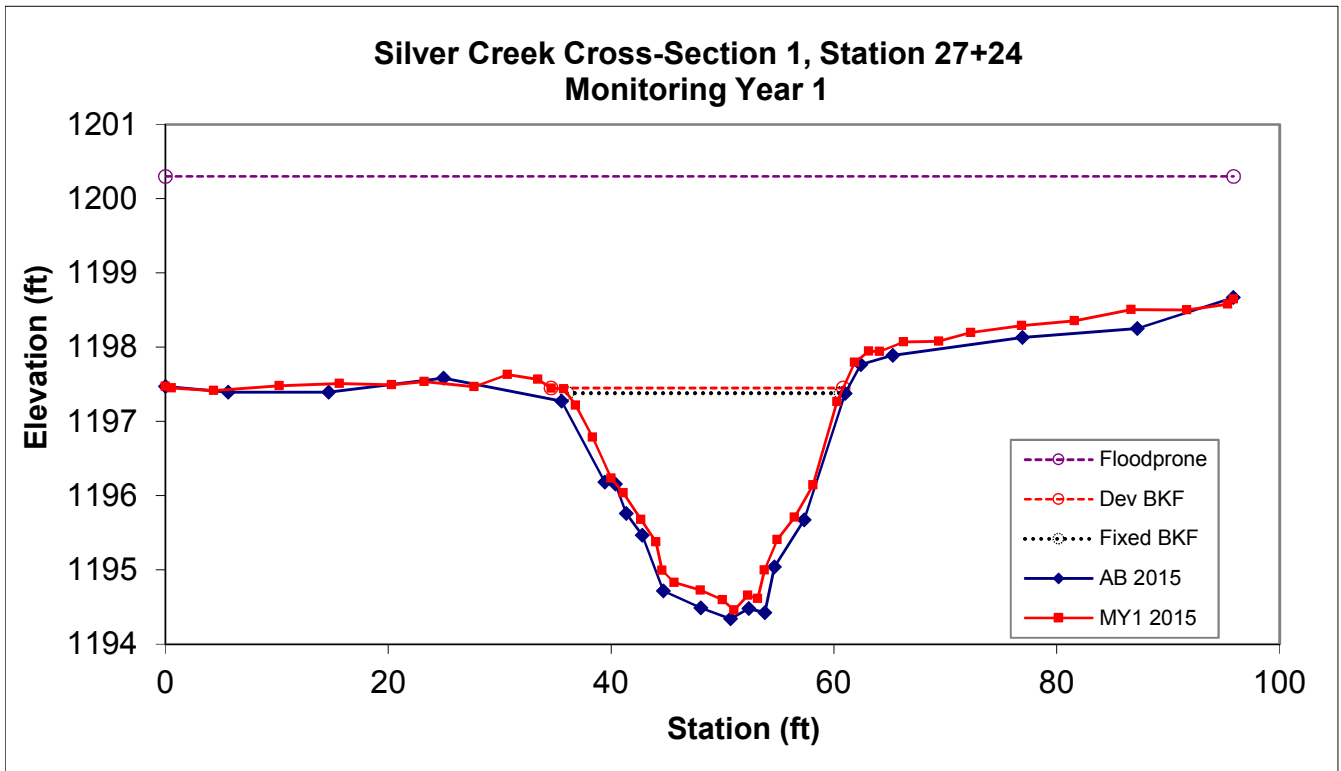

Looking at the Left Bank




Looking at the Right Bank

Permanent Cross-Section 2
(MY1 Data - collected October, 2015)

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		51.9	29.5	1.76	3.92	16.76	1	3	1198.2	1198.23

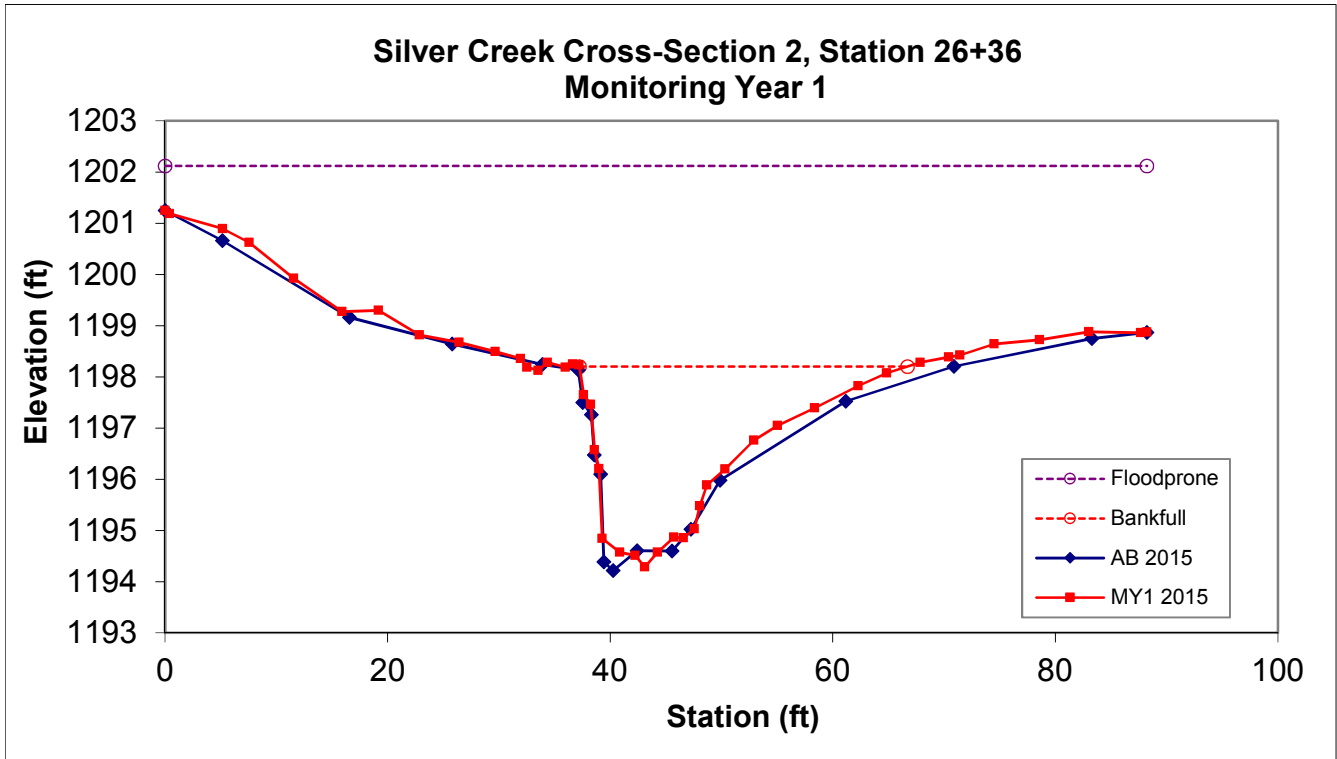

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 3
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		61.8	42.55	1.45	4.15	29.31	0.7	2.1	1202.45	1201.26

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		57.3	39.53	1.45	4.04	27.28	0.7	2.3	1202.34	1201.26

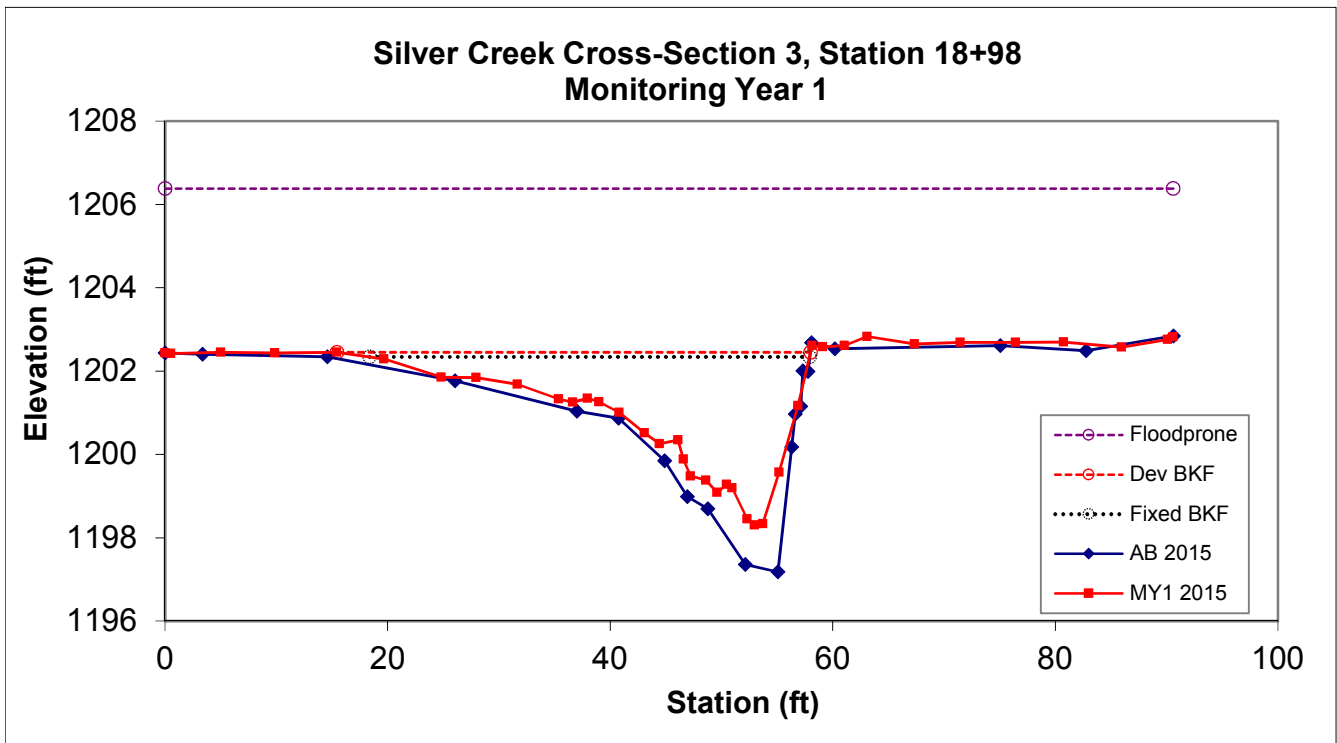

Looking at the Left Bank




Looking at the Right Bank

Permanent Cross-Section 4
(MY1 Data - collected October, 2015)

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	44.2	23.45	1.89	3.22	12.44	1	3.7	1203.01	1203.03

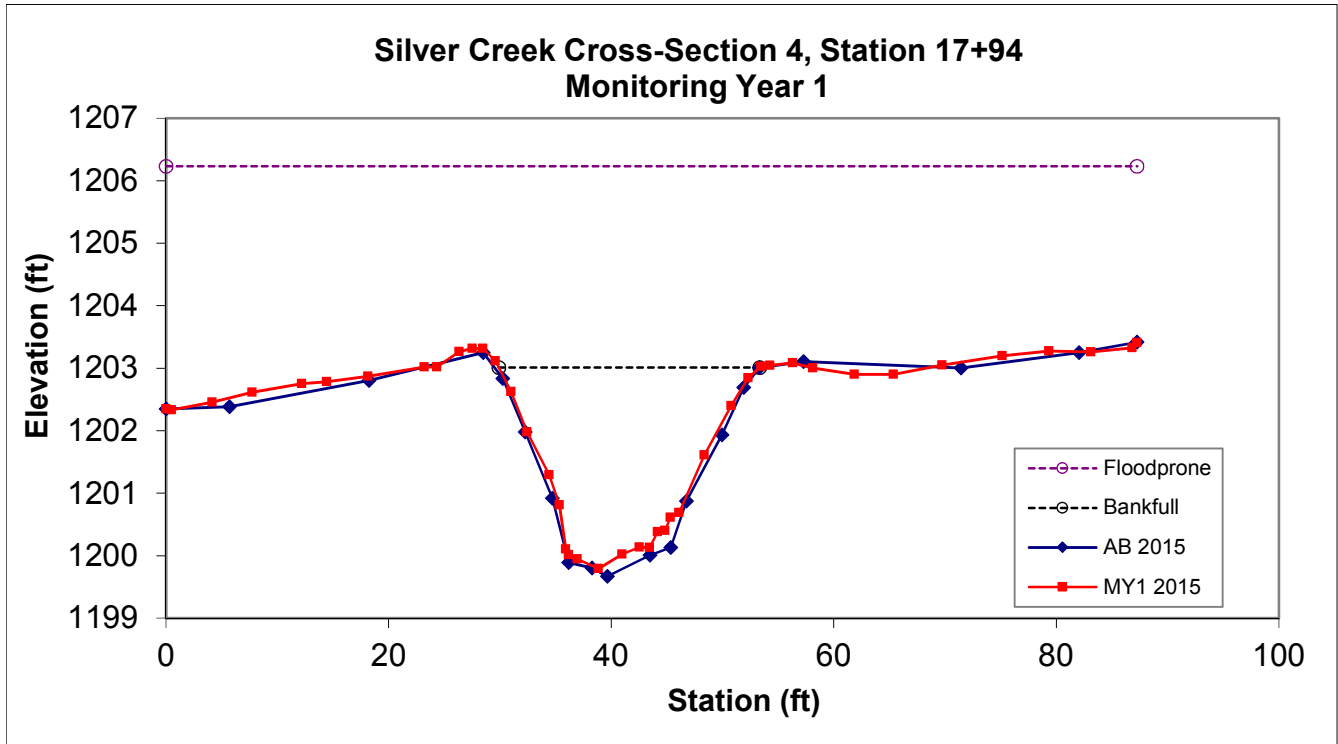

Looking at the Left Bank




Looking at the Right Bank

Permanent Cross-Section 5
(MY1 Data - collected October, 2015)

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	43.4	26.08	1.66	2.81	15.69	1	3.3	1204.82	1204.81

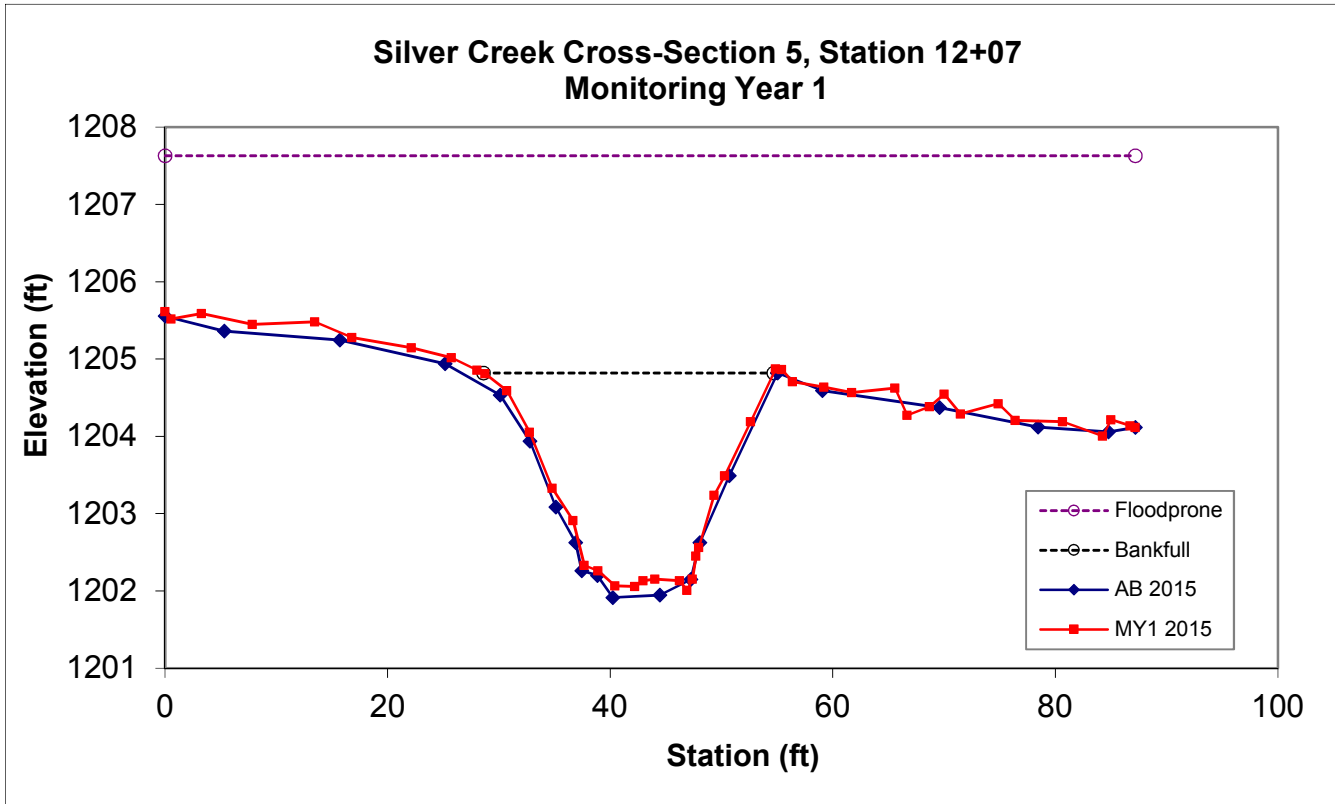

Looking at the Left Bank




Looking at the Right Bank

Permanent Cross-Section 6
(MY1 Data - collected October, 2015)

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		73.5	41.92	1.75	4.98	23.92	0.9	1.6	1208.14	1207.74

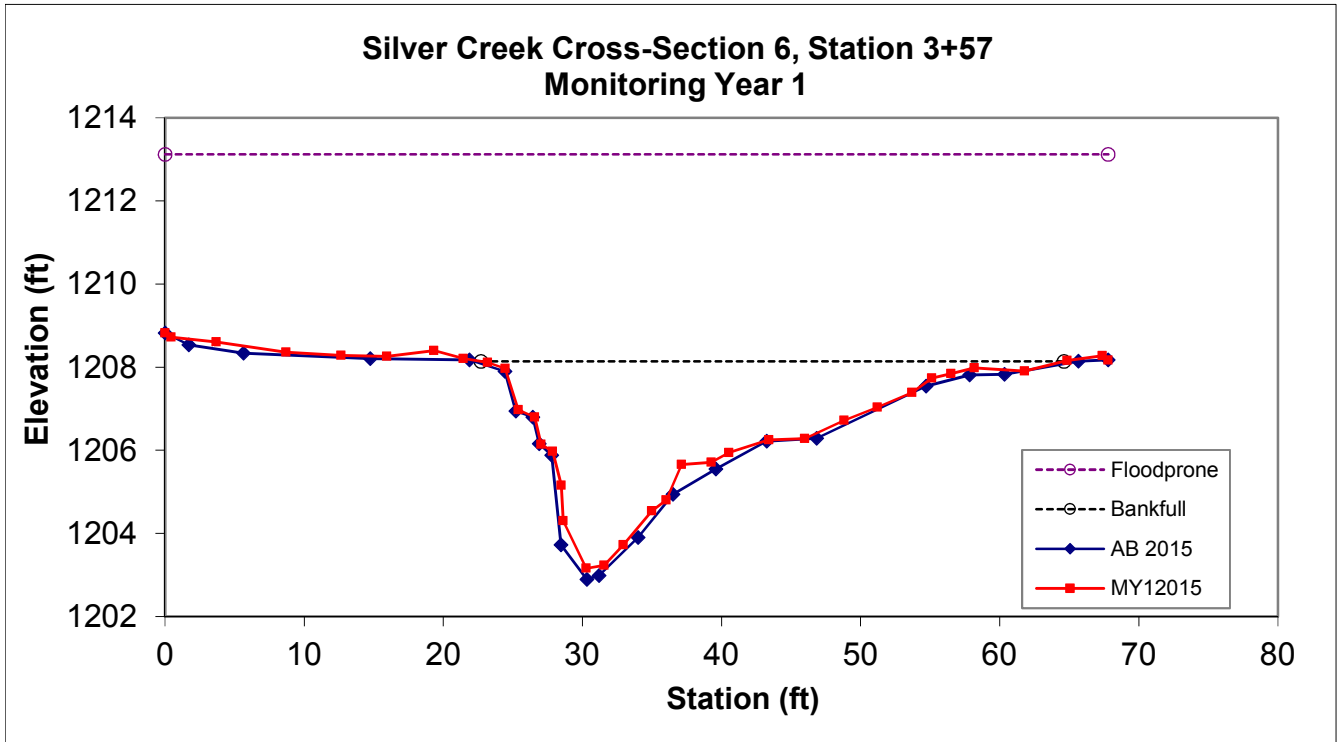

Looking at the Left Bank




Looking at the Right Bank

Permanent Cross-Section 7
(MY1 Data - collected October, 2015)

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	50.6	25.9	1.95	3.15	13.26	1	4.9	1208.23	1208.26

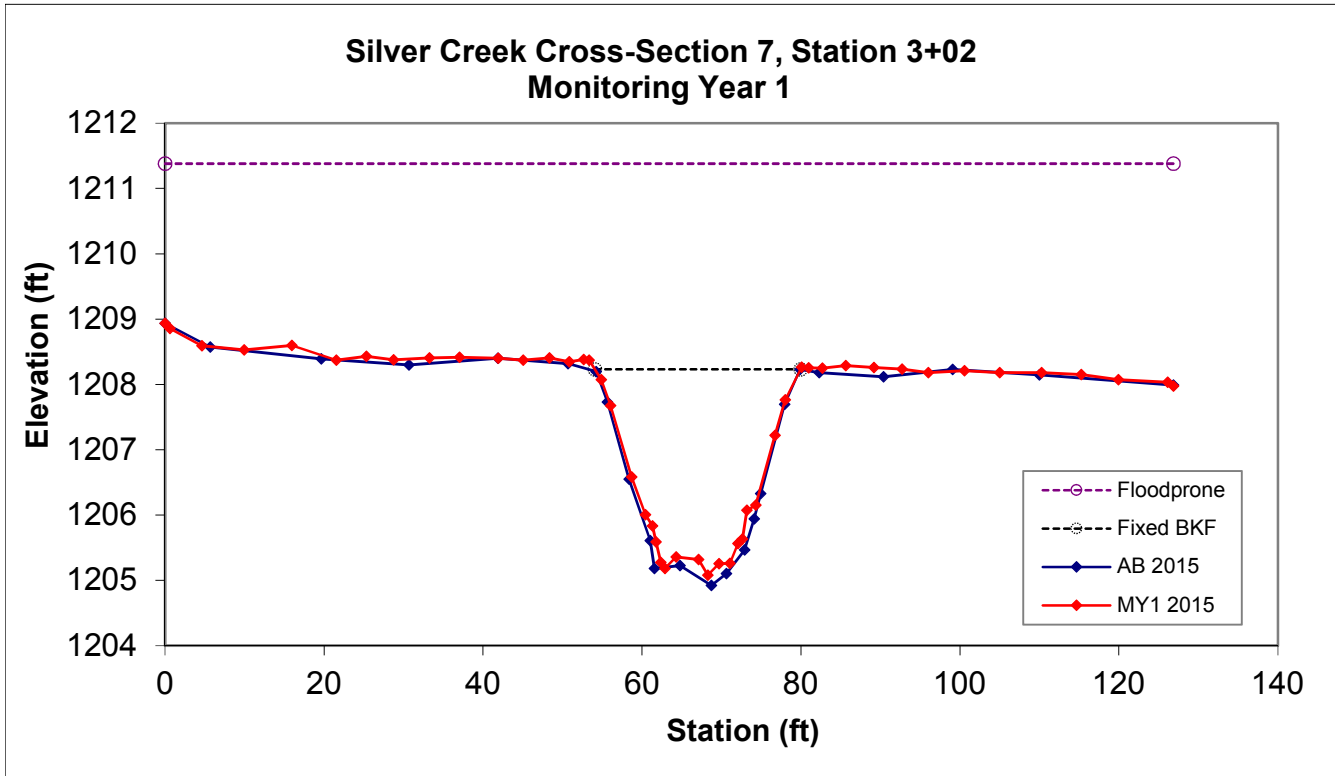

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 8
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	6.2	11.68	0.53	1.14	22.03	1	4.6	1215.47	1215.47

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	5.3	8.81	0.61	1.05	14.53	1.1	6.1	1215.38	1215.47

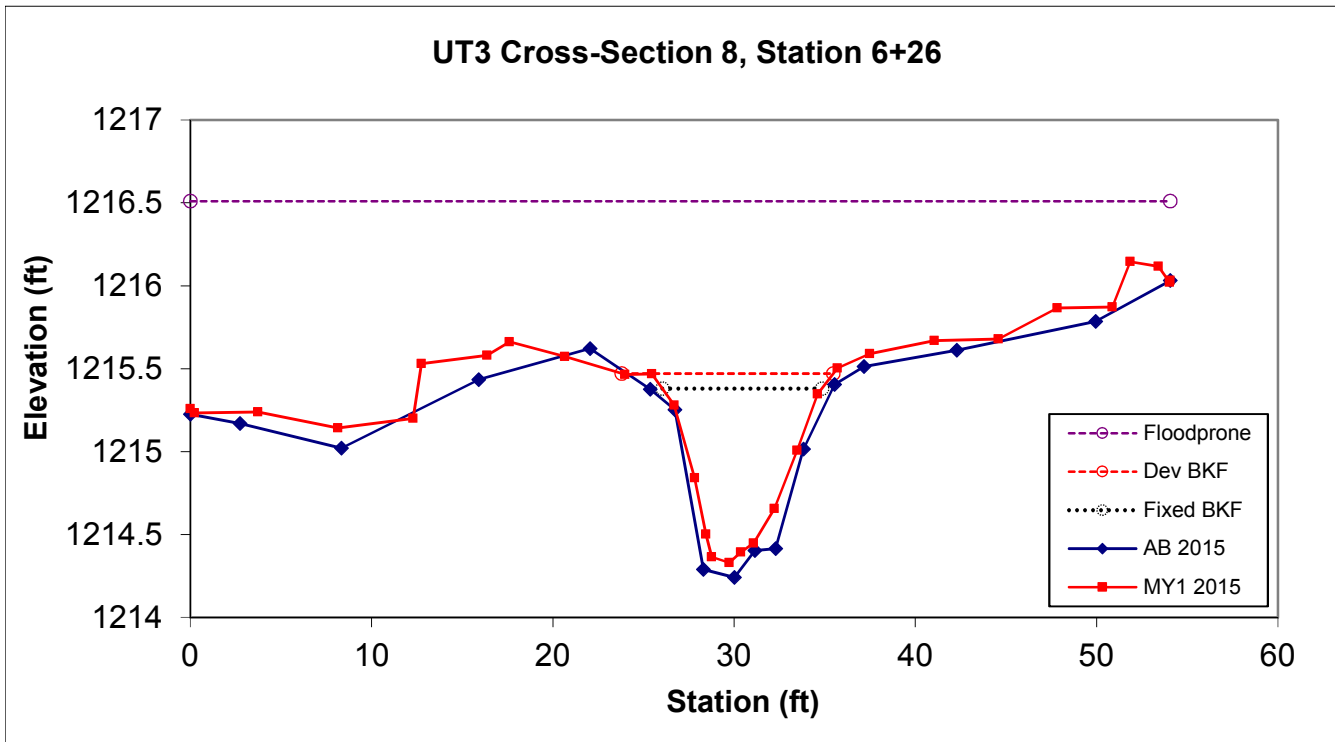

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 9
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		10.6	12.1	0.87	1.86	13.84	1	5.2	1213.08	1213.09

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		7.8	9.5	0.82	1.59	11.64	1.2	6.6	1212.81	1213.09

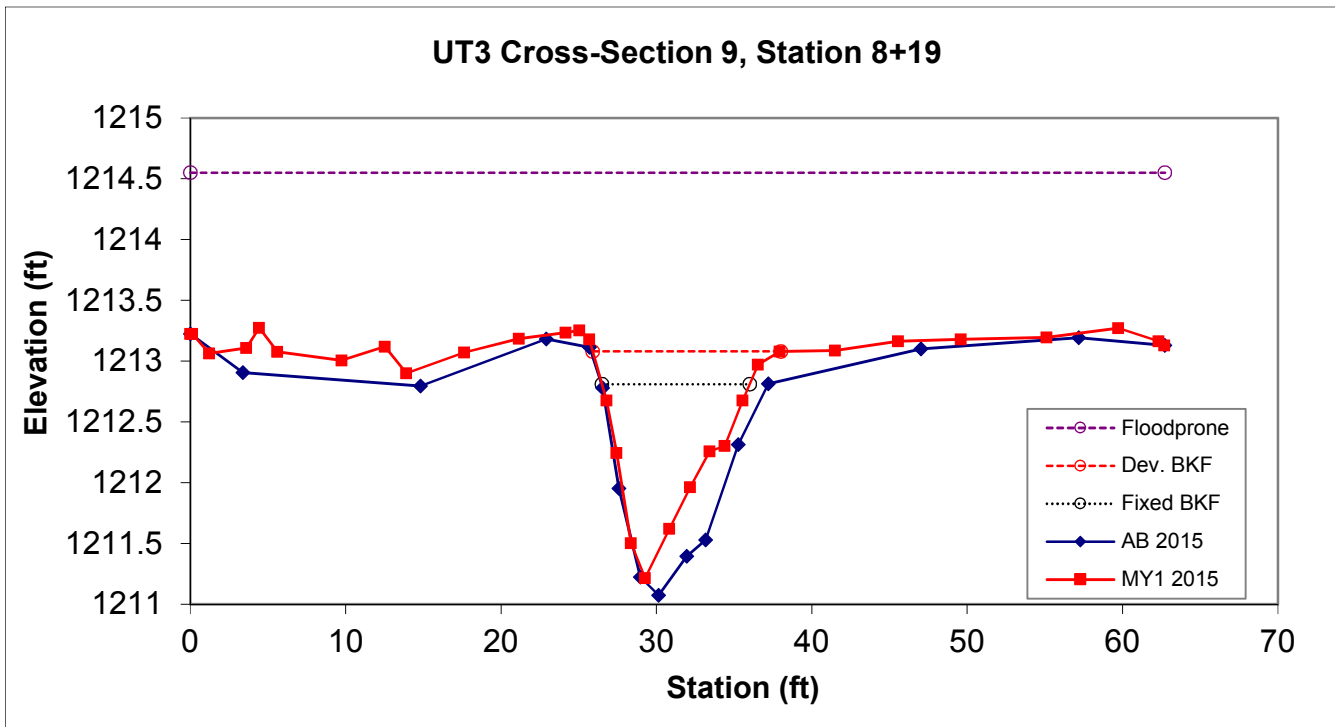

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 10
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	E	5.7	7.47	0.76	1.07	9.83	1.1	9.2	1213.02	1213.1

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	E	4.8	6.95	0.68	0.94	10.16	1.2	9.9	1212.89	1213.1

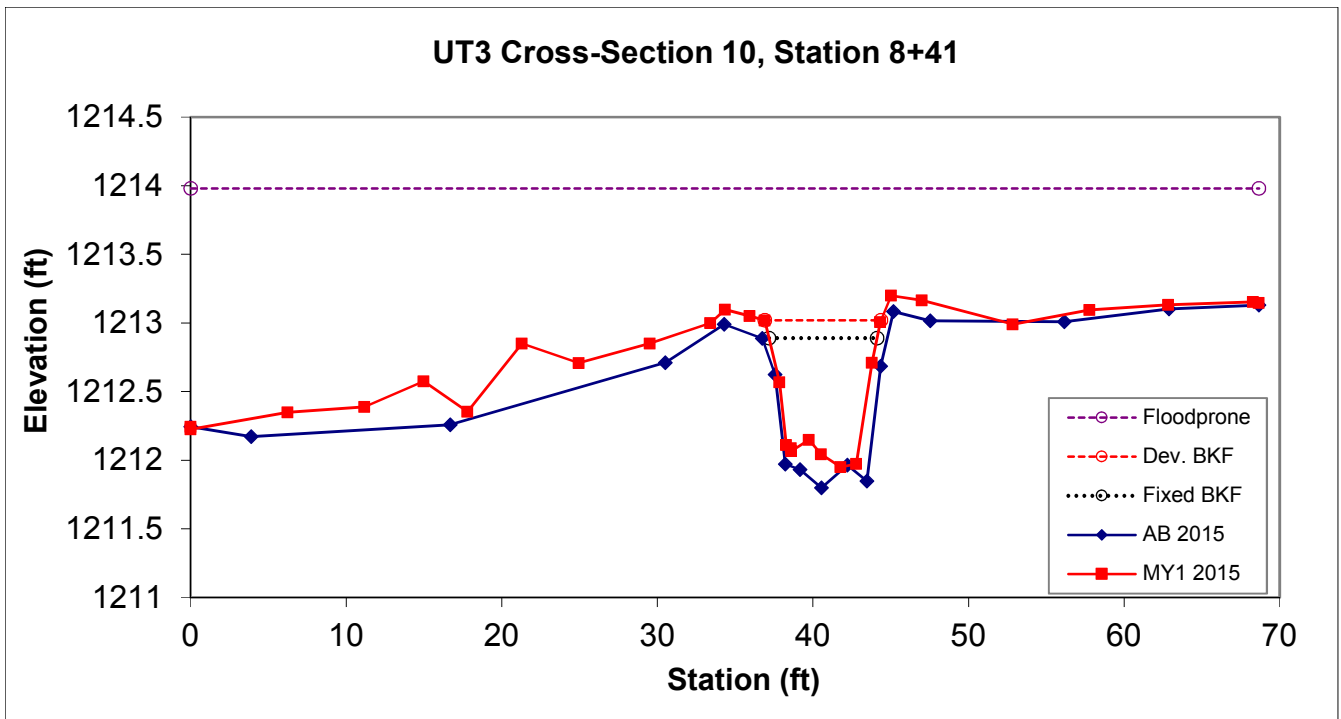

Looking at the Left Bank



Looking at the Right Bank



Permanent Cross-Section 11
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		11.9	13.02	0.92	2.06	14.21	1	5.6	1209.45	1209.42

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		9.7	11.53	0.85	1.88	13.65	1.1	6.3	1209.27	1209.42

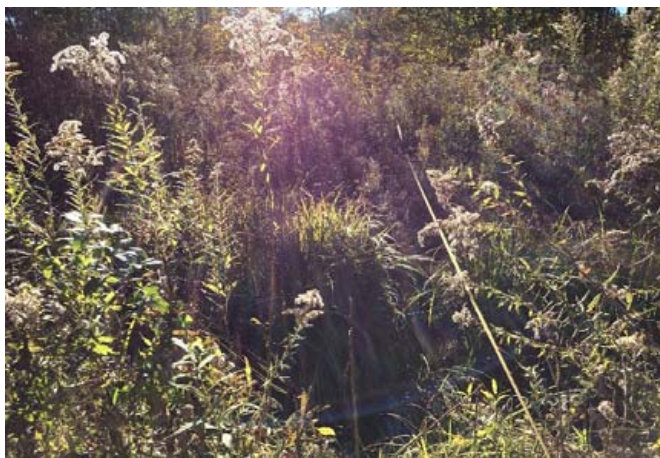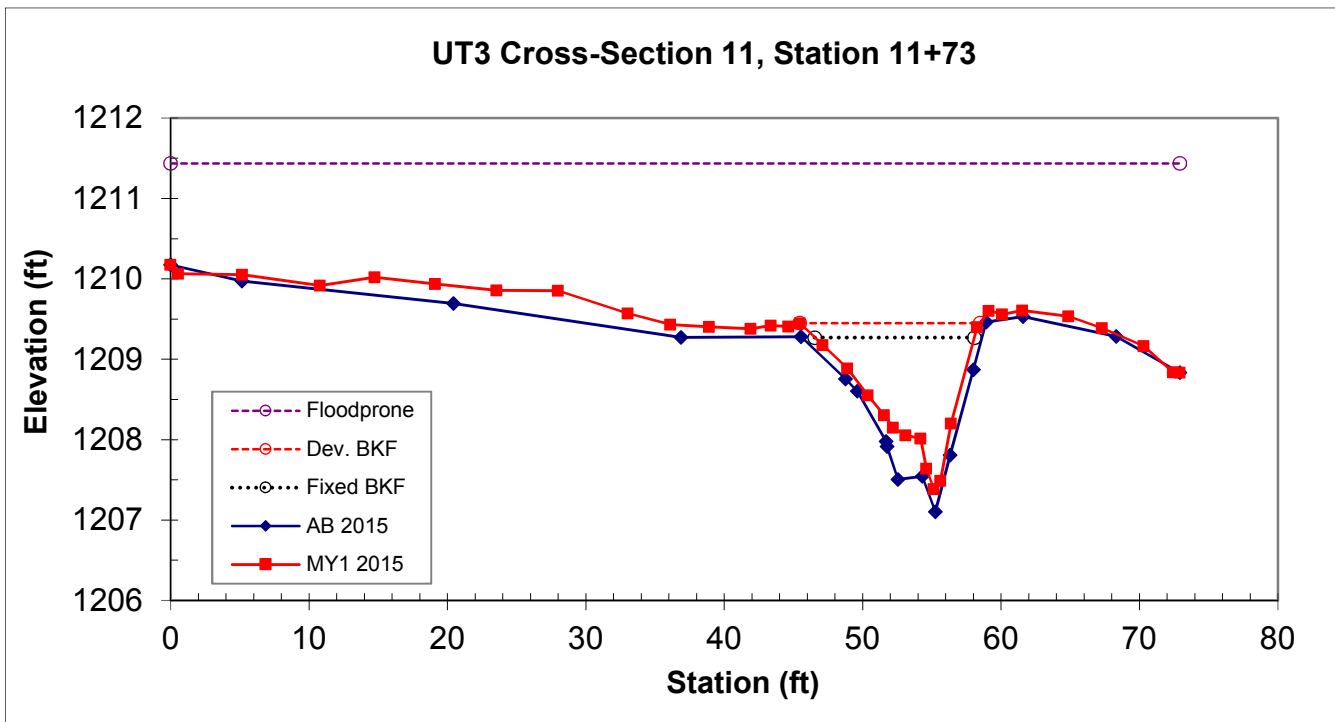

Looking at the Left Bank



Looking at the Right Bank

*Stationing was 10+55 in Baseline Plan, corrected in MY1 with more complete profile.


Permanent Cross-Section 12
(MY1 Data - collected October, 2015)

Based on developing BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	E	8	9.13	0.87	1.34	10.45	1	8.5	1209.04	1209.06

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	E	5.8	7.8	0.74	1.07	10.57	1.3	7	1208.77	1209.06

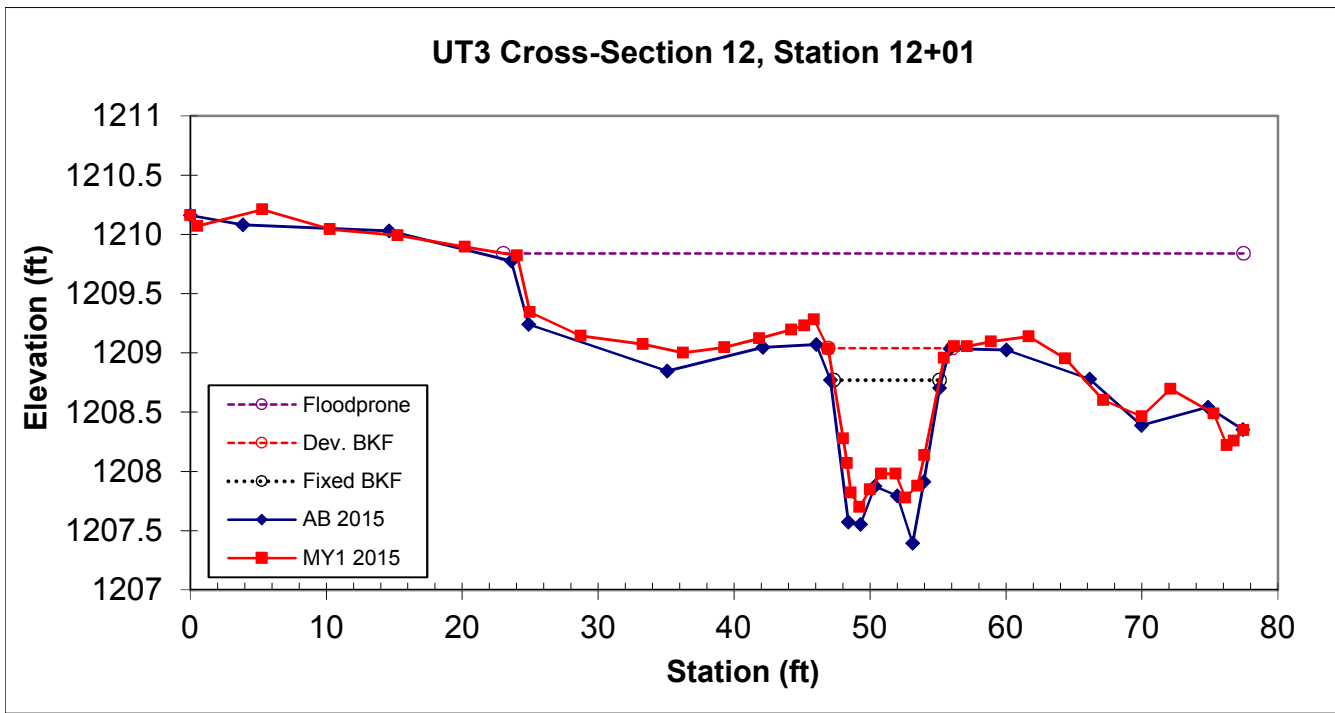

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 13
(MY1 Data - collected October, 2015)

Based on developing bankfull

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	7.9	9.75	0.81	1.23	12.04	1	5.2	1204.05	1205.28

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	C	7	9.28	0.75	1.13	12.32	1.1	5.4	1203.99	1204.08

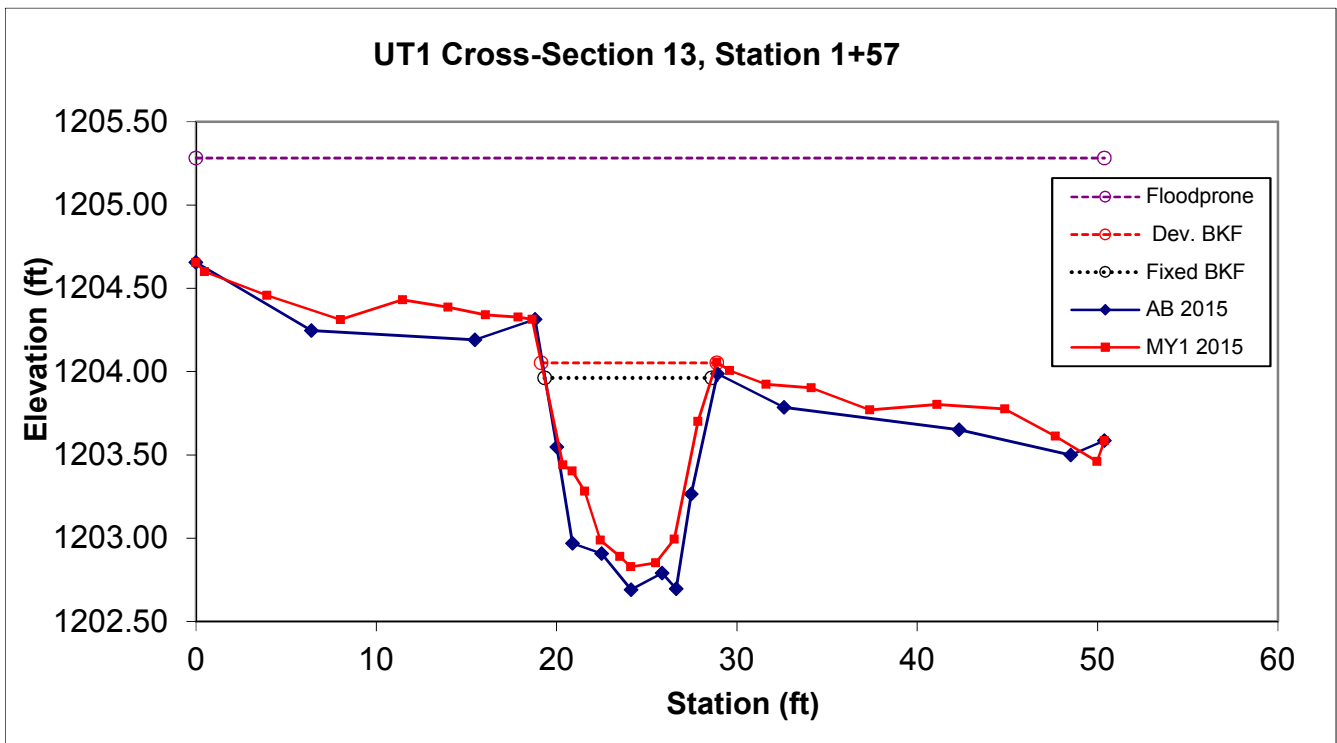

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 14
(MY1 Data - collected October, 2015)

Based on developing bankfull

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		15	10.96	1.36	2.89	8.03	1	7.4	1202	1202.14

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		10.9	8.59	1.27	2.48	6.75	1.2	9.4	1201.59	1202.14

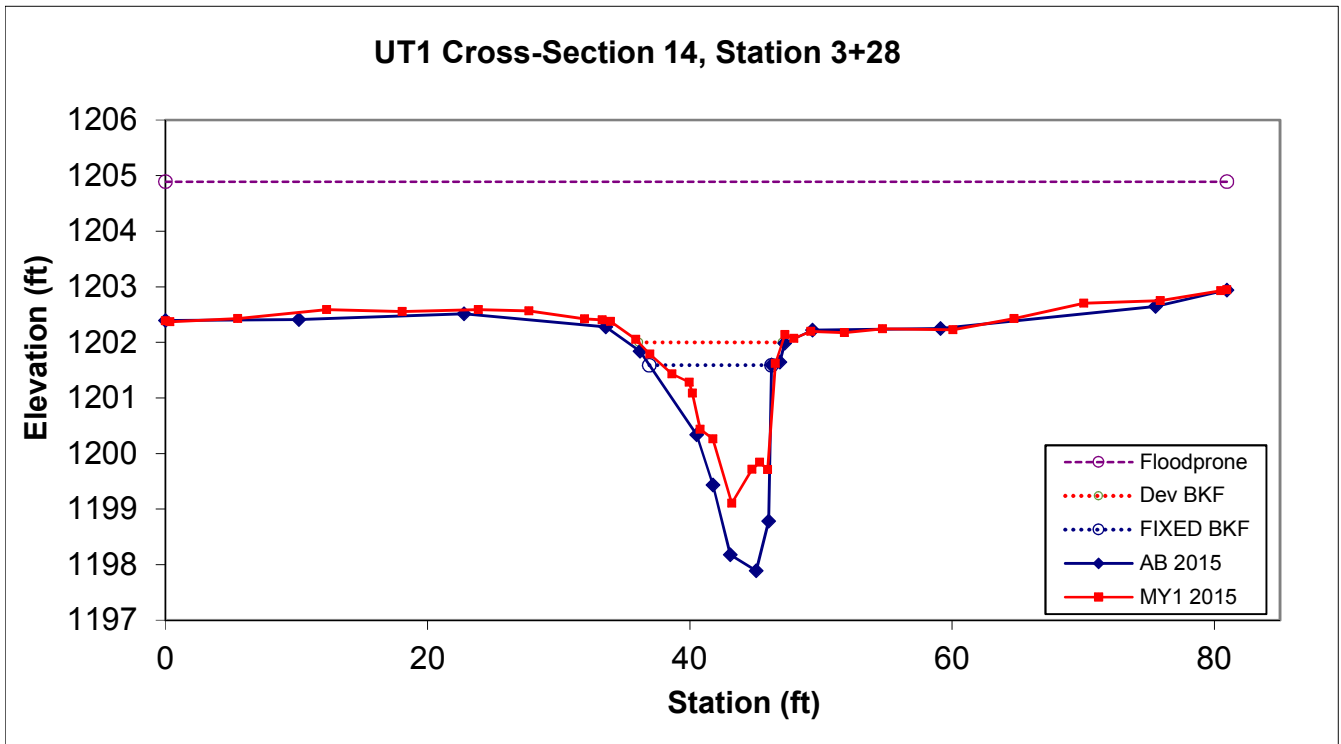

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 15
(MY1 Data - collected October, 2015)

Based on developing bankfull

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		4	8.35	0.48	0.98	17.41	1.1	8.1	1202.05	1202.11

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Pool		3	6.42	0.46	0.84	13.87	1.2	10.5	1201.91	1202.11

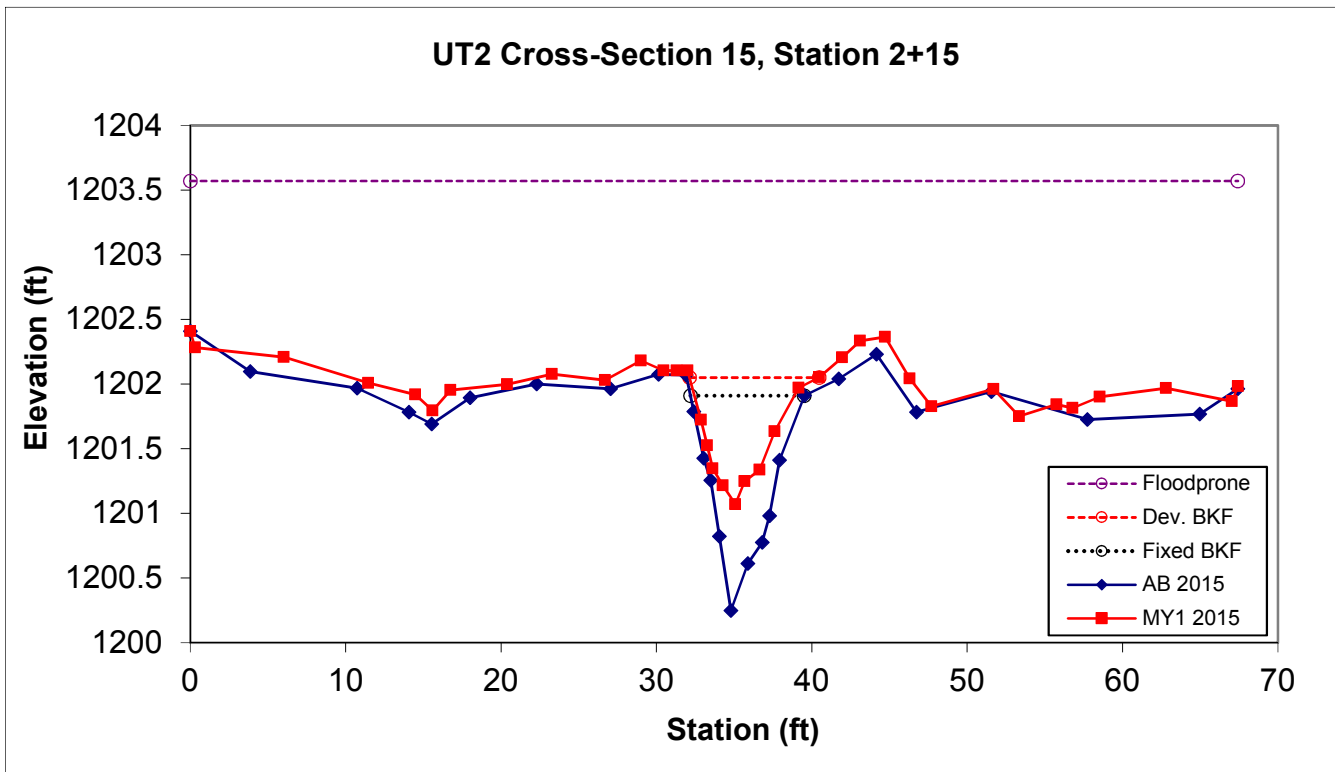

Looking at the Left Bank



Looking at the Right Bank


Permanent Cross-Section 16
(MY1 Data - collected October, 2015)

Based on developing bankfull

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	Cb	2.2	5.82	0.37	0.77	15.71	1	7.1	1201.21	1201.19

Based on fixed baseline BKF

Feature	Stream Type	BKF Area	BKF Width	BKF Depth	Max BKF Depth	W/D	BH Ratio	ER	BKF Elev	TOB Elev
Riffle	Cb	2.2	5.82	0.37	0.77	15.71	1	7.1	1201.21	1201.19

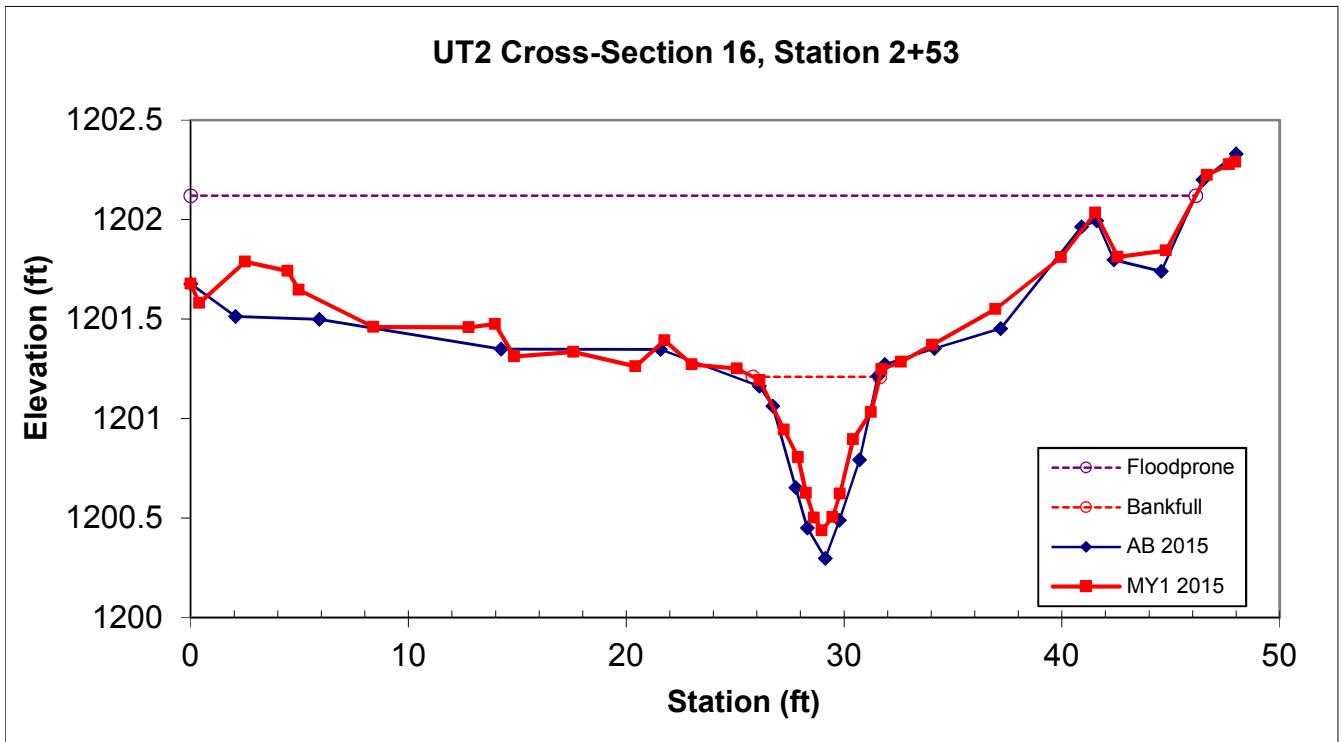


Looking at the Left Bank




Looking at the Right Bank

Figure 6. Longitudinal profiles with annual overlays.


Monitoring Year 1 Profile of U. Silver Creek, Station 0+00 to 32+00 Data collected October, 2015

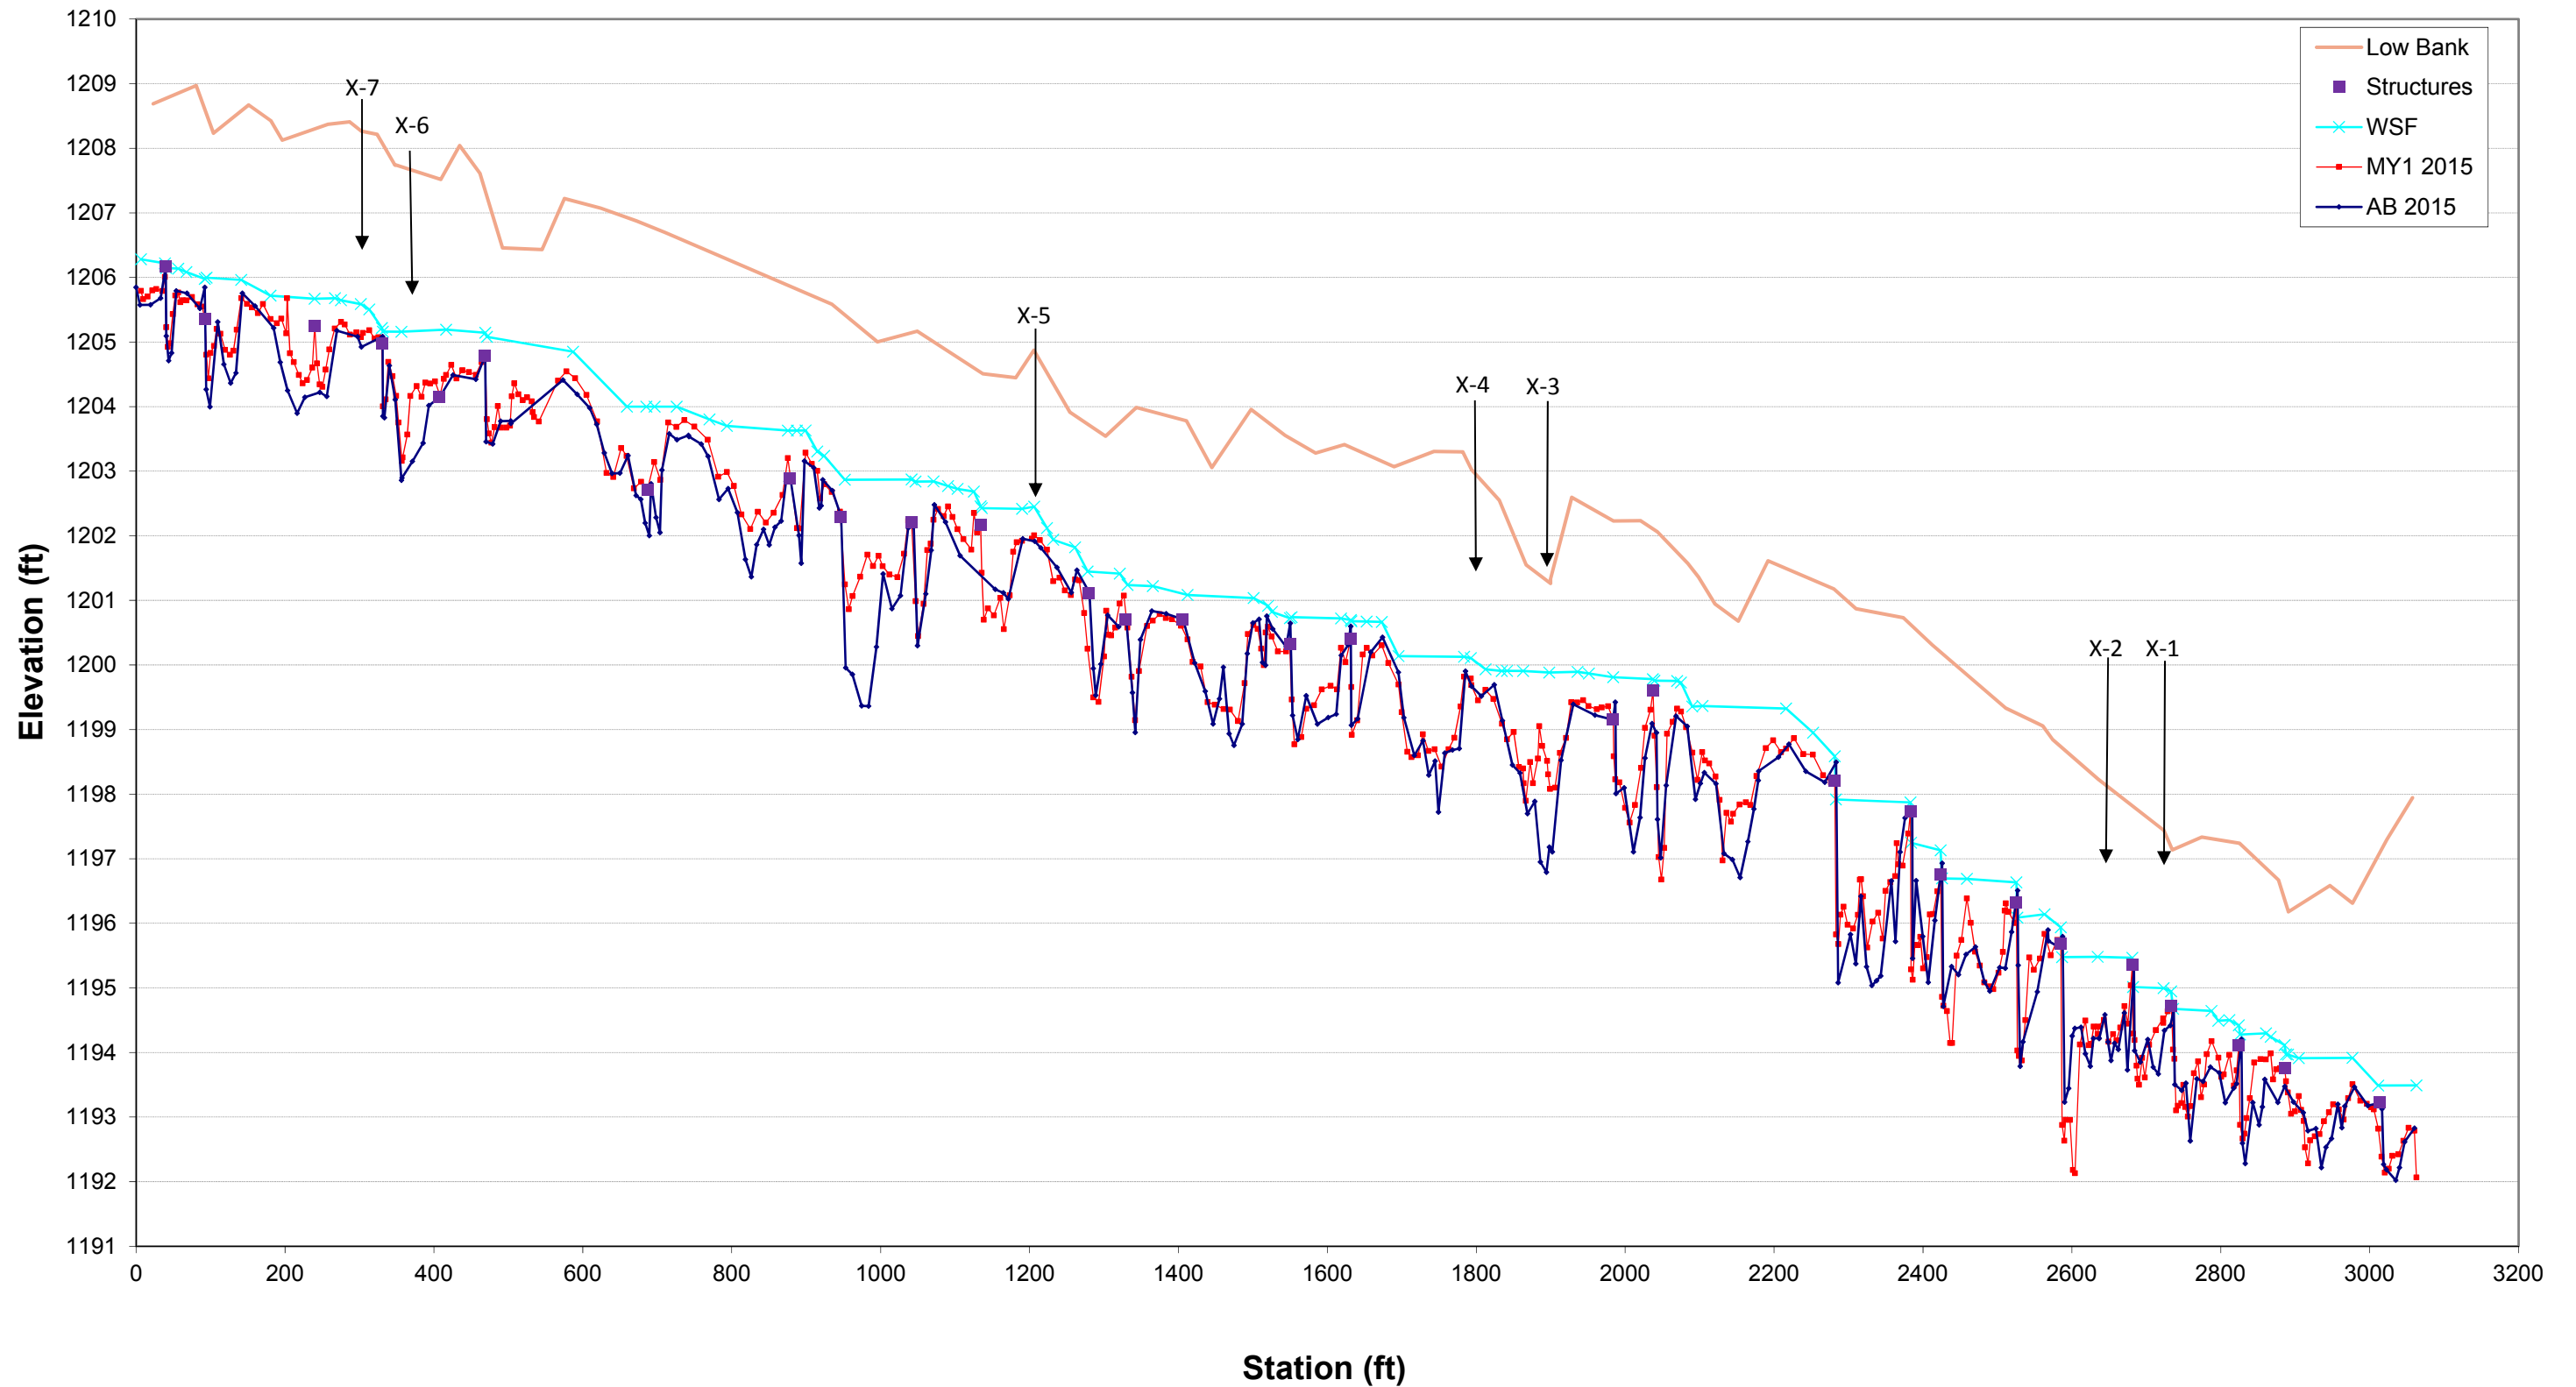

Monitoring Year 1, Profile of UT1, Station 0+00 to 5+00 Data collected October, 2015

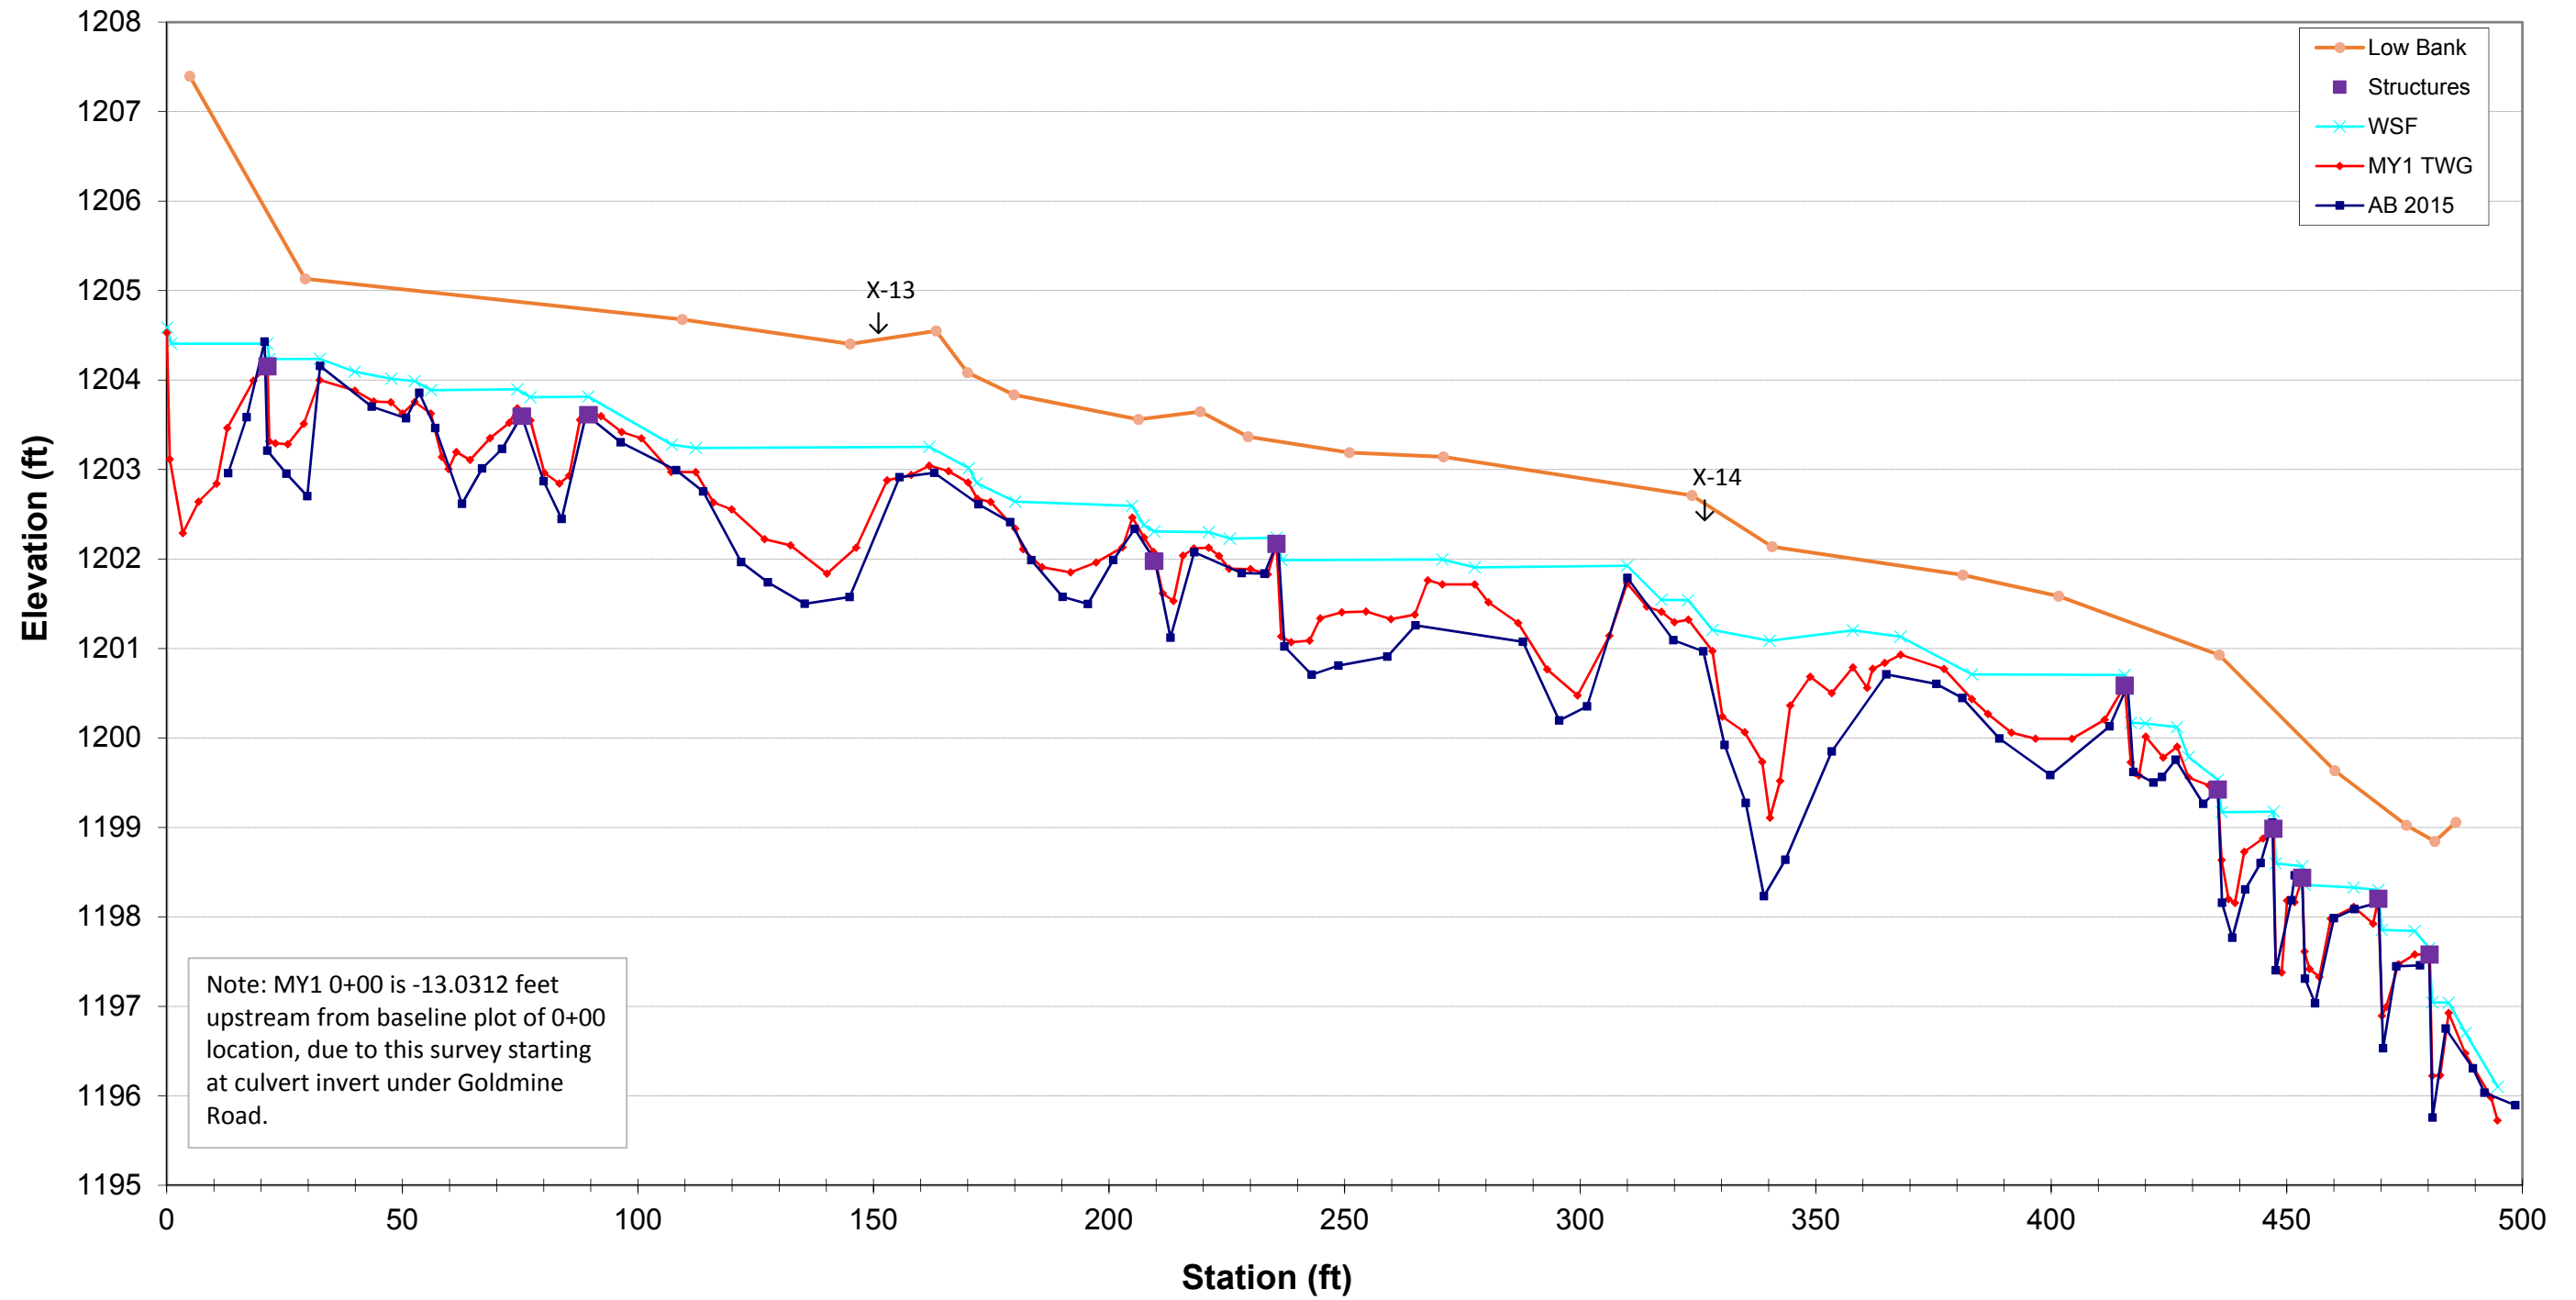

Monitoring Year 1 Profile of UT2, Station 0+00 to 3+20 Data collected October, 2015

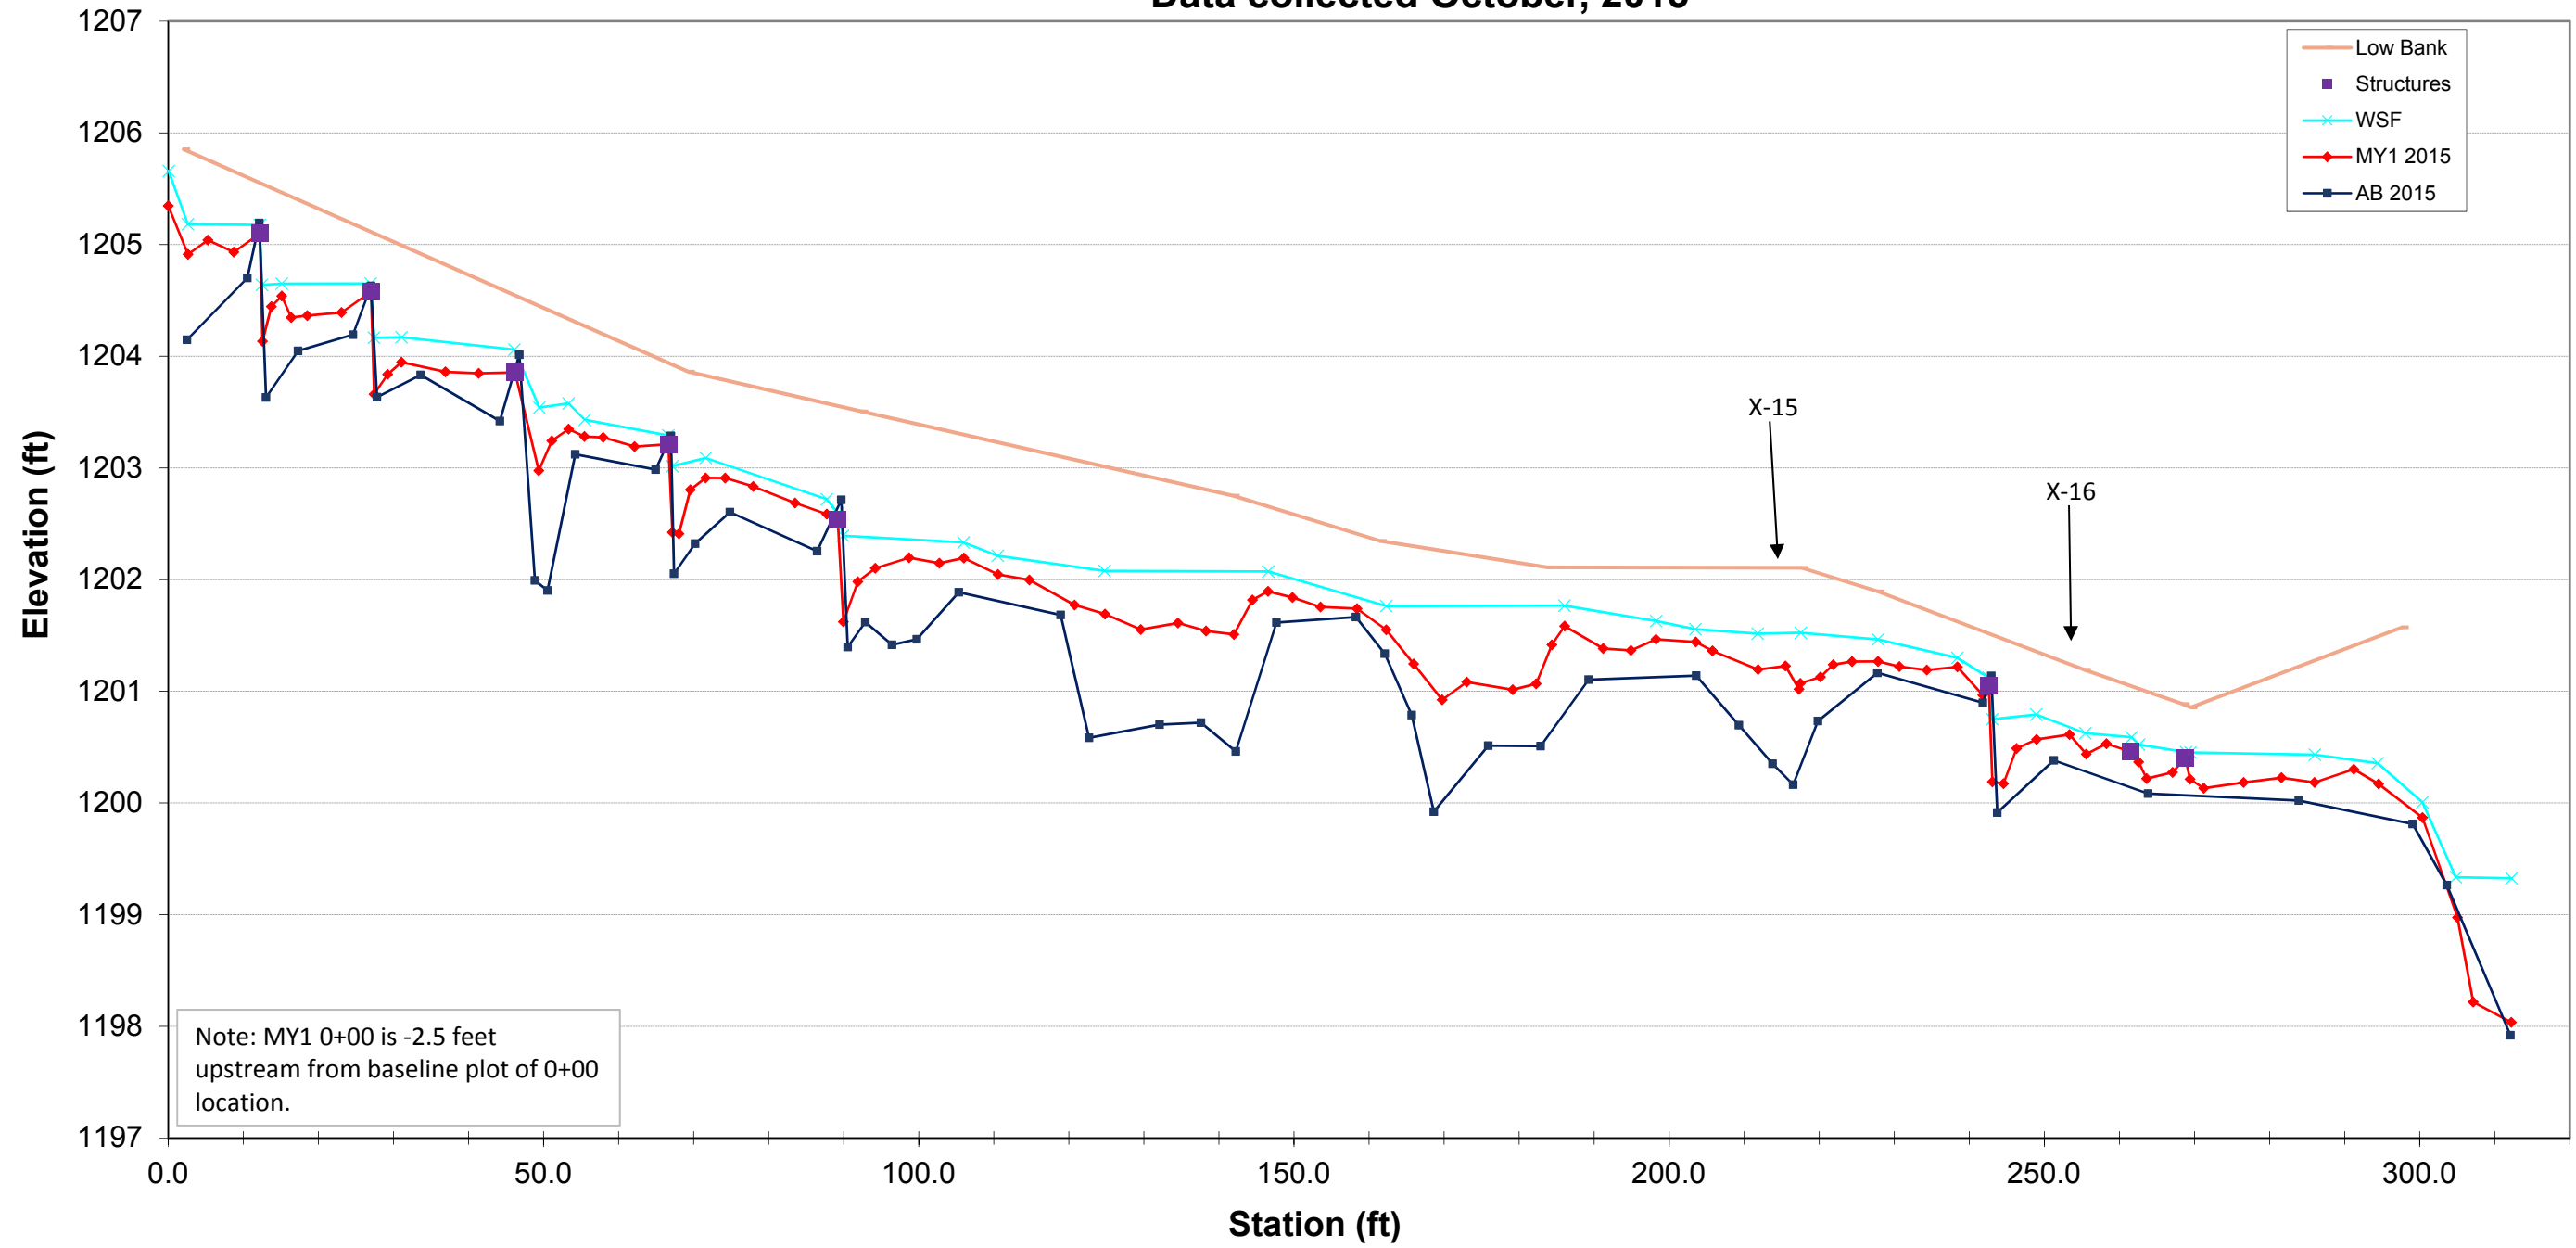

Monitoring Year 1, Profile of UT3, Station 0+00 to 14+00
Data collected October, 2015

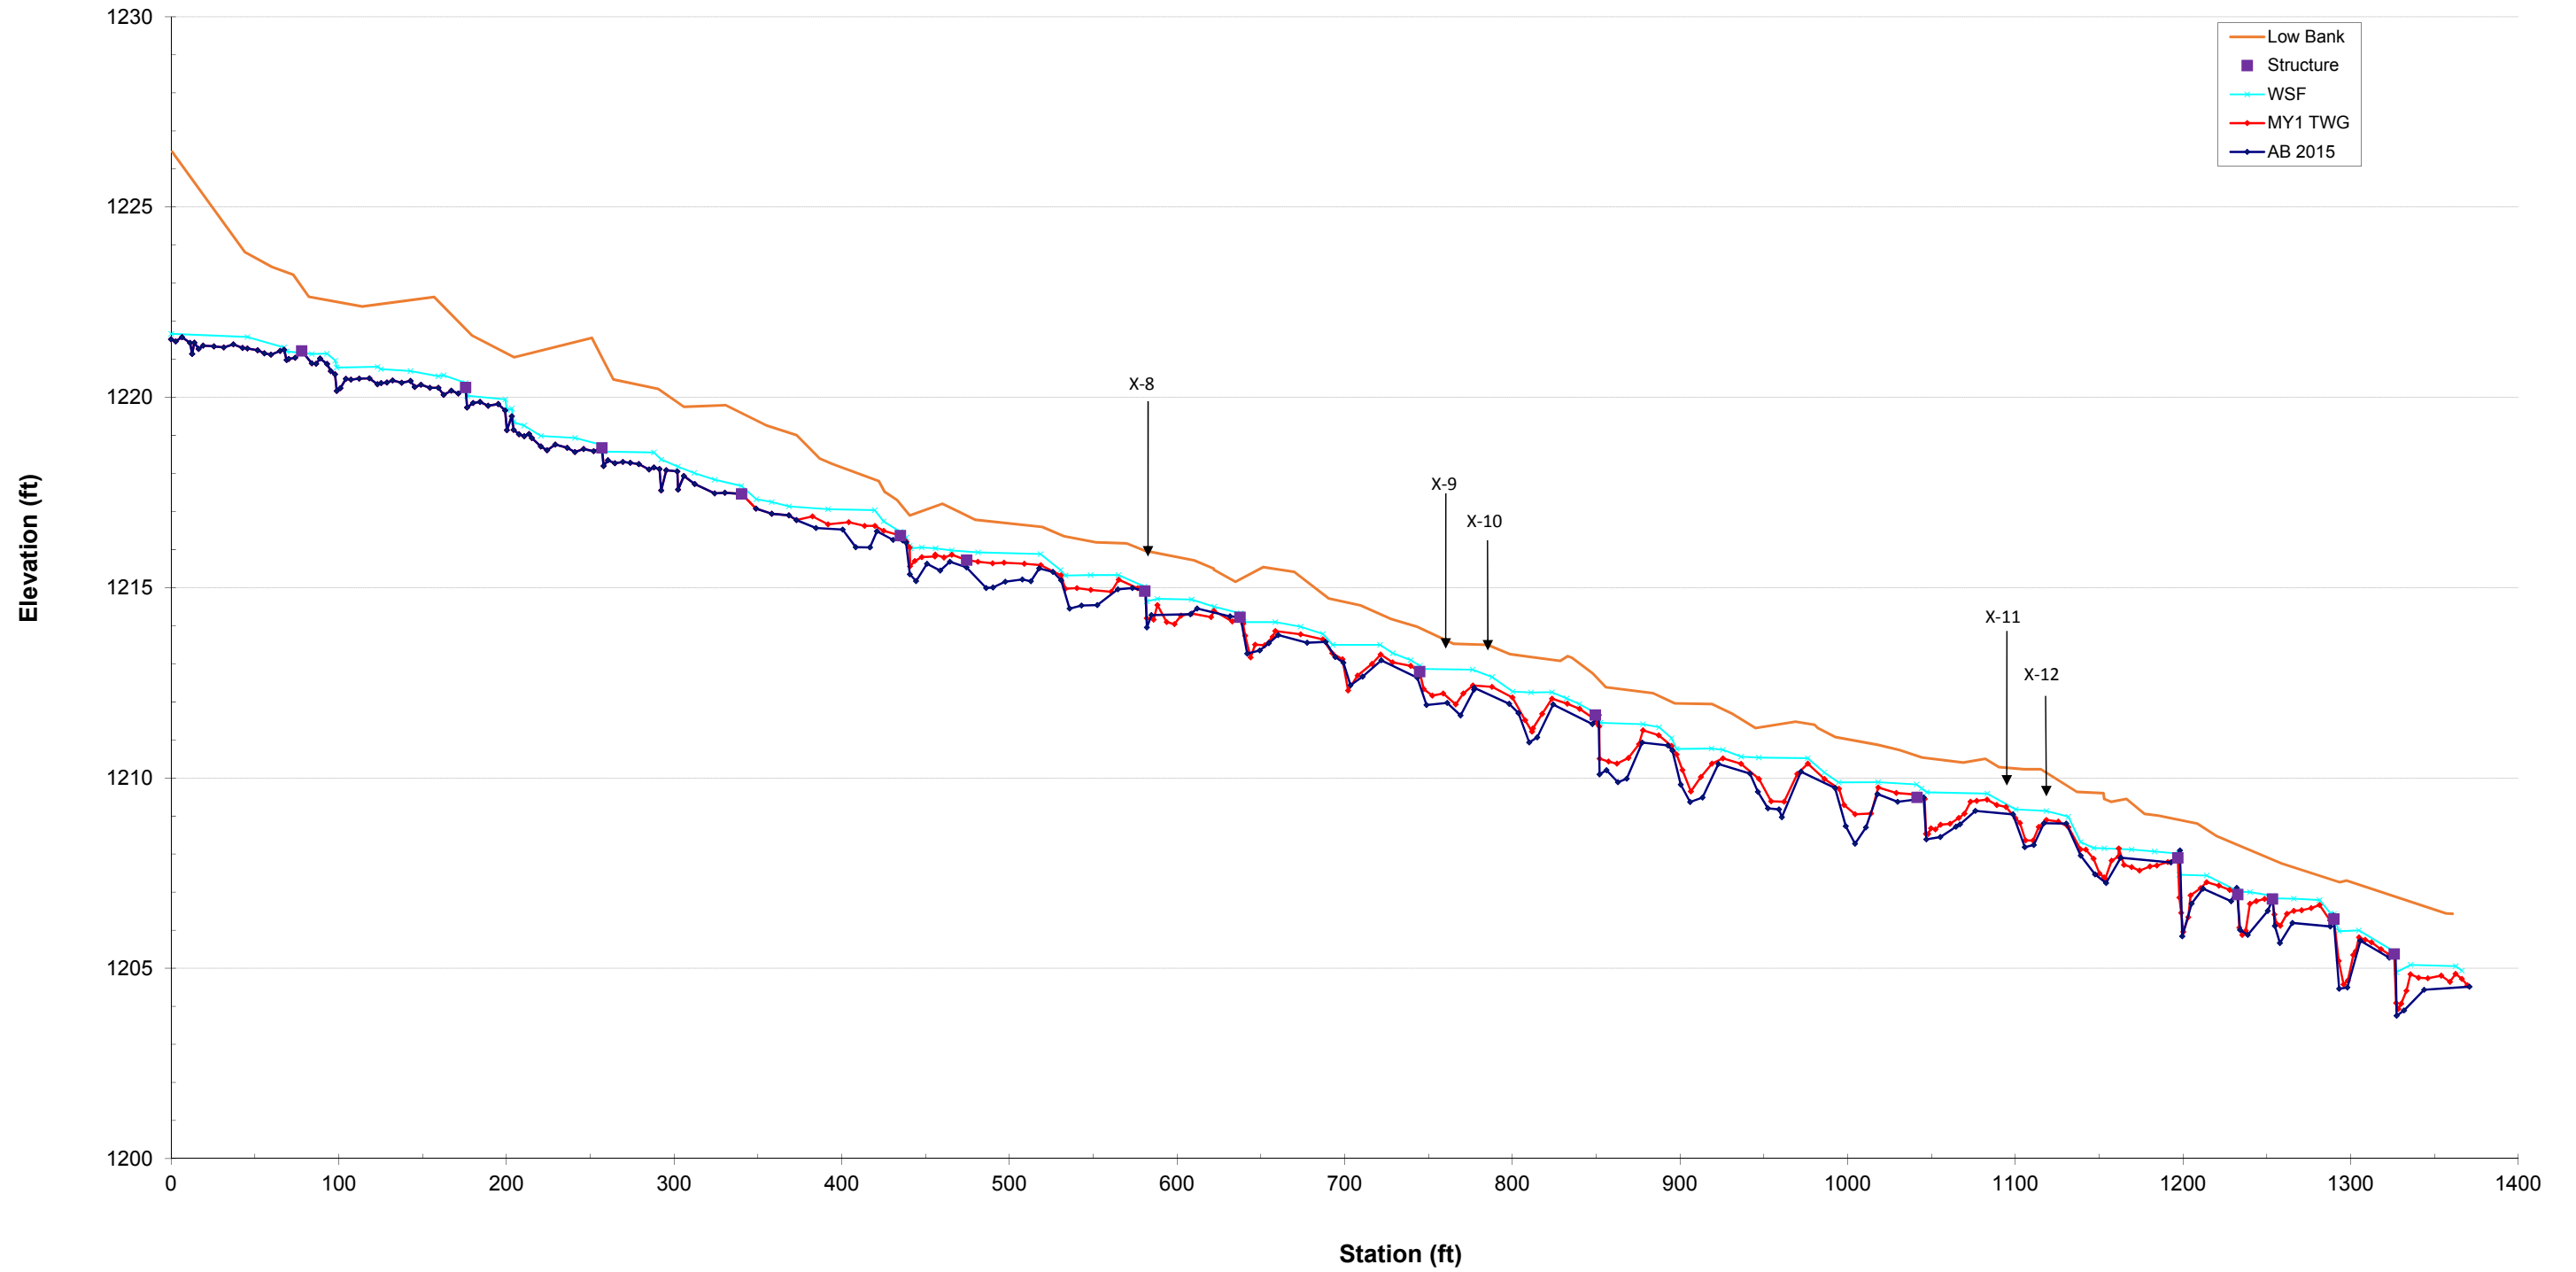




Figure 7. Pebble count plots with annual overlays.

Cross-Section Pebble Count; Monitoring Year 1
 U. Silver Creek Mitigation Project, DMS# 94645

SITE OR PROJECT:		U. Silver Cr				
REACH/LOCATION:		Riffle at XS4				
FEATURE:		Riffle				
DATE:		23-Oct-15				
		MY1 2015			Distribution	
MATERIAL	PARTICLE	SIZE (mm)	Total	Class %	% Cum	Plot Size (mm)
Silt/Clay	Silt / Clay	< .063			0%	0.063
Sand	Very Fine	.063 - .125			0%	0.125
	Fine	.125 - .25	1	1%	1%	0.25
	Medium	.25 - .50	2	2%	3%	0.50
	Coarse	.50 - 1.0			3%	1.0
Gravel	Very Coarse	1.0 - 2.0	4	4%	7%	2.0
	Very Fine	2.0 - 2.8			7%	2.8
	Very Fine	2.8 - 4.0	1	1%	8%	4.0
	Fine	4.0 - 5.6	2	2%	10%	5.6
	Fine	5.6 - 8.0	3	3%	13%	8.0
	Medium	8.0 - 11.0	3	3%	16%	11.0
	Medium	11.0 - 16.0	6	6%	22%	16.0
	Coarse	16 - 22.6	9	9%	31%	22.6
	Coarse	22.6 - 32	7	7%	38%	32
Cobble	Very Coarse	32 - 45	16	16%	54%	45
	Very Coarse	45 - 64	30	30%	84%	64
	Small	64 - 90	10	10%	94%	90
	Small	90 - 128	3	3%	97%	128
Boulder	Large	128 - 180	1	1%	98%	180
	Large	180 - 256	2	2%	100%	256
	Small	256 - 362			100%	362
	Small	362 - 512			100%	512
Boulder	Medium	512 - 1024			100%	1024
	Large-Very Large	1024 - 2048			100%	2048
Bedrock	Bedrock	> 2048			100%	5000
Total % of whole count			100	100%		

Largest particle = 235



Summary Data			
Channel materials			
D16 =	11.0	D84 =	64.0
D35 =	27.6	D95 =	101.2
D50 =	41.3	D100 =	180 - 256

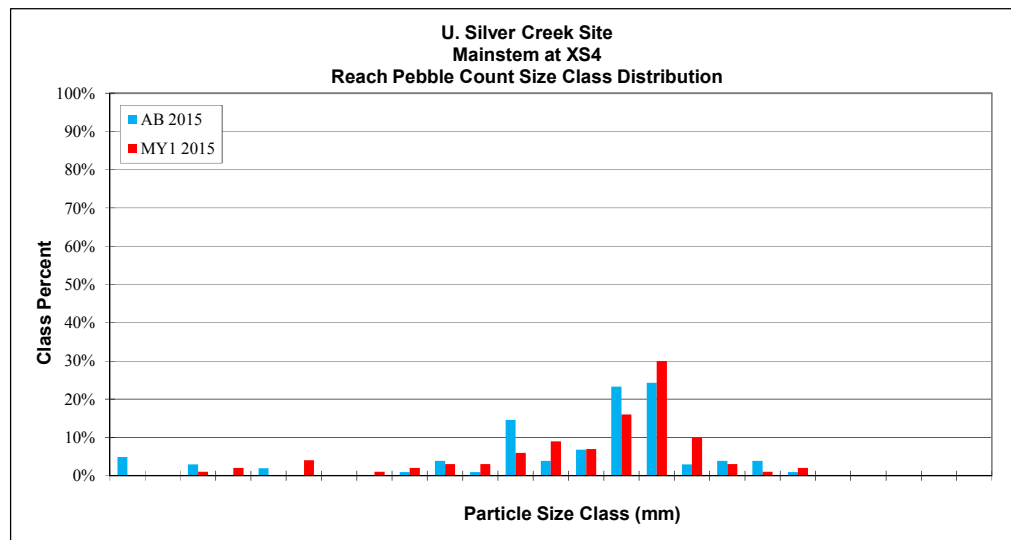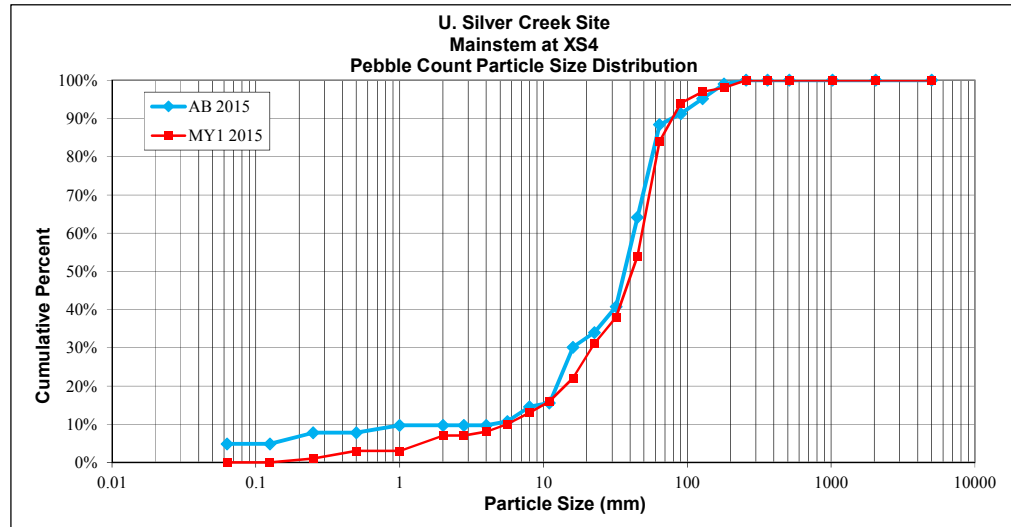

Cross-Section Pebble Count; Monitoring Year 1
 U. Silver Creek Mitigation Project, DMS# 94645

SITE OR PROJECT:		U. Silver Cr				
REACH/LOCATION:		Riffle at XS7				
FEATURE:		Riffle				
DATE:		23-Oct-15				
			MY1 2015			Distribution Plot Size (mm)
MATERIAL	PARTICLE	SIZE (mm)	Total	Class %	% Cum	
Silt/Clay	Silt / Clay	< .063			0%	0.063
Sand	Very Fine	.063 - .125			0%	0.125
	Fine	.125 - .25			0%	0.25
	Medium	.25 - .50	5	5%	5%	0.50
	Coarse	.50 - 1.0	8	8%	13%	1.0
	Very Coarse	1.0 - 2.0	4	4%	17%	2.0
Gravel	Very Fine	2.0 - 2.8			17%	2.8
	Very Fine	2.8 - 4.0	3	3%	20%	4.0
	Fine	4.0 - 5.6	7	7%	27%	5.6
	Fine	5.6 - 8.0	3	3%	30%	8.0
	Medium	8.0 - 11.0	7	7%	37%	11.0
	Medium	11.0 - 16.0	15	15%	52%	16.0
	Coarse	16 - 22.6	6	6%	58%	22.6
	Coarse	22.6 - 32	5	5%	63%	32
	Very Coarse	32 - 45	6	6%	69%	45
	Very Coarse	45 - 64	12	12%	81%	64
Cobble	Small	64 - 90	12	12%	93%	90
	Small	90 - 128	3	3%	96%	128
	Large	128 - 180	2	2%	98%	180
	Large	180 - 256	2	2%	100%	256
Boulder	Small	256 - 362			100%	362
	Small	362 - 512			100%	512
	Medium	512 - 1024			100%	1024
	Large-Very Large	1024 - 2048			100%	2048
Bedrock	Bedrock	> 2048			100%	5000
Total % of whole count			100	100%		

Summary Data			
Channel materials			
D16 =	1.7	D84 =	69.7
D35 =	10.0	D95 =	113.8
D50 =	15.2	D100 =	180 - 256

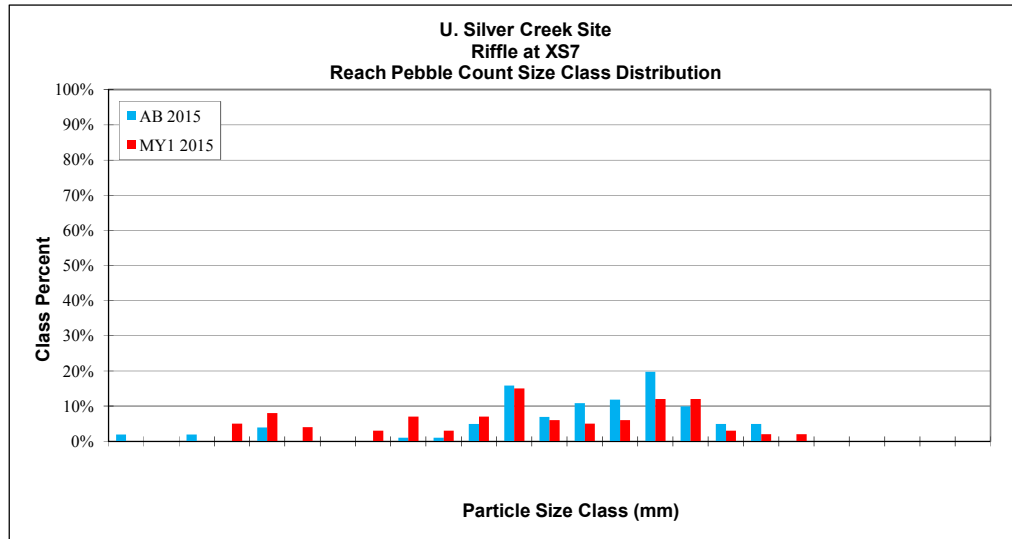
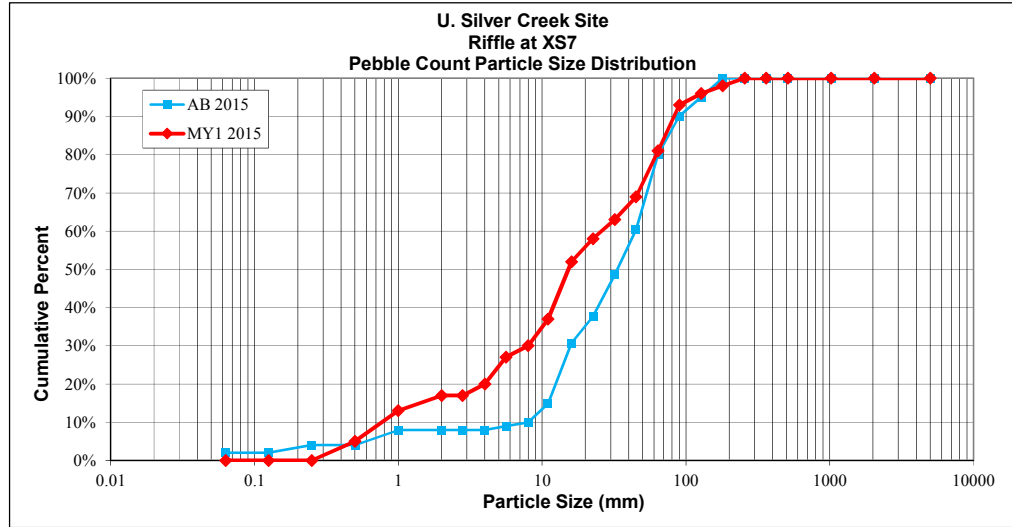


Cross-Section Pebble Count; Monitoring Year 1
 U. Silver Creek Mitigation Project, DMS# 94645

SITE OR PROJECT:		U. Silver Cr				
REACH/LOCATION:		UT1 XS13				
FEATURE:		Riffle				
DATE:		23-Oct-15				
		MY1 2015			Distribution	
MATERIAL	PARTICLE SIZE (mm)	Total	Class %	% Cum	Plot Size (mm)	
Silt/Clay	Silt / Clay < .063			0%	0.063	
Sand	Very Fine .063 - .125			0%	0.125	
	Fine .125 - .25			0%	0.25	
	Medium .25 - .50			0%	0.50	
	Coarse .50 - 1.0			0%	1.0	
Gravel	Very Coarse 1.0 - 2.0	2	2%	2%	2.0	
	Very Fine 2.0 - 2.8			2%	2.8	
	Very Fine 2.8 - 4.0			2%	4.0	
	Fine 4.0 - 5.6	1	1%	3%	5.6	
	Fine 5.6 - 8.0			3%	8.0	
	Medium 8.0 - 11.0	3	3%	6%	11.0	
	Medium 11.0 - 16.0	14	14%	20%	16.0	
	Coarse 16 - 22.6	4	4%	24%	22.6	
	Coarse 22.6 - 32	6	6%	30%	32	
	Very Coarse 32 - 45	22	22%	52%	45	
Cobble	Very Coarse 45 - 64	30	30%	82%	64	
	Small 64 - 90	9	9%	91%	90	
	Small 90 - 128	6	6%	97%	128	
	Large 128 - 180	3	3%	100%	180	
Boulder	Large 180 - 256			100%	256	
	Small 256 - 362			100%	362	
	Small 362 - 512			100%	512	
	Medium 512 - 1024			100%	1024	
Bedrock	Large-Very Large 1024 - 2048			100%	2048	
	Bedrock > 2048			100%	5000	
Total % of whole count		100		100%		

Largest particle= 180

Summary Data			
Channel materials			
D16 =	14.4	D84 =	69.0
D35 =	34.6	D95 =	113.8
D50 =	43.6	D100 =	128 - 180

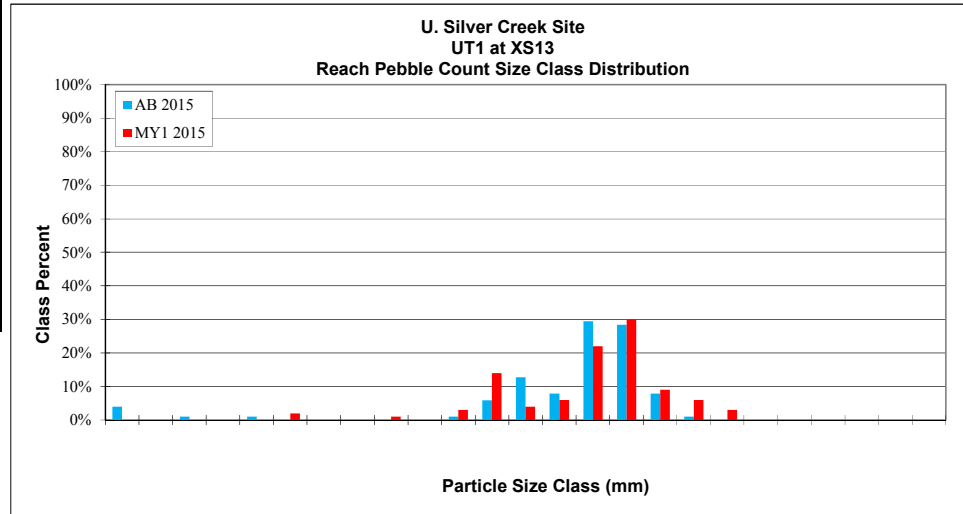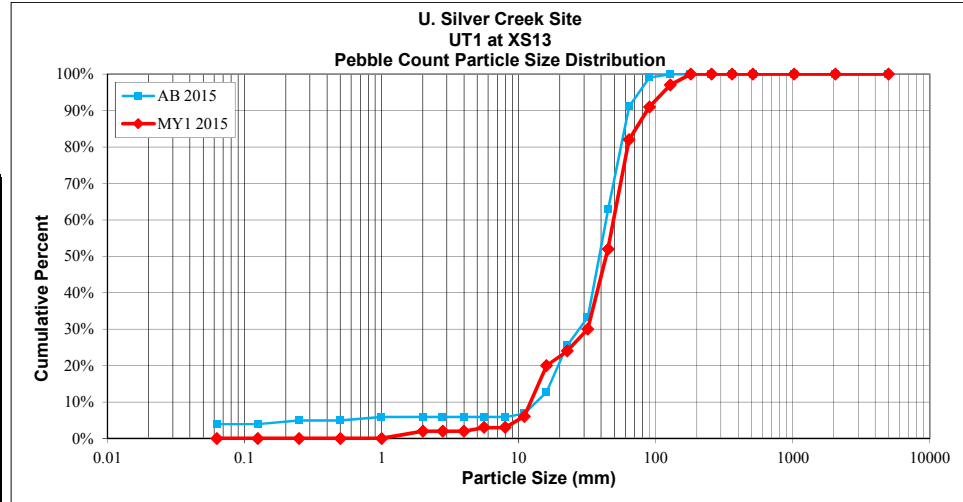



Cross-Section Pebble Count; Monitoring Year 1
 U. Silver Creek Mitigation Project, DMS# 94645

SITE OR PROJECT:	U. Silver Cr
REACH/LOCATION:	UT2 XS16
FEATURE:	Riffle
DATE:	23-Oct-15

			MY1 2015			Distribution
MATERIAL	PARTICLE	SIZE (mm)	Total	Class %	% Cum	Plot Size (mm)
Silt/Clay	Silt / Clay	< .063			0%	0.063
Sand	Very Fine	.063 - .125			0%	0.125
	Fine	.125 - .25	3	3%	3%	0.25
	Medium	.25 - .50	9	9%	12%	0.50
	Coarse	.50 - 1.0	6	6%	18%	1.0
Gravel	Very Coarse	1.0 - 2.0			18%	2.0
	Very Fine	2.0 - 2.8			18%	2.8
	Very Fine	2.8 - 4.0	2	2%	20%	4.0
	Fine	4.0 - 5.6	7	7%	27%	5.6
	Fine	5.6 - 8.0	14	14%	41%	8.0
	Medium	8.0 - 11.0	18	18%	58%	11.0
	Medium	11.0 - 16.0	18	18%	76%	16.0
	Coarse	16 - 22.6	11	11%	87%	22.6
Cobble	Coarse	22.6 - 32	6	6%	93%	32
	Very Coarse	32 - 45	2	2%	95%	45
	Very Coarse	45 - 64	2	2%	97%	64
	Small	64 - 90			97%	90
Boulder	Small	90 - 128	1	1%	98%	128
	Large	128 - 180	2	2%	100%	180
	Large	180 - 256			100%	256
	Small	256 - 362			100%	362
Boulder	Small	362 - 512			100%	512
	Medium	512 - 1024			100%	1024
	Large-Very Large	1024 - 2048			100%	2048
Bedrock	Bedrock	> 2048			100%	5000
Total % of whole count			101	100%		

Largest particle=

Summary Data			
Channel materials			
D16 =	0.8	D84 =	20.5
D35 =	6.9	D95 =	44.6
D50 =	9.5	D100 =	128 - 180

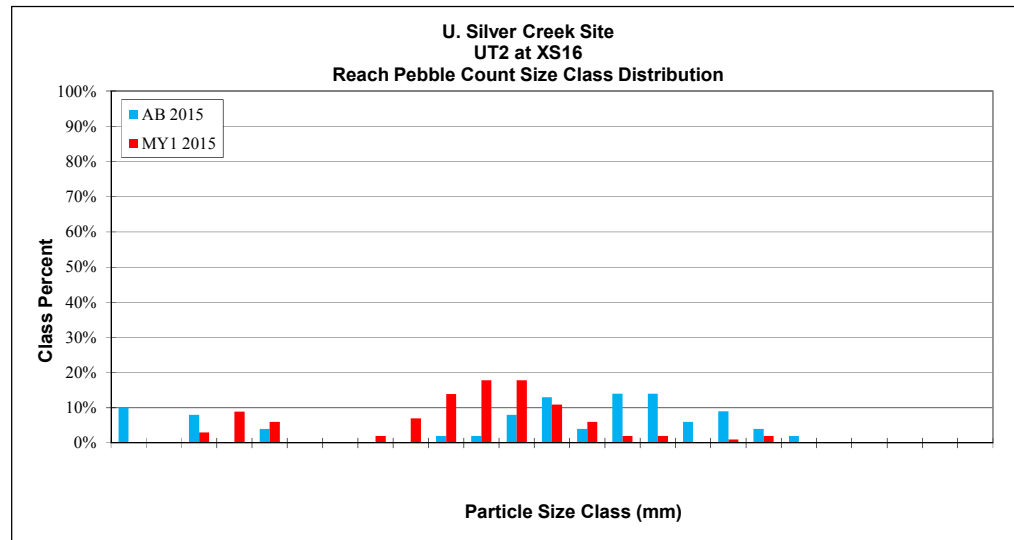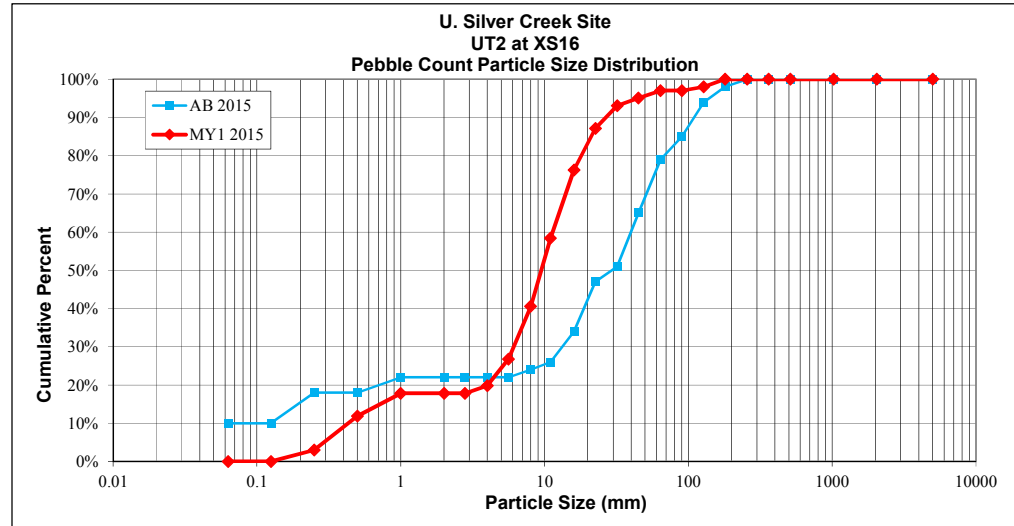

Cross-Section Pebble Count; Monitoring Year 1
 U. Silver Creek Mitigation Project, DMS# 94645

SITE OR PROJECT:	U. Silver Cr
REACH/LOCATION:	UT3 XS8
FEATURE:	Riffle
DATE:	23-Oct-15

MATERIAL	PARTICLE	SIZE (mm)	MY1 2015			Distribution Plot Size (mm)
			Total	Class %	% Cum	
Silt/Clay	Silt / Clay	< .063			0%	0.063
Sand	Very Fine	.063 - .125			0%	0.125
	Fine	.125 - .25	10	10%	10%	0.25
	Medium	.25 - .50	20	20%	30%	0.50
	Coarse	.50 - 1.0			30%	1.0
	Very Coarse	1.0 - 2.0			30%	2.0
Gravel	Very Fine	2.0 - 2.8			30%	2.8
	Very Fine	2.8 - 4.0			30%	4.0
	Fine	4.0 - 5.6			30%	5.6
	Fine	5.6 - 8.0			30%	8.0
	Medium	8.0 - 11.0	2	2%	32%	11.0
	Medium	11.0 - 16.0	11	11%	43%	16.0
	Coarse	16 - 22.6	10	10%	53%	22.6
	Coarse	22.6 - 32	2	2%	55%	32
	Very Coarse	32 - 45	13	13%	68%	45
	Very Coarse	45 - 64	19	19%	87%	64
Cobble	Small	64 - 90	9	9%	96%	90
	Small	90 - 128	2	2%	98%	128
	Large	128 - 180	1	1%	99%	180
	Large	180 - 256	1	1%	100%	256
Boulder	Small	256 - 362			100%	362
	Small	362 - 512			100%	512
	Medium	512 - 1024			100%	1024
	Large-Very Large	1024 - 2048			100%	2048
Bedrock	Bedrock	> 2048			100%	5000
Total % of whole count			100	100%		

Largest particle= 190

Summary Data			
Channel materials			
D16 =	0.3	D84 =	60.5
D35 =	12.2	D95 =	86.7
D50 =	20.4	D100 =	180 - 256

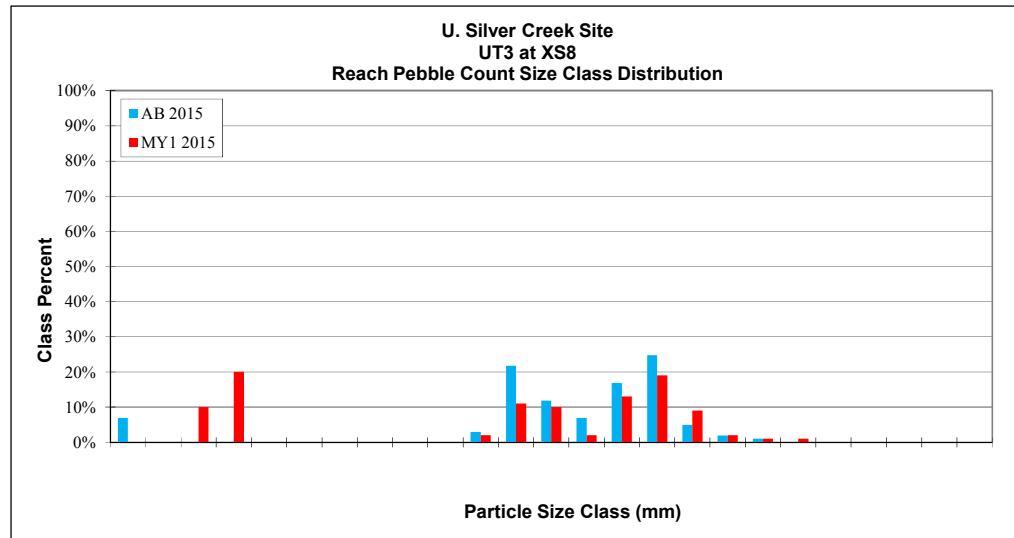
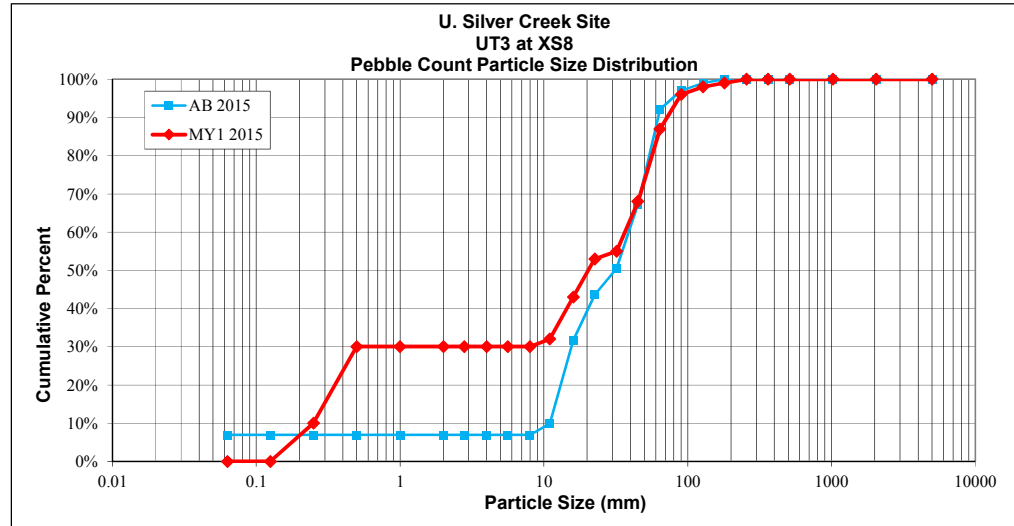


Table 10. Monitoring Year 1 Stream Summary
Upper Silver Creek Restoration Project: DMS Project ID No. 94645

UT2																																	
Parameter	USGS Gauge	Regional Curve Interval ^{1,2}				Pre-Existing Condition ¹					Reference Reach Data					Design					As-built					MY1							
		NC Mtn/NC Pied. Rural				Min	Mean	Med	Max	SD	n	Morgan Creek					Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD	n	Min	Mean	Med	Max	SD
Dimension and Substrate - Riffle																																	
BF Width (ft)		6.0	3.1	-	3.1	-	3.4	-	2	6.3	-	7.9	-	-	-	6.0	-	120.0	-	-	-	-	6.6	-	-	1	-	5.8	-	-	1		
Floodprone Width (ft)		-	-	-	5.1	-	6.4	-	2	15	-	19	-	-	60	-	-	-	-	-	-	-	>100	-	-	1	-	>100	-	-	1		
BF Mean Depth (ft)		0.4	0.6	-	0.84	-	0.90	-	2	0.7	-	0.9	-	-	0.5	-	-	-	-	-	-	0.4	-	-	1	-	0.4	-	-	1			
BF Max Depth (ft)		-	-	-	1.1	-	1.4	-	2	1.0	-	1.35	-	-	0.6	-	-	-	-	-	-	0.9	-	-	1	-	0.8	-	-	1			
BF Cross-sectional Area (ft ²)		2.6	2.6	-	2.8	-	2.9	-	2	5.5	-	6.5	-	-	3.0	-	-	-	-	-	-	2.7	-	-	1	-	2.2	-	-	1			
Width/Depth Ratio		-	-	-	3.5	-	4.0	-	2	7.3	-	11.7	-	-	12.0	-	-	-	-	-	-	16.0	-	-	1	-	15.7	-	-	1			
Entrenchment Ratio		-	-	-	1.6	-	1.9	-	2	1.9	-	3.0	-	-	10	-	20	-	-	-	-	7.0	-	-	1	-	7.1	-	-	1			
Bank Height Ratio		-	-	-	2.2	-	2.4	-	2	-	-	-	-	-	1.1	-	-	-	-	-	-	1.2	-	-	1	-	1.0	-	-	1			
d50 (mm)		-	-	-	18.00	-	-	-	-	-	3.0	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-			
Pattern																																	
Channel Beltwidth (ft)		-	-	-	-	-	-	-	-	-	-	-	-	-	22	-	30	-	-	-	-	30.4	32.6	32.2	35.3	2.02	3	30.4	32.6	32.2	35.3	2.02	3
Radius of Curvature (ft)		-	-	-	-	-	-	-	-	-	-	-	-	-	12	-	18	-	-	-	-	14.3	15.5	14.4	17.7	1.58	3	14.3	15.5	14.4	17.7	1.58	3
Rc: Bankfull width (ft/ft)		-	-	-	-	-	-	-	-	-	-	-	-	-	2.0	-	3.0	-	-	-	-	2.17	2.34	2.18	2.68	0.24	3	2.17	2.34	2.18	2.68	0.24	3
Meander Wavelength (ft)		-	-	-	-	-	-	-	-	-	-	-	-	-	45	-	75	-	-	-	-	52.1	54.9	54.9	57.6	2.8	2	52.1	54.9	54.9	57.6	2.8	2
Meander Width Ratio		-	-	-	-	-	-	-	-	-	-	-	-	-	1.2	-	1.2	-	-	-	-	7.9	8.3	8.3	8.7	0.4	2	7.9	8.3	8.3	8.7	0.4	2
Profile																																	
Riffle Length (ft)		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	13.6	20.8	14.3	47.8	13.5	5	8.7	14.5	15.1	17.6	2.6	9
Riffle Slope (ft/ft)		-	-	-	0.014	-	0.057	-	-	0.013	-	0.054	-	-	0.014	-	0.033	-	-	-	-	0.0000	0.0131	0.0147	0.0214	0.0081	5	0.0000	0.0130	0.0129	0.0230	0.0072	9
Pool Length (ft)		-	-	-	5.2	-	12.7	-	-	17.41	-	-	-	-	7.5	-	26.03	-	-	-	-	7.5	17.3	15.6	28.8	8.0	8	2.9	11.9	9.5	25.7	8.1	9
Pool Spacing (ft)		-	-	-	9.5	-	51	-	-	39.9	-	62.3	-	-	9	-	30	-	-	-	-	14.8	28.8	25.2	47.9	11.5	8	14.8	32.9	22.8	73.4	18.9	7
Pool Max Depth (ft)		-	-	-	-	-	-	-	-	-	1.8	-	-	-	-	1.4	-	-	-	-	-	1.7	-	-	-	1	-	0.8	-	-	-	-	1
Pool Volume (ft ³)		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
Substrate and Transport Parameters																																	
Ri% / Ru% / P% / G% / S%		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SC% / Sa% / G% / B% / Be%		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
d16 / d35 / d50 / d84 / d95		-	-	-	-	-	5.6 / 13 / 18 / 43 / 60	-	-	-	-	-	-	-	-	-	-	-	-	-	-	0.2 / 16.4 / 29.3 / 85.0 / 139.4	-	-	-	-	-	0.8 / 6.9 / 9.5 / 20.5 / 44.6	-	-	-	-	
Reach Shear Stress (competency) lb/ft ²		-	-	-	-	-	-	-	-	0.2	-	0.6	-	-	0.3	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Max part size (mm) mobilized at bankfull (Rosgen Curve)		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Stream Power (transport capacity) W/m ²		-	-	-	45	-	51	-	-	6.5	-	28.5	-	-	33	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Additional Reach Parameters																																	
Drainage Area (SM)		-	0.05	-	0.05	-	-	-	-	-	0.12	-	-	-	0.05	-	0.05	-	-	-	-	2.73	-	-	3.35	-	2.73	-	-	3.35	-	-	
Impervious cover estimate (%)		-	-	-	<5%	-	-	-	-	<5%	-	-	-	-	<5%	-	-	-	-	-	-	<5%	-	-	-	-	<5%	-	-	-	-	-	
Rosgen Classification		-	-	-	G/B ³	-	-	-	-	E/Bc	-	-	-	-	Cb, C	-	-	-	-	-	-	C	-	-	-	-	C	-	-	-	-		
BF Velocity (fps)		-	-	-	3.2	-	3.9	-	-	2.1	-	3.4	-	-	3.50	-	-	-	-	-	-	2.98	-	-	-	-	2.92	-	-	-	-		
BF Discharge (cfs)		-	9.5	-	9	-	11	-	-	18	-	-	-	-	10.0	-	-	-	-	-	-	8.0	-	-	-	-	6.4	-	-	-	-		
Valley Length		-	-	-	194	-	-	-	-	-	-	-	-	-	248.0	-	-	-	-	-	-	248.0	-	-	-	-	248.0	-	-	-	-		
Channel length (ft) ²		-	-	-	209	-	-	-	-	134.5	-	-	-	-	333	-	-	-	-	-	-	310	-	-	-	-	310	-	-	-	-		
Sinuosity		-	-	-	1.08	-	-	-	-	1.05	-	-	-	-	1.34	-	-	-	-	-	-	1.2	-	-	-	-	1.2	-	-	-	-		
Water Surface Slope (Channel) (ft/ft)		-	-	-	0.01	-	0.17	-	-	0.0197	-	-	-	-	0.0070	0.02	0.0310	-	-	-	-	0.0101	0.0198	-	0.0295	-	-	0.0241	-	-	-		
BF slope (ft/ft)		-	-	-	0.024	-	-	-	-	-	-	-	-	-	0.0077	0.0175	-	-	-	-	-	0.0077	0.0175	-	0.0272	-	-	0.0203	-	-	-		
Bankfull Floodplain Area (acres)		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	5.2	-	-	-	-	5.2	-	-	-	-		
BEHI VL% / L% / M% / H% / VH% / E%		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-		
Channel Stability or Habitat Metric		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	
Biological or Other		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	

¹ Harman, W.A., G.D. Jennings, J.M. Patterson, D.R. Clinton, L.O. Slate, A.G. Jessup, J.R. Everhart and R.E. Smith. 1999. Bankfull hydraulic geometry relationships for North Carolina streams. Wetland Hydrology. AWRA Symposium Proceedings. D.S. Olsen and J.P. Potony, eds. American Water Resources Association. June 30-July 2, 1999. Bozeman, MT.
² Harman, W.A., D.E. Wise, M.A. Walker, R. Morris, M.A. Cantrell, M. Clemmons, G.D. Jennings, D.R. Clinton, J.M. Patterson. 2000. Bankfull Regional Curves for North Carolina Mountain Streams. In: AWRA Conference Proceedings, D.L. Kane, editor. American Water Resources Specialty Conference on Water Resources in Extreme Environments. Anchorage, Alaska.

Table 11. Morphology and Hydraulic Monitoring Summary
Upper Silver Creek Restoration Project: DMS Project ID No. 94645

Silver Creek (3,016 LF)																												
Dimension and substrate	Cross-section X-1, Station 2724.3 (Riffle)							Cross-section X-2, Station 2636.7 (Pool)							Cross-section X-3, Station 1898.2 (Pool)							Cross-section X-4, Station 1793.8 (Riffle)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Based on fixed baseline bankfull elevation																												
BF Width (ft)	29.1	24.6						35.7	29.5							43.5	39.5						23.8	23.5				
BF Mean Depth (ft)	1.7	1.8						1.6	1.8							1.7	1.5						2.0	1.9				
Width/Depth Ratio	17.2	13.9						21.8	16.8							25.2	27.3						11.8	12.4				
BF Cross-sectional Area (ft²)	49.2	43.4						58.3	51.9							74.9	57.3						48.0	44.2				
BF Max Depth (ft)	3.0	2.9						4.0	3.9							5.2	4.0						3.3	3.2				
Width of Floodprone Area (ft)	>300	>300						>300	>300							>300	90.6						>300	87.3				
Entrenchment Ratio	3.3	3.9						2.5	3.0							2.1	2.3						3.7	3.7				
Bank Height Ratio	1.1	1.0						1.0	1.0							0.7	0.7						1.0	1.0				
Wetted Perimeter (ft)	32.4	28.1						38.9	33.0							46.9	42.4						27.8	27.3				
Hydraulic Radius (ft)	1.5*	1.5						1.5*	1.6							1.6*	1.4						1.7*	1.6				
Fixed baseline bankfull elevation	1197.4	1197.4						1198.2	1198.2							1202.3	1202.3						1203.0	1203.0				
Based on current/developing bankfull feature																												
BF Width (ft)	29.1	26.2						35.7	29.5							43.5	42.55						23.8	23.5				
BF Mean Depth (ft)	1.7	1.7						1.6	1.8							1.7	1.45						2.0	1.9				
Width/Depth Ratio	17.2	15.2						21.8	16.8							25.2	29.31						11.8	12.4				
BF Cross-sectional Area (ft²)	49.2	45.1						58.3	51.9							74.9	61.8						48.0	44.2				
BF Max Depth (ft)	3.0	3.0						4.0	3.9							5.2	4.15						3.3	3.2				
Width of Floodprone Area (ft)	>300	>300						>300	>300							>300	>300						>300	87.3				
Entrenchment Ratio	3.3	3.7						2.5	3.0							2.1	2.1						3.7	3.7				
Bank Height Ratio	1.1	1.0						1.0	1.0							0.7	0.7						1.0	1.0				
Wetted Perimeter (ft)	32.4	29.7						38.9	33.0							46.9	45.5						27.8	27.3				
Hydraulic Radius (ft)	1.5	1.5						1.5	1.6							1.6	1.4						1.7	1.6				
Cross Sectional Area between end pins (ft²)	-	-						-	-							-	-						-	-				
d50 (mm)	-	-						-	-							-	-						36.6	41.3				
* Corrected from baseline report.																												
Dimension and substrate	Cross-section X-5, Station 1206.9 (Riffle)							Cross-section X-6, Station 357.2 (Pool)							Cross-section 7, Station 302.5 (Riffle)													
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Based on fixed baseline bankfull elevation																												
BF Width (ft)	28.4	26.1						43.5	41.9							26.6	25.9											
BF Mean Depth (ft)	1.7	1.7						1.8	1.8							2.1	2.0											
Width/Depth Ratio	17.3	15.7						23.6	23.9							13.0	13.3											
BF Cross-sectional Area (ft²)	46.9	43.4						80.1	73.5							54.5	50.6											
BF Max Depth (ft)	2.9	2.8						5.3	5.0							3.3	3.2											
Width of Floodprone Area (ft)	>300	>300						>300	>300							>300	>300											
Entrenchment Ratio	3.1	3.3						1.6	1.6							4.8	4.9											
Bank Height Ratio	1.0	1.0						1.0	0.9							1.0	1.0											
Wetted Perimeter (ft)	31.7	29.4						47.2	45.4							30.7	29.8											
Hydraulic Radius (ft)	2	2						1.7	1.7							1.8	1.7											
Fixed baseline bankfull elevation	1208.8	1208.8						1208.1	1208.1							1208.2	1208.2											
Based on current/developing bankfull feature																												
BF Width (ft)	28.4	26.1						43.5	41.9							26.6	25.9											
BF Mean Depth (ft)	1.7	1.7						1.8	1.8							2.1	2.0											
Width/Depth Ratio	17.3	15.7						23.6	23.9							13.0	13.3											
BF Cross-sectional Area (ft²)	46.9	43.4						80.1	73.5							54.5	50.6											
BF Max Depth (ft)	2.9	2.8						5.3	5.0							3.3	3.2											
Width of Floodprone Area (ft)	>300	>300						>300	>300							>300	>300											
Entrenchment Ratio	3.1	3.3						1.6	1.6							4.8	4.9											
Bank Height Ratio	1.0	1.0						1.0	0.9							1.0	1.0											
Wetted Perimeter (ft)	31.7	29.4						47.2	45.4							30.7	29.8											
Hydraulic Radius (ft)*	2	2						1.7	1.7							1.8	1.7											
Cross Sectional Area between end pins (ft²)	-	-						-	-							-	-											
d50 (mm)	-	-						-	-							33.4	15.2											

Table 11. Morphology and Hydraulic Monitoring Summary
Upper Silver Creek Restoration Project: DMS Project ID No. 94645

UT1 (495 LF)																												
Dimension and substrate	Cross-section X-13, Station 1+57 (Riffle)							Cross-section X-14, Station 3+28 (Pool)							Cross-section X-15, Station 2+15 (Pool)							Cross-section X-16, Station 2+53 (Riffle)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Based on fixed baseline bankfull elevation																												
BF Width (ft)	9.6	9.3						9.3	8.6																			
BF Mean Depth (ft)	0.9	0.8						2.0	1.3																			
Width/Depth Ratio	10.3	12.3						4.7	6.8																			
BF Cross-sectional Area (ft²)	8.9	7.0						18.5	10.9																			
BF Max Depth (ft)	1.3	1.1						3.7	2.5																			
Width of Floodprone Area (ft)	>150	>150						>150	>150																			
Entrenchment Ratio	5.3	5.4						8.7	9.4																			
Bank Height Ratio	1.0	1.1						1.1	1.2																			
Wetted Perimeter (ft)	11.5	10.8						13.3	11.1																			
Hydraulic Radius (ft)	0.8	0.6						1.4	1.0																			
Fixed baseline bankfull elevation	1204.0	1204.0						1201.6	1201.6																			
Based on current/developing bankfull feature																												
BF Width (ft)	9.6	9.8						9.3	10.96																			
BF Mean Depth (ft)	0.9	0.8						2.0	1.36																			
Width/Depth Ratio	10.3	12.0						4.7	8.03																			
BF Cross-sectional Area (ft²)	8.9	7.9						18.5	15																			
BF Max Depth (ft)	1.3	1.2						3.7	2.89																			
Width of Floodprone Area (ft)	>150	>150						>150	>150																			
Entrenchment Ratio	5.3	5.2						8.7	7.4																			
Bank Height Ratio	1.0	1.0						1.1	1																			
Wetted Perimeter (ft)	11.5	11.4						13.3	13.7																			
Hydraulic Radius (ft)	0.8	0.7						1.4	1.1																			
Cross Sectional Area between end pins (ft²)	-	-						-	-																			
d50 (mm)	38.8	43.6						-	-																			
UT2 (310 LF)																												
Dimension and substrate	Cross-section X-15, Station 2+15 (Pool)							Cross-section X-16, Station 2+53 (Riffle)							Cross-section X-17, Station 2+10 (Pool)							Cross-section X-18, Station 2+35 (Riffle)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Based on fixed baseline bankfull elevation																												
BF Width (ft)	7.3	6.4						6.6	5.8																			
BF Mean Depth (ft)	0.8	0.5						0.4	0.4																			
Width/Depth Ratio	8.9	13.9						16.0	15.7																			
BF Cross-sectional Area (ft²)	6.1	3.0						2.7	2.2																			
BF Max Depth (ft)	1.7	0.8						0.9	0.8																			
Width of Floodprone Area (ft)	>100	>100						>100	>100																			
Entrenchment Ratio	9.2	10.5						7.0	7.1																			
Bank Height Ratio	1.1	1.2						1.2	1.0																			
Wetted Perimeter (ft)	9.0	7.3						7.4	6.6																			
Hydraulic Radius (ft)	0.7	0.4						0.4	0.3																			
Fixed baseline bankfull elevation	1201.9	1201.9						1201.2	1201.2																			
Based on current/developing bankfull feature																												
BF Width (ft)	7.3	8.35						6.6	5.8																			
BF Mean Depth (ft)	0.8	0.46						0.4	0.4																			
Width/Depth Ratio	8.9	13.87						16.0	15.7																			
BF Cross-sectional Area (ft²)	6.1	4						2.7	2.2																			
BF Max Depth (ft)	1.7	0.98						0.9	0.8																			
Width of Floodprone Area (ft)	>100	>100						>100	>100																			
Entrenchment Ratio	9.2	8.1						7.0	7.1																			
Bank Height Ratio	1.1	1.1						1.2	1.0																			
Wetted Perimeter (ft)	9.0	9.3						7.4	6.6																			
Hydraulic Radius (ft)	0.7	0.4						0.4	0.3																			
Cross Sectional Area between end pins (ft²)	-	-						-	-																			
d50 (mm)	-	-						29.3	9.5																			

Table 11. Morphology and Hydraulic Monitoring Summary
Upper Silver Creek Restoration Project: DMS Project ID No. 94645

UT3 (L348 LF)																												
Dimension and substrate	Cross-section X-8, Station 5+29 (Riffle)							Cross-section X-9, Station 7+16 (Pool)							Cross-section X-10, Station 7+37 (Riffle)							Cross-section X-11, Station 10+55 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Based on fixed baseline bankfull elevation																												
BF Width (ft)	10.1	8.8					10.7	9.5						8.1	7.0						13.0	11.5						
BF Mean Depth (ft)	0.65	0.61					1.0	0.82						0.78	0.68						1.0	0.85						
Width/Depth Ratio	15.5	14.5					10.5	11.6						10.3	10.2						12.8	13.7						
BF Cross-sectional Area (ft ²)	6.5	5.3					10.9	7.8						6.3	4.8						13.2	9.7						
BF Max Depth (ft)	1.1	1.1					1.7	1.6						1.1	0.9						2.2	1.9						
Width of Floodprone Area (ft)	>150	>150					>150	>150						>150	>150						>150	>150						
Entrenchment Ratio	5.4	6.1					5.8	6.6						8.5	9.9						5.6	6.3						
Bank Height Ratio	1.0	1.1					1.0	1.2						1.1	1.2						1.0	1.1						
Wetted Perimeter (ft)	11.4	10.0					12.8	11.1						9.6	8.3						15.1	13.2						
Hydraulic Radius (ft)	0.6	0.5					0.9	0.7						0.7	0.6						0.9	0.7						
Fixed baseline bankfull elevation	1215.4	1215.4					1212.8	1212.8						1212.9	1212.9						1209.3	1209.3						
Based on current/developing bankfull feature																												
BF Width (ft)	10.1	11.68					10.7	12.1						8.1	7.47						13	13.02						
BF Mean Depth (ft)	0.65	0.53					1.0	0.87						0.78	0.76						1.0	0.92						
Width/Depth Ratio	15.5	22.03					10.5	13.84						10.3	9.83						12.8	14.21						
BF Cross-sectional Area (ft ²)	6.5	6.2					10.9	10.6						6.3	5.7						13.2	11.9						
BF Max Depth (ft)	1.1	1.14					1.7	1.86						1.1	1.1						2.2	2.06						
Width of Floodprone Area (ft)	>150	>150					>150	>150						>150	>150						>150	>150						
Entrenchment Ratio	5.4	4.6					5.8	5.2						8.5	9.2						5.6	5.6						
Bank Height Ratio	1.0	1					1.0	1						1.1	1.1						1.0	1.0						
Wetted Perimeter (ft)	11.4	12.7					12.7	13.8						9.7	9.0						15.0	14.9						
Hydraulic Radius (ft)	0.6	0.5					0.9	0.8						0.7	0.6						0.9	0.8						
Cross Sectional Area between end pins (ft ²)	-	-					-	-						-	-						-	-						
d50 (mm)	31.2	20.4					-	-						-	-						-	-						
Based on current/developing bankfull feature																												
BF Width (ft)	8.2	7.8																										
BF Mean Depth (ft)	0.9	0.7																										
Width/Depth Ratio	9.1	10.6																										
BF Cross-sectional Area (ft ²)	7.3	5.8																										
BF Max Depth (ft)	1.4	1.1																										
Width of Floodprone Area (ft)	>150	>150																										
Entrenchment Ratio	9.4	7.0																										
Bank Height Ratio	1.2	1.3																										
Wetted Perimeter (ft)	10.0	9.3																										
Hydraulic Radius (ft)	0.7	0.6																										
Fixed baseline bankfull elevation	1208.8	1208.8																										
Based on current/developing bankfull feature																												
BF Width (ft)	8.2	9.13																										
BF Mean Depth (ft)	0.9	0.87																										
Width/Depth Ratio	9.1	10.45																										
BF Cross-sectional Area (ft ²)	7.3	8																										
BF Max Depth (ft)	1.4	1.34																										
Width of Floodprone Area (ft)	>150	>150																										
Entrenchment Ratio	9.4	8.5																										
Bank Height Ratio	1.2	1																										
Wetted Perimeter (ft)	10.0	10.9																										
Hydraulic Radius (ft)	0.7	0.7																										
Cross Sectional Area between end pins (ft ²)	-	-																										
d50 (mm)	-	-																										

Appendix E

Wetland Assessment Data

Includes:

Figure 8. Observed Rainfall vs. Historical Average


Figure 9. Wetland Gauge Graphs

Table 12. Wetland Gauge Attainment data

Table 12a. Wetland Area Well Success


Figure 10. Wetland Photo Log

Figure 8. Observed Rainfall at four nearby recording stations and historic average at the Casar (311538) station near the U. Silver Creek Project, with 30th and 70th percentiles of monthly averages from 1958 to 2012.

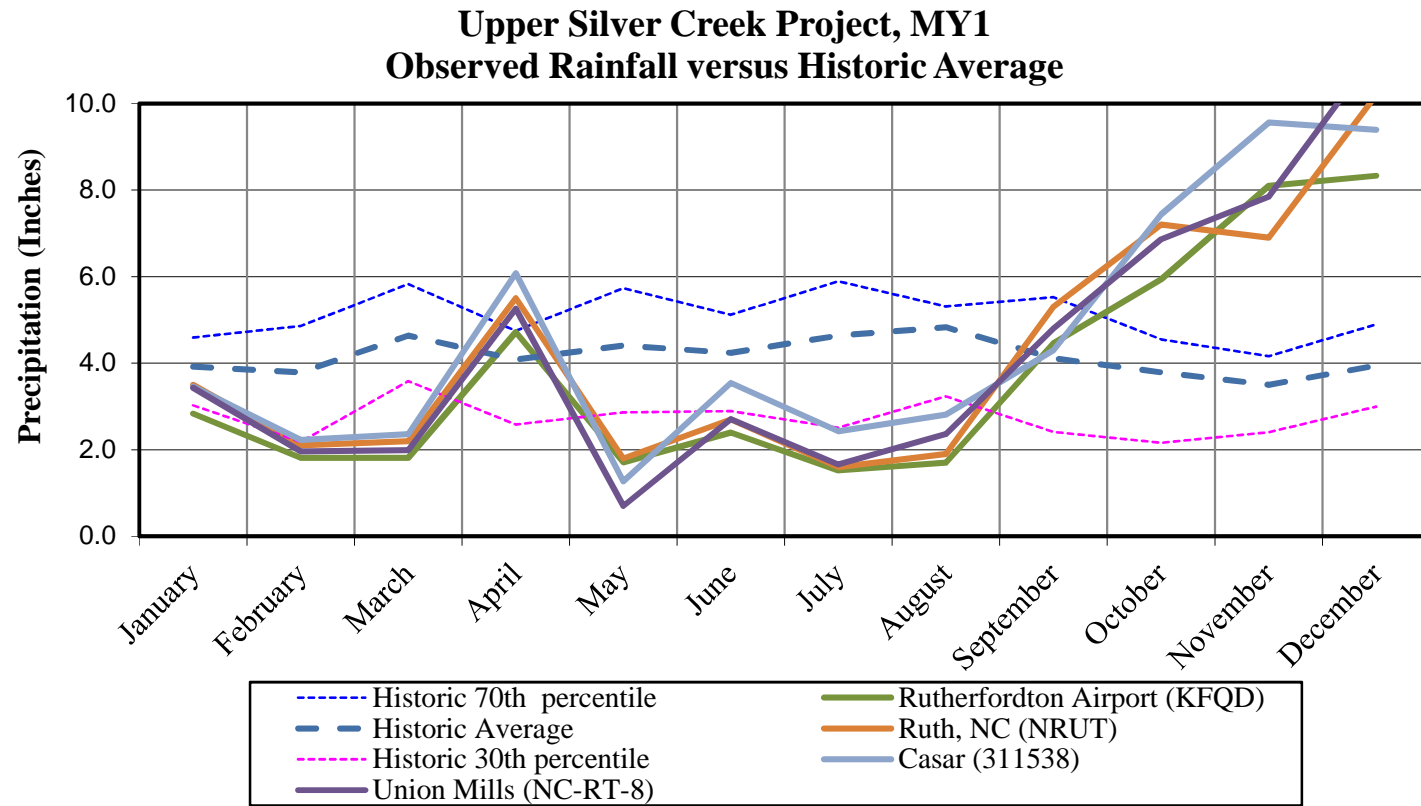


Rainfall data source for KGQD: <http://climate.ncsu.edu/cronos?station=KFQD&temporal=monthly>
 Rainfall data source for NRUT: <http://climate.ncsu.edu/cronos?station=NRUT&temporal=monthly>
 Rainfall data source for NC-RT-8: <http://climate.ncsu.edu/cronos/?station=NC-RT-8&temporal=monthly>
 Rainfall data source for 311538: <http://climate.ncsu.edu/cronos/?station=311538&temporal=monthly>

Figure 9. Wetland gauge graphs for each well, showing depth to groundwater and rainfall during MY1.

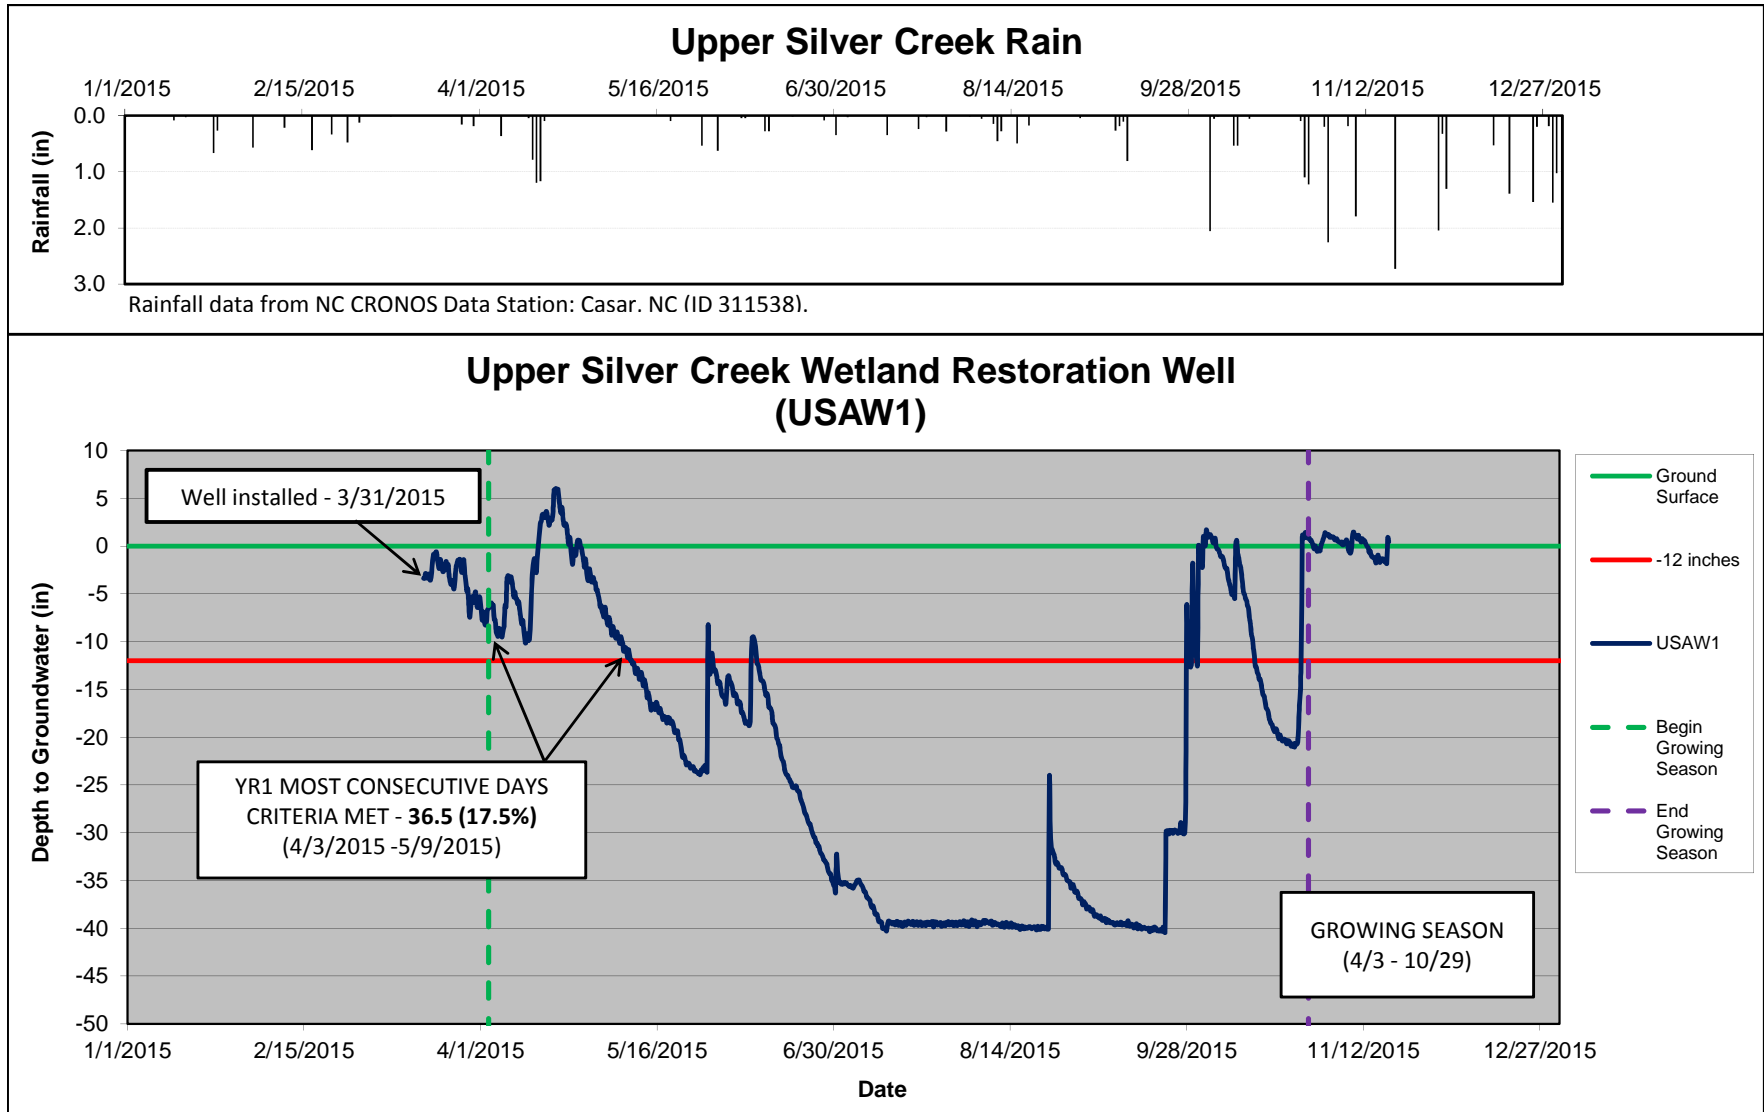


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW2)

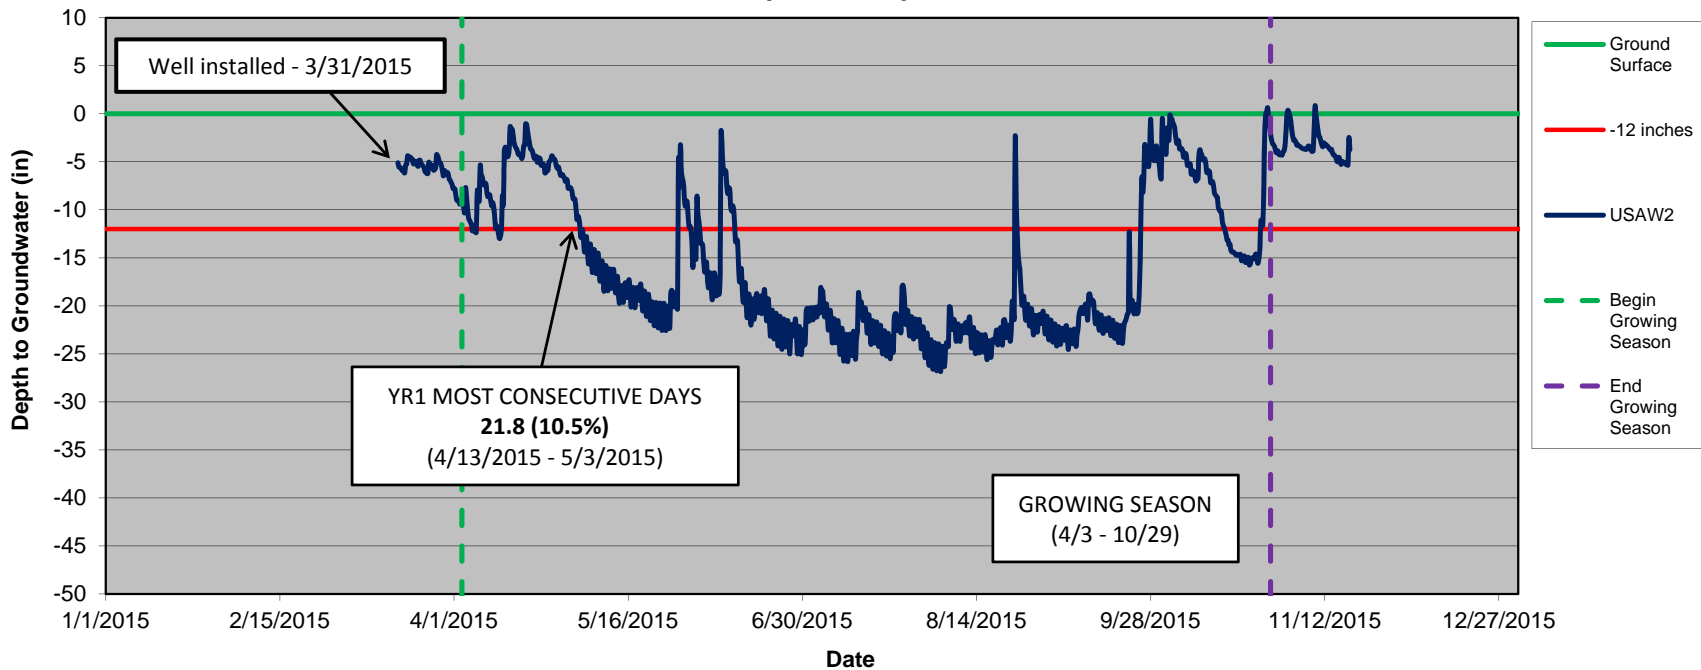


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW3)

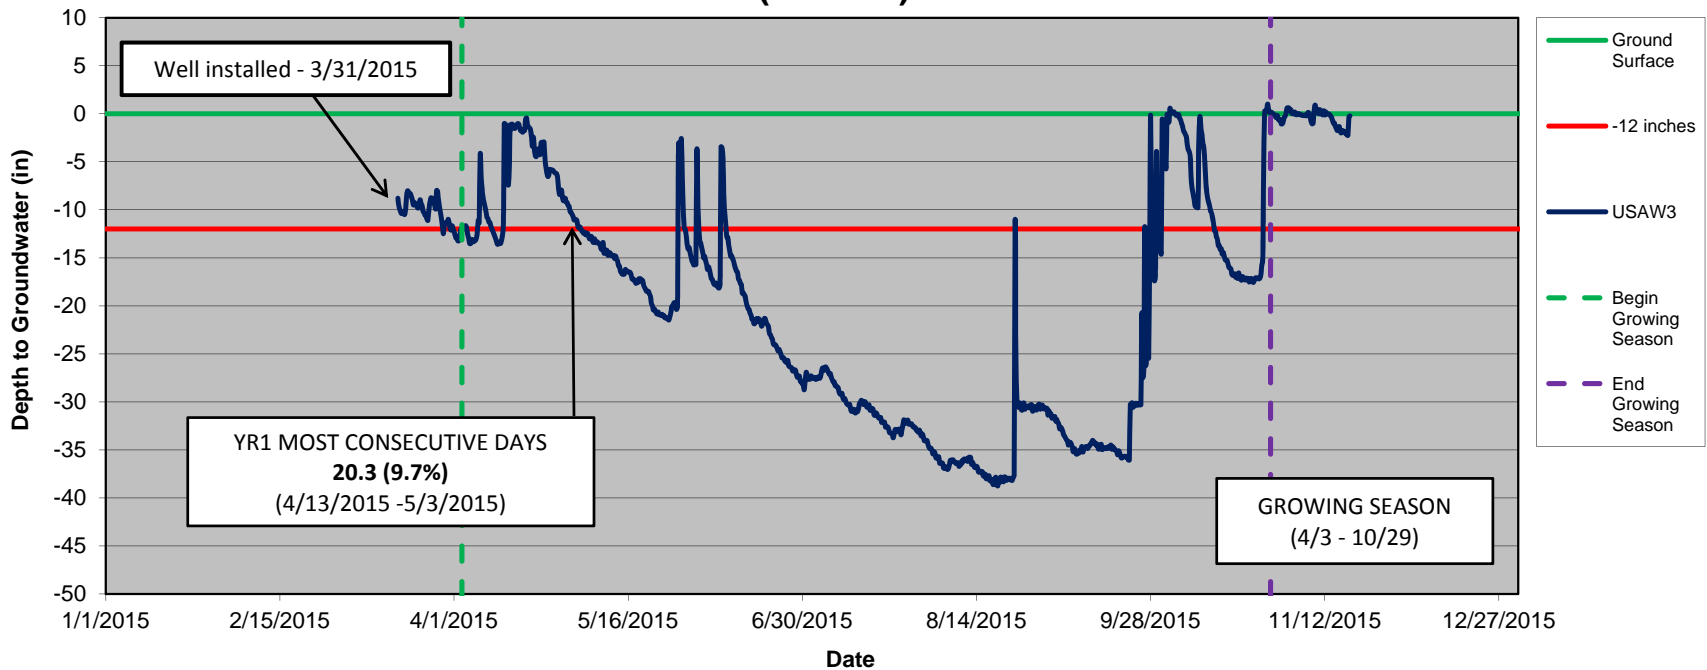


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW4)

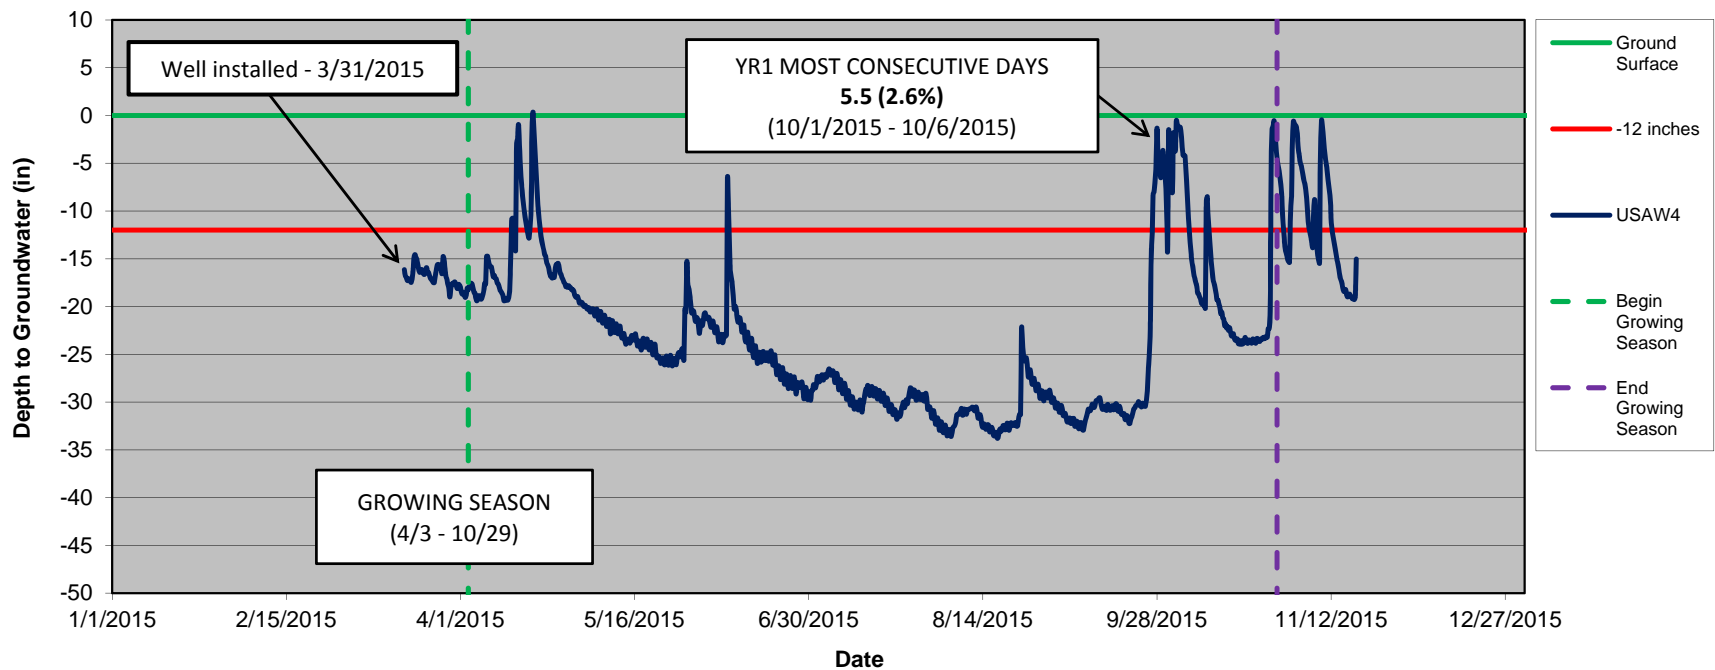


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW5)

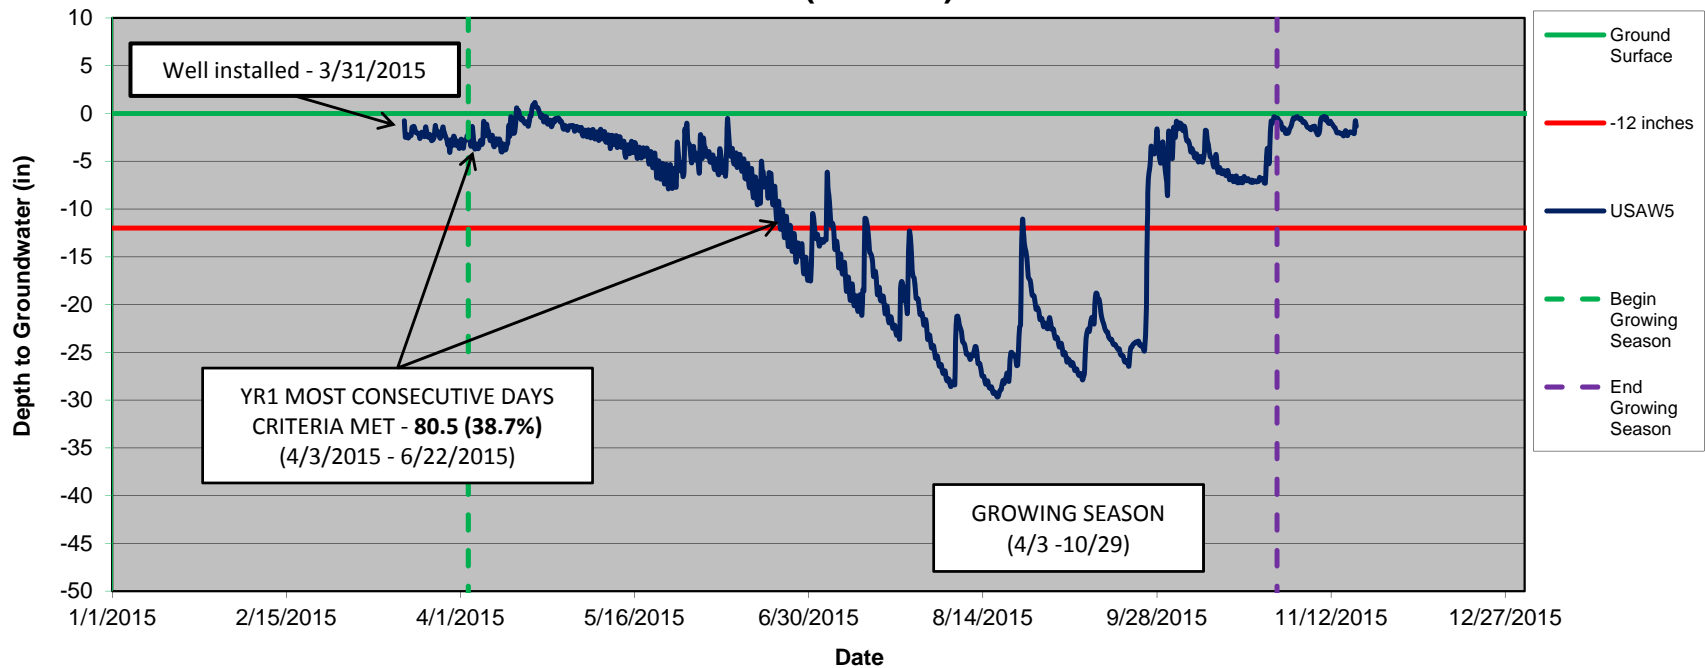


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).


Upper Silver Creek Wetland Restoration Well (USAW6)

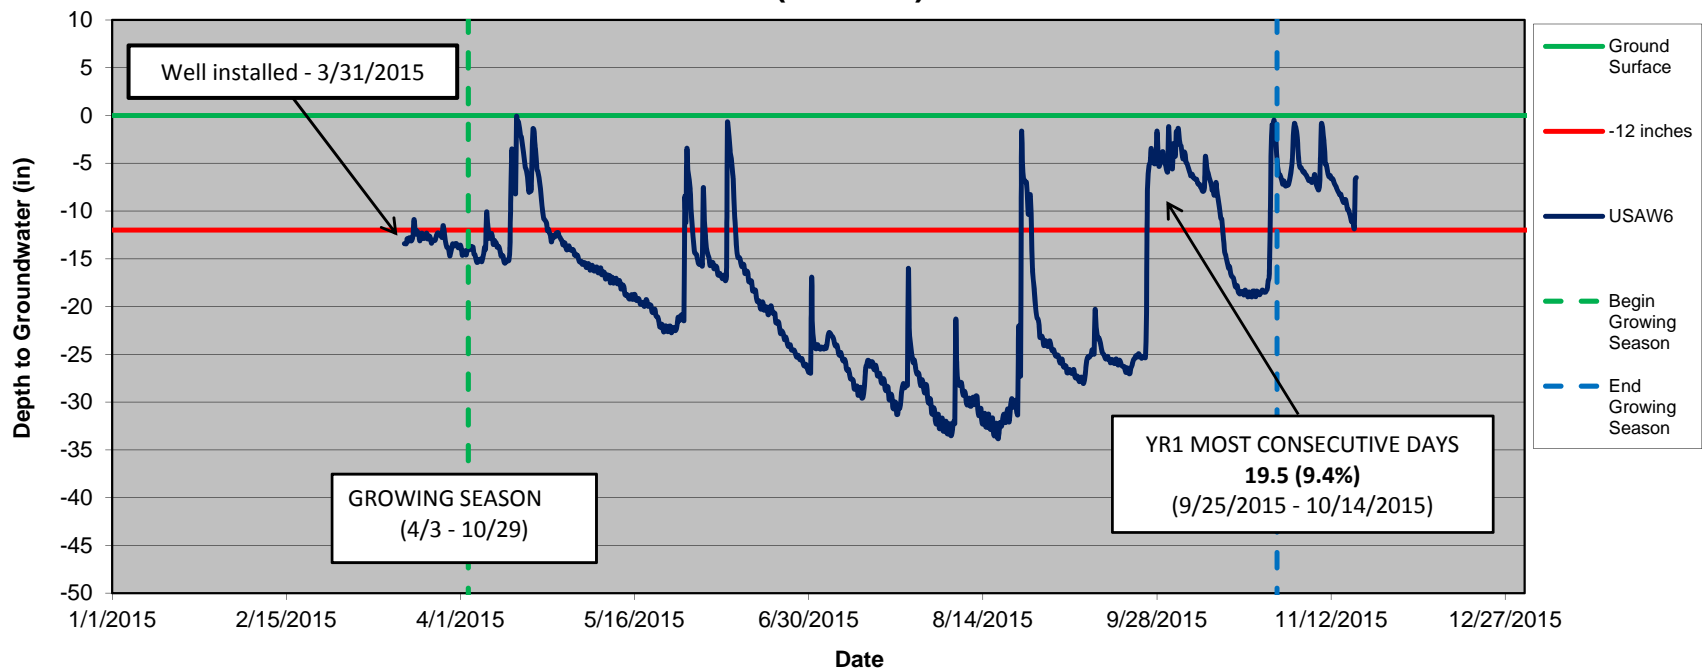


Upper Silver Creek Rain



Upper Silver Creek Wetland Restoration Well (USAW7)

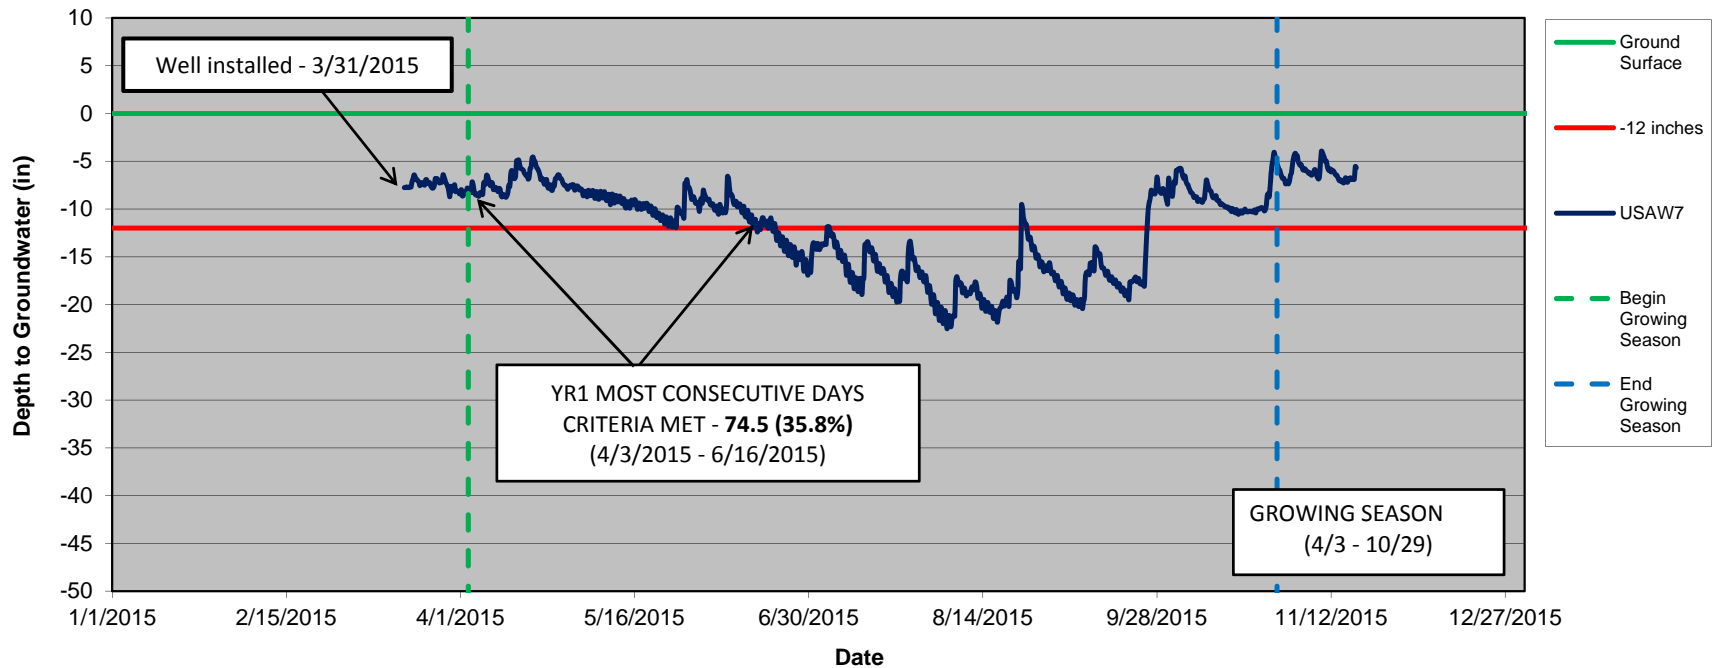


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW8)

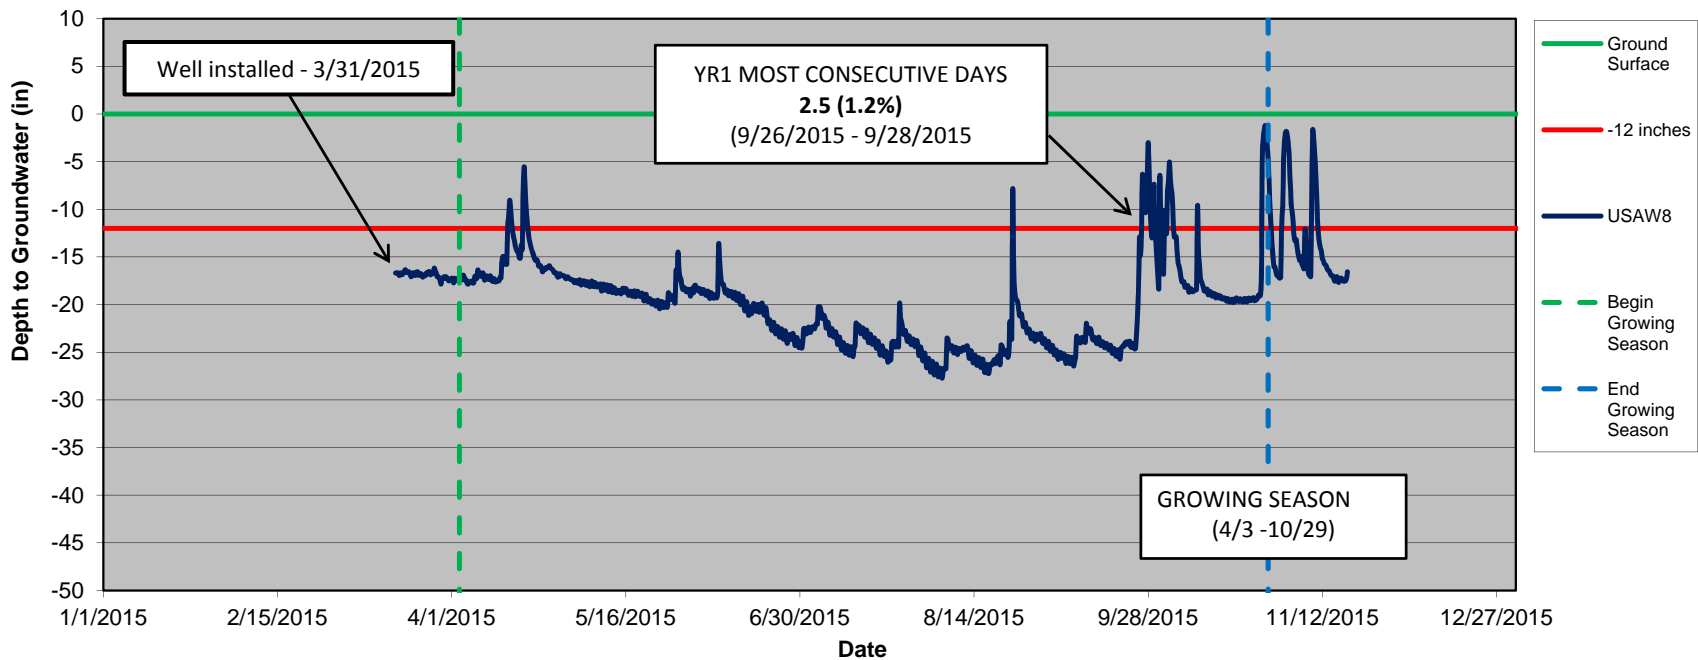


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar. NC (ID 311538).


Upper Silver Creek Wetland Restoration Well (USAW9)

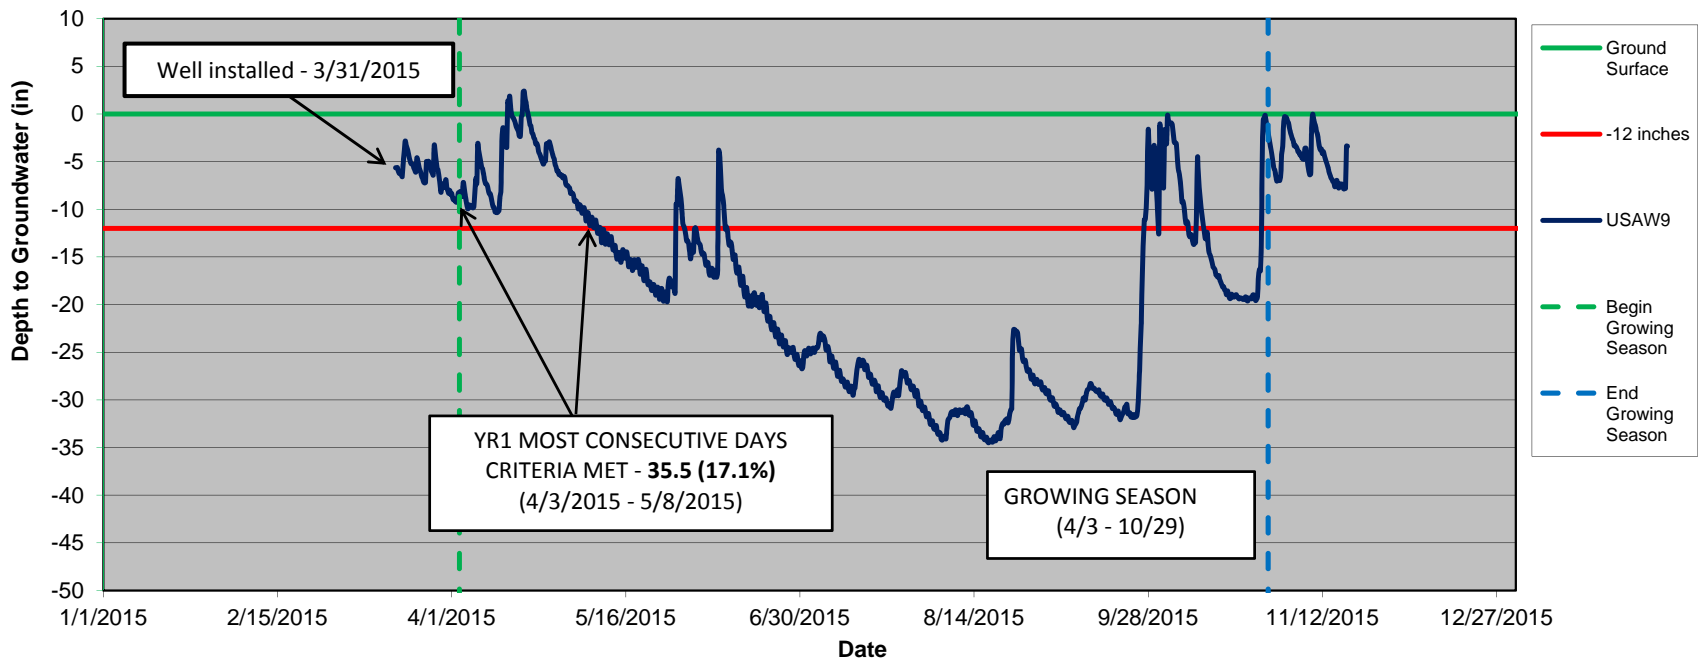


Upper Silver Creek Rain



Upper Silver Creek Wetland Restoration Well (USAW10)

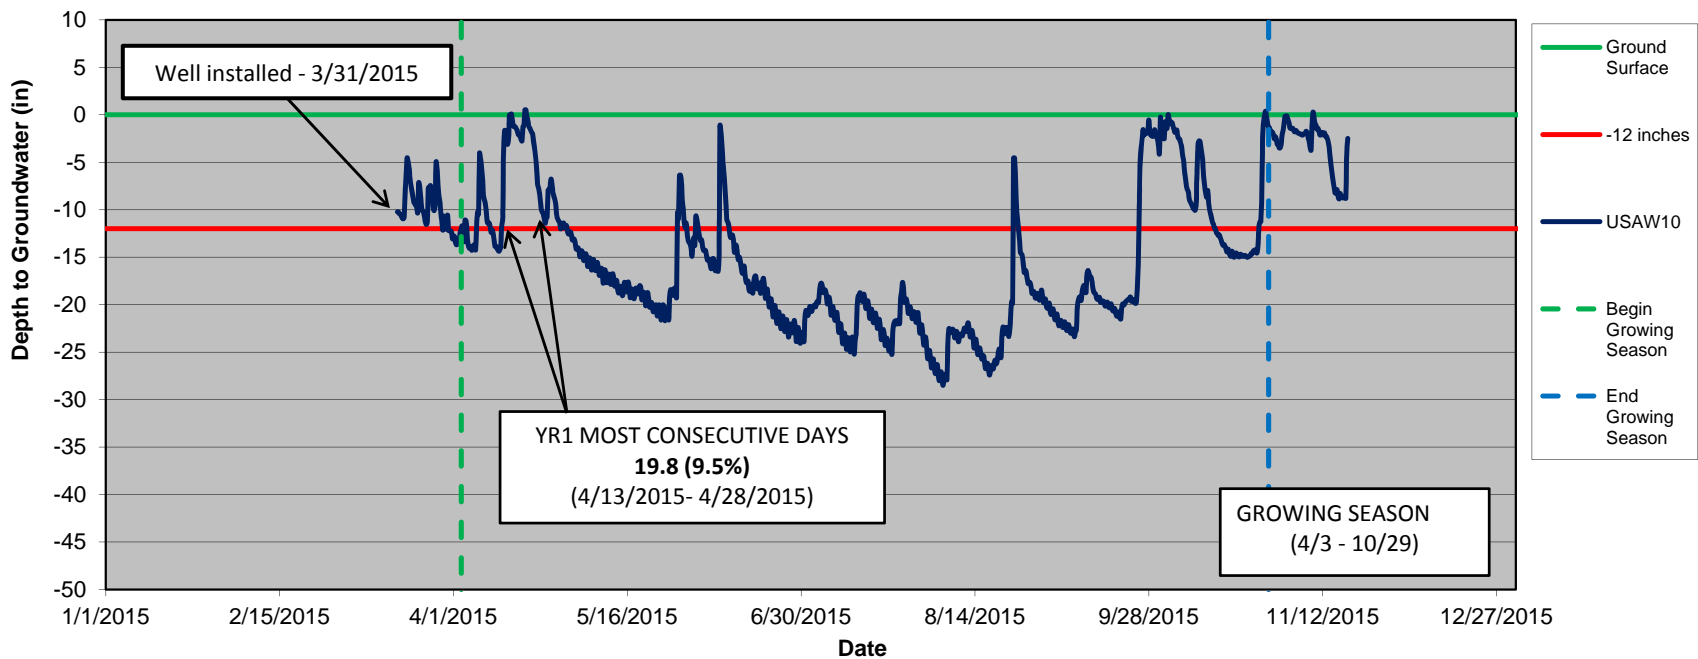


Upper Silver Creek Rain




Rainfall data from NC CRONOS Data Station: Casar, NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW11)



Upper Silver Creek Rain



Rainfall data from NC CRONOS Data Station: Casar, NC (ID 311538).

Upper Silver Creek Wetland Restoration Well (USAW12)

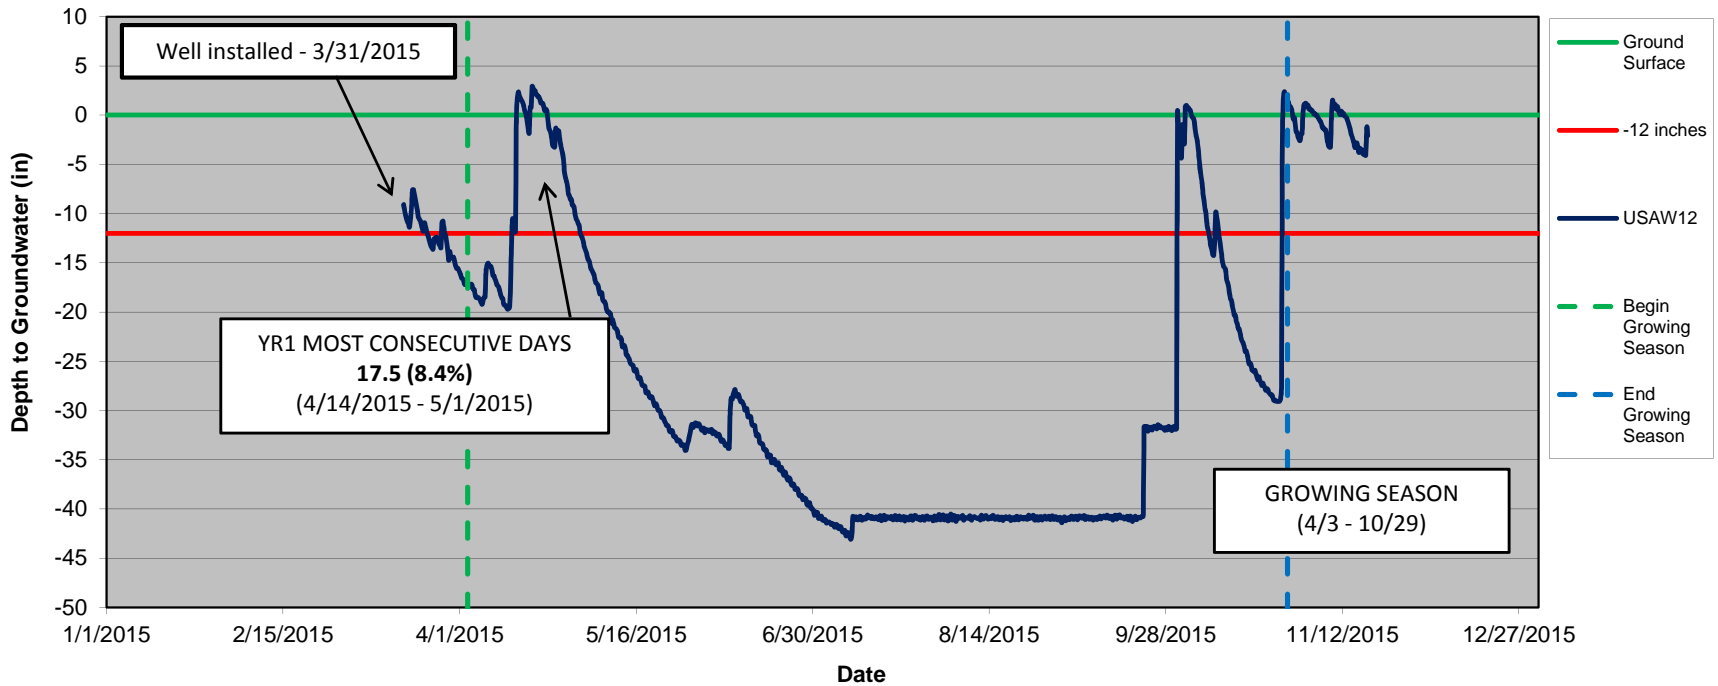


Table 12. Wetland gauge attainment data, summary of groundwater gauge results for MY 1 through 5 at the U. Silver Creek Project Site, DMS Project #94645.

Gauge	Success Criteria Achieved/Max Consecutive Days During Growing Season (Percentage)				
	Monitoring Year 1 (2015)	Monitoring Year 2 (2016)	Monitoring Year 3 (2017)	Monitoring Year 4 (2018)	Monitoring Year 5 (2019)
USAW1	Yes/36.5 days (17.5 %)				
USAW2	No/21.8 days (10.5 %)				
USAW3	No/20.3 days (9.7 %)				
USAW4	No/5.5 days (2.6 %)				
USAW5	Yes/80.5 days (38.7 %)				
USAW6	No/19.5 days (9.4 %)				
USAW7	Yes/74.5 days (35.8 %)				
USAW8	No/2.5 days (1.2 %)				
USAW9	Yes/35.5 days (17.1 %)				
USAW10	No/19.8 days (9.5 %)				
USAW11	No/18.5 days (8.9 %)				
USAW12	No/17.5 days (8.4 %)				

Table 12. Wetland Restoration Area Well Success
Upper Silver Creek Restoration Project: Project ID No. 94645

Well ID	Percentage of Consecutive Days <12 inches from Ground Surface ¹	Most Consecutive Days Meeting Criteria ²	Percentage of Cumulative Days <12 inches from Ground Surface ¹	Cumulative Days Meeting Criteria ³	Number of Instances where Water Table is 12 inches from Ground Surface ⁴
Cross-sectional Well Arrays					
USAW1	17.5	36.5	27.9	58.0	8
USAW2	10.5	21.8	29.9	62.3	10
USAW3	9.7	20.3	22.6	47.0	7
USAW4	2.6	5.5	9.3	19.3	5
USAW5	38.7	80.5	57.7	120.0	9
USAW6	9.4	19.5	19.4	40.3	9
USAW7	35.8	74.5	55.3	115.0	8
USAW8	1.2	2.5	5.4	11.3	10
USAW9	17.1	35.5	27.0	56.3	10
USAW10	9.5	19.8	24.9	51.8	11
USAW11	8.9	18.5	20.4	42.5	7
USAW12	8.4	17.5	13.8	28.8	4

Notes:

¹Indicates the percentage of most consecutive number of days within the monitored growing season with water table 12 inches or less from the soil surface.

²Indicates the most consecutive number of days within the monitored growing season with a water table 12 inches or less from the soil surface.

³Indicates the cumulative number of days within the monitored growing season with a water table 12 inches or less from the soil surface.

⁴Indicates the number of instances within the monitored growing season when the water table rose to 12 inches or less from the soil surface.

Growing season for Burke County is from April 3 to October 29 and is 208 days long.

Growing season percentage for success is 12% of 208 days = 25 days; where water table is 12 inches or less from the ground surface

HIGHLIGHTED indicates wells that *did not* meet the success criteria for the most consecutive number of days within the monitored growing season with a water 12 inches or less from the soil surface. Following Year 1 wetland monitoring, eight of twelve wells did not exhibit a hydroperiod of 12% or greater during the growing season. These wells will be observed closely throughout monitoring Year 2.

All In-Situ groundwater monitoring dataloggers were installed on 3/17/2015. Installation of the dataloggers was completed following construction in spring 2015 when groundwater levels are normally closer to the ground surface.

**Figure 10. Upper Silver Creek Wetland Photos
Monitoring Year 1 (2015)**



Photo 1. Wetland Photo Point – W1, replicates photo 50 in Baseline Report (taken March 2016).



Photo 2. Wetland Photo Point – W2, replicates photo 51 in Baseline Report (taken March 2016).



Photo 3. Wetland Photo Point – W3 replicates photo 52 in Baseline Report (taken March 2016).



Photo 4. Wetland Photo Point – W4, replicates photo 53 in Baseline Report (taken March 2016).



Photo 5. Wetland Photo Point – W5, replicates photo 54 in Baseline Report (taken March 2016).



Photo 6. Wetland Photo Point – W6, replicates photo 55 in Baseline Report (taken March 2016).



Photo 7. Wetland Photo Point – W7, replicates photo 56 in Baseline Report (taken March 2016).



Photo 8. Wetland Photo Point – W8, replicates photo 57 in Baseline Report (taken March 2016).



Photo 9. Wetland Photo Point – W9, replicates photo 58 in Baseline Report (taken March 2016).



Photo 10. Wetland Photo Point – W10, replicates photo 59 in Baseline Report (taken March 2016).

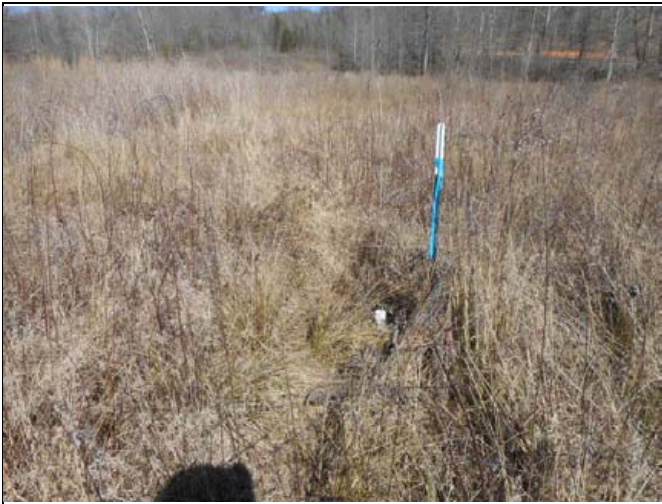


Photo 11. Wetland Photo Point – W11, replicates photo 60 in Baseline Report (taken March 2016).



Photo 12. Wetland Photo Point – W12, replicates photo 61 in Baseline Report (taken March 2016).



Photo 13. Wetland Photo Point – W13 added between time of baseline and MY1 survey, (April 1, 2015)



Photo 14. Wetland Photo Point – downstream of deer-stand. Replicates photo 62 in Baseline Report (taken March 2016).



Photo 15. Wetland Photo Point – upstream of deer-stand. Replicates photo 63 in Baseline Report (taken March 2016).



Photo 16. Wetland Photo Point – left bank cross-section 7 pin to veg plot 5. Replicates photo 64 in Baseline Report (taken March 2016).



Photo 17. Wetland Photo Point – left bank cross-section 7 pin to veg plot 4. Replicates photo 65 in Baseline Report (taken March 2016).



Photo 18. Wetland Photo Point upstream of well 2 toward vegetation plot 3. Replicates photo 66 in Baseline Report (taken March 2016).



Photo 19. Wetland Photo Point – up valley from left bank at station 22+00. Replicates photo 67 in Baseline Report (taken March 2016).
