

## **YEAR 2 MONITORING REPORT**

### **UT MILLERS CREEK**

Duplin County, North Carolina

DMS Project ID No. 95719, Contract No. 5000, USACE Action ID No. SAW-2013-00386

DWR Project No. 13-0187



Prepared for:

### **NCDEQ Division of Mitigation Services (DMS)**

217 West Jones St., Suite 3000A

Raleigh, North Carolina 27603

Construction Completed: February 2015

Morphology Data Collected: April 26, 2016

Vegetation Data Collected: October 10, 2016

Submitted: February 2017

Prepared by:



**ICA Engineering, Inc.**  
**5121 Kingdom Way, Suite 100**  
**Raleigh, North Carolina 27607**  
919.851.6066  
919.851.6846 (fax)

I HEREBY CERTIFY THAT THE DOCUMENT CONTAINED HEREIN, UT MILLERS CREEK YEAR 2 MONITORING REPORT WAS PREPARED BY ME OR UNDER MY DIRECT SUPERVISION.

SIGNED SEALED, AND DATED THIS 1<sup>ST</sup> DAY OF FEBRUARY 2017.



A handwritten signature in blue ink, appearing to read 'Chris L. Smith', written over a horizontal line.

Chris L. Smith, PE

## TABLE OF CONTENTS

<b><u>SECTION</u></b>	<b><u>PAGE</u></b>
<b>1.0 PROJECT SUMMARY</b> .....	<b>2</b>
1.1 GOALS AND OBJECTIVES .....	2
1.2 SUCCESS CRITERIA.....	3
1.3 BACKGROUND SUMMARY .....	3
1.4 VEGETATION .....	3
1.5 STREAM STABILITY .....	3
1.6 WETLANDS.....	4
<b>2.0 METHODOLOGY</b> .....	<b>5</b>
<b>3.0 REFERENCES</b> .....	<b>5</b>
APPENDIX A. PROJECT VICINITY MAP AND BACKGROUND TABLES.....	7
APPENDIX B. VISUAL ASSESSMENT DATA .....	13
APPENDIX C. VEGETATION PLOT DATA .....	27
APPENDIX D. STREAM SURVEY DATA.....	28
APPENDIX E. HYDROLOGIC DATA.....	42

## LIST OF FIGURES

<b><u>FIGURE</u></b>	<b><u>PAGE</u></b>
Figure 1. Vicinity Map .....	8
Figure 2.0 – 2.6. Current Condition Plan View (Sheets 1-7).....	14
Figures 3.1 - 3.14. Vegetation Plot Photos and Problem Areas.....	23
Figures 4.1 – 4.10. Cross Section Plots.....	29
Figures 5.1 - 5.4 Crest Gauge Photos .....	42
Figure 6.0. Monthly Precipitation.....	45
Figure 6.1 - 6.8. Wetland Gauges.....	46

## LIST OF TABLES

<b><u>TABLE</u></b>	<b><u>PAGE</u></b>
Table 1. Project Components and Mitigation Credits.....	9
Table 2. Project Activity and Reporting History.....	10
Table 3. Project Contacts Table .....	11
Table 4. Project Information .....	12
Table 5. Visual Stream Morphology Stability Assessment.....	21
Table 6. Vegetation Condition Assessment.....	22
Table 7. Vegetation Plot Mitigation Success Summary .....	27
Table 8. Baseline Stream Data Summary.....	39
Table 9. Monitoring Data - Dimensional Morphology Summary.....	40
Table 10. Monitoring Data - Stream Reach Data Summary.....	41
Table 11. Verification of Bankfull Events.....	42
Table 12. Summary of Gauge Hydrologic Data .....	44

## 1.0 PROJECT SUMMARY

The following report summarizes the vegetation establishment, stream stability, and wetland hydrology for Year 2 monitoring for the UT Millers Creek Site (hereafter referred to as the “Site”) in Duplin County, North Carolina.

### 1.1 Goals and Objectives

The primary goals of the UT Millers Creek stream and wetland mitigation project focus on:

- Reducing stressors to water quality
- Providing and enhancing flood attenuation
- Restoring and enhancing aquatic, semi-aquatic and riparian habitat, and
- Restoring and enhancing habitat connectivity with adjacent natural habitats.

The following objectives accomplish the goals listed above:

1. Removing stressors to water quality and increasing attenuation is directly tied to:
  - a. Restoration of the formerly deeply incised and entrenched UT as a Priority I (PI) restoration where bankfull and larger flows access the historic floodplain allowing nutrients, sedimentation, trash and debris from upstream urban runoff to settle from floodwaters.
  - b. Restoration of the UT as PI restoration allows the Site to mitigate flood flows by reconnecting bankfull and higher flows to its historic floodplain.
  - c. Restoration of the riparian buffers and wetlands adjacent to the UT (i.e. restoration of an existing pond and ditch back to riparian wetlands) allows floodwaters to attenuate, in turn reducing stressors from upstream impacts.
  - d. Restoration of wetland hydrology within the riparian buffer supports hydrophytic vegetation, which assists in the uptake, storage and fixation of nutrients and sedimentation from overbank flows. Adjacent low quality pine plantations were removed and planted with native hydrophytic vegetation.
2. Restoring and enhancing aquatic, semi-aquatic and terrestrial habitat is directly tied to:
  - a. Introduction of woody materials such as planted vegetation, log sills, soil lifts and toe wood to the restored channel. Woody materials will promote shading, bed form diversity and foraging opportunities for aquatic organisms, benthic macroinvertebrates, and fish.
  - b. Restoration of native vegetation to the stream channel banks and the adjacent riparian corridor has diversified flora and provides an abundance of available foraging and cover habitat for amphibians, reptiles, mammals and birds.
  - c. Restoration of wetland hydrology and introducing floodwaters back to the historic floodplain provides a diversity of habitats for semi-aquatic flora and fauna that may have not been seen on the Site since before anthropogenic disturbances.
3. Habitat restoration and connectivity can be directly tied to:
  - a. The removal of existing pine plantations and replanting of native vegetation.
  - b. The restored community ensures a protected habitat corridor between the Site and the downstream mature riparian buffers and upland habitats.



## 1.2 Success Criteria

Monitoring of restoration efforts will be performed until success criteria are fulfilled. Monitoring includes stream channel/hydraulics, wetland hydrology, and vegetation. In general, the restoration success criteria, and required remediation actions, are based on the Stream Mitigation Guidelines (USACE et al. 2003) and the Ecosystem Enhancement Program Monitoring Requirements and Performance Standards for stream and/or Wetland Mitigation (NCEEP 2011). Project success criteria are further detailed in the Baseline Monitoring Document & As-Built Baseline Report (ICA 2015).

## 1.3 Background Summary

The North Carolina Department of Environmental and Natural Resources Department of Mitigation Services (DMS) contracted ICA Engineering, Inc. (ICA) to restore 2,625 linear feet of the Unnamed Tributary to Millers Creek (UT) and 4.5 acres of riparian wetlands within the Site to assist in fulfilling stream mitigation goals in the watershed (Table 1 and Table 4). The Site is located approximately one-half (0.5) mile west of Magnolia in Duplin County, North Carolina and contains an unnamed tributary to Millers Creek and associated restored riparian wetlands (Figure 1). The Site is located within DMS Targeted Local Watershed Catalogue Unit (CU) 03030006. The Site is comprised of one property owned by William Jeffrey Hatcher and wife Susan King Hatcher (PIN # 247100987405). Additional information concerning project history is presented in Table 2.

## 1.4 Vegetation

Vegetation is meeting success criteria across the site following the second year of monitoring. Overall, the site is averaging 714 planted stems per acre; easily exceeding the success criteria of 320 stems per acre after Year 3 Monitoring. Additionally, all plots are individually exceeding success criteria by well over 10%.

A small amount of morning glory (*Ipomoea sp.*) was noted within Plot 1, however the cover totaled less than 5% of the plot. It is not expected that morning glory will lead to reduced survival rates on-site; however, HDR|ICA will continue to monitor the status of this species.

Four bare areas and two areas of thin grass are present on-site. The total acreage of bare areas is 0.23 (1.9% of planted acreage) and the total acreage of thin grass is 0.24 (2% of planted acreage). These areas have decreased slightly over the monitoring year but additional seeding may be required.

## 1.5 Stream Stability

UT Millers Creek appears to be stable and functioning as designed. Cross section data shows that riffle sections have maintained bankfull cross sectional area as well as width/depth ratio over the course of the monitoring period. Additionally, the stream pattern has not changed over the monitoring year. The gullies noted at and below STA 33+00 are still present; however, it is apparent that the areas are not actively eroding and vegetation is beginning to fill in on the banks. To further stabilize the area, ICA|HDR anticipates flattening the gullies using hand rakes and planting juncus in the disturbed areas.

Tag alder species planted as live stakes in the banks are surviving well and average approximately 3 feet tall. It is expected that the stream will remain in a stable condition as vegetation continues to mature.

The site has experienced several bankfull flows throughout the monitoring period. Crest gauges were inspected on-site following the Hurricane Matthew rain event and showed that the site experienced a bankfull flow during the event. Additional bankfull event documentation can be found in Appendix E.

Bank pins were inspected on-site and showed no signs of bank erosion over the course of the monitoring period.

### 1.6 Wetlands

Based upon the Final Mitigation Plan, the hydrologic criteria for restored wetlands at the Site are as follows (based upon the corresponding landscape position and wetland community type):

- a. For the **riparian bottomland hardwood forest community**, the hydrologic criterion will be the establishment of a static water table at, or within, 12 inches of the soil surface for a minimum of 12.5 percent of the growing season, equivalent to 38 days based upon hydrologic monitoring undertaken from Feb 1st through Nov 30th of each monitoring year.
- b. For the **headwater riparian community (zero-order geomorphic position)**, the hydrologic criterion will be the establishment of a static water table at, or within, 12 inches of the soil surface for a minimum of 10 percent of the growing season, equivalent to 30 days based upon hydrologic monitoring undertaken from Feb 1st through Nov 30th of each monitoring year.

The UT Millers site exhibits a range of hydrologic conditions characteristic of small stream swamp wetland community types of the inner Coastal Plain of North Carolina. Several of the groundwater gauges documented elevated groundwater levels at or near the soil surface for extended periods of time during the growing season. In addition, portions of the site exhibited intermittent to prolonged periods of surface inundation. Hurricane Matthew generated abnormally wet conditions during the month of October, otherwise groundwater conditions were normal for the majority of the growing season. Refer to the attached gauge hydrographs depicting recorded groundwater and surface water levels from February 1 through November 30.

All of the groundwater gauges located on the mitigation site exhibit hydrology indicative of jurisdictional wetlands (i.e. hydroperiods greater than 5% of the growing season), and all gauges exceeded the minimum success criteria as outlined above. While the specific durations of wetland hydrology at each gauge varied across the site, each gauge also displayed prolonged wetland hydroperiods during normal rainfall conditions. In addition, on-site restoration gauges generally exhibited similar hydroperiods as the off-site reference gauges.

The summary of hydroperiods for each gauge is presented in Table 12 and gauge locations are depicted in Figure 2.0 – 2.6.

## 2.0 METHODOLOGY

Year 2 monitoring surveys were completed using a Total Station. Each cross section was marked with a rebar monument at their beginning and ending points. The rebar has been located vertically and horizontally in NAD 83-State Plane. Surveying these monuments throughout the Site ensured proper orientation. The survey data was imported into MicroStation for verification. RIVERMorph and the Ohio Department of Natural Resources' "The Reference Reach Spreadsheet Version 4.3L" were used to analyze cross section data (Mecklenburg 2006). Tables and figures were created using Microsoft Excel. The channel is entirely a sand bed system; therefore, a pebble count was not conducted. Bank pins were not observed and therefore were not surveyed.

Vegetation monitoring was completed using CVS level II methods, for nine, 100 square meter vegetation plots (Lee et al. 2006). The taxonomic standard for vegetation used for this document was Flora of the Southern and Mid-Atlantic States (Weakley 2011).

Groundwater hydrology was monitored using six automated gauges (RDS, Inc. WM-20s) located within the riparian wetland restoration areas. Two reference gauges were installed; one in a Headwater Riparian Wetland and one in a Bottomland Hardwood Wetland. Gauges were installed in accordance with installation methods outlined in the Wetlands Regulatory Assistance Program (WRAP) Technical Note 00-02 (Sprecher, 2000). Water levels were recorded once daily and the data was downloaded every two months.

## 3.0 REFERENCES

ICA Engineering, Inc. As-Built Monitoring Document & As-Built Baseline Report for UT Millers Creek Full Delivery Site. 2015.

Lee, Michael T., R. K. Peet, S. D. Roberts, and T. R. Wentworth. 2006. CVS-EEP Protocol for Recording Vegetation, Version 4.0 (<http://cvs.bio.unc.edu/methods.htm>).

Mecklenburg, Dan. 2006. The Reference Reach Spreadsheet Version 4.3L. 2006. Ohio Department of Natural Resources. Division of Soil and Water. (<http://www.dnr.state.oh.us/tabid/9188/default.aspx>)

NCEEP. Ecosystem Enhancement Program Monitoring Requirements and Performance Standards for stream and/or Wetland Mitigation. 2011.

Sprecher, S. W. (2000). "Installing Monitoring Wells/Piezometers in Wetlands," ERDC TN-WRAP-00-02, U.S. Army Research and Development Center, Vicksburg, MS.

US Army Corps of Engineers Wilmington District. Stream Mitigation Guidelines. 2003

Weakley, Alan S. 2011. Flora of the Southern and Mid-Atlantic States (online). Available: [http://www.herbarium.unc.edu/FloraArchives/WeakleyFlora\\_2011-May-nav.pdf](http://www.herbarium.unc.edu/FloraArchives/WeakleyFlora_2011-May-nav.pdf) [May 15, 2011]. University of North Carolina Herbarium, North Carolina Botanical Garden, University of North Carolina, Chapel Hill, North Carolina.

APPENDICES

**Appendix A. Project Vicinity Map and Background Tables**





Project Site

### Vicinity Map

UT to Millers Creek Mitigation Site, Duplin County, NC

0 750 1,500 3,000 4,500 6,000 Feet

1 inch = 2,000 feet



Figure  
1



**Table 1. Project Components and Mitigation Credits UT to the Millers Creek, Duplin County DMS Project ID No. 95719**

Mitigation Credits											
Type	Stream (SMU)		Riparian Wetland (WMU)		Non-riparian Wetland		Buffer	Nitrogen Nutrient Offset	Phosphorous Nutrient Offset	Totals	
	R	RE	R	RE	R	RE					
Totals	2,709		8.00				--	--	--		
Project Components											
Project Component or Reach ID	Stationing/Location	Existing Footage/Acreage	Approach (PI, PII, etc.)	Restoration or Restoration Equivalent	Restoration Footage or Acreage	Mitigation Ratio	SMU or WMU				
UT Millers Creek	10+13 – 37+22	2,100	PI	Restoration	2,709	1:1	2,709				
Drained Wetland (Pines)	NA	5.00	NA	Restoration	5.00	1:1	5.00				
Drained Wetland (Mature Woods)	NA	2.55	NA	Restoration	2.55	1.25:1	2.04				
Drained Wetland (Berm/Spoil Along UT)	NA	0.45	NA	Restoration	0.45	1:1	0.45				
Pond	NA	0.77	NA	Restoration	0.77	1.5:1	0.51				
TOTAL	NA	2,100/8.77	PI/NA	Restoration	2,709/8.77	1 – 1.5:1	2,709/8.00				

Component Summation					
Restoration Level	Stream (linear feet)	Riparian Wetland (acres)		Non-Riparian Wetland (acres)	Upland (acres)
		Riverine	Non-Riverine		
Restoration	2,709	8.77			
BMP Elements					
Element	Location	Purpose/Function	Notes		
Forested Buffer	UT Millers buffer	Buffer to protect stream	Filter nutrients and provide cover, foraging areas, habitat, woody debris, and wildlife		

**Table 2. Project Activity and Reporting History**  
 UT to Millers Creek (DMS Project ID No. 95719)

Activity or Report	Data Collection Complete	Completion or Delivery
Restoration Plan	Aug-13	Sep-14
Final Design – Construction Plans	Sep-14	Sep-14
Construction	3-Nov-14	23-Jan-15
Temporary S&E Mix Applied to Entire Project Area	---	23-Jan-15
Permanent Seed Mix Applied to Entire Project Area	---	23-Jan-15
Bare Root, Containerized, and B&B plantings for Entire Project Area	---	10-Mar-15
Mitigation Plan/As-built (Year 0 Monitoring-Baseline)	Mar-15	Apr-15
Year 1 Monitoring	Oct-15	Dec-15
Year 2 Monitoring	Nov-16	Feb-17
Year 3 Monitoring		
Year 4 Monitoring		
Year 5 Monitoring		
Year 6 Monitoring		
Year 7 Monitoring		

<b>Table 3. Project Contacts Table</b> UT to Millers Creek (DMS Project ID No. 95719)	
<b>Designer</b>  Primary project design POC	HDR   ICA Engineering 5121 Kingdom Way, Suite 100 Raleigh, North Carolina 27607 Kevin Williams (919) 851-6066
<b>Construction Contractor</b>  Construction Contractor POC	Land Mechanic Designs, Inc. 126 Circle G Lane Willow Spring, NC 27592 Lloyd Glover (919) 639-6132
<b>Planting Contractor</b>  Planting Contractor POC	River Works, Inc. 6105 Chapel Hill Road Raleigh, NC 27607 Phillip Todd (919) 582-3574
<b>Seeding Contractor</b>  Seeding Contractor POC	Land Mechanic Designs, Inc. 126 Circle G Lane Willow Spring, NC 27592 Lloyd Glover (919) 639-6132
Seed Mix Sources	Green Resources – Triangle Office
Nursery Stock Suppliers	1) ArborGen 2) Mellow Marsh Farm, Inc. 3) Foggy Mountain Nursery (live stakes)
<b>Monitoring Performers</b>	HDR   ICA Engineering 5121 Kingdom Way, Suite 100 Raleigh, North Carolina 27607 William Wollman (919) 801-6251
Stream Monitoring POC	HDR   ICA Engineering 5121 Kingdom Way, Suite 100 Raleigh, North Carolina 27607 William Wollman (919) 801-6251
Vegetation Monitoring POC	Land Management Group, Inc 3805 Wrightsville Avenue, Suite 15 Wilmington, NC 28403 Kim Williams (910) 452-0001 x 1908

**Table 4. Project Information**  
UT to Millers Creek (DMS Project ID No. 95719)

Project Information	
Project Name	UT to Millers Creek Stream and Wetland Mitigation Site
Project County	Duplin
Project Area (acres)	15.944 AC
Project Coordinates	34.894467,-78.067625
Project Watershed Summary Information	
Physiographic Region	Coastal Plain
Ecoregion	Southeastern Plains
Project River Basin	Cape Fear
USGS 8-digit HUC	3030006
USGS 14-digit HUC	3030006110040
NCDWQ Subbasin	03-06-19
Project Drainage Area	250 AC
Watershed Land Use	Cultivated, Southern Yellow Pine, Bottomland Forest / Hardwood Swamps

Reach Summary Information	
Parameters	UT to Millers Creek
Restored length	2,709 linear feet
Drainage Area	250 AC.
NCDWQ Index Number	36
NCDWQ Classification	C, Sw
Valley Type/Morphological Description	X/Existing G/5/Restored E5
Dominant Soil Series	Bibb sandy loam and Torhunta fine sandy loam (USDA/NRCS records). Cape Fear, Rains, Plummer, Rutlege and Lynn Haven Soil series (additional series mapped by LMG)
Drainage Class	Poorly and very poorly
Soil Hydric Status	Bibb sandy loam (hydric) Torhunta mucky fine sandy loam (hydric)
Slope	0.0016
FEMA Classification	Zone X
Native Vegetation Community	Mixed stand of hardwoods and pine
Percent Composition of Exotic Invasives	<5%

Wetland Summary Information			
Parameters	Wetland 1	Wetland 2	Wetland 3
Size of Wetland (acres)	0.21	0.12	0.59
Wetland Type (non-riparian riverine or riparian non-riverine)	Riparian Non-Riverine	Riparian Non-Riverine	Riparian Non-Riverine
Mapped Soil Series	BbA	ToA	BnB
Drainage class	Poorly Drained	Very Poorly Drained	Moderately Well Drained
Soil Hydric Status	Hydric	Hydric	Partially Hydric
Source of Hydrology	Groundwater	Groundwater	Groundwater
Hydrologic Impairment	Stream Incision	Stream Incision	Stream Incision/Beavers
Native vegetation community	Forested	Forested	Emergent
Percent composition of exotic invasion vegetation	0	0	0

Regulatory Considerations			
Regulation	Applicable	Resolved	Supporting Documentation
Waters of the U.S. --Sections 404 and 401	Yes	Yes	Restoration Plan/NW 27
Endangered Species Act	No	Yes	NCNHP/USFWS
Historic Preservation Act	No	Yes	NCSHPO
CZMA/CAMA	No	Yes	--
FEMA Floodplain Compliance	Yes	Yes	HECRAS
Essential Fisheries Habitat	No	N/A	--



**Appendix B. Visual Assessment Data**


**Figure 2.0 – 2.6. Current Condition Plan View (Sheets 1-7)**



2/19/2016  
 R:\6.0\_CAD\_BIM\6.2\_Work\_In\_Progress\stream\Pro\Monitoring Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_01.dgn  
 ICA Engineering

**CONTRACT: UT MILLERS CREEK**    **DMS PROJECT # 95719**

**NCDEQ CONTRACT # 5000**

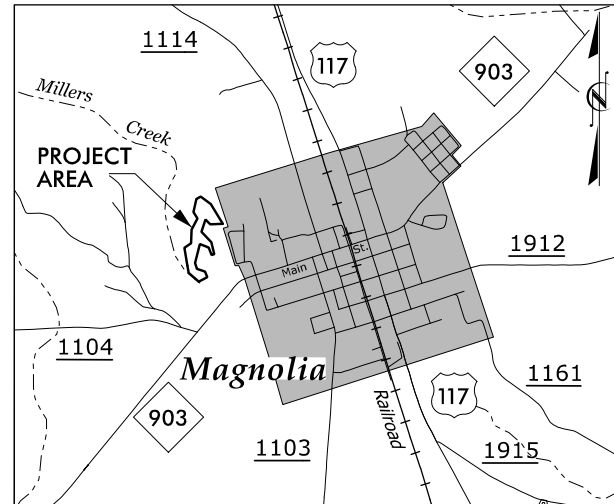


**VICINITY MAP**

# CURRENT CONDITIONS PLAN VIEW (CCPV) UT MILLERS CREEK

**LOCATION: DUPLIN COUNTY, NORTH CAROLINA**  
**LAT: 34°53'48" N      LONG: 78°04'04" W**  
**TYPE OF WORK: CCPV PLANS - YEAR 2**


STATE	UT MILLERS CREEK	SHEET NO.	TOTAL SHEETS
N.C.		1	7

YEAR 2 CONDITIONS		LEGEND	
<b>BANK/BED CONDITION</b>		CONSERVATION EASEMENT LINE	THALWEG
GULLY	VEGETATION PROBLEM AREAS	BANKFULL	ASBUILT TOP OF TRAY
THIN GRASS	NO GRASS (BARE)	ASBUILT TOE OF TRAY	CROSS-SECTION LOCATIONS
<b>VEGETATION PLOT CONDITIONS</b>		CONSTRUCTION REVISIONS	LOG SILL
CRITERIA MET	CRITERIA UNMET	10M x 10M VEG PLOT	VEG PLOT ORIGIN
		FLOODPLAIN INTERCEPTOR	SOIL LIFT
		MONITORING WELL	CREST GAUGE
		BANK PIN	BRUSH TOE

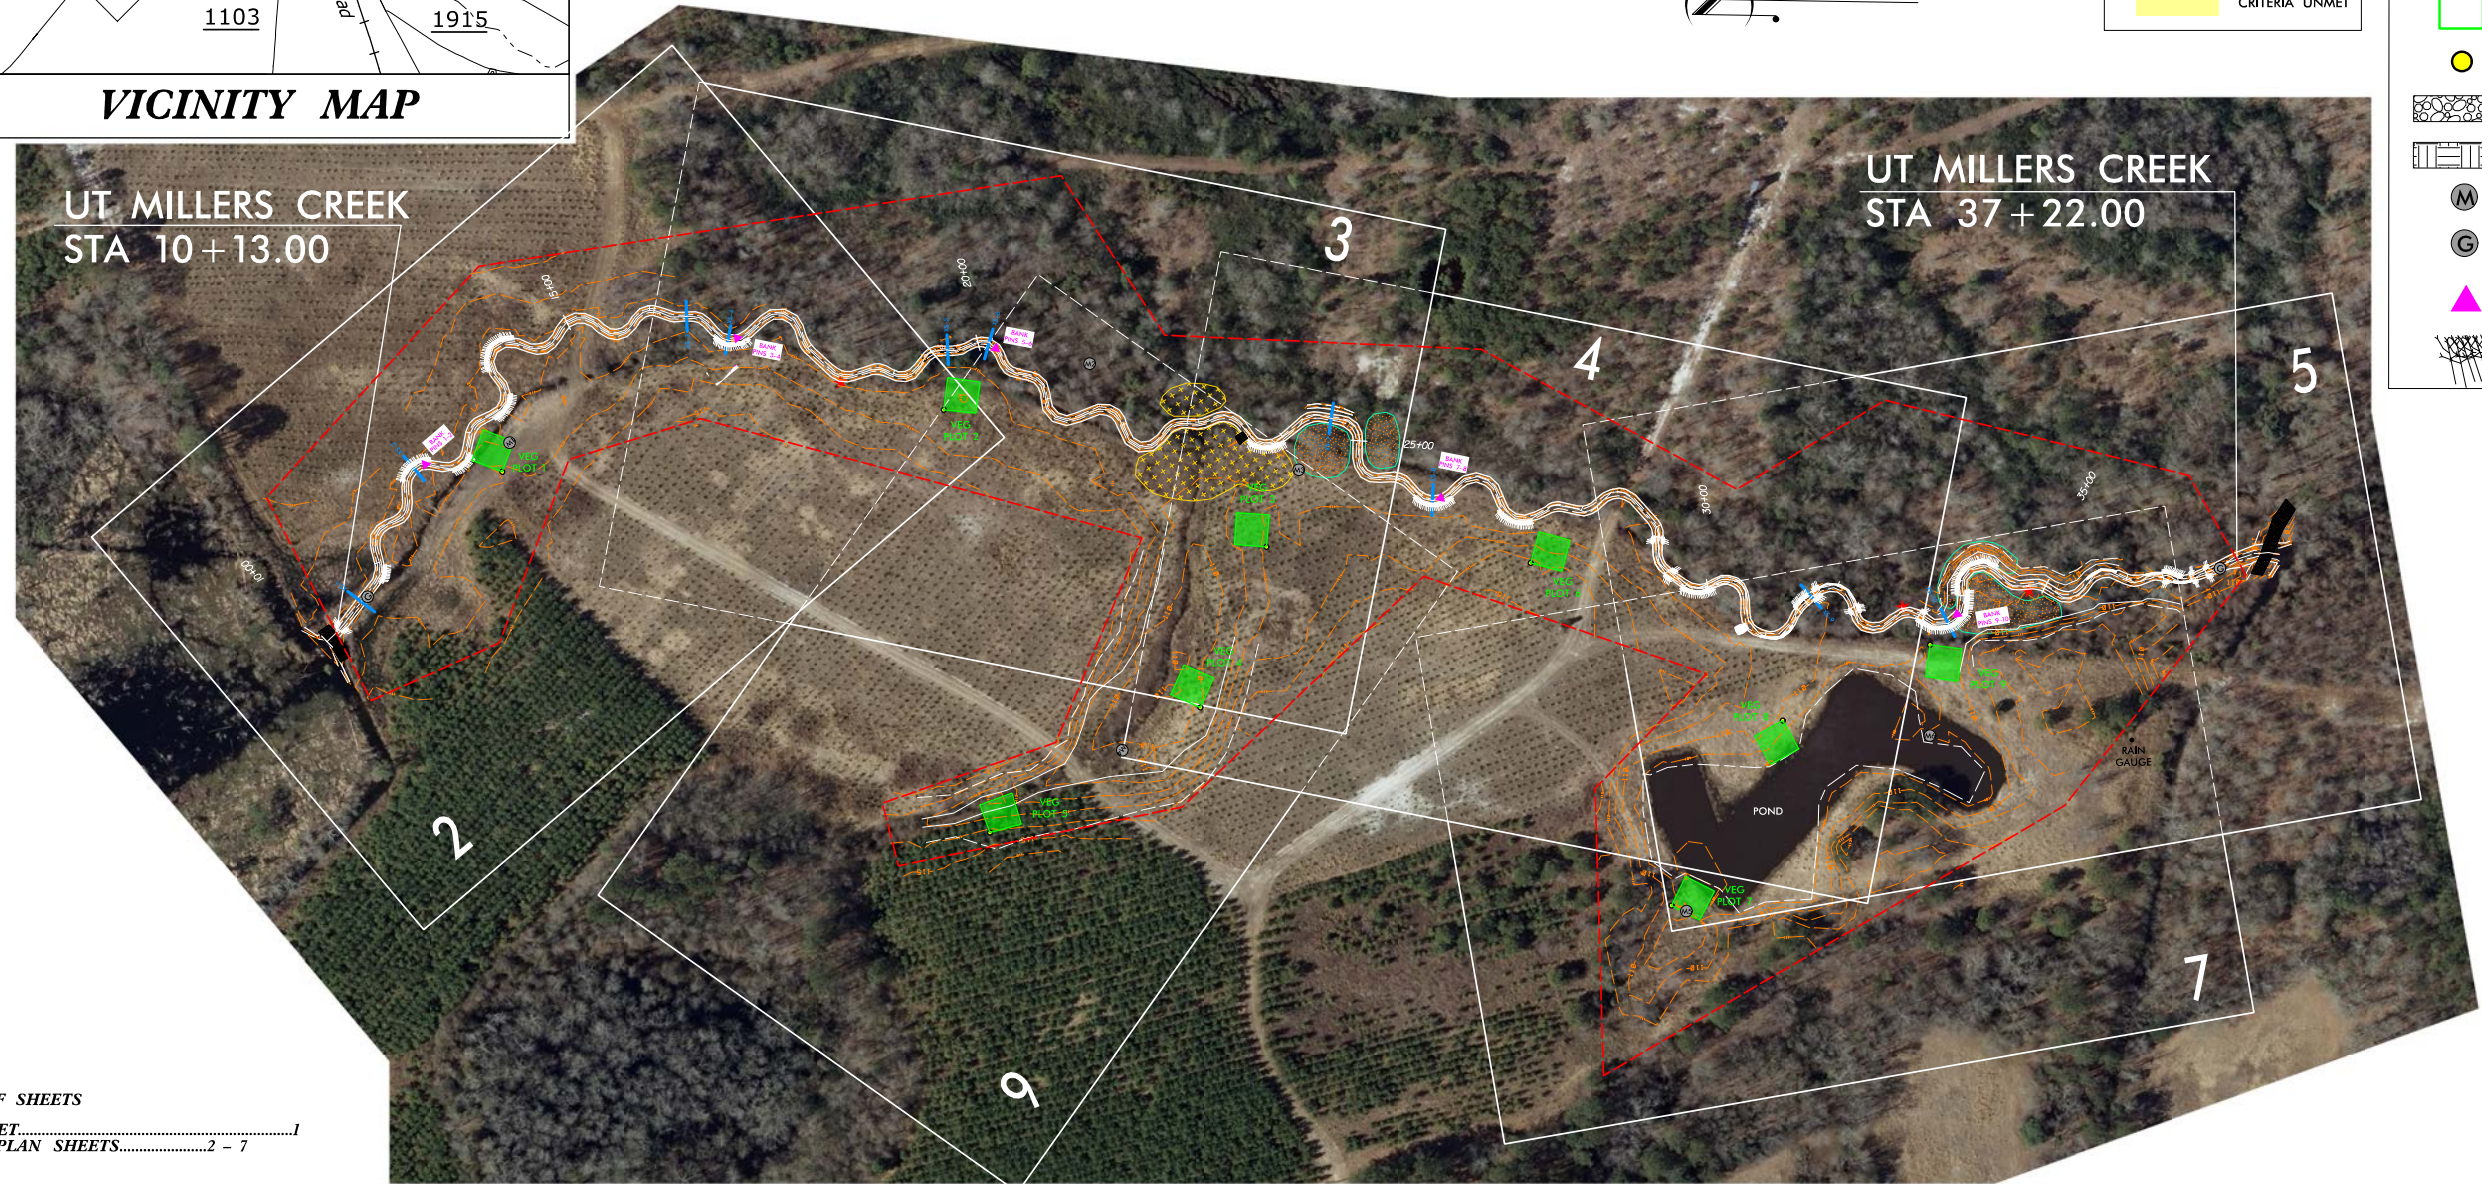

**INDEX OF SHEETS**

TITLE SHEET	1
CCPV YR1 PLAN SHEETS	2 - 7

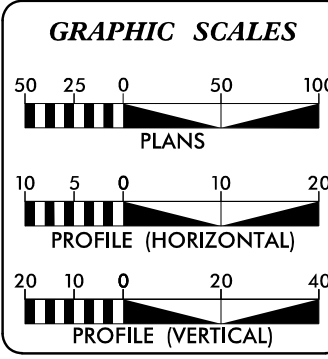

**DESIGN DATA**

DESIGN STREAM TYPE	=	E5
BANKFULL AREA (FT <sup>2</sup> ) CROSS-SECTIONED	=	8.06
BANKFULL WIDTH (FT)	=	8.8
MAX DEPTH (FT)	=	1.40
WIDTH /DEPTH RATIO	=	9.5
DRAINAGE AREA (MI <sup>2</sup> )	=	0.39
BANKFULL SLOPE(FT/FT)	=	0.0005

**PROJECT LENGTH**

EXISTING STREAM LENGTH	=	2,095 FT
PROPOSED DESIGN STREAM LENGTH	=	2,696 FT
ASBUILT STREAM LENGTH	=	2,709 FT

<b>R. KEVIN WILLIAMS</b> PROJECT ENGINEER <b>KATHLEEN M. McKEITHIAN</b> PROJECT DESIGNER <b>RYAN V. SMITH</b> PROJECT MANAGER
--

**INCOMPLETE PLANS**  
**PRELIMINARY PLANS**  
DO NOT USE FOR CONSTRUCTION

SURVEY PREPARED BY:  
 STEWART - PROCTOR, PLLC  
 319 CHAPANOKE ROAD  
 RALEIGH NC 27603  
 HERBERT H. PROCTOR, JR. L-3621

Prepared In the Office of:


5121 Kingdom Way,  
Suite 100  
Raleigh, NC 27607  
NC License No: F-0258



# CURRENT CONDITIONS PLAN VIEW (CCPV) YEAR 2

### LEGEND

	CONSERVATION EASEMENT LINE		FLOODPLAIN INTERCEPTOR
	THALWEG		SOIL LIFT
	BANKFULL		MONITORING WELL
	ASBUILT TOP OF TRAY		CREST GAUGE
	ASBUILT TOE OF TRAY		BANK PIN
	CROSS-SECTION LOCATIONS		BRUSH TOE
	CONSTRUCTION REVISIONS		
	LOG SILL		
	10M x 10M VEG PLOT		
	VEG PLOT ORIGIN		

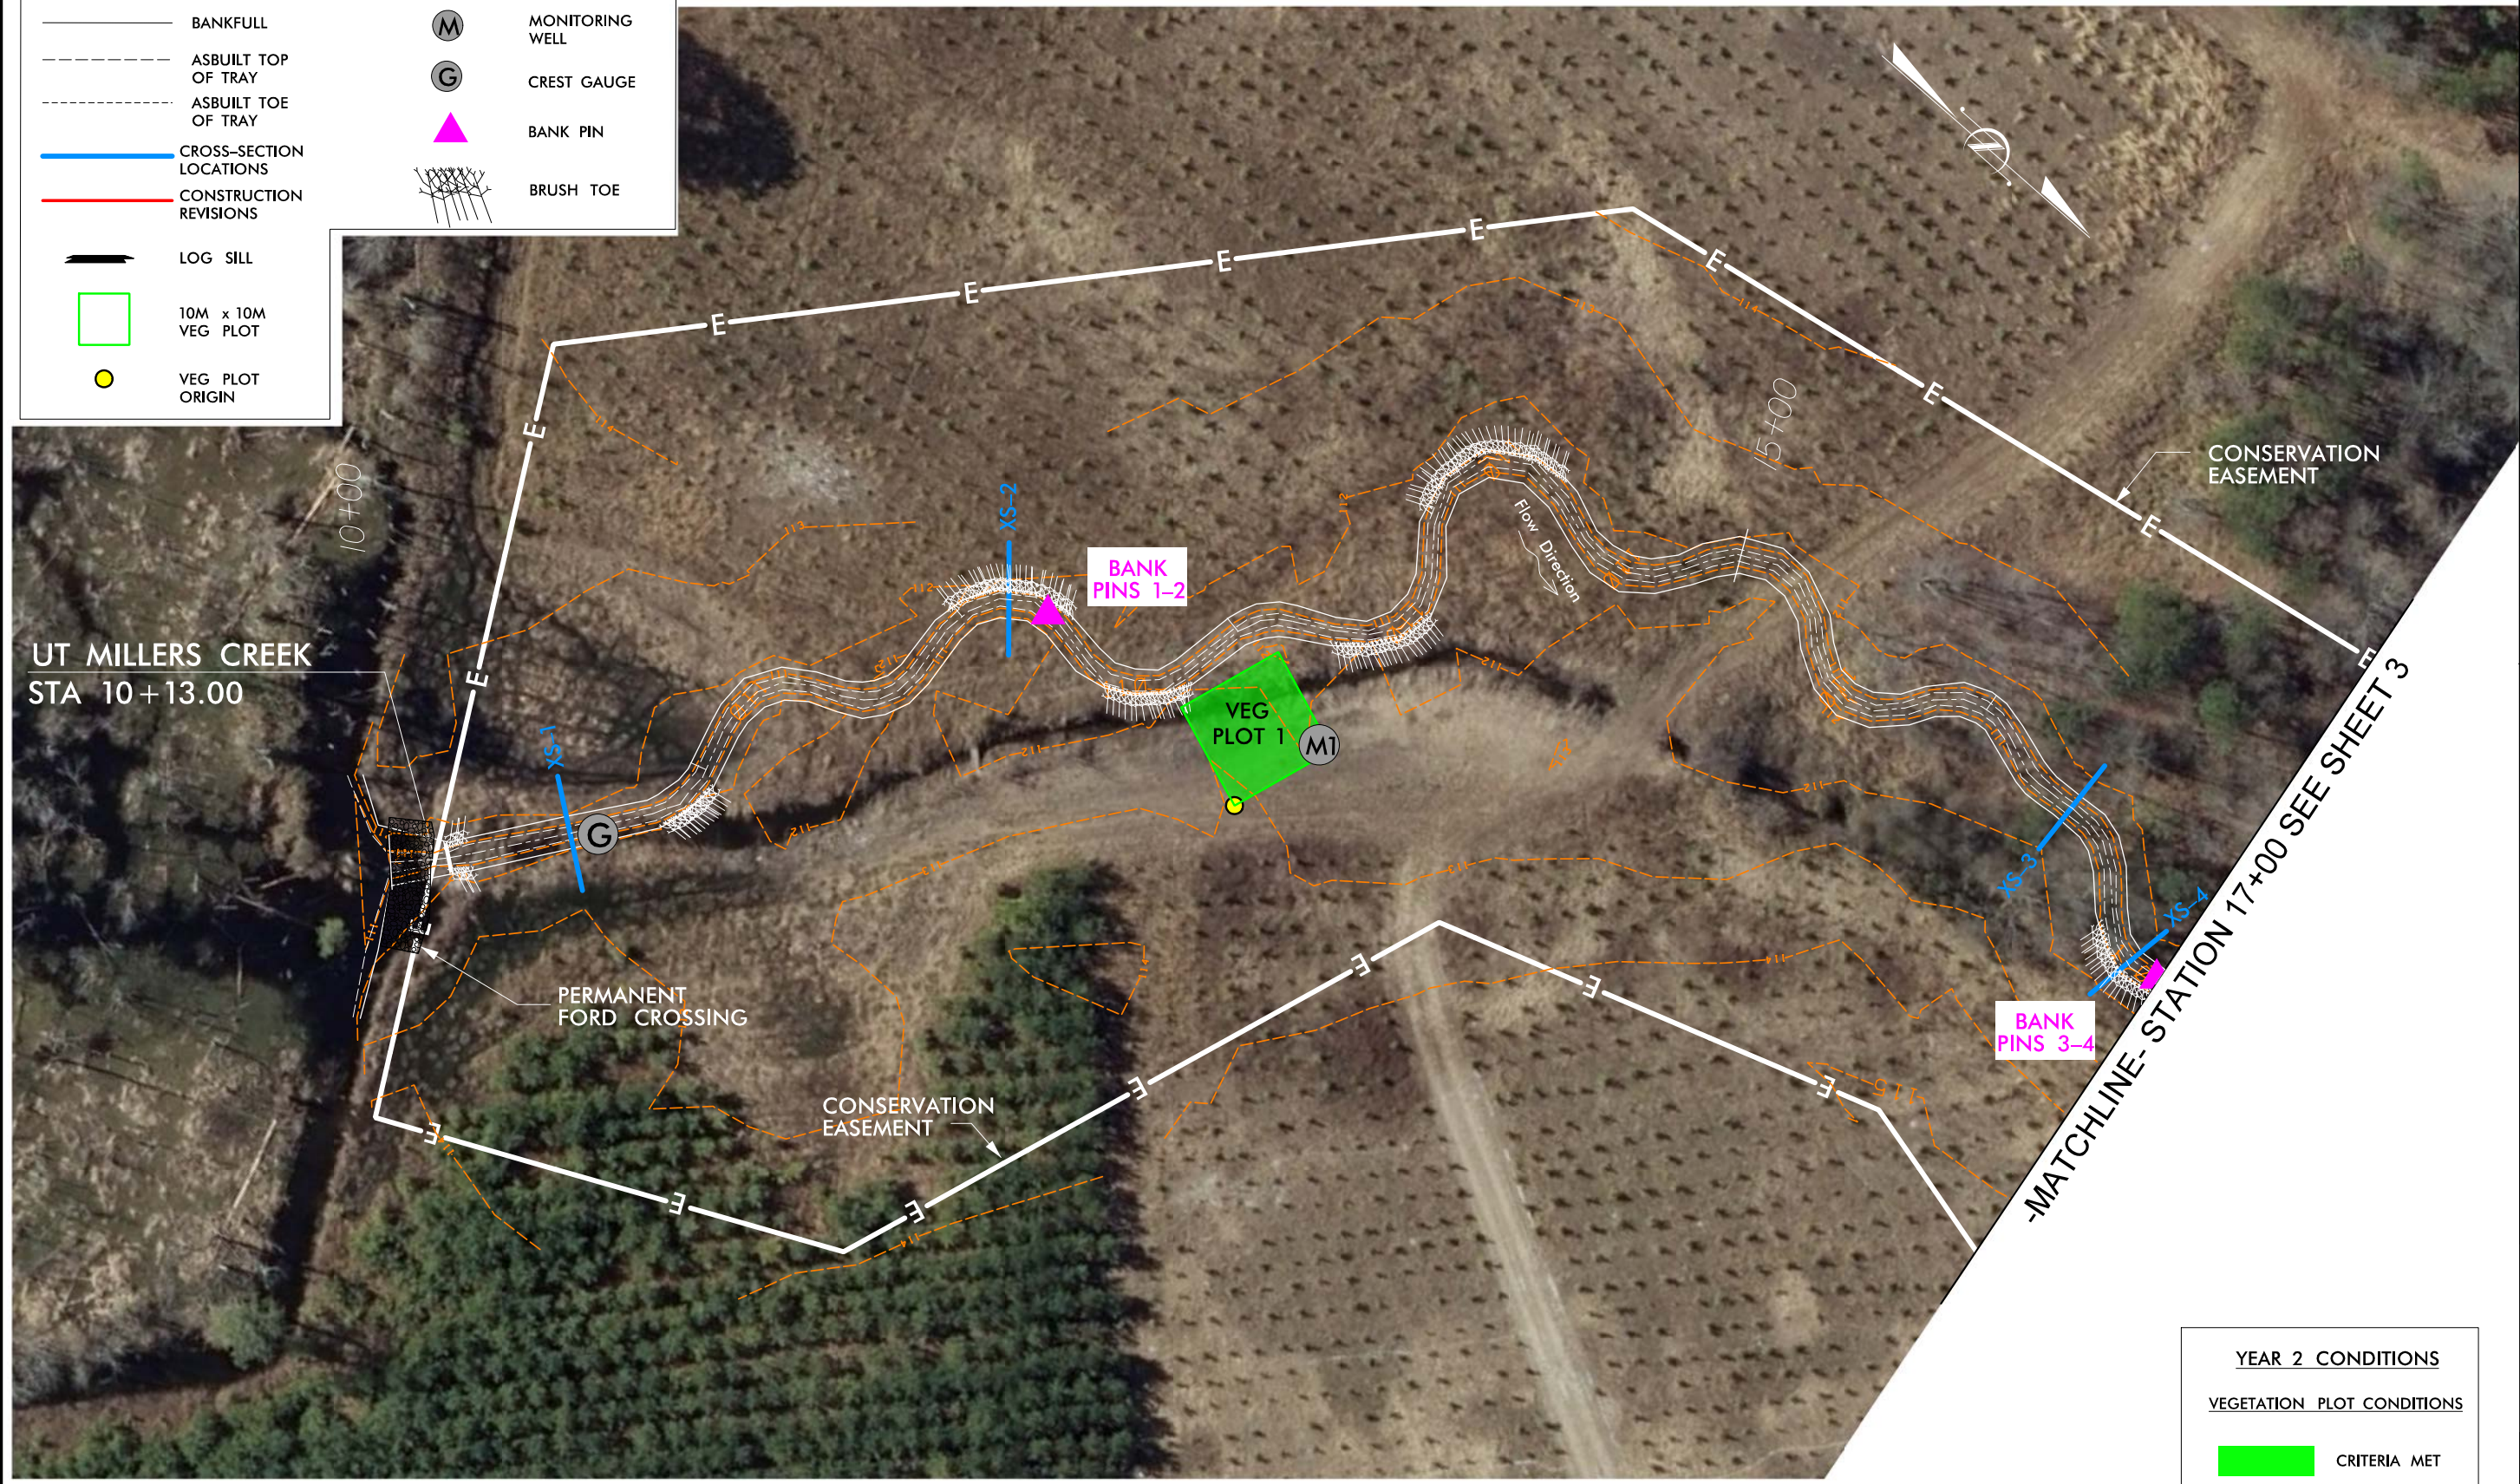


#### YEAR 2 CONDITIONS

VEGETATION PLOT CONDITIONS

	CRITERIA MET
	CRITERIA UNMET

**FOR ICA**

UT MILLERS CREEK  
STREAM RESTORATION PROJECT  
DUPLIN COUNTY, NORTH CAROLINA  
STA 10+13 - STA 17+00



DATE: 12-19-16  
CCVP YR2 PLAN  
SHEET 2 OF 7

12/19/2016 11:16:00 CAD\_BIM\6.2\_Work-In-Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_02.dgn

FOR CCPV YR2 PLANS SEE SHEETS 2 THRU 7



# CURRENT CONDITIONS PLAN VIEW (CCPV) YEAR 2

**YEAR 2 CONDITIONS**

**BANKBED CONDITION**

★ GULLY


**VEGETATION PROBLEM AREAS**

x x x NO GRASS (BARE)

**VEGETATION PLOT CONDITIONS**

CRITERIA MET

CRITERIA UNMET

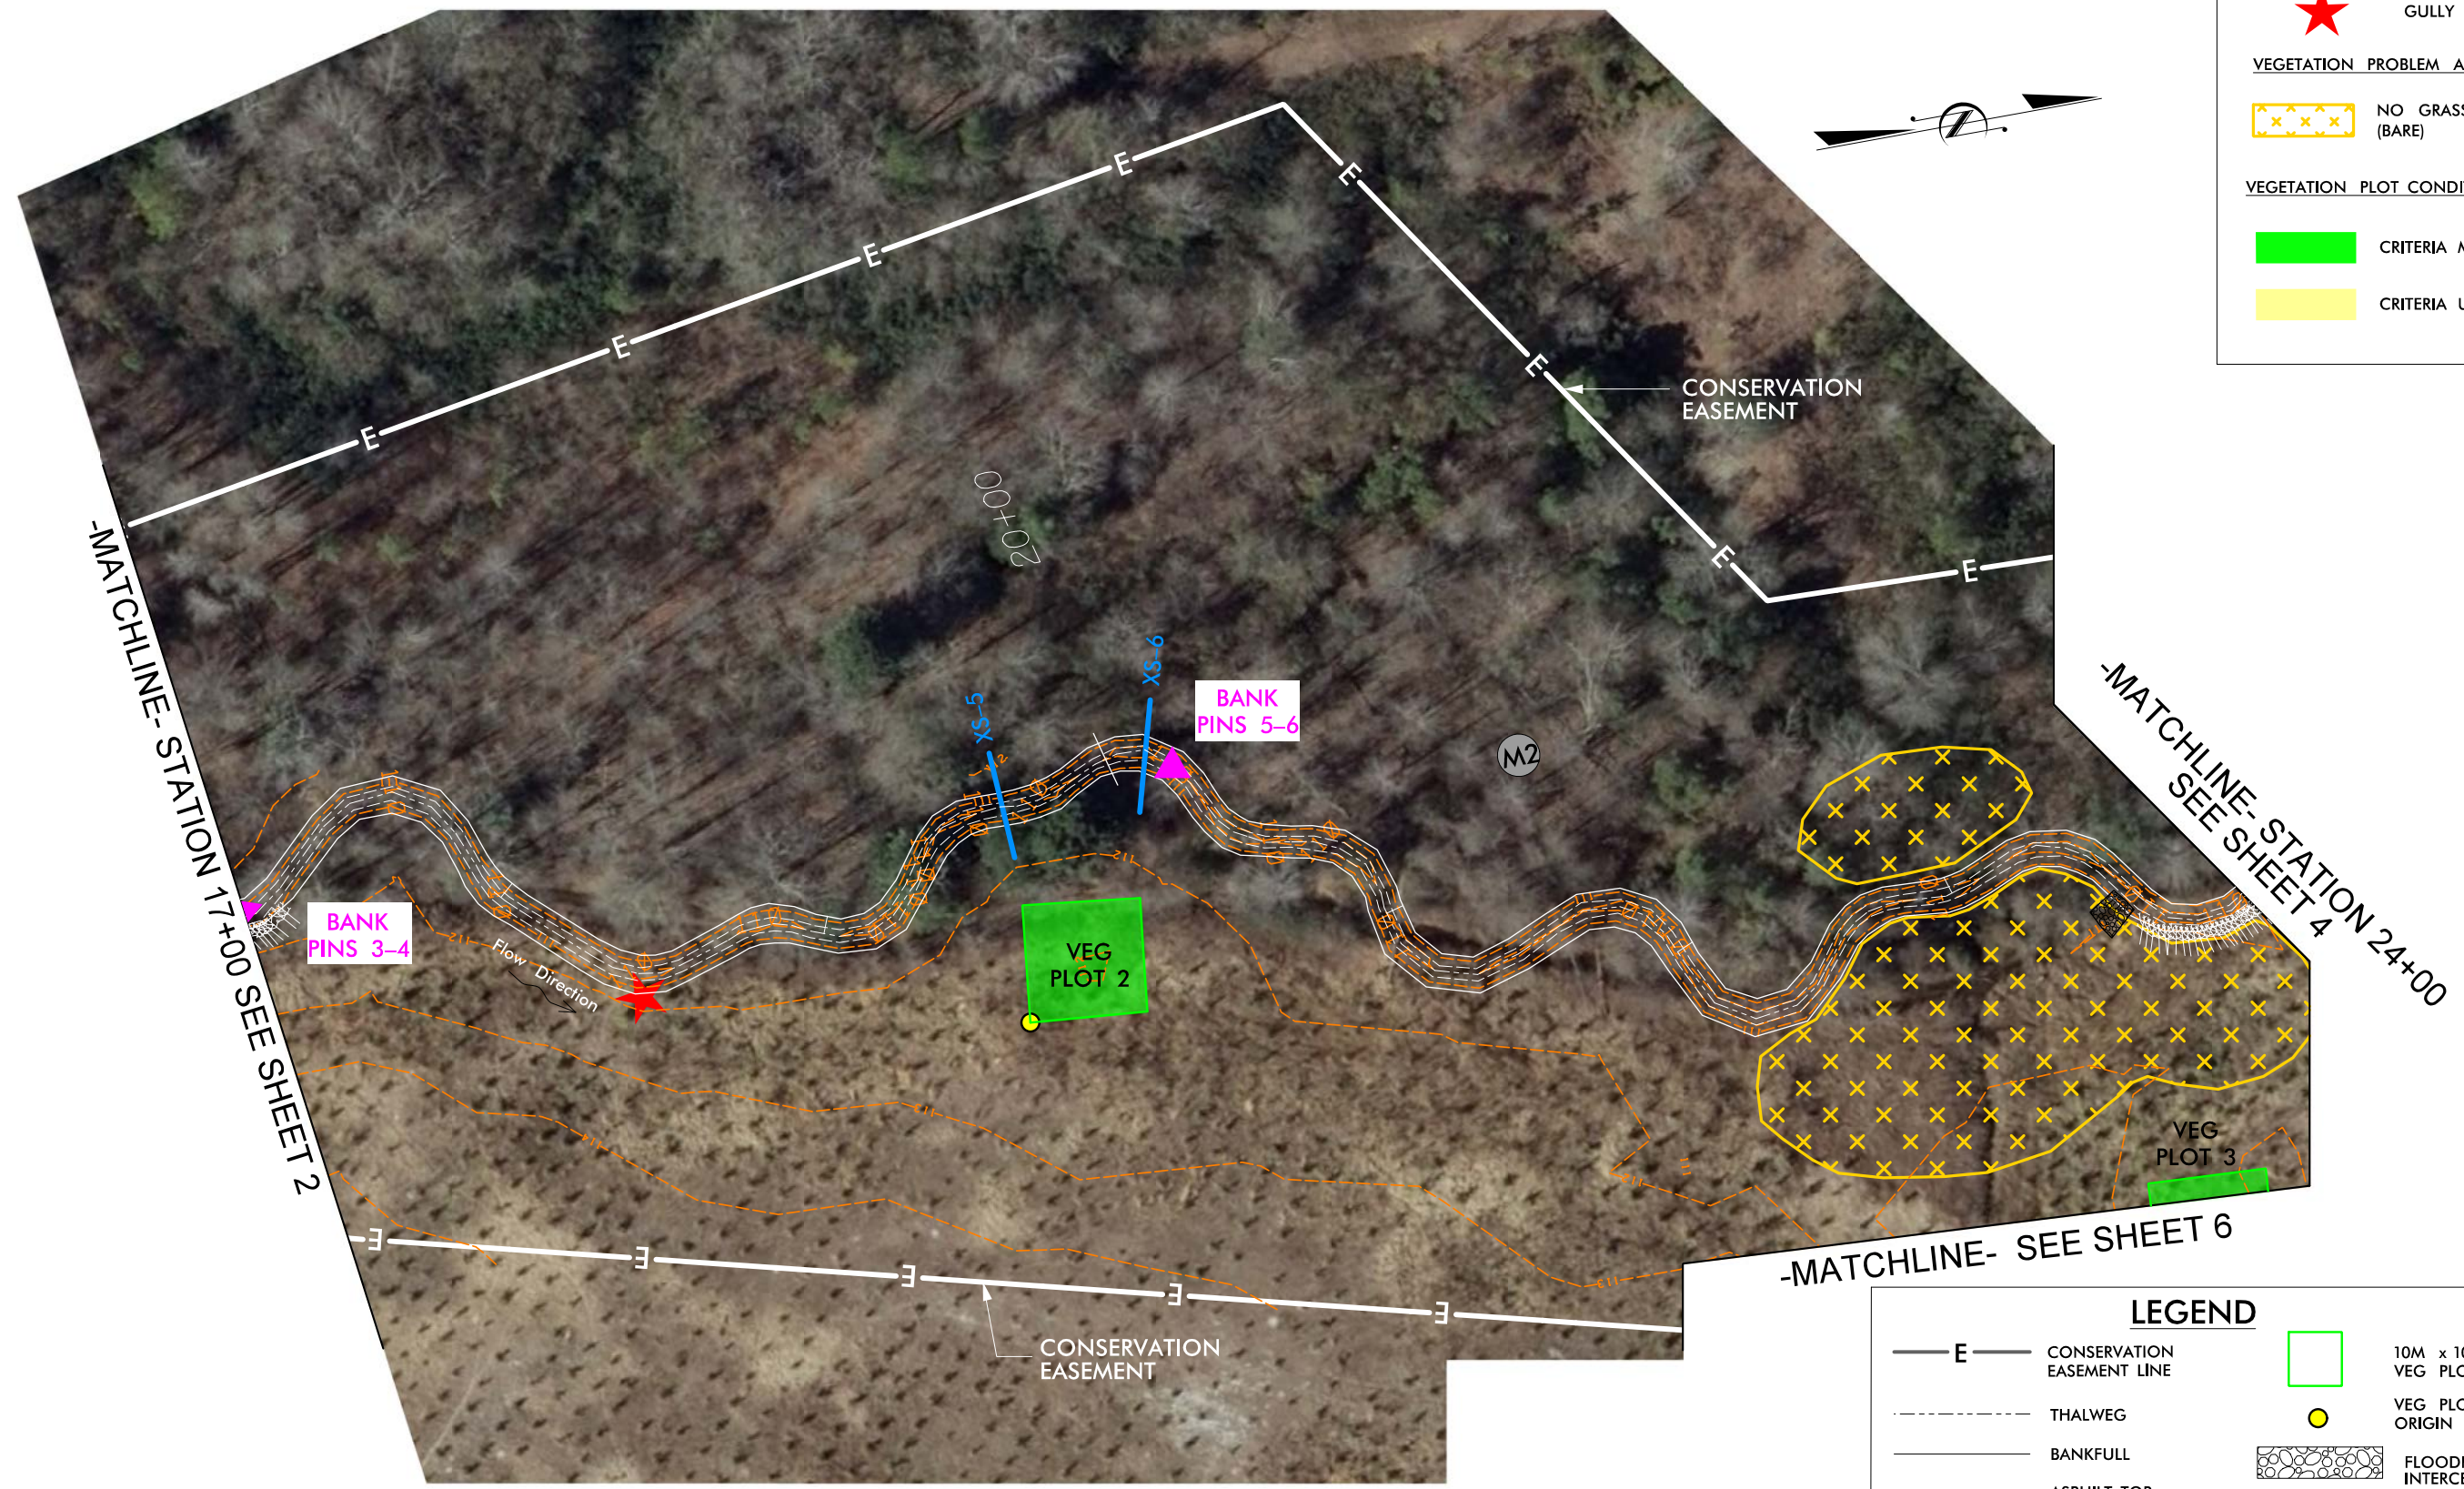


**LEGEND**

<span style="border-bottom: 1px solid black; width: 50px; display: inline-block;"></span> E	CONSERVATION EASEMENT LINE	<span style="border: 1px solid green; width: 20px; height: 10px; display: inline-block;"></span>	10M x 10M VEG PLOT
<span style="border-bottom: 1px dashed black; width: 50px; display: inline-block;"></span>	THALWEG	<span style="background-color: yellow; width: 10px; height: 10px; display: inline-block; border-radius: 50%;"></span>	VEG PLOT ORIGIN
<span style="border-bottom: 1px solid black; width: 50px; display: inline-block;"></span>	BANKFULL	<span style="border: 1px dashed black; width: 20px; height: 10px; display: inline-block;"></span>	FLOODPLAIN INTERCEPTOR
<span style="border-bottom: 1px dashed black; width: 50px; display: inline-block;"></span>	ASBUILT TOP OF TRAY	<span style="border: 1px solid black; width: 20px; height: 10px; display: inline-block;"></span>	SOIL LIFT
<span style="border-bottom: 1px dashed black; width: 50px; display: inline-block;"></span>	ASBUILT TOE OF TRAY	<span style="border: 1px solid black; width: 10px; height: 10px; display: inline-block; border-radius: 50%;"></span> M	MONITORING WELL
<span style="border-bottom: 1px solid red; width: 50px; display: inline-block;"></span>	CROSS-SECTION LOCATIONS	<span style="color: pink;">▲</span>	BANK PIN
<span style="border-bottom: 1px solid red; width: 50px; display: inline-block;"></span>	CONSTRUCTION REVISIONS	<span style="border: 1px dashed black; width: 20px; height: 10px; display: inline-block;"></span>	BRUSH TOE
<span style="border-bottom: 1px solid black; width: 50px; display: inline-block;"></span>	LOG SILL		

**FOR ICA**

UT MILLERS CREEK  
STREAM RESTORATION PROJECT  
DUPLIN COUNTY, NORTH CAROLINA  
STA 17+00 - STA 24+00



DATE: 12-19-16

CCVP YR2 PLAN


SHEET  
**3**  
OF 7

12/19/2016 11:16:00 CAD\_BIM\6.2\_Work-In-Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_03.dgn  
ICA Engineering

FOR CCPV YR2 PLANS SEE SHEETS 2 THRU 7



**CURRENT CONDITIONS PLAN VIEW (CCPV)  
YEAR 2**

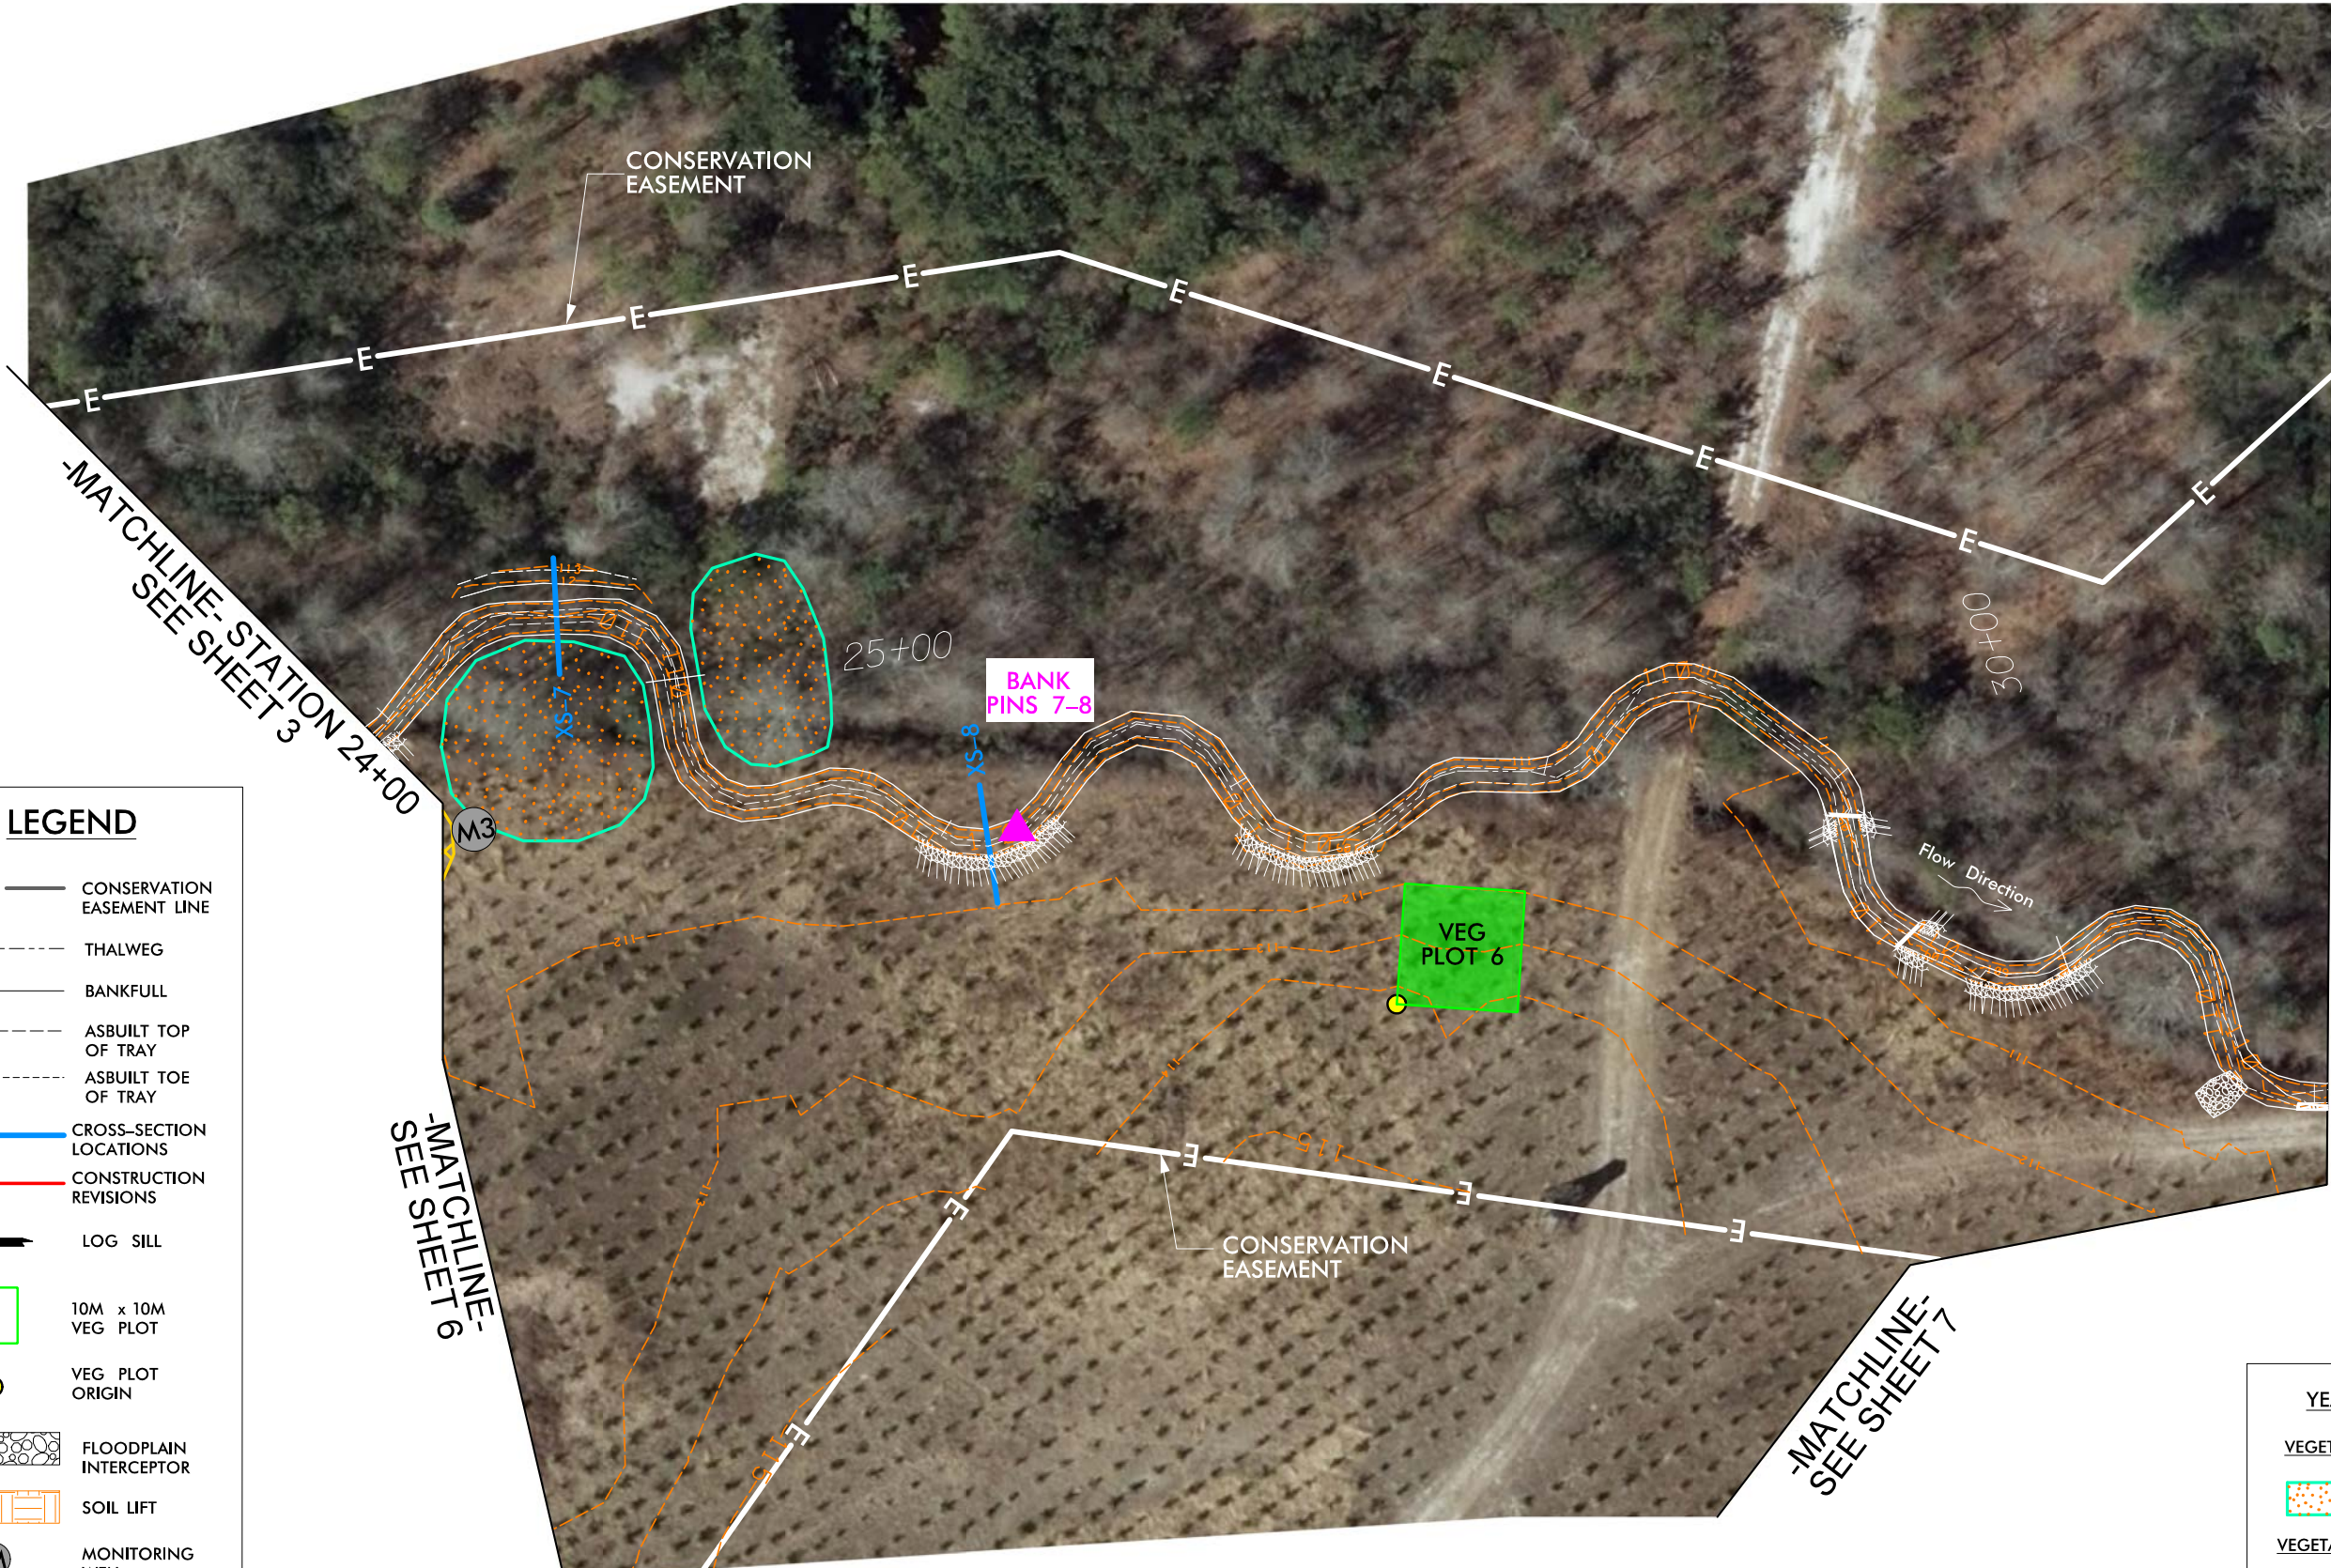

**LEGEND**


- CONSERVATION EASEMENT LINE
- THALWEG
- BANKFULL
- ASBUILT TOP OF TRAY
- ASBUILT TOE OF TRAY
- CROSS-SECTION LOCATIONS
- CONSTRUCTION REVISIONS
- LOG SILL
- 10M x 10M VEG PLOT
- VEG PLOT ORIGIN
- FLOODPLAIN INTERCEPTOR
- SOIL LIFT
- MONITORING WELL
- BANK PIN
- BRUSH TOE

**CONSTRUCTION REVISIONS**

A FLOODPLAIN INTERCEPTOR WAS ADDED AT STA 30+79±.

**YEAR 2 CONDITIONS**

- VEGETATION PROBLEM AREAS**
- THIN GRASS
- VEGETATION PLOT CONDITIONS**
- CRITERIA MET
- CRITERIA UNMET



DATE: 12-19-16

CCVP YR2 PLAN

SHEET  
4  
OF 7

**FOR ICA**

UT MILLERS CREEK  
STREAM RESTORATION PROJECT  
DUPLIN COUNTY, NORTH CAROLINA  
STA 24+00 - STA 31+00

12/19/2016 11:16:00 CAD\_BIM\6.2\_Work-In-Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_04.dgn

FOR CCPV YR2 PLANS SEE SHEETS 2 THRU 7




12/19/2016  
 R:\60\_CAD\_BIM\6.2\_Work-In-Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_05.dgn  
 ICA Engineering

### LEGEND

- CONSERVATION EASEMENT LINE
- THALWEG
- BANKFULL
- ASBUILT TOP OF TRAY
- ASBUILT TOE OF TRAY
- CROSS-SECTION LOCATIONS
- CONSTRUCTION REVISIONS
- LOG SILL
- 10M x 10M VEG PLOT
- VEG PLOT ORIGIN
- FLOODPLAIN INTERCEPTOR
- SOIL LIFT
- CREST GAUGE
- BANK PIN
- BRUSH TOE


### YEAR 2 CONDITIONS

- BANKBED CONDITION**
- GULLY
- VEGETATION PROBLEM AREAS**
- THIN GRASS
- VEGETATION PLOT CONDITIONS**
- CRITERIA MET
- CRITERIA UNMET

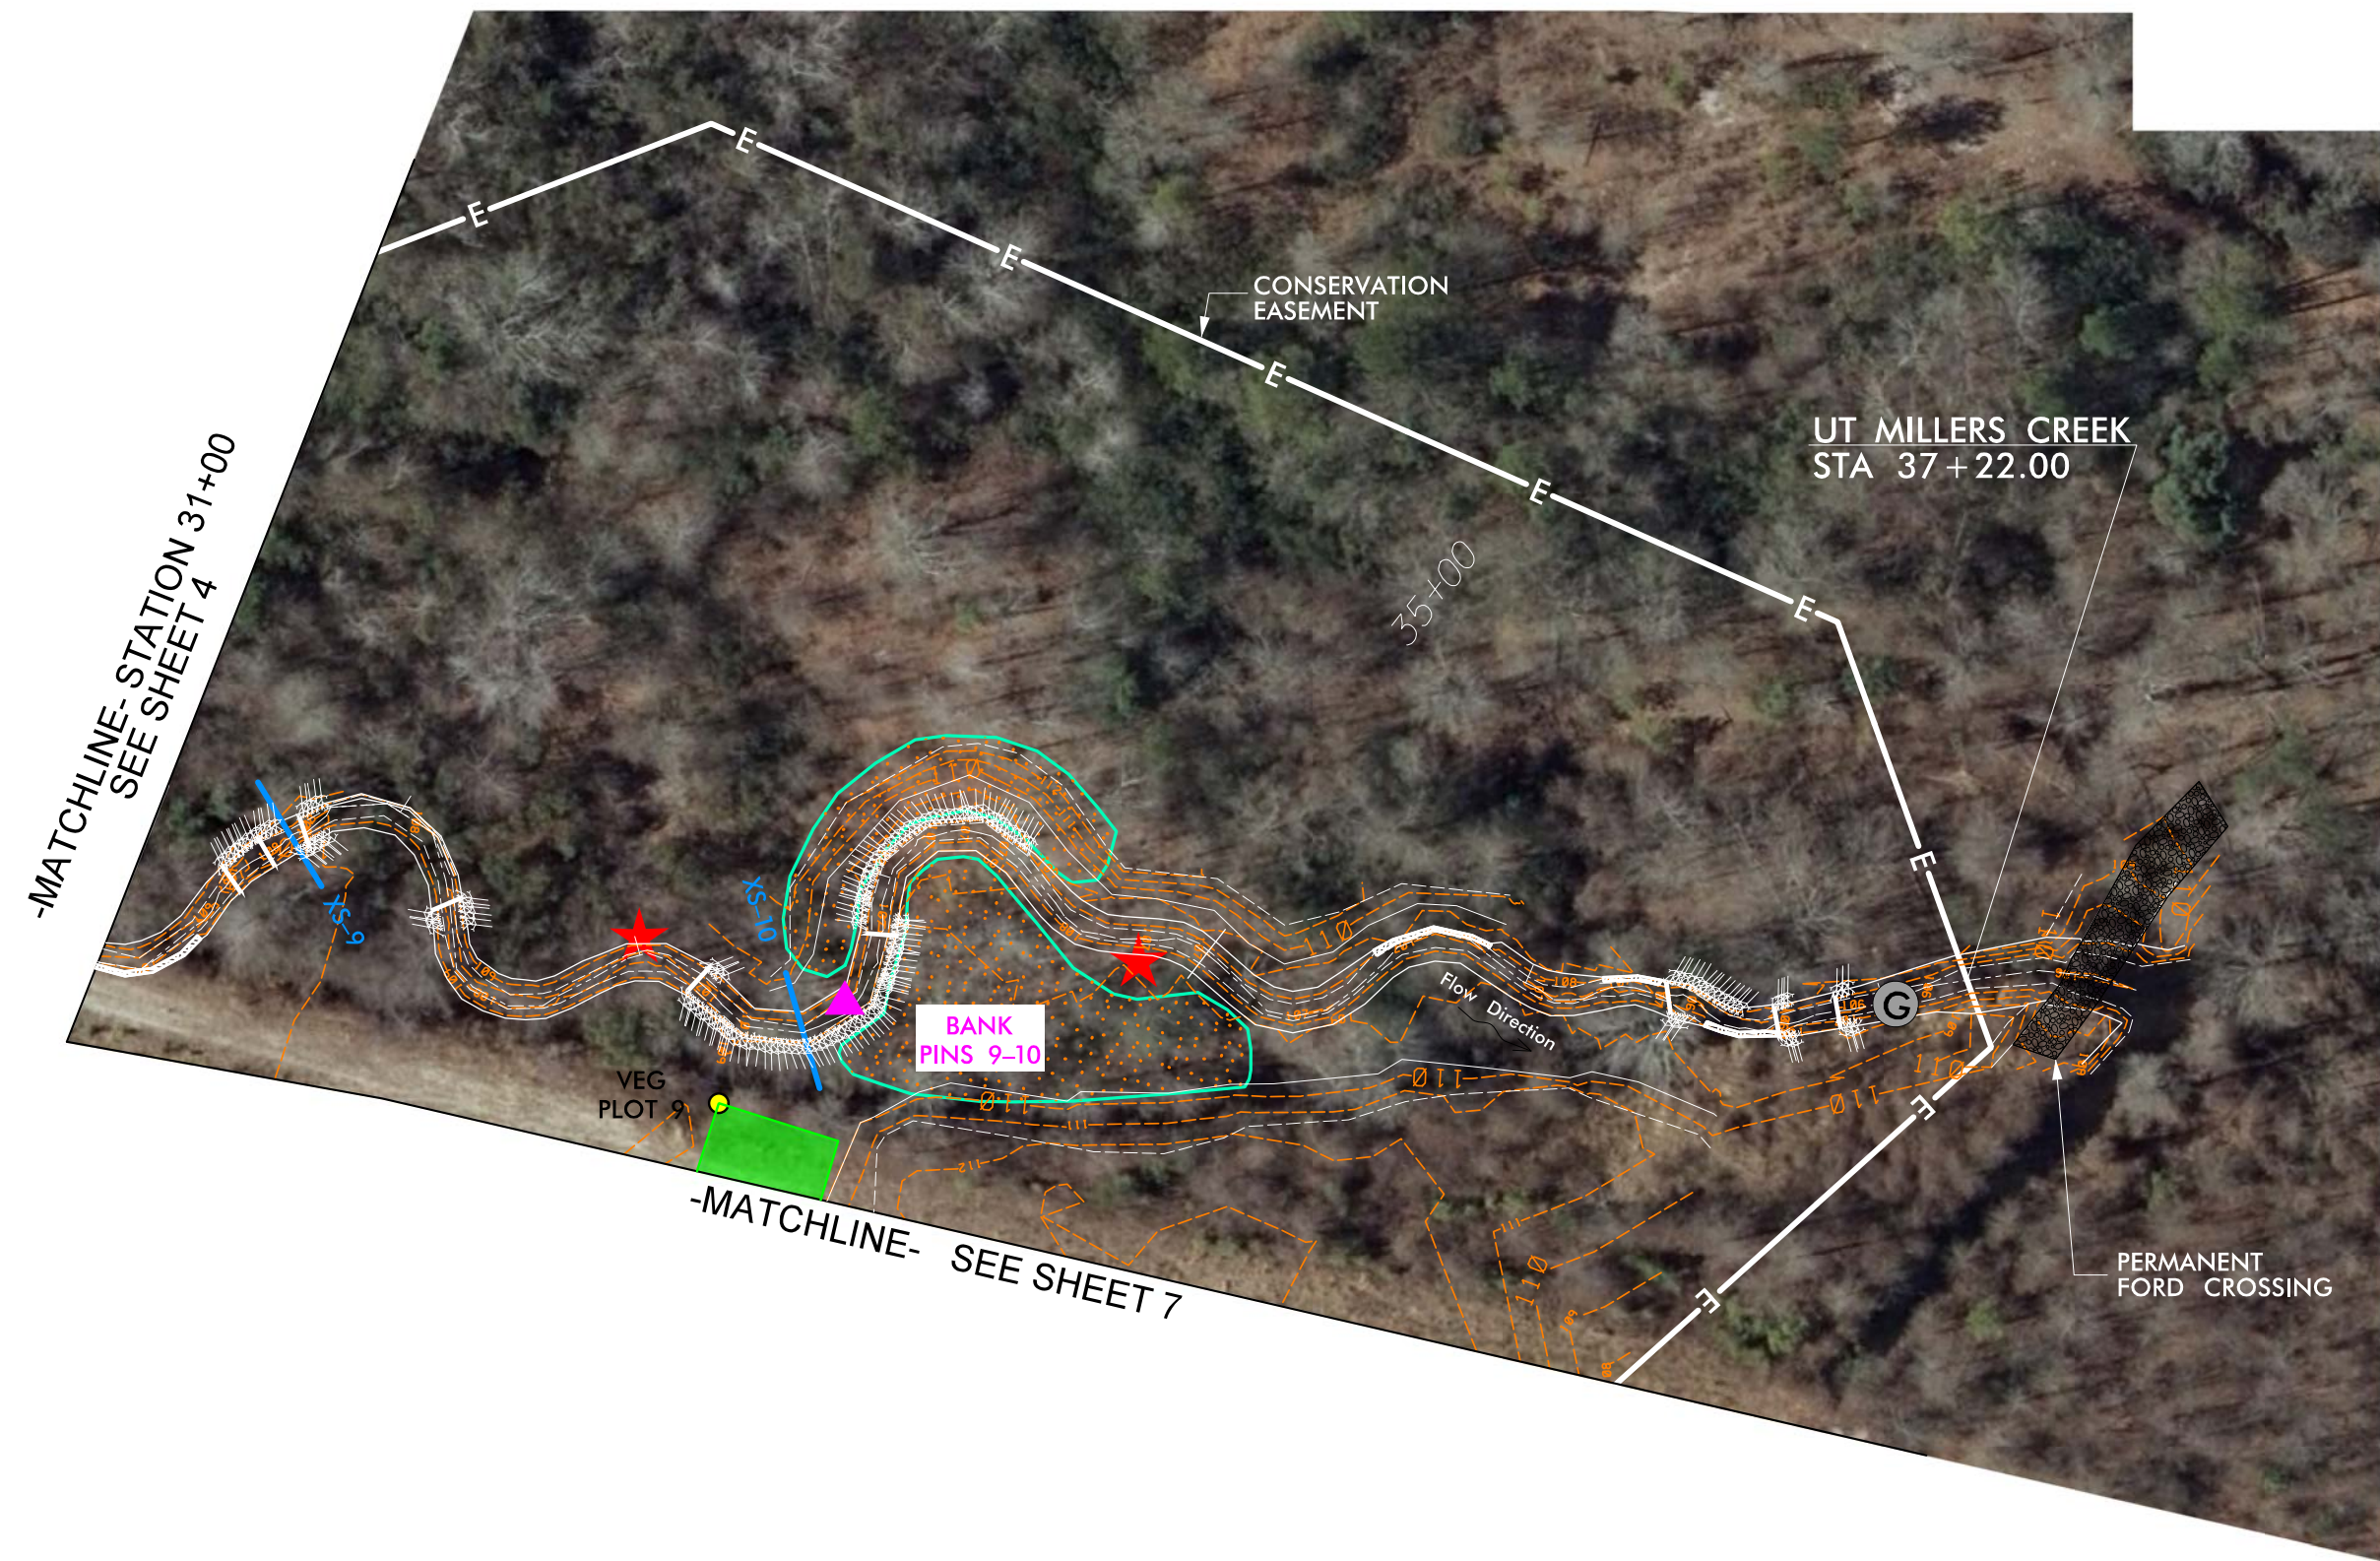

**FOR ICA**

UT MILLERS CREEK  
 STREAM RESTORATION PROJECT  
 DUPLIN COUNTY, NORTH CAROLINA  
 STA 31+00 - STA 37+22



DATE: 12-19-16

CCVP YR2 PLAN

SHEET  
5  
OF 7



**CURRENT CONDITIONS PLAN VIEW (CCPV)  
YEAR 2**



**YEAR 2 CONDITIONS**

VEGETATION PLOT CONDITIONS

<span style="display:inline-block; width:15px; height:15px; background-color: #00FF00; border: 1px solid black;"></span>	CRITERIA MET
<span style="display:inline-block; width:15px; height:15px; background-color: #FFFF00; border: 1px solid black;"></span>	CRITERIA UNMET

**LEGEND**


	CONSERVATION EASEMENT LINE
	10M x 10M VEG PLOT
	VEG PLOT ORIGIN
	MONITORING WELL

FOR CCPV YR2 PLANS SEE SHEETS 2 THRU 7

12/19/2016 12:16:00 CAD\_BIM\6.2\_Work-In-Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_06.dgn ICA Engineering

**FOR ICA**

UT MILLERS CREEK  
STREAM RESTORATION PROJECT  
DUPLIN COUNTY, NORTH CAROLINA



DATE: 12-19-16

CCVP YR2  
PLAN

SHEET  
**6**  
OF 7



CURRENT CONDITIONS PLAN VIEW (CCPV)  
YEAR 2



-MATCHLINE- SEE SHEET 4

-MATCHLINE- SEE SHEET 5

VEG PLOT 8

VEG PLOT 9

POND

RAIN GAUGE


VEG PLOT 7

CONSERVATION EASEMENT

CONSERVATION EASEMENT

YEAR 2 CONDITIONS	
VEGETATION PLOT CONDITIONS	
	CRITERIA MET
	CRITERIA UNMET

LEGEND	
	CONSERVATION EASEMENT LINE
	10M x 10M VEG PLOT
	VEG PLOT ORIGIN
	MONITORING WELL



DATE: 12-19-16

CCVP YR2 PLAN

SHEET 7

OF 7

FOR ICA

UT MILLERS CREEK  
STREAM RESTORATION PROJECT  
DUPLIN COUNTY, NORTH CAROLINA  
POND

12/19/2016 11:16:00 CAD\_BIM\6.2\_Work\_In\_Progress\Stream\Proj\Monitoring\_Plans\Year 2\UTMillersCrk\_psh\_Mon\_YR2\_07.dgn

FOR CCPV YR2 PLANS SEE SHEETS 2 THRU 7







**Table 5: Visual Stream Morphology Stability Assessment**

Reach ID: UT Millers Creek  
Assessed Length: 2,079 FT

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation	
1. Bed	1. Vertical Stability (Rifle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (DOT to include point bars)			0	0	100%				
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%				
	2. Rifle Condition	1. <u>Texture/Substrate</u> - Rifle maintains coarser substrate	N/A	N/A				100%			
		3. <u>Meander Pool Condition</u>	1. <u>Depth</u> : Sufficient (Max Pool Depth: Mean Bankfull Depth $\geq$ 1.6)	5	5			100%			
	4. <u>Thalweg Position</u>	1. Thalweg centering at upstream of meander bend (Run)	2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream rifle and head of downstream rifle)	61	61			100%			
			1. Thalweg centering at upstream of meander bend (Run)	57	57			100%			
		2. Thalweg centering at downstream of meander (Glide)	1. Thalweg centering at upstream of meander bend (Run)	57	57			100%			
			2. Thalweg centering at downstream of meander (Glide)	57	57			100%			
	2. Bank	1. <u>Scoured/Eroding</u>	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			3	15	99.6%	N/A	N/A	N/A
		2. <u>Undercut</u>	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	N/A	N/A	N/A
3. <u>Mass Wasting</u>		Bank slumping, calving, or collapse			0	0	100%	N/A	N/A	N/A	
			<b>Totals</b>		3	15	99.6%	N/A	N/A	N/A	
3. Engineered Structures	1. <u>Overall Integrity</u>	Structures physically intact with no dislodged boulders or logs.	12	12			100%				
	2. <u>Grade Control</u>	Grade control structures exhibiting maintenance of grade across the sill.	12	12			100%				
	2a. <u>Piping</u>	Structures lacking any substantial flow underneath sills or arms.	12	12			100%				
	3. <u>Bank Protection</u>	Bank erosion within the structures extent of influence does not exceed 15%. (See guidance for this table in EEP monitoring guidance document)	12	12			100%				
	4. <u>Habitat</u>	Pool forming structures maintaining - Max Pool Depth : Mean Bankfull Depth ratio $\geq$ 1.6 Rootwads/logs providing some cover at base-flow.	12	12			100%				

**Table 6** Vegetation Condition Assessment

Planted Acreage 12.35

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	0.05 acres	polygons filled with orange dots and x's	6	0.48	3.9%
2. Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	N/A	N/A	N/A	N/A	N/A
<b>Total</b>						
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	N/A	Pattern and Color	N/A	N/A	N/A
<b>Cumulative Total</b>						

Easement Acreage 15.94

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern	Areas or points (if too small to render as polygons at map scale).	1000 SF	Pattern and Color	N/A	N/A	N/A
5. Easement Encroachment Areas	Areas or points (if too small to render as polygons at map scale).	none	Pattern and Color	N/A	N/A	N/A

**Figures 3.1 - 3.14. Vegetation Plot Photos and Problem Areas**



**3.1 Vegetation Plot 1**



**3.2 Vegetation Plot 2**



**3.3 Vegetation Plot 3**



**3.4 Vegetation Plot 4**





**3.5 Vegetation Plot 5**



**3.6 Vegetation Plot 6**



**3.7 Vegetation Plot 7**



**3.8 Vegetation Plot 8**



**3.9 Vegetation Plot 9**



**3.10 Bare area STA 25+00**



**3.11 Bare area adjacent to XS-10**



**3.12 Minor gully near STA 19+00**





**3.13 Gully on left bank at STA 34+00**




**3.14 Gully on right bank at STA 34+50**




**Appendix D. Stream Survey Data**

**Figure 4.1, XS-1 Riffle**

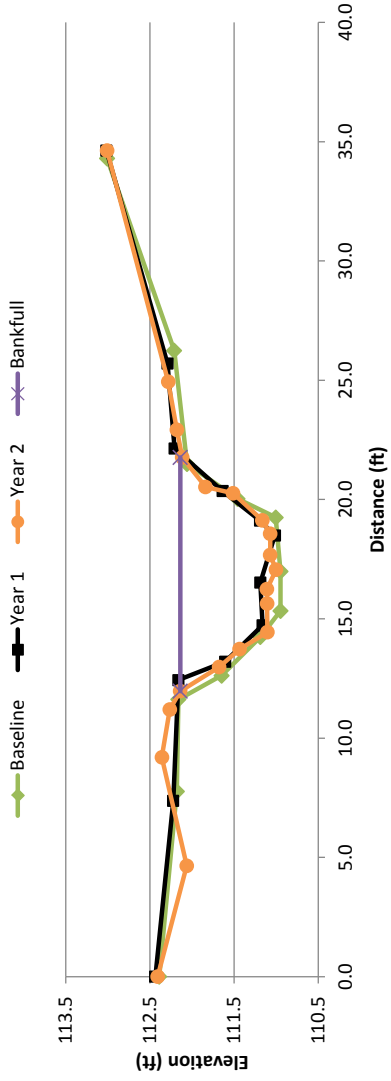

Dimension	Cross Section 1 (Riffle)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.7	9.6	9.6			
Floodprone Width (ft)	195.2	195.2	195.2			
Bankfull Mean Depth (ft)	0.8	0.8	0.7			
Bankfull Max Depth (ft)	1.1	1.1	1.1			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	7.7	7.3	6.8			
Bankfull Width/Depth Ratio	12.2	12.6	13.5			
Bankfull Entrenchment Ratio	20.2	20.3	20.3			
Bankfull Bank Height Ratio	1.0	1.0	1.0			


**Figure 4.2, XS-2 Pool**

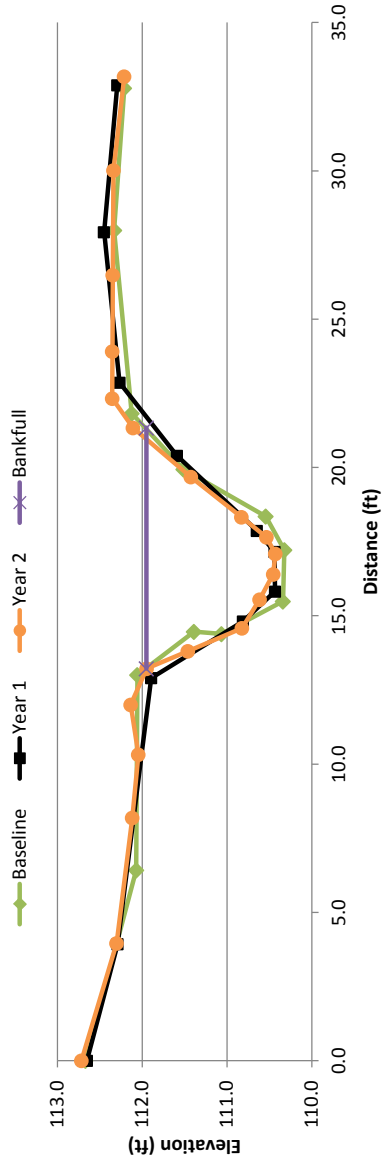

Dimension	Cross Section 2 (Pool)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	8.6	8.6	7.80			
Floodprone Width (ft)						
Bankfull Mean Depth (ft)	1.0	0.9	1.00			
Bankfull Max Depth (ft)	1.7	1.5	1.50			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.8	7.3	7.30			
Bankfull Width/Depth Ratio						
Bankfull Entrenchment Ratio						
Bankfull Bank Height Ratio						




**Figure 4.3, XS-3 Riffle**

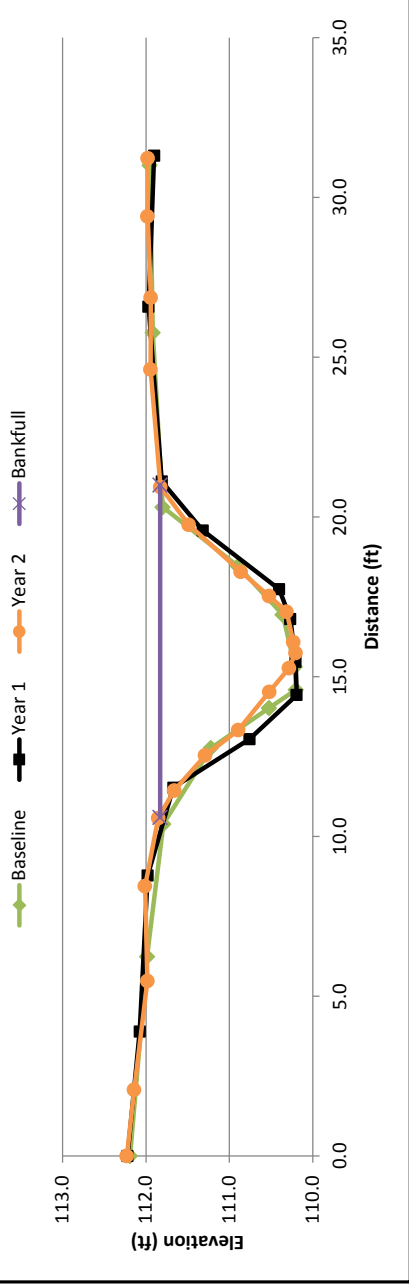


Dimension	Cross Section 3 (Riffle)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.9	9.2	10.40			
Floodprone Width (ft)	126.3	126.3	126.30			
Bankfull Mean Depth (ft)	0.9	1.0	0.90			
Bankfull Max Depth (ft)	1.6	1.5	1.60			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.8	8.7	9.00			
Bankfull Width/Depth Ratio	11.1	9.6	12.10			
Bankfull Entrenchment Ratio	12.8	13.7	12.20			
Bankfull Bank Height Ratio	1.0	1.0	1.00			

**Figure 4.4, XS-4 Pool**

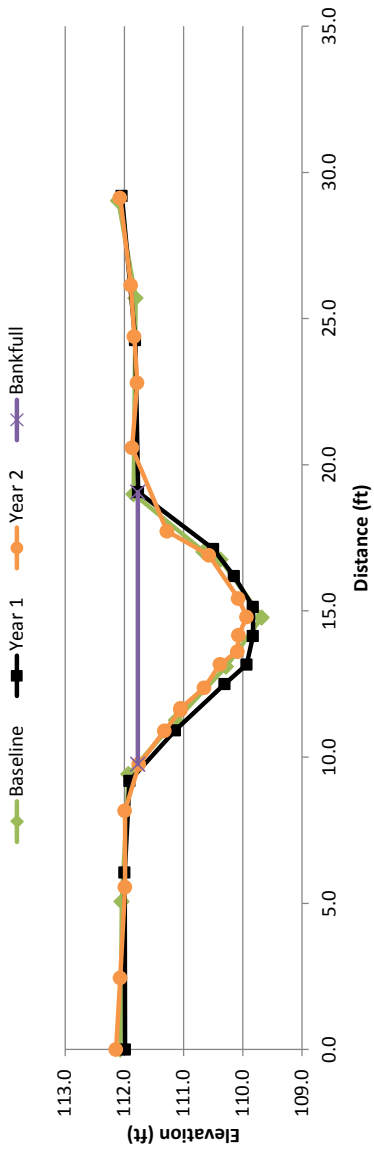

Dimension	Cross Section 4 (Pool)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.4	9.8	10.20			
Floodprone Width (ft)						
Bankfull Mean Depth (ft)	1.2	1.2	0.90			
Bankfull Max Depth (ft)	2.2	1.9	1.80			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	10.9	11.4	9.40			
Bankfull Width/Depth Ratio						
Bankfull Entrenchment Ratio						
Bankfull Bank Height Ratio						


**Figure 4.5, XS-5 Riffle**

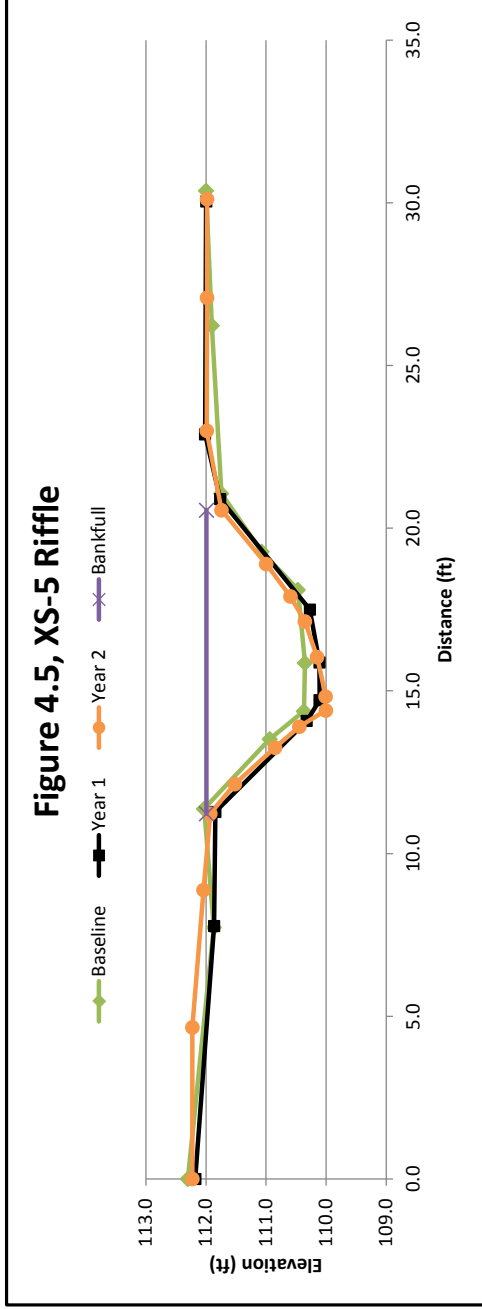


Dimension	Cross Section 5 (Riffle)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.1	10.2	8.90			
Floodprone Width (ft)	182.9	182.9	182.90			
Bankfull Mean Depth (ft)	0.9	1.0	1.00			
Bankfull Max Depth (ft)	1.4	1.7	1.70			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.4	10.7	9.10			
Bankfull Width/Depth Ratio	10.0	9.8	8.70			
Bankfull Entrenchment Ratio	20.0	17.9	20.50			
Bankfull Bank Height Ratio	1.0	1.0	1.00			



**Figure 4.6, XS-6 Pool**

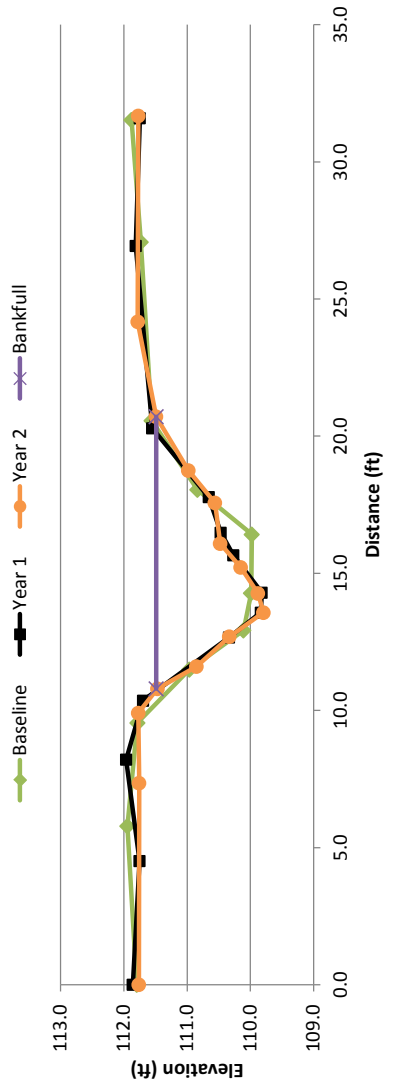

Dimension	Cross Section 6 (Pool)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	10.5	9.7	9.80			
Floodprone Width (ft)						
Bankfull Mean Depth (ft)	1.0	1.0	0.90			
Bankfull Max Depth (ft)	1.6	1.7	1.70			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	10.1	9.3	8.70			
Bankfull Width/Depth Ratio						
Bankfull Entrenchment Ratio						
Bankfull Bank Height Ratio						

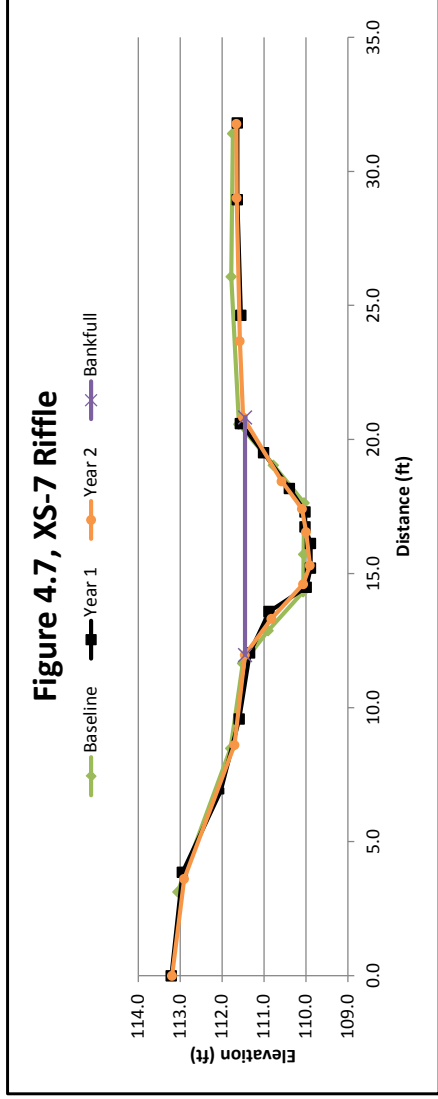


\*Baseline cross-section was not started on left pin


Dimension	Cross Section 7 (Riffle)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	8.8	8.1	8.70			
Floodprone Width (ft)	162.2	162.2	162.20			
Bankfull Mean Depth (ft)	1.0	0.9	0.90			
Bankfull Max Depth (ft)	1.5	1.4	1.60			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.7	7.0	8.00			
Bankfull Width/Depth Ratio	8.8	9.4	9.60			
Bankfull Entrenchment Ratio	18.5	19.9	18.60			
Bankfull Bank Height Ratio	1.0	1.0	1.00			



**Figure 4.8, XS-8 Pool**

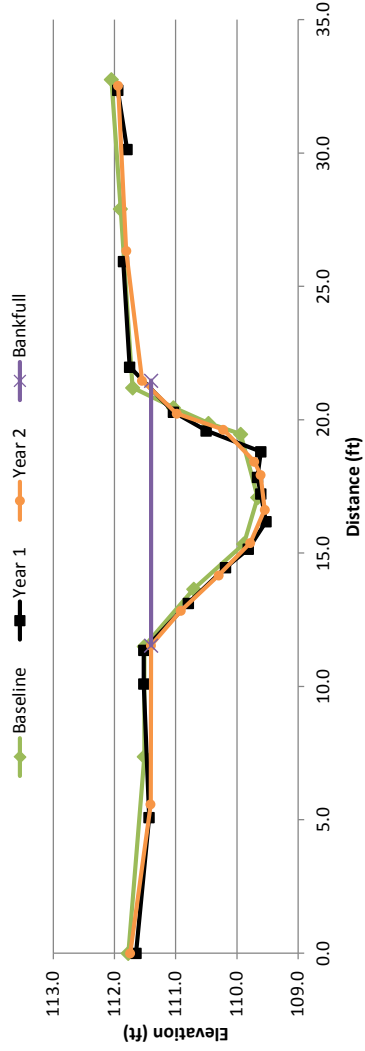


Dimension	Cross Section 8 (Pool)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.5	10.0	9.60			
Floodprone Width (ft)						
Bankfull Mean Depth (ft)	1.2	1.2	1.10			
Bankfull Max Depth (ft)	1.9	2.0	1.90			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	11.1	11.9	10.80			
Bankfull Width/Depth Ratio						
Bankfull Entrenchment Ratio						
Bankfull Bank Height Ratio						

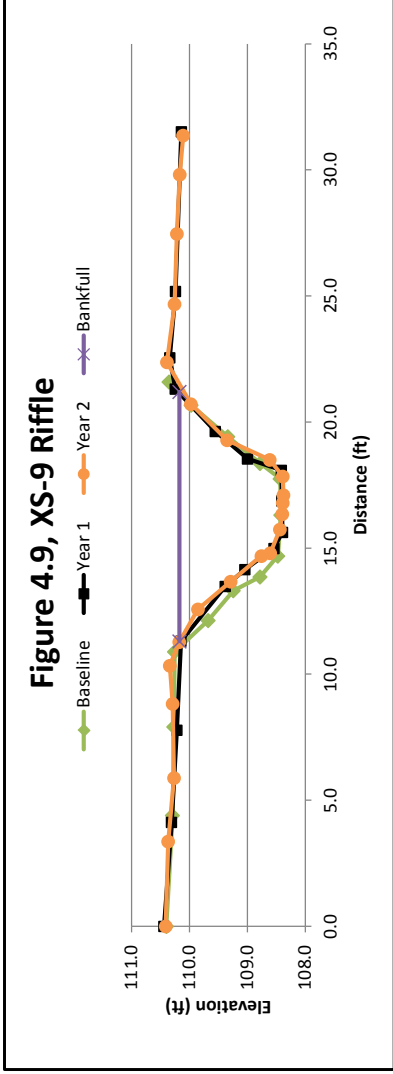

Dimension	Cross Section 9 (Riffle)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	10.5	9.9	9.8			
Floodprone Width (ft)	219.0	219.0	219.0			
Bankfull Mean Depth (ft)	1.1	1.0	1.0			
Bankfull Max Depth (ft)	1.8	1.8	1.7			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	12.0	9.9	9.7			
Bankfull Width/Depth Ratio	9.1	9.9	9.9			
Bankfull Entrenchment Ratio	20.9	22.1	22.3			
Bankfull Bank Height Ratio	1.0	1.0	1.0			



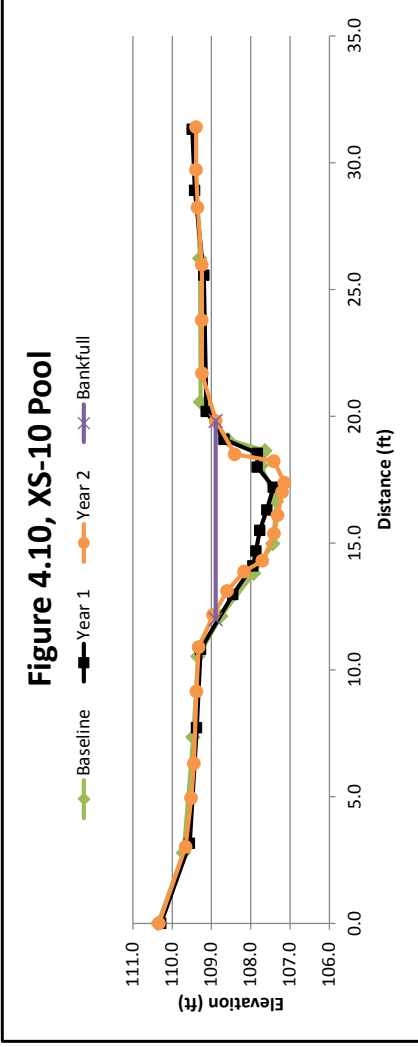

Dimension	Cross Section 10 (Pool)					
	Base	MY1	MY2	MY3	MY4	MY5
<b>Based on fixed baseline bankfull elevation</b>						
Bankfull Width (ft)	9.8	9.2	10.50			
Floodprone Width (ft)						
Bankfull Mean Depth (ft)	1.2	1.0	1.00			
Bankfull Max Depth (ft)	1.9	1.7	2.10			
Bankfull Cross Sectional Area (ft <sup>2</sup> )	11.4	8.7	10.70			
Bankfull Width/Depth Ratio						
Bankfull Entrenchment Ratio						
Bankfull Bank Height Ratio						

**Table 8. Baseline Stream Data Summary**  
**UT to Millers Creek, DMS Project ID No. 95719**  
**UT to Millers Creek: 2,709 LF**

Parameter	Regional Curve	Pre-Existing Condition	Reference - Wildcat Branch	Reference - UT Brick Bound Swamp	Design	As-built/Baseline					
						Min	Mean	Med	Max	SD	n
<b>Dimension and Substrate - Riffle</b>											
	Eq.	Mean	Mean	Mean	Mean	Min	Mean	Med	Max	SD	n
Bankfull Width (ft)		9.7	8.2	6.1	8.8	8.8	9.6	9.7	10.5	0.7	5
Floodprone Width (ft)		12.3	130.0	24.5	125.0	126.3	177.1	182.9	219.0	35.1	5
Bankfull Mean Depth (ft)		0.75	1.03	0.50	0.92	0.8	0.9	0.9	1.1	0.1	5
Bankfull Max Depth (ft)		1.1	1.6	1.0	1.4	1.1	1.5	1.5	1.8	0.3	5
Bankfull Cross Sectional Area (ft <sup>2</sup> )		7.2	8.5	3.1	8.3	7.7	9.1	8.7	12.0	1.7	5
Width/Depth Ratio		12.9	8.0	12.2	9.5	8.8	10.2	10.0	12.2	1.4	5
Entrenchment Ratio		1.3	15.9	4.0	14.3	11.9	13.1	12.9	14.3	0.9	5
Bank Height Ratio		4.83	1.09	1.00	1.00	1.0	1.0	1.0	1.0	0.0	5
d50 (mm)		sand	sand	sand	sand						
<b>Profile</b>											
Riffle Length (ft)						8.6	21.9	22.8	33.6	9.0	7
Riffle Slope (ft/ft)		Channelized	0.0022	0.0012	0.0007	0.0039	0.0069	0.0075	0.0096	0.0019	7
Pool Length (ft)						9.1	27.0	25.7	53.9	11.6	61
Pool Max depth (ft)		Channelized	1.75	1.25	1.75	1.60	1.86	1.90	2.20	0.23	5
Pool Spacing (ft)		Channelized	14.0 - 16.6	15.29 - 27.81	20.1 - 84.9	12.5	41.8	40.3	96.3	18.4	63
Pool Cross Sectional Area (ft <sup>2</sup> )						8.80	10.46	10.90	11.40	1.05	5
<b>Pattern</b>											
Channel Beltwidth (ft)		Channelized	13.8 - 19.4	13.8 - 19.4	17.5 - 52.5						
Radius of Curvature (ft)		Channelized	10.9 - 15.3	5.0 - 9.0	20.1 - 22.8						
Rc: Bankfull Width (ft/ft)		Channelized	1.3 - 1.9	0.9 - 1.5	2.3 - 2.6						
Meander Wavelength (ft)		Channelized	22.5 - 29.0	23.0 - 29.0	14.0 - 56.0						
Meander Width Ratio		Channelized	1.7 - 2.4	2.3 - 3.2	2.0 - 6.0						
<b>Substrate, bed and transport parameters</b>											
Ri% / P%										33/67	
SC% / Sa% / G% / C% / B% / Be%											
d16 / d35 / d50 / d84 / d95/ d <sub>p</sub> <sup>95</sup> / d <sub>p</sub> <sup>99</sup> (mm)											
Reach Shear Stress (competency) lb/ft <sup>2</sup>											
Max part size (mm) mobilized at bankfull											
Unit Stream Power (transport capacity) lbs/ft.s		0.01			0.01					0.02	
<b>Additional Reach Parameters</b>											
Drainage Area (SM)		0.37	0.44	0.11	0.37						
Impervious cover estimate (%)											
Rosgen Classification		G-F/5	E5	E5	E5				E5		
Bankfull Velocity (fps)			1.00	0.97	0.80						
Bankfull Discharge (cfs)		8.4	8.5	3.0	8.4						
Valley length (ft)		2126			2126				2126		
Channel Thalweg length (ft)		2339			2679				2709		
Sinuosity (ft)		1.10	1.15	1.35	1.26				1.27		
Water Surface Slope (Channel) (ft/ft)		0.0011	0.0024	0.0016	0.0005				0.0005		
BF slope (ft/ft)					0.0005				0.0005		
Bankfull Floodplain Area (acres)											
Proportion over wide (%)											
Entrenchment Class (ER Range)											
Incision Class (BHR Range)											
BEHI VL% / L% / M% / H% / VH% / E%											
Channel Stability or Habitat Metric											
Biological or Other											



**Table 9. Morphology and Hydraulic Monitoring Summary (Dimensional Parameters - Cross Section)**  
**UT to Millers Creek (DMS Project No. 95719)**  
**UT to Millers Creek: 2,709 LF**

Dimension	Cross Section 1 (Riffle)							Cross Section 2 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
<b>Based on fixed baseline bankfull elevation</b>														
Bankfull Width (ft)	9.7	9.6	9.6					8.6	8.6	7.8				
Floodprone Width (ft)	195.2	195.2	195.2											
Bankfull Mean Depth (ft)	0.8	0.8	0.7					1.0	0.9	1.0				
Bankfull Max Depth (ft)	1.1	1.1	1.1					1.7	1.5	1.5				
Bankfull Cross Sectional Area (ft <sup>2</sup> )	7.7	7.3	6.8					8.8	7.3	7.3				
Bankfull Width/Depth Ratio	12.2	12.6	13.5											
Bankfull Entrenchment Ratio	20.2	20.3	20.3											
Bankfull Bank Height Ratio	1.0	1.0	1.0											
Dimension	Cross Section 3 (Riffle)							Cross Section 4 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
<b>Based on fixed baseline bankfull elevation</b>														
Bankfull Width (ft)	9.9	9.2	10.4					9.4	9.8	10.2				
Floodprone Width (ft)	126.3	126.3	126.3											
Bankfull Mean Depth (ft)	0.9	1.0	0.9					1.2	1.2	0.9				
Bankfull Max Depth (ft)	1.6	1.5	1.6					2.2	1.9	1.8				
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.8	8.7	9.0					10.9	11.4	9.4				
Bankfull Width/Depth Ratio	11.1	9.6	12.1											
Bankfull Entrenchment Ratio	12.8	13.7	12.2											
Bankfull Bank Height Ratio	1.0	1.0	1.0											
Dimension	Cross Section 5 (Riffle)							Cross Section 6 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
<b>Based on fixed baseline bankfull elevation<sup>1</sup></b>														
Bankfull Width (ft)	9.1	10.2	8.9					10.5	9.7	9.8				
Floodprone Width (ft)	182.9	182.9	182.9											
Bankfull Mean Depth (ft)	0.9	1.0	1.0					1.0	1.0	0.9				
Bankfull Max Depth (ft)	1.4	1.7	1.7					1.6	1.7	1.7				
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.4	10.7	9.1					10.1	9.3	8.7				
Bankfull Width/Depth Ratio	10.0	9.8	8.7											
Bankfull Entrenchment Ratio	20.0	17.9	20.5											
Bankfull Bank Height Ratio	1.0	1.0	1.0											
Dimension	Cross Section 7 (Riffle)							Cross Section 8 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
<b>Based on fixed baseline bankfull elevation</b>														
Bankfull Width (ft)	8.8	8.1	8.7					9.5	10.0	9.6				
Floodprone Width (ft)	162.2	162.2	162.2											
Bankfull Mean Depth (ft)	1.0	0.9	0.9					1.2	1.2	1.1				
Bankfull Max Depth (ft)	1.5	1.4	1.6					1.9	2.0	1.9				
Bankfull Cross Sectional Area (ft <sup>2</sup> )	8.7	7.0	8.0					11.1	11.9	10.8				
Bankfull Width/Depth Ratio	8.8	9.4	9.6											
Bankfull Entrenchment Ratio	18.5	19.9	18.6											
Bankfull Bank Height Ratio	1.0	1.0	1.0											
Dimension	Cross Section 9 (Riffle)							Cross Section 10 (Pool)						
	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
<b>Based on fixed baseline bankfull elevation</b>														
Bankfull Width (ft)	10.5	9.9	9.8					9.8	9.2	10.5				
Floodprone Width (ft)	219.0	219.0	219.0											
Bankfull Mean Depth (ft)	1.1	1.0	1.0					1.2	1.0	1.0				
Bankfull Max Depth (ft)	1.8	1.8	1.7					1.9	1.7	2.1				
Bankfull Cross Sectional Area (ft <sup>2</sup> )	12.0	9.9	9.7					11.4	8.7	10.7				
Bankfull Width/Depth Ratio	9.1	9.9	9.9											
Bankfull Entrenchment Ratio	20.9	22.1	22.3											
Bankfull Bank Height Ratio	1.0	1.0	1.0											





**Appendix E. Hydrologic Data**

**Table 11. Verification of Bankfull Events**

Date	Crest Gauge Info		Gauge Reading (ft)	Gauge Elevation (ft)	Crest Elevation (ft)	Bankfull Elevation (ft)	Height above Bankfull (ft)
	Site	Sta.					
7/14/2015	1	10+62	0.42	111.46	111.88	112.07	-0.19
7/14/2015	2	37+03	2.29	107.16	109.45	107.71	1.74
10/19/2015	1	10+62	1.50	111.46	112.96	112.07	0.89
4/27/2016	1	10+62	1.88	111.46	113.34	112.07	1.26
4/27/2016	2	37+03	3.70	107.16	110.87	107.71	3.15
10/10/2016	1	10+62	2.79	111.46	114.25	112.07	2.18
10/10/2016	2	37+03	3.43	107.16	110.59	107.71	2.88
10/10/2016	N/A	Approx. 20+00	Visual	Visual	Visual	Visual	Visual

**Figures 5.1 - 5.4 Crest Gauge Photos**



**5.1 Crest Gauge 2 (4/27/2016)**



**5.2 Crest Gauge 1 (10/10/2016)**



**5.3 Crest Gauge 2 (10/10/2016)**



**5.4 Overbank flow (10/10/2016)**


**Table 12. Summary of Gauge Hydrologic Data**

<b>Gauge Number</b>	<b>Wetland Community Type</b>	<b>Target Hydroperiod</b>	<b>Percentage of Growing Season Year 1</b>	<b>Longest Number Of Consecutive Days Meeting Wetland Hydrology Criteria During Year 1 Growing Season</b>	<b>Percentage of Growing Season Year 2</b>	<b>Longest Number Of Consecutive Days Meeting Wetland Hydrology Criteria During Year 2 Growing Season</b>
1	Riparian Bottomland Hardwood	12.5%	43	130	23	69
2	Riparian Bottomland Hardwood	12.5%	53	161	49	149
3	Riparian Bottomland Hardwood	12.5%	10	30	21	65
4	Headwater Riparian (Zero Order)	10%	70	212	100	304
5	Riparian Bottomland Hardwood	12.5%	32	97	49	149
6	Riparian Bottomland Hardwood	12.5%	52	158	48	146
Reference	Headwater Riparian (Zero Order)	10%	39	118	46	141
Reference	Riparian Bottomland Hardwood	12.5%	36	108	26	79



**Figure 6.0-8. Monthly Precipitation Data and Wetland Gauge Data**

**Figure 6.0 UT to Millers Creek  
Monthly Precipitation 2016 (30th/70th Percentiles)**

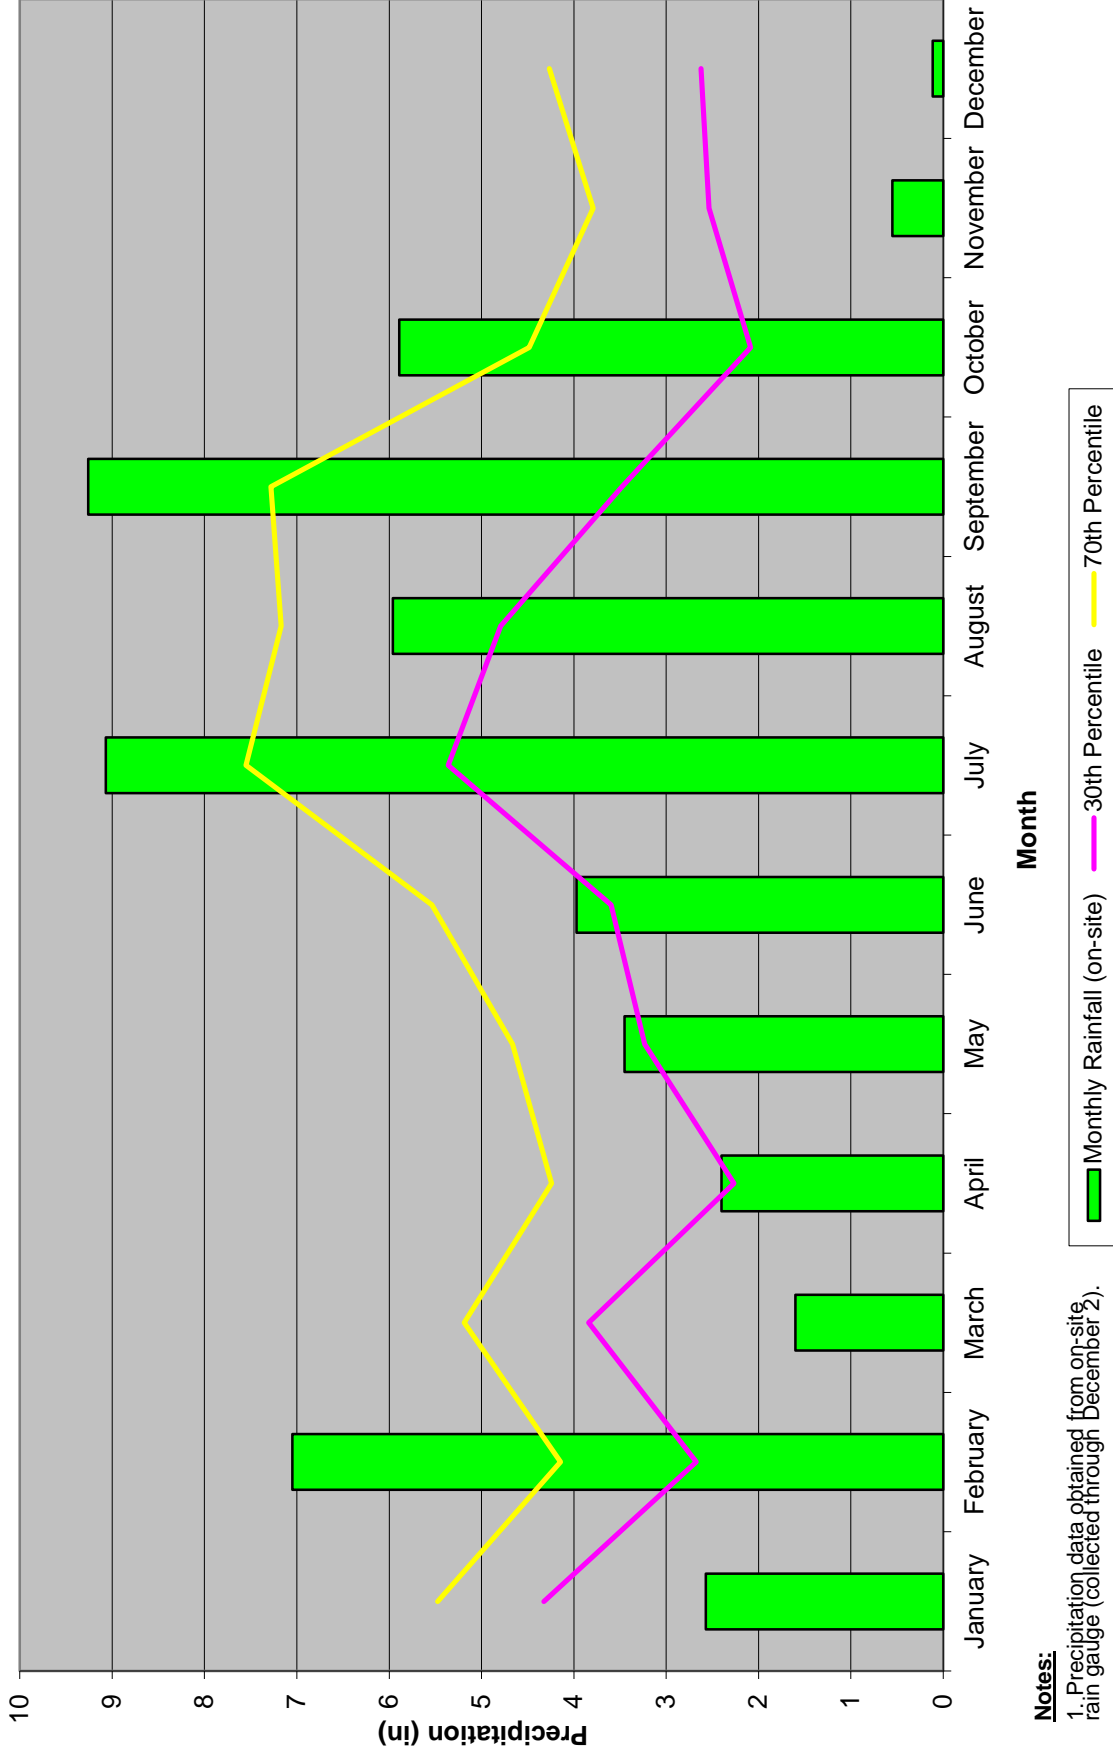

**Notes:**

1. Precipitation data obtained from on-site rain gauge (collected through December 2).
2. 30th and 70th percentiles calculated from long-term climatic data ([www.wcc.nrcs.usda.gov](http://www.wcc.nrcs.usda.gov))

Figure 6.1 Gauge 1 (A282F9D)

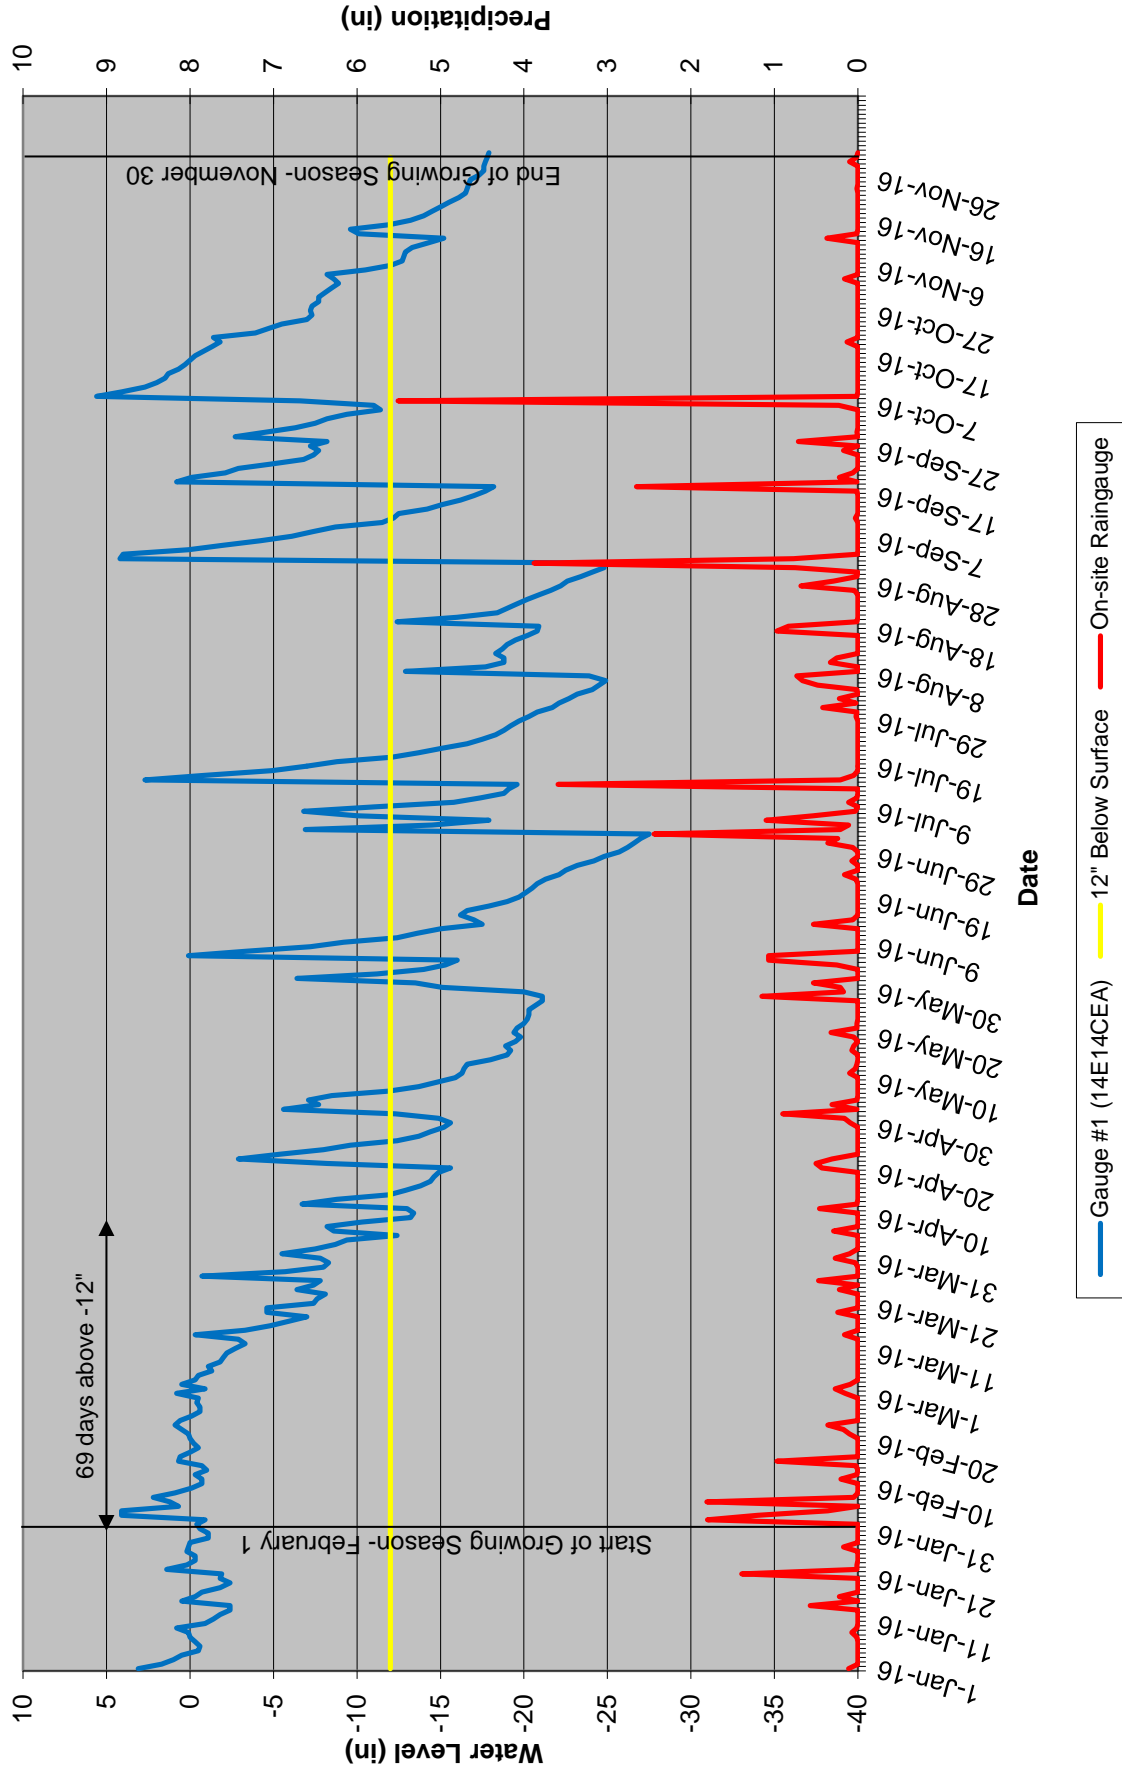




Figure 6.2 Gauge #2 (A2873A5)

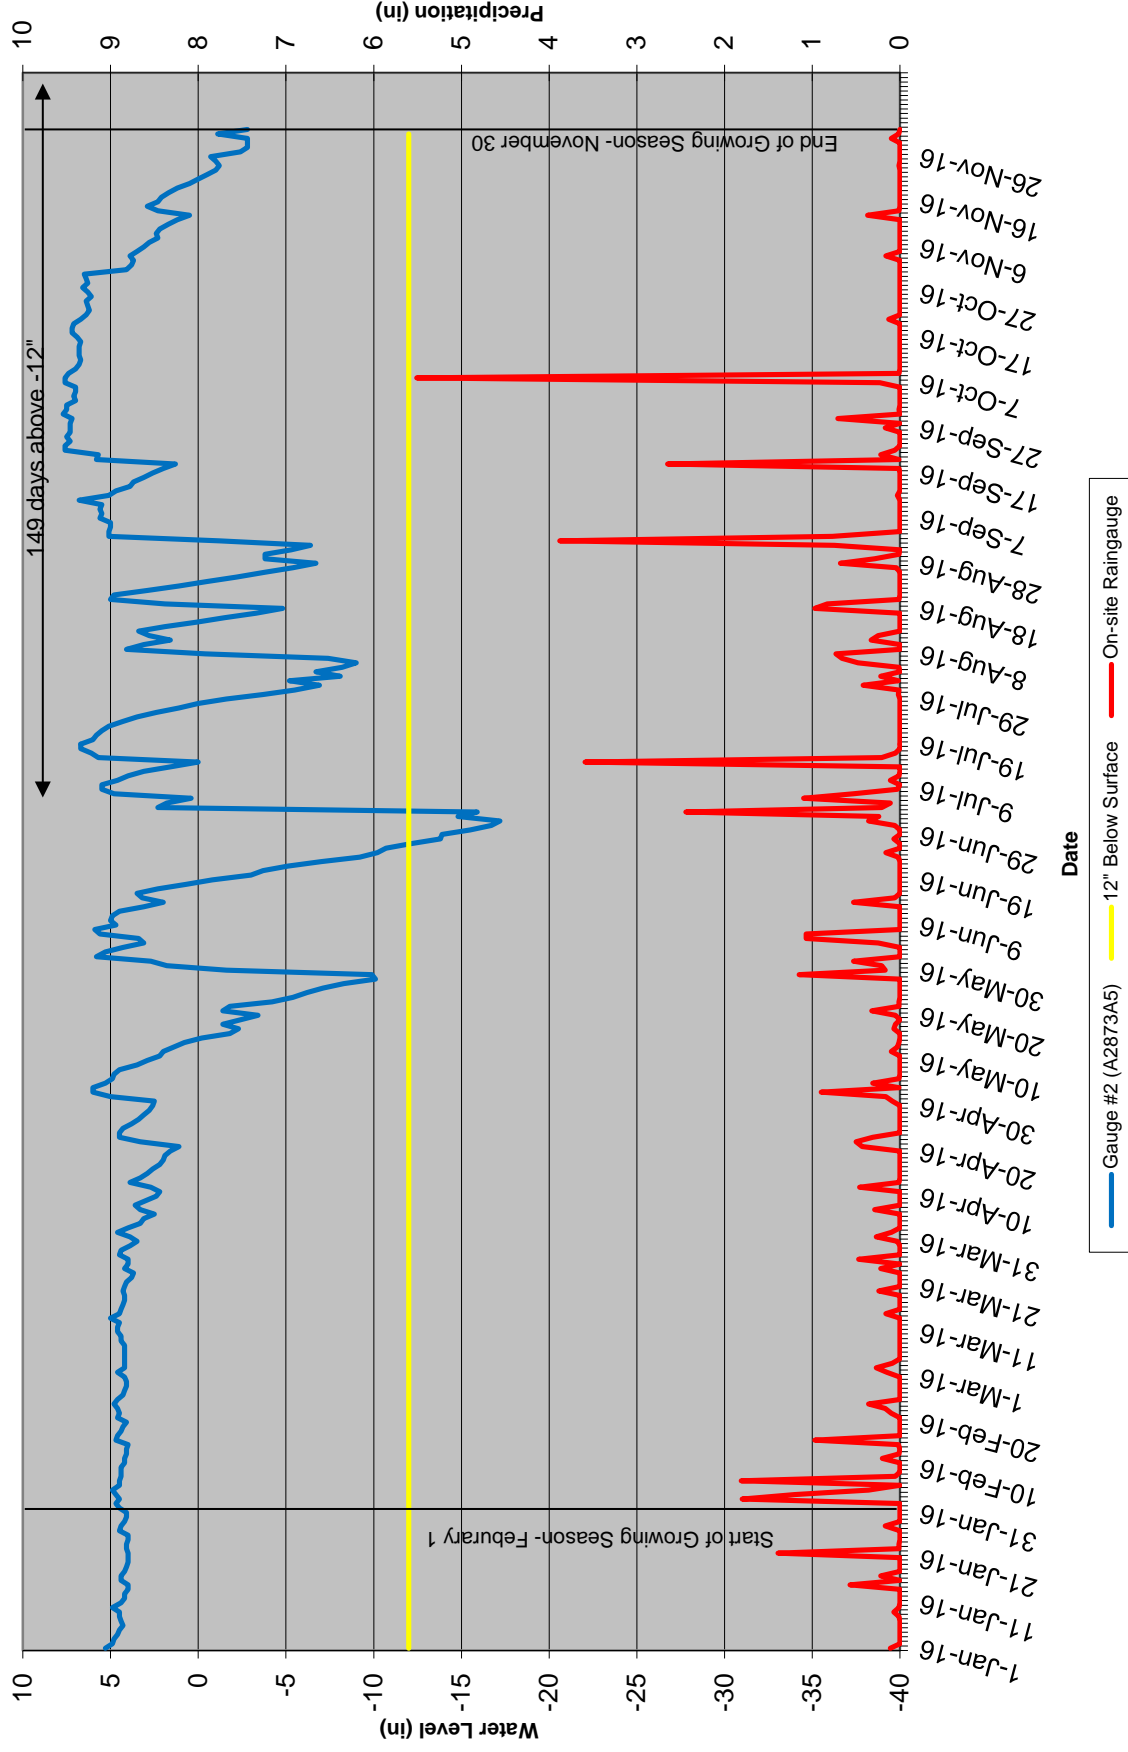
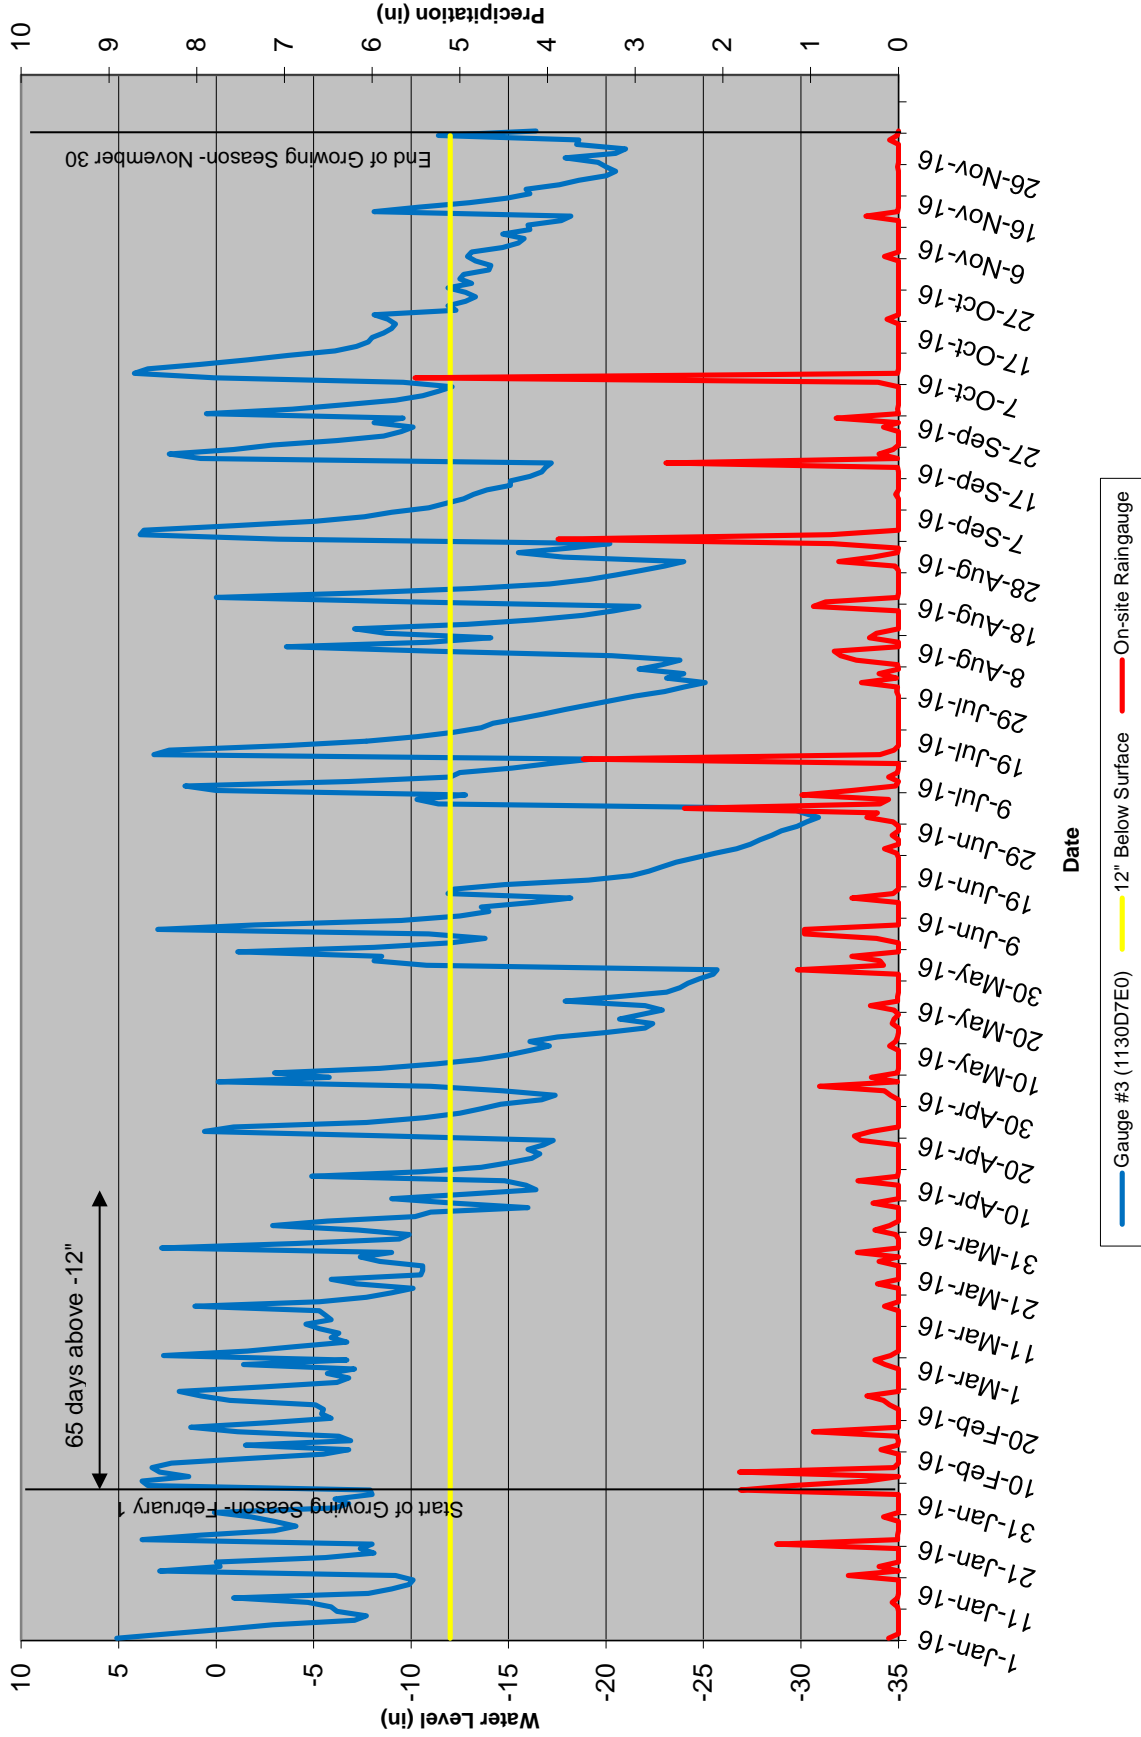


Figure 6.3 Gauge 3 (1130D7ED)



**Figure 6.4 Gauge 4 (14E194AD)**

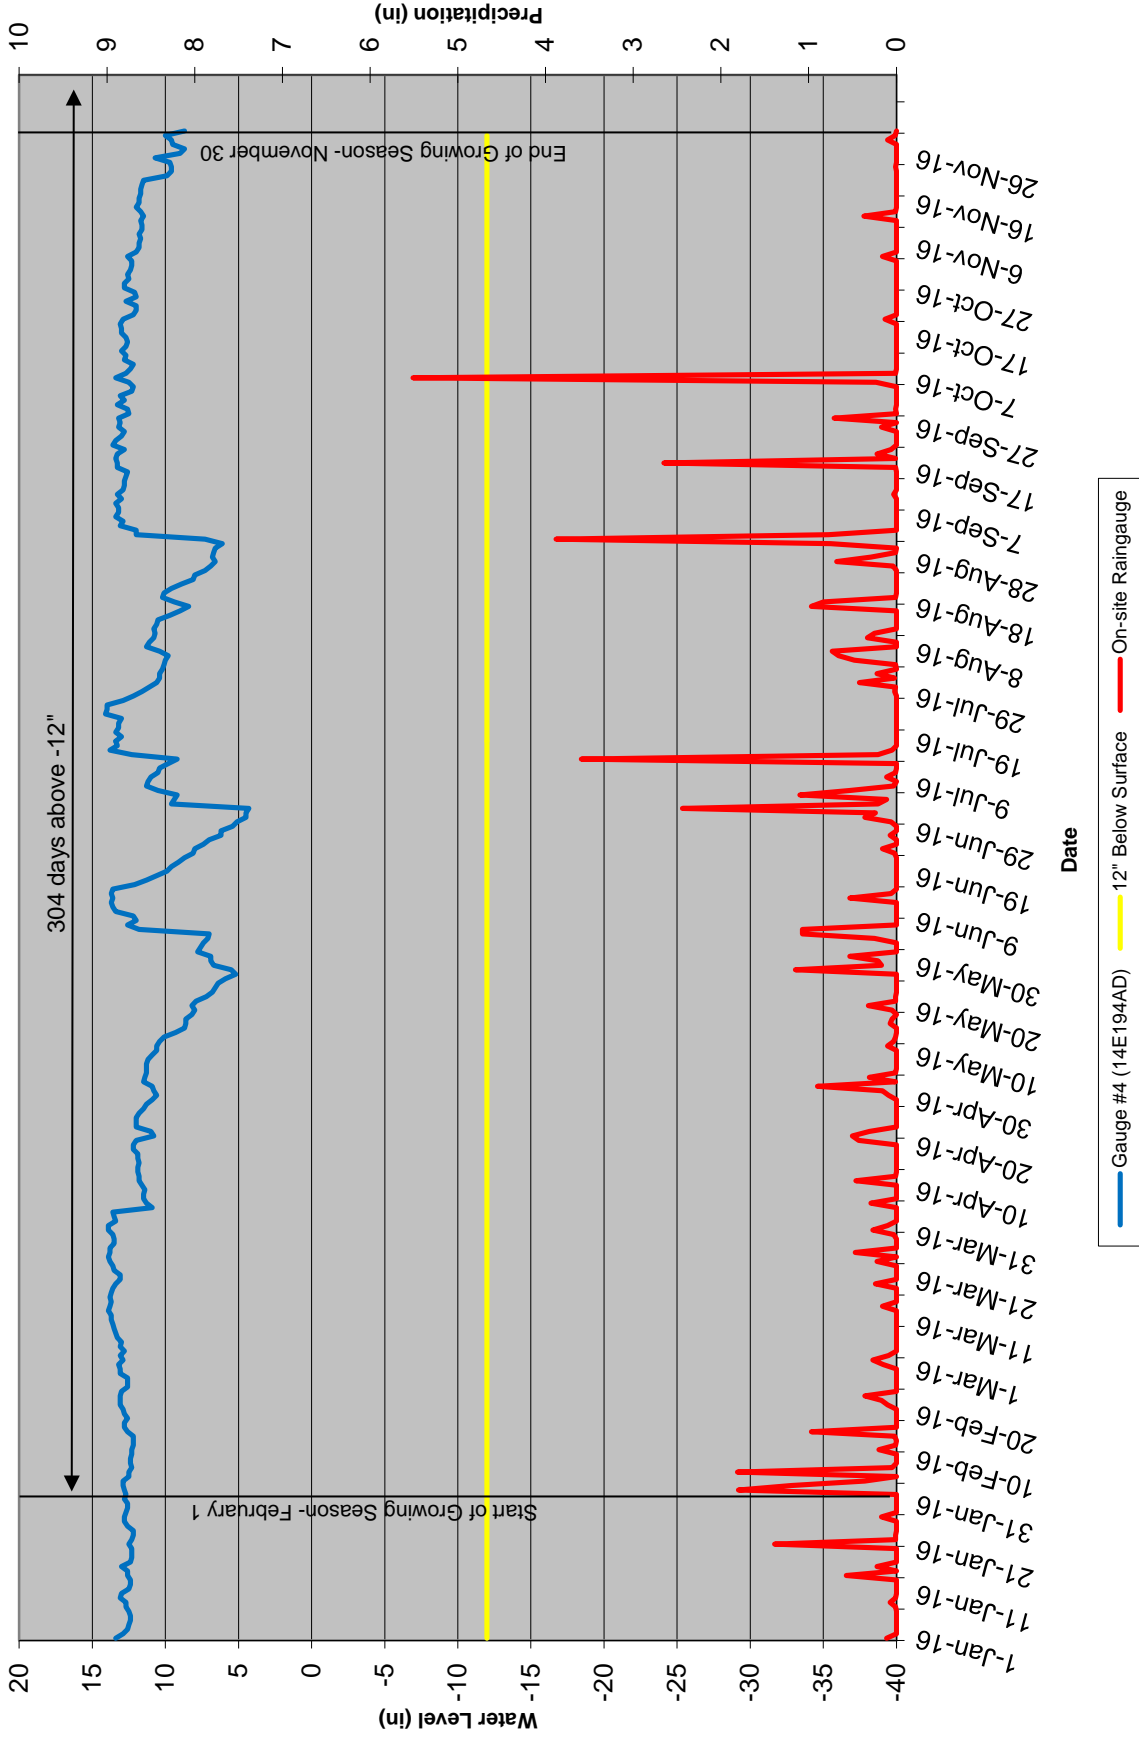




Figure 6.5 Gauge 5 (14E1ABFA)

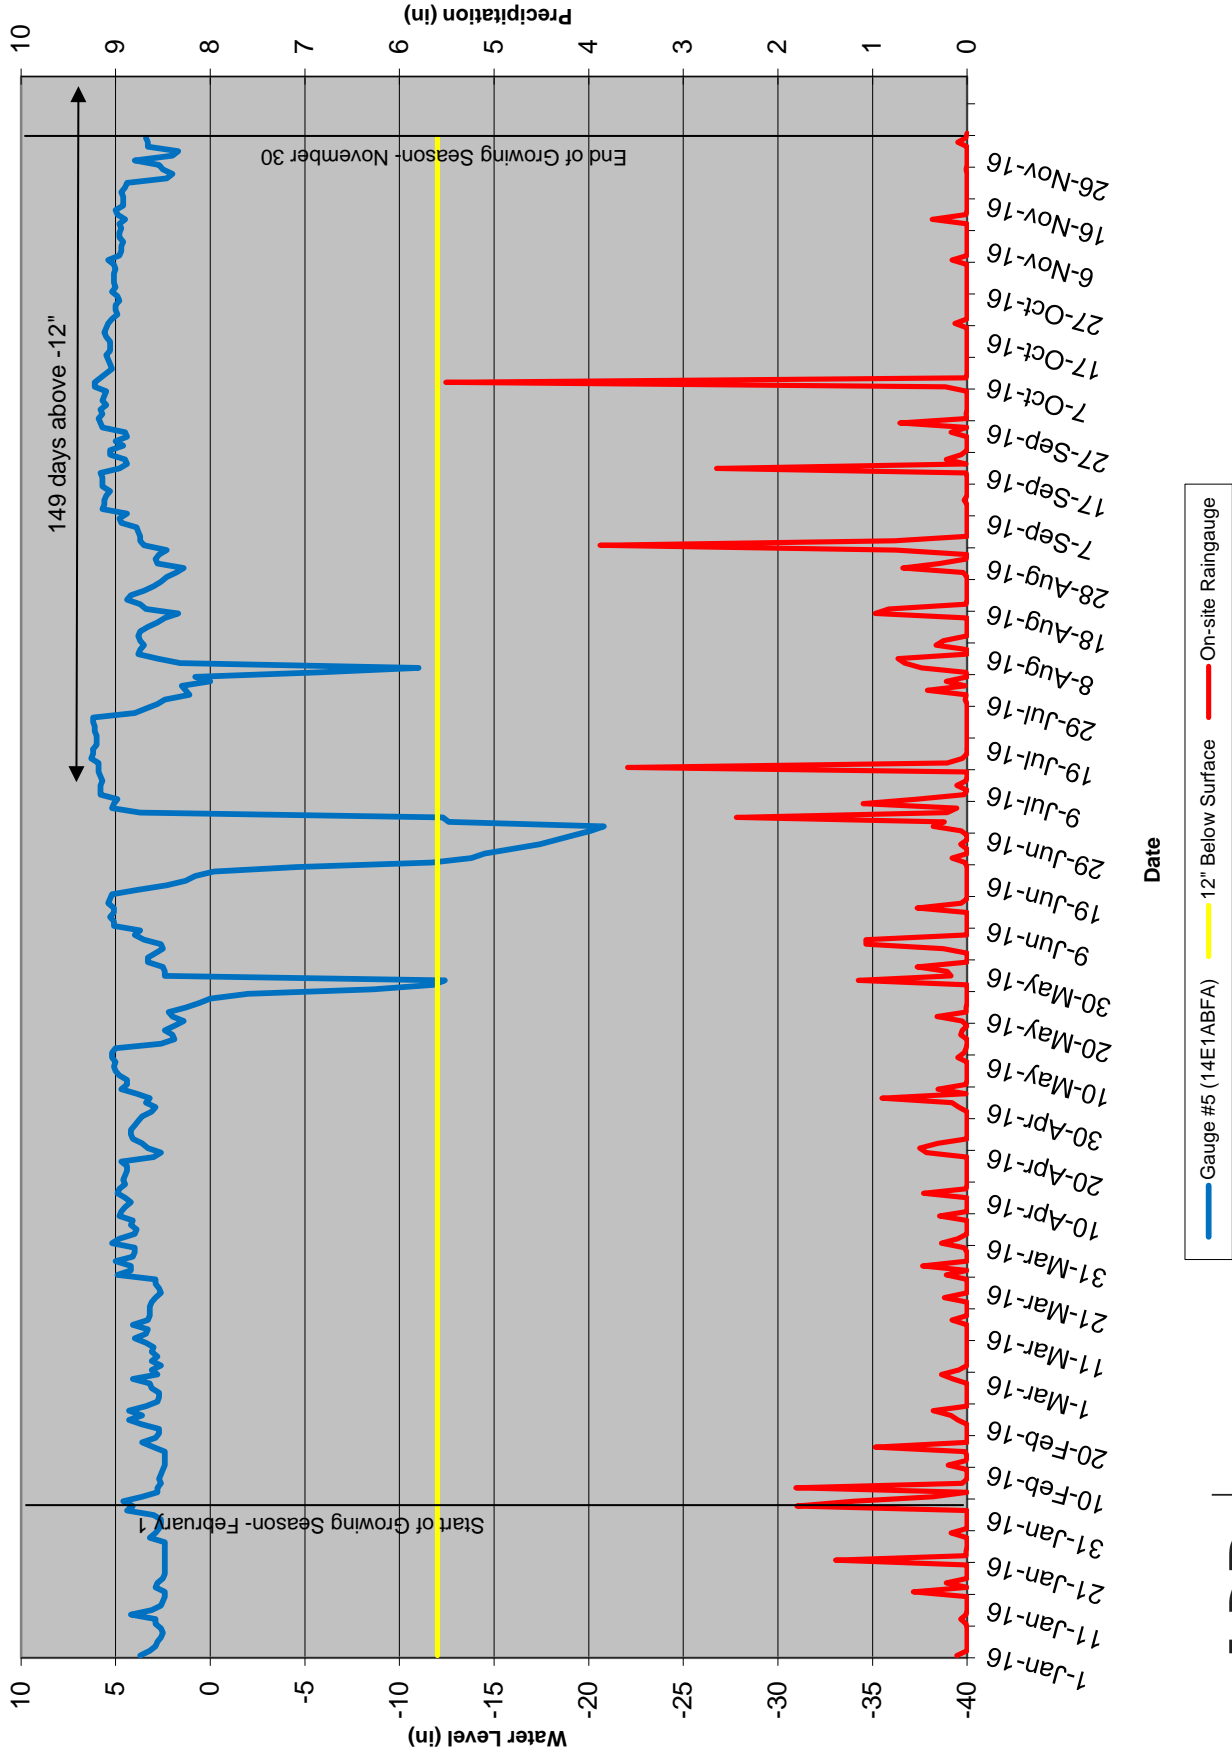


Figure 6.6 Gauge 6 (14E142FD)

