

Mitigation Project Name Aycok Springs Stream and Wetland
 DMS ID 96312
 River Basin Cape Fear
 Cataloging Unit 03030002

County Alamance
 Date Project Instituted 2/21/2014
 Date Prepared 5/22/2018

USACE Action ID 2014-01711
 NCDWR Permit No 2014-0335


Credit Release Milestone	Stream Credits						Wetland Credits							
	Scheduled Releases (Stream)	Warm	Cool	Cold	Anticipated Release Year (Stream)	Actual Release Date (Stream)	Scheduled Releases (Forested)	Riparian Riverine	Riparian Non-riverine	Non-riparian	Scheduled Releases (Coastal)	Coastal	Anticipated Release Year (Wetland)	Actual Release Date (Wetland)
Potential Credits (Mitigation Plan)		3,587,130						0.500						
Potential Credits (As-Built Survey)		3,581,131						0.500						
1 (Site Establishment)	N/A				N/A	N/A	N/A				N/A		N/A	N/A
2 (Year 0 / As-Built)	30%	1,074,339			2016	8/2/2016	30%	0.150			30%		2016	8/2/2016
3 (Year 1 Monitoring)	10%	358,113			2017	4/3/2017	10%	0.050			10%		2017	4/3/2017
4 (Year 2 Monitoring)	10%	358,113			2018	4/25/2018	10%	0.050			10%		2018	4/25/2018
5 (Year 3 Monitoring)	10%				2019		10%				10%		2019	
6 (Year 4 Monitoring)	10%				2020		10%				10%		2020	
7 (Year 5 Monitoring)	15%				2021		10%				10%		2021	
8 (Year 6 Monitoring)	N/A				2022		10%				10%		2022	
9 (Year 7 Monitoring)	N/A				2023		10%				10%		2023	
Stream Bankfull Standard	15%						N/A				N/A			
Total Credits Released to Date		1,790,565						0.250						

DEBITS (released credits only)

			Ratios	1.012256	1.5	2.5	5	1	3	2	5	1	3	2	5			
			Stream Restoration	Stream Enhancement	Stream Enhancement	Stream Preservation	Riparian Restoration	Riparian Creation	Riparian Enhancement	Riparian Preservation	Nonriparian Restoration	Nonriparian Creation	Nonriparian Enhancement	Nonriparian Preservation	Coastal Marsh Restoration	Coastal Marsh Creation	Coastal Marsh Enhancement	Coastal Marsh Preservation
As-Built Amounts (feet and acres)			3,359,000		657,000			0.500										
As-Built Amounts (mitigation credits)			3,318,331		262,800			0.500										
Percentage Released			50.0000%		50.0000%			50.0000%										
Released Amounts (feet / acres)			1,679,500		328,500			0.250										
Released Amounts (credits)			1,659,165		131,400			0.250										
NCDWR Permit	USACE Action ID	Project Name																
2013-0517	2013-00557	NCDOT TIP R-2413A/B - NC 68 Connector, Guilford County	846,280															
2013-0912	2013-01990	NCDOT TIP R-2612B - US 421 Improvements, Guilford County	161,440		187,100													
2013-0918	2005-21386	NCDOT TIP U-2525B/C - Greensboro Eastern Loop, Guilford County					0.150											
2013-0912	2013-01990	NCDOT TIP R-2612B - US 421 Improvements, Guilford County	308,406															
2013-0918	2005-21386	NCDOT TIP U-2525B/C - Greensboro Eastern Loop, Guilford County					0.050											
2013-0918	2005-21386	NCDOT TIP U-2525B/C - Greensboro Eastern Loop, Guilford County	363,394		131,400													
2017-1466	2009-02018	NCDOT TIP U-4734 - Division 9					0.050											
Remaining Amounts (feet / acres)			0.000		0.000			0.000										
Remaining Amounts (credits)			0.000		0.000			0.000										

Contingencies (if any): None

Aycock Springs



Signature of Wilmington District Official Approving Credit Release

9/6/18

Date

- 1 - For NCDMS, no credits are released during the first milestone
- 2 - For NCDMS projects, the second credit release milestone occurs automatically when the as-built report (baseline monitoring report) has been made available to the NCIRT by posting it to the NCDMS Portal, provided the following criteria have been met:
 - 1) Approval of the final Mitigation Plan
 - 2) Recordation of the preservation mechanism, as well as a title opinion acceptable to the USACE covering the property
 - 3) Completion of all physical and biological improvements to the mitigation site pursuant to the mitigation plan
 - 4) Receipt of necessary DA permit authorization or written DA approval for projects where DA permit issuance is not required
- 3 - A 15% reserve of credits is to be held back until the bankfull event performance standard has been met

YEAR 3 (2018) MONITORING REPORT
AYCOCK SPRINGS
STREAM AND WETLAND MITIGATION SITE
ALAMANCE COUNTY, NORTH CAROLINA
DMS PROJECT NO. 96312
FULL DELIVERY CONTRACT NO. 5791

CAPE FEAR RIVER BASIN
CATALOGING UNIT 03030002

Data Collection – May-October 2018



PREPARED FOR:

N.C. DEPARTMENT OF ENVIRONMENTAL QUALITY
DIVISION OF MITIGATION SERVICES
1601 MAIL SERVICE CENTER
RALEIGH, NORTH CAROLINA 27699-1601

January 2019

YEAR 3 (2018) MONITORING REPORT
AYCOCK SPRINGS
STREAM AND WETLAND MITIGATION SITE
ALAMANCE COUNTY, NORTH CAROLINA
DMS PROJECT NO. 96312
FULL DELIVERY CONTRACT NO. 5791

CAPE FEAR RIVER BASIN
CATALOGING UNIT 03030002

Data Collection – May-October 2018



PREPARED BY:

RESTORATION SYSTEMS, LLC
1101 HAYNES STREET, SUITE 211
RALEIGH, NORTH CAROLINA 27604

AND

AXIOM ENVIRONMENTAL, INC.
218 SNOW AVENUE
RALEIGH, NORTH CAROLINA 27603

January 2019

Table of Contents

1.0	PROJECT SUMMARY	1
2.0	METHODOLOGY	6
2.1	Streams.....	6
2.2	Vegetation.....	7
2.3	Wetland Hydrology.....	8
2.4	Biotic Community Change.....	8
3.0	REMEDIAL ACTION PLAN	9
3.1	Stream	9
3.2	Vegetation.....	9
4.0	REFERENCES	9

Appendices

APPENDIX A. PROJECT BACKGROUND DATA AND MAPS

Figure 1. Site Location

Table 1. Project Components and Mitigation Credits

Table 2. Project Activity and Reporting History

Table 3. Project Contacts Table

Table 4. Project Baseline Information and Attributes

APPENDIX B. VISUAL ASSESSMENT DATA

Figure 2. Current Conditions Plan View

Tables 5A-5E. Visual Stream Morphology Stability Assessment

Table 6. Vegetation Condition Assessment

Vegetation Monitoring Photographs

APPENDIX C. VEGETATION PLOT DATA

Table 7. Vegetation Plot Criteria Attainment

Table 8. CVS Vegetation Plot Metadata

Table 9. Total and Planted Stems by Plot and Species

Table 10. Supplemental Vegetation Transect Data

APPENDIX D. STREAM SURVEY DATA

Cross-section Plots

Table 11a-11e. Baseline Stream Data Summary

Table 12a-12f. Monitoring Data

APPENDIX E. HYDROLOGY DATA

Table 13. UT3 Channel Evidence

Stream Gauge Graph

Table 14. Verification of Bankfull Events

Groundwater Gauge Graphs

Table 15. Groundwater Hydrology Data

APPENDIX F. BENTHIC DATA

Results

Habitat Assessment Data Sheets

APPENDIX G. REMEDIAL ACTION PLAN

APPENDIX H. HERBICIDE APPLICATION FORMS

APPENDIX I. PHOTO LOG

1.0 PROJECT SUMMARY

The Aycock Springs Stream and Wetland Mitigation Site (Site) encompasses approximately 13 acres located roughly 1.5 miles north of Elon and Gibsonville in western Alamance County within 14-digit Cataloging Unit and Targeted Local Watershed 03030002030010 of the Cape Fear River Basin (Figure 1, Appendix B and Table 4, Appendix A). Prior to construction, the Site consisted of agricultural land used for livestock grazing, hay production, and timber harvest. Streams were cleared, trampled by livestock, eroded vertically and laterally, and received extensive sediment and nutrient inputs from livestock and timber harvest activities. Stream impacts in Travis Creek also occurred due to a breached dam that impounded water during storm events. In addition, streamside wetlands were drained by channel incision, soil compaction, the loss of forest vegetation, and land uses. Completed project activities, reporting history, completion dates, project contacts, and project attributes are summarized in Tables 1-4 (Appendix A).

Positive aspects supporting mitigation activities at the Site include the following.

- Streams have a Best Usage Classification of WS-V, NSW
- Located in a Targeted Local Watershed and within the NCDMS Travis, Tickle, Little Alamance Local Watershed Planning (LWP) Area
- Travis Creek is listed on the NCDENR 2012 303(d) list for ecological/biological integrity
- Immediately south and abutting the Site is a property identified in the *Little Alamance, Travis, & Tickle Creek Watersheds Restoration Plan* (PTCOG 2008) as a target property for wetland restoration and streambank enhancement/conservation
- Immediately west of the Site is a large tract associated with Guilford County open space

Based on the *Cape Fear River Basin Restoration Priorities Report 2009* (NCEEP 2009) and the *Little Alamance, Travis, & Tickle Creek Watersheds Restoration Plan* (PTCOG 2008), Targeted Local Watershed 03030002030010 is not meeting its designated use of supporting aquatic life. Agricultural land use appears to be the main source of stress in the Hydrologic Unit, as well as land clearing and poor riparian management. This project will meet the eight priority goals of the Travis, Tickle, Little Alamance Local Watershed Plan (LWP) including the following.

- 1) Reduce sediment loading
- 2) Reduce nutrient loading
- 3) Manage stormwater runoff
- 4) Reduce toxic inputs
- 5) Provide and improve instream habitat
- 6) Provide and improve terrestrial habitat
- 7) Improve stream stability
- 8) Improve hydrologic function

The following six goals were identified by the Stakeholder group of the Travis, Tickle, Little Alamance LWP Phase I assessment which address the water quality impacts and watershed needs in all of the Little Alamance, Travis, Tickle watersheds in 2006.

- 1) Increase local government awareness of the impacts of urban growth on water resources
- 2) Strengthen watershed protection standards
- 3) Improve water quality through stormwater management
- 4) Identify and rank parcels for retrofits, stream repair, preservation, and/or conservation
- 5) Assess aquatic health to identify stressors that are the most likely causes of poor biological conditions
- 6) Meet requirements of outside funding sources for implementation of projects

The following table summarizes the project goals/objectives and proposed functional uplift based on restoration activities and observations of two reference areas located in the vicinity of the Site. Goals and objectives target functional uplift identified in the Travis, Tickle, Little Alamance LWP and based on stream/wetland functional assessments developed by the regulatory agencies.

Project Goals and Objectives

Project Goal/Objective	How Goal/Objective will be Accomplished
Improve Hydrology	
Restore Floodplain Access	Building a new channel at the historic floodplain elevation to restore overbank flows
Restore Wooded Riparian Buffer	Planting a woody riparian buffer
Restore Stream Stability	Providing proper channel width and depth, stabilizing channel banks, providing gravel/cobble substrate, planting a woody riparian buffer, and removing cattle
Improve Sediment Transport to Convert the UTs from Sand/Silt Dominated to Gravel/Cobble Dominated Streams	
Improve Stream Geomorphology	
Increase Surface Storage and Retention	Building a new channel at the historic floodplain elevation restoring overbank flows, removing cattle, scarifying compacted soils, and planting woody vegetation
Restore Appropriate Inundation/Duration	
Increase Subsurface Storage and Retention	Raising the stream bed elevation and rip compacted soils
Improve Water Quality	
Increase Upland Pollutant Filtration	Planting a native, woody riparian buffer
Increase Thermoregulation	Planting a native, woody riparian buffer
Reduce Stressors and Sources of Pollution	Removing cattle and other agricultural inputs
Increase Removal and Retention of Pathogens, Particulates (Sediments), Dissolved Materials (Nutrients), and Toxins from the Water Column	Raising the stream bed elevation, restoring overbank flows, planting with woody vegetation, removing cattle, increasing surface storage and retention, and restoring appropriate inundation/duration
Increase Energy Dissipation of Overbank/Overland Flows/Stormwater Runoff	Raising the stream bed elevation, restoring overbank flows, and planting with woody vegetation
Restore Habitat	
Restore In-stream Habitat	Building a stable channel with a cobble/gravel bed and planting a woody riparian buffer
Restore Stream-side Habitat	Planting a woody riparian buffer
Improve Vegetation Composition and Structure	

Project construction was completed April 6, 2016 and planting was completed April 8, 2016. Site activities included the restoration of perennial and intermittent stream channels, enhancement (Level II) of perennial stream channel, and re-establishment of riparian wetlands. Priority I restoration of intermittent channels at the Site is imperative to provide significant functional uplift to Site hydrology, water quality, and habitat, in addition to restore adjacent streamside, riparian wetlands. A total of **3581.1 Stream Mitigation Units (SMUs) and 0.5 Riparian Wetland Mitigation Units (WMUs)** are being provided as depicted in the following table.

Stream Mitigation Type	Perennial Stream (linear feet)	Intermittent Stream (linear feet)	Ratio	Stream Mitigation Units
Restoration	3147	90	1:1	3237
Restoration (See Notes below)**		122	1:5:1	81.3
Enhancement (Level II)	657	--	2.5:1	262.8
TOTAL	3804	212		3581.1
Wetland Mitigation Type	Acreage	Ratio	Riparian Wetland Mitigation Units	
Riparian Re-establishment	0.5	1:1	0.5	
Riparian Enhancement	1.5*		--	
TOTAL	2.0		0.5	

* Wetland enhancement acreage is not included in mitigation credit calculations as per RFP 16-005568 requirements.

** Prior to Site selection, the landowner received a violation for unauthorized discharge of fill material into Waters of the United States. Fill resulted from unpermitted upgrades to a farm pond dam, including widening the dam footprint, dredging stream channel, and casting spoil material adjacent to the stream channel on jurisdictional wetlands. Prior to restoration activities the landowner was required to obtain an after-the-fact permit to resolve the violations of Section 301 of the Clean Water Act (Action ID:SAW-2014-00665). In addition, stream reaches and wetland areas associated with the violation have been removed from credit generation.

In addition, the landowner received a violation for riparian buffer impacts due to clearing of trees adjacent to streams draining to Jordan Lake (NOV-2013-BV-0001). As a result of this violation, the upper 122 linear feet of UT 3 has a reduced credit ratio (1.5:1). On-site visits conducted with USACE representatives determined that the functional uplift of project restoration to UT 3 would be satisfactory to generate credit at this ratio.

Stream Success Criteria

Monitoring and success criteria for stream restoration should relate to project goals and objectives. From a mitigation perspective, several of the goals and objectives are assumed to be functionally elevated by restoration activities without direct measurement. Other goals and objectives will be considered successful upon achieving vegetation success criteria. The following summarizes stream success criteria related to goals and objectives.

Space Purposefully Left Blank

Project Goal/Objective	Stream Success Criteria
Improve Hydrology	
Restore Floodplain Access	Two overbank events in separate monitoring years will be documented during the monitoring period.
Restore Wooded Riparian Buffer	Attaining Vegetation Success Criteria.
Restore Stream Stability	Cross-sections, monitored annually, will be compared to as-built measurements to determine channel stability and maintenance of channel geomorphology.
Improve Stream Geomorphology	Convert stream channels from unstable G- and F-type channels to stable E- and C- type stream channels.
Increase Surface Storage and Retention	Two overbank events in separate monitoring years, and attaining Wetland and Vegetation Success Criteria.
Restore Appropriate Inundation/Duration	
Increase Subsurface Storage and Retention	Two overbank events will be documented, in separate years, during the monitoring period and documentation of an elevated groundwater table (within 12 inches of the soil surface) for greater than 10 percent of the growing season during average climatic conditions.
Improve Sediment Transport to Convert the UTs from Sand/Silt Dominated to Gravel/Cobble Dominated Streams	Pebble counts documenting coarsening of bed material from pre-existing conditions of sand and silt to post restoration conditions of gravel and cobble.
Improve Water Quality	
Increase Upland Pollutant Filtration	Attaining Wetland and Vegetation Success Criteria (Sections 2.3 and 2.2)
Increase Thermoregulation	Attaining Vegetation Success Criteria (Section 2.2).
Reduce Stressors and Sources of Pollution	Fencing maintained throughout the monitoring period and encroachment within the easement eliminated.
Increase Removal and Retention of Pathogens, Particulates (Sediments), Dissolved Materials (Nutrients), and Toxins from the Water Column	Removal of cattle, documentation of two overbank events in separate monitoring years, and attaining Vegetation Success Criteria (Section 2.2)
Increase Energy Dissipation of Overbank/Overland Flows/Stormwater Runoff	Documentation of two overbank events in separate monitoring years and attaining Vegetation Success Criteria (Section 2.2)
Restore Habitat	
Restore In-stream Habitat	Pebble counts documenting coarsening of bed material from pre-existing conditions of sand and silt to post restoration conditions of gravel and cobble, and attaining Vegetation Success Criteria (Section 2.2)
Restore Stream-side Habitat	Attaining Vegetation Success Criteria (Section 2.2)
Improve Vegetation Composition and Structure	Attaining Vegetation Success Criteria (Section 2.2)

Vegetation Success Criteria

An average density of 320 planted stems per acre must be surviving in the first three monitoring years. Subsequently, 290 planted stems per acre must be surviving in year 4, 260 planted stems per acre in year 5, and 210 planted stems per acre in year 7. In addition, planted vegetation must average 10 feet in height in each plot at year 7 since this Site is located in the Piedmont. Volunteer stems may be considered on a case-by-case basis in determining overall vegetation success; however, volunteer stems should be counted separately from planted stems.

Wetland Success Criteria

Monitoring and success criteria for wetland re-establishment should relate to project goals and objectives. From a mitigation perspective, several of the goals and objectives are assumed to be functionally elevated by restoration activities without direct measurement. Other goals and objectives will be considered successful upon achieving vegetation success criteria. The following summarizes wetland success criteria related to goals and objectives.

Wetland Goals and Success Criteria

Project Goal/Objective	Wetland Success Criteria
Improve Hydrology	
Restore Wooded Riparian Buffer	Attaining Vegetation Success Criteria.
Increase Surface Storage and Retention	Two overbank events in separate monitoring years, and attaining Wetland and Vegetation Success Criteria.
Restore Appropriate Inundation/Duration	
Increase Subsurface Storage and Retention	
Improve Water Quality	
Increase Upland Pollutant Filtration	Attaining Wetland and Vegetation Success Criteria.
Reduce Stressors and Sources of Pollution	Fencing maintained throughout the monitoring period and encroachment within the easement eliminated.
Increase Removal and Retention of Pathogens, Particulates (Sediments), Dissolved Materials (Nutrients), and Toxins from the Water Column	Removal of cattle, documentation of two overbank events in separate monitoring years, and attaining Vegetation Success Criteria.
Increase Energy Dissipation of Overbank/Overland Flows/Stormwater Runoff	Documentation of two overbank events in separate monitoring years, and attaining Vegetation Success Criteria.
Restore Habitat	
Restore Stream-side Habitat	Attaining Vegetation Success Criteria.
Improve Vegetation Composition and Structure	

According to the *Soil Survey of Alamance County*, the growing season for Alamance County is from April 17 – October 22 (USDA 1960). However, the start date for the growing season is not typical for the Piedmont region; therefore, for purposes of this project gauge hydrologic success will be determined using data from February 1 - October 22 to more accurately represent the period of biological activity. This will be confirmed annually by soil temperatures and/or bud burst. The growing season will be initiated each year on the documented date of biological activity. Photographic evidence of bud burst and field logs of date and temperature will be included in the annual monitoring reports.

Target hydrological characteristics include saturation or inundation for 10 percent of the monitored period (February 1-October 22), during average climatic conditions. During years with atypical climatic conditions, groundwater gauges in reference wetlands may dictate threshold hydrology success criteria (75 percent of reference). These areas are expected to support hydrophytic vegetation. If wetland parameters are marginal as indicated by vegetation and/or hydrology monitoring, a jurisdictional determination will be performed.

Summary of Monitoring Period/Hydrology Success Criteria by Year

Year	Soil Temperatures/Date Bud Burst Documented	Monitoring Period Used for Determining Success	10 Percent of Monitoring Period
2016 (Year 1)	--	April 17*-October 22 (198 days)	19 days
2017 (Year 2)	Bud burst on red maple (<i>Acer rubrum</i>) and soil temperature of 58°F documented on February 28, 2017	February 28-October 22 (237 days)	23 days
2018 (Year 3)	Bud burst and soil temperature of 44°F documented on March 6, 2018	March 6-October 22 (231 days)	23 days
2019 (Year 4)			
2020 (Year 5)			

*Gauges were installed on May 5 during year 1 (2016), so April 17 was used as the start of the growing season (NRCS).

Summary information/data related to the occurrence of items such as beaver or encroachment and statistics related to performance of various project and monitoring elements can be found in tables and figures within this report's appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report (formerly Mitigation Plan) and in the Mitigation Plan (formerly the Restoration Plan) documents available on the NC Division of Mitigation Services (NCDMS) website. All raw data supporting the tables and figures in the appendices are available from NCDMS upon request.

2.0 METHODOLOGY

Monitoring requirements and success criteria outlined in the latest guidance by US Army Corps of Engineers (USACE) in April 2003 (*Stream Mitigation Guidelines*) will be followed and are briefly outlined below. Monitoring data collected at the Site should include reference photos, plant survival analysis, channel stability analysis, and biological data, if specifically required by permit conditions.

Wetland hydrology is proposed to be monitored for a period of seven years (years 1-7). Riparian vegetation and stream morphology is proposed to be monitored for a period of seven years with measurements completed in years 1-3, year 5, and year 7. Monitoring reports for years 4 and 6 will include photo documentation of stream stability and wetland hydrology monitoring data. If monitoring demonstrates the Site is successful by year 5 and no concerns have been identified, Restoration Systems (RS) may propose to terminate monitoring at the Site and forego monitoring requirements for years 6 and 7. Early closure will only be provided through written approval from the USACE in consultation with the Interagency Review Team (NC IRT). Monitoring will be conducted by Axiom Environmental, Inc (AXE). Annual monitoring reports of the data collected will be submitted to the NCDMS by RS no later than December 31 of each monitoring year data is collected.

2.1 Streams

Annual monitoring will include development of channel cross-sections and substrate on riffles and pools. Data to be presented in graphic and tabular format will include 1) cross-sectional area, 2) bankfull width, 3) average depth, 4) maximum depth, 5) width-to-depth ratio, 6) bank height ratio, and 7) entrenchment ratio. Longitudinal profiles will not be measured routinely unless monitoring demonstrates channel bank or bed instability, in which case, longitudinal profiles may be required by the USACE along reaches of concern to track changes and demonstrate stability.

Visual assessment of in-stream structures will be conducted to determine if failure has occurred. Failure of a structure may be indicated by collapse of the structure, undermining of the structure, abandonment of the channel around the structure, and/or stream flow beneath the structure. In addition, visual assessments of the

entire channel will be conducted in years 1-3, 5, and 7 of monitoring as outlined in *NCDMS Monitoring Requirements and Reporting Standards for Stream and/or Wetland Mitigation*. Areas of concern will be depicted on a plan view figure identifying the location of concern along with a written assessment and photograph of the area.

Year 3 (2018) Stream measurements were performed mid-April 2018. As a whole, monitoring measurements indicate minimal changes in the cross-sections as compared to as-built data. The channel geometry compares favorably with the proposed conditions as set forth in the detailed mitigation plan and as constructed.

Immediately after construction, before ground cover was fully established, multiple heavy rain events (2+ inches) caused some sedimentation in the streambed. This aggradation can be seen in several Year 1 (2016) cross-sections, and it appeared to be reduced and stabilized during Years 2-3 (2017-2018).

The year 1 (2016) measurements for cross-sections 9 and 10 on UT-1 showed stream bed erosion when compared with as-built data. Stream bed erosion was noted shortly after as-built measurements were taken, and were the result of the above mentioned rain events. It was evident bed material used during construction in this area was finer than it should have been. Two riffles showed bed erosion, totaling approximately 50 feet in length (approximately 1 percent of the project length). RS created and implemented a remedial action plan during late winter of 2016/2017 (see Section 3.0 and Appendix G). These repairs appear stable during Year 3 (2018) monitoring, and they will continue to be monitored during subsequent monitoring years.

Across the site, all in-stream structures are intact and functioning as designed. No stream areas of concern were identified during Year 3 (2018) monitoring; however, three small areas of bank erosion were observed in the Enhancement (Level II) reach of Travis Creek. The pre-construction condition of Travis Creek included some stream bank erosion, and with the large amount of rainfall the Site received during Year 3 (2018), some of this erosion became more apparent. These areas will continue to be monitored for any significant change, but the erosion is not expected to cause any major stream stability problems. Additionally, several monitoring cross-sections (Travis XS-1, Travis XS-2, Travis XS-4, UT1 XS-2, UT2 XS-5, and UT2 XS-8) are showing Bank Height Ratios of <1. The bank height ratios were calculated based on fixing the cross-sectional area from last year's data, in accordance with the 2018 NCDMS "Standard Measurement of the BHR Monitoring Parameter" guidance. Each of these cross-sections exhibited a small amount of aggradation during Year 3 (2018). It is expected that this aggradation is the product of natural sediment transport and will not cause any long-term stream issues. Tables for annual quantitative assessments are included in Appendix D.

In 2017, a beaver dam was located and removed along Travis Creek between the outfalls of UT-4 and UT-3. The dam was removed in the winter of 2017, and no additional beaver activity was recorded during the 2018 monitoring season.

2.2 Vegetation

After planting was completed on April 8, 2016, an initial evaluation was performed to verify planting methods and to determine initial species composition and density. Supplemental planting and additional Site modifications will be implemented, if necessary.

During quantitative vegetation sampling, 14 sample plots (10-meter by 10-meter) were installed within the Site as per guidelines established in *CVS-EEP Protocol for Recording Vegetation, Version 4.2* (Lee et al. 2008). In each sample plot, vegetation parameters to be monitored include species composition and species density. Visual observations of the percent cover of shrub and herbaceous species will also be documented by photograph.

Working with Carolina Silvics, RS planted 1030 containerized trees consisting of 755 1-gallon pots and 275 3-gallon pots during the week of December 20th, 2016, which included the following species: *Betula nigra*,

Fraxinus pennsylvanica, *Platanus occiendentalis*, *Quercus falcata*, *Quercus nigra*, *Quercus palustris*, *Quercus phellos*, and *Quercus rubra*. A remedial planting plan report detailing location of planting and density is provided in Appendix G.

Year 3 (2018) stem count measurements were performed on July 19, 2018 and indicate an average of 370 planted stems per acre (excluding livestakes) across the Site; therefore, the Site is meeting vegetation success criteria. Ten of the fourteen individual vegetation plots met success criteria based on planted stems alone. When including naturally recruited stems of green ash (*Fraxinus pennsylvanica*), Plots 3 and 7 were above success criteria. Year 3 (2018) vegetation plot information can be found in Appendix C.

Five additional temporary 25-meter by 4-meter transects were established and stems counts were performed in March 2018. Survival of planted stems in these plots was above success standards with a range of 364-769 planted stems per acre; results are summarized in Table 10 (Appendix C).

Treatment of invasive plant species continued during 2018 throughout the Site, and Restoration Systems will continue to treat and monitor the site for invasive species throughout the monitoring period. In the late fall of 2017, a small patch (less than a ¼ of an acre) of cattails was noted at the confluence of UT-1 and UT-2. Treatment was conducted in May of 2018, additional treatments are planned for the spring of 2019 and will continue as needed. See Appendix H (Herbicide Application Forms) for a detailed account of site-wide treatments.

2.3 Wetland Hydrology

Three groundwater monitoring gauges were installed to take measurements after hydrological modifications were performed at the Site. Hydrological sampling will continue throughout the growing season at intervals necessary to satisfy jurisdictional hydrology success criteria (USEPA 1990). In addition, a surface water gauge has been installed in Tributary 3 to monitor flow regime of the tributary. Approximate locations of gauges are depicted on Figure 2 (Appendix A).

Hydrological sampling will continue throughout the growing season at intervals necessary to satisfy jurisdictional hydrology success criteria (USEPA 1990). In addition, an on-site rain gauge will document rainfall data for comparison of groundwater conditions with extended drought conditions and floodplain crest gauges will confirm overbank flooding events. All groundwater gauges were successful in year 3 (2018) (Appendix E).

2.4 Biotic Community Change

Changes in the biotic community are anticipated from a shift in habitat opportunities as tributaries are restored. In-stream, biological monitoring is proposed to track the changes during the monitoring period. The benthic macroinvertebrate community will be sampled using NCDWQ protocols found in the *Standard Operating Procedures for Benthic Macroinvertebrates* (NCDWQ 2006) and *Benthic Macroinvertebrate Protocols for Compensatory Stream Restoration Projects* (NCDWQ 2001). Biological sampling of benthic macroinvertebrates will be used to compare preconstruction baseline data with postconstruction restored conditions.

Two benthic macroinvertebrate monitoring locations will be established within restoration reaches. Postrestoration collections will occur in the approximate location of the prerestoration sampling. Benthic macroinvertebrate samples will be collected from individual reaches using the Qual-4 collection method. Sampling techniques of the Qual-4 collection method consist of kick nets, sweep nets, leaf packs, and visual searches. Preproject biological sampling occurred on June 26, 2014; postproject monitoring will occur in June of monitoring years 2-5.

Identification of collected organisms will be performed by personnel with North Carolina Division of Water Resources (NCDWR) or by a NCDWR certified laboratory. Other data collected will include D50 values/NCDWR habitat assessment forms. Biological sampling for year 3 (2018) occurred on June 13, 2018. The samples were sent to Pennington and Associates, a NCDWR certified laboratory, for identification and analysis. Results and Habitat Assessment Dataforms are included in Appendix F.

3.0 REMEDIAL ACTION PLAN

A remedial action plan was developed in order to address stream and vegetation problem areas observed during Year 1 (2016) monitoring. The completed remedial action report can be found in Appendix G.

3.1 Stream

The degradation observed during Year 1 (2016) in and adjacent to cross-sections 9 and 10 on UT-1 encompasses approximately 12 linear feet and 15 linear feet of stream, respectively (<1 percent of the project length). As noted above, bed material placed during construction was too fine. All of UT-1 used bed material harvested on-site. The material used along these stream reaches was too fine and washed from the riffles during heavy rainfall events, resulting in minor bed scour and a small, less than 6 inch head cut beginning to develop at the top of riffle. Suitable sized channel bed material was installed on February 23, 2017 at the proper elevation in the two riffles within UT-1. Bed material was installed such that bank toe protection is provided and planting with willow stakes will occur. Bank toe protection designates that channel bed material will extend up the lower one-third of the bank. This will be monitored by existing established cross-sections 9 and 10.

3.2 Vegetation

Multiple factors were contributing to poor vegetative success in Year 1 (2016) including a later than desired initial bare-root planting, heavy herbaceous competition primarily from fescue (Site was previously a cattle pasture), and sporadic rain events, which left upland areas of the site dry for extended periods of the growing season. Greater survival of planted species was observed within riparian areas. Upland areas of the site had the lowest survival rates.

The remedial action plan supplemented the bare-root planting over 5.44 acres with 1030 additional trees (755 1-gallon pots and 275 3-gallon pots). The remedial action plan figure (Appendix G) details the areas that received remedial planting along with density and number of species being placed into vegetation plots. Working with Carolina Silvics, RS acquired and re-planted identified areas during the week of December 20th, 2016. Species of planted tree included *Betula nigra*, *Fraxinus pennsylvanica*, *Platanus occidentalis*, *Quercus falcata*, *Quercus nigra*, *Quercus palustris*, *Quercus phellos*, and *Quercus rubra*.

4.0 REFERENCES

Environmental Laboratory. 1987. Corps of Engineers Wetlands Delineation Manual. Technical Report Y-87-1. United States Army Engineer Waterways Experiment Station, Vicksburg, Mississippi.

Environmental Laboratory. 2012. Regional Supplement to the Corps of Engineers Wetland Delineation Manual: Eastern Mountains and Piedmont Region (Version 2.0). United States Army Engineer Research and Development Station, Vicksburg, Mississippi.

Lee, M.T., R.K. Peet, S.D. Roberts, and T.R. Wentworth. 2008. CVS-EEP Protocol for Recording Vegetation. Version 4.2. North Carolina Department of Environment and Natural Resources, Ecosystem Enhancement Program. Raleigh, North Carolina.

North Carolina Division of Water Quality (NCDWQ). 2001. Benthic Macroinvertebrate Monitoring Protocols for Compensatory Mitigation. 401/Wetlands Unit, Department of Environment and Natural Resources. Raleigh, North Carolina.

North Carolina Division of Water Quality (NCDWQ). 2006. Standard Operating Procedures for Benthic Macroinvertebrates. Biological Assessment Unit, North Carolina Department of Environment and Natural Resources. Raleigh, North Carolina.

North Carolina Division of Mitigation Services (NCDMS 2009). Cape Fear River Basin Restoration Priorities 2009 (online). Available: http://portal.ncdenr.org/c/document_library/get_file?uuid=864e82e8-725c-415e-8ed9-c72dfcb55012&groupId=60329

Schafale, M.P. and A.S. Weakley. 1990. Classification of the Natural Communities of North Carolina: Third Approximation. North Carolina Natural Heritage Program, Division of Parks and Recreation, North Carolina Department of Environment, Health, and Natural Resources. Raleigh, North Carolina.

United States Department of Agriculture (USDA). 1960. Soil Survey of Alamance County, North Carolina. Soil Conservation Service.

United States Environmental Protection Agency (USEPA). 1990. Mitigation Site Type Classification (MiST). EPA Workshop, August 13-15, 1989. EPA Region IV and Hardwood Research Cooperative, NCSU, Raleigh, North Carolina.

APPENDIX A

PROJECT BACKGROUND DATA AND MAPS

Figure 1. Vicinity Map

Table 1. Project Components and Mitigation Credits

Table 2. Project Activity and Reporting History

Table 3. Project Contacts Table

Table 4. Project Baseline Information and Attributes



Prepared for:



Project:

Aycock Springs Stream and Wetland Mitigation Site

Alamance County, NC

Title:

Project Location

Notes:

- Background Imagery sources (provided by ESRI Data and Maps):
1. Physical Map of the United States (2009) created by the U.S. Park Service (upper inset).
 2. Delorme World Basemap digital mapping (2010, lower inset).
 3. Burlington, NC (1980), Lake Burlington, NC (1969), Gibsonville, NC (1970), and Ossipee, NC (1970) 7.5-minute topographic quadrangles provided by the U.S. Geological Survey.

Drawn by: SGD

Date: May 2016

Scale: As Shown



Project No.: 14-006

FIGURE

1


Directions to the Site from Interstates 40/85 in Burlington/Elon, NC:

- Exit onto University Drive (I-40/85 Exit 140) and travel north (toward Elon)
- Travel north for 2.8 miles and merge with NC 100
- Continue on University Drive (NC 100) for 0.5 mile and turn left onto Manning Street (SR 1503)
- Travel northwest for 0.8 mile and turn right onto Gibsonville-Ossipee Road (SR 1500)
- Travel north for 0.7 mile and Site is on the right

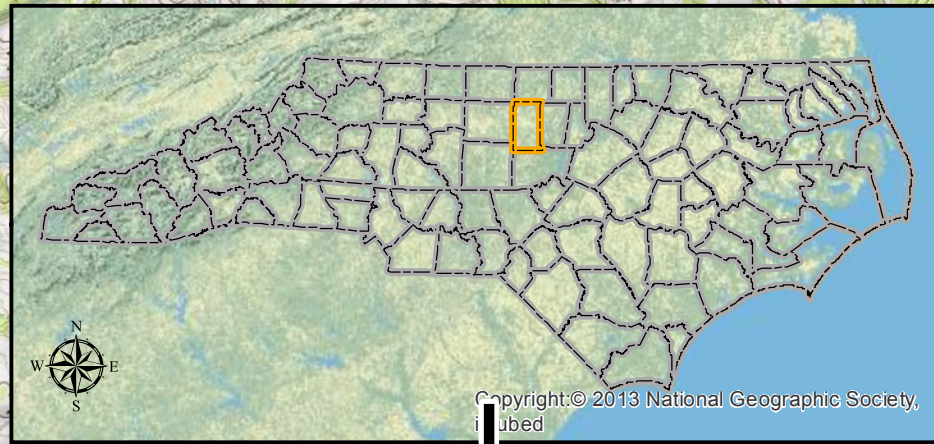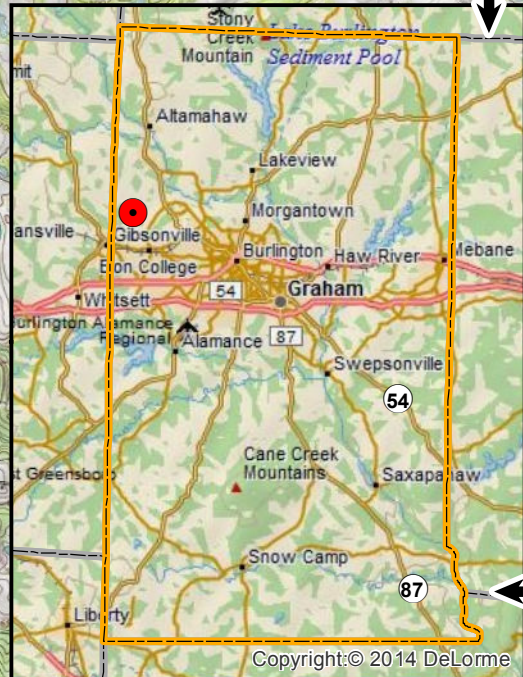

Aycock Springs Stream and Wetland Mitigation Site
 36.127271 N
 -79.525214 W

- Legend**
- Aycock Springs Stream and Wetland Mitigation Site
 - County lines



**Table 1. Project Components and Mitigation Credits
Aycock Springs Mitigation Site**

Mitigation Credits							
Stream	Stream	Riparian Wetland			Nonriparian Wetland		
Restoration	Enhancement	Re-establishment			Re-establishment		
3237	344.1	0.5			--		
Projects Components							
Station Range	Existing Linear Footage/ Acreage	Priority Approach	Restoration/ Restoration Equivalent	Restoration Linear Footage/ Acreage	Mitigation Ratio	Mitigation Credits	Comment
UT 1 Station 10+04 to 23+21	1173	PI	Restoration	$1317-24=1293$	1:1	1293	24 lf of UT 1 is located outside of easement and is not credit generating
UT 2 Station 10+00 to 16+75	723	PI	Restoration	675	1:1	675	
UT 3 Station 10+00 to 11+22	147	PI	Restoration	122	1.5:1	81.3	*** The upper 122 linear feet of channel is in a violation area and is generating credit at a reduced ratio of 1.5:1
UT 3 Station 11+22 to 12+12	16	PI	Restoration	90	1:1	90	
UT 4 Station 10+00 to 14+13	448	PI	Restoration	$413-107=306$	1:1	306	****The upper 107 linear feet of channel is in a violation area and is not credit generating
Travis Creek Station 10+00 to 15+78	578		EII	$578-20=558$	2.5:1	223.2	The upper 20 linear feet of Travis Creek is within a powerline easement and is not credit generating
Travis Creek Station 15+78 to 17+87	274	PII	Restoration	209	1:1	209	
Travis Creek Station 17+87 to 18+86	99		EII	99	2.5:1	39.6	
Travis Creek Station 23+71 to 30+35	936	PI	Restoration	664	1:1	664	

**Table 1. Project Components and Mitigation Credits (continued)
Aycock Springs Mitigation Site**

Component Summation			
Restoration Level	Stream (linear footage)	Riparian Wetland (acreage)	Nonriparian Wetland (acreage)
Restoration	3237	0.5	--
Enhancement (Level I)	122	--	--
Enhancement (Level II)	657	--	--
Enhancement	--	1.41**	--
Totals	4016	--	--
Mitigation Units	3581.1 SMUs	0.5 Riparian WMUs	0.00 Nonriparian WMUs

**Wetland enhancement acreage is not included in mitigation credit calculations as per RFP 16-005568 requirements.

***Prior to Site selection, the landowner received a violation for riparian buffer impacts due to clearing of trees adjacent to streams draining to Jordan Lake (NOV-2013-BV-0001). As a result of this violation, the upper 122 linear feet of UT 3 has a reduced credit ratio of 1.5:1. On-site visits conducted with USACE representatives determined that the functional uplift of project restoration to UT 3 would be satisfactory to generate credit at this ratio.

**** Prior to Site selection, the landowner received a violation for unauthorized discharge of fill material into Waters of the United States. Fill resulted from unpermitted upgrades to a farm pond dam, including widening the dam footprint, dredging stream channel, and casting spoil material adjacent to the stream channel on jurisdictional wetlands. Prior to restoration activities the landowner was required to obtain an after-the-fact permit to resolve the violations of Section 301 of the Clean Water Act (Action ID:SAW-2014-00665). In addition, stream reaches and wetland areas associated with the violation area have been removed from credit generation – UT 4 begins credit generation at Station 11+07).

**Table 2. Project Activity and Reporting History
Aycock Springs Mitigation Site**

Activity or Deliverable	Stream Monitoring Complete	Vegetation Monitoring Complete	All Data Collection Complete	Completion or Delivery
Technical Proposal (RFP No. 16-005568)	--	--	--	October 2013
DMS Contract No. 5791	--	--	--	February 2014
Mitigation Plan	--	--	October 2014	May 2015
Construction Plans	--	--	--	June 2015
Construction Earthwork	--	--	--	April 6, 2016
Planting	--	--	--	April 8, 2016
As-Built Documentation	April 6, 2016	April 13, 2016	April 2016	May 2016
Year 1 Monitoring	October 18, 2016	October 13, 2016	October 2016	December 2016
Supplemental Planting	--	--	--	December 2016
Year 2 Monitoring	April 19-20, 2017	July 25, 2017	October 2017	November 2017
Year 3 Monitoring	April 16-17, 2018	July 19, 2018	October 2018	October 2018

**Table 3. Project Contacts Table
Aycock Springs Mitigation Site**

Full Delivery Provider	Restoration Systems 1101 Haynes Street, Suite 211 Raleigh, North Carolina 27604 Worth Creech 919-755-9490
Designer and Monitoring Provider	Axiom Environmental, Inc. 218 Snow Avenue Raleigh, NC 27603 Grant Lewis 919-215-1693

**Table 4. Project Attribute Table
Aycock Springs Mitigation Site**

Project Information	
Project Name	Aycock Springs Restoration Site
Project County	Alamance County, North Carolina
Project Area (acres)	15
Project Coordinates (latitude & longitude)	36.127271°N, 79.525214°W
Project Watershed Summary Information	
Physiographic Province	Piedmont
Project River Basin	Cape Fear
USGS HUC for Project (14-digit)	03030002030010
NCDEQ Sub-basin for Project	03-06-02
Project Drainage Area (acres)	26-3008
Project Drainage Area Percentage of Impervious Area	<2%

Table 4. Project Attribute Table (continued)
Aycock Springs Mitigation Site

Reach Summary Information				
Parameters	Travis Cr	UT 1/UT2	UT 3	UT 4
Length of reach (linear feet)	1550	1966	212	413
Valley Classification	alluvial			
Drainage Area (acres)	3008	68	26	119
NCDWQ Stream ID Score	--	30.75/25.5	26.75	27.5
NCDWR Water Quality Classification	WS-V, NSW			
Existing Morphological Description (Rosgen 1996)	Cg 5/6-, Eg 5-, and Fc 5-type			
Existing Evolutionary Stage (Simon and Hupp 1986)	IV	IV	III	III
Underlying Mapped Soils	Cecil, Helena, Mixed Alluvial Land, Severely Gullied Land, Worsham			
Drainage Class	Well-drained, moderately well-drained, poorly drained, variable, poorly drained			
Hydric Soil Status	Nonhydric and Hydric			
Slope	0.0023	0.0249	0.0153	0.0093
FEMA Classification	AE	Special Hazard Flood Area		
Native Vegetation Community	Piedmont Alluvial Forest/Dry-Mesic Oak-Hickory Forest			
Watershed Land Use/Land Cover (Site)	42% forest, 53% agricultural land, <5% low density residential/impervious surface			
Watershed Land Use/Land Cover (Cedarock Reference Channel)	65% forest, 30% agricultural land, <5% low density residential/impervious surface			
Percent Composition of Exotic Invasive Vegetation	< 5%			
Wetland Summary Information				
Parameters	Wetlands			
Wetland acreage	1.6			
Wetland Type	Riparian			
Mapped Soil Series	Worsham and Mixed Alluvial Land			
Drainage Class	Poorly drained			
Hydric Soil Status	Hydric			
Source of Hydrology	Groundwater, stream overbank			
Hydrologic Impairment	Incised streams, compacted soils, livestock			
Native Vegetation Community	Piedmont/Low Mountain Alluvial Forest			
Percent Composition of Exotic Invasive Vegetation	<5%			
Regulatory Considerations				
Regulation	Applicable?	Resolved?	Supporting Documentation	
Waters of the United States-Section 401	Yes	Resolved	404 Permit	
Waters of the United States-Section 404	Yes	Resolved	401 Certification	
Endangered Species Act	No	--	CE Doc.	
Historic Preservation Act	No	--	CE Doc.	
Coastal Zone Management Act	No	--	NA	
FEMA Floodplain Compliance	Yes	In progress	CLOMR/LOMR	
Essential Fisheries Habitat	No	--	NA	

APPENDIX B


VISUAL ASSESSMENT DATA

Figure 2. Current Conditions Plan View (CCPV)

Tables 5A-5E. Visual Stream Morphology Stability Assessment

Table 6. Vegetation Condition Assessment


Vegetation Plot Photographs

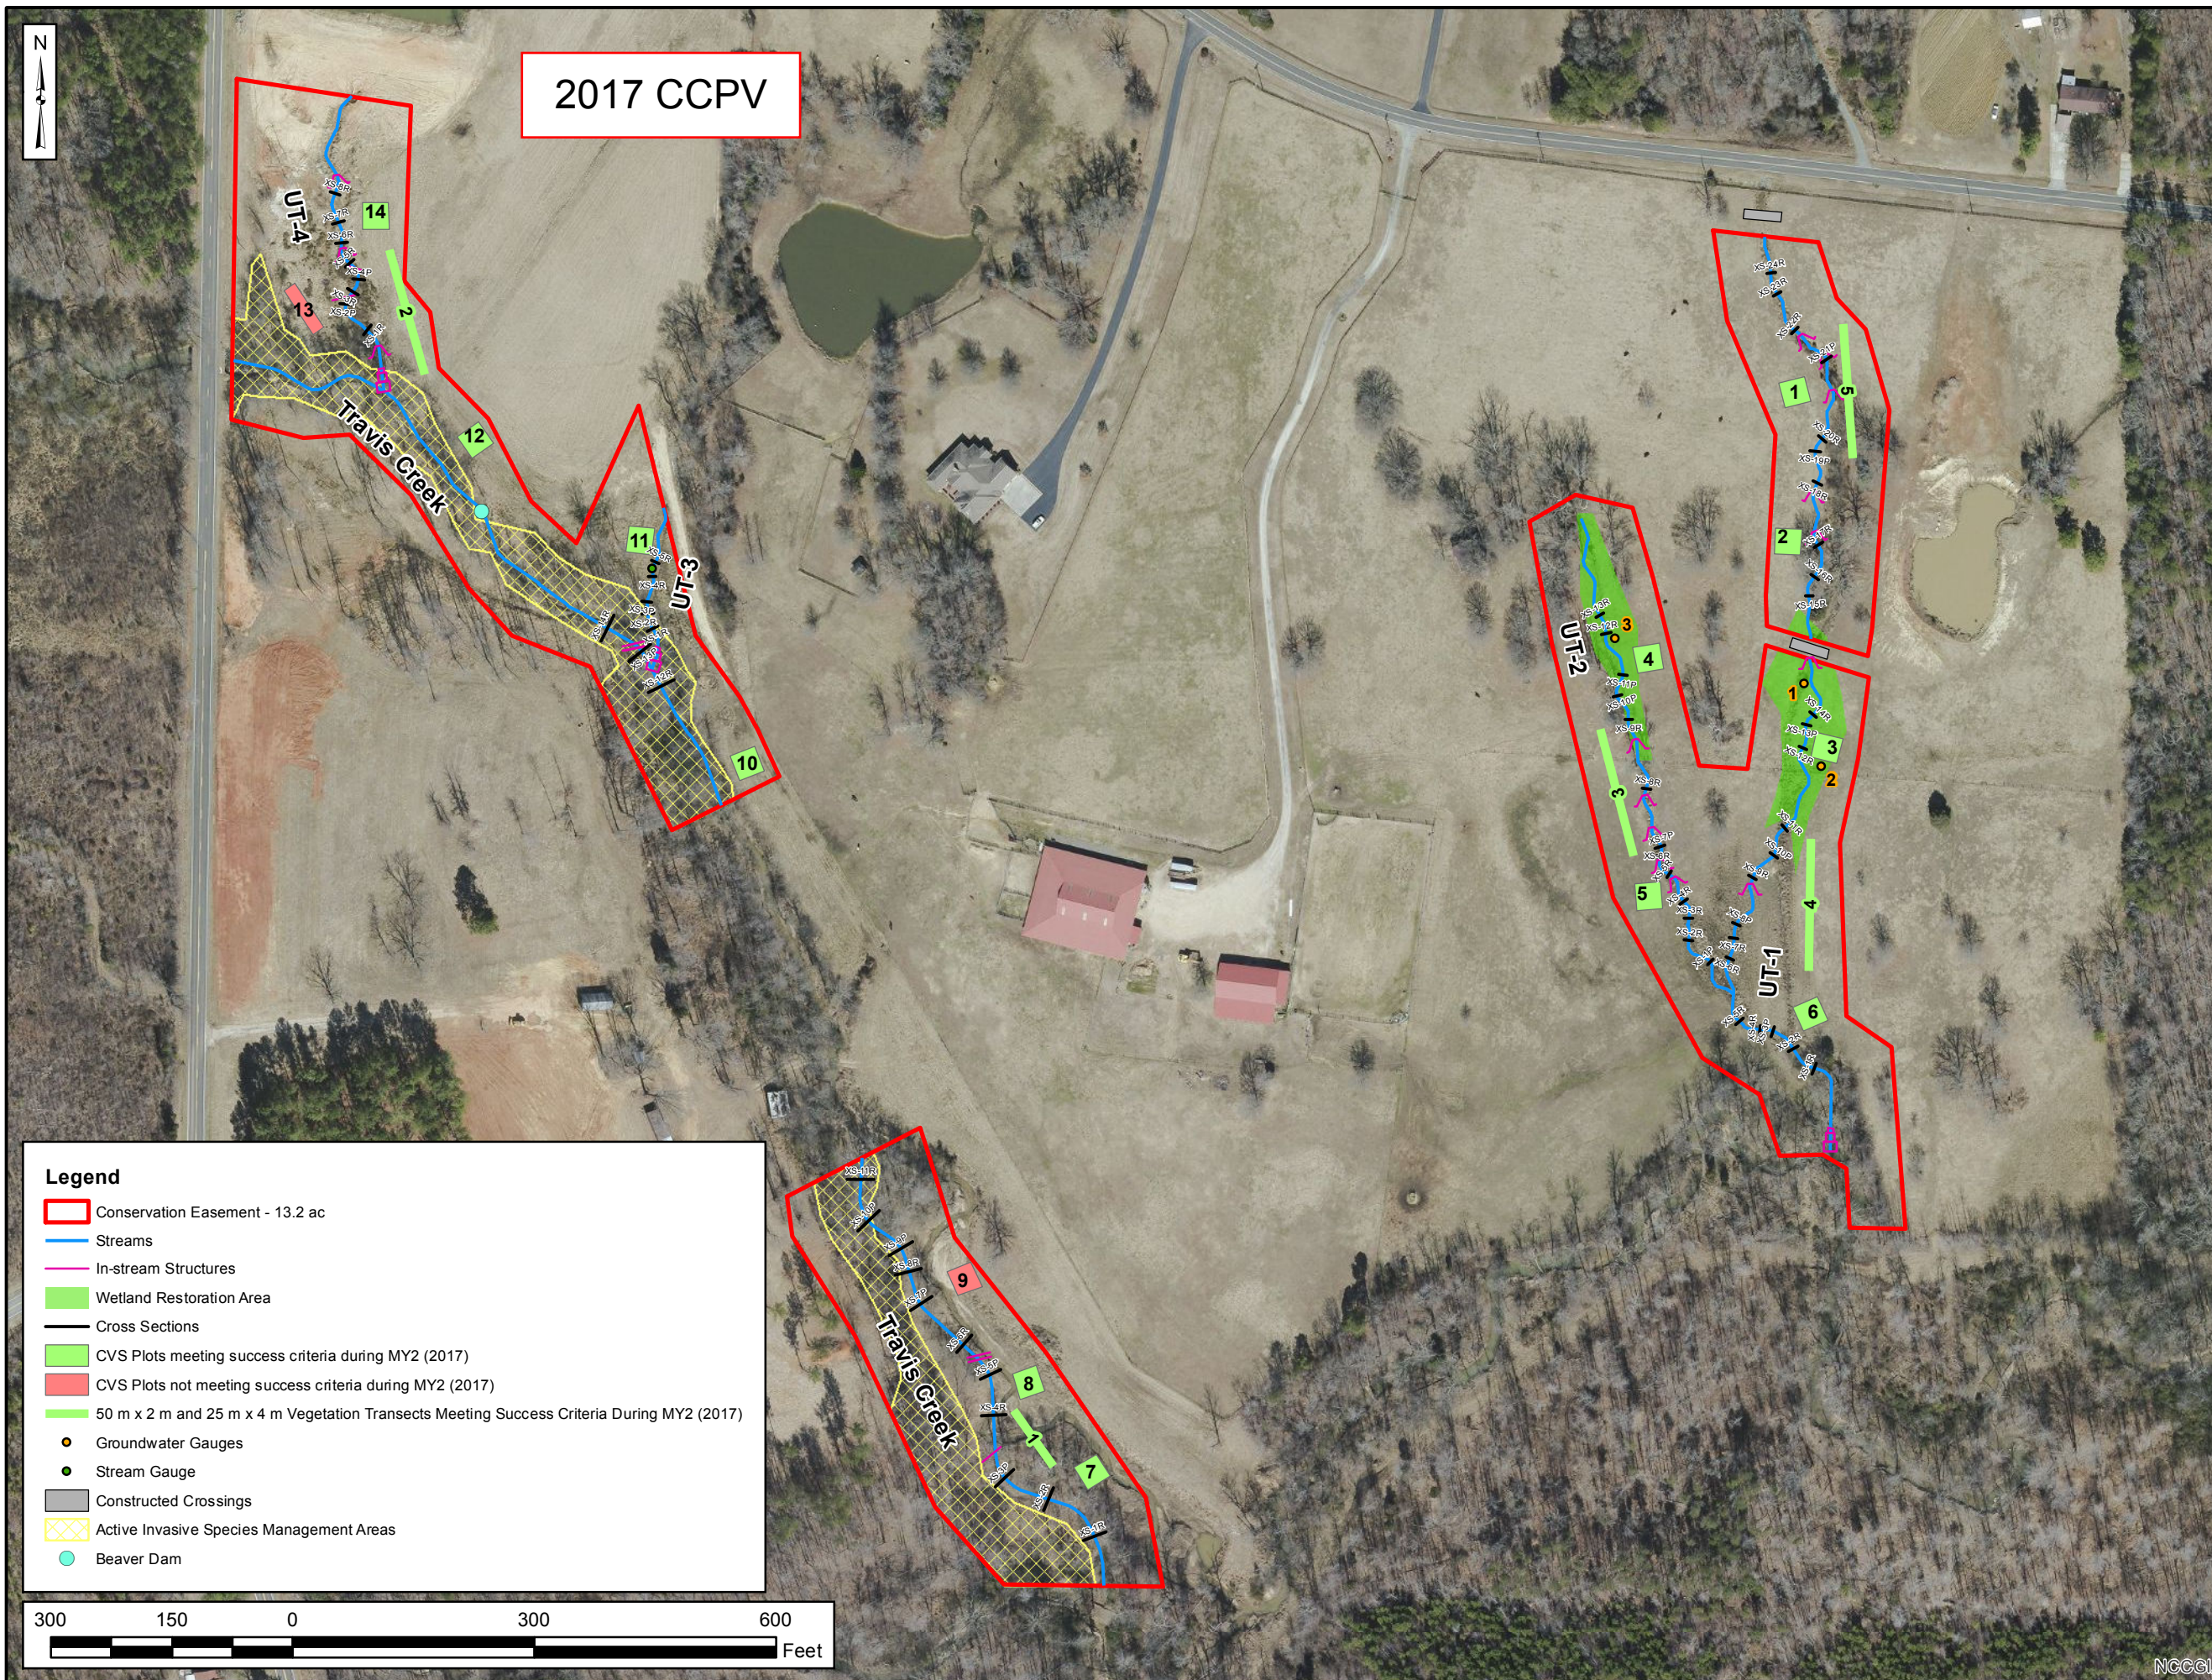

2017 CCPV

Legend

- Conservation Easement - 13.2 ac
- Streams
- In-stream Structures
- Wetland Restoration Area
- Cross Sections
- CVS Plots meeting success criteria during MY2 (2017)
- CVS Plots not meeting success criteria during MY2 (2017)
- 50 m x 2 m and 25 m x 4 m Vegetation Transects Meeting Success Criteria During MY2 (2017)
- Groundwater Gauges
- Stream Gauge
- Constructed Crossings
- Active Invasive Species Management Areas
- Beaver Dam



Prepared for:

Project:

Aycock Springs Stream and Wetland Mitigation Site

Alamance County, NC

Title:

Current Conditions Plan View

Notes:

1. Background Imagery source: 2014 aerial photography provided by the NC OneMap Program (online, supported by the NC Geographic Information Coordination Council).


Drawn by: KRJ

Date: OCT 2017

Scale: 1:2400

Project No.: 14-006

FIGURE 2

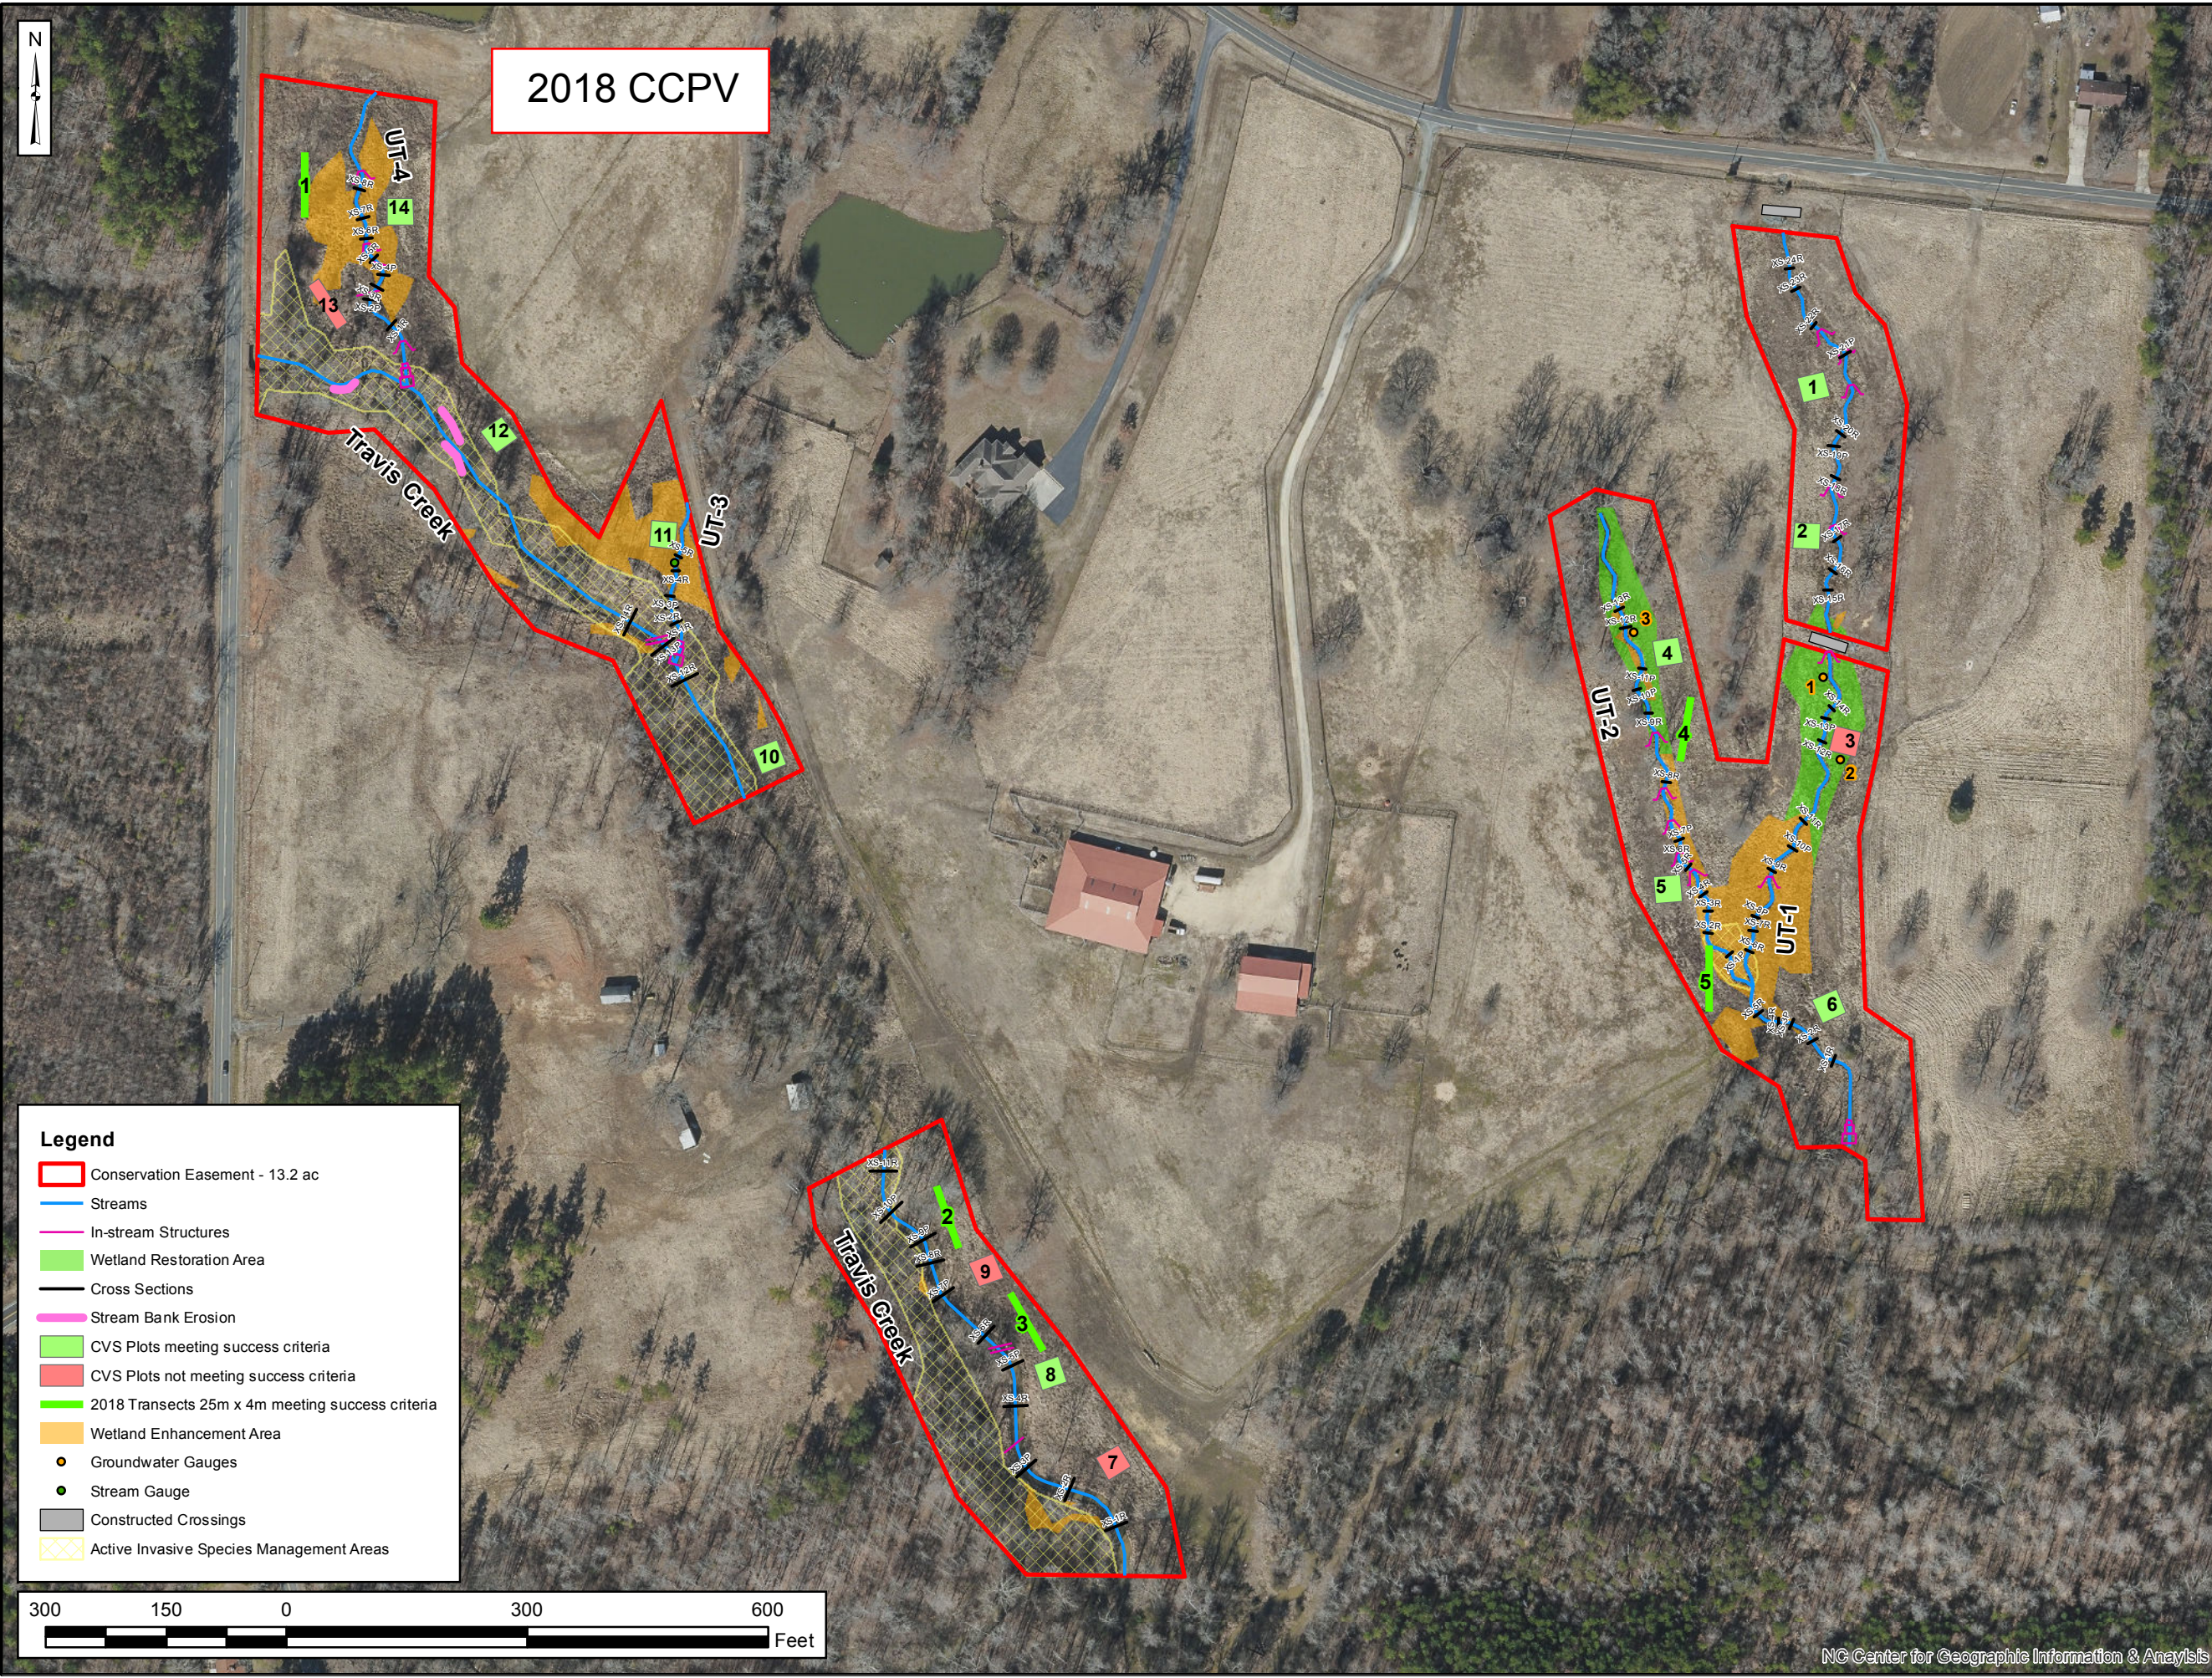

2018 CCPV



Prepared for:

 RESTORATION SYSTEMS LLC

Project:
Aycock Springs Stream and Wetland Mitigation Site
 Alamance County, NC

Title:
Current Conditions Plan View

Notes:
 1. Background Imagery source: 2014 aerial photography provided by the NC OneMap Program (online, supported by the NC Geographic Information Coordination Council).

Drawn by: KRJ/CLF
 Date: DEC 2018
 Scale: 1:2400
 Project No.: 14-006

FIGURE
2

Legend

- Conservation Easement - 13.2 ac
- Streams
- In-stream Structures
- Wetland Restoration Area
- Cross Sections
- Stream Bank Erosion
- CVS Plots meeting success criteria
- CVS Plots not meeting success criteria
- 2018 Transects 25m x 4m meeting success criteria
- Wetland Enhancement Area
- Groundwater Gauges
- Stream Gauge
- Constructed Crossings
- Active Invasive Species Management Areas




Table 5A
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Aycock Springs - Travis Creek
 2128

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended		Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)				0	0	100%			100%
		2. <u>Degradation</u> - Evidence of downcutting				0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	10	10				100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	9	9				100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	9	9				100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	9	9				100%			
2. Thalweg centering at downstream of meander (Glide)		9	9				100%				
Totals						0	0	100%	0	0	100%
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion				0	0	100%			100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.				0	0	100%			100%
	3. Mass Wasting	Bank slumping, calving, or collapse				0	0	100%			100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	9	9				100%			100%
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	9	9				100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	9	9				100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%.	9	9				100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	9	9				100%			

Table 5B
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Aycock Springs UT1
 1317

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			100%
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	45	45			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	44	44			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	44	44			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	44	44			100%			
2. Thalweg centering at downstream of meander (Glide)		44	44			100%				
Totals					0	0	100%	0	0	100%
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%			100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%			100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%			100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	10	10			100%			100%
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	10	10			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	10	10			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%.	10	10			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	10	10			100%			

Table 5C
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Aycock Springs UT2
 675

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	25	25			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	24	24			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	24	24			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	24	24			100%			
2. Thalweg centering at downstream of meander (Glide)		24	24			100%				
Totals										
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%			100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%			100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%			100%
Totals										
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	6	6			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	6	6			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	6	6			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%.	6	6			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	6	6			100%			

Table 5D
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Aycock Springs UT3
 212

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	9	9			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	8	8			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	8	8			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	8	8			100%			
2. Thalweg centering at downstream of meander (Glide)		8	8			100%				
Totals					0	0	100%	0	0	100%
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%			100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%			100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%			100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	1	1			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	1	1			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%.	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	1	1			100%			

Table 5E
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Aycock Springs UT4
 413

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended		Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)				0	0	100%			100%
		2. <u>Degradation</u> - Evidence of downcutting				0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	9	9				100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	8	8				100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	8	8				100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	8	8				100%			
2. Thalweg centering at downstream of meander (Glide)		8	8				100%				
Totals											
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion				0	0	100%			100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.				0	0	100%			100%
	3. Mass Wasting	Bank slumping, calving, or collapse				0	0	100%			100%
Totals											
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	5	5				100%			100%
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	5	5				100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	5	5				100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%.	5	5				100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	5	5				100%			

Table 6

Vegetation Condition Assessment

Aycock Springs

Planted Acreage¹

11.9

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage	
1. Bare Areas	None	0.1 acres	none	0	0.00	0.0%	
2. Low Stem Density Areas	None	0.1 acres	none	0	0.00	0.0%	
2B. Low Planted Stem Density Areas	None	0.1 acres	none	0	0.00	0.0%	
				Total	0	0.00	0.0%
3. Areas of Poor Growth Rates or Vigor	None	0.25 acres	none	0	0.00	0.0%	
				Cumulative Total	0	0.00	0.0%

Easement Acreage²

13.3

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Ongoing Invasive Species Management Areas ⁴	Management of Chinese privet and multiflora rose is active and ongoing along Travis Creek. 2017 invasives management has improved vegetation condition in this area, however treatment is ongoing.	1000 SF	yellow hatch	2	2.38	17.9%
5. Easement Encroachment Areas ³	None	none	none	0	0.00	0.0%


¹ = Enter the planted acreage within the easement. This number is calculated as the easement acreage minus any existing mature tree stands that were not subject to supplemental planting of the understory, the channel acreage, crossings or any other elements not directly planted as part of the project effort.

² = The acreage within the easement boundaries.

³ = Encroachment may occur within or outside of planted areas and will therefore be calculated against the overall easement acreage. In the event a polygon is cataloged into items 1, 2 or 3 in the table and is the result of encroachment, the associated acreage should be tallied in the relevant item (i.e., item 1,2 or 3) as well as a parallel tally in item 5.

⁴ = Invasives may occur in or out of planted areas, but still within the easement and will therefore be calculated against the overall easement acreage. Invasives of concern/interest are listed below. The list of high concern species are those with the potential to directly outcompete native, young, woody stems in the short-term (e.g. monitoring period or shortly thereafter) or affect the community structure for existing, more established tree/shrub stands over timeframes that are slightly longer (e.g. 1-2 decades). The low/moderate concern group are those species that generally do not have this capacity over the timeframes discussed and therefore are not expected to be mapped with regularity, but can be mapped, if in the judgement of the observer their coverage, density or distribution is suppressing the viability, density, or growth of planted woody stems. Decisions as to whether remediation will be needed are based on the integration of risk factors by DMS such as species present, their coverage, distribution relative to native biomass, and the practicality of treatment. For example, even modest amounts of Kudzu or Japanese Knotweed early in the projects history will warrant control, but potentially large coverages of Microstegium in the herb layer will not likely trigger control because of the limited capacities to impact tree/shrub layers within the timeframes discussed and the potential impacts of treating extensive amounts of ground cover. Those species with the "watch list" designator in gray shade are of interest as well, but have yet to be observed across the state with any frequency. Those in *red italics* are of particular interest given their extreme risk/threat level for mapping as points where isolated specimens are found, particularly early in a projects monitoring history. However, areas of discreet, dense patches will of course be mapped as polygons. The symbology scheme below was one that was found to be helpful for symbolizing invasives polygons, particularly for situations where the condition for an area is somewhere between isolated specimens and dense, discreet patches. In any case, the point or polygon/area feature can be symbolized to describe things like high or low concern and species can be listed as a map inset, in legend items if the number of species are limited or in the narrative section of the executive summary.

**Aycock Springs
Year 3 Vegetation Monitoring Photographs
Taken July 2018**

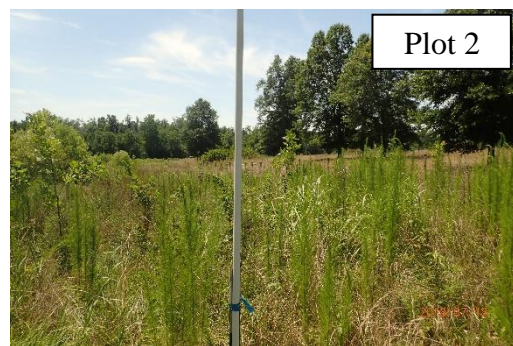

**Aycock Springs
Year 3 Vegetation Monitoring Photographs
Taken July 2018
(continued)**



APPENDIX C
VEGETATION PLOT DATA

Table 7. Vegetation Plot Criteria Attainment

Table 8. CVS Vegetation Plot Metadata

Table 9. Total and Planted Stems by Plot and Species

Table 10. Supplemental Vegetation Transect Data

Table 7. Vegetation Plot Criteria Attainment Based on Planted Stems

Vegetation Plot ID	Vegetation Survival Threshold Met?	Tract Mean
1	Yes	71.4%
2	Yes	
3	No*	
4	Yes	
5	Yes	
6	Yes	
7	No*	
8	Yes	
9	No	
10	Yes	
11	Yes	
12	Yes	
13	No	
14	Yes	

*These plots did not meet success criteria based on planted stems only; however, when including naturally recruited stems of green ash (*Fraxinus pennsylvanic*) these plots were above success criteria.

Table 8. CVS Vegetation Plot Metadata

Report Prepared By	Corri Faquin
Date Prepared	10/4/2018 13:02
database name	RS-Aycock_2018-v2.3.1.mdb
database location	S:\Business\Projects\14\14-006 Aycock Springs Detailed\2018 YEAR-03\CVS
computer name	CORRI2-PC
file size	56627200
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Proj, planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Proj, total stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY-----	
Project Code	14-006
project Name	Aycock Springs
Description	
River Basin	Cape Fear
length(ft)	
stream-to-edge width (ft)	
area (sq m)	
Required Plots (calculated)	
Sampled Plots	14

Table 9. Planted and Total Stems
 Project Code 14.006. Project Name: Aycock Springs

Scientific Name	Common Name	Species Type	Current Plot Data (MY3 2018)																																
			14.006-01-0001			14.006-01-0002			14.006-01-0003			14.006-01-0004			14.006-01-0005			14.006-01-0006			14.006-01-0007			14.006-01-0008			14.006-01-0009			14.006-01-0010					
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T			
Acer negundo	boxelder	Tree																																	
Acer rubrum	red maple	Tree																																	
Betula nigra	river birch	Tree			1	1	1	1									1	1	1				2	2	2										
Callicarpa	beautyberry	Shrub																																	
Callicarpa americana	American beautyberry	Shrub																																	
Carpinus caroliniana	American hornbeam	Tree															3	3	3							1	1	1							
Cephalanthus occidentalis	common buttonbush	Shrub																																	
Cornus amomum	silky dogwood	Shrub	9	9	9	3	3	3	3	3	3	3	3	3	3	10	10	10	4	4	4	4	4	4	1	1	1	3	3	3					
Cornus florida	flowering dogwood	Tree																																	
Diospyros virginiana	common persimmon	Tree																							1	1	1			1	1	1			
Fraxinus pennsylvanica	green ash	Tree			1			2			6	1	1	4	1	1	6						1	2	2	2	1	1	1	1	1	3			
Liquidambar	sweetgum	Tree																																	
Nyssa sylvatica	blackgum	Tree																				1	1	1											
Platanus occidentalis	American sycamore	Tree	2	2	5							1	1	1								1	1	1			1	1	1						
Quercus	oak	Tree																																	
Quercus alba	white oak	Tree	1	1	1																														
Quercus falcata	southern red oak	Tree														3	3	3							1	1	1								
Quercus michauxii	swamp chestnut oak	Tree								2	2	2	4	4	4																				
Quercus nigra	water oak	Tree													1	1	1																		
Quercus pagoda	cherrybark oak	Tree																																	
Quercus phellos	willow oak	Tree																				1	1	1					3	3	3				
Quercus rubra	northern red oak	Tree	6	6	6	2	2	3	2	2	2				1	1	1								1	1	1	1	1	1	1				
Salix nigra	black willow	Tree																																	
Sambucus canadensis	Common Elderberry	Shrub					2	2	2									1	1	1															
Ulmus	elm	Tree																																	
Ulmus alata	winged elm	Tree																																	
Ulmus americana	American elm	Tree																																	
Stem count			18	18	23	8	8	11	7	7	13	9	9	12	9	9	14	15	15	15	7	7	8	9	9	9	6	6	7	9	9	11			
size (ares)			1			1			1			1			1			1			1			1			1			1			1		
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02		
Species count			4	4	6	4	4	5	3	3	4	4	4	4	5	5	5	4	4	4	4	4	5	4	4	4	6	6	7	5	5	5			
Stems per ACRE			728.4	728.4	930.8	323.7	323.7	445.2	283.3	283.3	526.1	364.2	364.2	485.6	364.2	364.2	566.6	607	607	607	283.3	283.3	323.7	364.2	364.2	364.2	242.8	242.8	283.3	364.2	364.2	445.2			

Color for Density

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%

- PnoLS = Planted excluding livestakes
- P-all = Planting including livestakes
- T = All planted and natural recruits including livestakes
- T includes natural recruits

Table 9. Planted and Total Stems (continued)
 Project Code 14.006. Project Name: Aycock Springs

Scientific Name	Common Name	Species Type	Current Plot Data (MY3 2018)												Annual Means											
			14.006-01-0011			14.006-01-0012			14.006-01-0013			14.006-01-0014			MY3 (2018)			MY2 (2017)			MY1 (2016)			MY0 (2016)		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer negundo	boxelder	Tree																9			5			7		
Acer rubrum	red maple	Tree																2			5					
Betula nigra	river birch	Tree	1	1	1							2	2	2	7	7	8	5	5	5	5	5	5	9	9	9
Callicarpa	beautyberry	Shrub																1								
Callicarpa americana	American beautyberry	Shrub																			1					
Carpinus caroliniana	American hornbeam	Tree	1	1	1										5	5	5	6	6	6	5	5	5	7	7	7
Cephalanthus occidentalis	common buttonbush	Shrub																		2			4			
Cornus amomum	silky dogwood	Shrub	2	2	2				1	1	1				46	46	46	49	49	49	52	52	52	57	57	57
Cornus florida	flowering dogwood	Tree	2	2	2										2	2	2	2	2	2	4	4	4	4	4	4
Diospyros virginiana	common persimmon	Tree													2	2	2	2	2	2	1	1	1	2	2	2
Fraxinus pennsylvanica	green ash	Tree			3	4	4	4				3	3	3	13	13	36	10	10	31	5	5	13	3	3	5
Liquidambar	sweetgum	Tree																		1						
Nyssa sylvatica	blackgum	Tree				1	1	1							2	2	2	3	3	3	3	3	3	6	6	6
Platanus occidentalis	American sycamore	Tree	1	1	1							1	1	1	7	7	10	7	7	9	1	1	1	5	5	5
Quercus	oak	Tree																5	5	5	4	4	4	11	11	11
Quercus alba	white oak	Tree													1	1	1	1	1	1	1	1	1	2	2	2
Quercus falcata	southern red oak	Tree							1	1	1				5	5	5	4	4	4						
Quercus michauxii	swamp chestnut oak	Tree				1	1	1				3	3	3	10	10	10	7	7	7	5	5	5			
Quercus nigra	water oak	Tree				1	1	1							2	2	2	1	1	1						
Quercus pagoda	cherrybark oak	Tree																1	1	1	1	1	1	6	6	6
Quercus phellos	willow oak	Tree	3	3	3	1	1	1	1	1	1				9	9	9	9	9	9	6	6	6	18	18	18
Quercus rubra	northern red oak	Tree				1	1	1					1	14	14	16	12	12	12	11	11	11	13	13	13	
Salix nigra	black willow	Tree																		1						
Sambucus canadensis	Common Elderberry	Shrub													3	3	3	7	7	7	11	11	11	62	62	62
Ulmus	elm	Tree																		2						
Ulmus alata	winged elm	Tree																							2	
Ulmus americana	American elm	Tree																					3			
Stem count			10	10	13	9	9	9	3	3	3	9	9	10	128	128	158	131	131	171	115	115	141	205	205	216
size (ares)			1			1			1			1			14			14			14			14		
size (ACRES)			0.02			0.02			0.02			0.02			0.35			0.35			0.35			0.35		
Species count			6	6	7	6	6	6	3	3	3	4	4	5	15	15	16	17	17	23	15	15	20	14	14	16
Stems per ACRE			404.7	404.7	526.1	364.2	364.2	364.2	121.4	121.4	121.4	364.2	364.2	404.7	370	370	456.7	378.7	378.7	494.3	332.4	332.4	407.6	592.6	592.6	624.4

Color for Density

- Exceeds requirements by 10%
- Exceeds requirements, but by less than 10%
- Fails to meet requirements, by less than 10%
- Fails to meet requirements by more than 10%

- PnoLS = Planted excluding livestakes
- P-all = Planting including livestakes
- T = All planted and natural recruits including livestakes
- T includes natural recruits

Table 10a. Supplemental Vegetation Transect Data – April 2017

Scientific Name	Common Name	Species Type	Temporary Plot 1 2m x 50m	Temporary Plot 2 2m x 50m	Temporary Plot 3 2m x 50m	Temporary Plot 4 2m x 50m	Temporary Plot 5 2m x 50m
<i>Betula nigra</i>	River birch	Tree		1	1		
<i>Carpinus caroliniana</i>	American hornbeam	Tree	2		2		
<i>Cornus amomum</i>	Silky dogwood	Tree	1		3	6	3
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	2	3	3		2
<i>Platanus occidentalis</i>	Sycamore	Tree	2	1			
<i>Quercus lyrata</i>	Overcup oak	Tree					1
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree			1		
<i>Quercus nigra</i>	Water oak	Tree	1	1			2
<i>Quercus phellos</i>	Willow oak	Tree	3	2	1	1	1
<i>Quercus rubra</i>	Northern red oak	Tree	1	1	2	2	3
		Stem Count	12	9	13	9	12
		Size (Ares)	1	1	1	1	1
		Size (Acres)	0.0247	0.0247	0.0247	0.0247	0.0247
		Species count	7	6	7	3	6
		Stems per acre	485.8	364.4	526.3	364.4	485.8

Table 10b. Supplemental Vegetation Transect Data – October 2017

Scientific Name	Common Name	Species Type	Temporary Plot 1 2m x 50m	Temporary Plot 2 2m x 50m	Temporary Plot 3 2m x 50m	Temporary Plot 4 2m x 50m	Temporary Plot 5 2m x 50m
<i>Betula nigra</i>	River birch	Tree		1			
<i>Carpinus caroliniana</i>	American hornbeam	Tree	2		2		
<i>Cornus amomum</i>	Silky dogwood	Tree	1		3	6	3
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	2	3	3		2
<i>Platanus occidentalis</i>	Sycamore	Tree	8	2			
<i>Quercus lyrata</i>	Overcup oak	Tree					1
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree			1		
<i>Quercus nigra</i>	Water oak	Tree	1	1			1
<i>Quercus phellos</i>	Willow oak	Tree	3	2	1		1
<i>Quercus rubra</i>	Northern red oak	Tree	1	1	2	2	3
		Stem Count	18	10	12	8	11
		Size (Ares)	1	1	1	1	1
		Size (Acres)	0.0247	0.0247	0.0247	0.0247	0.0247
		Species count	7	6	6	2	6
		Stems per acre	728.7	404.9	485.8	323.9	445.3

Table 10. Supplemental Vegetation Transect Data – March 7, 2018

Scientific Name	Common Name	Species Type	Temporary Plot 1 4m x 25m 180°	Temporary Plot 2 4m x 25m 160°	Temporary Plot 3 4m x 25m 150°	Temporary Plot 4 4m x 25m 190°	Temporary Plot 5 4m x 25m 180°
<i>Betula nigra</i>	River birch	Tree	1	2	1		1
<i>Cornus amomum</i>	Silky dogwood	Tree		2		1	
<i>Fraxinus pennsylvanica</i>	Green ash	Tree	6	1	2	4	
<i>Platanus occidentalis</i>	Sycamore	Tree	8		1	1	2
<i>Quercus michauxii</i>	Swamp chestnut oak	Tree					1
<i>Quercus nigra</i>	Water oak	Tree	4	4	5	4	4
<i>Quercus rubra</i>	Northern red oak	Tree				2	4
	Stem Count		19	9	9	12	12
	Size (Ares)		1	1	1	1	1
	Size (Acres)		0.0247	0.0247	0.0247	0.0247	0.0247
	Species count		4	4	4	5	5
	Stems per acre		769.2	364.4	364.4	485.8	485.8

APPENDIX D
STREAM SURVEY DATA

Cross-section Plots

Tables 11a-e. Baseline Stream Data Summary

Tables 12a-f. Monitoring Data


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 1, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	594.90
4.1	594.93
8.2	595.00
9.6	594.45
11.1	593.87
12.4	593.25
13.7	592.75
15.2	592.07
16.5	592.20
18.1	592.04
19.6	592.24
21.0	592.41
22.0	592.49
22.6	592.41
24.1	592.48
25.7	592.51
26.7	592.65
27.6	592.80
28.2	592.93
30.0	592.91
31.9	593.0
33.2	593.5
34.8	593.9
36.9	594.3
40.8	594.9
43.7	594.8
46.5	595.4

SUMMARY DATA	
Bankfull Elevation:	594.4
Bankfull Cross-Sectional Area:	40.1
Bankfull Width:	27.3
Flood Prone Area Elevation:	596.7
Flood Prone Width:	150.0
Max Depth at Bankfull:	2.3
Mean Depth at Bankfull:	1.5
W / D Ratio:	18.6
Entrenchment Ratio:	5.5
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

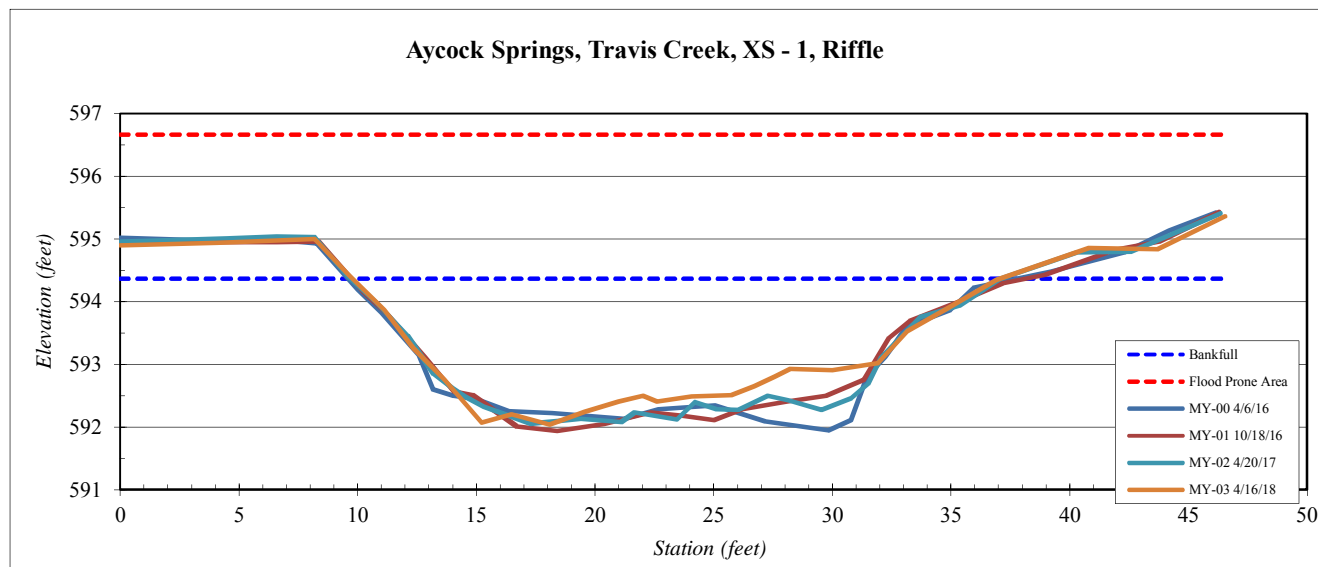


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 2, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	595.00
1.7	595.12
3.3	594.45
5.9	593.68
6.8	593.41
8.9	593.36
11.0	593.30
12.3	593.32
13.0	593.16
14.0	593.01
14.8	592.67
16.5	592.62
18.2	592.61
19.6	592.40
21.4	592.26
23.1	592.51
23.9	593.59
25.0	594.02
26.5	594.48
27.9	594.94
30.0	595.1

SUMMARY DATA	
Bankfull Elevation:	594.9
Bankfull Cross-Sectional Area:	41.6
Bankfull Width:	25.8
Flood Prone Area Elevation:	597.6
Flood Prone Width:	150.0
Max Depth at Bankfull:	2.7
Mean Depth at Bankfull:	1.6
W / D Ratio:	16.0
Entrenchment Ratio:	5.8
Bank Height Ratio:	1.00

Stream Type	C/E
--------------------	-----

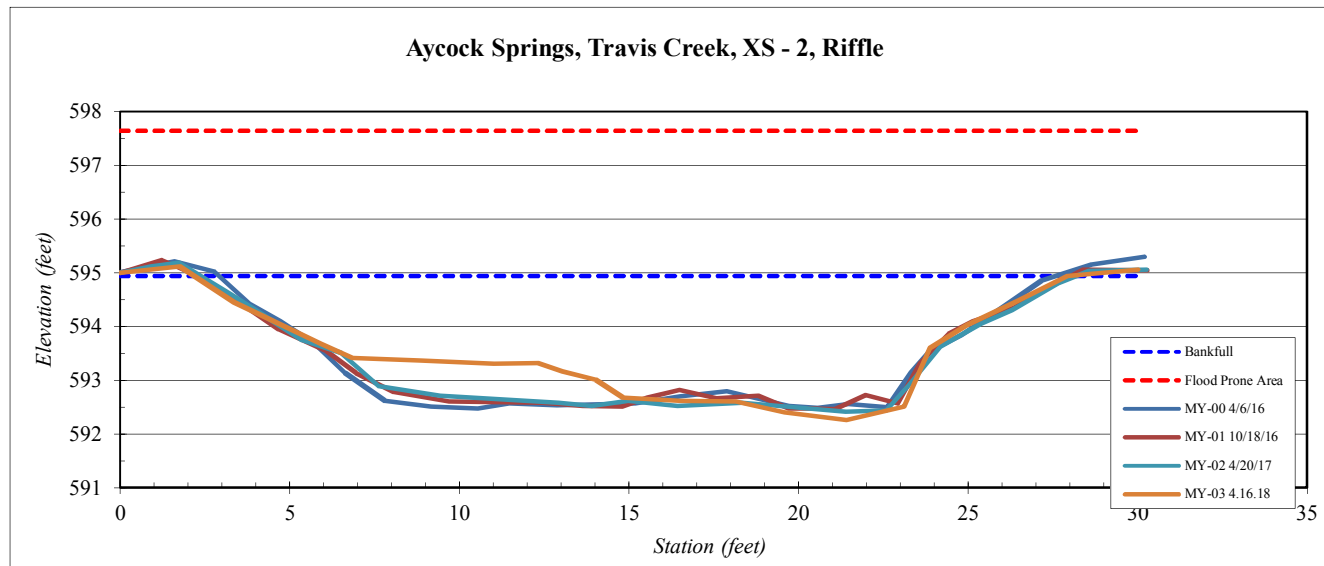


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 3, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	595.2
5.0	595.1
8.9	594.8
12.5	594.5
15.4	593.8
17.0	593.8
18.3	593.7
19.2	593.6
20.3	592.8
22.6	592.6
24.8	592.3
26.1	591.8
27.4	591.8
29.3	591.5
30.1	592.0
31.3	592.3
31.9	592.5
32.7	593.2
33.6	593.6
36.0	594.2
38.1	594.8
41.1	595.3
43.0	595.3
45.1	595.4

SUMMARY DATA	
Bankfull Elevation:	595.2
Bankfull Cross-Sectional Area:	57.2
Bankfull Width:	39.0
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	3.6
Mean Depth at Bankfull:	1.5
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

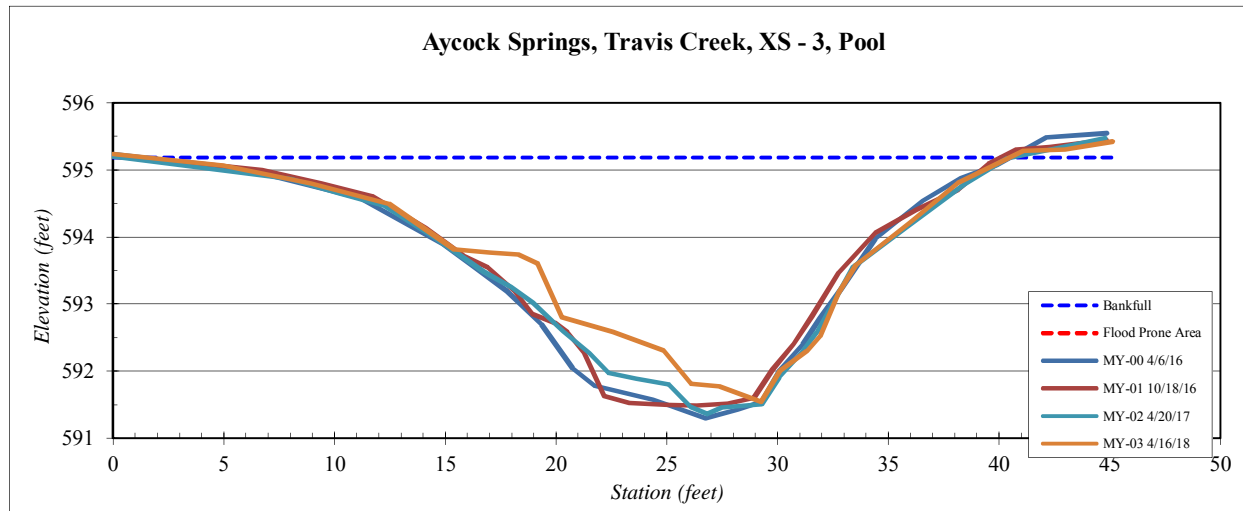


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 4, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	595.71
1.8	595.33
3.9	594.66
4.9	594.35
5.9	593.73
6.9	593.27
8.2	592.85
10.6	592.97
12.8	592.61
14.5	592.85
14.8	592.83
15.8	593.65
16.7	593.72
17.3	593.55
18.7	593.51
19.2	593.75
20.0	593.88
20.4	593.87
21.7	593.67
22.8	593.58
24.0	593.5
25.7	594.3
26.8	594.8
28.3	595.2
30.2	595.3

SUMMARY DATA	
Bankfull Elevation:	595.3
Bankfull Cross-Sectional Area:	43.8
Bankfull Width:	28.4
Flood Prone Area Elevation:	598.0
Flood Prone Width:	150.0
Max Depth at Bankfull:	2.7
Mean Depth at Bankfull:	1.5
W / D Ratio:	18.4
Entrenchment Ratio:	5.3
Bank Height Ratio:	<1

Stream Type	C/E
--------------------	-----

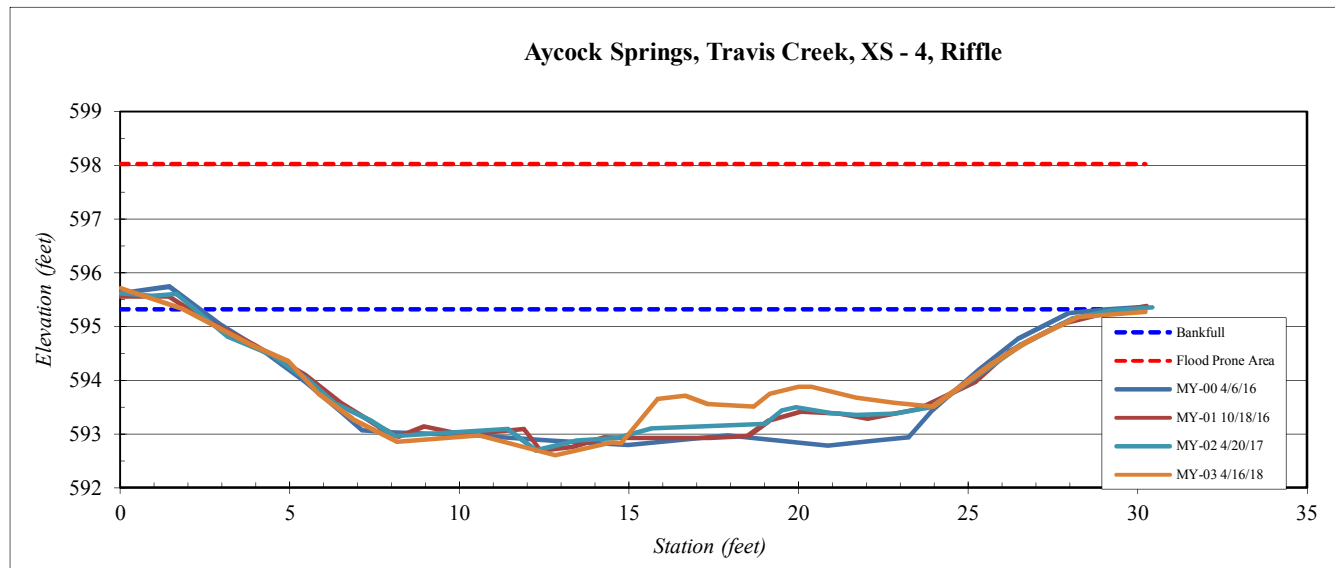


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 5, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	595.3
4.3	595.3
6.5	594.6
8.2	594.2
9.3	593.6
10.8	592.8
11.7	592.3
13.4	592.0
14.8	591.9
16.3	591.9
18.3	591.9
20.1	591.8
21.0	592.1
22.2	592.6
24.3	592.9
25.9	593.5
27.8	594.0
28.9	594.2
31.3	595.3
32.3	595.4

SUMMARY DATA	
Bankfull Elevation:	595.1
Bankfull Cross-Sectional Area:	52.3
Bankfull Width:	25.7
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	3.3
Mean Depth at Bankfull:	2.0
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.00

Stream Type C/E

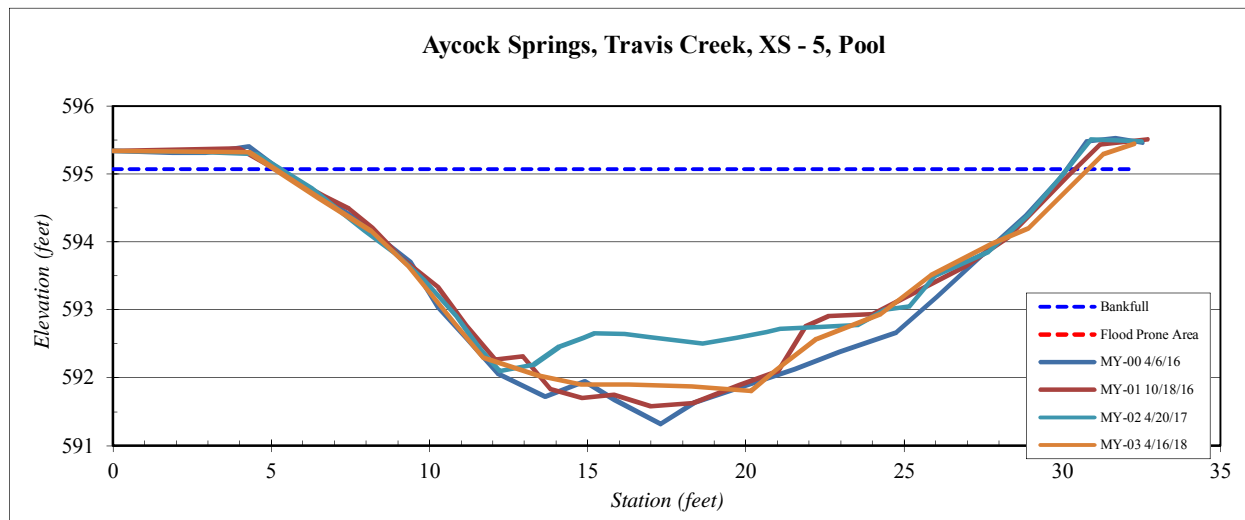

Note: Sediment Deposition in pool appears natural and is not expected to lead to instability.


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 6, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	596.09
3.3	595.61
5.5	594.93
6.8	594.30
9.4	594.46
11.0	594.50
12.6	594.52
13.4	593.52
16.1	593.57
18.7	593.25
20.6	593.01
23.3	593.18
24.4	593.73
26.2	594.84
28.7	595.95
29.8	596.20
31.0	596.54

SUMMARY DATA	
Bankfull Elevation:	596.1
Bankfull Cross-Sectional Area:	50.3
Bankfull Width:	28.9
Flood Prone Area Elevation:	599.1
Flood Prone Width:	150.0
Max Depth at Bankfull:	3.0
Mean Depth at Bankfull:	1.7
W / D Ratio:	16.6
Entrenchment Ratio:	5.2
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

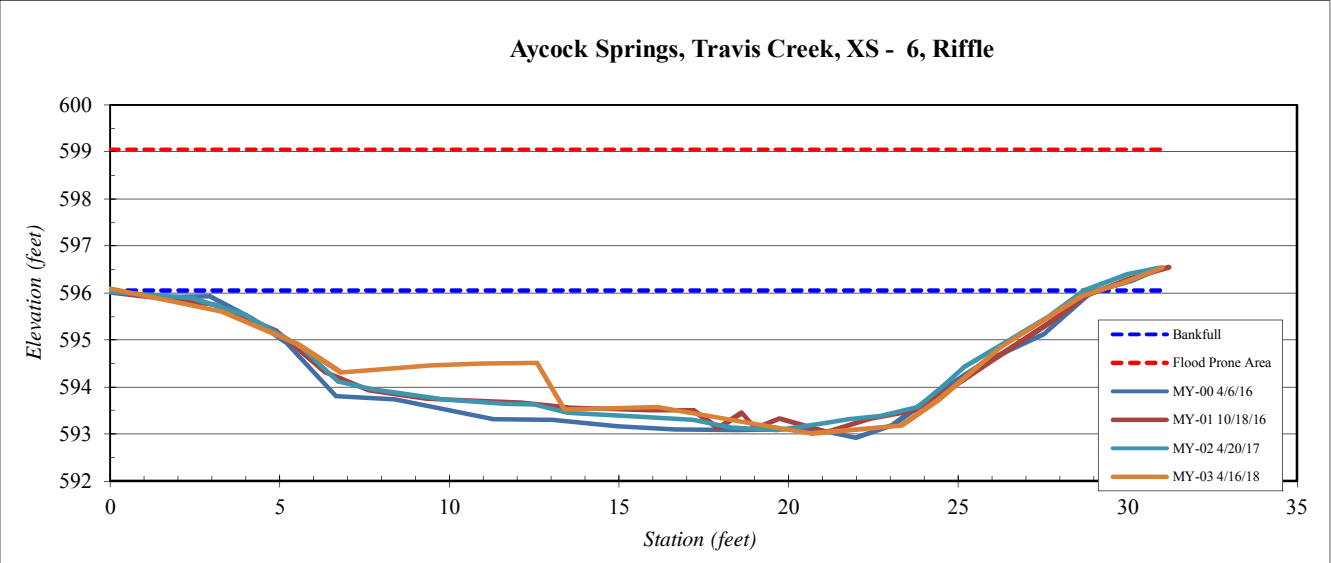


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 7, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	596.3
3.6	596.0
6.2	595.4
7.3	595.2
8.9	594.8
9.9	594.4
11.0	594.0
12.1	593.7
13.6	593.3
14.2	593.2
15.8	593.2
16.9	593.1
18.2	592.9
19.5	593.0
20.9	592.9
21.7	592.6
22.4	592.8
23.5	592.9
24.4	593.4
25.7	593.5
26.0	593.9
27.0	594.3
28.5	595.0
30.4	595.7
32.1	595.7

SUMMARY DATA	
Bankfull Elevation:	595.4
Bankfull Cross-Sectional Area:	44.9
Bankfull Width:	25.1
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	3.0
Mean Depth at Bankfull:	1.8
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

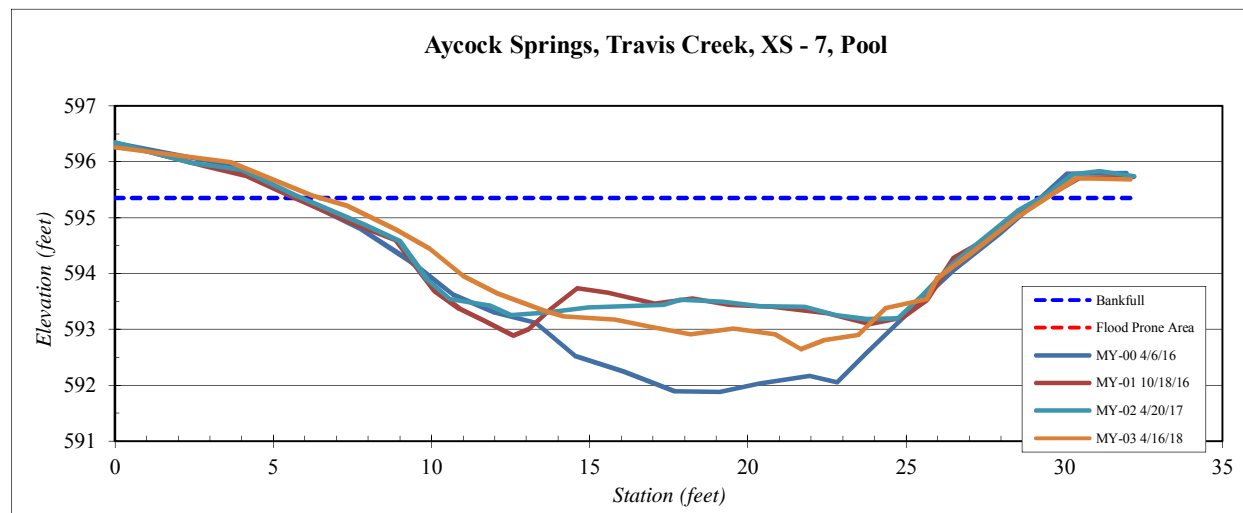

Note: Sediment Deposition in pool appears natural and is not expected to lead to instability.


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 8, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	596.49
2.4	596.25
4.8	595.54
6.5	594.70
8.4	593.25
11.1	592.95
13.0	593.07
14.8	592.90
16.2	593.11
16.8	593.62
19.1	593.29
20.5	593.51
21.7	594.56
23.4	594.42
25.4	594.39
27.2	595.06
29.5	595.96
30.7	596.37
31.6	596.78
32.6	597.17
34.5	597.5

SUMMARY DATA	
Bankfull Elevation:	596.3
Bankfull Cross-Sectional Area:	58.3
Bankfull Width:	28.0
Flood Prone Area Elevation:	599.7
Flood Prone Width:	150.0
Max Depth at Bankfull:	3.4
Mean Depth at Bankfull:	2.1
W / D Ratio:	13.4
Entrenchment Ratio:	5.4
Bank Height Ratio:	1.0

Stream Type C/E

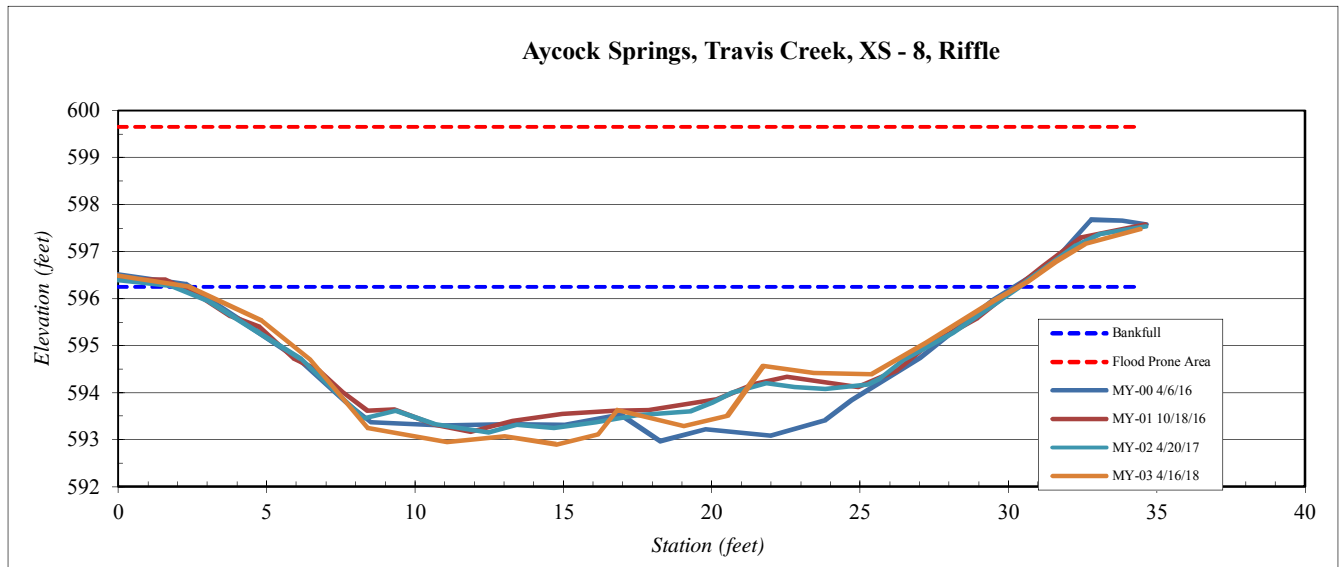


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 9, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.0	596.3
2.0	596.2
4.1	595.8
5.4	595.4
6.6	595.3
7.4	594.9
8.6	594.3
9.4	593.5
11.1	592.8
13.1	593.0
14.3	592.8
15.7	592.5
17.3	592.5
19.1	592.2
20.8	592.1
22.1	592.4
23.2	592.5
23.9	593.2
24.8	593.7
25.6	594.1
27.2	594.7
28.9	595.2
30.6	595.5
31.8	596.0
33.5	596.3
35.4	596.7

SUMMARY DATA	
Bankfull Elevation:	595.9
Bankfull Cross-Sectional Area:	60.8
Bankfull Width:	27.8
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	3.8
Mean Depth at Bankfull:	2.2
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.05



Stream Type	C/E
--------------------	-----

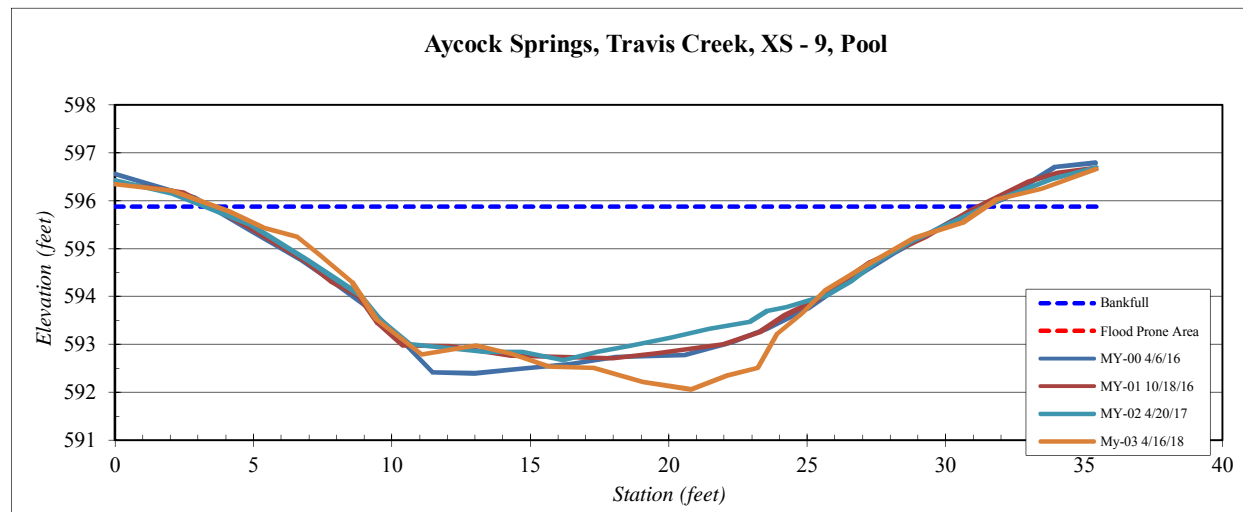


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 10, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
-0.2	597.6
6.5	596.5
9.9	595.9
12.2	595.6
14.1	595.6
16.4	595.1
17.9	594.4
19.1	594.4
20.4	594.2
21.4	593.7
22.1	593.5
23.3	593.4
24.1	593.3
25.3	593.0
26.7	592.9
28.2	592.8
29.7	592.6
31.0	592.6
32.2	592.6
33.5	592.7
34.2	592.9
34.8	593.3
35.8	593.9
36.7	594.5
38.4	595.5
39.4	596.0
40.2	596.2
41.6	596.8
43.2	597.1
44.5	597.3
46.2	597.7
48.0	597.9
49.6	597.9
51.3	598.1

SUMMARY DATA	
Bankfull Elevation:	596.9
Bankfull Cross-Sectional Area:	87.5
Bankfull Width:	37.5
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	4.3
Mean Depth at Bankfull:	2.3
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

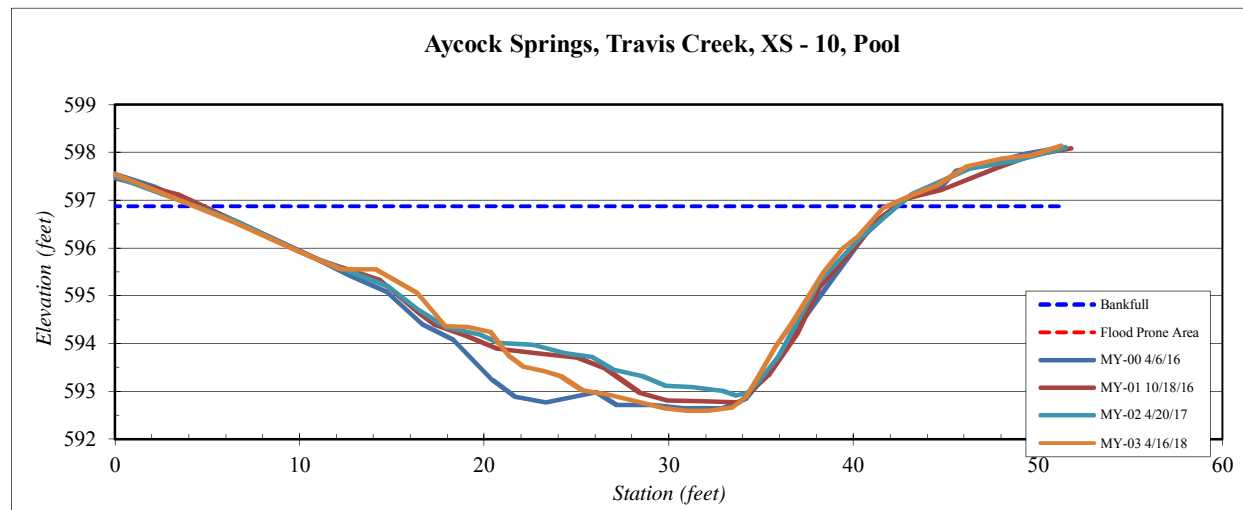


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 11, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.2	597.55
2.7	597.37
4.0	596.73
5.9	596.52
7.9	595.87
9.4	595.10
10.5	594.67
11.2	594.17
12.3	593.30
14.3	593.19
16.3	593.06
19.2	593.01
20.7	593.39
21.9	593.30
23.4	593.77
25.0	594.10
27.0	594.19
28.6	594.50
31.0	594.79
32.5	595.39
33.8	596.0
35.5	596.7
37.6	596.9
41.8	597.0

SUMMARY DATA	
Bankfull Elevation:	596.7
Bankfull Cross-Sectional Area:	69.6
Bankfull Width:	30.7
Flood Prone Area Elevation:	600.3
Flood Prone Width:	150.0
Max Depth at Bankfull:	3.6
Mean Depth at Bankfull:	2.3
W / D Ratio:	13.5
Entrenchment Ratio:	4.9
Bank Height Ratio:	1.00

Stream Type	C/E
-------------	-----

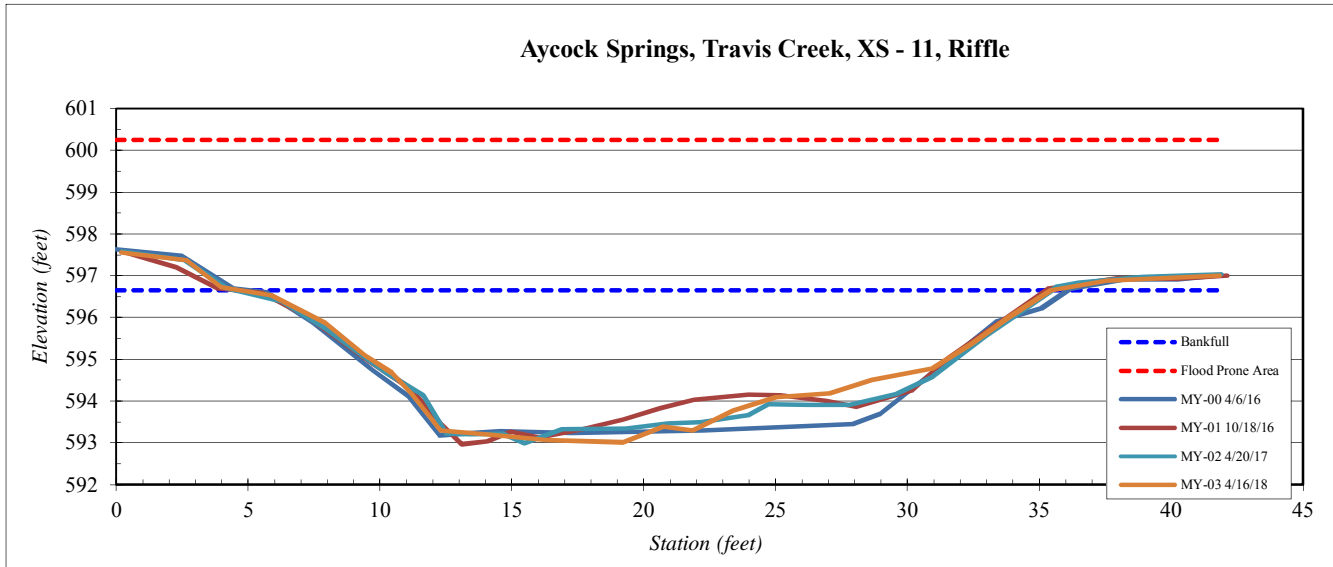


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 12, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	598.42
4.5	598.06
7.9	597.38
10.5	596.75
12.3	596.02
13.4	595.39
14.4	594.87
16.6	594.58
18.0	594.64
20.3	594.63
21.1	594.46
22.0	594.53
23.1	594.44
24.0	594.65
24.8	594.82
25.8	595.23
27.4	595.19
28.4	595.40
30.1	595.72
32.1	596.27
34.3	597.1
37.3	598.4
39.5	598.4

SUMMARY DATA	
Bankfull Elevation:	598.0
Bankfull Cross-Sectional Area:	67.9
Bankfull Width:	31.3
Flood Prone Area Elevation:	601.5
Flood Prone Width:	150.0
Max Depth at Bankfull:	3.5
Mean Depth at Bankfull:	2.2
W / D Ratio:	14.4
Entrenchment Ratio:	4.8
Bank Height Ratio:	1.03

Stream Type C/E

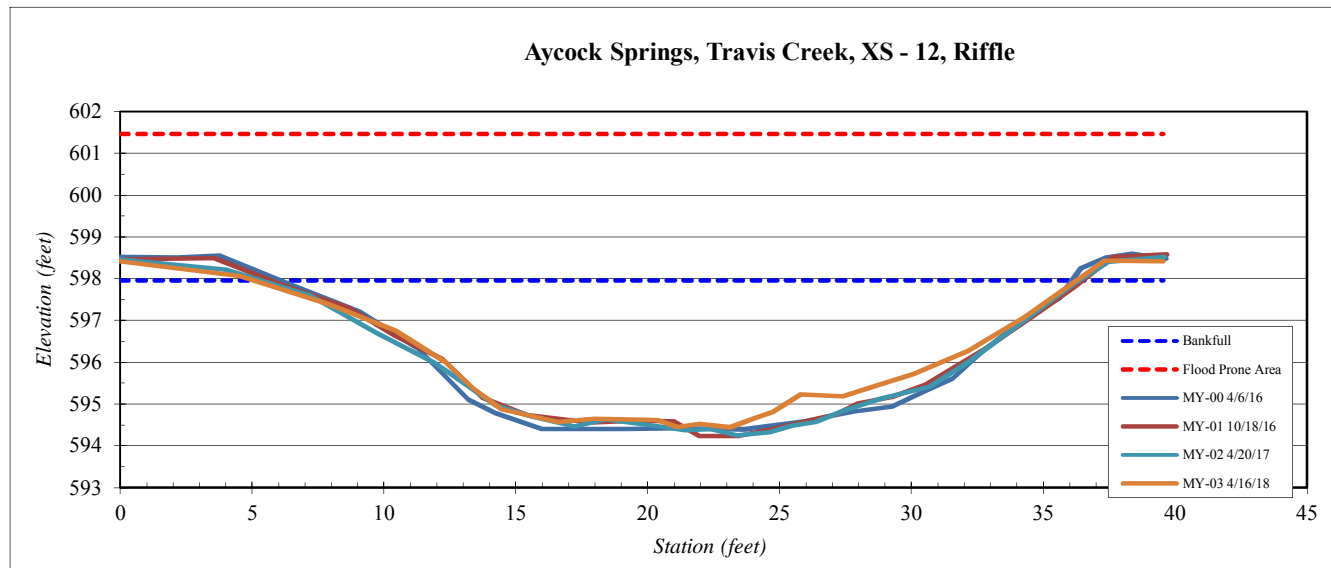


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 13, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	597.6
1.8	597.6
3.5	597.1
6.1	596.3
7.5	595.8
8.4	595.5
9.1	595.0
10.4	594.3
11.6	594.1
13.5	594.2
15.2	594.4
16.4	594.5
17.9	595.0
18.9	595.3
19.8	595.7
20.5	596.1
22.9	596.4
24.6	596.9
26.6	597.1
28.5	597.3
30.0	597.9
30.7	598.1
32.7	598.6
34.7	598.9

SUMMARY DATA	
Bankfull Elevation:	597.6
Bankfull Cross-Sectional Area:	48.2
Bankfull Width:	27.8
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	3.5
Mean Depth at Bankfull:	1.7
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

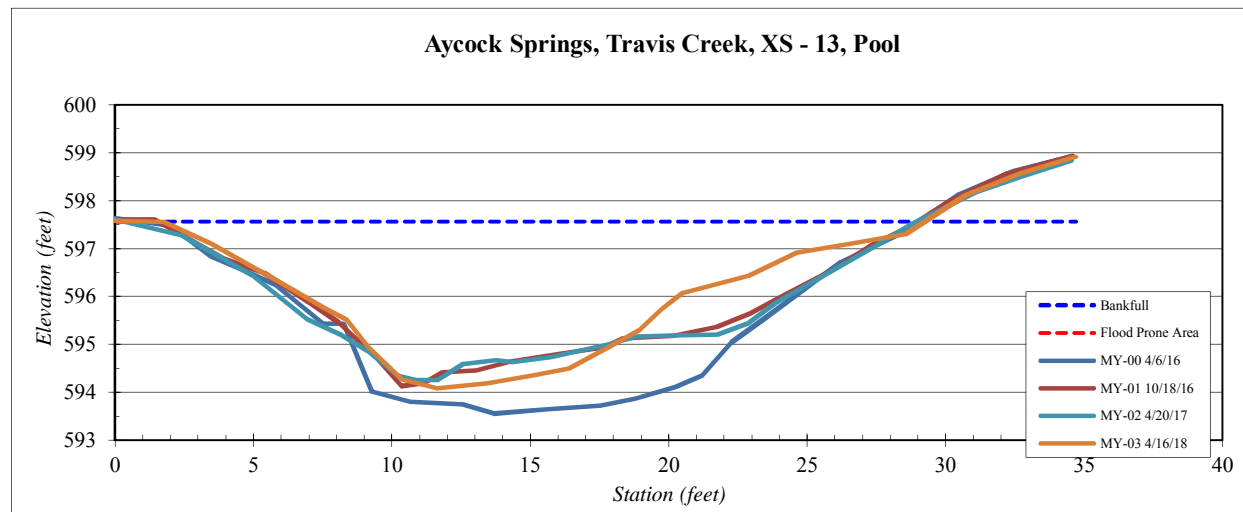

Note: Sediment Deposition in pool appears natural and is not expected to lead to instability.


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	Travis Creek, XS - 14, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.4	599.16
0.8	599.15
3.4	598.09
5.8	597.18
7.1	596.61
8.2	596.51
9.3	595.99
10.3	595.56
10.9	594.93
12.6	594.82
13.7	594.80
14.5	594.59
15.4	594.37
16.1	594.37
16.9	594.74
17.8	594.77
19.1	594.58
20.1	594.67
20.6	595.02
21.3	595.36
21.6	595.7
22.7	596.0
23.5	595.9
24.4	595.8
25.6	595.5
26.3	595.5
27.3	595.7
28.4	596.1
29.3	596.4
30.9	597.3
32.0	597.8
33.5	598.6
35.2	599.2
37.7	599.7

SUMMARY DATA	
Bankfull Elevation:	599.0
Bankfull Cross-Sectional Area:	94.6
Bankfull Width:	33.6
Flood Prone Area Elevation:	603.6
Flood Prone Width:	150.0
Max Depth at Bankfull:	4.6
Mean Depth at Bankfull:	2.8
W / D Ratio:	11.9
Entrenchment Ratio:	4.5
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

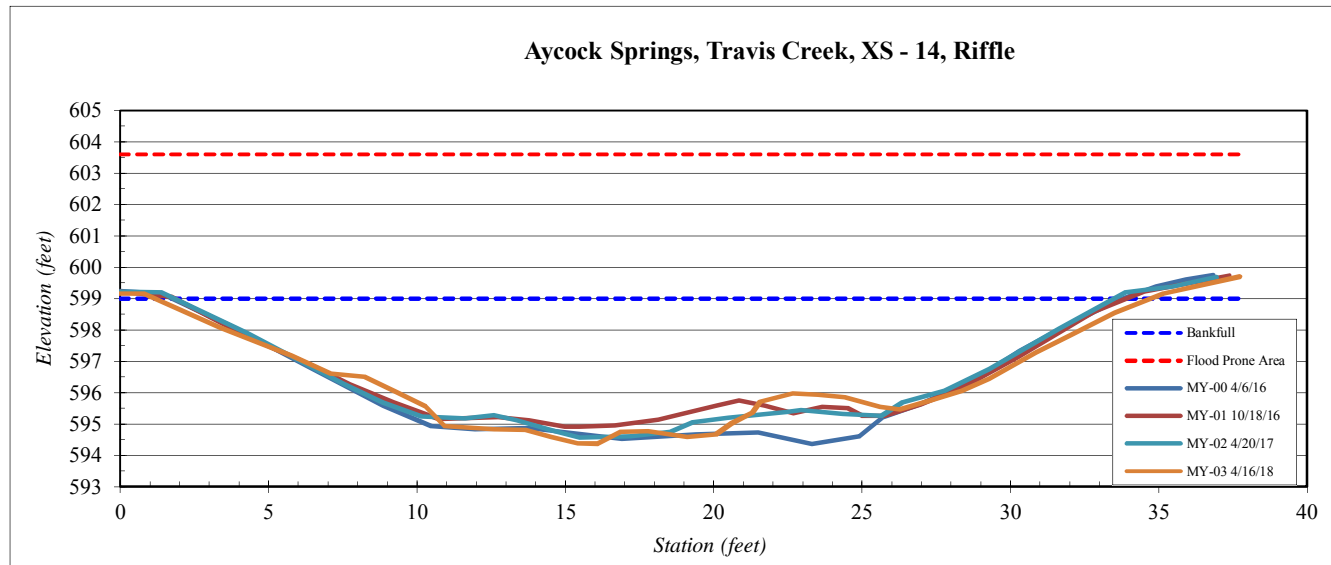


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 1, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	591.42
1.4	591.44
2.9	591.25
3.9	591.00
4.5	590.84
5.4	590.71
6.2	590.64
6.7	590.70
7.2	590.80
7.8	590.66
8.5	590.72
9.0	590.85
9.4	590.93
10.0	591.15
10.8	591.48
11.8	591.72
12.5	591.75
13.2	591.75
14.3	591.84

SUMMARY DATA	
Bankfull Elevation:	591.4
Bankfull Cross-Sectional Area:	4.4
Bankfull Width:	9.1
Flood Prone Area Elevation:	592.2
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.8
Mean Depth at Bankfull:	0.5
W / D Ratio:	18.8
Entrenchment Ratio:	9.9
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

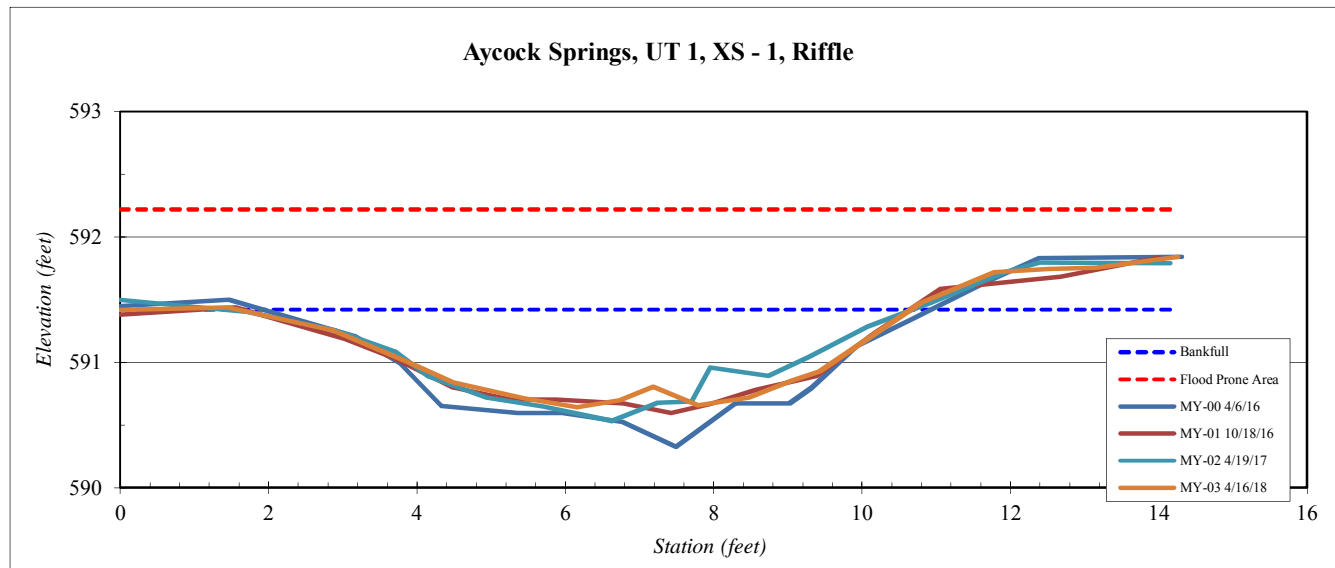


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 2, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	591.68
1.4	591.51
2.1	591.51
3.0	591.47
3.7	591.22
4.3	591.16
5.1	591.04
5.5	591.04
6.3	590.95
6.8	590.98
7.3	590.96
7.8	590.98
8.2	591.03
8.4	591.05
9.1	591.08
9.6	591.14
10.2	591.14
10.6	591.35
11.3	591.46
12.3	591.45
13.7	591.6

SUMMARY DATA	
Bankfull Elevation:	591.6
Bankfull Cross-Sectional Area:	3.7
Bankfull Width:	10.2
Flood Prone Area Elevation:	592.2
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.4
W / D Ratio:	28.1
Entrenchment Ratio:	8.8
Bank Height Ratio:	<1

Stream Type C/E

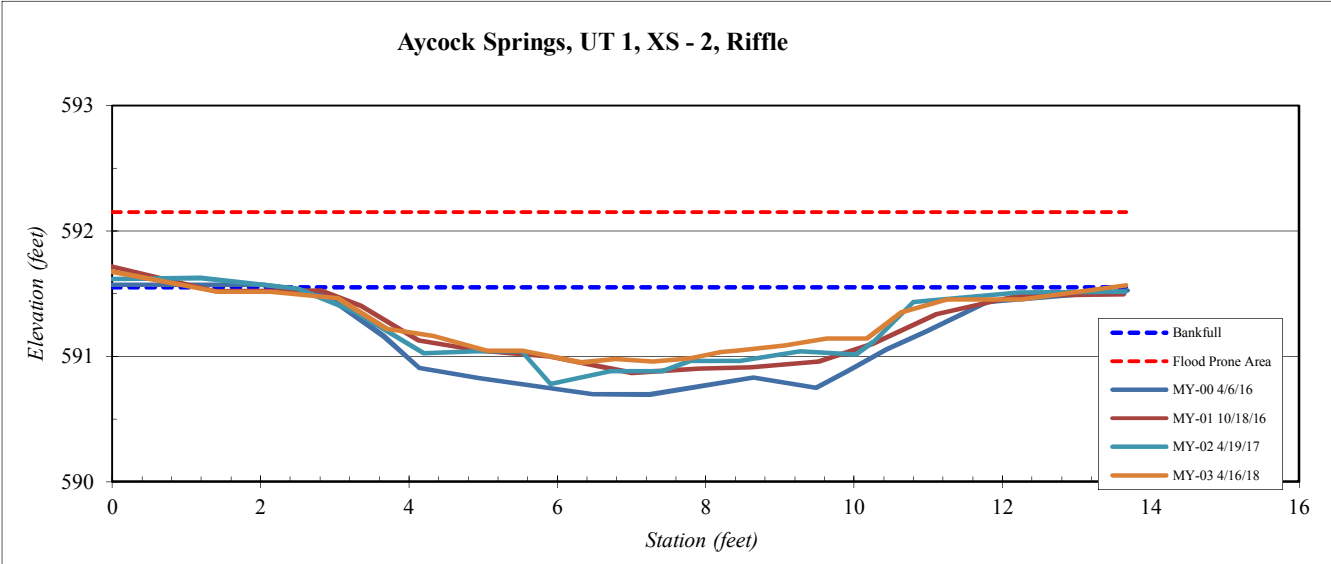


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 3, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.3	592.2
1.2	592.2
2.3	592.1
3.1	591.9
3.7	591.6
4.2	591.3
4.5	591.3
5.0	591.1
5.7	590.7
6.2	590.5
6.6	590.6
7.0	590.7
7.4	590.8
7.8	590.9
8.3	591.0
8.5	591.1
9.2	591.2
9.9	591.3
10.5	591.5
11.2	591.6
11.7	591.9
12.4	591.9
13.2	592.0
14.5	592.00

SUMMARY DATA	
Bankfull Elevation:	591.9
Bankfull Cross-Sectional Area:	6.4
Bankfull Width:	9.5
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.4
Mean Depth at Bankfull:	0.7
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

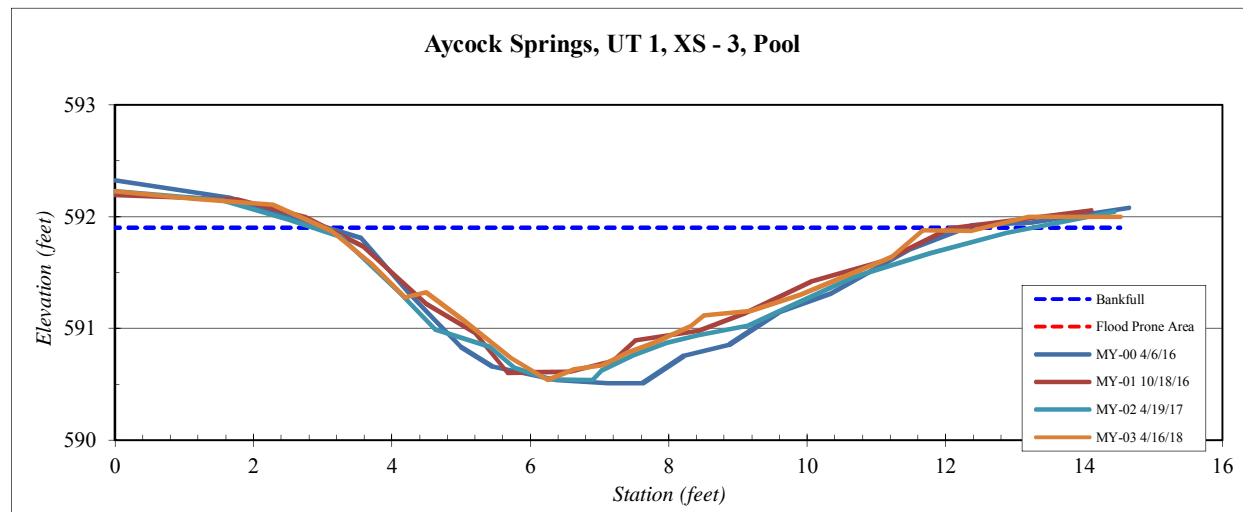


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 4, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	591.97
1.3	591.85
2.2	591.63
3.3	591.46
4.2	591.29
4.9	591.21
5.8	591.11
6.5	591.11
7.2	591.02
7.7	591.02
8.6	591.01
9.3	591.44
9.9	591.68
10.6	592.01
11.2	592.18
11.9	592.29
12.8	592.27

SUMMARY DATA	
Bankfull Elevation:	591.9
Bankfull Cross-Sectional Area:	5.7
Bankfull Width:	10.2
Flood Prone Area Elevation:	592.8
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.9
Mean Depth at Bankfull:	0.6
W / D Ratio:	18.3
Entrenchment Ratio:	8.8
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

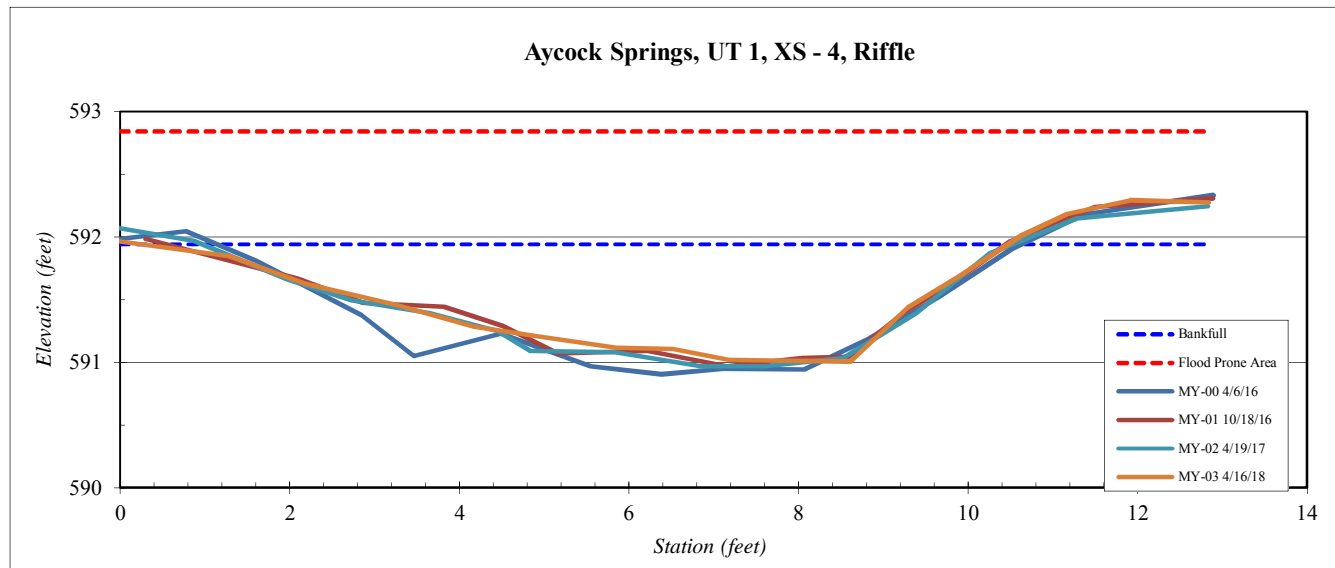


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 5, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	592.42
1.0	592.50
2.0	592.27
3.0	591.95
3.9	591.65
4.6	591.46
5.0	591.39
5.8	591.42
6.6	591.41
7.0	591.24
7.5	591.13
7.9	591.12
8.4	591.13
8.7	591.52
9.2	591.37
10.1	591.53
10.6	591.74
11.5	592.15
12.2	592.31
13.0	592.40
13.7	592.4

SUMMARY DATA	
Bankfull Elevation:	592.2
Bankfull Cross-Sectional Area:	5.8
Bankfull Width:	9.2
Flood Prone Area Elevation:	593.2
Flood Prone Width:	90.0
Max Depth at Bankfull:	1.0
Mean Depth at Bankfull:	0.6
W / D Ratio:	14.6
Entrenchment Ratio:	9.8
Bank Height Ratio:	1.0

Stream Type	C/E
-------------	-----

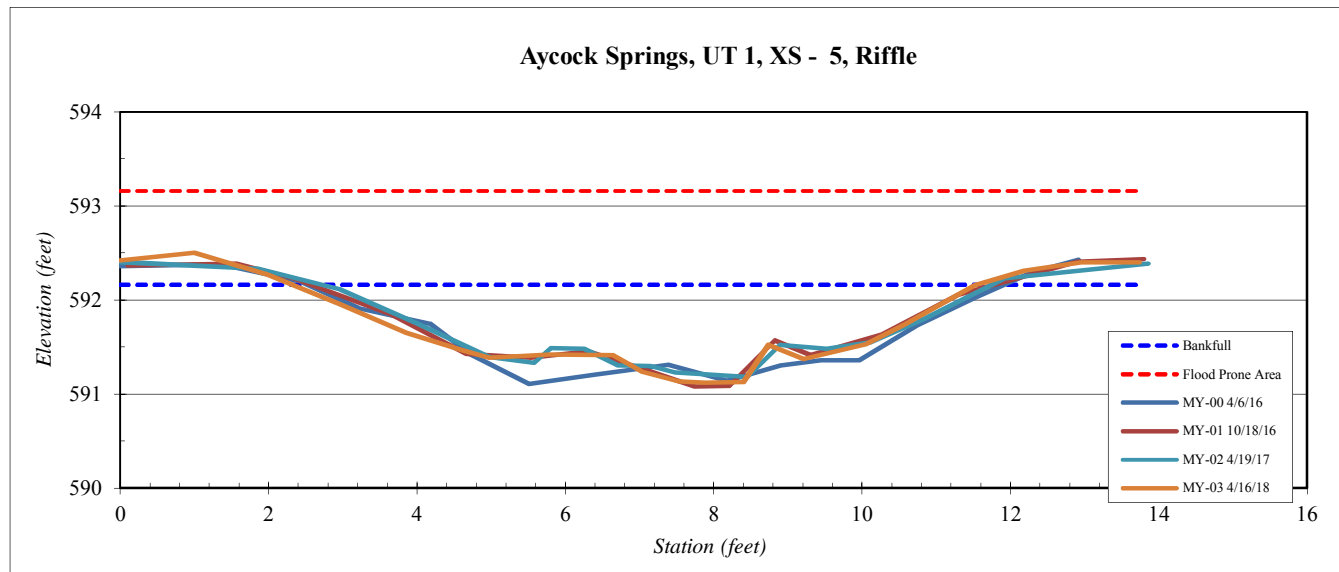


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 6, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	592.79
0.9	592.84
1.7	592.84
2.3	592.59
2.8	592.34
3.9	592.26
4.5	592.19
5.3	592.22
6.0	592.29
7.0	592.28
8.1	592.20
8.8	592.46
9.4	592.69
10.1	592.69
11.0	592.62
11.8	592.60

SUMMARY DATA	
Bankfull Elevation:	592.6
Bankfull Cross-Sectional Area:	2.2
Bankfull Width:	6.9
Flood Prone Area Elevation:	593.0
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.4
Mean Depth at Bankfull:	0.3
W / D Ratio:	21.6
Entrenchment Ratio:	13.0
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

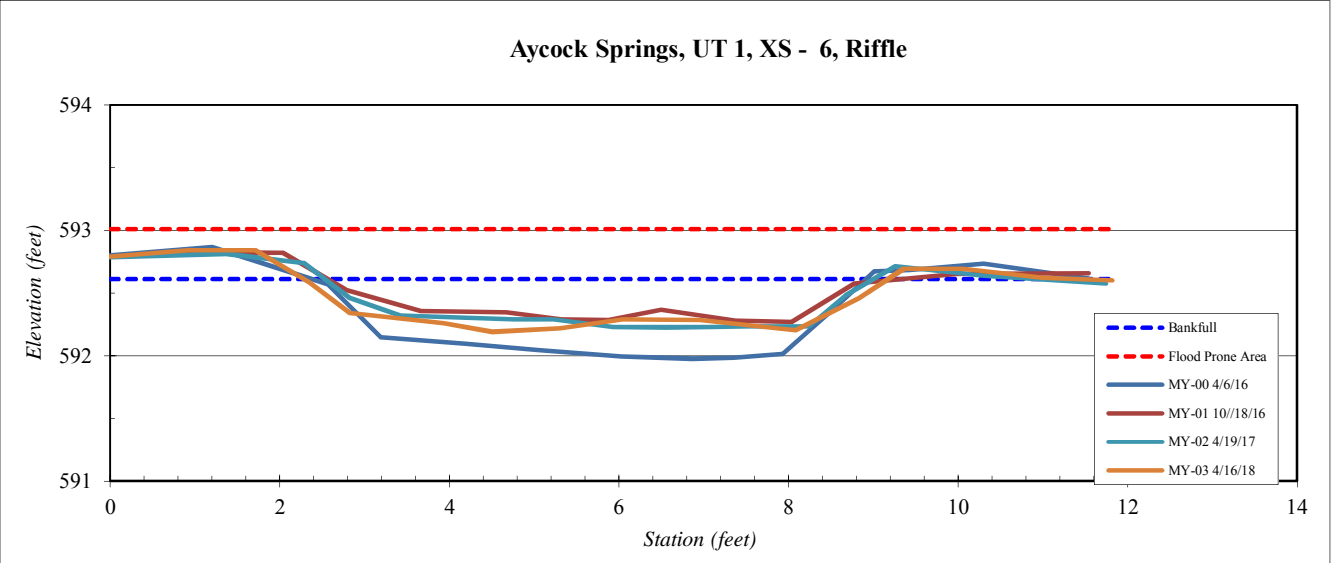


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 7, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.1	593.15
1.2	593.26
1.7	592.93
2.3	592.78
3.0	592.71
3.9	592.71
4.8	592.53
5.1	592.38
5.5	592.39
6.1	592.29
6.9	592.38
7.0	592.38
7.5	592.60
8.3	592.93
8.9	593.05
9.8	593.23
11.4	593.23

SUMMARY DATA	
Bankfull Elevation:	593.0
Bankfull Cross-Sectional Area:	2.4
Bankfull Width:	6.7
Flood Prone Area Elevation:	593.7
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.4
W / D Ratio:	18.7
Entrenchment Ratio:	13.4
Bank Height Ratio:	1.0



Stream Type	C/E
-------------	-----

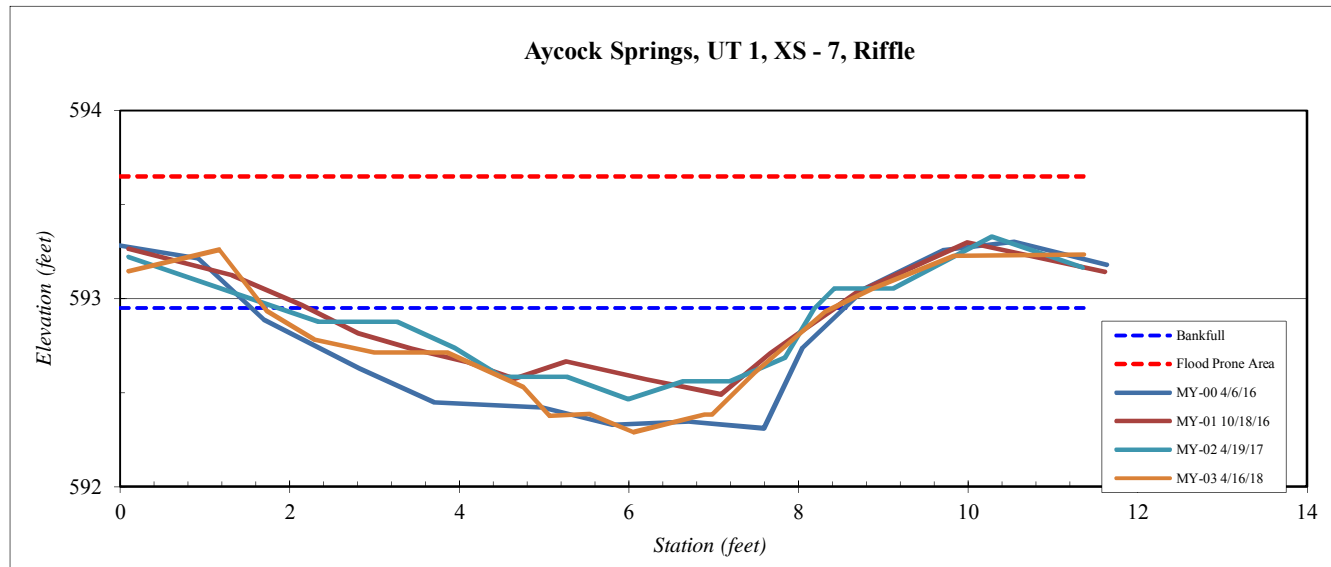


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 8, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	593.3
1.3	593.2
2.3	593.3
3.0	593.1
3.4	592.9
4.1	592.4
4.6	592.3
4.9	592.4
5.7	592.2
6.1	592.2
6.8	592.2
7.2	592.5
7.8	592.9
8.4	593.2
9.2	593.3
9.8	593.5
11.3	593.4

SUMMARY DATA	
Bankfull Elevation:	593.2
Bankfull Cross-Sectional Area:	3.6
Bankfull Width:	6.0
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.0
Mean Depth at Bankfull:	0.6
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

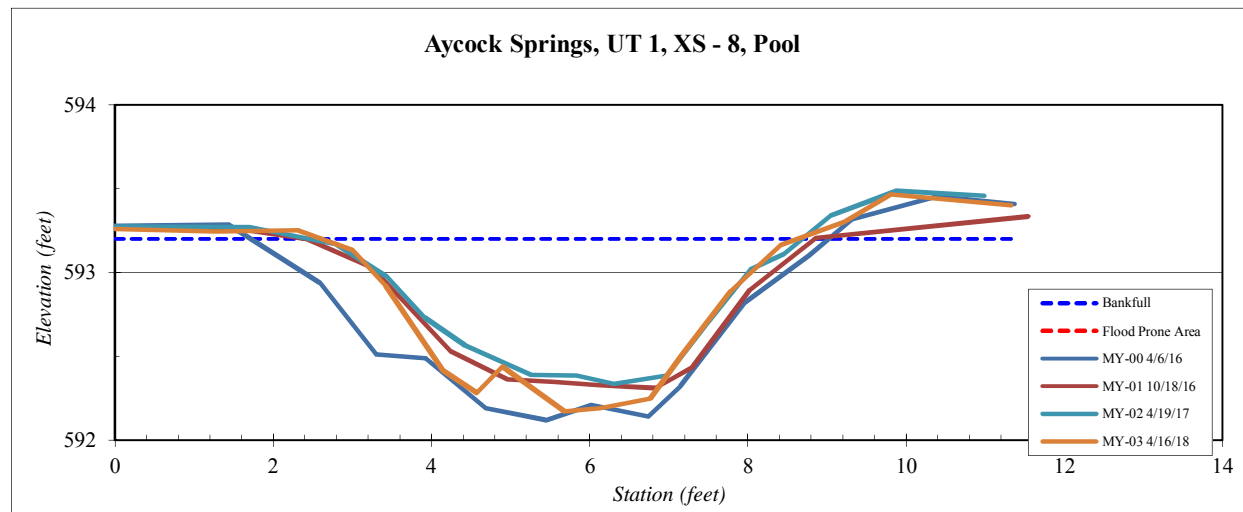

Note: Cross Sections 8 and 9 (UT 1) are located in the vicinity of a bed material repair. Additional bed material was added by hand in this reach.


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 9, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	594.89
1.3	594.85
1.9	594.64
3.3	594.64
4.0	594.53
4.5	594.39
4.9	594.27
5.5	594.42
5.8	594.06
6.4	594.19
7.1	594.36
7.5	594.58
8.3	594.68
9.2	594.95
10.5	594.83
11.6	594.82

SUMMARY DATA	
Bankfull Elevation:	594.7
Bankfull Cross-Sectional Area:	1.6
Bankfull Width:	6.7
Flood Prone Area Elevation:	595.3
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.2
W / D Ratio:	28.1
Entrenchment Ratio:	13.4
Bank Height Ratio:	1.0

Stream Type C/E

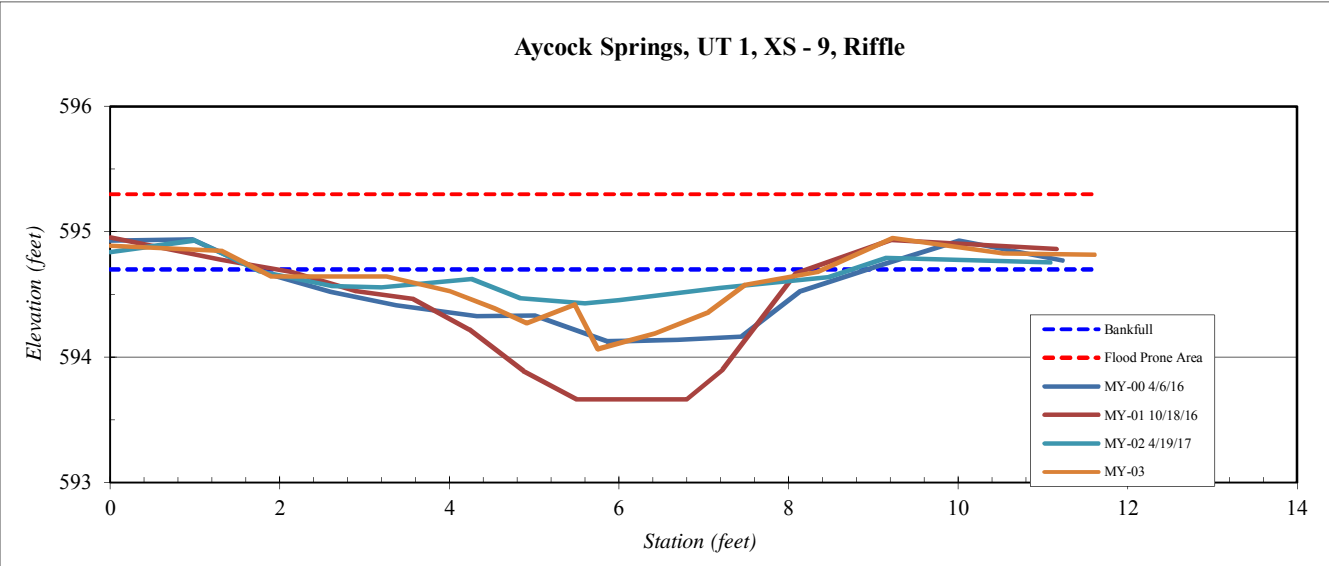

Note: Cross Sections 8 and 9 (UT 1) are located in the vicinity of a bed material repair. Additional bed material was added by hand in this reach.


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 10, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.2	595.7
0.7	595.6
1.6	595.5
2.4	595.3
3.1	595.1
3.6	594.7
4.3	594.3
4.9	593.9
5.8	593.5
6.5	593.5
7.0	593.5
7.5	593.6
8.0	593.7
8.5	594.0
8.9	595.0
9.6	595.4
10.2	595.5
11.1	595.6
12.5	595.8

SUMMARY DATA	
Bankfull Elevation:	594.9
Bankfull Cross-Sectional Area:	5.5
Bankfull Width:	5.5
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.4
Mean Depth at Bankfull:	1.0
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.14

Stream Type	C/E
--------------------	-----

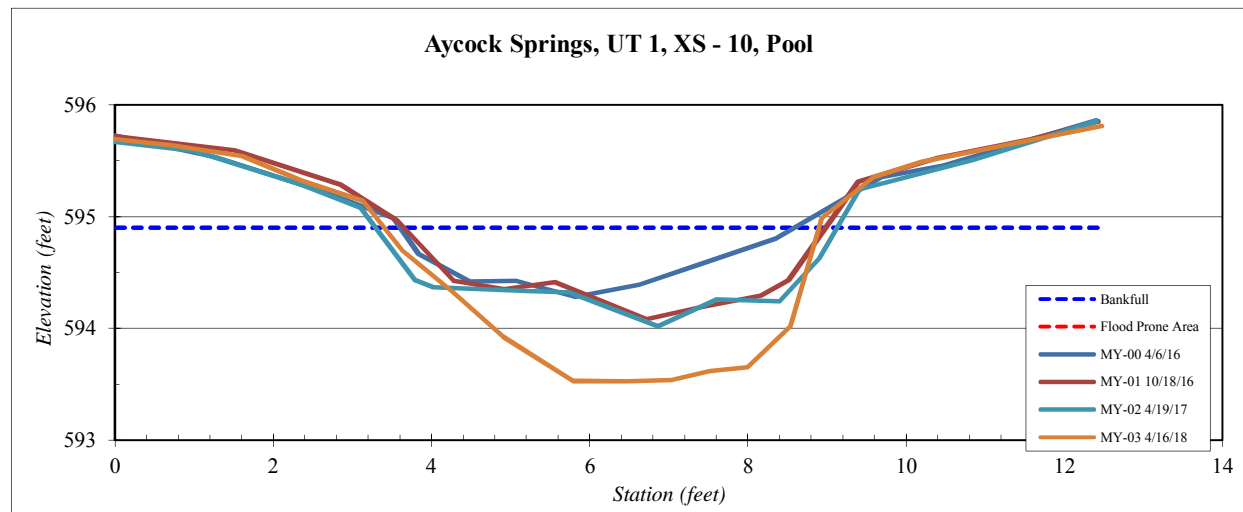


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 11, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	596.08
1.1	596.08
1.6	596.08
2.6	595.82
2.9	595.74
3.4	595.74
3.8	595.17
4.5	595.32
5.4	595.22
5.7	595.47
6.3	595.57
7.0	595.41
8.2	595.81
8.9	595.90
10.1	596.06
11.1	596.17
12.0	596.17

SUMMARY DATA	
Bankfull Elevation:	596.1
Bankfull Cross-Sectional Area:	3.5
Bankfull Width:	8.4
Flood Prone Area Elevation:	597.0
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.9
Mean Depth at Bankfull:	0.4
W / D Ratio:	20.2
Entrenchment Ratio:	10.7
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

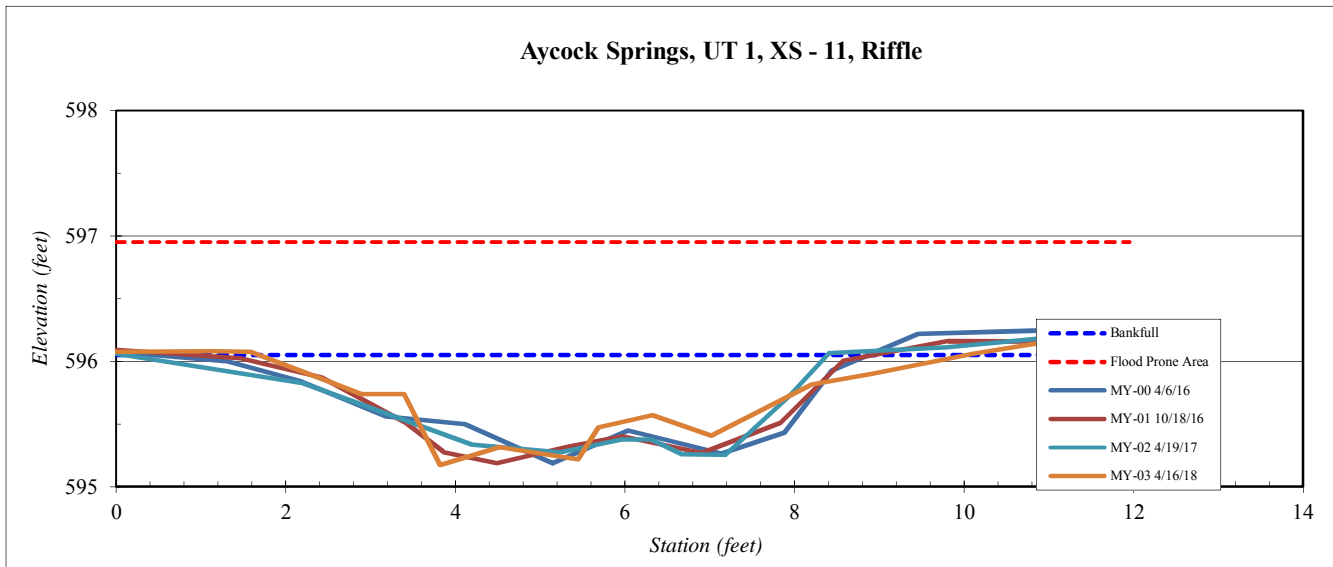


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 1, XS - 12, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	597.82
0.9	597.78
1.8	597.49
2.2	597.29
3.0	597.23
3.5	597.12
4.1	597.07
4.5	597.04
5.3	597.04
5.7	597.13
6.6	597.19
6.9	597.32
7.4	597.31
8.1	597.37
8.8	597.65
9.5	597.76
11.2	597.70

SUMMARY DATA	
Bankfull Elevation:	597.6
Bankfull Cross-Sectional Area:	2.8
Bankfull Width:	7.3
Flood Prone Area Elevation:	598.2
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.4
W / D Ratio:	19.0
Entrenchment Ratio:	12.3
Bank Height Ratio:	1.0

Stream Type: C/E

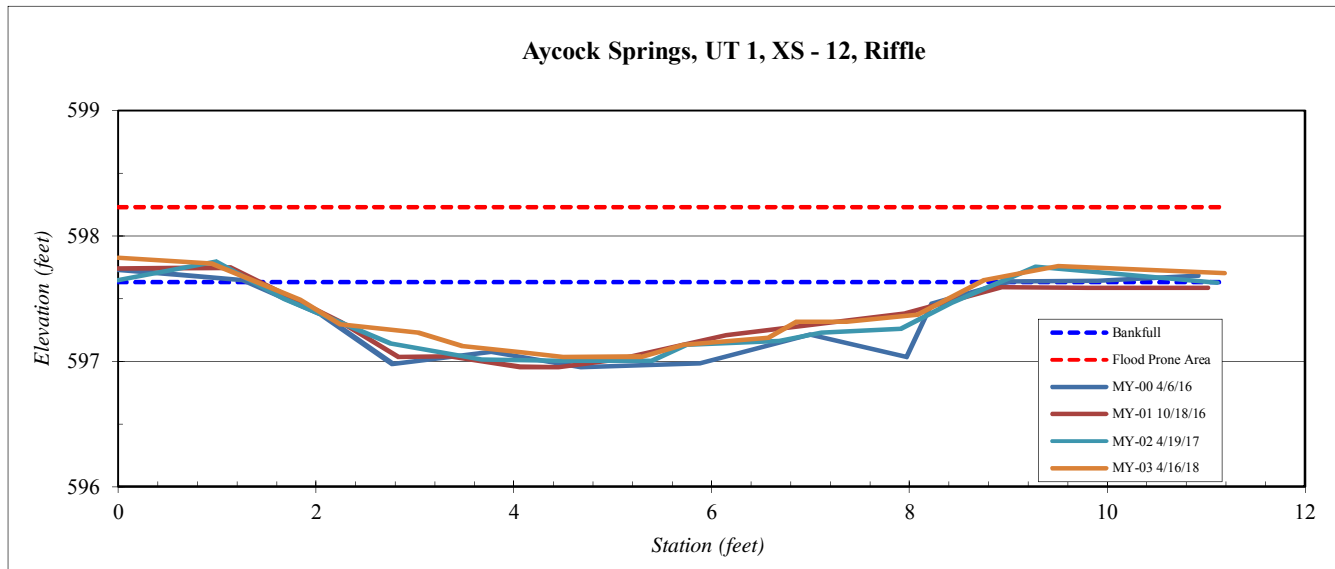


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 1, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
-0.2	593.3
1.3	593.5
2.2	593.3
3.0	593.0
3.3	592.9
3.8	592.8
4.3	592.8
5.0	592.8
5.6	592.9
6.5	593.0
7.1	593.3
7.9	593.3
8.9	593.4
9.6	593.4
10.2	593.5

SUMMARY DATA	
Bankfull Elevation:	593.4
Bankfull Cross-Sectional Area:	2.2
Bankfull Width:	7.3
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.3
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

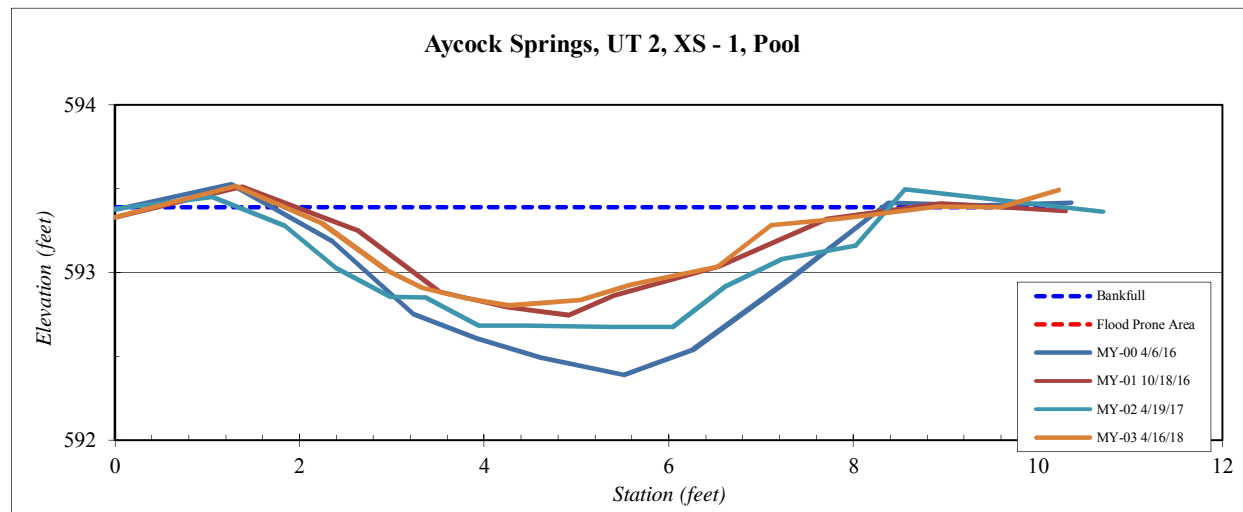


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 2, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	594.01
1.0	594.06
2.1	594.08
2.7	593.95
3.4	593.90
4.2	593.75
4.7	593.84
5.5	593.81
6.2	593.85
7.2	593.93
7.9	594.08
9.2	594.20
10.1	594.20
11.2	594.17

SUMMARY DATA	
Bankfull Elevation:	594.1
Bankfull Cross-Sectional Area:	1.0
Bankfull Width:	5.6
Flood Prone Area Elevation:	594.4
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.3
Mean Depth at Bankfull:	0.2
W / D Ratio:	31.4
Entrenchment Ratio:	16.1
Bank Height Ratio:	1.0

Stream Type C/E

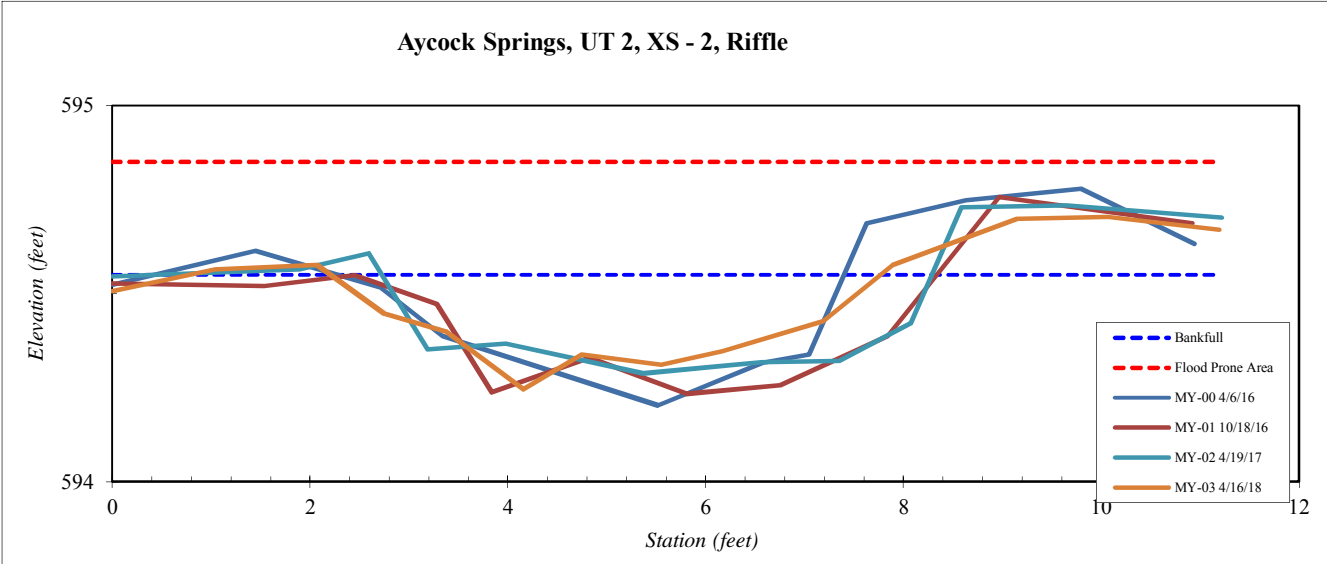


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 3, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	594.76
1.5	594.84
2.1	594.67
2.6	594.51
3.5	594.37
4.1	594.60
4.9	594.49
5.5	594.50
6.6	594.53
7.3	594.65
7.9	594.87
8.6	594.92
9.3	594.99
10.6	594.91

SUMMARY DATA	
Bankfull Elevation:	594.8
Bankfull Cross-Sectional Area:	1.2
Bankfull Width:	5.8
Flood Prone Area Elevation:	595.2
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.4
Mean Depth at Bankfull:	0.2
W / D Ratio:	28.0
Entrenchment Ratio:	15.5
Bank Height Ratio:	1.0

Stream Type C/E

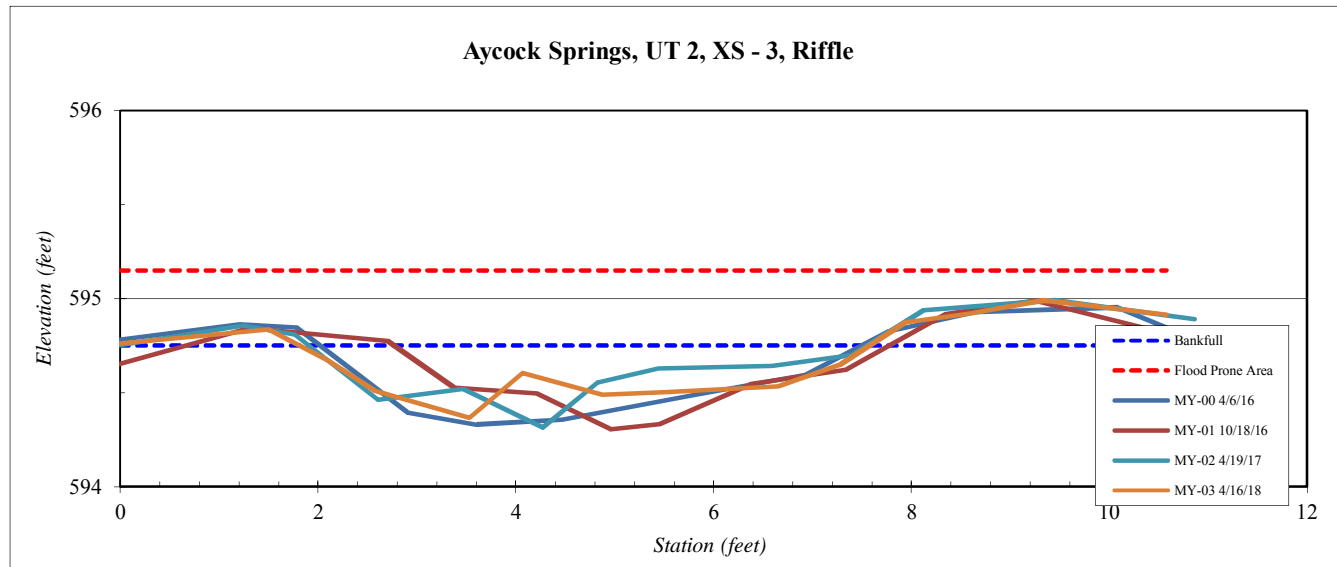


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 4, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.1	595.33
1.6	595.40
3.1	595.33
3.7	595.18
4.3	595.04
5.1	595.01
5.7	595.05
6.4	595.13
7.3	595.12
8.0	595.11
8.8	595.28
9.6	595.38
10.7	595.44
12.0	595.35

SUMMARY DATA	
Bankfull Elevation:	595.3
Bankfull Cross-Sectional Area:	0.9
Bankfull Width:	5.4
Flood Prone Area Elevation:	595.6
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.3
Mean Depth at Bankfull:	0.2
W / D Ratio:	32.4
Entrenchment Ratio:	16.7
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

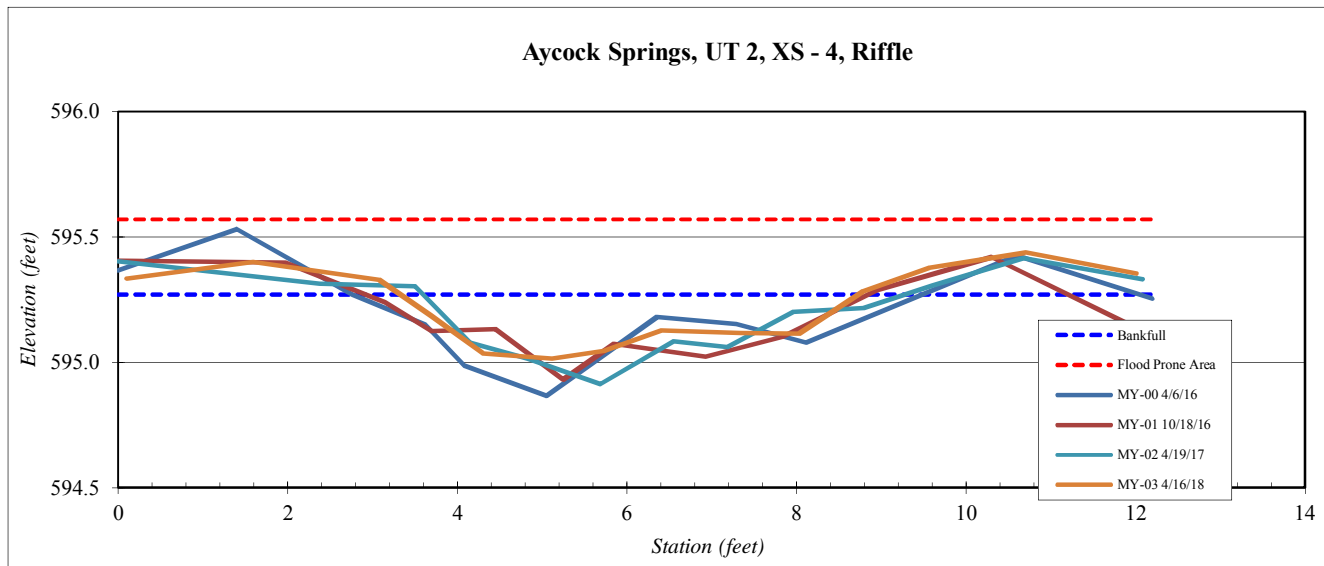


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 5, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	597.31
1.8	597.03
2.9	596.89
3.6	596.66
4.4	596.72
5.1	596.59
5.9	596.64
6.7	596.61
7.6	596.65
8.3	596.86
9.0	596.99
9.8	597.05
11.1	596.99

SUMMARY DATA	
Bankfull Elevation:	597.1
Bankfull Cross-Sectional Area:	2.9
Bankfull Width:	9.9
Flood Prone Area Elevation:	597.6
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.5
Mean Depth at Bankfull:	0.3
W / D Ratio:	33.8
Entrenchment Ratio:	9.1
Bank Height Ratio:	<1

Stream Type	C/E
-------------	-----

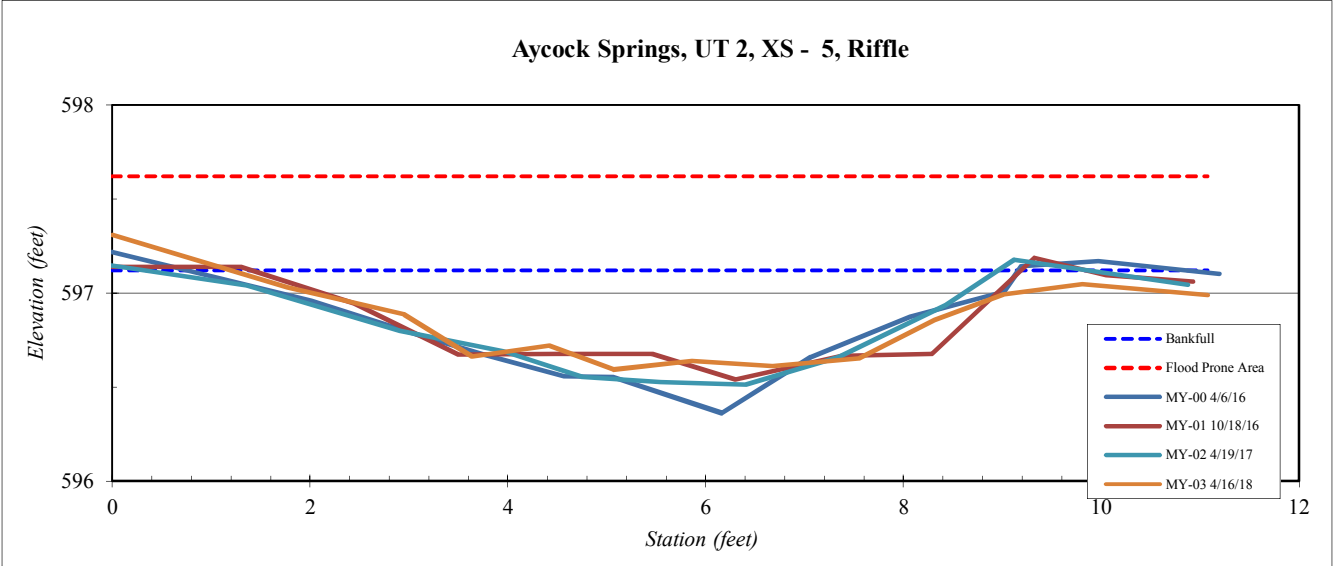


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 6, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.0	597.96
1.3	597.96
2.3	597.86
2.8	597.67
3.4	597.59
3.8	597.63
4.4	597.73
5.3	597.72
6.4	597.53
7.3	597.55
8.2	597.74
9.1	597.85
9.7	597.91
10.6	597.91
11.2	597.99

SUMMARY DATA	
Bankfull Elevation:	597.8
Bankfull Cross-Sectional Area:	1.0
Bankfull Width:	6.4
Flood Prone Area Elevation:	598.1
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.3
Mean Depth at Bankfull:	0.2
W / D Ratio:	41.0
Entrenchment Ratio:	14.1
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

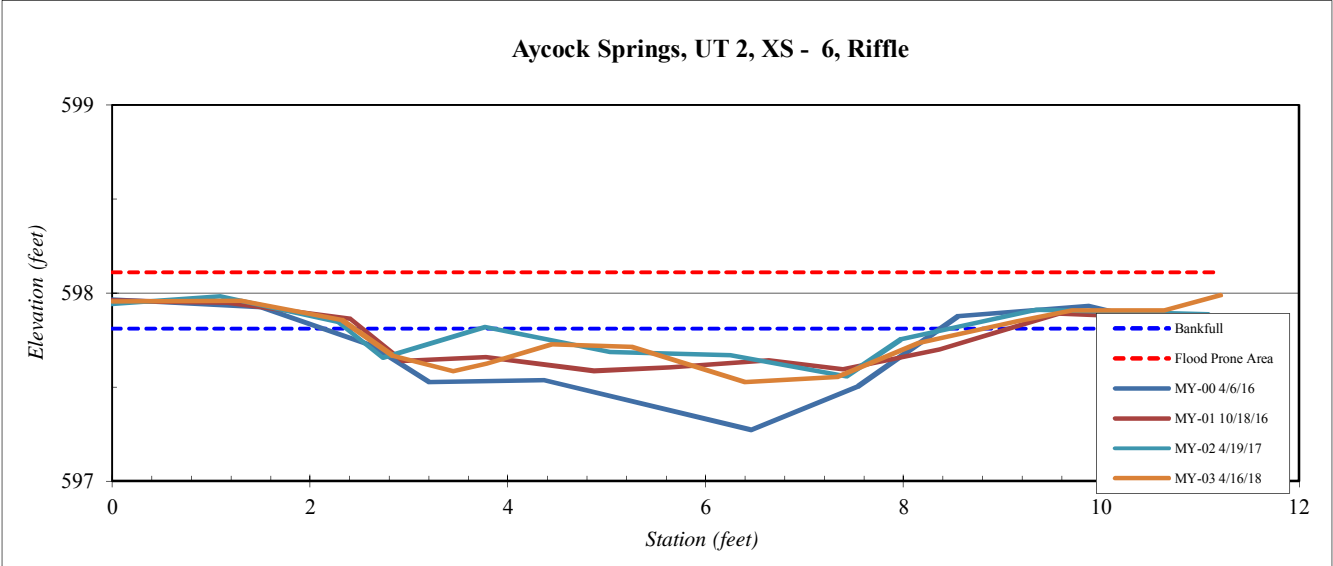


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 7, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.2	598.5
1.5	598.4
2.7	598.2
3.8	597.8
4.2	597.6
4.7	597.6
5.3	597.5
5.9	597.5
6.2	597.3
6.8	597.5
7.4	597.7
8.0	597.8
8.5	597.8
9.0	597.9
9.8	598.1
11.1	598.3
12.1	598.4
13.0	598.3

SUMMARY DATA	
Bankfull Elevation:	598.3
Bankfull Cross-Sectional Area:	3.8
Bankfull Width:	8.4
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	0.9
Mean Depth at Bankfull:	0.5
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

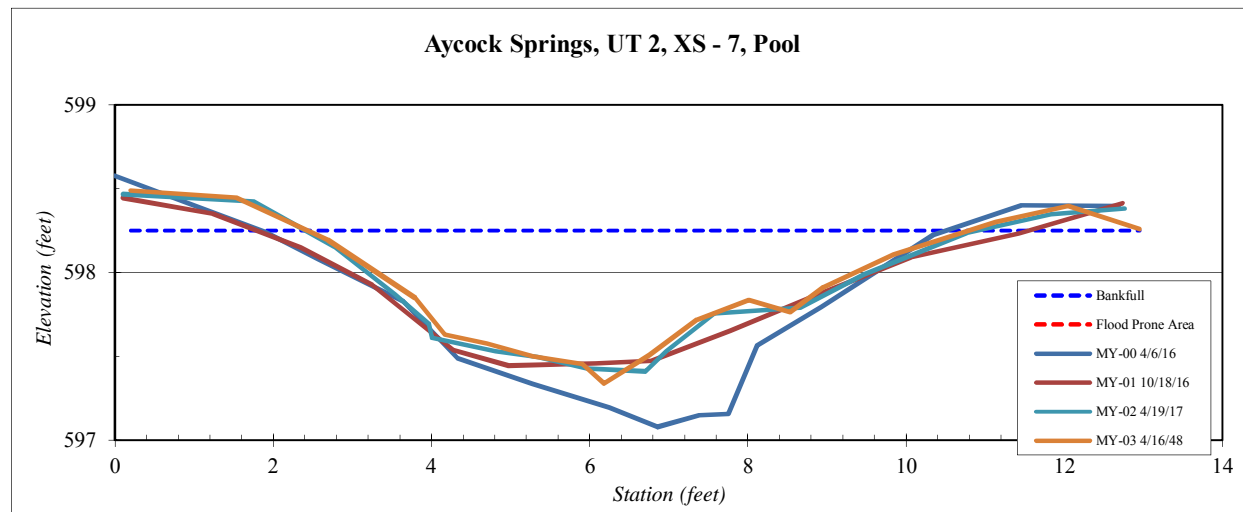


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 8, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	601.30
1.3	601.24
2.0	601.14
3.0	601.18
3.8	600.99
4.5	600.95
5.3	600.87
6.0	600.83
6.6	600.99
7.3	600.85
8.4	600.85
9.3	601.18
10.0	601.31
11.4	601.48

SUMMARY DATA	
Bankfull Elevation:	601.3
Bankfull Cross-Sectional Area:	2.8
Bankfull Width:	10.1
Flood Prone Area Elevation:	601.8
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.5
Mean Depth at Bankfull:	0.3
W / D Ratio:	36.4
Entrenchment Ratio:	8.9
Bank Height Ratio:	<1

Stream Type	C/E
--------------------	-----

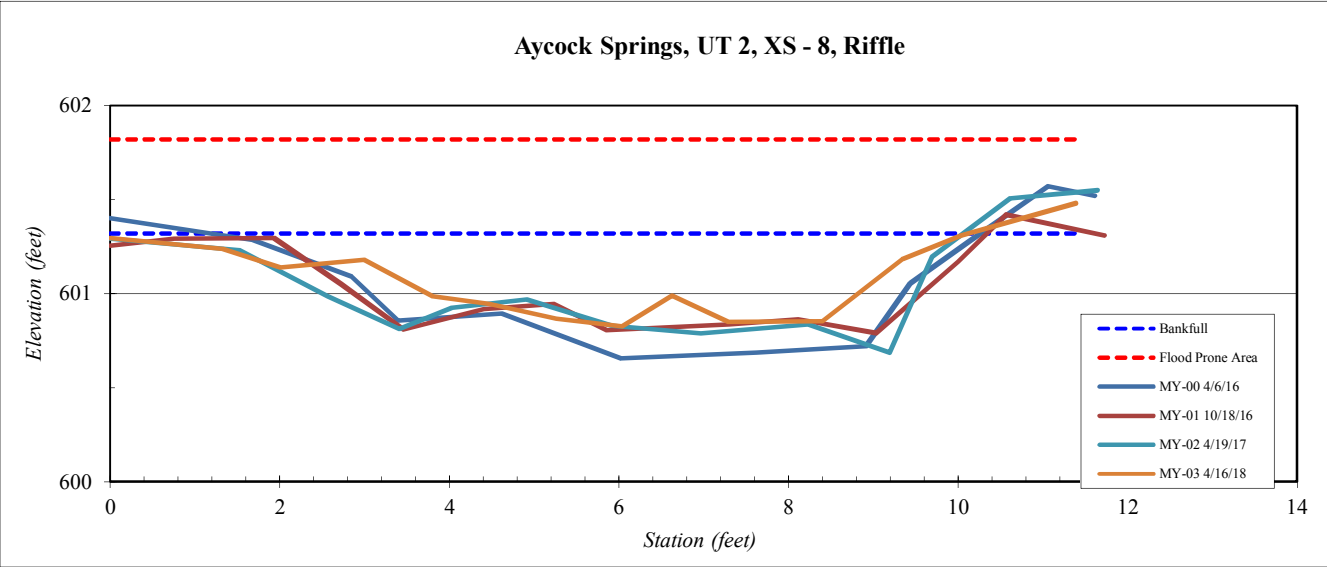


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 9, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.0	604.69
1.1	604.83
1.7	604.76
2.3	604.54
3.2	604.15
3.6	604.15
3.8	603.96
4.2	604.19
4.6	604.26
5.1	604.22
5.6	604.10
5.9	604.14
6.8	604.13
7.5	604.26
8.6	604.54
9.2	604.82
10.2	604.97

SUMMARY DATA	
Bankfull Elevation:	604.9
Bankfull Cross-Sectional Area:	4.4
Bankfull Width:	8.5
Flood Prone Area Elevation:	605.8
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.9
Mean Depth at Bankfull:	0.5
W / D Ratio:	16.4
Entrenchment Ratio:	10.6
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

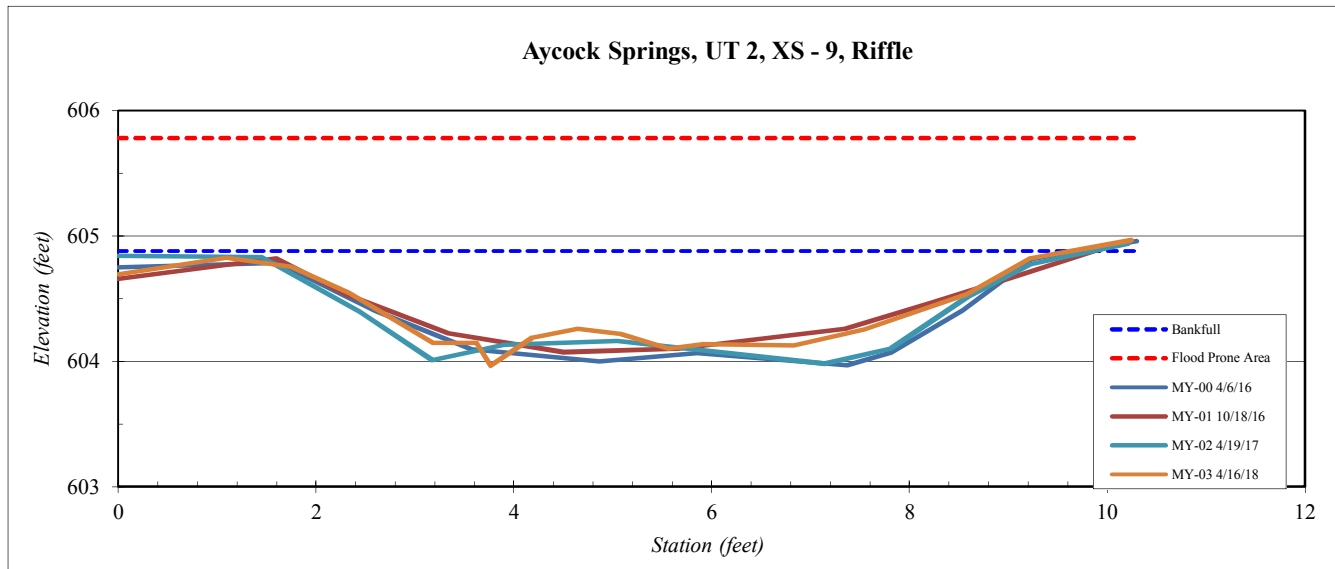


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 10, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.0	605.6
1.1	605.6
2.0	605.5
2.8	605.5
3.6	605.1
4.2	604.9
4.9	604.6
5.3	604.4
5.7	604.5
6.6	604.6
7.1	604.7
7.6	604.6
8.2	605.0
8.7	605.2
9.3	605.4
10.0	605.7
10.7	605.9
11.7	606.0

SUMMARY DATA	
Bankfull Elevation:	605.5
Bankfull Cross-Sectional Area:	4.0
Bankfull Width:	6.7
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.1
Mean Depth at Bankfull:	0.6
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

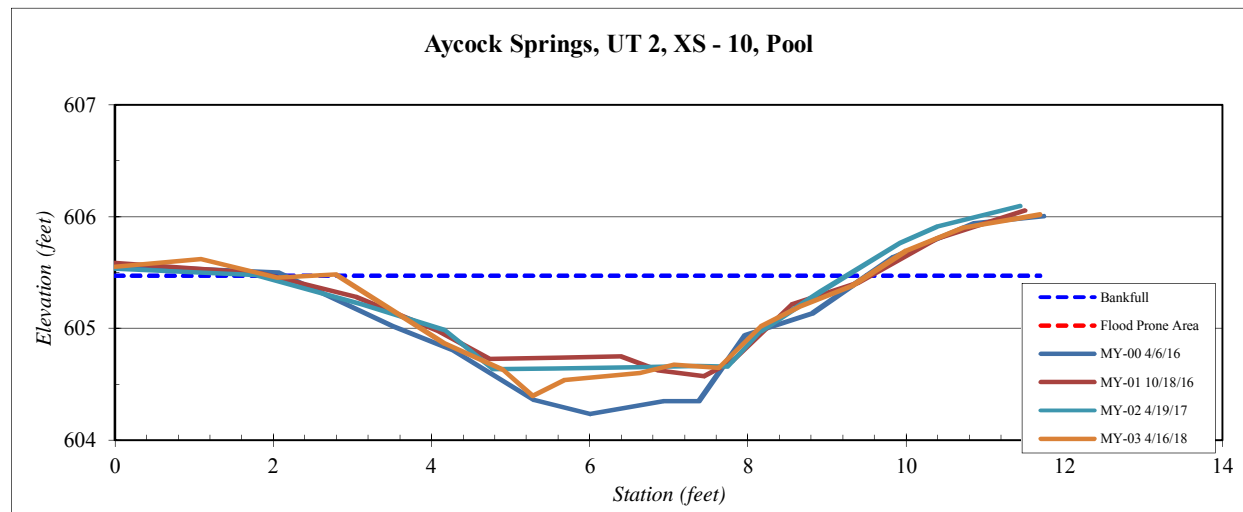


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 11, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	606.3
1.4	606.3
2.7	606.0
3.5	605.7
4.3	605.3
4.8	605.4
5.5	605.4
6.0	605.2
6.5	605.4
7.0	605.5
7.8	605.7
8.6	606.0
9.5	606.3
10.1	606.3
10.8	606.4

SUMMARY DATA	
Bankfull Elevation:	606.0
Bankfull Cross-Sectional Area:	2.5
Bankfull Width:	5.8
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.4
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

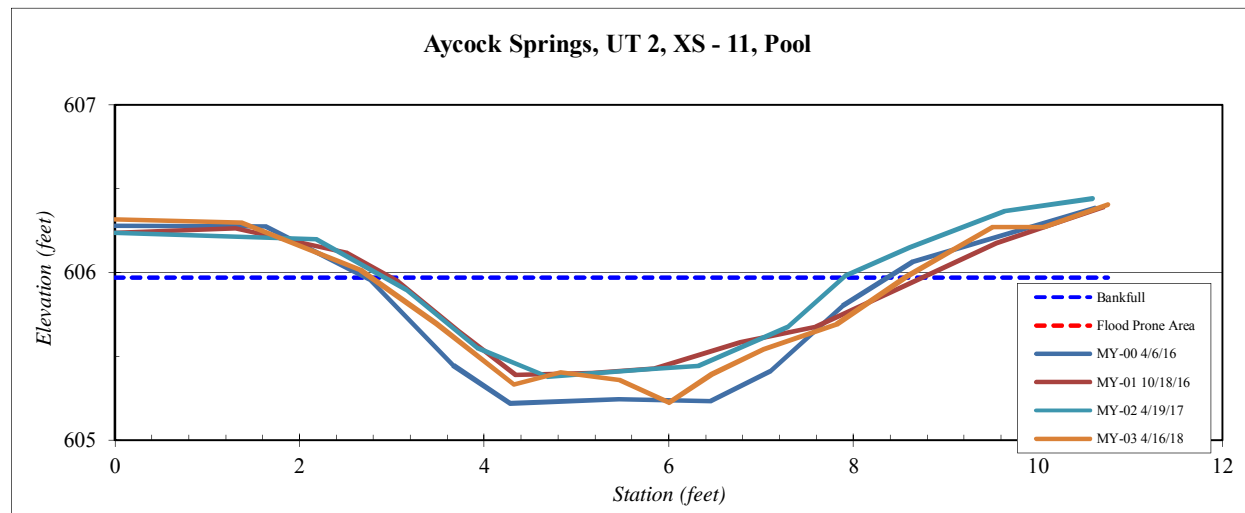


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 12, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.4	608.25
1.5	608.24
2.3	608.28
3.2	608.04
4.2	607.80
4.8	607.56
5.4	607.77
6.3	607.37
6.7	607.42
7.1	607.47
8.0	607.63
8.9	607.51
10.2	607.48
11.4	607.85
12.1	607.96
12.8	608.03

SUMMARY DATA	
Bankfull Elevation:	607.8
Bankfull Cross-Sectional Area:	1.9
Bankfull Width:	7.2
Flood Prone Area Elevation:	608.3
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.5
Mean Depth at Bankfull:	0.3
W / D Ratio:	27.3
Entrenchment Ratio:	12.5
Bank Height Ratio:	1.0

Stream Type	C/E
-------------	-----

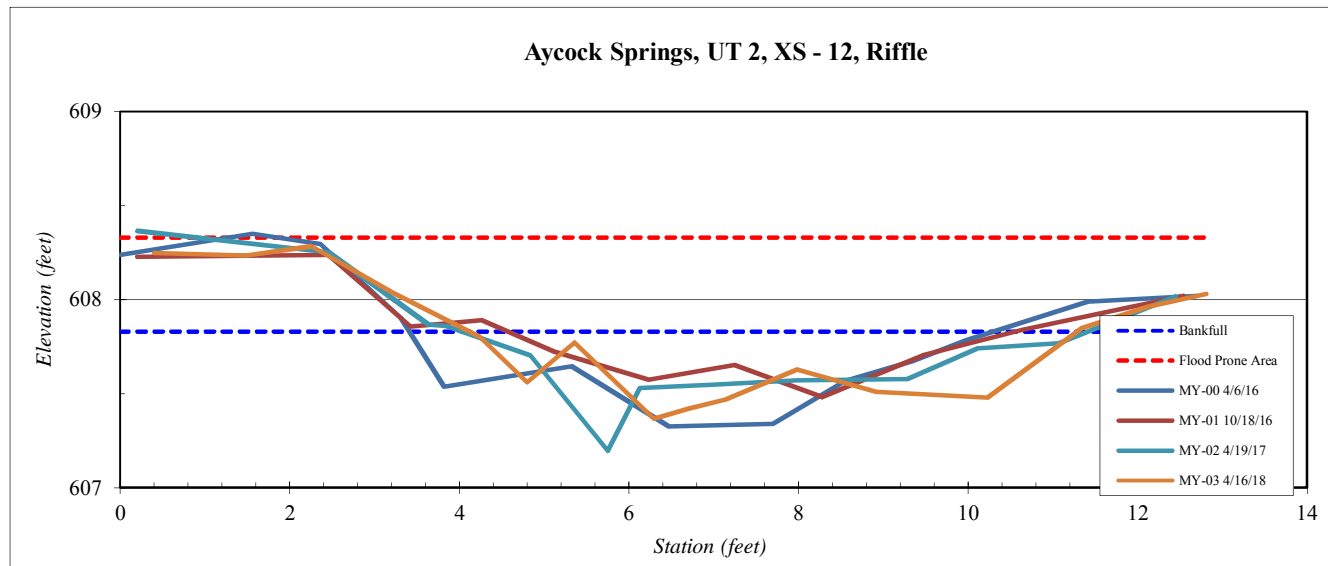


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 2, XS - 13, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.1	608.91
1.7	608.97
2.7	608.90
3.1	608.71
3.8	608.67
4.6	608.72
5.6	608.52
6.5	608.52
7.4	608.52
8.4	608.65
9.1	608.84
10.1	609.14
10.9	609.18
11.6	609.19
12.5	609.18

SUMMARY DATA	
Bankfull Elevation:	608.9
Bankfull Cross-Sectional Area:	1.8
Bankfull Width:	6.7
Flood Prone Area Elevation:	609.3
Flood Prone Width:	90.0
Max Depth at Bankfull:	0.4
Mean Depth at Bankfull:	0.3
W / D Ratio:	24.9
Entrenchment Ratio:	13.4
Bank Height Ratio:	1.0



Stream Type	C/E
-------------	-----

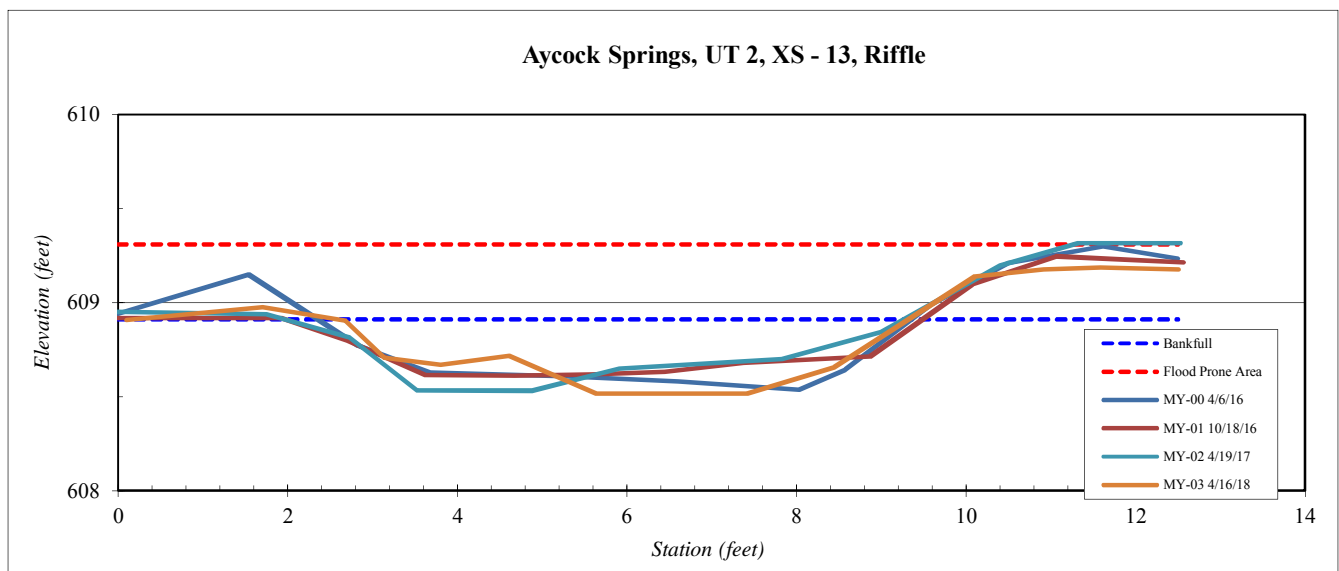


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 3, XS - 1, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	597.98
1.4	597.74
3.1	597.15
3.8	596.83
4.7	596.54
5.4	596.65
6.6	596.58
7.3	596.66
7.8	596.37
8.2	596.47
8.9	596.24
9.5	596.57
9.9	596.55
10.8	596.90
12.3	597.55
13.2	597.79
13.9	597.90
15.0	598.14

SUMMARY DATA	
Bankfull Elevation:	596.9
Bankfull Cross-Sectional Area:	2.4
Bankfull Width:	7.2
Flood Prone Area Elevation:	597.6
Flood Prone Width:	11.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.3
W / D Ratio:	21.6
Entrenchment Ratio:	1.5
Bank Height Ratio:	1.0

Stream Type: C/E

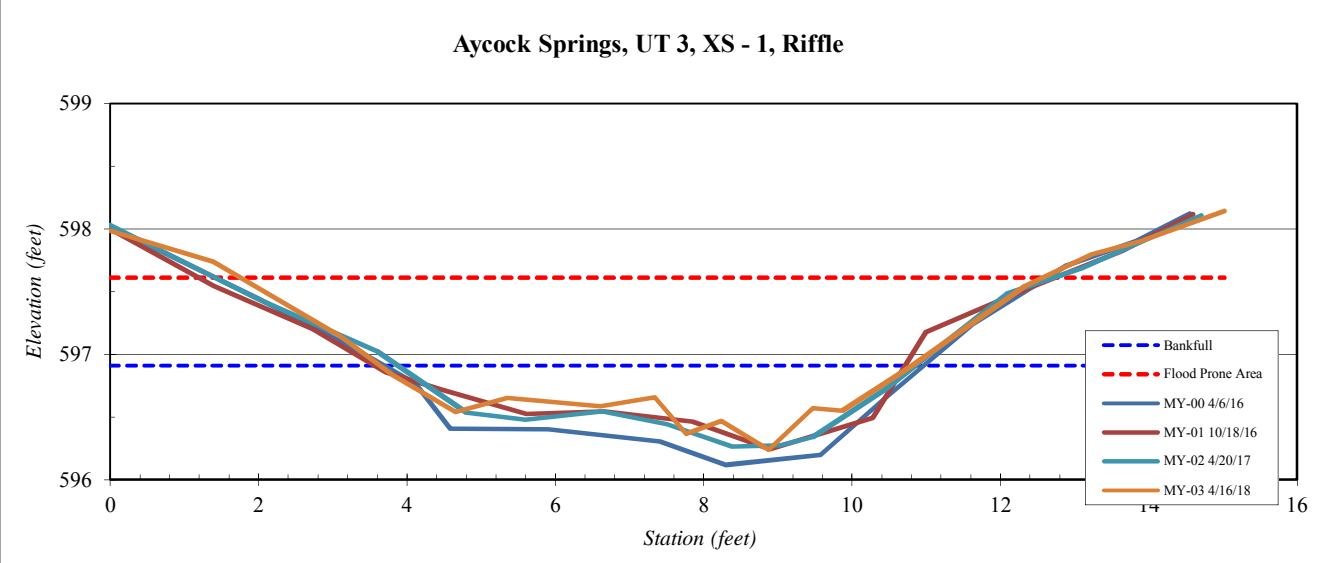


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 3, XS - 2, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
-0.2	597.65
2.1	597.49
3.9	597.34
5.2	596.69
5.8	596.60
6.3	596.57
6.8	596.43
7.1	596.38
7.6	596.45
8.2	596.42
8.8	596.56
9.7	596.90
11.3	597.58
12.8	598.05
14.9	598.71

SUMMARY DATA	
Bankfull Elevation:	597.0
Bankfull Cross-Sectional Area:	1.9
Bankfull Width:	5.1
Flood Prone Area Elevation:	597.6
Flood Prone Width:	8.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.4
W / D Ratio:	13.7
Entrenchment Ratio:	1.6
Bank Height Ratio:	1.0



Stream Type	C/E
--------------------	-----

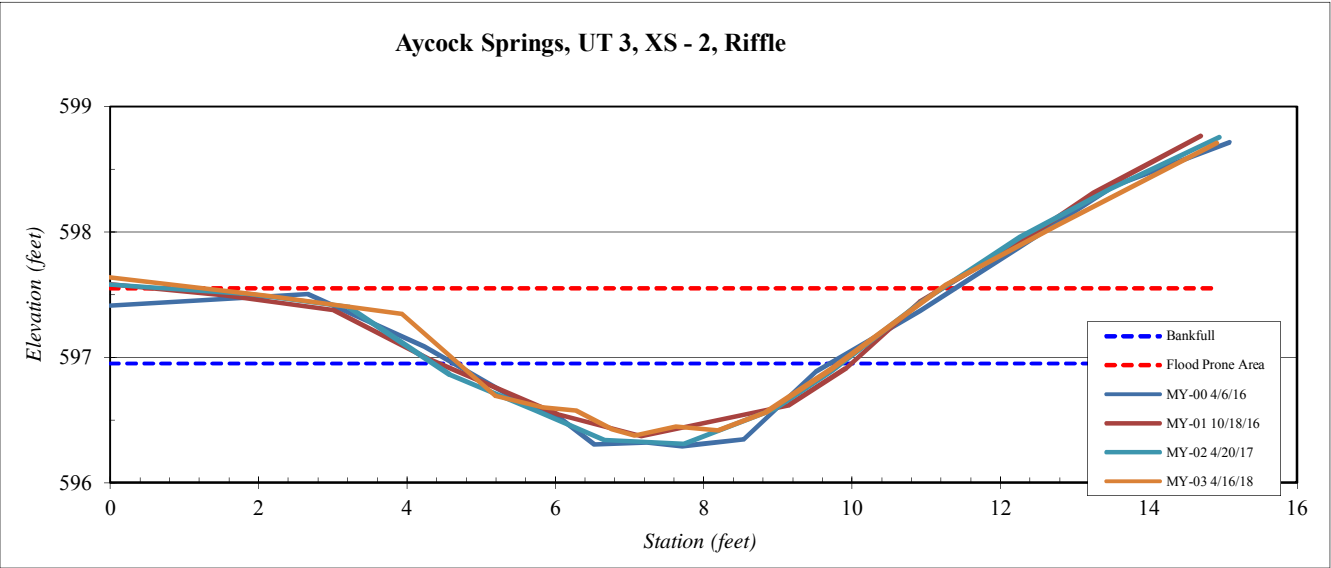


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 3, XS - 3, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.1	596.9
0.9	596.8
2.5	596.7
3.2	596.2
3.7	596.1
4.2	596.0
4.9	596.0
5.4	595.9
5.8	596.0
6.4	595.9
7.1	596.2
7.6	596.7
8.2	597.1
9.4	597.8
11.3	598.5
12.4	598.6

SUMMARY DATA	
Bankfull Elevation:	596.7
Bankfull Cross-Sectional Area:	3.2
Bankfull Width:	5.7
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	0.8
Mean Depth at Bankfull:	0.6
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type C/E

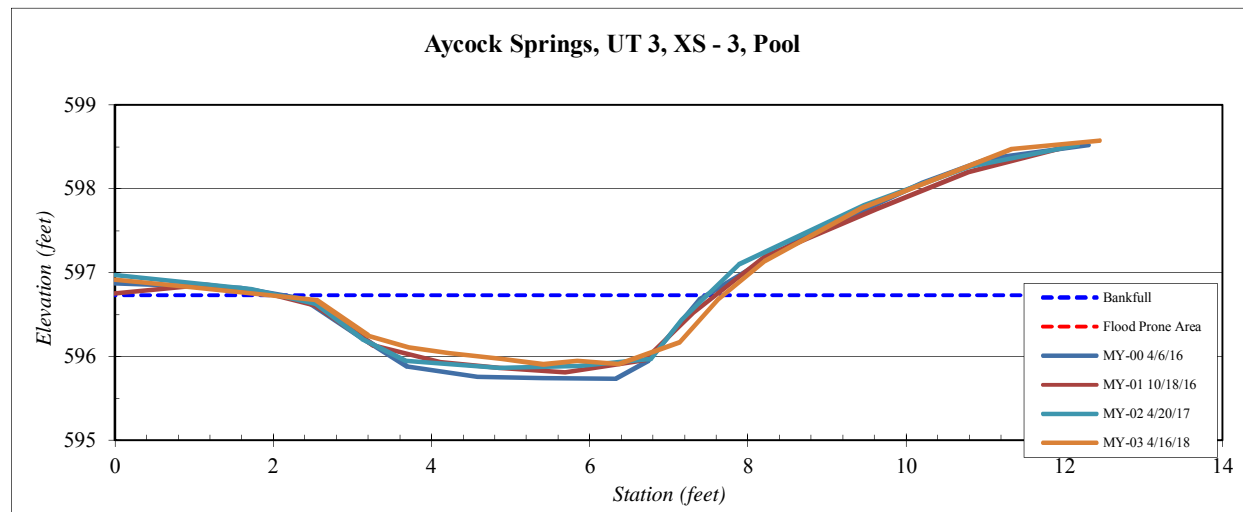


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 3, XS - 4, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
0.3	597.11
1.9	596.89
2.7	596.78
3.4	596.84
4.7	596.97
5.1	596.74
5.8	596.64
6.2	596.64
7.3	596.73
7.6	596.81
8.3	597.08
9.4	597.19
10.7	597.31

SUMMARY DATA	
Bankfull Elevation:	597.1
Bankfull Cross-Sectional Area:	1.7
Bankfull Width:	7.5
Flood Prone Area Elevation:	597.5
Flood Prone Width:	20.0
Max Depth at Bankfull:	0.4
Mean Depth at Bankfull:	0.2
W / D Ratio:	33.1
Entrenchment Ratio:	2.7
Bank Height Ratio:	1.0



Stream Type C/E

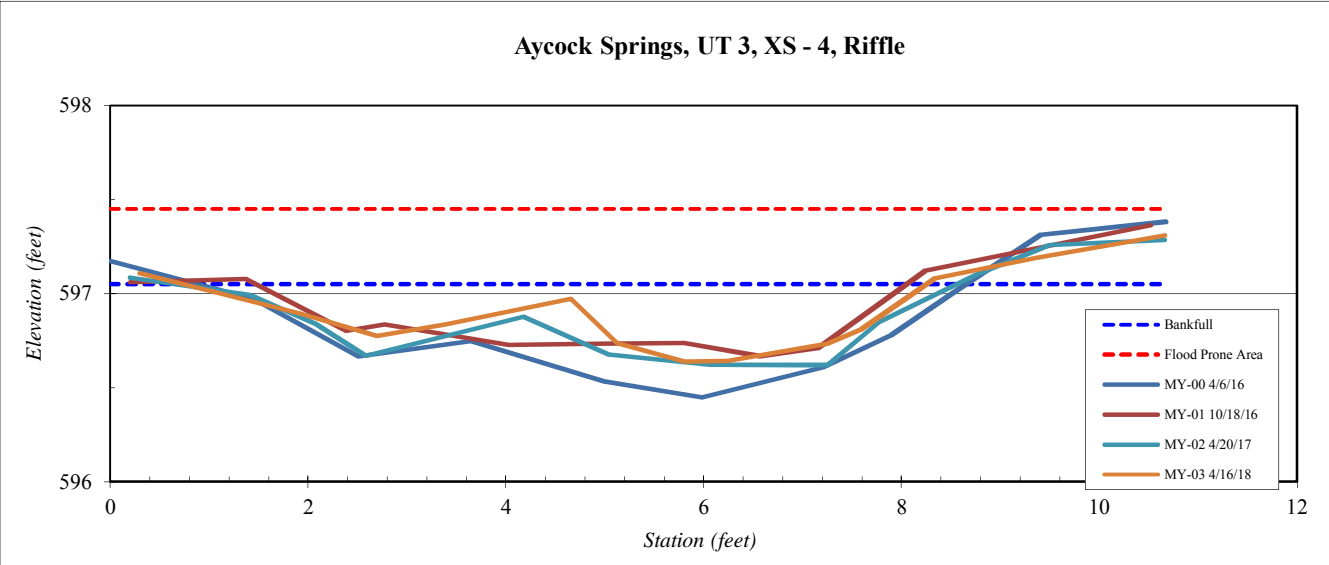


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 3, XS - 5, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.2	597.21
1.3	597.06
2.1	597.00
2.7	596.84
3.3	597.02
4.1	597.11
4.7	596.81
5.4	596.78
6.5	596.73
7.0	596.98
8.0	597.39
8.7	597.58
9.7	597.58

SUMMARY DATA	
Bankfull Elevation:	597.1
Bankfull Cross-Sectional Area:	1.2
Bankfull Width:	6.5
Flood Prone Area Elevation:	597.5
Flood Prone Width:	20.0
Max Depth at Bankfull:	0.4
Mean Depth at Bankfull:	0.2
W / D Ratio:	35.2
Entrenchment Ratio:	3.1
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

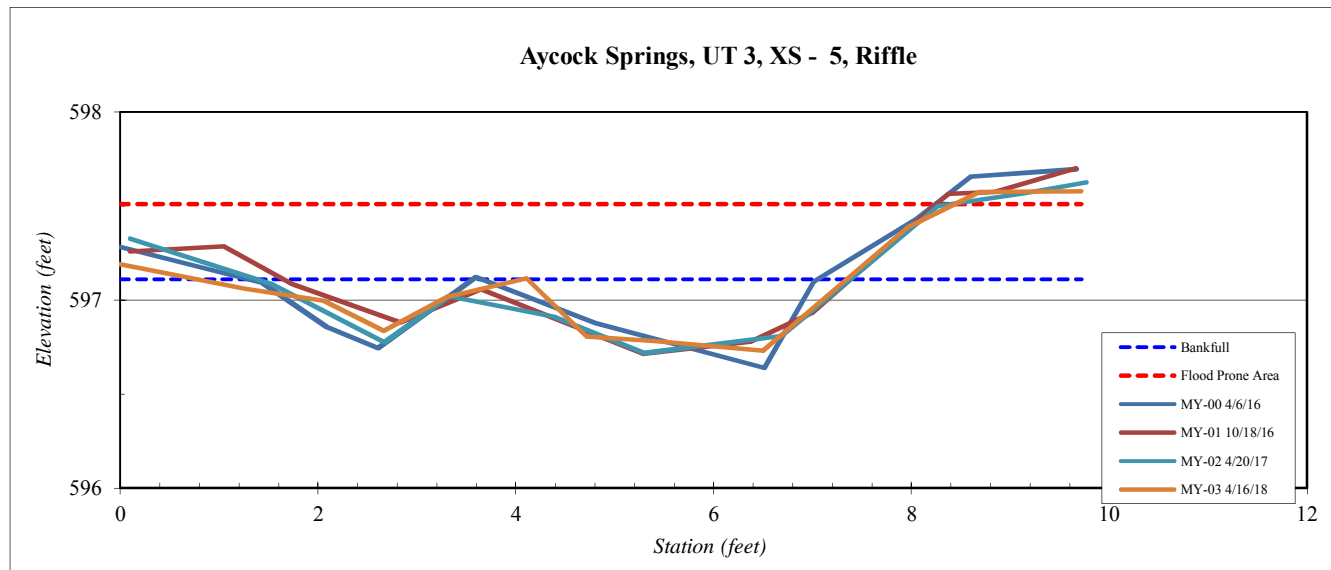


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 1, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.1	600.14
2.0	599.91
3.9	599.68
5.0	599.36
6.0	599.18
6.6	599.01
7.2	599.08
7.7	599.17
8.6	599.28
9.3	599.26
10.2	599.16
10.9	599.18
11.5	599.11
12.3	599.31
13.0	599.42
13.8	599.90
14.2	599.98
15.5	600.11
16.7	600.10

SUMMARY DATA	
Bankfull Elevation:	599.6
Bankfull Cross-Sectional Area:	3.3
Bankfull Width:	9.1
Flood Prone Area Elevation:	600.2
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.4
W / D Ratio:	25.1
Entrenchment Ratio:	5.5
Bank Height Ratio:	1.0

Stream Type C/E

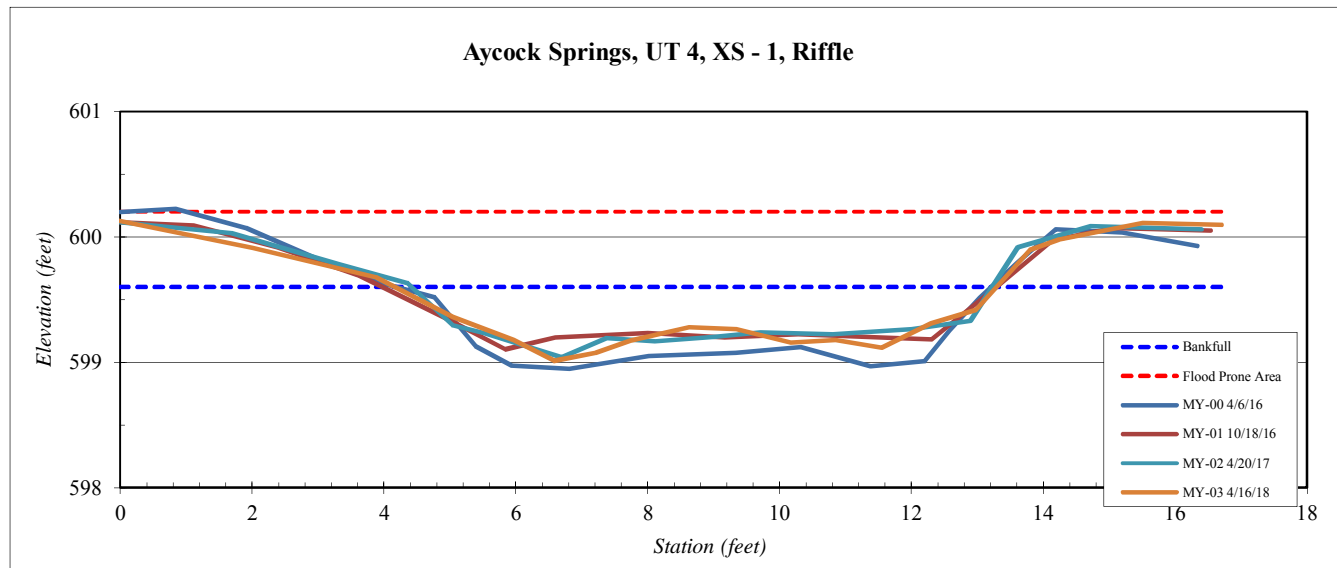


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 2, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	600.2
1.4	600.2
2.5	600.0
3.4	599.8
4.4	599.7
5.2	599.5
6.0	599.3
6.7	599.2
7.2	599.1
7.7	599.1
8.3	599.0
8.9	598.9
9.6	598.9
10.4	598.9
10.9	599.0
11.6	599.1
11.9	599.0
12.6	599.9
13.7	600.1
15.4	600.0

SUMMARY DATA	
Bankfull Elevation:	599.8
Bankfull Cross-Sectional Area:	5.8
Bankfull Width:	9.2
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.0
Mean Depth at Bankfull:	0.6
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

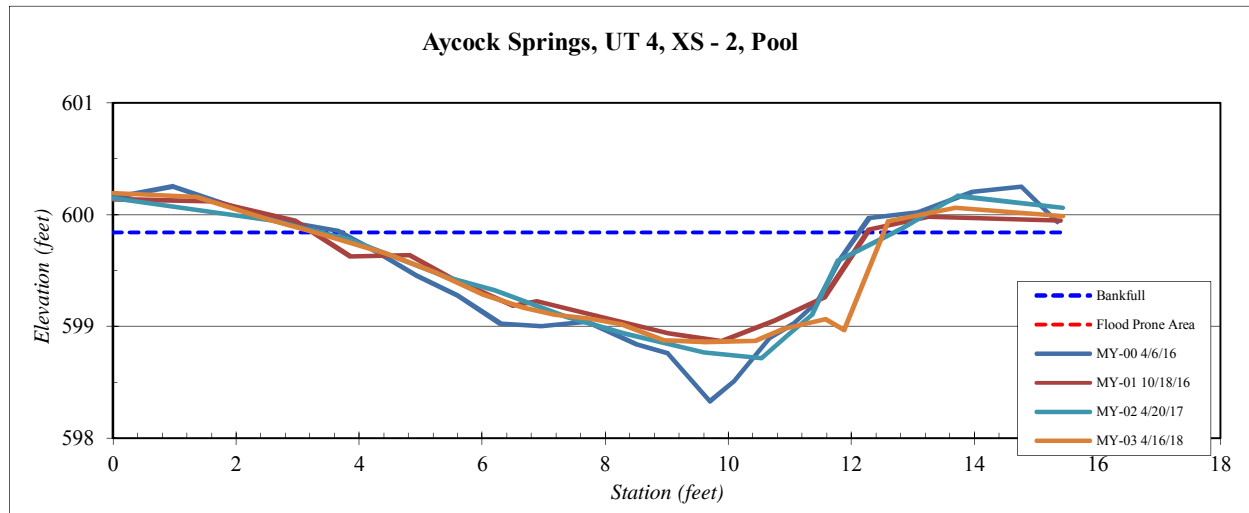


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 3, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	600.02
1.8	599.98
3.7	599.85
4.5	599.76
5.2	599.53
5.6	599.31
6.3	599.23
7.4	599.38
8.9	599.38
10.3	599.22
11.2	599.38
12.0	599.55
12.7	599.72
13.6	599.99
14.6	599.88
15.6	600.17
16.5	600.19

SUMMARY DATA	
Bankfull Elevation:	599.8
Bankfull Cross-Sectional Area:	3.5
Bankfull Width:	9.0
Flood Prone Area Elevation:	600.4
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.6
Mean Depth at Bankfull:	0.4
W / D Ratio:	23.1
Entrenchment Ratio:	5.6
Bank Height Ratio:	1.0

Stream Type C/E

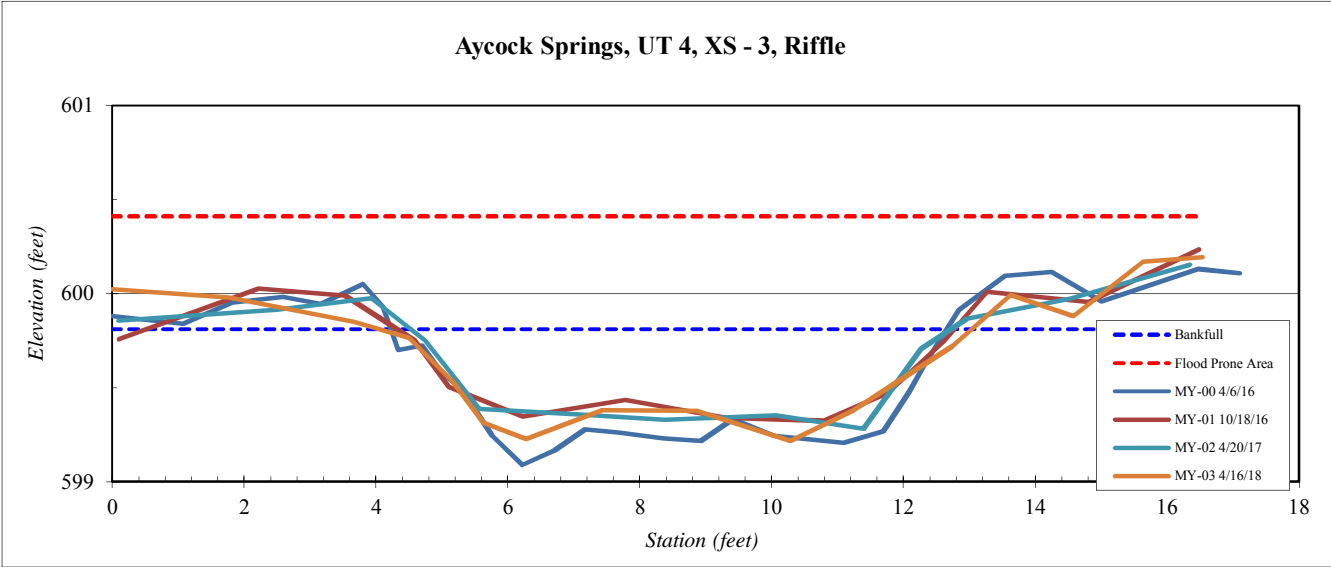


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 4, Pool
Feature	Pool
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.1	600.3
2.1	600.4
3.6	600.3
4.4	600.1
5.2	599.8
5.7	599.6
6.2	599.4
7.0	599.1
7.8	599.2
8.4	599.0
9.1	599.0
9.7	599.2
10.4	599.6
11.0	600.0
11.6	600.1
12.8	600.1
14.2	600.1
15.1	600.3

SUMMARY DATA	
Bankfull Elevation:	600.2
Bankfull Cross-Sectional Area:	5.6
Bankfull Width:	10.5
Flood Prone Area Elevation:	NA
Flood Prone Width:	NA
Max Depth at Bankfull:	1.2
Mean Depth at Bankfull:	0.5
W / D Ratio:	NA
Entrenchment Ratio:	NA
Bank Height Ratio:	1.0

Stream Type	C/E
-------------	-----

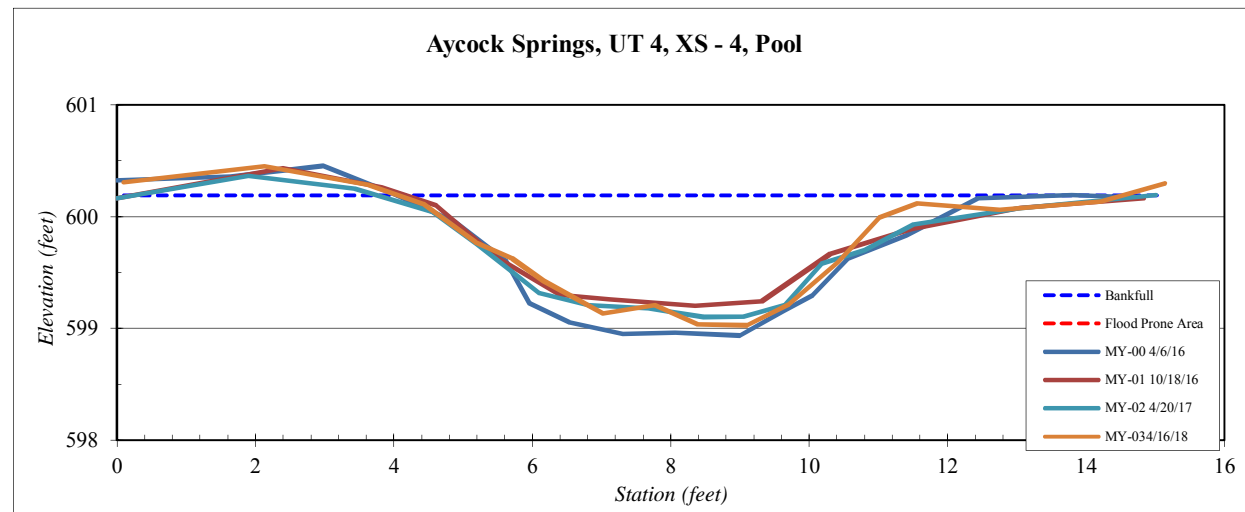


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 5, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
-0.2	600.34
1.7	600.34
2.8	600.26
3.7	599.89
4.4	599.58
5.0	599.45
5.9	599.41
6.9	599.54
7.7	599.50
8.4	599.35
9.2	599.48
9.8	599.49
10.2	599.65
11.0	600.02
12.1	600.24
13.1	600.24
14.5	600.21

SUMMARY DATA	
Bankfull Elevation:	600.1
Bankfull Cross-Sectional Area:	3.8
Bankfull Width:	7.9
Flood Prone Area Elevation:	600.8
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.5
W / D Ratio:	16.4
Entrenchment Ratio:	6.3
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

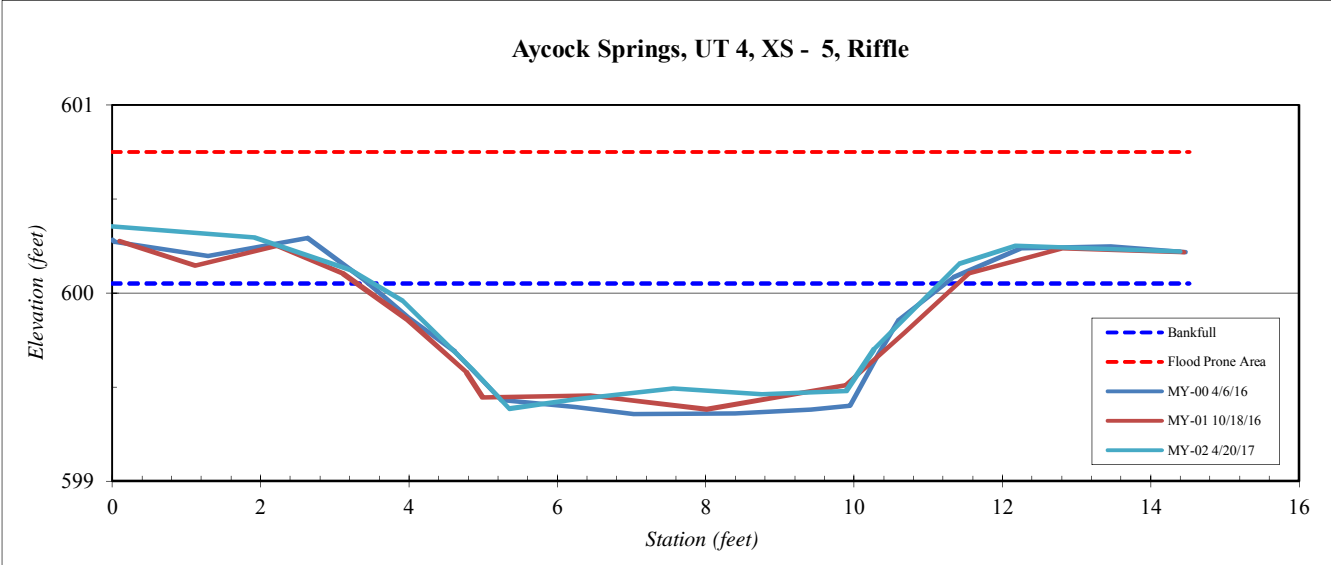


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 6, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler

Station	Elevation
-0.1	600.65
1.3	600.54
2.7	600.50
4.2	600.26
4.9	599.86
5.6	599.56
6.2	599.86
6.8	599.95
7.0	599.89
7.5	599.60
8.2	599.69
9.3	599.81
9.8	599.89
10.7	599.74
11.2	600.09
11.9	600.19
12.7	600.27
13.2	600.55
14.1	600.64
15.3	600.70

SUMMARY DATA	
Bankfull Elevation:	600.3
Bankfull Cross-Sectional Area:	3.3
Bankfull Width:	8.4
Flood Prone Area Elevation:	601.0
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.4
W / D Ratio:	21.4
Entrenchment Ratio:	6.0
Bank Height Ratio:	1.0



Stream Type: C/E

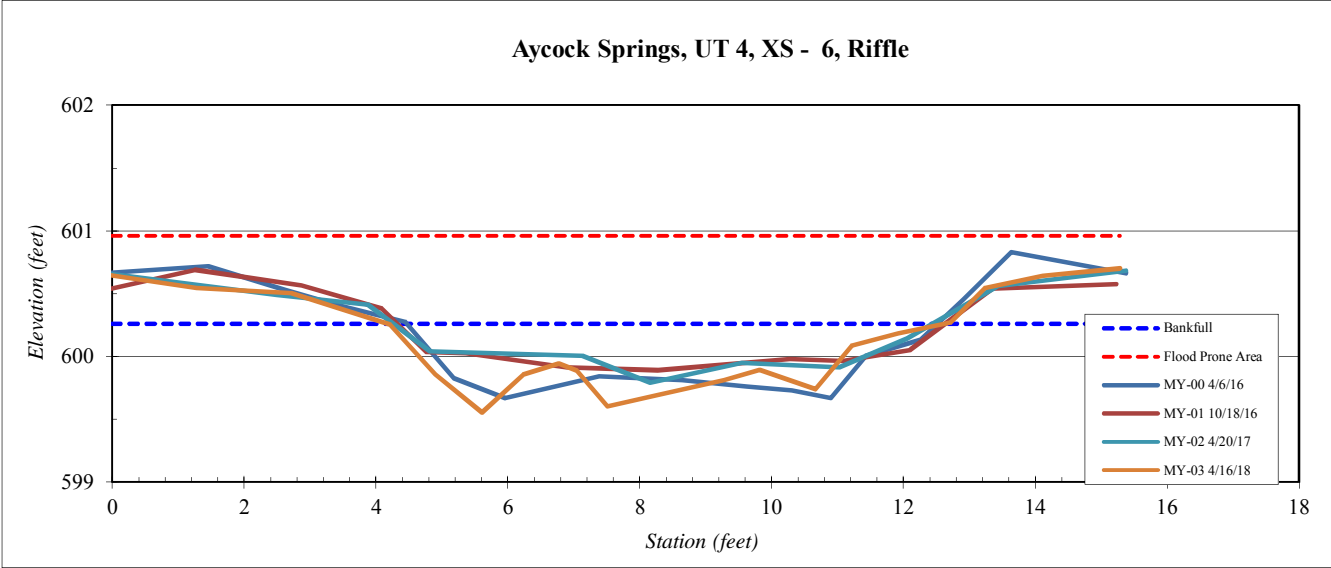


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 7, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	600.97
1.4	600.90
3.0	600.93
4.1	600.74
4.8	600.36
5.6	600.10
6.5	600.05
7.3	600.16
7.7	600.06
8.4	600.06
9.3	600.05
9.9	600.11
10.8	600.06
11.7	600.30
12.8	600.36
13.5	600.55
14.0	600.78
14.8	600.69
15.8	600.78

SUMMARY DATA	
Bankfull Elevation:	600.7
Bankfull Cross-Sectional Area:	5.0
Bankfull Width:	9.8
Flood Prone Area Elevation:	601.4
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.5
W / D Ratio:	19.2
Entrenchment Ratio:	5.1
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

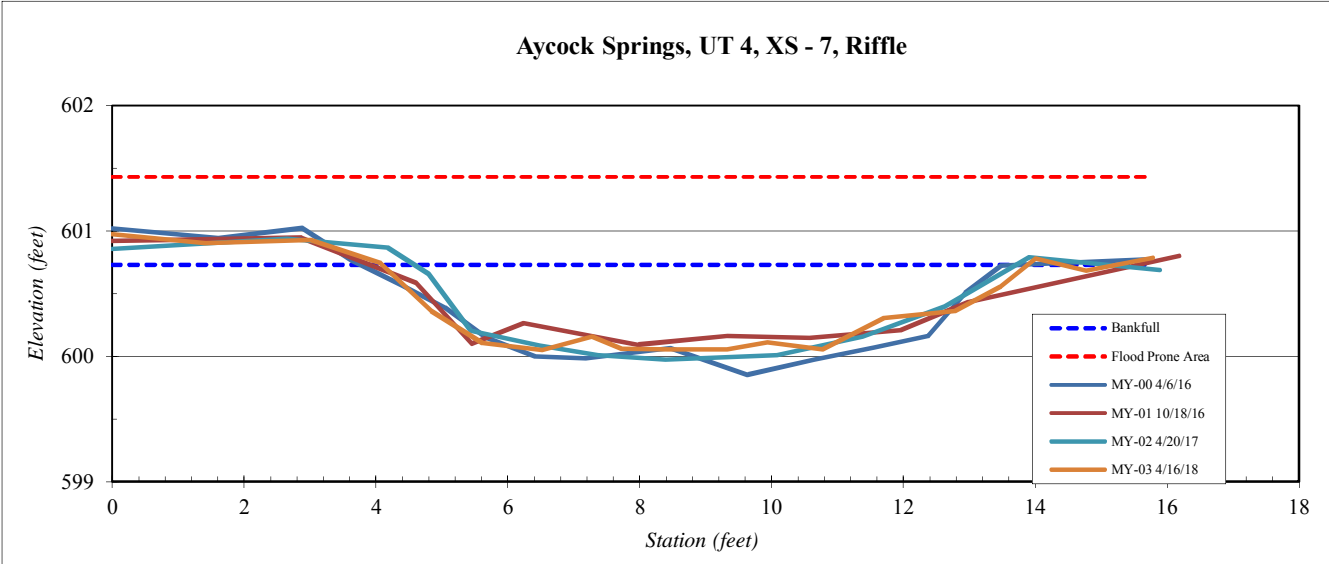


Site	Aycock Springs
Watershed:	Cape Fear, 0303002
XS ID	UT 4, XS - 8, Riffle
Feature	Riffle
Date:	4/16/2018
Field Crew:	Perkinson, Butler



Station	Elevation
0.0	601.19
1.7	601.12
2.5	600.74
3.3	600.64
4.1	600.57
4.8	600.67
5.5	600.60
5.8	600.45
6.5	600.41
7.1	600.36
7.9	600.36
8.3	600.41
9.0	600.41
9.8	600.59
10.5	600.70
11.1	600.90
12.4	601.09
13.1	601.16
14.1	601.26

SUMMARY DATA	
Bankfull Elevation:	601.1
Bankfull Cross-Sectional Area:	4.9
Bankfull Width:	10.6
Flood Prone Area Elevation:	601.8
Flood Prone Width:	50.0
Max Depth at Bankfull:	0.7
Mean Depth at Bankfull:	0.5
W / D Ratio:	22.9
Entrenchment Ratio:	4.7
Bank Height Ratio:	1.0

Stream Type	C/E
--------------------	-----

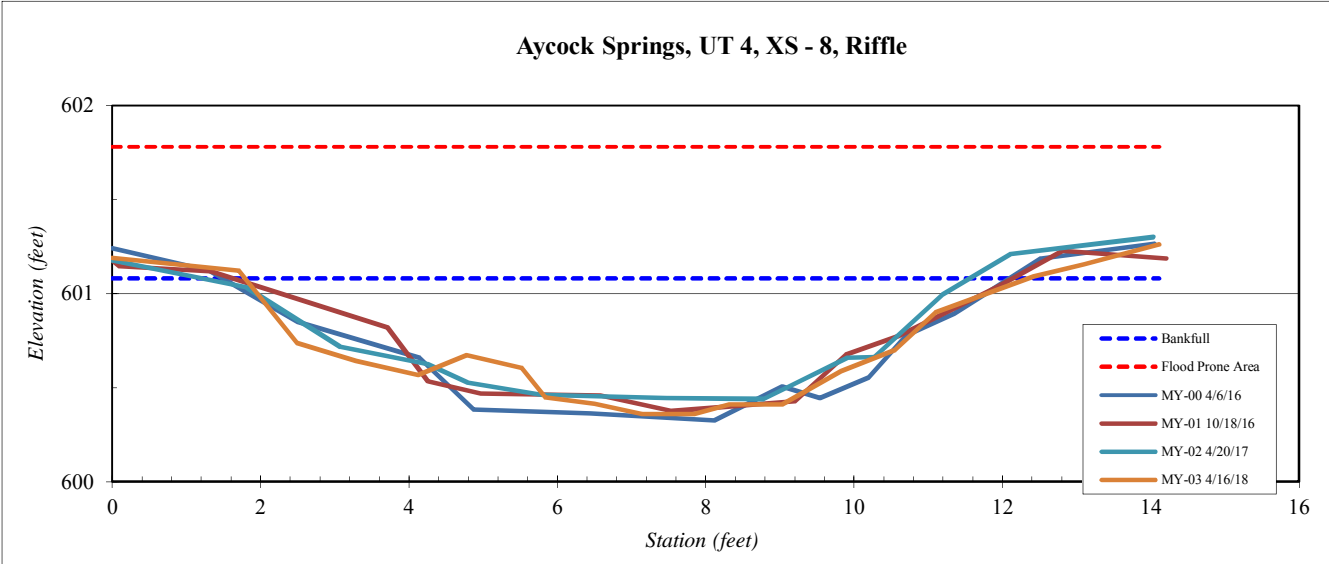

**Table 11A. Baseline Morphology and Hydraulic Summary
Aycock Springs UT 1**

Parameter	USGS Gage Data			Pre-Existing Condition			Project Reference Cedarrock Park			Project Reference Cripple Creek			Design			As-built				
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med		
BF Width (ft)	USGS gage data is unavailable for this project			3.8	9.6	6.7	8	12.1	8.1	3	6.1	4.6	7.2	8.3	7.8	6.4	9.6	8.0		
Floodprone Width (ft)				8	73	30	15	25	18	150	150	150	20	70	50					90
BF Cross Sectional Area (ft ²)						4.3			8			5.9			4.3	3	6.6	3.9		
BF Mean Depth (ft)				0.8	1	0.8	0.8	1	0.8	0.7	1.5	1.1	0.5	0.7	0.6	0.4	0.7	0.5		
BF Max Depth (ft)				1.1	1.4	1.4	1.1	1.4	1.4	1	2.3	1.7	0.7	0.9	0.8	0.6	1.1	0.7		
Width/Depth Ratio				8	15.1	10.1	8	15.1	10.1	4	4.3	4.2	12	16	14	11	19	15		
Entrenchment Ratio				1.9	2.2	2.1	1.9	2.2	2.1	24.6	50	37.3	2.6	9	6.4	9	14	11.3		
Bank Height Ratio				1	1.8	1	1	1.8	1	1	1.5	1.3	1	1.2	1			1		
Wetted Perimeter(ft)						===			===			===			===			===		
Hydraulic radius (ft)						===			===			===			===			===		
Pattern																				
Channel Beltwidth (ft)	No pattern of riffles and pools due to straightening activities			20	38	22.8	15.1	29.2	24.3	23	47	31	23	47	31					
Radius of Curvature (ft)				11	27	16.5	8.9	19.4	13.2	14	31	23	14	31	23					
Meander Wavelength (ft)				44	116	68.4	31	74	47.8	47	94	66	47	94	66					
Meander Width ratio				2.4	4.7	2.8	2.1	4	3.4	3	6	4	3	6	4					
Profile																				
Riffle length (ft)	No pattern of riffles and pools due to straightening activities					===			===			===			===	9	70	16		
Riffle slope (ft/ft)				1.00%	5.76%	3.16%	0.00%	1.54%	0.83%	2.77%	6.47%	4.16%	0.01%	4.33%	2.23%					
Pool length (ft)						===			===			===			===	4	23	9		
Pool spacing (ft)				25	69	37.2	14	39.6	32.4	23	62	31	23	62	31					
Substrate																				
d50 (mm)			===			===			===			===			===					
d84 (mm)			===			===			===			===			===					
Additional Reach Parameters																				
Valley Length (ft)			===			===			===			===			===					
Channel Length (ft)			===			===			===			===			===					
Sinuosity			1.02			1.2			1.22			1.1			1.1					
Water Surface Slope (ft/ft)			1.37% - 3.61%			2.58%			0.50%			1.27% - 3.35%			1.89%					
BF slope (ft/ft)			===			===			===			===			===					
Rosgen Classification			Cg			E			E			E/C			E/C					

**Table 11B. Baseline Morphology and Hydraulic Summary
Aycock Springs UT 2**

Parameter	USGS Gage Data			Pre-Existing Condition			Project Reference Cedarrock Park			Project Reference Cripple Creek			Design			As-built				
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med		
Dimension																				
BF Width (ft)	USGS gage data is unavailable for this project			3.8	9.6	6.7	8	12.1	8.1	3	6.1	4.6	7.2	8.3	7.8	4.8	8.6	7.2		
Floodprone Width (ft)				8	73	30	15	25	18	150	150	150	20	70	50					90
BF Cross Sectional Area (ft ²)						4.3			8					5.9			4.3	1	4.2	2.3
BF Mean Depth (ft)				0.8	1	0.8	0.8	1	0.8	0.7	1.5	1.1	0.5	0.7	0.6	0.2	0.6	0.3		
BF Max Depth (ft)				1.1	1.4	1.4	1.1	1.4	1.4	1	2.3	1.7	0.7	0.9	0.8	0.3	0.8	0.6		
Width/Depth Ratio				8	15.1	10.1	8	15.1	10.1	4	4.3	4.2	12	16	14	12	32	22		
Entrenchment Ratio				1.9	2.2	2.1	1.9	2.2	2.1	24.6	50	37.3	2.6	9	6.4	11	19	13		
Bank Height Ratio				1	1.8	1	1	1.8	1	1	1.5	1.3	1	1.2	1			1		
Wetted Perimeter(ft)						===			===			===			===			===		
Hydraulic radius (ft)						===			===			===			===			===		
Pattern																				
Channel Beltwidth (ft)				No pattern of riffles and pools due to straightening activities			20	38	22.8	15.1	29.2	24.3	23	47	31	23	47	31		
Radius of Curvature (ft)							11	27	16.5	8.9	19.4	13.2	14	31	23	14	31	23		
Meander Wavelength (ft)							44	116	68.4	31	74	47.8	47	94	66	47	94	66		
Meander Width ratio							2.4	4.7	2.8	2.1	4	3.4	3	6	4	3	6	4		
Profile																				
Riffle length (ft)				No pattern of riffles and pools due to straightening activities					===			===			===	9	23	14		
Riffle slope (ft/ft)							1.00%	5.76%	3.16%	0.00%	1.54%	0.83%	2.77%	6.47%	4.16%	0.00%	5.24%	2.88%		
Pool length (ft)									===			===			===	5	17	10		
Pool spacing (ft)							25	69	37.2	14	39.6	32.4	23	62	31	23	62	31		
Substrate																				
d50 (mm)									===			===			===			===		
d84 (mm)									===			===			===			===		
Additional Reach Parameters																				
Valley Length (ft)									===			===			===			===		
Channel Length (ft)									===			===			===			===		
Sinuosity									1.02			1.22			1.1			1.1		
Water Surface Slope (ft/ft)									1.37% 3.61%			2.58%			0.50%			1.27% 3.35%	3.01%	
BF slope (ft/ft)									===			===			===			===		
Rosgen Classification									Cg			E			E			E/C	E/C	

Note: UT 2 is characterized by a spring/seep, with a very small watershed. The channel was constructed with a smaller Bankfull Cross Sectional area to account for the smaller stormwater pulses and controlled discharge. In addition, the lower reaches of the channel are low slope wetlands that elevate the width-to-depth ratio in post construction measurements.

**Table 11C. Baseline Morphology and Hydraulic Summary
Aycock Springs UT 3**

Parameter	USGS Gage Data			Pre-Existing Condition			Project Reference Cedarrock Park			Project Reference Cripple Creek			Design			As-built				
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med		
Dimension																				
BF Width (ft)	USGS gage data is unavailable for this project			4.1	5	4.5	8	12.1	8.1	3	6.1	4.6	7.2	8.3	7.8	4.7	7	5.9		
Floodprone Width (ft)				7	18	12	15	25	18	150	150	150	20	70	50	10	20	20		
BF Cross Sectional Area (ft ²)						2.2			8			5.9			4.3	1.2	2.7	2.1		
BF Mean Depth (ft)				0.4	0.5	0.5	0.8	1	0.8	0.7	1.5	1.1	0.5	0.7	0.6	0.2	0.4	0.4		
BF Max Depth (ft)				0.8	1.1	1	1.1	1.4	1.4	1	2.3	1.7	0.7	0.9	0.8	0.5	0.6	0.6		
Width/Depth Ratio				8.2	12.5	9.9	8	15.1	10.1	4	4.3	4.2	12	16	14	12	26	20		
Entrenchment Ratio				1.7	3.6	2.5	1.9	2.2	2.1	24.6	50	37.3	2.6	9	6.4	2	4	3.3		
Bank Height Ratio				1	3	2	1	1.8	1	1	1.5	1.3	1	1.2	1			1		
Wetted Perimeter(ft)						===			===			===			===			===		
Hydraulic radius (ft)						===			===			===			===			===		
Pattern																				
Channel Beltwidth (ft)	No pattern of riffles and pools due to straightening activities			20	38	22.8	15.1	29.2	24.3	23	47	31	23	47	31					
Radius of Curvature (ft)				11	27	16.5	8.9	19.4	13.2	14	31	23	14	31	23					
Meander Wavelength (ft)				44	116	68.4	31	74	47.8	47	94	66	47	94	66					
Meander Width ratio				2.4	4.7	2.8	2.1	4	3.4	3	6	4	3	6	4					
Profile																				
Riffle length (ft)	No pattern of riffles and pools due to straightening activities					===			===			===			===	8	24	14		
Riffle slope (ft/ft)				1.00%	5.76%	3.16%	0.00%	1.54%	0.83%	2.77%	6.47%	4.16%	0.52%	2.54%	1.71%					
Pool length (ft)						===			===			===			===	6	10	8		
Pool spacing (ft)				25	69	37.2	14	39.6	32.4	23	62	31	23	62	31					
Substrate																				
d50 (mm)			===			===			===			===			===					
d84 (mm)			===			===			===			===			===					
Additional Reach Parameters																				
Valley Length (ft)			===			===			===			===			===					
Channel Length (ft)			===			===			===			===			===					
Sinuosity			1.01			1.2			1.22			1.1			1.1					
Water Surface Slope (ft/ft)			1.53%			2.58%			0.50%			1.27% - 3.35%			0.92%					
BF slope (ft/ft)			===			===			===			===			===					
Rosgen Classification			Eg			E			E			E/C			E/C					

Note: UT 3 is characterized by a pond in the headwaters; therefore, the channel was constructed with a smaller Bankfull Cross Sectional area than other tributaries associated with the project.

**Table 11D. Baseline Morphology and Hydraulic Summary
Aycock Springs UT 4**

Parameter	USGS Gage Data			Pre-Existing Condition			Project Reference Cedarrock Park			Project Reference Cripple Creek			Design			As-built				
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med		
Dimension																				
BF Width (ft)	USGS gage data is unavailable for this project			4.8	11.7	8.3	8	12.1	8.1	3	6.1	4.6	8.7	10	9.4	8	10.9	8.5		
Floodprone Width (ft)				8	70	39	15	25	18	150	150	150	70	200	150					50
BF Cross Sectional Area (ft ²)						6.3			8					5.9			6.3	3.5	5.6	4.3
BF Mean Depth (ft)				0.5	1.3	0.8	0.8	1	0.8	0.7	1.5	1.1	0.6	0.8	0.7	0.4	0.6	0.5		
BF Max Depth (ft)				0.9	2	1.5	1.1	1.4	1.4	1	2.3	1.7	0.8	1.1	1	0.6	0.9	0.8		
Width/Depth Ratio				3.7	23.4	12.4	8	15.1	10.1	4	4.3	4.2	12	16	14	16	22	19		
Entrenchment Ratio				1.2	11.5	4.9	1.9	2.2	2.1	24.6	50	37.3	7.5	21.3	16	5	6	6		
Bank Height Ratio				1.2	2.4	1.8	1	1.8	1	1	1.5	1.3	1	1.2	1			1		
Wetted Perimeter(ft)						===			===			===			===			===		
Hydraulic radius (ft)						===			===			===			===			===		
Pattern																				
Channel Beltwidth (ft)	No pattern of riffles and pools due to straightening activities			20	38	22.8	15.1	29.2	24.3	28	56	38	28	56	38					
Radius of Curvature (ft)				11	27	16.5	8.9	19.4	13.2	17	38	28	17	38	28					
Meander Wavelength (ft)				44	116	68.4	31	74	47.8	56	113	80	56	113	80					
Meander Width ratio				2.4	4.7	2.8	2.1	4	3.4	3	6	4	3	6	4					
Profile																				
Riffle length (ft)	No pattern of riffles and pools due to straightening activities					===			===			===			12	35	16			
Riffle slope (ft/ft)				1.00%	5.76%	3.16%	0.00%	1.54%	0.83%	1.12%	2.60%	1.67%	0.61%	2.42%	1.28%					
Pool length (ft)						===			===			===			14	42	22			
Pool spacing (ft)				25	69	37.2	14	39.6	32.4	28	75	38	28	75	38					
Substrate																				
d50 (mm)			===			===			===			===			===					
d84 (mm)			===			===			===			===			===					
Additional Reach Parameters																				
Valley Length (ft)			===			===			===			===			===					
Channel Length (ft)			===			===			===			===			===					
Sinuosity			1.1			1.2			1.22			1.1			1.1					
Water Surface Slope (ft/ft)			0.93%			2.58%			0.50%			0.93%			0.66%					
BF slope (ft/ft)			===			===			===			===			===					
Rosgen Classification			Eg			E			E			E/C			E/C					

**Table 11E. Baseline Morphology and Hydraulic Summary
Aycock Springs Travis Creek**

Parameter	USGS Gage Data			Pre-Existing Condition			Project Reference Cedarrock Park			Project Reference Cripple Creek			Design			As-built				
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med		
Dimension																				
BF Width (ft)	USGS gage data is unavailable for this project			30	51.7	41.4	8	12.1	8.1	3	6.1	4.6	25.7	29.6	27.7	25.2	30.3	26.7		
Floodprone Width (ft)				68	160	122	15	25	18	150	150	150	200	300	250					150
BF Cross Sectional Area (ft ²)						54.9			8			5.9			54.9	41.3	73.9	51.2		
BF Mean Depth (ft)				1.1	1.8	1.4	0.8	1	0.8	0.7	1.5	1.1	1.9	2.1	2	1.6	2.4	2		
BF Max Depth (ft)				3.3	4.1	3.7	1.1	1.4	1.4	1	2.3	1.7	2.7	3	2.8	2.3	3.4	2.8		
Width/Depth Ratio				16.7	47	32.1	8	15.1	10.1	4	4.3	4.2	12	16	14	12	16	13		
Entrenchment Ratio				1.6	5.3	3.2	1.9	2.2	2.1	24.6	50	37.3	7.2	10.8	9	5	6	5.6		
Bank Height Ratio				1	1.1	1	1	1.8	1	1	1.5	1.3	1	1.2	1			1		
Wetted Perimeter(ft)						===			===			===			===			===		
Hydraulic radius (ft)						===			===			===			===			===		
Pattern																				
Channel Beltwidth (ft)	No pattern of riffles and pools due to straightening activities			20	38	22.8	15.1	29.2	24.3	83	166	111	83	166	111					
Radius of Curvature (ft)				11	27	16.5	8.9	19.4	13.2	55	111	83	55	111	83					
Meander Wavelength (ft)				44	116	68.4	31	74	47.8	166	332	236	166	332	236					
Meander Width ratio				2.4	4.7	2.8	2.1	4	3.4	3	6	4	3	6	4					
Profile																				
Riffle length (ft)	No pattern of riffles and pools due to straightening activities					===			===			===			===	16	87	54		
Riffle slope (ft/ft)				1.00%	5.76%	3.16%	0.00%	1.54%	0.83%	0.28%	0.64%	0.41%	0.00%	0.70%	0.19%					
Pool length (ft)						===			===			===			===	27	70	43		
Pool spacing (ft)				25	69	37.2	14	39.6	32.4	83	222	111	83	222	111					
Substrate																				
d50 (mm)			===			===			===			===			===					
d84 (mm)			===			===			===			===			===					
Additional Reach Parameters																				
Valley Length (ft)			===			===			===			===			===					
Channel Length (ft)			===			===			===			===			===					
Sinuosity			1.05			1.2			1.22			1.05			1.05					
Water Surface Slope (ft/ft)			NA			2.58%			0.50%			0.23%			0.10%					
BF slope (ft/ft)			===			===			===			===			===					
Rosgen Classification			Fc			E			E			E/C			E/C					

**Table 12A. Morphology and Hydraulic Monitoring Summary
Aycock Travis Creek (Downstream) - Stream and Wetland Restoration Site**

Parameter	XS 1 Riffle (Travis Down)						XS 2 Riffle (Travis Down)						XS 3 Pool (Travis Down)						XS 4 Riffle (Travis Down)						XS 5 Pool (Travis Down)						XS 6 Riffle (Travis Down)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																																				
BF Width (ft)	26	26.7	26.4	27.3			25.2	26.2	26.3	28.3			33.7	33.2	35.4	39			25.5	27	26.5	28.4			26	26.7	26	25.7			27.3	27.7	26.8	28.9		
Floodprone Width (ft)	150	150	150	150			150	150	150	150			----	----	----	----			150	150	150	150			----	----	----	----			150	150	150	150		
BF Cross Sectional Area (ft2)	41.3	40	40.1	40.1			47.5	47.4	47.9	47.9			58.7	55.8	57.2	57.2			47.2	44.6	43.8	43.8			61.4	58.1	52.3	52.3			54.9	50.6	50.3	50.3		
BF Mean Depth (ft)	1.6	1.5	1.5	1.5			1.9	1.8	1.8	1.7			1.7	1.7	1.6	1.5			1.9	1.7	1.7	1.5			2.4	2.2	2.0	2			2.0	1.8	1.9	1.7		
BF Max Depth (ft)	2.3	2.3	2.2	2.3			2.5	2.5	2.6	2.9			3.7	3.5	3.7	3.6			2.5	2.6	2.6	2.7			4	3.7	3.2	3.3			3	2.9	2.8	3		
Width/Depth Ratio	16.4	17.8	17.4	18.6			13.4	14.5	14.4	16.7			----	----	----	----			13.8	16.3	16.0	18.4			----	----	----	----			13.6	15.2	14.3	16.6		
Entrenchment Ratio	5.8	5.6	5.7	5.5			6.0	5.7	5.7	5.3			----	----	----	----			5.9	5.6	5.7	5.3			----	----	----	----			5.5	5.4	5.6	5.2		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.04	<1.0			----	----	----	----			1.0	1.04	1.04	<1			----	----	----	----			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	27.1	27.4	27.2	28			26.4	27.5	27.3	29.5			34.8	34.4	36.4	40.2			26.6	28	27.5	29.6			27.6	28.2	27.3	26.9			28.7	29.1	27.9	30.4		
Hydraulic Radius (ft)	1.5	1.5	1.5	1.4			1.8	1.7	1.8	1.6			1.7	1.6	1.6	1.4			1.8	1.6	1.6	1.5			2.2	2.1	1.9	1.9			1.9	1.7	1.8	1.7		
Substrate																																				
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

Parameter	XS 7 Pool (Travis Down)						XS 8 Riffle (Travis Down)						XS 9 Pool (Travis Down)						XS 10 Pool (Travis Down)						XS 11 Riffle (Travis Down)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	25.9	27.7	25.7	25.1			28.1	28.5	28.6	28			29.3	29.1	29.7	27.8			38.6	38.6	39.1	37.5			30.3	29.8	30.5	30.7		
Floodprone Width (ft)	----	----	----	----			150	150	150	150			----	----	----	----			----	----	----	----			150	150	150	150		
BF Cross Sectional Area (ft2)	60	45.8	44.9	44.9			64.6	57.4	58.3	58.3			65.9	63.1	60.8	60.8			100.1	91	87.5	87.5			73.9	66.6	69.6	69.6		
BF Mean Depth (ft)	2.3	1.7	1.7	1.8			2.3	2.0	2.0	2.1			2.2	2.2	2.0	2.2			2.6	2.4	2.2	2.3			2.4	2.2	2.3	2.3		
BF Max Depth (ft)	3.9	2.8	2.5	3			3.3	3.1	3.1	3.4			3.7	3.4	3.4	3.8			4.3	4.2	4.1	4.3			3.4	3.6	3.6	3.6		
Width/Depth Ratio	----	----	----	----			12.2	14.2	14.0	13.4			----	----	----	----			----	----	----	----			12.4	13.3	13.4	13.6		
Entrenchment Ratio	----	----	----	----			5.3	5.3	5.2	5.4			----	----	----	----			----	----	----	----			5.0	5.0	4.9	4.9		
Bank Height Ratio	----	----	----	----			1.0	1.0	1.0	1.0			----	----	----	----			----	----	----	----			1.00	1.06	1.06	1.0		
Wetted Perimeter (ft)	27.5	29.1	26.8	26.2			29.5	29.7	29.8	29.8			30.6	30.3	30.8	29.4			40.2	40	40.4	39.1			31.8	31.4	32.1	32.1		
Hydraulic Radius (ft)	2.2	1.6	1.7	1.7			2.2	1.9	2.0	2			2.2	2.1	2.0	2.1			2.5	2.3	2.2	2.2			2.3	2.1	2.2	2.2		
Substrate																														
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

**Table 12B. Morphology and Hydraulic Monitoring Summary
Aycock Travis Creek (Upstream) - Stream and Wetland Restoration Site**

Parameter	XS 12 Riffle (Travis Up)						XS 13 Pool (Travis Up)						XS 14 Riffle (Travis Up)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																		
BF Width (ft)	29	29.6	29.7	31.3			26.9	26.9	27.8	27.8			32.8	32.3	31.9	33.6		
Floodprone Width (ft)	150	150	150	150			----	----	----	----			150	150	150	150		
BF Cross Sectional Area (ft2)	68.7	66.4	67.9	67.9			64.0	50.3	51.9	48.2			104.5	92.4	94.6	94.6		
BF Mean Depth (ft)	2.4	2.2	2.3	2.2			2.4	1.9	1.9	1.7			3.2	2.9	3.0	2.8		
BF Max Depth (ft)	3.4	3.5	3.5	3.5			3.9	3.3	3.2	3.5			4.8	4.1	4.5	4.6		
Width/Depth Ratio	12.2	13.2	13.0	14.4			----	----	----	----			10.295	11.29	10.76	11.9		
Entrenchment Ratio	5.2	5.1	5.1	4.8			----	----	----	----			4.6	4.6	4.7	4.5		
Bank Height Ratio	1.00	1.03	1.03	1.03			----	----	----	----			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	30.4	30.8	30.9	32.5			28.8	28.1	28.8	32.5			35.0	34.2	33.8	35.8		
Hydraulic Radius (ft)	2.3	2.2	2.2	2.1			2.2	1.8	1.8	2.1			3.0	2.7	2.8	2.6		
Substrate																		
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----		

**Table 12C. Morphology and Hydraulic Monitoring Summary
Aycock UT-1 - Stream and Wetland Restoration Site**

Parameter	XS 1 Riffle (UT 1)						XS 2 Riffle (UT 1)						XS 3 Pool (UT 1)						XS 4 Riffle (UT 1)						XS 5 Riffle (UT 1)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	9.3	9.2	9.7	9.1			8.8	9.3	9.2	10.2			8.4	8.4	9.3	9.5			9.3	9.7	9.3	10.2			9.6	9.5	9.3	9.2		
Floodprone Width (ft)	90	90	90	90			90	90	90	90			---	---	---	---			90	90	90	90			90	90	90	90		
BF Cross Sectional Area (ft2)	5.6	4.7	4.4	4.4			4.6	3.7	3.7	3.7			6.7	5.6	6.4	6.4			6.2	5.5	5.7	5.7			6.6	5.9	5.8	5.8		
BF Mean Depth (ft)	0.6	0.5	0.5	0.5			0.5	0.4	0.4	0.4			0.8	0.7	0.7	0.7			0.7	0.6	0.6	0.6			0.7	0.6	0.6	0.6		
BF Max Depth (ft)	1.1	0.8	0.9	0.8			0.7	0.6	0.7	0.6			1.3	1.2	1.3	1.4			1	0.9	0.9	0.9			1.1	1.1	1	1		
Width/Depth Ratio	15.4	18.0	21.4	18.8			16.8	23.4	22.9	28.1			---	---	---	---			14.0	17.1	15.2	18.4			14.0	15.3	14.9	14.8		
Entrenchment Ratio	9.7	9.8	9.3	9.9			10.2	9.7	9.8	8.8			---	---	---	---			9.7	9.3	9.7	8.8			9.4	9.5	9.7	9.8		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.0	<1			---	---	---	---			1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	9.7	9.4	10	9.3			9	9.4	9.4	10.3			8.9	8.9	9.8	10			9.7	10	9.6	10.5			10	10	9.8	9.7		
Hydraulic Radius (ft)	0.6	0.5	0.4	0.5			0.5	0.4	0.4	0.4			0.7	0.6	0.7	0.6			0.6	0.6	0.6	0.5			0.7	0.6	0.6	0.6		
Substrate																														
d50 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		
d84 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		

Parameter	XS 6 Riffle (UT 1)						XS 7 Riffle (UT 1)						XS 8 Pool (UT 1)						XS 9 Riffle (UT 1)						XS 10 Pool (UT 1)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	6.9	7.5	6.7	6.9			7.5	7.2	7.3	6.7			7.8	8.7	7.2	6			7.9	7.2	7.6	6.7			7.6	7	6.9	5.5		
Floodprone Width (ft)	90	90	90	90			90	90	90	90			---	---	---	---			90	90	90	90			---	---	---	---		
BF Cross Sectional Area (ft2)	3.6	1.9	2.2	2.2			3.9	2.4	2.4	2.4			5.7	4.1	3.6	3.6			3	4.1	1.6	1.6			4.7	5.6	5.5	5.5		
BF Mean Depth (ft)	0.5	0.3	0.3	0.3			0.5	0.3	0.3	0.4			0.7	0.5	0.5	0.6			0.4	0.6	0.2	0.2			0.6	0.8	0.8	1		
BF Max Depth (ft)	0.7	0.4	0.4	0.4			0.7	0.6	0.6	0.7			1.2	1	0.9	1			0.7	1.1	0.4	0.6			1.1	1.3	1.2	1.4		
Width/Depth Ratio	13.2	29.6	20.4	21.9			14.4	21.6	22.2	18.9			---	---	---	---			20.8	12.6	36.1	28.1			---	---	---	---		
Entrenchment Ratio	13.0	12.0	13.4	13.1			12.0	12.5	12.3	13.4			---	---	---	---			11.4	12.5	11.8	13.5			---	---	---	---		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0			---	---	---	---			1.0	1.0	1.0	1.0			---	---	---	---		
Wetted Perimeter (ft)	7.2	7.6	6.8	7			7.8	7.3	7.5	6.9			8.3	9.1	7.5	6.6			8	7.8	7.7	7			8	7.7	7.7	6.6		
Hydraulic Radius (ft)	0.5	0.3	0.3	0.3			0.5	0.3	0.3	0.3			0.7	0.5	0.5	0.6			0.4	0.5	0.2	0.2			0.6	0.7	0.7	0.8		
Substrate																														
d50 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		
d84 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		

Parameter	XS 11 Riffle (UT 1)						XS 12 Riffle (UT 1)						XS 13 Pool (UT 1)						XS 14 Riffle (UT 1)						XS 15 Riffle (UT 1)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	7.4	7	7.8	8.4			8	7.4	6.4	7.3			8.6	8	8.3	8.3			6.4	6.3	6.3	6.2			7.1	7.2	6.3	5.6		
Floodprone Width (ft)	90	90	90	90			90	90	90	90			---	---	---	---			90	90	90	90			90	90	90	90		
BF Cross Sectional Area (ft2)	3.5	3.5	3.5	3.5			3.7	2.8	2.8	2.8			6.5	4.3	4.7	4.7			3.1	2.8	2.8	2.8			4	3.3	2.4	2.4		
BF Mean Depth (ft)	0.5	0.5	0.4	0.4			0.5	0.4	0.4	0.4			0.8	0.5	0.6	0.6			0.5	0.4	0.4	0.4			0.6	0.5	0.4	0.4		
BF Max Depth (ft)	0.8	0.8	0.7	0.9			0.7	0.6	0.6	0.6			1.2	1.2	1.3	1.3			0.7	0.6	0.7	0.6			0.9	0.8	0.7	0.9		
Width/Depth Ratio	15.6	14.0	17.4	19.8			17.3	19.6	14.6	18.8			---	---	---	---			13.2	14.2	14.2	14.0			12.6	15.7	16.5	13.0		
Entrenchment Ratio	12.2	12.9	11.5	10.8			11.3	12.2	14.1	12.3			---	---	---	---			14.1	14.3	14.3	14.4			12.7	12.5	14.3	16.1		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0			---	---	---	---			1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	7.8	7.3	8.1	8.9			8.5	7.6	6.6	7.5			9.2	8.5	9.0	9.0			6.8	6.5	6.6	6.5			7.4	7.6	6.6	6.1		
Hydraulic Radius (ft)	0.4	0.5	0.4	0.4			0.4	0.4	0.4	0.4			0.7	0.5	0.5	0.5			0.5	0.4	0.4	0.4			0.5	0.4	0.4	0.4		
Substrate																														
d50 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		
d84 (mm)	---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---			---	---	---	---		

**Table 12C continued. Morphology and Hydraulic Monitoring Summary
Aycock UT-1 - Stream and Wetland Restoration Site**

Parameter	XS 16 Riffle (UT 1)					XS 17 Riffle (UT 1)					XS 18 Riffle (UT 1)					XS 19 Pool (UT 1)					XS 20 Riffle (UT 1)									
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	9	8.3	8.5	8.8			8.5	8.1	7.4	7.4			7.1	7.2	6.7	6.9			7.6	7.7	8.1	8.1			9.1	8.5	8.7	9.4		
Floodprone Width (ft)	90	90	90	90			90	90	90	90			90	90	90	90			----	----	----	----			90	90	90	90		
BF Cross Sectional Area (ft2)	4.6	2.6	2.8	2.8			3.9	3.6	3.7	3.7			3.5	3.4	3.6	3.6			6.5	5.4	5.3	5.3			5.3	4.4	4.9	4.9		
BF Mean Depth (ft)	0.5	0.3	0.3	0.3			0.5	0.4	0.5	0.5			0.5	0.5	0.5	0.5			0.9	0.7	0.7	0.7			0.6	0.5	0.6	0.5		
BF Max Depth (ft)	0.8	0.5	0.5	0.5			0.7	0.7	0.8	0.9			0.6	0.7	0.8	0.9			1.3	1	1.1	1.2			0.9	0.7	0.8	0.8		
Width/Depth Ratio	17.6	26.5	25.8	27.6			18.5	18.2	14.8	14.5			14.4	15.2	12.5	13.5			----	----	----	----			15.6	16.4	15.4	18.1		
Entrenchment Ratio	10.0	10.8	10.6	10.2			10.6	11.1	12.2	12.2			12.7	12.5	13.4	13.0			----	----	----	----			9.9	10.6	10.3	9.6		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.14	1.11			1.0	1.16	1.33	1.22			----	----	----	----			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	9.3	8.4	8.7	9.0			8.7	8.3	7.7	7.7			7.4	7.4	7.0	7.4			8.2	8.3	8.7	8.6			9.4	8.7	9.0	9.8		
Hydraulic Radius (ft)	0.5	0.3	0.3	0.3			0.5	0.4	0.5	0.5			0.5	0.5	0.5	0.5			0.8	0.7	0.6	0.6			0.6	0.5	0.5	0.5		
Substrate																														
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

Parameter	XS 21 Pool (UT 1)					XS 22 Riffle (UT 1)					XS 23 Riffle (UT 1)					XS 24 Riffle (UT 1)								
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																								
BF Width (ft)	8.3	8.2	9.7	8.4			7.2	7.5	7.3	6.4			7.6	6.8	7	7			8	7.7	7.6	7.8		
Floodprone Width (ft)	----	----	----	----			90	90	90	90			90	90	90	90			90	90	90	90		
BF Cross Sectional Area (ft2)	9.3	5.9	5.4	5.4			3.6	3.4	3.3	3.3			3.2	3.2	3	3			4	3.2	3.4	3.4		
BF Mean Depth (ft)	1.1	0.7	0.6	0.6			0.5	0.5	0.5	0.5			0.4	0.5	0.4	0.4			0.5	0.4	0.4	0.4		
BF Max Depth (ft)	2.1	1.4	1.3	1.7			0.7	0.7	0.7	1.0			0.6	0.6	0.7	0.9			0.7	0.7	0.7	0.7		
Width/Depth Ratio	----	----	----	----			14.4	16.5	16.1	12.4			18.1	14.5	16.3	16.1			16.0	18.5	17.0	17.7		
Entrenchment Ratio	----	----	----	----			12.5	12.0	12.3	14.1			11.8	13.2	12.9	12.9			11.3	11.7	11.8	11.6		
Bank Height Ratio	----	----	----	----			1.0	1.0	1.0	1.0			1.0	1.0	1.17	1.10			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	9.5	9.2	10.4	10			7.5	7.8	7.5	6.8			9.3	7.0	7.2	7.4			9.3	7.8	7.8	8		
Hydraulic Radius (ft)	1	0.6	0.5	0.5			0.5	0.4	0.4	0.5			0.5	0.5	0.4	0.4			0.5	0.4	0.4	0.4		
Substrate																								
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

**Table 12E. Morphology and Hydraulic Monitoring Summary
Aycock UT-3 - Stream and Wetland Restoration Site**

Parameter	XS 1 Riffle (UT 3)						XS 2 Riffle (UT 3)						XS 3 Pool (UT 3)						XS 4 Riffle (UT 3)						XS 5 Riffle (UT 3)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	6.5	6.9	6.7	7.2			4.7	5.2	5.2	5.1			5	5.4	5.2	5.7			7	6.8	6.9	7.5			5.3	5.6	5.8	6.5		
Floodprone Width (ft)	10	11	11	11			20	8	8	8			----	----	----	----			20	20	20	20			20	20	20	20		
BF Cross Sectional Area (ft2)	2.7	2.3	2.4	2.4			1.9	1.6	1.9	1.9			3.6	3.2	3.2	3.2			2.2	1.9	1.7	1.7			1.2	1.1	1.2	1.2		
BF Mean Depth (ft)	0.4	0.3	0.4	0.3			0.4	0.3	0.4	0.4			0.7	0.6	0.6	0.6			0.3	0.3	0.2	0.2			0.2	0.2	0.2	0.2		
BF Max Depth (ft)	0.6	0.6	0.6	0.7			0.6	0.5	0.6	0.6			1	0.9	0.8	0.8			0.5	0.4	0.4	0.4			0.5	0.4	0.4	0.4		
Width/Depth Ratio	15.6	20.7	18.7	21.8			11.6	16.9	14.2	13.9			----	----	----	----			22.3	24.3	28.0	33.7			23.4	28.5	28.0	35.4		
Entrenchment Ratio	1.5	1.6	1.6	1.5			4.3	1.5	1.5	1.6			----	----	----	----			2.9	2.9	2.9	2.7			3.8	3.6	3.4	3.1		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0			----	----	----	----			1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	6.8	7.1	6.9	7.5			5.0	5.3	5.4	5.3			5.7	5.8	5.7	6.2			7.1	6.9	7.0	7.7			5.7	5.8	6.0	6.7		
Hydraulic Radius (ft)	0.4	0.3	0.3	0.3			0.4	0.3	0.4	0.4			0.6	0.6	0.6	0.5			0.3	0.3	0.2	0.2			0.2	0.2	0.2	0.2		
Substrate																														
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

**Table 12F. Morphology and Hydraulic Monitoring Summary
Aycock UT-4 - Stream and Wetland Restoration Site**

Parameter	XS 1 Riffle (UT 4)						XS 2 Pool (UT 4)						XS 3 Riffle (UT 4)						XS 4 Pool (UT 4)						XS 5 Riffle (UT 4)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																														
BF Width (ft)	8.3	9.4	8.8	9.1			8.5	9.1	9.5	9.2			8.6	8.7	8.4	9			8.5	10.6	10.7	10.5			8	8.3	7.8	7.9		
Floodprone Width (ft)	50	50	50	50			----	----	----	----			50	50	50	50			----	----	----	----			50	50	50	50		
BF Cross Sectional Area (ft2)	3.7	3.3	3.3	3.3			6.4	5.4	5.8	5.8			4.3	3.4	3.5	3.5			6.2	5.2	5.6	5.6			4.3	4.1	3.8	3.8		
BF Mean Depth (ft)	0.4	0.4	0.4	0.4			0.8	0.6	0.6	0.6			0.5	0.4	0.4	0.4			0.7	0.5	0.5	0.5			0.5	0.5	0.5	0.5		
BF Max Depth (ft)	0.6	0.5	0.6	0.6			1.5	1	1.1	1			0.8	0.5	0.6	0.6			1.2	1	1.1	1.2			0.7	0.7	0.7	0.7		
Width/Depth Ratio	18.6	26.8	23.5	25.2			----	----	----	----			17.2	22.3	20.2	23.2			----	----	----	----			14.9	16.8	16.0	16.5		
Entrenchment Ratio	6.0	5.3	5.7	5.5			----	----	----	----			5.8	5.7	6.0	5.6			----	----	----	----			6.3	6.0	6.4	6.3		
Bank Height Ratio	1.0	1.0	1.0	1.0			----	----	----	----			1.0	1.0	1.0	1.0			----	----	----	----			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	8.6	9.5	9.0	9.3			9.2	9.5	10.0	9.8			9.0	8.8	8.6	9.1			9.1	10.9	11.1	11.0			8.3	8.5	8.1	8.2		
Hydraulic Radius (ft)	0.4	0.3	0.4	0.4			0.7	0.6	0.6	0.6			0.5	0.4	0.4	5.6			0.7	0.5	0.5	0.5			0.5	0.5	0.5	0.5		
Substrate																														
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----			----	----	----	----		

Parameter	XS 6 Riffle (UT 4)						XS 7 Riffle (UT 4)						XS 8 Riffle (UT 4)					
	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5	MY 0	MY1	MY2	MY3	MY4	MY5
Dimension																		
BF Width (ft)	8.1	8.9	8.9	8.4			9.9	11.7	9.1	9.8			10.9	11.1	11	10.6		
Floodprone Width (ft)	50	50	50	50			50	50	50	50			50	50	50	50		
BF Cross Sectional Area (ft2)	3.5	3.3	3.3	3.3			5.6	4.9	5	5			5.6	4.9	4.9	4.9		
BF Mean Depth (ft)	0.4	0.4	0.4	0.4			0.6	0.4	0.5	0.5			0.5	0.4	0.4	0.5		
BF Max Depth (ft)	0.6	0.5	0.6	0.7			0.9	0.6	0.8	0.7			0.8	0.7	0.7	0.7		
Width/Depth Ratio	18.7	24.0	24.0	21.7			17.5	27.9	16.6	19			21.2	25.1	24.7	22.9		
Entrenchment Ratio	6.2	5.6	5.6	5.9			5.1	4.3	5.5	5.1			4.6	4.5	4.5	4.7		
Bank Height Ratio	1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0			1.0	1.0	1.0	1.0		
Wetted Perimeter (ft)	8.4	9.0	9.0	8.9			10.2	11.9	9.4	10			11.1	11.3	11.2	10.8		
Hydraulic Radius (ft)	0.4	0.4	0.4	0.4			0.6	0.4	0.5	0.5			0.5	0.4	0.4	0.5		
Substrate																		
d50 (mm)	----	----	----	----			----	----	----	----			----	----	----	----		
d84 (mm)	----	----	----	----			----	----	----	----			----	----	----	----		

APPENDIX E
HYDROLOGY DATA

Table 13. UT3 Channel Evidence

Stream Gauge Graphs

Table 14. Verification of Bankfull Events

Groundwater Gauge Graphs

Table 15. Groundwater Hydrology Data

Table 13. UT3 Channel Evidence

UT3 Channel Evidence	Year 1 (2016)	Year 2 (2017)	Year 3 (2018)
Max consecutive days channel flow	37	110	276
Presence of litter and debris (wracking)	Yes	Yes	Yes
Leaf litter disturbed or washed away	Yes	Yes	Yes
Matted, bent, or absence of vegetation (herbaceous or otherwise)	Yes	Yes	Yes
Sediment deposition and/or scour indicating sediment transport	Yes	Yes	Yes
Water staining due to continual presence of water	Yes	Yes	Yes
Formation of channel bed and banks	Yes	Yes	Yes
Sediment sorting within the primary path of flow	Yes	Yes	Yes
Sediment shelving or a natural line impressed on the banks	Yes	Yes	Yes
Change in plant community (absence or destruction of terrestrial vegetation and/or transition to species adapted for flow or inundation for a long duration, including hydrophytes)	Yes	Yes	Yes
Development of channel pattern (meander bends and/or channel braiding) at natural topographic breaks, woody debris piles, or plant root systems	Yes	Yes	Yes
Exposure of woody plant roots within the primary path of flow	No	No	No
Other:			



Aycock Springs Surface Gauge UT-3 Year 3 (2018 Data)

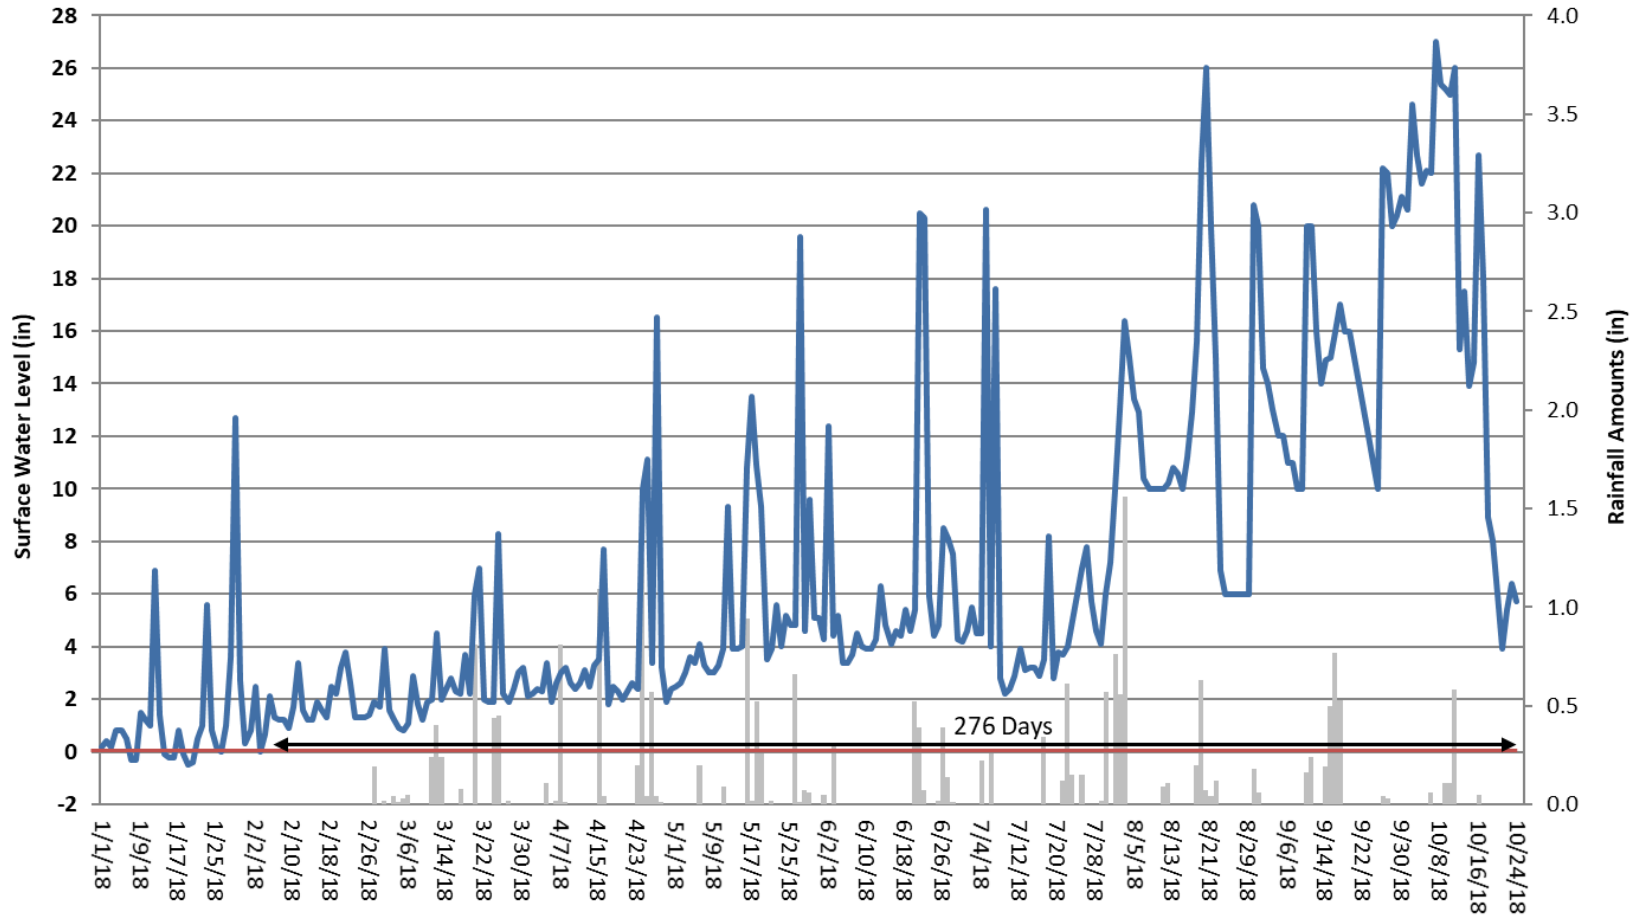


Table 14. Verification of Bankfull Events

Date of Data Collection	Date of Occurrence	Method	Photo (if available)
May 5, 2016	May 3, 2016	Wrack, laid-back vegetation, sediment, and standing water observed in the floodplain after 1.55 inches of rain documented* on May 3, 2016 at a nearby rain gauge.	1
October 13, 2016	September 28, 2016	2.05 inches of rain was recorded on September 28, 2016 at an onsite rain gauge.	--
October 13, 2016	October 8, 2016	Wrack and laid-back vegetation observed on top of bank after 3.05 inches of rain was recorded on October 8, 2016 at an onsite rain gauge.	2
June 15, 2017	April 25, 2017	4.66 inches of rain was recorded between April 23 and 25, 2017 at an onsite rain gauge.	--
October 27, 2017	June 19, 2017	Wrack and laid back vegetation observed in the floodplain of Travis Creek after 1.93 inches of rain was recorded on June 19, 2017 at an onsite rain gauge	3
October 24, 2018	September 17, 2018	Overbank as the result of Hurricane Florence on September 15-17, 2018.	--
October 24, 2018	October 11, 2018	Overbank as the result of Hurricane Michael on October 11, 2018.	--

*The onsite rain gauge was installed on May 18, 2016, therefore rain data from a nearby Site (Abbey Lamm Stream and Wetland Mitigation Site) was used to confirm this bankfull event.

Bankfull Photo 1: Wrack, laid-back vegetation, and sediment in the floodplain of Travis Creek



Bankfull Photo 2: Wrack and laid-back vegetation on the top of bank of Travis Creek



Bankfull Photo 3: Wrack and laid-back vegetation around a cross-section marker in the floodplain of Travis Creek



Table 15. Groundwater Hydrology Data

Gauge	Success Criteria Achieved/Max Consecutive Days During Growing Season (Percentage)						
	Year 1* (2016)	Year 2 (2017)	Year 3 (2018)	Year 4 (2019)	Year 5 (2020)	Year 6 (2021)	Year 7 (2022)
1	Yes/55 days (29.1 percent)	Yes/26 days (11.0 percent)	Yes/58 days (25.1 percent)				
2	Yes/46 days (24.3 percent)	Yes/25 days (10.5 percent)	Yes/65 days (28.1 percent)				
3	Yes/44 days (23.3 percent)	Yes/25 days (10.5 percent)	Yes/46 days (19.9 percent)				

*Due to Site construction activities, groundwater gauges were not installed until May 5, 2016; therefore, the growing season for Year 1 (2016) is based on the soil survey start date of April 17. It is expected that all gauges would meet success criteria at the beginning of the growing season.

APPENDIX F
BENTHIC DATA

Results

Habitat Assessment Data Sheets

PAI ID NO			51449	51450	51451
STATION			UT-1	UT-2	UT-4
DATE			6/15/2018	6/15/2018	6/15/2018
SPECIES	T.V.	F.F.G.			
MOLLUSCA					
Bivalvia					
Veneroidea					
Sphaeriidae		FC			
<i>Pisidium sp.</i>	6.6	FC			5
<i>Sphaerium sp.</i>	7.2	FC		1	
Gastropoda					
Basommatophora					
Planorbidae		SC			
<i>Menetus dilatatus</i>	7.6	SC	1		
ANNELIDA					
Clitellata					
Oligochaeta		CG			
Naididae					
Tubificida					
Tubificinae w.h.c.		CG	1		
Lumbriculida					
Lumbriculidae		CG	1		
Hirudinea		P			
Arhynchobdellida					
Erpobdellidae		P		4	1
Rhynchobdellida					
Glossiphoniidae		P			
<i>Placobdella papillifera</i>	8.2	P			2
ARTHROPODA					
Crustacea					
Ostracoda			1		
Isopoda					
Asellidae		SH			
<i>Caecidotea sp.</i>	8.4	CG	16	16	30
Amphipoda		CG			
Crangonyctidae					
<i>Crangonyx sp.</i>	7.2	CG	3	19	3
Insecta					
Ephemeroptera					
Baetidae		CG			
<i>Neocloeon triangulifer</i>			5		
Caenidae		CG			
<i>Caenis sp.</i>	6.8	CG	52		2
Odonata					
Coenagrionidae		P			
<i>Argia sp.</i>	8.3	P	8		
<i>Ischnura sp.</i>	9.5		2		3
Corduliidae					
<i>Somatochlora sp.</i>	8.9	P		1	1
Libellulidae		P		1	

PAI ID NO			51449	51450	51451
STATION			UT-1	UT-2	UT-4
DATE			6/15/2018	6/15/2018	6/15/2018
SPECIES	T.V.	F.F.G.			
Hemiptera					
Belostomatidae					
<i>Belostoma sp.</i>	9.5	P			1
Corixidae		PI	1		
Megaloptera					
Corydalidae					
<i>Chauliodes sp.</i>		P	1		
Sialidae		P			
<i>Sialis sp.</i>	7	P			1
Coleoptera					
Dytiscidae					
<i>Celina sp.</i>		P	1		
<i>Hydrovatus sp.</i>					9
<i>Neoporus sp.</i>	5				3
Elmidae					
<i>Dubiraphia sp.</i>	5.5	SC	1		
Haliplidae					
<i>Pelodytes muticus</i>	8.4	SH		1	1
Hydrophilidae					
<i>Enochrus ocnraceus</i>	8.5	CG		1	
<i>Tropisternus sp.</i>	9.3	P	1	1	2
Diptera					
Chironomidae					
<i>Chironomus sp.</i>	9.3	CG	2	34	
<i>Clinotanypus sp.</i>	7.8	P	1		2
<i>Conchapelopia sp.</i>	8.4	P			1
<i>Paratendipes albimanus/duplicatus</i>	5.6		2		
<i>Polypedilum flavum</i>	5.7	SH			1
<i>Polypedilum illinoense gp.</i>	8.7	SH	1		
<i>Psectrotanypus sp.</i>				3	
<i>Rheotanytarsus exiguus gp.</i>	6.5	FC			1
Culicidae					
<i>Anopheles sp.</i>	8.6	FC	6		
<i>Culex sp.</i>		FC		1	
Ptychopteridae					
<i>Bittacomorpha clavipes</i>				9	22
Tabanidae					
<i>Chrysops sp.</i>	6.7	PI		1	
Tipulidae					
<i>Tipula sp.</i>	7.5	SH	2	1	
TOTAL NO. OF ORGANISMS					
			110	94	93
TOTAL NO. OF TAXA					
			22	15	20
EPT TAXA					
			2	0	1
BIOTIC INDEX Assigned values					
			7.77	8.26	7.74

180613

Habitat Assessment Field Data Sheet
Mountain/ Piedmont Streams

Aycock UT-1

Biological Assessment Unit, DWQ

TOTAL SCORE [REDACTED] 82

Directions for use: The observer is to survey a minimum of 100 meters with 200 meters preferred of stream, preferably in an upstream direction starting above the bridge pool and the road right-of-way. The segment which is assessed should represent average stream conditions. To perform a proper habitat evaluation the observer needs to get into the stream. To complete the form, select the description which best fits the observed habitats and then circle the score. If the observed habitat falls in between two descriptions, select an intermediate score. A final habitat score is determined by adding the results from the different metrics.

Stream UT to Travis Creek Location/road: Off Gibsonville (Mississippi Road) (Road Name) County Alamance

Date 180613 CC# 03030002 Basin Cape Fear Subbasin 03-06-02

Observer(s) Fagun/Reynolds Type of Study: Fish Benthos Basinwide Special Study (Describe) _____

Latitude 36.128077 Longitude -77.521127 Ecoregion: MT P Slate Belt Triassic Basin

Water Quality: Temperature _____ °C DO _____ mg/l Conductivity (corr.) _____ μS/cm pH _____

Physical Characterization: Visible land use refers to immediate area that you can see from sampling location - include what you estimate driving thru the watershed in watershed land use.

Visible Land Use: 10 %Forest _____ %Residential 90 %Active Pasture _____ % Active Crops
_____ %Fallow Fields _____ % Commercial _____ %Industrial _____ %Other - Describe: _____

Watershed land use: Forest Agriculture Urban Animal operations upstream

Width: (meters) Stream 0.5 Channel (at top of bank) 1.5 Stream Depth: (m) Avg 0.1 Max 0.3
 Width variable Large river >25m wide

Bank Height (from deepest part of riffle to top of bank-first flat surface you stand on): (m) 0.5

Bank Angle: 45 ° or NA (Vertical is 90°, horizontal is 0°. Angles > 90° indicate slope is towards mid-channel, < 90° indicate slope is away from channel. NA if bank is too low for bank angle to matter.)

Channelized Ditch

Deeply incised-steep, straight banks Both banks undercut at bend Channel filled in with sediment
 Recent overbank deposits Bar development Buried structures Exposed bedrock
 Excessive periphyton growth Heavy filamentous algae growth Green tinge Sewage smell

Manmade Stabilization: N Y: Rip-rap, cement, gabions Sediment/grade-control structure Berm/levee

Flow conditions: High Normal Low

Turbidity: Clear Slightly Turbid Turbid Tannic Milky Colored (from dyes)

Good potential for Wetlands Restoration Project?? YES NO Details Mitigation site

Channel Flow Status

Useful especially under abnormal or low flow conditions.

- A. Water reaches base of both lower banks, minimal channel substrate exposed
- B. Water fills >75% of available channel, or <25% of channel substrate is exposed.....
- C. Water fills 25-75% of available channel, many logs/snags exposed.....
- D. Root mats out of water.....
- E. Very little water in channel, mostly present as standing pools.....

Weather Conditions: hot, sunny Photos: N Y Digital 35mm

Remarks: Restoration project; fish (small minnows) abundant; water beetles, crayfish, water boatmen, algae present; abundance of eggs on under side of rocks; abundance of snails

Vegetation has improved, lots of marshes and snails

I. Channel Modification

A. channel natural, frequent bends.....	Score	5
B. channel natural, infrequent bends (channelization could be old).....		4
C. some channelization present.....		3
D. more extensive channelization, >40% of stream disrupted.....		2
E. no bends, completely channelized or rip rapped or gabioned, etc.....		0

Evidence of dredging Evidence of desnagging=no large woody debris in stream Banks of uniform shape/height

Remarks Restoration reach Subtotal 5

II. Instream Habitat: Consider the percentage of the reach that is favorable for benthos colonization or fish cover. If >70% of the reach is rocks, 1 type is present, circle the score of 17. Definition: leafpacks consist of older leaves that are packed together and have begun to decay (not piles of leaves in pool areas). Mark as Rare, Common, or Abundant.

C Rocks A Macrophytes R Sticks and leafpacks Snags and logs C Undercut banks or root mats

AMOUNT OF REACH FAVORABLE FOR COLONIZATION OR COVER

	>70%	40-70%	20-40%	<20%
	Score	Score	Score	Score
4 or 5 types present.....	20	16	12	8
3 types present.....	19	15	11	7
2 types present.....	18	14	10	6
1 type present.....	17	13	9	5
No types present.....	0			

No woody vegetation in riparian zone Remarks _____ Subtotal 16

III. Bottom Substrate (silt, sand, detritus, gravel, cobble, boulder) Look at entire reach for substrate scoring, but only look at riffle for embeddedness, and use rocks from all parts of riffle-look for "mud line" or difficulty extracting rocks.

A. substrate with good mix of gravel, cobble and boulders	Score
1. embeddedness <20% (very little sand, usually only behind large boulders).....	15
2. embeddedness 20-40%.....	12
3. embeddedness 40-80%.....	8
4. embeddedness >80%.....	3
B. substrate gravel and cobble	
1. embeddedness <20%.....	14
2. embeddedness 20-40%.....	11
3. embeddedness 40-80%.....	6
4. embeddedness >80%.....	2
C. substrate mostly gravel	
1. embeddedness <50%.....	8
2. embeddedness >50%.....	4
D. substrate homogeneous	
1. substrate nearly all bedrock.....	3
2. substrate nearly all sand.....	3
3. substrate nearly all detritus.....	2
4. substrate nearly all silt/ clay.....	1

Remarks _____ Subtotal 6

IV. Pool Variety Pools are areas of deeper than average maximum depths with little or no surface turbulence. Water velocities associated with pools are always slow. Pools may take the form of "pocket water", small pools behind boulders or obstructions, in large high gradient streams, or side eddies.

A. Pools present	Score
1. Pools Frequent (>30% of 200m area surveyed)	
a. variety of pool sizes.....	10
b. pools about the same size (indicates pools filling in).....	8
2. Pools Infrequent (<30% of the 200m area surveyed)	
a. variety of pool sizes.....	6
b. pools about the same size.....	4
B. Pools absent.....	0

Pool bottom boulder-cobble=hard Bottom sandy-sink as you walk Silt bottom Some pools over wader depth

Remarks _____ Subtotal 10

V. Riffle Habitats

Definition: Riffle is area of reaeration-can be debris dam, or narrow channel area. **Riffles Frequent** **Riffles Infrequent**

	Score	Score
A. well defined riffle and run, riffle as wide as stream and extends 2X width of stream....	16	12
B. riffle as wide as stream but riffle length is not 2X stream width	14	7
C. riffle not as wide as stream and riffle length is not 2X stream width	10	3
D. riffles absent.....	0	

Channel Slope: Typical for area Steep=fast flow Low=like a coastal stream Subtotal 16

VI. Bank Stability and Vegetation

FACE UPSTREAM

	Left Bank Score	Rt. Bank Score
A. Banks stable		
1. little evidence of erosion or bank failure(except outside of bends), little potential for erosion.	7	7
B. Erosion areas present		
1. diverse trees, shrubs, grass; plants healthy with good root systems.....	6	6
2. few trees or small trees and shrubs; vegetation appears generally healthy.....	5	5
3. sparse mixed vegetation; plant types and conditions suggest poorer soil binding.....	3	3
4. mostly grasses, few if any trees and shrubs, high erosion and failure potential at high flow..	2	2
5. little or no bank vegetation, mass erosion and bank failure evident.....	0	0
		Total <u>14</u>

Remarks _____

VII. Light Penetration Canopy is defined as tree or vegetative cover directly above the stream's surface. Canopy would block out sunlight when the sun is directly overhead. Note shading from mountains, but not use to score this metric.

	Score
A. Stream with good canopy with some breaks for light penetration	10
B. Stream with full canopy - breaks for light penetration absent.....	8
C. Stream with partial canopy - sunlight and shading are essentially equal.....	7
D. Stream with minimal canopy - full sun in all but a few areas.....	2
E. No canopy and no shading.....	0

Remarks Year 3 post restoration. Subtotal 7

VIII. Riparian Vegetative Zone Width

Definition: Riparian zone for this form is area of natural vegetation adjacent to stream (can go beyond floodplain). Definition: A break in the riparian zone is any place on the stream banks which allows sediment or pollutants to directly enter the stream, such as paths down to stream, storm drains, uprooted trees, otter slides, etc.

FACE UPSTREAM

Dominant vegetation: <input checked="" type="checkbox"/> Trees <input checked="" type="checkbox"/> Shrubs <input checked="" type="checkbox"/> Grasses <input type="checkbox"/> Weeds/old field <input type="checkbox"/> Exotics (kudzu, etc)	Lft. Bank Score	Rt. Bank Score
A. Riparian zone intact (no breaks)		
1. width > 18 meters.....	5	5
2. width 12-18 meters.....	4	4
3. width 6-12 meters.....	3	3
4. width < 6 meters.....	2	2
B. Riparian zone not intact (breaks)		
1. breaks rare		
a. width > 18 meters.....	4	4
b. width 12-18 meters.....	3	3
c. width 6-12 meters.....	2	2
d. width < 6 meters.....	1	1
2. breaks common		
a. width > 18 meters.....	3	3
b. width 12-18 meters.....	2	2
c. width 6-12 meters.....	1	1
d. width < 6 meters.....	0	0



Remarks Year 2 post restoration Total 8

Disclaimer-form filled out, but score doesn't match subjective opinion-atypical stream.

Page Total 40
TOTAL SCORE 24

Supplement for Habitat Assessment Field Data Sheet

Diagram to determine bank angle:

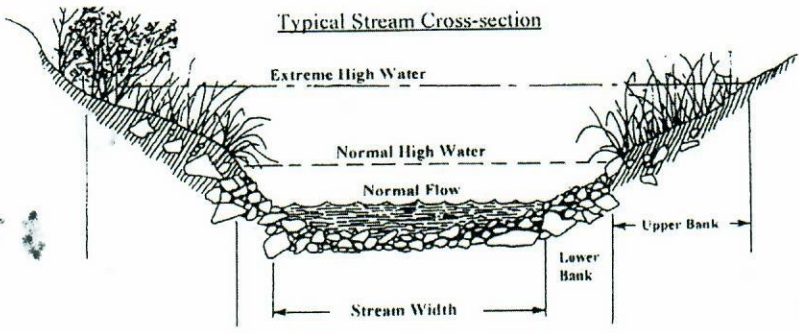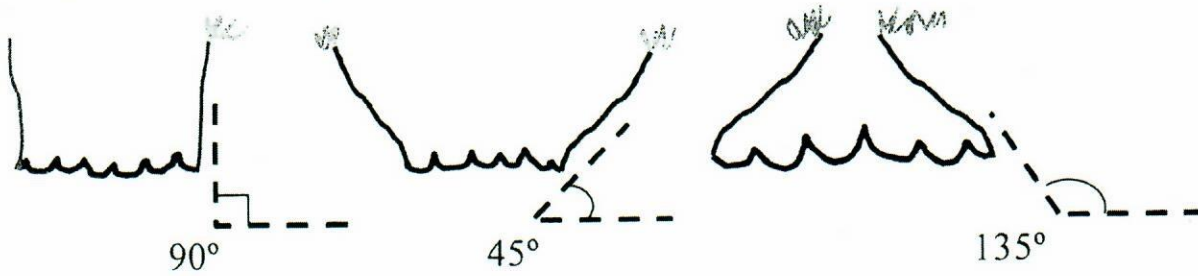

This side is 45° bank angle.

Site Sketch:

Other comments: _____

190613
Aycock - UT-2

Habitat Assessment Field Data Sheet
Mountain/ Piedmont Streams

Biological Assessment Unit, DWQ

TOTAL SCORE 79

Directions for use: The observer is to survey a minimum of 100 meters with 200 meters preferred of stream, preferably in an upstream direction starting above the bridge pool and the road right-of-way. The segment which is assessed should represent average stream conditions. To perform a proper habitat evaluation the observer needs to get into the stream. To complete the form, select the description which best fits the observed habitats and then circle the score. If the observed habitat falls in between two descriptions, select an intermediate score. A final habitat score is determined by adding the results from the different metrics.

Stream UT to Travis Creek Location/road: off Gibsonville Ossipee Road (Road Name _____) County Alamance

Date 190613 CC# 03030002 Basin Cape Fear Subbasin 03-06-02

Observer(s) Faquin PERKINSON Type of Study: Fish Benthos Basinwide Special Study (Describe) _____

Latitude 36.128128 Longitude -79.521813 Ecoregion: MT P Slate Belt Triassic Basin

Water Quality: Temperature _____ °C DO _____ mg/l Conductivity (corr.) _____ µS/cm pH _____

Physical Characterization: Visible land use refers to immediate area that you can see from sampling location - include what you estimate driving thru the watershed in watershed land use.

Visible Land Use: 10 %Forest _____ %Residential 90 %Active Pasture _____ % Active Crops
_____ %Fallow Fields _____ % Commercial _____ %Industrial _____ %Other - Describe: _____

Watershed land use: Forest Agriculture Urban Animal operations upstream

Width: (meters) Stream 0.3 Channel (at top of bank) 1.5 Stream Depth: (m) Avg 0.025 Max 0.05
 Width variable Large river >25m wide

Bank Height (from deepest part of riffle to top of bank-first flat surface you stand on): (m) 0.25-0.5

Bank Angle: 45 ° or NA (Vertical is 90°, horizontal is 0°. Angles > 90° indicate slope is towards mid-channel, < 90° indicate slope is away from channel. NA if bank is too low for bank angle to matter.)

- Channelized Ditch
- Deeply incised-steep, straight banks Both banks undercut at bend Channel filled in with sediment
- Recent overbank deposits Bar development Buried structures Exposed bedrock
- Excessive periphyton growth Heavy filamentous algae growth Green tinge Sewage smell

Manmade Stabilization: N Y: Rip-rap, cement, gabions Sediment/grade-control structure Berm/levee

Flow conditions: High Normal Low
Turbidity: Clear Slightly Turbid Turbid Tannic Milky Colored (from dyes)

Good potential for Wetlands Restoration Project?? YES NO Details Mitigation site

Channel Flow Status

- Useful especially under abnormal or low flow conditions.
- A. Water reaches base of both lower banks, minimal channel substrate exposed
- B. Water fills >75% of available channel, or <25% of channel substrate is exposed.....
- C. Water fills 25-75% of available channel, many logs/snags exposed.....
- D. Root mats out of water.....
- E. Very little water in channel, mostly present as standing pools.....

Weather Conditions: hot sunny Photos: N Y Digital 35mm

Remarks: aquatic vegetation in channel is abundant; abundance of tadpoles; abundance of snails

lots of *Juncus* in channel, also lots of *fe*
many scuds!!; LH snails
No small *to* 11/16/12

I. Channel Modification

- A. channel natural, frequent bends..... 5
- B. channel natural, infrequent bends (channelization could be old)..... 4
- C. some channelization present..... 3
- D. more extensive channelization, >40% of stream disrupted..... 2
- E. no bends, completely channelized or rip rapped or gabioned, etc..... 0

Evidence of dredging Evidence of desnagging=no large woody debris in stream Banks of uniform shape/height
 Remarks _____ Subtotal 5

II. Instream Habitat: Consider the percentage of the reach that is favorable for benthos colonization or fish cover. If >70% of the reach is rocks, 1 type is present, circle the score of 17. Definition: leafpacks consist of older leaves that are packed together and have begun to decay (not piles of leaves in pool areas). Mark as Rare, Common, or Abundant.

R Rocks A Macrophytes R Sticks and leafpacks _____ Snags and logs A Undercut banks or root mats

AMOUNT OF REACH FAVORABLE FOR COLONIZATION OR COVER

	>70%	40-70%	20-40%	<20%
	Score	Score	Score	Score
4 or 5 types present.....	<u>20</u>	16	12	8
3 types present.....	19	15	11	7
2 types present.....	18	14	10	6
1 type present.....	17	13	9	5
No types present.....	0			

No woody vegetation in riparian zone _____ Remarks _____ Subtotal 20

III. Bottom Substrate (silt, sand, detritus, gravel, cobble, boulder) Look at entire reach for substrate scoring, but only look at riffle for embeddedness, and use rocks from all parts of riffle-look for "mud line" or difficulty extracting rocks.

A. substrate with good mix of gravel, cobble and boulders

- 1. embeddedness <20% (very little sand, usually only behind large boulders)..... 15
- 2. embeddedness 20-40%..... 12
- 3. embeddedness 40-80%..... 8
- 4. embeddedness >80%..... 3

B. substrate gravel and cobble

- 1. embeddedness <20%..... 14
- 2. embeddedness 20-40%..... 11
- 3. embeddedness 40-80%..... 6 ✓
- 4. embeddedness >80%..... 2

C. substrate mostly gravel

- 1. embeddedness <50%..... 8
- 2. embeddedness >50%..... 4

D. substrate homogeneous

- 1. substrate nearly all bedrock..... 3
- 2. substrate nearly all sand..... 3
- 3. substrate nearly all detritus..... 2
- 4. substrate nearly all silt/ clay..... 1

Remarks _____ Subtotal 6

IV. Pool Variety Pools are areas of deeper than average maximum depths with little or no surface turbulence. Water velocities associated with pools are always slow. Pools may take the form of "pocket water", small pools behind boulders or obstructions, in large high gradient streams, or side eddies.

A. Pools present

- 1. Pools Frequent (>30% of 200m area surveyed)
 - a. variety of pool sizes..... 10
 - b. pools about the same size (indicates pools filling in)..... 8
- 2. Pools Infrequent (<30% of the 200m area surveyed)
 - a. variety of pool sizes..... 6
 - b. pools about the same size..... 4

B. Pools absent

_____ Subtotal 0
 Pool bottom boulder-cobble=hard Bottom sandy-sink as you walk Silt bottom Some pools over water depth
 Remarks _____

V. Riffle Habitats

Definition: Riffle is area of reeration-can be debris dam, or narrow channel area. Riffles Frequent Riffles Infrequent

	Score	Score
A. well defined riffle and run, riffle as wide as stream and extends 2X width of stream....	16	12
B. riffle as wide as stream but riffle length is not 2X stream width	14	7
C. riffle not as wide as stream and riffle length is not 2X stream width	10	3
D. riffles absent.....	0	
Channel Slope: <input checked="" type="checkbox"/> Typical for area <input type="checkbox"/> Steep=fast flow <input type="checkbox"/> Low=like a coastal stream		Subtotal 16

VI. Bank Stability and Vegetation

FACE UPSTREAM

	Left Bank Score	Rt. Bank Score
A. Banks stable		
1. little evidence of erosion or bank failure(except outside of bends), little potential for erosion..	7	7
B. Erosion areas present		
1. diverse trees, shrubs, grass; plants healthy with good root systems.....	6	6
2. few trees or small trees and shrubs; vegetation appears generally healthy.....	5	5
3. sparse mixed vegetation; plant types and conditions suggest poorer soil binding.....	3	3
4. mostly grasses, few if any trees and shrubs, high erosion and failure potential at high flow..	2	2
5. little or no bank vegetation, mass erosion and bank failure evident.....	0	0
Remarks _____	Total 14	

VII. Light Penetration Canopy is defined as tree or vegetative cover directly above the stream's surface. Canopy would block out sunlight when the sun is directly overhead. Note shading from mountains, but not use to score this metric.

	Score
A. Stream with good canopy with some breaks for light penetration	10
B. Stream with full canopy - breaks for light penetration absent.....	8
C. Stream with partial canopy - sunlight and shading are essentially equal.....	7
D. Stream with minimal canopy - full sun in all but a few areas.....	2
E. No canopy and no shading.....	0

Remarks Year 3 post construction Subtotal 2 ✓

VIII. Riparian Vegetative Zone Width

Definition: Riparian zone for this form is area of natural vegetation adjacent to stream (can go beyond floodplain). Definition: A break in the riparian zone is any place on the stream banks which allows sediment or pollutants to directly enter the stream, such as paths down to stream, storm drains, uprooted trees, otter slides, etc.



Dominant vegetation: <input checked="" type="checkbox"/> Trees <input checked="" type="checkbox"/> Shrubs <input checked="" type="checkbox"/> Grasses <input type="checkbox"/> Weeds/old field <input type="checkbox"/> Exotics (kudzu, etc)		Lft. Bank Score	Rt. Bank Score
FACE UPSTREAM			
A. Riparian zone intact (no breaks)			
1. width > 18 meters.....		5	5
2. width 12-18 meters.....	4	4	4
3. width 6-12 meters.....	3	3	3
4. width < 6 meters.....	2	2	2
B. Riparian zone not intact (breaks)			
1. breaks rare			
a. width > 18 meters.....	4	4	4
b. width 12-18 meters.....	3	3	3
c. width 6-12 meters.....	2	2	2
d. width < 6 meters.....	1	1	1
2. breaks common			
a. width > 18 meters.....	3	3	3
b. width 12-18 meters.....	2	2	2
c. width 6-12 meters.....	1	1	1
d. width < 6 meters.....	0	0	0
Remarks <u>Year 2 post restoration</u>	Total 8		

Disclaimer-form filled out, but score doesn't match subjective opinion-atypical stream.

Page Total 40
TOTAL SCORE 79

Supplement for Habitat Assessment Field Data Sheet

Diagram to determine bank angle:

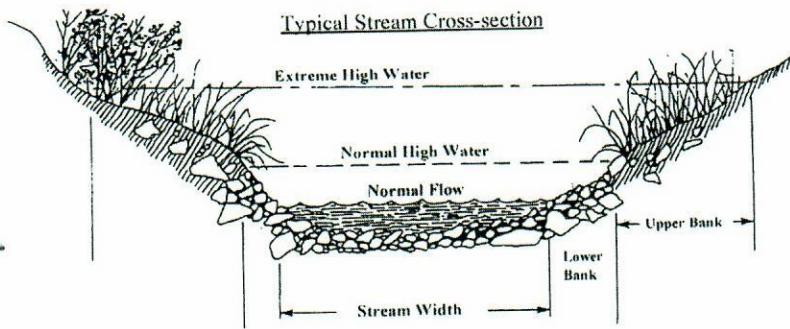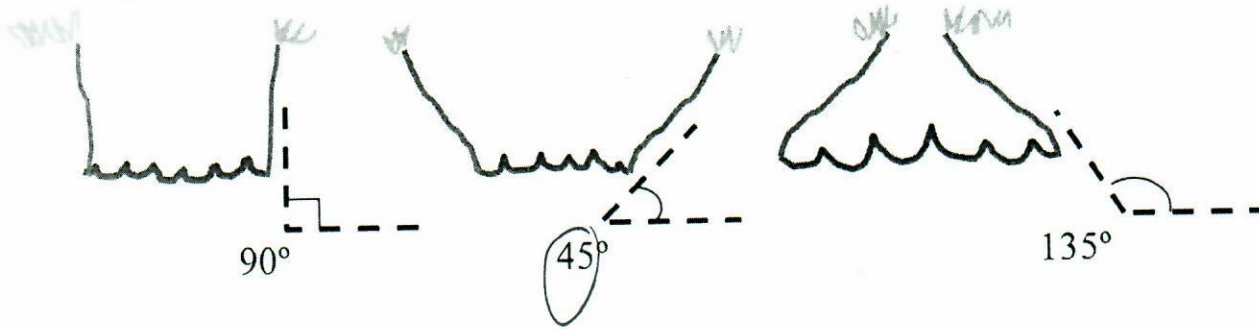

This side is 45° bank angle.

Site Sketch:

Other comments: _____

Habitat Assessment Field Data Sheet
Mountain/ Piedmont Streams

Aycock UT-4

Biological Assessment Unit, DWQ

TOTAL SCORE 80

Directions for use: The observer is to survey a minimum of 100 meters with 200 meters preferred of stream, preferably in an upstream direction starting above the bridge pool and the road right-of-way. The segment which is assessed should represent average stream conditions. To perform a proper habitat evaluation the observer needs to get into the stream. To complete the form, select the description which best fits the observed habitats and then circle the score. If the observed habitat falls in between two descriptions, select an intermediate score. A final habitat score is determined by adding the results from the different metrics.

Stream UT + Travis Creek Location/road: Gibsonville Ossipee Road (Road Name _____) County Alumance

Date 06/13/10 CC# 03030002 Basin Cape Fear Subbasin 03-06-02

Observer(s) Fagin, Robinson Type of Study: Fish Benthos Basinwide Special Study (Describe) _____

Latitude 36.129805 Longitude -79.527165 Ecoregion: MT P Slate Belt Triassic Basin

Water Quality: Temperature _____ °C DO _____ mg/l Conductivity (corr.) _____ µS/cm pH _____

Physical Characterization: Visible land use refers to immediate area that you can see from sampling location - include what you estimate driving thru the watershed in watershed land use.

Visible Land Use: 10 %Forest _____ %Residential 90 %Active Pasture _____ % Active Crops
_____ %Fallow Fields _____ % Commercial _____ %Industrial _____ %Other - Describe: _____

Watershed land use : Forest Agriculture Urban Animal operations upstream

Width: (meters) Stream 1.5 Channel (at top of bank) 2 Stream Depth: (m) Avg 0.1 Max 0.25
 Width variable Large river >25m wide

Bank Height (from deepest part of riffle to top of bank-first flat surface you stand on): (m) 1.0

Bank Angle: 45 ° or NA (Vertical is 90°, horizontal is 0°. Angles > 90° indicate slope is towards mid-channel, < 90° indicate slope is away from channel. NA if bank is too low for bank angle to matter.)

- Channelized Ditch
- Deeply incised-steep, straight banks Both banks undercut at bend Channel filled in with sediment
- Recent overbank deposits Bar development Buried structures Exposed bedrock
- Excessive periphyton growth Heavy filamentous algae growth Green tinge Sewage smell

Manmade Stabilization: N Y: Rip-rap, cement, gabions Sediment/grade-control structure Berm/levee

Flow conditions : High Normal Low
Turbidity: Clear Slightly Turbid Turbid Tannic Milky Colored (from dyes)

Good potential for Wetlands Restoration Project?? YES NO Details _____

Channel Flow Status

Useful especially under abnormal or low flow conditions.

- A. Water reaches base of both lower banks, minimal channel substrate exposed
- B. Water fills >75% of available channel, or <25% of channel substrate is exposed.....
- C. Water fills 25-75% of available channel, many logs/snags exposed.....
- D. Root mats out of water.....
- E. Very little water in channel, mostly present as standing pools.....

Weather Conditions: hot, sunny Photos: N Y Digital 35mm

Remarks: abundance of eggs on under side of rocks; abundance of snails

- I. Channel Modification**
- | | | |
|-------------------------------------------------------------------------|-------|---|
| A. channel natural, frequent bends..... | Score | 5 |
| B. channel natural, infrequent bends (channelization could be old)..... | | 4 |
| C. some channelization present..... | | 3 |
| D. more extensive channelization, >40% of stream disrupted..... | | 2 |
| E. no bends, completely channelized or rip rapped or gabioned, etc..... | | 0 |
- Evidence of dredging Evidence of desnagging=no large woody debris in stream Banks of uniform shape/height
- Remarks _____ Subtotal 5

II. Instream Habitat: Consider the percentage of the reach that is favorable for benthos colonization or fish cover. If >70% of the reach is rocks, 1 type is present, circle the score of 17. Definition: leafpacks consist of older leaves that are packed together and have begun to decay (not piles of leaves in pool areas). Mark as Rare, Common, or Abundant.

C Rocks R Macrophytes R Sticks and leafpacks Snags and logs R Undercut banks or root mats

AMOUNT OF REACH FAVORABLE FOR COLONIZATION OR COVER

	>70%	40-70%	20-40%	<20%
	Score	Score	Score	Score
4 or 5 types present.....	20	16	12	8
3 types present.....	19	15	11	7
2 types present.....	18	14	10	6
1 type present.....	17	13	9	5
No types present.....	0			

No woody vegetation in riparian zone Remarks _____ Subtotal 16

III. Bottom Substrate (silt, sand, detritus, gravel, cobble, boulder) Look at entire reach for substrate scoring, but only look at riffle for embeddedness, and use rocks from all parts of riffle-look for "mud line" or difficulty extracting rocks.

- | | |
|----------------------------------------------------------------------------------|--------------|
| A. substrate with good mix of gravel, cobble and boulders | Score |
| 1. embeddedness <20% (very little sand, usually only behind large boulders)..... | 15 |
| 2. embeddedness 20-40%..... | 12 |
| 3. embeddedness 40-80%..... | 8 |
| 4. embeddedness >80%..... | 3 |
| B. substrate gravel and cobble | |
| 1. embeddedness <20%..... | 14 |
| 2. embeddedness 20-40%..... | 11 |
| 3. embeddedness 40-80%..... | 6 |
| 4. embeddedness >80%..... | 2 |
| C. substrate mostly gravel | |
| 1. embeddedness <50%..... | 8 |
| 2. embeddedness >50%..... | 4 |
| D. substrate homogeneous | |
| 1. substrate nearly all bedrock..... | 3 |
| 2. substrate nearly all sand..... | 3 |
| 3. substrate nearly all detritus..... | 2 |
| 4. substrate nearly all silt/ clay..... | 1 |
- Remarks _____ Subtotal 11

IV. Pool Variety Pools are areas of deeper than average maximum depths with little or no surface turbulence. Water velocities associated with pools are always slow. Pools may take the form of "pocket water", small pools behind boulders or obstructions, in large high gradient streams, or side eddies.

- | | |
|----------------------------------------------------------------|--------------|
| A. Pools present | Score |
| 1. Pools Frequent (>30% of 200m area surveyed) | |
| a. variety of pool sizes..... | 10 |
| b. pools about the same size (indicates pools filling in)..... | 8 |
| 2. Pools Infrequent (<30% of the 200m area surveyed) | |
| a. variety of pool sizes..... | 6 |
| b. pools about the same size..... | 4 |
| B. Pools absent..... | 0 |
- Subtotal 8

Pool bottom boulder-cobble=hard Bottom sandy-sink as you walk Silt bottom Some pools over wader depth

Remarks _____

Page Total 40

V. Riffle Habitats

Definition: Riffle is area of reaeration-can be debris dam, or narrow channel area. Riffles **Frequent** Riffles **Infrequent**

	<u>Score</u>	<u>Score</u>
A. well defined riffle and run, riffle as wide as stream and extends 2X width of stream....	16	12
B. riffle as wide as stream but riffle length is not 2X stream width	14	7
C. riffle not as wide as stream and riffle length is not 2X stream width	10	3
D. riffles absent.....	0	
Channel Slope: <input type="checkbox"/> Typical for area <input type="checkbox"/> Steep=fast flow <input type="checkbox"/> Low=like a coastal stream		Subtotal <u>16</u>

VI. Bank Stability and Vegetation

FACE UPSTREAM

	<u>Left Bank Score</u>	<u>Rt. Bank Score</u>
A. Banks stable		
1. little evidence of erosion or bank failure(except outside of bends), little potential for erosion.	7	7
B. Erosion areas present		
1. diverse trees , shrubs, grass; plants healthy with good root systems.....	6	6
2. few trees or small trees and shrubs ; vegetation appears generally healthy.....	5	5
3. sparse mixed vegetation; plant types and conditions suggest poorer soil binding.....	3	3
4. mostly grasses , few if any trees and shrubs, high erosion and failure potential at high flow..	2	2
5. little or no bank vegetation, mass erosion and bank failure evident.....	0	0
Remarks _____		Total <u>14</u>

VII. Light Penetration Canopy is defined as tree or vegetative cover directly above the stream's surface. Canopy would block out sunlight when the sun is directly overhead. Note shading from mountains, but not use to score this metric.

	<u>Score</u>
A. Stream with good canopy with some breaks for light penetration	10
B. Stream with full canopy - breaks for light penetration absent.....	8
C. Stream with partial canopy - sunlight and shading are essentially equal.....	7
D. Stream with minimal canopy - full sun in all but a few areas.....	2
E. No canopy and no shading.....	0

Remarks Year 3 Post Restoration Subtotal 2

VIII. Riparian Vegetative Zone Width

Definition: Riparian zone for this form is area of natural vegetation adjacent to stream (can go beyond floodplain). Definition: A break in the riparian zone is any place on the stream banks which allows sediment or pollutants to directly enter the stream, such as paths down to stream, storm drains, uprooted trees, otter slides, etc.



		FACE UPSTREAM	
Dominant vegetation: <input checked="" type="checkbox"/> Trees <input checked="" type="checkbox"/> Shrubs <input checked="" type="checkbox"/> Grasses <input type="checkbox"/> Weeds/old field <input type="checkbox"/> Exotics (kudzu, etc)		<u>Lft. Bank Score</u>	<u>Rt. Bank Score</u>
A. Riparian zone intact (no breaks)			
1. width > 18 meters.....		5	5
2. width 12-18 meters.....		4	4
3. width 6-12 meters.....		3	3
4. width < 6 meters.....		2	2
B. Riparian zone not intact (breaks)			
1. breaks rare			
a. width > 18 meters.....		4	4
b. width 12-18 meters.....		3	3
c. width 6-12 meters.....		2	2
d. width < 6 meters.....		1	1
2. breaks common			
a. width > 18 meters.....		3	3
b. width 12-18 meters.....		2	2
c. width 6-12 meters.....		1	1
d. width < 6 meters.....		0	0
Remarks <u>Year 3 Post Restoration</u>			Total <u>9</u>

Disclaimer-form filled out, but score doesn't match subjective opinion-atypical stream.

Page Total 40
TOTAL SCORE 90

Supplement for Habitat Assessment Field Data Sheet

Diagram to determine bank angle:

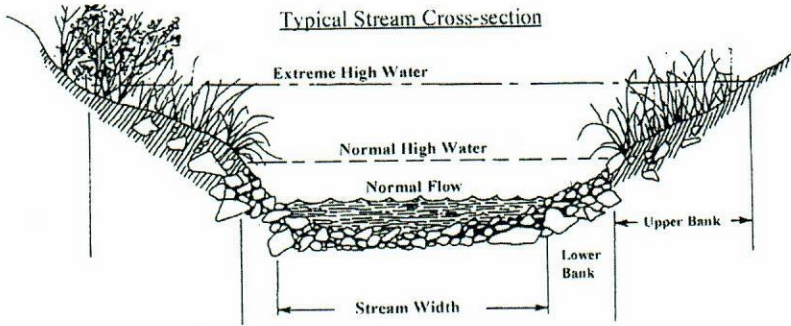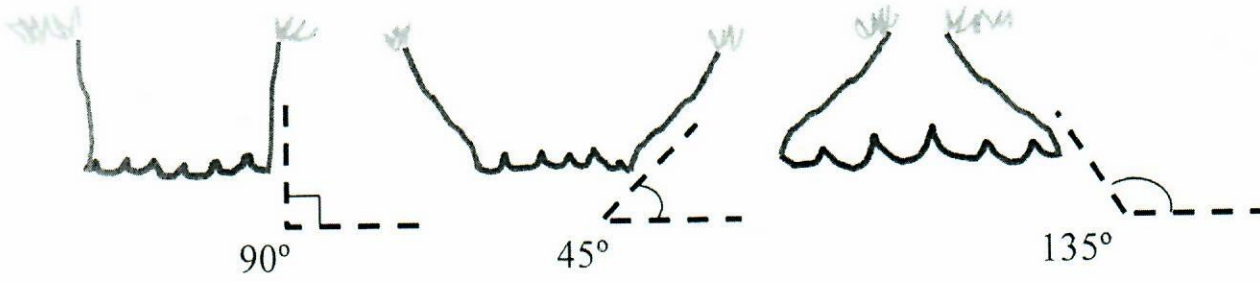

This side is 45° bank angle.

Site Sketch:


Other comments: _____

APPENDIX G
REMEDIAL ACTION PLAN

Aycock Springs Stream and Wetland Mitigation Site Remedial Action Update March 3, 2017 NC DMS Contract #5791



Aycock Springs- Remedial Action Plan - Vegetation Update

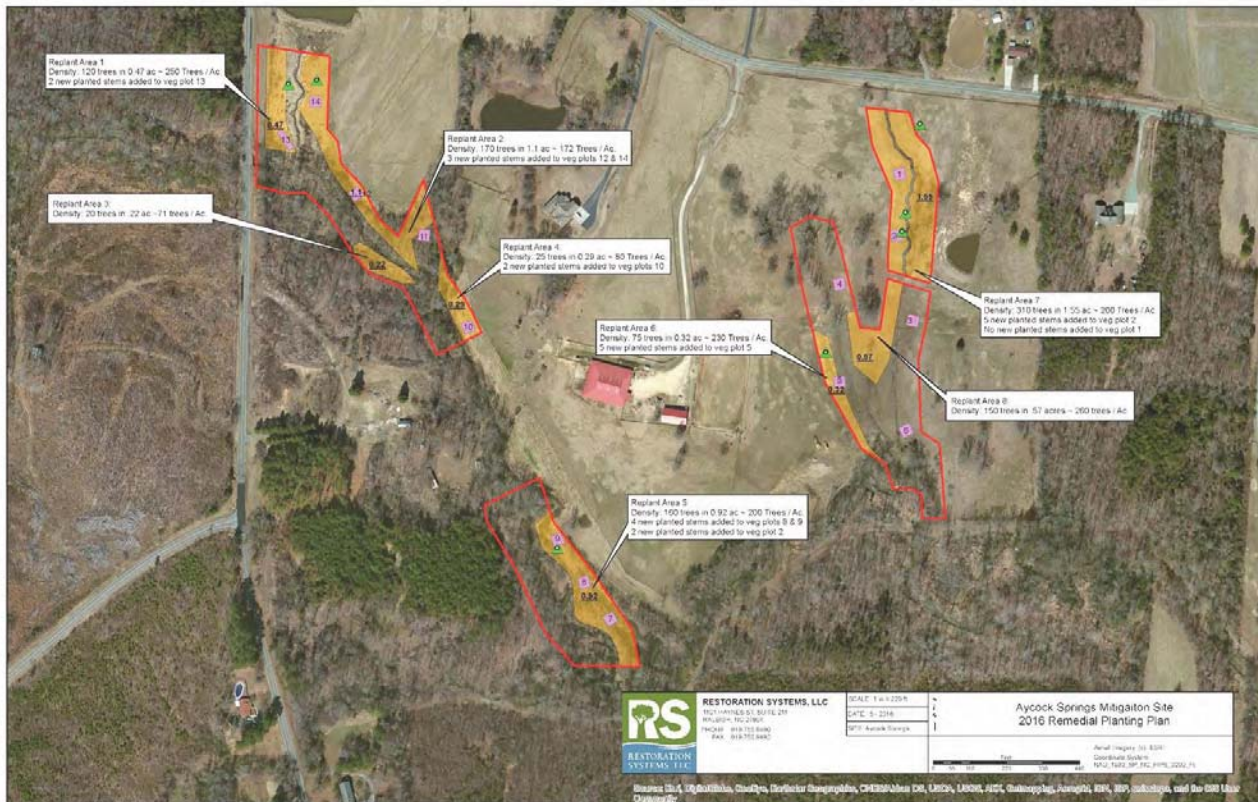

Map of Replant Areas- green dots indicate approximate location of where photos were taken.



Photo 1: Looking SW. along Replant Area -1

Photo Date: 1-13-2017



Photo 2: Looking S. in Replant Area 2, just N. of veg. plot 14

Photo Date: 1-13-2017



Photo 3: Looking SE. in Replant Area 4, near veg. plot 9

Photo Date: 1-13-2017



Photo 5: Looking S. in Replant Area 5, N. of veg. plot 5

Photo Date: 1-13-2017



Photo 4: Looking S. in Replant Area 6, from outside of the easement

Photo Date: 1-13-2017

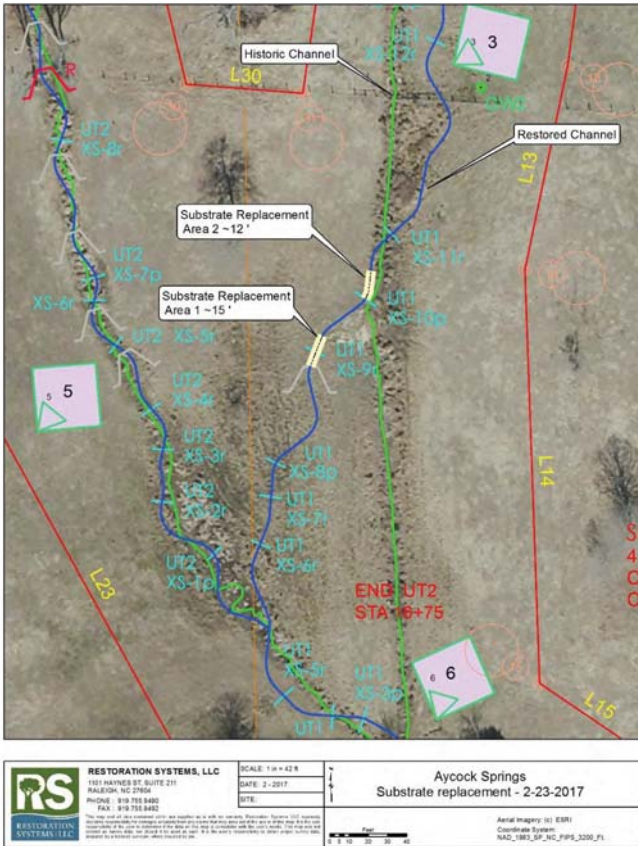


Photo 6 / 7: Live stake establishment on bank in Replant area 6



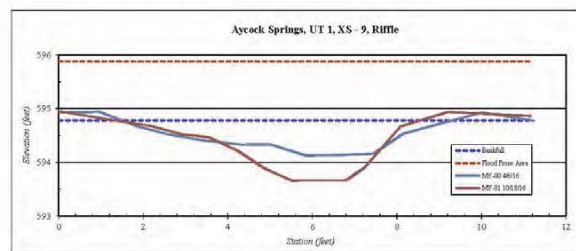


Photo Date: 1-13-2017

Aycock Springs– Remedial Action Plan Substrate Replacement - Update



Map of Area – UT 1, XC 9, 10, 11



Aycock Springs– Remedial Action Plan Substrate Replacement – Update

Photo Date: 2-23-2017



Photo 1: Substrate loss, 6" head-cut at UT 1, XC 9



Photo 2: Pool, upstream of 6" head-cut at UT 1, XC 9 (XC 10 in background)



Photo 3: Substrate replacement at UT 1, XC 9



Photo 3: Substrate loss, upstream riffle of XC 10 (pool)



Photo 4: Substrate replaced, upstream riffle of XC 10 (pool)



Photo 5: post replacement overview



Photo 6: UT-1 looking downstream from XC-11



Photo 7: XC-9 – Post 3-1-2017 0.92 inch rain event (Per USGS Guage at BUFFALO CREEK (SR2819 NR MCLEANSVILLE, NC) ~ 7 miles from Site



Photo 7: XC-10 – Post 3-1-2017 0.92 inch rain event (Per USGS Guage at BUFFALO CREEK (SR2819 NR MCLEANSVILLE, NC) ~ 7 miles from Site

APPENDIX H
HERBICIDE APPLICATION FORMS

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0529

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	05-10-2018		
Start Time	11:00	End Time	16:30
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	3 of 3
Sky Cover	Clear	Temp (F)	85
Wind Direction	SW	Wind Speed	6-10 mph
Applicators	Joshua G Merritt (NC 026-33717)		
Application Method	Basal Bark		
Herbicide	Garlon® 4 (triclopyr)		
Herbicide Rate (%)	15	Total Concentrate	29 fl oz
Surfactant or Adjuvant (1)			
Surfactant/Adjuvant 1 Rate (%)			
Other			
Other Rate/Amt			
Diluent	Diesel fuel		
Total Solution	1.5 gallon		
Species Controlled	Multiflora Rose		
Area Description	Patches of rose scattered through the entire branch, most were smaller but some were large in size.		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0528

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	05-10-2018		
Start Time	9:00	End Time	14:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	2 of 3
Sky Cover	Clear	Temp (F)	85
Wind Direction	SW	Wind Speed	6-10 mph
Applicators	Joshua G Merritt (NC 026-33717) Grainger Coughtrey (NC 026-34612)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Refuge® (glyphosate)		
Herbicide Rate (%)	4	Total Concentrate	30 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	6 gallons		
Species Controlled	Jap. Honeysuckle Privet spp. Multiflora Rose Cattail		
Area Description	There was a lot of cattail growing where the pond used to be. Rose found throughout the entire branch while privet and honeysuckle found at the far end of the site, mostly in the understory		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0527

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	05-10-2018		
Start Time	11:00	End Time	14:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	1 of 3
Sky Cover	Clear	Temp (F)	85
Wind Direction	SW	Wind Speed	6-10 mph
Applicators	Grainger Coughtrey (NC 026-34612)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Other (see comments)		
Herbicide Rate (%)		Total Concentrate	15 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	4 gallons		
Species Controlled	herbaceous growth		
Area Description	The tributaries were well defined but had some herbaceous species encroaching and blocking water flow.		
Additional Comments	Habitat herbicide used.		

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0526

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	05-09-2018		
Start Time	9:00	End Time	17:00
Only PAL for Site for This Day?	Yes	If NO, this is PAL # of ##	
Sky Cover	Clear	Temp (F)	81
Wind Direction	ENE	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717) Grainger Coughtrey (NC 026-34612)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Refuge® (glyphosate)		
Herbicide Rate (%)	4	Total Concentrate	45 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	9 gallons		
Species Controlled	Jap. Honeysuckle Privet spp. Multiflora Rose		
Area Description	Worked on the main branch, where there are invasives present mostly in the understory and near the stream. Mostly smaller plants needed to be treated, with the exception of some larger honeysuckle vines.		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0469

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	09-05-2017		
Start Time	9:00	End Time	16:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	2 of 2
Sky Cover	Clear	Temp (F)	81
Wind Direction	S	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717) Grainger Coughtrey (NC 026-34612) Sebastian Kimlinger (NC 026-34613)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Refuge® (glyphosate)		
Herbicide Rate (%)	5	Total Concentrate	78 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	12 gallons		
Species Controlled	Privet spp. Multiflora Rose		
Area Description	Large amount of privet in back corner of site, some small invasives near the stream		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0468

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	09-05-2017		
Start Time	9:00	End Time	16:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	1 of 2
Sky Cover	Clear	Temp (F)	81
Wind Direction	S	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Garlon® 3A (triclopyr)		
Herbicide Rate (%)	3	Total Concentrate	8 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)			
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	2 gallons		
Species Controlled	Privet spp. Multiflora Rose		
Area Description	Large amount of privet in back corner of site		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0465

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	09-05-2017		
Start Time	14:00	End Time	16:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	3 of 3
Sky Cover	Clear	Temp (F)	81
Wind Direction	S	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717) Grainger Coughtrey (NC 026-34612) Sebastian Kimlinger (NC 026-34613)		
Application Method	Cut and Stump Spray		
Herbicide	Garlon® 3A (triclopyr)		
Herbicide Rate (%)	50	Total Concentrate	50 fl oz
Surfactant or Adjuvant (1)			
Surfactant/Adjuvant 1 Rate (%)			
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	100 fl oz		
Species Controlled	Jap. Honeysuckle Privet spp. Tree-of-Heaven Multiflora Rose		
Area Description	Cut and Stump Sprayed a large patch of all invasive species listed above. The patch itself was only 20 ft by 50 ft consisting of small specimen. Loppers were used to clear the area.		
Additional Comments	The area cut is actually located outside of the easement boundaries according to PDF maps. I spoke with Ray Holz and he gave the green light to carry on with the treatment in this area. A map can be provided upon request.		

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0464

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	09-05-2017		
Start Time	9:00	End Time	14:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	2 of 2
Sky Cover	Clear	Temp (F)	81
Wind Direction	S	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717) Grainger Coughtrey (NC 026-34612) Sebastian Kimlinger (NC 026-34613)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Roundup® Custom (glyphosate)		
Herbicide Rate (%)	5	Total Concentrate	78 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other	Blue Dye		
Other Rate/Amt	1 fl oz		
Diluent	Water		
Total Solution	12 gallons		
Species Controlled	Privet spp. Multiflora Rose		
Area Description	The majority of the site is clear of invasive species. The privet and rose present were small re-sproutes from recent treatments.		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0463

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	09-05-2017		
Start Time	9:00	End Time	16:00
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	1 of 3
Sky Cover	Clear	Temp (F)	81
Wind Direction	S	Wind Speed	1-5 mph
Applicators	Joshua G Merritt (NC 026-33717)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Garlon® 3A (triclopyr)		
Herbicide Rate (%)	3	Total Concentrate	8 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other	Blue Dye		
Other Rate/Amt	1 fl oz z		
Diluent	Water		
Total Solution	2 gal		
Species Controlled	Callery Pear Privet spp. Multiflora Rose		
Area Description	The majority of the site is clear of invasive species. The privet and rose present were small re-sproutes from recent treatments.		
Additional Comments			

Carolina Silvics, Inc. Pesticide Application Log

CarSilv - 0398

Client	Restoration Systems		
Project Site	Aycock Springs		
Date	04-06-2017		
Start Time	12:30	End Time	14:30
Only PAL for Site for This Day?	No	If NO, this is PAL # of ##	2 of 2
Sky Cover	Cloudy	Temp (F)	61
Wind Direction	W	Wind Speed	11-15mph
Applicators	Sebastian Kimlinger (NC 026-34613)		
Application Method	Foliar Spray (Backpack)		
Herbicide	Roundup® Custom (glyphosate)		
Herbicide Rate (%)	5	Total Concentrate	20 fl oz
Surfactant or Adjuvant (1)	Hel-fire®		
Surfactant/Adjuvant 1 Rate (%)	.5		
Other			
Other Rate/Amt			
Diluent	Water		
Total Solution	3 gallons		
Species Controlled	Privet spp. Multiflora Rose		
Area Description			
Additional Comments			

APPENDIX I
PHOTO LOG

Photo 1: UT-1 Outfall (Terracell)



Photo 2: UT-4 Outfall (Terracell)



Photo 3: 02-23-2017 Repair near UT-1 XC 9



Photo 4: 02-23-2017 Repair near UT-1 XC 10



Photo 5: Travis Creek XS-3P (Rack litter along willows)



Photo 6: Travis Creek – Enhancement 2 Reach near Gibsonville Ossipee Rd.



Photo 7: Travis Creek – Enhancement 2 Reach below UT-4 outfall (approx. 50 ft.)

