

Holly Grove Stream Restoration Site


Guilford County, North Carolina

Cataloging Unit: 03030002

EEP Contract #: D06028-B

November 6, 2012

MONITORING REPORT 2012 (YEAR 4)

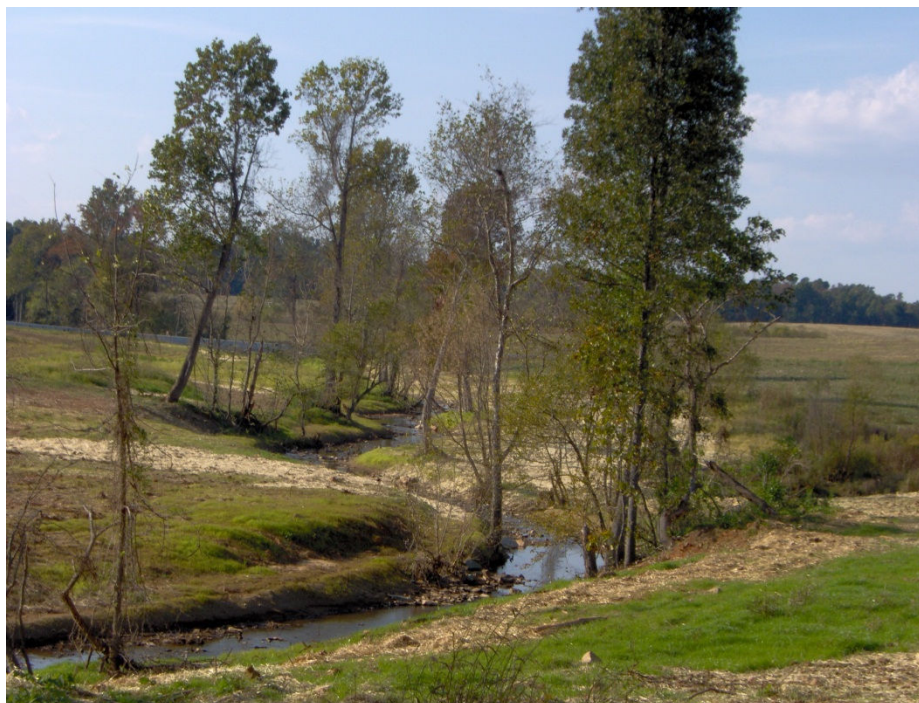

Submitted to:

North Carolina Department of Environment and Natural Resources

North Carolina Ecosystem Enhancement Program

1652 Mail Service Center

Raleigh, NC 27699-1652



Submitted by:

Restoration Systems, LLC

1101 Haynes Street, Suite 211

Raleigh, North Carolina 27604

Point of Contact: Tara Disy Allden

Phone: 919-755-9490

Holly Grove Stream Restoration Site

MONITORING REPORT 2012 (YEAR 4)

Prepared for:



Restoration Systems, LLC
1101 Haynes Street, Suite 211
Raleigh, North Carolina 27604

Prepared by:



Wolf Creek Engineering, pllc
7 Florida Avenue
Weaverville, NC 28787

TABLE OF CONTENTS

EXECUTIVE SUMMARY iii

1.0 Project Goals, Background, and Attributes..... 1

 1.1 General Project Description..... 1

 1.1.1 USGS and NCDWQ River Basin Designations..... 1

 1.1.2 NCDWQ Surface Water Classification 1

 1.2 Project Goals and Objectives 2

 1.3 Project Structure..... 2

 1.4 Restoration Type and Approach 2

 1.5 Project History, Contacts and Attribute Data 3

2.0 Project condition and monitoring results 21

 2.1 Vegetation Assessment 21

 2.1.1 Vegetative Problem..... 22

 2.1.2 Vegetation Plot Photos..... 22

 2.2 Stream Assessment 22

 2.2.1 Hydrology 23

 2.2.2 Geomorphology 23

 2.2.3 Problem Areas..... 23

 2.2.4 Photo Reference Stations 24

 2.2.5 Stability Assessment Table..... 25

LIST OF TABLES

Table I. Project Components Page 7

Table II. Project Activity and Reporting History Page 8

Table III. Project Contacts Page 8

Table IV. Project Attributes Page 9

Table V. Vegetation Summary..... Page 21

Table VI. Verification of Bankfull Events Page 23

Table VII. BEHI and Sediment Export Estimates..... Page 24

Table VIII. Categorical Stream Feature Visual Stability Assessment..... Page 25 - 26

Table IX. Baseline Morphology and Hydraulic Summary..... Page 27 - 32

Table X. Morphology and Hydraulic Monitoring Summary..... Page 33 - 40

LIST OF FIGURES

Figure 1. Vicinity Map..... Page 5

Figure 2. Vicinity Map..... Page 6

Figure 3. Monitoring Plans..... Page 11 - 20

APPENDIX A: Vegetative Raw Data
 APPENDIX B: Geomorphic Raw Data

EXECUTIVE SUMMARY

The Holly Grove Site is located in Guilford County, North Carolina within the Cape Fear River Basin, Cataloging Unit 03030002. The project consisted of restoring, enhancing, and preserving approximately 21,000 linear feet of stream, restoring approximately 42 acres of riparian buffers, and preserving approximately 1.11 acres of wetlands. The Site is in a rural setting in the Southern Outer Piedmont hydrophysiographic ecoregion and was previously used to grow row crops with woody vegetation confined to isolated areas. Prior to restoration, the channels were highly degraded due to unrestricted livestock access, channelization activities, and lack of riparian vegetation. The restoration design was based on a Priority Level 1 and 2 approach to restore proper channel dimension and allow for appropriate sediment transport. Restoration practices on this project were implemented with the intent of minimizing unnecessary disturbance to adjacent land and to protect mature riparian vegetation where it existed. The constructed stream profile has restored stable bed morphology including appropriate riffle-pool sequencing. Cross-vanes, J-Hook vanes, and in-stream log structures have been integrated into the channel to provide grade control, maintain stable streambanks while the riparian vegetation establishes, and provide in-stream habitat. Biodegradable fiber matting was used to provide temporary stabilization on the newly graded streambanks. Excavated materials from the existing channel were used to backfill around in-stream structures and to build riffles with a natural substrate and function.

Hydrology

Following completion of the construction in October of 2008, the Site has been subjected to one greater-than-bankfull event and at least four bankfull or near-bankfull events. It should be noted that, prior to completion of construction, Tropical Storm Fay (August 2008) produced a high-flow event in which floodwaters crested 2.5 feet above bankfull. Approximately seventy percent (70%) of the project was complete at that time and subjected to this high water event. In late September, 2010, Tropical Storm Nicole resulted in 3 and 4.5 inches of rain on the site and over-bankfull flows. Since this time there has been at least one bankfull event in the past two years.

Stream

The restored stream reaches have successfully managed the bankfull and above bankfull flow events of the first four years. The overall grade of the channel has been maintained and the banks of the channels are stable throughout the Site. There is one location with minor bank scour and one structure along East Branch is piping. Three beaver dams were identified and removed on upper Buckhorn Creek that were impounding water to the top of bank.

Vegetation

Native woody and herbaceous species were used to establish, at minimum, a fifty-foot riparian buffer on each side of the restored reach. Herbaceous species have established throughout the site and there is significant evidence of additional volunteer species becoming established within the buffer. The riparian buffer bare-root planting had an average survival rate of 309 stems per acre through the fourth year. There is an average density of 2,347 stems per acre including planted stems and natural volunteers.

Planned Action

Continued visual monitoring is planned for the few stream areas that have been identified as “Areas of Concern”. Repairs will be performed on the structure on East Branch that is piping to prevent the possibility of a headcut formation. Additional live staking will be installed on the bank of Buckhorn at STA 153+00 that is exhibiting evidence of erosion. Also, continued monitoring and maintenance of the beaver population will be conducted for the entire site.

1.0 PROJECT GOALS, BACKGROUND, AND ATTRIBUTES

The purpose of the Holly Grove Stream Restoration Site (Site) was to restore degraded sections of Buckhorn Creek and several of its tributaries located in Guilford County, North Carolina. This monitoring report presents information regarding the site and watershed conditions, the restoration approach for the project, the monitoring results, remedial action plan and detailed monitoring drawings of the site.

1.1 General Project Description

Buckhorn Creek is located approximately 15 miles northeast of the City of Greensboro in rural Guilford County, North Carolina (Figure 1: Vicinity Map). The site consists of approximately 42 acres of floodplain, approximately 21,000 linear feet of stream designated as Buckhorn Creek and its tributaries, and 1.11 acres of existing wetlands (Figure 2: Project Map). The stream reaches consist of perennial, first and second order streams that have historically been impacted by riparian and bank vegetation removal, channel straightening, unrestricted livestock access, and agricultural land-use practices. Existing land use within the site consists of forested areas and row crops. The site is located within moderately sloping colluvial valleys and elevations range from approximately 615 to 720 feet above sea level. Past land management activities have consisted of timber harvesting with subsequent land clearing for agricultural uses including cattle and row crop farming. The land outside of the conservation easement remains in active agricultural production.

1.1.1 USGS and NCDWQ River Basin Designations

The project reach is located in the Haw River watershed of the Cape Fear River Basin (United States Geological Survey (USGS) 14-digit Hydrologic Unit 03030002020070) within North Carolina Division of Water Quality (NCDWQ) sub-basin 03-06-02. This sub-basin is primarily rural agriculture, although residential land use accounts for a significant portion. Buckhorn Creek drains into Reedy Fork Creek approximately $\frac{3}{4}$ miles downstream of the Site, which in turn flows to the Haw River eight miles downstream.

1.1.2 NCDWQ Surface Water Classification

Reedy Fork Creek in the vicinity of the Site is assigned a best usage classification of C, NSW by the NCDWQ and as such there are no restrictions on watershed development or types of discharge. These waters are suitable for aquatic life propagation and survival, fishing, wildlife, secondary recreation, and agriculture. Secondary recreation includes wading, boating, and other uses not involving human body contact with water on an organized or frequent basis. The supplemental classification, NSW (Nutrient Sensitive Waters) includes areas with water quality problems associated with excessive plant growth resulting from nutrient enrichment.

The portion of Reedy Fork Creek to which Buckhorn Creek drains and the portion of the Haw River that is approximately two miles east of the Site are listed on the DWQ final

2004 and draft 2006 303(d) lists. Streams which are included in the 303(d) list do not meet water quality standards or have impaired uses.

1.2 Project Goals and Objectives

The primary goals of the Holly Grove Stream Restoration Project are to:

- Restore aquatic and riparian habitat within the on-site portions of the Buckhorn Creek watershed.
- Restore geomorphic stability to the subject stream reaches.

These goals will be accomplished through the following objectives:

- Restoration of approximately forty-two acres of Mesic Mixed Hardwood Forest along both sides of Buckhorn Creek and its tributaries.
- Removing nonpoint sources of pollution associated with agricultural activities including the establishment of a native woody riparian buffer (at least 50' wide) adjacent to streams and wetlands to treat surface runoff which may be laden with sediment and/or agricultural pollutants from the adjacent landscape.
- Reestablishing stream stability and the capacity to transport watershed flows and sediment loads by restoring a stable dimension, pattern, and profile supported by natural in-stream habitat and grade/bank stabilization structures.
- Promoting floodwater attenuation through a) conveying bankfull stream flows through construction of bankfull bench, b) restoring secondary, entrenched tributaries thereby reducing floodwater velocities, and c) re-vegetating floodplains to increase frictional resistance on floodwaters crossing the Site.
- Improving aquatic habitat by enhancing stream bed variability and the use of in-stream structures.
- Providing wildlife habitat including fringe and forest edge.

These accomplishments will result in:

- Restoration and enhancement of **15,822** Stream Mitigation Units.
- Protecting the Site with a perpetual conservation easement.

1.3 Project Structure

The project is composed of seven distinct reaches; the main channel, Buckhorn Creek, and each of its tributaries, Middle Branch, West Branch, East Branch, Lower East Branch, Southeast Creek, and Southwest Creek. The project structure is tabulated in the corresponding Table 1 (See Below).

1.4 Restoration Type and Approach

Restoration and enhancement practices implemented on this project were designed to minimize unnecessary disturbance to adjacent land and to protect mature riparian vegetation where it exists. Consideration was given to the potential functional lift provided by restoration activities in comparison to the functional lift that could be realized through the natural process of channel evolution. Included in this consideration was an attempt to determine the disturbance and sedimentation that could occur as a result of this natural process. Where restoration was determined to be warranted,

consideration was given to which reaches could best be served by maintaining as much of the existing channel pattern as possible.

The proposed channels of Buckhorn Creek and its tributaries were designed as Type B4c streams with the exception of the lower reach of Middle Branch. This channel configuration provides the most stable and natural form in the moderately sloping colluvial valleys that are found throughout the Site. Not only does it effectively convey bankfull discharge and sediment load but also conforms to the natural conveyance of flood flows. Additionally, since broad alluvial valleys are generally not found within the Site, the lower sinuosity of the Type B4c streams allowed for minimization grading and earthwork activities. The constructed channel dimensions, patterns, and profiles were based on hydraulic relationships and morphologic dimensionless ratios of the reference reaches.

Restoration activities included restoring stable channel morphology supported by natural in-stream habitat and grade/bank stabilization structures, the elimination of accelerated bank erosion, and reestablishment of native riparian buffers at least 50 feet in width. Exotic riparian vegetation was removed in areas of the project to allow for replanting of native riparian species. In-stream structures were installed to provide for enhanced aquatic habitat, protection of the newly constructed stream banks, and grade control for the newly constructed channel.

1.5 Project History, Contacts and Attribute Data

The summary of the project history, contacts, and attribute data is tabulated in Tables II, III, and IV (See Below).

DIRECTIONS TO SITE FROM RALEIGH:
 FOLLOW I-40 WEST TO GREENSBORO
 FOLLOW NC-61N TO GIBSONVILLE VIA EXIT 138
 AFTER 1.8 MI TURN RIGHT ON NC-61/100
 AFTER 1.7 MI TURN LEFT ON NC-61 (GIBSONVILLE)
 AFTER 2 MI TAKE RIGHT FORK ON NC-61 @
 CEMETARY
 AFTER 4.3 MI TURN RIGHT ON TICKLE RD.
 AFTER 1 MI BRIDGE CROSSES BUCKHORN CREEK

GREENSBORO

BURLINGTON →


← **HIGH POINT**

HOLLY GROVE RESTORATION SITE



THE SUBJECT PROJECT SITE IS AN ENVIRONMENTAL RESTORATION SITE OF THE NCDENR ECOSYSTEM ENHANCEMENT PROGRAM (EEP) AND IS ENCOMPASSED BY A RECORDED CONSERVATION EASEMENT, BUT IS BORDERED BY LAND UNDER PRIVATE OWNERSHIP. ACCESSING THE SITE MAY REQUIRE TRAVERSING AREAS NEAR OR ALONG THE EASEMENT BOUNDARY AND THEREFORE ACCESS BY THE GENERAL PUBLIC IS NOT PERMITTED. ACCESS BY AUTHORIZED PERSONEL OF STATE AND FEDERAL AGENCIES OR THEIR DESIGNERS/CONTRACTORS INVOLVED IN THE DEVELOPMENT, OVERSIGHT AND STEWARDSHIP OF THE RESTORATION SITE IS PERMITTED WITHIN THE TERMS AND TIMEFRAMES OF THEIR DEFINED ROLES. ANY INTENDED SITE VISITATION OR ACTIVITY BY ANY PERSON OUTSIDE OF THESE PREVIOUSLY SANCTIONED ROLES AND ACTIVITIES REQUIRES PRIOR COORDINATION WITH EEP.


PREPARED FOR: PREPARED BY: AND BY:



SITE VICINITY MAP

HOLLY GROVE RESTORATION SITE
 GUILFORD COUNTY, NORTH CAROLINA
 EEP Contract #: D06028-B

FIGURE 1

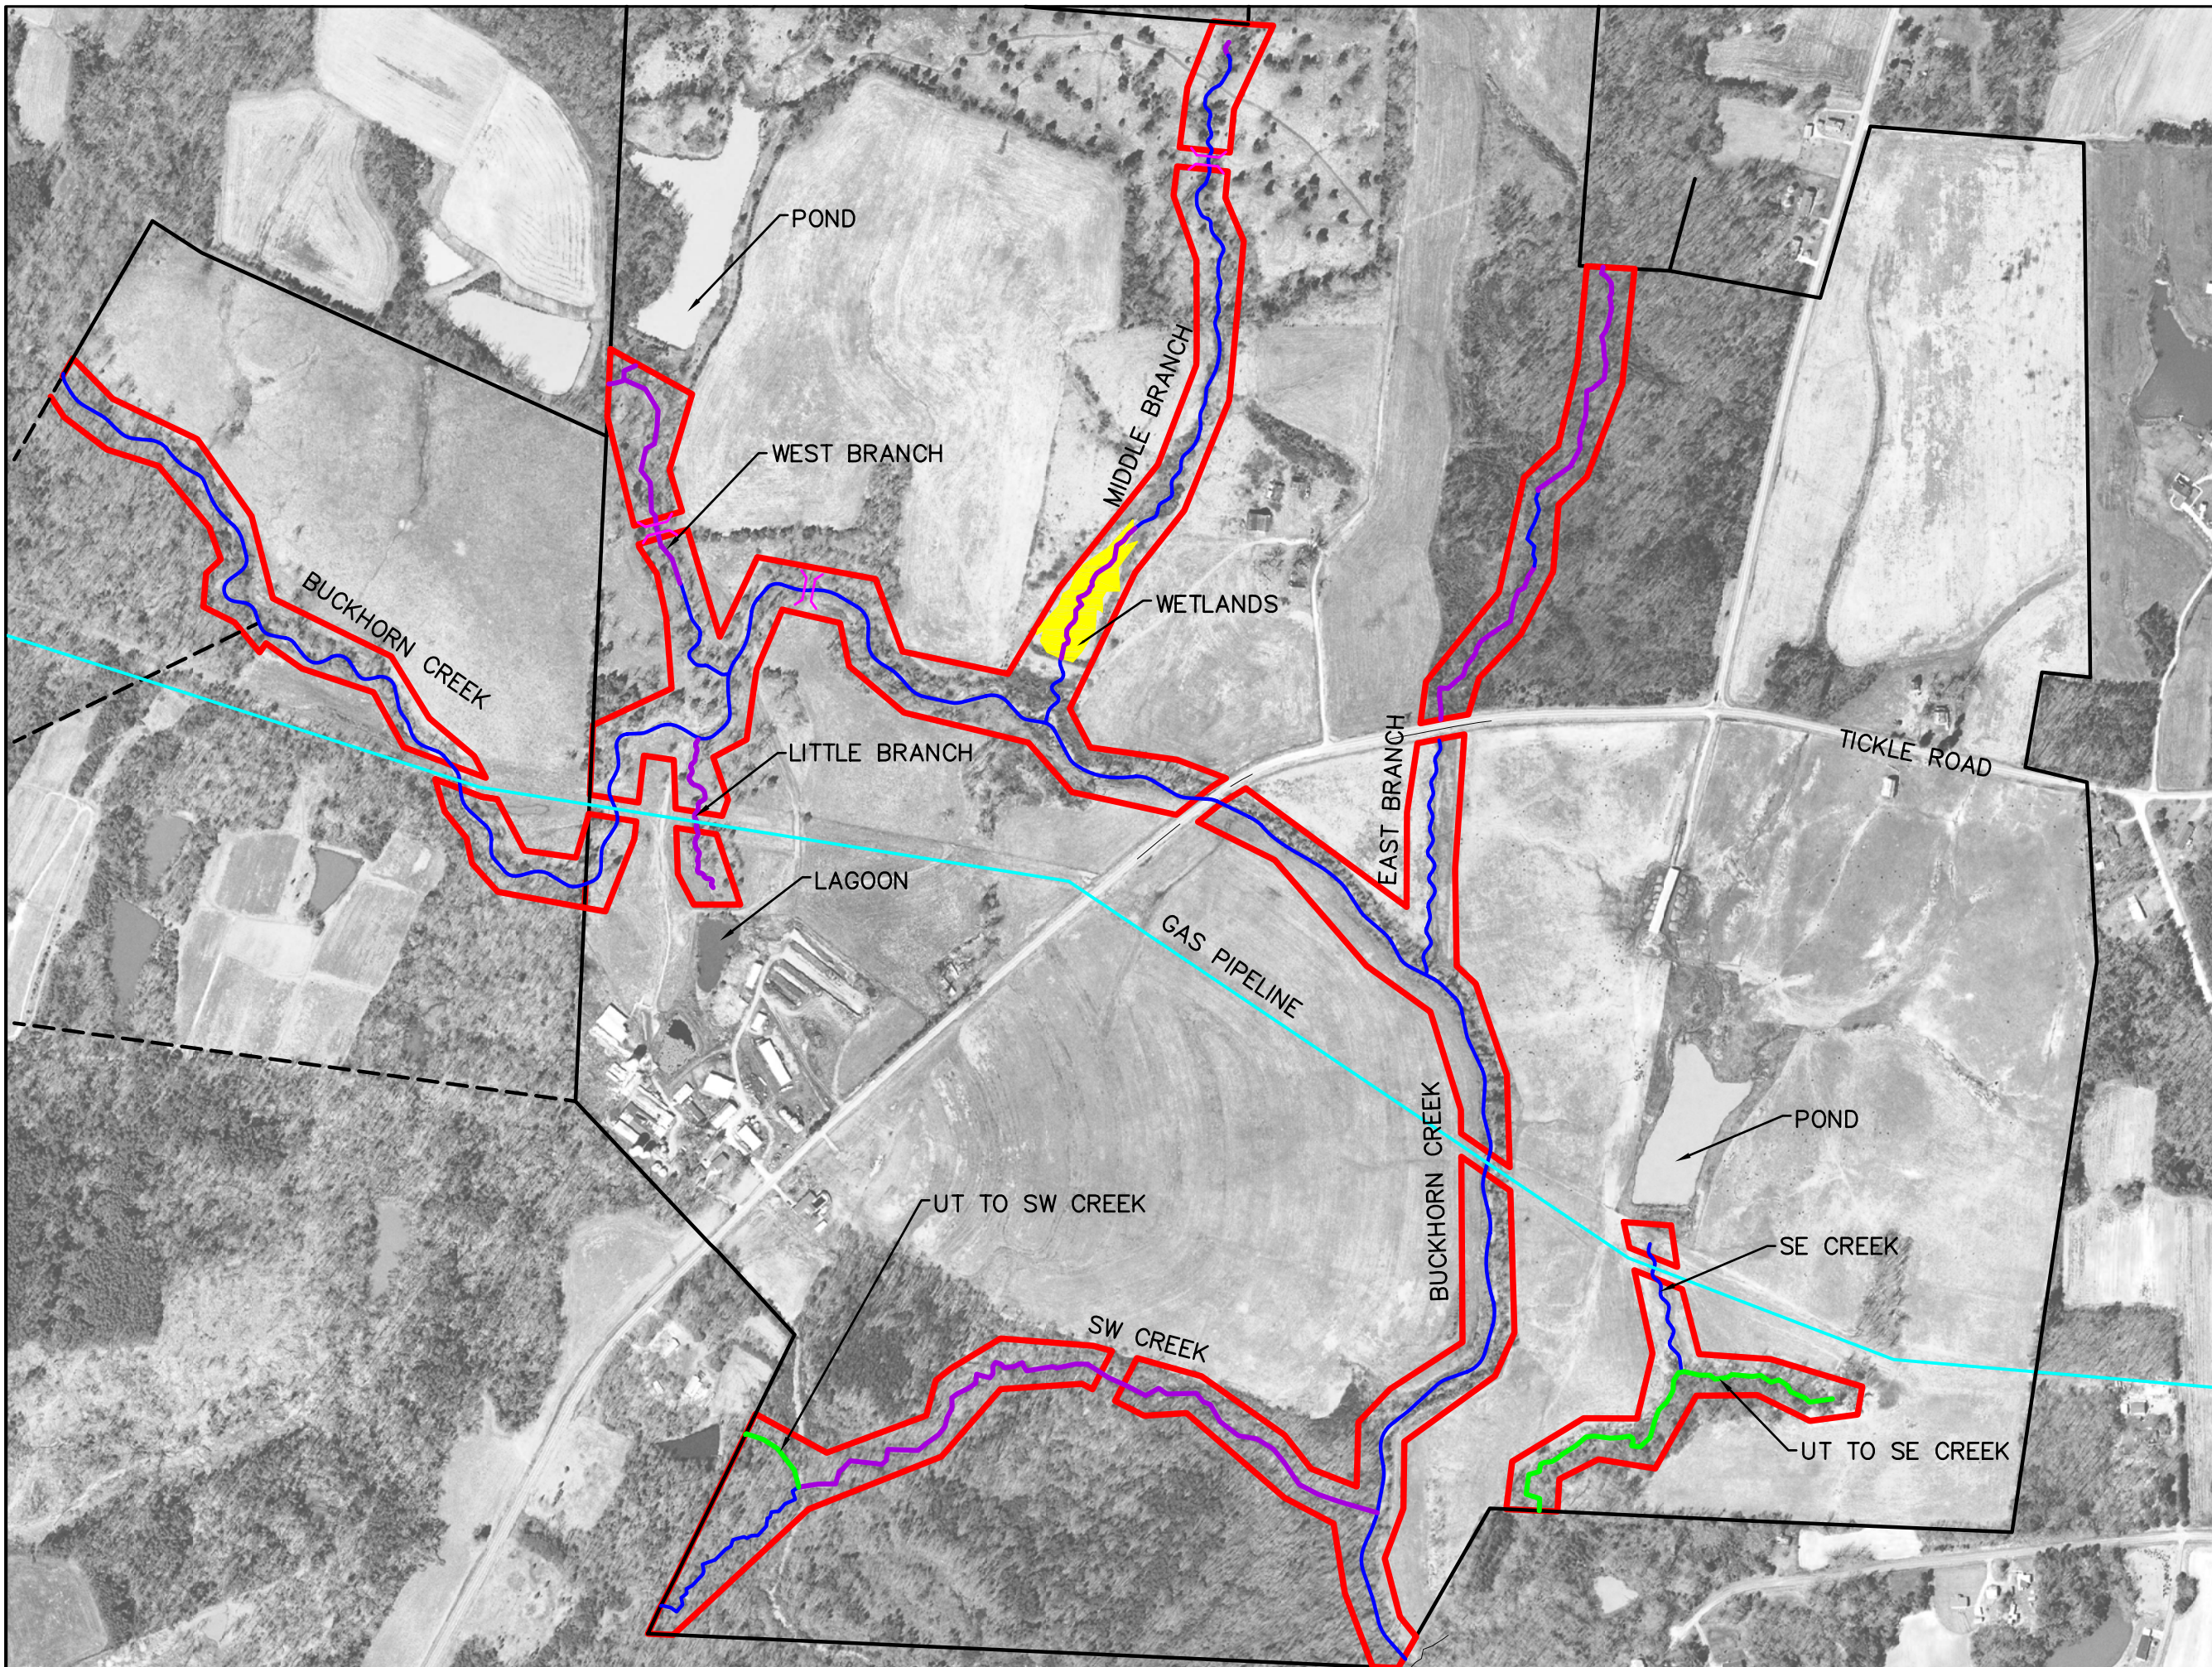

PREPARED FOR:











PREPARED BY:




AND BY:



LEGEND

-  STREAM RESTORATION
-  STREAM PRESERVATION
-  STREAM ENHANCEMENT
-  WETLANDS
-  FORD
-  CONSERVATION EASEMENT
-  PROPERTY BOUNDARY
-  GAS PIPELINE



SITE MAP

HOLLY GROVE RESTORATION SITE
 GUILFORD COUNTY, NORTH CAROLINA
 EEP Contract #: D06028-B

FIGURE 2

Table I Project Components						
Holly Grove Stream Restoration Site / EEP Contact #D06028-B						
Restoration Reach/Area	Restoration Level	Approach	Pre-Restoration LF or AC	Post-Restoration LF or AC	Station Range/Location	Comments
Buckhorn Creek	R	P2	8,757	8,848	100+00 - 194+50	
West Branch	E2	E2	870	870	300+00 - 308+00	
West Branch	R	P2	390	391	300+00 - 303+91	
Middle Branch	E2	E2	240	240	398+91 - 401+31	
Middle Branch	R	P1	1,549	1,561	401+31 - 417+37	
Middle Branch	E2	E2	472	472	417+37 - 422+09	
Middle Branch	R	P1	90	194	423+00 - 425+40	
East Branch	P	-	960	960	480+00 - 498+80	
East Branch	E2	E2	920	920	480+00 - 498+80	
East Branch	R	P1	300	329	490+00 - 493+29	
East Branch	R	P1	739	761	500+00 - 507+61	
Little Branch	E2	E2	553	553	19+945 - 205+54	
SW Creek	R	P1	723	723	600+00 - 607+34	
SW Creek	E2	E2	2,229	2,229	608+26 - 630+55	
UT to SW Creek	P	-	325	325	650+00 - 653+50	
SE Creek	R	P1	342	363	700+00 - 704+36	
SE Creek	P	-	881	881	706+25 - 715+06	
UT to SE Creek	P	-	528	528	750+00 - 755+28	
Wetland A	E	-	1.11	1.11	Middle Branch	

Component Summation							
Restoration Level	Stream (LF)	Riparian Wetland (Ac)		Non-Riparian (Ac)	Upland (Ac)	Buffer (Ac)	BMP
		Riverine	Non-Riverine				
Restoration	13,170						
Enhancement		1.11					
Enhancement I							
Enhancement II	5,284						
Creation							
Preservation	2,694						
HQ Preservation							
		1.11					
Totals	21,148	1.11				42	BMP Count

= Non-Applicable

Table II Project Activity and Reporting History Holly Grove Restoration Project		
Activity or Report	Data Collection Complete	Completion or Delivery
Restoration Plan	Apr 2007	Jun 2007
Final Design - Construction Plans	N/A	Oct 2007
Construction	N/A	Oct 2008
Temporary S&E mix applied to entire project area	N/A	Sep 2008
Permanent seed mix applied to entire site	N/A	Sep 2008
Bare-root plantings for floodplain and uplands	N/A	Dec 2008
Mitigation Plan / As-Built (Year 0 Monitoring - baseline)	Oct 2008	Dec 2008
Year 1 Monitoring	Oct 2009	Dec 2009
Year 2 Monitoring	Oct 2010	Nov 2010
Year 3 Monitoring	Oct 2011	Oct 2011
Year 4 Monitoring	Oct 2012	Nov 2012
Year 5 Monitoring		

Table III Project Contact Table Holly Grove Restoration Project		
Designer Wolf Creek Engineering, pllc S. Grant Ginn	7 Florida Avenue Weaverville NC, 28787 828-658-3649	
Construction Contractor North State Environmental, Inc Darrell Westmoreland	2889 Lowery St. Winston-Salem, NC 27101 336-725-2010	
Planting & Seeding Contractor North State Environmental, Inc Stephen Joyce	2889 Lowery St. Winston-Salem, NC 27101 336-725-2010	
Monitoring Performers Stream Monitoring - Wolf Creek Engineering, pllc Vegetation Monitoring - Catena Group	S. Grant Ginn Mike Wood	828-658-3649 919-732-1300

Table IV Project Attribute Table Holly Grove Restoration Project						
Project County	Guilford					
Physiographic Region	Piedmont					
Ecoregion	Southern Outer Piedmont					
Project River Basin	Cape Fear River Basin					
USGS HUC for Project (14 digit)	03030002020070					
NCDWQ Sub-basin for Project	03-06-02					
Within extent of EEP Watershed Plan?						
WRC Class (Warm, Cool, Cold)						
% of project easement fenced or demarcated	100% Demarcated Easement Corners					
Beaver activity observed during design phase?	Yes, on Buckhorn Creek upstream of bridge					
Restoration Component Attribute Table						
	Buckhorn	West	Middle	East	Southeast	Southwest
Drainage area (mi ²)	4.27	0.2	0.2	0.2	0.14	0.19
Stream order	Second	First	First	First	First	First
Restored length (feet)	8757	390	1639	1039	342	723
Perennial or Intermittent	Perennial	Perennial	Perennial	Perennial	Perennial	Perennial
Watershed type	Rural	Rural	Rural	Rural	Rural	Rural
Watershed LULC Distribution (e.g.)						
Residential	20%	10%	5%	10%	5%	10%
Ag-Row Crop	40%	60%	50%	10%	90%	10%
Ag-Livestock	10%	5%	10%	0%	0%	0%
Forested	30%	25%	35%	80%	5%	80%
Watershed impervious cover (%)	10	5	5	5	2	2
NCDWQ AU/Index number	16-(1)a					
NCDWQ classification	C, NSW	C, NSW	C, NSW	C, NSW	C, NSW	C, NSW
303d listed?	No					
Upstream of a 303d listed segment?	Yes					
Reasons for 303d listing or stressor	non-point urban and agricultural runoff					
Total acreage of easement	64.87					
Total vegetated acreage within easement	47.06					
Total planted acreage as part of the restoration	45.3					
Rosgen classification of pre-existing	F, G	G	G	G	G	G
Rosgen classification of As-Built	B4c	B4c	B4c	B4c	B4c	B4c
Valley type	II	II	II	II	II	II
Valley slope	0.0051	0.0239	0.0165	0.0119	0.0159	0.0169
Valley side slope range	4% - 40%					
Valley toe slope range	0.4% - 2%					
Cowardin classification	N/A					
Trout waters designation	N/A					
Species of concern, endangered?	Yes, Bald Eagle & Carolina Darter					
Dominant soil series and characteristics	Ch, Co	CcD	Ch	CcD, Ch	CcD	CcD
Series	Congaree	Cecil	Chewacla	Chewacla	Cecil	Cecil
Depth (in)	0-80	0-80	0-70	0-70	0-80	0-80
Clay %	5-35	5-70	5-35	5-35	5-70	5-70
K	Moderate	Moderate	Moderate	Moderate	Moderate	Moderate
T	-	-	-	-	-	-


Wolf Creek Engineering
 ENGINEERING & ENVIRONMENTAL CONSULTING
 51 North Knob Lane Weaverville, NC 28787
 PHONE: (828) 658-3649 WWW.WOLFCREEKENG.COM

PROJECT HOLLY GROVE STREAM RESTORATION SITE
 OWNER RESTORATION SYSTEMS, LLC

TITLE
MONITORING PLANS

SCALE AS NOTED DRAWN BY c/mc PROJECT NO. 1024 SHEET NUMBER MP-1
 DATE 9/17/2012 CHECKED BY SGG

DATE	BY	REV.	DESCRIPTION

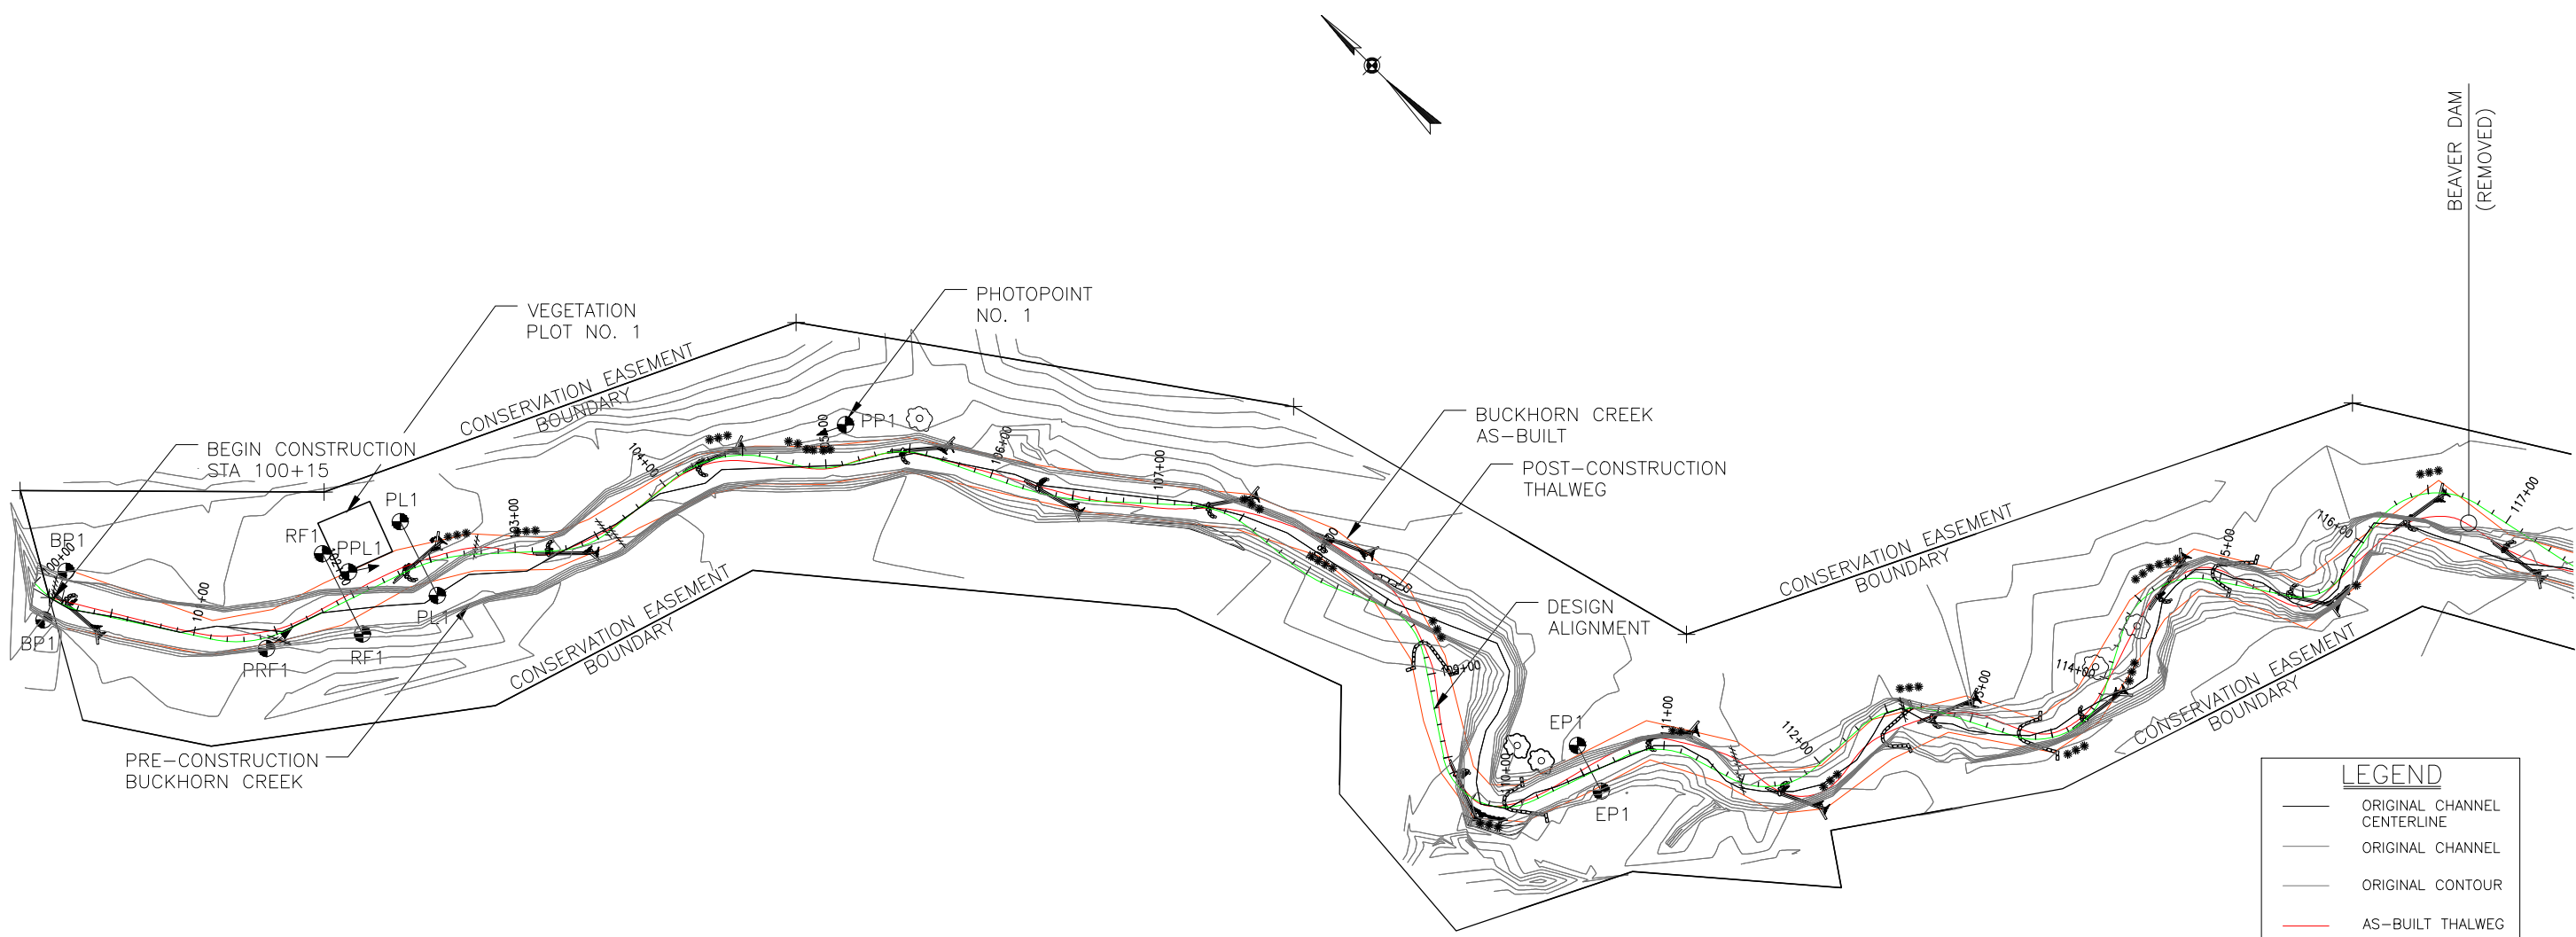


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
BP1 RT	BEGIN PROFILE	892186.64	1827088.87	99.94
BP1 LT	BEGIN PROFILE	892197.58	1827118.27	-
PRF1	PHOTO PT. RIFFLE	892081.9	1827168.92	-
RF1 RT	RIFFLE X.S.	892047.92	1827214.63	98.00
RF1 LT	RIFFLE X.S.	892097.66	1827231.6	98.66
PPL1	PHOTO PT. POOL	892079.26	1827234.84	97.28
PL1 RT	POOL X.S.	892032.47	1827261.68	97.34
PL1 LT	POOL X.S.	892078.62	1827277.13	98.46
EP1 RT	END PROFILE	891450.75	1827684.19	94.53
EP1 LT	END PROFILE	891490.02	1827699.27	95.11
PP1	PHOTO POINT NO. 1	891932.76	1827501.67	-


LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NO AREAS OF CONCERN ON THIS SHEET



NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER

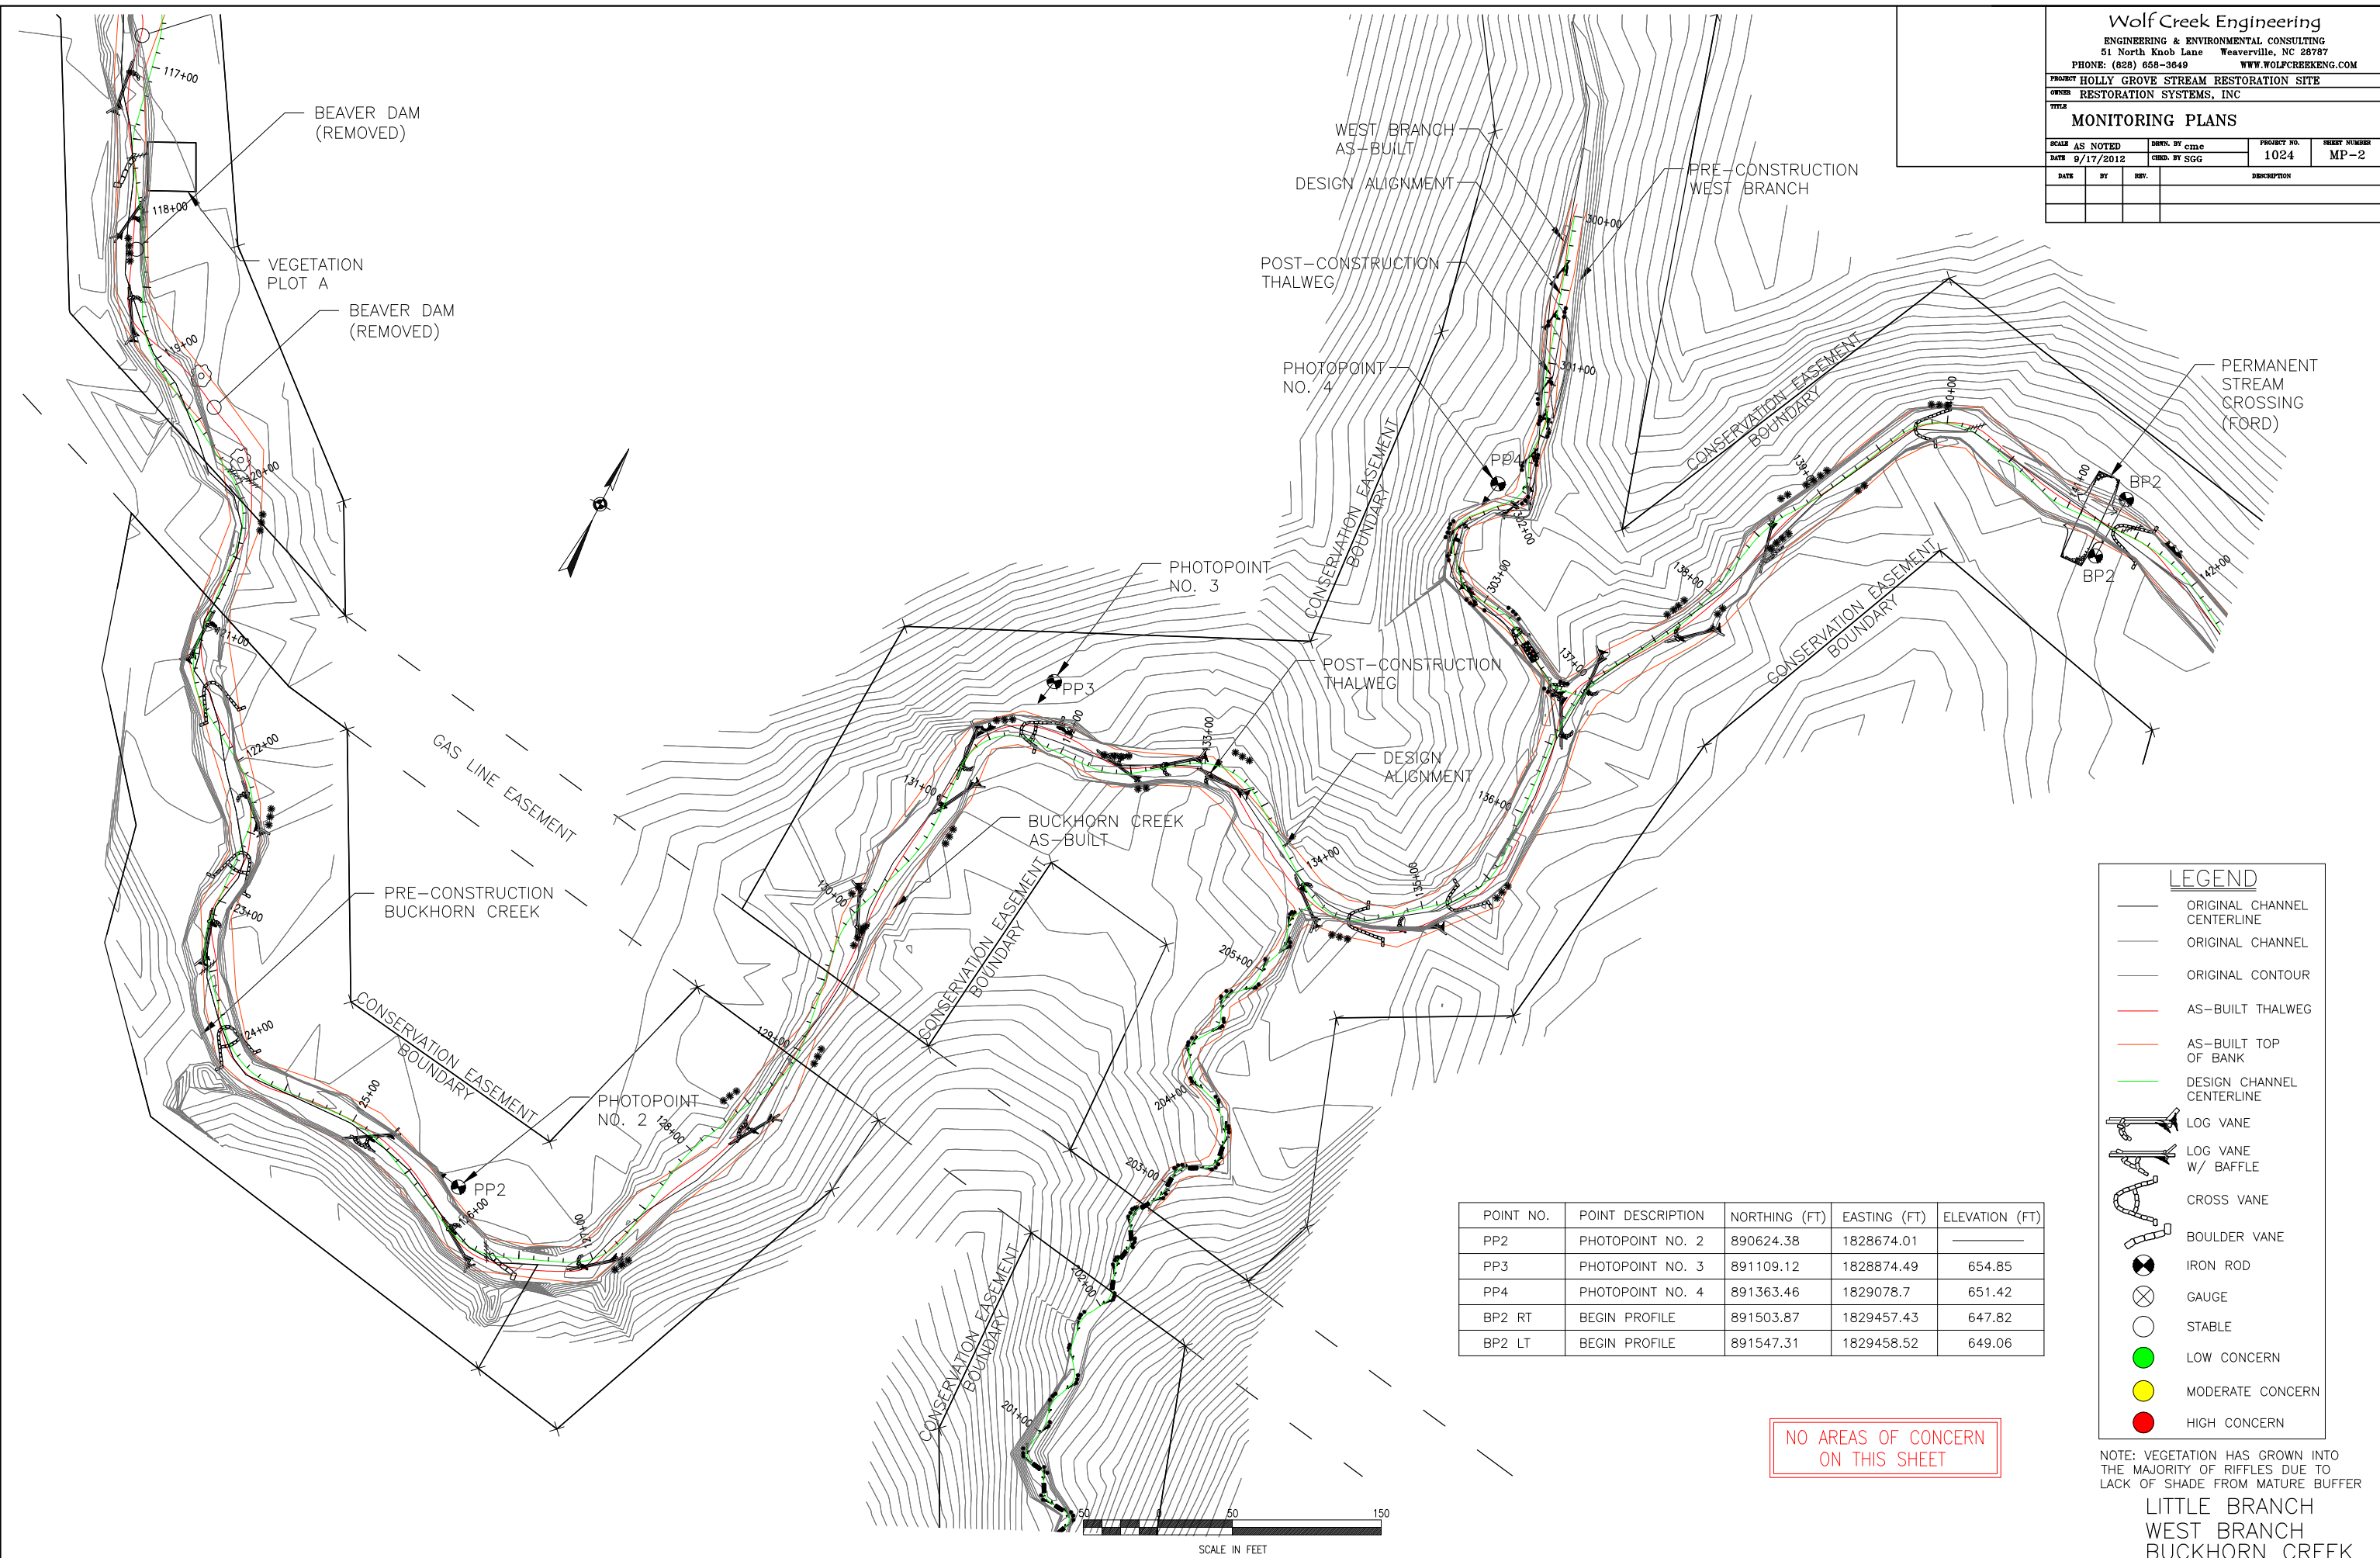


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
PP2	PHOTOPOINT NO. 2	890624.38	1828674.01	
PP3	PHOTOPOINT NO. 3	891109.12	1828874.49	654.85
PP4	PHOTOPOINT NO. 4	891363.46	1829078.7	651.42
BP2 RT	BEGIN PROFILE	891503.87	1829457.43	647.82
BP2 LT	BEGIN PROFILE	891547.31	1829458.52	649.06


LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- ⊗ GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NO AREAS OF CONCERN ON THIS SHEET

NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER
 LITTLE BRANCH
 WEST BRANCH
 BUCKHORN CREEK



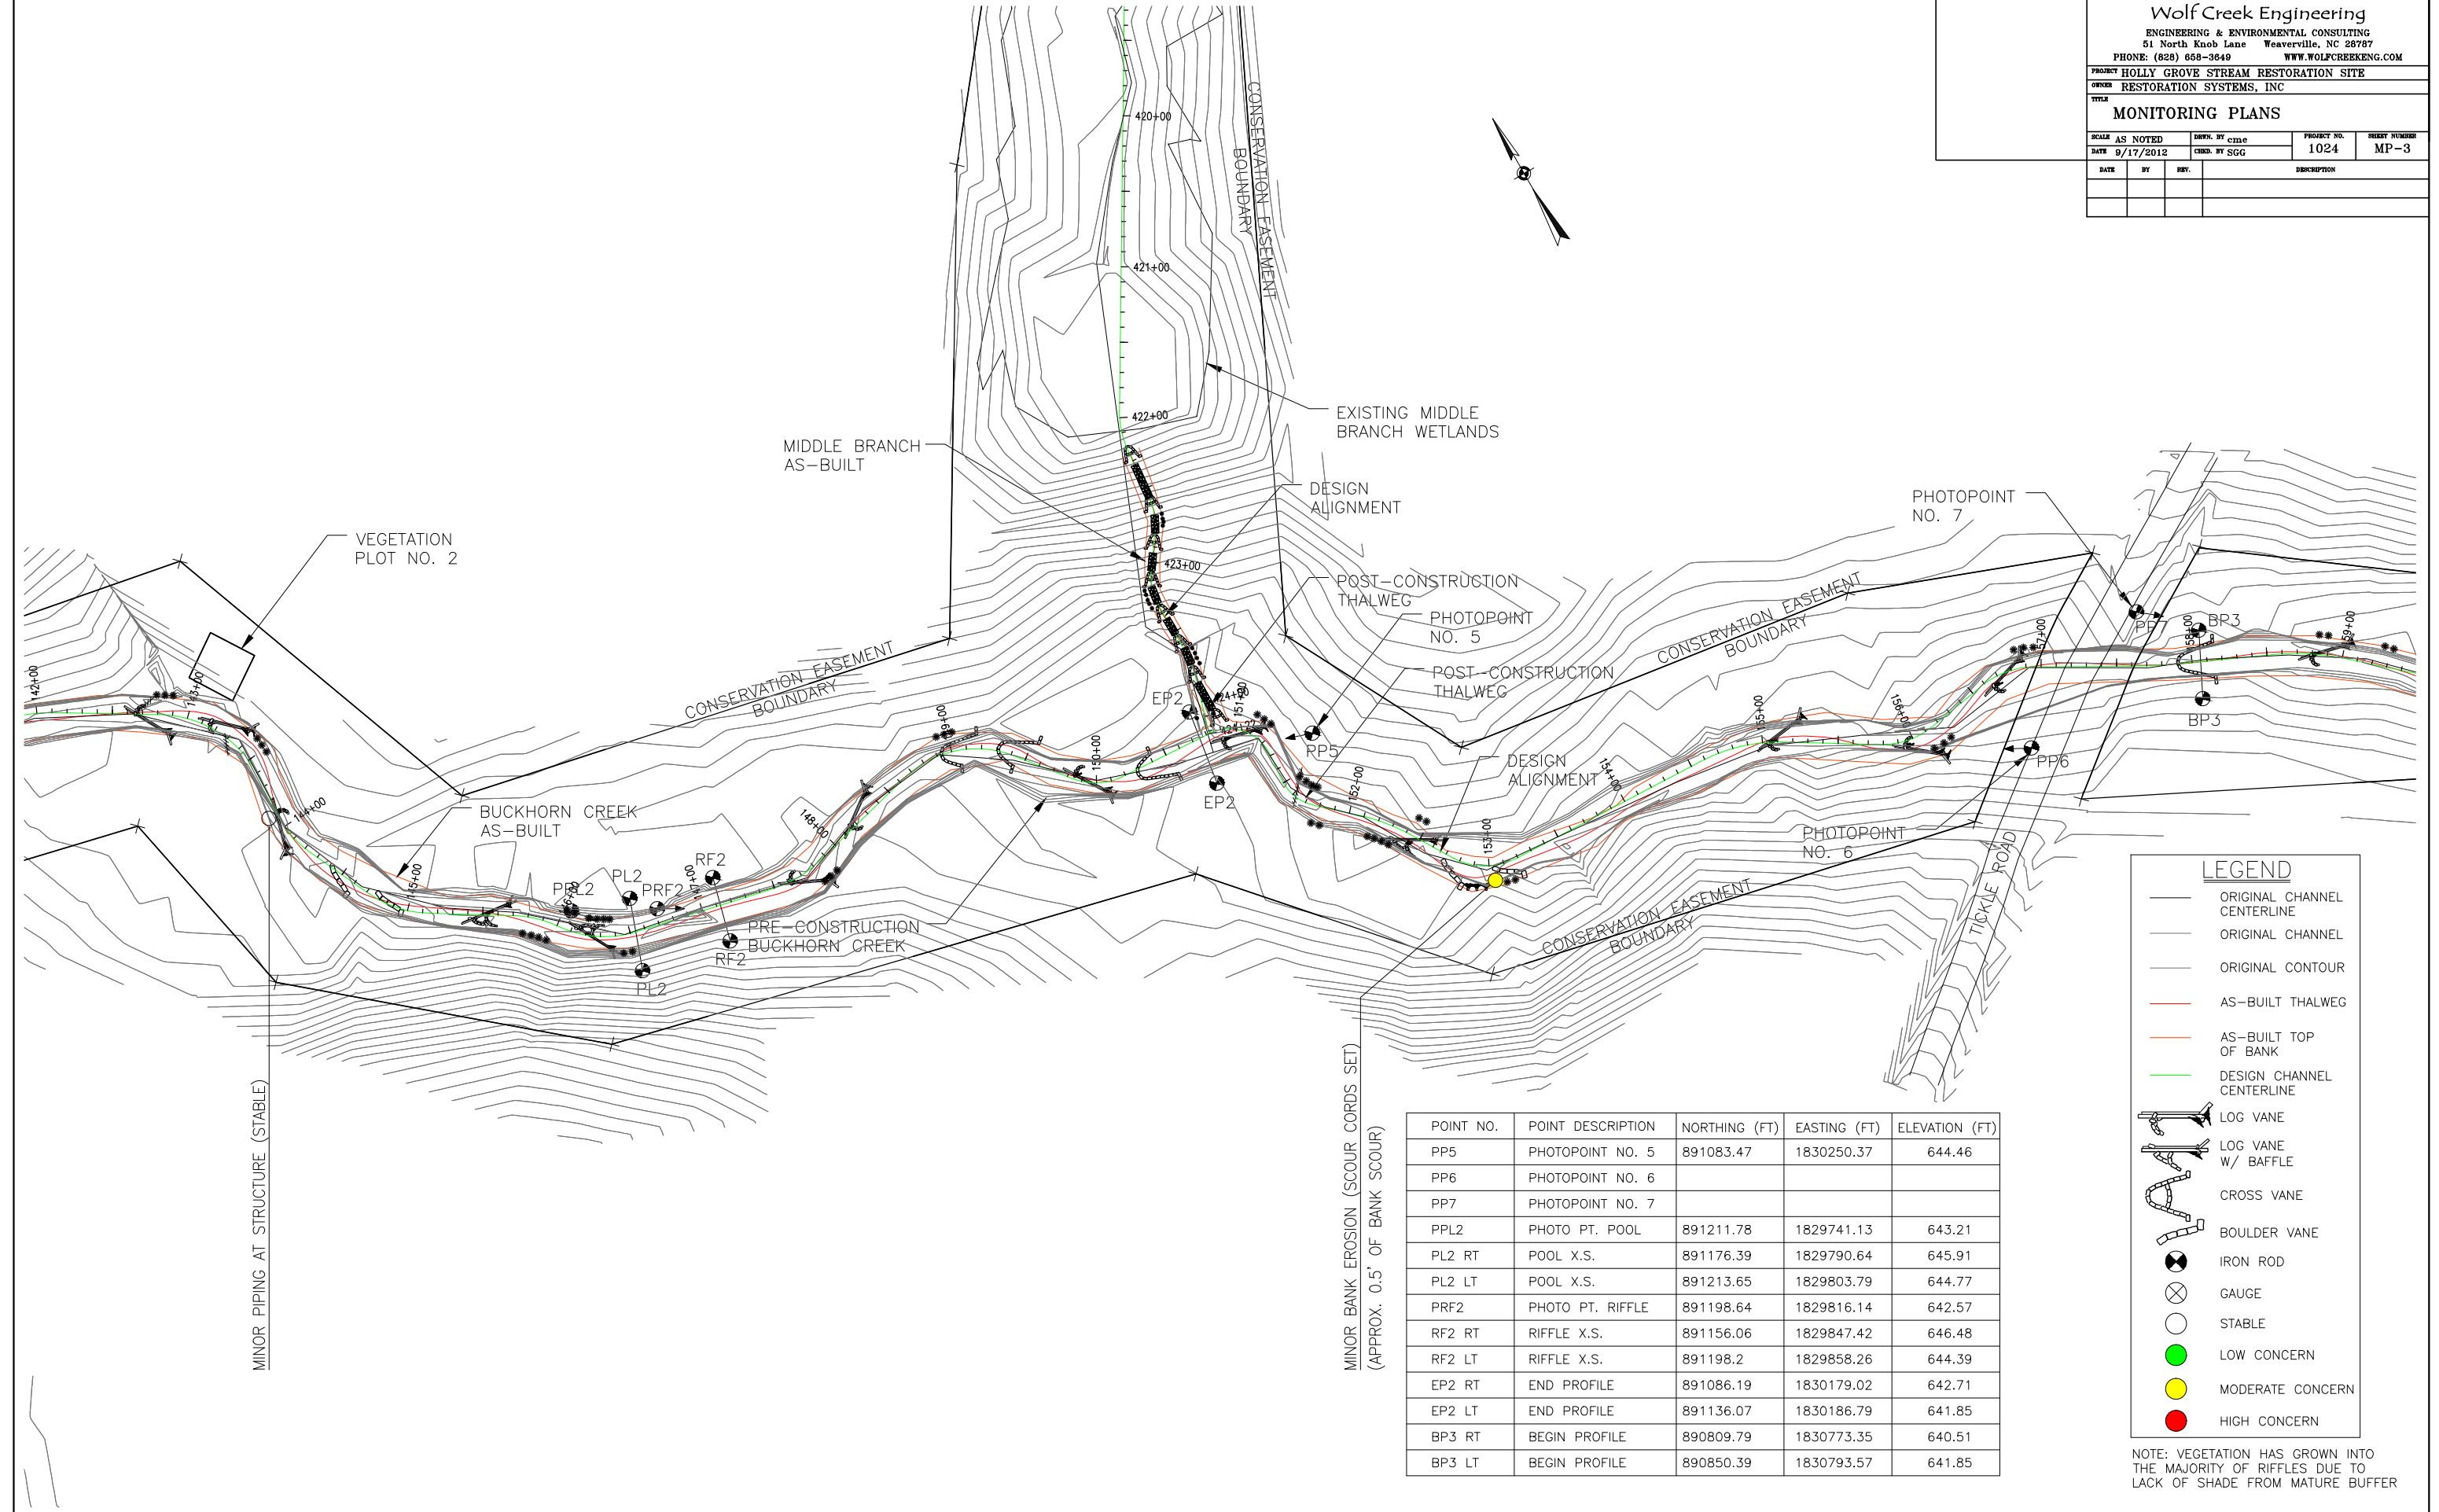


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
PP5	PHOTOPOINT NO. 5	891083.47	1830250.37	644.46
PP6	PHOTOPOINT NO. 6			
PP7	PHOTOPOINT NO. 7			
PPL2	PHOTO PT. POOL	891211.78	1829741.13	643.21
PL2 RT	POOL X.S.	891176.39	1829790.64	645.91
PL2 LT	POOL X.S.	891213.65	1829803.79	644.77
PRF2	PHOTO PT. RIFFLE	891198.64	1829816.14	642.57
RF2 RT	RIFFLE X.S.	891156.06	1829847.42	646.48
RF2 LT	RIFFLE X.S.	891198.2	1829858.26	644.39
EP2 RT	END PROFILE	891086.19	1830179.02	642.71
EP2 LT	END PROFILE	891136.07	1830186.79	641.85
BP3 RT	BEGIN PROFILE	890809.79	1830773.35	640.51
BP3 LT	BEGIN PROFILE	890850.39	1830793.57	641.85

LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN


NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER




LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER


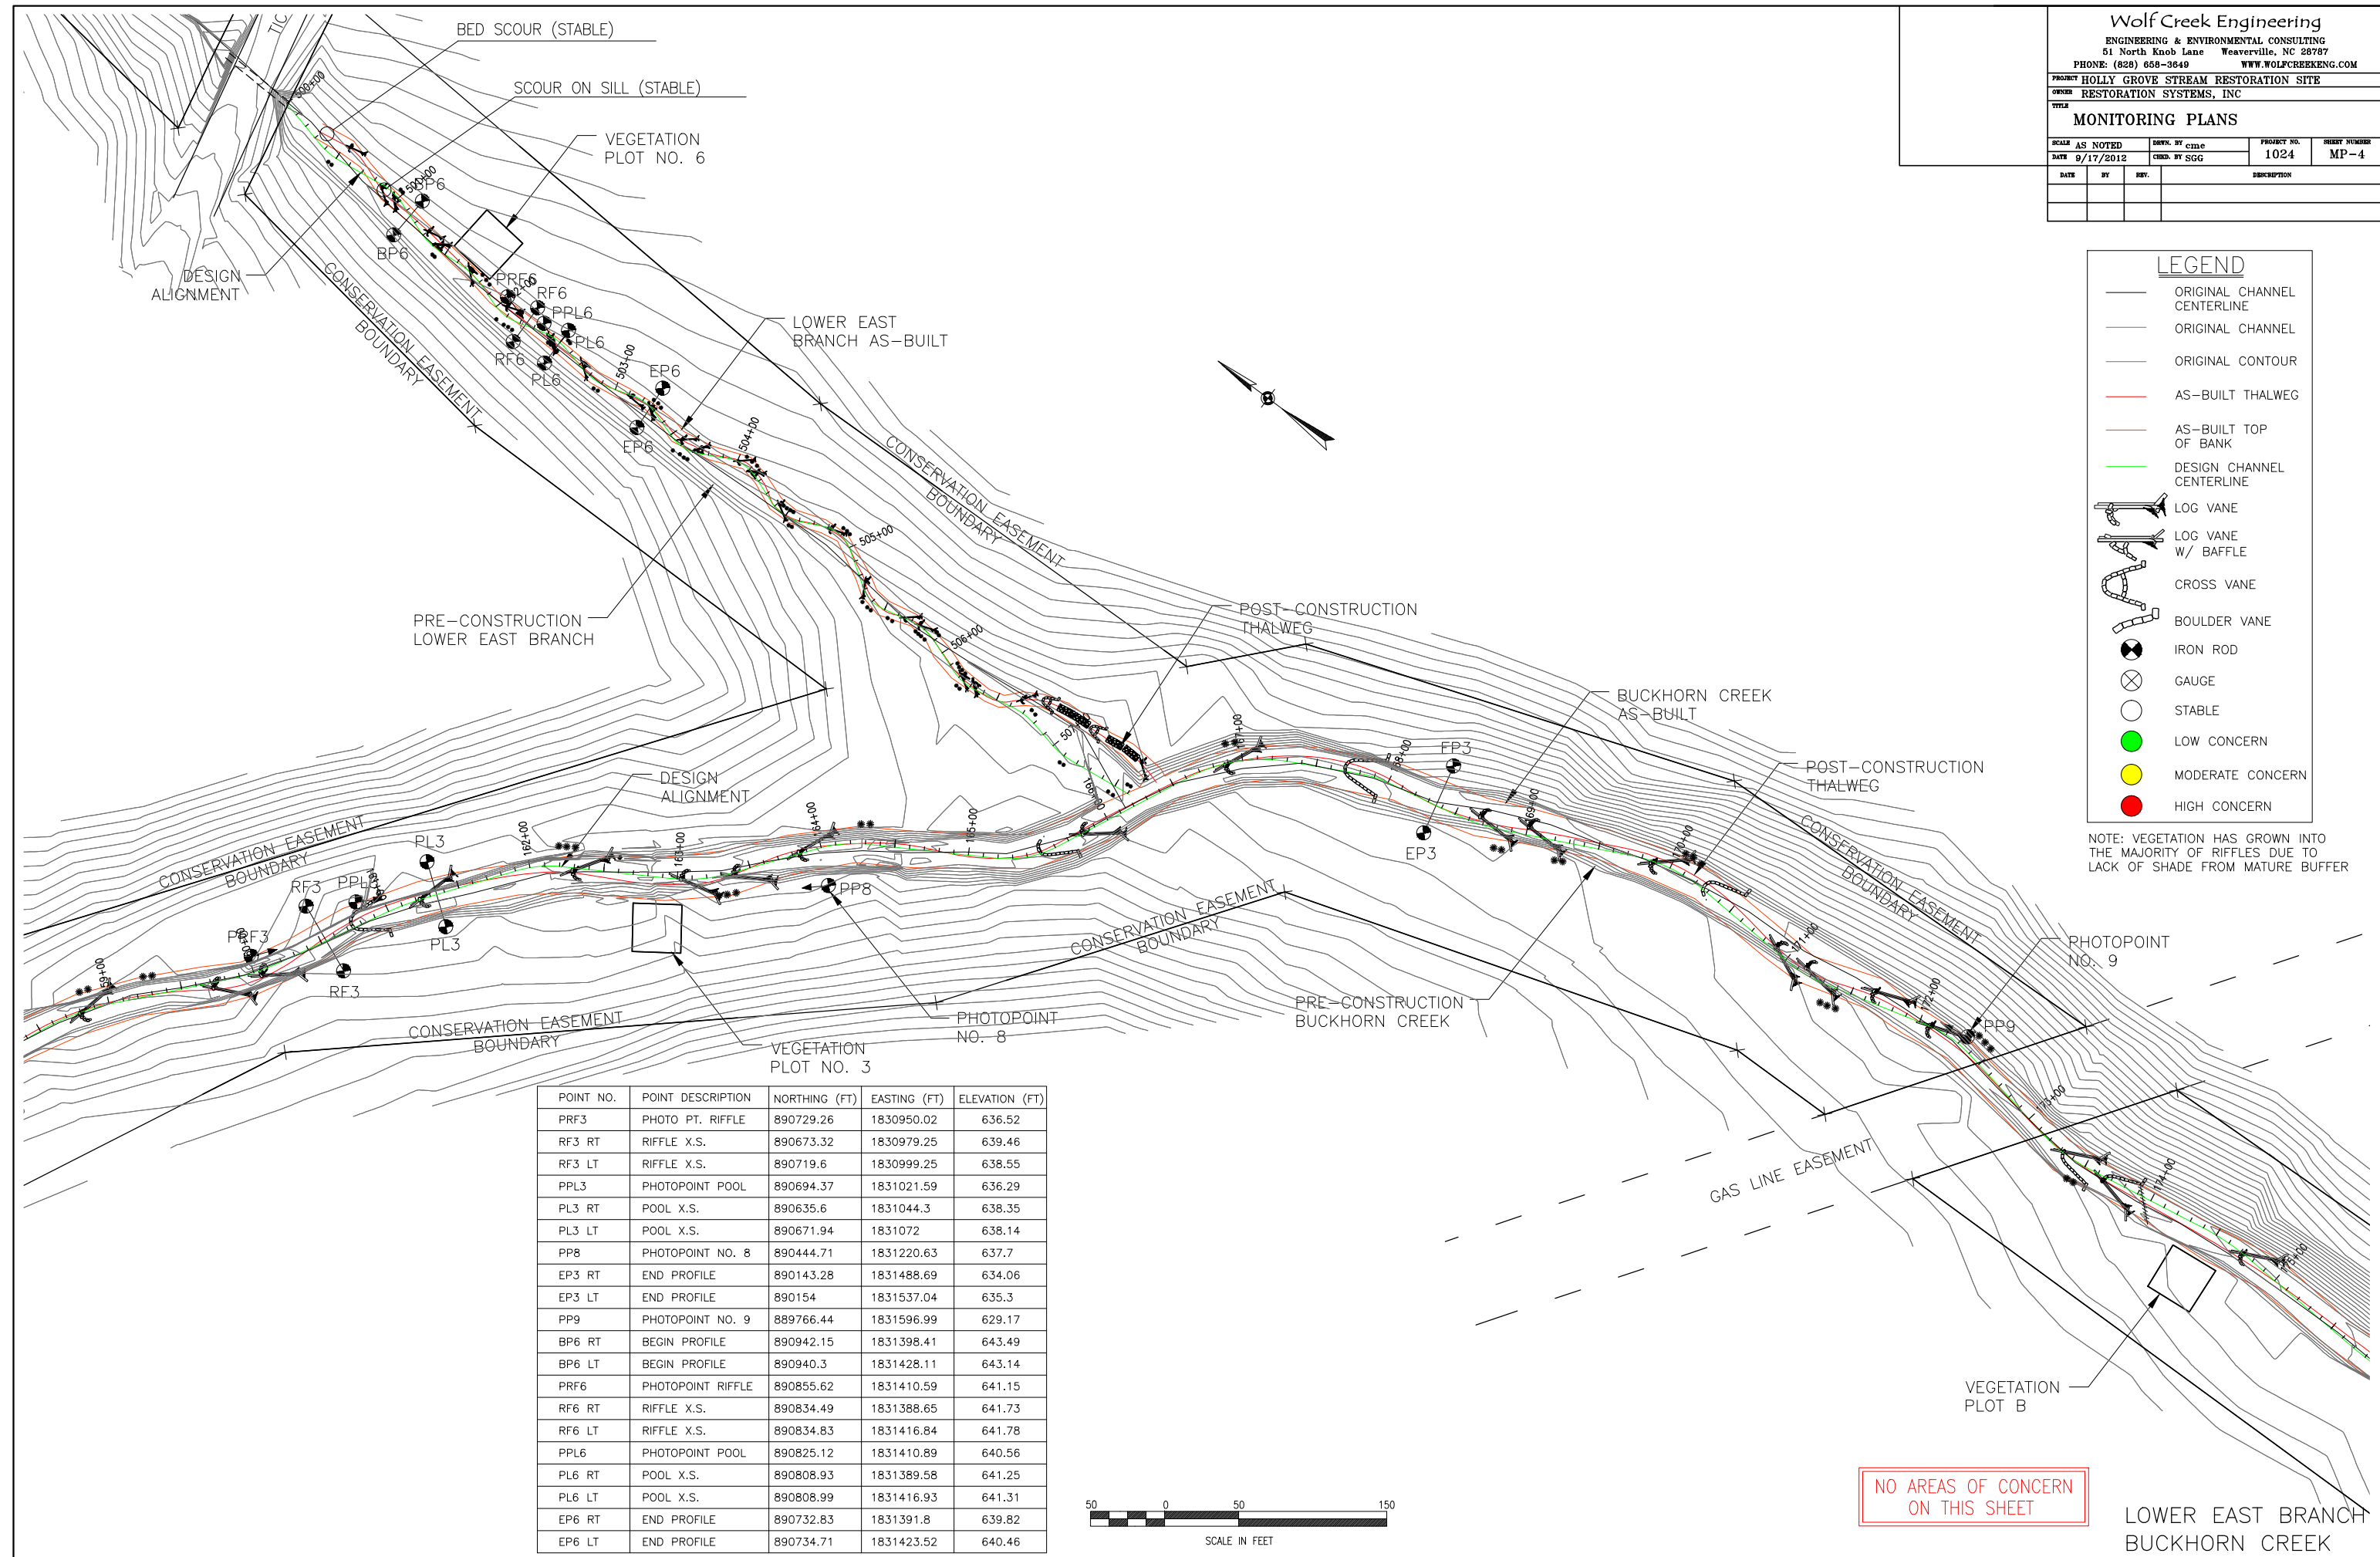


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
PRF3	PHOTO PT. RIFFLE	890729.26	1830950.02	636.52
RF3 RT	RIFFLE X.S.	890673.32	1830979.25	639.46
RF3 LT	RIFFLE X.S.	890719.6	1830999.25	638.55
PPL3	PHOTOPOINT POOL	890694.37	1831021.59	636.29
PL3 RT	POOL X.S.	890635.6	1831044.3	638.35
PL3 LT	POOL X.S.	890671.94	1831072	638.14
PP8	PHOTOPOINT NO. 8	890444.71	1831220.63	637.7
EP3 RT	END PROFILE	890143.28	1831488.69	634.06
EP3 LT	END PROFILE	890154	1831537.04	635.3
PP9	PHOTOPOINT NO. 9	889766.44	1831596.99	629.17
BP6 RT	BEGIN PROFILE	890942.15	1831398.41	643.49
BP6 LT	BEGIN PROFILE	890940.3	1831428.11	643.14
PRF6	PHOTOPOINT RIFFLE	890855.62	1831410.59	641.15
RF6 RT	RIFFLE X.S.	890834.49	1831388.65	641.73
RF6 LT	RIFFLE X.S.	890834.83	1831416.84	641.78
PPL6	PHOTOPOINT POOL	890825.12	1831410.89	640.56
PL6 RT	POOL X.S.	890808.93	1831389.58	641.25
PL6 LT	POOL X.S.	890808.99	1831416.93	641.31
EP6 RT	END PROFILE	890732.83	1831391.8	639.82
EP6 LT	END PROFILE	890734.71	1831423.52	640.46



NO AREAS OF CONCERN ON THIS SHEET

LOWER EAST BRANCH BUCKHORN CREEK

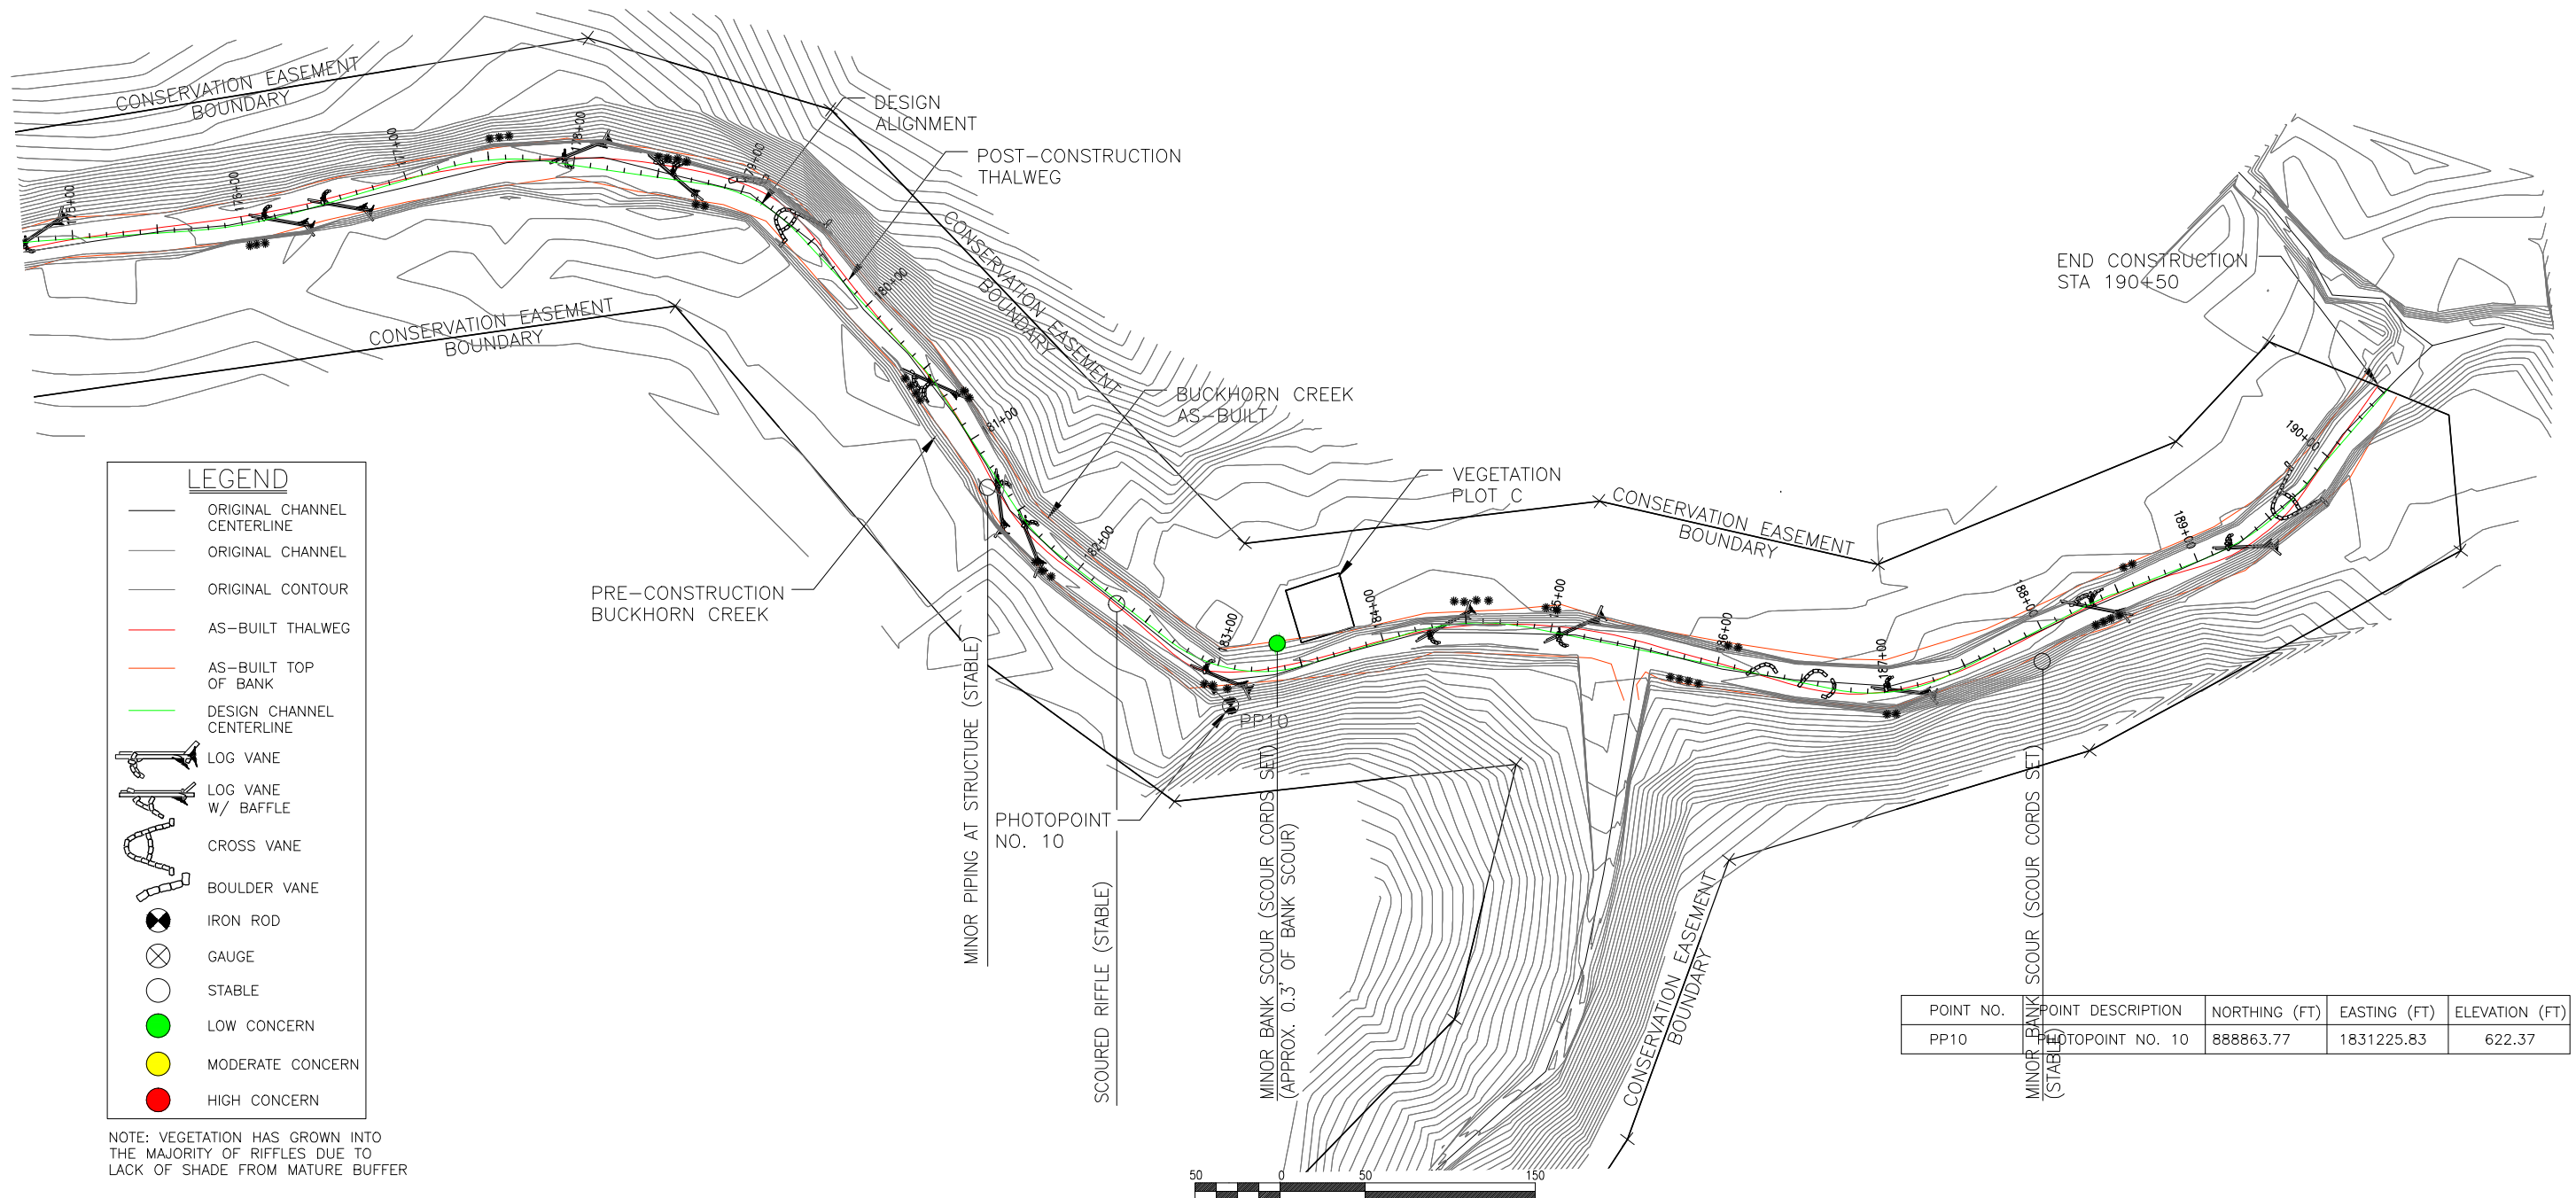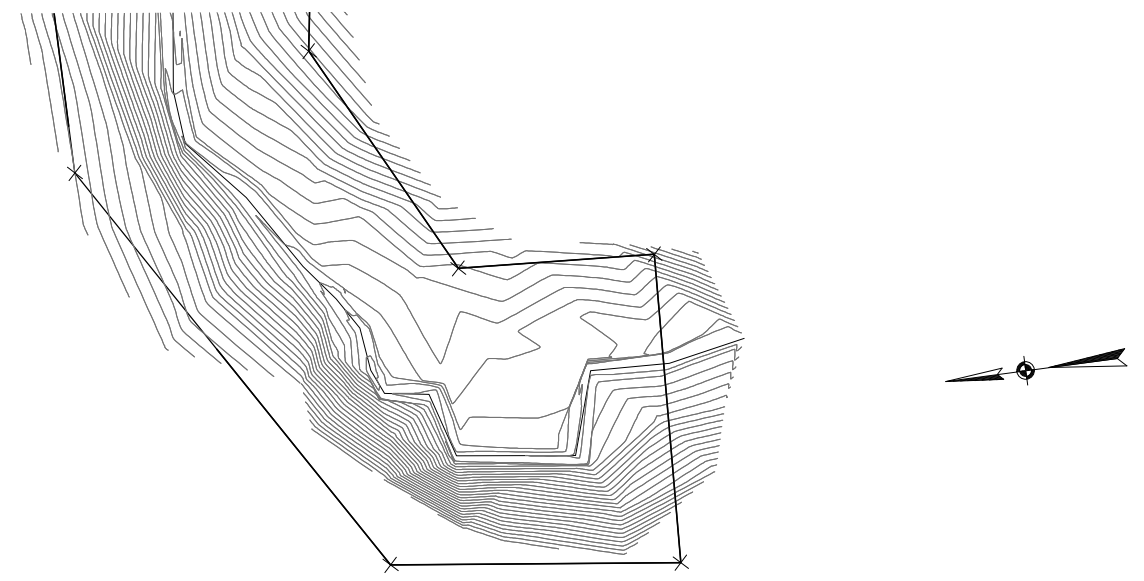


LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER

POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
PP10	PHOTOPOINT NO. 10	888863.77	1831225.83	622.37

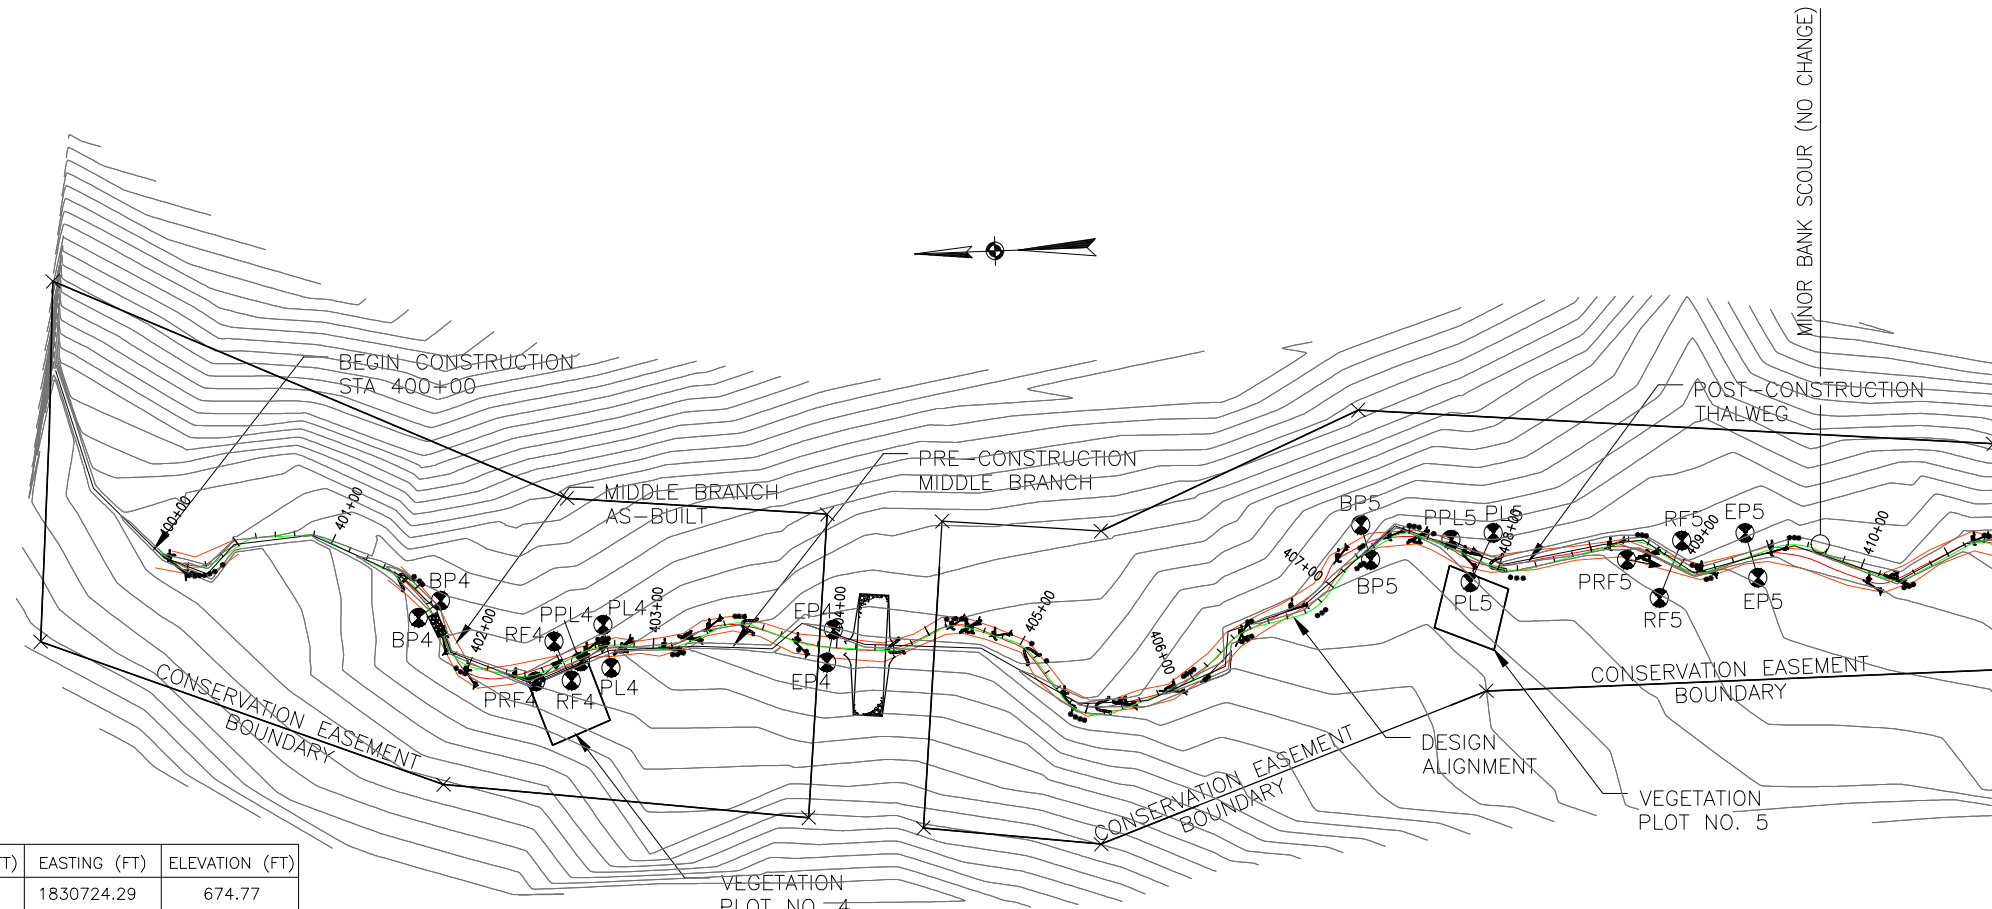


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
BP4 RT	BEGIN PROFILE	893112.11	1830724.29	674.77
BP4 LT	BEGIN PROFILE	893100.16	1830732.75	674.94
PRF 4	PHOTOPOINT RIFFLE	893052.14	1830688.91	672.84
RF4 RT	RIFFLE X.S.	893033.61	1830688.71	672.97
RF4 LT	RIFFLE X.S.	893041.95	1830709.35	673.1
PPL4	PHOTOPOINT POOL	893028.41	1830698.43	672.27
PL4 RT	POOL X.S.	893012.69	1830694.5	672.34
PL4 LT	POOL X.S.	893016.06	1830717.08	672.37
EP4 RT	END PROFILE	892900.43	1830693.07	670.12
EP4 LT	END PROFILE	892896.35	1830710.01	670.19
BP5 RT	BEGIN PROFILE	892615.37	1830735.78	665.53
BP5 LT	BEGIN PROFILE	892619.77	1830754.12	665.59
PRF 5	PHOTOPOINT RIFFLE	892481.99	1830730.82	662.8
RF5 RT	RIFFLE X.S.	892465.75	1830710.28	663.37
RF5 LT	RIFFLE X.S.	892453.05	1830739.76	662.65
PPL5	PHOTOPOINT POOL	892573.02	1830744.67	663.74
PL5 RT	POOL X.S.	892563.99	1830722.2	664.33
PL5 LT	POOL X.S.	892551	1830747.44	664.4
EP5 RT	END PROFILE	892414.15	1830718.87	661.96
EP5 LT	END PROFILE	892419.91	1830742.4	661.71


LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- ⊗ GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NO AREAS OF CONCERN ON THIS SHEET


NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER



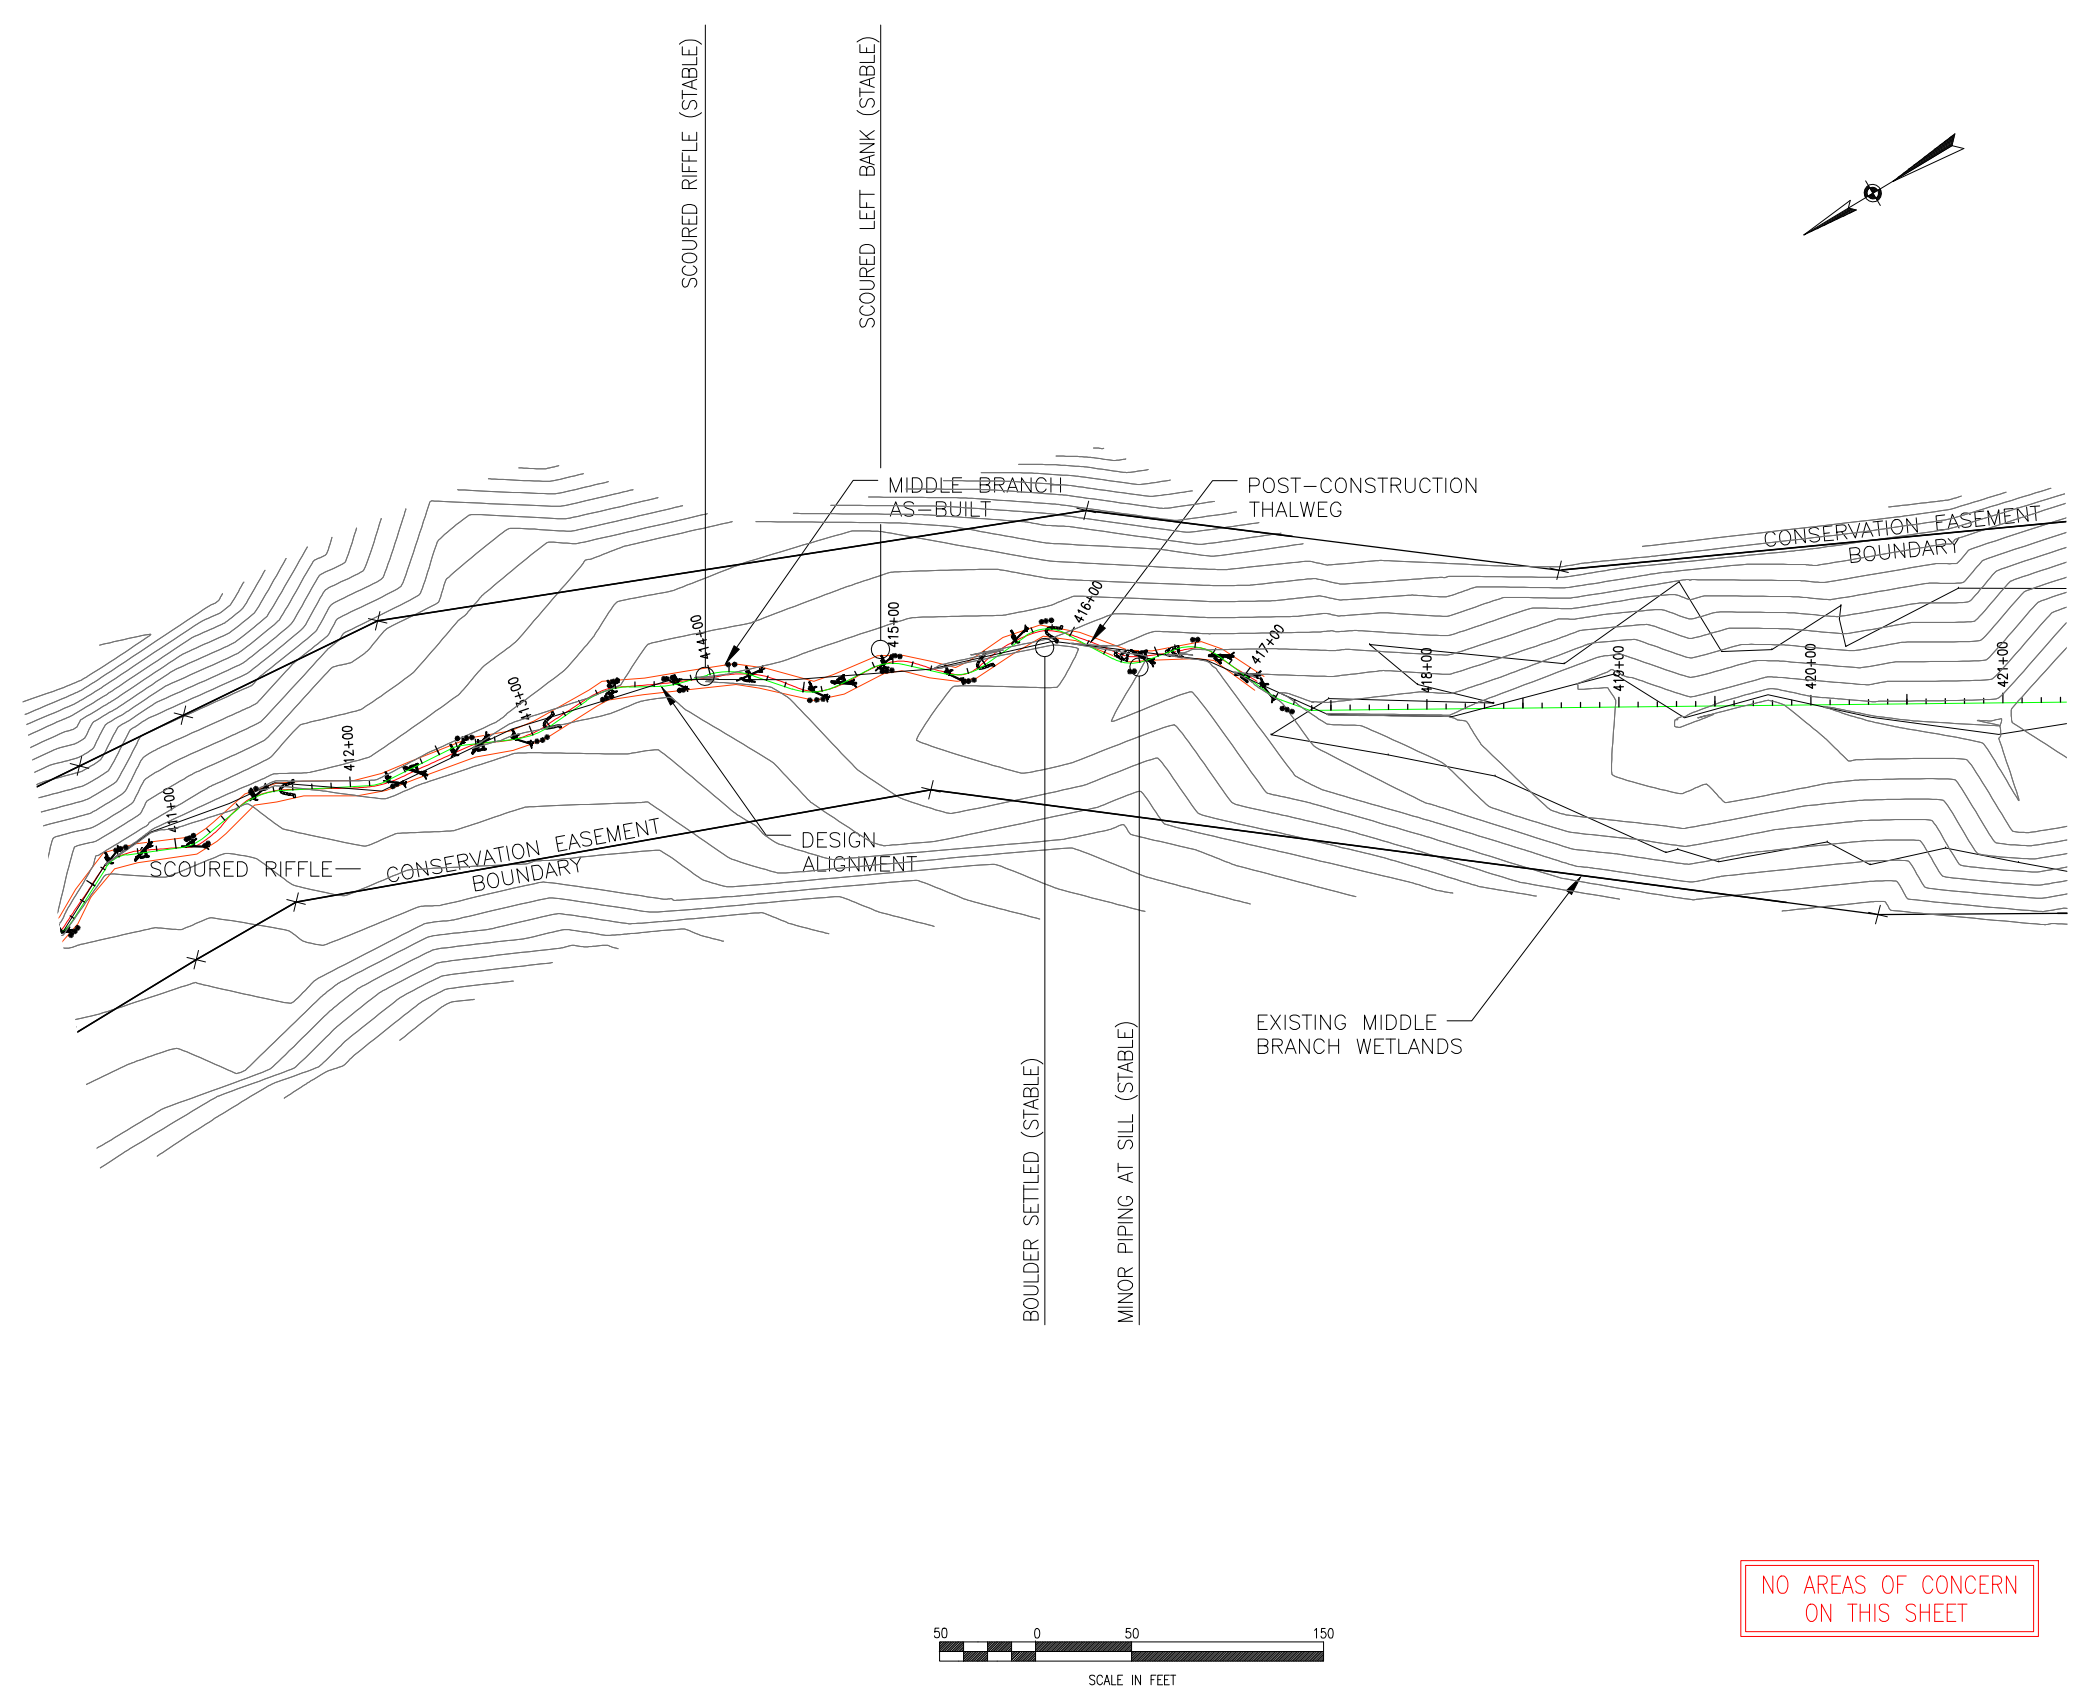


- LEGEND**
- ORIGINAL CHANNEL CENTERLINE
 - ORIGINAL CHANNEL
 - ORIGINAL CONTOUR
 - AS-BUILT THALWEG
 - AS-BUILT TOP OF BANK
 - DESIGN CHANNEL CENTERLINE
 - LOG VANE
 - LOG VANE W/ BAFFLE
 - CROSS VANE
 - BOULDER VANE
 - IRON ROD
 - GAUGE
 - STABLE
 - LOW CONCERN
 - MODERATE CONCERN
 - HIGH CONCERN

NO AREAS OF CONCERN ON THIS SHEET





NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER

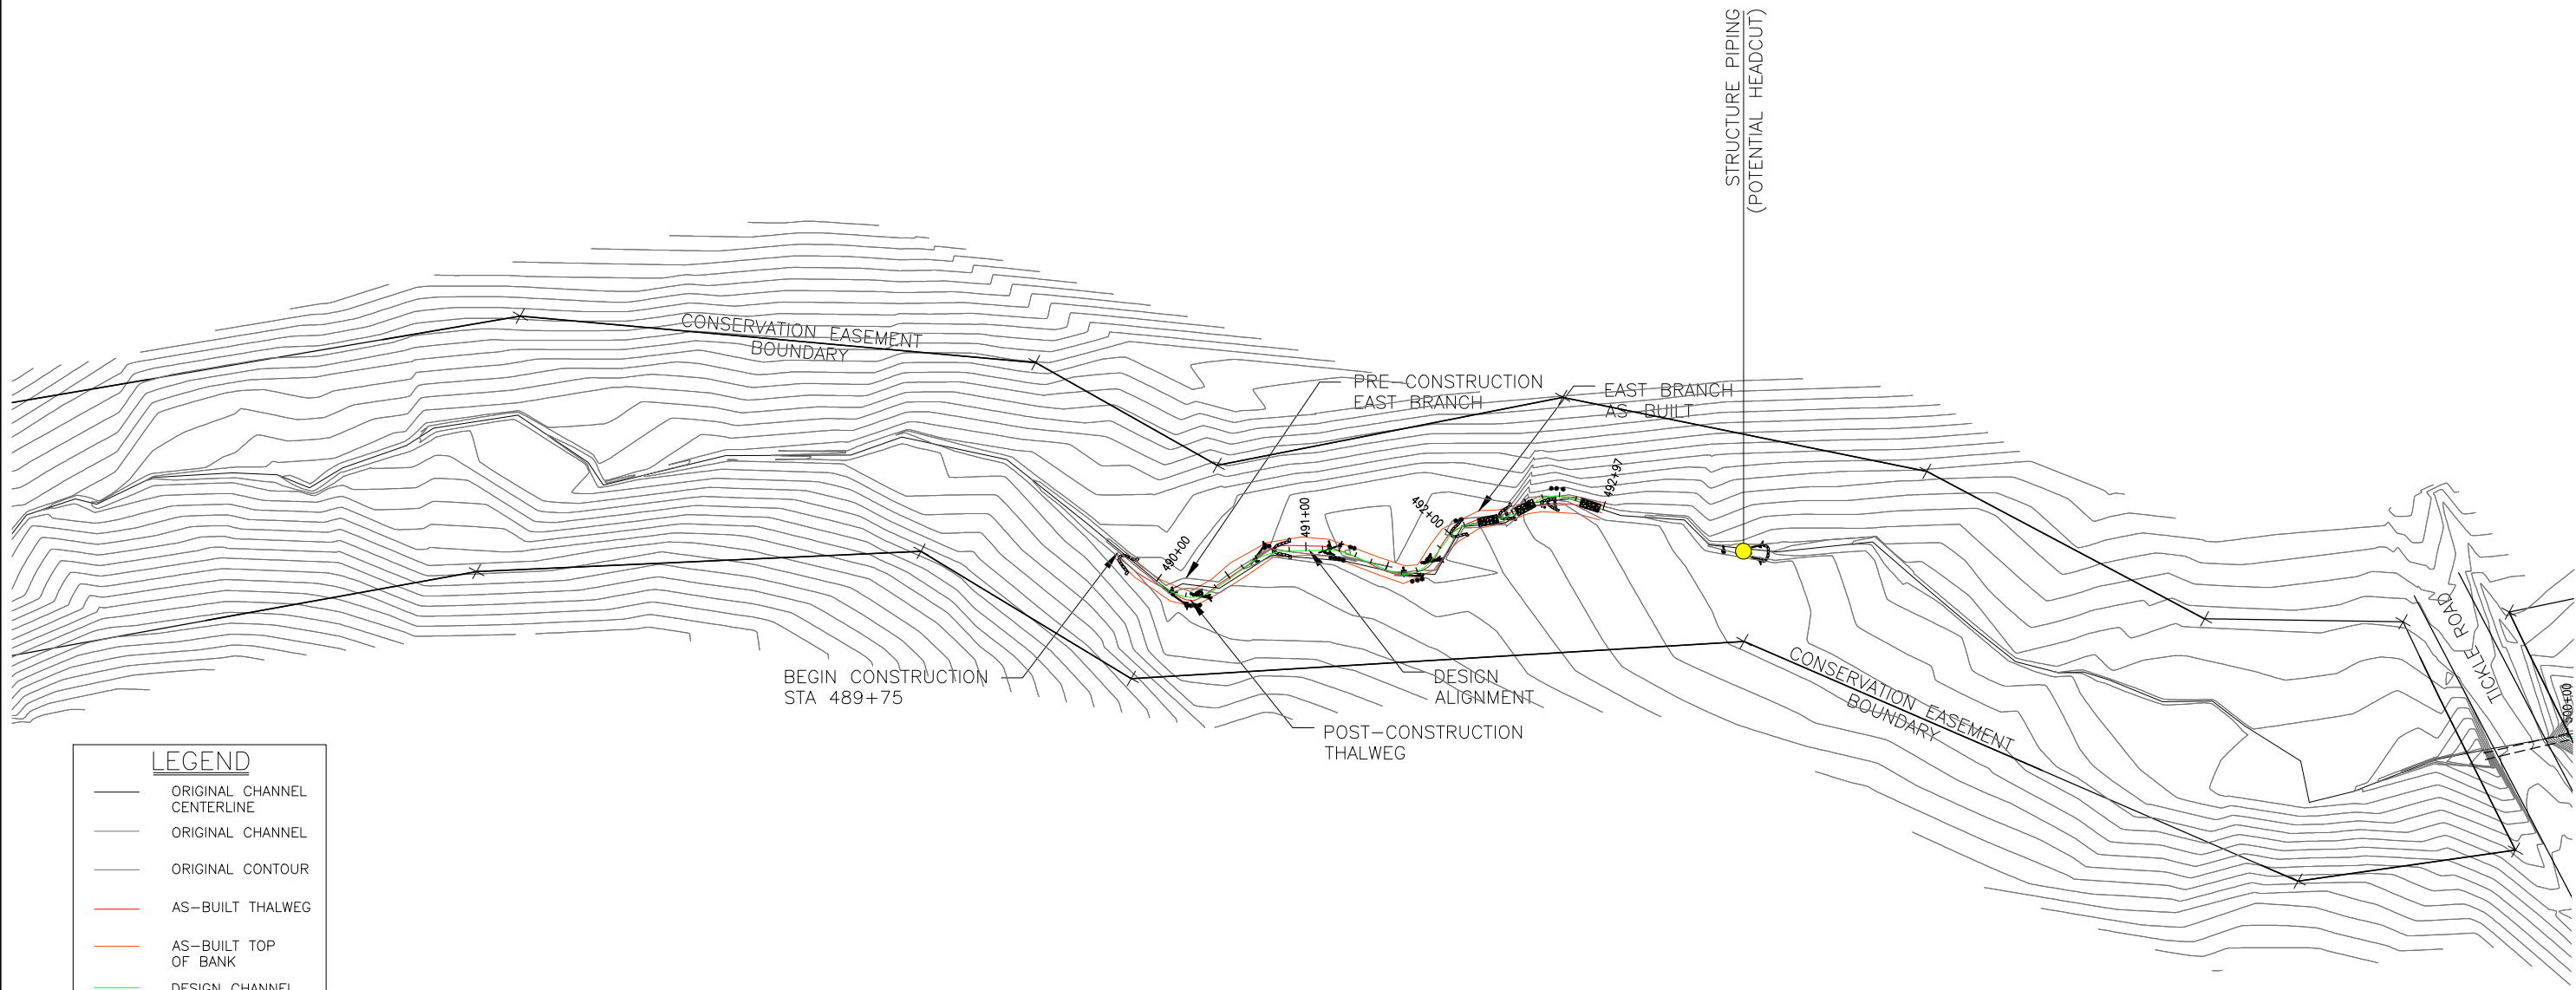

- LEGEND**
- ORIGINAL CHANNEL CENTERLINE
 - ORIGINAL CHANNEL
 - ORIGINAL CONTOUR
 - AS-BUILT THALWEG
 - AS-BUILT TOP OF BANK
 - DESIGN CHANNEL CENTERLINE
 - LOG VANE
 - LOG VANE W/ BAFFLE
 - CROSS VANE
 - BOULDER VANE
 - IRON ROD
 - GAUGE
 - STABLE
 - LOW CONCERN
 - MODERATE CONCERN
 - HIGH CONCERN

NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER



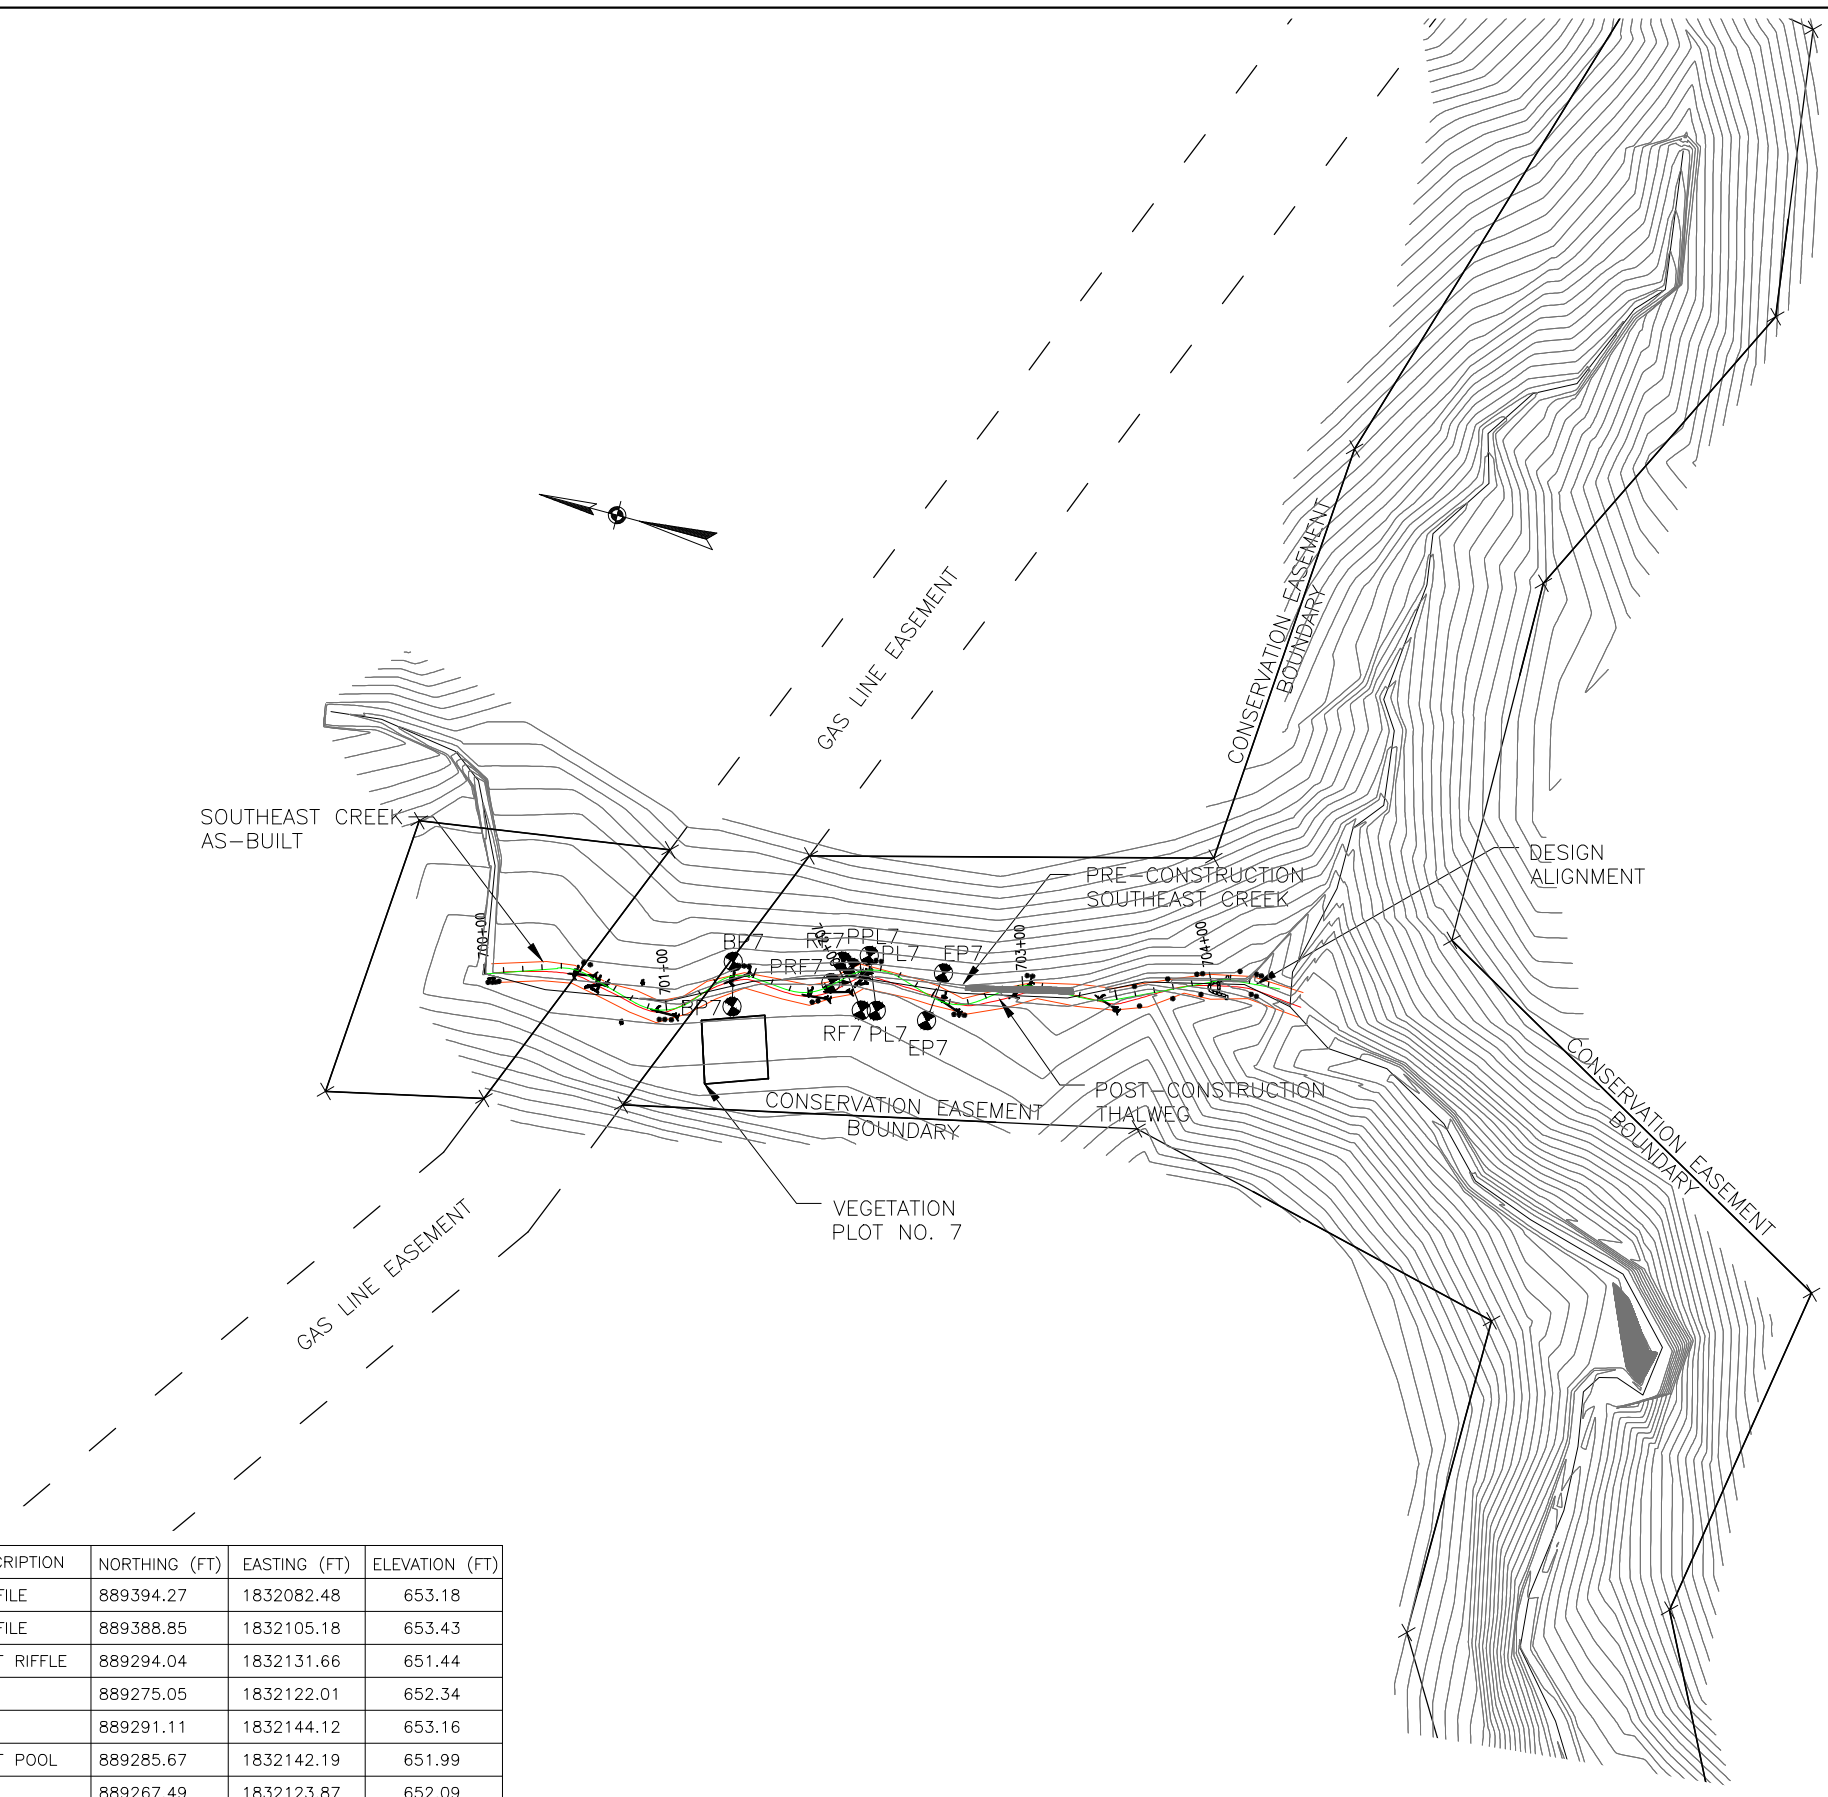


POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
BP7 RT	BEGIN PROFILE	889394.27	1832082.48	653.18
BP7 LT	BEGIN PROFILE	889388.85	1832105.18	653.43
PRF 7	PHOTOPOINT RIFFLE	889294.04	1832131.66	651.44
RF7 RT	RIFFLE X.S.	889275.05	1832122.01	652.34
RF7 LT	RIFFLE X.S.	889291.11	1832144.12	653.16
PPL7	PHOTOPOINT POOL	889285.67	1832142.19	651.99
PL7 RT	POOL X.S.	889267.49	1832123.87	652.09
PL7 LT	POOL X.S.	889278.35	1832150.58	653.53
EP7 RT	END PROFILE	889240.74	1832125.74	651.43
EP7 LT	END PROFILE	889238.74	1832151.82	653.54


LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN

NO AREAS OF CONCERN ON THIS SHEET




NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER

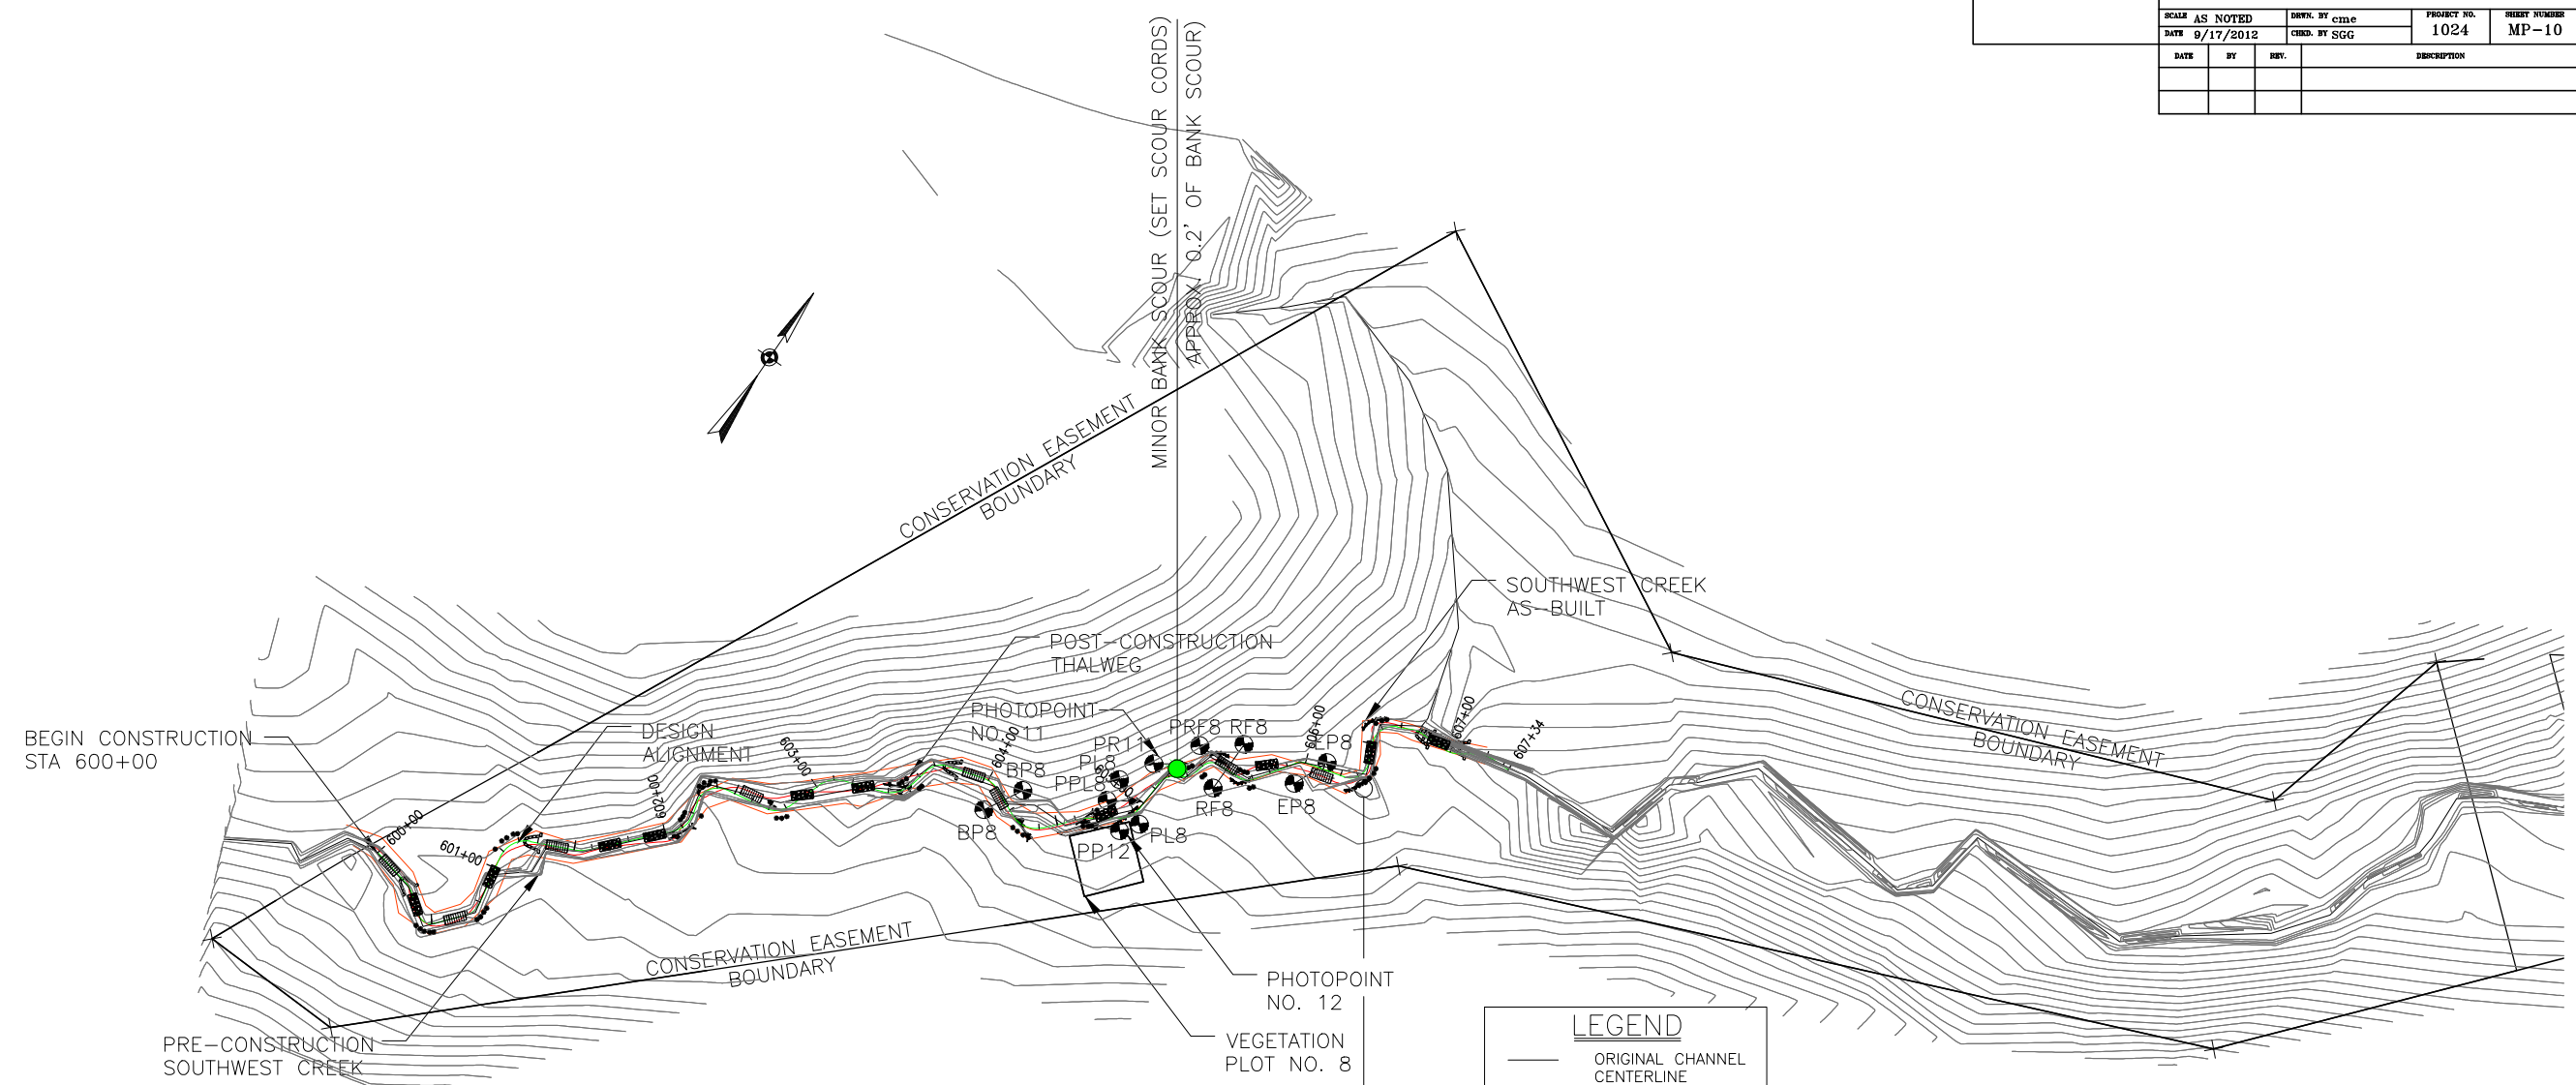

POINT NO.	POINT DESCRIPTION	NORTHING (FT)	EASTING (FT)	ELEVATION (FT)
BP8 RT	BEGIN PROFILE	888530.2	1829244.79	—
BP8 LT	BEGIN PROFILE	888550.58	1829256.28	—
PR8 5	PHOTOPOINT RIFFLE	888624.26	1829321.4	—
RF8 RT	RIFFLE X.S.	888609.33	1829340.21	—
RF8 LT	RIFFLE X.S.	888638.13	1829340.74	—
PPL8	PHOTOPOINT POOL	888571.69	1829296.89	—
PL8 RT	POOL X.S.	888570.92	1829318.35	—
PL8 LT	POOL X.S.	888584.77	1829295.99	—
EP8 RT	END PROFILE	888635.95	1829374.79	—
EP8 LT	END PROFILE	888655.17	1829383.15	—
PP11	PHOTOPOINT NO. 11	888602.23	1829306.57	—
PP12	PHOTOPOINT NO. 12	888562.04	1829311.53	—

LEGEND

- ORIGINAL CHANNEL CENTERLINE
- ORIGINAL CHANNEL
- ORIGINAL CONTOUR
- AS-BUILT THALWEG
- AS-BUILT TOP OF BANK
- DESIGN CHANNEL CENTERLINE
- LOG VANE
- LOG VANE W/ BAFFLE
- CROSS VANE
- BOULDER VANE
- IRON ROD
- GAUGE
- STABLE
- LOW CONCERN
- MODERATE CONCERN
- HIGH CONCERN



NOTE: VEGETATION HAS GROWN INTO THE MAJORITY OF RIFFLES DUE TO LACK OF SHADE FROM MATURE BUFFER

2.0 Project condition and monitoring results

2.1 Vegetation Assessment

The Carolina Vegetation Survey – Ecosystem Enhancement Program (CVS-EEP) 2008 protocol for recording vegetation (Lee et. al 2008) was used to determine the planting pattern of woody stems with respect to species, spacing, and density as well as to forecast survivability and growth of planted stems in subsequent monitoring years. Eleven (11) randomly placed 10 meter by 10 meter vegetative sampling plots were established within the project easement area. The corners of each monitoring plot have been marked in the field and their position documented by GPS survey. Plots were placed within the applicable planting zones to capture the heterogeneity of the designed vegetative communities. Plot corners were permanently marked with rebar and recorded during the baseline survey. All planted stems and plot corners were marked with orange flagging tape to facilitate relocation during subsequent monitoring years. A reference photograph was taken for each plot at the origin looking diagonally across the plot to the opposite corner.

There are eleven vegetation plots that were monitored using the CVS-EEP vegetation monitoring protocol, which was implemented for monitoring year (MY) -01, MY-02, MY-03, and MY-04. Vegetation Plot 7 was relocated during MY-02 to avoid disturbance from gas line easement maintenance. Including Plots 1-8, and A-C, there are 309 planted stems/acre which excludes live stakes. There are 2,347 stems/acre that includes planted stems, livestakes, and natural volunteers. Vegetation plots 1, 4, 6, A, B, and C contain planted stem counts above the success criteria. The success criterion for planted woody species is 320 stems/acre after MY-03. A mortality rate of 10 percent will be allowed after MY-04 (288 stems/acre), with another 10 percent allowed after MY-05 (260 stems/acre).

Table V: Vegetation Summary

Plot	Date Sampled	Planted Living Stems	Dead or Missing Stems	Volunteer Stems	Total Living Stems	Average Stems Per Acre	# species
1	9/13/2012	8	1	56	64	324	7
2	9/13/2012	4	0	83	87	162	3
3	9/13/2012	7	0	43	50	283	6
4	9/13/2012	9	2	105	114	364	7
5	9/13/2012	5	0	38	43	202	4
6	9/13/2012	10	0	6	16	405	5
7	9/13/2012	4	0	1	5	162	3
8	9/13/2012	6	0	92	98	243	3
A	9/13/2012	9	2	48	57	364	6
B	9/13/2012	10	3	26	36	405	3
C	9/13/2012	13	0	55	68	526	5

2.1.1 Vegetative Problems

The vegetation problem areas are composed of areas of low planted stem density in the vicinity of plots, 2, 3, 5, 7, and 8, due to the CVS data results. Invasive exotics observed throughout the conservation easement that are a threat to native vegetation include tree of heaven (*Ailanthus altissima*), princess tree (*Paulownia tomentosa*), and Johnson grass (*Sorghum halapense*). Other invasive exotics infrequently observed that did not seem to be an imminent threat include tall fescue (*Schedonurus arundinaceus*), Japanese honeysuckle (*Lonicera japonica*), Multiflora rose (*Rosa multiflora*), and Chinese privet (*Ligustrum sinense*). According to the EEP Invasives of Concern/Interest List, tree of heaven, princess tree, multiflora rose, Chinese privet, and Japanese honeysuckle are all classified as “High Concern” species and fescue as a “Low/Moderate Concern” species.

2.1.2 Vegetative Plot Photos

A photo point was established in each vegetation plot. Photo points are positioned for each plot at the origin facing diagonally across the plot to the opposite corner. The photographs were captured on the same day as the vegetation plot surveys (Appendix A).

2.2 Stream Assessment

Monitoring protocol follows that outlined within the EEP Site Specific Mitigation Plan and detailed in the U.S. Army Corps of Engineers (USACE) Stream Mitigation Guidelines for Monitoring Level I. Specifically, stream monitoring included measurements of stream dimension, profile, pattern, bed materials, photo documentation, and stream bankfull return interval.

Streambanks remain intact and stable and fully vegetated throughout the site. Vegetation has grown into many riffles on the main channel due to a lack of shade and mature buffer. This has limited the mobility of bed material but has not had noticeable effects on overall stability.

2.2.1 Hydrology

Since completion of construction in October of 2008, the site has been subjected to at least one greater-than-bankfull event and several bankfull or near-bankfull events. In August of 2008, Tropical Storm Fay crossed central North Carolina resulting in eight (8) inches of rainfall on-site and water elevations 2.5 feet above bankfull on Buckhorn Creek. Approximately seventy percent (70%) of the project was complete at that time and subjected to this estimated fifty-year storm event. In October of 2008, locally heavy rainfall produced a bankfull event at the Site during the final stages of construction. In June of 2009, heavy rainfall resulted in water elevations 0.2 to 0.3 feet above bankfull. Heavy rainfall associated with remnants of Hurricane Ida produced one additional event in November of 2009, after Year 1 monitoring was completed which again resulted in an elevated flow event. In late September of 2010, Tropical Storm Nicole moved north across central and eastern North Carolina and produced approximately 4.5 inches of rain over 48 hours resulting in flood waters which crested 0.4 feet above bankfull. During Year 3, at least one rainfall event occurred resulting in water which crested 0.1 feet above bankfull. There was no evidence of a greater than bankfull event during Year 4 monitoring.

Table VI Verification of Bankfull Events – Lick Creek Stream Restoration Site (D04013-1)

Date of Data Collection	Date of Occurrence of Bankfull Event	Height above Bankfull (ft)	Method of Data Collection
9/3/08	8/27/08	2.5	Debris Evidence
8/13/09	June 2009	0.2	Crest Gauge
10/11/10	September 2010	0.4	Crest Gauge
9/26/11	2011	0.1	Crest Gauge
9/17/12	2012	-0.4	Crest Gauge

2.2.2 Geomorphology

Following the procedures established in the USDA Forest Service Manual (Harrelson et al 1994) and the methodologies utilized in the Rosgen stream assessment and classification system (Rosgen 1994, 1996), data collected consisted of detailed dimension and pattern measurements, longitudinal profiles, and bed materials sampling.

Re-survey of the permanent cross sections and profile reaches have shown only minimal alterations in local bed elevations with the bed form and the channel pattern remaining consistent with the As-built condition. Overall, Buckhorn Creek showed little or no adjustments in the riffle cross sections. Middle Branch, Lower East Branch, Southeast Creek and Southwest Creek all showed evidence of minor adjustment in the riffle cross sections, displaying a slight increase in cross-sectional area while maintaining nearly the same maximum depth as the As-built. Location of bed features relative to the pattern is consistent with the As-built survey.

Pebble counts were conducted at each riffle cross-section, as well as across the overall study reaches. Pebble count data was plotted by size distribution in order to assess the D_{50} and D_{84} size class. Pebble count data from Reaches 2, 4, 5, 6 and 7 showed no conclusive variations from the Year 3 survey. Reach 1 and 8 showed an increase in both the D_{50} and the D_{84} values. Reach 3 showed a general decrease in both the D_{50} and the D_{84} . This may be due in part to significant growth of vegetation in the riffles that may be trapping finer particles in the bed.

Table VII. BEHI and Sediment Export Estimates – (Only Required in Year 5)

2.2.3 Problem Areas

In Year 4 Monitoring of the Holly Grove Stream Restoration Site, some minor problem areas remain that were identified during Year 3.

- 1.) Several riffles on Buckhorn Creek and Southeast Branch still exhibit excessive vegetation in the channel bed.
- 2.) There was one (1) location of moderate piping at a log vane.
- 3.) There were three (3) areas of local bank scour.

Inadequate shade due to lack of mature riparian buffer has allowed vegetation to take root in the bed matrix. It is anticipated that this vegetation will die back during the winter but will reestablish during each growing season until sufficient shading is provided by the canopy of the

buffer. This has affected bedload transport by limiting bed mobility, but it is not expected to have any significant impact on the overall stability or integrity of the channel bed.

Continued visual monitoring is planned for the few stream areas that have been identified as “Areas of Concern”. Repairs will be performed on the structure on East Branch that is piping to prevent the possibility of a headcut formation. Additional live staking will be installed on the bank of Buckhorn at STA 153+00 that is exhibiting evidence of erosion. Also, three beaver dams on upper Buckhorn Creek were manually removed prior to Year 4 monitoring. Continued monitoring and maintenance of the beaver population will be conducted for the entire site.

2.2.4 Photo Reference Stations

Photograph reference Stations (PRSs) have been established to assist in characterizing the site and to allow qualitative evaluation of the site conditions. The location of each photo station has been permanently marked in the field and the bearing/orientation of the photograph is indicated on the As-built plans to allow for consistent repetition. A total of twenty-eight (28) PRSs have been established along the restored stream (Appendix B). Sixteen (16) of these PRSs have been located upstream of the permanent monitoring cross sections. These photographs are taken facing downstream looking at the section, and show as much of the banks and channel as possible

2.2.5 Stability Assessment Table

Table VIII. Categorical Stream Feature Visual Stability Assessment

Feature	Performance Percentage Buckhorn Creek (8,848 ft)					
	Initial	MY-01	MY-02	MY-03	MY-04	MY-05
Riffles	100%	100%	100%	100%	100%	100%
Pools	100%	100%	100%	100%	100%	100%
Thalweg	100%	100%	100%	100%	100%	100%
Meanders	100%	100%	100%	100%	100%	100%
Bed General	100%	100%	100%	100%	100%	100%
Vanes / J Hooks etc.	100%	99%	100%	100%	100%	100%
Wads and Boulders	100%	100%	100%	100%	100%	100%

Feature	Performance Percentage Middle Branch (1,755 ft)					
	Initial	MY-01	MY-02	MY-03	MY-04	MY-05
Riffles	100%	97%	99%	100%	100%	100%
Pools	100%	100%	100%	100%	100%	100%
Thalweg	100%	100%	100%	100%	100%	100%
Meanders	100%	100%	99%	100%	100%	100%
Bed General	100%	100%	100%	100%	100%	100%
Vanes / J Hooks etc.	100%	98%	99%	100%	100%	100%
Wads and Boulders	100%	83%	83%	100%	100%	100%

Feature	Performance Percentage East Branch (1,090 ft)					
	Initial	MY-01	MY-02	MY-03	MY-04	MY-05
Riffles	100%	100%	99%	99%	99%	99%
Pools	100%	100%	100%	100%	100%	100%
Thalweg	100%	100%	100%	100%	100%	100%
Meanders	100%	100%	100%	100%	100%	100%
Bed General	100%	100%	100%	100%	100%	100%
Vanes / J Hooks etc.	100%	100%	99%	99%	99%	99%
Wads and Boulders	100%	100%	100%	100%	100%	100%

Feature	Performance Percentage Southeast Creek (363 ft)					
	Initial	MY-01	MY-02	MY-03	MY-04	MY-05
Riffles	100%	96%	100%	100%	100%	
Pools	100%	100%	100%	100%	100%	
Thalweg	100%	100%	100%	100%	100%	
Meanders	100%	100%	100%	100%	100%	
Bed General	100%	100%	100%	100%	100%	
Vanes / J Hooks etc.	100%	100%	100%	100%	100%	
Wads and Boulders	100%	100%	100%	100%	100%	

Feature	Performance Percentage Southwest Creek (723 ft)					
	Initial	MY-01	MY-02	MY-03	MY-04	MY-05
Riffles	100%	100%	100%	100%	100%	
Pools	100%	100%	100%	100%	100%	
Thalweg	100%	100%	100%	100%	100%	
Meanders	100%	100%	100%	100%	100%	
Bed General	100%	100%	100%	100%	100%	
Vanes / J Hooks etc.	100%	100%	100%	100%	100%	
Wads and Boulders	100%	100%	100%	100%	100%	

**Table X-a Morphology and Hydraulic Monitoring Summary
Holly Grove Stream Restoration Site (D06028-B)
Reach 1: Buckhorn Creek**

Parameter	Cross Section 1 Riffle						Cross Section 2 Pool						Cross Section					
	MY1	MY2	MY3	MY4	MY5	MY+	MY1	MY2	MY3	MY4	MY5	MY+	MY1	MY2	MY3	MY4	MY5	MY+
Dimension																		
Bkf Width (ft)	20	23.7	23.7	23.3			22	23.4	23.5	23.5	23.5							
Floodprone Width (ft)	70	82	82	82			-	-	-	-	-							
Bkf Cross Sectional Area (ft ²)	35.4	35.3	31.3	32.8			48	46.8	48.4	47.2								
Bkf Mean Depth (ft)	1.5	1.5	1.3	1.4			2.2	2	2.1	2								
Bkf Max Depth (ft)	2.1	2.6	2.3	2.4			3.9	4.2	4.3	4.2								
Width/Depth Ratio	15.3	15.9	18	16.6			-	-	-	-								
Entrenchment Ratio	>3	>3	>3	>3			-	-	-	-								
Bank Height Ratio	1	1	1	1			-	-	-	-								
Wetted Perimeter (ft)																		
Hydraulic Radius (ft)																		
Substrate																		
D ₅₀ (mm)	26.5	4.7	36.6	38.7														
D ₈₄ (mm)	64	55	77	98														

Parameter	MY-1 (2006)						MY-2 (2007)						MY-3 (2008)						MY-4 (2009)						MY-5 (2010)						MY+ (2011)					
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med						
Pattern																																				
Beltwidth (ft)	40	115	65	40	115	65	40	115	65	40	115	65	40	115	65	40	115	65	40	115	65	40	115	65												
Radius of Curvature (ft)	29	371	105	29	371	105	29	371	105	29	371	105	29	371	105	29	371	105	29	371	105	29	371	105												
Meander Wavelength (ft)	125	320	180	125	320	180	125	320	180	125	320	180	125	320	180	125	320	180	125	320	180	125	320	180												
Meander Width Ratio	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25	2	5.75	3.25												
Profile																																				
Riffle Length (ft)	28	81	47	20.5	80.2	37.5	23	51	38	31.6	71.3	47.8																								
Riffle Slope (ft/ft)	0.0024	0.0126	0.0094	0	0.0212	0.0071	0.0004	0.0138	0.0042	0.003	0.0241	0.0113																								
Pool length (ft)	24.4	38	29.5	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-												
Pool Spacing (ft)	37	130	82	59.5	164	93	20	123.8	85.8	74.2	119.5	86.1																								
Additional Reach Parameters																																				
Valley Length (ft)	-	-	967	-	-	967	-	-	967	-	-	967	-	-	967	-	-	967	-	-	967	-	-	967												
Channel Length (ft)	-	-	1085	-	-	1085	-	-	1085	-	-	1085	-	-	1085	-	-	1085	-	-	1085	-	-	1085												
Sinuosity	-	-	1.1	-	-	1.1	-	-	1.1	-	-	1.1	-	-	1.1	-	-	1.1	-	-	1.1	-	-	1.1												
Water Surface Slope (ft/ft)	0.0024	0.0126	0.0094	0.0039	0.0081	-	0.0036	0.0042	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-												
Bkf Slope (ft/ft)	-	-	0.006	-	-	0.0056	-	-	0.0047	-	-	0.006	-	-	0.006	-	-	0.006	-	-	0.006	-	-	0.006												
Rosgen Classification	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c												
Habitat Index																																				
Macrobenthos																																				

Table X-f Morphology and Hydraulic Monitoring Summary
Holly Grove Stream Restoration Site (D06028-B)
Reach 6: Lower East Branch

Parameter	Cross Section 5 Riffle						Cross Section 6 Pool						Cross Section					
	MY1	MY2	MY3	MY4	MY5	MY+	MY1	MY2	MY3	MY4	MY5	MY+	MY1	MY2	MY3	MY4	MY5	MY+
Dimension																		
Bkf Width (ft)	7.1	8	7.7	6.5			12.1	9.2	10	10.8								
Floodprone Width (ft)	30	30	30	30			-	-	-	-								
Bkf Cross Sectional Area (ft ²)	2.7	3	2.9	2.6			11.5	10.2	10.3	10.5								
Bkf Mean Depth (ft)	0.4	0.4	0.4	0.4			1	1.1	1	1								
Bkf Max Depth (ft)	0.6	0.7	0.7	0.7			2.5	2	2.1	1.9								
Width/Depth Ratio	18.6	21.6	20.3	20.3			-	-	-	-								
Entrenchment Ratio	>3	>3	>3	>3			-	-	-	-								
Bank Height Ratio	1	1	1	1			-	-	-	-								
Wetted Perimeter (ft)																		
Hydraulic Radius (ft)																		
Substrate																		
D ₅₀ (mm)	9.8	0.1	0.1	0.1														
D ₈₄ (mm)	29	23	19	23														

Parameter	MY-1 (2006)						MY-2 (2007)						MY-3 (2008)						MY-4 (2009)						MY-5 (2010)						MY+ (2011)					
	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med	Min	Max	Med						
Pattern																																				
Beltwidth (ft)	16	17	16	16	16	16	16	17	16	16	16	16	16	17	16	16	16	16	16	17	16	16	16	16	16	17	16	16	16	16						
Radius of Curvature (ft)	-	-	193	-	193	-	-	-	193	-	193	-	-	-	193	-	193	-	-	-	193	-	193	-	-	-	193	-	193	-						
Meander Wavelength (ft)	-	-	87	-	87	-	-	-	87	-	87	-	-	-	87	-	87	-	-	-	87	-	87	-	-	-	87	-	87	-						
Meander Width Ratio	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3	2.3	2.4	2.3						
Profile																																				
Riffle Length (ft)	17.5	27	18.8	11.7	22.5	16.9	11.7	22.5	16.9	4	24	12	6.7	25.4	11.2																					
Riffle Slope (ft)	0.0037	0.0176	0.012	0.0107	0.0222	0.0107	0.0107	0.0222	0.0107	0.0125	0.0825	0.0149	0.0037	0.0245	0.018																					
Pool length (ft)	6.5	12.5	9.5	-	-	-	-	-	-	-	-	-	-	-	-																					
Pool Spacing (ft)	30	44	38.4	28.6	39.5	33.6	25	39	31.3	12	63.6	34.5																								
Additional Reach Parameters																																				
Valley Length (ft)	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4	-	-	207.4						
Channel Length (ft)	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7	-	-	209.7						
Sinuosity	-	-	1.0	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01	-	-	1.01						
Water Surface Slope (ft/ft)	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-						
Bkf Slope (ft/ft)	-	-	0.0104	-	-	0.0141	-	-	0.0141	-	-	0.0134	-	-	0.0102	-	-	0.0102	-	-	0.0102	-	-	0.0102	-	-	0.0102	-	-	0.0102						
Rosgen Classification	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c	-	-	B4c						
Habitat Index																																				
Macrobenthos																																				

APPENDIX A
VEGETATION RAW DATA



Vegetation Plot 1 – Year 4



Vegetation Plot 2– Year 4



Vegetation Plot 3– Year 4



Vegetation Plot 4– Year 4



Vegetation Plot 5– Year 4



Vegetation Plot 6– Year 4



Vegetation Plot 7– Year 4



Vegetation Plot 8– Year 4



Vegetation Plot A– Year 4



Vegetation Plot B– Year 4



Vegetation Plot C– Year 4

Plot (continued): E92523-01-VP1

Sep 2011 Data

THIS YEAR'S DATA

ID	Species	map char	source	X (m)	Y (m)	ddh (mm)	Height (cm)	DBH (cm)	Notes*	ddh (mm)	Height (cm)	DBH (cm)	Re-sprout	Vigor*	Damage*	Notes
----	---------	----------	--------	-------	-------	----------	-------------	----------	--------	----------	-------------	----------	-----------	--------	---------	-------

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP1

Party: Sheets, C
 Role: Roberts, J
 Date last planted: 9/13/12
 New planting date m/yy? 9/13/12
 Check box if plot was not sampled, specify reason below
 Notes: samp'd, specify reason below
Pink flagging photo: 8059
cms 3100 camera

VMD Year (1-5): 4 Date: 9/13/12 - 9/13/12
 Taxonomic Standard: _____
 Taxonomic Standard DATE: _____
 Latitude or UTM-N: 36.19963 Datum: NAD83/W
 (dec.deg. or m)
 Longitude or UTM-E: -79.58552 UTM Zone: 18Q
 Coordinate Accuracy (m): 10 X-Axis bearing (deg): 116
 Plot Dimensions: X: 10 Y: 10 Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Height 1cm*	DBH 1 cm	Notes*	Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
722	Salix nigra	<u>X</u> (f)	R	<u>7.0</u>	<u>1.9</u>	164.0	0.3	<input type="checkbox"/>	<u>249</u>	<u>1.0</u>	<input type="checkbox"/>	3	<u>INS/VINE</u>	
723	Quercus michauxii	<u>✓</u> (c)	R	2.3	7.8	65.0		<input type="checkbox"/>	<u>109</u>		<input type="checkbox"/>	3	<u>D/S INS</u>	<u>Alb?</u>
728	Quercus sp.	<u>M</u> (f)	R	7.0	1.9	54.0		<input type="checkbox"/>			<input type="checkbox"/>	M		
734	Corylus americana	<u>✓</u> (g)	R	7.5	0.0	150.0	0.2	<input type="checkbox"/>	<u>182</u>	<u>0.4</u>	<input type="checkbox"/>	3	<u>INS</u>	<u>5 maternal</u>
735	Ulmus alata	<u>✓</u> (h)	R	8.2	4.9	108.0	DBH?	<input type="checkbox"/>	<u>211</u>	<u>0.5</u>	<input type="checkbox"/>	3	<u>INS</u>	
738	Diospyros virginiana	<u>✓</u> (b)	R	1.9	5.2	85.0		<input type="checkbox"/>	<u>89</u>		<input type="checkbox"/>	3	<u>D/S</u>	
740	Platanus occidentalis var. occidentalis	<u>✓</u> (d)	R	2.7	0.0	282.0	1.4	<input type="checkbox"/>	<u>530</u>	<u>3.5</u>	<input type="checkbox"/>	3	<u>INS</u>	
741	Corylus americana	<u>✓</u> (e)	R	5.3	1.5	77.0		<input type="checkbox"/>	<u>89</u>		<input type="checkbox"/>	3	<u>D/S</u>	
886	Quercus pagoda	<u>✓</u> (a)	R	0.0	8.6	52.0		<input type="checkbox"/>	<u>54</u>		<input type="checkbox"/>	3	<u>D/S</u>	

stems: 9 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

Herbs: Microstegium, Impatiens, Goldenrod, Juncus, Andropogon
 Vines: Rubus, Lonicera

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
 ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.
 p. 1
 Printed in the CVS-EEP Entry Tool ver. 2.3.1

Plot (continued): **E92523-01-VP1**

Sep 2011 Data

THIS YEAR'S DATA

ID Species map source X Y ddh Height DBH Notes* ddh Height DBH Re-sprout Vigor* Damage* Notes
 char (m) (m) (mm) (cm) (cm) (mm) (cm) (cm) sprout

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>S. nigra</i>										
<i>L. styraciflua</i>										
<i>P. occidentalis</i>										
<i>D. virginiana</i>										
<i>L. tulipifera</i>										
<i>C. canadensis</i>										
<i>U. glabra</i>										

**Required if cut-off >10cm or subsample ? 100%.



Form WS2, ver 9.1

Corylus americana
R. multiflora
F. penn.
A. rubrum

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.


Map of stems on plot E92523-01-VP1

X-axis: 116°



stems: 9
map size:
LARGE

There are multiple stems represented by some letters, shown in bold on the map.

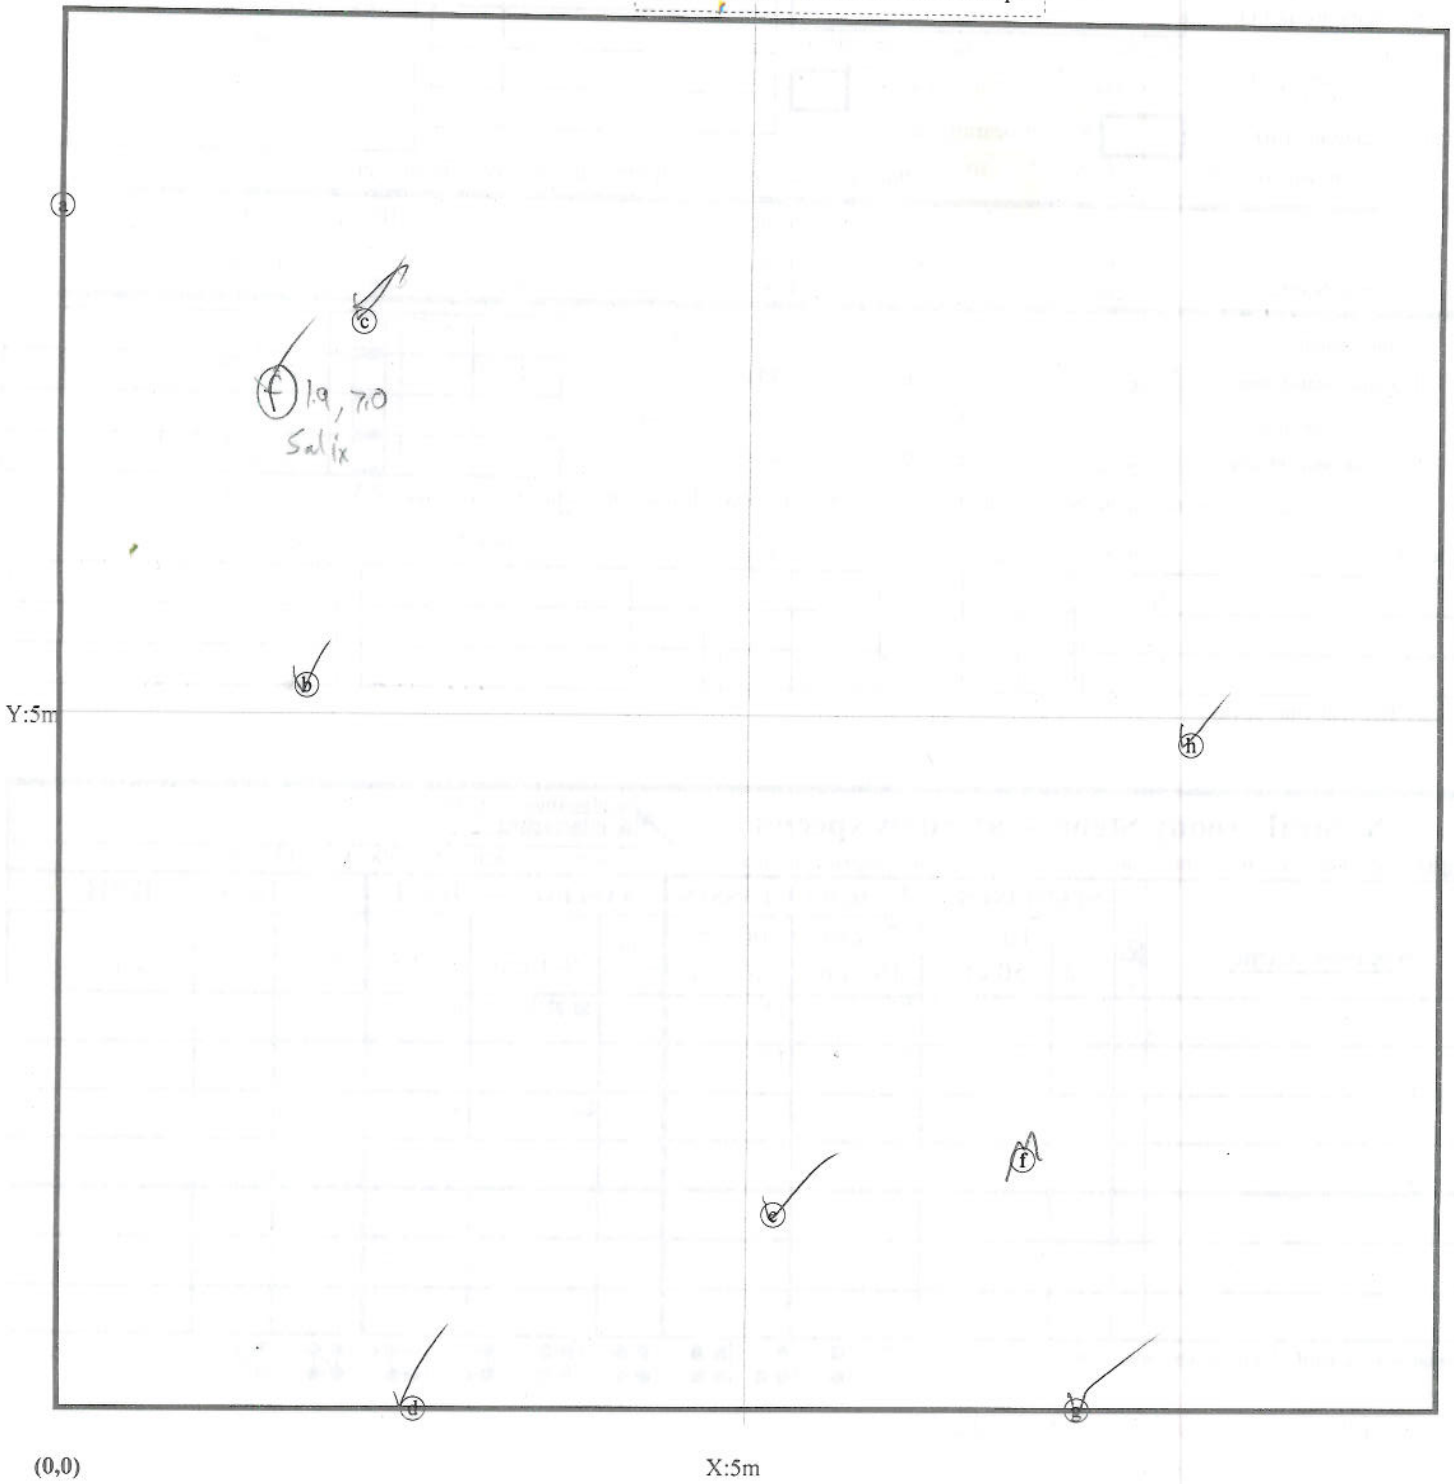

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 3
 *VIGOR: 4=excellent, 3=good, 2=fair, *DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
 1=unlikely to survive year, 0=dead, ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRricane, DISeased, VINE
 M=missing. Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP2

VMD Year (1-5): Date: -

Taxonomic Standard:

Taxonomic Standard DATE:

Latitude or UTM-N: Datum: (dec. deg. or m)

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party: Role:

Date last planted:

New planting date m/yy?

Check box if plot was not

Notes: sampled, specify reason below

*Pink flagging
Photo # 8061
Cms 0100*

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
600	Cornus amomum	(a)	R	2.2	3.4	131.0	DBH?	<input type="checkbox"/>	166	0.5	<input type="checkbox"/>	3	INS	
602	Fraxinus pennsylvanica	X (c)	R	7.5	3.6	80.0		<input type="checkbox"/>	84		<input type="checkbox"/>	3	TRAM	
603	Diospyros virginiana	Y (d)	R	9.4	0.6	9.0		<input checked="" type="checkbox"/>	24		<input type="checkbox"/>	3	0.5	
605	Fraxinus pennsylvanica	Y (b)	R	7.2	9.0	62.0		<input type="checkbox"/>	75		<input type="checkbox"/>	3	0.5	

stems: 4 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

*Notes by ID: 603-vine, disease

Natural Woody Stems - tallied by species										
Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>L. styraciflua</i>			1	1		1	1			
<i>F. pennsylvanica</i>				1						
<i>P. occidentalis</i>						1				
<i>C. caroliniana</i>										
<i>R. multiflora</i>						1				
<i>V. virginiana</i>										
<i>Rhus glabra</i>										

****Required if cut-off >10cm or subsample ? 100%.**

●1 ●2 ●3 ●4 ●5 ●6 ●7 ●8 ●9 ●10 Form WS2, ver 9.1

Herbs: Rubus, microstegium, Junco

Alexandria

L. tulipifera

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 4

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.


Printed in the CVS-EEP Entry Tool ver. 2.3.1

Map of stems on plot E92523-01-VP2

→ X-axis: 147°



stems: 4
map size:
LARGE

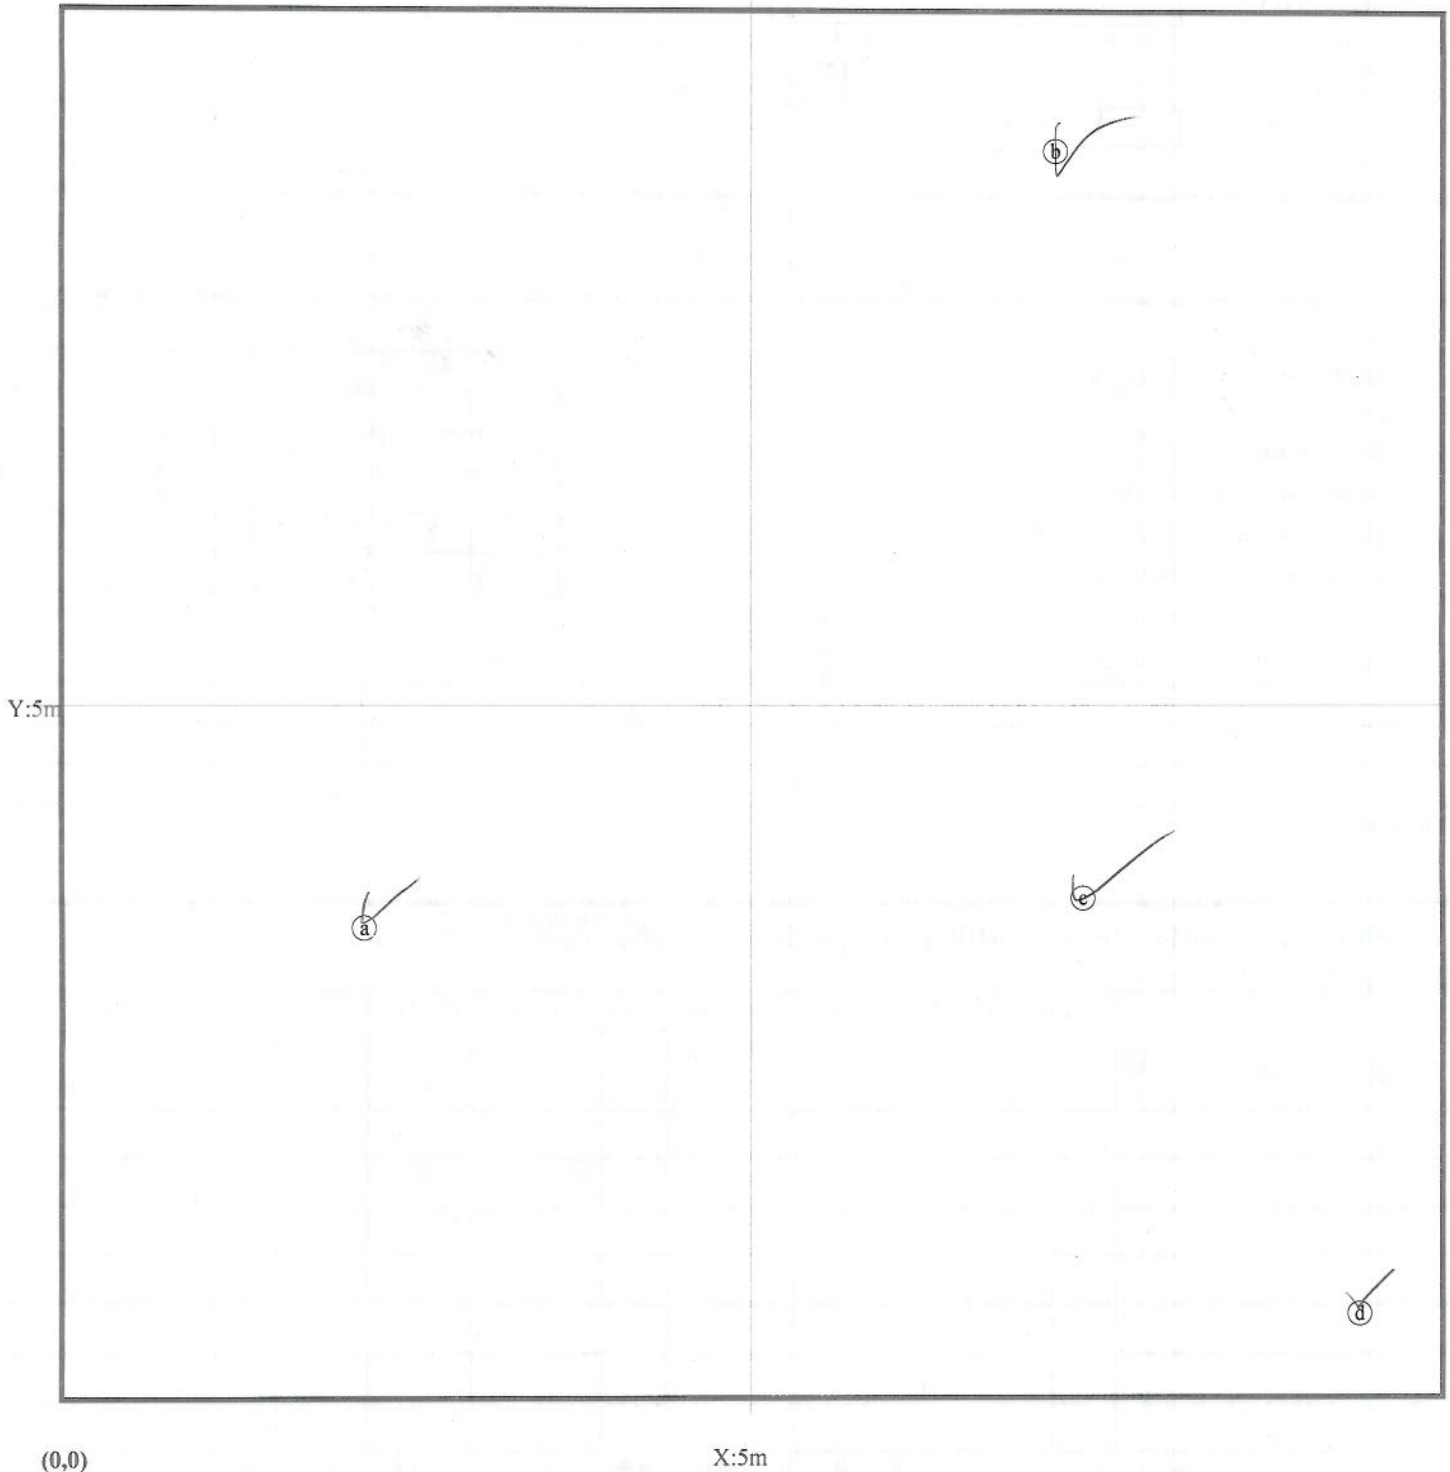

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

p. 5

*VIGOR: 4=excellent, 3=good, 2=fair,
1=unlikely to survive year, 0=dead,
M=missing.

*DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
ANIMAl, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRricane, DISeased, VINE
Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP3

VMD Year (1-5): Date: -

Taxonomic Standard: _____

Taxonomic Standard DATE: _____

Latitude or UTM-N: Datum: (dec. deg. or m)

Longitude or UTM-E: UTM Zone: (dec. deg. or m)

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role: _____

Date last planted: _____

New planting date m/yy?

Check box if plot was not sampled, specify reason below

Notes:

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
612	Fraxinus pennsylvanica	✓(a)	R	1.7	3.0	123.0	DBH?	✓	163	0.8	<input type="checkbox"/>	3	INS	BIS
613	Cornus amomum	✓(b)	R	1.8	5.3	161.0	0.4	<input type="checkbox"/>	216	0.8	<input type="checkbox"/>	3	INS	
614	Quercus michauxii	✓(c)	R	2.2	7.6	80.0		<input type="checkbox"/>	160	0.5	<input type="checkbox"/>	3	INS	VINE
616	Corylus americana	✓(f)	R	6.5	4.3	51.0		<input type="checkbox"/>	144	0.2	<input type="checkbox"/>	3	INS	
617	Viburnum dentatum var. dentatum	✓(e)	R	6.3	0.1	104.0	DBH?	<input type="checkbox"/>	117		<input type="checkbox"/>	3	INS	
619	Quercus michauxii	✓(g)	R	9.3	7.0	70.0		<input type="checkbox"/>	173	0.8	<input type="checkbox"/>	3	INS	
620	Cercis canadensis var. canadensis	✓(d)	R	4.5	6.0	107.0	DBH?	<input type="checkbox"/>	288	1.0	<input type="checkbox"/>	3	INS	

stems: 7 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1cm*	DBH 1 cm	Vigor*	Damage*	Notes

*Notes by ID: 612-disease

Natural Woody Stems - tallied by species										
Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>D. virginiana</i>	<input type="checkbox"/>									
<i>A. negundo</i>	<input type="checkbox"/>									
<i>F. pennsylvanica</i>	<input type="checkbox"/>									
<i>C. americana</i>	<input type="checkbox"/>									
<i>L. styraciflua</i>	<input type="checkbox"/>									

Explanation of cut-off & subsampling:** 10cm 50cm 100cm 137cm

**Required if cut-off >10cm or subsample ? 100%.

●1 ●2 ●3 ●4 ●5 ●6 ●7 ●8 ●9 ●10 Form WS2, ver 9.1

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 6

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.


*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Herbs: Rubus, Lonicera, Lonicera, Goldenrod, Pokeberry, Johnsongrass

Map of stems on plot E92523-01-VP3

→ X-axis: 236°

stems: 7
map size:
LARGE

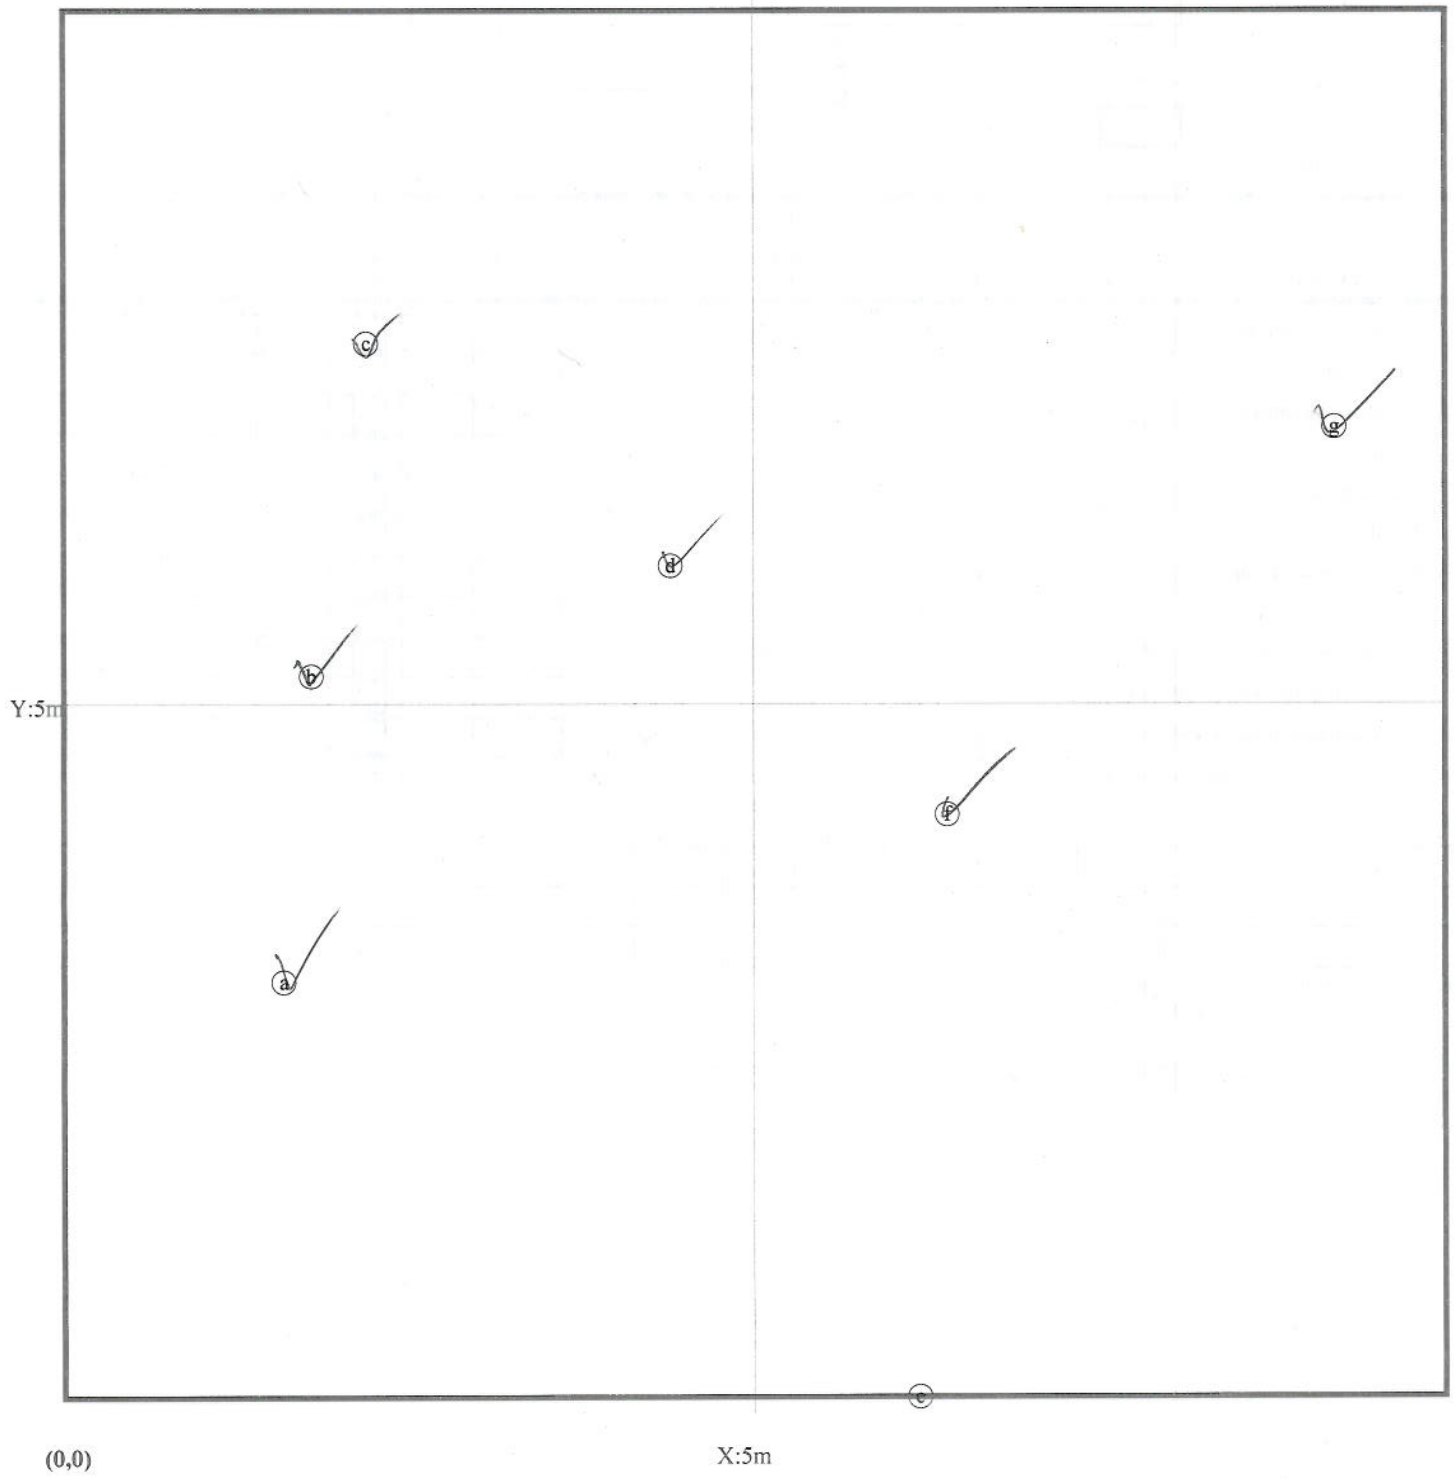

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 7
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP4

VMD Year (1-5): Date: -

Taxonomic Standard: _____
 Taxonomic Standard DATE: _____

Latitude or UTM-N: Datum: (dec. deg. or m)
 Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

 Role: _____
 Date last planted: _____
 New planting date m/yy?
 Check box if plot was not
 Notes: sampled, specify reason below

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
625	Diospyros virginiana	✓(b)	R	1.5	0.1	57.0			59			3	DIS	
626	Quercus phellos	✓(d)	R	2.3	2.9	50.0			58			3	DIS	
627	Diospyros virginiana	✓(f)	R	5.5	7.6	37.0			32			2	DIS INS	
629	Unknown sp.	✓(g)	R	6.2	4.4	Missing						M		
630	Betula nigra	✓(e)	R	5.3	1.7	129.0	DBH?		185	0.4		4		
631	Ilex decidua	✓(i)	R	7.0	1.4	49.0						0		
633	Fraxinus pennsylvanica	✓(k)	R	9.7	8.2	55.0		✓	72			3	DIS	
634	Diospyros virginiana	✓(j)	R	8.3	8.4	28.0			39			3	DIS	
635	Corylus americana	✓(c)	R	1.9	4.4	40.0			48			3	INS	
636	Cercis canadensis var. canadensis <i>Sweet gum</i>	(h)	R	6.5	2.1	Missing			41		✓	3	DIS	
909	Cercis canadensis var. canadensis	(a)	R	0.0 3.0	7.5	35.0		✓	50			3		

stems: 11 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes
Cercis can.		3.2	7.9	50		3	INS	


*Notes by ID: 633-did not measure resprout
 909-(New this year; the x is unknown)

Herbs: Andropogon, Goldenrod, Lonicera jap, Rubus

Map of stems on plot E92523-01-VP4

→ X-axis: 252°

stems: 11
map size:
LARGE

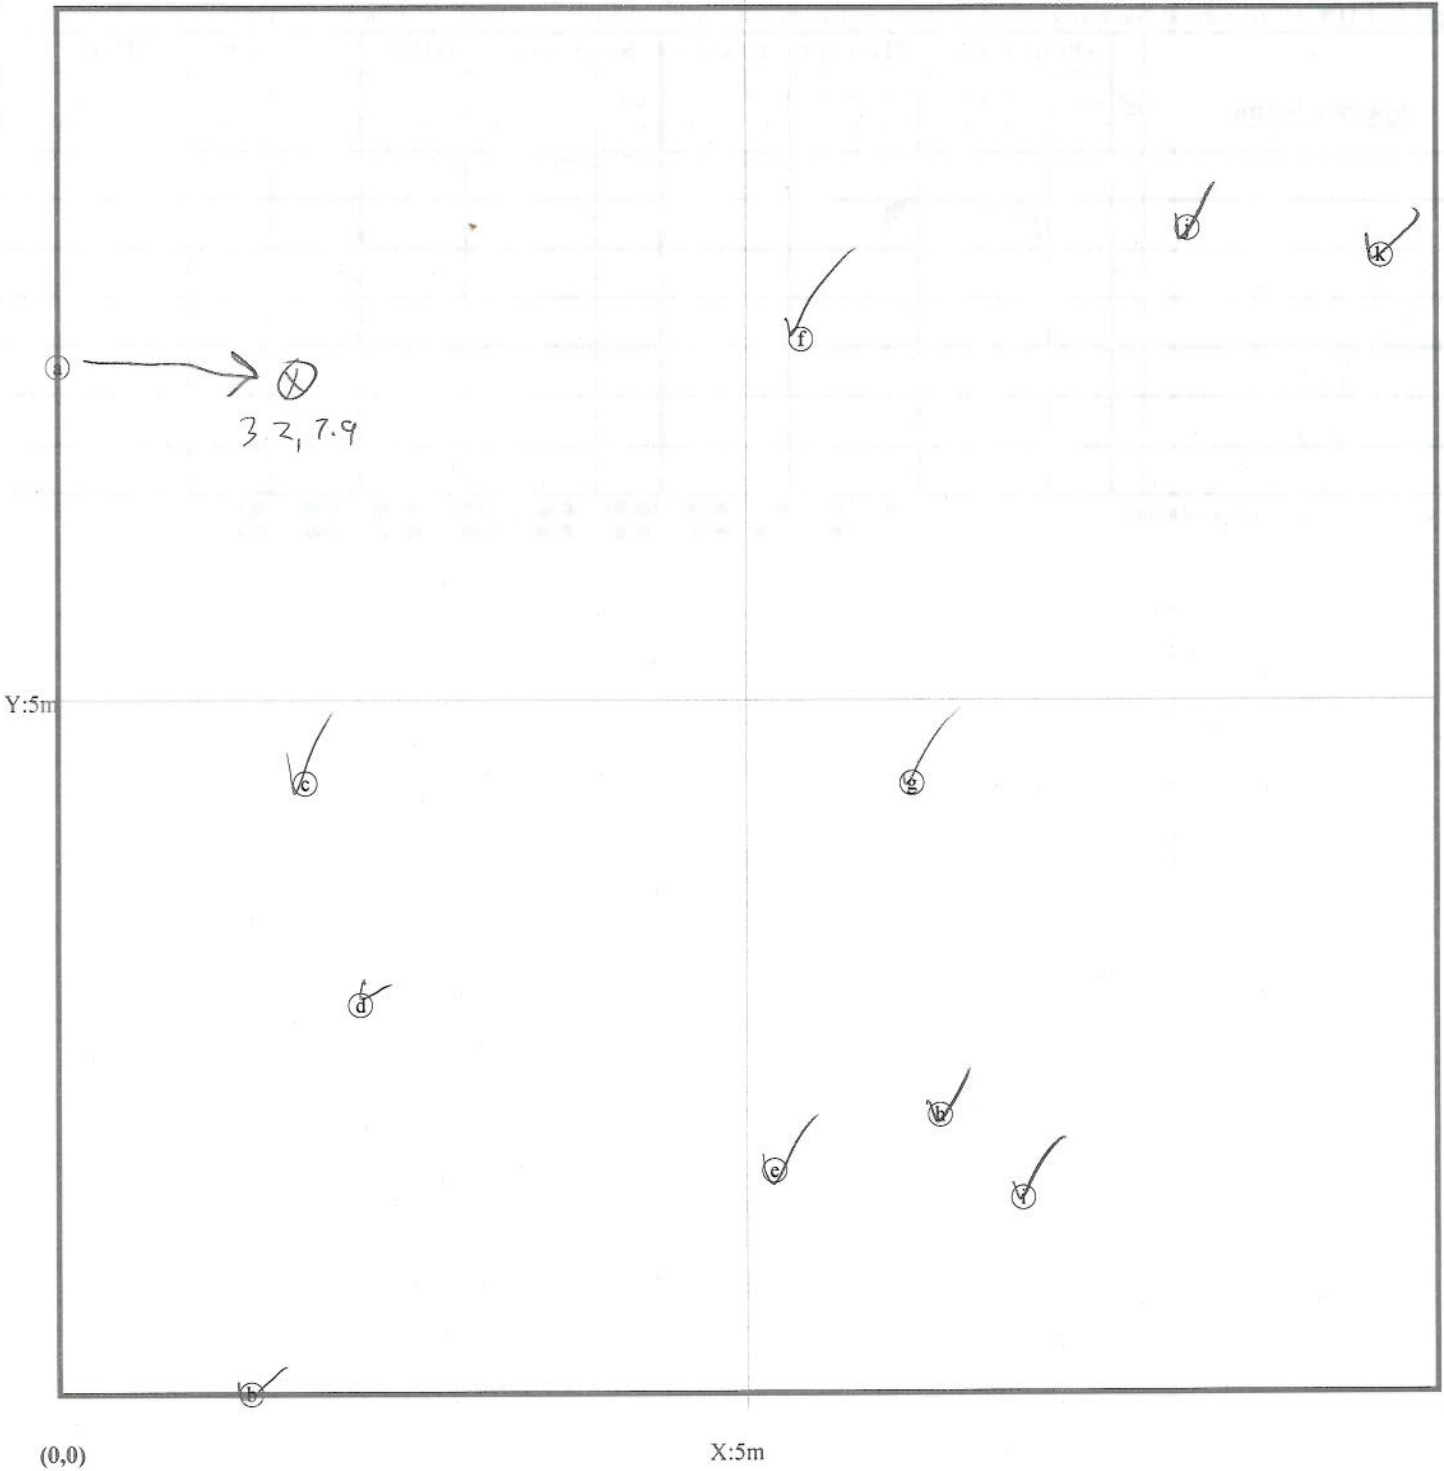

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

p. 10

*VIGOR: 4=excellent, 3=good, 2=fair,
1=unlikely to survive year, 0=dead,
M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCts, GAME, LIVESTock, Other/Unknown
ANIMal, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE
Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EEP Entry Tool ver. 2.3.1

Plot (continued): **E92523-01-VP4**

Sep 2011 Data

THIS YEAR'S DATA

ID	Species	map source char	X (m)	Y (m)	ddh (mm)	Height (cm)	DBH (cm)	Notes*	ddh (mm)	Height (cm)	DBH (cm)	Re-sprout	Vigor*	Damage*	Notes

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>L. styraciflua</i>		1	2			1	2			
<i>F. pennsylvanicus</i>		1	1			1				
<i>I. tree</i>										
<i>D. virginiana</i>										
<i>V. dentata</i>										
<i>V. virginiana</i>										
<i>C. americana</i>										

**Required if cut-off >10cm or subsample ? 100%.



Form WS2, ver 9.1

B. halimifolia

C. americana

Rhus winged

Q. phellos

Q. michauxii

L. tulipifera

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMOVAL, CUT, MOWING, BEAVER, DEER, RODENTS, INSECTS, GAME, LIVESTOCK, Other/Unknown ANIMAL, Human TRAMPLED, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICANE, DISEASED, VINE Strangulation, UNKNOW, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Plot E92523-01-VP5

VMD Year (1-5): Date: -

Taxonomic Standard:

Taxonomic Standard DATE:

Latitude or UTM-N: Datum: (dec.deg. or m)

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role:

Date last planted:

New planting date m/yy?

Check box if plot was not sampled, specify reason below

Notes:

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
647	Celtis laevigata	✓ c	R	7.5	0.2	123.0	DBH? ✓		172	0.3	<input type="checkbox"/>	3	INS	
648	Cercis canadensis var. canadensis	✓ d	R	8.0	0.9	104.0	DBH? ✓		124		<input type="checkbox"/>	3	INS	
649	Cercis canadensis var. canadensis	✓ e	R	8.4	3.5	162.0	0.3 <input type="checkbox"/>		190	0.7	<input type="checkbox"/>	3	INS D.S	
652	Quercus sp.	✓ b	R	5.3	9.2	60.0	<input type="checkbox"/>		111		<input type="checkbox"/>	3	INS	
655	Cornus amomum Cephaelis occ.	✓ a	R	0.6	9.7	165.0	0.5 ✓		193	0.7	<input type="checkbox"/>	3	INS D.S	

stems: 5 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

*Notes by ID: 647-insect
648-insects
655-diseased

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right): 10cm 50cm 100cm 137cm

Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm- 50 cm	50 cm- 100 cm	100 cm- 137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>P. occidentalis</i>	—				—					
<i>R. multiflora</i>	—				—	••				
<i>L. sinense</i>	—				—	•				
<i>J. nigra</i>	—				—	••	••			
<i>Cercis can.</i>	—				—		•			
<i>F. pennsylvanicum</i>	—	••	••	••	—	••				

**Required if cut-off >10cm or subsample >100%. Form WS2, ver 9.1


*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 11
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCTS, GAME, LIVESTock, Other/Unknown
 ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Herbs: *Lonicera* (dominant), Goldenrod, *R. kbus*, Johnsongrass (some treated), winged stem

Map of stems on plot E92523-01-VP5

X-axis: 286°

stems: 5
map size:
LARGE

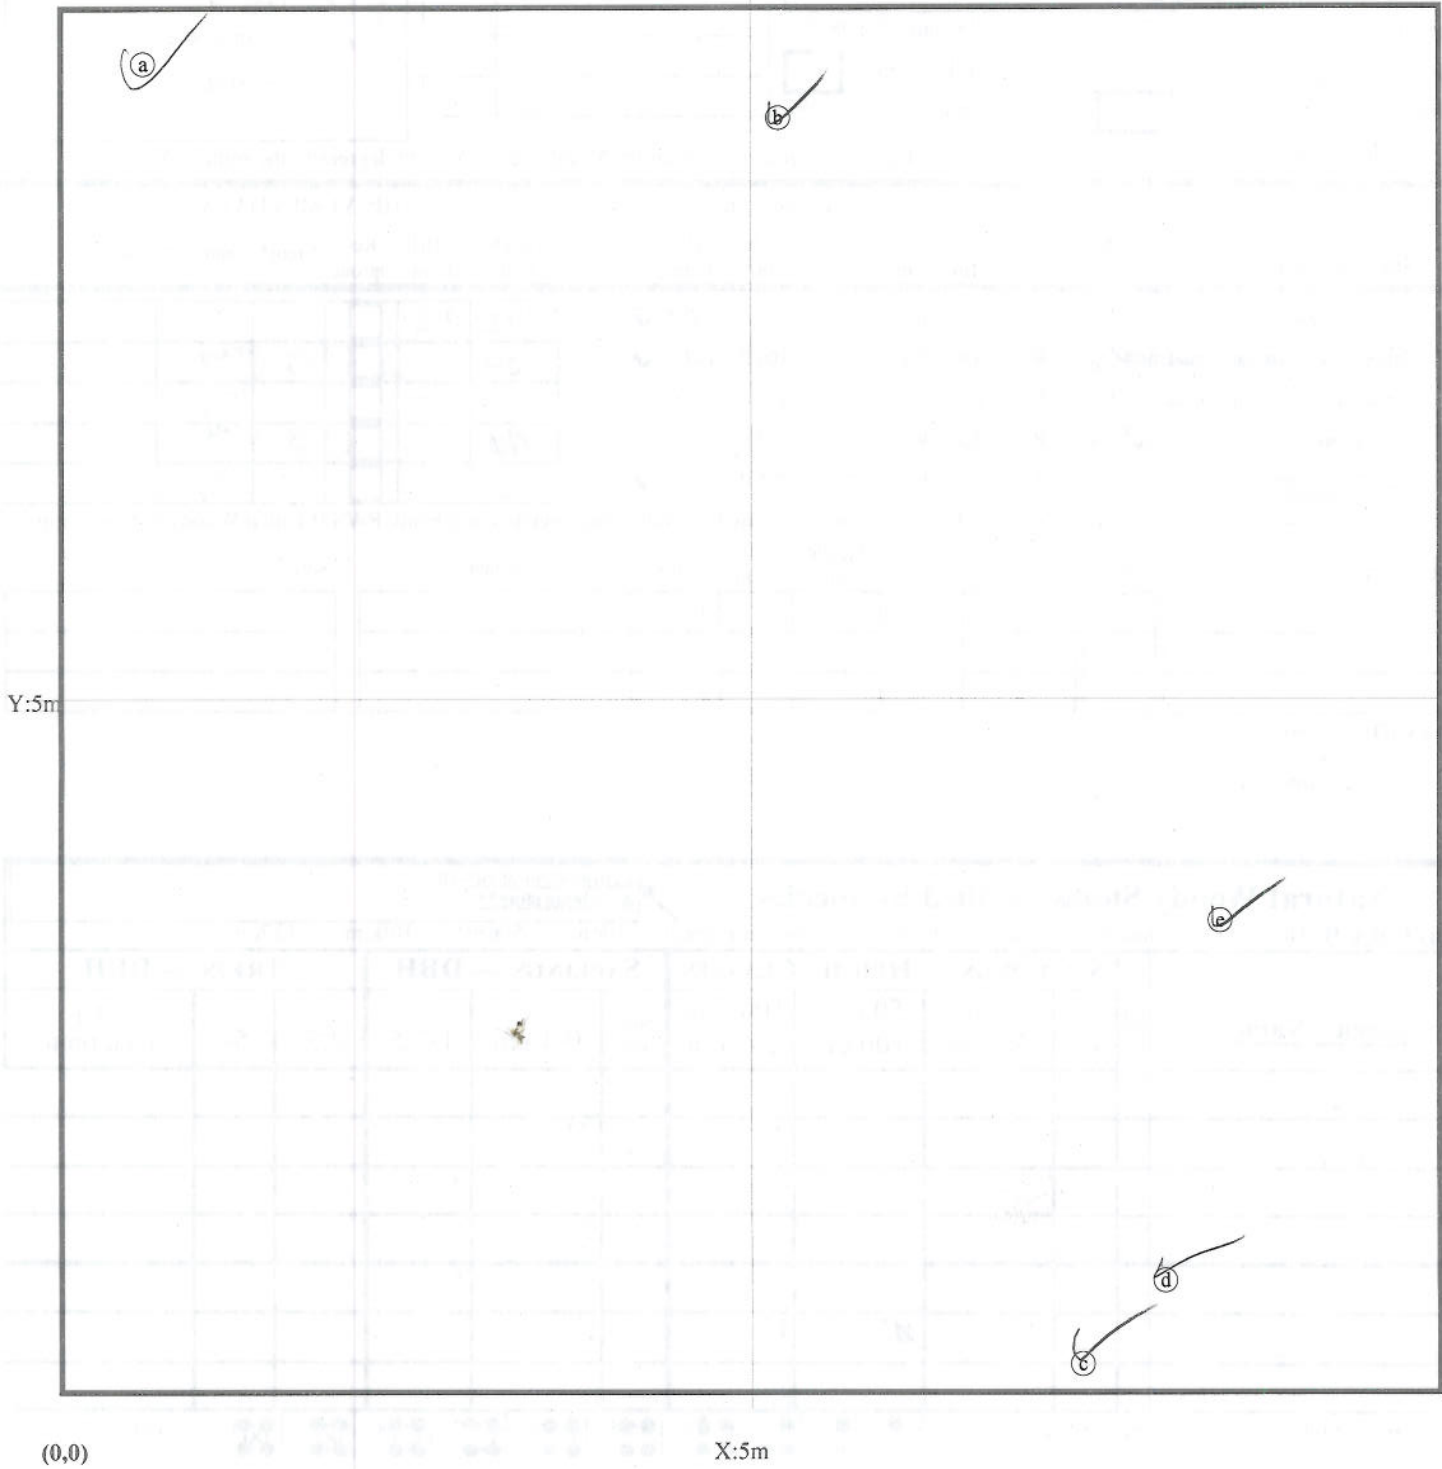

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 12
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE
Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP6

VMD Year (1-5): Date: -

Taxonomic Standard:

Taxonomic Standard DATE:

Latitude or UTM-N: Datum: (dec.deg. or m)

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role:

Date last planted:

New planting date m/yy?

Check box if plot was not

Notes: sampled, specify reason below

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
660	Quercus lyrata	X	(c)	R	1.7	1.6	92.0		161	0.4	<input type="checkbox"/>	4	INS	
662	Quercus lyrata	X	(i)	R	8.7	1.3	42.0		41		<input type="checkbox"/>	3	DEER	
663	Fraxinus pennsylvanica	X	(h)	R	7.7	4.3	52.0		78		<input type="checkbox"/>	3	INS	
664	Liriodendron tulipifera var. tulipifera	X	(f)	R	5.2	4.3	64.0		70		<input type="checkbox"/>	3	DIS	
665	Betula nigra	X	(d)	R	2.8	4.3	91.0		110		<input type="checkbox"/>	3	INS	
666	Platanus occidentalis var. occidentalis	X	(a)	R	0.7	4.4	41.0		69		<input type="checkbox"/>	3	INS DIS	
667	Platanus occidentalis var. occidentalis	X	(b)	R	1.3	7.1	95.0		110		<input type="checkbox"/>	3	INS	
668	Quercus lyrata	X	(e)	R	3.6	7.2	48.0		51		<input type="checkbox"/>	3	INS	
669	Fraxinus pennsylvanica	X	(g)	R	7.5	9.9	62.0		87		<input type="checkbox"/>	3	DIS	
672	Quercus lyrata	X	(i)	R	8.6	8.0	80.0		138	0.2	<input type="checkbox"/>	3	INS	

stems: 10 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes
<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>	<input type="text"/>

Herbs: Goldenrod, Andropogon

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 13
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCTS, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EPP Entry Tool ver. 2.3.1

Plot (continued): E92523-01-VP6		Sep 2011 Data			Notes*	THIS YEAR'S DATA					
ID	Species	map source char	X Y (m) (m)	ddh (mm)		Height (cm)	DBH (cm)	ddh (mm)	Height (cm)	DBH (cm)	Re-sprout

Natural Woody Stems - tallied by species Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	<input checked="" type="checkbox"/> Sub-seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-5-	5-10 (write DBH)	
<i>F. per...</i>	—				—					
<i>S. nigra</i>	—				—					
<i>L. tulipifera</i>	—				—					
<i>P. occidentalis</i>	—				—					
	—				—					
	—				—					
	—				—					

**Required if cut-off >10cm or subsample ? 100%. ●1 ●2 ●3 ●4 ●5 ●6 ●7 ●8 ●9 ●10 Form WS2, ver 9.1

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 14

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRricane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1


Map of stems on plot E92523-01-VP6

→ X-axis: 184°

stems: 10

map size:

LARGE

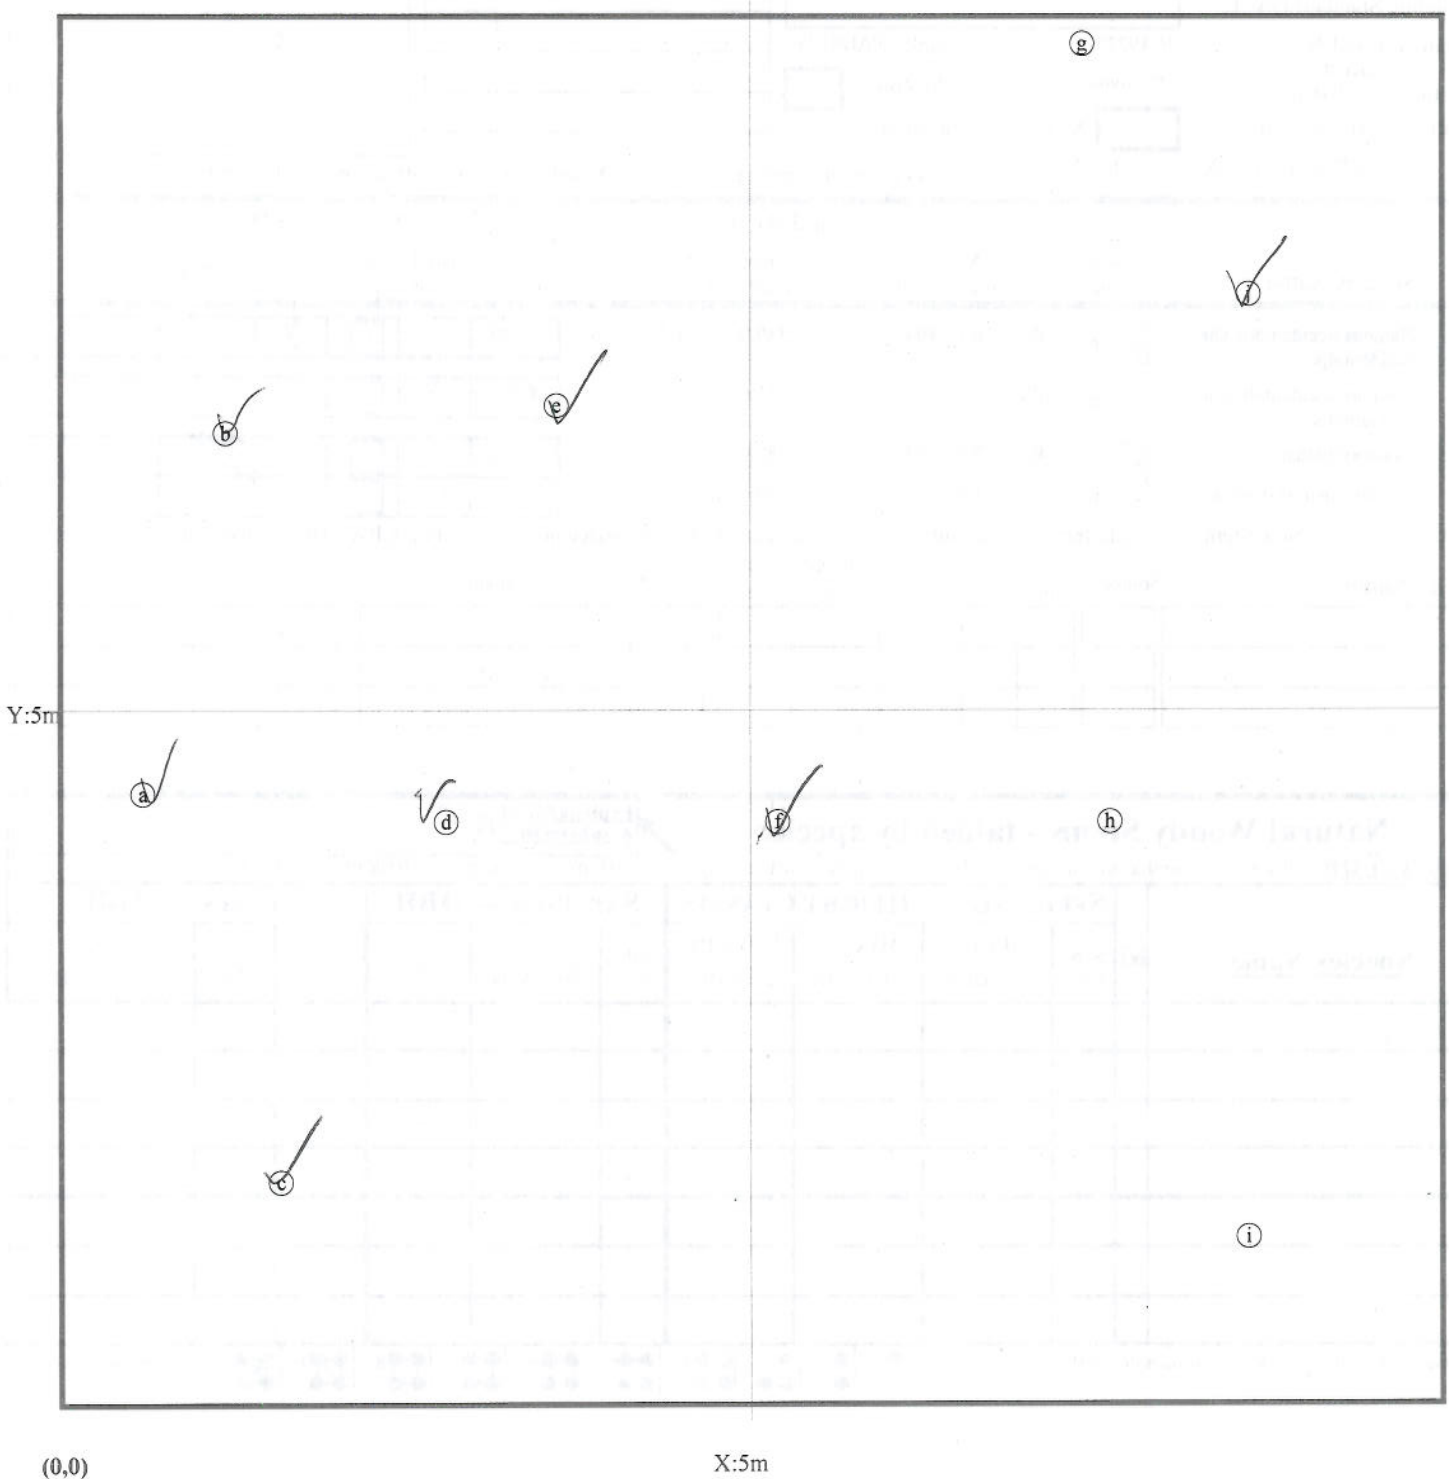

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

p. 15

*VIGOR: 4=excellent, 3=good, 2=fair,
1=unlikely to survive year, 0=dead,
M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
ANIMal, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRricane, DISeased, VINE
Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VP7

VMD Year (1-5): Date: -

Taxonomic Standard: _____
 Taxonomic Standard DATE: _____

Latitude or UTM-N: Datum:
 (dec.deg. or m)

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role: _____

Date last planted: _____
 New planting date m/yy?

Check box if plot was not
 Notes: sampled, specify reason below

pink flagging photo # 9066 CMS 8100

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
675	Platanus occidentalis var. occidentalis	✓ (a)	R	0.1	10.0	330.0	2.9		470	6.5		3	0.5 INS	
676	Platanus occidentalis var. occidentalis	✗ (d)	R	8.7	2.3	254.0	1.4		345	3.0		3	0.5 INS	
677	Nyssa sylvatica	✗ (c)	R	7.7	6.0	82.0			104			3	DEER INS	
933	Fraxinus pennsylvanica	✓ (b)	P	1.0	1.5	69.0			150	0.3		3	0.5 INS	

stems: 4 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

Natural Woody Stems - tallied by species										
Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): <input type="checkbox"/> 10cm <input type="checkbox"/> 50cm <input type="checkbox"/> 100cm <input type="checkbox"/> 137cm										
Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>P. occidentalis</i>										

****Required if cut-off >10cm or subsample >100%.**

●1 ●2 ●3 ●4 ●5 ●6 ●7 ●8 ●9 ●10

Form WS2, ver 9.1


*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 16
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCTS, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EPP Entry Tool ver. 2.3.1

*Herbs: Goldenrod, Johnson grass, Andropogon, Juncus
 ↳ some treated*

Map of stems on plot E92523-01-VP7

→ X-axis: 250°

stems: 4
map size:
LARGE

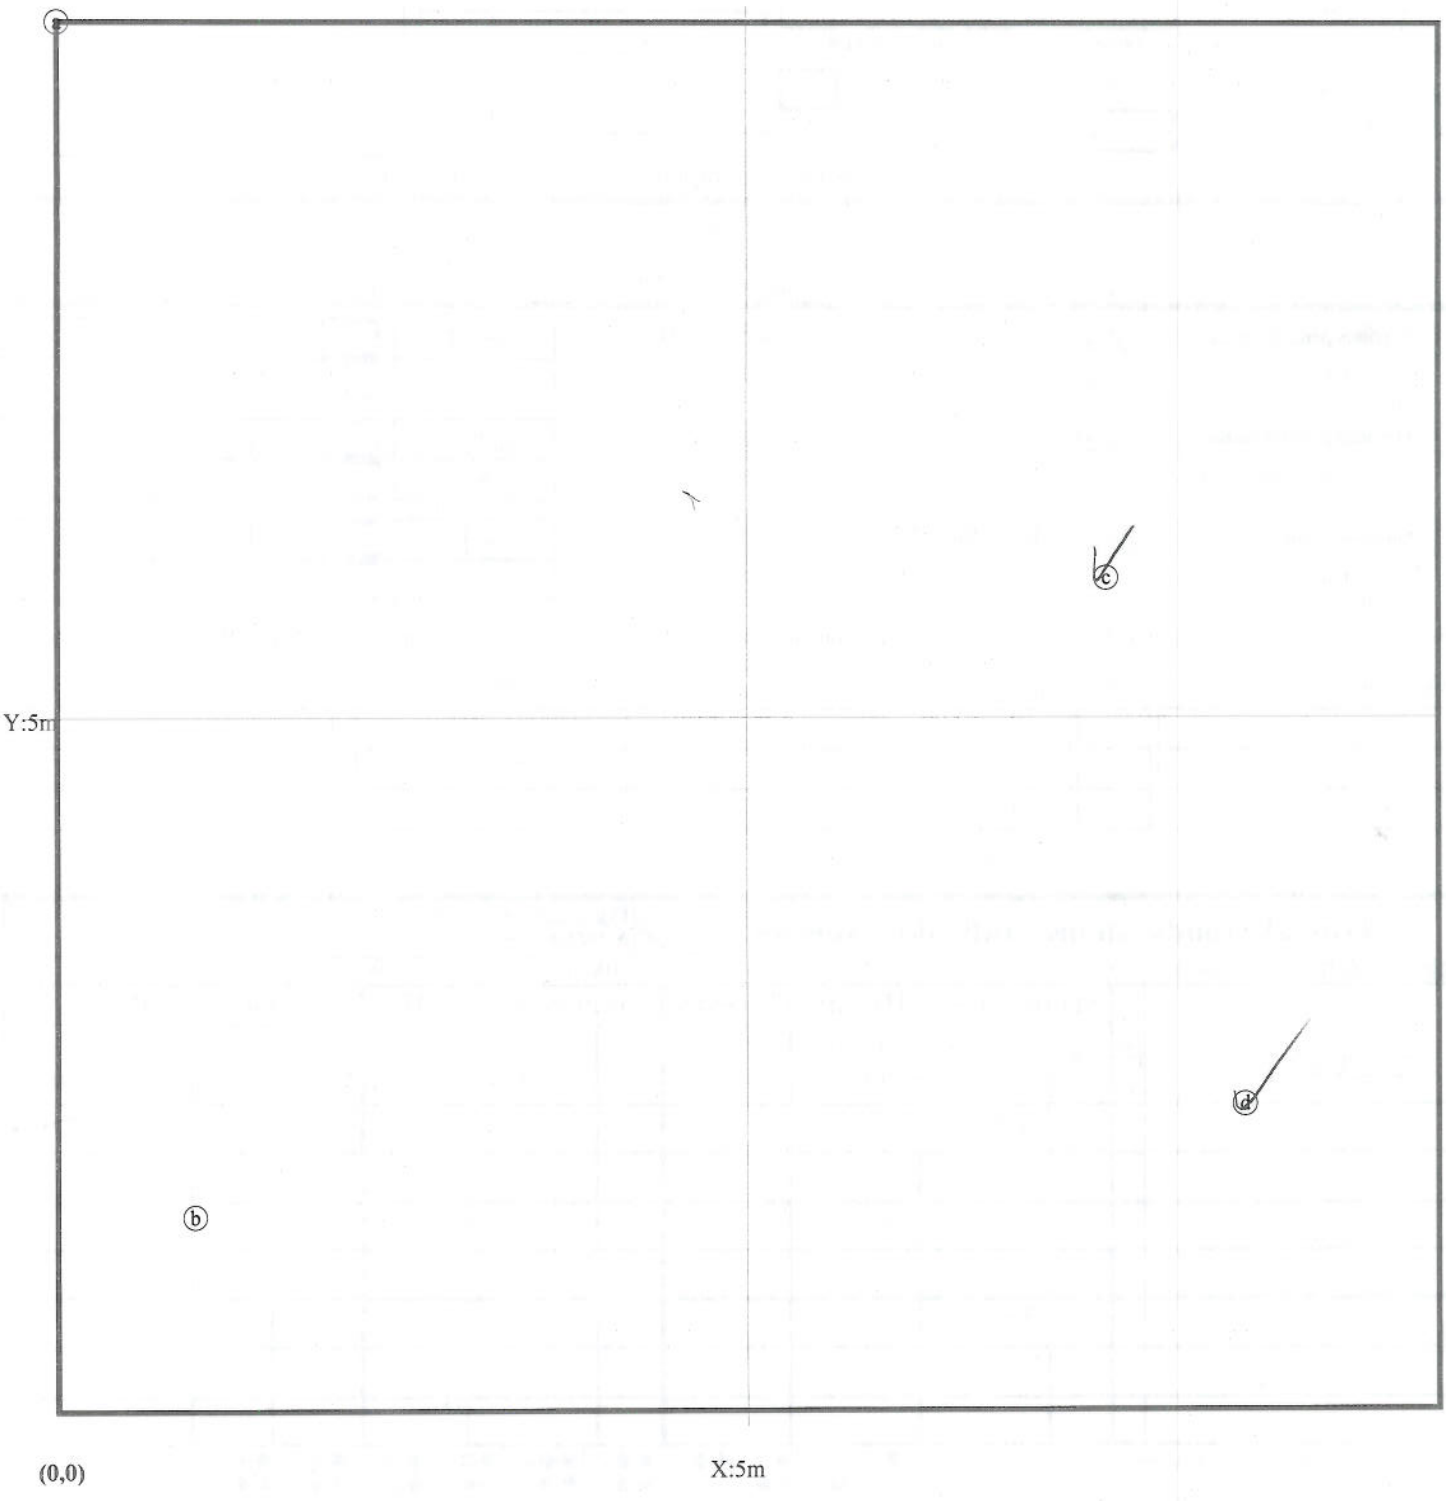

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 17
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot **E92523-01-VP8**

VMD Year (1-5): **4** Date: **9/13/12 - 9/13/12**

Taxonomic Standard:

Taxonomic Standard DATE:

Latitude or UTM-N: **36.18998**

Longitude or UTM-E: **-79.57815**

Coordinate Accuracy (m):

Plot Dimensions: X: **10** Y: **10**

Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party: **Sheats, C**

Role:

Date last planted:

New planting date m/y/y? **1**

Check box if plot was not

Notes: sampled, specify reason below

*Pink flags
photo # 8069
Cms 8100*

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
679	Fraxinus pennsylvanica	✓(a)	R	2.3	1.5	201.0	0.8		299	1.3		3	INS DIS	
680	Liriodendron tulipifera var. tulipifera	✓(d)	R	6.3	2.5	177.0	0.8		329	2.0		3	INS DIS	
681	Fraxinus pennsylvanica	✓(f)	R	9.0	3.7	241.0	1.0		330	1.4		3	INS DIS	
682	Liriodendron tulipifera var. tulipifera	✓(e)	R	8.0	6.2	191.0	1.0		260	1.4		3	INS DIS	
683	Quercus lyrata	✓(c)	R	5.6	7.9	54.0			74			3	INS DIS	
684	Liriodendron tulipifera var. tulipifera	✓(b)	R	4.2	10.0	138.0	0.3		154	0.3		3	INS DIS	Top Dead

stems: 6 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

N. sylvatica 4.5 DBH, >50

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>L. styraciflua</i>		☒☒	☒							10, 12, 10, 15
<i>A. rubrum</i>										
<i>L. tulipifera</i>		☒☒	☒							
<i>L. opaca</i>		☒								
<i>Q. sp</i>		☒☒								
<i>F. pennsylvanica</i>		☒☒								
<i>Ailanthus</i>										

**Required if cut-off >10cm or subsample >100%.



Form WS2, ver 9.1

P. occidentalis

Carya alba

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 18

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EPP Entry Tool ver. 2.3.1

Herbs: Microstegium, Dog fennel, Andropogon

Ulmus alata


Sami. canadensis

Map of stems on plot E92523-01-VP8

X-axis: 132°



stems: 6
map size:
LARGE

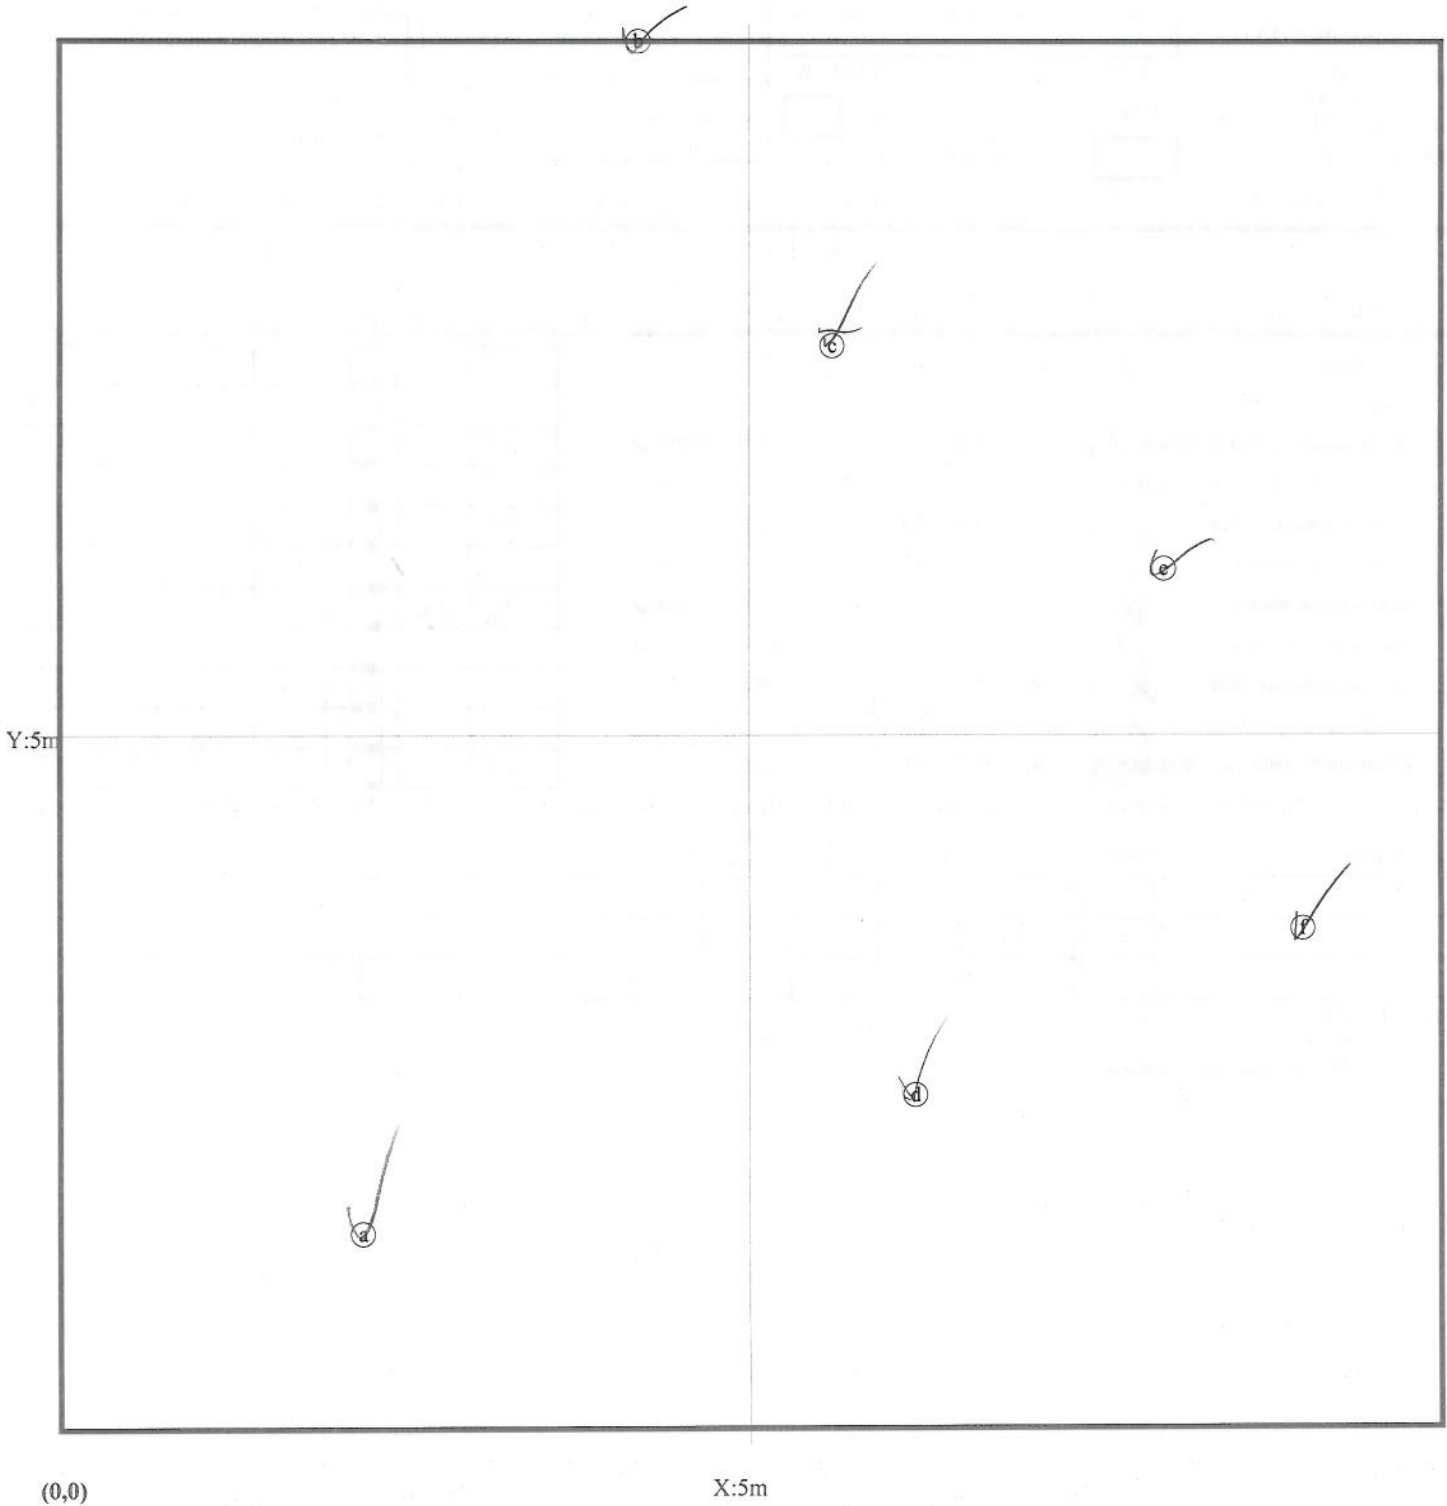

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 19
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
 ANIMal, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRricane, DISeased, VINE
 Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VPA

VMD Year (1-5): Date: -

Taxonomic Standard: _____

Taxonomic Standard DATE: _____

Latitude or UTM-N: Datum: (dec. deg. or m)

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role: _____

Date last planted: _____

New planting date m/yy?

Check box if plot was not

Notes: sampled, specify reason below

Pink flagging
Photo: 8060
CMS #100

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
578	Quercus sp.	✓(j)	R	8.7	8.0	56.0			89			3	DIS	
579	Diospyros virginiana	✓(i)	R	8.4	9.1	60.0			138	0.3		3	INS	
580	Cercis canadensis var. canadensis	✓(g)	R	7.2	5.7	116.0	DBH? ✓		123			3	INS DIS	
581	Viburnum dentatum var. dentatum	✓(e)	R	4.3	5.2	177.0	0.4		225	1.0		4	INS	
582	Fraxinus pennsylvanica	✓(b)	R	1.7	5.3	83.0			95			2	INS	
584	Sambucus canadensis	✓(d)	L	3.1	0.1	187.0	0.6					0		
585	Sambucus canadensis	✓(c)	L	2.1	0.1	137.0	0.5 ✓		186	0.6		3	INS DIS	
586	Sambucus canadensis	✓(a)	L	1.7	0.1	105.0	DBH? ✓					0		
589	Fraxinus pennsylvanica	✓(f)	R	6.0	3.6	74.0			67			1		NO LEAVES
590	Fraxinus pennsylvanica	✓(h)	R	8.1	3.5	67.0			71			3	INS DIS	
591	Viburnum dentatum var. dentatum	✓(k)	R	9.7	0.6	62.0			65			3	DIS	smothered

stems: 11 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1 cm*	DBH 1 cm	Vigor*	Damage*	Notes

*Notes by ID: 580-yr2: insects | yr3: vine
585-insect
586-top dead, insect damage

Herbs: Goldenrod, winged stem, Johnson grass
Vines: Rubus (don), Lonicera

Plot (continued): **E92523-01-VPA**

Sep 2011 Data

THIS YEAR'S DATA

ID	Species	map char	source X (m)	Y (m)	ddh (mm)	Height (cm)	DBH (cm)	Notes*	ddh (mm)	Height (cm)	DBH (cm)	Re-sprout	Vigor*	Damage*	Notes

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	c	SEEDLINGS — HEIGHT CLASSES				SAPLINGS — DBH			TREES — DBH							
		Sub-Seed	10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)					
<i>V. dentatum</i>																
<i>S. canadensis</i>																
<i>L. styraciflua</i>																
<i>C. caroliniana</i>																
<i>L. tulipifera</i>																
<i>P. occidentalis</i>																
<i>A. phellos</i>																

**Required if cut-off >10cm or subsample ? 100%

●1 ●2 ●3 ●4 ●5 ●6 ●7 ●8 ●9 ●10

Form WS2, ver 9.1

D. virginiana

Ulmus rubra

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROught, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.


*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Map of stems on plot E92523-01-VPA

→ X-axis: 152°



stems: 11
map size:
LARGE

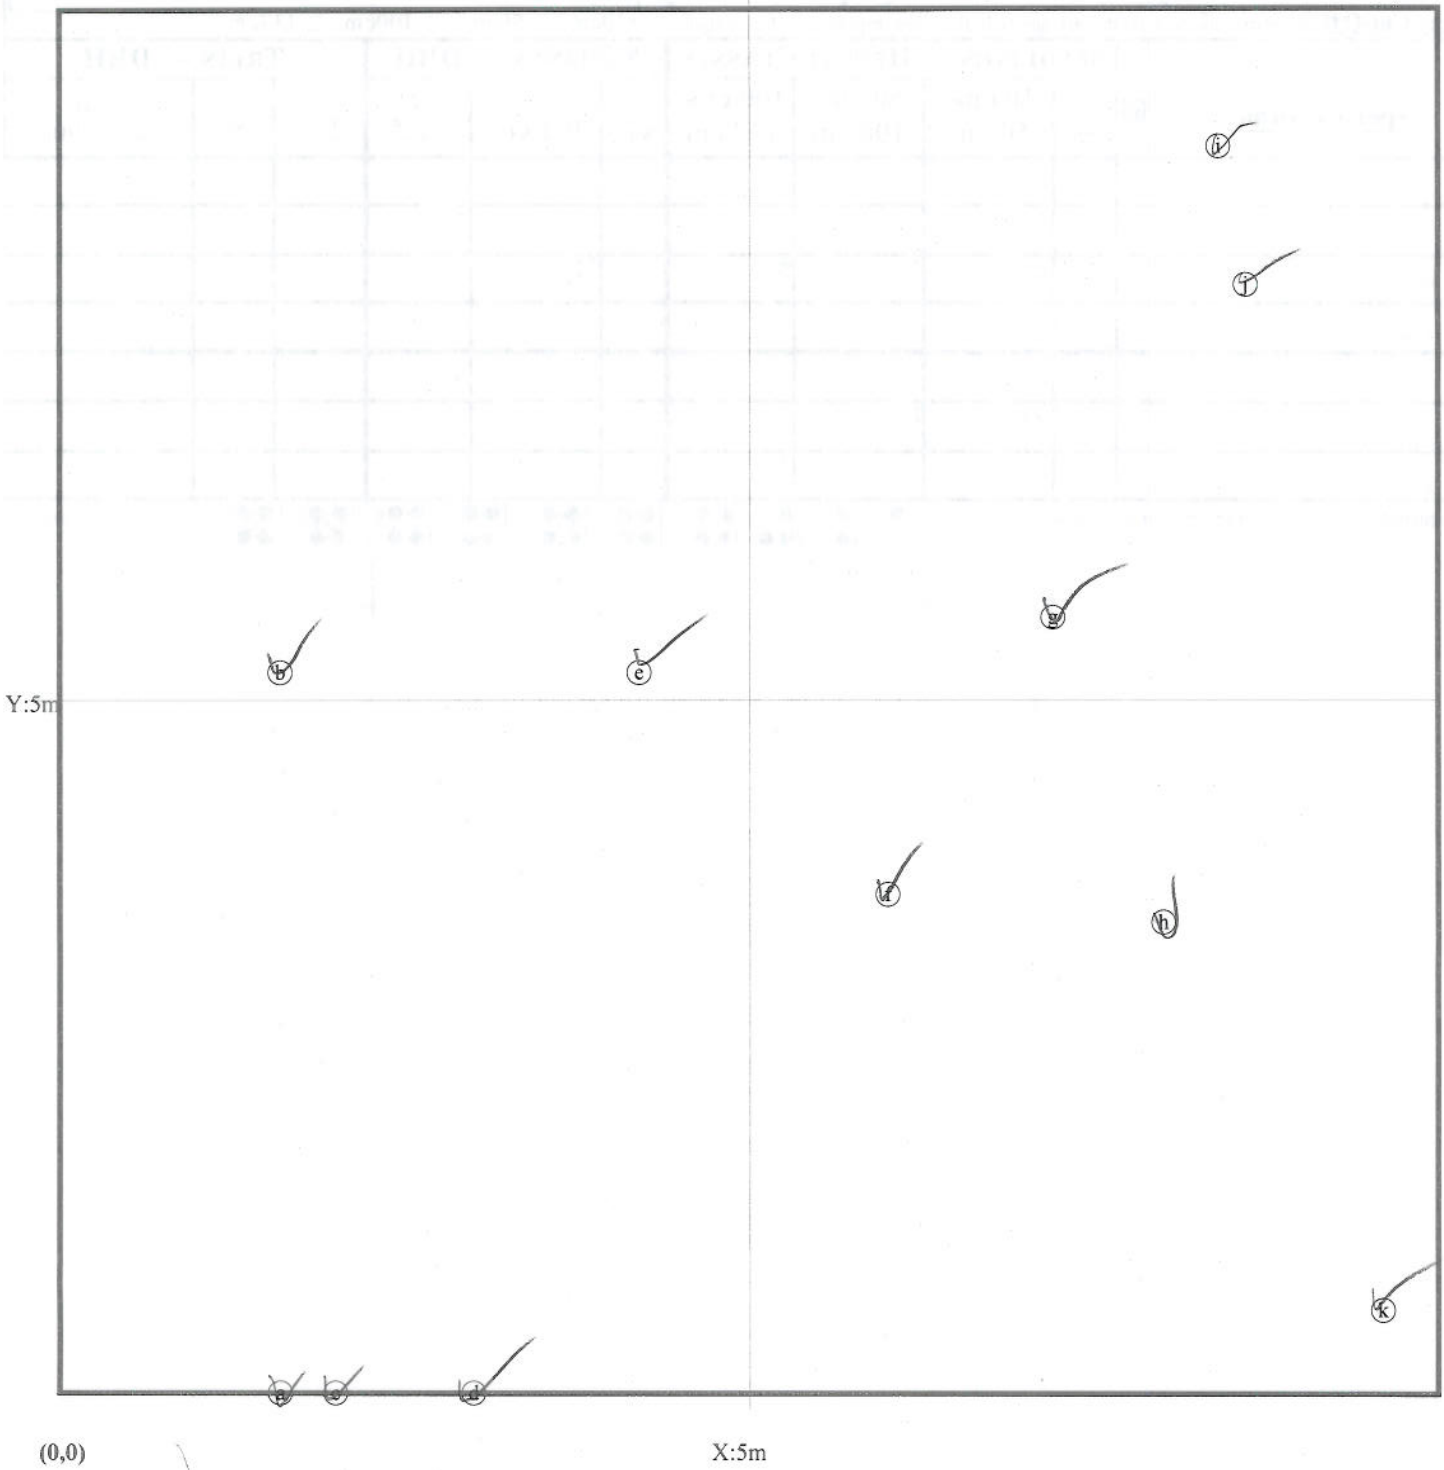

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 22
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMal, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRIcane, DISeased, VINE Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot E92523-01-VPB

VMD Year (1-5): 1 2 3 4 5 Date: 9/13/12 - 9/13/12

Taxonomic Standard: _____
 Taxonomic Standard DATE: _____

Latitude or UTM-N: 36.19282 Datum: NAD83/W
 (dec.deg. or m)
 Longitude or UTM-E: -79.57080 UTM Zone: _____

Coordinate Accuracy (m): _____ X-Axis bearing (deg): 266

Plot Dimensions: X: 10 Y: 10 Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party: _____ Role: _____ Date last planted: _____

New planting date m/yy? 1 2 3 4 5 6 7 8 9 10

Check box if plot was not sampled

Notes: sampled, specify reason below

Pin & Flag's photo # 8067

ID	Species Name	Map char	Source*	X 0.1m	Y 0.1m	Sep 2011 Data		Notes*	THIS YEAR'S DATA					
						Height 1cm*	DBH 1 cm		Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
951	Fraxinus pennsylvanica	✓(a)	R	1.8	1.7	86.0		✓	123		<input type="checkbox"/>	3	DIS	
952	Fraxinus pennsylvanica	✓(b)	R	1.8	4.3	94.0		✓	163	0.9	<input type="checkbox"/>	3	DIS	
953	Fraxinus pennsylvanica	✓(c)	R	1.9	6.7	140.0	0.7	✓	219	1.3	<input type="checkbox"/>	3	DIS	
954	Unknown sp.	✓(h)	U	4.7	9.2	Missing		✓			<input type="checkbox"/>	M		
955	Unknown sp.	✓(g)	U	4.4	7.1	Missing		✓			<input type="checkbox"/>	M		
956	Unknown sp.	✓(f)	U	4.4	4.7	Missing		✓			<input type="checkbox"/>	M		
957	Nyssa sylvatica	✓(e)	R	4.4	2.6	63.0		✓	127		<input type="checkbox"/>	3	DIS	
958	Nyssa sylvatica	✓(d)	R	4.4	0.3	82.0		✓	100		<input type="checkbox"/>	3	DIS	
959	Fraxinus pennsylvanica	✓(i)	R	6.8	4.2	157.0	0.6	✓	253	1.5	<input type="checkbox"/>	3	DIS	
960	Nyssa sylvatica	✓(j)	R	6.8	6.7	98.0		✓	102		<input type="checkbox"/>	3	DEER	
962	Fraxinus pennsylvanica	✓(m)	R	9.0	7.6	124.0	DBH?	✓	202	1.2	<input type="checkbox"/>	3	DIS	
963	Corylus americana	✓(l)	R	9.0	3.1	92.0		✓	198	0.5	<input type="checkbox"/>	3	DIS	
964	Corylus americana	✓(k)	R	9.0	0.9	65.0		✓	117		<input type="checkbox"/>	3	DIS	

stems: 13 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1cm*	DBH 1 cm	Vigor*	Damage*	Notes

***Notes by ID:** 951-Stem ID 501
 952-Stem ID 502
 953-Stem ID 503
 954-504
 955-505
 956-506
 957-507
 958-508
 959-510
 960-511
 962-514
 963-516
 964-517

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown
 *VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.
 *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.
 Herbs: Rubus, Goldenrod, Junco

Plot (continued): **E92523-01-VPB**

Sep 2011 Data

Notes*

THIS YEAR'S DATA

ID Species

map source X Y
char (m) (m)

ddh Height DBH
(mm) (cm) (cm)

ddh Height DBH Re- Vigor* Damage* Notes
(mm) (cm) (cm) sprout

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	Sub-Seed	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH		
		10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)
<i>F. pennsylvanica</i>				••		••	••	••		
<i>A. rugosa</i>				•		••	•			
<i>S. nigra</i>							••			
<i>L. styraciflua</i>							•			
<i>C. canadensis</i>						••				
<i>P. occidentalis</i>							•			
<i>Corylus amer.</i>						•				

**Required if cut-off >10cm or subsample ? 100%.



Form WS2, ver 9.1

S. canadensis

--	--	--	--	--	--	--	--	--	--	--

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing.

*DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.


*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Map of stems on plot E92523-01-VPB

→ X-axis: 266°

stems: 13

map size:
LARGE

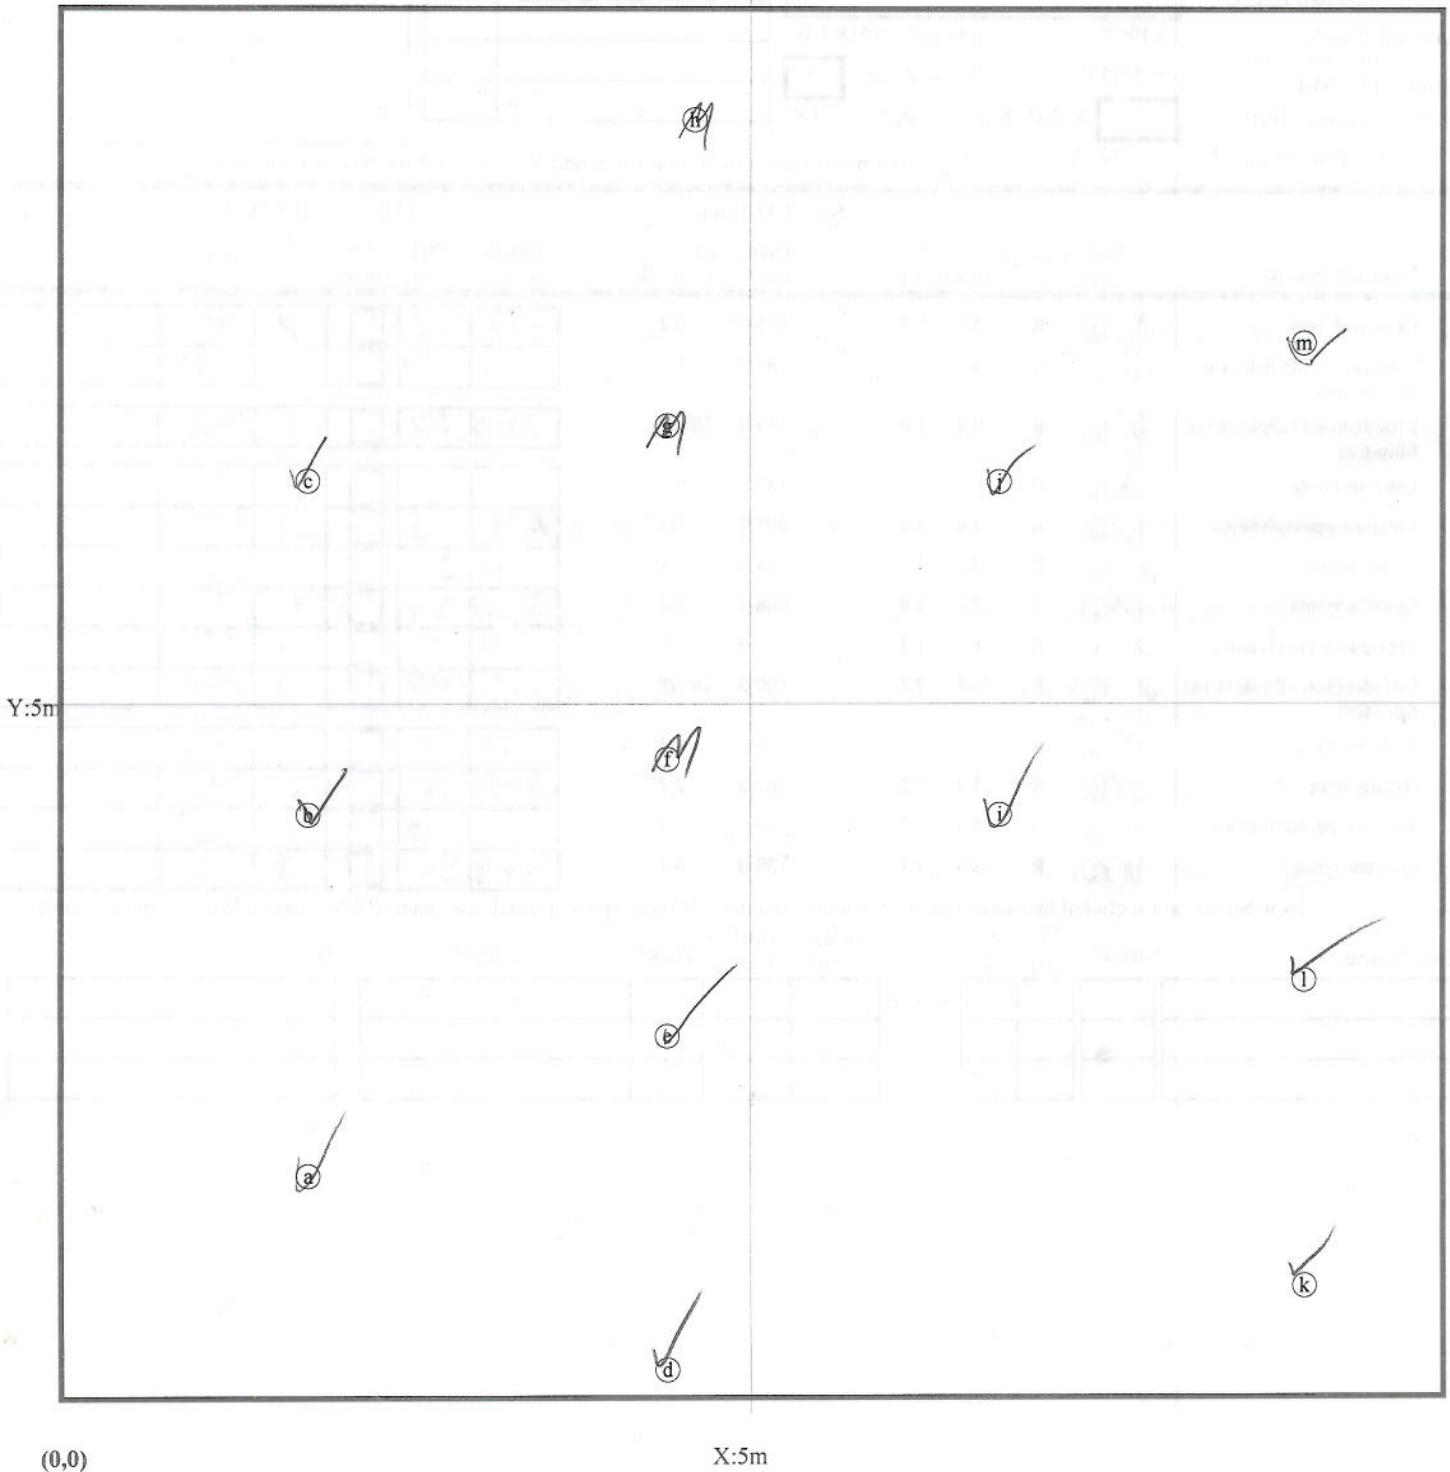

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

p. 25

*VIGOR: 4=excellent, 3=good, 2=fair,
1=unlikely to survive year, 0=dead,
M=missing.

*DAMAGE: REMOVAL, CUT, MOWING, BEAVER, DEER, RODENTS, INSECTS, GAME, LIVESTOCK, Other/Unknown
ANIMAL, Human TRAMPLED, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICANE, DISEASED, VINE
Strangulation, UNKNOW, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EEP Entry Tool ver. 2.3.1

Vegetation Monitoring Data (VMD) Datasheet

Please fill in any missing data and correct any errors.

Plot **E92523-01-VPC**

VMD Year (1-5): Date: -

Taxonomic Standard: _____

Taxonomic Standard DATE: _____

Latitude or UTM-N: Datum:

Longitude or UTM-E: UTM Zone:

Coordinate Accuracy (m): X-Axis bearing (deg):

Plot Dimensions: X: Y: Plot has reverse orientation for X and Y axis (Y is 90 degrees to the right of X)

Party:

Role: _____

Date last planted: _____

New planting date m/yy?

Check box if plot was not

Notes: sampled, specify reason below

*Pink flagging
photo # 8068
Cms 8/10*

ID	Species Name	Map char	Source*	Sep 2011 Data		Height 1cm*	DBH 1 cm	Notes*	THIS YEAR'S DATA					
				X 0.1m	Y 0.1m				Height 1cm*	DBH 1 cm	Re-sprout	Vigor*	Damage*	Notes
698	Quercus lyrata	X (f)	R	5.6	0.4	146.0	0.2	<input type="checkbox"/>	202	1.0	<input type="checkbox"/>	3	INS	
699	Platanus occidentalis var. occidentalis	X (i)	R	8.3	0.4	188.0	0.6	<input type="checkbox"/>	334	2.0	<input type="checkbox"/>	3	INS DIS	
700	Liriodendron tulipifera var. tulipifera	X (m)	R	9.4	1.6	135.0	DBH?	<input type="checkbox"/>	250	1.2	<input type="checkbox"/>	3	INS DIS	
701	Quercus lyrata	X (h)	R	6.8	2.1	187.0	0.7	<input type="checkbox"/>	232	1.2	<input type="checkbox"/>	3	INS	
702	Fraxinus pennsylvanica	X (d)	R	4.0	2.2	308.0	1.3	<input type="checkbox"/>	298	1.2	<input type="checkbox"/>	3	VINE	
703	Betula nigra	X (a)	R	0.2	4.9	244.0	0.9	<input type="checkbox"/>	306	2.0	<input type="checkbox"/>	3	INS PLS	
704	Quercus lyrata	X (c)	R	2.6	4.9	268.0	2.2	<input type="checkbox"/>	360	3.4	<input type="checkbox"/>	4	INS	
705	Fraxinus pennsylvanica	X (k)	R	8.3	4.4	175.0	0.5	<input type="checkbox"/>	234	1.2	<input type="checkbox"/>	3	VINE	smothered
707	Liriodendron tulipifera var. tulipifera	X (i)	R	6.8	7.2	109.0	DBH?	<input type="checkbox"/>	161	0.4	<input type="checkbox"/>	3	INS	
708	Quercus lyrata	X (e)	R	4.1	7.2	177.0	0.3	<input type="checkbox"/>	265	1.5	<input type="checkbox"/>	3	INS DIS	
709	Betula nigra	X (b)	R	1.4	7.2	362.0	2.7	<input type="checkbox"/>	475	5.5	<input type="checkbox"/>	3	INS DIS	
711	Fraxinus pennsylvanica	X (g)	R	5.8	9.7	349.0	2.4	<input type="checkbox"/>	460	4.0	<input type="checkbox"/>	3	INS DIS	
712	Quercus lyrata	X (l)	R	8.5	9.7	159.0	0.4	<input type="checkbox"/>	293	2.4	<input type="checkbox"/>	3	INS DIS	

stems: 13 New Stems, not included last year, but are obviously planted. If more space needed, use blank PWS (Planted Woody Stems) Form:

Species Name	Source*	X (m)	Y (m)	Height 1cm*	DBH 1 cm	Vigor*	Damage*	Notes

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 26
 *VIGOR: 4=excellent, 3=good, 2=fair, *DAMAGE: REMOval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown
 1=unlikely to survive year, 0=dead, ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROUGHT, STORM, HURRICane, DISeased, VINE
 M=missing. Strangulation, UNKNown, specify other.
 *HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m. Printed in the CVS-EEP Entry Tool ver. 2.3.1

*Herbs: Johnson grass, Rhus, Goldenrod, Lonicera, Wingedstem, Andropogon
 Junco*

Plot (continued): **E92523-01-VPC**

Sep 2011 Data

THIS YEAR'S DATA

ID	Species	map char	source	X (m)	Y (m)	ddh (mm)	Height (cm)	DBH (cm)	Notes *	ddh (mm)	Height (cm)	DBH (cm)	Re-sprout	Vigor*	Damage*	Notes

Natural Woody Stems - tallied by species

Explanation of cut-off & subsampling**:

Height Cut-Off (All stems shorter than this are ignored. If >10cm, explain why to the right.): 10cm 50cm 100cm 137cm

Species Name	c	SEEDLINGS — HEIGHT CLASSES			SAPLINGS — DBH			TREES — DBH						
		Sub-Seed	10 cm-50 cm	50 cm-100 cm	100 cm-137 cm	Sub-Sapl	0-1 cm	1-2.5	2.5-	5-	=10 (write DBH)			
<i>P. occidentalis</i>														
<i>B. nigra</i>														
<i>N. sylvatica</i>														
<i>Cercus canad.</i>														
<i>Corylus amer.</i>														
<i>P. virginiana</i>				1										
**Required if cut-off >10cm or subsample > 100%				●1	●2	●3	●4	●5	●6	●7	●8	●9	●10	Form WS2, ver 9.1

F. pennsylvanica

L. tulipifera

S. canadensis

Ailanthus altissima

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown p. 27

*VIGOR: 4=excellent, 3=good, 2=fair, 1=unlikely to survive year, 0=dead, M=missing. *DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSeCTS, GAME, LIVESTock, Other/Unknown ANIMAl, Human TRAMPled, Site Too WET, Site Too DRY, FLOOD, DROUght, STORM, HURRICane, DISeased, VINE Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.


Map of stems on plot E92523-01-VPC

X-axis: 168°

stems: 13

map size:

LARGE

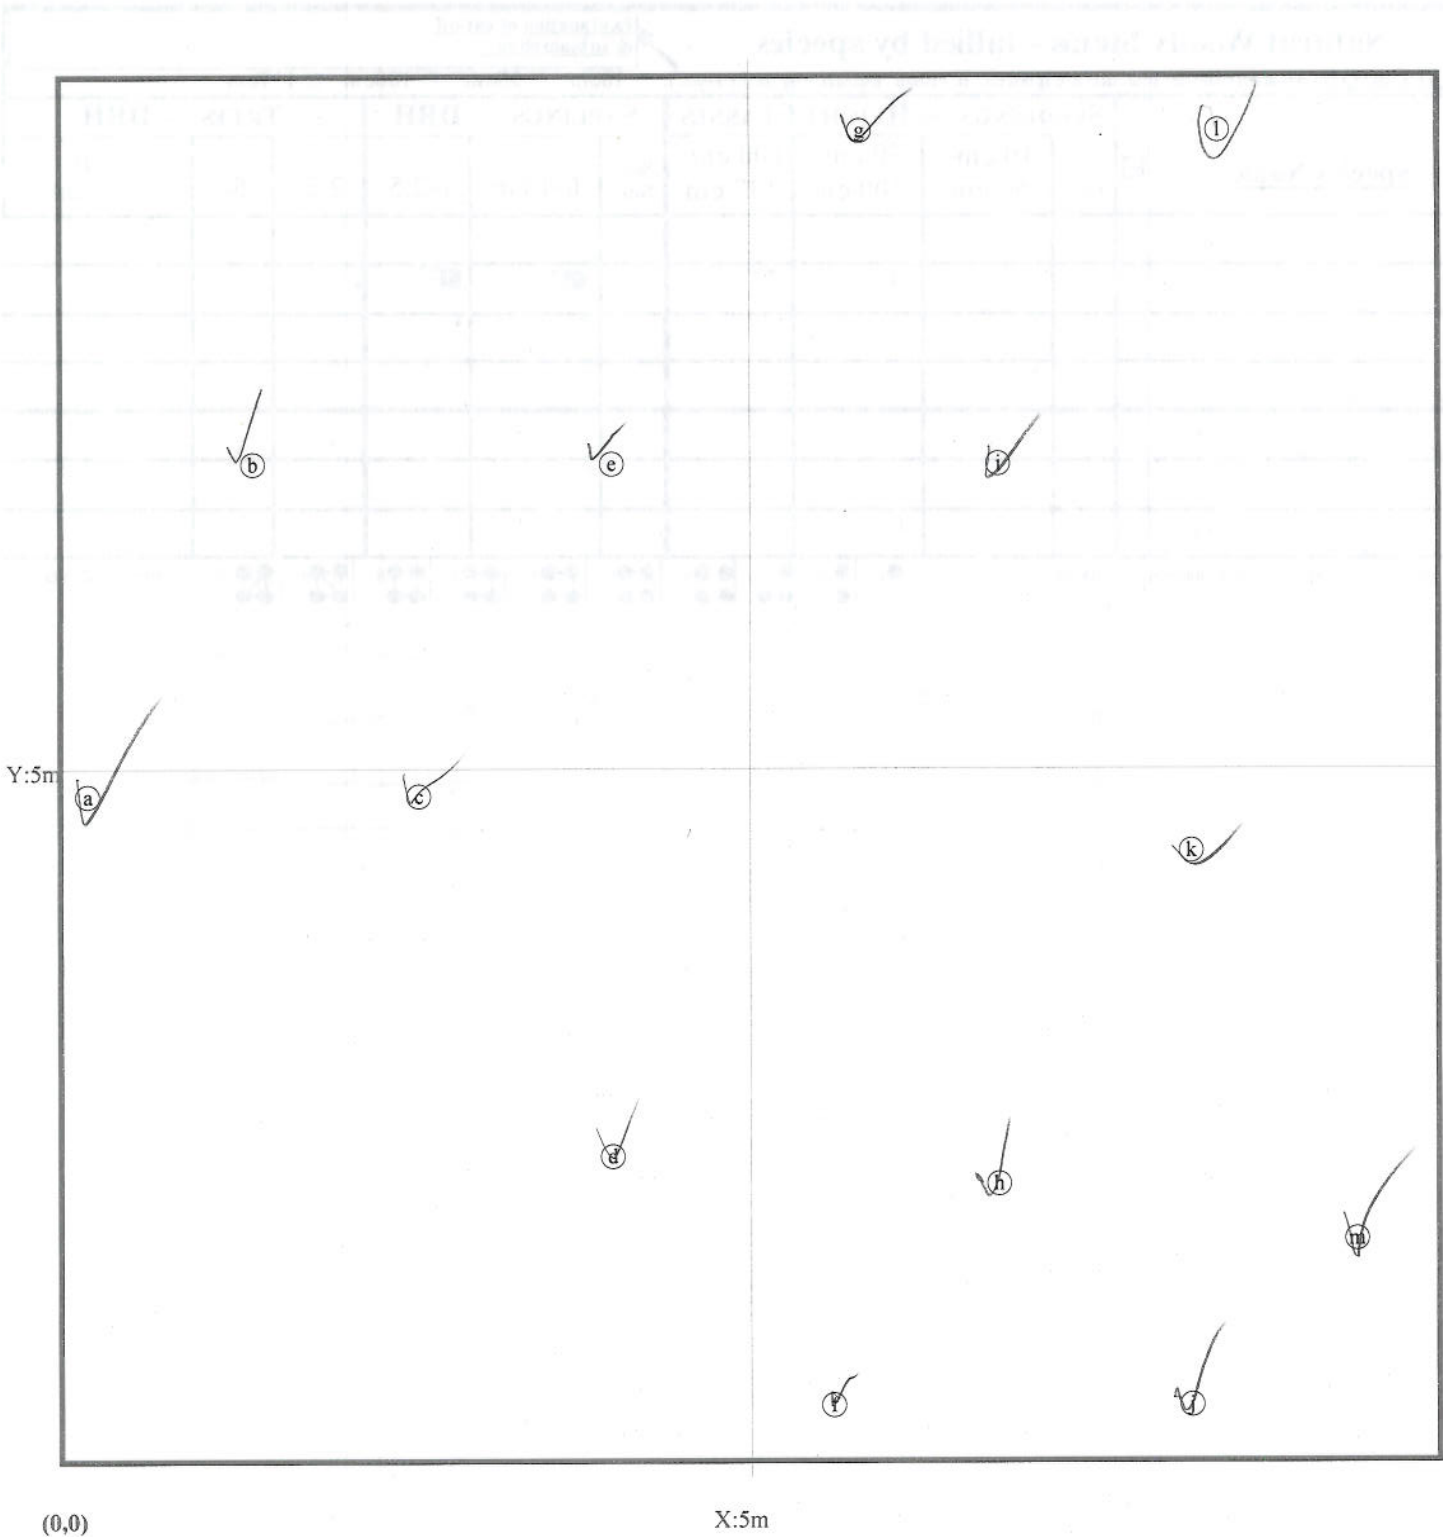

*SOURCE: Tr=Transplant, L=Live stake, B=Ball and burlap, P=Potted, Tu=Tubling, R=bare Root, M=Mechanically, U=Unknown

p. 28

*VIGOR: 4=excellent, 3=good, 2=fair,

1=unlikely to survive year, 0=dead,

M=missing.

*DAMAGE: REMoval, CUT, MOWing, BEAVer, DEER, RODents, INSEcts, GAME, LIVESTock, Other/Unknown

ANIMAL, Human TRAMpled, Site Too WET, Site Too DRY, FLOOD, DROught, STORM, HURRICane, DISeased, VINE

Strangulation, UNKNown, specify other.

*HEIGHT PRECISION drops to 10cm if >2.5m and 50cm if >4m.

Printed in the CVS-EEP Entry Tool ver. 2.3.1

APPENDIX B
GEOMORPHIC RAW DATA

REPRESENTATIVE PROBLEM AREA PHOTOS

Representative Problem Area Photos



Buckhorn Creek, minor bank scour, Sta 152+90

9/17/12

Photo No. 61

PHOTOPOINTS

Photo Point 1



Buckhorn Creek facing upstream Year 0 Photo No. 1



Buckhorn Creek facing upstream Year 3 Photo No. 4



Buckhorn Creek facing upstream Year 1 Photo No. 2



Buckhorn Creek facing upstream Year 4 Photo No. 5



Buckhorn Creek facing upstream Year 2 Photo No. 3

Buckhorn Creek facing upstream Year 5

Photo Point 2



Buckhorn Creek facing upstream Year 0 Photo No. 6



Buckhorn Creek facing upstream Year 3 Photo No. 9



Buckhorn Creek facing upstream Year 1 Photo No. 7



Buckhorn Creek facing upstream Year 4 Photo No. 10



Buckhorn Creek facing upstream Year 2 Photo No. 8

Buckhorn Creek facing upstream Year 5

Photo Point 3



Buckhorn Creek facing upstream Year 0 Photo No. 11




Buckhorn Creek facing upstream Year 3 Photo No. 14



Buckhorn Creek facing upstream Year 1 Photo No. 12



Buckhorn Creek facing upstream Year 4 Photo No. 15

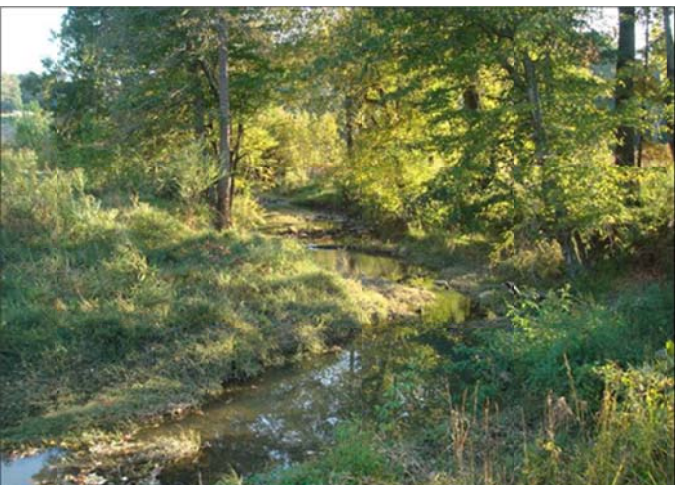

Buckhorn Creek facing upstream Year 2 Photo No. 13

Buckhorn Creek facing upstream Year 5

Photo Point 4



West Branch facing downstream Year 0 Photo No. 16



West Branch facing downstream Year 3 Photo No. 19



West Branch facing downstream Year 1 Photo No. 17



West Branch facing downstream Year 4 Photo No. 20



West Branch facing downstream Year 2 Photo No. 18

West Branch facing downstream Year 5

Photo Point 5



Buckhorn Creek facing upstream Year 0 Photo No. 21



Buckhorn Creek facing upstream Year 3 Photo No. 24



Buckhorn Creek facing upstream Year 1 Photo No. 22



Buckhorn Creek facing upstream Year 4 Photo No. 25



Buckhorn Creek facing upstream Year 2 Photo No. 23

Buckhorn Creek facing upstream Year 5

Photo Point 6



Buckhorn Creek at bridge, facing upstream Year 0 Photo No. 26



Buckhorn Creek at bridge, facing upstream Year 3 Photo No. 29



Buckhorn Creek at bridge, facing upstream Year 1 Photo No. 27



Buckhorn Creek at bridge, facing upstream Year 4 Photo No. 30



Buckhorn Creek at bridge, facing upstream Year 2 Photo No. 28

Buckhorn Creek at bridge, facing upstream Year 5

Photo Point 7



Buckhorn Creek at bridge, facing downstream Year 0 Photo No. 31



Buckhorn Creek at bridge, facing downstream Year 3 Photo No.34



Buckhorn Creek at bridge, facing downstream Year 1 Photo No. 32



Buckhorn Creek at bridge, facing downstream Year 4 Photo No. 35



Buckhorn Creek at bridge, facing downstream Year 2 Photo No. 33

Buckhorn Creek at bridge, facing downstream Year 5

Photo Point 8



Buckhorn Creek facing upstream Year 0 Photo No. 36



Buckhorn Creek facing upstream Year 3 Photo No. 39



Buckhorn Creek facing upstream Year 1 Photo No. 37



Buckhorn Creek facing upstream Year 4 Photo No. 40



Buckhorn Creek facing upstream Year 2 Photo No. 38

Buckhorn Creek facing upstream Year 5

Photo Point 9




Buckhorn Creek facing upstream Year 0 Photo No. 41



Buckhorn Creek facing upstream Year 3 Photo No. 44



Buckhorn Creek facing upstream Year 1 Photo No. 42

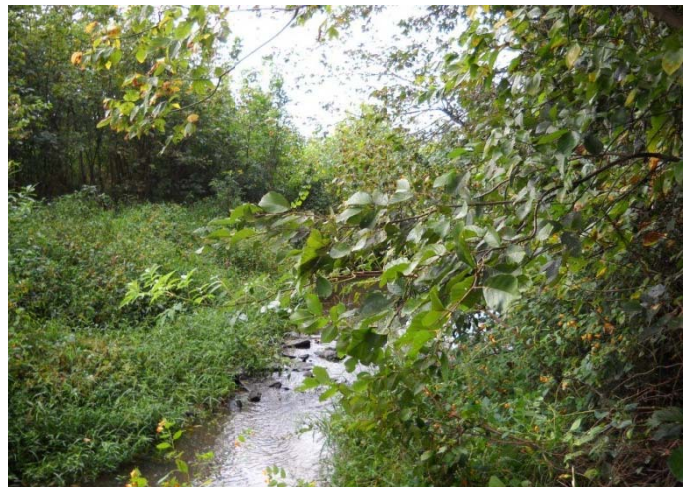

Buckhorn Creek facing upstream Year 4 Photo No. 45



Buckhorn Creek facing upstream Year 2 Photo No. 43

Buckhorn Creek facing upstream Year 5

Photo Point 10



Buckhorn Creek facing upstream Year 0 Photo No. 46



Buckhorn Creek facing upstream Year 3 Photo No. 49



Buckhorn Creek facing upstream Year 1 Photo No. 47



Buckhorn Creek facing upstream Year 4 Photo No. 50



Buckhorn Creek facing upstream Year 2 Photo No. 48



Buckhorn Creek facing upstream Year 5

Photo Point 11



Southwest Creek facing downstream Year 0 Photo No. 51

Southwest Creek facing downstream Year 3 Photo No. 54



Southwest Creek facing downstream Year 1 Photo No. 52

Southwest Creek facing downstream Year 4 Photo No. 55



Southwest Creek facing downstream Year 2 Photo No. 53

Southwest Creek facing downstream Year 5

Photo Point 12



Southwest Creek facing upstream Year 0 Photo No. 56



Southwest Creek facing upstream Year 3 Photo No. 59



Southwest Creek facing upstream Year 1 Photo No. 57



Southwest Creek facing upstream Year 4 Photo No. 60



Southwest Creek facing upstream Year 2 Photo No. 58

Southwest Creek facing upstream Year 5

GEOMORPHIC DATA

Table B2. Visual Morphological Stability Assessment						
Holly Grove Stream Restoration Site (D06028-B)						
Buckhorn Creek 8,848 ft						
Feature Category	Metric	(# Stable) Number Performing as Intended	Total Number per As-built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performing Mean or Total
A. Riffles	1. Present	86	86	N/A	100%	
	2. Armor stable	86	86	N/A	100%	
	3. Facet grade appears stable	86	86	N/A	100%	
	4. Minimal evidence of embedding/fining	86	86	N/A	100%	
	5. Length appropriate	86	86	N/A	100%	100%
B. Pools	1. Present	88	88	0	100%	
	2. Sufficiently deep	88	88	N/A	100%	
	3. Length appropriate	88	88	N/A	100%	100%
C. Thalweg	1. Upstream of meander bend centered	86	86	N/A	100%	
	2. Downstream of meander bend centered	86	86	N/A	100%	100%
D. Meanders	1. Outer bend in state of limited erosion	84	88	N/A	95%	
	2. Of those eroding, # w/ concomitant point bar formation	0	N/A	N/A	100%	
	3. Apparent Rc within specification	88	88	N/A	100%	
	4. Sufficient floodplain access and relief	88	88	N/A	100%	100%
E. Bed General	1. General channel bed aggradation areas	N/A	N/A	0/0	100%	
	2. Channel bed degradation - areas of increasing down-cutting or head-cutting	N/A	N/A	0/200	100%	100%
F. Vanes	1. Free of back or arm scour	108	108	N/A	100%	
	2. Height appropriate	108	108	N/A	100%	
	3. Angle and geometry appear appropriate	108	108	N/A	100%	
	4. Free of piping or other structural failures	108	108	N/A	100%	100%
G. Wads/Boulders	1. Free of scour	23	23	N/A	100%	
	2. Footing stable	23	23	N/A	100%	100%

Table B2. Visual Morphological Stability Assessment						
Holly Grove Stream Restoration Site (D06028-B)						
Middle Branch 1,755 ft						
Feature Category	Metric	(# Stable) Number Performing as Intended	Total Number per As-built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performing Mean or Total
A. Riffles	1. Present	44	44	N/A	100%	
	2. Armor stable	44	44	N/A	100%	
	3. Facet grade appears stable	43	44	N/A	98%	
	4. Minimal evidence of embedding/fining	44	44	N/A	100%	
	5. Length appropriate	44	44	N/A	100%	100%
B. Pools	1. Present	46	46	N/A	100%	
	2. Sufficiently deep	46	46	N/A	100%	
	3. Length appropriate	46	46	N/A	100%	100%
C. Thalweg	1. Upstream of meander bend centered	44	44	N/A	100%	
	2. Downstream of meander bend centered	44	44	N/A	100%	100%
D. Meanders	1. Outer bend in state of limited erosion	45	46	N/A	98%	
	2. Of those eroding, # w/ concomitant point bar formation	0	N/A	N/A	100%	
	3. Apparent Rc within specification	46	46	N/A	100%	
	4. Sufficient floodplain access and relief	46	46	N/A	100%	99%
E. Bed General	1. General channel bed aggradation areas	N/A	N/A	0/0	100%	
	2. Channel bed degradation - areas of increasing down-cutting or head-cutting	N/A	N/A	0/0	100%	100%
F. Vanes	1. Free of back or arm scour	69	69	N/A	100%	
	2. Height appropriate	69	69	N/A	100%	
	3. Angle and geometry appear appropriate	69	69	N/A	100%	
	4. Free of piping or other structural failures	69	69	N/A	100%	100%
G. Wads/Boulders	1. Free of scour	3	3	N/A	100%	
	2. Footing stable	3	3	N/A	100%	100%

Table B2. Visual Morphological Stability Assessment
Holly Grove Stream Restoration Site (D06028-B)
East Branch 1,090 ft

Feature Category	Metric	(# Stable) Number Performing as Intended	Total Number per As-built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performing Mean or Total
A. Riffles	1. Present	25	25	N/A	100%	
	2. Armor stable	24	25	N/A	96%	
	3. Facet grade appears stable	25	25	N/A	100%	
	4. Minimal evidence of embedding/fining	25	25	N/A	100%	
	5. Length appropriate	25	25	N/A	100%	99%
B. Pools	1. Present	25	25	N/A	100%	
	2. Sufficiently deep	25	25	N/A	100%	
	3. Length appropriate	25	25	N/A	100%	100%
C. Thalweg	1. Upstream of meander bend centered	25	25	N/A	100%	
	2. Downstream of meander bend centered	25	25	N/A	100%	100%
D. Meanders	1. Outer bend in state of limited erosion	25	25	N/A	100%	
	2. Of those eroding, # w/ concomitant point bar formation	0	N/A	N/A	100%	
	3. Apparent Rc within specification	25	25	N/A	100%	
	4. Sufficient floodplain access and relief	25	25	N/A	100%	100%
E. Bed General	1. General channel bed aggradation areas	N/A	N/A	0/0	100%	
	2. Channel bed degradation - areas of increasing down-cutting or head-cutting	N/A	N/A	0/0	100%	100%
F. Vanes	1. Free of back or arm scour	37	38	N/A	97%	
	2. Height appropriate	38	38	N/A	100%	
	3. Angle and geometry appear appropriate	38	38	N/A	100%	
	4. Free of piping or other structural failures	37	38	N/A	97%	99%
G. Wads/Boulders	1. Free of scour	1	1	N/A	100%	
	2. Footing stable	1	1	N/A	100%	100%

Table B2. Visual Morphological Stability Assessment
Holly Grove Stream Restoration Site (D06028-B)
Southeast Creek 363 ft

Feature Category	Metric	(# Stable) Number Performing as Intended	Total Number per As-built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performing Mean or Total
A. Riffles	1. Present	10	10	N/A	100%	
	2. Armor stable	10	10	N/A	100%	
	3. Facet grade appears stable	10	10	N/A	100%	
	4. Minimal evidence of embedding/fining	10	10	N/A	100%	
	5. Length appropriate	10	10	N/A	100%	100%
B. Pools	1. Present	10	10	N/A	100%	
	2. Sufficiently deep	10	10	N/A	100%	
	3. Length appropriate	10	10	N/A	100%	100%
C. Thalweg	1. Upstream of meander bend centered	10	10	N/A	100%	
	2. Downstream of meander bend centered	10	10	N/A	100%	100%
D. Meanders	1. Outer bend in state of limited erosion	9	9	N/A	100%	
	2. Of those eroding, # w/ concomitant point bar formation	0	N/A	N/A	100%	
	3. Apparent Rc within specification	9	9	N/A	100%	
	4. Sufficient floodplain access and relief	9	9	N/A	100%	100%
E. Bed General	1. General channel bed aggradation areas	N/A	N/A	0/0	100%	
	2. Channel bed degradation - areas of increasing down-cutting or head-cutting	N/A	N/A	0/0	100%	100%
F. Vanes	1. Free of back or arm scour	11	11	N/A	100%	
	2. Height appropriate	11	11	N/A	100%	
	3. Angle and geometry appear appropriate	11	11	N/A	100%	
	4. Free of piping or other structural failures	11	11	N/A	100%	100%
G. Wads/Boulders	1. Free of scour	2	2	N/A	100%	
	2. Footing stable	2	2	N/A	100%	100%

Table B2. Visual Morphological Stability Assessment
Holly Grove Stream Restoration Site (D06028-B)
Southwest Creek 723 ft


Feature Category	Metric	(# Stable) Number Performing as Intended	Total Number per As-built	Total Number / feet in unstable state	% Performing in Stable Condition	Feature Performing Mean or Total
A. Riffles	1. Present	23	23	N/A	100%	
	2. Armor stable	23	23	N/A	100%	
	3. Facet grade appears stable	23	23	N/A	100%	
	4. Minimal evidence of embedding/fining	23	23	N/A	100%	
	5. Length appropriate	23	23	N/A	100%	100%
B. Pools	1. Present	25	25	N/A	100%	
	2. Sufficiently deep	25	25	N/A	100%	
	3. Length appropriate	25	25	N/A	100%	100%
C. Thalweg	1. Upstream of meander bend centered	23	23	N/A	100%	
	2. Downstream of meander bend centered	23	23	N/A	100%	100%
D. Meanders	1. Outer bend in state of limited erosion	23	25	N/A	92%	
	2. Of those eroding, # w/ concomitant point bar formation	0	N/A	N/A	100%	
	3. Apparent Rc within specification	25	25	N/A	100%	
	4. Sufficient floodplain access and relief	25	25	N/A	100%	100%
E. Bed General	1. General channel bed aggradation areas	N/A	N/A	0/0	100%	
	2. Channel bed degradation - areas of increasing down-cutting or head-cutting	N/A	N/A	0/0	100%	100%
F. Vanes	1. Free of back or arm scour	9	9	N/A	100%	
	2. Height appropriate	9	9	N/A	100%	
	3. Angle and geometry appear appropriate	9	9	N/A	100%	
	4. Free of piping or other structural failures	9	9	N/A	100%	100%
G. Wads/Boulders	1. Free of scour	34	34	N/A	100%	
	2. Footing stable	34	34	N/A	100%	100%

Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 1 - Buckhorn Creek

Profile

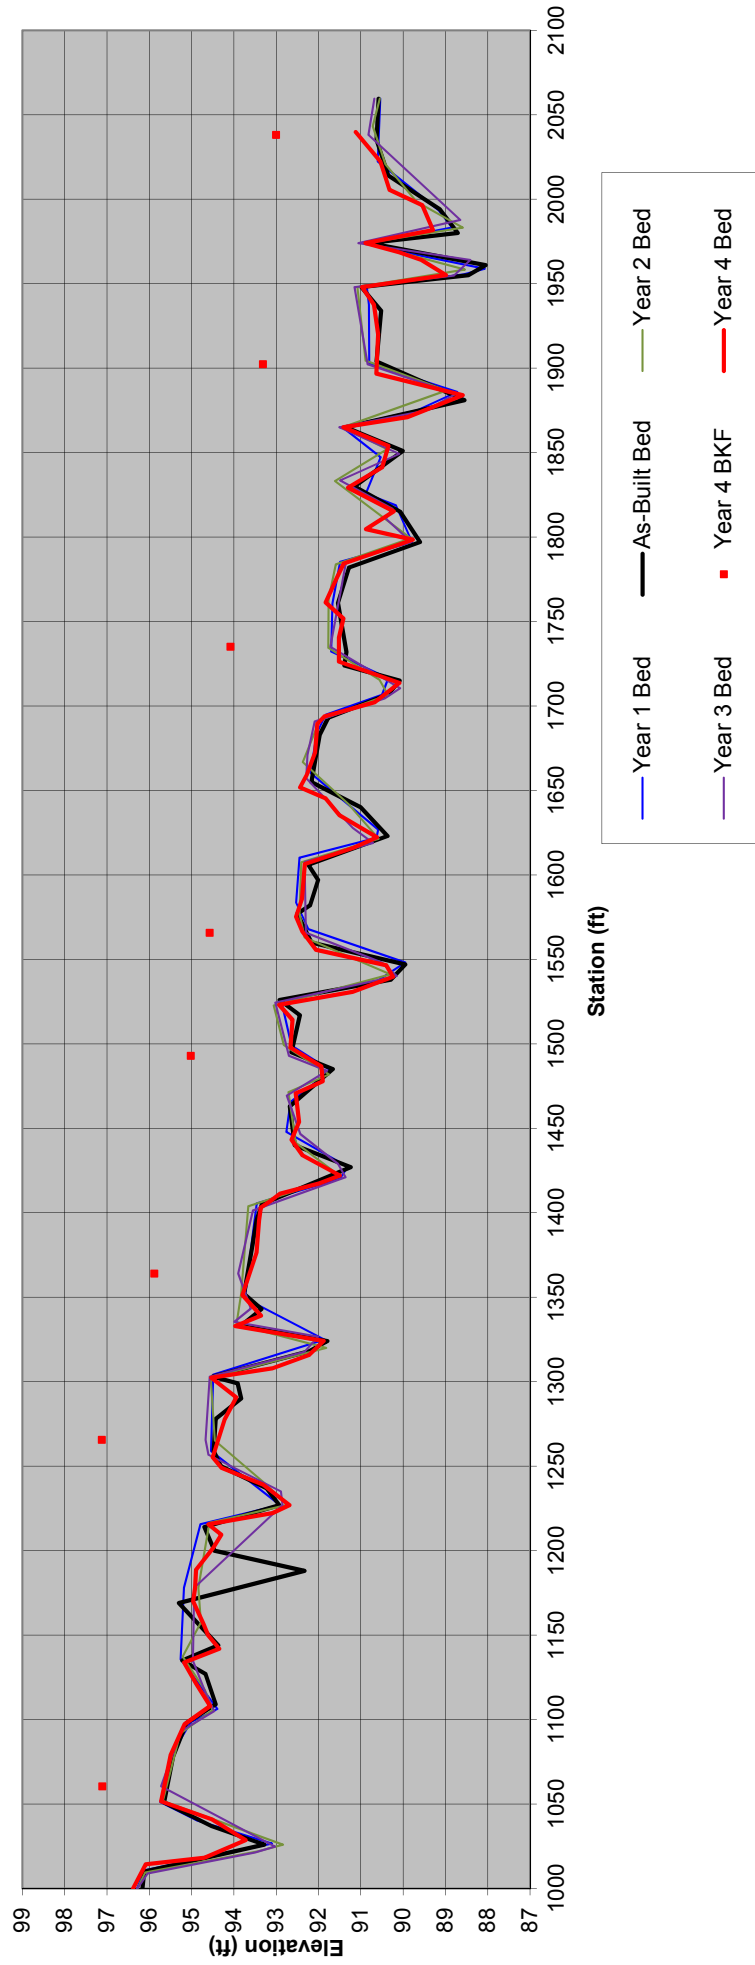


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 2 - Buckhorn Creek

Profile

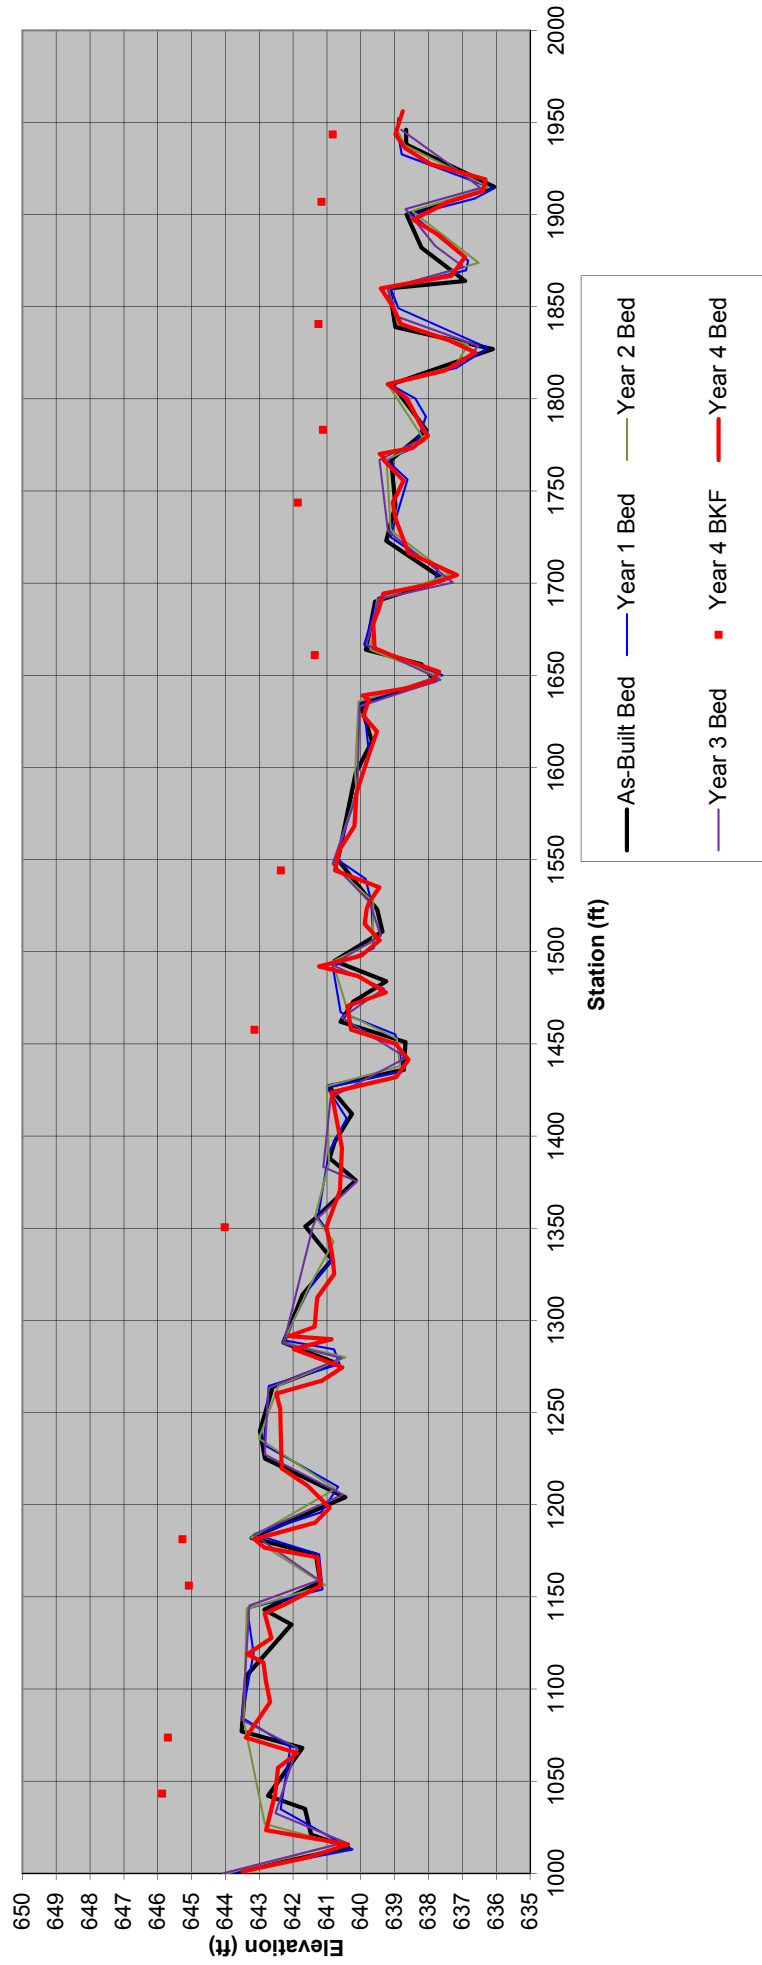


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 3 - Buckhorn Creek

Profile

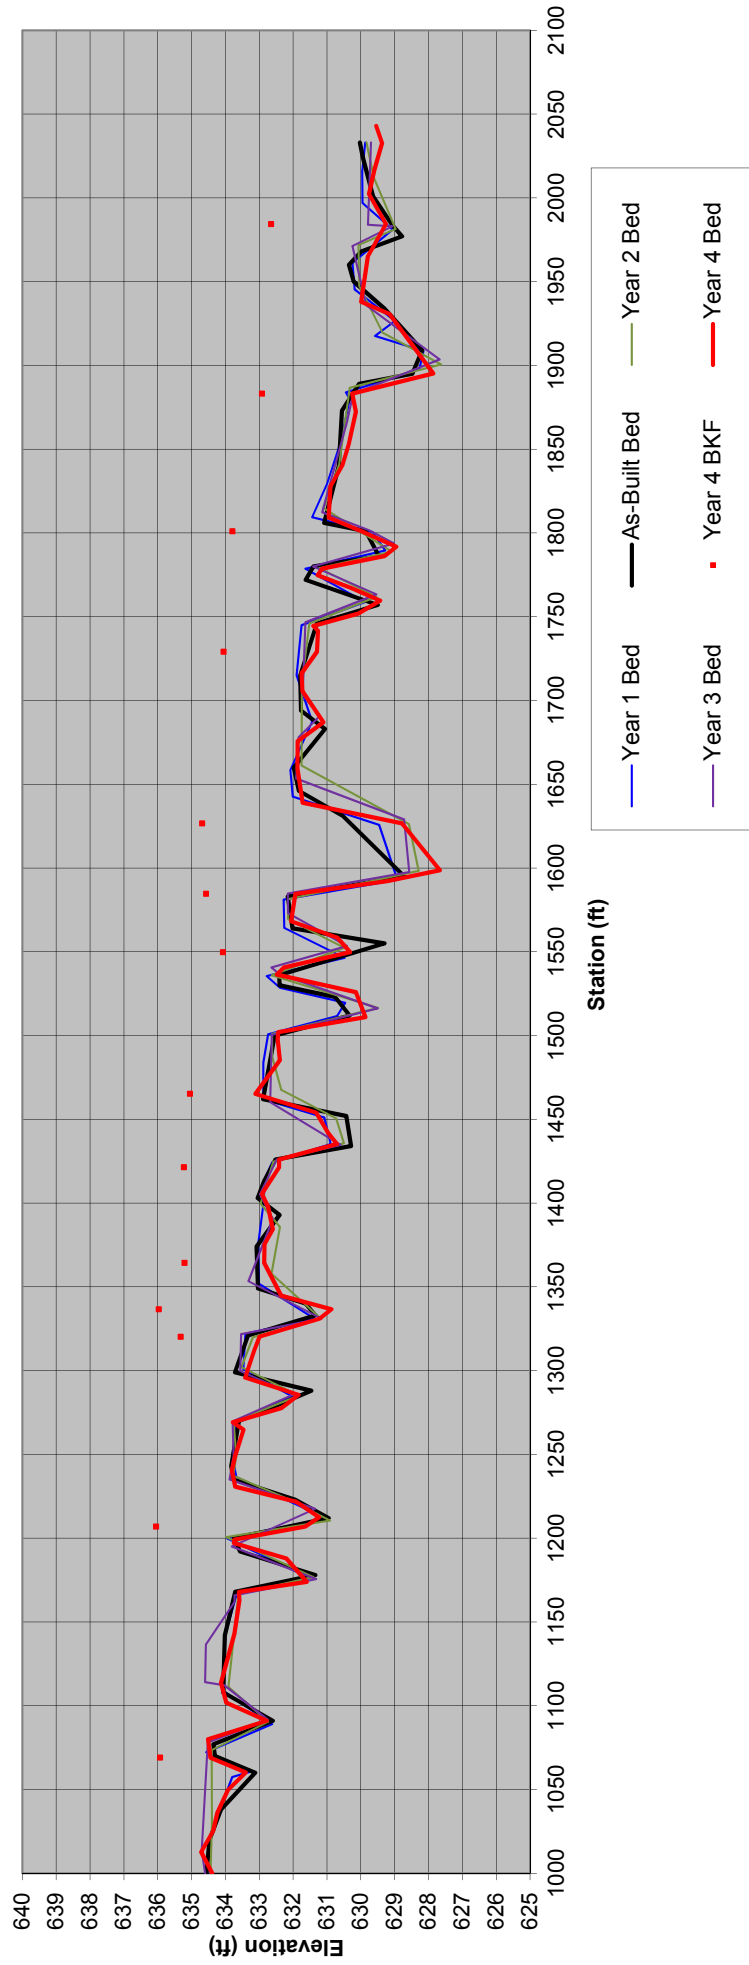


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 4 - Middle Branch

Profile

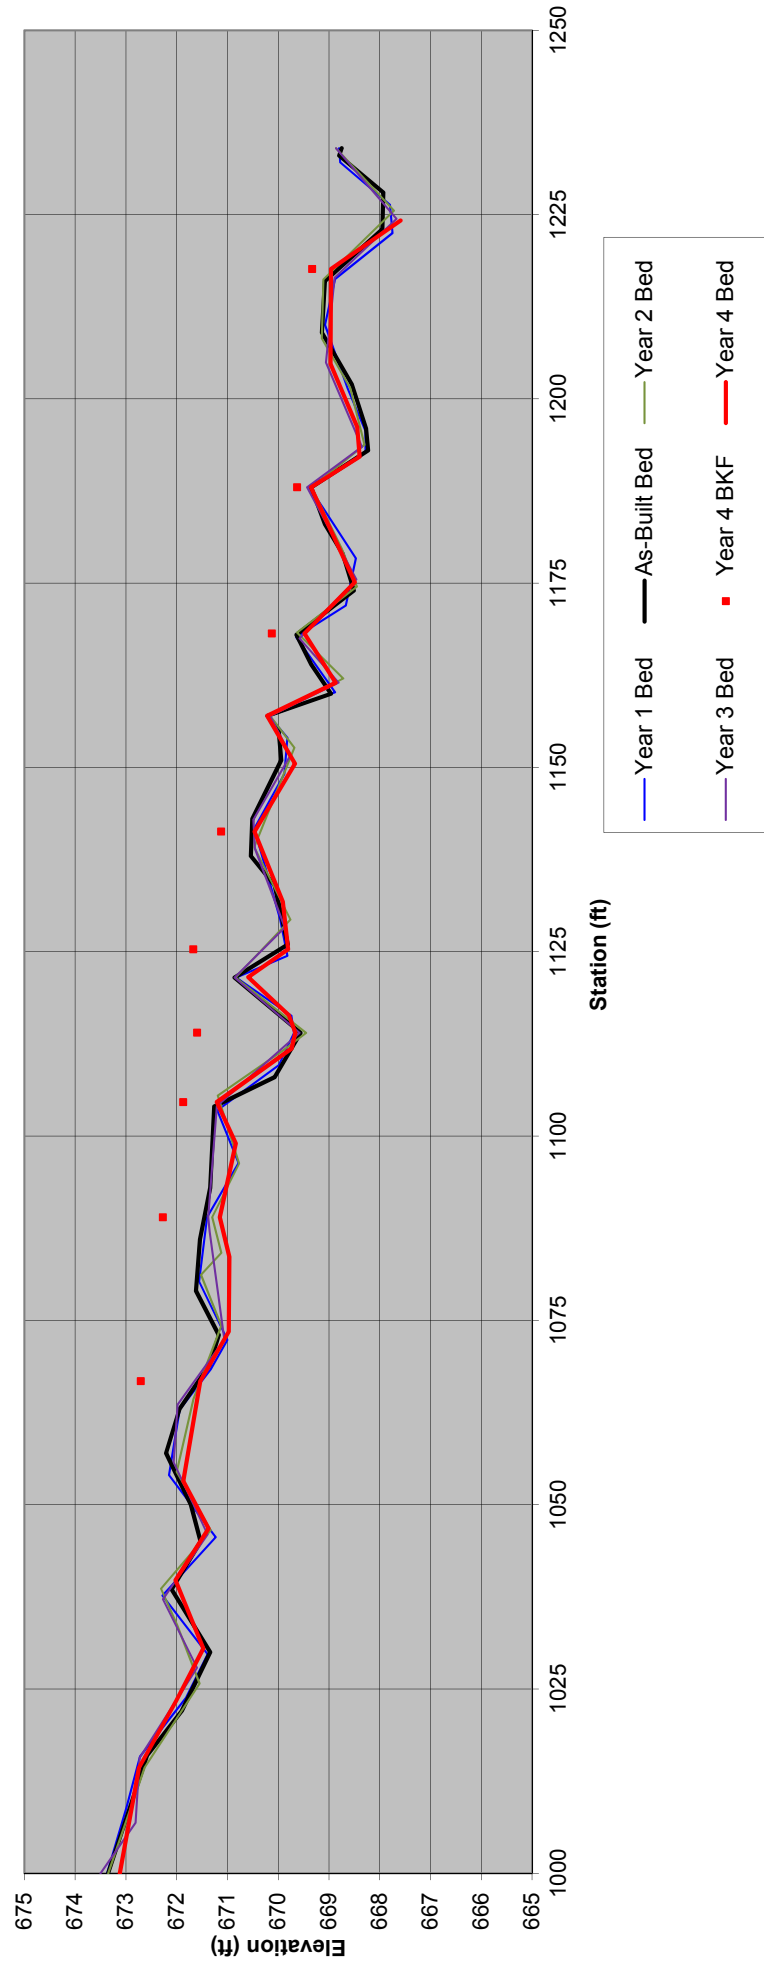


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 5 - Middle Branch

Profile

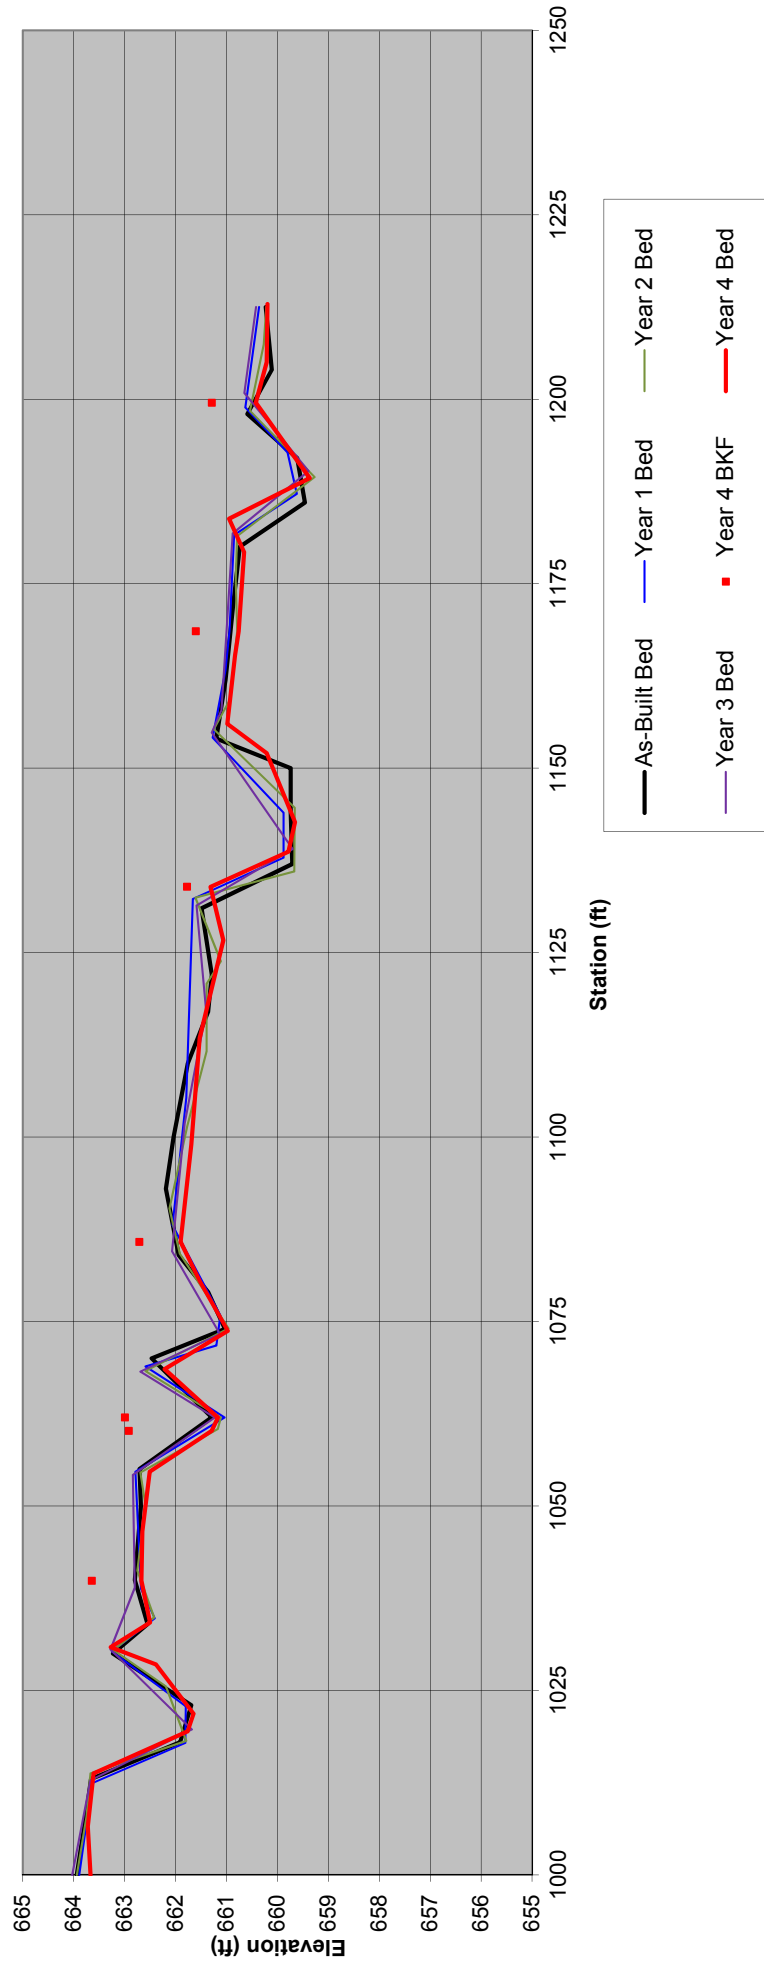


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 6 - Lower East Branch

Profile

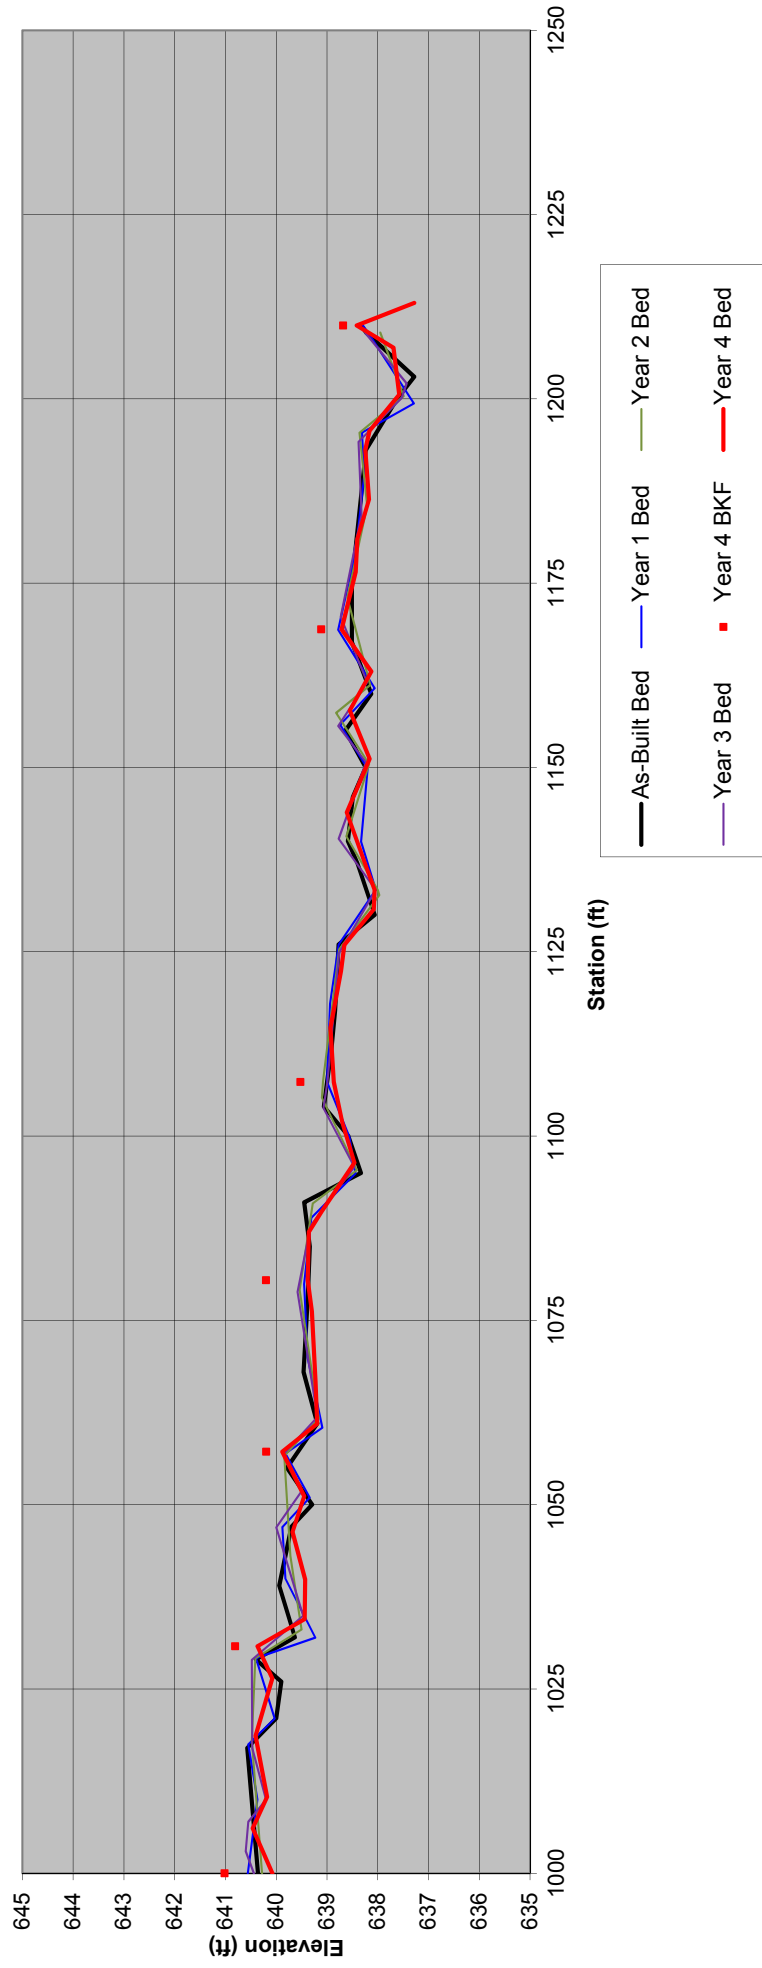


Holly Grove Stream Restoration Site

Guilford County, NC

Profile Reach 7 - Southeast Creek


Profile

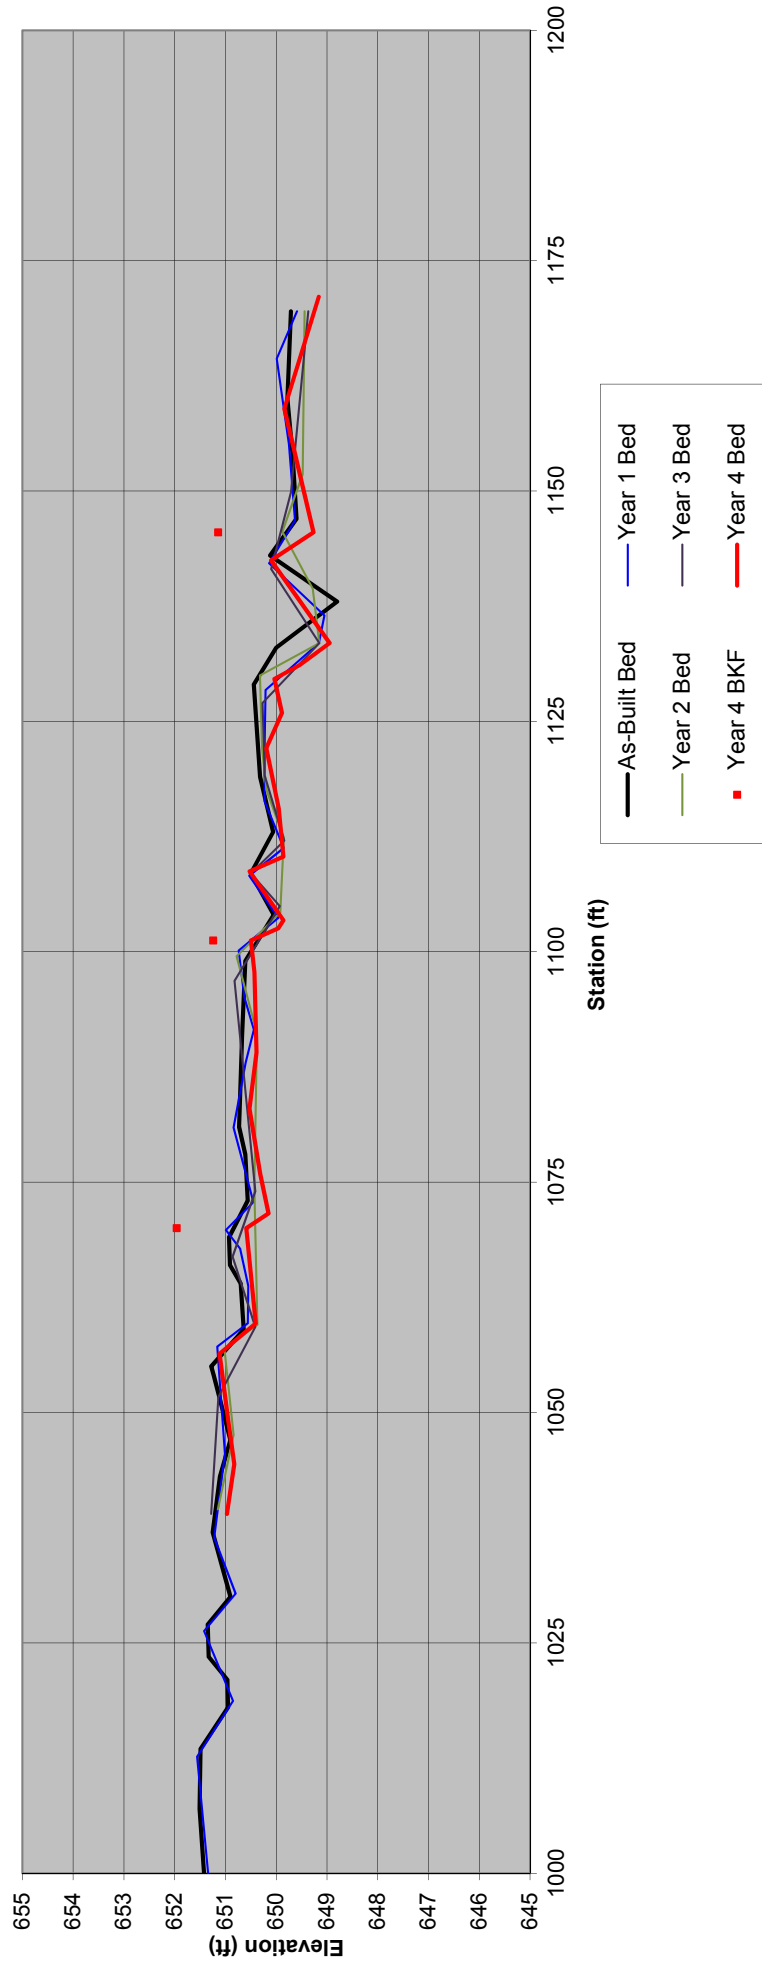

Holly Grove Stream Restoration Site

Guilford County, NC
Profile Reach 8 - Southwest Creek

Profile

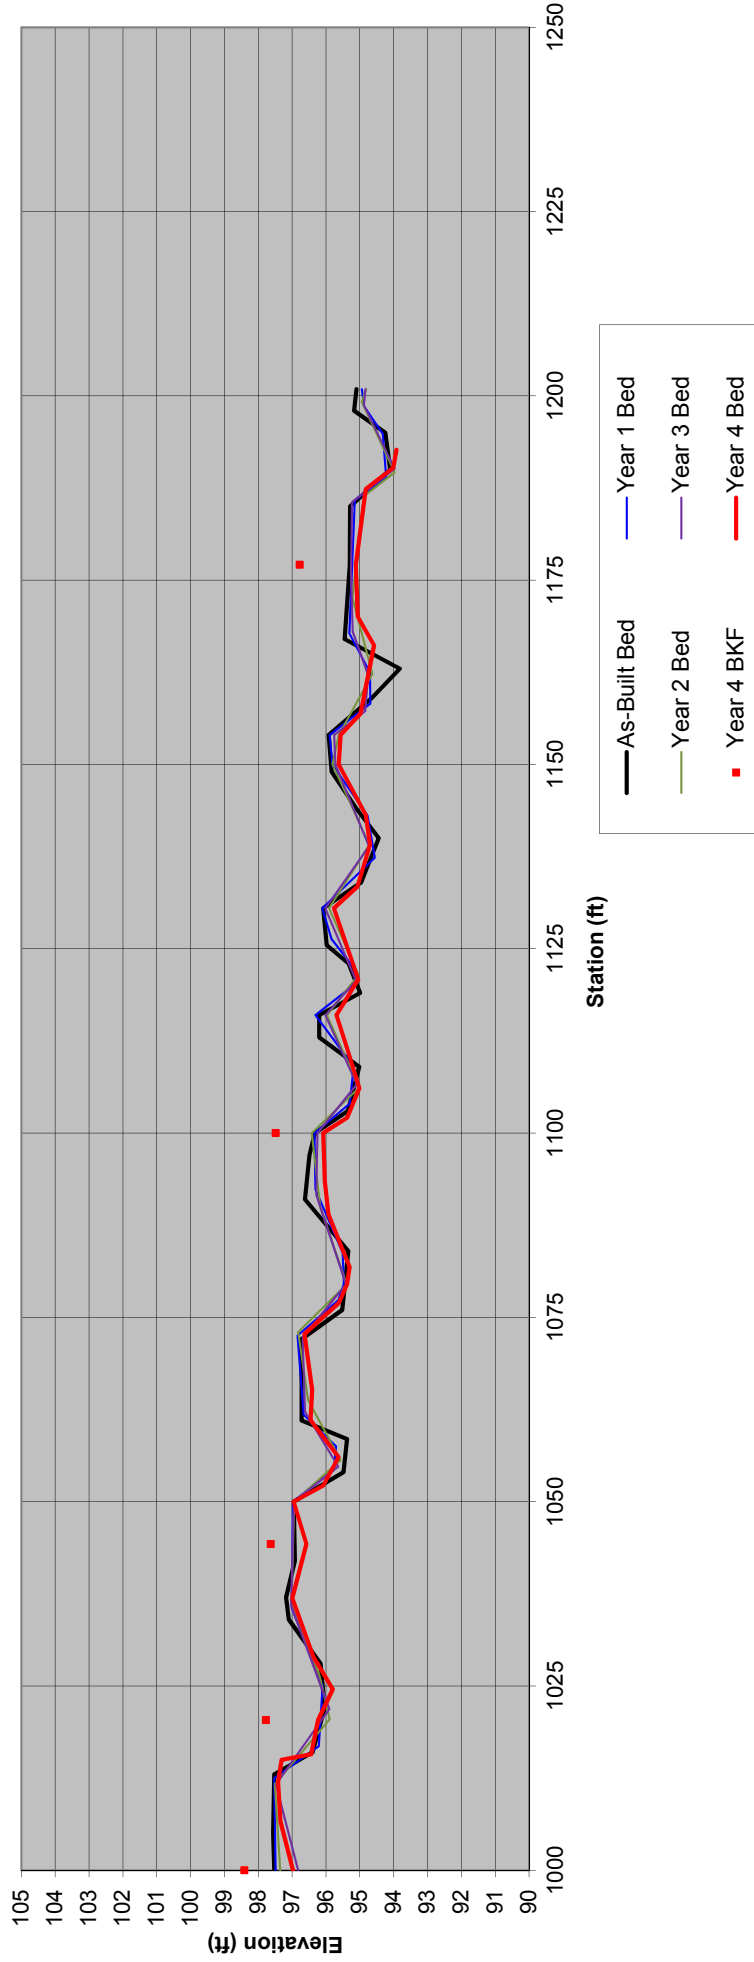


Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF1
 Reach 1 - Buckhorn Creek - Sta 11+78.6



Year 4

Facing Downstream

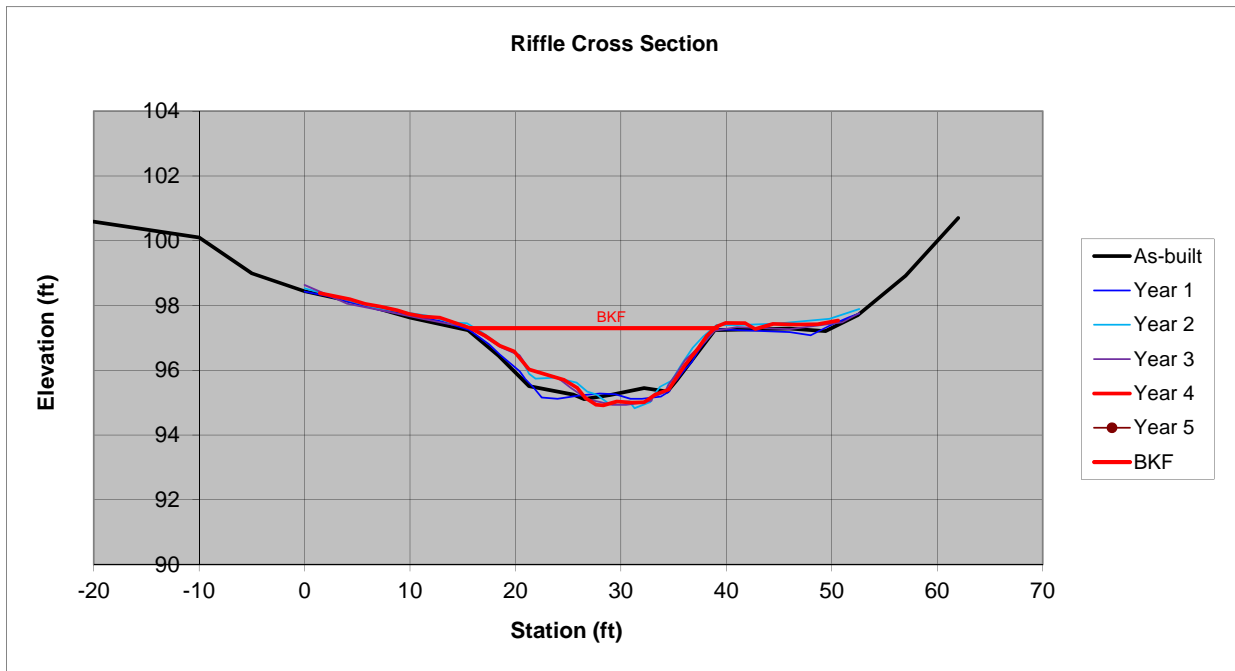

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	34.3	Area	35.4	Area	35.3	Area	31.3	Area	32.8	Area	0.0
Bkf W	23.4	Bkf W	23.3	Bkf W	23.7	Bkf W	23.7	Bkf W	23.3	Bkf W	10
Dmean	1.5	Dmean	1.5	Dmean	1.5	Dmean	1.3	Dmean	1.4	Dmean	0.0
Dmax	2.1	Dmax	2.1	Dmax	2.6	Dmax	2.3	Dmax	2.4	Dmax	0.0
W/d	16.0	W/d	15.3	W/d	15.9	W/d	18.0	W/d	16.6	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Riffle Cross Section RF1

Reach 1 - Buckhorn Creek - Sta 11+78.6

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	6.36	97.34	PL1 IR Lt	BM HI	3.78	98.67	RF1 IR Lt	BM HI	4.81	98.73	IR Lt
		103.70				102.45				103.54	
-20	3.11	100.59	GRND	0	4.02	98.43	GRND	0	5.01	98.53	GRND
-10	3.60	100.10		2	4.15	98.30	GRND	2.8	5.26	98.28	GRND
-5	4.71	98.99		7	4.58	97.87	GRND	6.8	5.62	97.92	GRND
0	5.26	98.44	GRND	13	4.94	97.51	GRND	11.8	5.86	97.68	GRND
5	5.61	98.09		15.6	5.20	97.25	GRND	13.8	6.06	97.48	GRND
10	6.07	97.63		17.5	5.65	96.80	BKF LT	15.4	6.09	97.45	BKF
15.5	6.46	97.24	BKF	18.5	5.96	96.49	BNK	16.8	6.36	97.18	BNK
18.4	7.25	96.45		20	6.37	96.08	BNK	18.8	6.83	96.71	BNK
21.3	8.19	95.51	TOE	20.4	6.48	95.97	BNK	20.3	7.06	96.48	BNK
25.5	8.45	95.25	EOW	20.9	6.71	95.74	BNK	21.3	7.65	95.89	BNK
26.5	8.59	95.11	THL	21.7	6.98	95.47	EOW	21.9	7.80	95.74	BED
29	8.46	95.24		22.5	7.29	95.16	BED	23.8	7.77	95.77	BED
32.2	8.25	95.45		24	7.33	95.12	BED	25.8	7.92	95.62	BED
34.4	8.36	95.34	EOW	26	7.23	95.22	BED	26.8	8.20	95.34	BED
35.3	8.01	95.69	TOE	28	7.17	95.28	BED	27.7	8.29	95.25	EOW
38.9	6.46	97.24	BKF	29.5	7.19	95.26	BED	28.8	8.56	94.98	BED
46	6.41	97.29		30.9	7.33	95.12	BED	30.8	8.50	95.04	BED
49.4	6.49	97.21		32	7.33	95.12	BED	31.3	8.71	94.83	THL
52.5	5.99	97.71	GRND	33.8	7.26	95.19	BED	32.8	8.52	95.02	BED
57	4.78	98.92		34.6	7.10	95.35	BED	33.1	8.32	95.22	EOW
62	3.00	100.70		34.8	6.89	95.56	EOW	33.7	8.05	95.49	BED
				35.3	6.75	95.70	BNK	34.8	7.86	95.68	BED
				36	6.45	96.00	BNK	35.8	7.33	96.21	BNK
				36.7	6.21	96.24	BNK	36.8	6.85	96.69	BNK
				37.4	5.83	96.62	BKF RT	37.8	6.50	97.04	BNK
				38.9	5.18	97.27	GRND	39.1	6.14	97.40	BKF
				42	5.22	97.23	GRND	40.8	6.15	97.39	GRND
				46	5.27	97.18	GRND	44.8	6.10	97.44	GRND
				48	5.37	97.08	GRND	49.8	5.95	97.59	GRND
				50	5.04	97.41	GRND	52.6	5.65	97.89	GRND
				51.6	4.82	97.63	GRND				
				52.6	4.7	97.75	GRND				
				25		97.14					

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	5.82	98.66	IR Lt
		104.48	
0	5.85	98.63	GRND
2	6.13	98.35	
4	6.42	98.06	
8	6.68	97.80	
11	6.88	97.60	
14	7.07	97.41	
15.2	7.09	97.39	BKF
17	7.43	97.05	BNK
18.5	7.75	96.73	
20.4	8.02	96.46	
21.3	8.46	96.02	BED
24	8.71	95.77	
25.2	9.01	95.47	
26.5	9.30	95.18	EOW
26.6	9.36	95.12	BED
28	9.46	95.02	
29.2	9.55	94.93	THL
30.5	9.55	94.93	BED
32	9.48	95.00	
32.9	9.42	95.06	
33	9.31	95.17	EOW
34.2	9.16	95.32	BNK
34.5	8.93	95.55	
35.2	8.62	95.86	
36.1	8.16	96.32	
38	7.59	96.89	
38.9	7.26	97.22	BKF
41	7.15	97.33	GRND
46	7.21	97.27	
51	7	97.48	
52.6	6.72	97.76	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	0.00	IR Lt
1.4		98.38	
4.3		98.19	
5.7		98.05	
7.2		97.96	
8.8		97.85	
9.9		97.74	
11.3		97.66	
12.8		97.62	
14.1		97.48	
15.8		97.30	BKF
17.1		97.06	
18.5		96.76	
19.9		96.58	
21.3		96.03	
23.2		95.84	
24.7		95.70	
25.8		95.46	
26.6		95.16	
27.6		94.94	
28.3		94.92	
29.6		95.03	
31.0		95.00	
32.2		95.01	
33.3		95.25	
34.5		95.40	
36.1		96.16	
37.4		96.69	
38.2		97.07	
39.1		97.35	
39.9		97.46	
41.8		97.45	

Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL1


Reach 1 - Buckhorn Creek - Sta 12+28.7



Year 4

Facing Downstream

Pool Cross Section

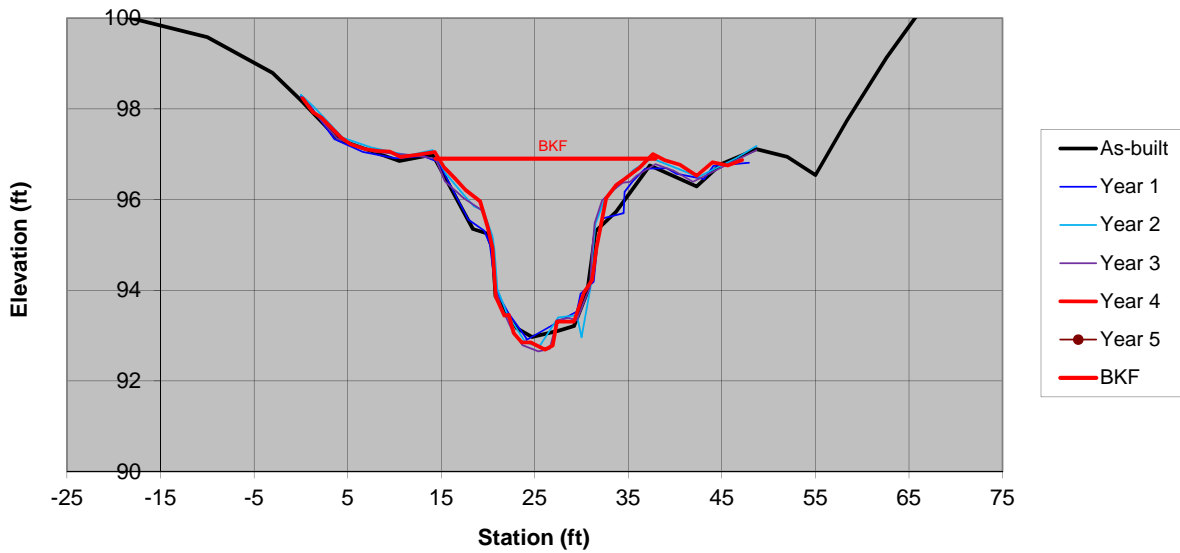

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	52.7	Area	48.0	Area	46.8	Area	48.4	Area	47.2	Area	0.0
Bkf W	23.2	Bkf W	22.1	Bkf W	23.4	Bkf W	23.5	Bkf W	23.5	Bkf W	10
Dmean	2.3	Dmean	2.2	Dmean	2.0	Dmean	2.1	Dmean	2.0	Dmean	0.0
Dmax	4.0	Dmax	3.9	Dmax	4.2	Dmax	4.3	Dmax	4.2	Dmax	0.0
W/d	10.2	W/d	10.2	W/d	11.7	W/d	11.4	W/d	11.7	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL1

Reach 1 - Buckhorn Creek - Sta 12+28.7

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	6.36	97.34	PL1 IR Rt	BM	3.78	98.67	RF1 IR Lt	BM	5.91	98.55	IR Lt
HI		103.70		HI		102.45		HI		104.46	
-25	3.35	100.35		0	4.17	98.28	GRND	0	6.15	98.31	GRND
-10	4.12	99.58		1.1	4.41	98.04	GRND	1.5	6.44	98.02	GRND
-3	4.91	98.79		3.6	5.12	97.33	GRND	4.5	7.10	97.36	GRND
0	5.51	98.19	GRND	6.6	5.40	97.05	GRND	7.5	7.31	97.15	GRND
4	6.37	97.33		10.1	5.54	96.91	GRND	11.5	7.49	96.97	GRND
10.5	6.85	96.85		13.1	5.49	96.96	GRND	14.1	7.37	97.09	BKF
14.1	6.71	96.99	BKF	14.7	5.62	96.83	GRND	15.5	7.89	96.57	BNK
18.4	8.35	95.35		16.8	6.46	95.99	GRND	17.5	8.38	96.08	BNK
19.9	8.45	95.25		17.9	6.89	95.56	BKF LT	18.5	8.61	95.85	BNK
20.5	8.80	94.90	EOW	19.6	7.14	95.31	BNK	19.5	8.70	95.76	BNK
20.8	9.83	93.87		20.2	7.43	95.02	LOG	20.5	9.28	95.18	BNK
23.1	10.54	93.16		20.8	8.44	94.01	EOW	20.7	9.59	94.87	EOW
24.7	10.73	92.97		22.2	8.96	93.49	BED	21	10.44	94.02	BED
27.6	10.59	93.11		24.1	9.51	92.94	BED	22	10.96	93.50	BED
29.2	10.49	93.21		24.1	9.55	92.9	BED	24	11.61	92.85	BED
30.6	9.75	93.95		28.7	9.01	93.44	BED	25.5	11.70	92.76	BED
31.2	8.84	94.86	EOW	29.5	8.92	93.53	BED	27.5	11.06	93.40	BED
31.5	8.40	95.30		29.9	8.53	93.92	BED	29.5	11.01	93.45	BED
33.7	7.97	95.73		31.3	8.26	94.19	BED	30	11.50	92.96	BED
37.3	6.95	96.75	BKF	31.7	7.43	95.02	BED	31	10.35	94.11	BED
42.3	7.41	96.29		32.2	6.87	95.58	EOW	31.2	9.62	94.84	EOW
44.9	6.92	96.78		34.5	6.75	95.7	BNK	31.5	8.99	95.47	BNK
48.7	6.59	97.11		34.6	6.28	96.17	BNK	32.5	8.45	96.01	BNK
52	6.76	96.94		35.5	6.04	96.41	BNK	33.5	8.24	96.22	BNK
55	7.16	96.54		36.8	5.77	96.68	BKF RT	34.5	8.05	96.41	BNK
58.4	5.95	97.75		39.1	5.76	96.69	GRND	35.5	7.82	96.64	BKF
62.6	4.57	99.13		40.1	5.88	96.57	GRND	37.5	7.55	96.91	GRND
67.5	3.17	100.53		43.1	6	96.45	GRND	42.5	7.96	96.50	GRND
				44.1	5.71	96.74	GRND	46.5	7.55	96.91	GRND
				47.9	5.64	96.81	GRND	48.7	7.28	97.18	GRND
				25		97.14					

Year 3			
Station	FS/BS	Elev.	Desc.
BM	5.71	98.46	IR Lt
HI		104.17	
0	5.91	98.26	GRND
3.9	6.83	97.34	
7.9	7.12	97.05	
11.9	7.19	96.98	
14.4	7.27	96.90	BKF
15.4	7.77	96.40	BNK
17.4	8.14	96.03	
19.3	8.40	95.77	
20	8.74	95.43	
20.4	9.12	95.05	
20.5	9.38	94.79	EOW
20.8	10.14	94.03	TOE
21.4	10.53	93.64	BED
22.5	11.01	93.16	
23.7	11.38	92.79	
25.4	11.52	92.65	
26.6	11.46	92.71	THL
27.4	10.83	93.34	BED
28.6	10.78	93.39	
29.5	10.83	93.34	
30.5	10.31	93.86	
30.9	10.13	94.04	
31.1	9.37	94.80	EOW
31.4	8.69	95.48	BNK
32.2	8.19	95.98	
33.4	7.96	96.21	
34.4	7.80	96.37	
35.2	7.78	96.39	BKF
35.9	7.64	96.53	GRND
37.9	7.39	96.78	
39.9	7.54	96.63	
41.9	7.78	96.39	
48.7	7.08	97.09	

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	
0.2		98.23	
1.3		97.92	
2.2		97.80	
4.3		97.37	
5.4		97.22	
6.9		97.11	
8.3		97.07	
9.5		97.06	
10.7		96.94	
12.6		96.99	
14.3		97.05	
15.3		96.71	
16.5		96.47	
17.6		96.21	
19.2		95.96	
20.0		95.37	
20.5		94.92	
20.8		93.86	
21.8		93.44	
22.2		93.46	
22.8		93.05	
23.6		92.85	
24.6		92.85	
26.1		92.69	
26.9		92.78	
27.4		93.31	
29.2		93.31	
30.3		93.95	
31.1		94.23	
31.6		94.93	
32.6		96.03	
33.7		96.32	
34.6		96.45	
36.3		96.71	
37.6		97.00	


Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF2
 Reach 2 - Buckhorn Creek - Sta 15+89.6



Year 4

Facing Downstream

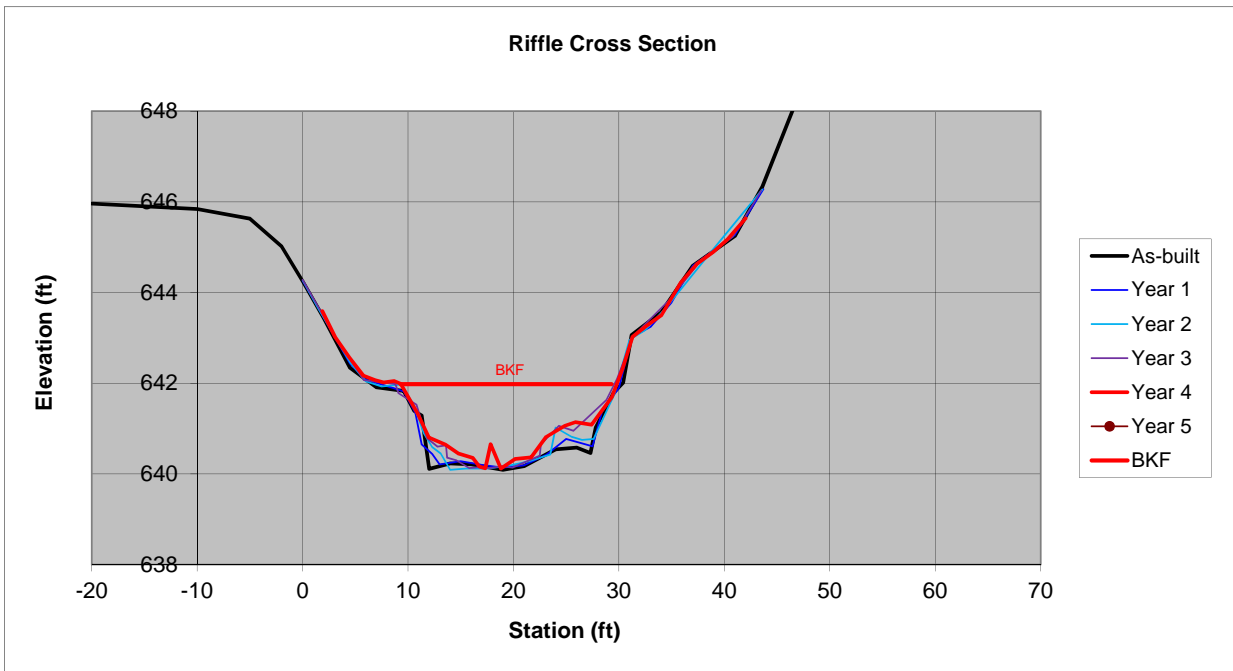

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	26.3	Area	25.4	Area	27.6	Area	21.1	Area	22.7	Area	0.0
Bkf W	19.9	Bkf W	20.4	Bkf W	20.2	Bkf W	19.7	Bkf W	20	Bkf W	10
Dmean	1.3	Dmean	1.2	Dmean	1.4	Dmean	1.1	Dmean	1.1	Dmean	0.0
Dmax	1.7	Dmax	1.7	Dmax	1.9	Dmax	1.6	Dmax	1.9	Dmax	0.0
W/d	15.1	W/d	16.4	W/d	14.8	W/d	18.4	W/d	17.6	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Riffle Cross Section RF2

Reach 2 - Buckhorn Creek - Sta 15+89.6

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	6.90	644.39	RF2 IR Lt	BM HI	6.55	644.77	PL2 IR Lt	BM HI	6.50	644.77	IR Lt
		651.29				651.32				651.27	
-20	5.33	645.96		0	7.06	644.26	GRND	0	7.00	644.27	GRND
-10	5.45	645.84		4.5	8.89	642.43	GRND	1.5	7.63	643.64	GRND
-5	5.66	645.63		6	9.24	642.08	GRND	4.5	8.81	642.46	GRND
-2	6.27	645.02		8.5	9.42	641.90	GRND	6	9.23	642.04	GRND
0	7.04	644.25	GRND	9.6	9.50	641.82	BKF LT	7.5	9.34	641.93	GRND
2	7.85	643.44		10.7	9.98	641.34	BNK	9.3	9.30	641.97	BKF
4.5	8.95	642.34		11.3	10.67	640.65	BNK	10.5	9.73	641.54	BNK
7	9.38	641.91		12.3	10.88	640.44	EOW	11.5	10.38	640.89	BNK
9.6	9.46	641.83	BKF	13	11.11	640.21	BED	12.3	10.68	640.59	BNK
10.6	9.90	641.39		15	11.04	640.28	BED	13.1	10.82	640.45	EOW
11.3	10.00	641.29	EOW	17	11.12	640.20	BED	14	11.18	640.09	BED
12	11.18	640.11		19	11.18	640.14	BED	15.5	11.15	640.12	BED
14	11.06	640.23		21	11.13	640.19	BED	17.5	11.15	640.12	BED
16	11.08	640.21		23.1	10.90	640.42	EOW	19.5	11.09	640.18	BED
19	11.20	640.09		25	10.55	640.77	BED	21.5	10.99	640.28	BED
21	11.12	640.17		27.5	10.71	640.61	BED	23.5	10.84	640.43	EOW
24	10.75	640.54		28.4	9.95	641.37	BANK	24	10.25	641.02	BED
26	10.71	640.58		30	9.42	641.90	BANK	25.5	10.45	640.82	BED
27.3	10.83	640.46	EOW	31.2	8.31	643.01	BKF RT	26.5	10.52	640.75	BED
27.8	10.27	641.02		33	8.08	643.24	GRND	27.6	10.50	640.77	BED
29.5	9.50	641.79		35	7.54	643.78	GRND	29.5	9.55	641.72	BNK
30.4	9.28	642.01		37	6.73	644.59	GRND	31	8.31	642.96	BKF
31.2	8.23	643.06	BKF	41	6.05	645.27	GRND	32.5	8.10	643.17	GRND
34	7.73	643.56		43.7	5.04	646.28	GRND	34.5	7.60	643.67	GRND
37	6.70	644.59						38.5	6.44	644.83	GRND
41	6.04	645.25						43.6	5.00	646.27	GRND
43.6	4.96	646.33	GRND								
48	2.38	648.91									

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	6.59	644.39	IR Lt
		650.98	
0	6.70	644.28	GRND
1.8	7.42	643.56	
2.8	7.85	643.13	
5.8	8.91	642.07	
8.8	9.00	641.98	
9.1	9.20	641.78	BKF
10.8	9.45	641.53	BNK
11.8	10.19	640.79	
12.8	10.38	640.60	
13.6	10.35	640.63	EOW
13.7	10.62	640.36	
14.6	10.68	640.30	BED
15.8	10.85	640.13	
16.8	10.83	640.15	
17.8	10.85	640.13	
18.9	10.81	640.17	
19.9	10.84	640.14	
22.5	10.58	640.40	
22.6	10.33	640.65	EOW
24.3	9.92	641.06	BNK
25.7	10.03	640.95	
28.8	9.35	641.63	
29.8	8.89	642.09	
31.4	7.93	643.05	GRND
34.8	7.14	643.84	
37.8	6.26	644.72	
40.8	5.75	645.23	
42.8	5	645.98	
43.5	4.73	646.25	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	
1.9		643.59	
3.1		643.02	
4.4		642.57	
5.8		642.17	
6.9		642.07	BKF
7.7		642.02	
8.7		642.05	
9.3		641.98	
10.9		641.33	
12.0		640.80	
13.5		640.65	
14.8		640.45	
16.2		640.35	
16.8		640.16	
17.3		640.13	
17.8		640.65	
18.8		640.12	
20.2		640.33	
21.7		640.37	
23.1		640.81	
24.9		641.06	
25.9		641.14	
27.4		641.09	
29.3		641.70	
30.4		642.32	BKF
31.3		643.02	
32.6		643.26	
34.0		643.50	
35.8		644.22	
37.4		644.63	
39.0		644.90	


Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL2
 Reach 2 - Buckhorn Creek - Sta 15+30.7



Year 4

Facing Downstream

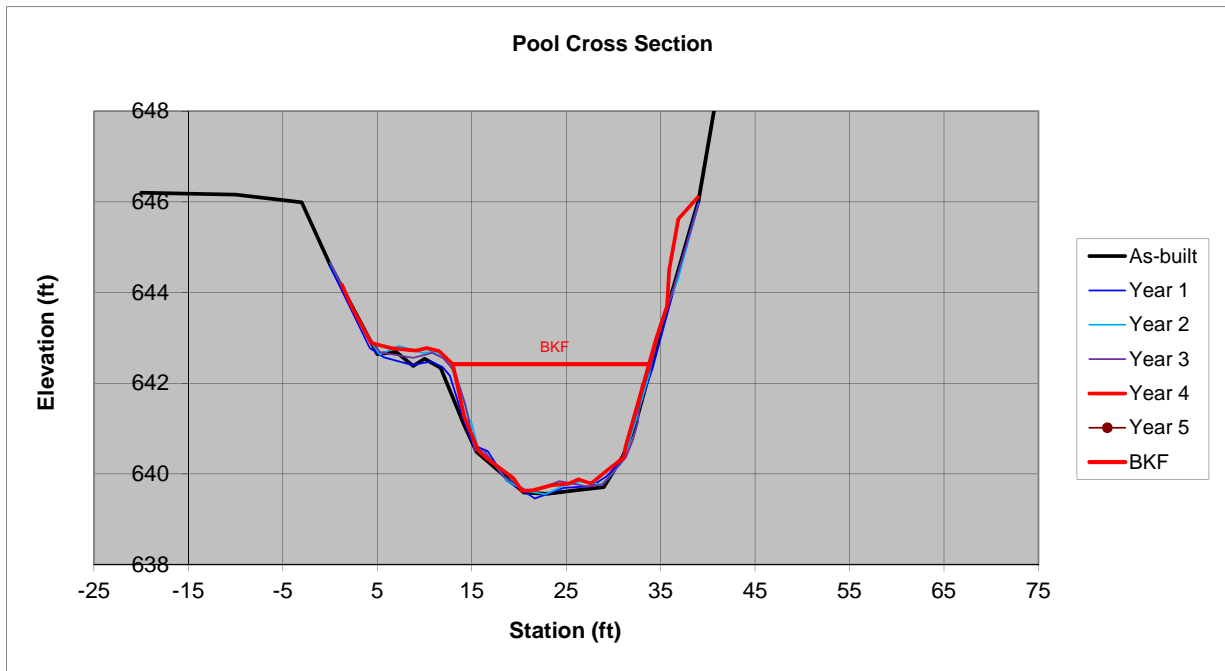

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	45.6	Area	43.8	Area	49.1	Area	47.6	Area	43.2	Area	0.0
Bkf W	23.3	Bkf W	22.2	Bkf W	22	Bkf W	22.8	Bkf W	20.6	Bkf W	10
Dmean	2.0	Dmean	2.0	Dmean	2.2	Dmean	2.1	Dmean	2.1	Dmean	0.0
Dmax	2.8	Dmax	2.9	Dmax	3.1	Dmax	2.9	Dmax	2.8	Dmax	0.0
W/d	11.9	W/d	11.2	W/d	9.9	W/d	10.9	W/d	9.8	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL2

Reach 2 - Buckhorn Creek - Sta 15+30.7

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	6.90	644.39	RF2 IR Lt	BM	6.55	644.77	PL2 IT Lt	BM	6.50	644.77	IR Lt
HI		651.29		HI		651.32		HI		651.27	
-20	5.09	646.20		0	6.75	644.57	GRND	0	6.62	644.65	GRND
-10	5.13	646.16		4.2	8.54	642.78	GRND	1.8	7.37	643.90	GRND
-3	5.30	645.99		5.7	8.75	642.57	GRND	3.8	8.23	643.04	GRND
0	6.68	644.61	GRND	8.7	8.92	642.4	GRND	5.3	8.64	642.63	GRND
5	8.65	642.64		10.7	8.84	642.48	GRND	7.3	8.45	642.82	GRND
7	8.60	642.69		11.9	8.96	642.36	BKF LT	9.8	8.60	642.67	GRND
8.8	8.91	642.38		12.7	9.16	642.16	BNK	10.8	8.58	642.69	GRND
10	8.75	642.54		14.2	10.17	641.15	EOW	11.8	8.67	642.60	BKF
11.7	8.95	642.34	BKF	15.2	10.69	640.63	BED	12.8	8.90	642.37	BNK
14.2	10.22	641.07		16.7	10.82	640.5	BED	13.8	9.43	641.84	BNK
15.5	10.80	640.49		18.7	11.47	639.85	BED	14.8	10.10	641.17	BNK
18	11.25	640.04		21.7	11.86	639.46	BED	15	10.16	641.11	EOW
20.5	11.70	639.59		24.7	11.63	639.69	BED	15.7	10.74	640.53	BED
23	11.73	639.56	BR	27.7	11.59	639.73	BED	16.8	10.90	640.37	BED
26	11.65	639.64	BR	29.3	11.37	639.95	BED	18.8	11.43	639.84	BED
29	11.58	639.71		30.9	11.01	640.31	BED	20.8	11.65	639.62	BED
31	10.90	640.39		32.2	10.14	641.18	EOW	22.8	11.72	639.55	BED
32.3	10.22	641.07	EOW	34.1	9.03	642.29	BNK	24.8	11.53	639.74	BED
35	8.15	643.14		36.7	7.01	644.31	BNK	26.8	11.43	639.84	BED
38	5.98	645.31		39	5.32	646	GRND	28.8	11.51	639.76	BED
39	5.27	646.02						29.8	11.28	639.99	BED
40.8	3.10	648.19						30.8	11.04	640.23	BED
								31.3	10.81	640.46	BED
								32.3	10.15	641.12	EOW
								33.8	9.06	642.21	BNK
								34.8	8.05	643.22	BNK
								36.8	7.00	644.27	BNK
								39	5.31	645.96	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM	6.41	644.77	IR Lt
HI		651.18	
0	6.51	644.67	GRND
3.3	7.92	643.26	
5.3	8.50	642.68	
8.8	8.62	642.56	
10.8	8.51	642.67	
12	8.63	642.55	BKF
13.2	8.92	642.26	BNK
14.3	9.64	641.54	
14.7	10.01	641.17	EOW
15.3	10.66	640.52	BED
16.3	10.67	640.51	
18.3	11.22	639.96	
20.8	11.55	639.63	
21.8	11.54	639.64	
24.3	11.34	639.84	
27.3	11.46	639.72	THL
28.8	11.41	639.77	BED
31.3	10.82	640.36	
32.1	10.41	640.77	
32.6	10.03	641.15	EOW
33	9.22	641.96	BNK
33.8	8.91	642.27	
34.8	8.12	643.06	
36.3	7.13	644.05	
39	5.24	645.94	GRND

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	
1.3		644.17	
2.3		643.67	
4.4		642.89	
6.5		642.77	
7.7		642.75	
9.1		642.72	
10.2		642.77	
11.5		642.71	
13.0		642.42	BKF
14.2		641.26	
15.7		640.52	
16.5		640.36	
19.4		639.91	
20.3		639.63	
21.5		639.64	
23.4		639.75	
25.3		639.79	
26.3		639.88	
27.6		639.79	
29.5		640.10	
31.1		640.37	
31.3		640.60	
33.4		642.13	
34.5		642.96	
35.7		643.71	
35.9		644.50	
36.9		645.62	
38.9		646.103	


Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF3
 Reach 3 - Buckhorn Creek - Sta 12+50.7



Year 4

Facing Downstream

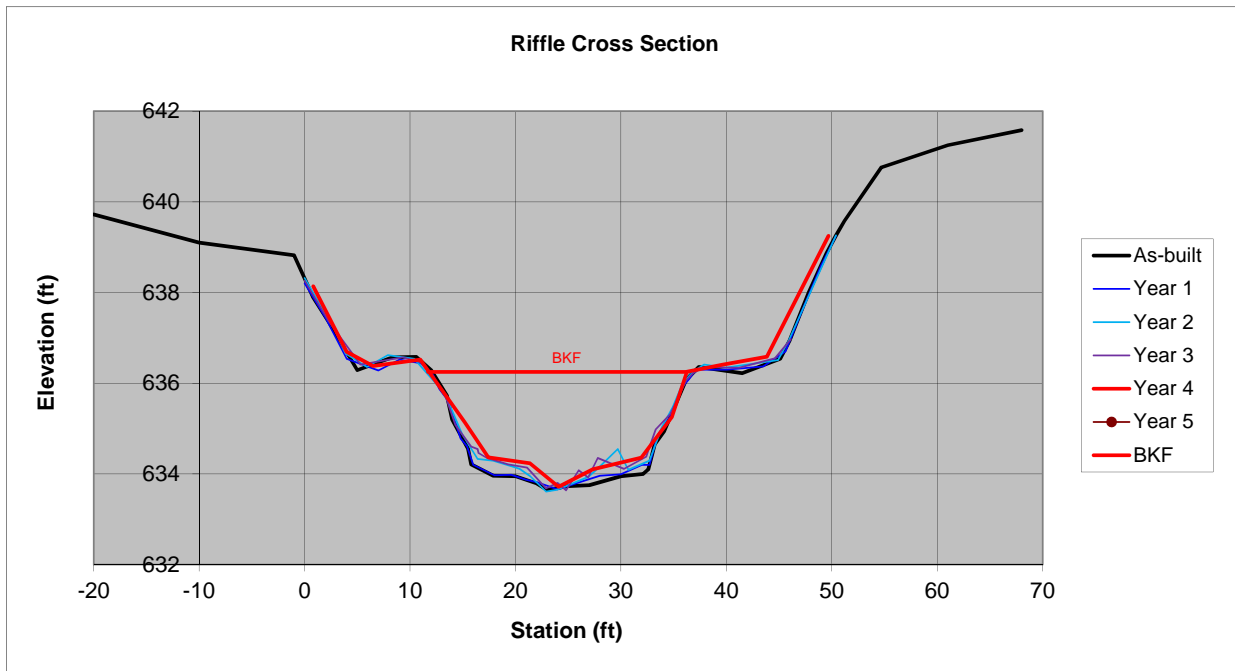

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	48.3	Area	47.5	Area	47.7	Area	45.2	Area	39.0	Area	0.0
Bkf W	25.4	Bkf W	25.5	Bkf W	27.5	Bkf W	26.8	Bkf W	24.55	Bkf W	10
Dmean	1.9	Dmean	1.9	Dmean	1.7	Dmean	1.7	Dmean	1.6	Dmean	0.0
Dmax	2.6	Dmax	2.6	Dmax	2.8	Dmax	2.7	Dmax	2.5	Dmax	0.0
W/d	13.4	W/d	13.7	W/d	15.9	W/d	15.9	W/d	15.5	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC
Riffle Cross Section RF3

Reach 3 - Buckhorn Creek - Sta 12+50.7

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	5.88	638.55	RF3 IR Lt	BM HI	3.92	638.55	RF3 IR Lt	BM HI	3.11	638.55	IR Lt
		644.43				642.47				641.66	
-20	4.71	639.72	GRND	0	4.27	638.20	GRND	0	3.34	638.32	GRND
-10	5.33	639.10		2	5.04	637.43	GRND	2.9	4.50	637.16	GRND
-1	5.61	638.82		4	5.93	636.54	GRND	3.9	5.01	636.65	GRND
0	6.12	638.31		7	6.19	636.28	GRND	5.9	5.30	636.36	GRND
0.8	6.53	637.90		9	5.95	636.52	GRND	7.9	5.04	636.62	GRND
2.3	7.08	637.35		11	6.03	636.44	BKF LT?	10.4	5.12	636.54	GRND
5	8.14	636.29		11.6	6.14	636.33	BKF LT	12.9	5.78	635.88	GRND
8.3	7.86	636.57		12.2	6.29	636.18	BKF LT	13.5	6.00	635.66	BKF
10.6	7.85	636.58		12.8	6.60	635.87	BANK	14.9	6.77	634.89	BNK
12	8.14	636.29		13.6	6.85	635.62	BANK	16.4	7.33	634.33	BED
13.5	8.70	635.73	BKF	14.8	7.69	634.78	BANK	17.9	7.37	634.29	BED
14	9.23	635.20		15.4	7.86	634.61	BANK	19.9	7.51	634.15	BED
15.5	9.87	634.56		16	8.27	634.20	EOW	20.4	7.55	634.11	EOW
15.8	10.22	634.21		18	8.50	633.97	BED	21.4	7.71	633.95	BED
16.9	10.35	634.08		19.6	8.49	633.98	BED	22.9	8.05	633.61	BED
17.9	10.47	633.96		21	8.60	633.87	BED	23.9	8.01	633.65	BED
20	10.48	633.95		22	8.65	633.82	BED	24.9	7.92	633.74	BED
22	10.64	633.79		24	8.81	633.66	BED	26.9	7.73	633.93	BED
23	10.78	633.65		26	8.66	633.81	BED	27.9	7.52	634.14	BED
25	10.70	633.73		28	8.51	633.96	BED	29.7	7.11	634.55	BED
27	10.68	633.75	30	8.48	633.99	BED	30.7	7.57	634.09	BED	
30	10.48	633.95	32	8.27	634.20	BED	32.7	7.37	634.29	BED	
32.1	10.43	634.00	32.7	8.27	634.20	TOE	33.9	6.62	635.04	BNK	
32.6	10.33	634.10	33.5	7.61	634.86	BNK	34.9	6.19	635.47	BNK	
33.2	9.78	634.65	34.8	7.16	635.31	BNK	35.9	5.64	636.02	BKF	
34.1	9.49	634.94	35.8	6.56	635.91	BNK	36.9	5.40	636.26	GRND	
36.2	8.35	636.08	36.5	6.37	636.10	BNK	37.9	5.25	636.41	GRND	
37.4	8.07	636.36	37.1	6.17	636.30	BKF	39.9	5.32	636.34	GRND	
41.5	8.21	636.22	40	6.17	636.30	GRND	44.9	5.15	636.51	GRND	
45.1	7.89	636.54	43.5	6.1	636.37	GRND	45.9	4.73	636.93	GRND	
46	7.49	636.94	45.6	5.77	636.70	GRND	50.4	2.40	639.26	GRND	
47.8	6.43	638.00	47	4.97	637.50	GRND					
49.5	5.56	638.87	49	3.87	638.60	GRND					
50.4	5.17	639.26	50.4	3.22	639.25	GRND					
51.2	4.85	639.58									
54.7	3.67	640.76									
61	3.18	641.25									
68	2.85	641.58									

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	3.29	638.55	IR Lt
		641.84	
0	3.58	638.26	GRND
2.3	4.48	637.36	
5.3	5.43	636.41	
9.3	5.27	636.57	
11	5.38	636.46	BKF
12.3	5.75	636.09	BNK
13.4	6.15	635.69	
14.3	6.76	635.08	
15.8	7.24	634.60	
16.4	7.29	634.55	EOW
16.5	7.38	634.46	BED
17.3	7.49	634.35	
19.3	7.63	634.21	
21.1	7.70	634.14	
22.9	8.16	633.68	
24	8.04	633.80	
24.8	8.20	633.64	THL
26	7.76	634.08	BED
26.9	7.92	633.92	
27.8	7.49	634.35	
30.3	7.73	634.11	
32.4	7.46	634.38	
32.6	7.32	634.52	EOW
33.3	6.86	634.98	BNK
34.7	6.52	635.32	
36.2	5.78	636.06	BKF
36.8	5.63	636.21	GRND
37.8	5.49	636.35	
41.2	5.5	636.34	
44.6	5.29	636.55	
46.1	4.87	636.97	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	
0.83		638.14	
3.98		636.70	
6.49		636.38	
10.97		636.52	BKF
15.2		635.14	
17.43		634.37	
21.37		634.23	
24.09		633.72	
27.32		634.10	
31.93		634.36	
34.84		635.26	
36.25		636.25	BKF
39.63		636.41	
43.84		636.58	
49.69		639.25	


Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL3
 Reach 3 - Buckhorn Creek - Sta 13+33.1



Year 4

Facing Downstream

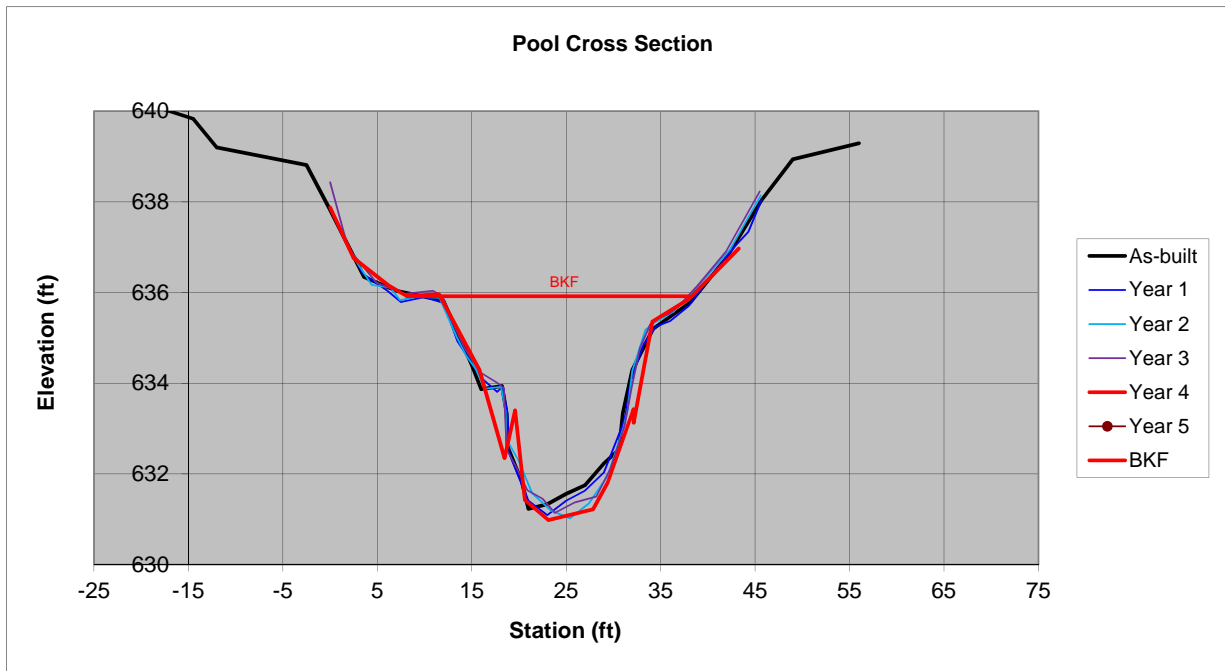

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	62.7	Area	62.8	Area	66.2	Area	66.2	Area	64.9	Area	0.0
Bkf W	22.2	Bkf W	22.5	Bkf W	22.8	Bkf W	22.9	Bkf W	29.9	Bkf W	10
Dmean	2.8	Dmean	2.8	Dmean	2.9	Dmean	2.9	Dmean	2.2	Dmean	0.0
Dmax	4.6	Dmax	4.7	Dmax	4.9	Dmax	4.8	Dmax	4.8	Dmax	0.0
W/d	7.9	W/d	8.1	W/d	7.9	W/d	7.9	W/d	13.8	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL3

Reach 3 - Buckhorn Creek - Sta 13+33.1

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	5.88	638.55	RF3 IR Lt	BM	3.92	638.55	PL2 IT Lt	BM	3.11	638.55	IR Lt
HI		644.43		HI		642.47		HI		641.66	
-20	4.23	640.20		0	4.62	637.85	GRND	0	3.82	637.84	GRND
-14.5	4.60	639.83		2	5.48	636.99	GRND	2.4	4.86	636.80	GRND
-12	5.23	639.20		3.5	6.06	636.41	GRND	4.4	5.49	636.17	GRND
-2.5	5.62	638.81		6	6.42	636.05	GRND	6.4	5.55	636.11	GRND
0	6.61	637.82		7.5	6.68	635.79	GRND	7.4	5.83	635.83	GRND
3.6	8.09	636.34		10	6.57	635.9	GRND	9.4	5.75	635.91	GRND
7	8.39	636.04		12	6.70	635.77	BKF LT	11.6	5.78	635.88	BKF
12	8.61	635.82	BKF	13.5	7.55	634.92	BNK	13.4	6.64	635.02	BNK
15	10.03	634.40		16	8.35	634.12	BNK	14.4	7.05	634.61	BNK
16	10.56	633.87		17.7	8.66	633.81	BNK	15.4	7.34	634.32	BNK
18.2	10.49	633.94	LOG	18.3	8.54	633.93	LOG	16.4	7.78	633.88	BED
18.7	11.09	633.34	EOW	18.8	9.17	633.3	EOW	18.1	7.74	633.92	LOG
18.8	11.83	632.60		19	10.03	632.44	BED	18.6	8.29	633.37	EOW
20.3	12.60	631.83		21	11.06	631.41	BED	18.7	8.90	632.76	BED
21	13.20	631.23		23	11.38	631.09	BED	19.9	9.34	632.32	BED
23	13.10	631.33		25	11.06	631.41	BED	21.4	10.09	631.57	BED
25	12.87	631.56		27	10.84	631.63	BED	23.4	10.47	631.19	BED
27	12.68	631.75		29	10.44	632.03	BED	25.4	10.64	631.02	BED
29	12.20	632.23		31	9.38	633.09	BED	27.4	10.31	631.35	BED
30.6	11.89	632.54		31.3	9.14	633.33	EOW	29.4	9.70	631.96	BED
31	11.09	633.34	EOW	31.8	8.44	634.03	BNK	31.1	8.61	633.05	BED
32	10.14	634.29		33.2	7.61	634.86	BNK	31.5	8.25	633.41	EOW
34.2	9.23	635.20	BKF	34.5	7.22	635.25	BKF RT	32	7.39	634.27	BNK
38.2	8.64	635.79		36	7.10	635.37	GRND	33.4	6.48	635.18	BNK
42	7.65	636.78		38	6.76	635.71	GRND	34.4	6.32	635.34	BKF
45.7	6.39	638.04	GRND	40	6.19	636.28	GRND	36.4	6.08	635.58	GRND
49	5.49	638.94		43	5.42	637.05	GRND	39.4	5.42	636.24	GRND
56	5.14	639.29		44.3	5.13	637.34	GRND	42.4	4.70	636.96	GRND
66	4.82	639.61		45.7	4.42	638.05	GRND	45.6	3.52	638.14	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM	5.64	638.14	IR Lt
HI		643.78	
0	5.35	638.43	GRND
1.9	6.80	636.98	
4.9	7.56	636.22	
7.9	7.81	635.97	
10.9	7.74	636.04	
11.4	7.80	635.98	BKF
11.9	7.87	635.91	BNK
12.9	8.41	635.37	
14.3	9.03	634.75	
15.9	9.54	634.24	
17.7	9.77	634.01	
18.4	9.89	633.89	EOW
18.7	11.25	632.53	BED
19.7	11.62	632.16	
20.9	12.14	631.64	
22.5	12.33	631.45	
23.8	12.64	631.14	THL
25.9	12.41	631.37	BED
28.2	12.28	631.50	
29.7	11.65	632.13	
31.2	10.71	633.07	
31.9	9.90	633.88	EOW
32.8	9.01	634.77	BNK
33.9	8.48	635.30	
34.8	8.34	635.44	
35.4	8.29	635.49	BKF
35.9	8.25	635.53	GRND
36.9	8.08	635.7	
38.9	7.63	636.15	
41.9	6.88	636.9	
45.5	5.55	638.23	

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00		IR Lt
HI		0.00	
0		637.88	
2.48		636.76	
6.17		636.16	
8.12		635.92	
11.52		635.97	
15.82		634.30	
18.48		632.35	
19.6		633.40	
20.62		631.42	
23.12		630.98	
27.85		631.22	
29.4		631.81	
32.13		633.43	
32.14		633.13	
34.13		635.36	BKF
38.02		635.86	
43.27		636.97	

Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	

Holly Grove Stream Restoration Site

Guilford County, NC

Riffle Cross Section RF4


Reach 4 - Middle Branch - Sta 10+89.9



Year 4

Facing Downstream

Riffle Cross Section

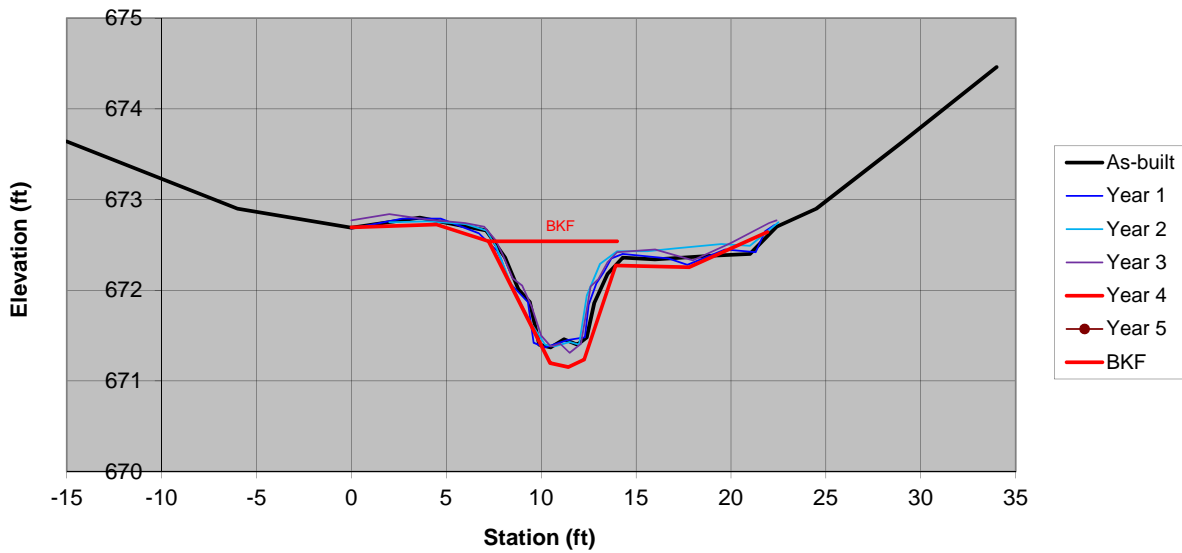

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	3.7	Area	3.5	Area	3.8	Area	3.7	Area	3.7	Area	0.0
Bkf W	6.2	Bkf W	6.4	Bkf W	6.9	Bkf W	6	Bkf W	6	Bkf W	10
Dmean	0.6	Dmean	0.5	Dmean	0.5	Dmean	0.6	Dmean	0.6	Dmean	0.0
Dmax	1.0	Dmax	1.0	Dmax	1.0	Dmax	1.1	Dmax	1.4	Dmax	0.0
W/d	10.4	W/d	11.8	W/d	12.6	W/d	9.9	W/d	9.6	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC
Riffle Cross Section RF4

Reach 4 - Middle Branch - Sta 10+89.9

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	3.96	674.94	BP4 IR Lt	BM HI	4.31	674.77	BP4 IR Rt	BM HI	4.75	674.77	IR Rt
		678.90				679.08				679.52	
-15	5.26	673.64		0	6.40	672.68	GRND	2	6.77	672.75	GRND
-6	6.00	672.90		2.7	6.29	672.79	GRND	4	6.76	672.76	GRND
0	6.21	672.69		4.7	6.29	672.79	GRND	6	6.79	672.73	GRND
3.6	6.10	672.80		6.7	6.45	672.63	GRND	7.1	6.86	672.66	BKF
7.1	6.24	672.66		7.7	6.65	672.43	GRND	7.6	7.03	672.49	BNK
8.1	6.54	672.36	bkf	7.9	6.74	672.34	BKF LT	8.3	7.40	672.12	BNK
8.8	6.89	672.01		8.3	6.99	672.09	BNK	9.4	7.86	671.66	BNK
9.4	7.03	671.87		9.3	7.21	671.87	BNK	10.2	8.12	671.40	BED
9.9	7.50	671.40		9.6	7.66	671.42	BED	10.7	8.14	671.38	BED
10.5	7.53	671.37		10.2	7.71	671.37	BED	11.5	8.09	671.43	BED
11.2	7.44	671.46		10.8	7.67	671.41	BED	12	8.12	671.40	BED
11.9	7.50	671.40		11.4	7.63	671.45	BED	12.4	7.58	671.94	BNK
12.4	7.42	671.48		12.3	7.60	671.48	BED	13.1	7.23	672.29	BNK
12.8	7.04	671.86		12.5	7.24	671.84	BNK	14	7.09	672.43	BKF
13.5	6.72	672.18		12.9	7.01	672.07	BKF	15.6	7.09	672.43	GRND
14.3	6.54	672.36	bkf	13.3	6.88	672.20	GRND	17	7.06	672.46	GRND
16	6.56	672.34		13.7	6.73	672.35	GRND	19.5	7.01	672.51	GRND
19	6.52	672.38		14.3	6.68	672.40	GRND	21	7.03	672.49	GRND
21	6.50	672.40		16.7	6.73	672.35	GRND	22.5	6.77	672.75	GRND
22.4	6.20	672.70		17.7	6.80	672.28	GRND				
24.5	6.00	672.90		19.7	6.63	672.45	GRND				
29	5.27	673.63		21.3	6.66	672.42	GRND				
34	4.44	674.46		21.8	6.43	672.65	GRND				
				22.3	6.36	672.72	GRND				

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	6.00	673.10	IR Lt
		679.10	
0	6.33	672.77	GRND
2	6.26	672.84	
4	6.32	672.78	
6	6.36	672.74	
7	6.40	672.70	BKF
7.6	6.55	672.55	BNK
8	6.72	672.38	
8.5	6.97	672.13	
9	7.05	672.05	
9.5	7.28	671.82	
10	7.60	671.50	TOE
10.5	7.72	671.38	BED
11	7.69	671.41	THL
11.5	7.79	671.31	BED
12.1	7.69	671.41	
12.6	7.06	672.04	BNK
13	6.98	672.12	
13.5	6.79	672.31	BNK
14	6.68	672.42	BKF
16	6.65	672.45	GRND
18	6.77	672.33	
20	6.58	672.52	
22	6.36	672.74	
22.4	6.33	672.77	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	
0		672.69	
4.48		672.72	
7.23		672.54	BKF
10.47		671.20	
11.43		671.15	
12.27		671.24	
13.93		672.27	BKF
17.8		672.25	
21.92		672.64	

Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL4


Reach 4 - Middle Branch - Sta 11+14.3



Year 4

Facing Downstream

Pool Cross Section

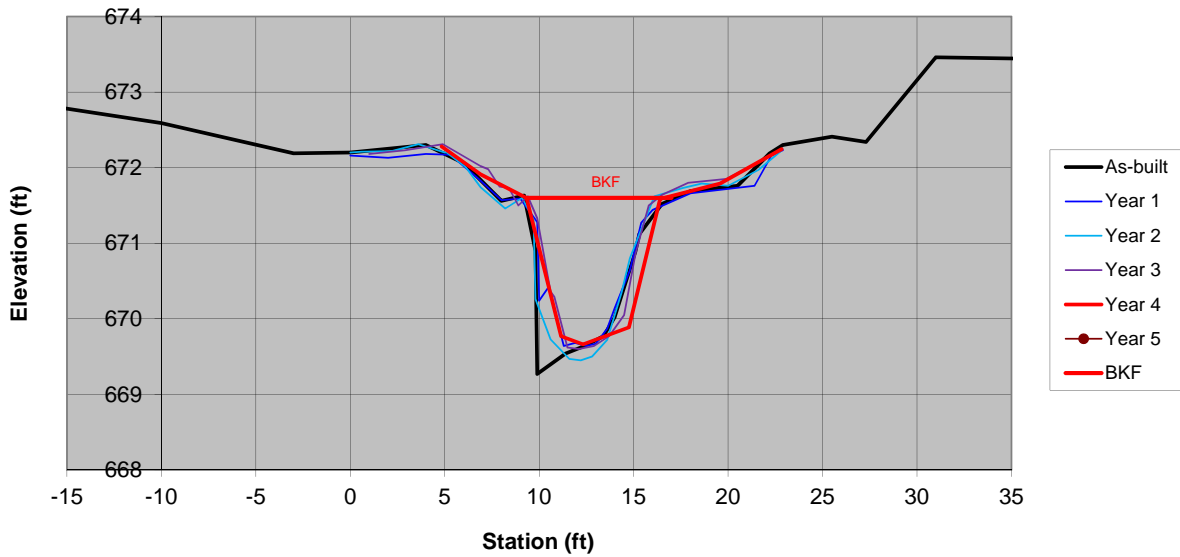

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	11.2	Area	9.4	Area	11.1	Area	10.2	Area	9.7	Area	0.0
Bkf W	10.5	Bkf W	10.5	Bkf W	10.7	Bkf W	10	Bkf W	7.67	Bkf W	10
Dmean	1.1	Dmean	0.9	Dmean	1.0	Dmean	1.0	Dmean	1.3	Dmean	0.0
Dmax	2.4	Dmax	2.0	Dmax	2.3	Dmax	2.2	Dmax	1.9	Dmax	0.0
W/d	9.9	W/d	11.8	W/d	10.3	W/d	9.8	W/d	6.0	W/d	0.0


Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF5
 Reach 5 - Middle Branch - Sta 11+68.1



Year 4

Facing Downstream

Riffle Cross Section

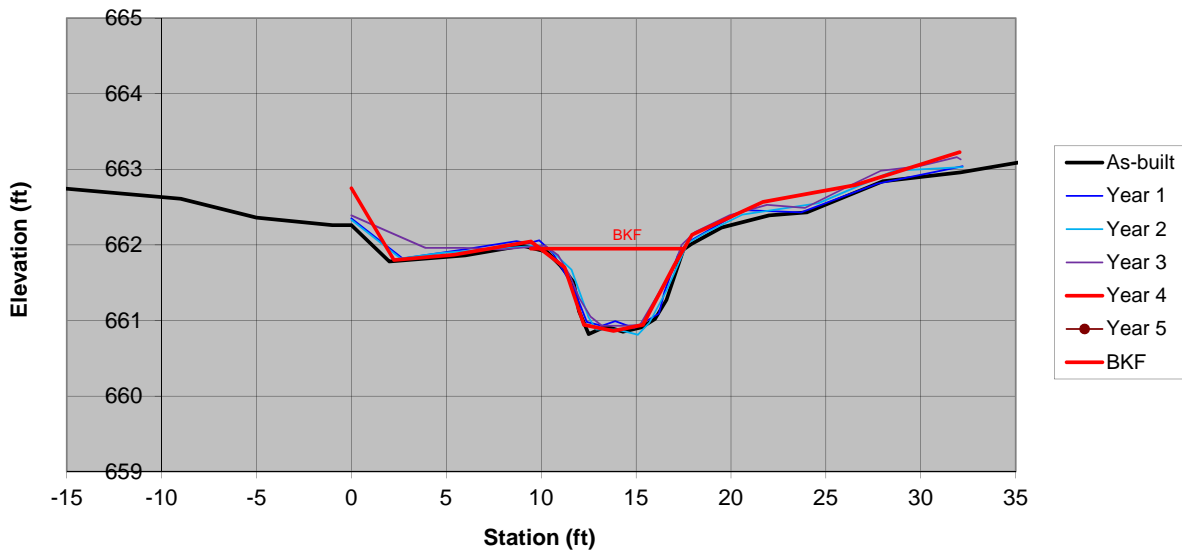

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	6.0	Area	5.9	Area	5.6	Area	4.9	Area	5.0	Area	0.0
Bkf W	8.9	Bkf W	8.2	Bkf W	7.9	Bkf W	7.2	Bkf W	8.04	Bkf W	10
Dmean	0.7	Dmean	0.7	Dmean	0.7	Dmean	0.7	Dmean	0.6	Dmean	0.0
Dmax	1.2	Dmax	1.2	Dmax	1.2	Dmax	1.1	Dmax	1.1	Dmax	0.0
W/d	13.2	W/d	11.5	W/d	11.1	W/d	10.5	W/d	12.8	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC
Riffle Cross Section RF5

Reach 5 - Middle Branch - Sta 11+68.1

As-Built			
Station	FS/BS	Elev.	Desc.
BM HI	2.82	665.59	BP5 IR Lt
		668.41	
-18	5.60	662.81	
-9	5.80	662.61	
-5	6.05	662.36	
-1	6.15	662.26	
0	6.15	662.26	
2	6.63	661.78	
6	6.55	661.86	
9	6.42	661.99	
10.3	6.50	661.91	
11	6.68	661.73	
11.7	6.90	661.51	
12	7.29	661.12	
12.5	7.59	660.82	
13.4	7.49	660.92	
14.3	7.56	660.85	
15.3	7.50	660.91	
16	7.39	661.02	
16.6	7.14	661.27	
17.5	6.47	661.94	
17.9	6.40	662.01	
19.5	6.18	662.23	
22	6.02	662.39	
24	5.98	662.43	
28	5.57	662.84	
32.1	5.45	662.96	
37	5.24	663.17	
42	5.42	662.99	
52	5.3	663.11	

Year 1			
Station	FS/BS	Elev.	Desc.
BM HI	3.98	665.59	BP5 IR Lt
		669.57	
0	7.22	662.35	GRND
2.7	7.75	661.82	GRND
5.7	7.64	661.93	GRND
8.7	7.52	662.05	GRND
9.3	7.55	662.02	GRND
9.9	7.51	662.06	BKF LT
10.6	7.67	661.90	BNK
11.7	8.14	661.43	BNK
12.4	8.59	660.98	BED
13.2	8.64	660.93	BED
13.9	8.58	660.99	BED
14.9	8.67	660.90	BED
16.2	8.48	661.09	BED
16.5	8.19	661.38	BANK
17.2	7.71	661.86	BANK
17.7	7.54	662.03	BANK
18.1	7.48	662.09	BKF RT
19	7.35	662.22	GRND
20.7	7.11	662.46	GRND
23.7	7.14	662.43	GRND
27.7	6.76	662.81	GRND
32.2	6.53	663.04	GRND

Year 2			
Station	FS/BS	Elev.	Desc.
BM HI	5.57	662.74	IR Lt
		668.31	
0	5.98	662.33	GRND
2.6	6.49	661.82	GRND
4.6	6.42	661.89	GRND
9.8	6.32	661.99	GRND
10.5	6.38	661.93	BKF
11.6	6.64	661.67	BNK
12.5	7.27	661.04	BED
12.9	7.43	660.88	BED
14	7.43	660.88	BED
15.1	7.50	660.81	BED
15.7	7.34	660.97	TOE
16.6	6.92	661.39	BNK
17.7	6.29	662.02	BNK
18.6	6.16	662.15	BKF
20.6	5.91	662.40	GRND
24.6	5.76	662.55	GRND
28.6	5.33	662.98	GRND
32.2	5.28	663.03	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	5.66	662.65	IR Lt
		668.31	
0	5.92	662.39	GRND
1.9	6.13	662.18	
3.9	6.35	661.96	
5.9	6.35	661.96	
7.9	6.37	661.94	
10.2	6.32	661.99	BKF
10.9	6.45	661.86	BNK
11.5	6.71	661.60	
12	7.01	661.30	TOE
12.6	7.26	661.05	
13.2	7.38	660.93	
14.3	7.38	660.93	
15.2	7.37	660.94	BANK
16.3	6.90	661.41	BNK
16.9	6.67	661.64	BNK
17.4	6.31	662.00	BNK
18.1	6.14	662.17	BKF
19.9	5.92	662.39	GRND
21.9	5.78	662.53	
23.9	5.82	662.49	
25.9	5.57	662.74	
27.9	5.33	662.98	
29.9	5.27	663.04	
31.9	5.15	663.16	
32.1	5.18	663.13	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	0.00	IR Lt
0		662.75	
2.24		661.80	
5.41		661.87	
9.46		662.05	BKF
11.23		661.70	
12.25		660.94	
13.81		660.86	
15.36		660.94	
17.02		661.73	BKF
17.95		662.13	
21.68		662.57	
26.53		662.79	
32.05		663.23	

Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL5


Reach 5 - Middle Branch - Sta 10+63.1



Year 4

Facing Downstream

Pool Cross Section

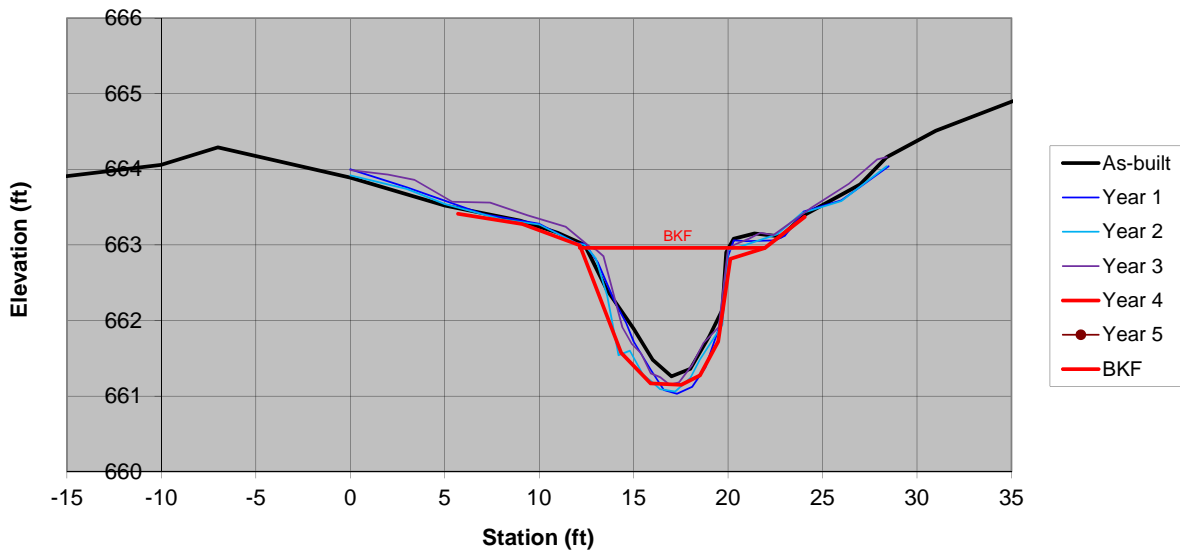


As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/11/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	8.4	Area	9.7	Area	10.1	Area	8.5	Area	10.6	Area	0.0
Bkf W	7.9	Bkf W	8.6	Bkf W	8.4	Bkf W	7.3	Bkf W	9.78	Bkf W	10
Dmean	1.1	Dmean	1.1	Dmean	1.2	Dmean	1.2	Dmean	1.1	Dmean	0.0
Dmax	1.7	Dmax	2.0	Dmax	1.9	Dmax	1.8	Dmax	1.8	Dmax	0.0
W/d	7.4	W/d	7.6	W/d	7.0	W/d	6.3	W/d	9.0	W/d	0.0

Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF6
 Reach 6 - Lower East Branch - Sta 11+07.2



Year 4

Facing Downstream

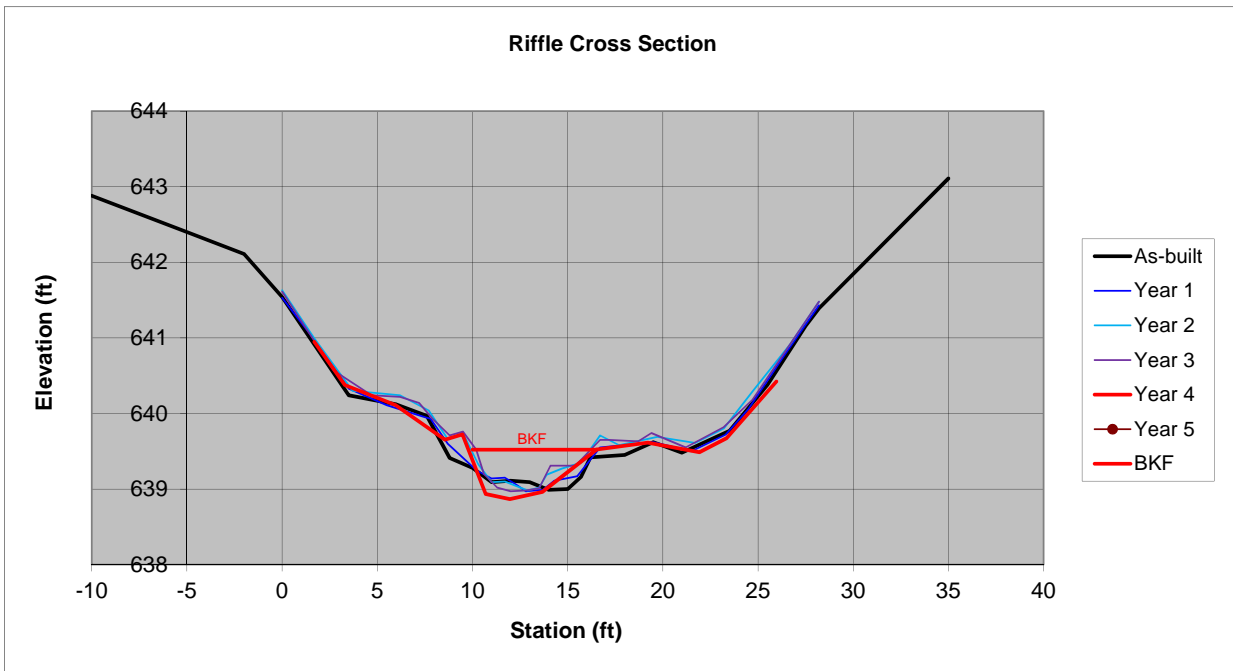

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	4.0	Area	2.8	Area	3.0	Area	2.9	Area	2.6	Area	0.0
Bkf W	10.7	Bkf W	8	Bkf W	8	Bkf W	7.7	Bkf W	6.52	Bkf W	10
Dmean	0.4	Dmean	0.4	Dmean	0.4	Dmean	0.4	Dmean	0.4	Dmean	0.0
Dmax	0.6	Dmax	0.6	Dmax	0.7	Dmax	0.7	Dmax	0.7	Dmax	0.0
W/d	28.5	W/d	22.7	W/d	21.6	W/d	20.3	W/d	16.3	W/d	0.0

Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF6
 Reach 6 - Lower East Branch - Sta 11+07.2

As-Built			
Station	FS/BS	Elev.	Desc.
BM HI	5.02	643.14	BP6 IR Lt
-10	5.28	642.88	
-5	5.76	642.40	
-2	6.05	642.11	
0	6.62	641.54	
3.5	7.92	640.24	
6	8.04	640.12	
7.6	8.19	639.97	
8.8	8.75	639.41	
10	8.88	639.28	
11	9.07	639.09	
12	9.05	639.11	
13	9.07	639.09	
14	9.17	638.99	
15	9.16	639.00	
15.7	9.00	639.16	
16.2	8.74	639.42	
18	8.71	639.45	
19.5	8.54	639.62	
21	8.68	639.48	
23.5	8.39	639.77	
25.5	7.78	640.38	
27.5	7.00	641.16	
28.2	6.77	641.39	
35	5.05	643.11	

Year 1			
Station	FS/BS	Elev.	Desc.
BM HI	6.06	643.14	BP6 IR Lt
0	7.67	641.53	GRND
1.5	8.16	641.04	GRND
3.5	8.87	640.33	GRND
5.5	9.09	640.11	GRND
7.5	9.25	639.95	GRND
7.8	9.27	639.93	BKF LT
8.7	9.60	639.60	BNK
9.6	9.81	639.39	BNK
10.2	9.95	639.25	BED
11	10.06	639.14	BED
11.7	10.05	639.15	BED
12.3	10.14	639.06	BED
12.8	10.23	638.97	BED
13.7	10.21	638.99	BED
14.3	10.09	639.11	BED
15.5	10.03	639.17	BNK
16.7	9.65	639.55	BKF RT
19.5	9.58	639.62	GRND
21.5	9.70	639.50	GRND
23.3	9.48	639.72	GRND
24.5	9.14	640.06	GRND
26.3	8.46	640.74	GRND
28.2	7.77	641.43	GRND

Year 2			
Station	FS/BS	Elev.	Desc.
BM HI	4.08	641.78	IR Lt
0	4.23	641.63	GRND
1.7	4.87	640.99	GRND
3.7	5.56	640.30	GRND
6.2	5.62	640.24	GRND
7.7	5.82	640.04	GRND
8.7	6.20	639.66	BKF
9.5	6.12	639.74	BNK
10.3	6.53	639.33	BED
11	6.77	639.09	BED
11.7	6.76	639.10	BED
12.9	6.88	638.98	BED
13.5	6.84	639.02	BED
13.9	6.67	639.19	BED
14.7	6.59	639.27	BNK
15.7	6.51	639.35	BNK
16.7	6.15	639.71	BKF
17.7	6.28	639.58	GRND
19.7	6.17	639.69	GRND
21.7	6.25	639.61	GRND
23.2	6.06	639.80	GRND
24.7	5.57	640.29	GRND
26.7	4.94	640.92	GRND
28.2	4.38	641.48	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	6.17	641.78	IR Lt
		647.95	
0	6.34	641.61	GRND
2.7	7.38	640.57	
4.7	7.71	640.24	
6.2	7.73	640.22	
7.2	7.81	640.14	BKF
7.9	8.02	639.93	BNK
8.8	8.24	639.71	
9.5	8.19	639.76	
10.2	8.43	639.52	
10.6	8.75	639.20	TOE
11.3	8.93	639.02	BED
12	8.98	638.97	THL
12.8	8.97	638.98	BED
13.5	8.94	639.01	TOE
14.1	8.64	639.31	BNK
15.4	8.64	639.31	
16.7	8.30	639.65	
17.2	8.30	639.65	BKF
18.7	8.32	639.63	GRND
19.4	8.21	639.74	
21.2	8.40	639.55	
23.2	8.13	639.82	
24.7	7.77	640.18	
28.2	6.47	641.48	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	0.00	IR Lt
1.69		640.95	
3.3		640.38	
5.95		640.11	
8.56		639.65	BKF
9.47		639.72	
10.69		638.93	
11.96		638.87	
13.67		638.96	
16.52		639.52	BKF
19.21		639.61	
21.92		639.49	
23.35		639.67	
25.96		640.42	


Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL6
 Reach 6 - Lower East Branch - Sta 11+33.0



Year 4

Facing Downstream

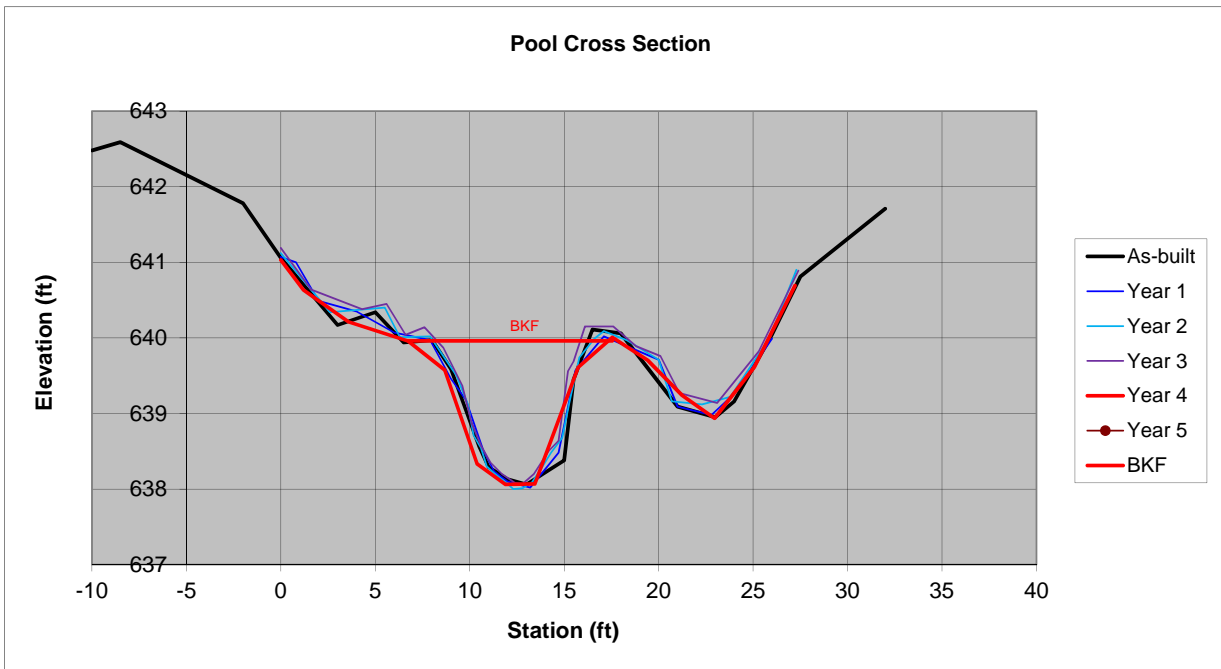

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	10.2	Area	10.0	Area	10.2	Area	10.3	Area	10.5	Area	0.0
Bkf W	8.5	Bkf W	9.2	Bkf W	9.2	Bkf W	10	Bkf W	10.82	Bkf W	10
Dmean	1.2	Dmean	1.1	Dmean	1.1	Dmean	1.0	Dmean	1.0	Dmean	0.0
Dmax	1.9	Dmax	2.0	Dmax	2.0	Dmax	2.1	Dmax	1.9	Dmax	0.0
W/d	7.1	W/d	8.5	W/d	8.3	W/d	9.7	W/d	11.1	W/d	0.0

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL6
 Reach 6 - Lower East Branch - Sta 11+33.0

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	5.02	643.14	BP6 IR Lt	BM	6.06	643.14	BP6 IR Lt	BM	3.25	641.75	IR Lt
HI		648.16		HI		649.20		HI		645.00	
-10	5.68	642.48		0	8.13	641.07	GRND	0	3.88	641.12	GRND
-8.5	5.57	642.59		0.8	8.20	641	GRND	2.6	4.66	640.34	GRND
-2	6.38	641.78		2	8.71	640.49	GRND	5.5	4.60	640.40	GRND
0	7.10	641.06		4	8.85	640.35	GRND	6.3	4.99	640.01	GRND
3	7.99	640.17		6	9.13	640.07	GRND	7.9	4.98	640.02	BKF
5	7.82	640.34		7.9	9.23	639.97	BKF LT	9.3	5.50	639.50	BNK
6.5	8.22	639.94		9	9.74	639.46	BNK	9.9	5.88	639.12	BNK
8	8.19	639.97		9.8	10.02	639.18	BNK	10.2	6.29	638.71	BNK
9	8.57	639.59		10.7	10.68	638.52	BNK	10.6	6.46	638.54	BED
10.5	9.60	638.56		11.3	10.97	638.23	BED	10.9	6.70	638.30	TOE
11	9.87	638.29		12	11.10	638.1	BED	11.3	6.79	638.21	BED
12	10.03	638.13		13.2	11.18	638.02	BED	12	6.93	638.07	BED
13	10.10	638.06		14.7	10.72	638.48	BED	12.3	7.00	638.00	BED
14	9.94	638.22		15.6	9.63	639.57	BED	12.8	6.99	638.01	BED
15	9.78	638.38		17.1	9.18	640.02	BED	13.3	6.91	638.09	BED
15.5	8.71	639.45		20	9.49	639.71	BNK	13.8	6.72	638.28	BED
16.5	8.05	640.11		21	10.11	639.09	LOG	14.3	6.52	638.48	BED
18	8.10	640.06		22.8	10.22	638.98	LOG	14.9	6.32	638.68	BED
21	9.07	639.09		24	9.94	639.26	BNK	15.3	5.82	639.18	ROOTWAL
23	9.21	638.95		26	9.21	639.99	GRND	15.8	5.26	639.74	ROOTWAL
24	9.00	639.16						16.6	5.01	639.99	BNK
26	8.12	640.04						17.1	4.91	640.09	BKF
27.5	7.35	640.81						18.3	5.03	639.97	GRND
32	6.45	641.71						20	5.29	639.71	GRND
								20.7	5.84	639.16	GRND
								22.3	5.88	639.12	GRND
								23.8	5.78	639.22	GRND
								25.9	4.99	640.01	GRND
								27.3	4.10	640.90	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM	6.00	641.31	IR Lt
HI		647.31	
0	6.12	641.19	GRND
1.6	6.67	640.64	
4.3	6.93	640.38	
5.6	6.86	640.45	
6.6	7.27	640.04	
7.6	7.17	640.14	
8.6	7.44	639.87	BKF
9.6	7.94	639.37	BNK
10.1	8.44	638.87	BNK
10.6	8.74	638.57	TOE
11.1	8.96	638.35	BED
11.7	9.11	638.20	EOW
12.4	9.23	638.08	THL
12.8	9.24	638.07	BED
13.4	9.11	638.20	EOW
14.2	8.80	638.51	BED
14.7	8.67	638.64	TOE
15.2	7.75	639.56	BNK
15.5	7.62	639.69	BKF
16.1	7.16	640.15	GRND
17.6	7.16	640.15	
18.8	7.42	639.89	
20.1	7.55	639.76	
21.1	8.04	639.27	
23.1	8.17	639.14	
25.3	7.49	639.82	
27.4	6.42	640.89	

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00		IR Lt
HI		0.00	
0		641.03	
1.2		640.63	
3.58		640.21	
6.73		639.96	BKF
8.68		639.57	
10.39		638.33	
11.89		638.06	
13.45		638.07	
15.74		639.61	
17.55		640.01	
19.42		639.70	
21.25		639.24	
22.96		638.94	
25.07		639.62	
27.22		640.69	


Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF7
 Reach 7 - Southeast Creek - Sta 11+20.6



Year 4

Facing Downstream

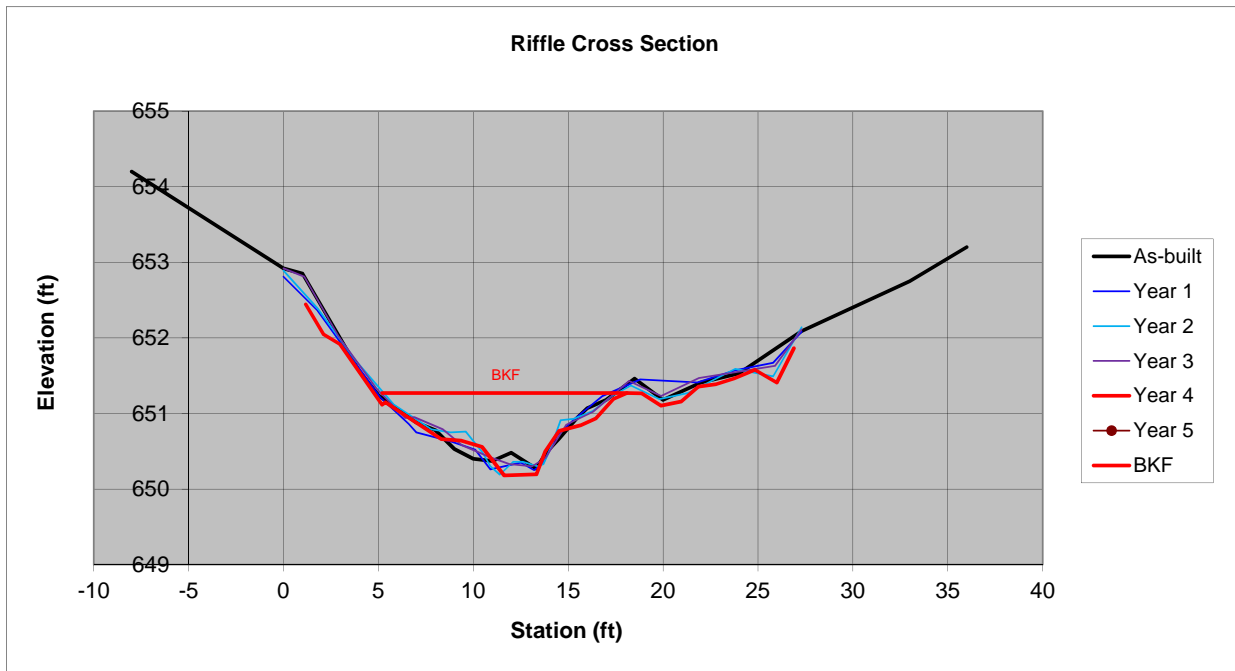

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	9.4	Area	9.5	Area	7.6	Area	8.8	Area	7.3	Area	0.0
Bkf W	14.5	Bkf W	15	Bkf W	14.5	Bkf W	13.3	Bkf W	12.9	Bkf W	10
Dmean	0.6	Dmean	0.6	Dmean	0.5	Dmean	0.7	Dmean	0.6	Dmean	0.0
Dmax	1.2	Dmax	1.2	Dmax	1.2	Dmax	1.1	Dmax	1.1	Dmax	0.0
W/d	22.3	W/d	23.8	W/d	27.7	W/d	20.2	W/d	22.8	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Riffle Cross Section RF7

Reach 7 - Southeast Creek - Sta 11+20.6

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	7.17	653.43	BP7 IR Lt	BM HI	5.15	653.43	BP7 IR Lt	BM HI	5.27	653.16	IR Lt
-8	6.40	654.20		0	5.77	652.81	GRND	0	5.54	652.89	GRND
0	7.68	652.92		1.8	6.22	652.36	GRND	1.8	6.04	652.39	GRND
1	7.75	652.85		3.8	6.92	651.66	GRND	3.8	6.73	651.70	GRND
4	9.04	651.56		5.1	7.37	651.21	GRND	5.8	7.31	651.12	GRND
5	9.36	651.24		6.6	7.72	650.86	BKF LT	7.8	7.64	650.79	GRND
7	9.72	650.88		7	7.83	650.75		8.8	7.68	650.75	GRND
8	9.82	650.78		8.8	7.95	650.63		9.6	7.67	650.76	BKF
9	10.07	650.53		10.1	8.06	650.52		10.5	7.95	650.48	BNK
10	10.20	650.40		10.9	8.32	650.26		10.9	8.13	650.30	EOW
11	10.23	650.37		12.5	8.23	650.35		11.4	8.24	650.19	BED
12	10.12	650.48		13.2	8.33	650.25		12.1	8.07	650.36	BED
13.3	10.33	650.27		13.7	8.23	650.35		12.6	8.07	650.36	BED
13.9	10.10	650.50		14.4	7.88	650.70		13.4	8.13	650.30	BED
14.5	9.94	650.66		15.3	7.66	650.92	BKF RT	13.7	8.10	650.33	EOW
15.5	9.65	650.95		16.8	7.35	651.23	GRND	14.1	7.88	650.55	BNK
16	9.53	651.07		18.8	7.13	651.45	GRND	14.6	7.52	650.91	BKF
17	9.42	651.18		21.8	7.17	651.41	GRND	15.3	7.50	650.93	GRND
18.5	9.14	651.46		23.8	7.01	651.57	GRND	16.3	7.40	651.03	GRND
20	9.42	651.18		25.8	6.91	651.67	GRND	17.3	7.20	651.23	GRND
22	9.19	651.41		27.3	6.50	652.08	GRND	18.3	7.06	651.37	GRND
24	9.07	651.53						19.8	7.24	651.19	GRND
27.3	8.51	652.09						21.3	7.16	651.27	GRND
33	7.85	652.75						23.8	6.84	651.59	GRND
36	7.40	653.20						25.8	6.94	651.49	GRND
								27.3	6.29	652.14	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	2.97	653.16	IR Lt
		656.13	
0	3.21	652.92	GRND
1.1	3.32	652.81	
2.9	4.11	652.02	
4.9	4.80	651.33	
6.4	5.19	650.94	
6.9	5.18	650.95	
8.4	5.34	650.79	BKF
9.4	5.55	650.58	BNK
10.9	5.71	650.42	EOW
11.9	5.80	650.33	BED
13.1	5.83	650.30	THL
13.8	5.72	650.41	EOW
14.9	5.28	650.85	BNK/BKF
16.3	5.11	651.02	GRND
17.2	4.92	651.21	
18.2	4.70	651.43	
19.9	4.90	651.23	
21.9	4.66	651.47	
25.9	4.50	651.63	
27.3	4.02	652.11	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	
1.2		652.44	
2.1		652.05	
3.0		651.92	
5.2		651.12	
5.4		651.15	BKF
8.3		650.66	
9.3		650.64	
10.5		650.56	
11.6		650.18	
13.3		650.19	
13.8		650.50	
14.5		650.77	
15.7		650.84	
16.5		650.93	
17.4		651.19	
18.1		651.27	BKF
18.9		651.27	
19.9		651.10	
21.0		651.16	
21.9		651.35	
22.8		651.39	
23.8		651.46	
24.8		651.58	
26.0		651.41	
26.9		651.86	


Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL7
 Reach 7 - Southeast Creek - Sta 11+32.3



Year 4

Facing Downstream

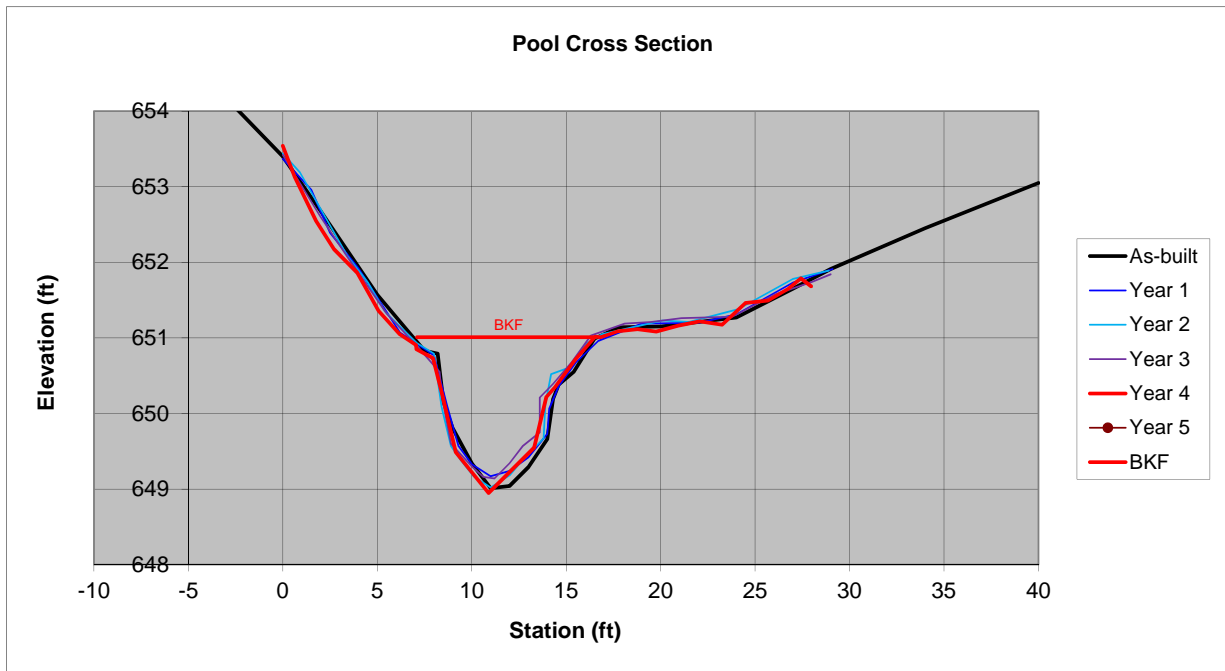

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	10.5	Area	9.6	Area	9.6	Area	9.9	Area	10.0	Area	0.0
Bkf W	9.5	Bkf W	9.7	Bkf W	9.8	Bkf W	9.3	Bkf W	9.4	Bkf W	10
Dmean	1.1	Dmean	1.0	Dmean	1.0	Dmean	1.1	Dmean	1.1	Dmean	0.0
Dmax	2.0	Dmax	1.8	Dmax	1.9	Dmax	1.9	Dmax	2.1	Dmax	0.0
W/d	8.6	W/d	9.8	W/d	10.0	W/d	8.7	W/d	8.8	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL7

Reach 7 - Southeast Creek - Sta 11+32.3

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	7.17	653.43	BP7 IR Lt	BM	5.15	653.43	BP7 IR Lt	BM	4.94	652.34	IR Lt
HI		660.60		HI		658.58		HI		657.28	
-4	6.17	654.43		0	5.21	653.37	GRND	0	3.84	653.44	GRND
0	7.20	653.40		1.5	5.62	652.96	GRND	0.9	4.09	653.19	GRND
2	7.92	652.68		2.5	6.19	652.39	GRND	3.4	5.19	652.09	GRND
5	9.03	651.57		4	6.66	651.92	GRND	4.5	5.55	651.73	GRND
7.5	9.77	650.83		6.2	7.51	651.07	GRND	5.4	5.93	651.35	GRND
8.2	9.81	650.79		8	7.81	650.77	LOG	7.1	6.35	650.93	GRND
8.5	10.45	650.15		8.7	8.48	650.1	EOW	8	6.49	650.79	LOG
9	10.80	649.80		9.3	9.01	649.57		8.4	7.19	650.09	LOG/EOW
10	11.26	649.34		10	9.25	649.33		8.9	7.71	649.57	BED
11	11.59	649.01		11	9.41	649.17		9.4	7.89	649.39	BED
12	11.56	649.04		12	9.34	649.24		10.1	8.11	649.17	BED
13	11.31	649.29		13	9.16	649.42		11	8.26	649.02	BED
14	10.94	649.66		14	8.85	649.73		12	8.10	649.18	BED
14.3	10.41	650.19		14.1	8.52	650.06	EOW	12.7	7.89	649.39	BED
14.6	10.22	650.38		14.6	8.22	650.36		13.8	7.61	649.67	BED
15.4	10.05	650.55		15.5	7.91	650.67	BKF RT	13.9	7.16	650.12	EOW
16.5	9.61	650.99		16.7	7.62	650.96	GRND	14.2	6.76	650.52	BNK
17.8	9.46	651.14		19	7.39	651.19	GRND	15.2	6.67	650.61	BNK
20	9.45	651.15		22	7.38	651.2	GRND	16.1	6.35	650.93	BNK
24	9.33	651.27		24	7.27	651.31	GRND	16.9	6.23	651.05	BKF
27	8.95	651.65		27	6.85	651.73	GRND	20.1	6.05	651.23	GRND
29	8.69	651.91		29.1	6.67	651.91	GRND	21.5	6.07	651.21	GRND
34	8.15	652.45						24.1	5.90	651.38	GRND
40	7.55	660.60						27	5.50	651.78	GRND
								28.9	5.39	651.89	GRND

Year 3			
Station	FS/BS	Elev.	Desc.
BM	6.60	653.53	IR Lt
HI		660.13	
0	6.71	653.42	GRND
2	7.53	652.60	
3.5	8.09	652.04	
5.5	8.81	651.32	
7	9.21	650.92	
8.3	9.58	650.55	BKF
8.4	9.87	650.26	WS
8.9	10.53	649.60	TOE
10	10.83	649.30	BED
10.6	10.97	649.16	THAL
11.2	10.99	649.14	BED
12	10.79	649.34	BED
12.7	10.56	649.57	BED
13.6	10.38	649.75	BED
13.6	9.92	650.21	WS
14.3	9.74	650.39	BNK
15.3	9.45	650.68	BNK
16.3	9.10	651.03	BKF
18.1	8.94	651.19	GRND
19.5	8.92	651.21	
21.1	8.87	651.26	
23.8	8.85	651.28	
26	8.56	651.57	
28	8.39	651.74	
29	8.29	651.84	

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	
0.0		653.54	
0.6		653.13	
1.8		652.55	
2.7		652.17	
3.9		651.86	
5.1		651.35	
6.2		651.05	
7.1		650.91	BKF
7.1		650.85	
8.0		650.73	
8.5		650.22	
9.2		649.49	
10.9		648.95	
13.3		649.55	
14.0		650.22	
14.4		650.35	
15.5		650.72	
16.5		651.01	BKF
16.8		651.01	
17.7		651.09	
18.8		651.11	
19.8		651.08	
20.9		651.16	
22.1		651.22	
23.3		651.17	
24.5		651.46	
25.7		651.49	
26.8		651.65	
27.4		651.79	
28.0		651.68	

Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	


Holly Grove Stream Restoration Site
 Guilford County, NC
 Riffle Cross Section RF8
 Reach 8 - Southwest Creek - Sta 11+49.9



Year 4

Facing Downstream

Riffle Cross Section

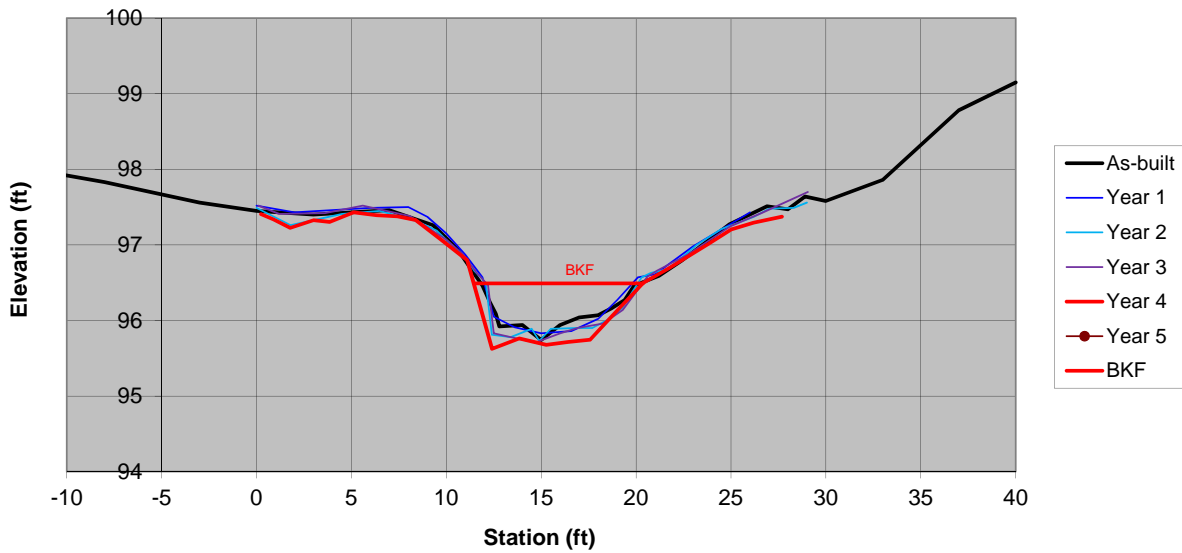

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	3.4	Area	4.4	Area	4.9	Area	5.3	Area	5.1	Area	0.0
Bkf W	8	Bkf W	8.2	Bkf W	8.4	Bkf W	9	Bkf W	8.87	Bkf W	10
Dmean	0.4	Dmean	0.5	Dmean	0.6	Dmean	0.6	Dmean	0.6	Dmean	0.0
Dmax	0.7	Dmax	0.7	Dmax	0.8	Dmax	0.9	Dmax	0.9	Dmax	0.0
W/d	18.6	W/d	15.2	W/d	14.5	W/d	15.2	W/d	15.5	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Riffle Cross Section RF8

Reach 8 - Southwest Creek - Sta 11+49.9

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM HI	2.51	98.99	Stump	BM HI	3.78	100.42	BP8 IR Rt	BM HI	5.42	97.59	IR Lt
		101.50				104.20				103.01	
-15	3.36	98.14		0	6.68	97.52	GRND	0	5.52	97.49	GRND
-8	3.67	97.83		2	6.77	97.43	GRND	1.8	5.75	97.26	GRND
-3	3.94	97.56		6	6.71	97.49	GRND	4.5	5.60	97.41	GRND
0	4.05	97.45		8	6.70	97.50	GRND	6.5	5.56	97.45	GRND
3	4.10	97.40		9	6.83	97.37	GRND	8.5	5.70	97.31	GRND
7	4.04	97.46		10	7.05	97.15	GRND	9.5	5.82	97.19	GRND
9.3	4.24	97.26		11	7.33	96.87	BKF	11.1	6.21	96.80	GRND
10.6	4.56	96.94		11.9	7.63	96.57	BNK	11.5	6.36	96.65	GRND
11.9	5.04	96.46		12.5	8.15	96.05	BED	11.9	6.46	96.55	BKF
12.3	5.26	96.24		13.6	8.29	95.91	BED	12.1	6.54	96.47	BNK
12.6	5.41	96.09		15	8.37	95.83	BED	12.4	7.20	95.81	TOE
12.8	5.58	95.92		16.6	8.34	95.86	BED	13.4	7.23	95.78	BED
14	5.56	95.94		18	8.18	96.02	BED	14.5	7.12	95.89	BED
15	5.76	95.74		19	7.93	96.27	BNK	14.9	7.28	95.73	BED
16	5.56	95.94		20.1	7.63	96.57	BKF	15.5	7.12	95.89	BED
17	5.46	96.04		21	7.59	96.61	GRND	16.8	7.11	95.90	BED
18	5.43	96.07		23	7.22	96.98	GRND	17.7	7.11	95.90	BED
18.7	5.34	96.16		26	6.77	97.43	GRND	18.5	7.00	96.01	BED
19.4	5.23	96.27						19.3	6.84	96.17	BED
19.9	5.04	96.46						19.8	6.63	96.38	BNK
21.2	4.91	96.59						20.3	6.44	96.57	BNK
22.4	4.71	96.79						20.8	6.38	96.63	BKF
24.9	4.23	97.27						21.7	6.33	96.68	GRND
26.9	3.99	97.51						23.2	6.01	97.00	GRND
28	4.03	97.47						24.5	5.80	97.21	GRND
28.9	3.86	97.64						26.2	5.64	97.37	GRND
30	3.92	97.58						27	5.53	97.48	GRND
33	3.64	97.86						28.3	5.52	97.49	GRND
37	2.72	98.78						29	5.45	97.56	GRND
40	2.35	99.15									

Year 3			
Station	FS/BS	Elev.	Desc.
BM HI	5.11	97.60	IR Lt
		102.71	
0.1	5.19	97.52	GRND
1.2	5.30	97.41	
3.6	5.29	97.42	
5.6	5.19	97.52	
8.1	5.33	97.38	
10	5.64	97.07	
10.9	5.84	96.87	BKF
11.6	6.08	96.63	BNK
12.2	6.24	96.47	
12.5	6.88	95.83	TOE
13.4	6.93	95.78	BED
14.7	7.00	95.71	THL
16	6.88	95.83	BED
16.9	6.81	95.90	
18.25	6.75	95.96	TOE
19.3	6.57	96.14	BNK
20.6	6.13	96.58	BKF
21.1	6.05	96.66	GRND
22.7	5.84	96.87	
25	5.46	97.25	
26.6	5.29	97.42	
29.05	5.01	97.70	

Year 4			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	
0.24		97.41	
0.89		97.34	
1.78		97.23	
3.01		97.33	
3.85		97.30	
5.12		97.43	
6.33		97.39	
7.44		97.38	
8.39		97.33	
9.71		97.07	
11.1		96.80	BKF
12.41		95.62	
13.84		95.76	
15.27		95.68	
16.43		95.72	
17.58		95.75	
18.85		96.09	
20.37		96.49	BKF
21.71		96.69	
23.81		97.01	
25		97.20	
26.19		97.29	
27.69		97.37	


Year 5			
Station	FS/BS	Elev.	Desc.
BM HI	0.00	100.00	IR Lt
		100.00	

Holly Grove Stream Restoration Site
 Guilford County, NC
 Pool Cross Section PL8
 Reach 8 - Southwest Creek - Sta 100+78.5



Year 4

Facing Downstream

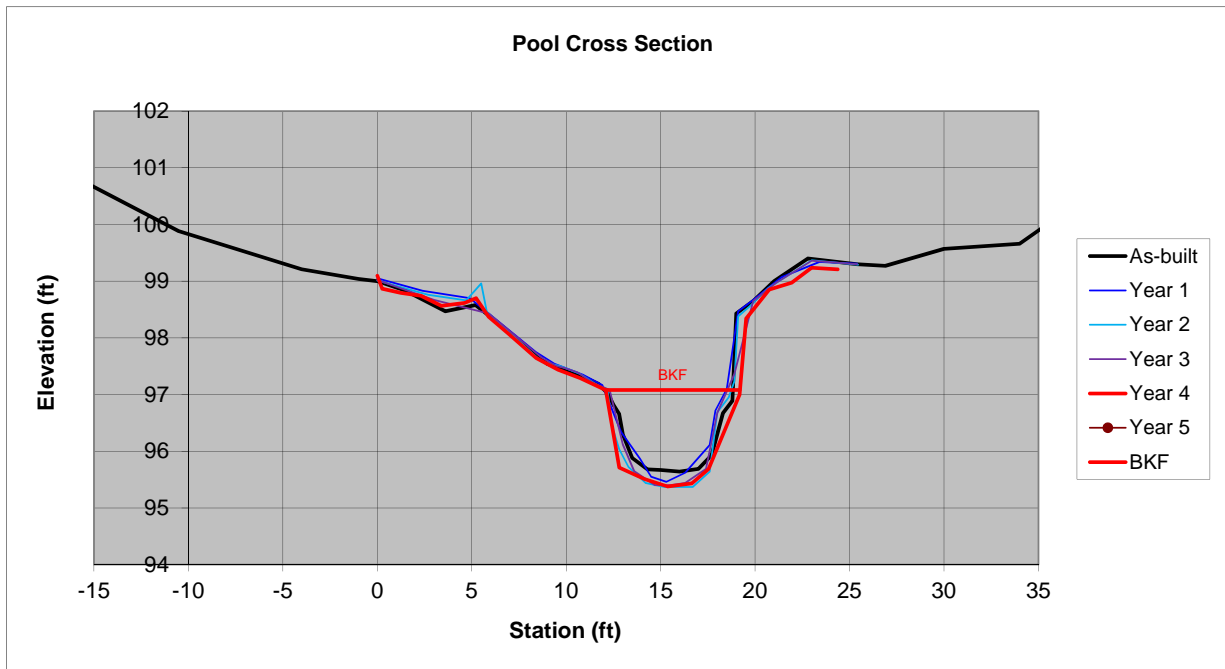

As-Built		Year 1		Year 2		Year 3		Year 4		Year 5	
Date	1/8/09	Date	10/20/09	Date	10/12/10	Date	10/5/11	Date	9/17/12	Date	0/0/0
Area	7.9	Area	7.4	Area	9.1	Area	8.6	Area	9.2	Area	0.0
Bkf W	7.1	Bkf W	6.6	Bkf W	7.2	Bkf W	7.5	Bkf W	7.08	Bkf W	10
Dmean	1.1	Dmean	1.1	Dmean	1.3	Dmean	1.1	Dmean	1.3	Dmean	0.0
Dmax	1.6	Dmax	1.7	Dmax	1.8	Dmax	1.8	Dmax	1.7	Dmax	0.0
W/d	6.4	W/d	5.9	W/d	5.7	W/d	6.5	W/d	5.5	W/d	0.0

Holly Grove Stream Restoration Site

Guilford County, NC

Pool Cross Section PL8

Reach 8 - Southwest Creek - Sta 100+78.5

As-Built				Year 1				Year 2			
Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.	Station	FS/BS	Elev.	Desc.
BM	5.31	98.99	Stump	BM	3.78	100.42	BP8 IR Rt	BM	5.61	99.09	IR Lt
HI		104.30		HI		104.20		HI		104.70	
-17	3.29	101.01		0	5.15	99.05	GRND	0	5.69	99.01	GRND
-10.5	4.42	99.88		2.4	5.37	98.83	GRND	2.7	5.94	98.76	GRND
-4	5.09	99.21		4.9	5.50	98.7	GRND	4.7	6.04	98.66	GRND
-1	5.26	99.04		8.4	6.45	97.75	GRND	5.5	5.74	98.96	LOG
0	5.30	99.00		9.4	6.66	97.54	GRND	5.8	6.24	98.46	GRND
1.5	5.47	98.83		10.9	6.85	97.35	GRND	8.7	7.12	97.58	GRND
3.6	5.83	98.47		11.9	7.03	97.17	BKF	9.7	7.20	97.50	BKF
5.2	5.72	98.58		12.9	7.86	96.34	BNK	10.7	7.33	97.37	BNK
6	5.93	98.37		13.9	8.33	95.87	BED	11.7	7.54	97.16	BNK
9	6.76	97.54		14.5	8.65	95.55	BED	12.2	7.64	97.06	BNK
11	7.00	97.30		15.3	8.74	95.46	BED	12.4	8.23	96.47	BED
11.7	7.11	97.19		16.3	8.58	95.62	BED	12.8	8.66	96.04	EOW
12.2	7.28	97.02		17.6	8.09	96.11	BED	13.3	8.98	95.72	BED
12.5	7.48	96.82		17.9	7.48	96.72	ROOTWAD	14.2	9.26	95.44	BED
12.8	7.64	96.66		18.5	7.10	97.1	ROOT	15.2	9.33	95.37	BED
13	8.00	96.30		19.1	5.73	98.47	TOB	16.7	9.33	95.37	BED
13.5	8.42	95.88		19.9	5.53	98.67	GRND	17.6	9.06	95.64	BED
14.3	8.62	95.68		21.4	5.13	99.07	GRND	18	8.01	96.69	BNK
15	8.63	95.67		23.4	4.86	99.34	GRND	18.6	7.75	96.95	BNK
16	8.66	95.64		25.4	4.89	99.31	GRND	18.9	7.47	97.23	BNK
17	8.61	95.69						19.1	6.32	98.38	GRND
17.7	8.37	95.93						19.7	6.15	98.55	GRND
18.3	7.63	96.67						20.7	5.82	98.88	GRND
18.8	7.41	96.89						23	5.33	99.37	GRND
19	5.87	98.43						25.45	5.41	99.29	GRND
19.9	5.65	98.65									
21	5.30	99.00									
22.8	4.9	99.40									
25.4		5	99.30								
26.9		5.03	99.27								
30		4.73	99.57								
34		4.64	99.66								
36		4.17	100.13								
40		4.06	100.24								


Year 3			
Station	FS/BS	Elev.	Desc.
BM	5.13	99.09	IR Lt
HI		104.22	
0	5.20	99.02	GRND
3	5.55	98.67	
5.9	5.79	98.43	
8.7	6.57	97.65	
9.5	6.72	97.50	
9.9	6.75	97.47	BKF
10.6	6.83	97.39	BNK
11.4	7.01	97.21	
12.3	7.14	97.08	
13	8.10	96.12	TOE
13.6	8.57	95.65	BED
14.7	8.82	95.40	
15.5	8.82	95.40	THL
16.3	8.78	95.44	BED
17.4	8.53	95.69	TOE
18	7.54	96.68	BNK
18.9	6.86	97.36	
19.9	5.57	98.65	
21.1	5.25	98.97	GRND
23	4.86	99.36	
25.4	4.92	99.30	

Year 4			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	
0.0		99.10	
0.3		98.87	
1.3		98.79	
2.3		98.74	
3.4		98.57	
4.6		98.62	
5.2		98.70	
5.9		98.37	
6.9		98.07	
8.4		97.65	
9.6		97.44	
10.7		97.29	
12.1		97.08	BKF
12.8		95.71	
14.1		95.51	
15.4		95.38	
16.7		95.43	
17.5		95.69	
19.2		97.00	
19.5		98.34	
20.8		98.85	
21.9		98.97	
23.0		99.24	
24.4		99.21	

Year 5			
Station	FS/BS	Elev.	Desc.
BM	0.00	100.00	IR Lt
HI		100.00	

Pebble Count Weighted by Channel Feature			
Percent Riffle:	22.8	Percent Run:	31.7
Percent Pool:	33.7	Percent Glide:	11.9

Material	Size Range (mm)	weighted
silt/clay	0 - 0.062	13.7
very fine sand	0.062 - 0.13	0.0
fine sand	0.13 - 0.25	0.0
medium sand	0.25 - 0.5	7.3
coarse sand	0.5 - 1	3.9
very coarse sand	1 - 2	9.7
very fine gravel	2 - 4	0.0
fine gravel	4 - 6	1.7
fine gravel	6 - 8	1.4
medium gravel	8 - 11	0.7
medium gravel	11 - 16	1.4
coarse gravel	16 - 22	4.2
coarse gravel	22 - 32	2.3
very coarse gravel	32 - 45	3.5
very coarse gravel	45 - 64	18.1
small cobble	64 - 90	10.7
medium cobble	90 - 128	8.3
large cobble	128 - 180	7.6
very large cobble	180 - 256	0.7
small boulder	256 - 362	0.0
small boulder	362 - 512	0.0
medium boulder	512 - 1024	0.0
large boulder	1024 - 2048	0.0
very large boulder	2048 - 4096	0.0

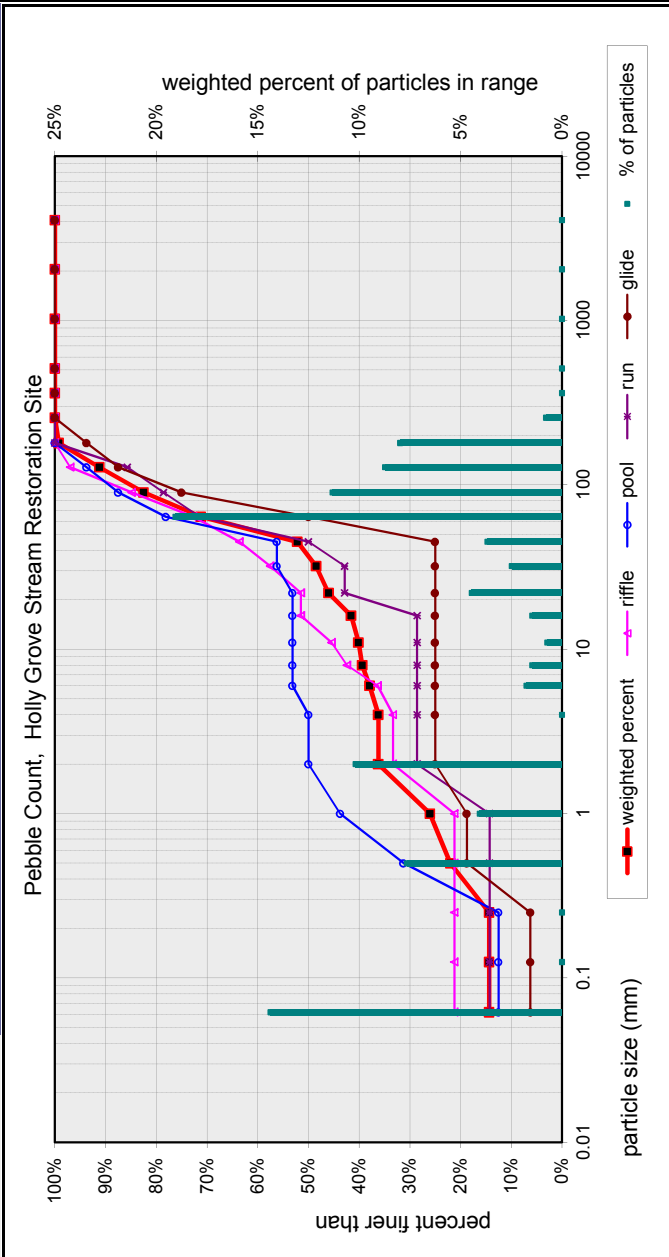

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation geo mean	std dev	
	0.290	1.84	36.8	57	96	150	64.7	18.1	
based on total count	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det	artificial
	14%	21%	33%	27%	0%	5%	0%	0%	0%

bedrock	5.0
clay hardpan	0.0
detritus/wood	0.0
artificial	0.0
weighted total count:	100.1


weighted particle count: 95.1

Pebble Count of Channel Reach

Material	Size Range (mm)	Count
silt/clay	0	13
very fine sand	0.062	1
fine sand	0.13	4
medium sand	0.25	3
coarse sand	0.5	4
very coarse sand	1	4
very fine gravel	2	4
fine gravel	4	1
fine gravel	6	1
medium gravel	8	2
medium gravel	11	2
medium gravel	16	1
coarse gravel	22	4
coarse gravel	32	5
coarse gravel	45	9
very coarse gravel	64	16
small cobble	90	10
medium cobble	128	11
large cobble	180	5
very large cobble	256	2
small boulder	362	
small boulder	512	
medium boulder	1024	
large boulder	2048	
very large boulder	4096	
total particle count:		96

bedrock		3
clay hardpan		
detritus/wood		
artificial		
total count:		99


Holly Grove Stream Restoration Site
 Guilford County, NC
 Buckhorn Creek: Reach 1
 Note: Riffle RF-1

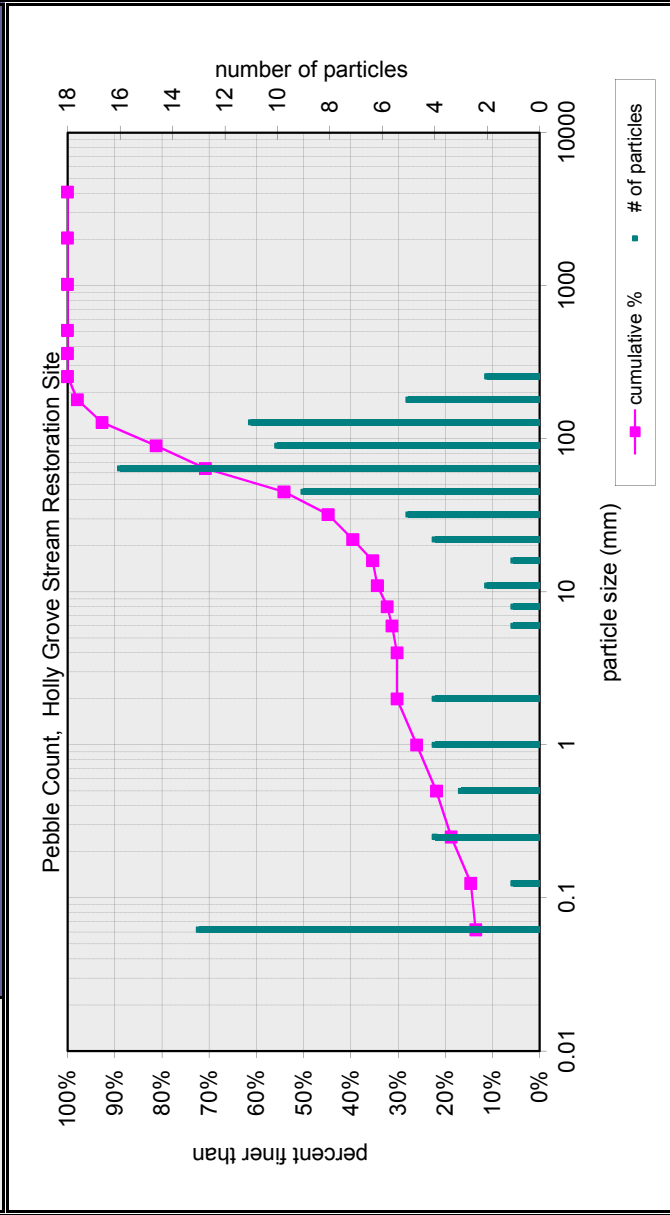

based on sediment particles only	size percent less than (mm)					particle size distribution			
	D16	D35	D50	D65	D84	D95	gradation	geo mean	std dev
	0.158	13.77	38.7	57	98	149	123.5	3.9	24.9
based on total count	percent by substrate type					bedrock	hardpan	wood/det	artificial
	silt/clay	sand	gravel	cobble	boulder	3%	0%	0%	0%
	13%	16%	39%	28%	0%	3%	0%	0%	0%

Pebble Count Weighted by Channel Feature			
Percent Riffle:	37.8	Percent Run:	20.7
Percent Pool:	22.5	Percent Glide:	18.9

Material	Size Range (mm)	weighted
silt/clay	0	0.062
very fine sand	0.062	0.13
fine sand	0.13	0.25
medium sand	0.25	0.5
coarse sand	0.5	1
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	16
coarse gravel	16	22
coarse gravel	22	32
very coarse gravel	32	45
very coarse gravel	45	64
small cobble	64	90
medium cobble	90	128
large cobble	128	180
very large cobble	180	256
small boulder	256	362
small boulder	362	512
medium boulder	512	1024
large boulder	1024	2048
very large boulder	2048	4096

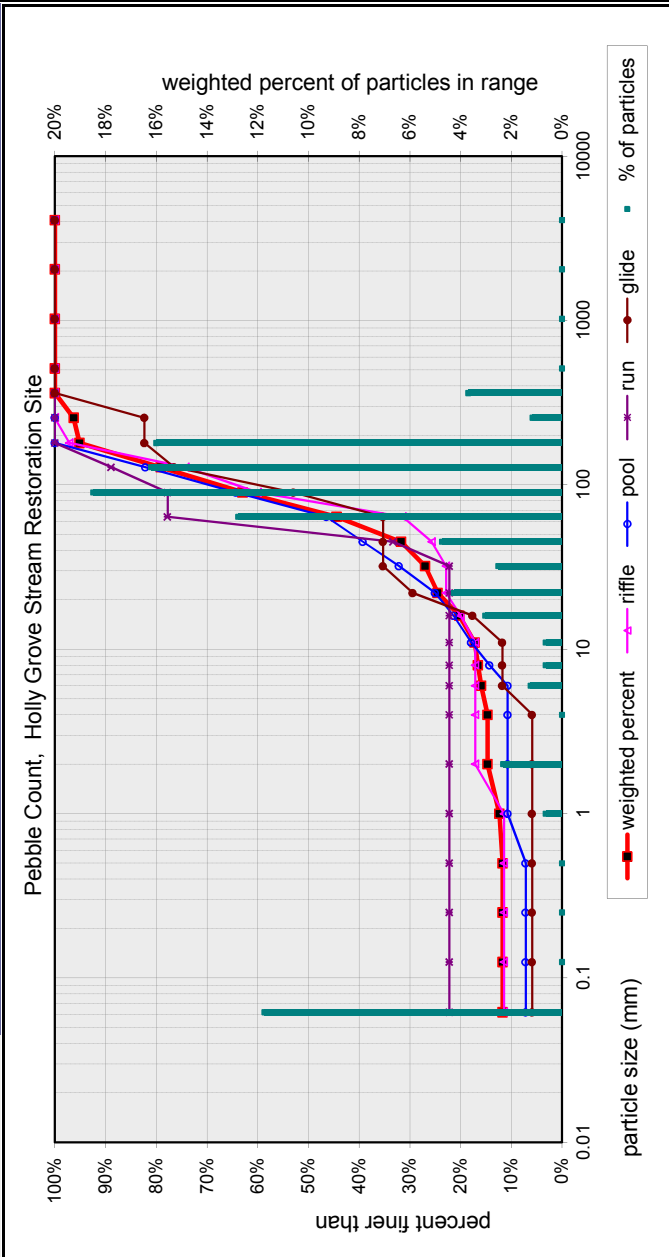

weighted particle count:	90.4
bedrock	9.5
clay hardpan	0.0
detritus/wood	0.0
artificial	0.0
weighted total count:	99.9

percent finer than	100%	90%	80%	70%	60%	50%	40%	30%	20%	10%	0%
particle size (mm)	10000	1000	100	10	1	0.1	0.01				
weighted percent	—	—	—	—	—	—	—	—	—	—	—
riffle	—	—	—	—	—	—	—	—	—	—	—
pool	—	—	—	—	—	—	—	—	—	—	—
run	—	—	—	—	—	—	—	—	—	—	—
glide	—	—	—	—	—	—	—	—	—	—	—
% of particles	—	—	—	—	—	—	—	—	—	—	—


Holly Grove Stream Restoration Site		Buckhorn Creek: Reach 2							
Guilford County, NC		Note: Reach Data 2							
based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation geo mean	std dev	
based on total count	11%	3%	27%	47%	3%	9%	6.7	4.8	
percent by substrate type		percent by substrate type		percent by substrate type		percent by substrate type		percent by substrate type	
silt/clay	11%	sand	3%	gravel	27%	cobble	47%	boulder	3%
bedrock	0%	hardpan	0%	wood/det	0%	artificial	0%		

Pebble Count of Channel Reach

Material	Size Range (mm)	Count
silt/clay	0	26
very fine sand	0.062	1
fine sand	0.13	1
medium sand	0.25	1
coarse sand	0.5	2
very coarse sand	1	5
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	1
medium gravel	16	3
coarse gravel	16	1
coarse gravel	22	1
coarse gravel	32	4
very coarse gravel	32	4
very coarse gravel	45	5
small cobble	64	13
medium cobble	90	18
large cobble	128	9
very large cobble	180	5
small boulder	256	2
small boulder	362	2
medium boulder	512	0
large boulder	1024	0
very large boulder	2048	0
	4096	0
total particle count:		96

bedrock	4
clay hardpan	
detritus/wood	
artificial	
total count: 100	


Holly Grove Stream Restoration Site
 Guilford County, NC
 Buckhorn Creek: Reach 2
 Note: Riffle RF2

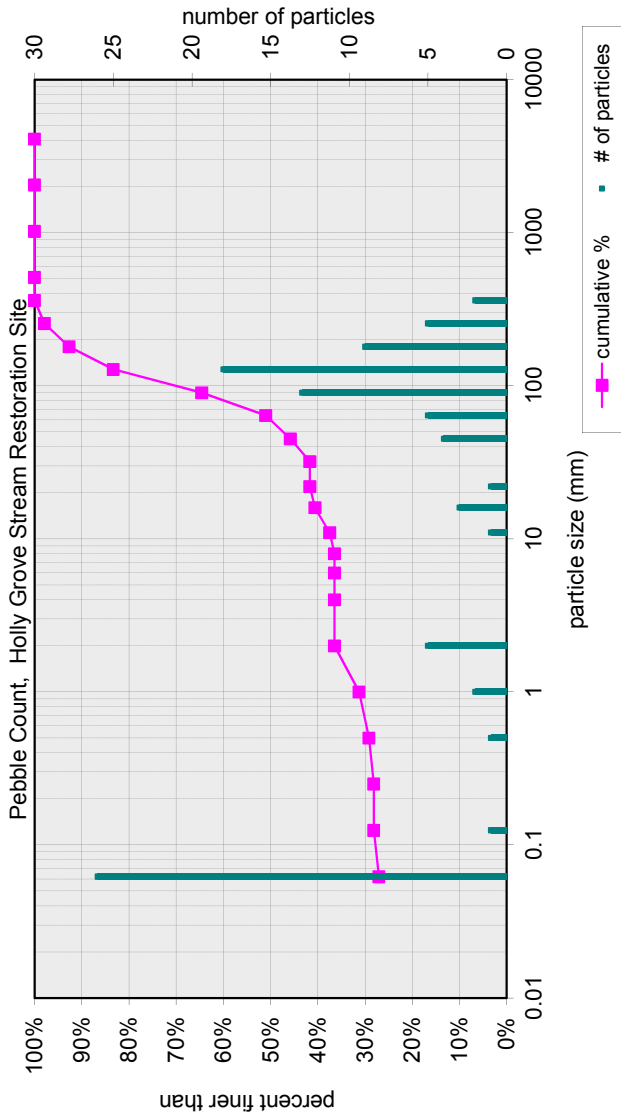

based on sediment particles only	size percent less than (mm)					particle size distribution gradation		std dev		
	D16	D35	D50	D65	D84	D95	geo mean			
	0.062	1.65	59.6	91	131	210	482.1	2.9		
based on total count	percent by substrate type		cobble		boulder		bedrock		artificial	
	silt/clay	sand	gravel	45%	2%	4%	0%	0%	0%	
	26%	9%	14%	45%	2%	4%	0%	0%	0%	

Pebble Count Weighted by Channel Feature			
Percent Riffle:	36.6	Percent Run:	19.8
Percent Pool:	20.8	Percent Glide:	22.8

Material	Size Range (mm)	weighted
silt/clay	0	0.062
very fine sand	0.062	0.13
fine sand	0.13	0.25
medium sand	0.25	0.5
coarse sand	0.5	1
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	16
coarse gravel	16	22
coarse gravel	22	32
very coarse gravel	32	45
very coarse gravel	45	64
small cobble	64	90
medium cobble	90	128
large cobble	128	180
very large cobble	180	256
small boulder	256	362
small boulder	362	512
medium boulder	512	1024
large boulder	1024	2048
very large boulder	2048	4096

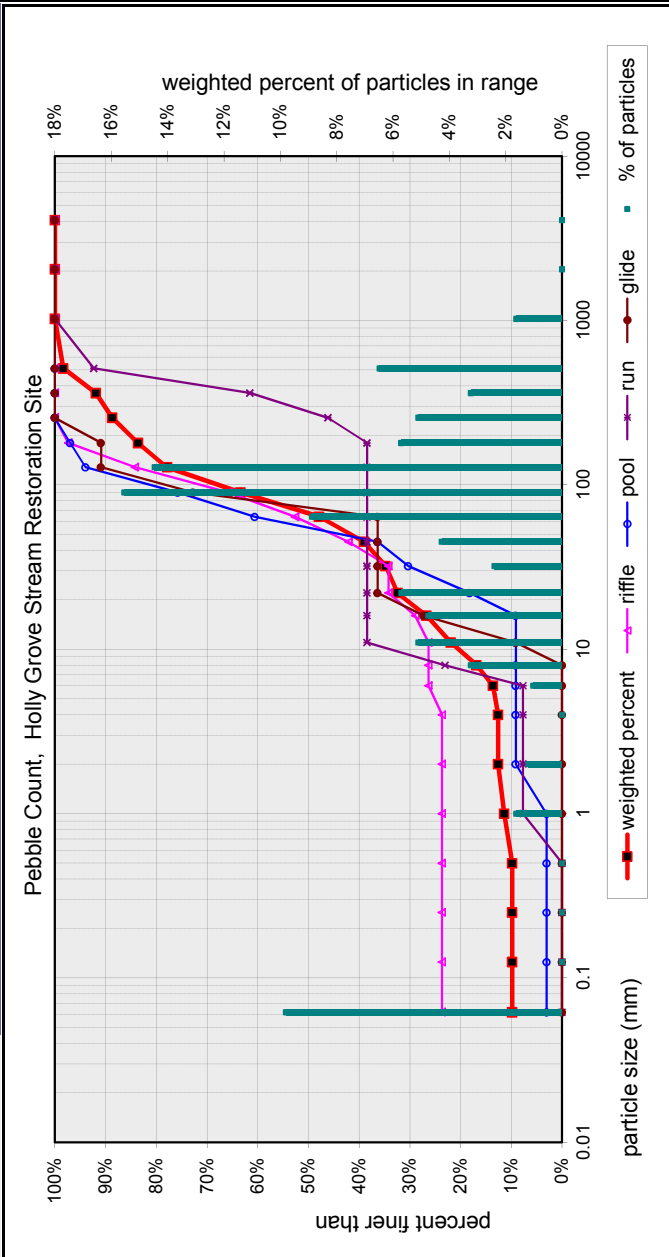

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation geo mean	std dev	
	7.412	32.58	67.0	94	185	427	5.9	5.0	
based on total count	percent by substrate type								
	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det	artificial
	9%	3%	33%	38%	11%	6%	0%	0%	0%

bedrock	5.8
clay hardpan	0.0
detritus/wood	0.0
artificial	0.0
weighted total count:	100


weighted particle count: 94.2

Pebble Count of Channel Reach

Material	Size Range (mm)	Count
silt/clay	0	45
very fine sand	0.062	1
fine sand	0.13	2
medium sand	0.25	2
coarse sand	0.5	2
very coarse sand	1	2
very fine gravel	2	2
fine gravel	4	2
fine gravel	6	2
fine gravel	8	2
medium gravel	11	2
medium gravel	16	3
coarse gravel	22	1
coarse gravel	32	2
very coarse gravel	45	3
very coarse gravel	64	7
small cobble	90	12
medium cobble	128	7
large cobble	180	4
very large cobble	256	1
small boulder	362	1
small boulder	512	
medium boulder	1024	
large boulder	2048	
very large boulder	4096	
total particle count:		99

bedrock		3
clay hardpan		
detritus/wood		
artificial		
total count:		102


Holly Grove Stream Restoration Site
 Guilford County, NC
 Buckhorn Creek: Reach 3
 Note: Riffle RF3

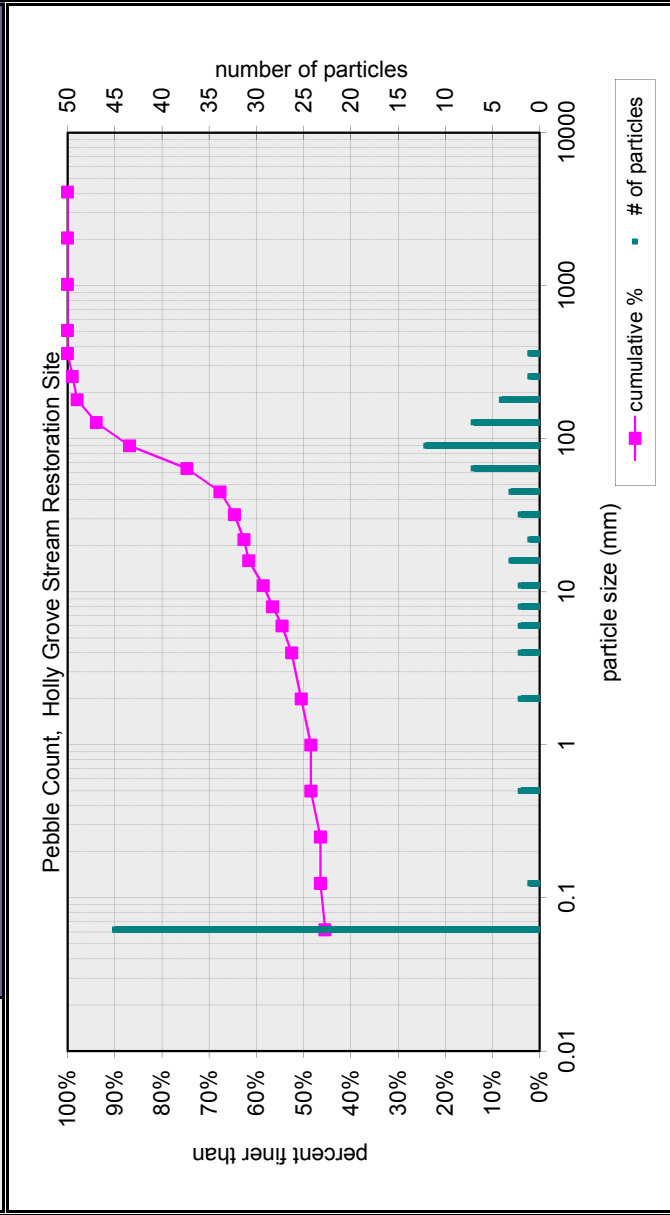

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation	geo mean	std dev
	0.062	0.06	1.7	33	83	140		2.3	36.6
based on total count	percent by substrate type						hardpan	wood/det	artificial
	silt/clay	sand	gravel	cobble	boulder	bedrock		0%	0%
	44%	5%	24%	24%	1%	3%	0%	0%	0%

Pebble Count Weighted by Channel Feature			
Percent Riffle:	45.6	Percent Run:	21.4
Percent Pool:	21.4	Percent Glide:	11.7

Material		Size Range (mm)	weighted
silt/clay		0	57.0
very fine sand		0.062	0.0
fine sand		0.13	0.0
medium sand		0.25	0.0
coarse sand		0.5	0.0
very coarse sand		1	0.0
very fine gravel		2	0.0
fine gravel		4	5.1
fine gravel		6	5.5
fine gravel		8	0.0
medium gravel		11	4.1
medium gravel		16	4.5
coarse gravel		22	5.8
coarse gravel		32	2.6
very coarse gravel		45	3.5
very coarse gravel		64	5.5
small cobble		90	2.6
medium cobble		128	2.9
large cobble		180	0.0
very large cobble		256	0.0
small boulder		362	1.1
small boulder		512	0.0
medium boulder		1024	0.0
large boulder		2048	0.0
very large boulder		4096	0.0

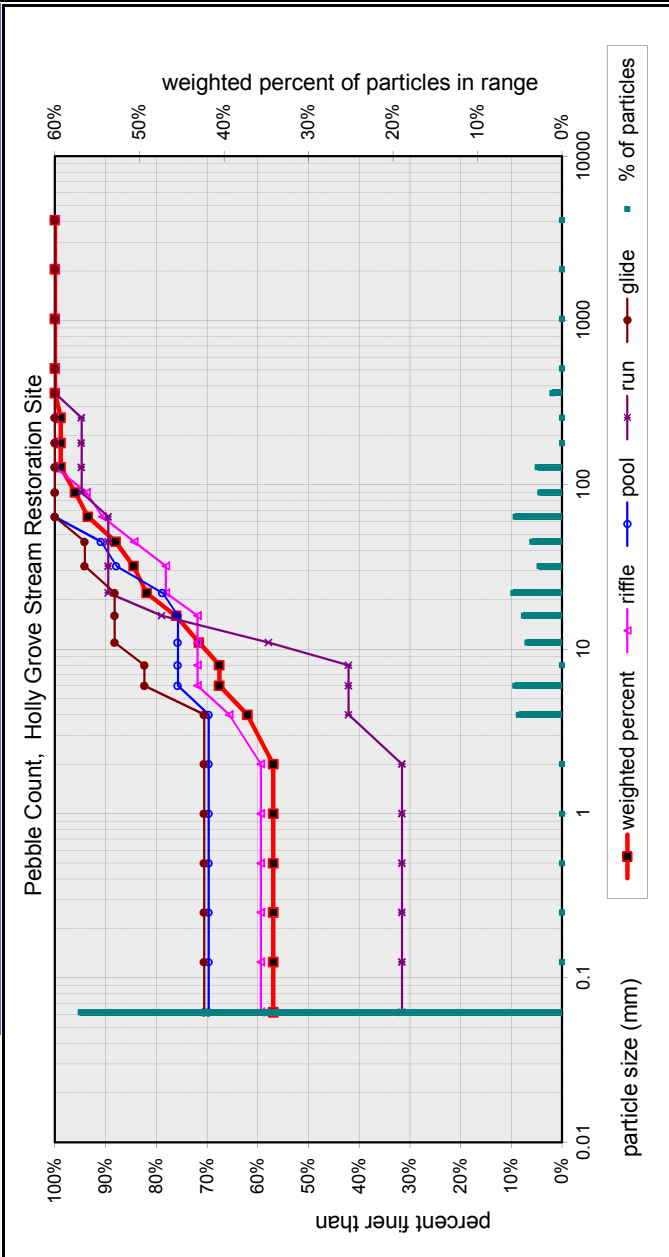

based on sediment particles only	size percent less than (mm)					particle size distribution																	
	D16	D35	D50	D65	D84	D95	gradation	geo mean	std dev														
based on total count	0.062	0.06	0.1	5	30	78	240.6	1.4	21.9														
	percent by substrate type																						
silt/clay		0%	sand		37%	cobble		5%	boulder		1%	bedrock		0%	hardpan		0%	wood/det		0%	artificial		0%

weighted particle count:		100.1
bedrock		0.0
clay hardpan		0.0
detritus/wood		0.0
artificial		0.0
weighted total count:		100.1

Pebble Count of Channel Reach


Material	Size Range (mm)	Count
silt/clay	0	58
very fine sand	0.062	
fine sand	0.13	
medium sand	0.25	
coarse sand	0.5	1
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	16
coarse gravel	16	22
coarse gravel	22	32
very coarse gravel	32	45
very coarse gravel	45	64
small cobble	64	90
medium cobble	90	128
large cobble	128	180
very large cobble	180	256
small boulder	256	362
small boulder	362	512
medium boulder	512	1024
large boulder	1024	2048
very large boulder	2048	4096
total particle count:		99

Holly Grove Stream Restoration Site

Guilford County, NC

Middle Branch: Reach 4


Note: Riffle RF-4

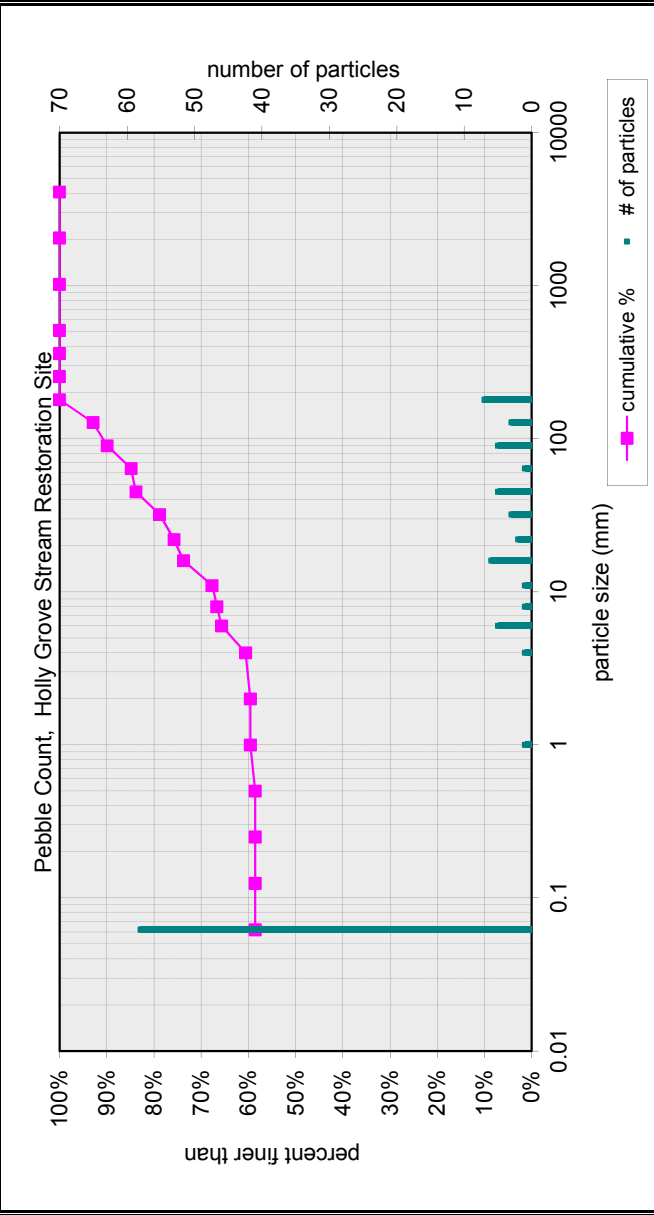

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation geo mean	std dev	
	0.062	0.06	0.1	6	48	141	384.4	1.7	
based on total count	percent by substrate type			percent by substrate type			hardpan	wood/det	artificial
	silt/clay	sand	gravel	cobble	boulder	bedrock	0%	0%	0%
	59%	1%	25%	15%	0%	0%	0%	0%	0%

Pebble Count Weighted by Channel Feature			
Percent Riffle:	35.4	Percent Run:	23.2
Percent Pool:	28.3	Percent Glide:	13.1

Material	Size Range (mm)	weighted
silt/clay	0	38.6
very fine sand	0.062	0.0
fine sand	0.13	0.0
medium sand	0.25	0.0
coarse sand	0.5	0.0
very coarse sand	1	0.0
very fine gravel	2	0.0
fine gravel	4	2.1
fine gravel	6	3.6
fine gravel	8	1.1
medium gravel	11	4.6
medium gravel	16	9.3
coarse gravel	22	4.7
coarse gravel	32	6.0
very coarse gravel	45	6.0
very coarse gravel	64	11.4
small cobble	90	8.3
medium cobble	128	3.2
large cobble	180	0.0
very large cobble	256	0.0
small boulder	362	0.0
small boulder	512	1.1
medium boulder	1024	0.0
large boulder	2048	0.0
very large boulder	4096	0.0

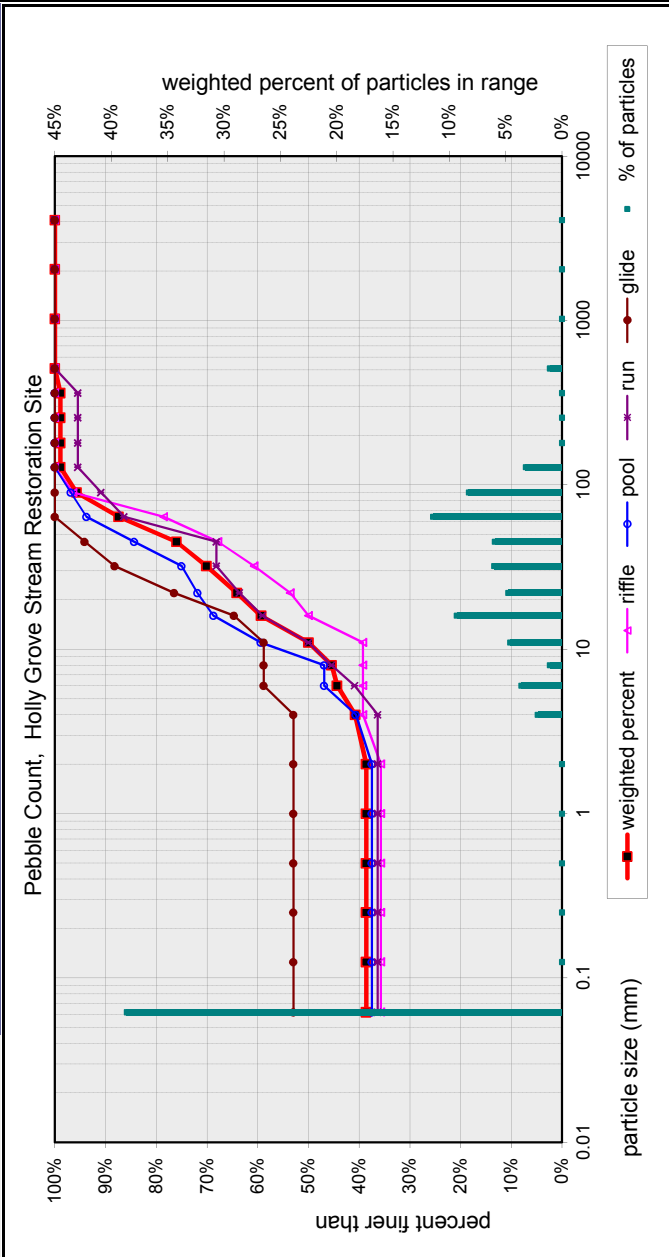

based on sediment particles only	size percent less than (mm)					particle size distribution				
	D16	D35	D50	D65	D84	D95	gradation	geo mean	std dev	
based on total count	0.062	0.06	11.0	23	57	87	91.2	1.9	30.5	
	percent by substrate type					bedrock	hardpan	wood/det	artificial	0%
					silt/clay	sand	gravel	cobble	boulder	0%
					39%	0%	49%	11%	1%	0%

weighted particle count:		100.0
bedrock		0.0
clay hardpan		0.0
detritus/wood		0.0
artificial		0.0
weighted total count:		100

Pebble Count of Channel Reach


Material	Size Range (mm)	Count
silt/clay	0	36
very fine sand	0.062	
fine sand	0.13	
medium sand	0.25	
coarse sand	0.5	8
very coarse sand	1	
	2	
very fine gravel	4	
fine gravel	6	3
fine gravel	8	1
medium gravel	11	5
medium gravel	16	8
coarse gravel	22	5
coarse gravel	32	8
very coarse gravel	45	9
very coarse gravel	64	11
small cobble	90	3
medium cobble	128	2
large cobble	180	
very large cobble	256	
small boulder	362	
small boulder	512	
medium boulder	1024	
large boulder	2048	
very large boulder	4096	
total particle count:		99

Holly Grove Stream Restoration Site

Guilford County, NC

Middle Branch: Reach 5


Note: Riffle RF-5

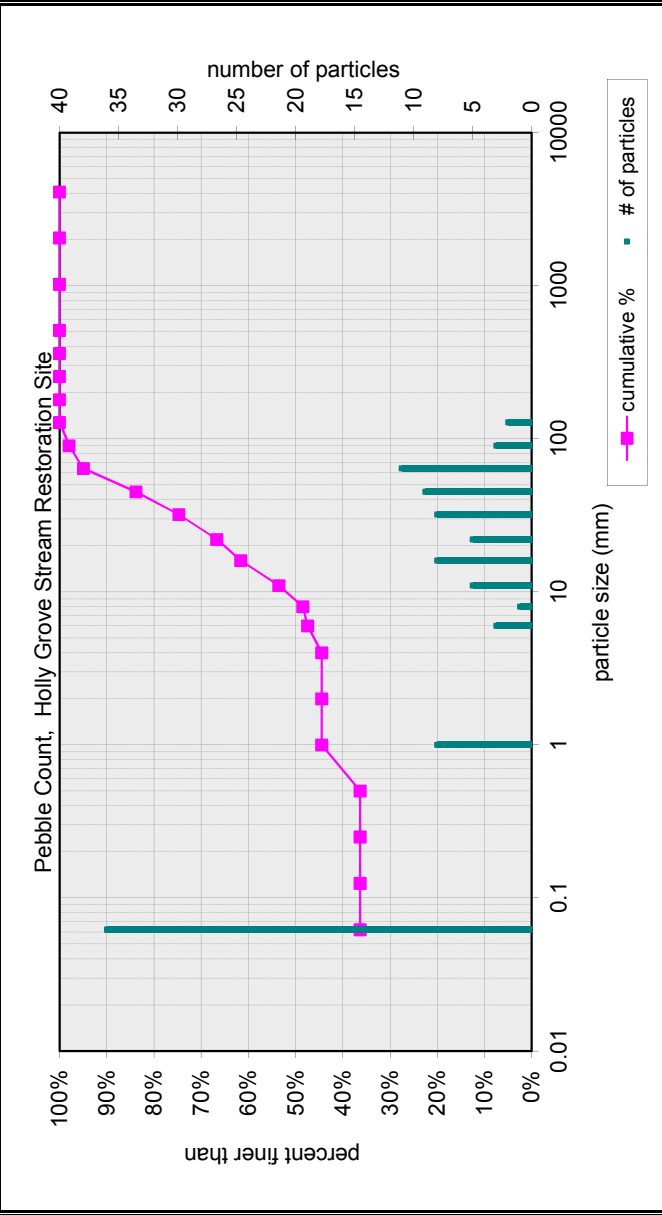

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation	geo mean	std dev	
	0.062	0.06	8.8	20	45	64		73.6	1.7	
based on total count	percent by substrate type						bedrock	hardpan	wood/det	artificial
	silt/clay	sand	gravel	cobble	boulder			0%	0%	
	36%	8%	51%	5%	0%	0%	0%	0%	0%	

Pebble Count Weighted by Channel Feature			
Percent Riffle:	39.2	Percent Run:	18.6
Percent Pool:	29.4	Percent Glide:	12.7

Material		Size Range (mm)	weighted
silt/clay		0	0.062
very fine sand		0.062	0.13
fine sand		0.13	0.25
medium sand		0.25	0.5
coarse sand		0.5	1
very coarse sand		1	2
very fine gravel		2	4
fine gravel		4	6
fine gravel		6	8
medium gravel		8	11
medium gravel		11	16
coarse gravel		16	22
coarse gravel		22	32
very coarse gravel		32	45
very coarse gravel		45	64
small cobble		64	90
medium cobble		90	128
large cobble		128	180
very large cobble		180	256
small boulder		256	362
small boulder		362	512
medium boulder		512	1024
large boulder		1024	2048
very large boulder		2048	4096

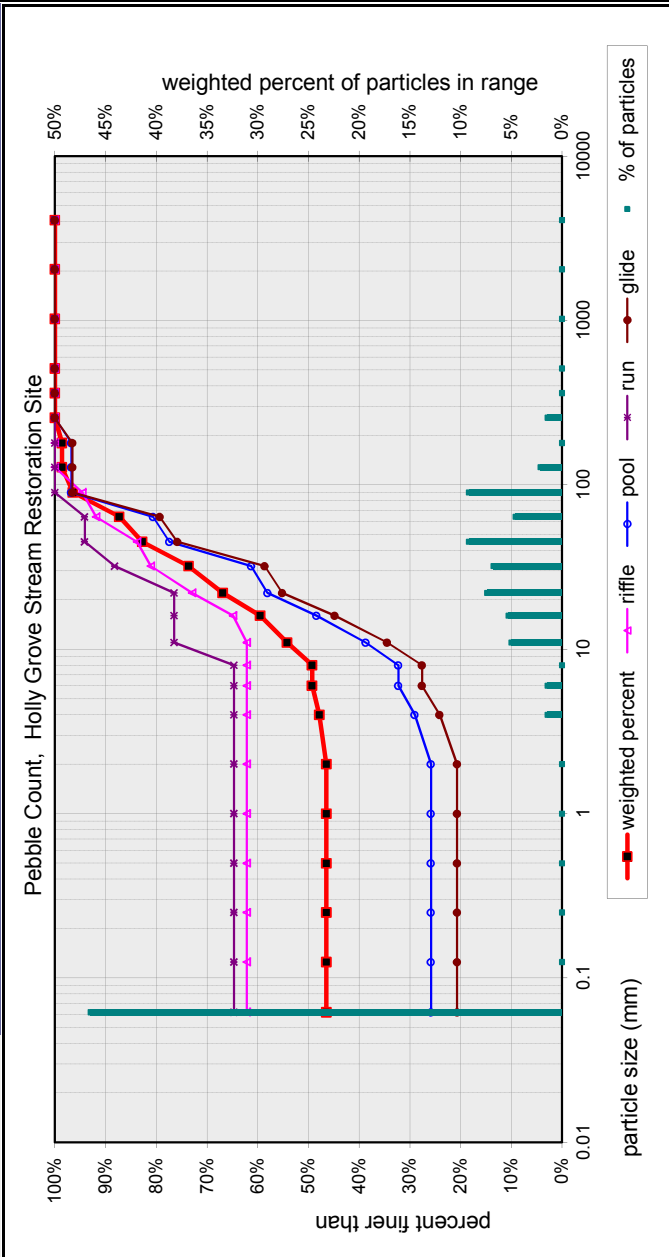

based on sediment particles only	size percent less than (mm)					particle size distribution					
	D16	D35	D50	D65	D84	D95	gradation	geo mean	std dev		
based on total count	0.062	0.06	8.4	20	49	85	70.6	1.8	28.3		
	percent by substrate type										
silt/clay		0%	sand		39%	cobble		12%	boulder		0%
bedrock		44%	hardpan		0%	wood/det		0%	artificial		0%

weighted particle count:		95.5
bedrock		4.4
clay hardpan		0.0
detritus/wood		0.0
artificial		0.0
weighted total count:		99.9

Pebble Count of Channel Reach


Material	Size Range (mm)	Count
silt/clay	0	63
very fine sand	0.062	
fine sand	0.13	
medium sand	0.25	
coarse sand	0.5	
very coarse sand	1	
	2	
very fine gravel	4	
fine gravel	6	
fine gravel	8	2
medium gravel	11	3
medium gravel	16	8
coarse gravel	22	9
coarse gravel	32	7
very coarse gravel	45	5
very coarse gravel	64	3
small cobble	90	
medium cobble	128	2
large cobble	180	
very large cobble	256	
small boulder	362	
small boulder	512	
medium boulder	1024	
large boulder	2048	
very large boulder	4096	
total particle count:		102

Holly Grove Stream Restoration Site

Guilford County, NC

East Branch: Reach 6


Note: Riffle RF-6

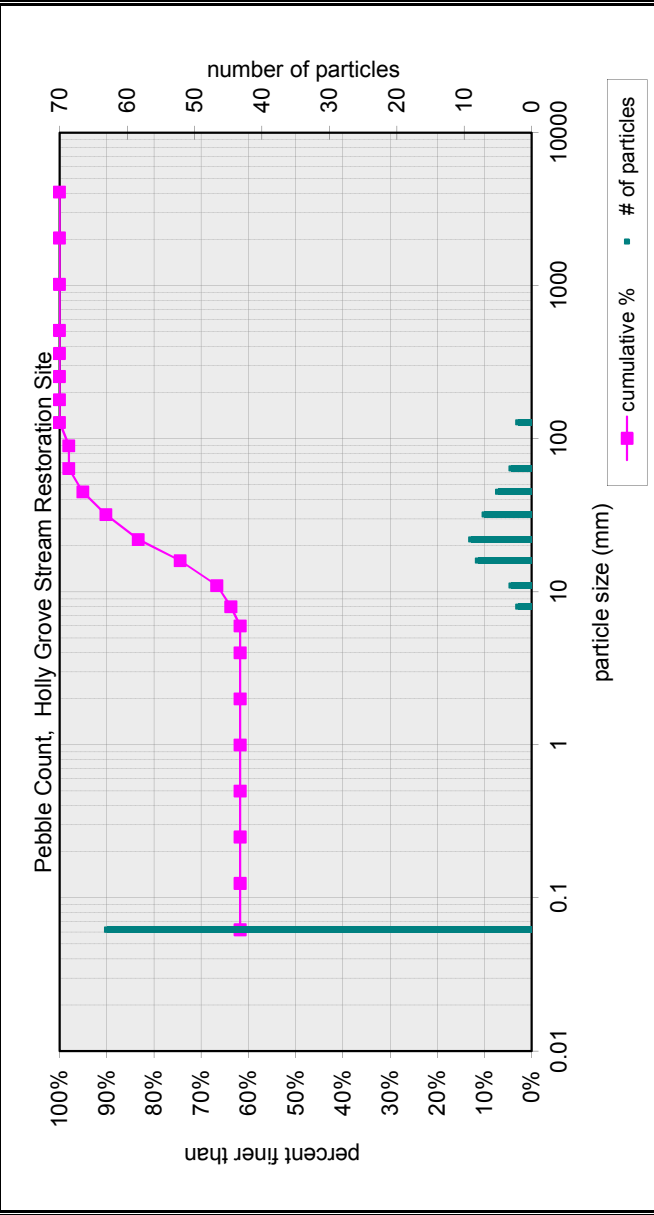

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation	geo mean	std dev	
	0.062	0.06	0.1	9	23	45	184.5	1.2	19.2	
based on total count	percent by substrate type									
	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det	artificial	
	62%	0%	36%	2%	0%	0%	0%	0%	0%	0%

Pebble Count Weighted by Channel Feature			
Percent Riffle:	29.6	Percent Run:	20.4
Percent Pool:	38.9	Percent Glide:	11.1

Material		Size Range (mm)	weighted
silt/clay		0	71.3
very fine sand		0.062	0.9
fine sand		0.13	1.9
medium sand		0.25	0.0
coarse sand		0.5	0.0
very coarse sand		1	2.8
very fine gravel		2	1.9
fine gravel		4	0.9
fine gravel		6	0.0
medium gravel		8	2.8
medium gravel		11	2.8
coarse gravel		16	2.8
coarse gravel		22	0.0
coarse gravel		32	1.9
very coarse gravel		45	0.0
very coarse gravel		64	4.6
small cobble		90	3.7
medium cobble		128	2.8
large cobble		180	0.9
very large cobble		256	0.9
small boulder		362	0.0
small boulder		512	0.0
medium boulder		1024	0.0
large boulder		2048	0.0
very large boulder		4096	0.0

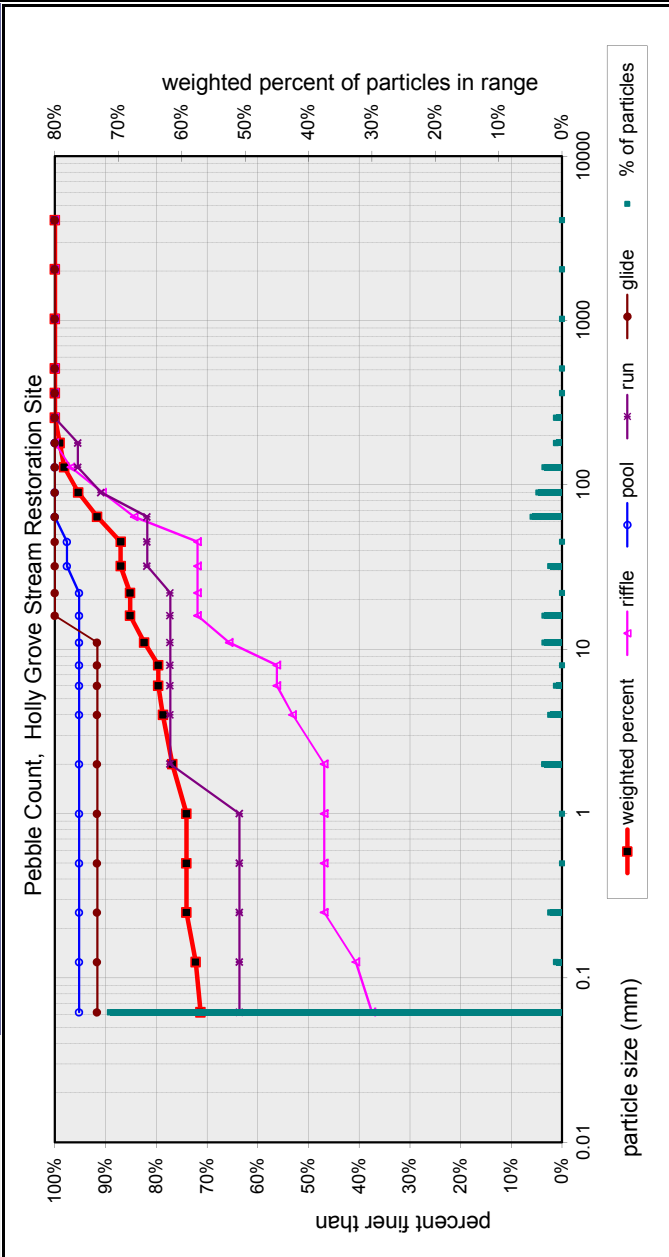

based on sediment particles only	size percent less than (mm)					particle size distribution			
	D16	D35	D50	D65	D84	D95	gradation	geo mean	std dev
based on total count	0.062	0.06	0.1	0	14	87	110.4	0.9	14.8
	percent by substrate type						bedrock	hardpan	wood/det
	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det	artificial
	71%	6%	15%	8%	0%	0%	0%	0%	0%


weighted particle count:		100.0
bedrock		0.0
clay hardpan		0.0
detritus/wood		0.0
artificial		0.0
weighted total count:		100

Pebble Count of Channel Reach

Material	Size Range (mm)	Count
silt/clay	0	70
very fine sand	0.062	1
fine sand	0.13	1
medium sand	0.25	
coarse sand	0.5	
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	9
fine gravel	8	3
medium gravel	11	3
medium gravel	16	3
coarse gravel	22	
coarse gravel	32	5
coarse gravel	45	
very coarse gravel	64	5
small cobble	90	1
medium cobble	128	1
large cobble	180	
very large cobble	256	
small boulder	362	
small boulder	512	
medium boulder	1024	
large boulder	2048	
very large boulder	4096	
total particle count:		104

bedrock	
clay hardpan	
debris/wood	
artificial	
total count:	104


Holly Grove Stream Restoration Site
 Guilford County, NC
 Southeast Creek: Reach 7
 Note: Riffle RF7

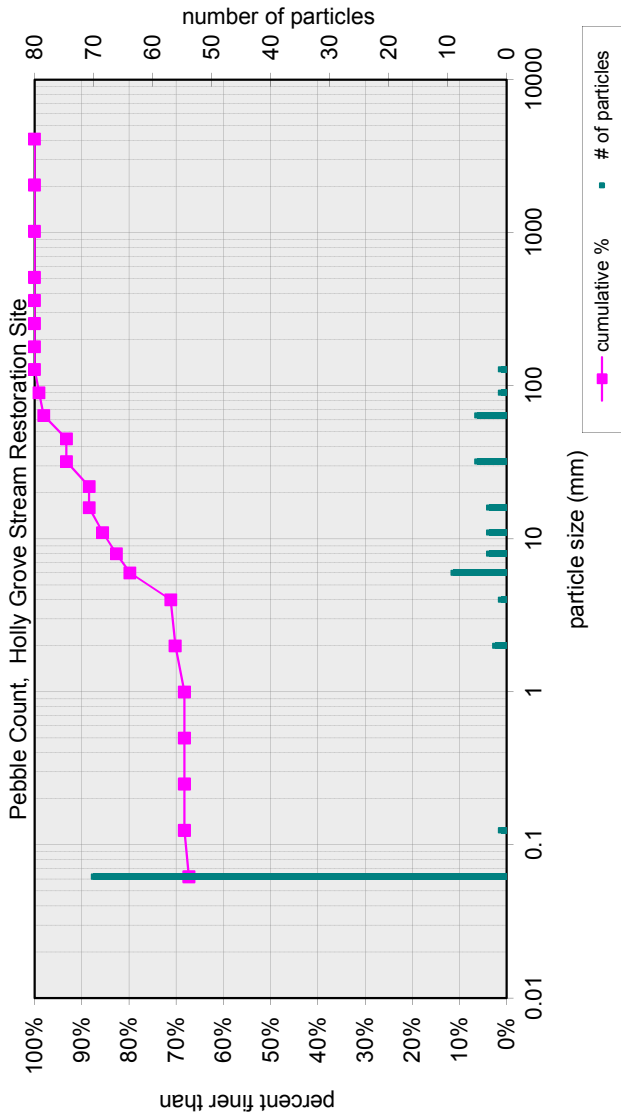

based on sediment particles only	size percent less than (mm)					particle size distribution			
	D16	D35	D50	D65	D84	D95	gradation geo mean	std dev	
	0.062	0.06	0.1	0	9	51	75.0	12.2	
based on total count	percent by substrate type					bedrock	hardpan	wood/det	artificial
	silt/clay	sand	gravel	cobble	boulder	0%	0%	0%	0%
	67%	3%	28%	2%	0%	0%	0%	0%	

Pebble Count Weighted by Channel Feature			
Percent Riffle:	32	Percent Run:	19.4
Percent Pool:	30.1	Percent Glide:	18.4

Material	Size Range (mm)	weighted
silt/clay	0	0.062
very fine sand	0.062	0.13
fine sand	0.13	0.25
medium sand	0.25	0.5
coarse sand	0.5	1
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	16
coarse gravel	16	22
coarse gravel	22	32
very coarse gravel	32	45
very coarse gravel	45	64
small cobble	64	90
medium cobble	90	128
large cobble	128	180
very large cobble	180	256
small boulder	256	362
small boulder	362	512
medium boulder	512	1024
large boulder	1024	2048
very large boulder	2048	4096

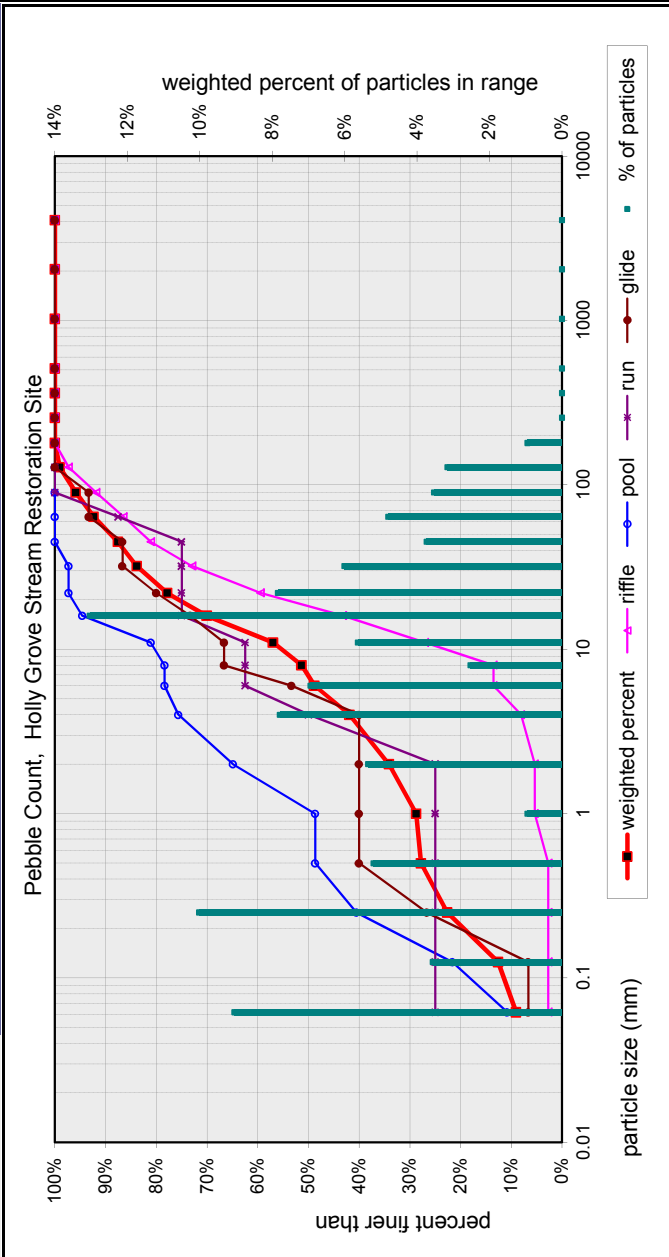

based on sediment particles only	D16	D35	D50	D65	D84	D95	particle size distribution gradation geo mean	std dev
	0.158	2.16	6.9	14	32	83	24.1	2.3
based on total count	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det
	8%	23%	53%	7%	0%	9%	0%	0%

bedrock	8.6
clay hardpan	0.0
detritus/wood	0.0
artificial	0.0
weighted total count:	99.9

Pebble Count of Channel Reach


Material	Size Range (mm)	Count
silt/clay	0	11
very fine sand	0.062	
fine sand	0.13	
medium sand	0.25	2
coarse sand	0.5	1
very coarse sand	1	2
very fine gravel	2	4
fine gravel	4	6
fine gravel	6	8
medium gravel	8	11
medium gravel	11	16
coarse gravel	16	22
coarse gravel	22	32
very coarse gravel	32	45
very coarse gravel	45	64
small cobble	64	90
medium cobble	90	128
large cobble	128	180
very large cobble	180	256
small boulder	256	362
small boulder	362	512
medium boulder	512	1024
large boulder	1024	2048
very large boulder	2048	4096
total particle count:		101

Holly Grove Stream Restoration Site

Guilford County, NC

Southwest Creek: Reach 8

Note: Riffle RF8

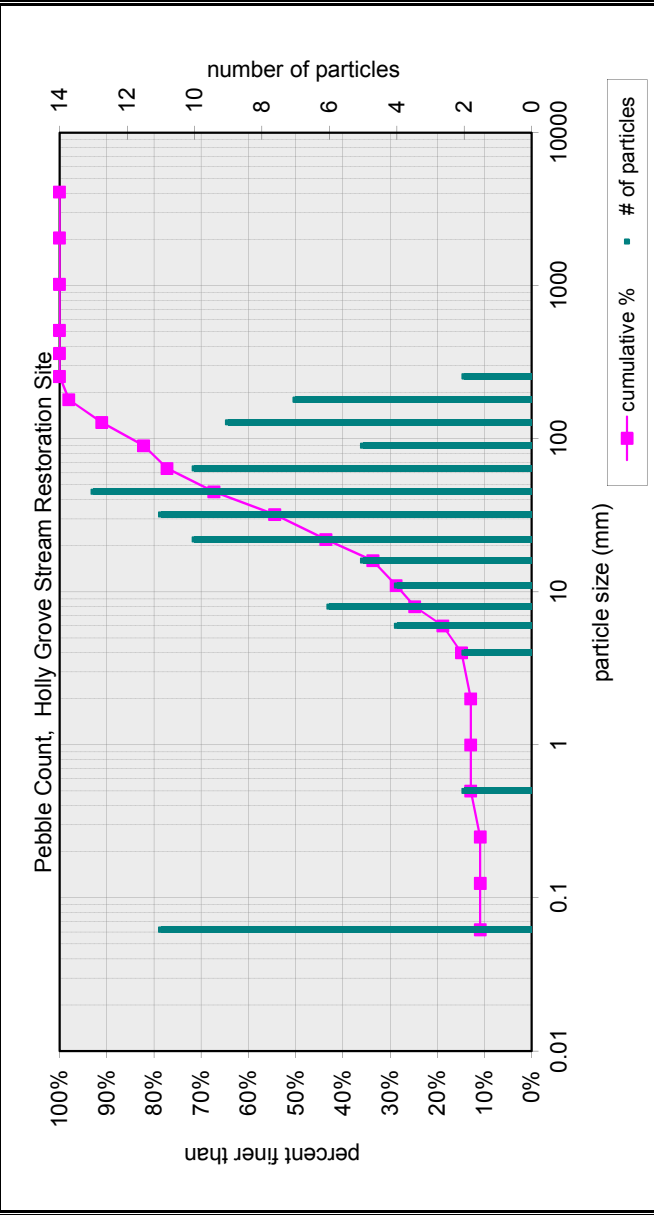

based on sediment particles only	D16	D35	D50	D65	D84	D95	D95 gradation	particle size distribution geo mean	std dev	
	4.499	16.70	27.5	42	97	155	4.8	20.9	4.6	
based on total count	percent by substrate type									
	silt/clay	sand	gravel	cobble	boulder	bedrock	hardpan	wood/det	artificial	
	11%	2%	64%	23%	0%	0%	0%	0%	0%	0%

bedrock	
clay hardpan	
detritus/wood	
artificial	
total count:	101
