

Little Alamance Creek (Burlington Park) Stream Restoration 2013 Monitoring Report Monitoring Year 1 of 5

Alamance County, NC
Cape Fear River Basin
Cataloging Unit: 03030002
NCEEP Project Number: 92372
NCEEP Contract Number: 4998



Submitted To:

North Carolina Department of Environment and Natural Resources
Ecosystem Enhancement Program
1652 Mail Service Center
Raleigh, NC 27699-1652

FINAL – 2013 Monitoring Report – Year 1 of 5

Project Construction Completed: 2012
Data Collection for Monitoring Year 1 of 5
Report Submitted: July 2013



**Little Alamance Creek (Burlington Park) Stream Restoration
2013 Monitoring Report
Monitoring Year 1 of 5**

**Alamance County, NC
Cape Fear River Basin**

Submitted to:
North Carolina Department of Environment and Natural Resources
Ecosystem Enhancement Program
1652 Mail Service Center
Raleigh, NC 27699-1652

Prepared by:
EEE Consulting, Inc.
601 Cascade Pointe Lane, Suite 101
Cary, NC 27513

Project Manager:
Ray Bode, PWS
(919) 650-2463 ext. 225
rbode@eee-consulting.com

July 2013

FINAL

TABLE OF CONTENTS

1. Executive Summary/Project Abstract.....1
2. Methodology.....3
 2.1 Stream Survey Methodology.....4
 2.2 Vegetation Survey Methodology.....4
3. References.....5

APPENDICES, FIGURES, and TABLES

Appendix A: Project Vicinity Map and Background Tables

Figure 1: Vicinity Map
Table 1a: Project Components
Table 1b: Component Summations
Table 2: Project Activity and Reporting History
Table 3: Project Contacts Table
Table 4: Project Attribute Table

Appendix B: Visual Assessment Data

Figure 2: Current Condition Plan View
Figure 3: Conservation Easement Marked Posts
Figure 4: Final Conservation Easement Plat
Figure 5: Conservation Easement Coordinate List
Table 5: Visual Stream Morphology Stability Assessment
Table 6: Vegetation Condition Assessment
Photo Log 1: Established Photo Stations
Photo Log 2: Vegetation Plot Photos

Appendix C: Vegetation Plot Data

Table 7: Vegetation Plot Success by Project Asset Type
Table 8: CVS Stem Count Total and Planted with/without Livestakes by Plot and Species

Appendix D: Stream Survey Data

Figure 6: Cross Section with Annual Overlays
Figure 7: Longitudinal Profiles with Annual Overlays
Figure 8: Pebble Counts with Annual Overlays
Table 9: Stream Bank Erosion Pin Data Table
Table 10a: Baseline Stream Data Summary
Table 10b: Baseline Stream Data Summary (Substrate, Bed, Bank, and Hydrologic Containment Parameter Distributions)
Table 11a: Monitoring – Cross-Section Morphology Data Table
Table 11b: Monitoring – Stream Reach Morphology Data Table

Appendix E: Hydrologic Data

Table 12: Verification of Bankfull Events
Figure 9: Monthly Rainfall Data

1.0 EXECUTIVE SUMMARY / PROJECT ABSTRACT

The primary goals of this stream restoration project focus on improving water quality, enhancing flood attenuation, and restoring aquatic habitat. These goals will be accomplished by the following objectives:

- Reducing non-point sources of pollution associated with former lawn maintenance in the park area by providing a vegetative buffer adjacent to Little Alamance Creek and its unnamed tributary and the installation of stormwater best management practices to treat surface runoff. The riparian buffer will remain in a State-owned conservation easement in perpetuity.
- Reducing sedimentation on-site and in downstream receiving waters through a reduction of bank erosion associated with current vegetation maintenance practices and by providing a forested vegetative buffer adjacent to Little Alamance Creek and its tributary.
- Reestablishing stream stability and the capacity to transport watershed flows and sediment loads by restoring stable dimension, pattern, and profile.
- Promoting floodwater attenuation through increased flood storage capacity by construction of bankfull benches along Little Alamance Creek and its tributary.
- Improving aquatic habitat by enhancing stream bed variability.

The Site consists of 2,725 linear feet of enhanced (Level I and II) channel along Little Alamance Creek and its unnamed tributary. The project is located in City Park in the City of Burlington, Alamance County, North Carolina (Figure 1). The surrounding land use is recreational and the project is easily accessible by the public. Little Alamance Creek and its unnamed tributary are located in the 8-digit Hydrologic Unit Code (HUC) 03030002; the 14-digit Local Watershed Unit HUC 03030002-040010; and the North Carolina Division of Water Quality (NCDWQ) Subbasin 03-06-03 (NCDWQ, 2005). The project lies within the Southern Outer Piedmont ecoregion of the Piedmont physiographic province of NC (Griffith *et al.*, 2002). The North Carolina Ecosystem Enhancement Program (NCEEP) has identified the Cape Fear HUC 03030002, and in particular Little Alamance Creek, in their Local Watershed Plan as needing repair along with conservation opportunities. Watersheds in this plan exhibit the need and opportunity for stream and riparian buffer restoration (NCDENR, 2001). In 2000, Little Alamance Creek was listed as impaired by the NCDWQ due to poor stream biological ratings (NCEEP, 2008).

Little Alamance Creek was originally planted in April, 2012. On September 11, 2012, the site was inspected by NCEEP and vegetative sampling reported higher mortality than contractually permissible. Of the 15 inspection plots, 6 did not meet the 80 percent survival warranty. The areas identified as needing supplemental planting were re-planted on December 12, 2012. Monitoring Year 1 efforts showed that the site is currently meeting vegetation success criteria of 320 stems per acre at most plot locations. Vegetation plots 1 through 6 have met this

requirement; however, vegetation plots 7 and 8 did not (Table 1). Volunteer species are establishing on site as expected and thus increasing the overall stems per acre. The Total Mean Density of the site is 809 stems per acre. Three areas were identified with invasive species in the conservations easement (Figure 2). Along the upper reaches of the unnamed tributary, multiflora rose (*Rosa multiflora*) was observed. These areas are negligible in size and are represented as point features. Along the upper reach of the mainstem, Chinese privet (*Ligustrum sinense*) was observed. This area was also negligible in size and is represented as a point feature. Individual stems of multiflora rose and Chinese privet were observed throughout the site, but at very low density. Both multiflora rose and Chinese privet are listed as high concern in the NCEEP Monitoring Report Template, Version 1.5. However, the presence of invasive species is minor, covering approximately 5 percent of the planted easement. These areas will continue to be monitored in the upcoming monitoring years. No other problems areas were observed.

Overall, the Little Alamance Creek Stream Restoration Site is in very good condition. All structures are intact and performing as intended. The Monitoring Year 1 thalweg has not deviated from the design thalweg. There is a notable lack of bank erosion, attributable to low bank angles and well established streamside vegetation. One small area along the unnamed tributary downstream of cross section 14 that has minor bank erosion (Figure 2). This area will continue to be monitored in the upcoming monitoring years. No other problems areas were observed. Two crest gauges were installed during Monitoring Year 1; one gauge along the mainstem of Little Alamance Creek and one gauge along the unnamed tributary. These gauges will be checked starting in Monitoring Year 2 to record the max height of the yearly storm event.

Wetland mitigation is not a part of this project.

Summary information/data related to the occurrence of items such as beaver or encroachment and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report (formerly Mitigation Plan) and in the Mitigation Plan (formerly the Restoration Plan). These documents are available on NCEEP's website. All raw data supporting the tables and figures in the appendices is available from NCEEP upon request. Due to contracting issues, no Baseline Monitoring Report was prepared for this project. As a result, the data collected during Monitoring Year 1 will serve as baseline data.

2.0 METHODOLOGY

All monitoring methodologies follow NCEEP's 2011 *Monitoring Requirements and Performance Standards for Stream and/or Wetland Mitigation* (NCEEP, 2011). This monitoring report is consistent with NCEEP's *Monitoring Report Template Version 1.5* adopted June 8, 2012. GPS data was collected using sub-meter accuracy Trimble Geo XH handheld unit. Stream and vegetation problems areas were identified and noted in the field on As-Built Plan Sheets prepared by ARCADIS G&M of North Carolina (ARCADIS, 2012). Twenty permanent photo stations were established during the project set up by EEE Consulting, Inc. (EEE) and

photographs were taken from these locations (Figure 2). Photographs were taken at a high resolution using a Sony Cyber-shot 14.1 megapixel digital camera.

2.1 STREAM SURVEY METHODOLOGY

Prior to Year 1 monitoring efforts, EEE established eight permanent riffle cross-sections and six permanent pool cross sections (Figure 2). GPS points were collected on both banks of each established cross section. The entire length of mitigation, 2,725 linear feet of stream profile, was surveyed. Stream monitoring and geomorphological surveys were performed consistent with the USACE 2003 *Stream Mitigation Guidelines* and the USDA 1994 Forest Service Manual *Stream Channel Reference Sites: An Illustrated Guide to Field Technique* (USACE, 2003; Harrelson *et al.*, 1994). Stream survey data was collected using a Nikon total station with a Recon data logger and is georeferenced in NAD83-State Plane Feet-FIPS3200. The data were analyzed using RIVERMorph. Pebble counts were conducted consistent with the 1954 Wolman Pebble Count technique (modified by Rosgen, 1996). A random sample of 100 pebbles from each feature of cross section was collected within the wetted perimeter of the channel. Samples were not taken from the banks. Photographs were taken at each cross section. A photo was taken from the left bank looking towards the right bank.

2.1 VEGETATION SURVEY METHODOLOGY

Prior to Year 1 monitoring efforts, EEE established eight vegetation plots per the CVS-EEP vegetation monitoring protocol (Figure 2). Five plots are 10 meters by 10 meters in size and 2 plots, (VP 6 and 7) are 20 meters by 5 meters in size. GPS points were collected all four corners of each established vegetation plot. Vegetation monitoring was performed in accordance with the 2008 CVS-EEP Protocol for Recording Vegetation for Level 1-2 Plot Sampling Only, Version 4.2 (Lee *et al.*, 2008). Level 2 sampling was performed for each vegetation plot. Each corner of the vegetation plot was marked with steel electrical metallic tubing (EMT) driven into the ground. Because the project is within a public park, minimal flagging was used to mark the stems and no flagging was used to mark the vegetation plot corner pins. Minimal orange flagging was used to mark only planted stems during vegetation counts. Photographs were taken at each vegetation plot from the southwest corner facing the northeast corner.

3.0 REFERENCES

- ARCADIS G&M of North Carolina, 2012. As-Built Survey of Little Alamance Creek Stream Restoration. Prepared for the NC Ecosystem Enhancement Program.
- Griffith, Glenn, J. Omemik, J. Comstock, 2002. Ecoregions of North Carolina Regional Descriptions. U.S. Department of Agriculture, Natural Resources Conservation Service. Corvallis. OR.
- Harrelson, Cheryl C., C.L. Rawlins, John P. Potyondy, 1994. US Department of Agriculture, Forest Service. Stream Channel Reference Sites: An Illustrated Guide to Field Technique. Available URL: http://www.fs.fed.us/rm/pubs_rm/rm_gtr245.pdf. [Date Accessed: 4 January 2013].
- Lee, Michael T., R. K. Peet, S. D. Roberts, and T. R. Wentworth. 2006. CVS-EEP Protocol for Recording Vegetation, Version 4.0 Available URL: <http://cvs.bio.unc.edu/methods.htm>. [Date Accessed: 4 January 2013].
- NC Division of Water Quality, 2005. Cape Fear River Basin Water Quality Plan. Available URL: <http://portal.ncdenr.org/web/wq/ps/bpu/basin/capefear/2005>. [Date Accessed: 4 January 2013].
- NC Department of Environment and Natural Resources, 2001. Watershed Restoration Plan for the Cape Fear River Basin. Prepared by: NCDENR, NCDWQ, and NCWRP. Available URL: http://www.nceep.net/services/restplans/cape_fear_2001.pdf. [Date Accessed: 4 January 2013].
- NC Ecosystem Enhancement Program, 2008. Little Alamance, Travis, & Tickle Creek Watershed Report & Project Atlas: An Ecosystem Enhancement Program Funded Local Watershed Plan Phase III. Prepared by Piedmont Triad Council of Governments. Available URL: http://www.ptcog.org/planning_services/environmental_planning/documents/water_LATTPhaseIII.pdf. [Date Accessed: 4 January 2013].
- NC Ecosystem Enhancement Program, 2011. Monitoring Requirements and Performance Standards for Stream and/or Wetland Mitigation. Available URL: http://portal.ncdenr.org/c/document_library/get_file?p_1_id=1169848&folderId=2288101&name=D_LFE-39234.pdf. [Date Accessed: 4 January 2013].
- RIVERMorph Stream Restoration Software, Version 5.1.0. Rivermorph LLC.
- Rosgen, D.L., 1996. Applied River Morphology. Wildland Hydrology, Pagosa Springs. CO.
- US Army Corps of Engineers, 2003. Stream Mitigation Guidelines. Prepared by: USACE, NCDWQ, USEPA, NCWRC. Available URL: http://www.in.gov/idem/files/headwater_nc_stream_mitigation_guide.pdf. [Date Accessed: 4 January 2013].

Appendix A: Project Vicinity Map and Background Tables

Figure 1: Project Vicinity Map

Table 1a: Project Components


Table 1b: Component Summations

Table 2: Project Activity and Reporting History

Table 3: Project Contacts Table

Table 4: Project Attribute Table

Directions to the Site:
 From Raleigh, take I-40W to exit 145 for NC 49 toward Burlington/Downtown/Liberty
 Turn right into NC 49 North / Maple Avenue
 Turn left onto Chapel Hill Road
 Turn right onto Pinecrest Street
 Turn right onto Overbrook Street
 Take second right to stay on Overbrook Street
 Slight right to stay on Overbrook Street

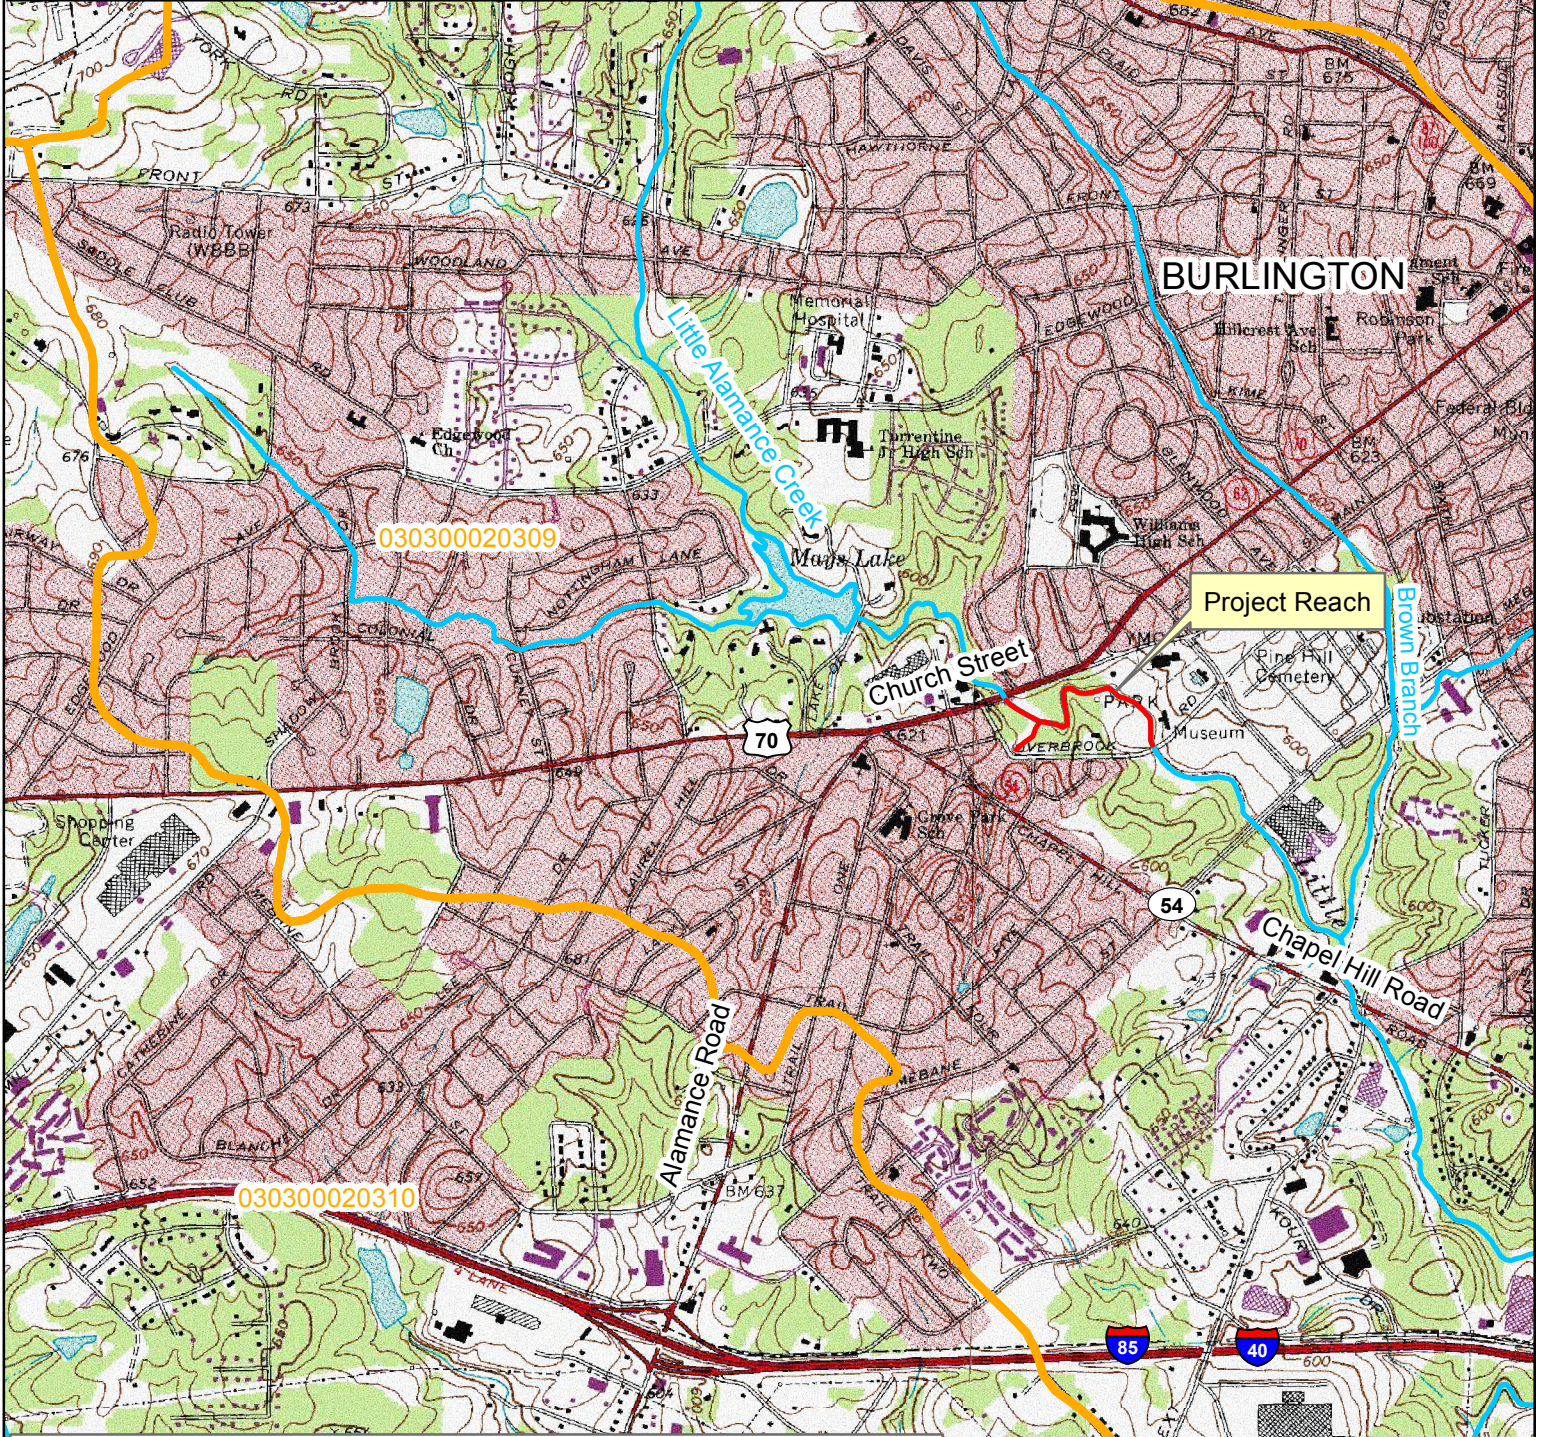

Source: USDA Digital Raster Graphic Mosaic of Alamance County, NC; 2012

Legend

- Project Reach
- Streams
- 12 Digit HUC




Figure 1: Vicinity Map
 Little Alamance Creek (Burlington Park) Stream Restoration
 Alamance County
 NCEP Project Number: 92372

EEE Consulting, Inc.
 Cary, NC

Monitoring Year 1 of 5
 June 2013

Table 1a. Project Components
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372)

Project Component or Reach ID	Existing Feet/Acres	Restoration Level	Approach	Footage or Acreage	Stationing	Mitigation Ratio	Mitigation Units	BMP Elements ¹	Comment
Reach I	425 lf	EI	P3	425 lf	10+25 - 11+75 12+25 - 15+00	1.5:1	283		
Reach II - Trib	450 lf	EI	P3	450 lf	10+00 - 14+50	1.5:1	300		
Reach III	350 lf	EII	-	350 lf	15+50 - 19+00	2.5:1	140	LS	
Reach IV	625 lf	EI	P3	625 lf	19+50 - 21+25 21+75 - 26+25	1.5:1	416	LS	
Reach V	75 lf	EII	-	75 lf	26+50 - 27+25	2.5:1	30		
Reach VI	500 lf	EI	P3	500 lf	27+75 - 31+50 31+75 - 33+00	1.5:1	333		
Reach VII	300 lf	EII	-	300 lf	33+50 - 36+50	2.5:1	120		

1 = BR = Bioretention Cell; SF = Sand Filter; SW = Stormwater Wetland; WDP = Wet Detention Pond; DDP = Dry Detention Pond;
 FS = Filter Strip; Grassed Swale = S; LS = Level Spreader; NI = Natural Infiltration Area, O = Other
 CF = Cattle Fencing; WS = Watering System; CH = Livestock Housing

Table 1b. Component Summations
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372)

Restoration Level	Stream (lf)	Riparian Wetland (Ac)		Non-Ripar (Ac)	Upland (Ac)	Buffer (Ac)	BMP
		Riverine	Non-Riverine				
Restoration							
Enhancement							
Enhancement I	2000						
Enhancement II	725						
Creation							
Preservation							
HQ Preservation							
Totals (Feet/Acres)	2725						2
MU Totals	1622						

Non-Applicable

**Table 2. Project Activity and Reporting History
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372)**

**Elapsed Time Since Grading Complete: 1 yrs 6 months
Elapsed Time Since Planting Complete: 1 yrs 6 Months
Number of Reporting Years¹: 1**

Activity or Deliverable	Data Collection Complete	Completion or Delivery
Institution Date	Nov-06	N/A
Categorical Exclusion	Sep-07	N/A
404 Permit Date	Apr-08	N/A
Restoration Plan	Jan-08	N/A
Final Design – Construction Plans	Sep-10	N/A
Construction	Feb-12	Apr-12
Seeding, bare roots, and live stake planting	Feb-12	Apr-12
Bare Root - Supplemental Planting	N/A	Dec-12
Mitigation Plan / As-built (Year 0 Monitoring - baseline)	N/A	N/A
Year 1 Monitoring	Mar-13	Jun-13
Year 2 Monitoring	TBD	TBD
Year 3 Monitoring	TBD	TBD
Year 4 Monitoring	TBD	TBD
Year 5 Monitoring	TBD	TBD

Due to contracting delays, no baseline data was collected for this project. Although there are no baseline cross sections to compare with MY1 (2013) measurements, the 2013 cross sections will serve as an adequate baseline for the remaining monitoring period. Similarly, no baseline vegetation data was collected until March 2013, approximately 13 months after planting occurred in February 2012.

Bolded items are examples of those items that are not standard, but may come up and should be included

Non-bolded items represent events that are standard components over the course of a typical project.

The above are obviously not the extent of potential relevant project activities, but are just provided as example as part of this exhibit.

If planting and morphology are on split monitoring schedules that should be made clear in the table

1 = Equals the number of reports or data points produced excluding the baseline

Table 3. Project Contacts Table Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372)	
Designer	ARCADIS G&M of North Carolina, Inc 801 Corporate Drive, Suite 300 Raleigh, NC 27607
Primary project design POC	Robert Lepsic (919) 854-1282 ext. 195
Construction Contractor	Shamrock Environmental Corporation 6106 Corporate Park Drive Browns Summit, NC 27214
Construction contractor POC	(336) 375-1989
Survey Contractor	Turner Land Surveying, PLLC 3201 Glenridge Drive Raleigh, NC 27604
Survey contractor POC	Elisabeth Turner (919) 875-1378
Planting Contractor	Carolina Wetland Services 550 East Westinghouse Boulevard Charlotte, NC 28273
Planting contractor POC	(704) 527-1177
Seeding Contractor	Information Not available
Contractor point of contact	POC name and phone
Seed Mix Sources	Information Not available
Nursery Stock Suppliers	Native, Inc. (704) 527-1177
Monitoring Performers	EEE Consulting, Inc. 601 Cascade Pointe Lane Suite 101 Cary, NC 27513
Stream Monitoring POC	Ray Bode, PWS (919) 650-2463 ext. 225
Vegetation Monitoring POC	Tina Sekula, PWS (919) 650-2463 ext. 223

**Table 4. Project Attribute Table
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372)**

Project Information							
Project Name	Little Alamance Creek (Burlington Park) Stream Restoration						
County	Alamance County						
Project Area (acres)	7.06 acres						
Project Coordinates (latitude and longitude)	36.083566 ; -79.454233						
Project Watershed Characteristics							
Physiographic Province	Piedmont						
River Basin	Cape Fear						
USGS Hydrologic Unit 8-digit: 03030002	USGS Hydrologic Unit 14-digit: 3030002040010						
DWQ Sub-basin	03-06-03						
Project Drainage Area (acres)	2690 acres						
Project Drainage Area Percentage of Impervious Area	40 percent						
CGIA Land Use Classification	Forest Land						
Reach Summary Information							
Parameters	Reach I	Reach III - Trib	Reach III	Reach IV	Reach V	Reach VI	Reach VII
Length of Reach (linear feet)	425 lf	450 lf	350 lf	625 lf	75 lf	500 lf	300 lf
Valley Classification	Type VIII	Type VIII	Type VIII	Type VIII	Type VIII	Type VIII	Type VIII
Drainage area (acres)	2600 ac	124 ac	2630 ac	2650 ac	2655 ac	2680 ac	2690 ac
NCDWQ Stream Identification Score	47.5	33	47.5	47.5	47.5	47.5	47.5
NCDWQ Water Quality Classification	WS-V;NSW	WS-V;NSW	WS-V;NSW	WS-V;NSW	WS-V;NSW	WS-V;NSW	WS-V;NSW
Morphological Description (stream type)	C/E5/1	E4/1	C/E5/1	C/E5/1	C/E5/1	C/E5/1	C/E5/1
Evolutionary Trend	C4/1	C4/1	C4/1	C4/1	C4/1	C4/1	C4/1
Underlying Mapped Soils	Cecil fine sandy loam (CbC2)						
Drainage Class	Well drained						
Soil Hydric Class	Non-Hydric						
Slope	6 to 10 percent slopes						
FEMA Classification	AE Floodzone	No Study	AE Floodzone	AE Floodzone	AE Floodzone	AE Floodzone	AE Floodzone
Native Vegetation Community	Mixed Mesic Forest						
Percent composition of exotic invasive vegetation	5 percent						
Regulatory Considerations							
Regulation	Applicable?	Resolved?	Supporting Documentation				
Waters of the United States - Section 404	Yes	Yes	Nationwide Permit 27 (Action ID SAW-2008-01198)				
Waters of the United States - Section 401	Yes	Yes	Nationwide Permit 27 (Action ID SAW-2008-01198)				
Endangered Species Act	No	N/A	N/A				
Historic Preservation Act	No	N/A	N/A				
Coastal Zone Management Act (CZMA)/ Coastal Area Management Act (CAMA)	No	N/A	N/A				
FEMA Floodplain Compliance	Yes	Yes	FEMA Floodplain Consistency Checklist (Categorical Exclusion)				
Essential Fisheries Habitat	No	N/A	N/A				

Appendix B: Visual Assessment Data

Figure 2: Current Condition Plan View

Figure 3: Conservation Easement Marked Posts

Figure 4: Final Conservation Easement Plat


Figure 5: Conservation Easement Coordinate List

Table 5: Visual Stream Morphology Stability Assessment

Table 6: Vegetation Condition Assessment

Photo Log 1: Established Photo Stations

Photo Log 2: Vegetation Monitoring Plot Photos

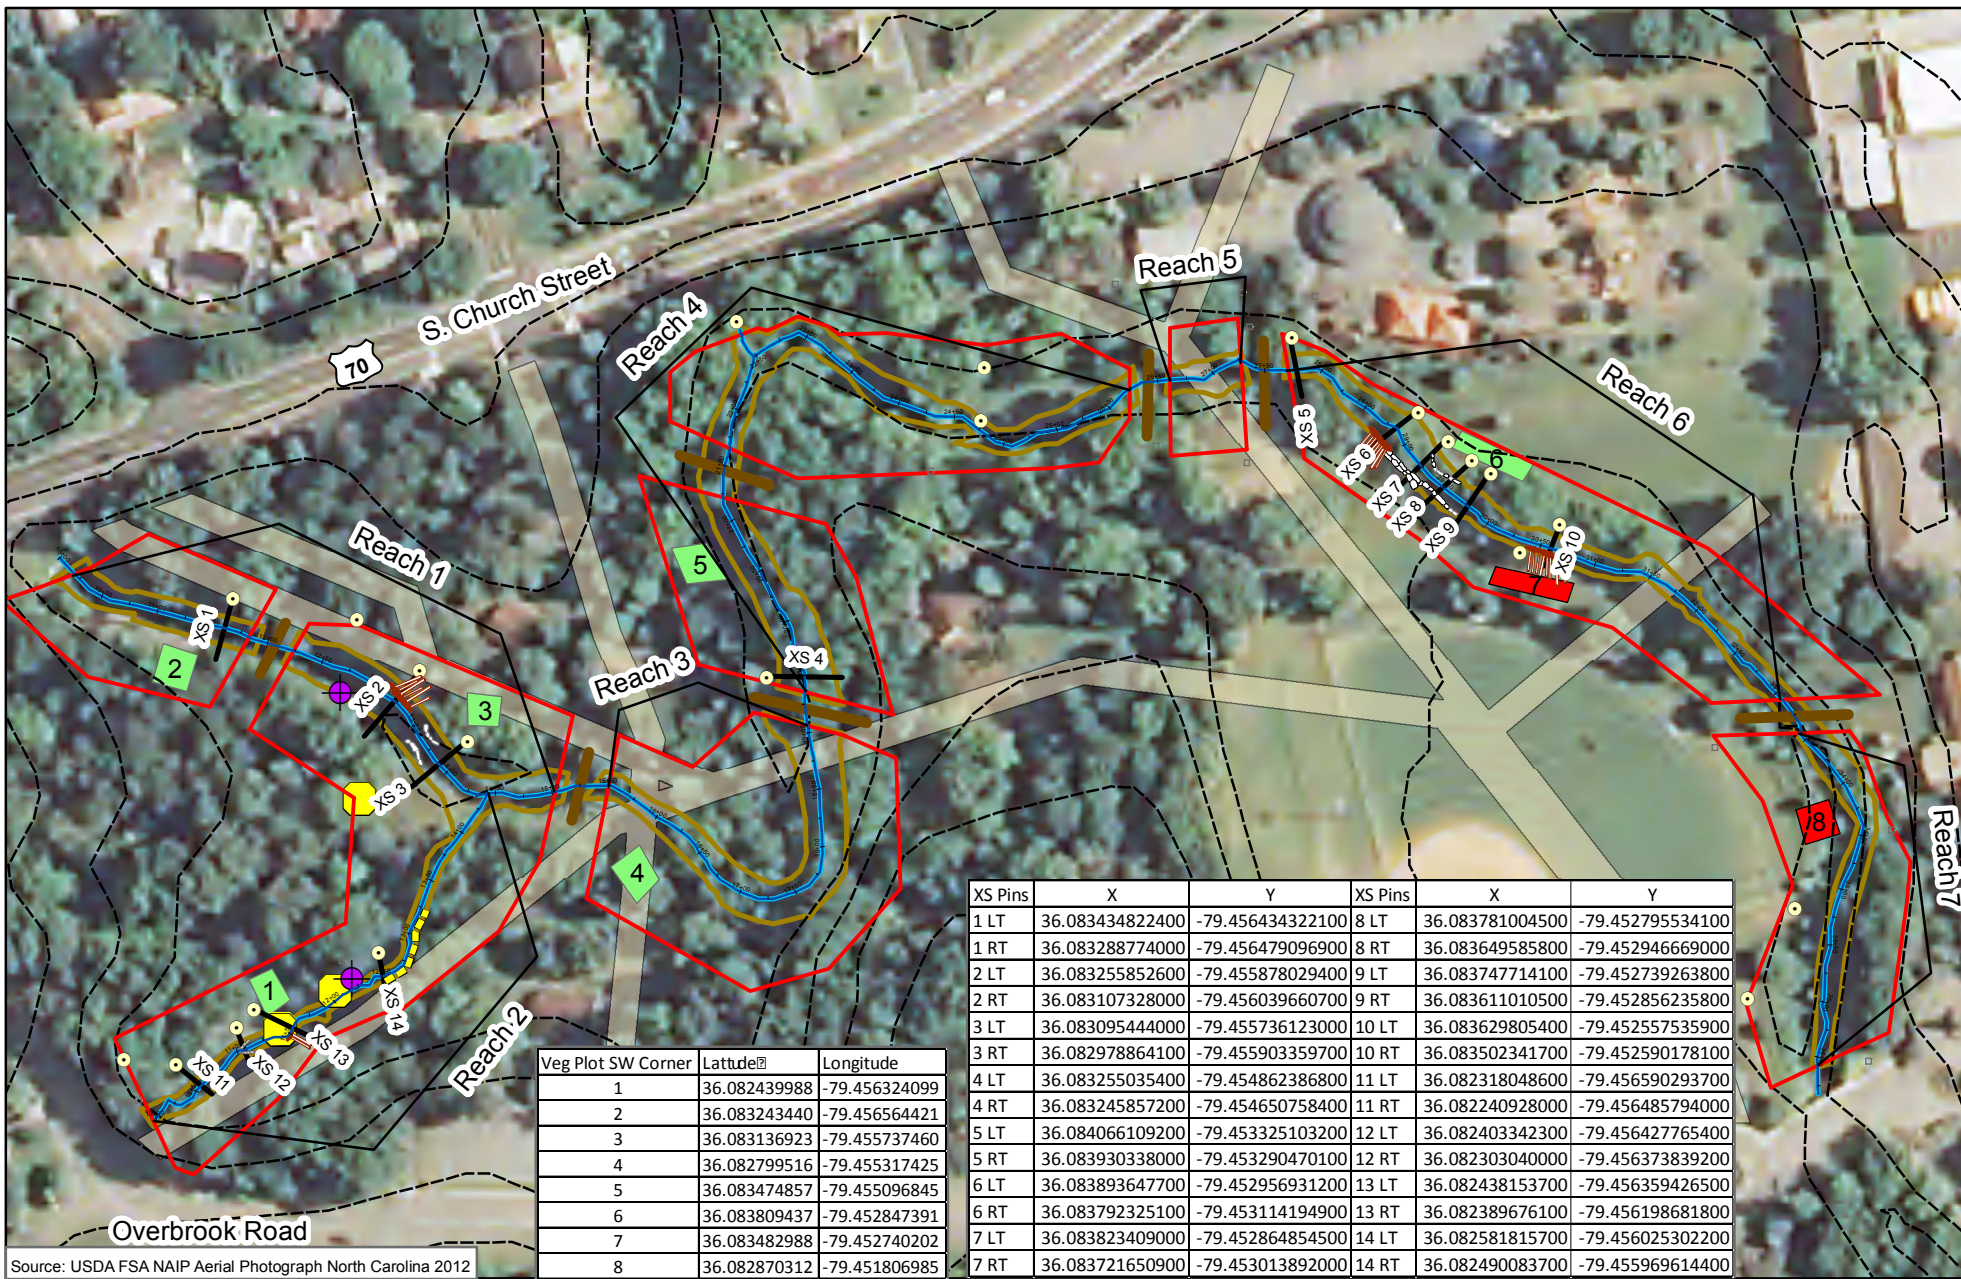

Source: USDA FSA NAIP Aerial Photograph North Carolina 2012


Veg Plot SW Corner	Latitude	Longitude
1	36.082439988	-79.456324099
2	36.083243440	-79.456564421
3	36.083136923	-79.455737460
4	36.082799516	-79.455317425
5	36.083474857	-79.455096845
6	36.083809437	-79.452847391
7	36.083482988	-79.452740202
8	36.082870312	-79.451806985


XS Pins	X	Y	XS Pins	X	Y
1 LT	36.083434822400	-79.456434322100	8 LT	36.083781004500	-79.452795534100
1 RT	36.083288774000	-79.456479096900	8 RT	36.083649585800	-79.452946669000
2 LT	36.083255852600	-79.455878029400	9 LT	36.083747714100	-79.452739263800
2 RT	36.083107328000	-79.456039660700	9 RT	36.083611010500	-79.452856235800
3 LT	36.083095444000	-79.455736123000	10 LT	36.083629805400	-79.452557535900
3 RT	36.082978864100	-79.455903359700	10 RT	36.083502341700	-79.452590178100
4 LT	36.083255035400	-79.454862386800	11 LT	36.082318048600	-79.456590293700
4 RT	36.083245857200	-79.454650758400	11 RT	36.082240928000	-79.456485794000
5 LT	36.084066109200	-79.453325103200	12 LT	36.082403342300	-79.456427765400
5 RT	36.083930338000	-79.453290470100	12 RT	36.082303040000	-79.456373839200
6 LT	36.083893647700	-79.452956931200	13 LT	36.082438153700	-79.456359426500
6 RT	36.083792325100	-79.453114194900	13 RT	36.082389676100	-79.456198681800
7 LT	36.083823409000	-79.4542864854500	14 LT	36.082581815700	-79.456025302200
7 RT	36.083721650900	-79.453013892000	14 RT	36.082490083700	-79.455969614400


Legend

- Crest Gauges
- Conservation Easement
- Structures
- Photostations
- Contours (4ft)
- VP Criteria Not Met
- Invasive Species
- Designed Centerline
- VP Criteria Met
- Bank Instability
- MY1 Thalweg
- Utility Easement
- Existing Crossings
- Designed Top of Bank
- Cross Sections

0 125 250 500 Feet


Figure 2: Current Condition Plan View
 Little Alamance Creek (Burlington Park) Stream Restoration
 Alamance County
 NCEP Project Number: 92372

 EEE Consulting, Inc.
Cary, NC
Monitoring Year 1 of 5
June 2013



Property Information:
 Owner: City of Burlington
 Alamance County Parcel ID# 8864790671
 Alamance County Tax Map # 104-442-217

Deed References: Deed Book 98 Page 220
 Deed Book 136 Page 46

Reference Boundary Survey Plat prepared by
 City of Burlington Engineering Department
 Entitled Final Plat Property of, City of Burlington
 City Park Map #1, Dated September 14, 1995

Conservation Easement Notes:
 Total Area in Conservation Easement: 6.98 Acres ±
 0.25 Acres± in Temporary Construction Easement

All corners of the Conservation Easement are marked
 with Rebar and Aluminum NCEEP Caps, unless noted.

LEGEND
 Existing Iron Pipe
 New Iron Pipe
 Man Hole
 Monument
 Power Pole
 Utility Line


LINE TABLE

Line #	Bearing	Distance
Tie L-1	S 39°26'01" W	60.99'

GPS CO-ORDINATES
 PROVIDED BY ARCADIS
 N 84926.62
 E 1864965.29

CURVE TABLE

Curve #	Bearing	Chord	Radius	Arc
C-1	N 82°35'42" W	28.28'	100.00'	28.38'
C-2	N 69°24'31" W	17.65'	100.00'	17.65'
C-3	N 46°32'36" W	61.15'	100.00'	62.15'

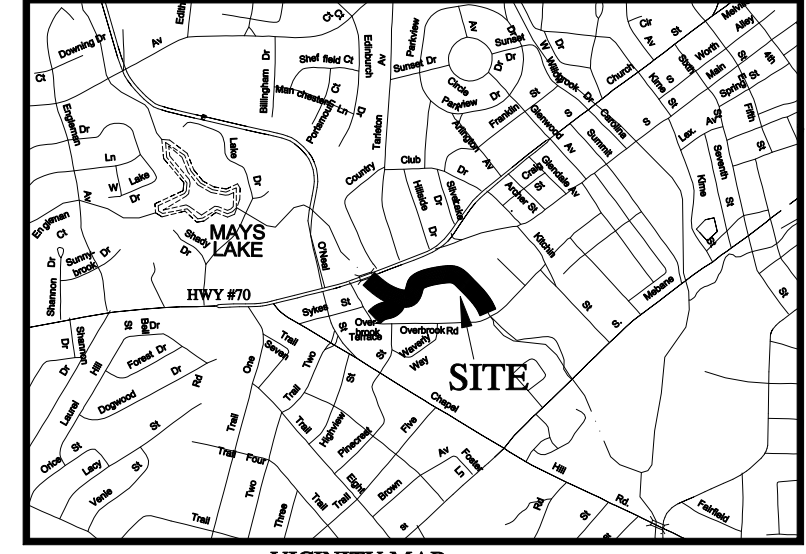

LINE TABLE

Line #	Bearing	Distance
L-1	N 70°36'20" E	36.93'
L-2	N 69°20'21" E	46.63'
L-3	N 59°47'13" E	57.06'
L-4	S 43°59'57" E	41.68'
L-5	S 60°52'02" E	40.00'
L-6	S 66°12'35" W	56.03'
L-7	S 37°12'39" W	64.04'
L-8	S 67°18'44" W	43.27'
L-9	N 51°42'28" W	51.48'
L-10	N 49°25'20" W	63.45'
L-11	N 04°58'22" W	38.00'
L-12	N 29°35'00" E	54.44'
L-13	S 32°05'35" E	46.29'
L-14	N 00°16'40" E	42.66'
L-15	N 50°23'34" E	27.84'
L-16	N 69°21'29" E	58.74'
L-17	S 71°40'25" E	7.97'
L-18	N 66°26'32" E	8.90'
L-19	N 63°50'04" E	20.72'
L-20	S 71°13'11" E	27.32'
L-21	S 56°14'03" E	12.12'
L-22	N 88°59'18" E	41.52'
L-23	S 83°12'35" E	86.33'
L-24	N 81°39'06" E	66.07'
L-25	S 63°06'28" E	67.20'
L-26	S 00°33'50" W	42.52'
L-27	S 34°22'35" W	46.94'
L-28	S 82°55'27" W	40.80'
L-29	N 44°24'47" E	49.65'
L-30	S 84°59'13" W	62.40'
L-31	S 54°17'14" E	48.24'
L-32	N 81°18'07" W	50.71'
L-33	S 39°38'58" W	41.12'
L-34	N 04°26'24" W	28.11'

Certificate of Accuracy

State of North Carolina, County of Alamance
 I, Douglas R. Yarbrough, certify that under my direction and supervision this map was drawn from an actual field land survey made by me; that the error of closure as calculated by latitudes and departures is: 1:10,000 for the perimeter and 1:10,000 for plotting of interior lot lines; that the boundaries not surveyed are shown as broken lines plotted from deed information found in deed book 136, page 46; that this map was prepared in accordance with G.S. 47-30 as amended; that the survey was requested by the owner or his duly authorized agent; that all required monuments and markers have been installed; that all new lines calculated from data not obtained in the field are indicated by a "C"; and that this plat is within the Jurisdiction of the City of Burlington.

Witness my hand and seal this 5th day of May, 2008.

Douglas R. Yarbrough, Professional Land Surveyor L-3395

- I, Douglas R. Yarbrough, Professional Land Surveyor, L-3395, Certify To one of the following:
- A. This survey creates a subdivision of land within the area of a county or municipality that has an ordinance that regulates parcels of land.
 - B. This survey is located in such portion of a county or municipality that is designated as to an ordinance that regulates parcels of land.
 - C. Any one of the following:
 1. That the survey is of an existing parcel or parcels of land and does not create a new street or change an existing street;
 2. That the survey is of an existing building or other structure, or natural feature, such as a watercourse; or
 3. The survey is a control survey.
 - D. This survey is of another category, such as the recombination of existing parcels, a court-ordered survey, or other exception to the definition of subdivision.
 - E. The information available to the surveyor is such that the surveyor is unable to make a determination to the best of his or her professional ability as to provisions contained in 1 - 4 above.

Douglas R. Yarbrough, Professional Land Surveyor, L-3395

Certificate of Ownership and Dedication

I, (we) hereby certify that I (we) am (are) the owner(s) of the property, shown and described hereon, which was conveyed to me (us) by deed as recorded in deed book 136, page 46, and that (we) hereby acknowledge this plat and allotment to be my(our) free act and deed and do hereby dedicate to public use as streets, rights-of-way, and easements forever, all areas so shown or indicated on said plat.

OWNER	Date
OWNER	Date
OWNER	Date

County of Alamance, State of North Carolina
 I, a notary public of the county and state aforesaid, certify that

personally appeared before me this day and acknowledged the execution of the foregoing instrument.
 Witness my hand and official stamp or seal, this _____ day of _____, 20____.

Notary Public
 My commission expires _____

Planning Director Certification

NO APPROVAL REQUIRED UNDER SECTION 33-1 OF THE CODE OF ORDINANCES OF THE CITY OF BURLINGTON.

PLANNING DIRECTOR

City of Burlington Certification

Recommended by the Burlington Planning and Zoning Commission on the _____ day of _____, 20____.

Chairman of Planning and Zoning Commission

Approved by the Burlington City Council on the _____ day of _____, 20____ provided that the plat be recorded within sixty (60) days of final approval.
 City Clerk

_____ date.

Review Officer Certification

State of North Carolina, County of Alamance
 I, _____ Review Officer of Alamance County, certify that the map or plat to which this certification is affixed meets all statutory requirements for recording.

Review Officer _____ Date _____


Final Plat
 Conservation Easement for
 the State of North Carolina,
 Ecosystem Enhancement Program,
 Little Alamance Creek at Burlington Park
 SPO#001-AAAG EEP#92372

BURLINGTON TOWNSHIP ALAMANCE COUNTY NORTH CAROLINA

DATE: 05/01/2008 SCALE 1" = 100'

LANDMARK SURVEYING, INC. - 109 EAST HARDEN STREET - GRAHAM, NC 27253
 PHONE: (336) 229-6275 - FACSIMILE: (336) 227-5919 - EMAIL: dylanmark@triad.rr.com
 Job Number: 08-04-01 - Drawing Name: Y080401 NCEEP Little Alamance Creek
 Field Crew: DWM & RMW - Drawn By: DRY - Checked By: _____

Revisions: 05/20/08 Revisions to Conservation Easement Boundaries, after 05/08/2008 walk-through with C.O.B. Representatives & NCEEP Staff.
 06/20/08 Revisions to Conservation Easement Boundaries, after 06/05/2008 2nd walk-through with C.O.B. Representatives & NCEEP Staff.
 07/15/08 Revisions to Conservation Easement Boundary Area "B" as per meeting with C.O.B. Representatives and NCEEP Staff.




Property Information:
 Owner: City of Burlington
 Alamance County Parcel ID# 8864790671
 Alamance County Tax Map # 104-442-217

Deed References: Deed Book 98 Page 220
 Deed Book 136 Page 46
 Reference Boundary Survey Plat prepared by
 City of Burlington Engineering Department
 Entitled Final Plat Property of, City of Burlington
 City Park Map #1, Dated September 14, 1995

Conservation Easement Notes:
 Total Area in Conservation Easement: 6.98 Acres ±
 0.25 Acres ± in Temporary Construction Easement


All corners of the Conservation Easement are marked
 with Rebar and Aluminum NCEEP Caps, unless noted.

LEGEND
 Existing Iron Pipe
 New Iron Pipe
 Man Hole
 Monument
 Power Pole
 Utility Line



Line #	Bearing	Distance
Tie L-1	S 39°26'01" W	60.99'

GPS CO-ORDINATES
 PROVIDED BY RCADIS
 N 84926.62
 E 1864965.29

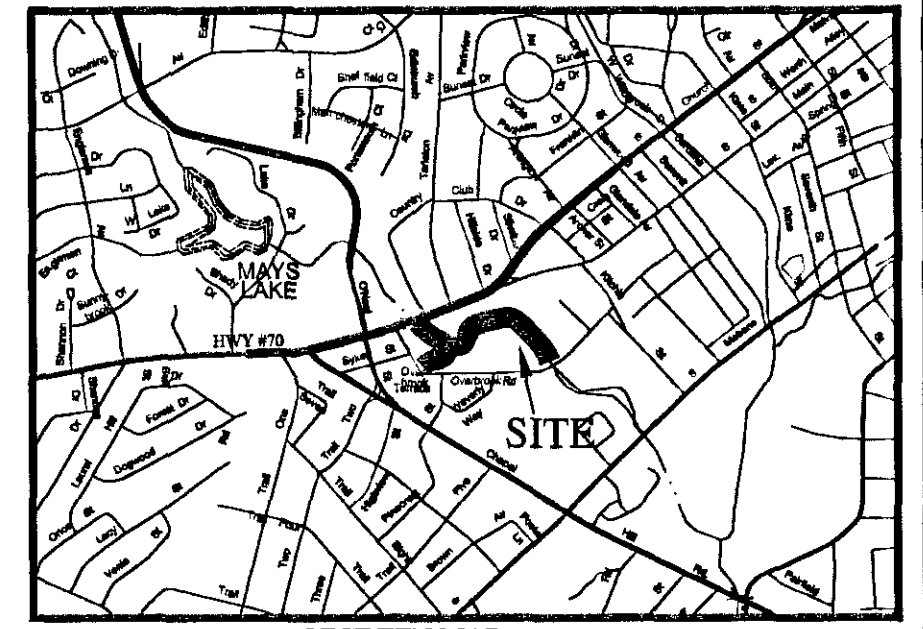

Line #	Bearing	Distance
L-1	N 70°36'20" E	36.93'
L-2	N 69°20'21" E	46.63'
L-3	N 59°47'13" E	57.06'
L-4	S 43°59'51" E	41.68'
L-5	S 60°52'02" E	40.00'
L-6	S 66°12'35" W	56.03'
L-7	S 37°12'39" W	64.04'
L-8	S 67°18'44" E	43.27'
L-9	N 51°42'28" W	51.48'
L-10	N 49°25'20" W	63.45'
L-11	N 04°58'22" E	38.00'
L-12	N 29°35'00" E	54.44'
L-13	S 32°05'35" E	46.29'
L-14	N 00°16'40" E	42.66'
L-15	N 50°22'34" E	27.84'
L-16	N 69°21'29" E	58.74'
L-17	N 71°40'25" E	7.97'
L-18	N 66°26'32" E	8.90'
L-19	N 63°50'04" E	20.72'
L-20	N 71°13'11" E	27.32'
L-21	S 56°14'03" E	12.12'
L-22	N 88°59'18" E	41.52'
L-23	S 83°12'35" E	86.33'
L-24	N 81°39'06" E	66.07'
L-25	S 63°06'28" E	67.20'
L-26	S 00°33'50" W	42.52'
L-27	S 34°22'35" W	46.94'
L-28	S 82°55'27" W	40.80'
L-29	N 44°24'47" E	49.65'
L-30	S 84°59'13" W	62.40'
L-31	S 54°17'14" E	48.24'
L-32	N 81°18'07" W	50.71'
L-33	S 39°38'58" W	41.12'
L-34	N 04°26'24" W	28.11'

Curve #	Bearing	Chord	Radius	Arc
C-1	N 82°35'42" W	28.28'	100.00'	28.38'
C-2	N 69°24'31" W	17.63'	100.00'	17.65'
C-3	N 46°32'56" W	61.15'	100.00'	62.15'

Certificate of Accuracy

I, Douglas R. Yarbrough, certify that under my direction and supervision this map was drawn from an actual field land survey made by me; that the error of closure as calculated by latitudes and departures is: 1:10,000 for the perimeter and 1:10,000 for plotting of interior lot lines; that the boundary not surveyed and not shown as broken lines plotted from deed information found in deed book L-3395, page 25-1; that this map was prepared in accordance with GS 47-30 as amended; that the survey was requested by the owner or his duly authorized agent; that all required monuments and markers have been installed; that all new lines calculated from data not obtained in the field are indicated by a "C"; and that this plat is within the jurisdiction of the City of Burlington.

Witness my hand and seal this 5th day of May, 2008.

Douglas R. Yarbrough
 Douglas R. Yarbrough, Professional Land Surveyor, L-3395



Certificate of Ownership and Dedication

I, (we) hereby certify that I (we) am (are) the owner(s) of the property, shown and described hereon, which was conveyed to me (us) by deed as recorded in deed book 136, page 46, and that I (we) hereby acknowledge this plat and allotment to be my(our) free act and deed and do hereby dedicate to public use as streets, rights-of-way, and easements forever, all areas so shown or indicated on said plat.

Ronnie K. Wall 2-5-09
 OWNER Date

OWNER Date

OWNER Date

County of Alamance, State of North Carolina
 I, a notary public of the county and state aforesaid, certify that

Ronnie K. Wall

personally appeared before me this day and acknowledged the execution of the foregoing instrument.

Witness my hand and official stamp or seal, this 5 day of Feb. 2008

Douglas D. Terry
 Notary Public

My commission expires 11-20-2011

Planning Director Certification

NO APPROVAL REQUIRED UNDER SECTION 33-1 OF THE CODE OF ORDINANCES OF THE CITY OF BURLINGTON.

[Signature] 2-6-09
 PLANNING DIRECTOR

City of Burlington Certification

Recommended by the Burlington Planning and Zoning Commission on the _____ day of _____, 20____.

Chairman of Planning and Zoning Commission

Approved by the Burlington City Council on the _____ day of _____, 20____, provided that the plat be recorded within sixty (60) days of final approval.

City Clerk

Review Officer Certification

State of North Carolina, County of Alamance

J. David Shaffer, Review Officer of Alamance County, certify that the map or plat to which this certification is affixed meets all statutory requirements for recording.

2/6/09
 Review Officer Date

I, Douglas R. Yarbrough, Professional Land Surveyor, L-3395, certify to one of the following:

A. This survey creates a subdivision of land within the area of a county or municipality that has an ordinance that regulates parcels of land.

B. This survey is located in such portion of a county or municipality that is recognized as an ordinance that regulates parcels of land.


C. Any one of the following:

1. That the survey is of an existing parcel or parcels of land and does not create a new street or change an existing street.
2. That the survey is of an existing building or other structure, or natural feature such as a watercourse; or
3. That the survey is a control survey.

D. This survey is of another category, such as the recombination of existing parcels, a court-ordered survey, or other exception to the definition of subdivision.

E. The information available to the surveyor is such that the surveyor is unable to make a determination to the best of his or her professional ability as to whether the survey is in 1 - 4 above.

Douglas R. Yarbrough
 Douglas R. Yarbrough, Professional Land Surveyor, L-3395



Final Plat
Conservation Easement for
the State of North Carolina,
Ecosystem Enhancement Program,
Little Alamance Creek at Burlington Park
SPO#001-AAAG EEP#92372

BURLINGTON TOWNSHIP ALAMANCE COUNTY NORTH CAROLINA

DATE: 05/01/2008 SCALE 1" = 100'

LANDMARK SURVEYING, INC. - 109 EAST HARDEN STREET - GRAHAM, NC 27253
 PHONE: (336) 229-6275 - FACSIMILE: (336) 227-5919 - EMAIL: dylanmark@triad.rr.com
 Job Number: 08-04-01 - Drawing Name: Y080401 NCEEP Little Alamance Creek
 Field Crew: DWM & RMW - Drawn By: DRY - Checked By:

Revisions: 05/20/08 Revisions to Conservation Easement Boundaries, after 05/08/02008 walk-through with C.O.B. Representatives & NCEEP Staff.
 06/20/08 Revisions to Conservation Easement Boundaries, after 06/05/02008 - 2nd walk-through with C.O.B. Representatives & NCEEP Staff.
 07/15/08 Revisions to Conservation Easement Boundary Area "B" as per meeting with C.O.B. Representatives and NCEEP Staff.

Doc ID: 009915410001 Type: CRP
 Recorded: 02/09/2008 at 02:24:46 PM
 Fee Amt: \$21.00 Page 1 of 1
 Alamance, NC
 DAVID J.P. BARBER REGISTER OF DEEDS
 BK 73 PG 122

138082

Figure 5: Conservation Easement Coordinate List

AREA "A"

NORTH	EAST	Point #
849579.51554	1864926.55171	395
849591.77729	1864961.38155	298
849608.22978	1865005.01204	299
849636.94197	1865054.31867	294
849589.39149	1865164.49481	129
849486.98274	1865107.29342	130
849513.45974	1865001.41137	131
849579.51554	1864926.55171	395

AREA "B"

NORTH	EAST	Point #
849559.40556	1865193.45108	134
849557.84265	1865237.72626	35
849479.25598	1865422.79011	136
849353.03468	1865393.66448	137
849291.86683	1865358.17065	105
849225.45240	1865275.15897	106
849221.25010	1865257.53874	140
849198.64891	1865206.27156	384
849147.64645	1865167.54338	107
849081.54893	1865093.68513	292
849087.74837	1865077.18420	293
849176.03999	1865035.54448	144
849199.39922	1865024.52791	385
849235.42971	1865096.89567	148
849299.41895	1865225.41897	149
849408.35898	1865232.57548	301
849467.50926	1865142.23314	151
849559.40556	1865193.45108	134

AREA "C"

NORTH	EAST	Point #
849462.56616	1865462.71229	152
849435.13638	1865526.69686	153
849482.39703	1865579.69130	155
849462.88378	1865657.23514	156
849442.70621	1865703.37024	157
849329.27516	1865707.26253	158
849260.03559	1865644.92151	159
849240.35724	1865576.32112	160
849321.13162	1865434.07191	396
849339.57571	1865437.80714	161
849462.56616	1865462.71229	152

AREA "D"

NORTH	EAST	Point #
849523.67028	1865531.49915	162
849606.54503	1865505.41990	300
849687.60418	1865479.86867	163
849646.26097	1865642.17633	164
849599.23801	1865668.60583	165
849480.56349	1865700.07636	166
849523.67028	1865531.49915	162

AREA "E"

NORTH	EAST	Point #
849734.94933	1865506.74625	386
849777.61339	1865506.95303	168
849795.36536	1865528.39325	169
849816.07420	1865583.36623	411
849813.56859	1865590.93079	172
849817.12503	1865599.08756	173
849826.26238	1865617.68539	174
849817.46632	1865643.55279	175
849810.73250	1865653.62464	176
849811.46562	1865695.14176	108
849801.25856	1865780.86612	410
849810.85135	1865846.23666	409
849780.45763	1865906.16581	180
849737.93964	1865905.74732	181
849699.19996	1865879.24506	182
849694.17460	1865838.75955	183
849689.79904	1865727.49867	312
849685.47681	1865617.58282	184
849734.94933	1865506.74625	386

AREA "F"

NORTH	EAST	Point #
849815.92160	1865940.90924	110
849824.39775	1865999.70351	109
849710.30838	1866007.56636	187
849704.65272	1865941.40823	388
849815.92160	1865940.90924	110

AREA "G"

NORTH	EAST	Point #
849811.20595	1866037.84131	189
849795.76690	1866075.73608	338
849767.10290	1866116.74370	191
849696.12266	1866262.27953	390
849631.25699	1866395.27823	391
849625.14242	1866407.81537	79 MH
849617.01962	1866417.32501	392
849561.30036	1866482.55746	393
849497.45831	1866557.29954	195
849490.28422	1866410.67696	196
849556.17669	1866325.00704	197
849591.11839	1866204.02424	404
849632.65737	1866156.80372	346
849702.64017	1866057.68956	199
849811.20595	1866037.84131	189

AREA "H"

NORTH	EAST	Point #
849465.79522	1866531.05945	200
849450.23363	1866542.12494	201
849390.76406	1866563.46603	202
849352.71701	1866583.54506	401
849315.71724	1866580.20684	203
849204.47066	1866564.90566	402
849156.80929	1866462.67261	403
849229.09022	1866442.93365	375
849332.80632	1866481.41733	399
849405.63461	1866455.34439	400
849462.25590	1866412.85336	210
849465.79522	1866531.05945	200

Table 5
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Mainstem
 2275 lf

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	6	6			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	4	4			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	4	4			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	4	4			100%			
		2. Thalweg centering at downstream of meander (Glide)	4	4			100%			
Totals					0	0	100%	0	0	100%
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%	0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	6	6			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	0	0			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	6	6			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	0	0			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	4	4			100%			

Table 5
 Reach ID
 Assessed Length

Visual Stream Morphology Stability Assessment
 Unnamed Tributary
 450 lf

Major Channel Category	Channel Sub-Category	Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended	Number with Stabilizing Woody Vegetation	Footage with Stabilizing Woody Vegetation	Adjusted % for Stabilizing Woody Vegetation
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%			
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%			
	2. Riffle Condition	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate	2	2			100%			
	3. Meander Pool Condition	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)	2	2			100%			
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)	2	2			100%			
	4. Thalweg Position	1. Thalweg centering at upstream of meander bend (Run)	2	2			100%			
		2. Thalweg centering at downstream of meander (Glide)	2	2			100%			
Totals					1	75	99%	0	0	99%
2. Bank	1. Scoured/Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			1	75	99%	0	0	99%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does NOT include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%	0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%	0	0	100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	2	2			100%			
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	1	1			100%			
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	2	2			100%			
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	1	1			100%			
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	2	2			100%			

Table 6

Vegetation Condition Assessment

Planted Acreage¹

7.06 ac

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	0.1 acres	N/A	0	0.00	0.0%
2. Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1 acres	N/A	0	0.00	0.0%
				Total	0	0.00
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 acres	N/A	0	0.00	0.0%
				Cumulative Total	0	0.00

Easement Acreage²

7.06 ac

Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Easement Acreage
4. Invasive Areas of Concern ⁴	Areas or points (if too small to render as polygons at map scale).	1000 SF	Yellow Point	3 points	0.35	5.0%
5. Easement Encroachment Areas ³	Areas or points (if too small to render as polygons at map scale).	none	N/A	0	0.00	0.0%

¹ = Enter the planted acreage within the easement. This number is calculated as the easement acreage minus any existing mature tree stands that were not subject to supplemental planting of the understory, the channel acreage, crossings or any other elements not directly planted as part of the project effort.

² = The acreage within the easement boundaries.

³ = Encroachment may occur within or outside of planted areas and will therefore be calculated against the overall easement acreage. In the event a polygon is cataloged into items 1, 2 or 3 in the table and is the result of encroachment, the associated acreage should be tallied in the relevant item (i.e., item 1, 2 or 3) as well as a parallel tally in item 5.

⁴ = Invasives may occur in or out of planted areas, but still within the easement and will therefore be calculated against the overall easement acreage. Invasives of concern/interest are listed below. The list of high concern species are those with the potential to directly outcompete native, young, woody stems in the short-term (e.g. monitoring period or shortly thereafter) or affect the community structure for existing, more established tree/shrub stands over timeframes that are slightly longer (e.g., 1-2 decades). The low/moderate concern group are those species that generally do not have this capacity over the timeframes discussed and therefore are not expected to be mapped with regularity, but can be mapped, if in the judgement of the observer their coverage, density or distribution is suppressing the viability, density, or growth of planted woody stems. Decisions as to whether remediation will be needed are based on the integration of risk factors by EEP such as species present, their coverage, distribution relative to native biomass, and the practicality of treatment. For example, even modest amounts of Kudzu or Japanese Knotweed early in the project's history will warrant control, but potentially large coverages of Microstegium in the herb layer will not likely trigger control because of the limited capacities to impact tree/shrub layers within the timeframes discussed and the potential impacts of treating extensive amounts of ground cover. Those species with the watch list designator in gray shade are of interest as well, but have yet to be observed across the state with any frequency. Those in *red italics* are of particular interest given their extreme risk/threat level for mapping as points where isolated specimens are found, particularly early in a project's monitoring history. However, areas of discrete, dense patches will of course be mapped as polygons. The symbology scheme below was one that was found to be helpful for symbolizing invasives polygons, particularly for situations where the condition for an area is somewhere between isolated specimens and dense, discrete patches. In any case, the point or polygon/area feature can be symbolized to describe things like high or low concern and species can be listed as a map inset, in legend items if the number of species are limited or in the narrative section of the executive summary.

Photo Log 1: Established Photo Stations



Photo Station 1, rail line at bollard 172, facing east
April 3, 2013



Photo Station 2, level spreader at bollard 410,
facing east; April 3, 2013



Photo Station 3, rail line discharge, facing south
April 3, 2013



Photo Station 4, discharge at bollard 312,
facing west; April 3, 2013



Photo Station 5, view of easement facing northwest
April 3, 2013



Photo Station 6, VP 7 at bollard 401,
facing west; April 3, 2013



Photo Station 7, XS 1, facing right bank
March 27, 2013



Photo Station 8, XS 2, facing right bank
March 27, 2013



Photo Station 9, XS 3, facing right bank
March 27, 2013



Photo Station 10, XS 4, facing right bank
April 3, 2013



Photo Station 11, XS 5, facing right bank
March 27, 2013



Photo Station 12, XS 6, facing right bank
April 3, 2013



Photo Station 13, XS 7, facing right bank
April 3, 2013



Photo Station 14, XS 8, facing right bank
April 3, 2013



Photo Station 15, XS 9, facing right bank
April 3, 2013



Photo Station 16, XS 10, facing right bank
April 3, 2013



Photo Station 17, XS 11, facing right bank
April 3, 2013



Photo Station 18, XS 12, facing right bank
April 3, 2013



Photo Station 19, XS 13, facing right bank
April 3, 2013



Photo Station 20, XS 14, facing right bank
April 3, 2013

Photo Log 2: Vegetation Monitoring Plot Photos



Veg Plot 1, view from southwest corner
March 27, 2013



Veg Plot 2, view from southwest corner
March 27, 2013



Veg Plot 3, view from southwest corner
March 27, 2013



Veg Plot 4, view from southwest corner
March 27, 2013



Veg Plot 5, view from southwest corner
March 27, 2013



Veg Plot 6, view from southwest corner
April 3, 2013



Veg Plot 7, view from southwest corner
April 3, 2013



Veg Plot 8, view from southwest corner
April 3, 2013

Appendix C: Vegetation Plot Data

Table 7: Vegetation Plot Success by Project Asset Type

Table 8: CVS Stem Count Total and Planted with/without Livestakes by
Plot and Species

Table 7: Little Alamance (#92372)

Year 1 (27-Mar-2013 to 03-Apr-2013)

Vegetation Plot Summary Information

Plot #	Riparian Buffer Stems ¹	Stream/ Wetland Stems ²	Live Stakes	Invasives	Volunteers ³	Total ⁴	Unknown Growth Form
1	n/a	9	0	0	13	22	12
2	n/a	10	0	25	38	23	0
3	n/a	8	0	1	24	31	0
4	n/a	9	0	0	0	10	1
5	n/a	9	0	0	1	10	0
6	n/a	15	0	0	12	27	1
7	n/a	3	1	0	0	4	0
8	n/a	5	0	0	2	7	0

Wetland/Stream Vegetation Totals

(per acre)

Plot #	Stream/ Wetland Stems ²	Volunteers ³	Total ⁴	Success Criteria Met?
1	364	526	890	Yes
2	405	1538	931	Yes
3	324	971	1255	Yes, barely
4	364	0	405	Yes
5	364	40	405	Yes
6	607	486	1093	Yes
7	121	0	162	No
8	202	81	283	No
Project Avg	344	455	678	Yes, barely

Riparian Buffer Vegetation Totals

(per acre)

Plot #	Riparian Buffer Stems ¹	Success Criteria Met?
1	n/a	
2	n/a	
3	n/a	
4	n/a	
5	n/a	
6	n/a	
7	n/a	
8	n/a	
Project Avg	n/a	

Stem Class characteristics

¹Buffer

Stems Native planted hardwood trees. Does NOT include shrubs. No pines. No vines.

²Stream/
Wetland

Stems

Native planted woody stems. Includes shrubs, does NOT include live stakes. No vines

³Volunteers Native woody stems. Not planted. No vines.

⁴Total

Planted + volunteer native woody stems. Includes live stakes. Excl. exotics. Excl. vines.

Table 8: EEP Project Code 92372. Project Name: Little Alamance

Scientific Name	Common Name	Species Type	Current Plot Data (MY1 2013)																								Annual Means												
			92372-01-0001			92372-01-0002			92372-01-0003			92372-01-0004			92372-01-0005			92372-01-0006			92372-01-0007			92372-01-0008			MY1 (2013)												
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T										
Acer negundo	boxelder	Tree																										1			1								
Acer rubrum	red maple	Tree																													2								
Baccharis halimifolia	eastern baccharis	Shrub																													1								
Betula nigra	river birch	Tree				2	2	2	1	1	1									2	2	2	1	1	1	1	1	1	1	1	7	7	7						
Carpinus caroliniana	American hornbeam	Tree	1	1	1	3	3	3	1	1	1	1	1	1						2	2	2									8	8	8						
Carya cordiformis	bitternut hickory	Tree																													2	2	2						
Carya ovata	shagbark hickory	Tree										1	1	1	1	1	1														2	2	2						
Celtis laevigata	sugarberry	Tree										6	6	6	4	4	4	3	3	3											13	13	15						
Cercis canadensis	eastern redbud	Tree																														5		5					
Cornus amomum	silky dogwood	Shrub	1	1	1	1	1	1							1	1	1											3	3	3	6	6	6						
Cornus florida	flowering dogwood	Tree		2	2	2	1	1	1																						3	3	3						
DONTKNOW: unsure record												1	1	1																	1	1	1						
Euonymus americanus																																	1		1				
Fraxinus americana	white ash	Tree																															1		1				
Fraxinus pennsylvanica	green ash	Tree	1	1	1	1	1	1																								2	2	2					
Ilex opaca	American holly	Tree		2	2	2																										2	2	2					
Ligustrum	privet	Exotic																																	1				
Ligustrum lucidum	glossy privet	Exotic																																	3				
Ligustrum sinense	Chinese privet	Exotic																																	22				
Liquidambar styraciflua	sweetgum	Tree															1																	6					
Morus rubra	red mulberry	Tree																																9					
Photinia	chokeberry																																		12				
Platanus occidentalis	American sycamore	Tree										2	2	2			1	1	1														3	3	3				
Prunus serotina	black cherry	Tree																																	2				
Quercus coccinea	scarlet oak	Tree																																	20				
Quercus pagoda	cherrybark oak	Tree	1	1	1				3	3	3				2	2	2	2	2	2	1	1	1											9	9	9			
Quercus velutina	black oak	Tree																																	1				
Salix nigra	black willow	Tree																																	1				
Sambucus canadensis	Common Elderberry	Shrub	1	1	1				1	1	1									1	1	1	1	1	1	1	1	1	1	1	1	1	1	5	5	5			
Viburnum dentatum	southern arrowwood	Shrub							2	2	2																								3	3	3		
Viburnum prunifolium	blackhaw	shrub																		3	3	3													3	3	3		
Stem count			9	9	22	10	10	48	8	8	32	10	10	10	9	9	10	15	15	27	3	4	4	5	5	7	69	70	160										
size (ares)			1			1			1			1			1			1			1			1			8												
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.02			0.20												
Species count			7	7	9	6	6	13	5	5	10	5	5	5	5	5	6	8	8	13	3	4	4	3	3	5	15	16	31										
Stems per ACRE			364.2	364.2	890.3	404.7	404.7	1942	323.7	323.7	1295	404.7	404.7	404.7	364.2	364.2	404.7	607	607	1093	121.4	161.9	161.9	202.3	202.3	283.3	349	354.1	809.4										

Appendix D: Stream Survey Data

Figure 6: Cross Sections with Annual Overlays

Figure 7: Longitudinal Profiles with Annual Overlays

Figure 8: Pebble Counts with Annual Overlays

Table 9: Stream Bank Erosion Pin Data Table


Table 10a: Baseline Stream Data Summary

Table 10b: Baseline Stream Data Summary (Substrate, Bed, Bank, and
Hydrologic Containment Parameter Distributions)


Table 11a: Monitoring – Cross Section Morphology Data Table

Table 11b: Monitoring – Stream Reach Morphology Data Table


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 1, XS 1
Riffle
Station 11+58.48

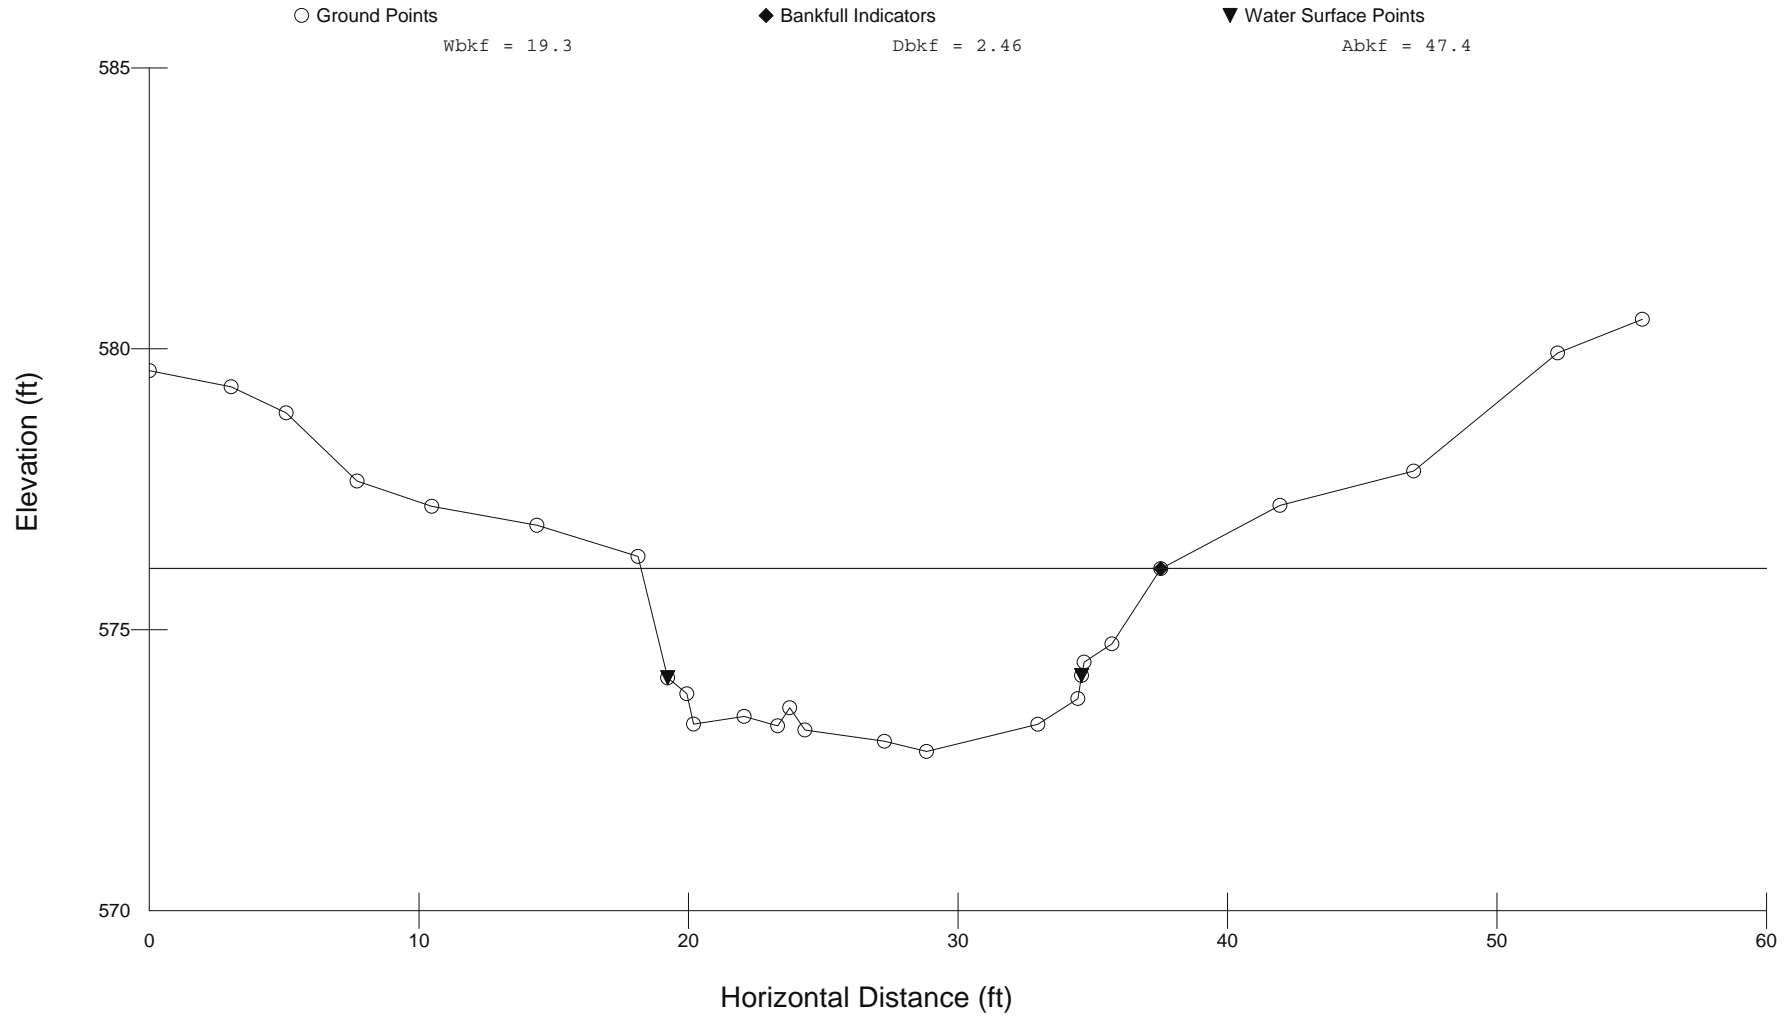


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 1, XS 2
Pool
Station 13+23.79

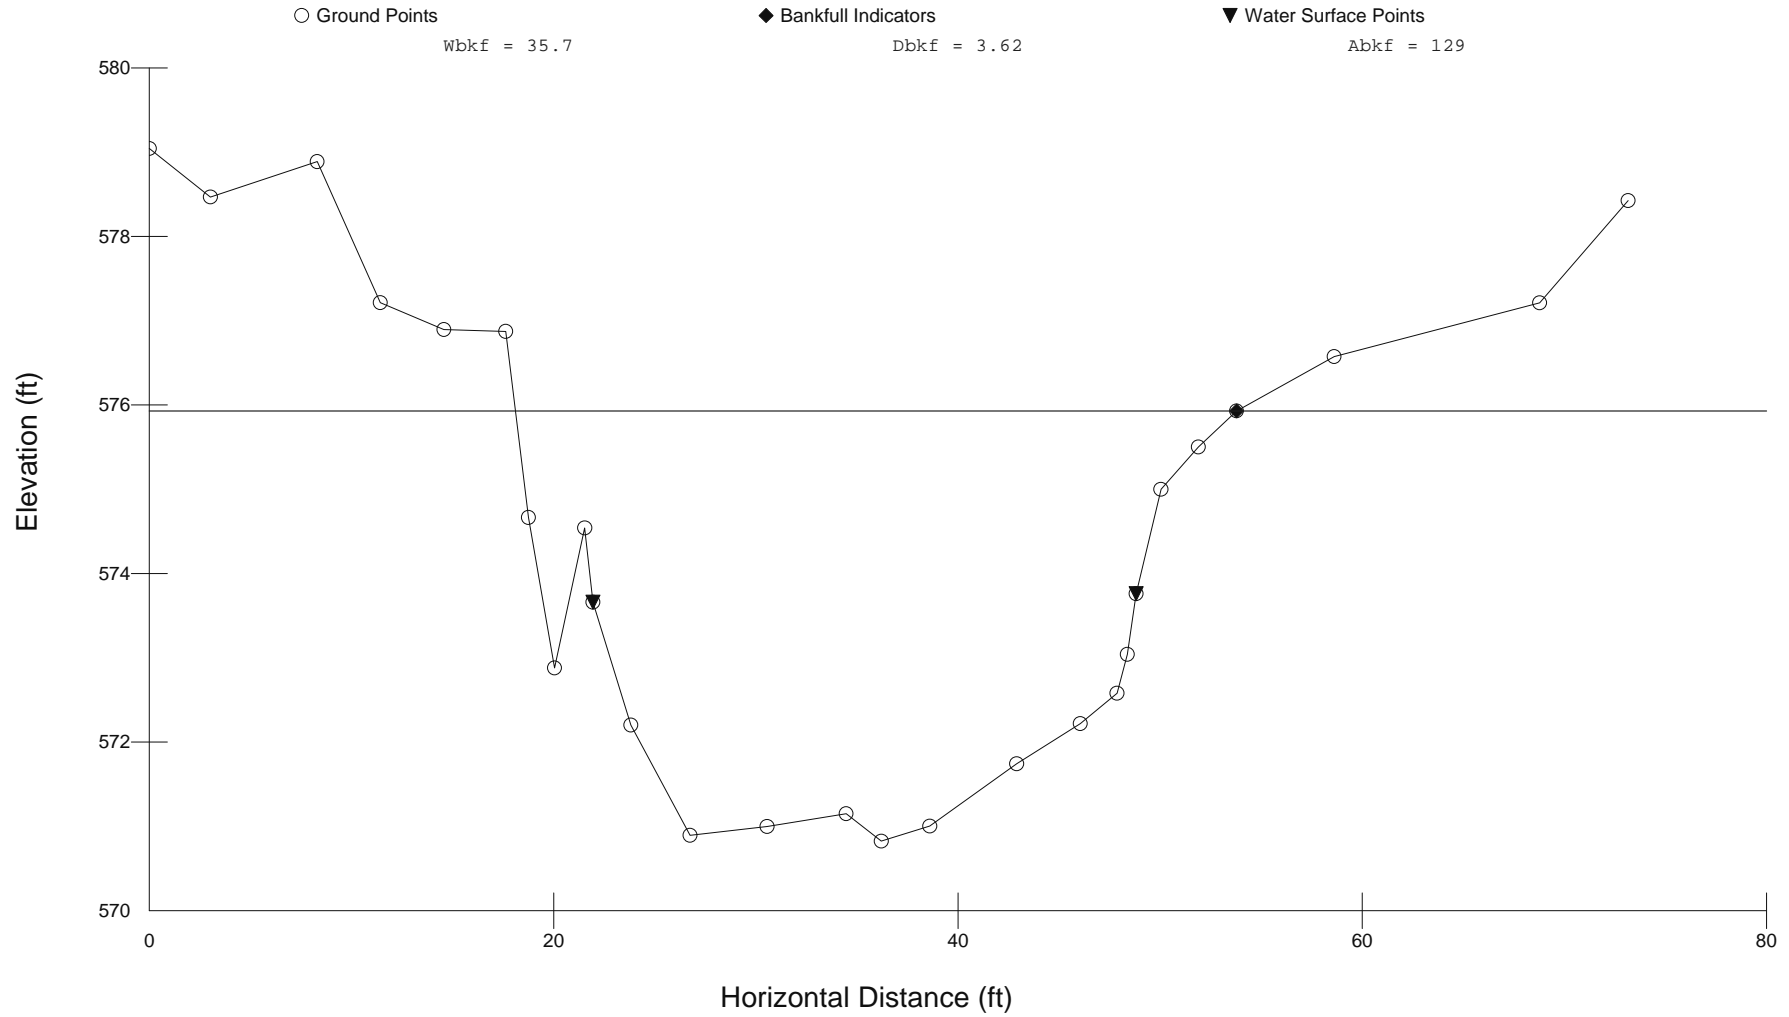


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 1, XS 3
Pool
Station 13+62.29

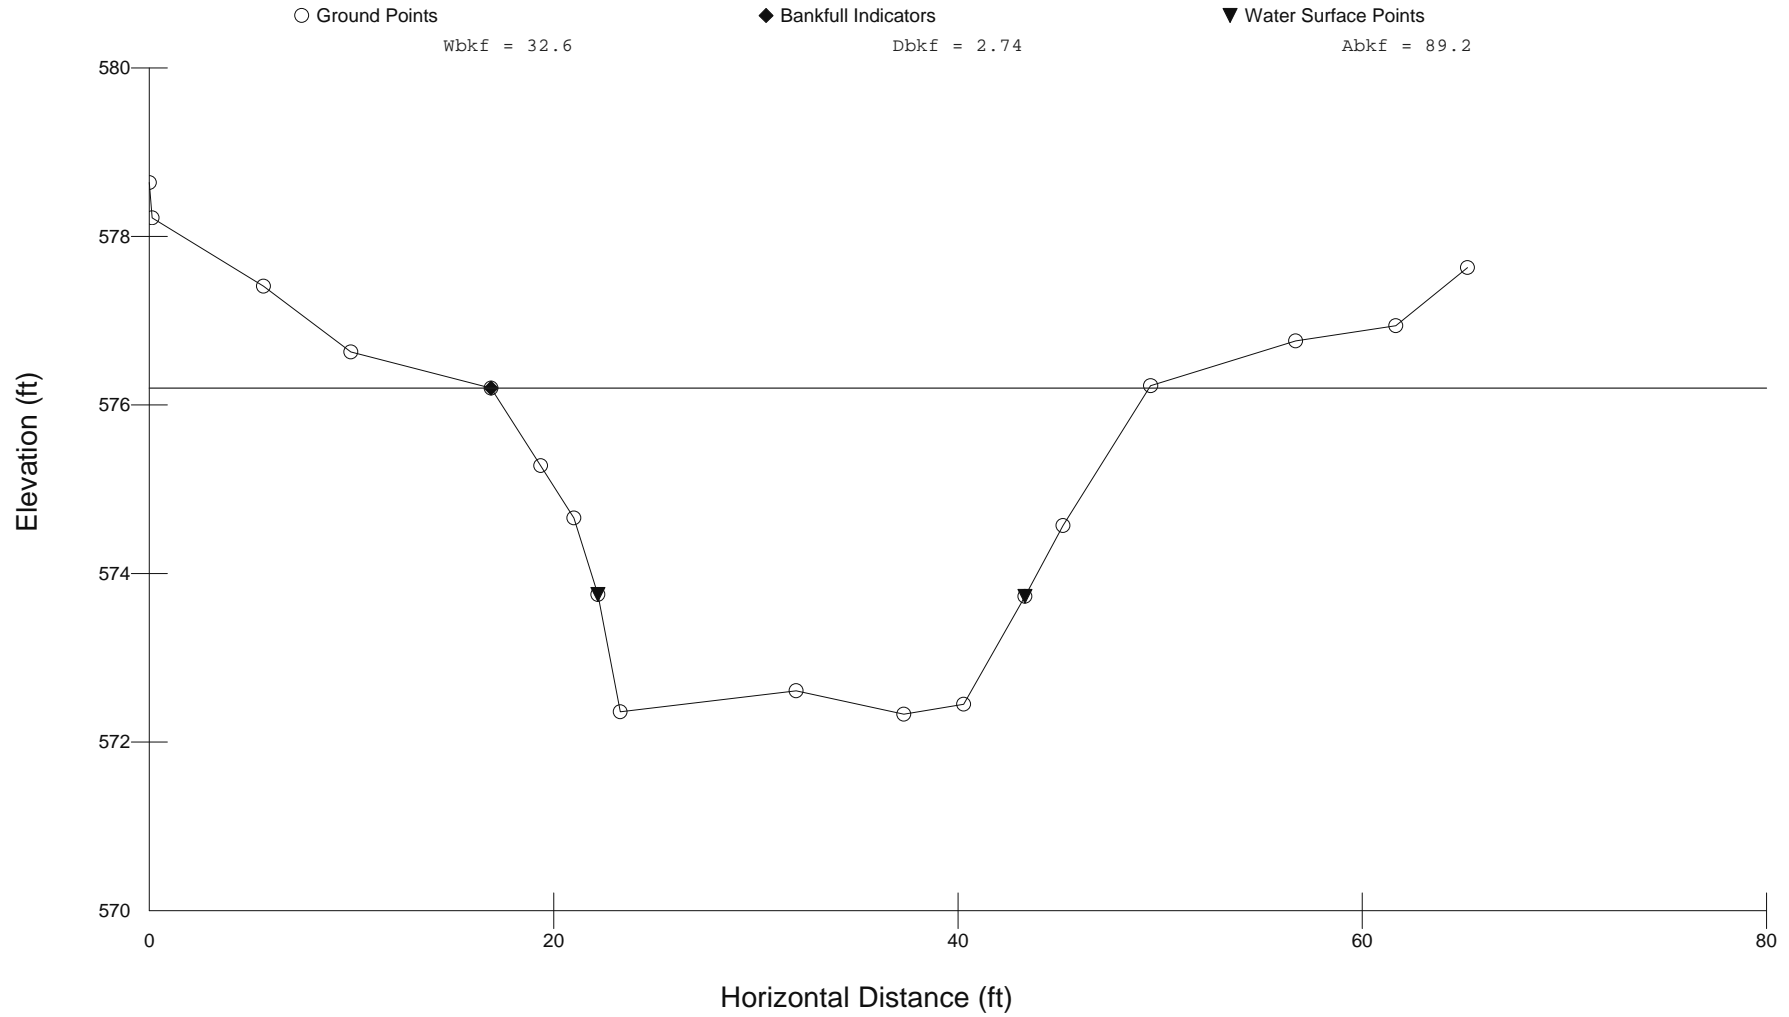


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 4, XS 4
Riffle
Station 19+69.54

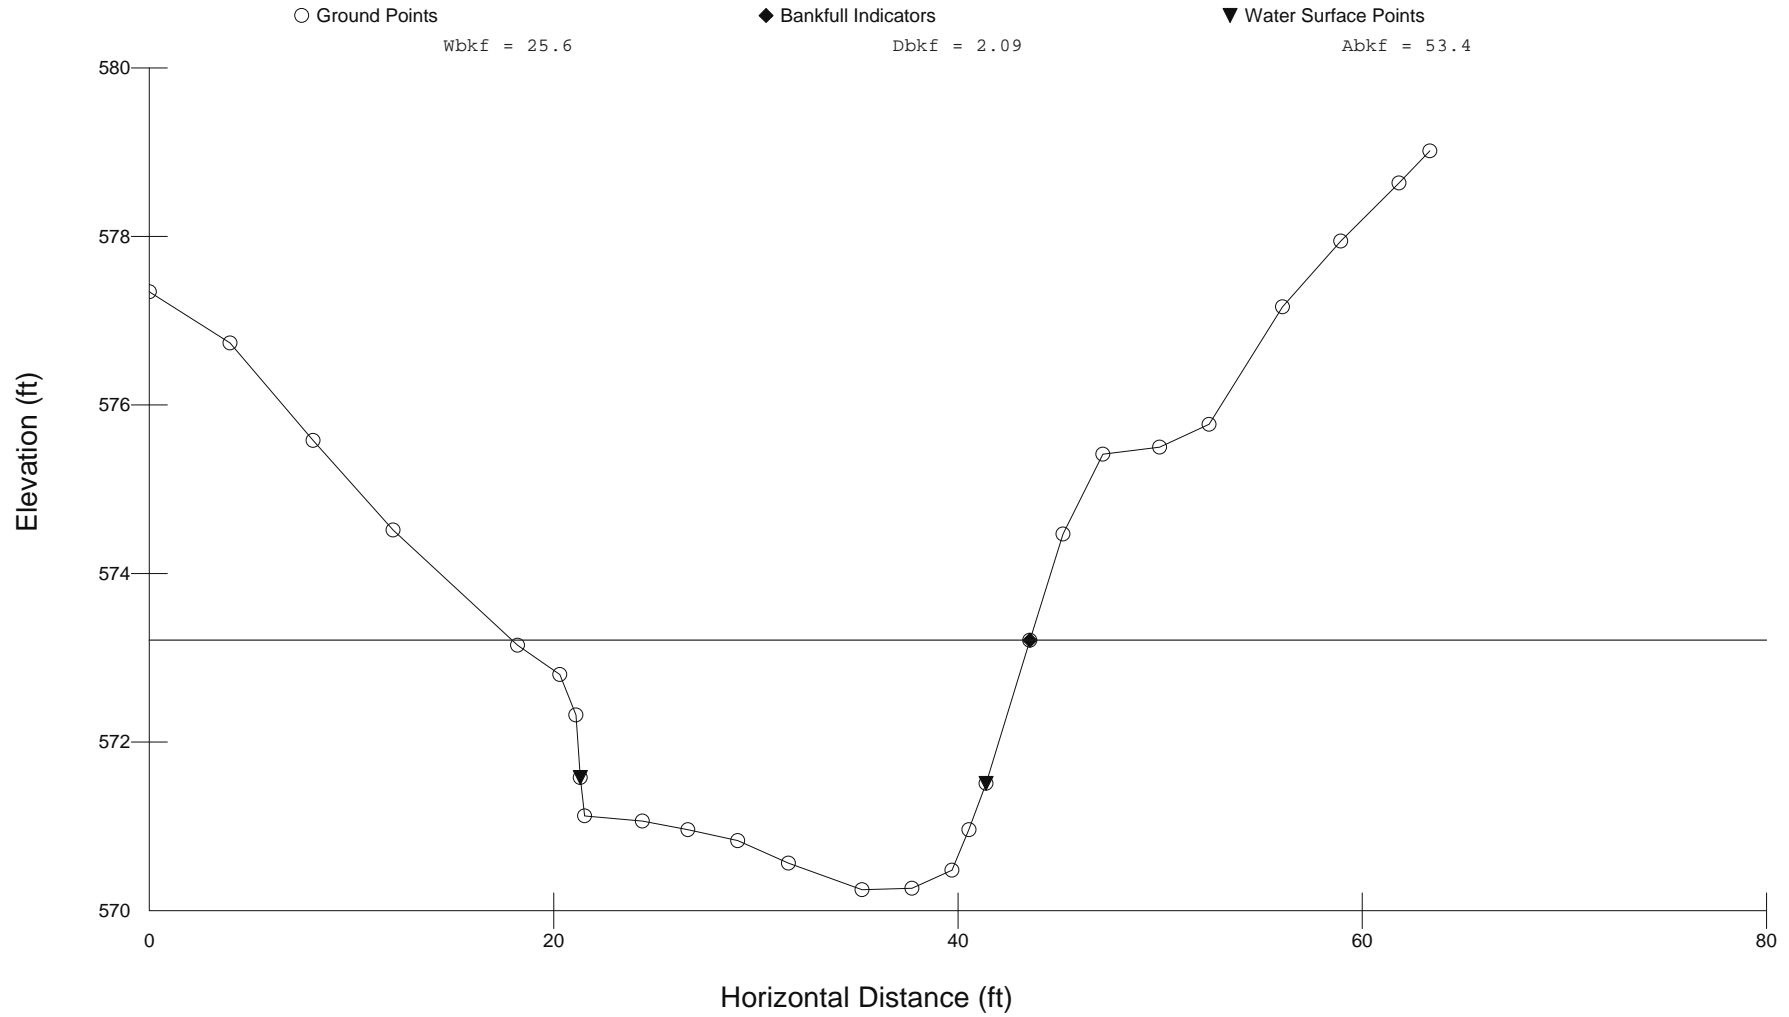


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 5
Riffle
Station 27+95.78

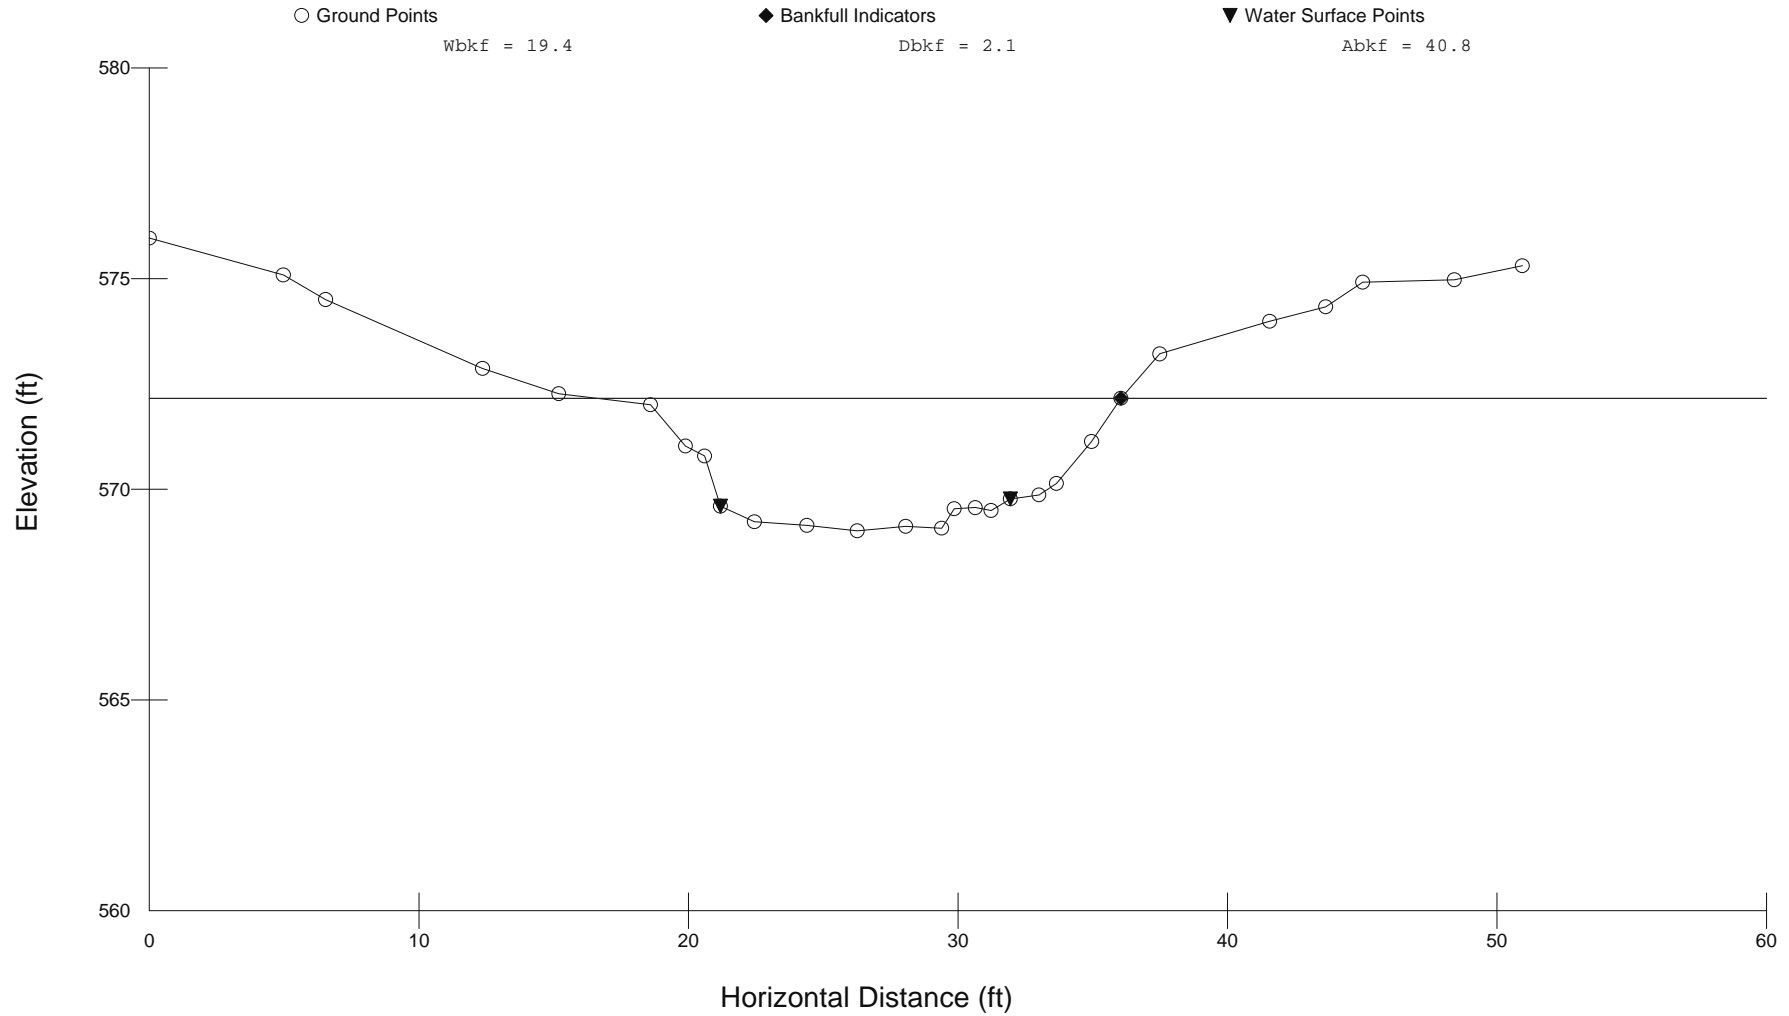


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 6
Pool
Station 28+83.61

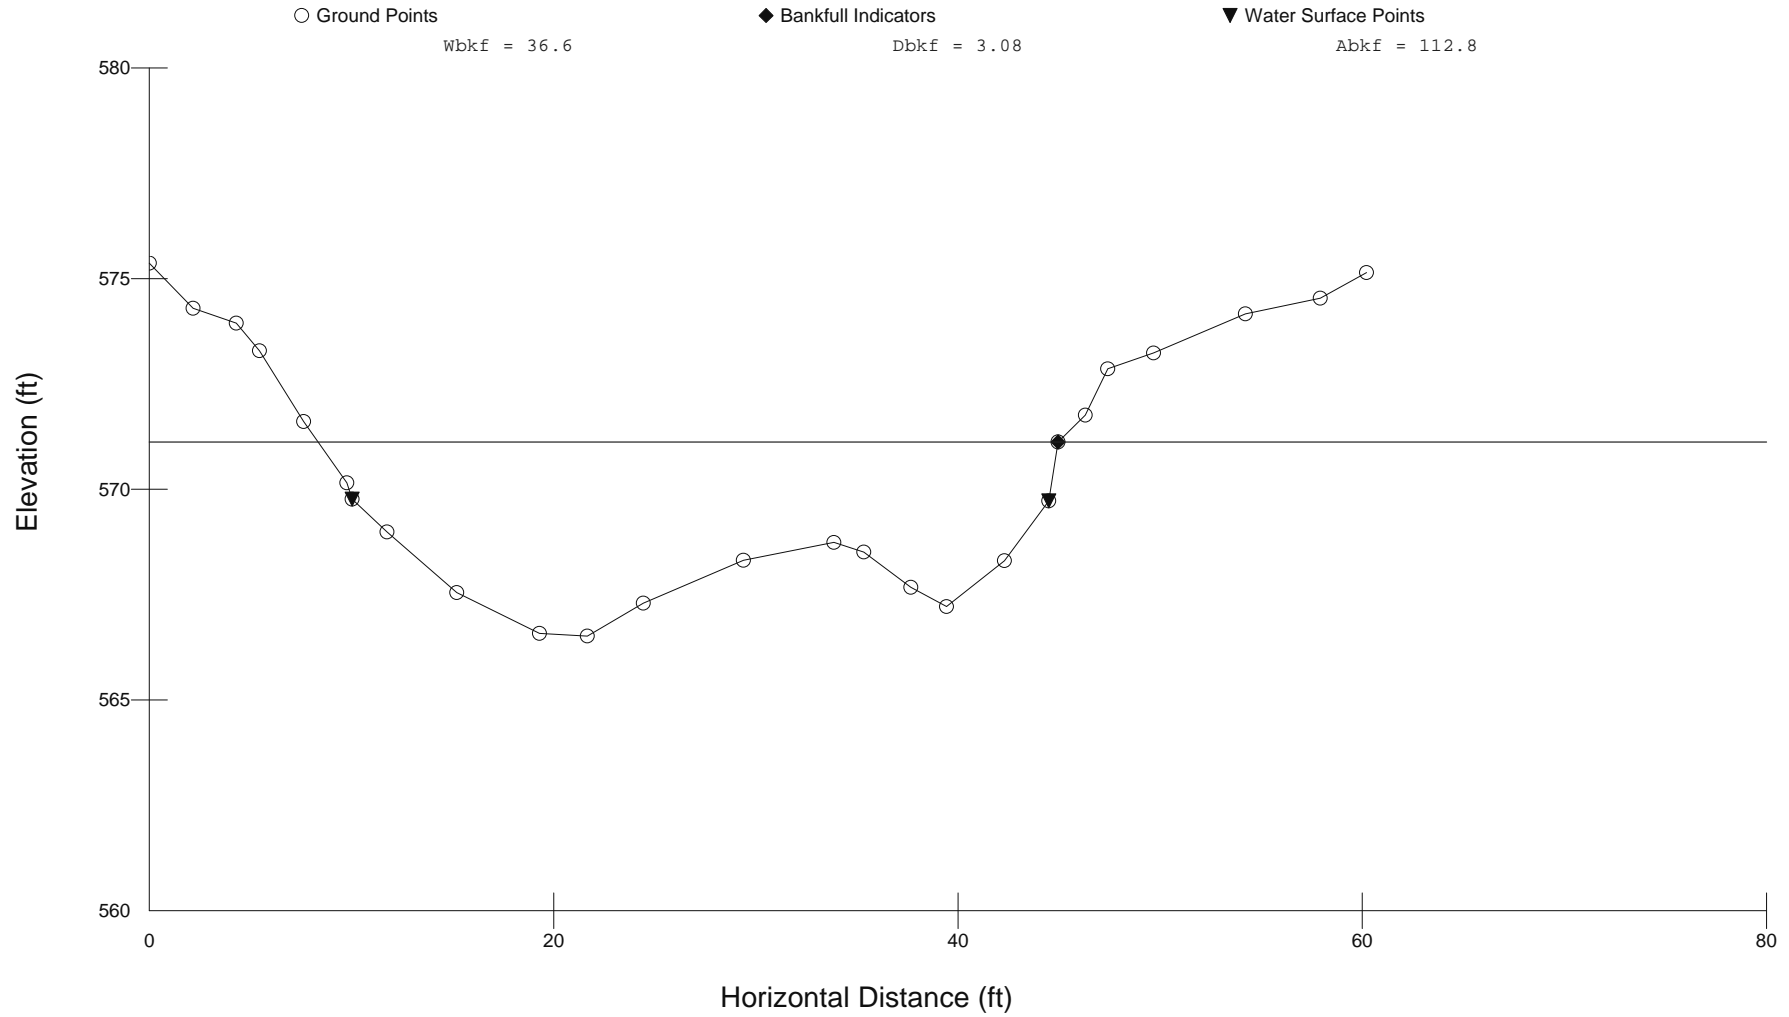


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 7
Pool
Station 29+17.31

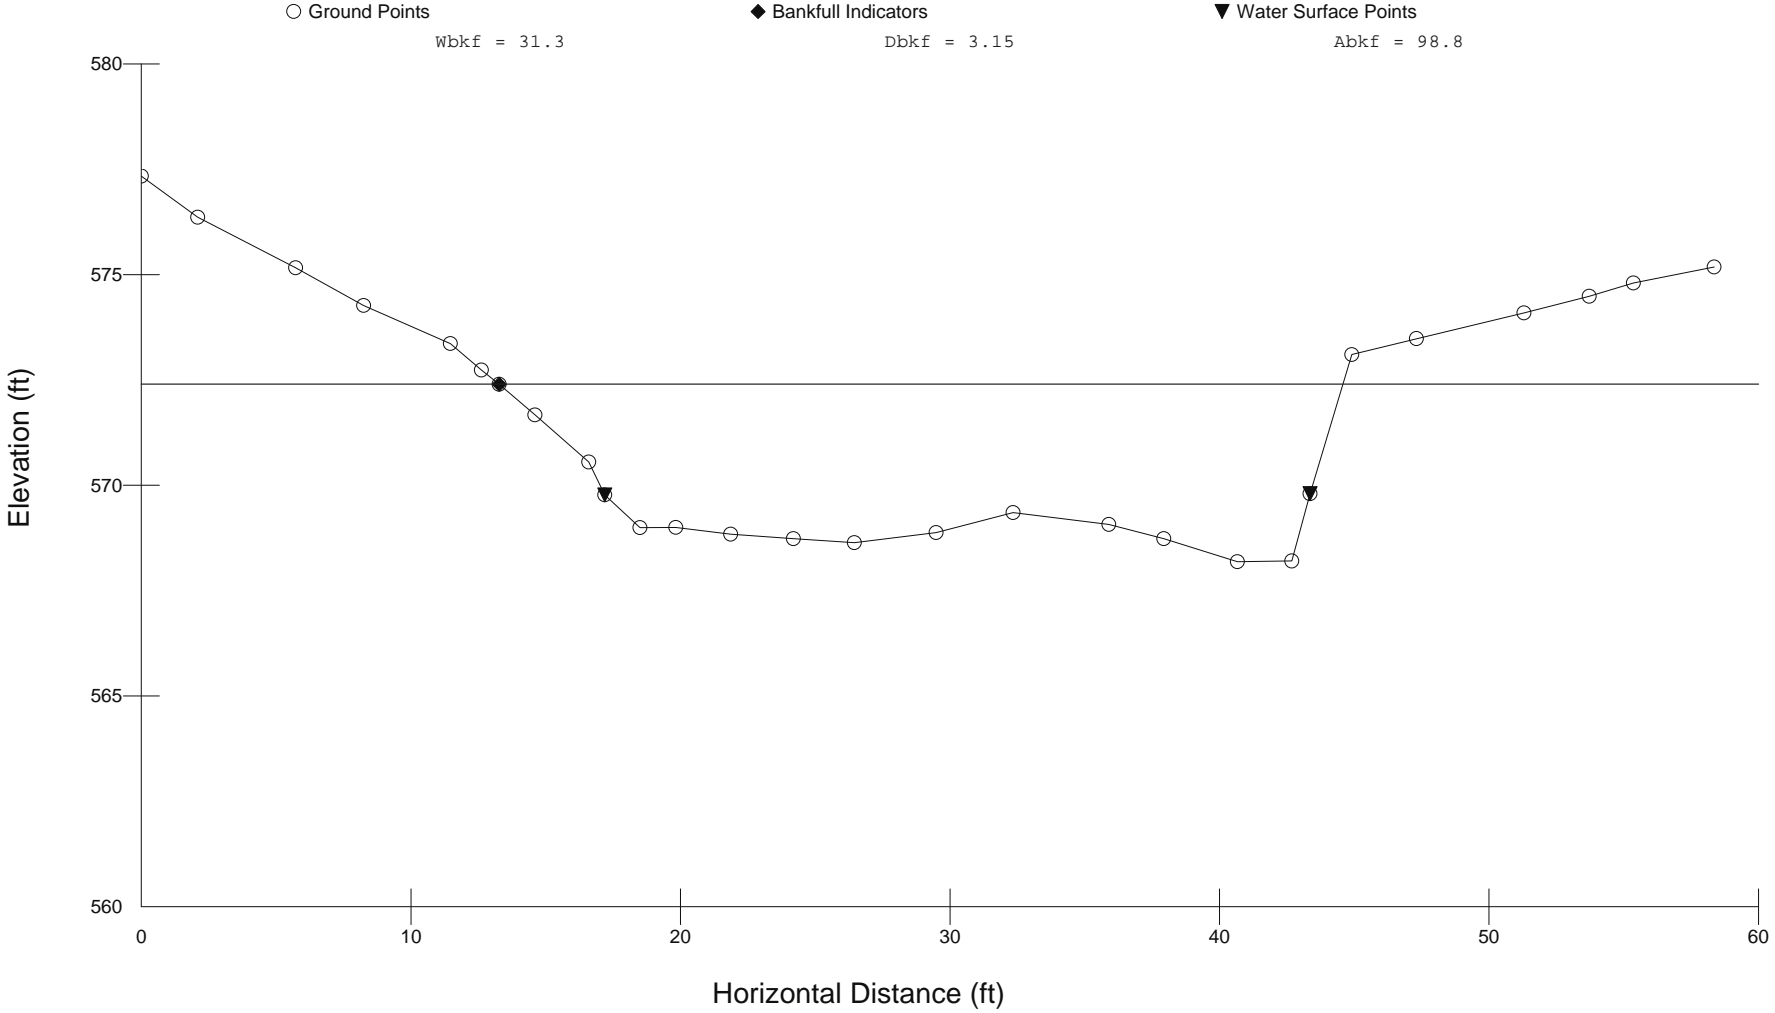


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 8
Riffle
Station 29+35.63

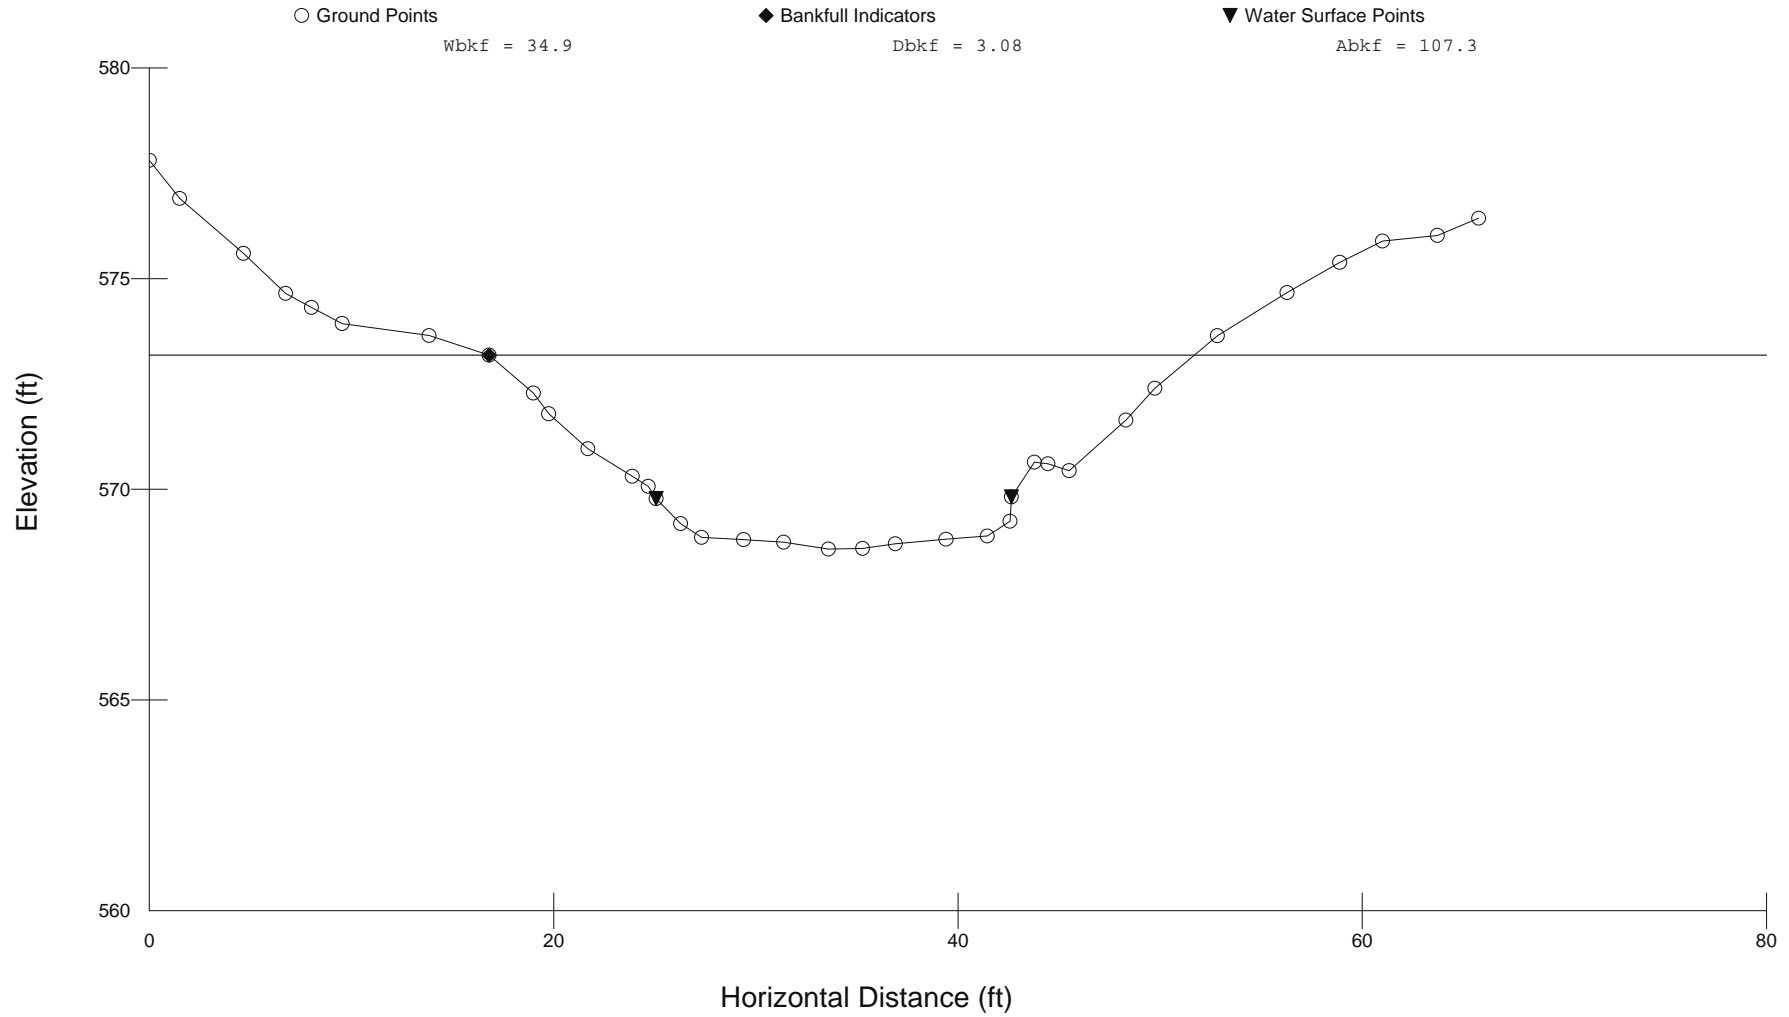


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 9
Riffle
Station 29+57.75

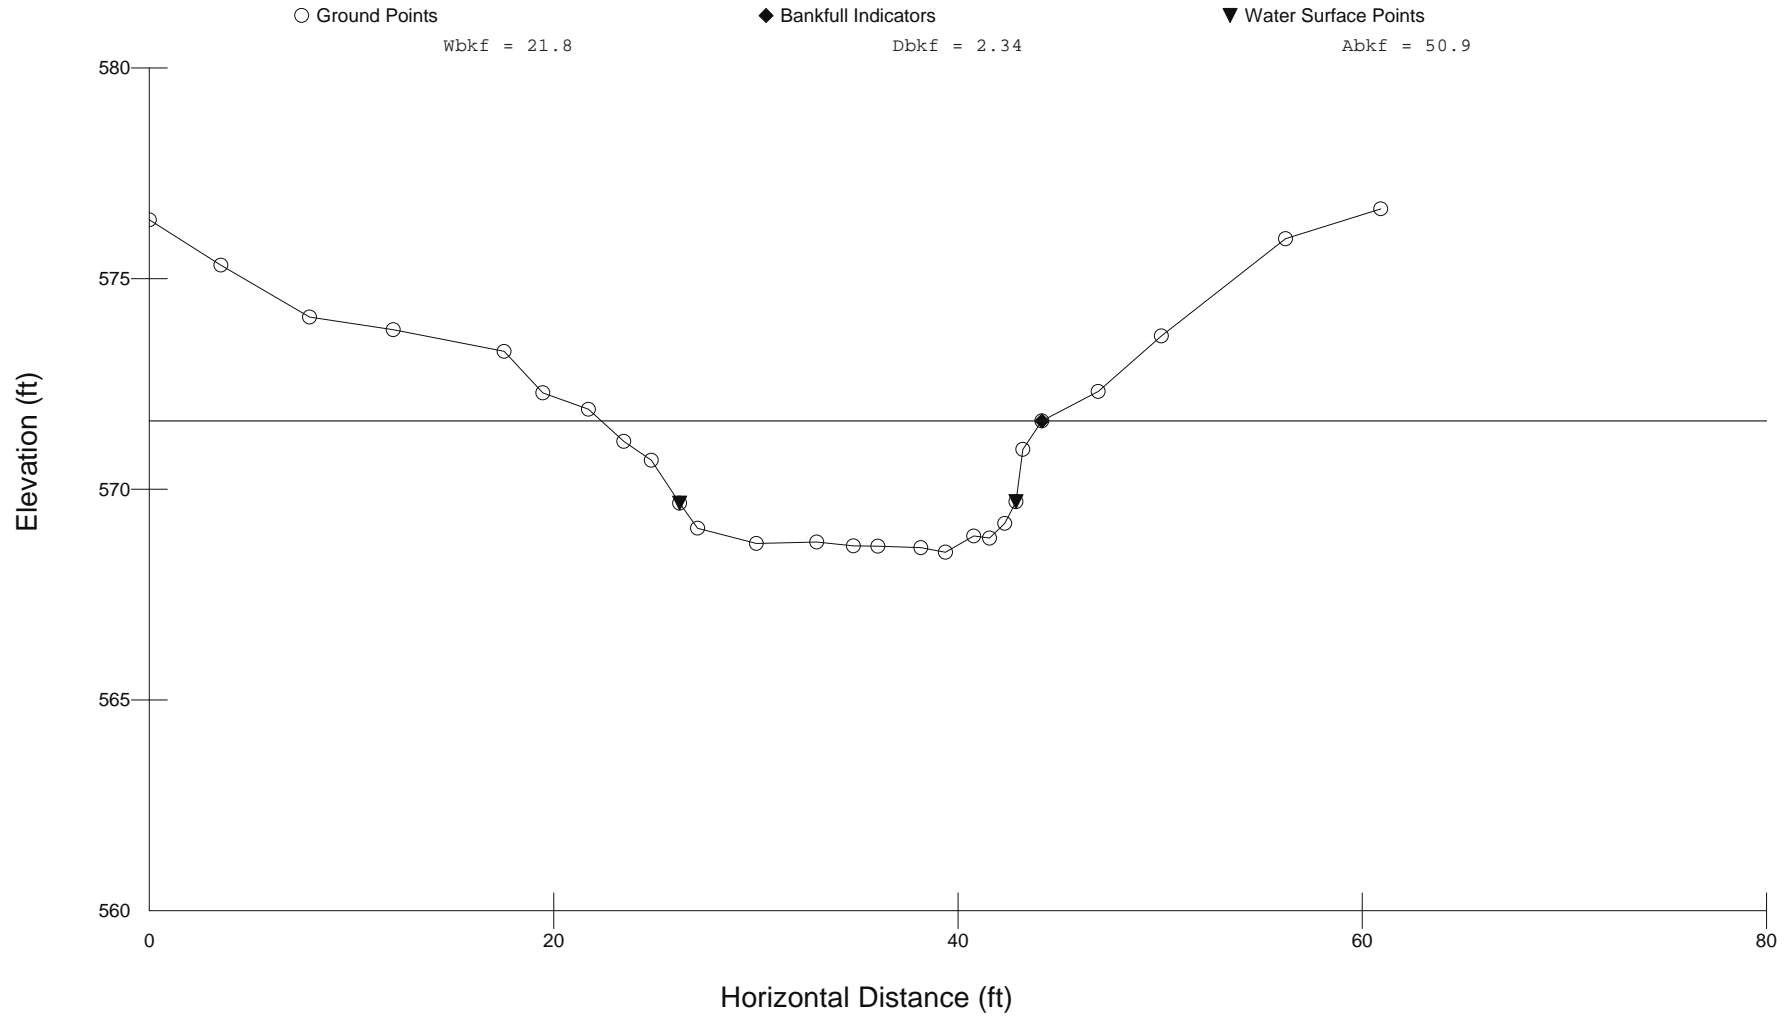


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 10
Riffle
Station 30+56.75

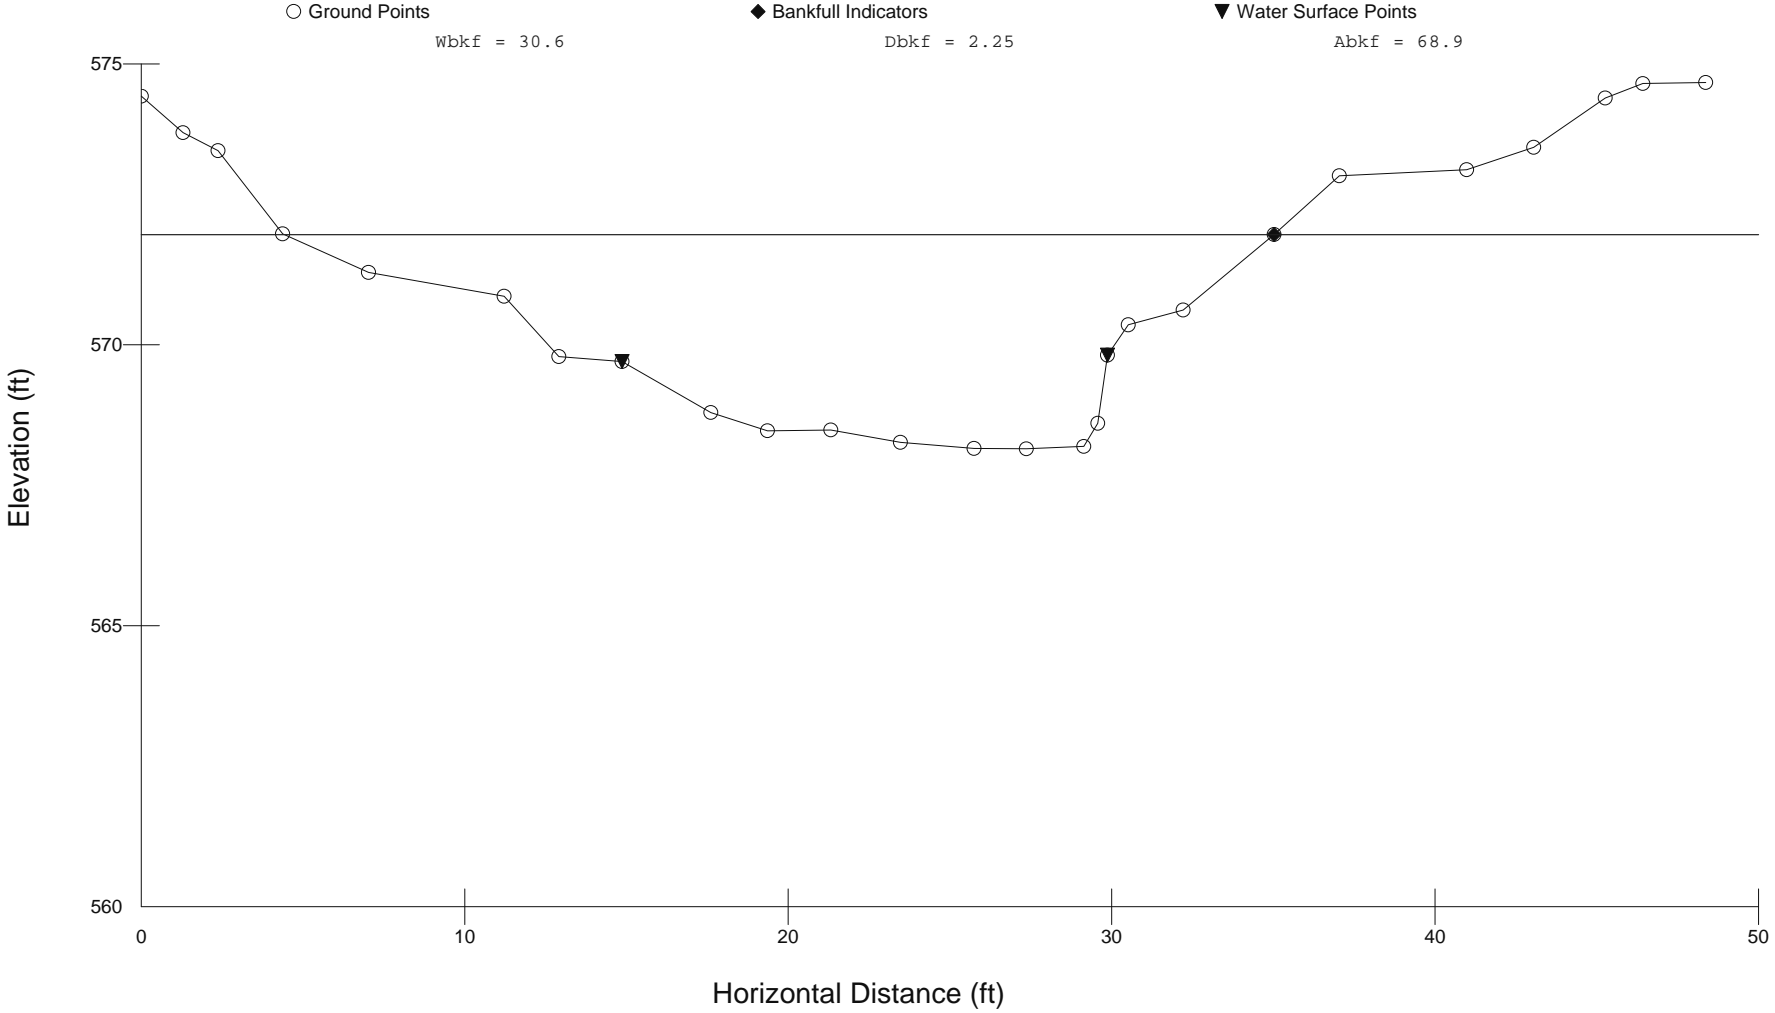


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 11
Pool
Station 10+50.94

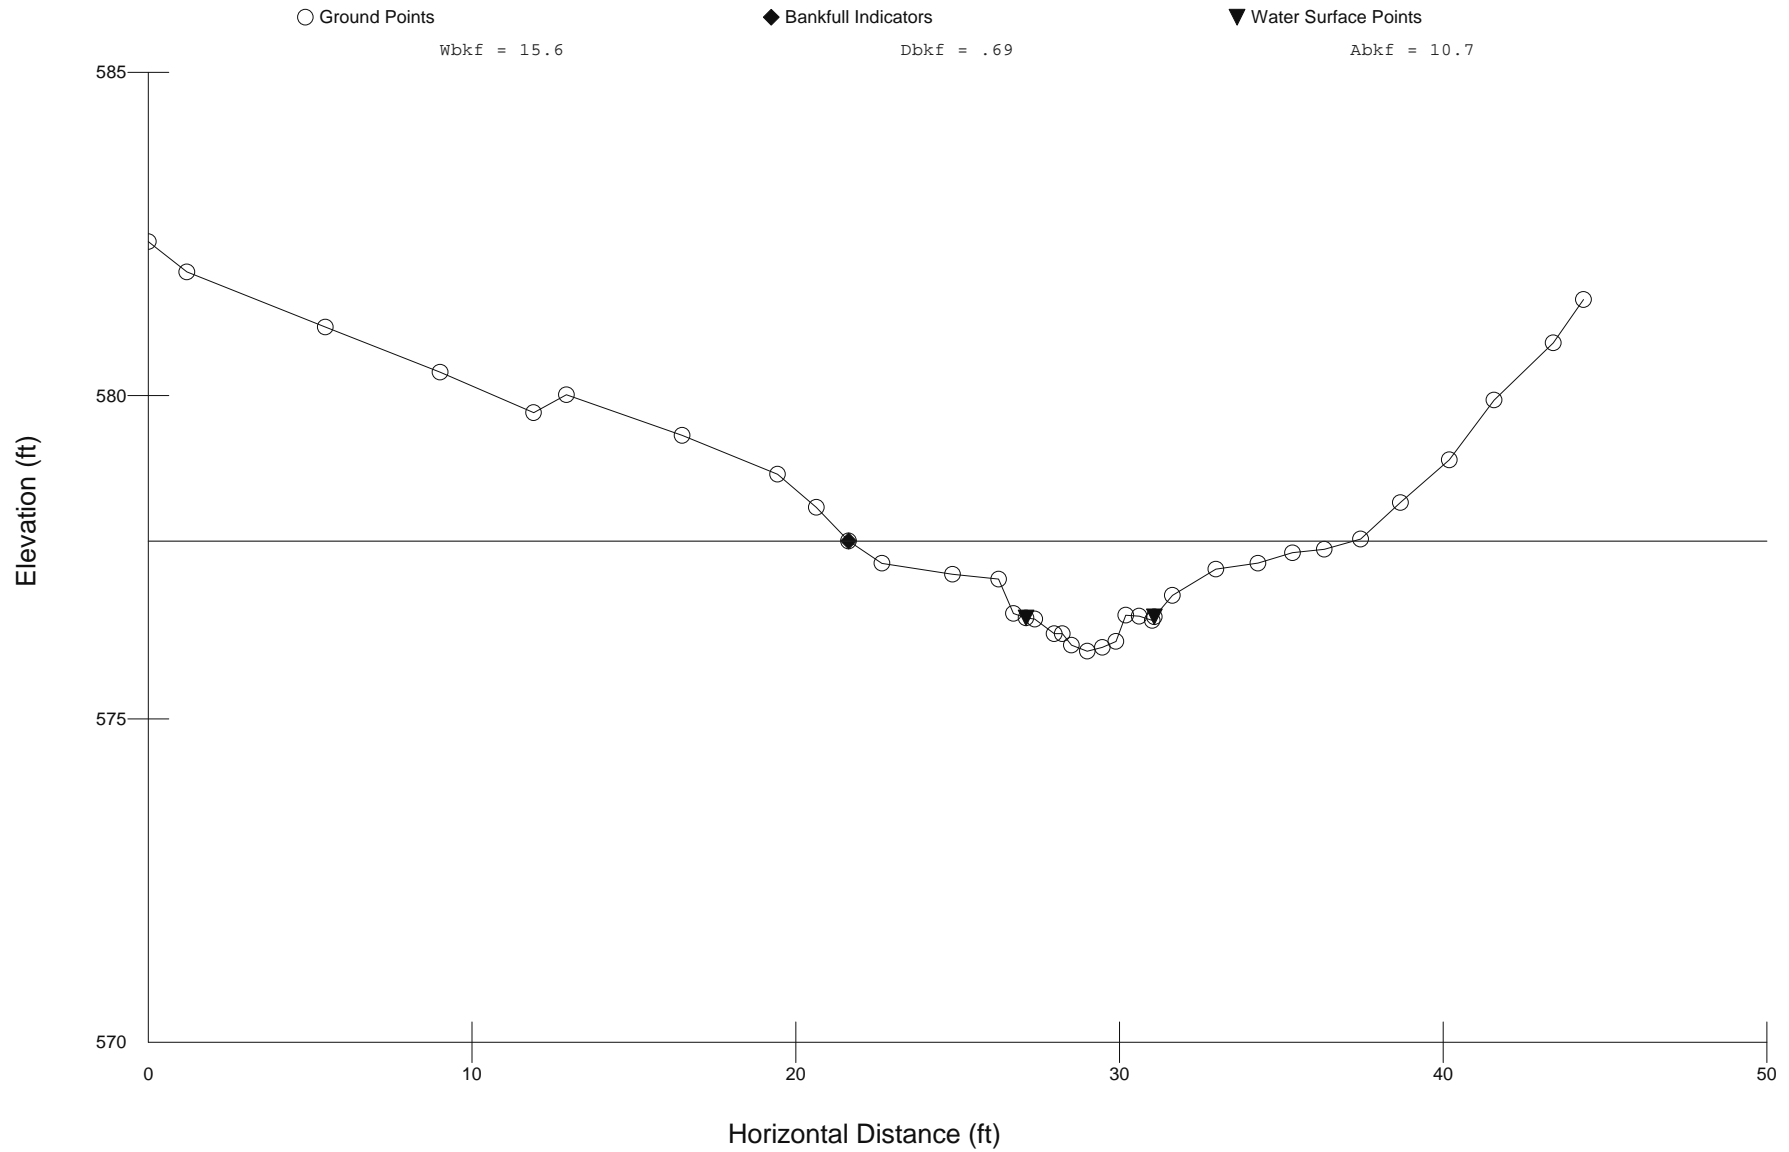


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 12
Riffle
Station 11+03.18

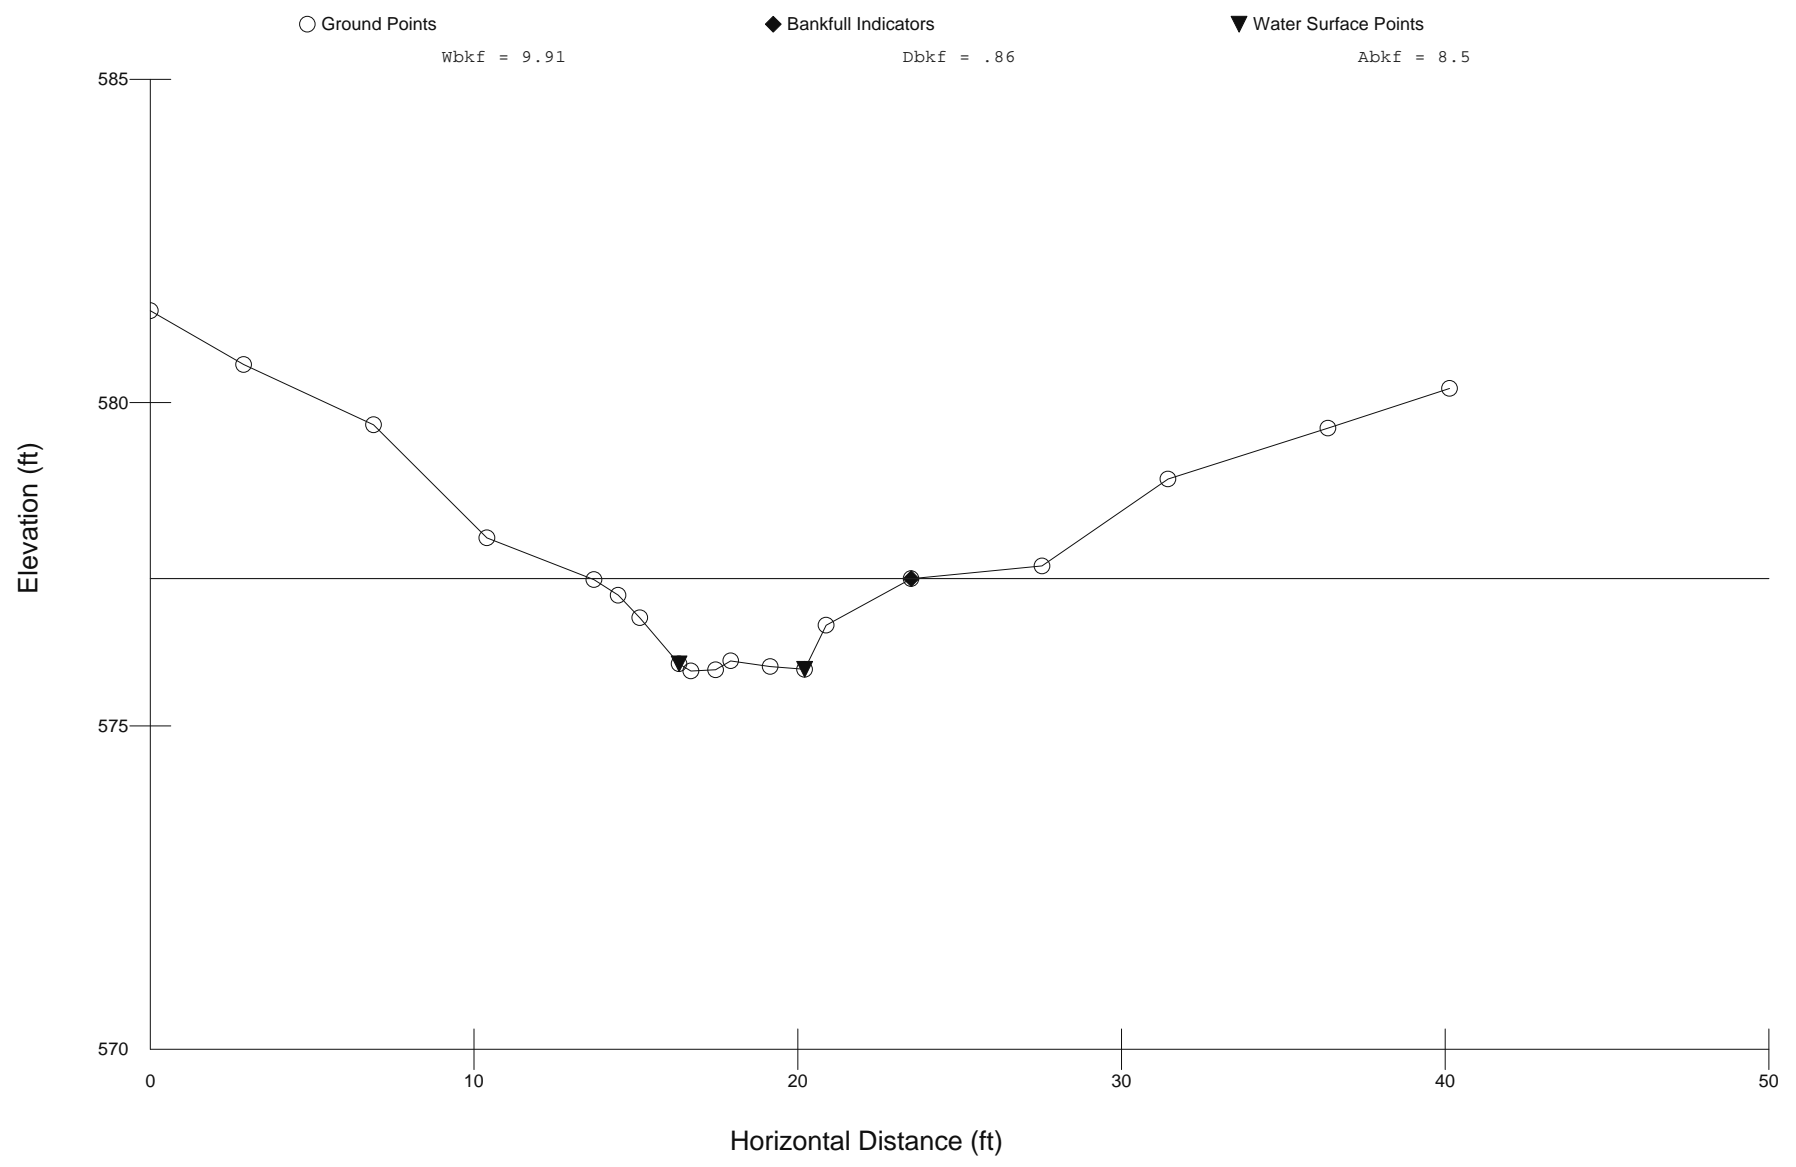


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 13
Pool
Station 11+49.64

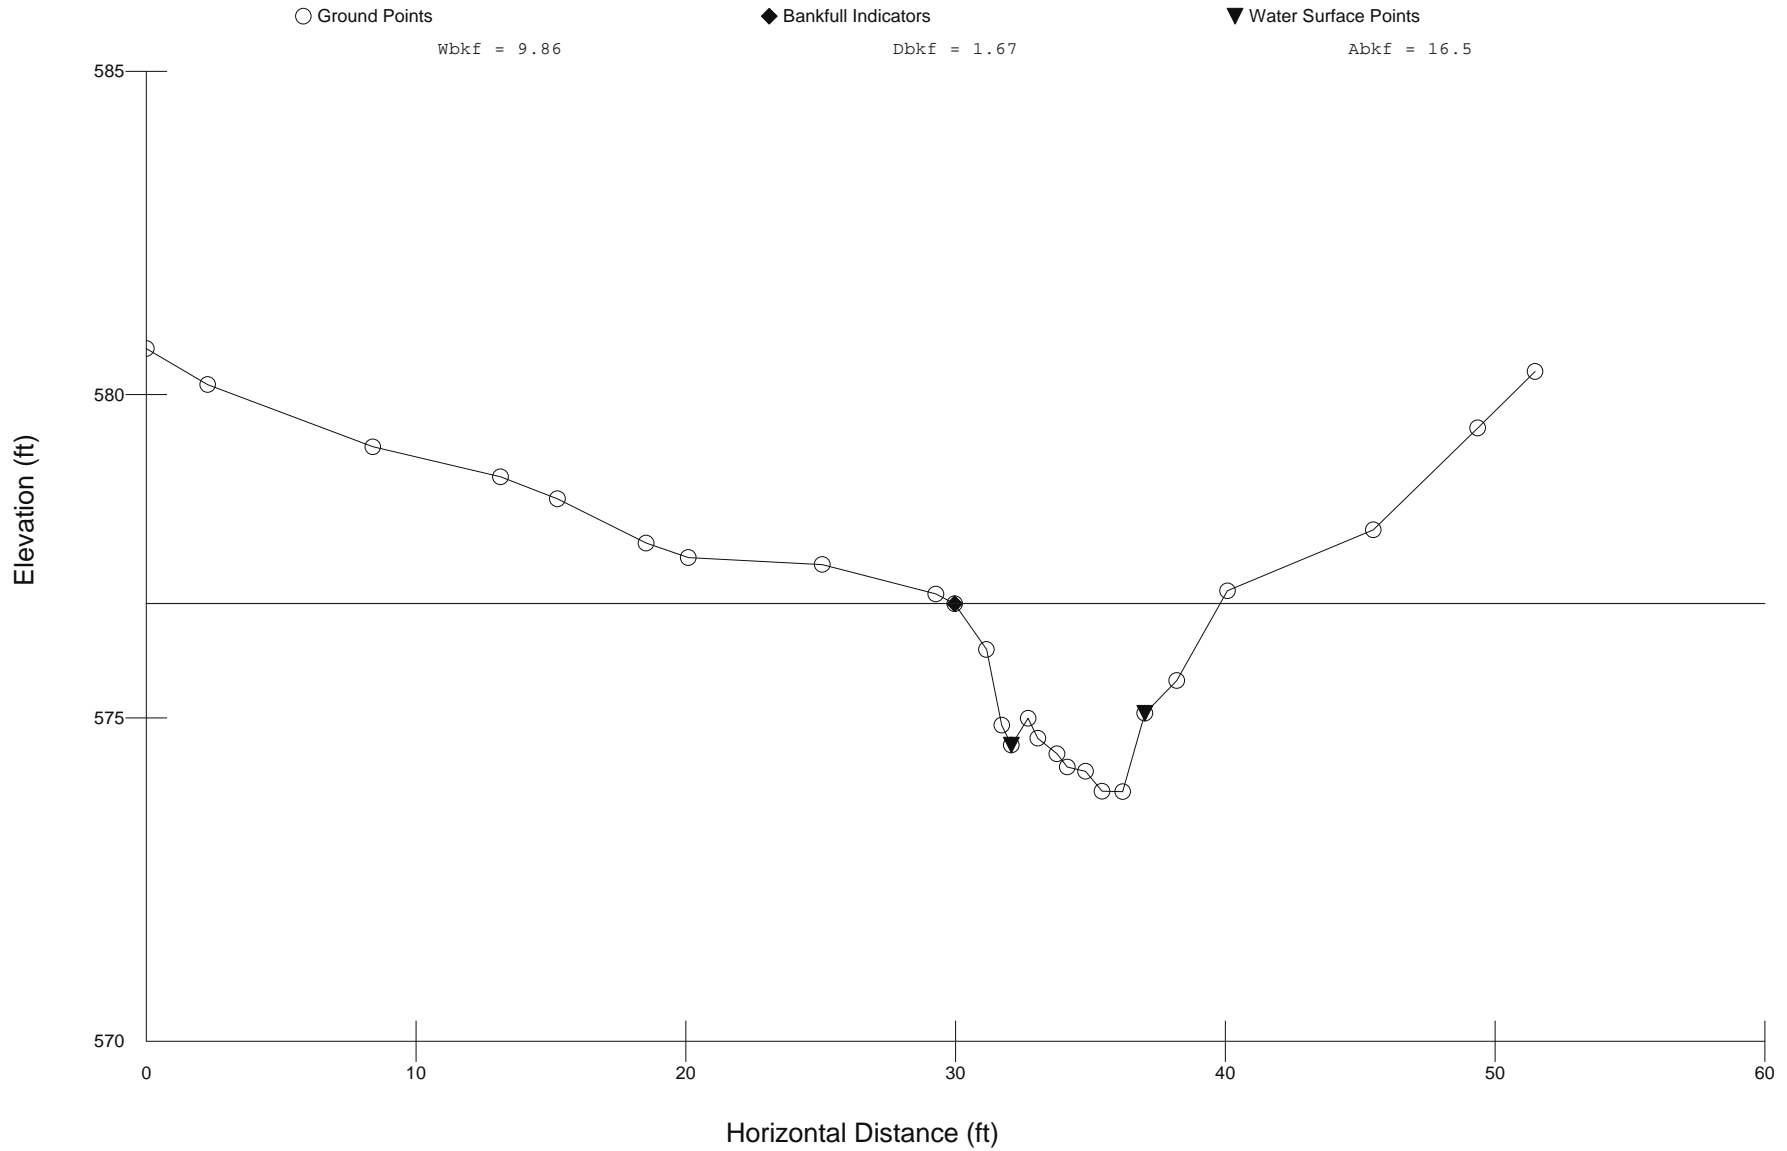


Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 14
Riffle
Station 12+50.43

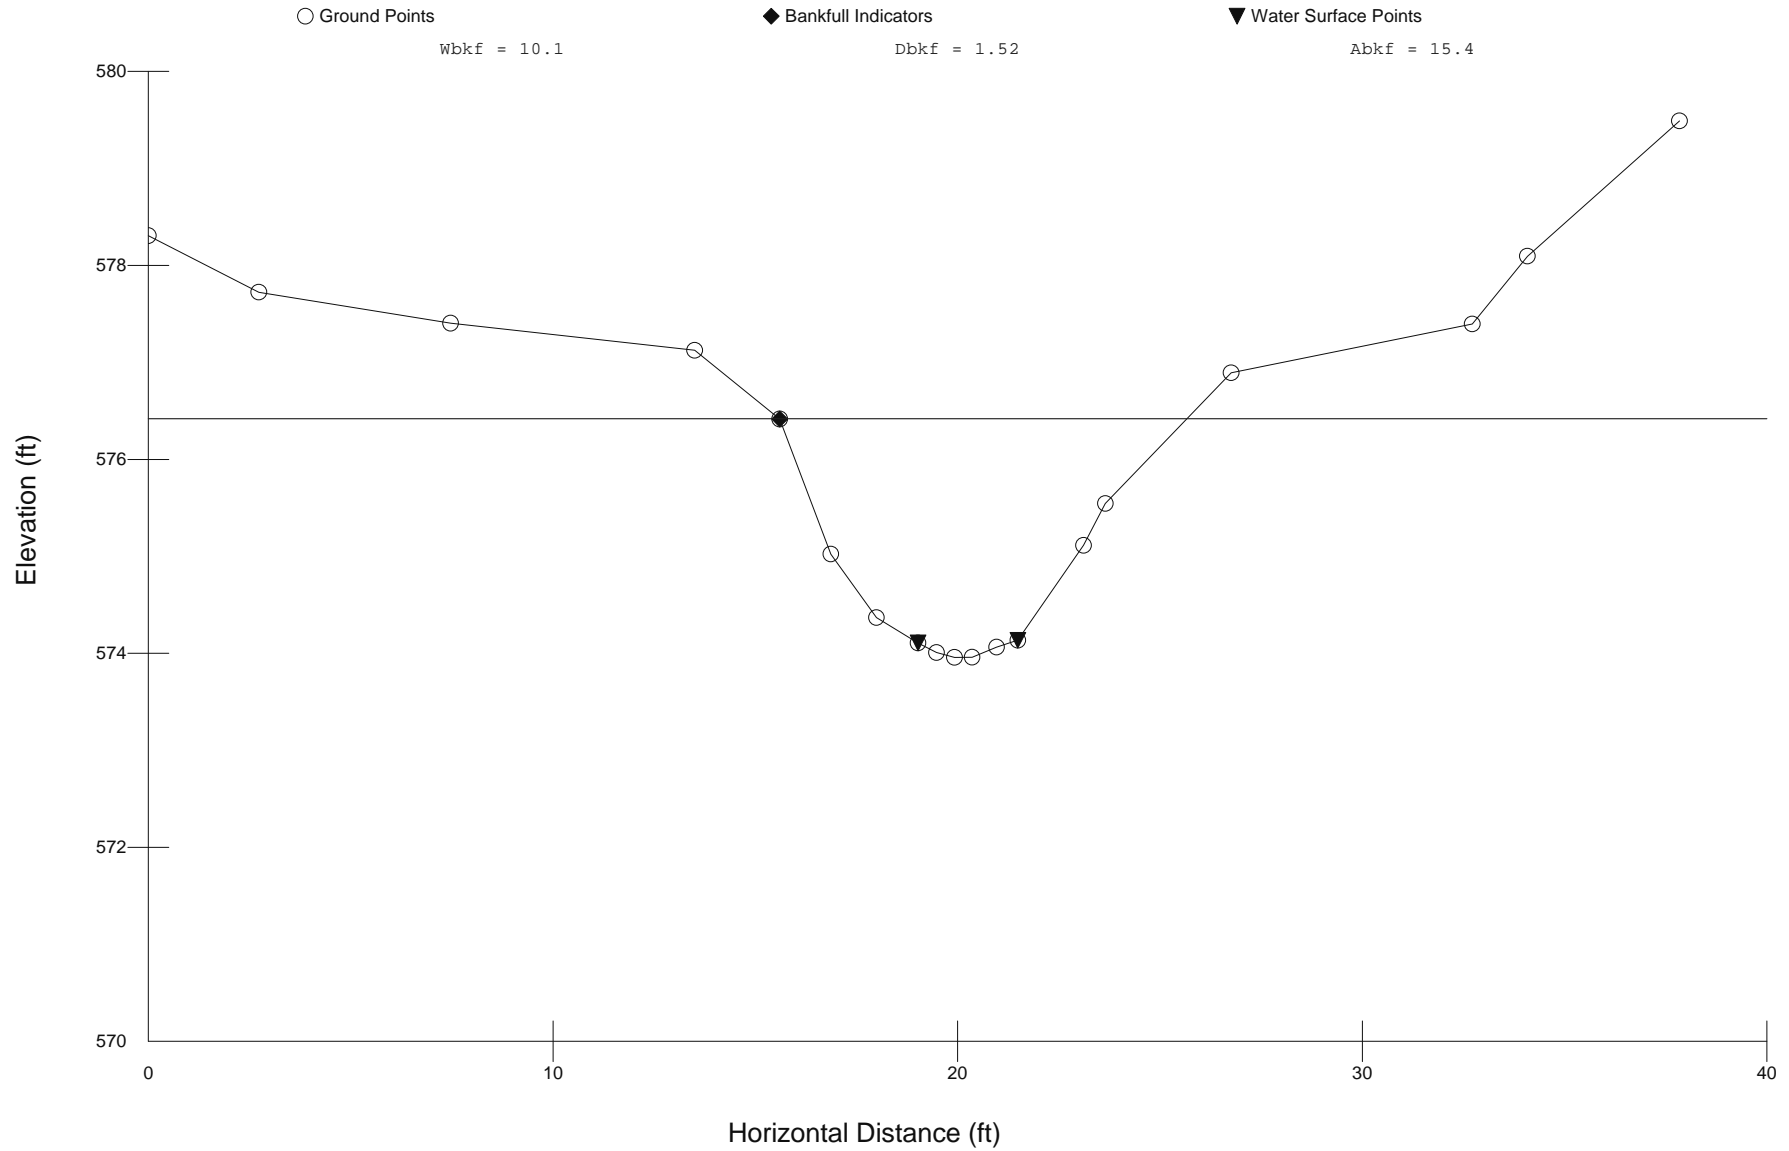

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Main Stem
Station 0+0.00 to 29+68.44

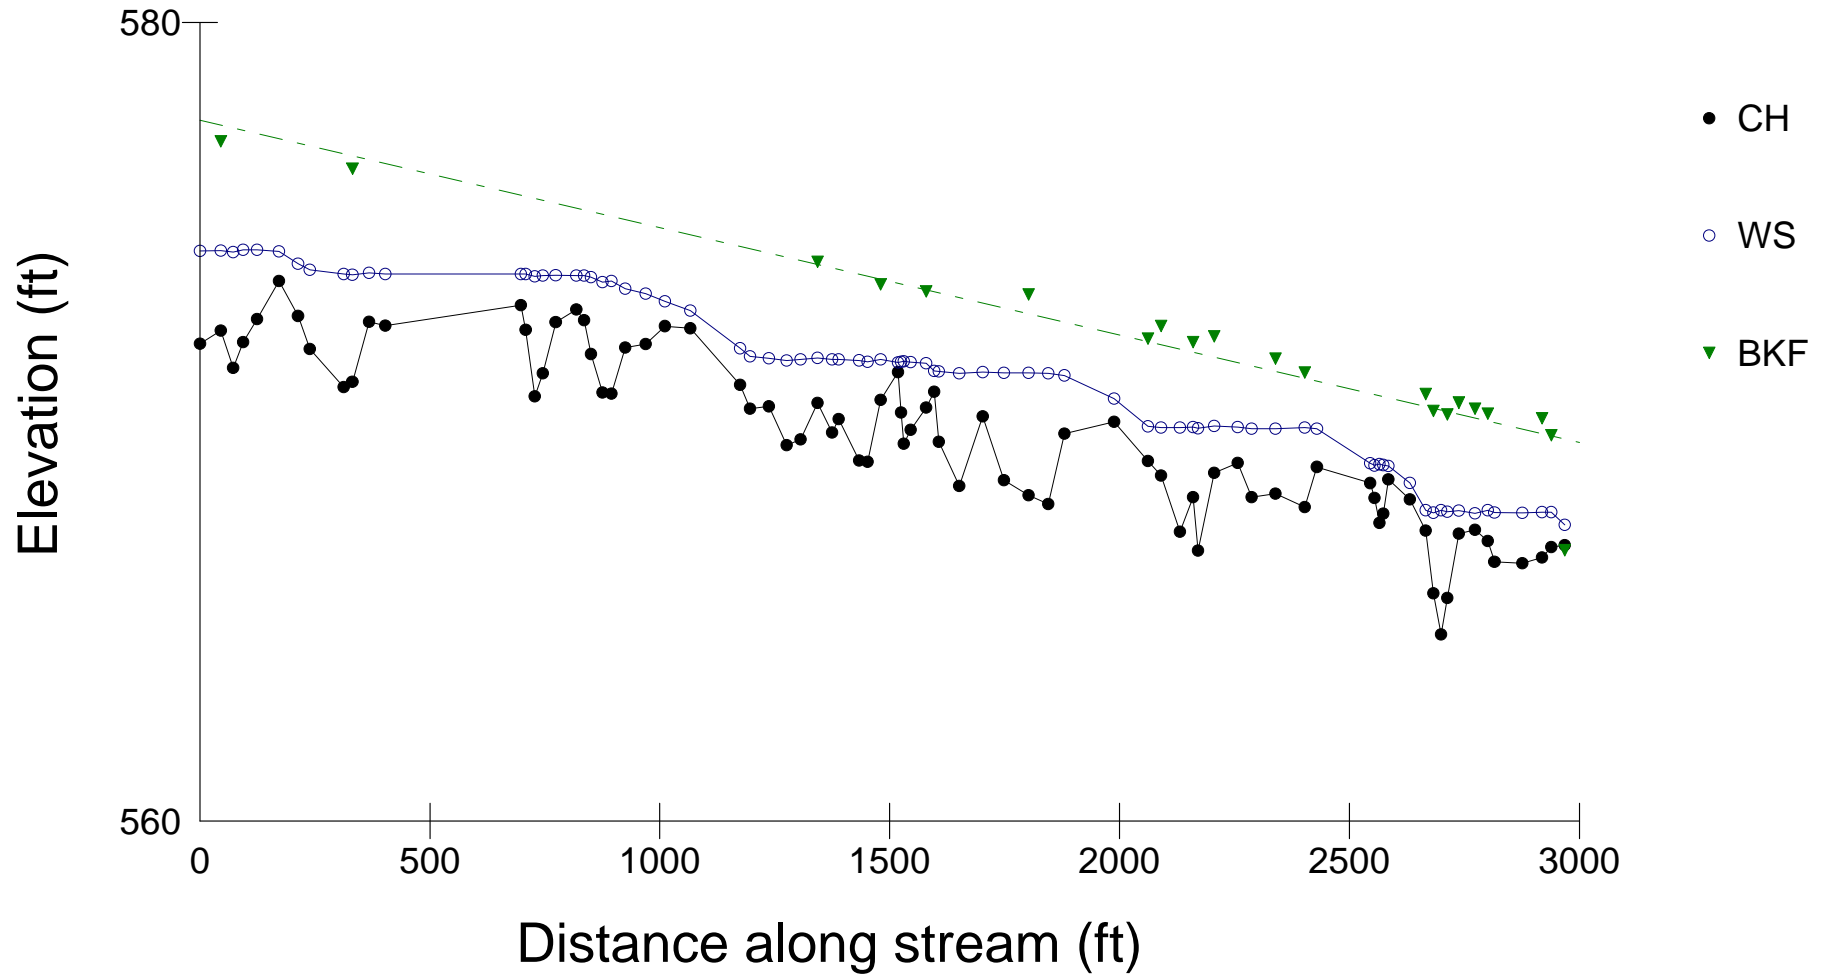

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Tributary
Station 10+0.00 to 14+40.85

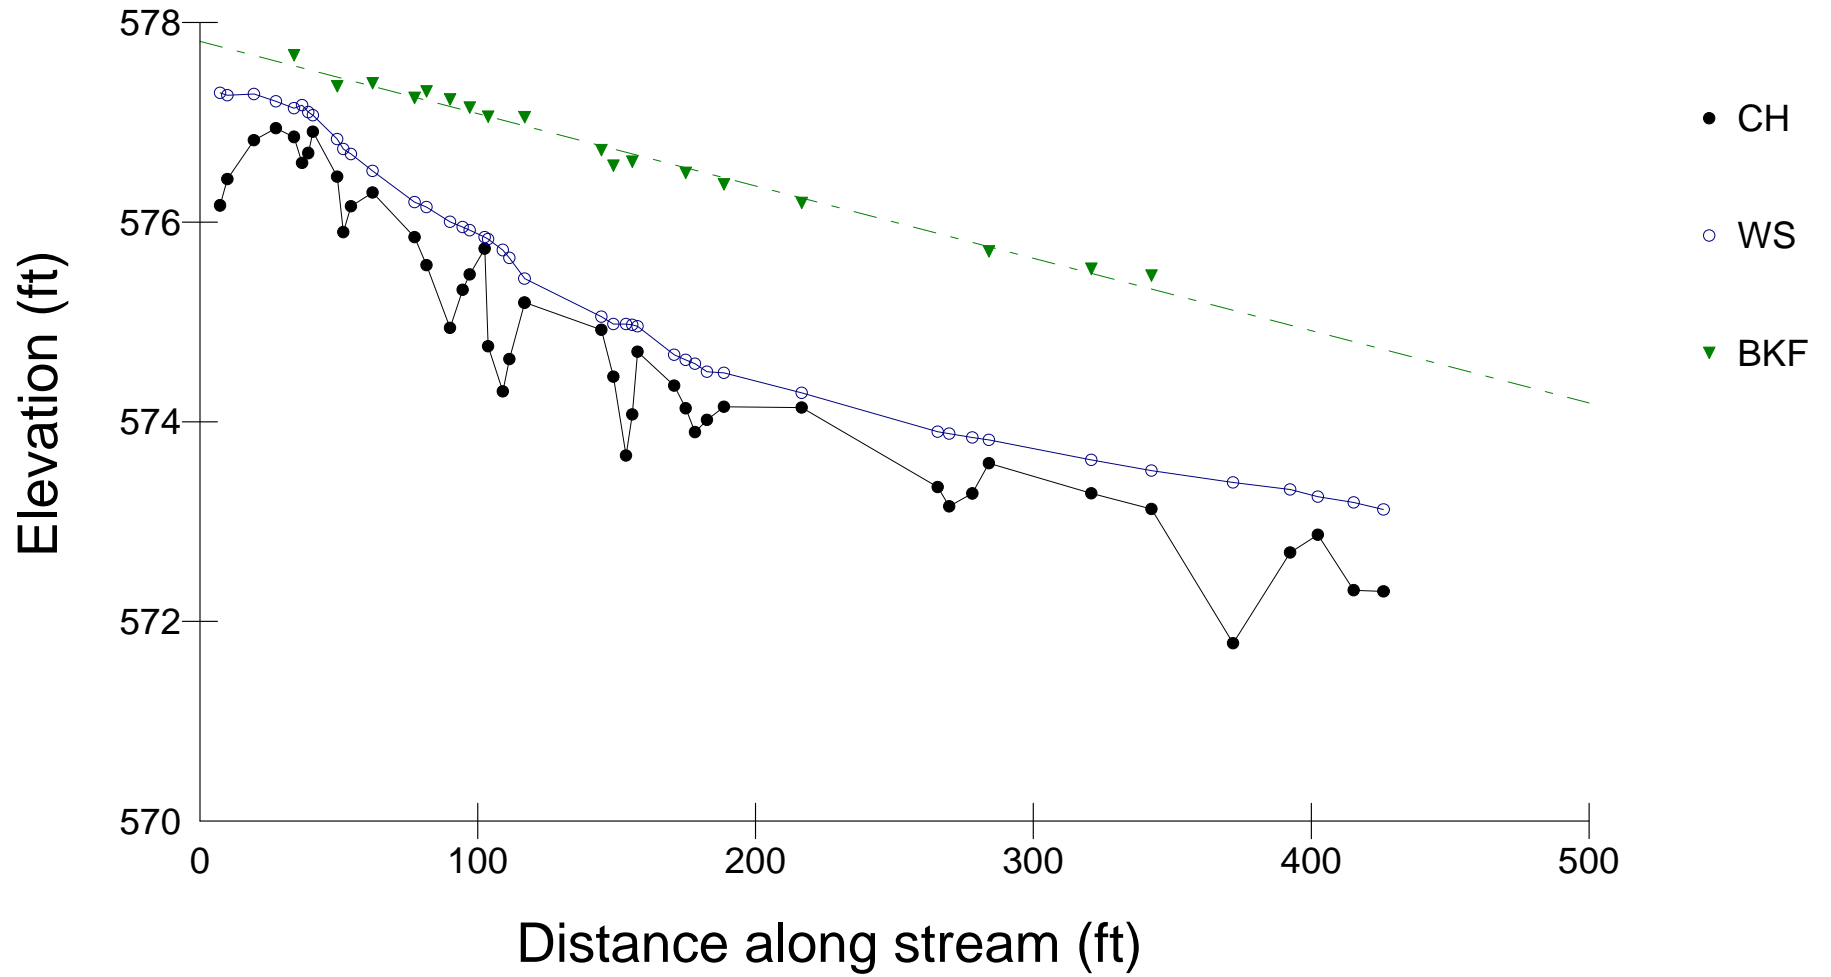

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 1, XS 1


Riffle

Station 11+58.48

D50: 6.21 mm

D84: 28.87 mm

D95: 112.8 mm

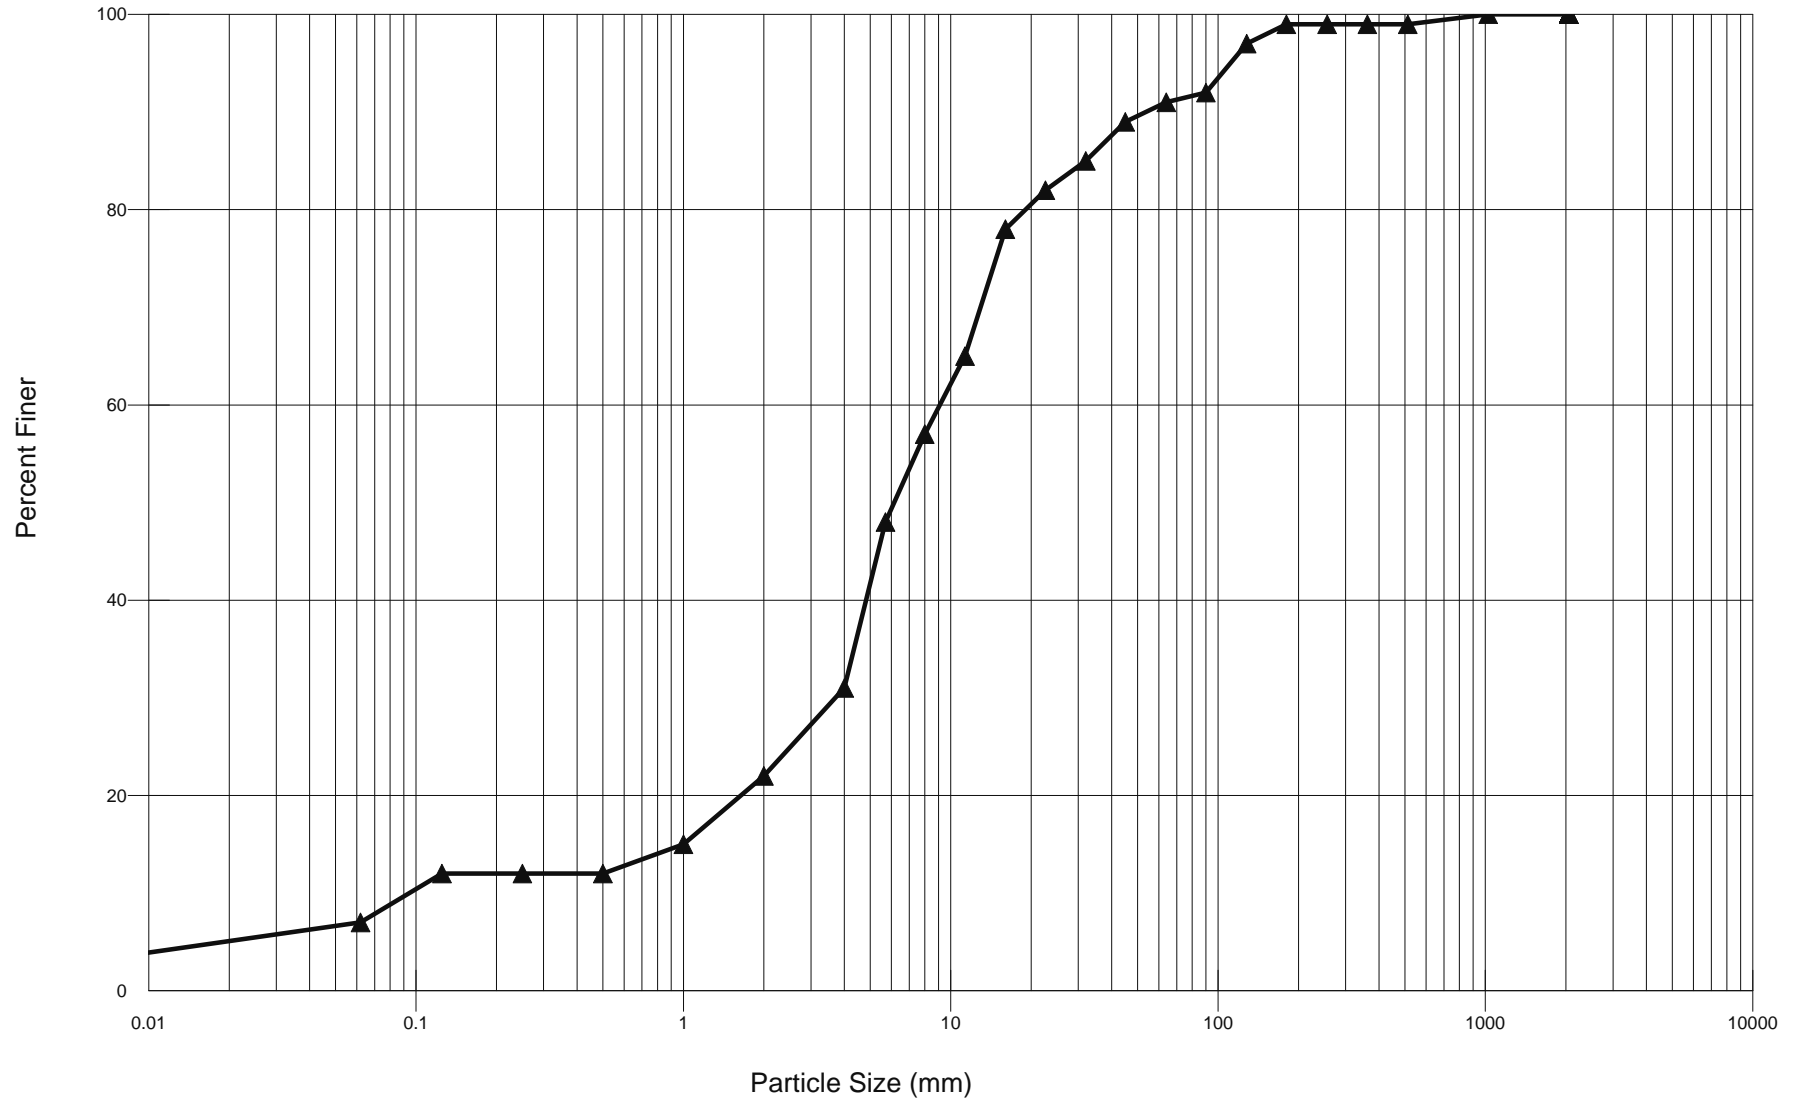

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 1, XS 1


Riffle

Station 11+58.48


D50: 6.21 mm

D84: 28.87 mm


D95: 112.8 mm

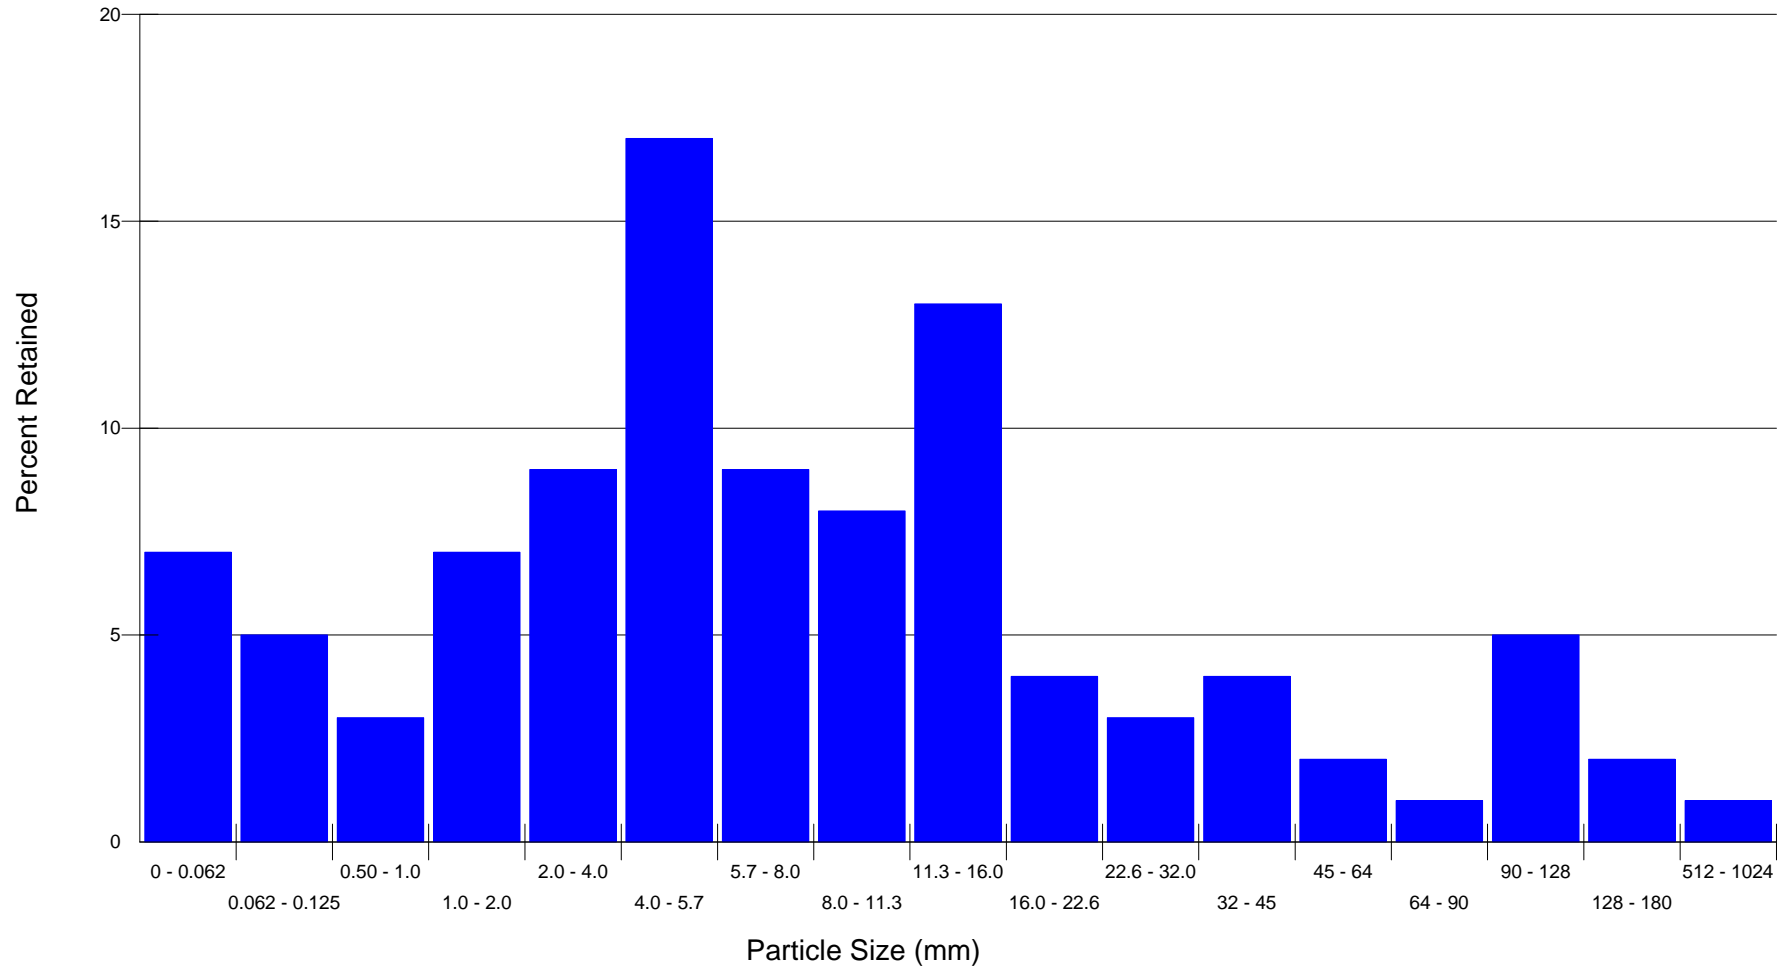

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 4, XS 4
Riffle
Station 19+69.54
D50: 2.18 mm
D84: 24.48 mm
D95: 90.0 mm

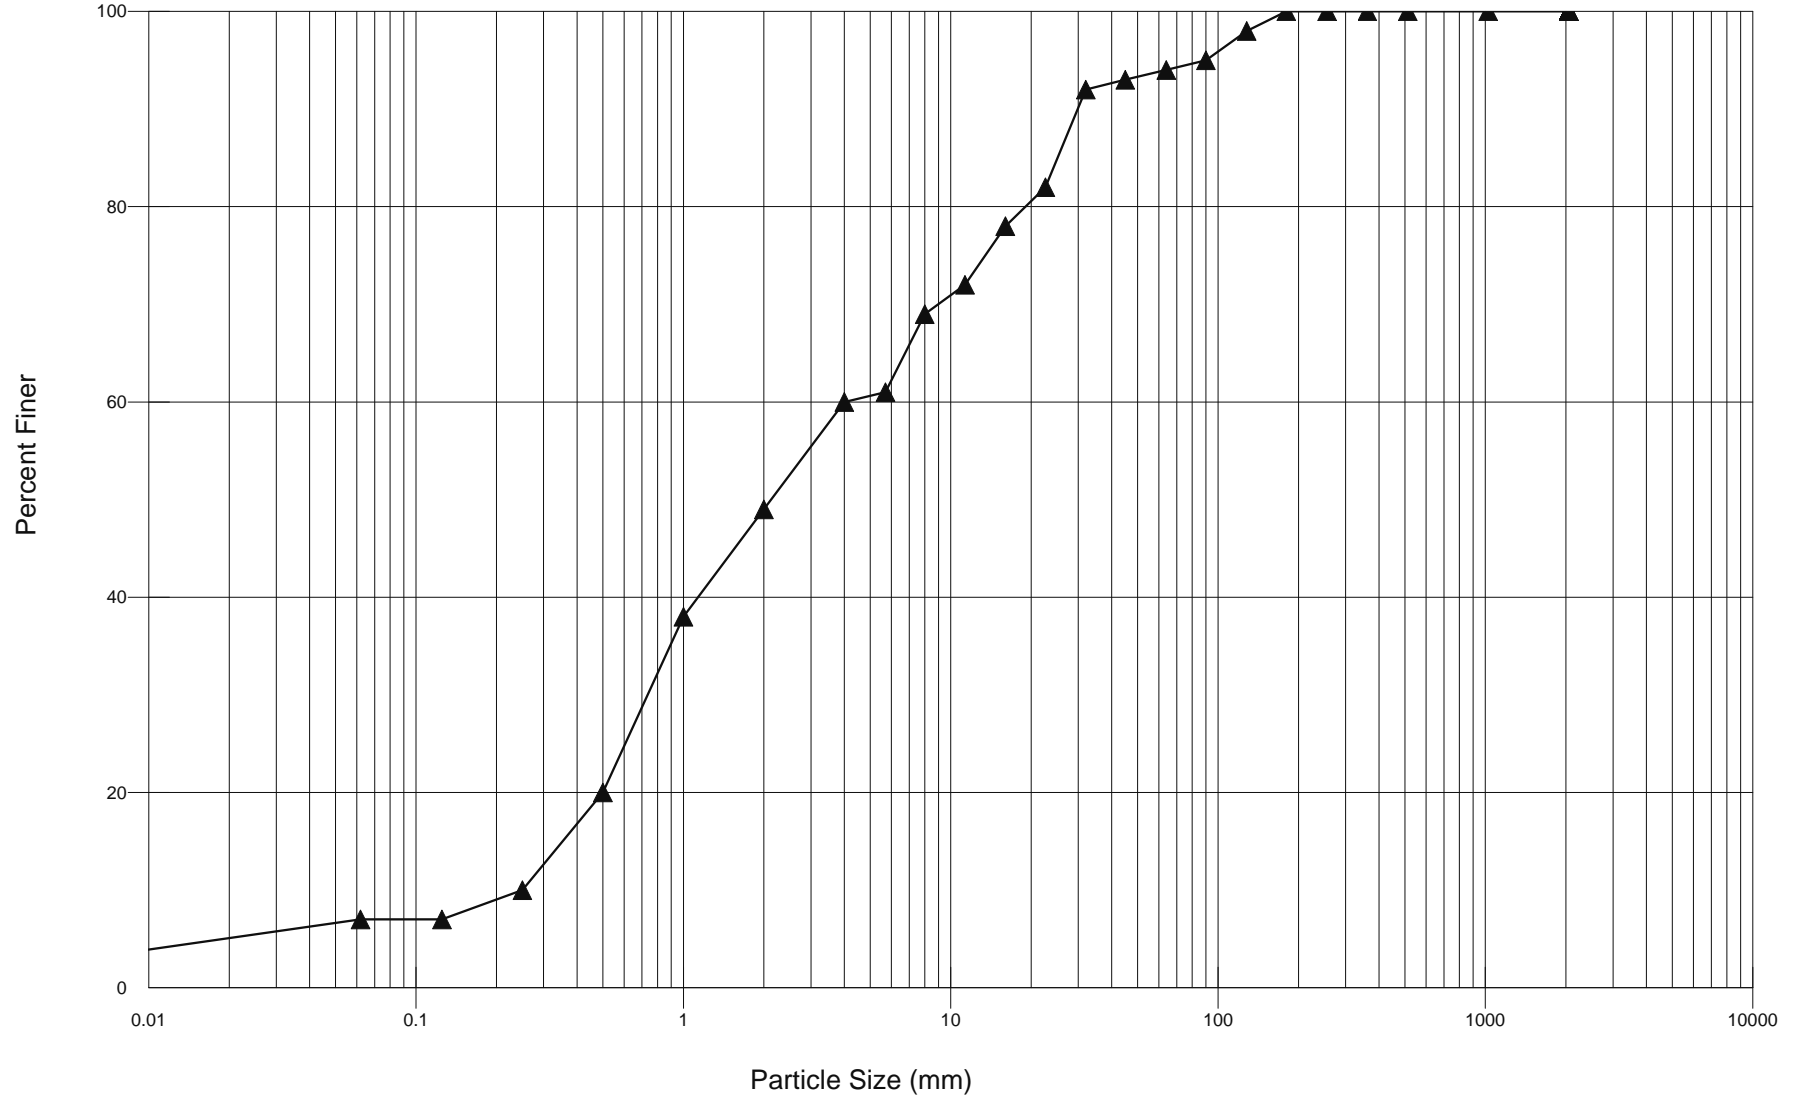

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 4, XS 4
Riffle
Station 19+69.54
D50: 2.18 mm
D84: 24.48 mm
D95: 90.0 mm

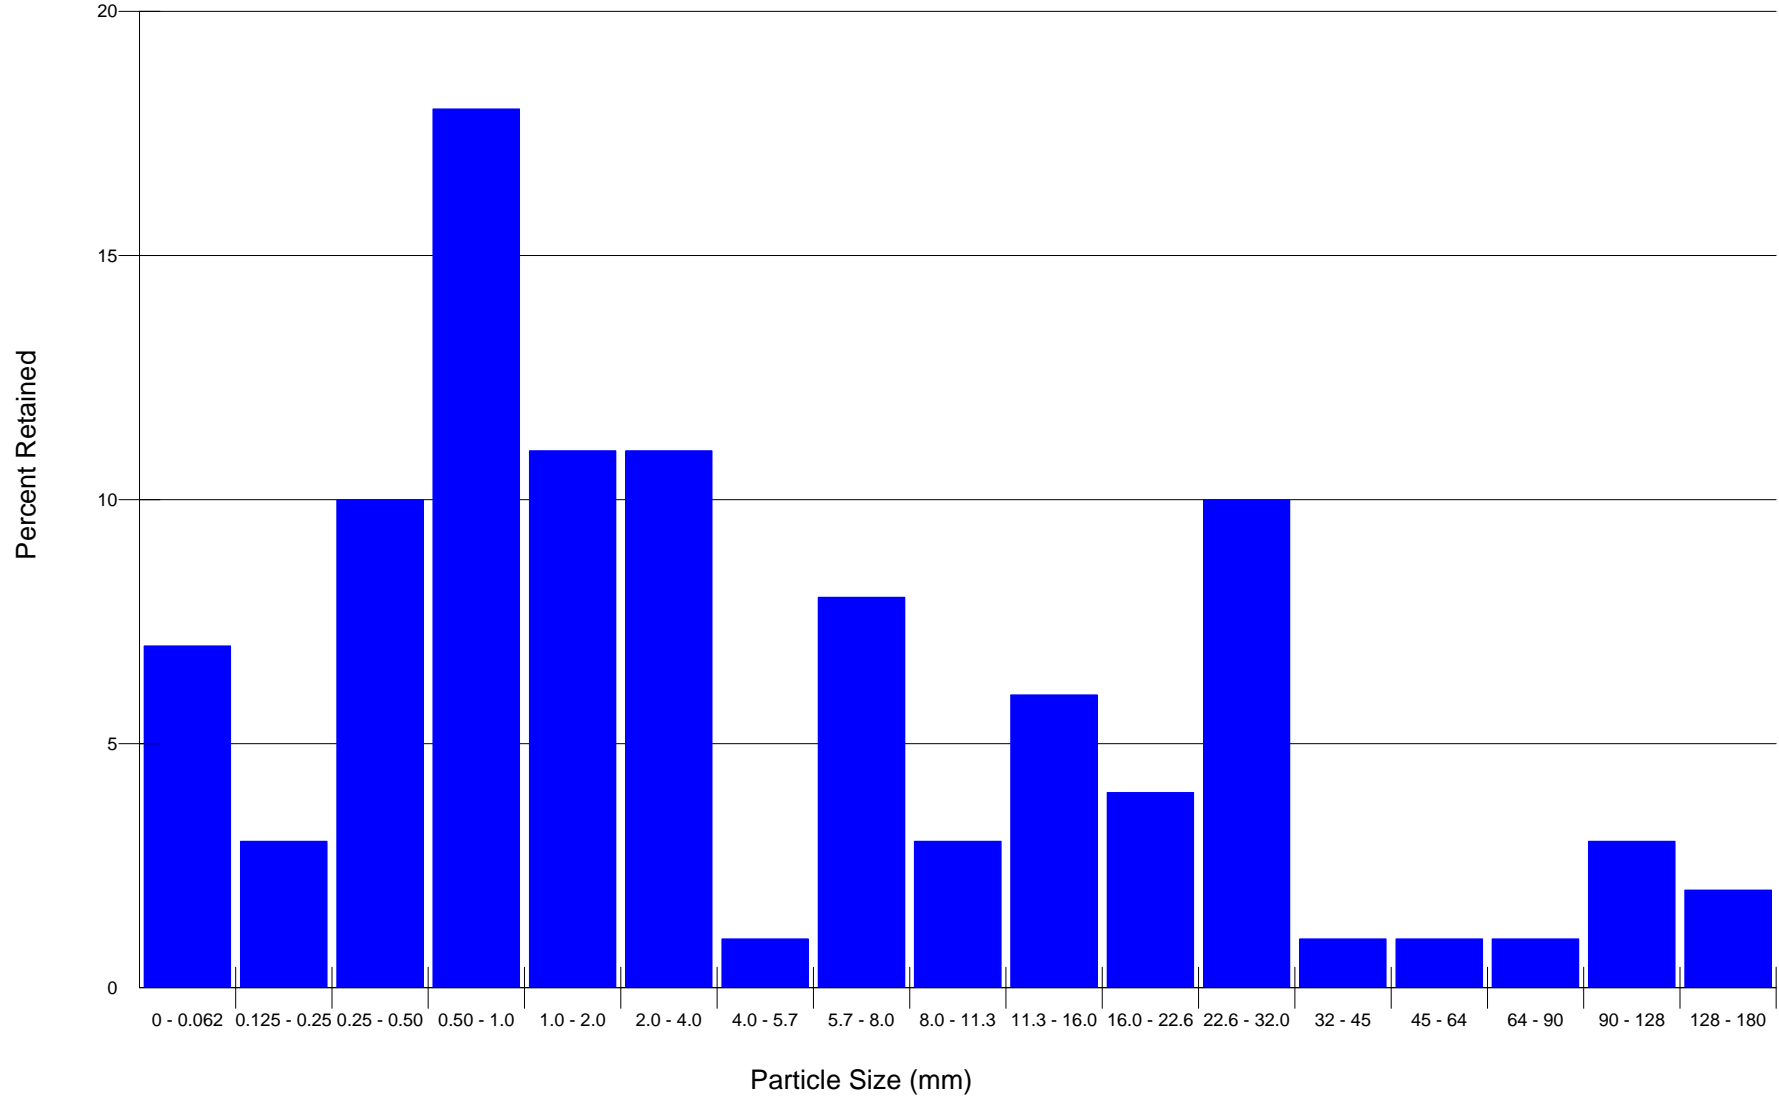

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 5


Riffle

Station 27+95.78

D50: 8.37 mm

D84: 25.49 mm

D95: 45.0 mm

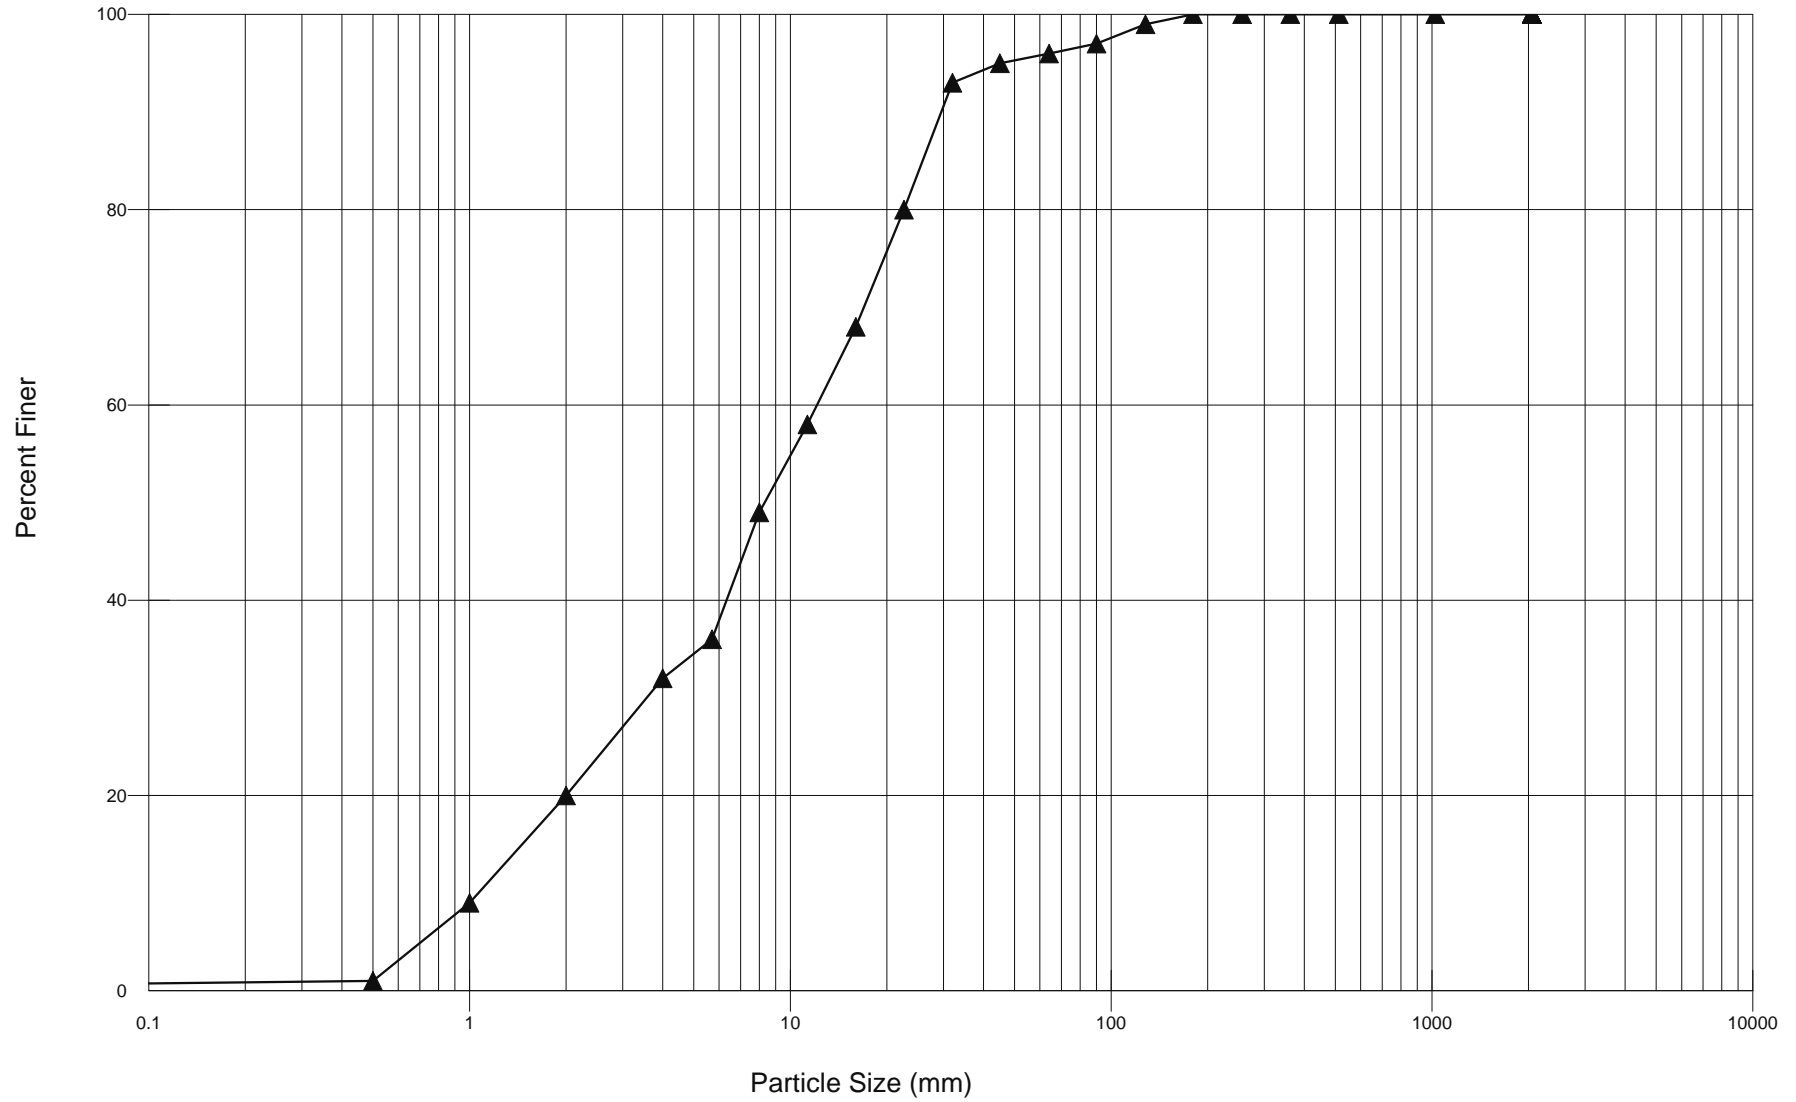

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 5


Riffle

Station 27+95.78

D50: 8.37 mm

D84: 25.49 mm

D95: 45.0 mm

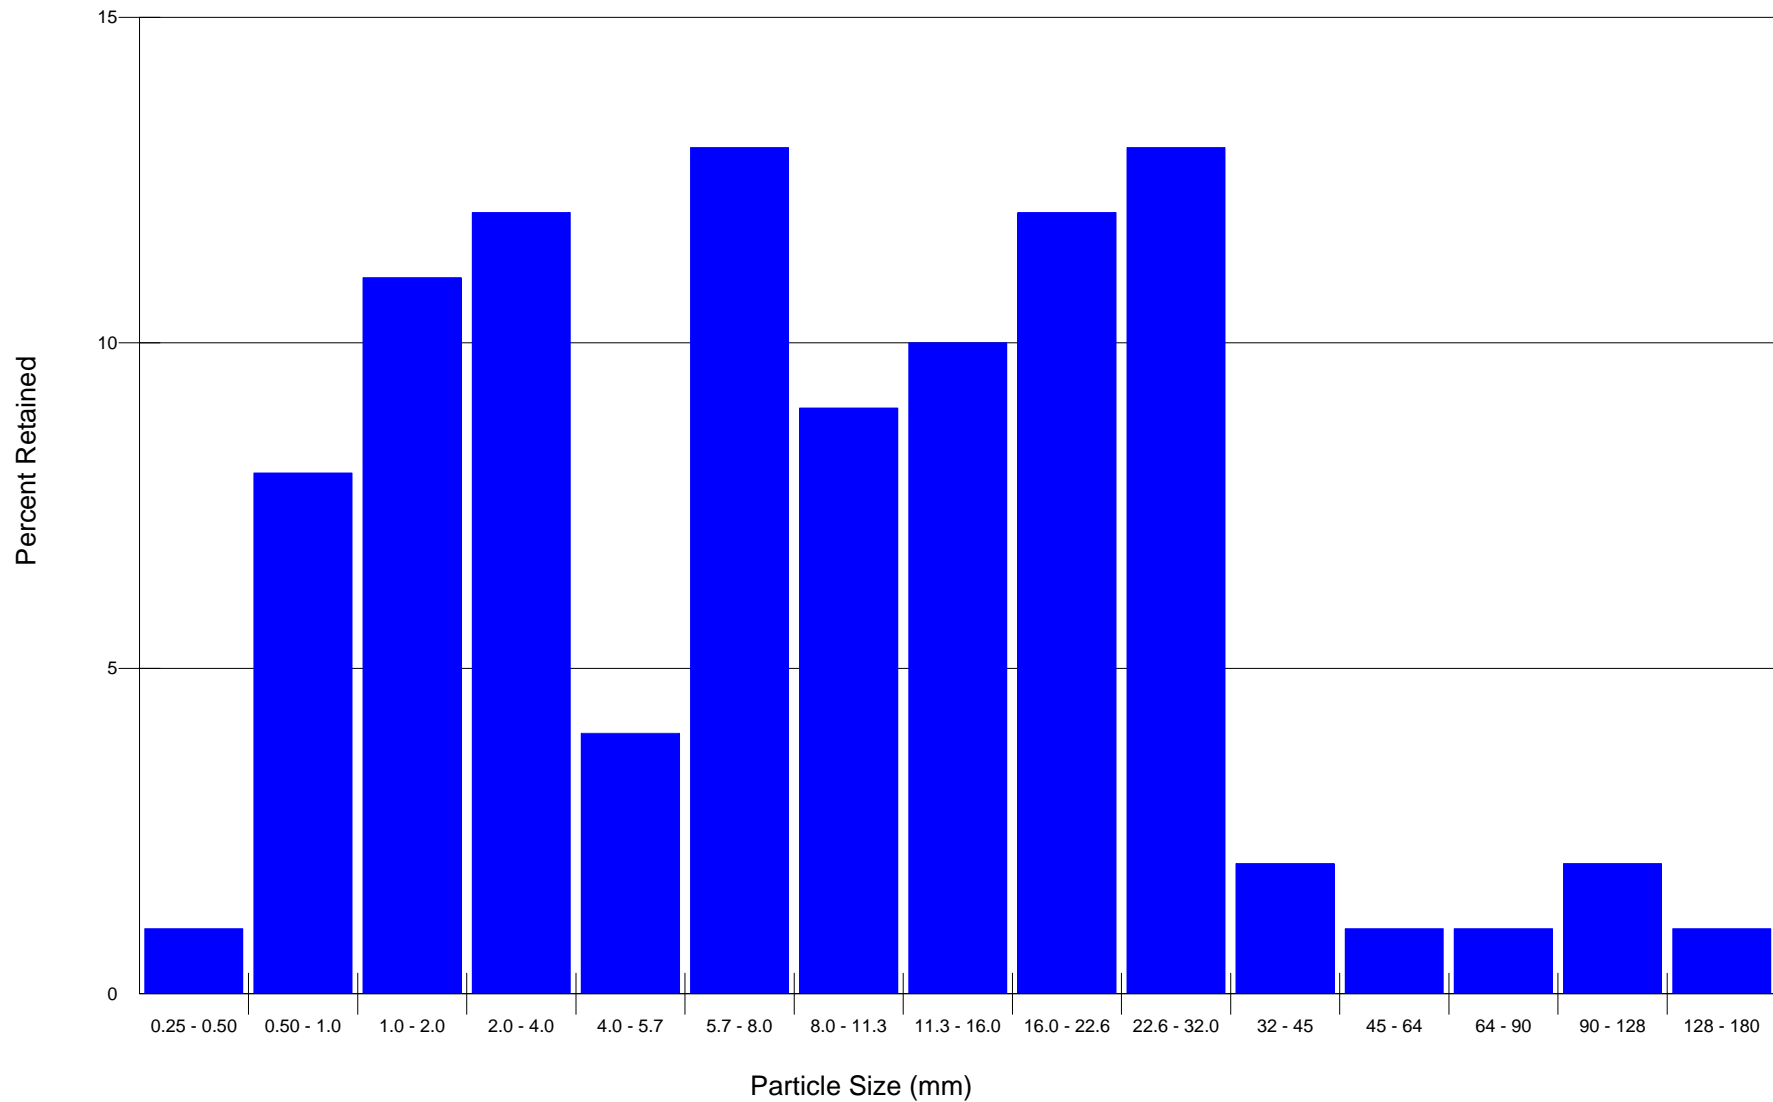

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 8


Riffle

Station 29+35.63

D50: 5.7 mm

D84: 14.72 mm

D95: 24.95 mm

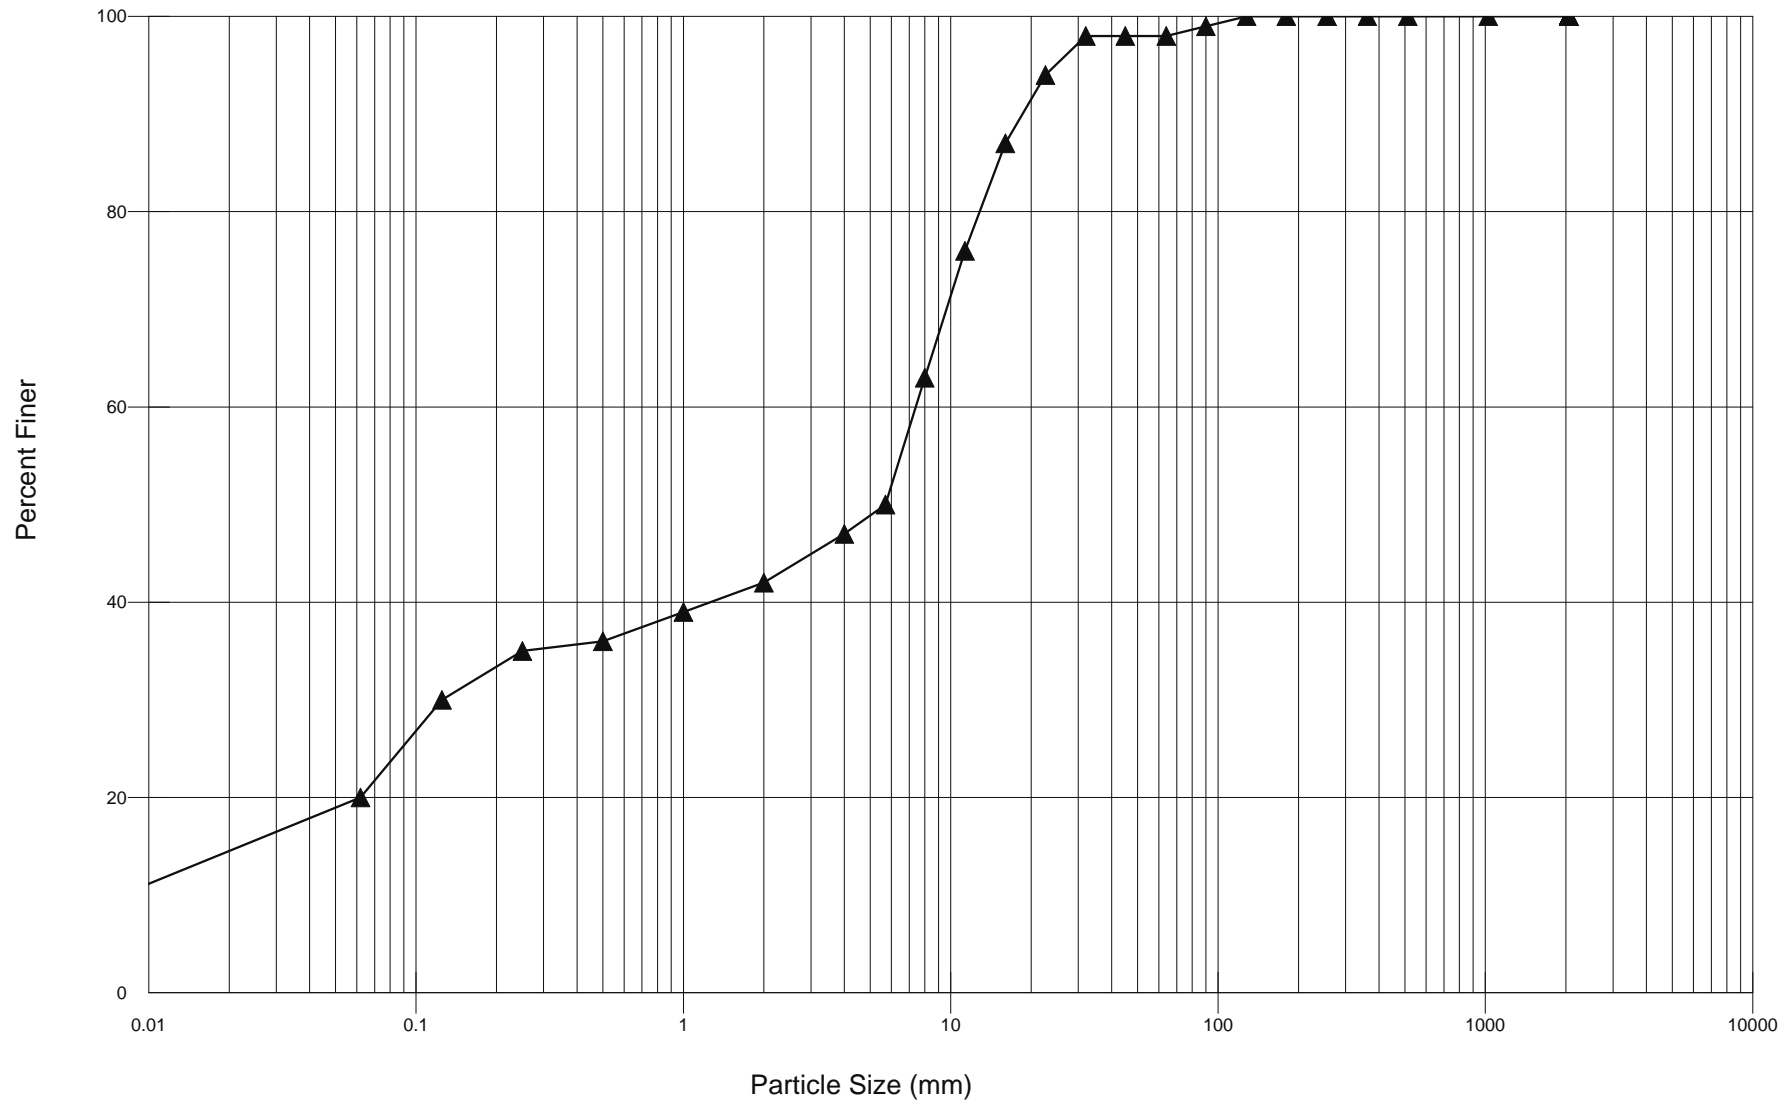

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 8


Riffle

Station 29+35.63

D50: 5.7 mm

D84: 14.72 mm

D95: 24.95 mm

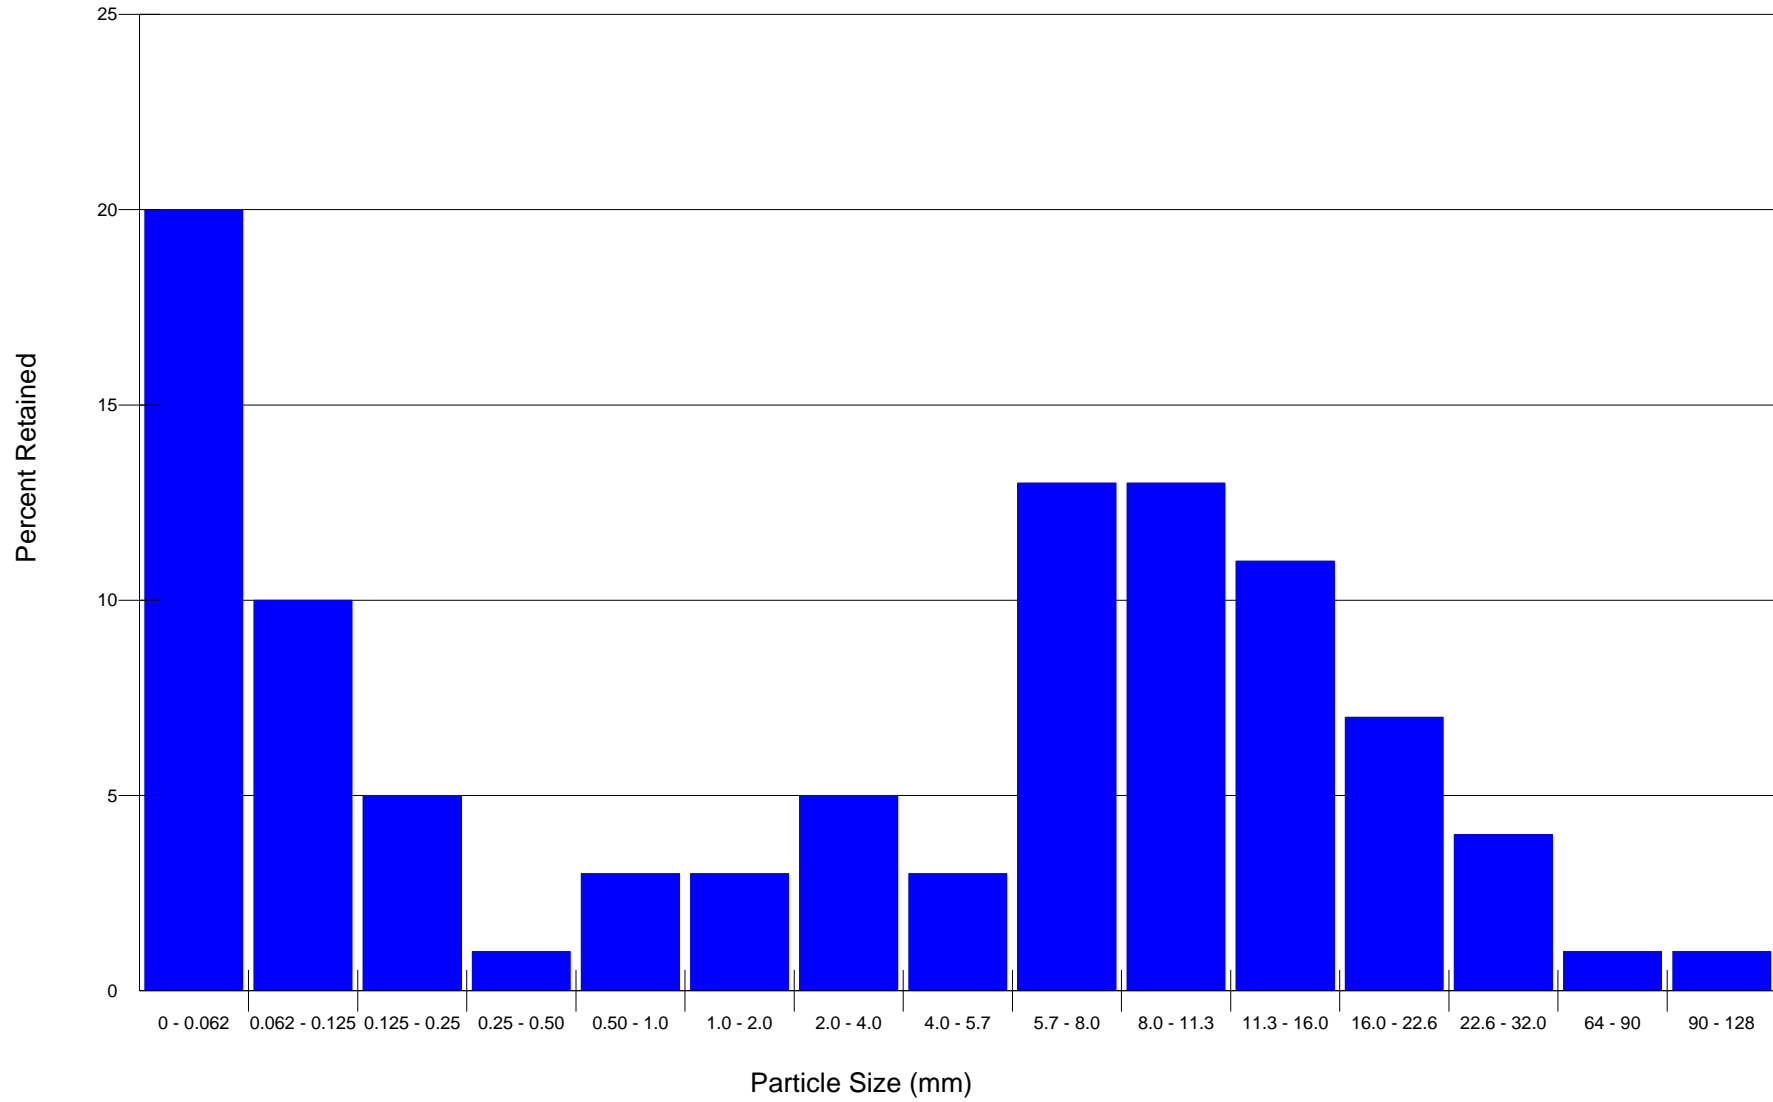

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 9


Riffle

Station 29+57.75


D50: 2.22 mm

D84: 14.83 mm


D95: 90.0 mm

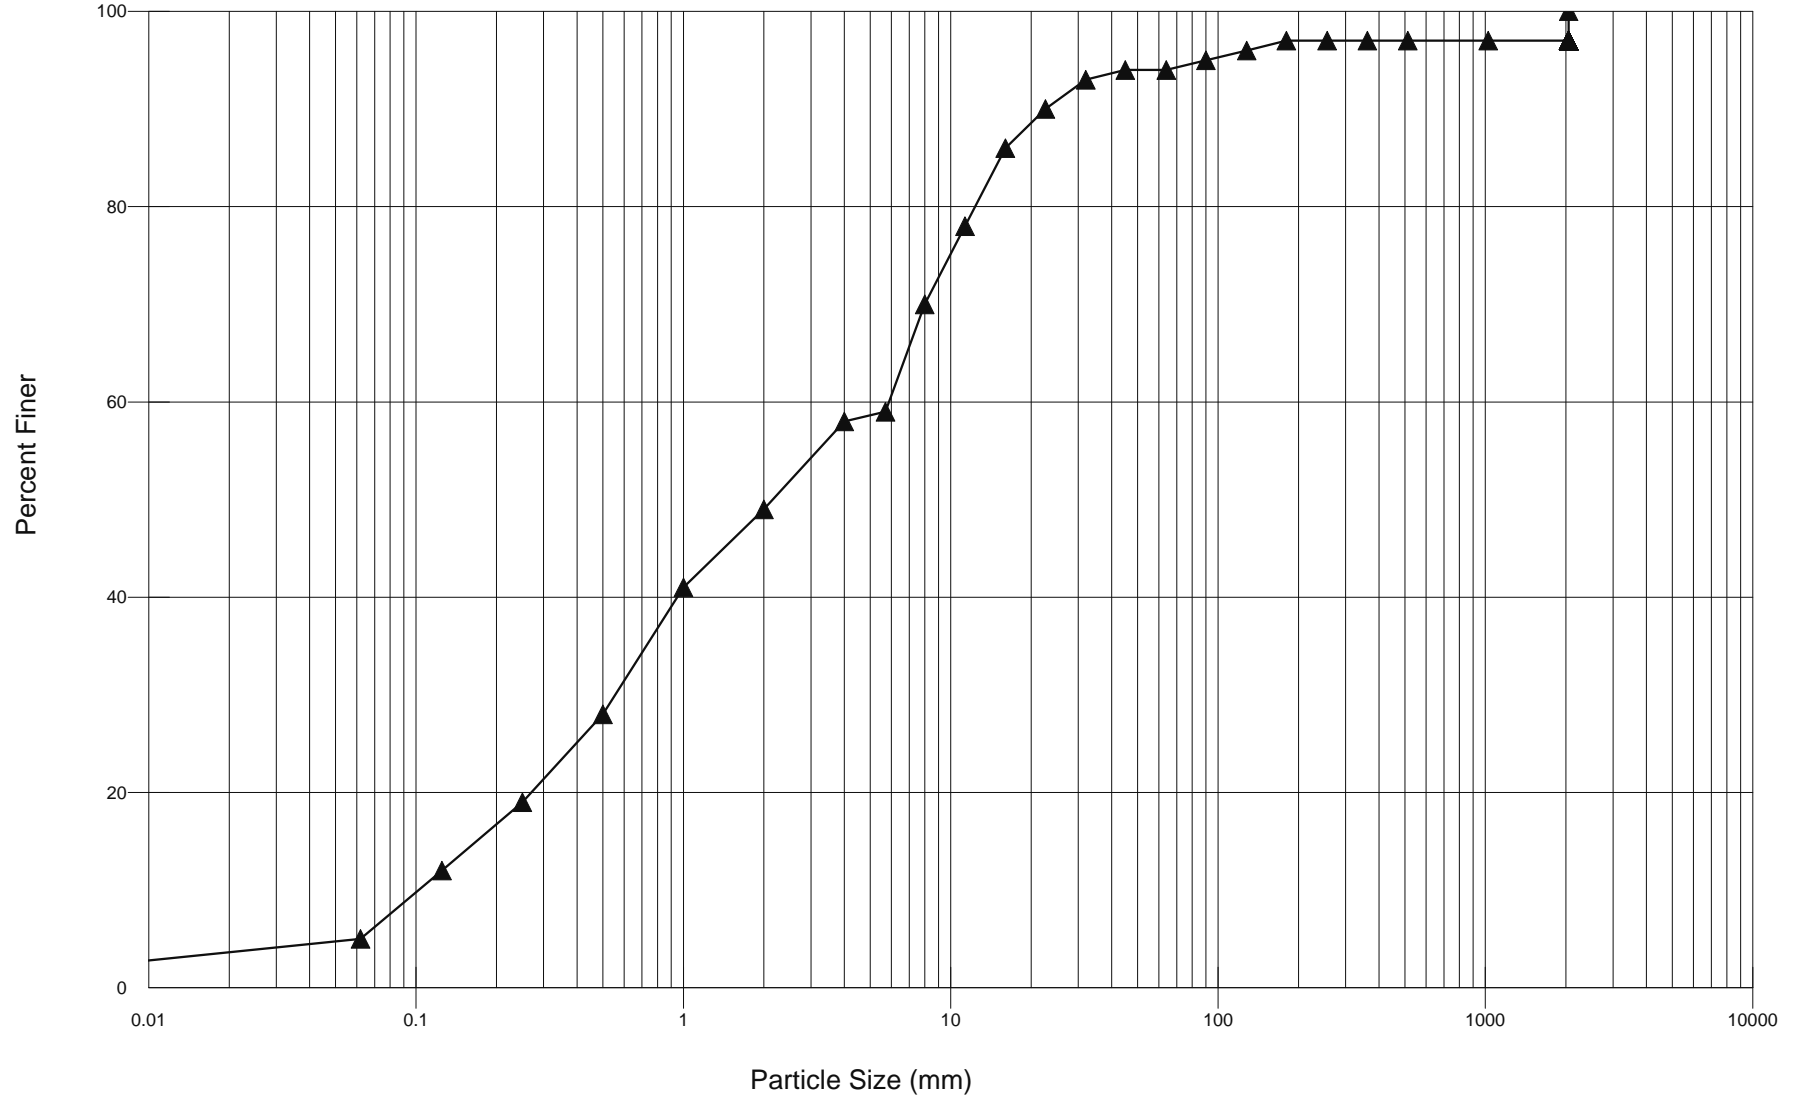

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 9
Riffle
Station 29+57.75
D50: 2.22 mm
D84: 14.83 mm
D95: 90.0 mm

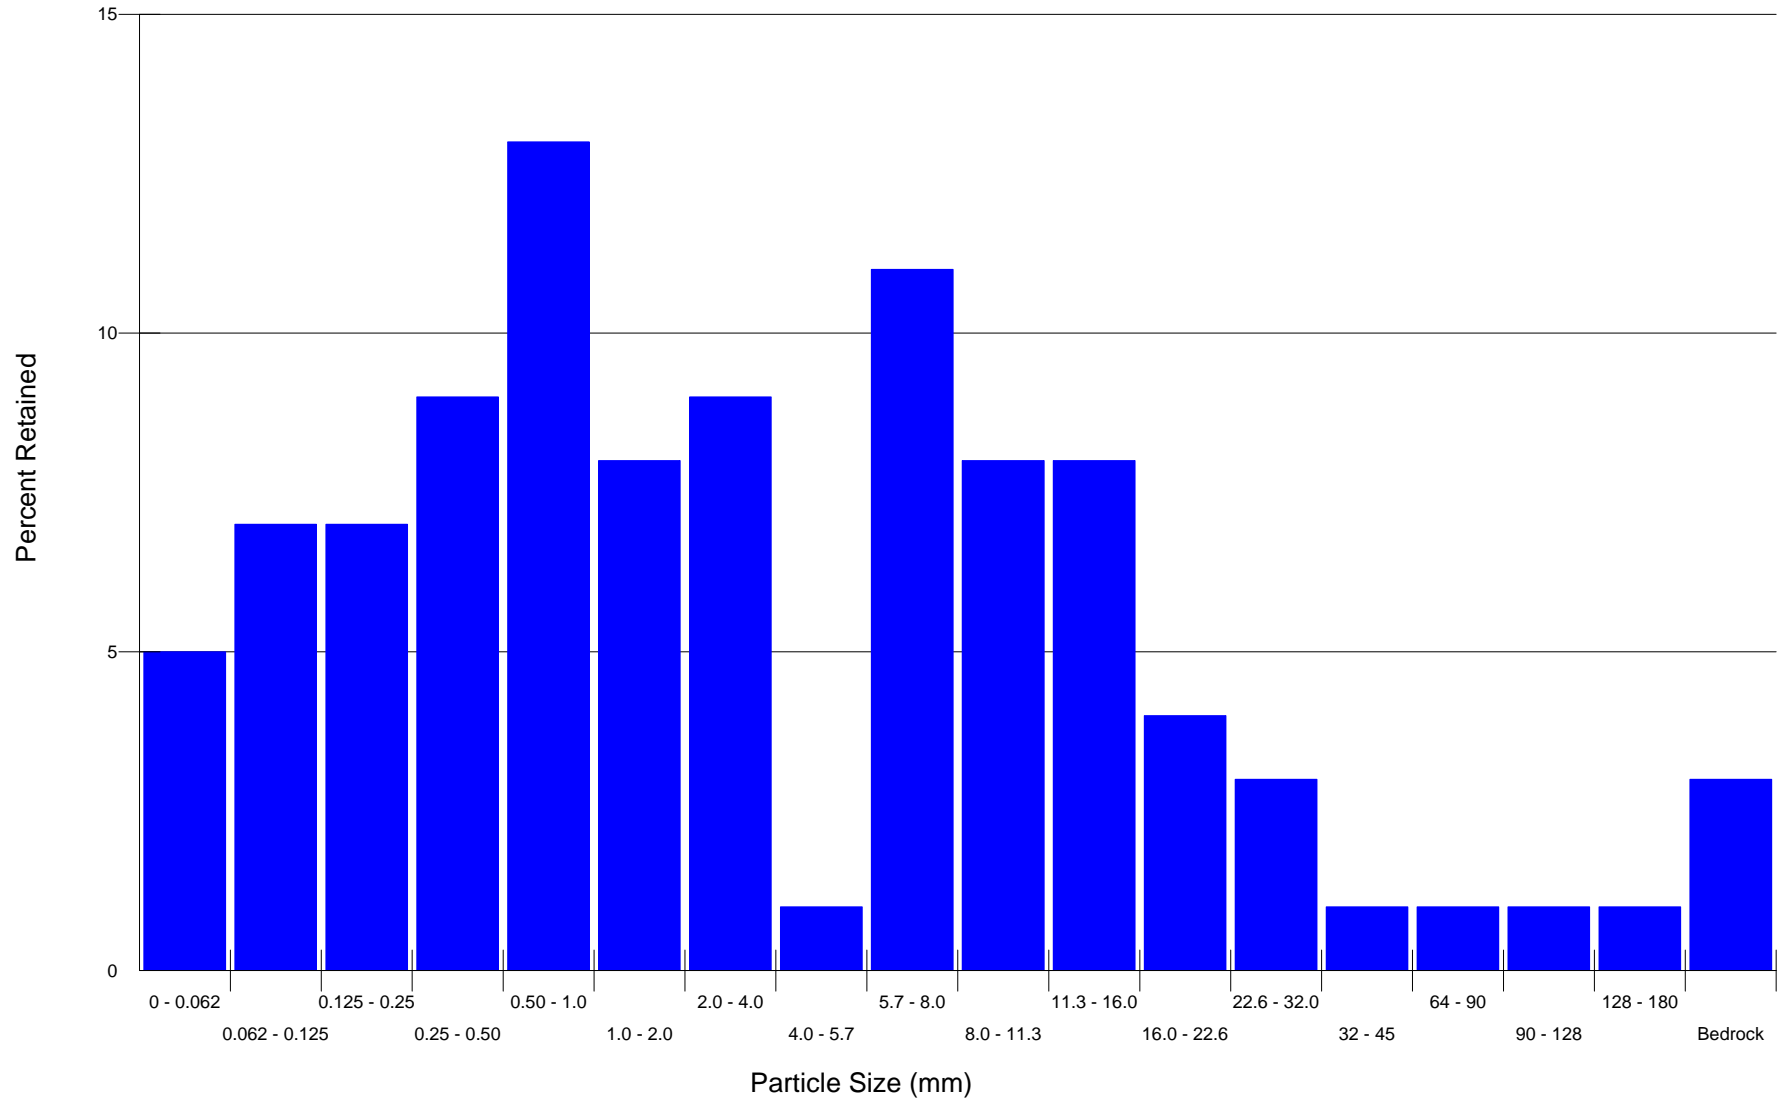

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 6, XS 10
Riffle
Station 30+56.75
D50: 3.50 mm
D84: 11.97 mm
D95: 28.87 mm

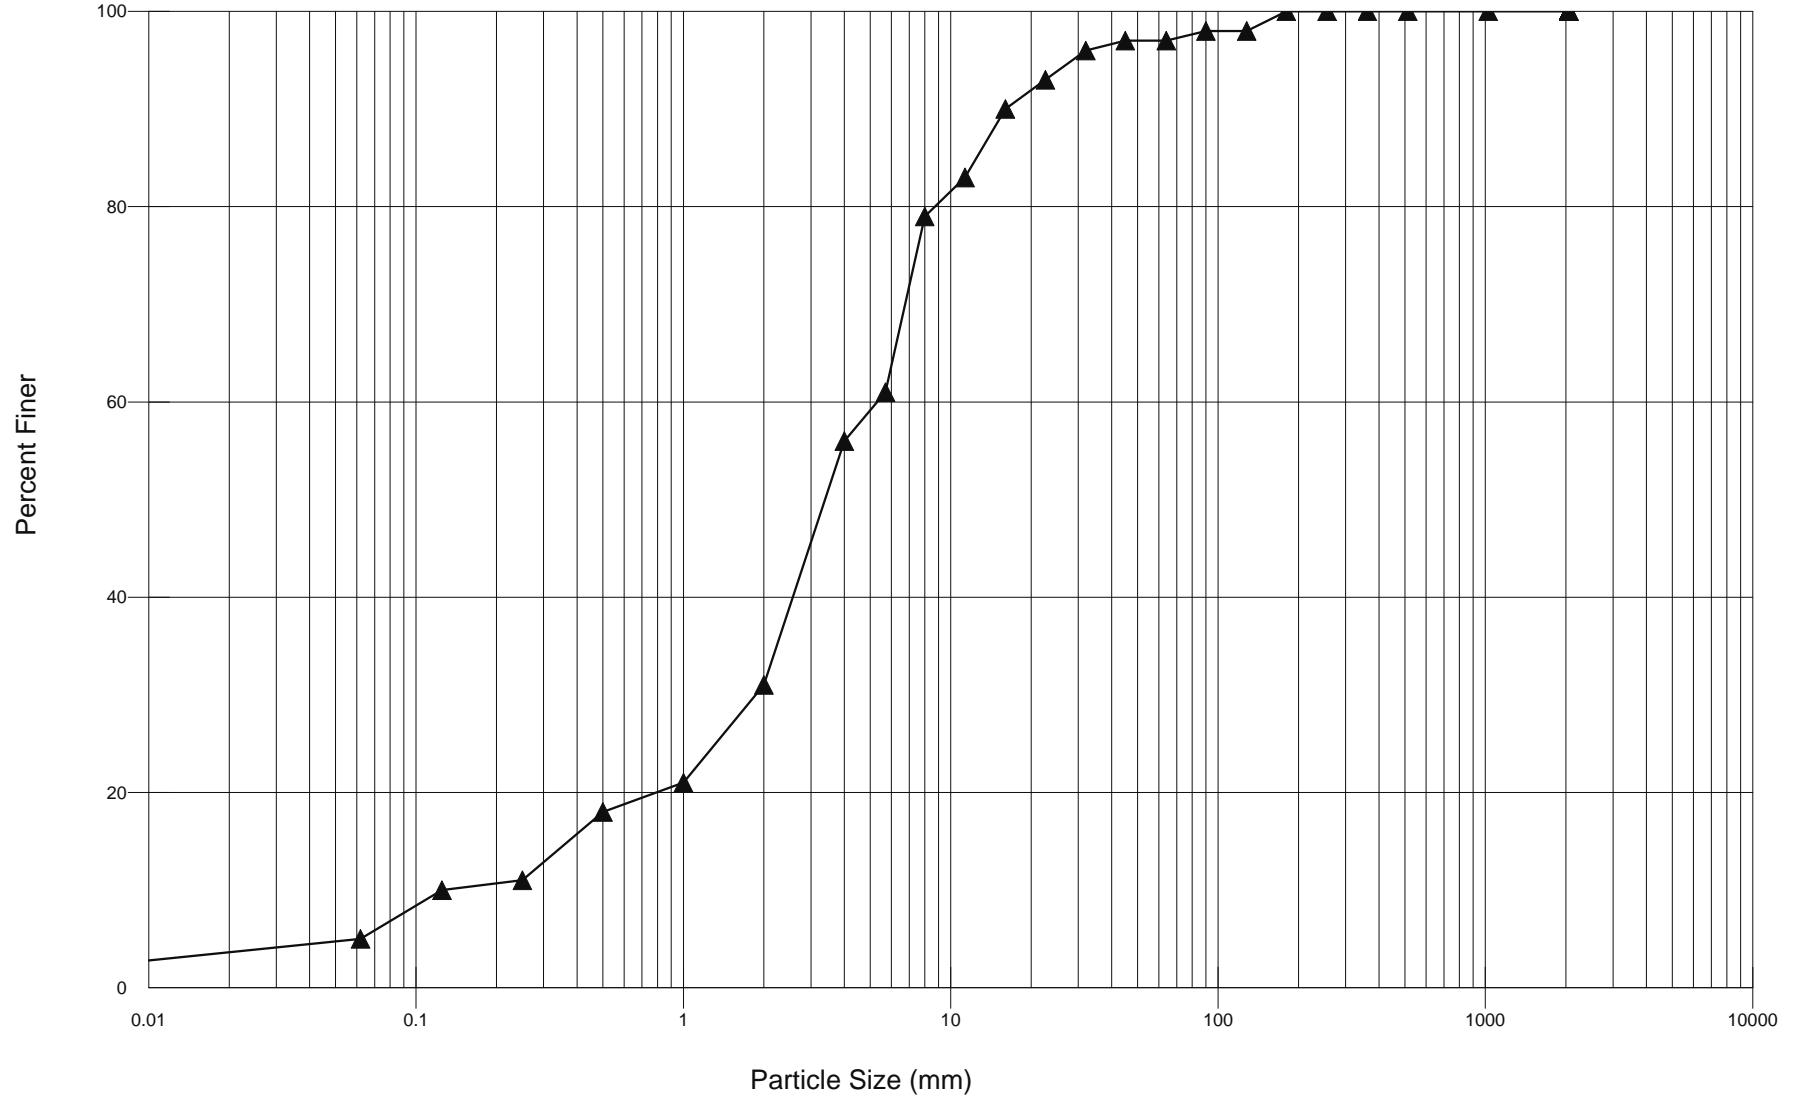

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 6, XS 10


Riffle

Station 30+56.75


D50: 3.50 mm

D84: 11.97 mm

D95: 28.87 mm

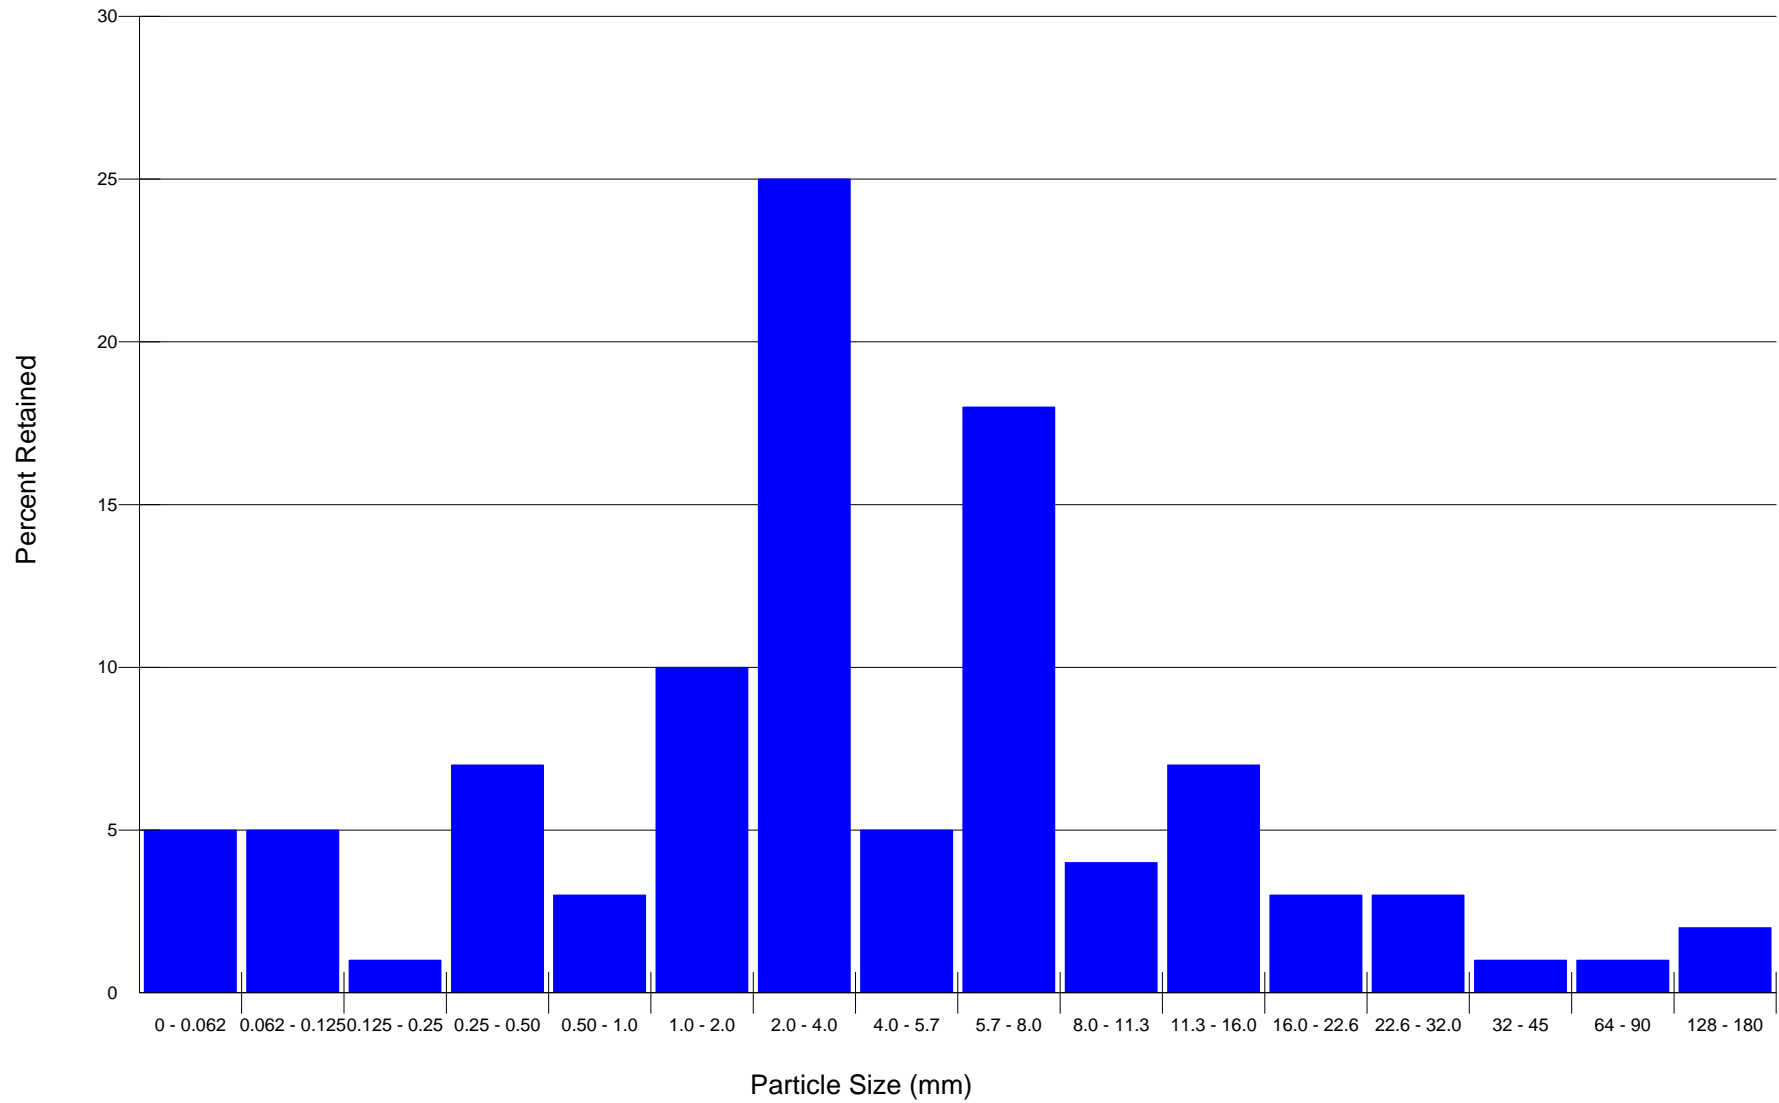

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 12
Riffle
Station 11+03.18
D50: 5.21 mm
D84: 25.73 mm
D95: 90 mm

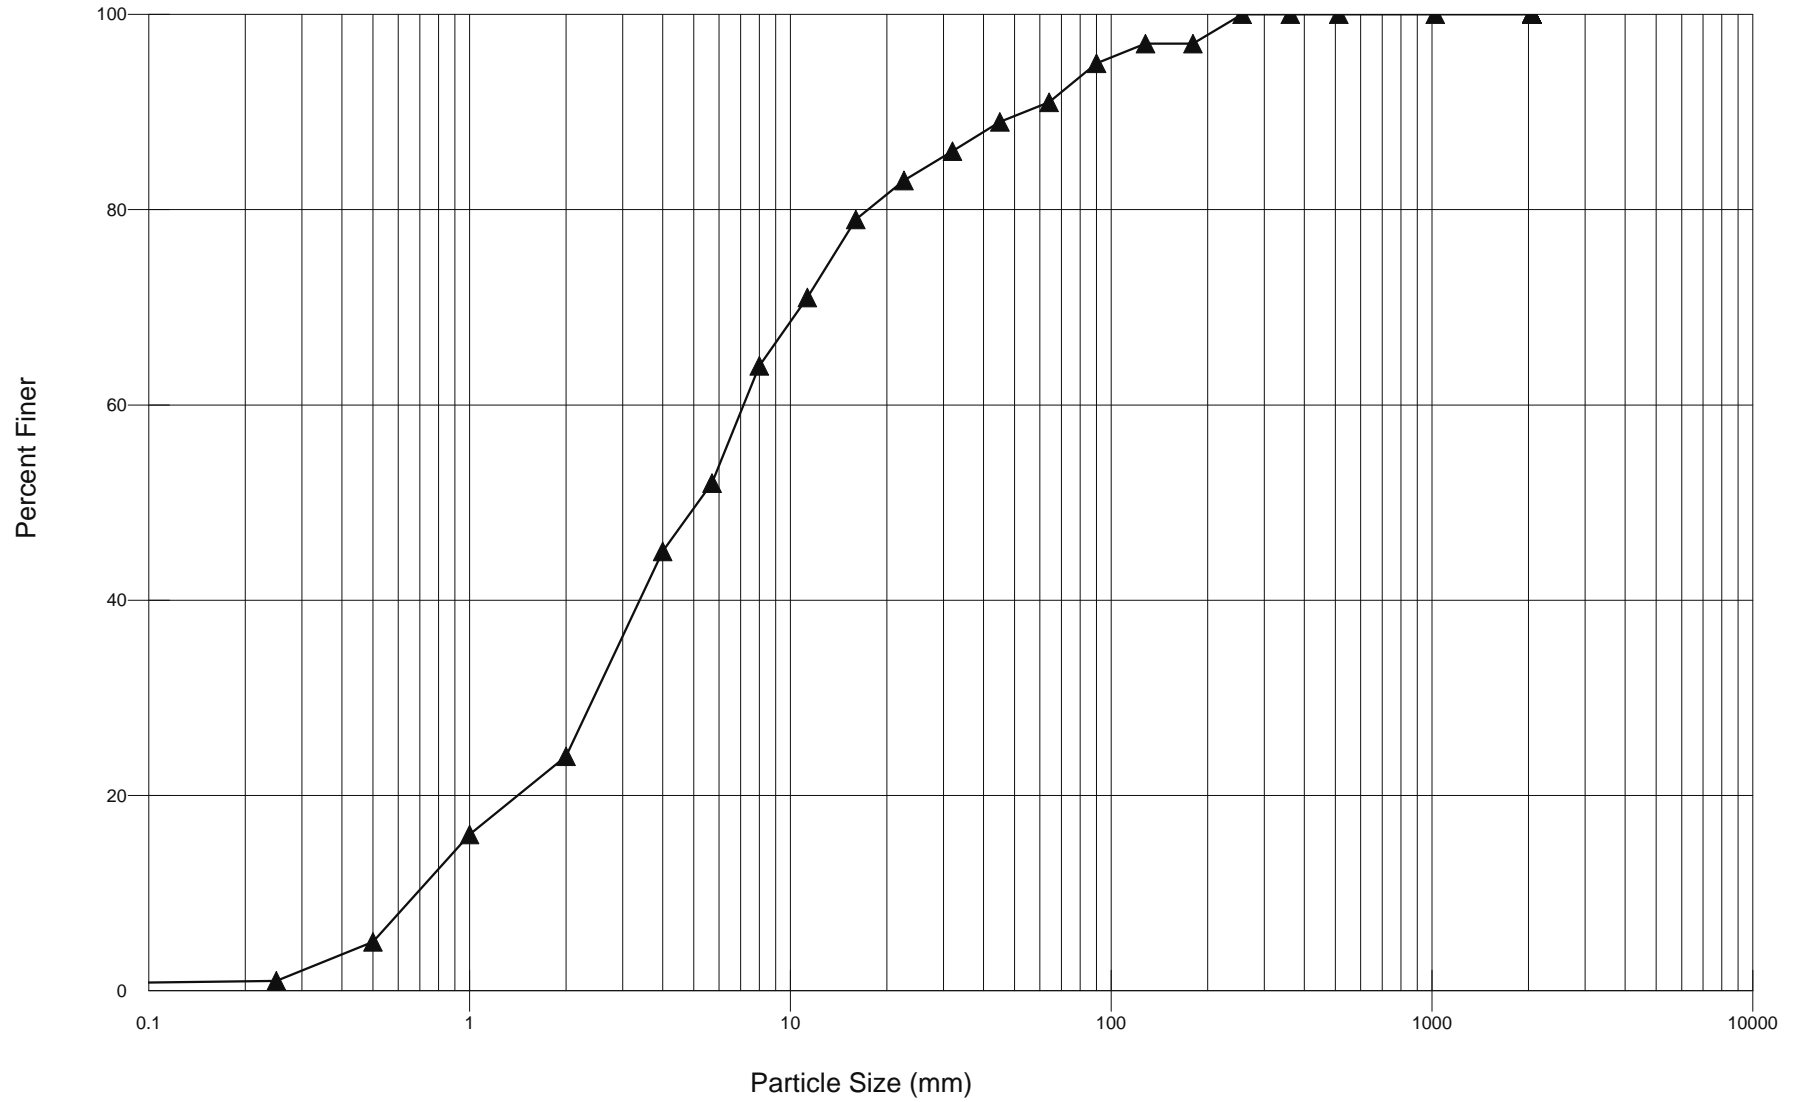

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 2, XS 12


Riffle

Station 11+03.18


D50: 5.21 mm

D84: 25.73 mm

D95: 90 mm

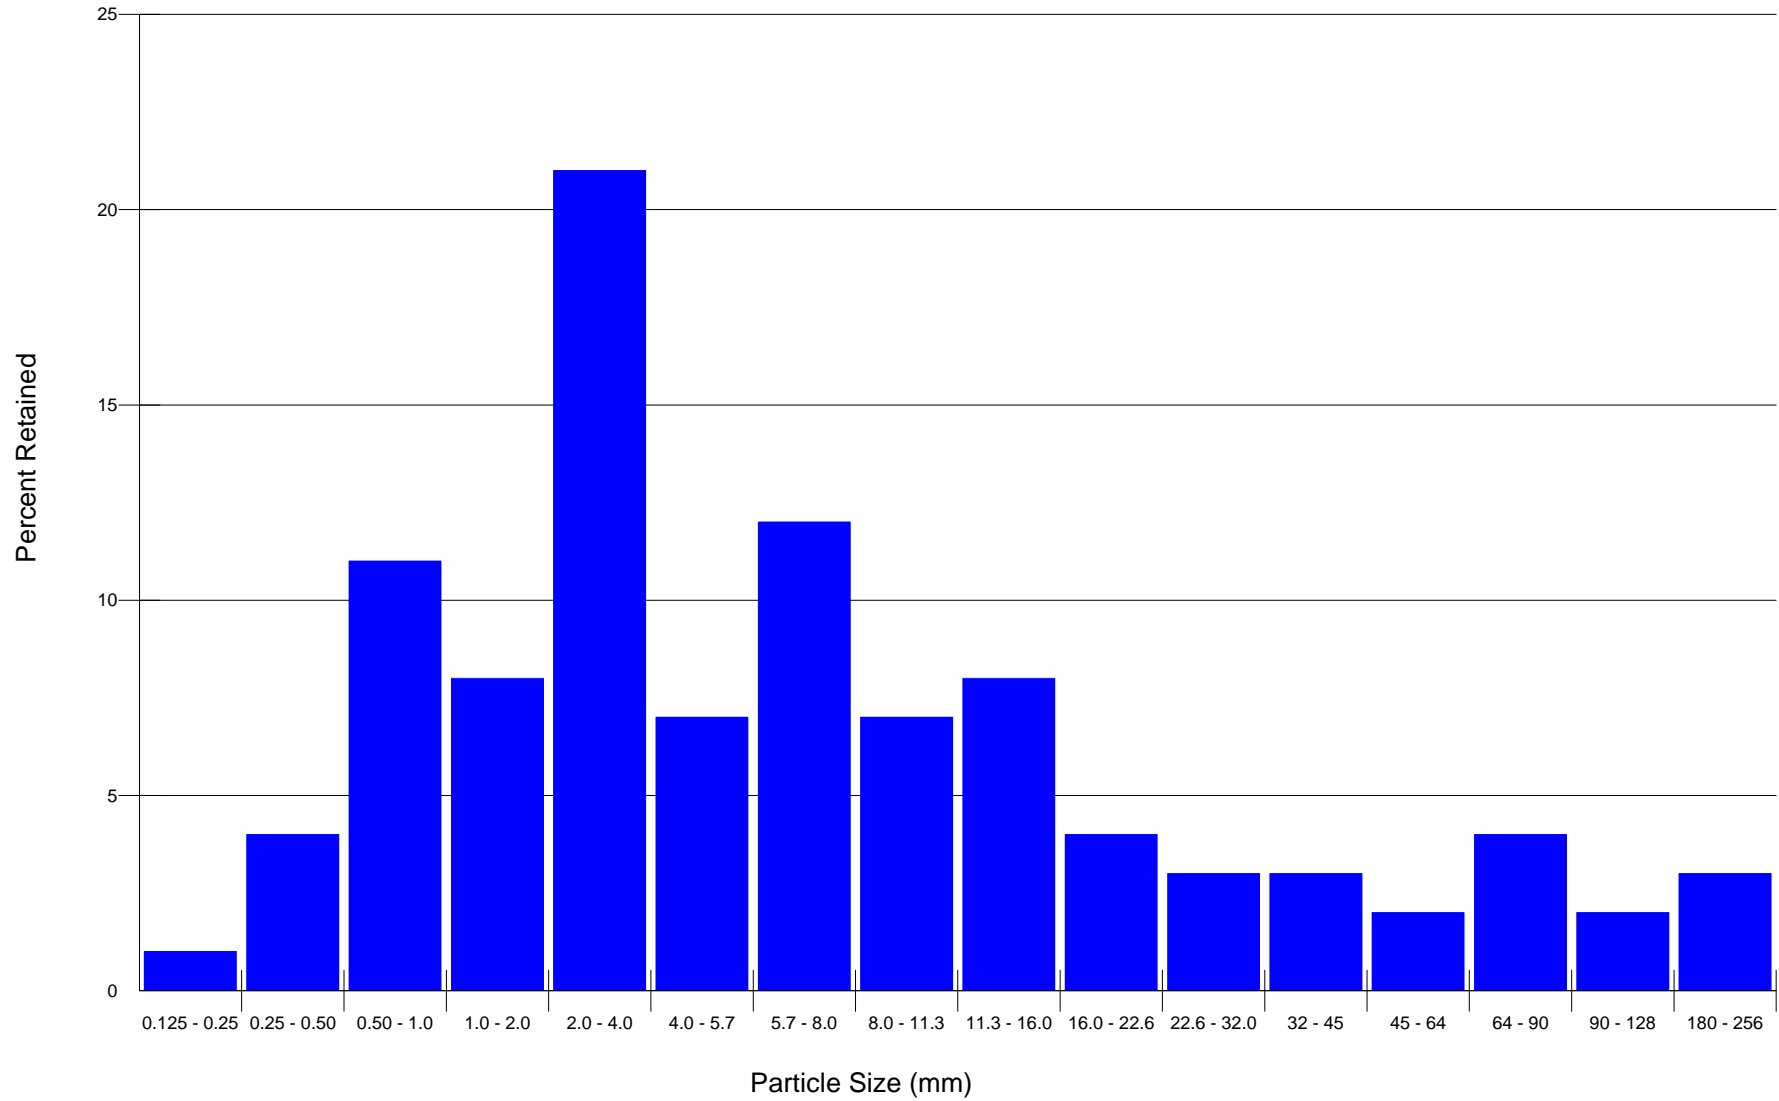

Little Alamance Creek (Burlington Park) Stream Restoration
EEP No. 92372
Reach 2, XS 14
Riffle
Station 12+50.43
D50: 3.3 mm
D84: 10.83 mm
D95: 27.3 mm

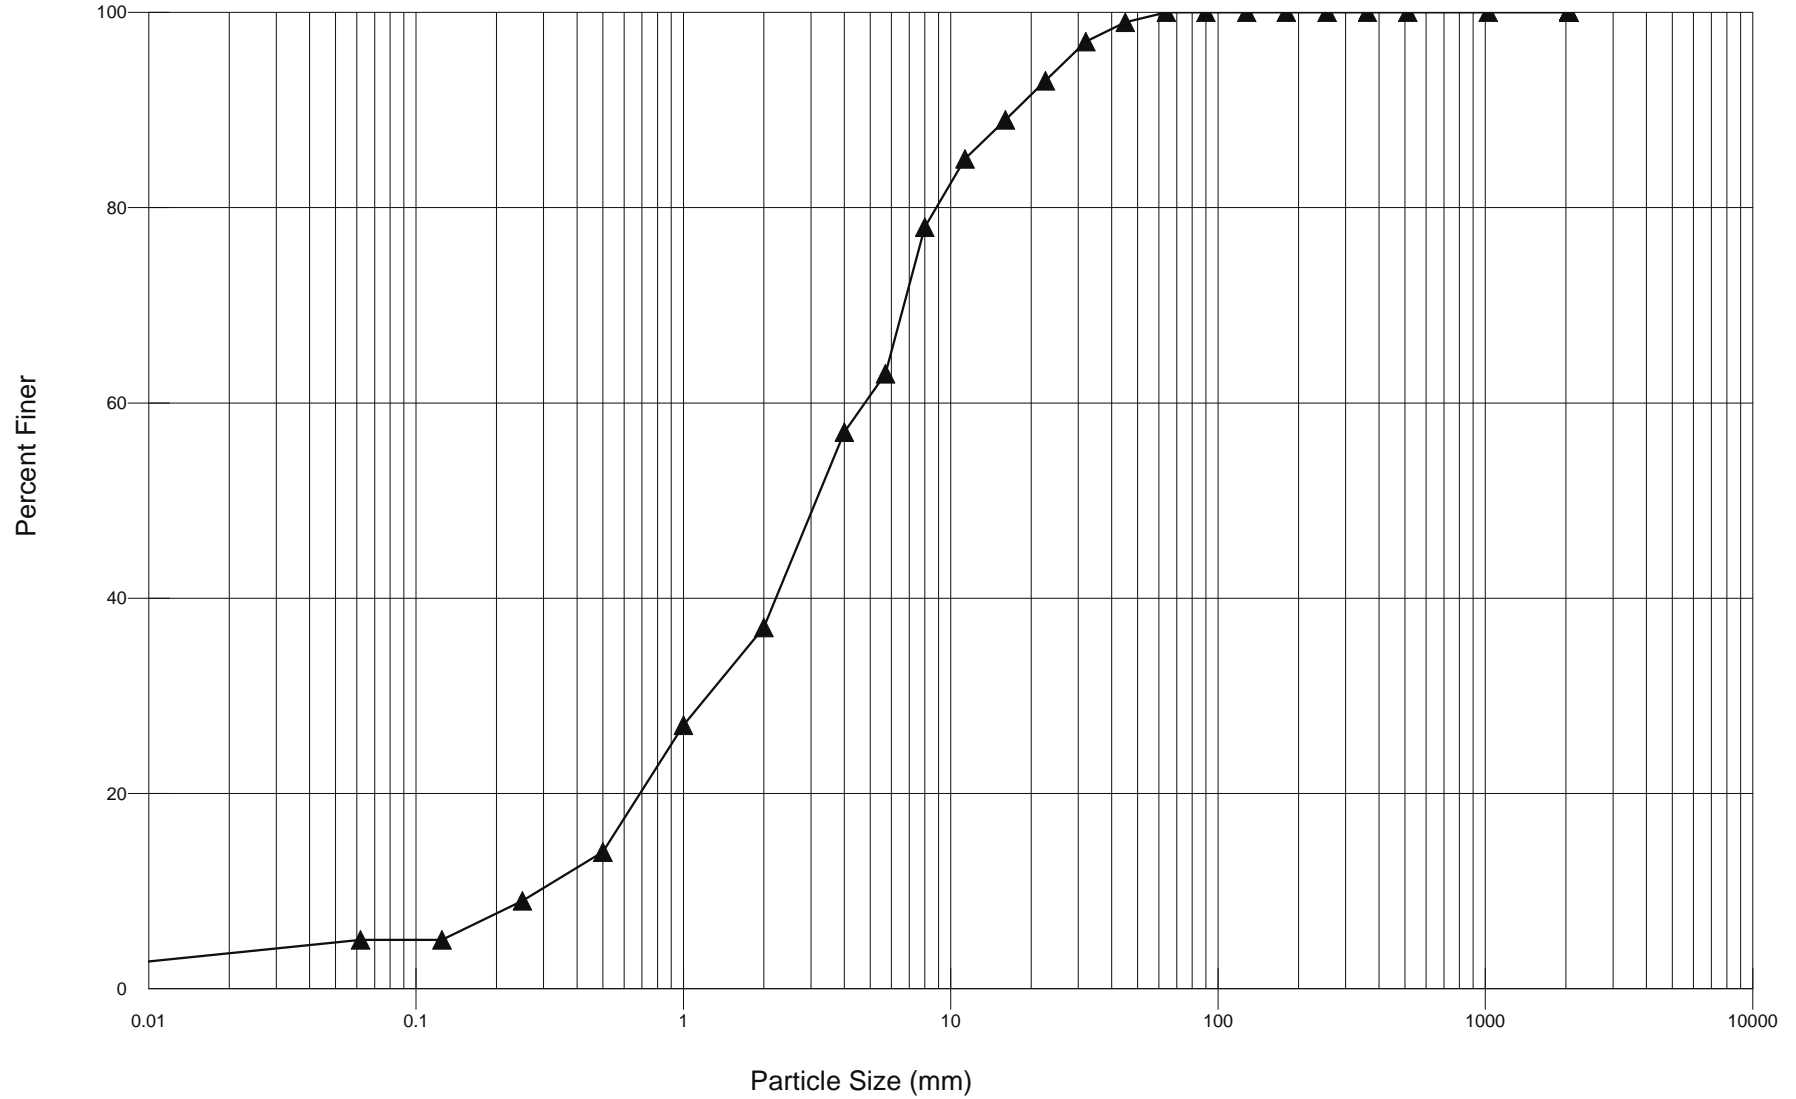

Little Alamance Creek (Burlington Park) Stream Restoration

EEP No. 92372

Reach 2, XS 14

Riffle

Station 12+50.43

D50: 3.3 mm

D84: 10.83 mm

D95: 27.3 mm

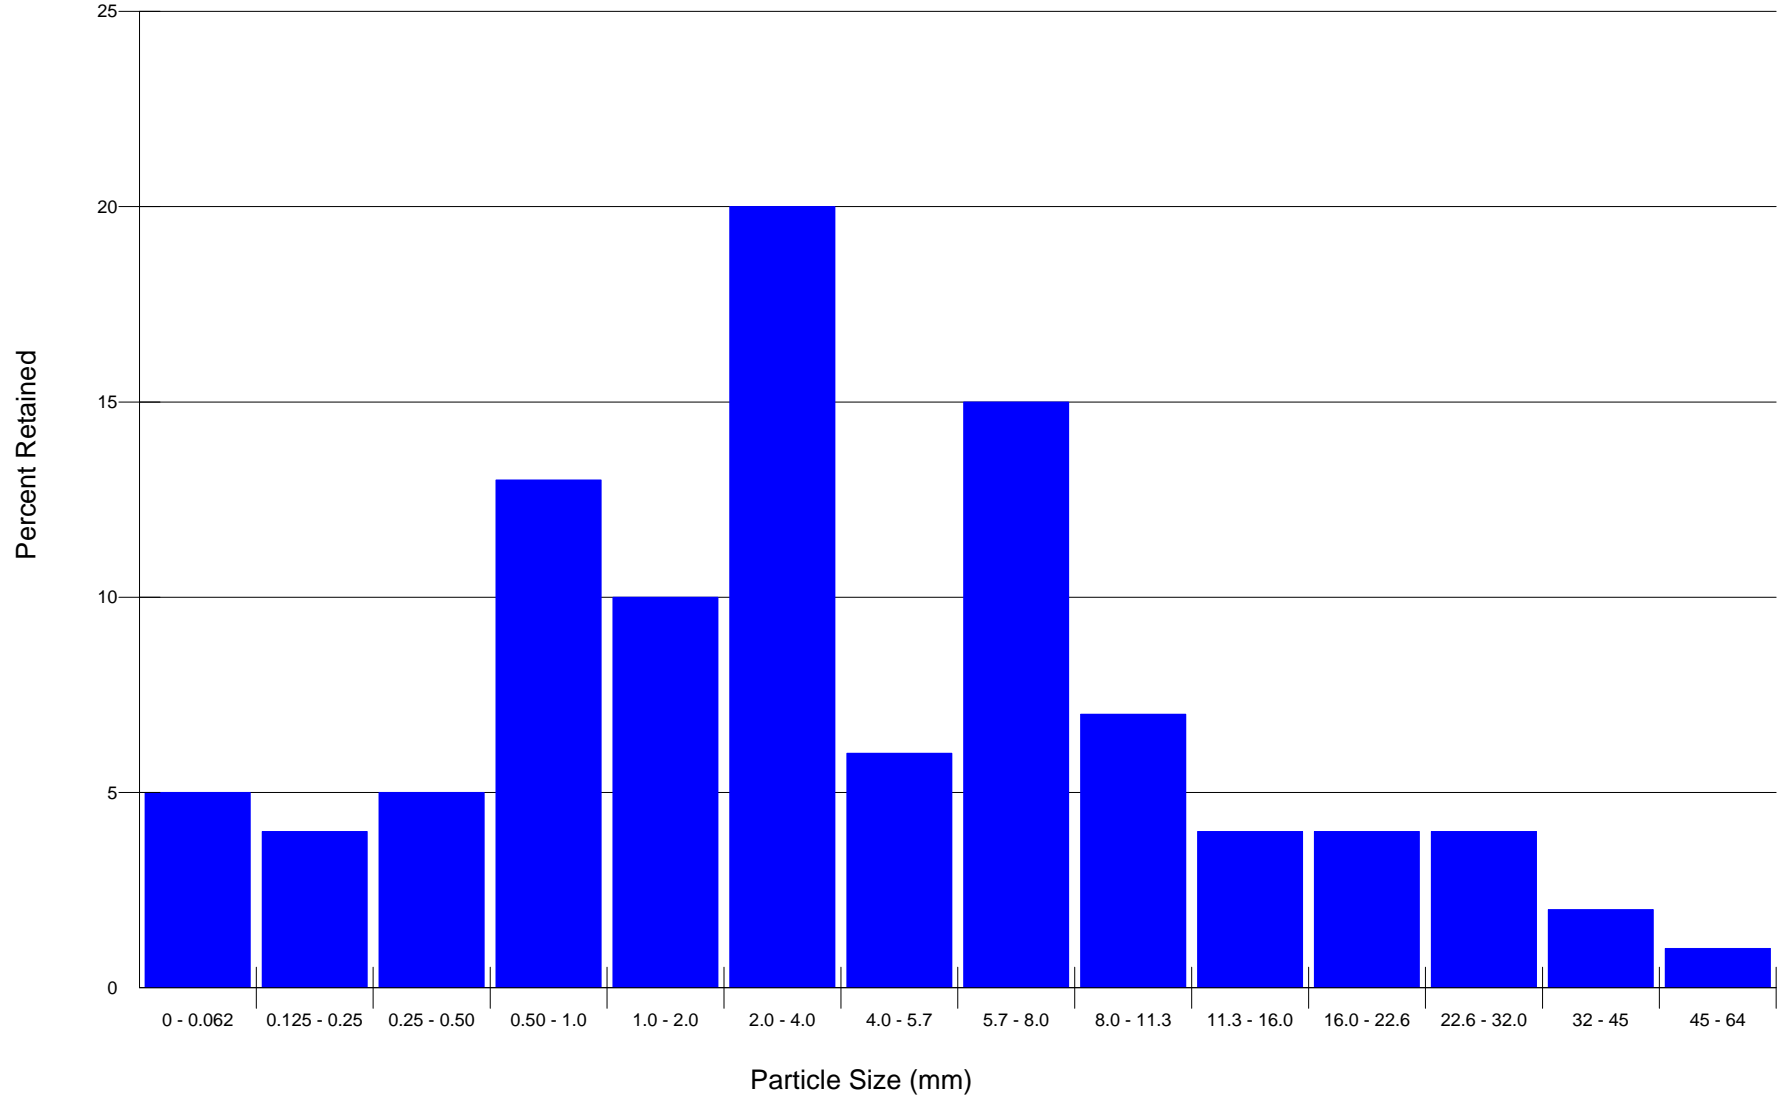


Table 9: Stream Bank Erosion Pin Data Table

Per discussions with NCEEP, bank pins are not required and therefore were not installed by EEE Consulting.

Table 10a. Baseline Stream Data Summary
 Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Mainstem (2275 lf)

Parameter	Gauge ²	Regional Curve			Pre-Existing Condition						Reference Reach(es) Data						Design			Monitoring Baseline						
Dimension and Substrate - Riffle Only		LL	UL	Eq.	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Med	Max	Min	Mean	Med	Max	SD ⁵	n	
Bankfull Width (ft)					31.8	36.2		42.5				15.1						36.2		19.3	26.3		36.6			
Floodprone Width (ft)					70	94		120				30						>80		47.2	52.7		65.7			
Bankfull Mean Depth (ft)					2.2	2.6		2.9				1.6						2.6		2.09	2.53		3.08			
¹ Bankfull Max Depth (ft)					3.9	4		4.1				2.6						4		2.96	3.61		4.6			
Bankfull Cross Sectional Area (ft ²)					79.3	95		125				24.3						95		40.83	68.78		112.77			
Width/Depth Ratio					11.6	14		17				9.3						13.8		7.85	10.31		12.26			
Entrenchment Ratio					2.1	2.6		3.8				2						>2.2		1.645	2.079		2.488			
¹ Bank Height Ratio					1	1.2		1.4				1						1		0.32	0.66		0.83			
Profile																										
Riffle Length (ft)																				62	159.33	137.16	353.24	119.9	5	
Riffle Slope (ft/ft)					0.003	0.013		0.025										0.003	0.013	0.025	0.0001	0.003326	0.00345	0.00983	0.0033	5
Pool Length (ft)					107.9	293.7		505.4										107.9	293.7	505.4	37.58	99.32	90.19	182.26	44.37	14
Pool Max depth (ft)					5.5	6.1		6.9										5.5	6.1	6.9	3.03	4.4	4.525	5.91	0.827	10
Pool Spacing (ft)					313.7	473.1		749.5										313.7	473.1	749.5	48.85	147.39	92.07	347.97	115.5	9
Pattern																										
Channel Beltwidth (ft)					33	70		255										33	70	255	87.3	233		462		
Radius of Curvature (ft)					45	115		220										45	115	220	51.2	118.8		280.7		
Rc:Bankfull width (ft/ft)					1.2	3.2		6.1										1.2	3.2	6.1	2	4.5		10.7		
Meander Wavelength (ft)					227	361		559										227	361	559	436.2	454.6		475.2		
Meander Width Ratio					0.9	1.9		7										0.9	1.9	7	7.7	17.3		24.1		
Transport parameters																										
Reach Shear Stress (competency) lb/ft ²								30										30						0.26		
Max part size (mm) mobilized at bankfull								80																	55.7	
Stream Power (transport capacity) W/m ²																										
Additional Reach Parameters																										
Rosgen Classification								C/E/5/1										C/E4							C 4/1	E4
Bankfull Velocity (fps)								2.5																	2.5	
Bankfull Discharge (cfs)								237.5																		
Valley length (ft)																										
Channel Thalweg length (ft)																										2968.4
Sinuosity (ft)								1.2																	1.2	1.2
Water Surface Slope (Channel) (ft/ft)								0.0024																	0.0024	0.0024
BF slope (ft/ft)																										0.00258
³ Bankfull Floodplain Area (acres)																										
⁴ % of Reach with Eroding Banks																										
Channel Stability or Habitat Metric																										
Biological or Other																										

Shaded cells indicate that these will typically not be filled in.

1 = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile. 2 = For projects with a proximal USGS gauge in-line with the project reach (added bankfull verification - rare).

3. Utilizing survey data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riser/slope.

4 = Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data; 5. Of value/needed only if the n exceeds 3

Table 10a. Baseline Stream Data Summary
 Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Unnamed Tributary (450 lf)

Parameter	Gauge ²	Regional Curve			Pre-Existing Condition						Reference Reach(es) Data						Design			Monitoring Baseline					
		LL	UL	Eq.	Min	Mean	Med	Max	SD ⁵	n	Min	Mean	Med	Max	SD ⁵	n	Min	Med	Max	Min	Mean	Med	Max	SD ⁵	n
Dimension and Substrate - Riffle Only																									
Bankfull Width (ft)					10.9	12		13					15.1				10.9	12	13	9.86	9.89		9.91		
Floodprone Width (ft)					27	33.5		40					30				27	33.5	40	8.5	12.5		16.5		
Bankfull Mean Depth (ft)					1.1	1.3		1.5					1.6				1.1	1.3	1.5	0.86	1.27		1.67		
¹ Bankfull Max Depth (ft)					2	2		2.1					2.6				2	2	2.1	1.43	2.17		2.91		
Bankfull Cross Sectional Area (ft ²)					14.8	15.8		16.7					24.3				14.8	15.8	16.7	8.5	12.5		16.5		
Width/Depth Ratio					7.1	9.3		11.5					9.3				7.1	9.3	11.5	5.9	8.71		11.52		
Entrenchment Ratio					2.1	2.9		3.7					2				2.1	2.9	3.7	2.25	3.38		4.52		
¹ Bank Height Ratio					1	1.2		1.3					1					1		0.99	1.27		2.56		
Profile																									
Riffle Length (ft)																				26.98	41.87		59.91		
Riffle Slope (ft/ft)					0.015	0.025		0.05									0.015	0.025	0.05	0.006	0.01		0.018		
Pool Length (ft)					4	18.2		163									4	18.2	163	12.96	28.2		60.96		
Pool Max depth (ft)						2.4												2.4		0.74	2.06		3.26		
Pool Spacing (ft)					23.4	34.1		54.8									23.4	34.1	54.8	12.52	30.1		60.61		
Pattern																									
Channel Beltwidth (ft)					13.5	24.6		33.7									13.5	24.6	33.7	5.5	10.39		18.97		
Radius of Curvature (ft)					15	29		55									15	29	55	5.22	15.81		31.25		
Rc:Bankfull width (ft/ft)					1.2	2.4		4.6									1.2	2.4	4.6	1.547	1.784		2.02		
Meander Wavelength (ft)					55.8	83.9		111.9									55.8	83.9	111.9	135.7	172.4		209.2		
Meander Width Ratio					4.7	7		9.3									4.7	7	9.3	0.556	1.051		1.918		
Transport parameters																									
Reach Shear Stress (competency) lb/ft ²								0.71											0.71						
Max part size (mm) mobilized at bankfull								48																	
Stream Power (transport capacity) W/m ²																									
Additional Reach Parameters																									
Rosgen Classification								E4/1					C/E4						C4/1				E4		
Bankfull Velocity (fps)								4.4											4.4						
Bankfull Discharge (cfs)								68.7																	
Valley length (ft)																									
Channel Thalweg length (ft)																									
Sinuosity (ft)								1.1											1.1						
Water Surface Slope (Channel) (ft/ft)								0.0095											0.0095						
BF slope (ft/ft)																									
³ Bankfull Floodplain Area (acres)																									
⁴ % of Reach with Eroding Banks																									
Channel Stability or Habitat Metric																									
Biological or Other																									

Shaded cells indicate that these will typically not be filled in.

1 = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile. 2 = For projects with a proximal USGS gauge in-line with the project reach (added bankfull verification - rare).

3. Utilizing survey data produce an estimate of the bankfull floodplain area in acres, which should be the area from the top of bank to the toe of the terrace riser/slope.

4 = Proportion of reach exhibiting banks that are eroding based on the visual survey for comparison to monitoring data; 5. Of value/needed only if the n exceeds 3

**Table 10b. Baseline Stream Data Summary (Substrate, Bed, Bank, and Hydrologic Containment Parameter Distributions)
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Mainstem (2275 lf)**

Parameter	Pre-Existing Condition						Reference Reach(es) Data						Design						As-built/Baseline					
¹ Ri% / Ru% / P% / G% / S%																								
¹ SC% / Sa% / G% / C% / B% / Be%																								
¹ d16 / d35 / d50 / d84 / d95 / di ^p / di ^{sp} (mm)	0.2	0.7	2.4	138	216																			
² Entrenchment Class <1.5 / 1.5-1.99 / 2.0-4.9 / 5.0-9.9 / >10																								
³ Incision Class <1.2 / 1.2-1.49 / 1.5-1.99 / >2.0																								

Shaded cells indicate that these will typically not be filled in.

1 = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave

2 = Entrenchment Class - Assign/bin the reach footage into the classes indicated and provide the percentage of the total reach footage in each class in the table. This will result from the measured cross-sections as well as visual estimates

3 = Assign/bin the reach footage into the classes indicated and provide the percentage of the total reach footage in each class in the table. This will result from the measured cross-sections as well as the longitudinal profile

Footnotes 2,3 - These classes are loosely built around the Rosgen classification and hazard ranking breaks, but were adjusted slightly to make for easier assignment to somewhat coarser bins based on visual estimates in the field such that measurement of every segment for ER would not be necessary.

The intent here is to provide the reader/consumer of design and monitoring information with a good general sense of the extent of hydrologic containment in the pre-existing and the rehabilitated states as well as comparisons to the reference distributions.

ER and BHR have been addressed in prior submissions as a subsample (cross-sections as part of the design survey), however, these subsamples have often focused entirely on facilitating design without providing a thorough pre-construction distribution of these parameters, leaving the reader/consumer with a sample that is weighted heavily on the stable sections of the reach. This means that the distributions for these parameters should include data from both the cross-section surveys and the longitudinal profile and in the case of ER, visual estimates. For example, the typical longitudinal profile permits sampling of the BHR at riffles beyond those subject to cross-sections and therefore can be readily integrated and provide a more complete sample distribution for these parameters, thereby providing the distribution/coverage necessary to provide meaningful comparisons.

**Table 10b. Baseline Stream Data Summary (Substrate, Bed, Bank, and Hydrologic Containment Parameter Distributions)
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Unnamed Tributary (450 lf)**

Parameter	Pre-Existing Condition						Reference Reach(es) Data						Design						As-built/Baseline					
¹ Ri% / Ru% / P% / G% / S%																								
¹ SC% / Sa% / G% / C% / B% / Be%																								
¹ d16 / d35 / d50 / d84 / d95 / di ^p / di ^{sp} (mm)	0.2	0.5	3.4	19	53																			
² Entrenchment Class <1.5 / 1.5-1.99 / 2.0-4.9 / 5.0-9.9 / >10																								
³ Incision Class <1.2 / 1.2-1.49 / 1.5-1.99 / >2.0																								

Shaded cells indicate that these will typically not be filled in.

1 = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave

2 = Entrenchment Class - Assign/bin the reach footage into the classes indicated and provide the percentage of the total reach footage in each class in the table. This will result from the measured cross-sections as well as visual estimates

3 = Assign/bin the reach footage into the classes indicated and provide the percentage of the total reach footage in each class in the table. This will result from the measured cross-sections as well as the longitudinal profile

Footnotes 2,3 - These classes are loosely built around the Rosgen classification and hazard ranking breaks, but were adjusted slightly to make for easier assignment to somewhat coarser bins based on visual estimates in the field such that measurement of every segment for ER would not be necessary.

The intent here is to provide the reader/consumer of design and monitoring information with a good general sense of the extent of hydrologic containment in the pre-existing and the rehabilitated states as well as comparisons to the reference distributions.

ER and BHR have been addressed in prior submissions as a subsample (cross-sections as part of the design survey), however, these subsamples have often focused entirely on facilitating design without providing a thorough pre-construction distribution of these parameters, leaving the reader/consumer with a sample that is weighted heavily on the stable sections of the reach. This means that the distributions for these parameters should include data from both the cross-section surveys and the longitudinal profile and in the case of ER, visual estimates. For example, the typical longitudinal profile permits sampling of the BHR at riffles beyond those subject to cross-sections and therefore can be readily integrated and provide a more complete sample distribution for these parameters, thereby providing the distribution/coverage necessary to provide meaningful comparisons.

**Table 11a. Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Mainstem (2275 lf)**

	Cross Section 1 (Riffle)							Cross Section 2 (Pool)							Cross Section 3 (Pool)							Cross Section 4 (Riffle)							Cross Section 5 (Riffle)						
Based on fixed baseline bankfull elevation¹	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Record elevation (datum) used	NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet						
Bankfull Width (ft)	19.3	19.3						35.68	35.68						32.55	32.55						25.62	25.62						19.43	19.43					
Floodprone Width (ft)	48.01	48.01						73.15	73.2						65.21	65.21						47.46	47.46						47.21	47.21					
Bankfull Mean Depth (ft)	2.46	2.46						3.62	3.62						2.74	2.74						2.09	2.09						2.1	2.1					
Bankfull Max Depth (ft)	3.26	3.26						5.1	5.1						3.87	3.87						2.96	2.96						3.15	3.15					
Bankfull Cross Sectional Area (ft ²)	47.41	47.41						129	129						89.22	89.22						53.43	53.43						40.83	40.83					
Bankfull Width/Depth Ratio	7.85	7.85						9.86	9.86						11.88	11.88						12.26	12.26						9.25	9.25					
Bankfull Entrenchment Ratio	2.49	2.49						2.05	2.05						2	2						1.85	1.85						2.43	2.43					
Bankfull Bank Height Ratio	1.06	1.06						1	1						1	1						1.75	1.75						0.95	0.95					
Cross Sectional Area between end pins (ft ²)	176.8	176.8						257.2	257.2						159.1	159.1						219.1	219.1						141.3	141.3					
d50 (mm)	50.6	50.6						67.5	67.5						58.1	58.1						47.1	47.1						46.2	46.2					
	Cross Section 6 (Pool)							Cross Section 7 (Pool)							Cross Section 8 (Riffle)							Cross Section 9 (Riffle)							Cross Section 10 (Riffle)						
Based on fixed baseline bankfull elevation¹	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Record elevation (datum) used	NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet							NAD 83 NC State Plane feet						
Bankfull Width (ft)	36.6	36.6						31.31	31.31						34.88	34.88						21.79	21.79						30.6	30.6					
Floodprone Width (ft)	60.21	60.21						56.8	56.8						65.72	65.72						47.34	47.34						48.37	48.37					
Bankfull Mean Depth (ft)	3.08	3.08						3.15	3.15						3.08	3.08						2.34	2.34						2.25	2.25					
Bankfull Max Depth (ft)	4.6	4.6						4.21	4.21						4.6	4.6						3.11	3.11						3.81	3.81					
Bankfull Cross Sectional Area (ft ²)	112.8	112.8						98.77	98.77						107.3	107.3						50.91	50.91						68.86	68.86					
Bankfull Width/Depth Ratio	11.88	11.88						9.94	9.94						11.32	11.32						9.31	9.31						13.6	13.6					
Bankfull Entrenchment Ratio	1.65	1.65						1.81	1.81						1.88	1.88						2.17	2.17						1.58	1.58					
Bankfull Bank Height Ratio	1.38	1.38						1.06	1.06						1.02	1.02						1	1						1.28	1.28					
Cross Sectional Area between end pins (ft ²)	295	295						210.6	210.6						271.4	271.4						245.3	245.3						162.4	162.4					
d50 (mm)	62.4	62.4						61.7	61.7						63	63						50.3	50.3						49.9	49.9					

¹ = Widths and depths for monitoring resurvey will be based on the baseline bankfull datum regardless of dimensional/depositional development. Input the elevation used as the datum, which should be consistent and based on the baseline datum established. If the performer has inherited the project and cannot acquire the datum used for prior years this must be discussed with EEP. If this cannot be resolved in time for a given years report submission a footnote in this should be included that states: "It is uncertain if the monitoring datum has been consistent over the monitoring history, which may influence calculated values. Additional data from a prior performer is being acquired to provide confirmation. Values will be recalculated in a future submission based on a consistent datum if determined to be necessary."

**Table 11a. Monitoring Data - Dimensional Morphology Summary (Dimensional Parameters – Cross Sections)
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Unnamed Tributary (450 lf)**

	Cross Section 11 (Pool)							Cross Section 12 (Riffle)							Cross Section 13 (Pool)							Cross Section 14 (Pool)						
Based on fixed baseline bankfull elevation¹	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+	Base	MY1	MY2	MY3	MY4	MY5	MY+
Record elevation (datum) used	NAD 83 NC State Plane feet							NAD 83 State Plane feet							NAD 83 State Plane feet							NAD 83 State Plane feet						
Bankfull Width (ft)	15.57	15.57						9.91	9.91						9.86	9.86						10.08	10.08					
Floodprone Width (ft)	24.74	24.74						22.32	22.32						44.52	44.52						36.5	36.2					
Bankfull Mean Depth (ft)	0.69	0.69						0.86	0.86						1.67	1.67						1.52	1.52					
Bankfull Max Depth (ft)	1.7	1.7						1.43	1.43						2.91	2.91						2.46	2.46					
Bankfull Cross Sectional Area (ft ²)	10.73	10.73						8.5	8.5						16.5	16.5						15.37	15.37					
Bankfull Width/Depth Ratio	22.57	22.57						11.52	11.52						5.9	5.9						6.63	6.63					
Bankfull Entrenchment Ratio	1.59	1.59						2.25	2.25						4.51	4.51						3.59	3.59					
Bankfull Bank Height Ratio	2.34	2.34						1	1						1	1						1.19	1.19					
Cross Sectional Area between end pins (ft ²)	113.4	113.4						76.3	76.3						133.6	133.6						60.3	60.3					
d50 (mm)	73.7	73.7						85.8	85.8						124.1	124.1						124.8	124.8					

¹ = Widths and depths for monitoring resurvey will be based on the baseline bankfull datum regardless of dimensional/depositional development. Input the elevation used as the datum, which should be consistent and based on the baseline datum established. If the performer has inherited the project and cannot acquire for prior years this must be discussed with EEP. If this cannot be resolved in time for a given years report submission a footnote in this should be included that states: "It is uncertain if the monitoring datum has been consistent over the monitoring history, which may influence calculated. Additional data from a prior performer is being acquired to provide confirmation. Values will be recalculated in a future submission based on a consistent datum if determined to be necessary."

**Exhibit Table 11b. Monitoring Data - Stream Reach Data Summary
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Mainstem (2275 lf)**

Parameter	Baseline						MY-1						MY-2						MY-3						MY-4						MY-5					
	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n
Dimension and Substrate - Riffle only																																				
Bankfull Width (ft)	19.3	26.3		36.6			19.3	26.3		36.6																										
Floodprone Width (ft)	47.2	52.7		65.7			47.2	52.7		65.7																										
Bankfull Mean Depth (ft)	2.09	2.53		3.08			2.09	2.53		3.08																										
¹ Bankfull Max Depth (ft)	2.96	3.61		4.6			2.96	3.61		4.6																										
Bankfull Cross Sectional Area (ft ²)	40.83	68.78		112.77			40.83	68.78		112.77																										
Width/Depth Ratio	7.85	10.31		12.26			7.85	10.31		12.26																										
Entrenchment Ratio	1.645	2.079		2.488			1.645	2.079		2.488																										
¹ Bank Height Ratio	0.32	0.66		0.83			0.32	0.66		0.83																										
Profile																																				
Riffle Length (ft)	62	159.33	137.16	353.24	119.9	5	62	159.33	137.16	353.24	119.9	5																								
Riffle Slope (ft/ft)	0.0001	0.003326	0.00345	0.00983	0.0033	5	0.0001	0.003326	0.00345	0.00983	0.0033	5																								
Pool Length (ft)	37.58	99.32	90.19	182.26	44.37	14	37.58	99.32	90.19	182.26	44.37	14																								
Pool Max depth (ft)	3.03	4.4	4.525	5.91	0.8265	10	3.03	4.4	4.525	5.91	0.8265	10																								
Pool Spacing (ft)	48.85	147.39	92.07	347.97	115.45	9	48.85	147.39	92.07	347.97	115.45	9																								
Pattern																																				
Channel Beltwidth (ft)	87.3	233		462																																
Radius of Curvature (ft)	51.2	118.8		280.7																																
Rc:Bankfull width (ft/ft)	2	4.5		10.7																																
Meander Wavelength (ft)	436.2	454.6		475.2																																
Meander Width Ratio	7.7	17.3		24.1																																
Additional Reach Parameters																																				
Rosgen Classification	E4																																			
Channel Thalweg length (ft)																																				
Sinuosity (ft)																																				
Water Surface Slope (Channel) (ft/ft)																																				
BF slope (ft/ft)																																				
³ Ri% / Ru% / P% / G% / S%																																				
³ SC% / Sa% / G% / C% / B% / Be%																																				
³ d16 / d35 / d50 / d84 / d95 /																																				
² % of Reach with Eroding Banks																																				
Channel Stability or Habitat Metric																																				
Biological or Other																																				

Pattern data will not typically be collected unless visual data, dimensional data or profile data indicate significant shifts from baseline

Shaded cells indicate that these will typically not be filled in.
 1 = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile.
 2 = Proportion of reach exhibiting banks that are eroding based on the visual survey from visual assessment table
 3 = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave
 4. = Of value/needed only if the n exceeds 3

**Exhibit Table 11b. Monitoring Data - Stream Reach Data Summary
Little Alamance Creek (Burlington Park) Stream Restoration/EEP Number (92372) Unnamed Tributary (450 lf)**

Parameter	Baseline						MY-1						MY-2						MY-3						MY-4						MY-5					
	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n	Min	Mean	Med	Max	SD ⁴	n
Dimension and Substrate - Riffle only																																				
Bankfull Width (ft)	9.86	9.89		9.91			9.86	9.89		9.91																										
Floodprone Width (ft)	8.5	12.5		16.5			8.5	12.5		16.5																										
Bankfull Mean Depth (ft)	0.86	1.27		1.67			0.86	1.27		1.67																										
¹ Bankfull Max Depth (ft)	1.43	2.17		2.91			1.43	2.17		2.91																										
Bankfull Cross Sectional Area (ft ²)	8.5	12.5		16.5			8.5	12.5		16.5																										
Width/Depth Ratio	5.9	8.71		11.52			5.9	8.71		11.52																										
Entrenchment Ratio	2.25	3.38		4.52			2.25	3.38		4.52																										
¹ Bank Height Ratio	0.99	1.27		2.56			0.99	1.27		2.56																										
Profile																																				
Riffle Length (ft)	26.98	41.87		59.91			26.98	41.87		59.91																										
Riffle Slope (ft/ft)	0.006	0.01		0.018			0.006	0.01		0.018																										
Pool Length (ft)	12.96	28.2		60.96			12.96	28.2		60.96																										
Pool Max depth (ft)	0.74	2.06		3.26			0.74	2.06		3.26																										
Pool Spacing (ft)	12.52	30.1		60.61			12.52	30.1		60.61																										
Pattern																																				
Channel Beltwidth (ft)	5.5	10.39		18.97																																
Radius of Curvature (ft)	5.22	15.81		31.25																																
Rc:Bankfull width (ft/ft)	1.547	1.784		2.02																																
Meander Wavelength (ft)	135.7	172.4		209.2																																
Meander Width Ratio	0.556	1.051		1.918																																
Additional Reach Parameters																																				
Rosgen Classification				E 4						E 4																										
Channel Thalweg length (ft)				426.02						426.02																										
Sinuosity (ft)				1.02						1.02																										
Water Surface Slope (Channel) (ft/ft)				0.00758						0.00758																										
BF slope (ft/ft)				0.00728						0.00728																										
³ Ri% / Ru% / P% / G% / S%																																				
³ SC% / Sa% / G% / C% / B% / Be%																																				
³ d16 / d35 / d50 / d84 / d95 /																																				
² % of Reach with Eroding Banks																																				
Channel Stability or Habitat Metric																																				
Biological or Other																																				

Pattern data will not typically be collected unless visual data, dimensional data or profile data indicate significant shifts from baseline

Shaded cells indicate that these will typically not be filled in.
 1 = The distributions for these parameters can include information from both the cross-section surveys and the longitudinal profile.
 2 = Proportion of reach exhibiting banks that are eroding based on the visual survey from visual assessment table
 3 = Riffle, Run, Pool, Glide, Step; Silt/Clay, Sand, Gravel, Cobble, Boulder, Bedrock; dip = max pave, disp = max subpave
 4. = Of value/needed only if the n exceeds 3

Appendix E: Hydrologic Data

Table 12: Verification of Bankfull Events

Figure 9: Monthly Rainfall Data

Insert Table 12: Verification of Bankfull Events

Crest gauges were installed during Monitoring Year 1 field work. No data is available for this report. Data will be available for the Monitoring Year 2 report and the following monitoring years.

LittleAlamance Creek 30-70 Percentile Graph
Burlington, North Carolina
(Source: NOAA Station GHCND:USC00311239)

