

ANNUAL WETLAND MONITORING REPORT YEAR 4 (2008)

SLEEPY CREEK WETLAND AND RIPARIAN BUFFER MITIGATION SITE LENOIR COUNTY, NORTH CAROLINA

Prepared for:

**NORTH CAROLINA DEPARTMENT OF ENVIRONMENT AND NATURAL RESOURCES
ECOSYSTEM ENHANCEMENT PROGRAM
RALEIGH, NORTH CAROLINA**



and


**NORTH CAROLINA DEPARTMENT OF TRANSPORTATION
RALIEGH, NORTH CAROLINA**



Prepared by:



**Restoration Systems, LLC
1101 Haynes Street, Suite 211
Raleigh, North Carolina 27604**



**Axiom Environmental, Inc.
2126 Rowland Pond Drive
Willow Spring, North Carolina 27592**

November 2008

EXECUTIVE SUMMARY

Restoration Systems established the Sleepy Creek Wetland and Riparian Buffer Mitigation Site (Project) in the Coastal Plain region of the Neuse River Basin (United States Geological Survey Hydrologic Unit 03020202). The Project will provide compensatory mitigation for in-kind, unavoidable wetland and riparian buffer impacts associated with development in the river basin. Mitigation generated by this project will be used by the North Carolina Ecosystem Enhancement Program (NCEEP) and North Carolina Department of Transportation (NCDOT) to ensure no net loss of wetland functions associated with transportation improvement projects (TIPs) in the region.

The Project comprises 534 acres within four parcels distributed within the floodplains of Bear Creek and the Neuse River. The 534-acre Project includes a 153.58-acre Core Restoration Site northwest of the Town of LaGrange in Lenoir County and approximately 380 acres of additional wetland management and preservation areas within the Bear Creek/Neuse River regional wetland corridor located near the City of Kinston.

A Detailed Wetland Restoration Plan was completed for the Core Restoration Site in July 2002. The plan outlined methods designed to restore agricultural fields that had been ditched, drained, and cleared for row crop production to pristine riverine wetlands. The plan outlined wetland restoration procedures including 1) ditch/canal backfilling, 2) ditch outlet plugs, 3) slough/drainageway construction, 4) embankment construction, 5) depressional wetland excavation, and 6) drainage control outlets.

The objectives of the Detailed Wetland Restoration Plan included the following.

- Establish a backwater cypress-tupelo swamp,
- Provide a perennial source for groundwater recharge through restored bottomland hardwood forest, and
- Facilitate nutrient reduction goals in the Neuse River Basin.

As constructed, the Core Restoration Site provides 96.4 acres of riverine wetland restoration, 39.2 acres of riverine wetland enhancement, and 18.0 acres of upland riparian buffer. In addition, the three wetland management and preservation areas provide 380 acres of riverine wetland preservation.

The Site achieved the defined (or targeted) success criteria for hydrology for 9 of 13 groundwater gauges within bottomland hardwood areas and all of the groundwater gauges within swamp forest areas in the Fourth Monitoring Year (Year 2008). A total of approximately 30.48 inches of rain was documented near the Site at a rain station in Goldsboro from March to October 2008, which is 5 inches below the 30-year historic (1971-2000) average normal rainfall for the same months (March to October) of 35.1 inches in Goldsboro.

As a whole, vegetation plots across the Site were well above the required 290 stems/acre with an average of 568 tree stems per acre within bottomland hardwood areas and 472 tree stems per acre within swamp forest areas in the Fourth Monitoring Year (Year 2008).

TABLE OF CONTENTS

1.0	INTRODUCTION	1
2.0	MONITORING PROGRAM.....	3
2.1	Wetland Hydrology.....	5
2.1.1	Hydrology Monitoring Procedure	5
2.1.2	Hydrologic Success Criteria.....	5
2.1.3	Hydrological Monitoring Results and Comparison with Success Criteria	6
2.2	Vegetation.....	6
2.2.1	Vegetation Monitoring Procedure	6
2.2.2	Vegetation Success Criteria	7
2.2.3	Vegetation Sampling Results and Comparison to Success Criteria	9
3.0	CONCLUSIONS	9
4.0	REFERENCES	13

LIST OF TABLES

Table 1.	2008 (Year 4) Groundwater Gauge Results	6
Table 2.	Inventory of Reference Wetland Tree Species in the Neuse River Corridor, Lenoir County	8
Table 3.	2008 Vegetation Monitoring Data and Results.....	10
Table 4.	Summary of Groundwater Gauge Results	11
Table 5.	Summary of Vegetation Plot Results	12

LIST OF FIGURES

Figure 1.	Site Location Map	2
Figure 2.	Monitoring Plan.....	4

APPENDICES

- Appendix A. Gauge Data
- Appendix B. Vegetation Plot Photographs

**SLEEPY CREEK WETLAND AND RIPARIAN BUFFER RESTORATION BANK
ANNUAL MONITORING REPORT
YEAR 4 (2008)
LENOIR COUNTY, NORTH CAROLINA**

1.0 INTRODUCTION

Restoration Systems established the Sleepy Creek Wetland and Riparian Buffer Mitigation Site (Project) in the Coastal Plain region of the Neuse River Basin (United States Geological Survey Hydrologic Unit 03020202). The Project will provide compensatory mitigation for in-kind, unavoidable wetland and riparian buffer impacts associated with development in the river basin. Mitigation generated by this project will be used by the North Carolina Ecosystem Enhancement Program (NCEEP) and North Carolina Department of Transportation (NCDOT) to ensure no net loss of wetland functions associated with transportation improvement projects (TIPs) in the region.

The Project comprises 534 acres within four parcels distributed within the floodplains of Bear Creek and the Neuse River. The 534-acre Project includes a 153.58-acre Core Restoration Site northwest of the Town of LaGrange in Lenoir County (Figure 1) and approximately 380 acres of additional wetland management and preservation areas within the Bear Creek/Neuse River regional wetland corridor located near the City of Kinston.

A Detailed Wetland Restoration Plan was completed for the Core Restoration Site in July 2002. The plan outlined methods designed to restore agricultural fields that had been ditched, drained, and cleared for row crop production to pristine riverine wetlands. The plan outlined wetland restoration procedures including 1) ditch/canal backfilling, 2) ditch outlet plugs, 3) slough/drainageway construction, 4) embankment construction, 5) depressional wetland excavation, and 6) drainage control outlets.

The objectives of the Detailed Wetland Restoration Plan included the following.

- Establish a backwater cypress-tupelo swamp,
- Provide a perennial source for groundwater recharge through restored bottomland hardwood forest, and
- Facilitate nutrient reduction goals in the Neuse River Basin.




As constructed, the Core Restoration Site provides 96.4 acres of riverine wetland restoration, 39.2 acres of riverine wetland enhancement, and 18.0 acres of upland riparian buffer. In addition, the three wetland management and preservation areas provide 380 acres of riverine wetland preservation.

A final amended Detailed Wetland and Riparian Buffer Restoration Plan was completed for the project in July 2004 with final issuance of permits occurring in September 30, 2002, conditioned upon approval of the Detailed Wetland and Riparian Buffer Restoration Plan (approved June 29, 2004). Upon completion of the detailed plan and issuance of permits, construction plans were developed and construction was initiated in October 15, 2004. Backwater Environmental, a subsidiary of Osborne Co. Inc., completed earthwork and grading at the Site on April 27, 2005. Carolina Silvics completed planting of the Site from April 1 through 15, 2005. Axiom Environmental, Inc. completed as-built mitigation plan and as-built construction drawings in July 2006.



Core Restoration Site Location

Reference Groundwater Gauge



2126 Rowland Pond Dr
Willow Spring, NC 27592
(919) 215-1693
(919) 341-3839 fax

SITE LOCATION SLEEPY CREEK MITIGATION SITE Lenoir County, North Carolina

Dwn. by:	WGL
Ckd by:	WGL
Date:	Nov 2008
Project:	08-007

FIGURE
1

Information on project managers, owners, and contractors follows:

Owner Information

Restoration Systems, LLC
George Howard and John Preyer
1101 Haynes Street, Suite 211
Raleigh, North Carolina 27604
(919) 755-9490

Monitoring Performer Information

Axiom Environmental, Inc.
Grant Lewis and Corri Faquin
2126 Rowland Pond Drive
Willow Spring, North Carolina 27529
(919) 215-1693

Designer and Earthwork Contractor Information

Backwater Environmental, Inc.
Wes Newell
P.O. Box 1654
Pittsboro, North Carolina 27312
(919) 523-4375

Planting Contractor Information

Carolina Silvics
Dwight McKinney
908 Indian Trail Road
Edenton, North Carolina 27932
(252) 482-8491

As outlined in the Detailed Wetland and Riparian Buffer Restoration Plan, this project was designed and constructed based upon reference (relatively undisturbed) wetlands downstream of the Site within the Bear Creek – Neuse River Regional Wetland Corridor (Figure 1).

This report represents the Fourth Year Annual Monitoring Report. Monitoring activities were performed throughout Year 2008, including recording groundwater table elevations and plant species densities.

2.0 MONITORING PROGRAM

The Site monitoring protocol consists of a comparison between reference and restoration areas along with evaluation of jurisdictional wetland criteria (Environmental Laboratory 1987). Monitoring will entail analysis of two primary parameters: hydrology and vegetation. Monitoring of restoration efforts will be performed for a minimum of 5 years or until success criteria are fulfilled. The monitoring program is described below.

The Core Restoration Site has been subdivided into two monitoring areas including swamp forest and bottomland hardwood forest as depicted in Figure 2. Bottomland hardwood forest areas include floodplain flats adjacent to Bear Creek that are characterized by elevated groundwater tables and a rich diversity of vegetative species. Swamp forest areas are characterized by backwater sloughs that are semipermanently impounded and composed primarily of cypress-tupelo vegetation. The margins between bottomland hardwood forest and swamp forest areas were delineated and located utilizing Global Positions System equipment with reported submeter accuracy.

Swamp forest areas are expected to aggrade due to organic matter accumulation, sediment deposition, and vegetation mat formation and may fluctuate in location and extent throughout the monitoring period. Similarly, bottomland hardwood forest areas may be affected by beaver activity, changes in upstream watershed land use, storm flows, and/or climactic variations. Therefore, provisions for reclassification of bottomland hardwood and swamp forest areas represents an important component to be observed throughout the monitoring period.



RESTORATION SYSTEMS
1101 HAYNES STREET, STE 107
RALEIGH, N.C. 27604




NOTES/REVISIONS

Project:
**Sleepy Creek
Wetland Restoration
Site**

Lenoir County
North Carolina

Title:
**MONITORING
PLAN**

Scale: 1" = 300'
Date: Oct 2008
Project No.: 08-007
SHEET NO. **2**

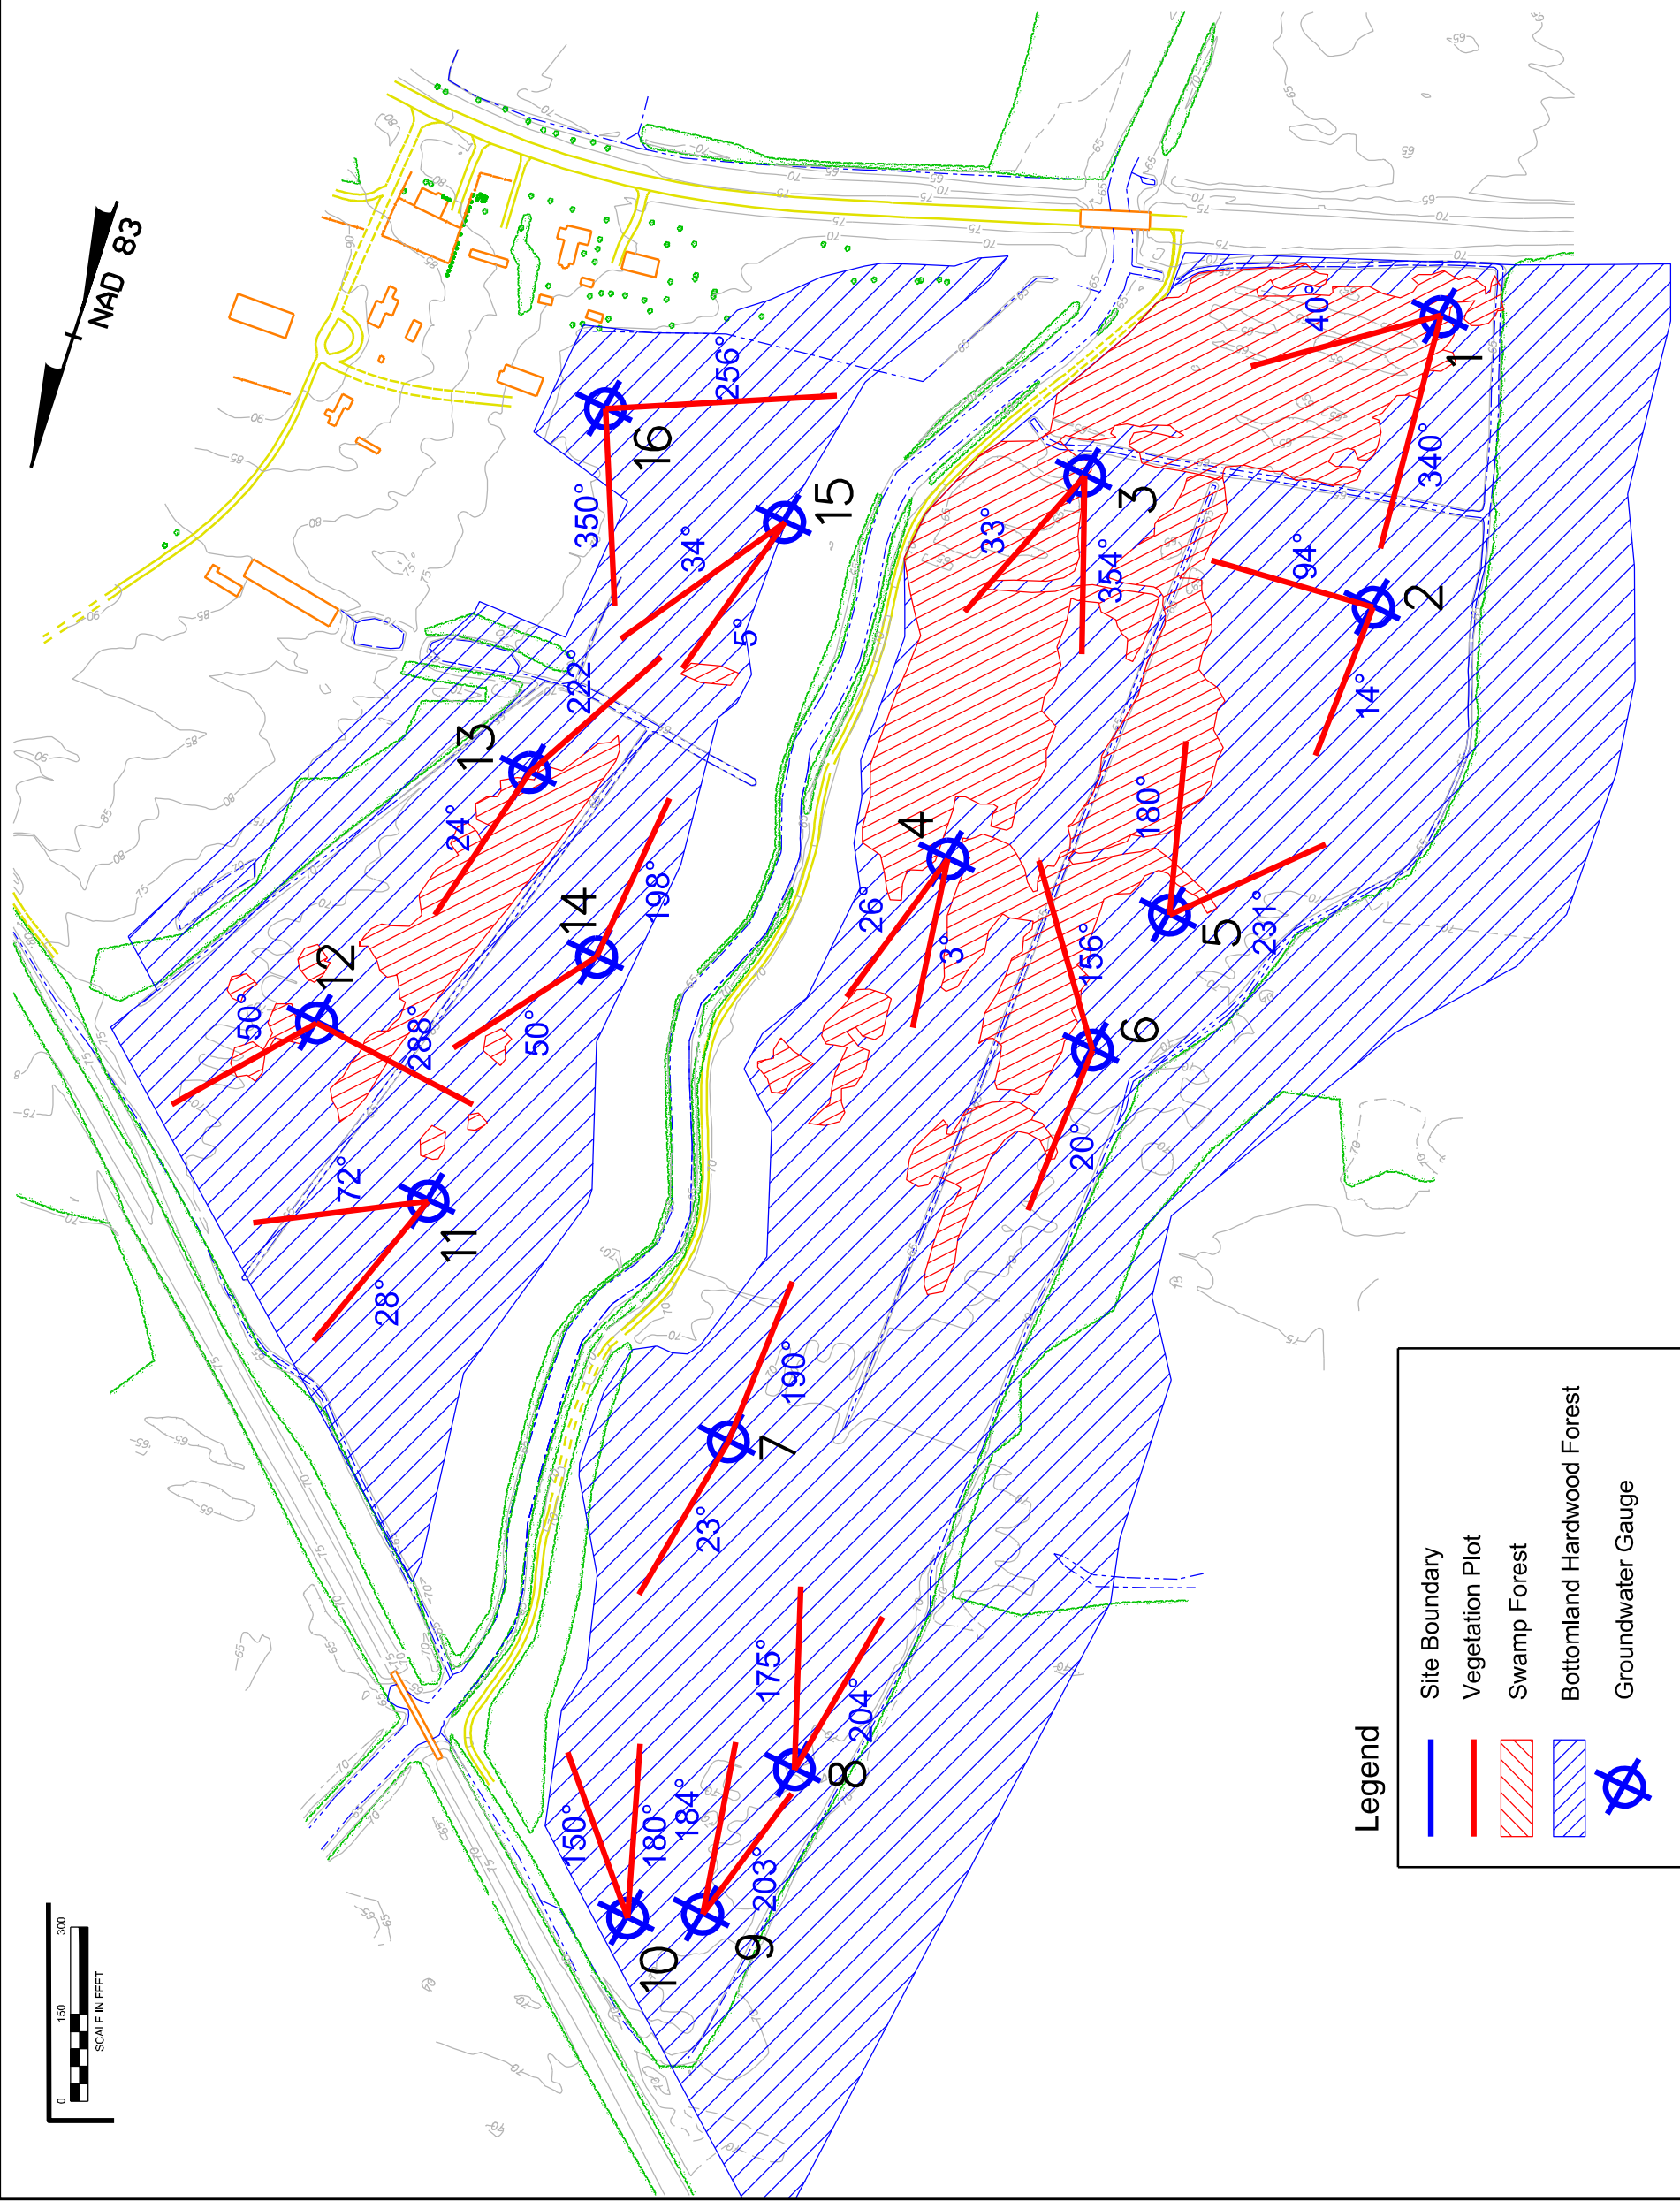

2.1 Wetland Hydrology

2.1.1 Hydrology Monitoring Procedure

After hydrological modifications were completed at the Site, continuous recording, surficial monitoring gauges were installed in accordance with specifications outlined in *Installing Monitoring Wells/Piezometers in Wetlands* (NCWRP 1993). Monitoring gauges were set to a depth of approximately 24 inches below the soil surface. Screened portions of each gauge were surrounded by filter fabric, buried in a sand screen, and sealed with a bentonite cap to prevent siltation and surface flow infiltration during floods.

Sixteen monitoring gauges were installed in wetland restoration areas to provide representative coverage within each physiographic landscape area (Figure 2). In addition, a monitoring gauges was installed in a reference area in a similar landscape position (Figure 1). The growing season dictated by the *Soil Survey of Lenoir County, North Carolina* (USDA 1977) indicates that the beginning and ending dates of the period between the last date in spring and the first date in the fall, on which the probability is 5 years in 10 that the air temperature at 5 feet above the ground surface will fall to 28 degrees Fahrenheit is March 12 through November 15. The Sleepy Creek Wetland and Riparian Restoration Plan dictated a growing season from February 25 to November 29; however, this was incorrectly based on a probability of 5 years in 10 that the air temperature will fall to 24 degrees Fahrenheit. Therefore, hydrologic sampling will be carried out in restoration areas during the growing season (March 12 to November 15) at daily intervals necessary to satisfy hydrology success criteria.

2.1.2 Hydrologic Success Criteria

Target hydrological goals have been developed using regulatory wetland hydrology criteria and reference wetland sites.

Regulatory Wetland Hydrology Criteria

The regulatory wetland hydrology criteria require saturation (free water) within 1 foot of the soil surface for 5 percent of the growing season under normal climatic conditions. In some instances, the regulatory wetland hydroperiod may extend between 5 and 12.5 percent of the growing season.

Reference Wetland Site

A monitoring gauge was placed in a reference wetland area located in the vicinity of the Site to provide reference hydroperiods for the bottomland hardwood forest areas.

Based on the *Sleepy Creek Wetland and Riparian Buffer Restoration Plan – Revised* (2004), under normal climatic conditions, the hydrologic success criteria require saturation (free water) within 1 foot of the soil surface for a minimum of 7.5 percent of the growing season for bottomland forest areas depicted in Figure 2 (Bottomland Hardwood Forest). The swamp forest areas as depicted in Figure 2 must support saturation (free water) within 1 foot of the soil surface for a minimum of 15 percent of the growing season (Swamp Forest). This hydroperiod translates to saturation for a minimum, 19-day (7.5 percent) to 37-day (15 percent) consecutive period during the growing season, which extends from March 12 to November 15 (249 days) (USDA 1977).

In drought years, the hydroperiod must exceed 75 percent of the hydroperiod exhibited by the reference gauges located within the same physiographic landscape area.

2.1.3 Hydrological Monitoring Results and Comparison with Success Criteria

Hydrographs for each monitoring location are provided in Appendix A along with daily rainfall totals for 2008 at a rain station in Goldsboro, North Carolina (Weather Underground 2008). Hydrographs show data for the growing season from March 12 through November 15, 2008.

The Site achieved the defined (or targeted) success criteria for hydrology for 9 of 13 groundwater gauges within bottomland hardwood areas and all of the groundwater gauges within swamp forest areas in the Fourth Monitoring Year (Year 2008) (Table 1). A total of approximately 30.48 inches of rain was documented near the Site at a rain station in Goldsboro (Weather Underground 2008) from March to October 2008, which is 5 inches below the 30-year historic (1971-2000) average normal rainfall for the same months (March to October) of 35.1 inches in Goldsboro (NOAA 2004).

Table 1. 2008 (Year 4) Groundwater Gauge Results

Gauge	Community	Max Consecutive Days Saturated During Growing Season (Percent)	Defined (or Targeted) Success Criteria Achieved
2	bottomland hardwood forest	87 days (34.9 %)	Yes
4	bottomland hardwood forest	66 days (26.5 %)	Yes
5	bottomland hardwood forest	84 days (33.7 %)	Yes
6	bottomland hardwood forest	81 days (32.5 %)	Yes
7	bottomland hardwood forest	21 days (8.4 %)	Yes
8	bottomland hardwood forest	45 days (18.1 %)	Yes
9	bottomland hardwood forest	61 days (24.5 %)	Yes
10	bottomland hardwood forest	8 days (3.2 %)	No
11	bottomland hardwood forest	13 days (5.2 %)	No
12	bottomland hardwood forest	84 days (33.7 %)	Yes
14	bottomland hardwood forest	13 days (5.2 %)	No
15	bottomland hardwood forest	6 days (2.4 %)	No
16	bottomland hardwood forest	73 days (29.3 %)	Yes
Ref BH100	bottomland hardwood forest	46 days (18.5 %)	Yes
1	swamp forest	104 days (41.8 %)	Yes
3	swamp forest	66 days (26.5 %)	Yes
13	swamp forest	80 days (32.1 %)	Yes

2.2 Vegetation

2.2.1 Vegetation Monitoring Procedure

Restoration monitoring procedures for vegetation are designed in accordance with guidelines presented in *Mitigation Site Classification* (MiST) documentation (USEPA 1990) and *Compensatory Hardwood Mitigation Guidelines* (USDOA 1993). The following presents a general discussion of the monitoring protocol.

Vegetation will receive visual evaluations during the periodic reading of monitoring gauges to ascertain the general conditions and degree of overtopping of planted elements by weeds. Subsequently, quantitative

sampling of vegetation will be performed once annually during the fall for a minimum of 5 years or until vegetation success criteria are achieved. Sampling dates may be modified to accommodate river flood events and plot inundation, if needed.

Sixteen sample plots were installed within planted areas of the Site to equally represent the various hydrologic regimes and plant communities (Figure 2). Each transect is 600 feet in length and 8 feet in width (0.11 acre) centered on each of the 16 groundwater monitoring gauges. In each sample plot, vegetation parameters to be monitored include species composition and species density. Visual observations of the percent cover of shrub and herbaceous species will also be recorded but not used for vegetative success criteria. Photographs of the 16 vegetation plots are included in Appendix B.

2.2.2 Vegetation Success Criteria

Success criteria have been established to verify that the vegetation component supports community elements necessary for floodplain forest development. Success criteria are dependent upon the density and growth of characteristic forest species. Additional success criteria are dependent upon density and growth of "Character Tree Species," which include planted species, species listed by Schafale and Weakley (1990) as occurring in bottomland and swamp forests, and species identified in the reference forest ecosystems (RFE's). All canopy tree species planted and identified in the reference forest ecosystem will be utilized to define "Character Tree Species" as termed in the success criteria (Table 2).

The vegetation success criteria have been designed to evaluate bottomland hardwood forest and riverine swamp forest separately. This division in success criteria by community type has been applied because bottomland hardwood forests typically contain relatively high tree species diversity while backwater swamp forests are characterized by relatively low diversity, sometimes dominated by one or two tree species.

Bottomland Hardwood Forest

The bottomland hardwood forest areas are depicted in Figure 2. For these vegetative monitoring transects, a minimum mean density of 320 character trees per acre must be surviving for 3 years after initial planting. Subsequently, 290 character trees per acre must be surviving in year 4 and 260 character trees per acre in year 5. In addition, at least five character tree species must be present, and no species can comprise more than 20 percent of the 320 stem per acre total. For species with stem counts above the 20 percent threshold, the excess stems will be discarded from the statistical analysis.

Riverine Swamp Forest

The riverine swamp forest areas are depicted in Figure 2. For these vegetative monitoring transects, an average density of 320 character tree species per acre must be surviving in the first three monitoring years. Subsequently, 290 character tree species per acre must be surviving in year 4 and 260 character tree species per acre in year 5. One planted species may represent up to 100 percent of the required stem per acre total (most likely bald cypress, water tupelo, and/or swamp tupelo).

If vegetation success criteria are not achieved based on average density calculations by community type, the individual plots that do not meet the stem per acre requirement will be identified. Supplemental planting will be performed in those vegetative community areas, as needed, until achievement of vegetation success criteria. Alternatively, that plot, or area adjacent to the plot, may be mapped and reclassified as riverine bottomland hardwood forest or riverine swamp forest habitat.

Table 2. Inventory of Reference Wetland Tree Species in the Neuse River Corridor, Lenoir County

Scientific Name	Common Name	Scientific Name	Common Name
<i>Acer rubrum</i> ¹	Red Maple ¹	<i>Platanus occidentalis</i>	American Sycamore
<i>Acer negundo</i>	Box Elder	<i>Populus heterophylla</i>	Swamp Cottonwood
<i>Betula nigra</i>	River Birch	<i>Prunus serotina</i>	Black Cherry
<i>Carpinus caroliniana</i>	Ironwood	<i>Quercus alba</i>	White Oak
<i>Carya aquatica</i>	Water Hickory	<i>Quercus laurifolia</i>	Laurel Oak
<i>Carya tomentosa</i>	Mockernut Hickory	<i>Quercus lyrata</i>	Overcup Oak
<i>Celtis laevigata</i>	Hackberry	<i>Quercus michauxii</i>	Swamp Chestnut Oak
<i>Chamaecyparis thyoides</i>	Atlantic White Cedar	<i>Quercus nigra</i>	Water Oak
<i>Cornus spp.</i>	Dogwood	<i>Quercus pagoda</i>	Cherrybark Oak
<i>Fagus grandifolia</i>	American Beech	<i>Quercus phellos</i>	Willow Oak
<i>Fraxinus caroliniana</i>	Carolina Ash	<i>Quercus rubra</i>	Northern Red Oak
<i>Fraxinus pennsylvanica</i>	Green Ash	<i>Salix caroliniana</i> ¹	Carolina Willow ¹
<i>Fraxinus profunda</i>	Pumpkin Ash	<i>Salix nigra</i> ¹	Black Willow ¹
<i>Gordonia lasianthus</i>	Loblolly Bay	<i>Symplocus tinctoria</i>	Horse Sugar
<i>Ilex opaca</i>	American Holly	<i>Taxodium distichum</i>	Bald Cypress
<i>Juglans nigra</i>	Black Walnut	<i>Ulmus alata</i>	Winged Elm
<i>Juniperus virginiana</i>	Eastern Red Cedar	<i>Ulmus americana</i>	American Elm
<i>Liquidambar styraciflua</i> ¹	Sweet Gum ¹	<i>Ulmus rubra</i>	Slippery Elm
<i>Liriodendron tulipifera</i>	Tulip Poplar		
<i>Magnolia virginiana</i>	Sweet Bay		
<i>Morus rubra</i>	Red Mulberry		
<i>Nyssa aquatica</i>	Water Tupelo		
<i>Nyssa biflora</i>	Swamp Tupelo		
<i>Nyssa sylvatica</i>	Black Gum		
<i>Oxydendrum arboreum</i>	Sourwood		
<i>Persea palustris</i>	Red Bay		
<i>Pinus serotina</i>	Pond Pine		
<i>Pinus taeda</i> ¹	Loblolly Pine ¹		

1: Loblolly pine, red maple, sweet gum, and willow species have been excluded as character elements by the Mitigation Banking Review Team.

2.2.3 Vegetation Sampling Results and Comparison to Success Criteria

Quantitative sampling of vegetation was conducted in late August and early September 2008. Results are provided in Table 3. Vegetation success criteria for year 4 (290 tree stems per acre) were exceeded for the 2008 annual monitoring year with 568 tree stems per acre for bottomland hardwood transects and 472 tree stems per acre for swamp forest transects across the Site. Each individual vegetation plot met success criteria with the exception of bottomland hardwood plots 2 and 5. These plots had decent species diversity and a total number of trees per acre of 273 and 173, respectively counting towards success criteria. Planted species survival may have been reduced within these plots as a result of the extended drought that immediately followed planting.

3.0 CONCLUSIONS

The Site achieved the defined (or targeted) success criteria for hydrology for 9 of 13 groundwater gauges within bottomland hardwood areas and all of the groundwater gauges within swamp forest areas in the Fourth Monitoring Year (Year 2008). A total of approximately 30.48 inches of rain was documented near the Site at a rain station in Goldsboro (Weather Underground 2008) from March to October 2008, which is 5 inches below the 30-year (1971-2000) average normal rainfall for the same months (March to October) of 35.1 inches in Goldsboro (NOAA 2004). Groundwater data over the entire monitoring period is summarized in the following table.

TABLE 3
2008 VEGETATION MONITORING DATA AND RESULTS

Note: Each plot totals 0.11 acre in size.

Community	Bottomland Hardwood Forest										Swamp Forest					Total Tree Stems/Acre Counting Towards Success Criteria*						
	Plot 2	Plot 4	Plot 5	Plot 6	Plot 7	Plot 8	Plot 9	Plot 10	Plot 11	Plot 12	Plot 14	Plot 15	Plot 16	Totals	Total/Acre		Total Tree Stems/Acre Counting Towards Success Criteria*	Plot 1	Plot 3	Plot 13	Totals	Total/Acre
<i>Acer rubrum</i> (red maple)	210	50	240	156	39	90	100	70	130	140	149	1	3	1378	964	0	60	10	260	330	1000	0
<i>Baccharis halimifolia</i> (eastern baccharis)	13	4	11	160	25	140	4	18	130	310	540	50	140	1545	1080	0	9	1	65	75	227	0
<i>Betula nigra</i> (river birch)	1	680	18	18	22	15	4	3	71	50	85	460	55	1464	1024	58		240	170	410	1242	58
<i>Carya cordiformis</i> (biternut hickory)														0	0	0				0	0	0
<i>Carya illinoensis</i> (pecan)						1							2	3	2	2				0	0	0
<i>Carya sp.</i> (hickory)				1								2	5	18	13	13				0	0	0
<i>Cornus amomum</i> (silky dogwood)												1		1	1	1				0	0	0
<i>Diospyros virginiana</i> (persimmon)												1		1	1	1				0	0	0
<i>Fraxinus pennsylvanica</i> (green ash)		12			5	8	24	4	21	20	8	6	3	111	78	58			1	1	3	3
<i>Ilex opaca</i> (American holly)													3	3	2	2				0	0	0
<i>Juniperus virginiana</i> (eastern red cedar)												6		0	0	0			1	1	3	3
<i>Ligustrum sinense</i> (Chinese privet)										20		6	6	32	22	0				0	0	0
<i>Liquidambar styraciflua</i> (sweetgum)	12		1	16	17	180	110	80	160	220	57	44	9	906	634	0	6		100	106	321	0
<i>Liriodendron tulipifera</i> (tulip poplar)					3	2	2	1	5	1		1	2	16	11	11				0	0	0
<i>Morella sp.</i> (wax myrtle)														1	1	1				0	0	0
<i>Morus sp.</i> (mulberry)													2	2	1	1				0	0	0
<i>Myrica cerifera</i> (wax myrtle)								1						1	1	1				0	0	0
<i>Nyssa aquatica</i> (water tupelo)	23	8	25	25	2	11	2	1	14	23	19	5	3	161	113	58	5	6	19	30	91	91
<i>Nyssa biflora</i> (swamp tupelo)						1			1			11	1	14	10	10				0	0	0
<i>Nyssa sp.</i> (swamp/water tupelo)	17	33	8	7	3	9	15	1	5	2	2	7	1	110	77	58	6		2	8	24	24
<i>Pinus taeda</i> (loblolly pine)	72	1	28	19	20	410	500	48	2		2	1	4	1107	774	0			3	3	9	0
<i>Platanus occidentalis</i> (American sycamore)		9	1	1	9	1	10	6	7	8	3	4	38	96	67	58		2		2	6	6
<i>Populus heterophylla</i> (cottonwood)													3	3	2	2				0	0	0
<i>Prunus angustifolia</i> (chickasaw plum)									1					1	1	1				0	0	0
<i>Prunus serotina</i> (black cherry)			1		2	1			1				2	7	5	5				0	0	0
<i>Quercus coccinea</i> (scarlet oak)														0	0	0			1	1	3	3
<i>Quercus falcata</i> (northern red oak)														0	0	0				1	3	3
<i>Quercus laurifolia</i> (laurel oak)														0	0	0				0	0	0
<i>Quercus lyrata</i> (overcup oak)		5		1	2	7	15	6	9	1	4	17	12	78	55	55	2	2	2	6	18	18
<i>Quercus michauxii</i> (swamp chestnut oak)		6		1	2	1	1	9	1		2	1		23	16	16		5		5	15	15
<i>Quercus nigra</i> (water oak)	5	8	3	3	3	6	9	5	3	1	1	4	4	52	36	36	4	5	4	13	39	39
<i>Quercus pagoda</i> (cherrybark oak)		4		2	2	2	1	9	2	2	3	1	1	24	17	17			1	1	3	3
<i>Quercus phellos</i> (willow oak)		3		6	9	9	12	8	4	4	1	5	2	54	38	38				0	0	0
<i>Quercus sp.</i> (oak)			1	1	1	1	1	1	1					4	3	3				0	0	0
<i>Rhus copallinum</i> (winged sumac)	13		3	3	80	6	1	2				1		109	76	0			20	20	61	0
<i>Rhus glabra</i> (smooth sumac)														0	0	0				0	0	0
<i>Salix caroliniana</i> (coastal plain willow)										1		2	8	11	8	0			2	6	6	0
<i>Salix nigra</i> (black willow)	2	8	4	4	1				8	5	28	9	8	73	51	0	4	22	16	42	127	0
<i>Salix sp.</i> (willow)											1			1	1	0				0	0	0
<i>Sassafras albidum</i> (sassafras)														0	0	0				0	0	0
<i>Taxodium distichum</i> (bald cypress)	9	1	15	29	6	15	3		30	28	32	20	9	197	138	58	25	15	28	68	206	206
<i>Ulmus sp.</i> (elm)		2				2								4	3	3				0	0	0
<i>Ulmus rubra</i> (slippery elm)		1							1					2	1	1				0	0	0
TOTAL	377	835	332	450	253	907	825	272	605	836	937	658	326	7613	5324	568	123	309	693	1125	3409	0
TOTAL COUNTING TOWARDS SUCCESS CRITERIA	30	63	19	37	49	61	57	45	85	41	40	59	90				42	42	65			
TOTAL/ACRE COUNTING TOWARDS SUCCESS CRITERIA	273	573	173	336	445	555	518	409	773	373	364	536	818			568	382	382	591			472

* Success criteria requires that within bottomland hardwood areas no species may make up more than 20 percent of the 290 stem/acre total. Using this criteria, no species can provide more than 58 stems/acre towards success criteria (or 6 stems/0.11 acre plot). Within swamp forest areas, success criteria dictates that one species may make up 100 percent of the 290 stem/acre requirement, most likely bald cypress, swamp tupelo, or water tupelo.

Table 4. Summary of Groundwater Gauge Results

Gauge	Success Criteria Achieved/Max Consecutive Days During Growing Season (Percentage)				
	Year 1 (2005)	Year 2 (2006)	Year 3 (2007)	Year 4 (2008)	Year 5 (2010)
Bottomland Hardwood					
2	Yes/102 days (41.0 percent)	Yes/81 days (33 percent)	Yes/249 days (100 percent)	Yes/87 days (34.9 percent)	
4	Yes/42 days (16.9 percent)	Yes/28 days (11 percent)	Yes/77 days (30.9 percent)	Yes/66 days (26.5 percent)	
5	Yes/97 days (39.0 percent)	Yes/77 days (31 percent)	Yes/157 days (63.1 percent)	Yes/84 days (33.7 percent)	
6	Yes/80 days (32.1 percent)	Yes/82 days (33 percent)	Yes/157 days (63.1 percent)	Yes/81 days (32.5 percent)	
7	Yes/26 days (10.4 percent)	No/6 days (2 percent)	No**/17 days (6.8 percent)	Yes/21 days (8.4 percent)	
8	No/18 days (7.2 percent)	No/12 days (5 percent)	Yes/77 days (30.9 percent)	Yes/45 days (18.1 percent)	
9	No/16 days (6.4 percent)	Yes/19 days (8 percent)	Yes/57 days (22.9 percent)	Yes/61 days (24.5 percent)	
10	Yes/25 days (10.0 percent)	No/12 days (5 percent)	Yes/43 days (17.3 percent)	No/8 days (3.2 percent)	
11	Yes/50 days (20.1 percent)	Yes/29 days (11 percent)	Yes/31 days (12.4 percent)	No/13 days (5.2 percent)	
12	Yes/249 days (100 percent)	Yes/100 days (40 percent)	Yes/157 days (63.1 percent)	Yes/84 days (33.7 percent)	
14	No/50 days (20.1 percent)	No/12 days (5 percent)	Yes/30 days (12.0 percent)	No/13 days (5.2 percent)	
15	No/11 days (4.4 percent)	No/12 days (5 percent)	Yes/34 days (13.7 percent)	No/6 days (2.4 percent)	
16	Yes/81 days (32.5 percent)	Yes/78 days (31 percent)	Yes/113 days (45.4 percent)	Yes/73 days (29.3 percent)	
Ref BH100	No/3 days (1.2 percent)*	Yes/89 days (36 percent)	Yes/86 days (34.5 percent)	Yes/46 days (18.5 percent)	
Swamp Forest					
1	Yes/100 days (40.2 percent)	Yes/81 days (33 percent)	Yes/249 days (100 percent)	Yes/104 days (41.8 percent)	
3	Yes/32 days (12.9 percent)	Yes/77 days (31 percent)	Yes/111 days (44.6 percent)	Yes/66 days (26.5 percent)	
13	Yes/36 days (14.5 percent)	Yes/82 days (33 percent)	Yes/144 days (57.8 percent)	Yes/80 days (32.1 percent)	

*Gauge malfunctioned April 10, 2005. Data only available for March 12 through April 10, 2005 for the 2005 growing season.

**Gauge readings were erratic and gauge was replaced prior to year 4 (2008) monitoring.

As a whole, vegetation plots across the Site were well above the required 290 stems/acre with an average of 568 tree stems per acre within bottomland hardwood areas and 472 tree stems per acre within swamp forest areas in the Fourth Monitoring Year (Year 2008). Vegetation data over the entire monitoring period is summarized in the following table.

Table 5. Summary of Vegetation Plot Results


Plot	Stems/Acre Counting Towards Success Criteria				
	Year 1 (2005)	Year 2 (2006)	Year 3 (2007)	Year 4 (2008)	Year 5 (2010)
Bottomland Hardwoods					
2	273	291	309	273	
4	455	700	655	573	
5	227	191	255	173	
6	218	345	446	336	
7	436	527	382	445	
8	327	600	564	555	
9	291	564	592	518	
10	264	509	391	409	
11	382	673	646	773	
12	473	464	400	373	
14	336	518	428	364	
15	300	582	410	536	
16	400	600	755	818	
Average Bottomland Hardwood Plots	433	734	624	568	
Swamp Forest					
1	527	564	501	382	
3	255	418	774	382	
13	436	645	1829	591	
Average Swamp Forest Plots	419	581	1032	472	

4.0 REFERENCES


- Environmental Laboratory. 1987. Corps of Engineers Wetland Delineation Manual. Technical Report Y-87-1. United States Army Corps of Engineers Waterways Experiment Station, Vicksburg, MS.
- National Oceanic and Atmospheric Administration (NOAA). 2004. Climatology of the United States No. 20; Monthly Station Climate Summaries, 1971-2000. National Oceanic and Atmospheric Administration, National Environmental Satellite, Data, and Information Service, National Climatic Data Center, Asheville, North Carolina.
- North Carolina Wetlands Restoration Program (NCWRP). 1993. Installing Monitoring Wells/Piezometers in Wetlands (WRP Technical Note HY-IA-3.1). North Carolina Department of Environment, Health, and Natural Resources, Raleigh, North Carolina.
- Schafale, M. P., A.S. Weakley. 1990. Classification of the Natural Communities of North Carolina: Third Approximation, NC Natural Heritage Program, Division of Parks and Recreation, NC DEM, Raleigh NC.
- United States Department of Agriculture (USDA). 1977. Soil Survey of Lenoir County, North Carolina. United States Department of Agriculture, Natural Resources Conservation Service.
- United States Department of the Army (USDOA). 1993 (unpublished). Compensatory Hardwood Mitigation Guidelines. United States Army Corps of Engineers, Wilmington District.
- United States Environmental Protection Agency (USEPA). 1990. Mitigation Site Classification (MiST). A Methodology to Classify Pre-Project Mitigation Sites and Develop Performance Standards for Construction and Restoration of Forested Wetlands. USEPA Workshop, August 13-15, 1989. USEPA Region IV and Hardwood Research Cooperative, North Carolina State University, Raleigh, NC.
- Weather Underground. 2008. Station in Goldsboro, North Carolina. (online). Available: <http://www.wunderground.com/cgi-bin/findweather/getForecast?query=35.33916855,-77.96055603> [November 16, 2008]. Weather Underground.

APPENDIX A GAUGE DATA


Sleepy Creek Gauge 1 Year 4 (2008) Data

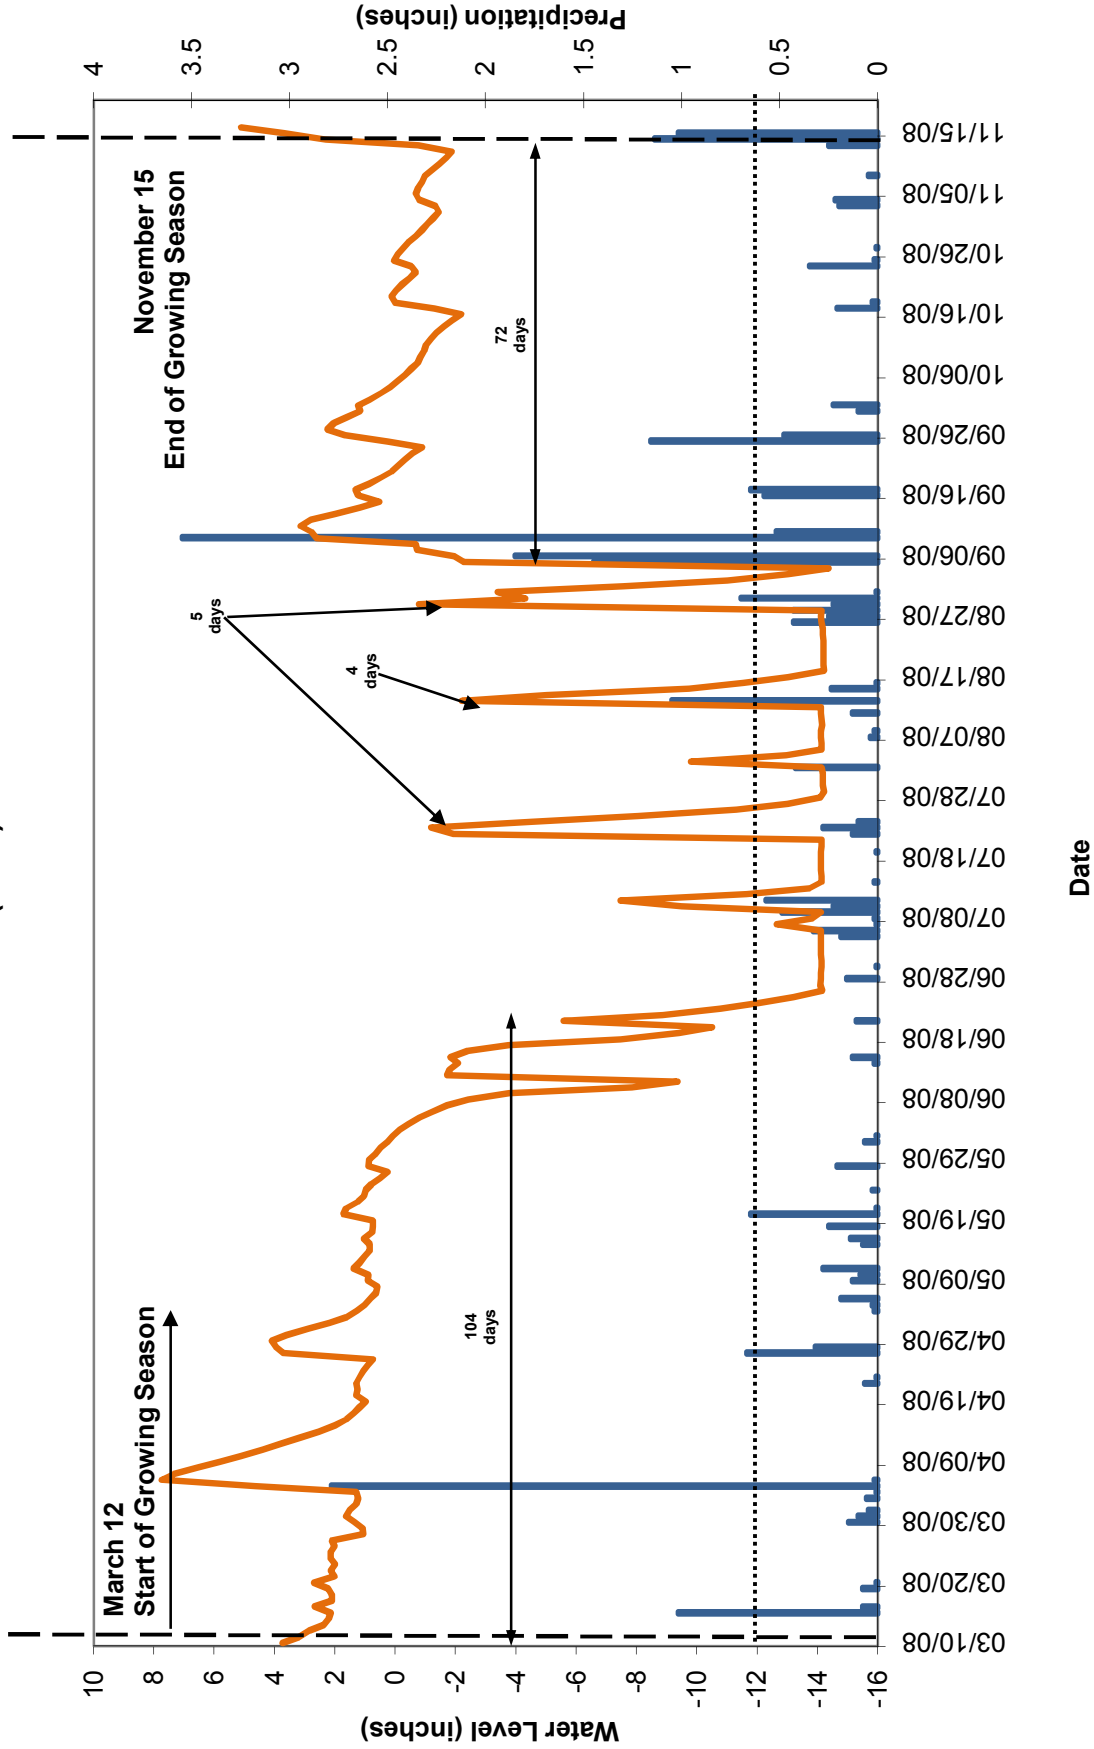


Sleepy Creek Gauge 2 Year 4 (2008) Data

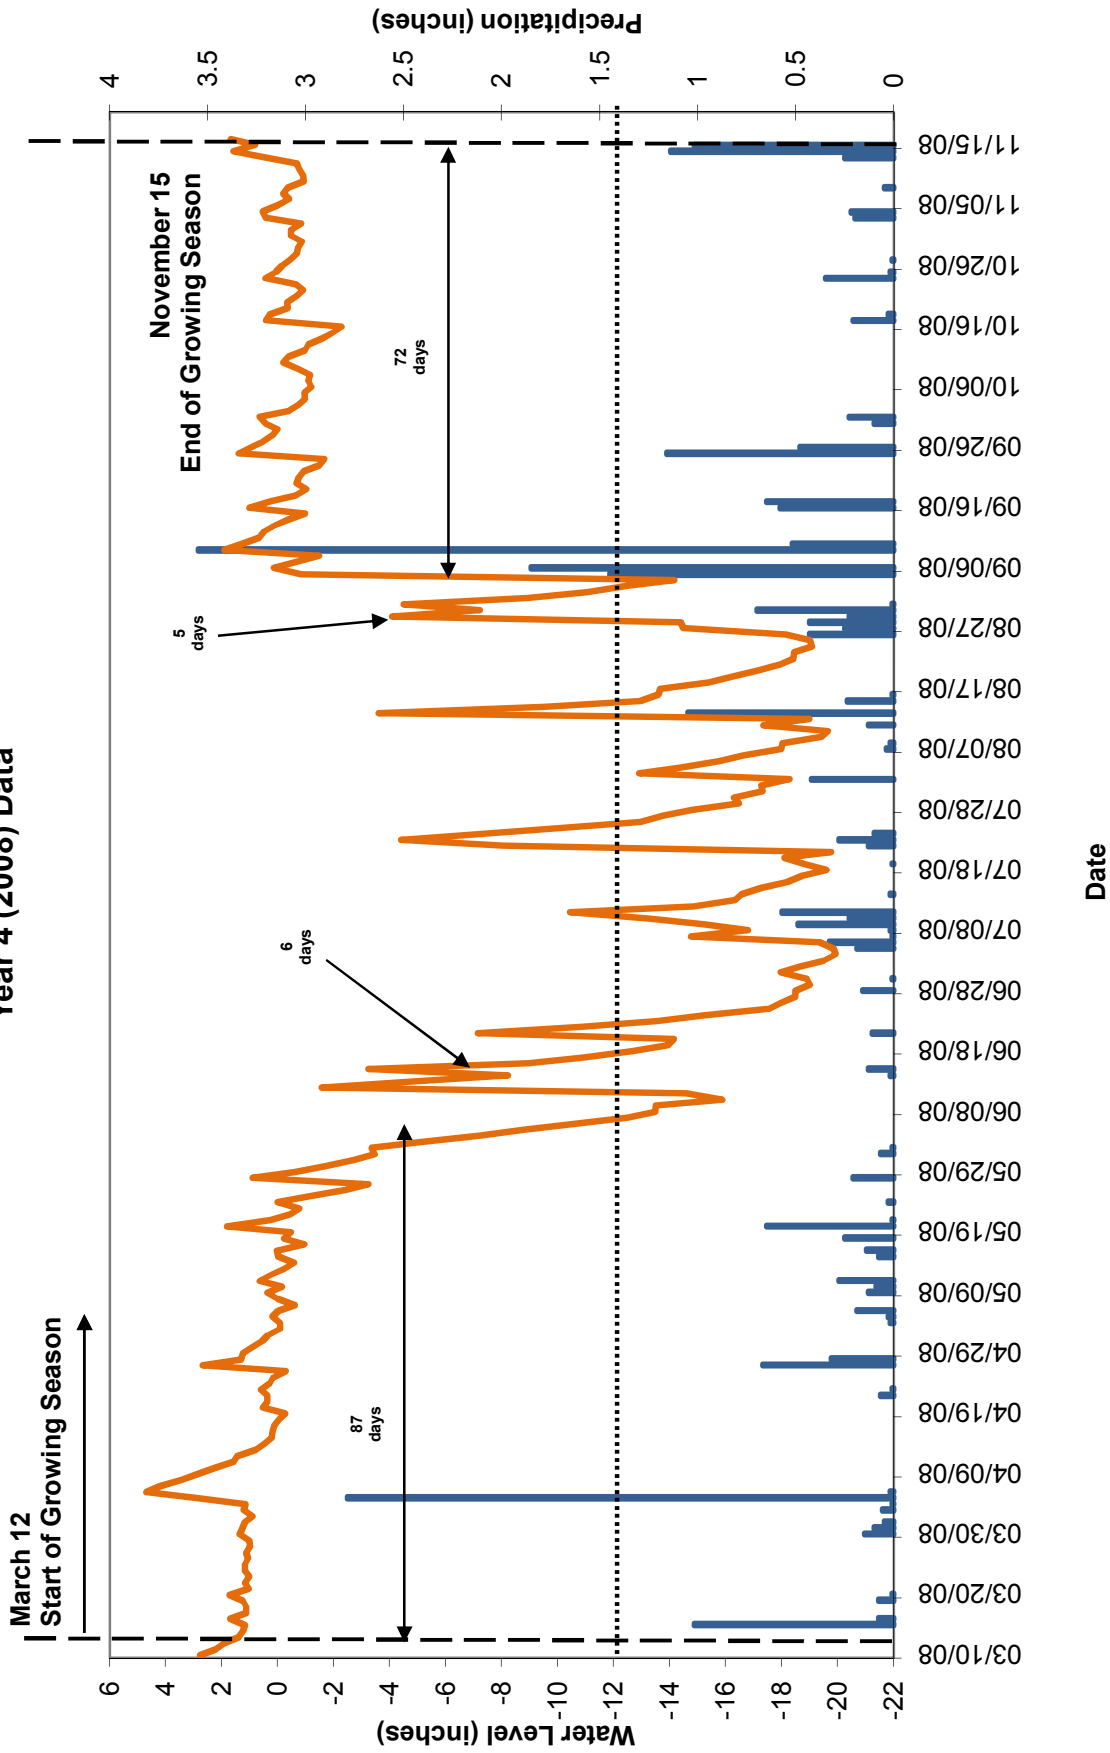


Sleepy Creek Gauge 3 Year 4 (2008) Data

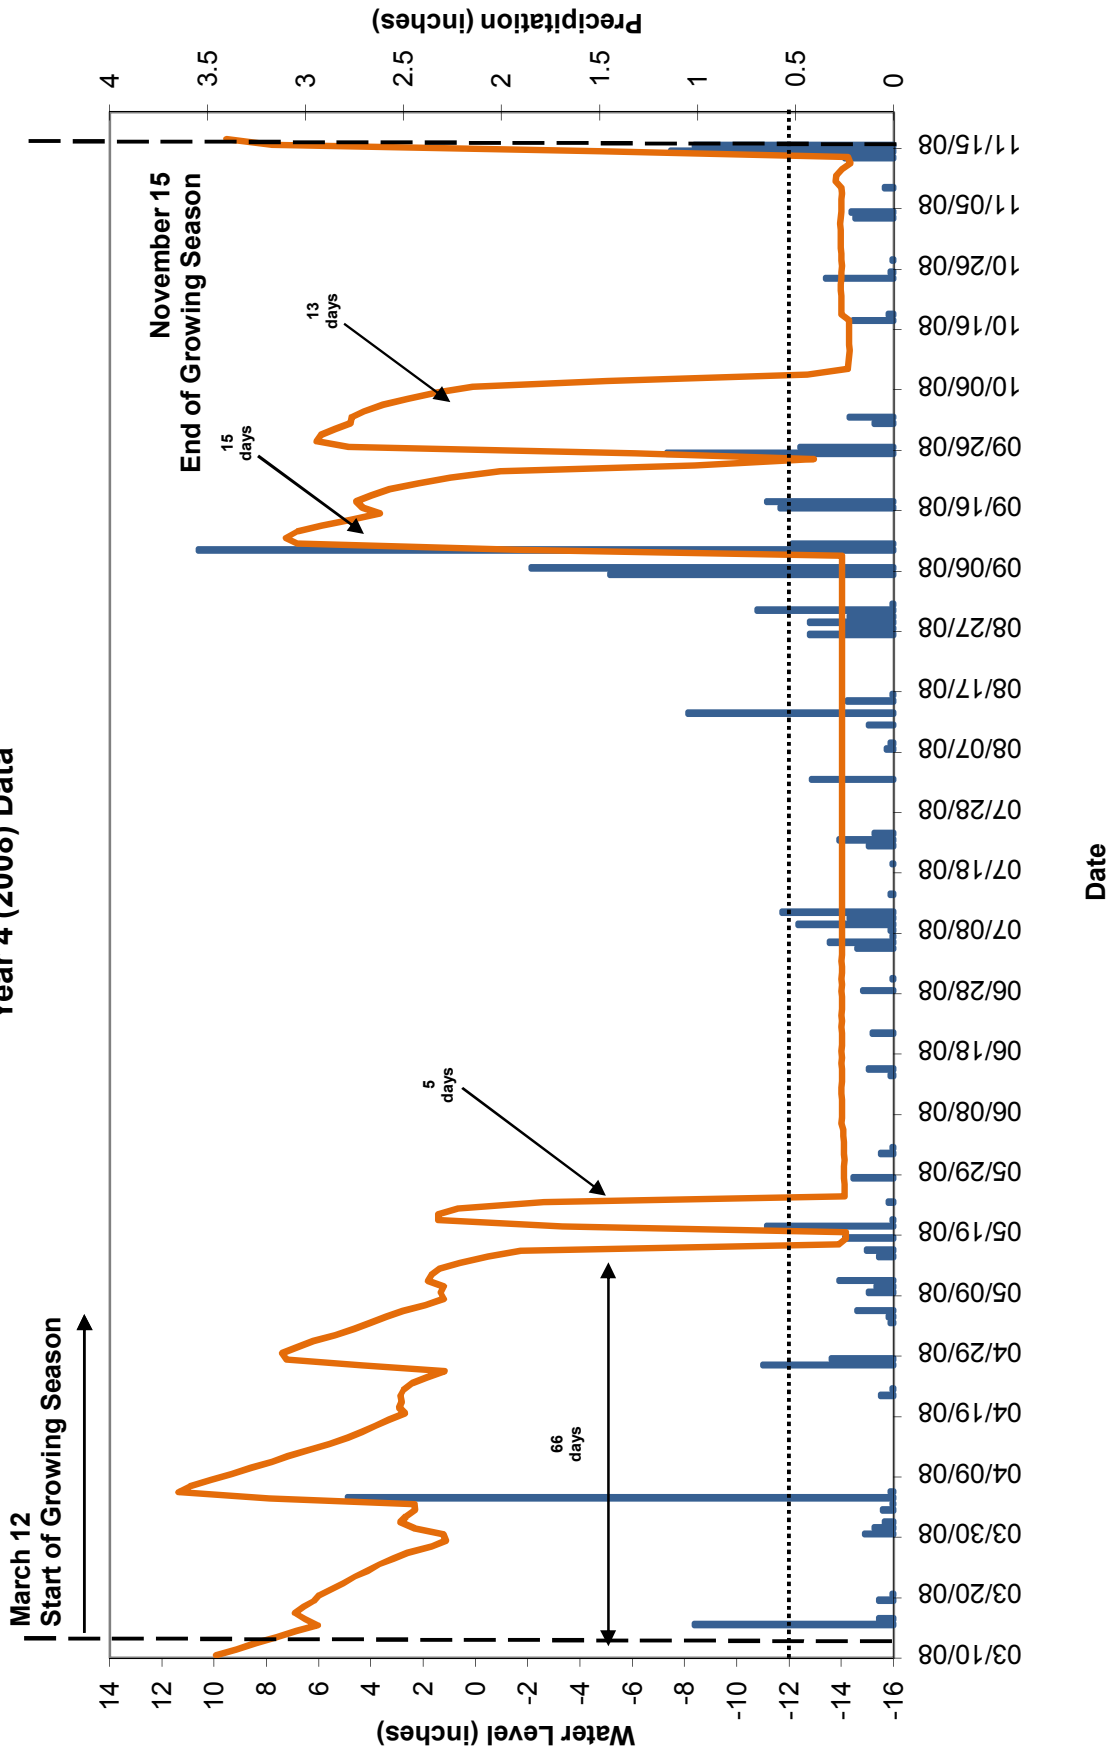


Sleepy Creek Gauge 4 Year 4 (2008) Data

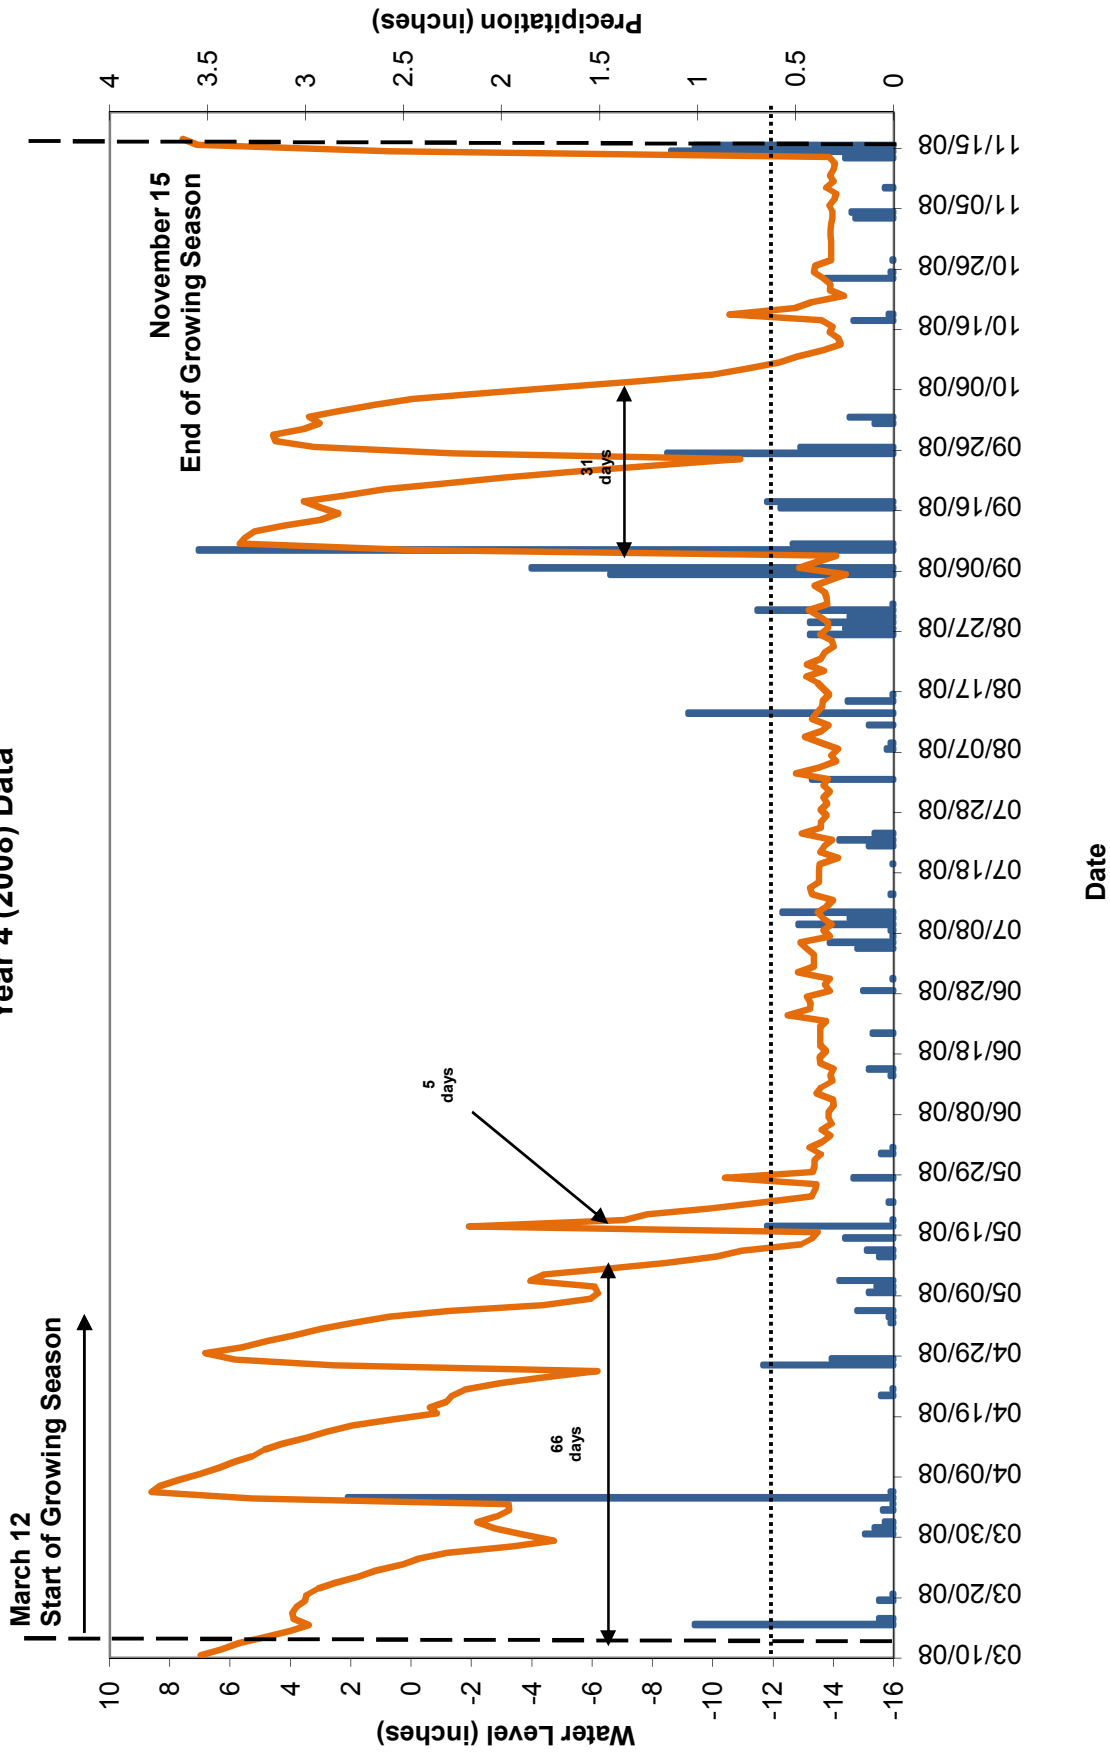


Sleepy Creek Gauge 5 Year 4 (2008) Data

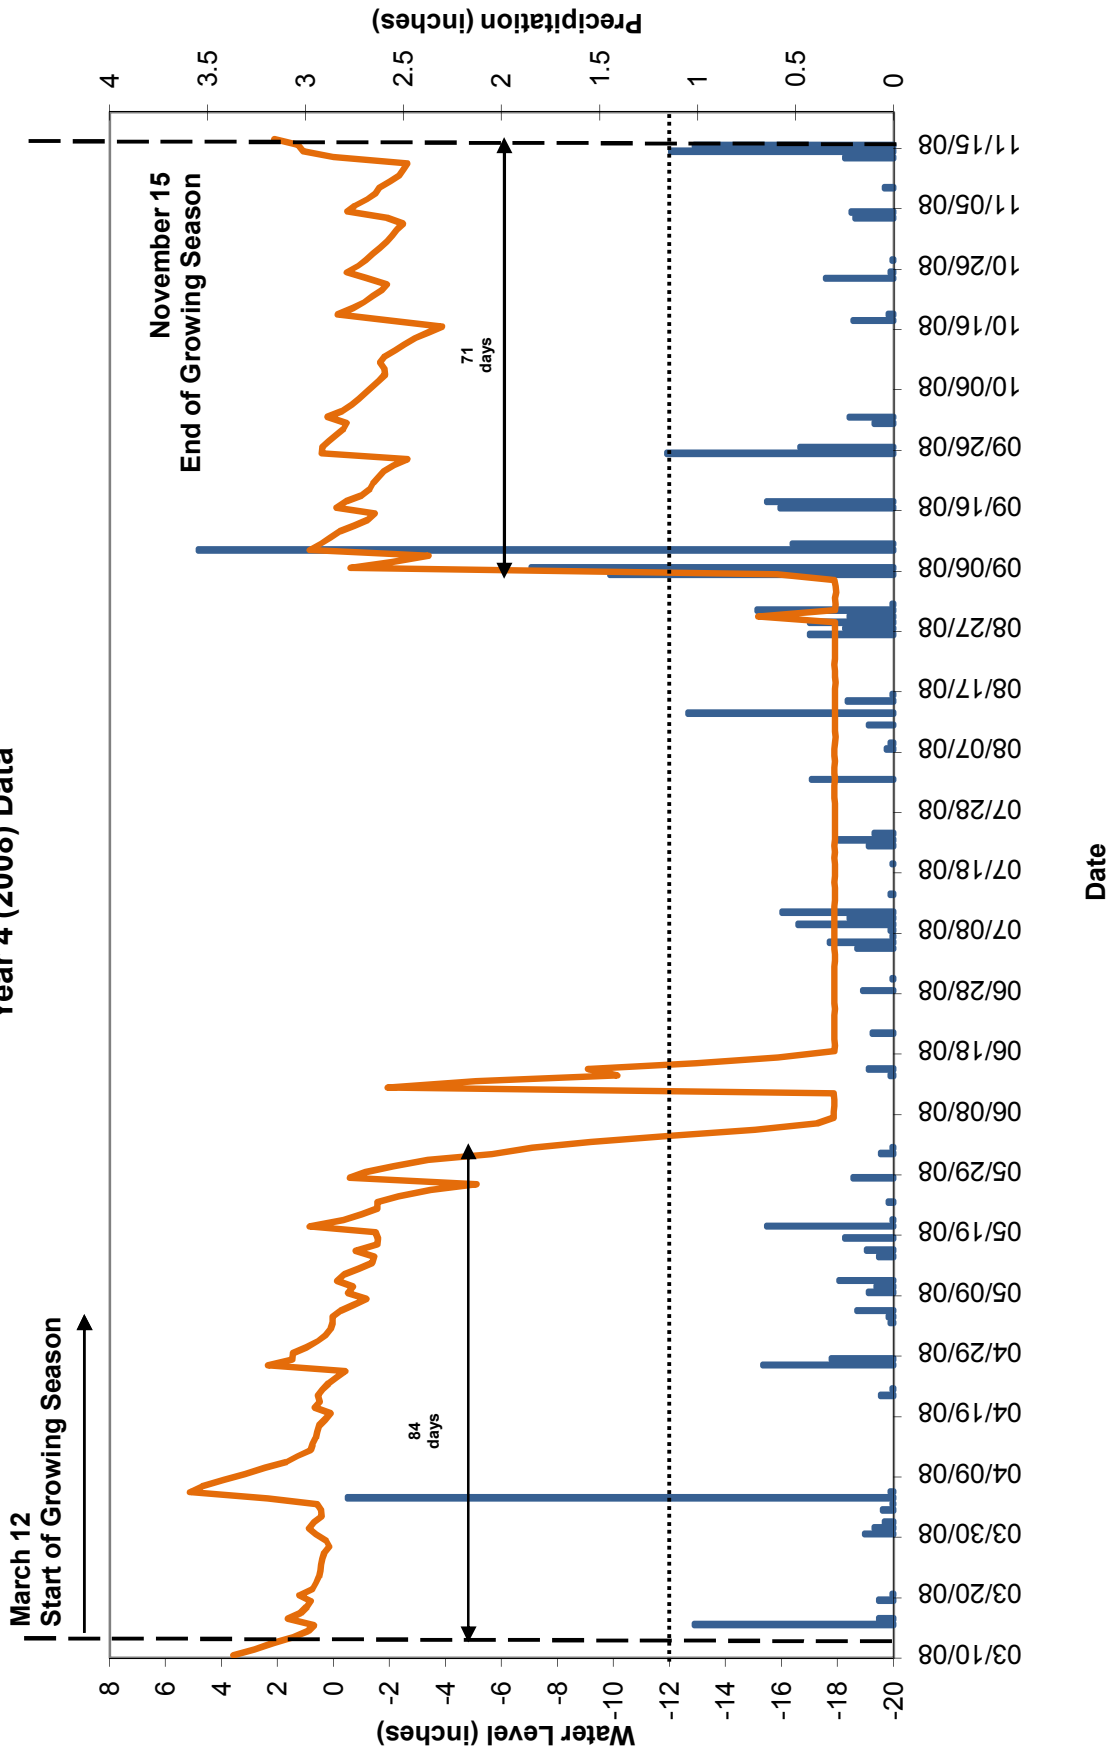


Sleepy Creek Gauge 6 Year 4 (2008) Data

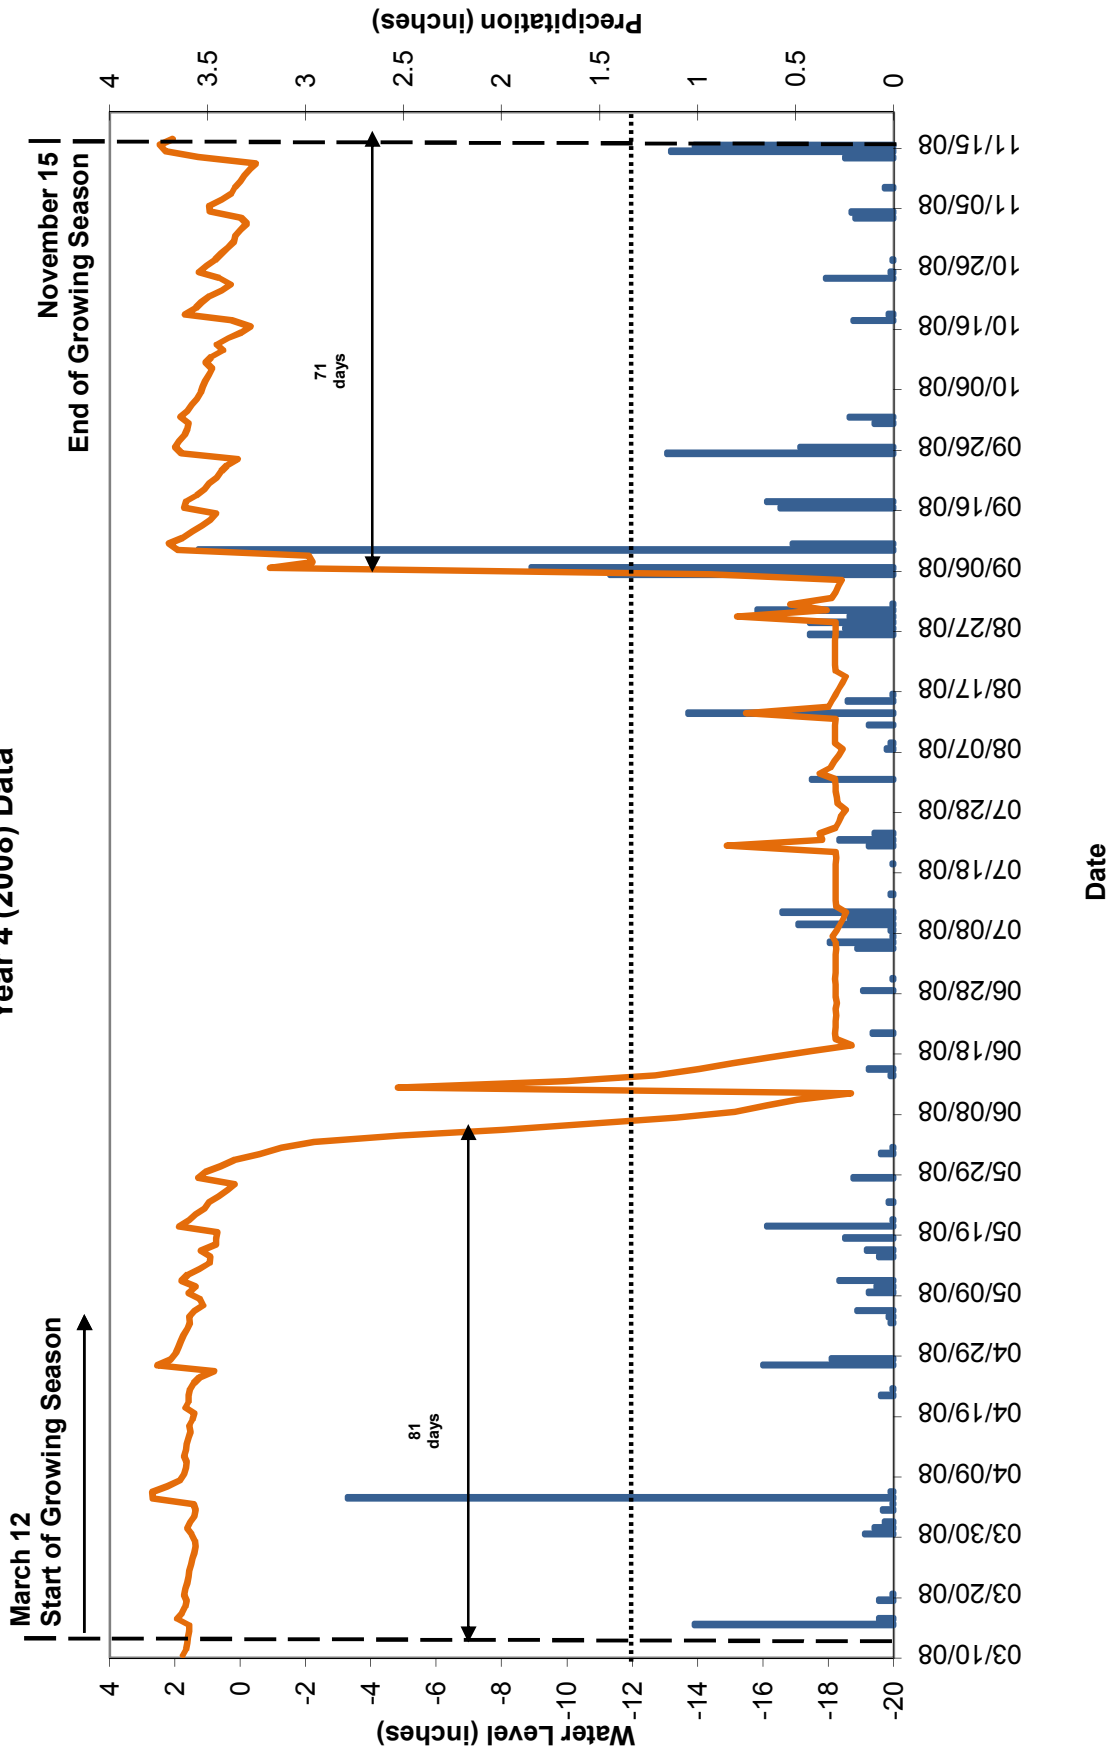


Sleepy Creek Gauge 7 Year 4 (2008) Data

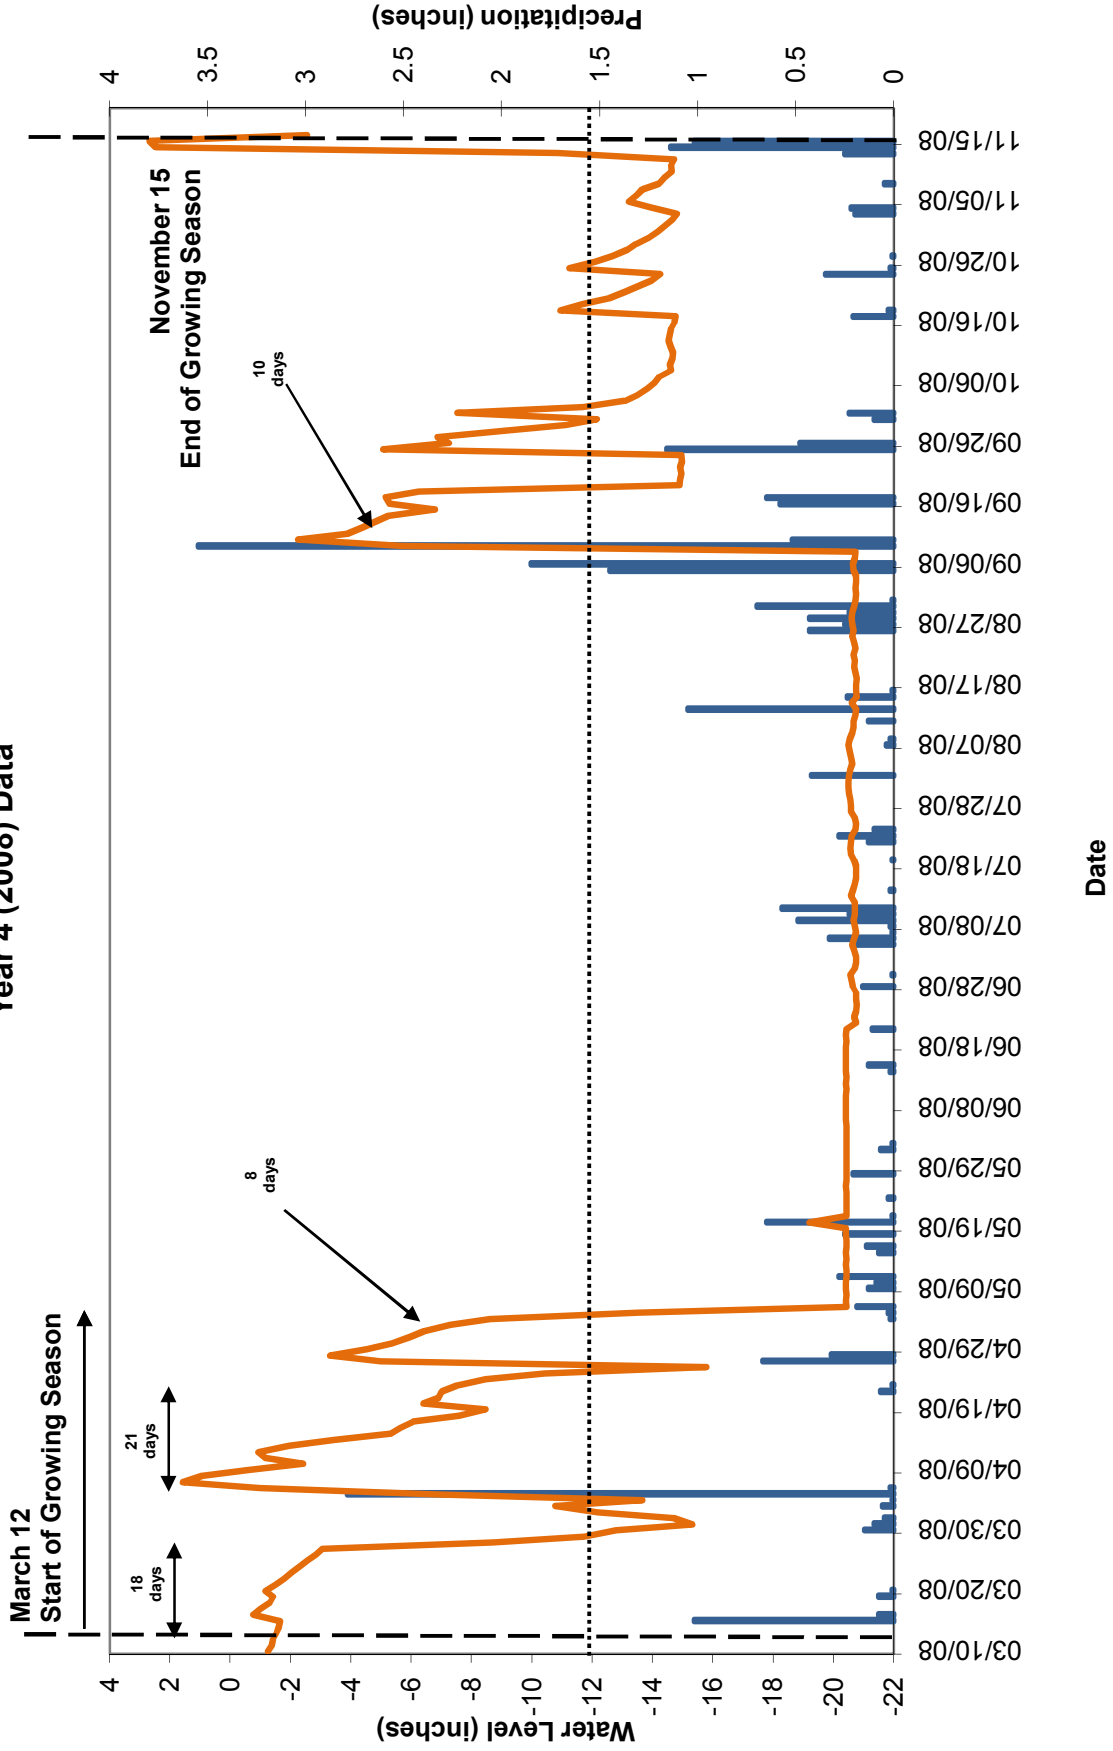


Sleepy Creek Gauge 8 Year 4 (2008) Data

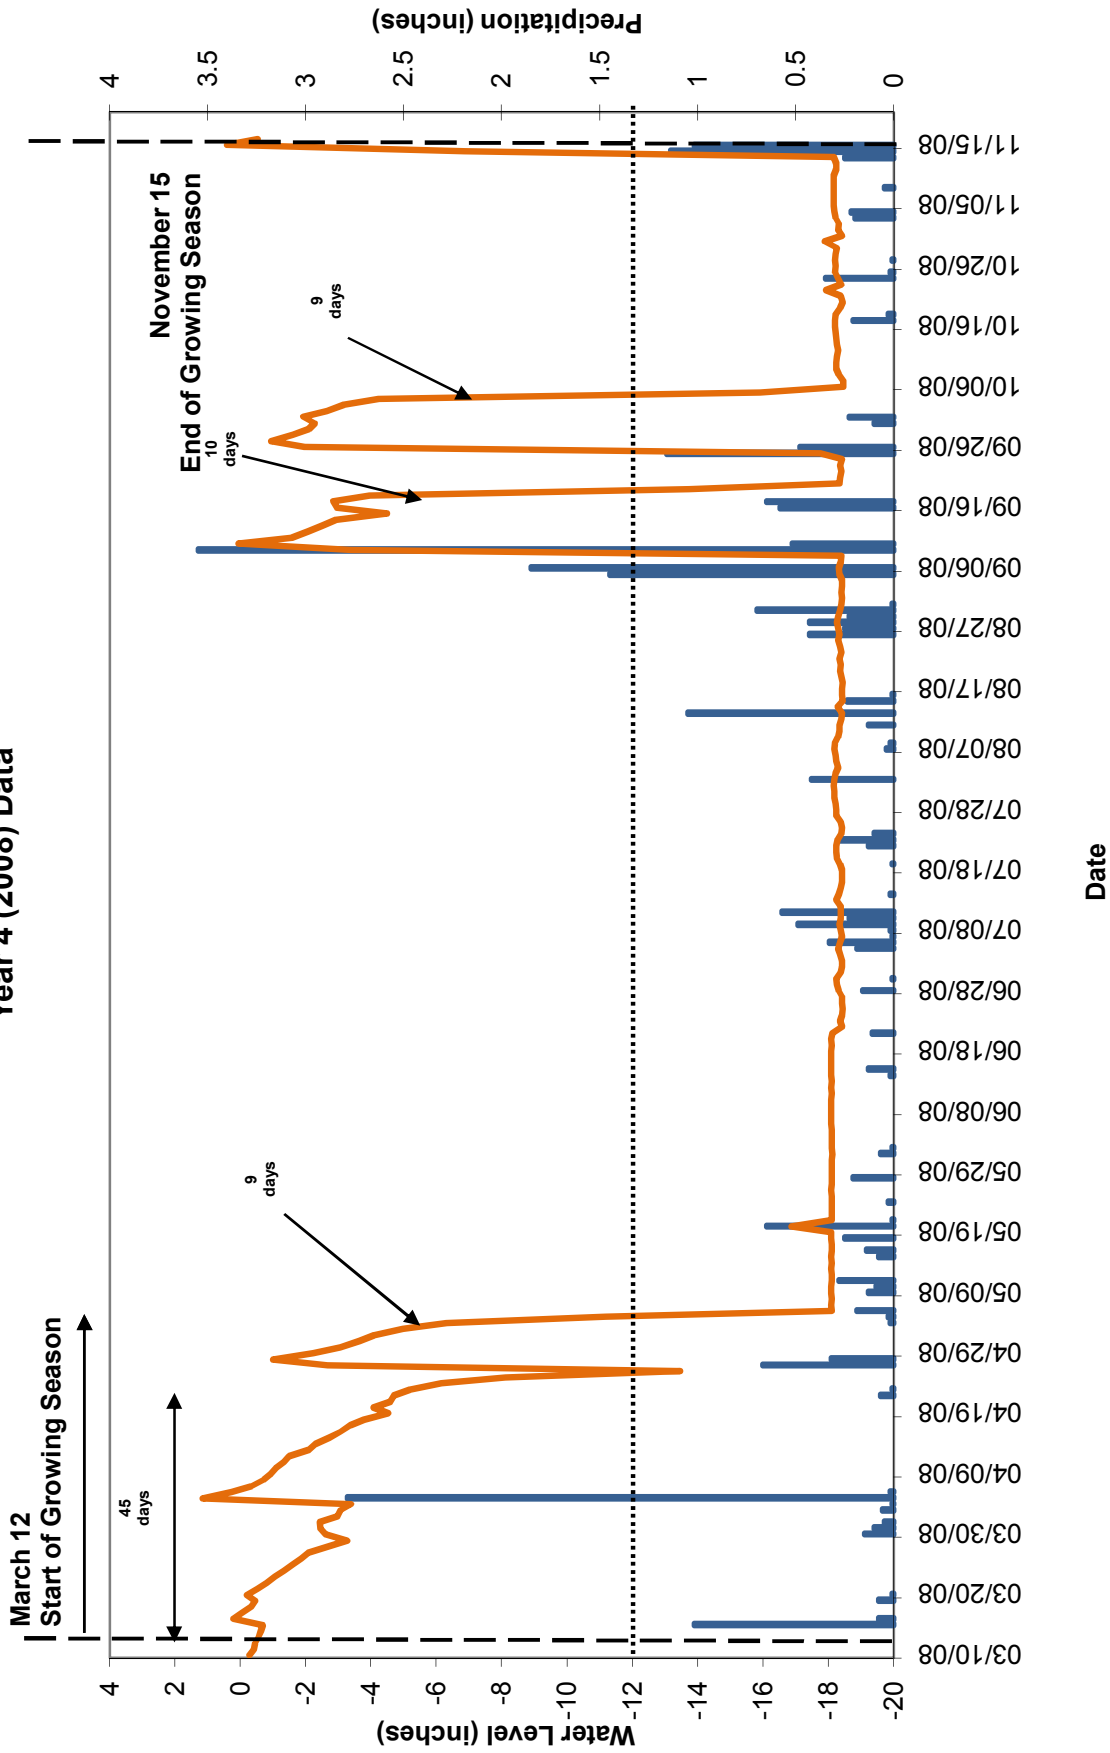


Sleepy Creek Gauge 9 Year 4 (2008) Data

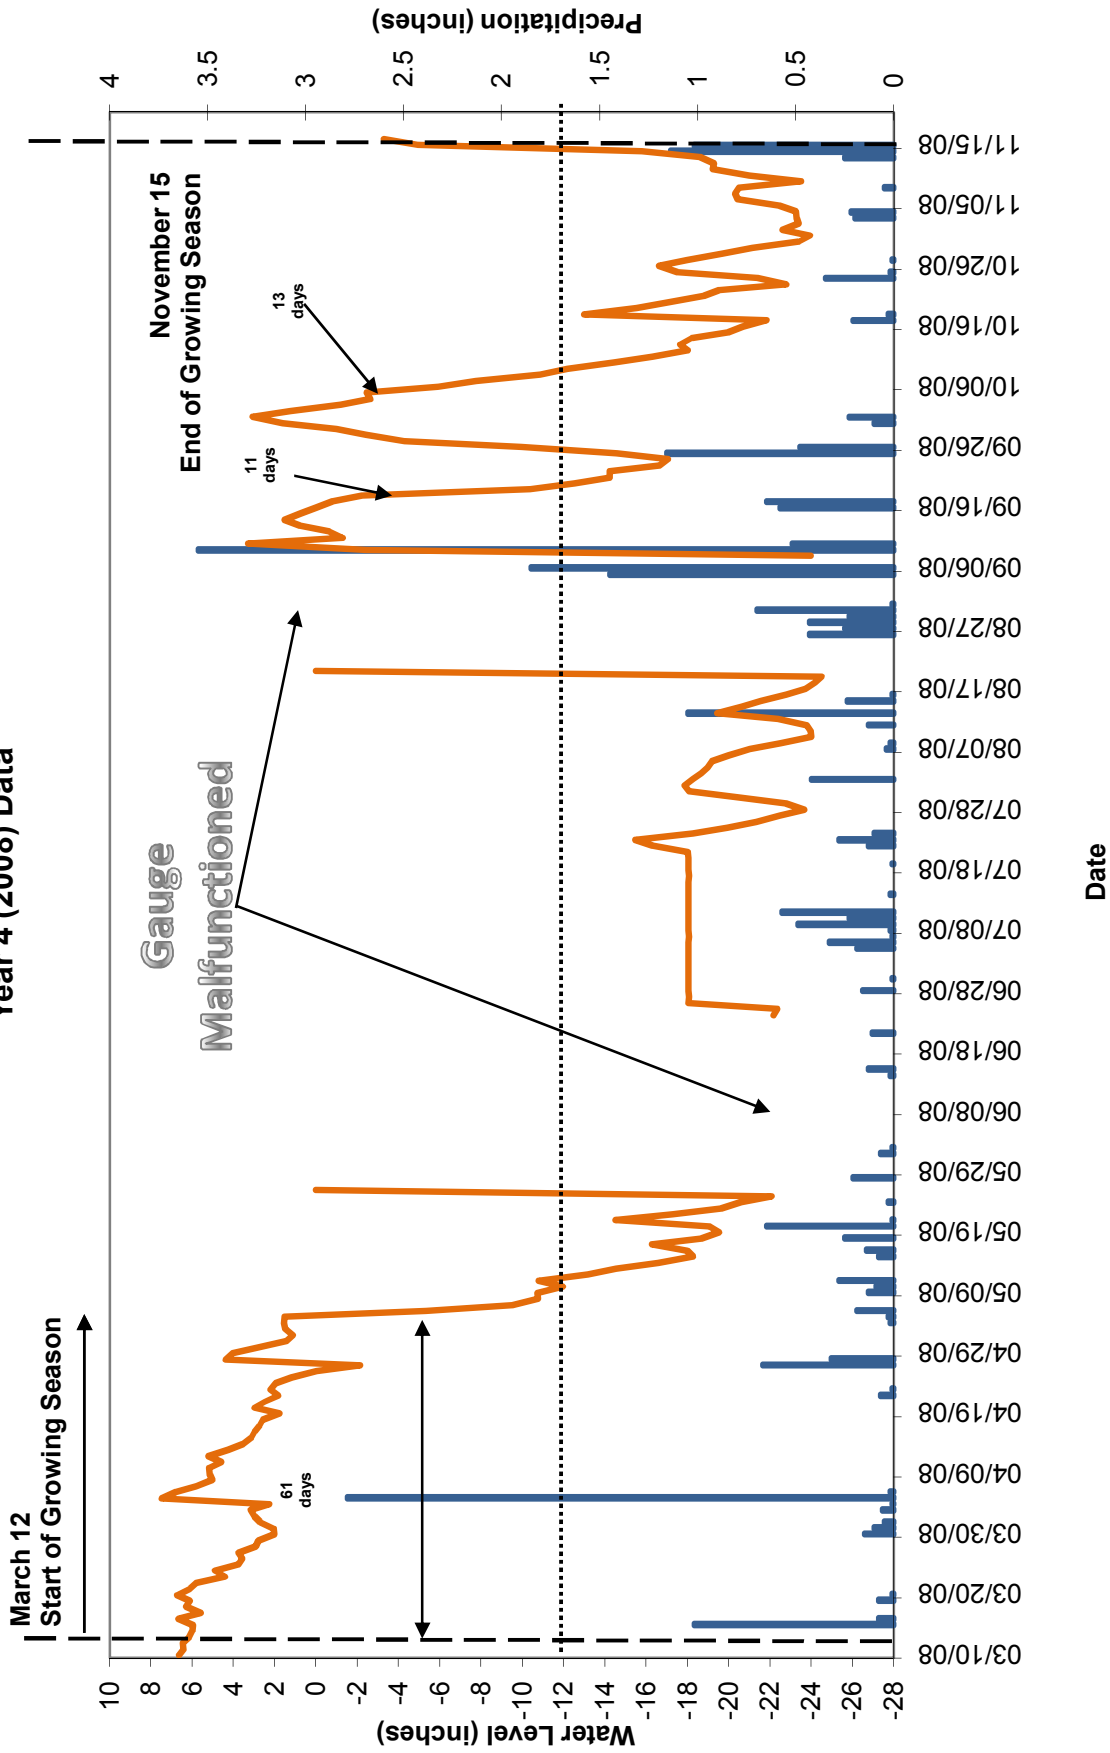


Sleepy Creek Gauge 10 Year 4 (2008) Data

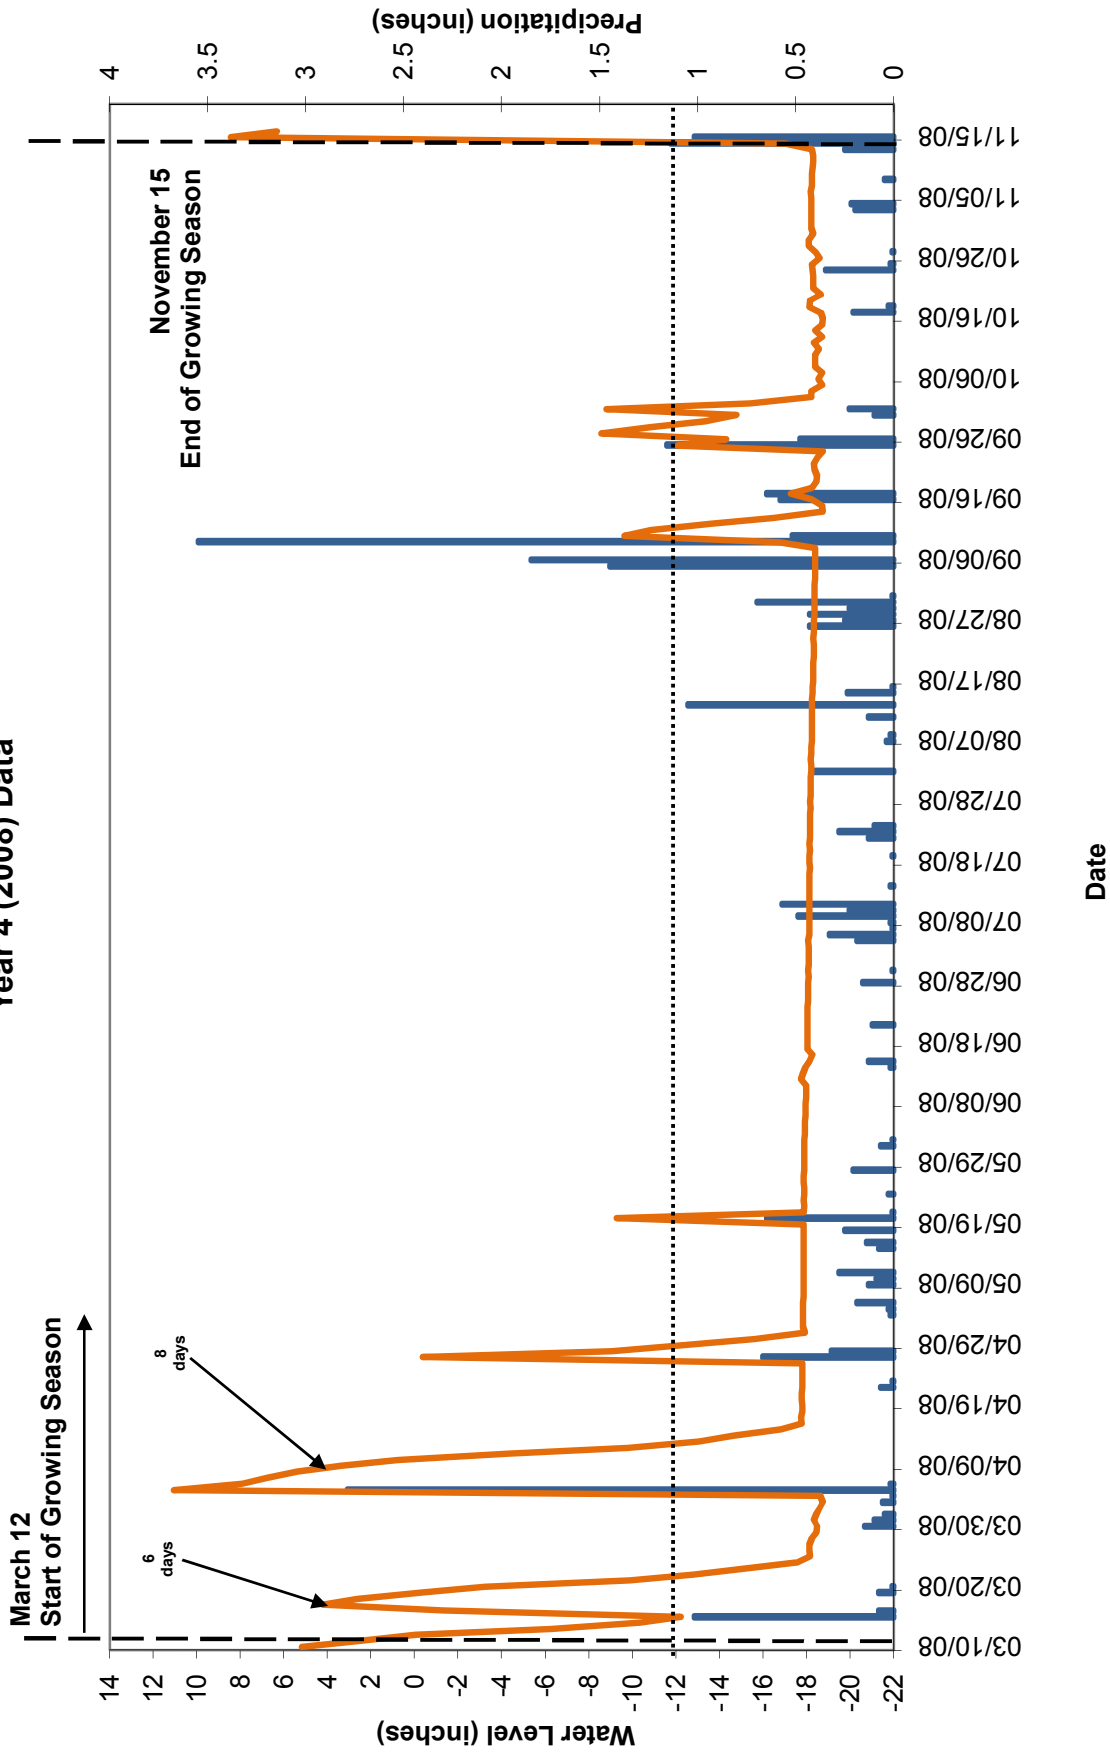


Sleepy Creek Gauge 11 Year 4 (2008) Data

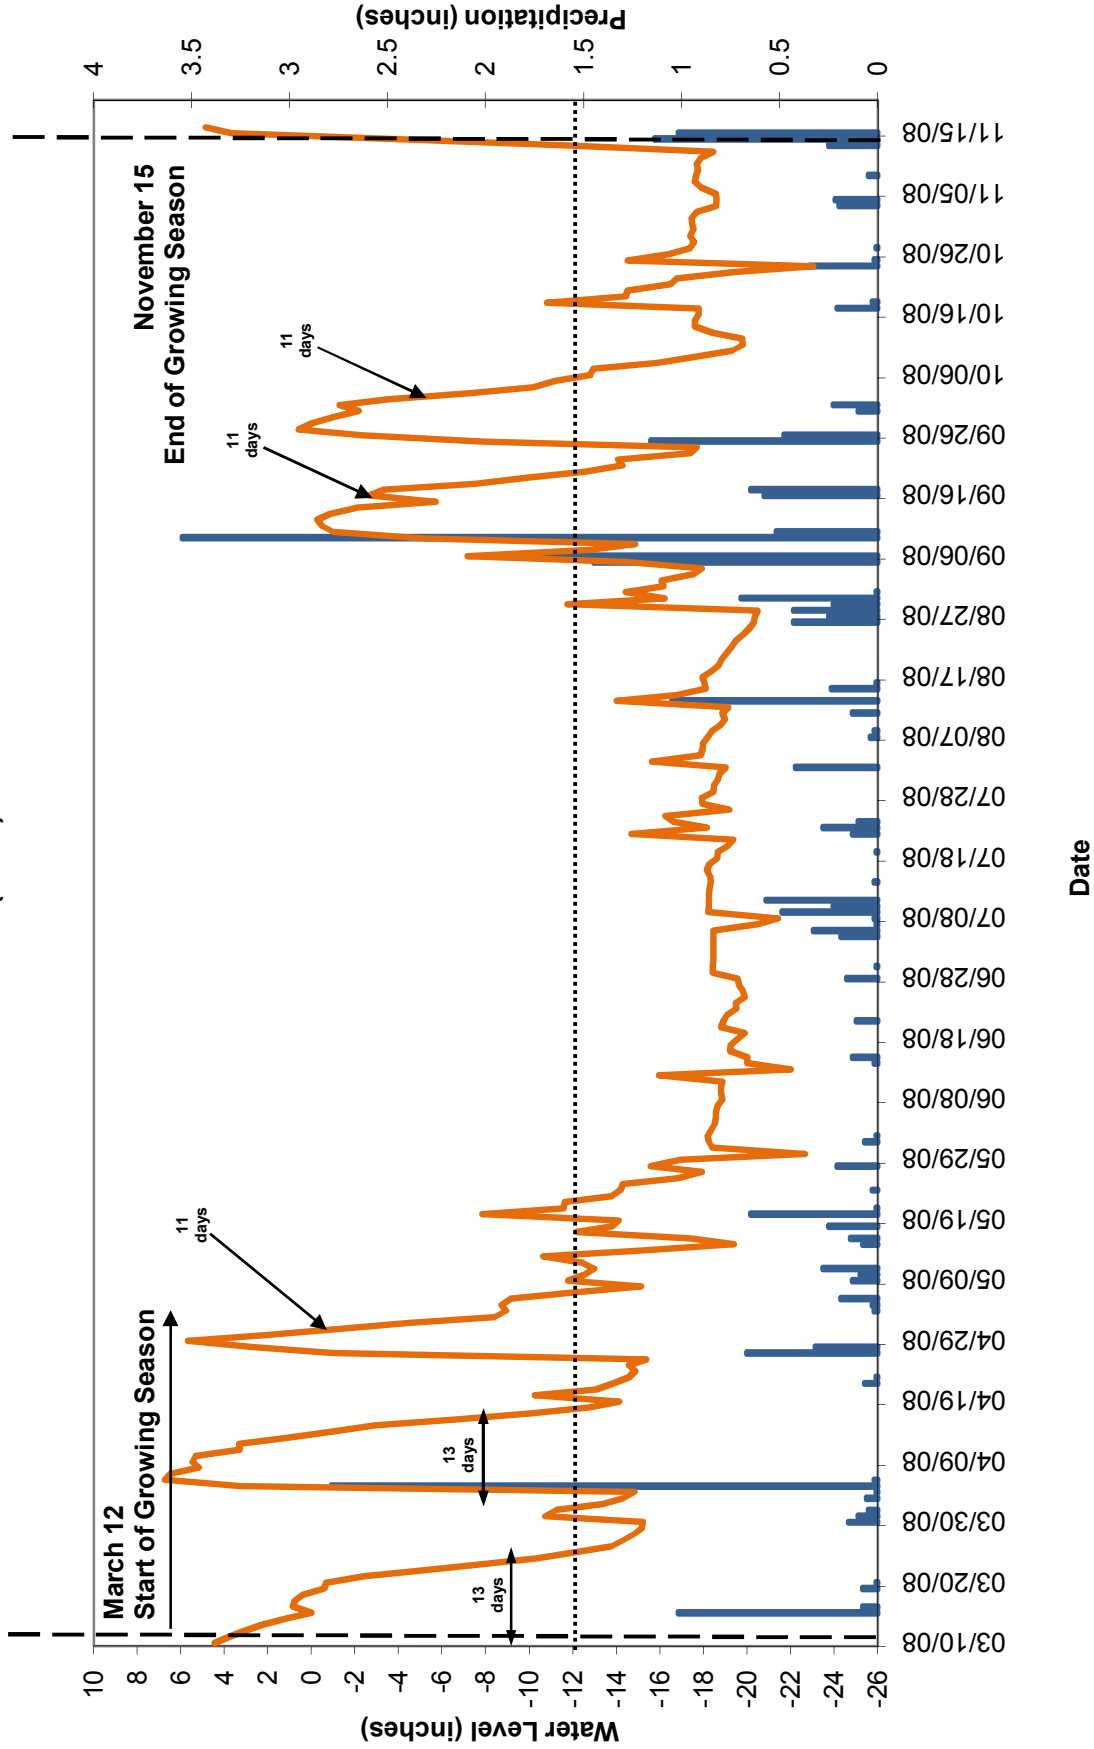


Sleepy Creek Gauge 12 Year 4 (2008) Data

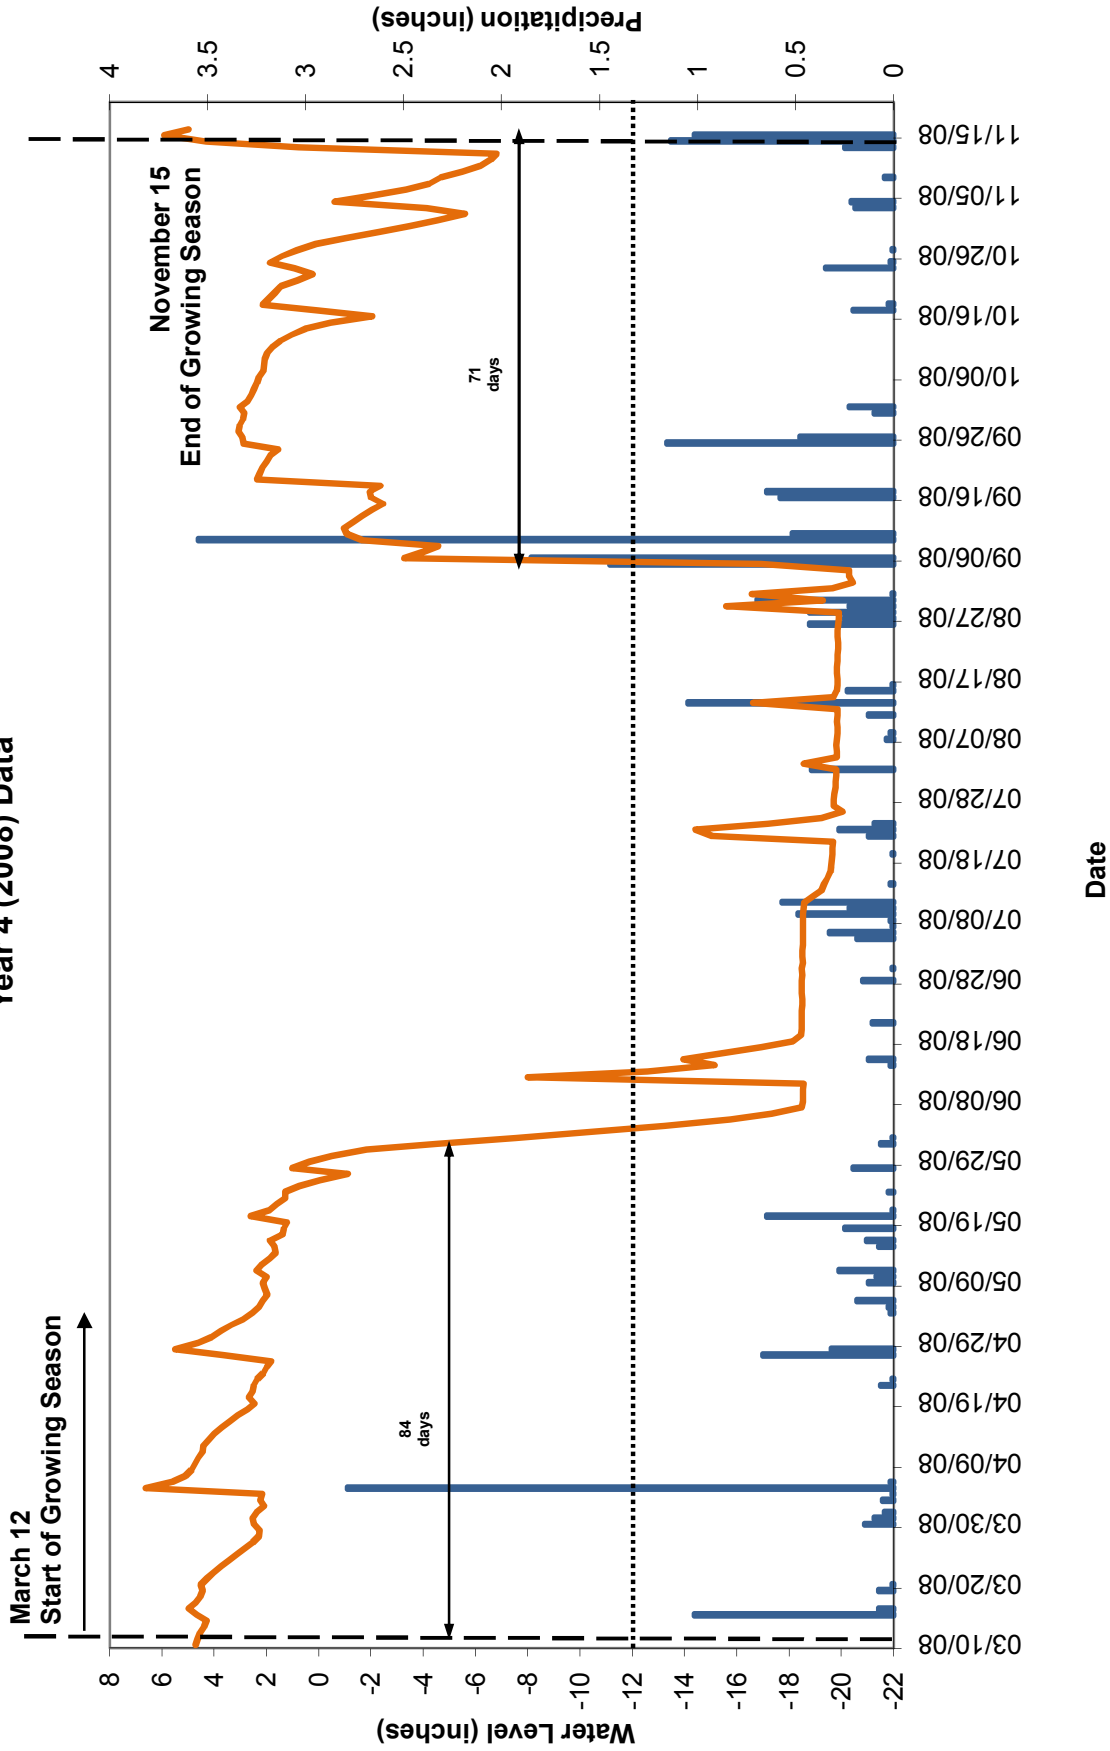


Sleepy Creek Gauge 13 Year 4 (2008) Data

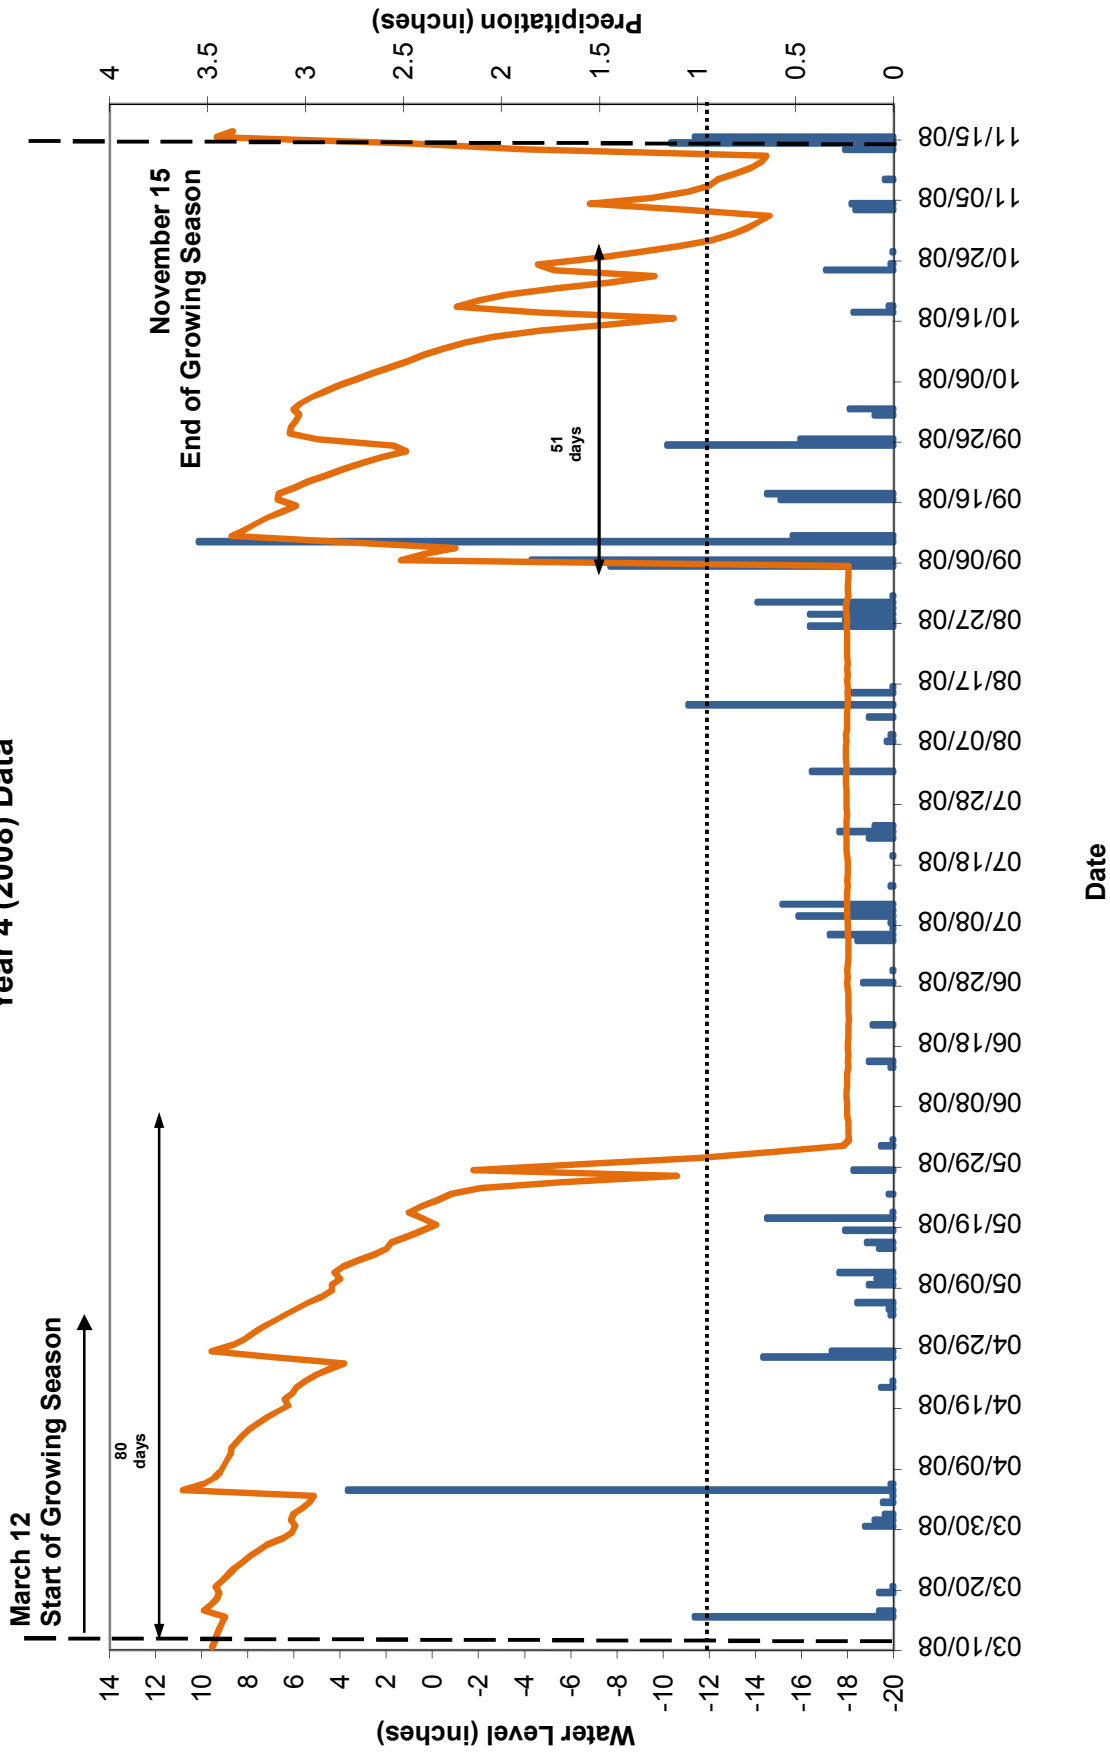


Sleepy Creek Gauge 14 Year 4 (2008) Data

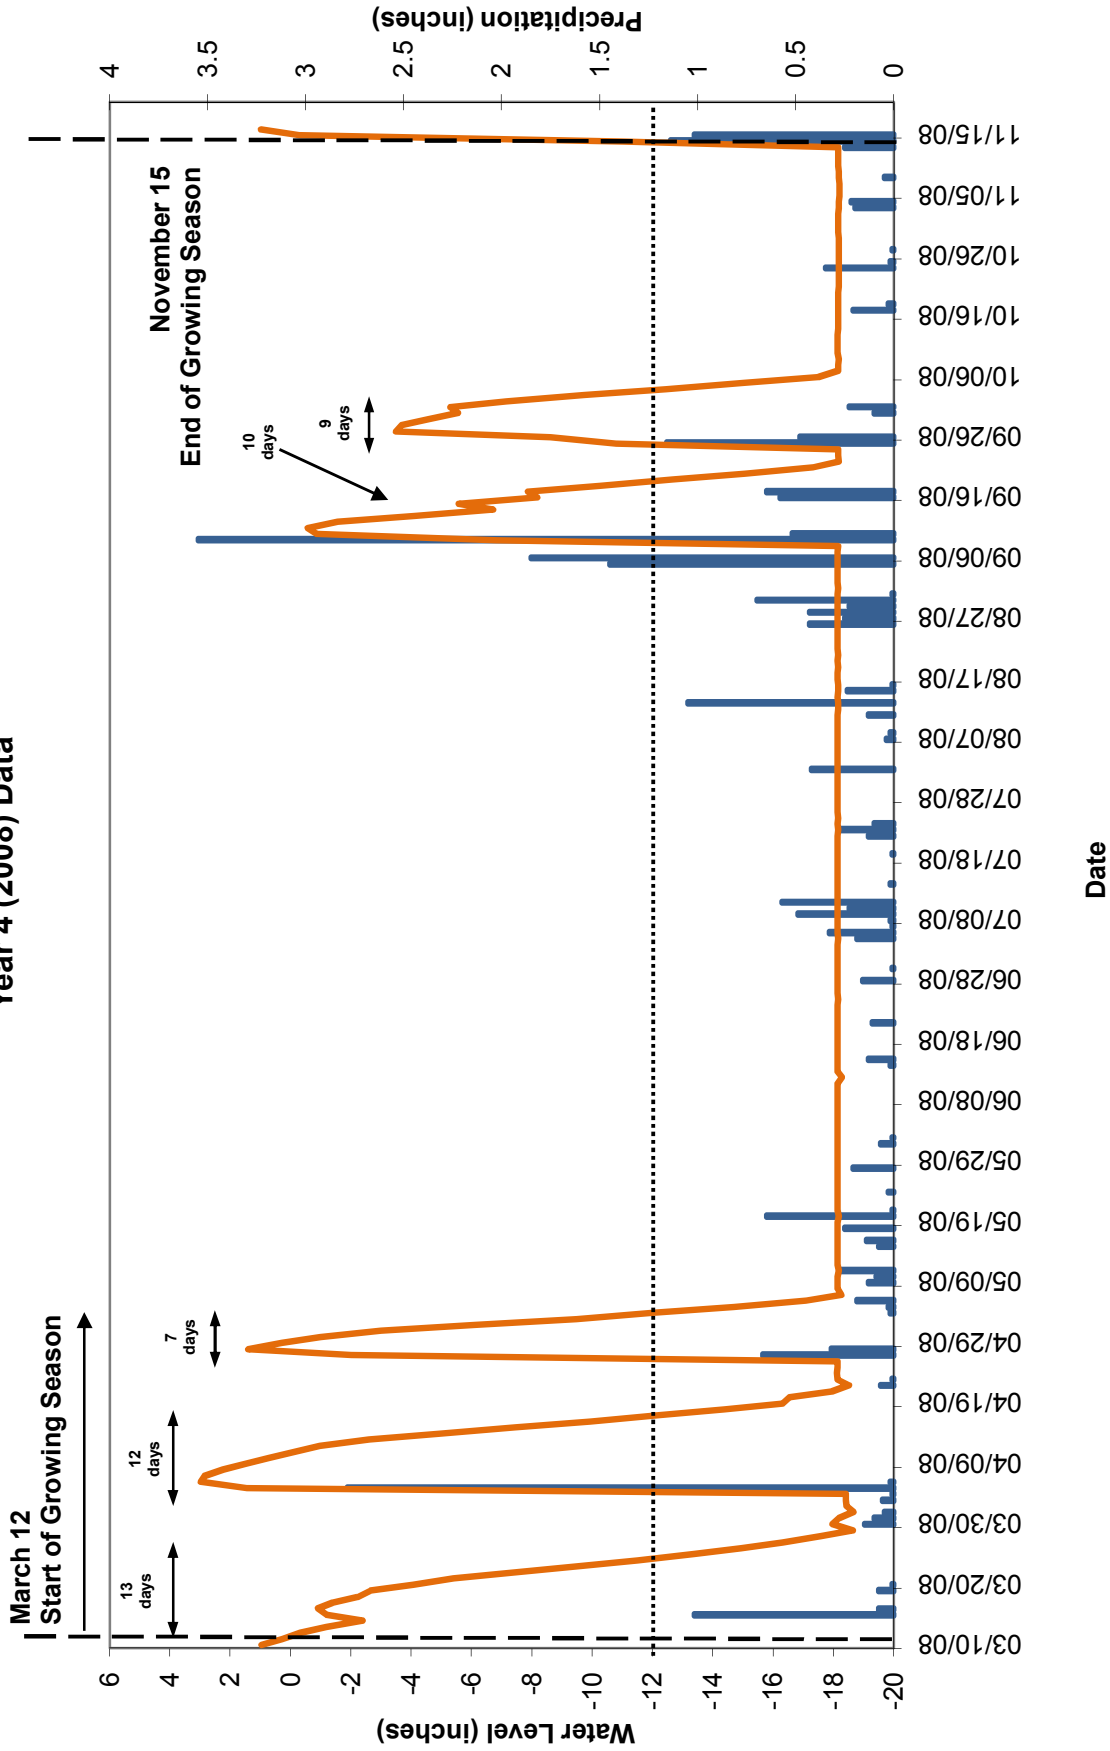


Sleepy Creek Gauge 15 Year 4 (2008) Data

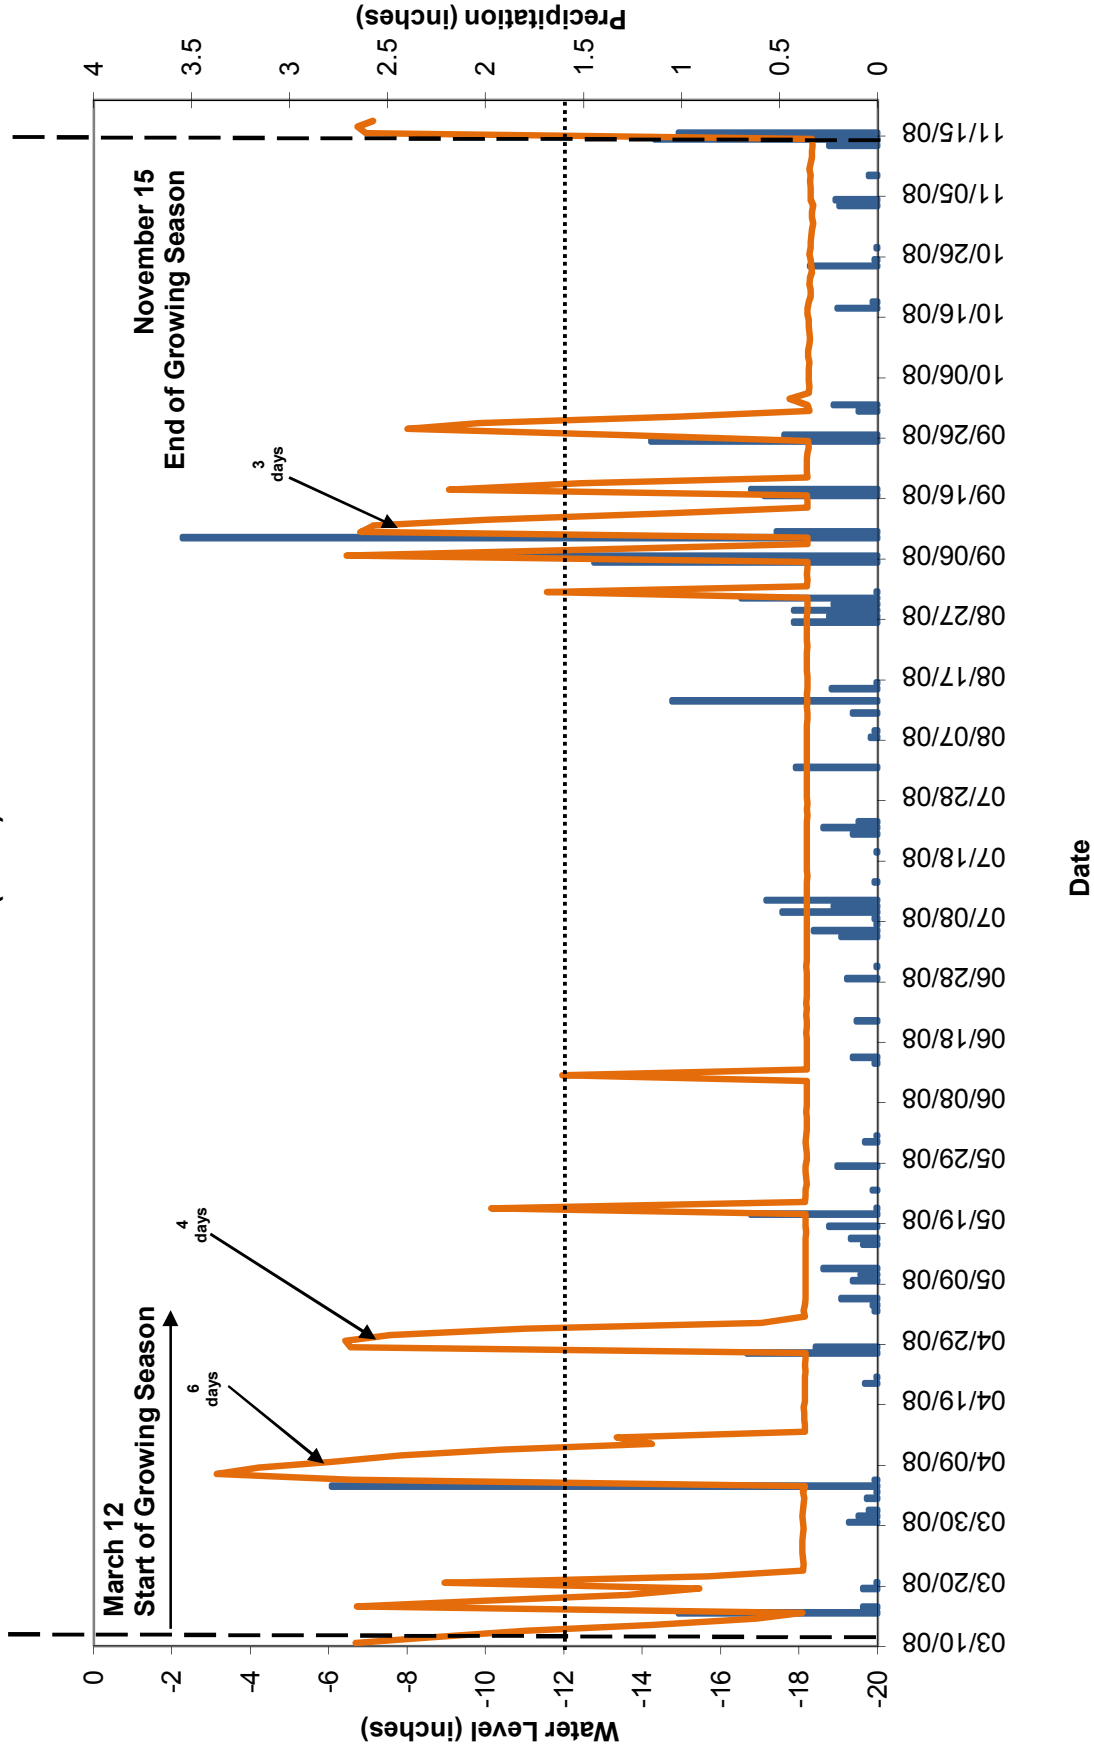

Sleepy Creek Gauge 16 Year 4 (2008) Data

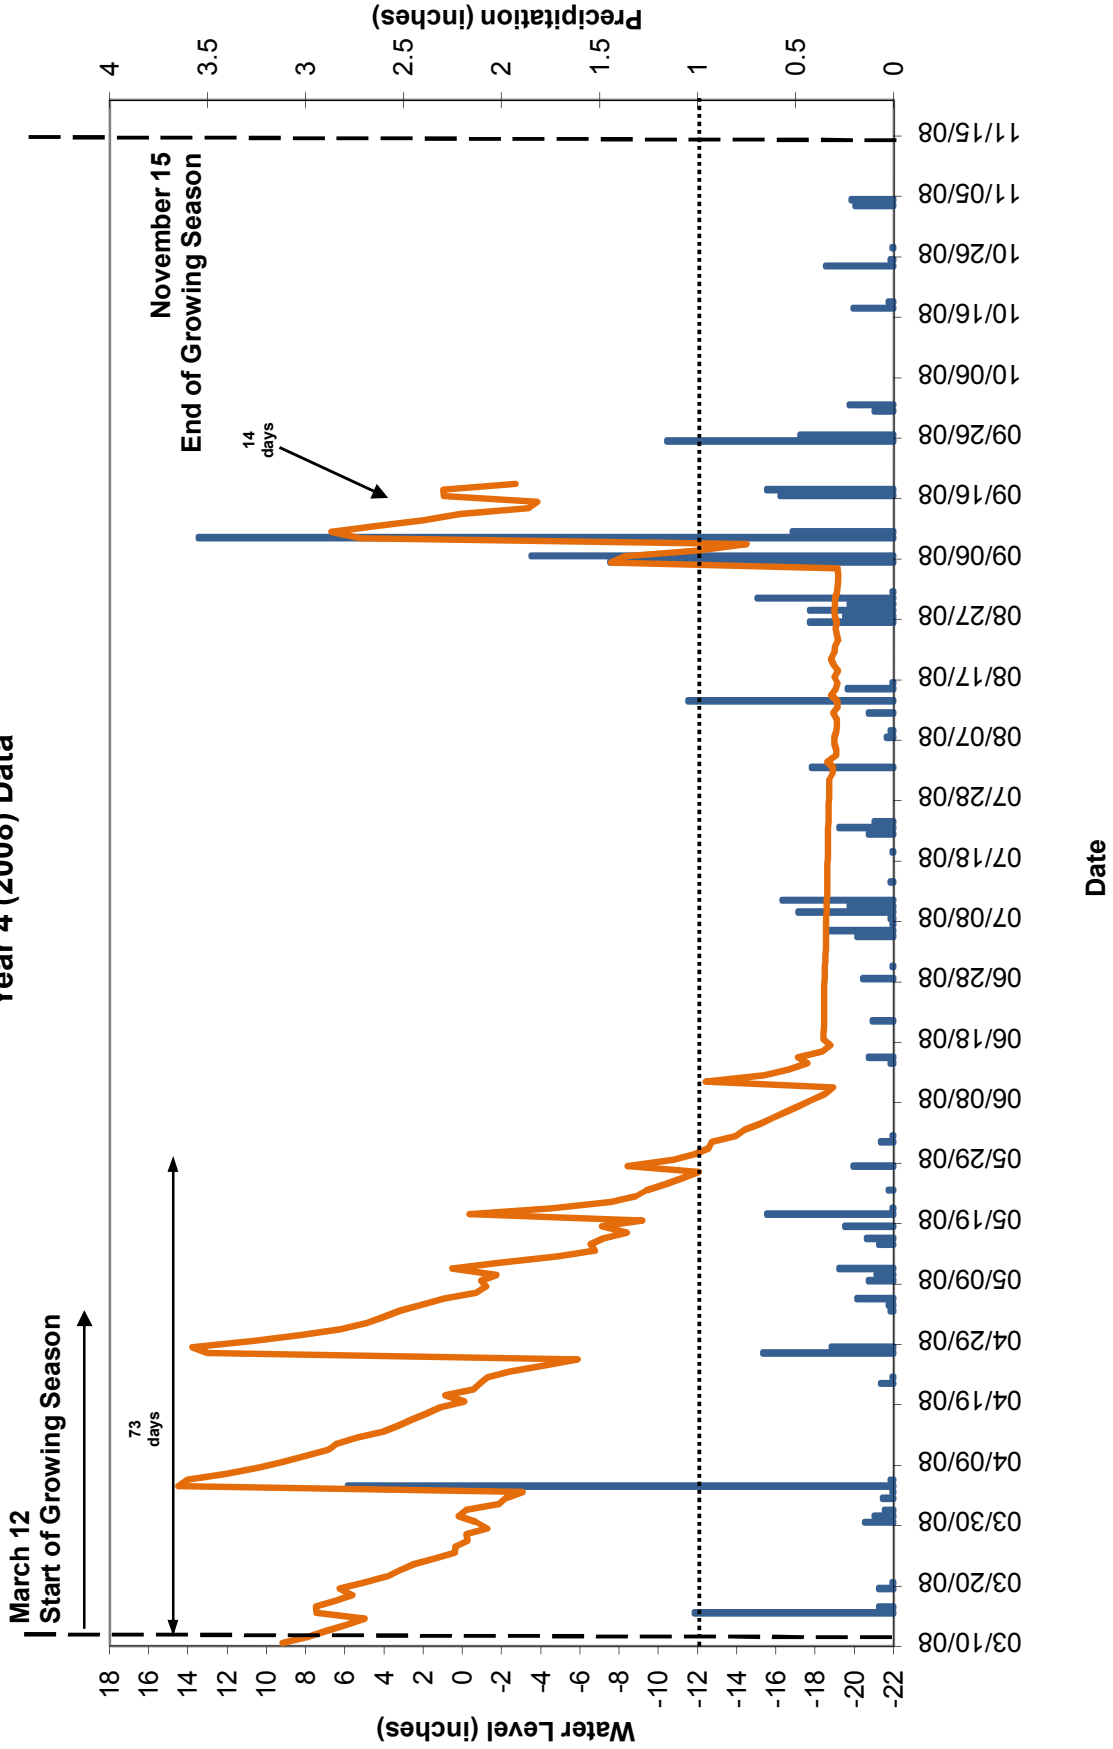





Sleepy Creek Gauge Reference Year 4 (2008) Data

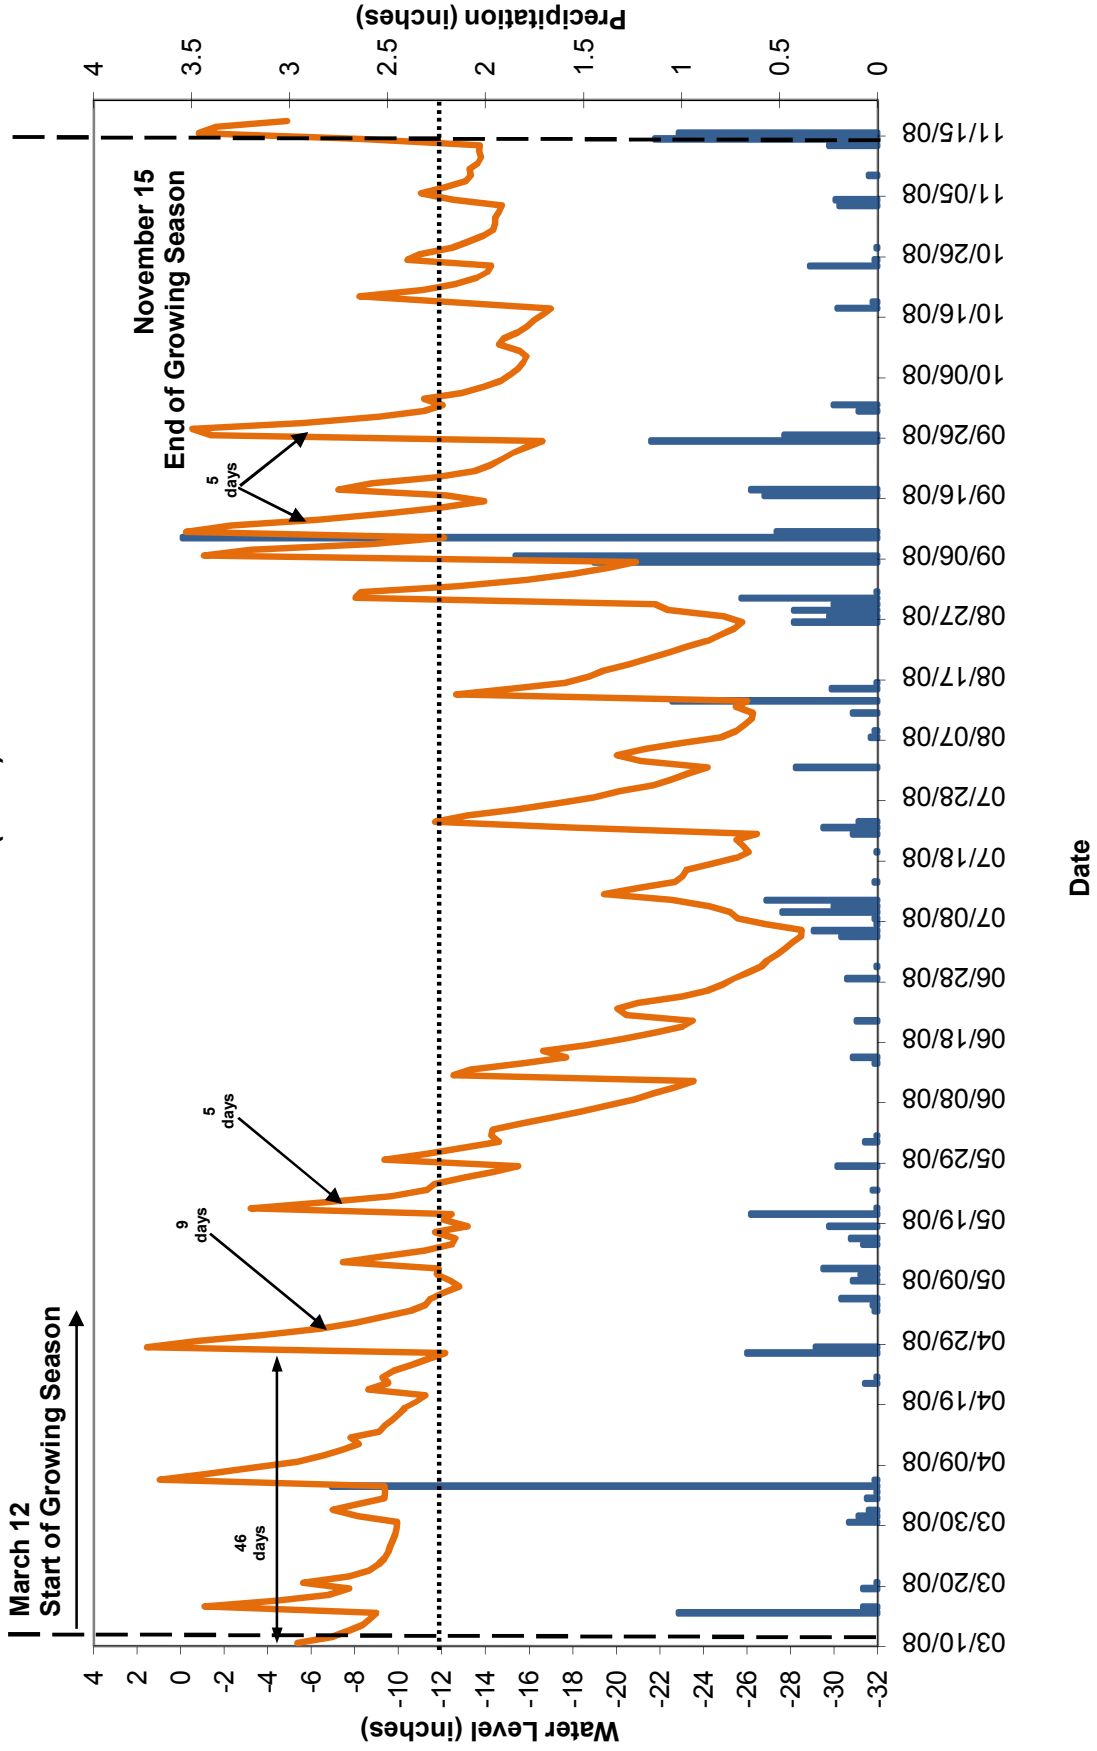

APPENDIX B

VEGETATION PLOT PHOTOGRAPHS

**Sleepy Creek Restoration Site
Vegetation Plot Photographs
Year 4 (2008) Annual Monitoring
Photos taken late August-early September 2008**

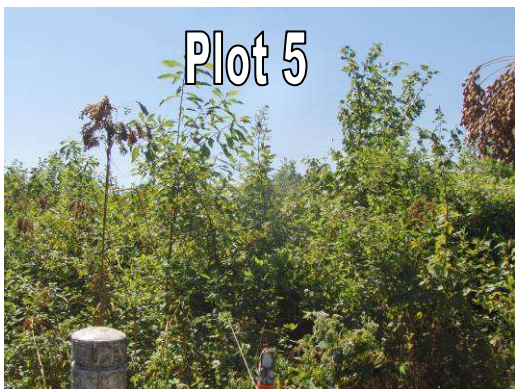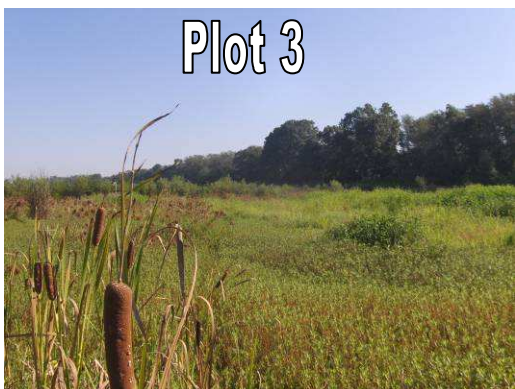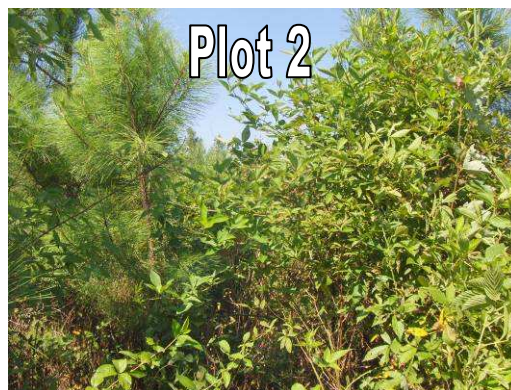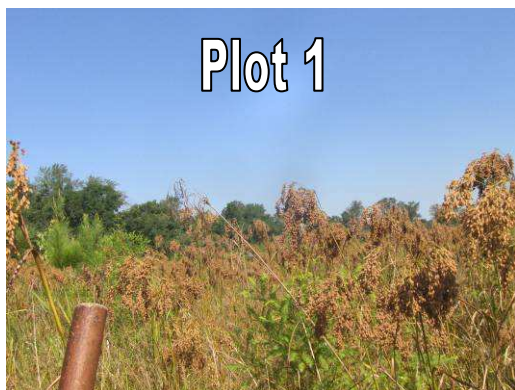

**Sleepy Creek Restoration Site
Vegetation Plot Photographs
Year 4 (2008) Annual Monitoring
Photos taken late August-early September 2008 (continued)**

