

Harrell Stream and Wetland Restoration Site Monitoring Report – MY01 Edgecombe County, NC



Submitted to:



NCEEP, 1652 Mail Service Center, Raleigh, NC 27699-1652

December 2008



**Landmark Center II, Suite 220
4601 Six Forks Road
Raleigh, NC 27609
Phone: (919) 783-9214
Fax: (919) 783-9266**

**Project Manager: Gary M. Mryncza, P.H., P.E.
Email: gmryncza@kci.com**

TABLE OF CONTENTS

1.0	PROJECT BACKGROUND.....	1
1.1	Project Structure, Restoration Type, and Approach	1
1.2	Location and Setting	1
1.3	Project History and Background.....	3
1.4	Monitoring Plan View.....	6
2.0	PROJECT CONDITIONS AND MONITORING RESULTS.....	13
2.1	Vegetation Assessment	13
2.2	Stream Assessment	13
2.2.1	Bankfull Events.....	14
2.2.2	Quantitative Measures Summary Tables	15
2.3	Wetland Assessment.....	22
2.3.1	Wetland Criteria Attainment Tables	22
3.0	SUCCESS CRITERIA.....	22
4.0	MAINTENANCE.....	23

LIST OF TABLES

Table I.	Project Structure Table	3
Table II.	Project Activity and Reporting History	3
Table III.	Project Contact Table.....	4
Table IV.	Project Background Table.....	5
Table V.	Hydrological (Bankfull) Verifications.....	14
Table VI.	Baseline Morphology and Hydraulic Summary	15
Table VII.	Morphology and Hydraulic Monitoring Summary	19
Table VIII.	Wetland Criteria Attainment.....	22

LIST OF FIGURES

Figure 1.	Vicinity Map.....	2
Figure 2.	Monitoring Plan View.....	6

APPENDIX A – VEGETATION DATA

A1. Vegetation Data Tables and Monitoring Data Sheets.....25

APPENDIX B – STREAM AND WETLAND PHOTOS

B1. Stream and Wetland Photo Stations.....90
B2. Representative Stream Problem Area Photos108

APPENDIX C – GEOMORPHOLOGIC AND HYDROLOGIC DATA

C1. Stream Cross-Sections111
C2. Stream Longitudinal Profiles125
C3. Stream Pebble Counts129
C4. Stream and Wetland Hydrographs143
C5. Precipitation 30-70 Percentile Graph.....151

APPENDIX D – CURRENT CONDITIONS PLAN VIEW

D1. Current Conditions Plan View153

EXECUTIVE SUMMARY

The Harrell Stream and Wetland Restoration Site is a full-delivery project that was developed for the North Carolina Ecosystem Enhancement Program (EEP). Construction was completed in September 2007 on an Unnamed Tributary to Swift Creek and 15.0 acres of Coastal Plain Small Stream Swamp wetland community. The 441-acre watershed at the downstream limits of the project stream and the 57-acre watershed draining into the project wetland are located within the USGS 14-digit HUC 03020101130090 and the NCDWQ Sub-basin 03-03-02 in the Tar-Pamlico River Basin. The project restored 6,808 linear feet of channel using a combination of Priority 2 and 3 approaches, and 15.0 acres of Coastal Plain Small Stream Swamp wetland community, generating 6,808 stream mitigation units and 15.0 wetland mitigation units. The stream design addressed vertical instability problems and a lack of bed variability by stabilizing stream banks, installing in-stream structures, adjusting stream planform, and replanting the riparian areas with native vegetation. The wetland was restored by filling ditches, creating microtopography, and planting native trees and shrubs. This report describes the results from the findings of the first year of monitoring that took place in 2008.

The riparian buffer was planted with twelve different species of bare root trees and shrubs and three different species of live stakes. The restored wetland was planted with eleven different species of bare root trees and shrubs. Vegetation monitoring plots were established during the as-built survey and included 18 monitoring plots placed throughout the stream buffer and 12 monitoring plots installed in the restored wetland. Vegetation must meet a minimum survival success rate of 320 stems/acre after five years. These plots were monitored during the first-year monitoring period. The first-year monitoring counted an average of 607 stems/acre in the stream plots and 533 stems/acre in the wetland plots. The first-year monitoring found the vegetation component of the project to be on track to meeting the success criteria.

The stream assessment completed during first-year monitoring found the stream to be stable and functioning properly. Channel dimensions have not changed significantly from the as-built conditions over the course of the growing season. Small portions of localized bed erosion and aggradation have been noted during the first-year monitoring. These areas have been documented in the Current Conditions Plan View. The on-site stream gauges have recorded 3 bankfull events since the project was constructed in September 2007.

During the 2008 monitoring year, wetland hydrology was achieved at all four wells in the restoration area. Groundwater was within 12 inches of the soil surface in excess of 12 consecutive days (5% of the growing season) at each well, with two of the gauges having groundwater within 12 inches of the soil surface for more than 12.5% of the growing season.

The daily rainfall data depicted on the gauge data graphs were obtained from the on-site precipitation gauge. The precipitation gauge was installed on the site prior to project implementation. The daily rainfall data obtained from a local weather station shows that the area had below average rainfall during the growing season in 2008 and correlated to the precipitation data recorded on-site.

1.0 PROJECT BACKGROUND

Project Goals and Objectives

The goals and objectives of the restoration project are as follows:

Restoration Goals:

- Protect aquatic resources from excess nutrients, sediment, and other pollutants coming from the agricultural watershed.
- Reestablish terrestrial and aquatic habitat and connect the site to the existing floodplain corridor along Swift Creek.

Restoration Objectives:


- Restore 6,808 linear feet of stable stream channel with the appropriate pattern, profile, and dimension that can support a sand transport system.
- Connect the stream to a functioning floodplain.
- Fill and plug ditches in the drained hydric soils to restore saturated hydrologic conditions for 5% of the growing season.
- Plant tree species typical of a Coastal Plain Small Swamp Stream along the stream riparian corridor and floodplain as well as in the restored wetland.

1.1 Project Structure, Restoration Type, and Approach

Prior to restoration, UT to Swift Creek had been channelized and straightened since at least 1948. The entire site, including where the wetland was restored, was under agricultural production. There were fields adjacent to the stream and the wetland that had been drained by a network of ditches. There were no remaining vegetated buffers or in-stream features in the channel and the banks were nearly vertical. The channel was characterized as having poor streambed variability and habitat diversity. Restoration of 6,808 linear feet of channel was accomplished utilizing a combination of Priority Levels 2 and 3 (Table 1). Reach 1 (Station 10+00 to 22+26) was restored using a Priority Level 3 approach. The restoration of a B5c channel with a sinuosity of 1.06 was accomplished by building a bankfull channel with a higher width/depth ratio than the existing stream, creating distinct bed features by adding pools and riffles to the profile, and grading back the upper slopes to create an appropriate valley for the stream. Reaches 2, 3, and 4 (Stations 22+26 to 36+91, 36+91 to 51+82, and 51+82 to 78+80, respectively) were restored to a C5 channel with a Priority Level 2 restoration. The restoration established a bankfull channel with a new floodplain where the designed bankfull stage equals the new floodplain elevation (bank height ratio=1.0). Reaches 2, 3, and 4 have sinuosity values of 1.07, 1.23, and 1.10, respectively. The four different reaches are shown in Figure 2.



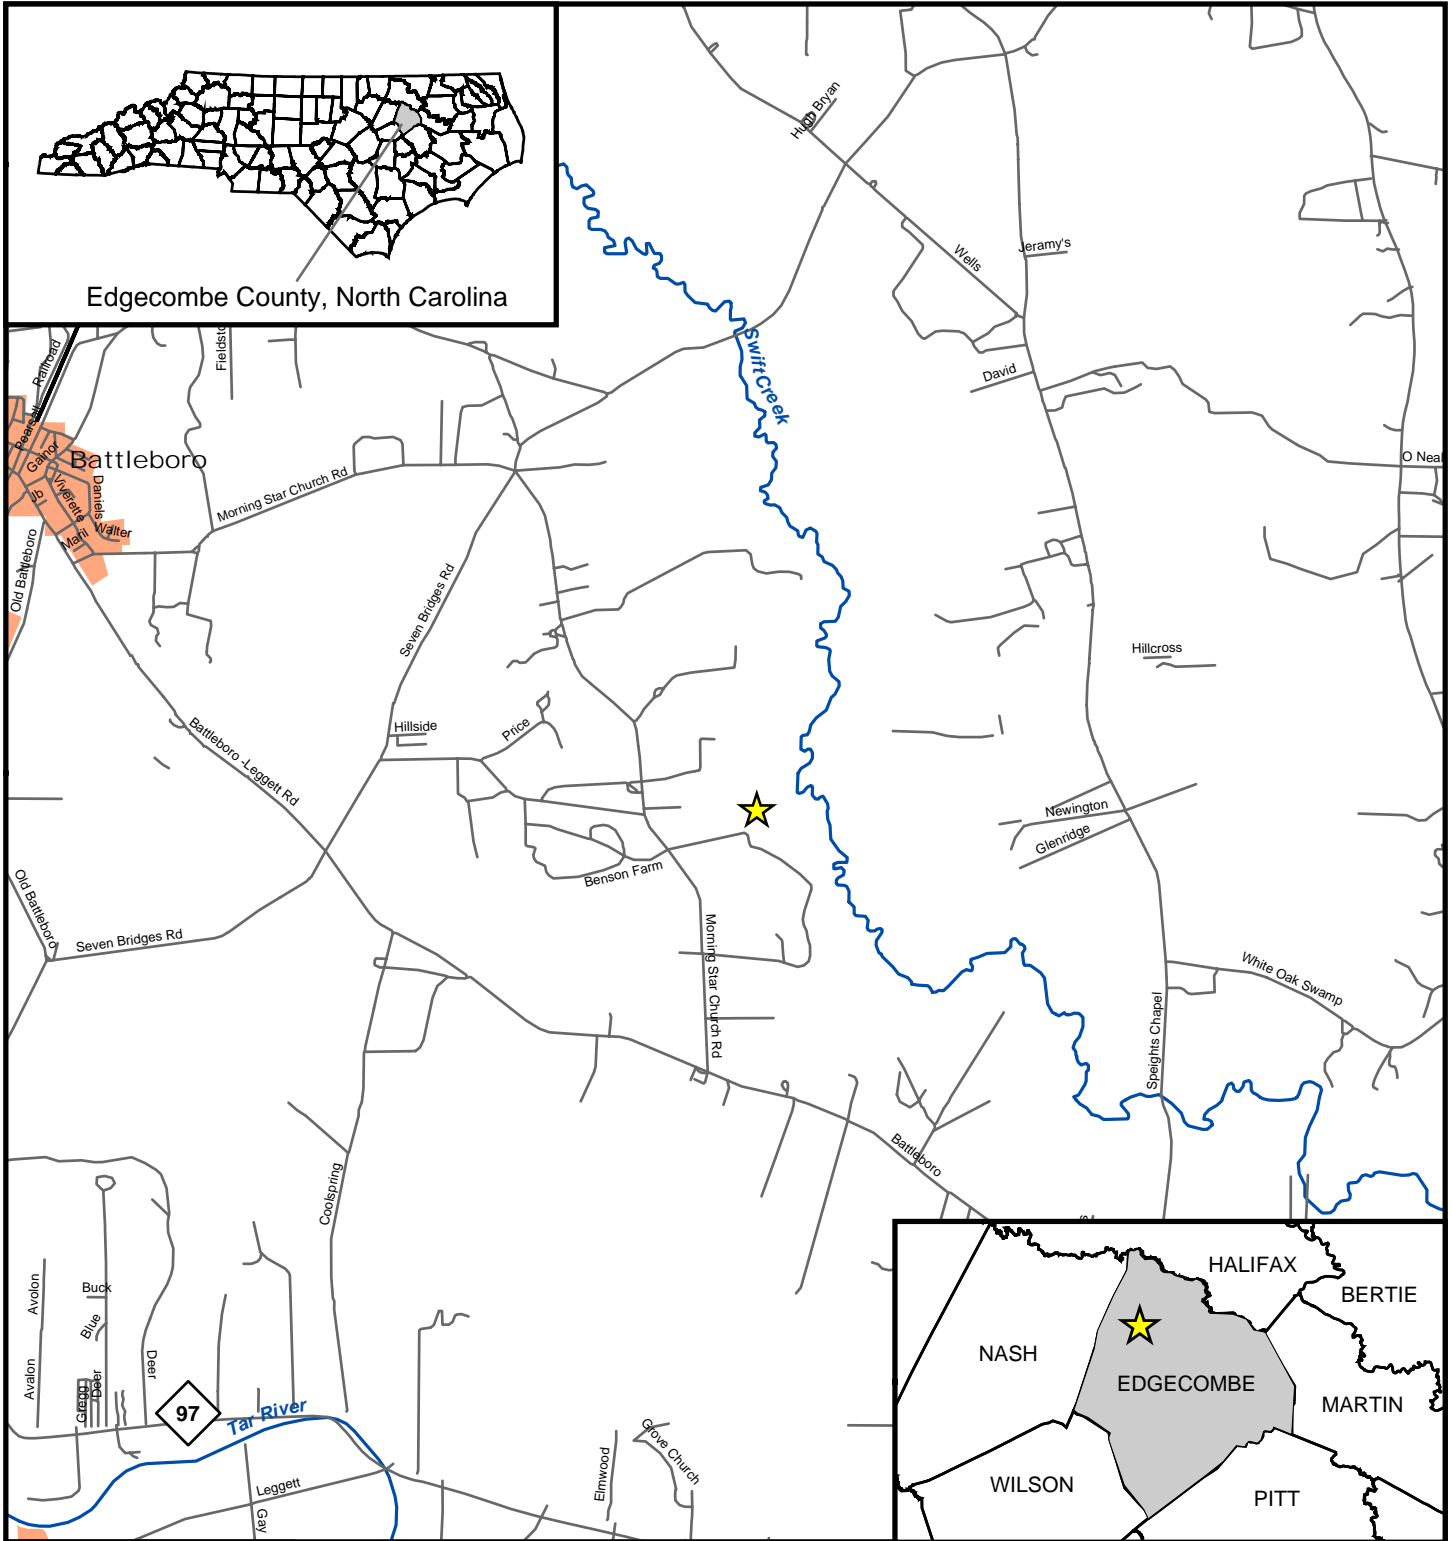

1.2 Location and Setting

The Harrell Stream and Wetland Restoration Site is located approximately six miles northeast of Rocky Mount, North Carolina in Edgecombe County (Figure 1). The latitude and longitude of the project site are 36.0201 North and 77.6807 West (WGS1984). To reach the site from Raleigh, proceed east on U.S. Route 264-East/64-East (US 264E/64E) for approximately 17 miles. Continue on US 64E for another 30 miles. Take the U.S. Route 301 Bypass and then U.S. Route 301 (US 301) north into Battleboro. Make a right onto Battleboro-Leggett Road and then turn left onto Morning Star Church Road just outside of town. Proceed through Cherry Crossroads and continue for 2.25 miles. The project site is on the left side of Morning Star Church Road and is directly opposite the junction with Benson Farm Road.



Edgemcombe County, North Carolina

Figure 1. Vicinity Map

-  Project Site Location
-  Major Streams and Rivers
-  Municipalities
-  Roads



1:63,360

1 inch equals 1 miles







Table III. Project Contact Table	
Harrell Stream and Wetland Restoration	
Design Firm	KCI Technologies, Inc. Landmark Center II, Suite 220 4601 Six Forks Rd. Raleigh, NC 27609 Contact: Mr. Gary Mryncza Phone: (919) 783-9214 Fax: (919) 783-9266
Construction Contractor	Environmental Technologies and Construction Landmark Center II, Suite 220 4601 Six Forks Rd. Raleigh, NC 27609 Contact: Mr. Ryan McDavitt Phone: (919) 783-9214 Fax: (919) 783-9266
Planting Contractor	H & J Forest Services PO Box 458 Holly Ridge, NC 28445 Phone: (910) 512-6754
Monitoring Performers	
MY-00 - MY-05	KCI Technologies, Inc. Landmark Center II, Suite 220 4601 Six Forks Rd. Raleigh, NC 27609 Contact: Mr. Adam Spiller Phone: (919) 783-9214 Fax: (919) 783-9266

Table IV. Project Background Table		
Harrell Stream and Wetland Restoration		
Project County	Edgecombe County	
Physiographic Region	Coastal Plain	
Ecoregion	Southeastern Floodplains and Low Terraces	
Project River Basin	Tar-Pamlico	
USGS HUC for Project and Reference	03020101130090 (UT to Swift Creek)	
	03040101080010 (Mitchell River)	
	03030002060140 (North Prong Creek)	
NCDWQ Sub-basin for Project and Reference	03-03-02 (UT to Swift Creek)	
	03-07-02 (Mitchell River)	
	03-06-05 (North Prong Creek)	
Drainage Area	Wetland	0.09 sq. mi.
	Stream	0.60 sq. mi.
Stream Order	Second Order	
Watershed Type (Rural, Urban, Developing, etc.)	Rural	
Watershed LULC Distribution	Urban	<1%
	Ag-Row Crop	95%
	Ag-Livestock	1%
	Forested	4%
	Water/Wetlands	<1%
Watershed impervious cover (%)	<1%	
Rosgen Classification of As-built (Stream)	B5c / C5	
Cowardin Classification (Wetland)	Palustrine - forested wetland	
NCDWQ Classification for Project	NSW, Class C	
Within EEP Watershed Plan?	No	
Any portion of the project segment upstream of a 303d listed segment?	No	
Reasons for 303d Listing or Stressor	N/A	
Total project acreage of easement	44.5 Acres	
Total planted acreage	43.0 Acres	
WRC Class (Warm, Cool, Cold)	warm	
Species of concern, endangered etc.	none	
Pre-construction Beaver activity?	Historically, according to landowner	
Dominant Soil Types	Wetland	Roanoke loam series
	Stream	Roanoke loam and Wagram loamy sand series
% of Project Easement Fenced	0%	

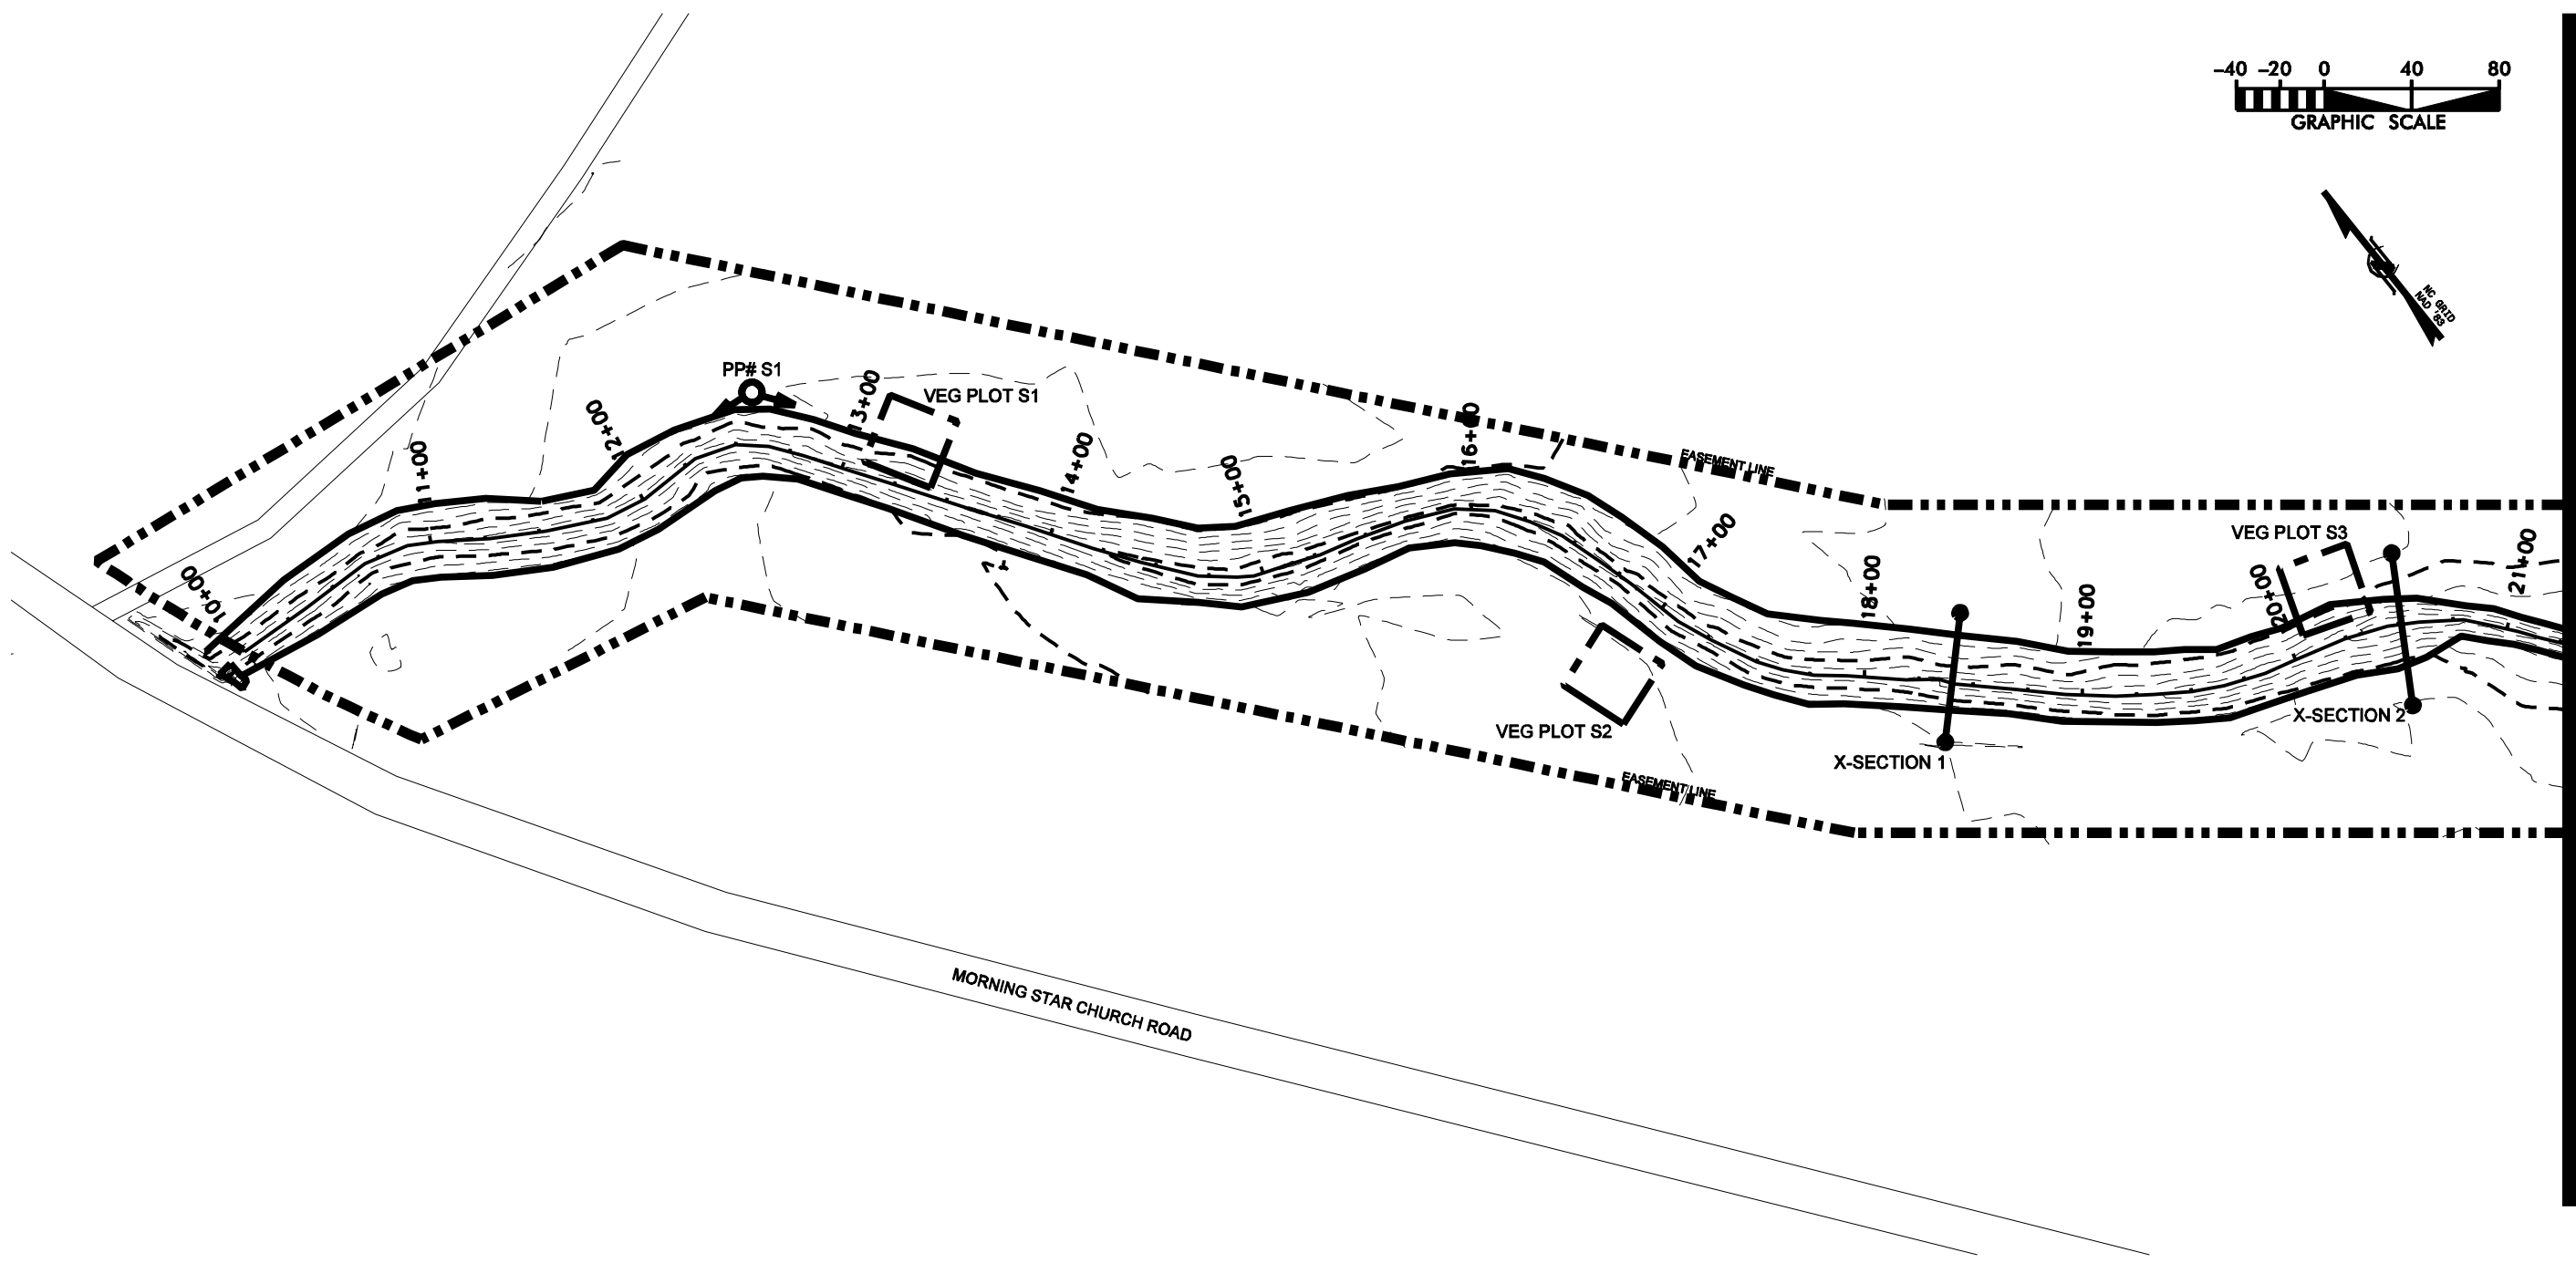



DATE	REVISION



KCI
 ASSOCIATES OF PC
 ENGINEERS • PLANNERS • SCIENTISTS
 460 SIX FORKS ROAD
 RALEIGH, NORTH CAROLINA 27609

HARRELL SITE
STREAM AND WETLAND RESTORATION
 EDGEcombe CO., NORTH CAROLINA
 STATION 10+00 TO STATION 21+29


DATE: DEC 2006
 SCALE: 1"=80'
STREAM MONITORING PLAN VIEW

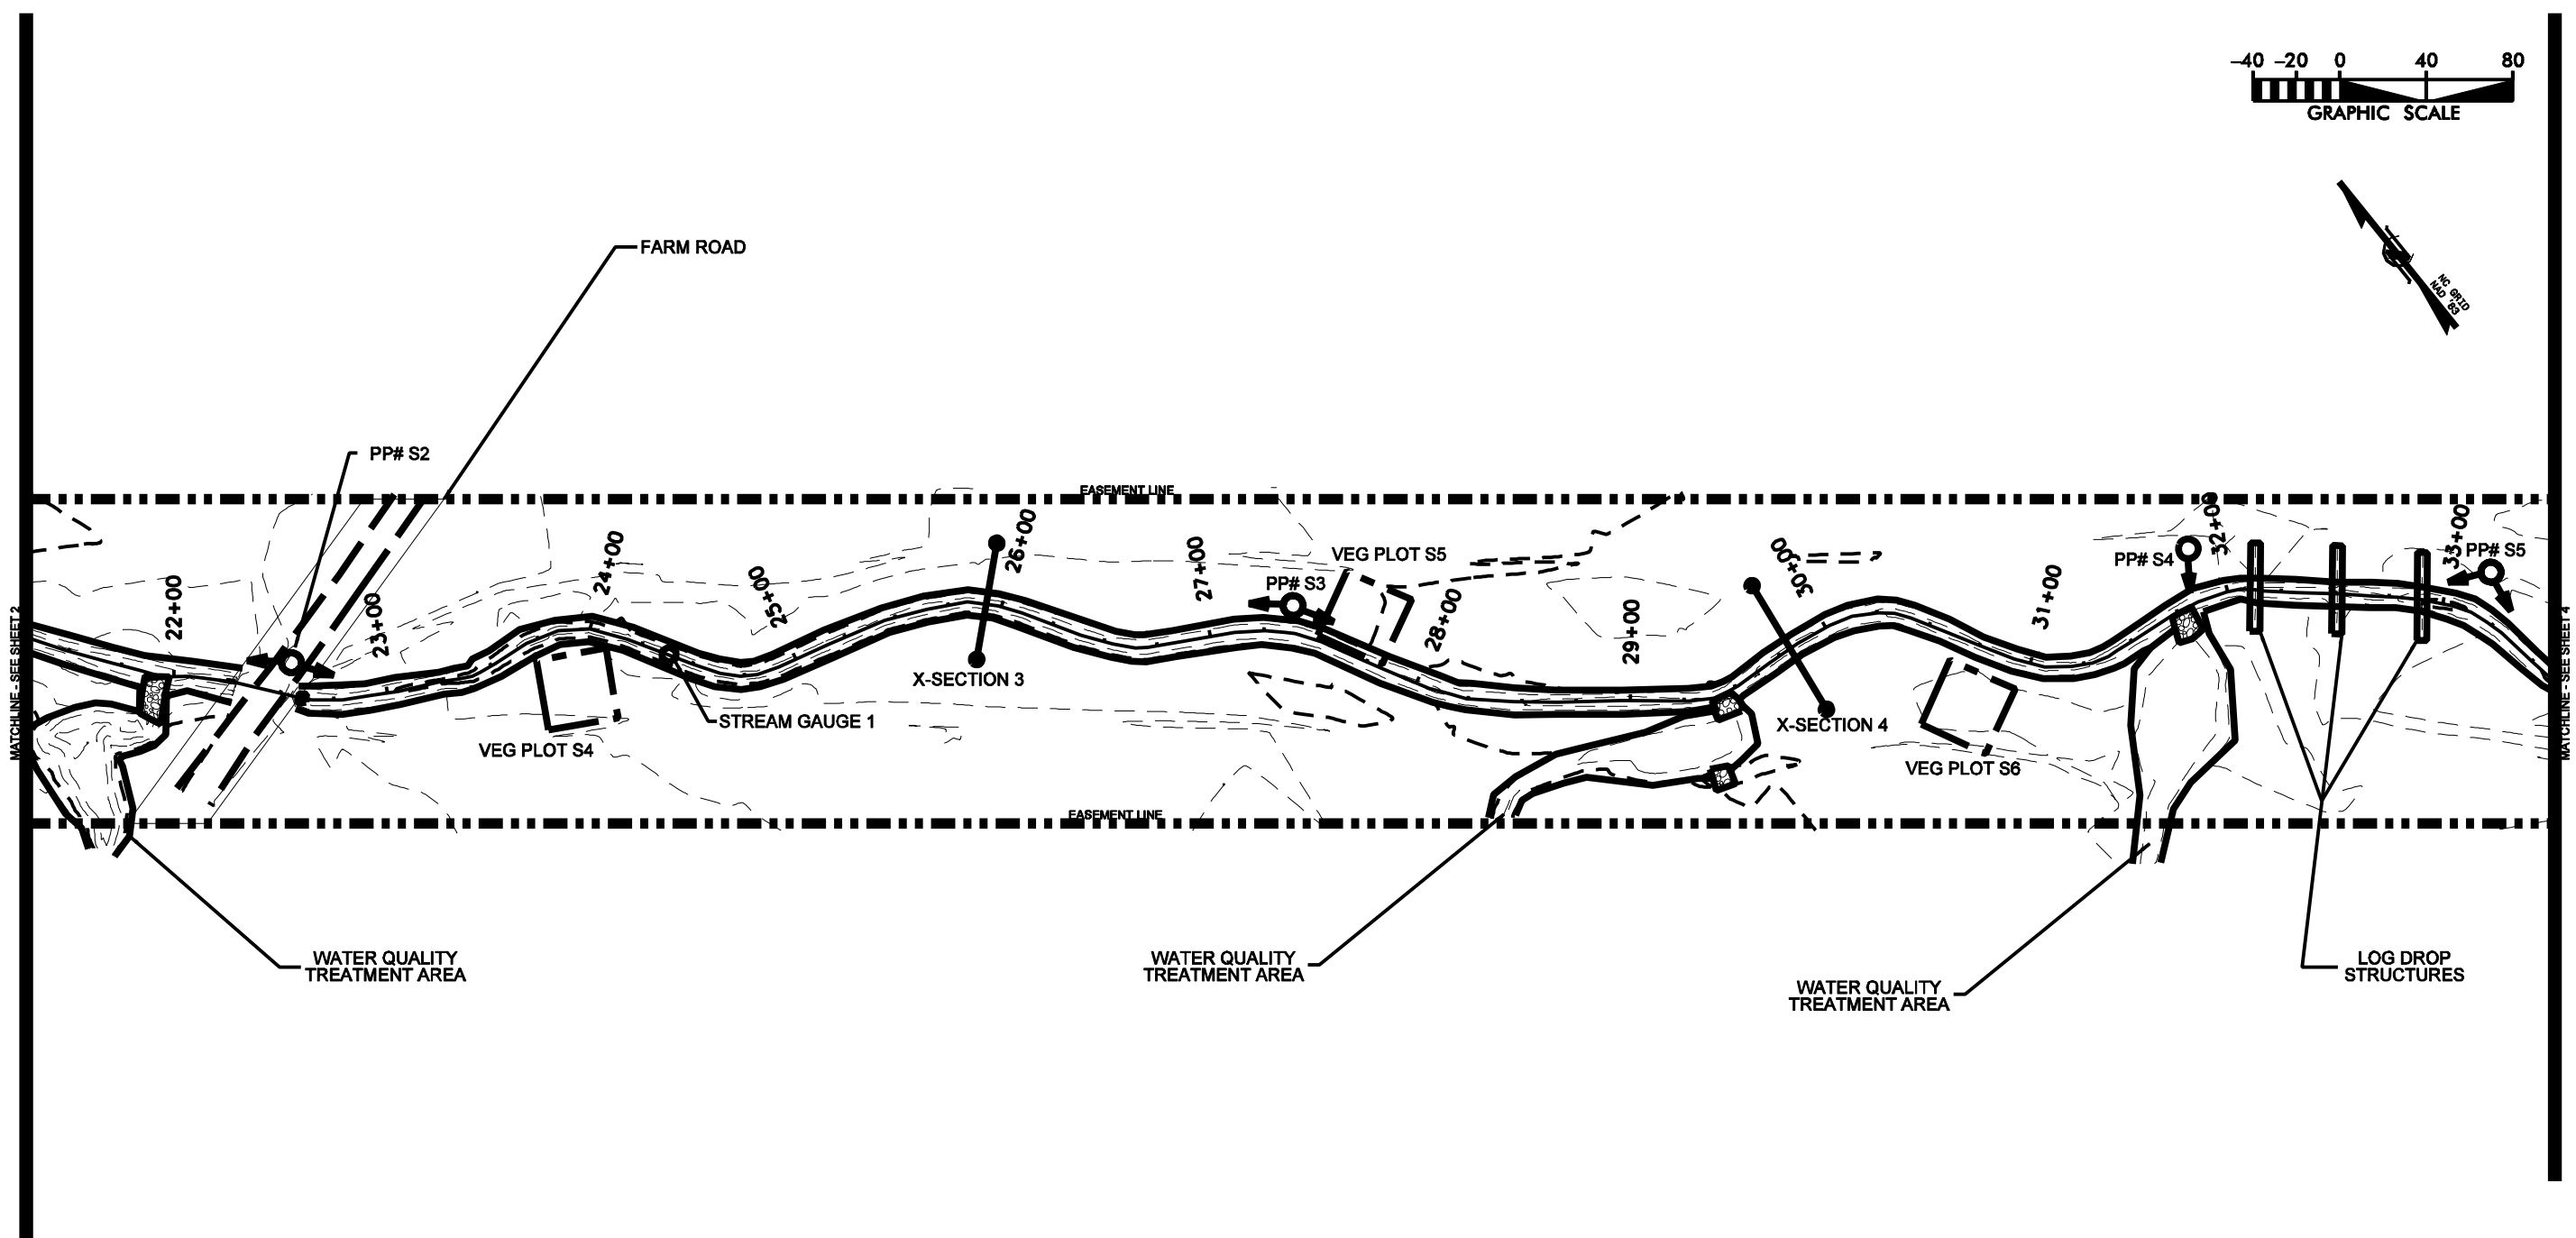

MATCHLINE - SEE SHEET 2



MATCHLINE - SEE SHEET 4

DATE	
DESIGNED BY	
CHECKED BY	
APPROVED BY	



HARRELL SITE
STREAM AND WETLAND RESTORATION
 EDGEcombe CO., NORTH CAROLINA
 STATION 21+29 TO STATION 33+64

DATE: DEC 2006
 SCALE: 1"=80'
STREAM MONITORING PLAN VIEW

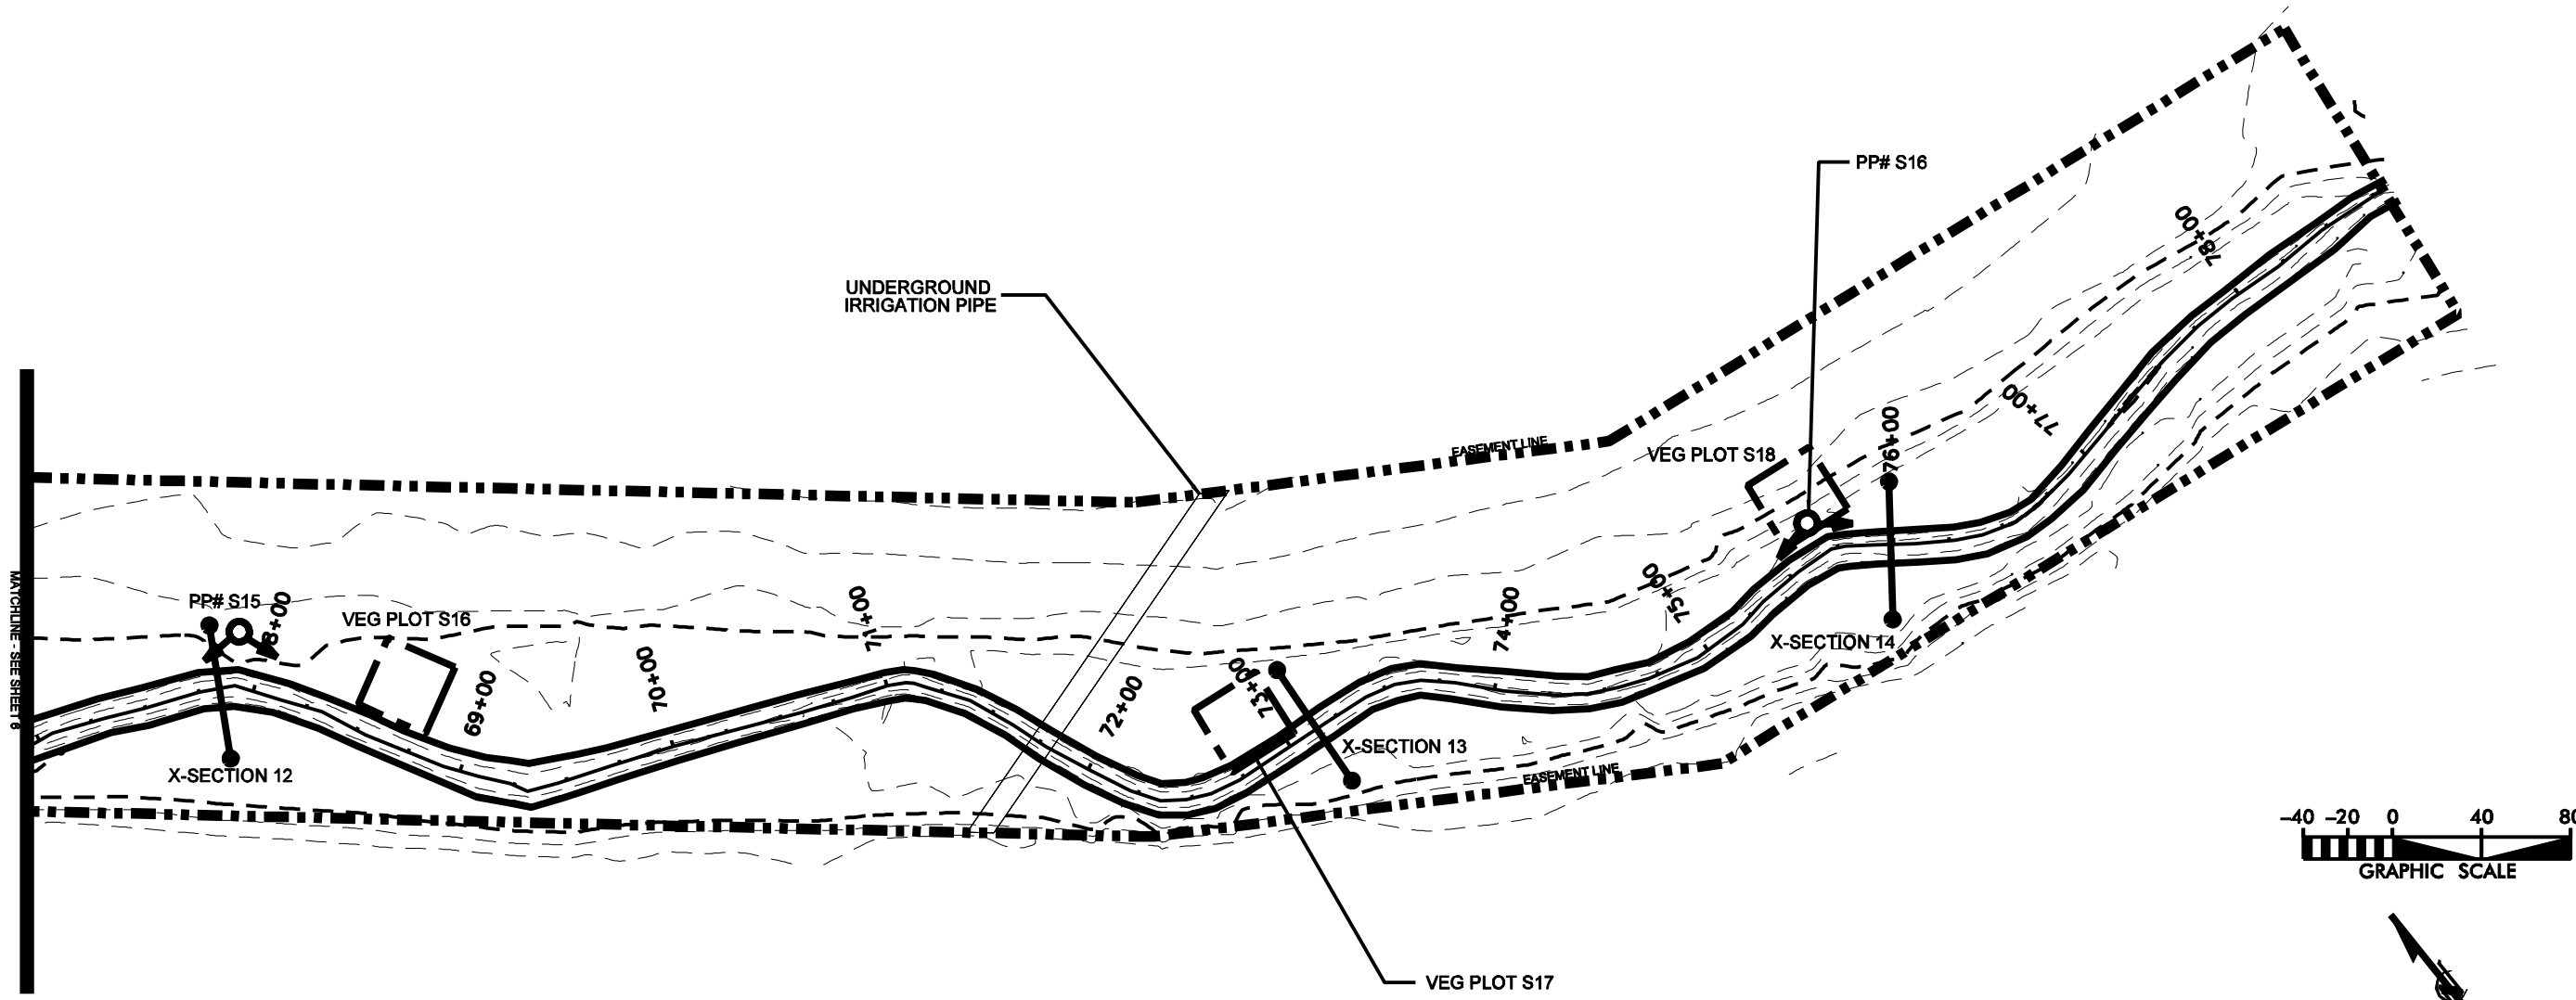

MATCHLINE - SEE SHEET 8

NO.	DATE	DESCRIPTION



KCI
 ASSOCIATES OF PC
 ENGINEERS • PLANNERS • SCIENTISTS
 4601 SIX FORKS ROAD
 RALEIGH, NORTH CAROLINA 27609

HARRELL SITE
 STREAM AND WETLAND RESTORATION
 EDGEcombe CO., NORTH CAROLINA
 STATION 66+94 TO STATION 78+80

DATE: DEC 2008
 SCALE: 1"=80'
 STREAM MONITORING
 PLAN VIEW

2.0 PROJECT CONDITIONS AND MONITORING RESULTS

2.1 Vegetation Assessment

The planted vegetation on the site is growing well. Due to the baseline vegetation monitoring occurring while the plants were in dormancy, some of the plants could not be identified and their species was recorded as unknown. During the first year of monitoring, most of these plants were identified. Some of the previously unknown plants were dead, damaged, or missing and could not be identified during the first year monitoring. These plants were again recorded as unknown.

The low stream flow throughout the summer months allowed vegetation to become established in the stream channel. This vegetation included grasses, rushes, cattails, and Asian dayflower (*Murdannia keisak*). While contributing to the overall stream stability, this vegetation could contribute to aggradation in the channel by trapping sediment. Further monitoring will determine if channel vegetation becomes a problem.

The floodplain, stream banks, and riparian buffer have small areas of sparse vegetation, but overall they are well vegetated. Some scattered populations of invasive species have been identified in the floodplain area, which include: Chinese lespedeza (*Lespedeza cuneata*) and tropical soda apple (*Solanum viarium*). Asian dayflower was present within the channel in isolated areas. Japanese honeysuckle (*Lonicera japonica*) was observed on the outer edges of the project. Although they are not a problem at this time, these populations will continue to be monitored to determine if invasive control is required in the future.

The monitored vegetation plots within the stream buffer and wetland revealed that the planted vegetation is growing well with 607 and 533 stems/acre, respectively. The overall vegetation assessment found the site to be on track to meeting the vegetative success criteria.

The vegetative monitoring results are displayed in Appendix A and the Current Conditions Plan View in Appendix C.

2.2 Stream Assessment

During the 2008 growing season, the stream experienced low flow throughout the summer. This flow allowed vegetation to become established in some areas of the stream. The vegetation has not caused any problematic aggradation at this time, but it will continue to be monitored. The on-site stream gauge recorded a bankfull event on July 6, 2008.

The stream assessment found the stream to be generally stable. Periodic storm events caused isolated bed degradation and aggradation in reaches 1 and 2. Some of these areas are visible on the longitudinal profile and cross-section plots. These patterns are typical for a stream like UT to Swift Creek. A sand bed system, like the project stream, is much more mobile than a gravel stream. Because of this, it is expected that patterns of aggradation and degradation are more dynamic within these systems. These dune/anti-dune streams will experience bed variation over time. The stream banks and floodplain experienced little to no erosion throughout the project. Piping is occurring at one instream structure, but the rest of the structures are performing as designed. Water quality treatment areas are stable and retaining water. All of these stream features will continue to be monitored to make sure that any observed changes are within the range of variability found in stable stream systems.

The stream assessment monitoring is described in Appendix B and the Current Conditions Plan View in Appendix C.

2.2.1 Bankfull Events

Table V. Hydrological (Bankfull) Verifications Harrell Stream and Wetland Restoration Site			
Date of Data Collection	Date of Occurrence	Method	Photo Number
10/10/2007	10/10/2007	Stream Gauge	N/A
10/27/2007	10/27/2007	Stream Gauge	N/A
7/6/2008	7/6/2008	Stream Gauge	N/A

2.2.2

Quantitative Measures Summary Tables

Table VI a. Reach 1 Baseline Stream Summary
Harrell Stream and Wetland Restoration

Parameter	Pre-Existing Condition					Reference Reach(es) Data					Design			As-built					
	Min	Mean	Med	Max	n	Min	Mean	Med	Max	n	Min	Max	Min	Max	Mean	Max	n		
Dimension - Riffle																			
Bankfull Width (ft)		5.4			1	29.2				35.0			10.0		10.2		1		
Floodprone Width (ft)		>70			1	44				64			>18		22		1		
Bankfull Mean Depth (ft)		1.3			1	2.0				2.1			0.9		1.2		1		
Bankfull Max Depth (ft)		2.0			1	2.7				2.8			1.4		2.1		1		
Bankfull Cross-Sectional Area (ft ²)		7.3			1	62.5				68.8			9.1		12.6		1		
Width/Depth Ratio		4.1			1	13.9				17.5			11.1		8.3		1		
Entrenchment Ratio		1.3			1	1.3				2.2			>1.8		2.7		1		
Bank Height Ratio		1.8			1								1.0		1.0		1		
Pattern																			
Channel Beltwidth (ft)						100				400			45		65		47		85
Radius of Curvature (ft)						70				220			30		80		31		65
Rc:Bankfull width (ft/ft)						2.2				12.5			3.0		8.0		3.0		6.4
Meander Wavelength (ft)						140				500			50		200		166		420
Meander Width Ratio						3				14			4		10		4.6		8.3
Profile																			
Riffle Length (ft)																			
Riffle Slope (ft/ft)						0.007				0.027									
Pool Length (ft)																			
Pool Spacing (ft)										400									
Substrate and Transport Parameters																			
SC% / Sa% / G% / C% / B% / Be%		100%	- / - / - / - / - / -							- / 11% / 89% / - / - / -									7% / 85% / 8% / - / - / -
d16 / d35 / d50 / d84 / d95 (mm)		0.062	/ 0.062 / 0.1 / 0.1 / 0.1							2.6 / 5.7 / 7.1 / - / 15.0									0.15 / 0.36 / 0.54 / 1.1 / 6.0
Additional Reach Parameters																			
Channel length (ft)		1,224													1,265				1,226
Drainage Area (SM)		0.20								6.00					0.20				0.20
Rosgen Classification		E5								B4c					B5c				B5c
Sinuosity		1.00								1.10					1.03				1.06
Water Surface Slope (ft/ft)		0.0067								0.0084					0.0067				0.0067
BF slope (ft/ft)															0.0067				0.0068

**Table VI b. Reach 2 Baseline Stream Summary
Harrell Stream and Wetland Restoration**

Parameter	Pre-Existing Condition					Reference Reach(es) Data					Design					As-Built				
	Min	Mean	Med	Max	n	Min	Mean	Med	Max	n	Min	Mean	Max	n	Min	Mean	Max	n		
Dimension - Riffle																				
Bankfull Width (ft)	5.7	6.1		6.5	2	13.6	15.7		17.8	2	10.0				9.2	10.2	11.5	3		
Floodprone Width (ft)	>65			>70	2	325	463		600	2	>30				56	>59	>67	3		
Bankfull Mean Depth (ft)	1.2	1.25		1.3	2	1.5	1.6		1.7	2	1.1				1.0	1.1	1.1	3		
Bankfull Max Depth (ft)	1.9	1.9		1.9	2	2.6	2.8		3.0	2	1.4				1.6	1.7	1.9	3		
Bankfull Cross-Sectional Area (ft ²)	7.5	7.75		8	2	22.6	24.4		26.2	2	11.2				8.8	10.5	12.5	3		
Width/Depth Ratio	4.3	4.8		5.3	2	8.2	10.1		11.9	2	9.1				9.3	9.8	10.6	3		
Entrenchment Ratio	10.8	11.1		11.4	2	23.8	28.8		33.7	2	>3.0				4.8	5.9	6.8	3		
Bank Height Ratio	1.4	1.6		1.8	2	1.0	1.0		1.0	2	1.0				1.0	1.0	1.0	3		
Pattern																				
Channel Beltwidth (ft)							158				45		60		24	32	41	8		
Radius of Curvature (ft)						37	158		40		30		50		30	36	43	14		
Re:Bankfull width (ft/ft)						2.1			2.3		3.0		5.0		2.9	3.5	4.2			
Meander Wavelength (ft)						94			143		100		200		125	157	186	8		
Meander Width Ratio							8.9				4.0		10.0		2.4	3.1	4.0			
Profile																				
Riffle Length (ft)																				
Riffle Slope (ft/ft)																				
Pool Length (ft)																				
Pool Spacing (ft)																				
Substrate and Transport Parameters																				
SC% / Sa% / G% / C% / B% / Be%							88% / 12% / - / - / - / -													
d16 / d35 / d50 / d84 / d95 (mm)							0.062 / 0.062 / 0.1 / - / -													
							0.075 / 0.14 / 0.2 / 0.4 / 0.6													
							11% / 89% / - / - / - / -													
							3% / 81% / 16% / - / - / -													
Additional Reach Parameters																				
Channel length (ft)		1,400											1,465							
Drainage Area (SM)		0.23					3.04						0.23							
Rosgen Classification		E5					C5						C5							
Sinuosity		1.00					1.28						1.05							
Water Surface Slope (ft/ft)		0.0023					0.0024						0.0023							
BF slope (ft/ft)													0.0023							

**Table VI c. Reach 3 Baseline Stream Summary
Harrell Stream and Wetland Restoration**

Parameter	Pre-Existing Condition							Reference Reach(es) Data							Design				As-built	
	Min	Mean	Med	Max	n	Min	Mean	Med	Max	n	Min	Mean	Max	Min	Mean	Max	n			
Dimension - Riffle																				
Bankfull Width (ft)	6.4	7.6	7.7	8.6	4	13.6	15.7		17.8	2	12.0			11.8	12.8	14.1	4			
Floodprone Width (ft)	>65			>80	4	325	463		600	2	>30			>50	>57	>61	4			
Bankfull Mean Depth (ft)	1.4	1.6	1.5	1.9	4	1.5	1.6		1.7	2	1.4			1.2	1.3	1.4	4			
Bankfull Max Depth (ft)	2.4	2.7	2.7	2.8	4	2.6	2.8		3.0	2	2.0			1.9	2.1	2.5	4			
Bankfull Cross-Sectional Area (ft ²)	10.4	11.6	12.0	12.1	4	22.6	24.4		26.2	2	16.8			14.4	16.2	19.1	4			
Width/Depth Ratio	3.3	5.0	5.3	6.2	4	8.2	10.1		11.9	2	8.6			8.9	10.1	10.8	4			
Entrenchment Ratio	7.6	9.5	9.8	10.9	4	23.8	28.8		33.7	2	>2.5			3.8	4.5	5.0	4			
Bank Height Ratio	1.5	1.6	1.6	1.7	4	1.0	1.0		1.0	2	1.0			1.0	1.0	1.0	4			
Pattern																				
Channel Beltwidth (ft)							158				60		100	41	70	107	11			
Radius of Curvature (ft)						37	158		40		40		60	21	35	46	13			
Rc:Bankfull width (ft/ft)						2.1			2.3		3.0		5.0	1.6	2.7	3.6				
Meander Wavelength (ft)						94			143		120		240	158	183	225	11			
Meander Width Ratio							8.9				4.0		10.0	3.2	5.5	8.4				
Profile																				
Riffle Length (ft)																				
Riffle Slope (ft/ft)																				
Pool Length (ft)																				
Pool Spacing (ft)																				
Substrate and Transport Parameters																				
SC% / Sa% / G% / C% / B% / Be%		65% / 35%	- / - / - / - / -						11% / 89%	- / - / - / - / -										
d16 / d35 / d50 / d84 / d95		0.062 / 0.062	0.1 / - / - / -						0.075 / 0.14	0.2 / 0.4 / 0.6										
Additional Reach Parameters																				
Channel length (ft)		1,225											1,560		1,491					
Drainage Area (SM)		0.42					3.04						0.42		0.42					
Rosgen Classification		E5					C5						C5		C5					
Sinuosity		1.00					1.28						1.27		1.23					
Water Surface Slope (ft/ft)		0.0023					0.0024						0.0023		0.0042					
BF slope (ft/ft)													0.0023		0.0042					

**Table VII. Morphology and Hydraulic Monitoring Summary
Harrell Stream and Wetland Restoration**

Parameter	Cross-Section 1 Reach 1					Cross-Section 2 Reach 1					Cross-Section 3 Reach 2							
	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5
Bankfull Width (ft)	10.2	10.4					12.4	12.7					11.5	13.1				
Floodprone Width (ft)	22	27					25	25					>55	>55				
Bankfull Cross-Sectional Area (ft ²)	12.6	13.4					17.1	12.9					12.5	12.6				
Bankfull Mean Depth (ft)	1.2	1.3					1.4	1.0					1.1	1.0				
Bankfull Maximum Depth (ft)	2.1	2.1					2.2	1.7					1.9	1.9				
Width/Depth Ratio	8.3	8.1					9.0	12.5					10.6	13.7				
Entrenchment Ratio	2.7	2.6					2.8	2.0					>5.0	>5.0				
Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	1.0				
Wetted Perimeter (ft)	11.2	11.5					13.3	13.6					12.2	13.9				
Hydraulic Radius (ft)	1.1	1.2					1.3	0.9					1.0	0.9				
Substrate																		
d50 (mm)	0.5	1.8					1.1	1.8					0.6	2.3				
d84 (mm)	1.1	14.0					1.8	5.3					1.4	4.3				

**Table VII. cont. Morphology and Hydraulic Monitoring Summary
Harrell Stream and Wetland Restoration**

Parameter	Cross-Section 4 Reach 2					Cross-Section 5 Reach 2					Cross-Section 6 Reach 3							
	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5
Bankfull Width (ft)	9.8	11.5					9.2	9.9					14.1	15.0				
Floodprone Width (ft)	>67	>67					56	56					>60	>60				
Bankfull Cross-Sectional Area (ft ²)	10.3	10.8					8.8	10.2					19.1	20.8				
Bankfull Mean Depth (ft)	1.1	0.9					1.0	1.0					1.4	1.4				
Bankfull Maximum Depth (ft)	1.7	1.7					1.6	2.0					2.5	2.7				
Width/Depth Ratio	9.3	12.2					9.6	9.7					10.4	10.8				
Entrenchment Ratio	>7.0	>7.0					6.1	5.7					4.3	>5.0				
Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	1.0				
Wetted Perimeter (ft)	10.7	12.2					10.0	10.9					15.2	16.3				
Hydraulic Radius (ft)	1.0	0.9					0.9	0.9					1.3	1.3				
Substrate																		
d50 (mm)	1.3	3.4					0.9	0.8					0.6	0.2				
d84 (mm)	4.4	6.2					4.6	3.8					2.0	7.7				

**Table VII. cont. Morphology and Hydraulic Monitoring Summary
Harrell Stream and Wetland Restoration**

Parameter	Cross-Section 7 Reach 3					Cross-Section 8 Reach 3					Cross-Section 9 Reach 3							
	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5
Bankfull Width (ft)	12.1	12.0					13.0	11.9					11.8	12.4				
Floodprone Width (ft)	>61						>50	>50					>58	>58				
Bankfull Cross-Sectional Area (ft ²)	14.4	16.2					15.6	15.8					15.6	15.2				
Bankfull Mean Depth (ft)	1.2	1.4					1.2	1.3					1.3	1.2				
Bankfull Maximum Depth (ft)	1.9	2.6					1.9	2.0					2.0	2.0				
Width/Depth Ratio	10.2	8.8					10.8	8.9					8.9	10.1				
Entrenchment Ratio	>5.0	>5.0					>4.0	>5.0					>5.0	>5.0				
Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	1.0				
Wetted Perimeter (ft)	12.8	13.2					14.0	12.8					12.8	13.2				
Hydraulic Radius (ft)	1.1	1.2					1.1	1.2					1.2	1.2				
Substrate																		
d50 (mm)	0.8	0.7					1.0	1.0					0.9	0.8				
d84 (mm)	2.0	7.3					1.9	5.5					1.7	1.7				

**Table VII. cont. Morphology and Hydraulic Monitoring Summary
Harrell Stream and Wetland Restoration**

Parameter	Cross-Section 10 Reach 4					Cross-Section 11 Reach 4					Cross-Section 12 Reach 4							
	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5
Bankfull Width (ft)	13.5	13.9					14.0	13.3					16.8	17.6				
Floodprone Width (ft)	>67	>67					>57	>57					>61	>61				
Bankfull Cross-Sectional Area (ft ²)	17.9	16.9					18.2	18.7					28.2	27.2				
Bankfull Mean Depth (ft)	1.3	1.2					1.3	1.4					1.7	1.5				
Bankfull Maximum Depth (ft)	2.0	2.0					2.1	2.3					2.5	2.5				
Width/Depth Ratio	10.2	11.5					10.8	9.5					10.0	11.4				
Entrenchment Ratio	>5.0	>5.0					>4.0	>4.0					>4.0	>4.0				
Bank Height Ratio	1.0	1.0					1.0	1.0					1.0	1.0				
Wetted Perimeter (ft)	14.3	14.7					15.0	14.4					17.8	18.7				
Hydraulic Radius (ft)	1.2	1.2					1.2	1.3					1.6	1.5				
Substrate																		
d50 (mm)	1.0	2.0					1.4	1.6					1.4	0.9				
d84 (mm)	2.6	4.2					2.0	5.9					3.0	2.7				

**Table VII. cont. Morphology and Hydraulic Monitoring Summary
Harrell Stream and Wetland Restoration**

Parameter	Cross-Section 13 Reach 4					Cross-Section 14 Reach 4						
	MY0	MY1	MY2	MY3	MY4	MY5	MY0	MY1	MY2	MY3	MY4	MY5
Dimension												
Bankfull Width (ft)	13.1	13.4					13.6	14.0				
Floodprone Width (ft)	>60	>60					>62	>62				
Bankfull Cross-Sectional Area (ft ²)	19.4	20.0					19.0	20.5				
Bankfull Mean Depth (ft)	1.5	1.5					1.4	1.5				
Bankfull Maximum Depth (ft)	2.4	2.3					2.1	2.3				
Width/Depth Ratio	8.8	8.9					9.7	9.6				
Entrenchment Ratio	>4	>4					>4	>4				
Bank Height Ratio	1.0	1.0					1.0	1.0				
Wetted Perimeter (ft)	14.1	14.3					14.5	15.1				
Hydraulic Radius (ft)	1.4	1.4					1.3	1.4				
Substrate												
d50 (mm)	1.5	1.6					1.3	0.1				
d84 (mm)	2.6	4.7					1.8	0.4				

2.3 Wetland Assessment

The maximum number of consecutive days that the groundwater was within 12 inches of the surface was determined for each groundwater gauge. This number was converted into a percentage of the 223-day growing season. Table 5 presents the hydrological monitoring results for 2008. The wetland wells used to monitor site hydrology were installed in the spring of 2007. During the first year of monitoring wetland hydrology was achieved at all of the wells on the site (Table 5). Based on these data, the site has exceeded the minimum duration of 12 consecutive days with the water table within 12 inches of the soil surface for the 2008 growing season (Appendix B). Climatic data for the 2008 growing season were analyzed in comparison to historical data to determine whether 2008 was a normal year in terms of climatic conditions. The historical data were collected from the NRCS, Water and Climate Center, "Climate Analysis for Wetlands by County" website. This evaluation concluded that 2008 was a below normal year for rainfall during the growing season. Rainfall was within the 30th to 70th percentiles for the months of July, August, September and November. Rainfall was less than the 30th percentile threshold in March, May, June and October and was greater than the 70th percentile threshold in April (Appendix B).

2.3.1 Wetland Criteria Attainment Tables

Table VIIIa. Hydrologic Monitoring Results						
Project Name: Harrell Stream and Wetland Restoration						
Well #	Hydroperiod				Max. No. of Consecutive Days	Dates Meeting Success
	<5%	5% - 8%	8% - 12.5%	>12.5%		
1		X			16	4/4/08-4/19/08
2				X	38.5	3/29/08-4/24/08
3		X			16	4/20/08-5/6/08
4				X	32	4/4/08-5/5/08

Table VIIIb. Hydroperiod History						
Harrell Stream and Wetland Restoration						
Well #	Pre-Restoration	Year 1	Year 2	Year 3	Year 4	Year 5
1	<5%	5%-8%				
2	<5%	>12.5%				
3	<5%	5%-8%				
4	<5%	>12.5				

3.0 SUCCESS CRITERIA

The stream is functioning as designed and has not developed any significant problems. The changes that are visible in the monitored cross-sections and profiles indicate adjustment of the stream due to its sand bed. Any feature changes will be tracked to see if the stream is moving beyond its expected variability. With three bankfull events since construction, the stream is on track to meeting the success criteria

The hydrology data in Section 2.3 indicates that the wetland is on track to meeting the success criteria.

The planted vegetation has been doing well, with some plots experiencing more mortality than others. This mortality can be attributed to normal losses after the initial planting as well as to the effects of last year's exceptional drought. Some invasive species have been identified on the site, which include Chinese lespedeza (*Lespedeza cuneata*), Japanese honeysuckle (*Lonicera japonica*), tropical soda apple (*Solanum viarium*) and Asian dayflower (*Murdannia keisak*). The exotic vegetation is not widespread across the project, but these populations will continue to be monitored to determine if control measures will be required in the future. The vegetation is on track to meeting the success criteria in the stream and wetland for the first year of monitoring.

4.0 MAINTENANCE

Maintenance was performed along the restored stream near stations 23+00, 37+00, 39+60 and 52+75. Minor bank and bed stabilization was conducted with rock at station 23+00 due to bed degradation. Near station 37+00 the banks of an incoming drainage ditch within the easement were sloped back and stabilized to alleviate bank erosion from the ditch. To further facilitate floodplain drainage, rock stabilization was added near Stations 39+60 and 52+75 where erosion was occurring as field drainage entered the channel. At each station erosion had been occurring. If any further maintenance actions are warranted, they will be documented in future monitoring reports.

Appendix A

Vegetation Data

**Table A1. Riparian Buffer Stem Density and Species Count by Plot
Harrell Stream and Wetland Restoration**

Plot Number	River Birch <i>Betula nigra</i>	American Beautyberry <i>Callicarpa americana</i>	Shagbark Hickory <i>Carya ovata</i>	Sugarberry <i>Celtis laevigata</i>	Silky Dogwood <i>Cornus amomum</i>	Persimmon <i>Diospyros virginiana</i>	Green Ash <i>Fraxinus pennsylvanica</i>	Sycamore <i>Platanus occidentalis</i>	Southern Red Oak <i>Quercus falcata</i>	Swamp Chestnut Oak <i>Quercus michauxii</i>	Willow Oak <i>Quercus phellos</i>	Black Willow <i>Salix nigra</i>	Elderberry <i>Sambucus canadensis</i>	Posumhaw <i>Viburnum nudum</i>	Cherrybark oak <i>Quercus pagoda</i>	Total (Year 1)	Density-Year 1 (Stems/Acre)
S1					8	1			3		2		1		1	16	640
S2		5	3						1							9	360
S3		2	2		5	6					1		5		1	22	880
S4	2	2		4						3	3					14	560
S5	4			2	8					4	2		1			21	840
S6	1	2								4						7	280
S7		7		3	7				1	3	4		3			28	1,120
S8		6		1							1					8	320
S9	4			1	4	5				2	4	3				23	920
S10		1		1		1		4			2					9	360
S11		4		1	6	2			1	2	1	1	1			19	760
S12	5	1		1				2		2						11	440
S13		5		7	2			1		4				2		21	840
S14	2	2				7				2						13	520
S15	4	4		3	9		1	3		1						25	1,000
S16	1	4				1		1		5						12	480
S17						1				3			1			5	200
S18	5						1				2					8	320
Average Density																607	

**Table A2. Wetland Stem Density and Species Count by Plot
Harrell Stream and Wetland Restoration**

Plot Number	Green Ash <i>Fraxinus pennsylvanica</i>	American Beautyberry <i>Callicarpa americana</i>	Water Hickory <i>Carya aquatica</i>	Buttonbush <i>Cephalanthus occidentalis</i>	Cherrybark Oak <i>Quercus pagoda</i>	Swamp Chestnut Oak <i>Quercus michauxii</i>	Willow Oak <i>Quercus phellos</i>	Laurel Oak <i>Quercus laurifolia</i>	Bald Cypress <i>Taxodium distichum</i>	Total (Year 1)	Density- Year 1 (Stems/Acre)
W1	4	1		1	2	1		1		10	400
W2				1	5		2	1		9	360
W3				2	1	1			6	10	400
W4	2	1		4	4	1	2	2		16	640
W5	4	1			1	4			4	14	560
W6				5			5	2	3	15	600
W7					1	2	3			6	240
W8		1	8	4	1				3	17	680
W9	2	2		1	4	1	1	3		14	560
W10	3	1		3	2			5	1	15	600
W11		1	3	4					6	14	560
W12			5	6					9	20	800
										Average Density	533

Table A3. Riparian Buffer Vegetation History (stems/acre)						
Harrell Stream and Wetland Restoration						
Plot Number	MY-00	MY-01	MY-02	MY-03	MY-04	MY-05
S1	1,120	640				
S2	720	360				
S3	1,120	880				
S4	480	560*				
S5	1,200	840				
S6	480	280				
S7	1,120	1,120				
S8	480	320				
S9	1,240	920				
S10	600	360				
S11	880	760				
S12	600	440				
S13	1,160	840				
S14	640	520				
S15	1,120	1,000				
S16	600	480				
S17	880	200				
S18	680	320				

*Uncounted plants during baseline were added to total


Table A4. Wetland Vegetation History (stems/acre)						
Harrell Stream and Wetland Restoration						
Plot Number	MY-00	MY-01	MY-02	MY-03	MY-04	MY-05
W1	520	400				
W2	640	360				
W3	600	400				
W4	800	640				
W5	600	560				
W6	720	600				
W7	680	240				
W8	760	680				
W9	640	560				
W10	600	600				
W11	680	560				
W12	1,080	800				

Vegetation Monitoring Data Sheets

Vegetation Monitoring Worksheet

Site: Harrell Plot: S1 Date: 8/19/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	<i>Quercus sp.</i>			Dead
2	Unknown			Dead
3	Southern Red Oak (<i>Quercus falcata</i>)			Dead
4	Southern Red Oak (<i>Quercus falcata</i>)	0.19	3	Resprout
5	Southern Red Oak (<i>Quercus falcata</i>)	0.02	2	Resprout, flag not on tree
6	Persimmon (<i>Diospyros virginiana</i>)	0.46	3	
7	Unknown			Dead
8	Unknown			Dead
9	Willow Oak (<i>Quercus phellos</i>)	0.51	3	
10	Willow Oak (<i>Quercus phellos</i>)	0.47	3	Rodent damage
11	Willow Oak (<i>Quercus phellos</i>)			Dead
12	Unknown			Dead
13	Southern Red Oak (<i>Quercus falcata</i>)			Dead
14	Southern Red Oak (<i>Quercus falcata</i>)	0.40	3	
15	Southern Red Oak (<i>Quercus falcata</i>)			Dead
16	Silky Dogwood (<i>Cornus amomum</i>)	0.11	3	Live Stake
17	Silky Dogwood (<i>Cornus amomum</i>)	0.37	3	Live stake, deer browse
18	Silky Dogwood (<i>Cornus amomum</i>)	0.31	3	Live stake, deer browse
19	Silky Dogwood (<i>Cornus amomum</i>)	0.17	3	Live stake, deer browse
20	Silky Dogwood (<i>Cornus amomum</i>)	0.16	3	Live stake, deer browse
21	Elderberry (<i>Sambucus canadensis</i>)	0.05	3	Live stake, deer browse
22	Silky Dogwood (<i>Cornus amomum</i>)	0.34	3	Live stake, deer browse
23	Silky Dogwood (<i>Cornus amomum</i>)	0.15	3	Live stake, deer browse
24	Silky Dogwood (<i>Cornus amomum</i>)	0.17	3	Live stake, deer browse
25	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
26	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
27	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
28	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year


Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	53.3%
Southern Red Oak (<i>Quercus falcata</i>)	20.0%
Elderberry (<i>Sambucus canadensis</i>)	6.7%
Willow Oak (<i>Quercus phellos</i>)	13.3%
Persimmon (<i>Diospyros virginiana</i>)	6.7%

Density:

Total Number of Trees 15 / 0.025 acres = 600 trees / acre

Survivability:

Total Number of Trees 15 / 28 trees x 100 = 54 % survivability

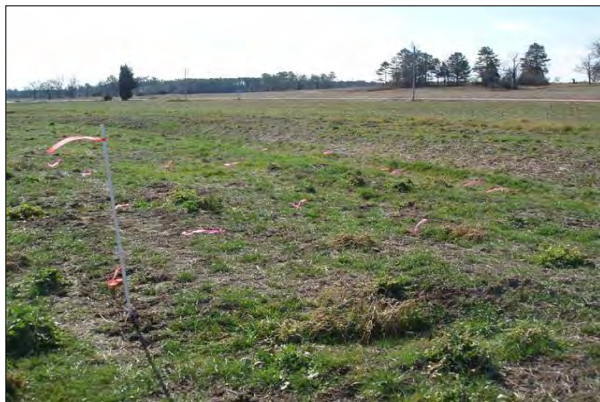

**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S2 Date: 8/18/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	American Beautyberry (<i>Callicarpa americana</i>)	0.10	2	Resprout
2	American Beautyberry (<i>Callicarpa americana</i>)	0.28	2	
3	Cherrybark Oak (<i>Quercus pagoda</i>)	0.10	2	Resprout
4	Southern Red Oak (<i>Quercus falcata</i>)	0.16	3	Resprout
5	American Beautyberry (<i>Callicarpa americana</i>)			Dead
6	American Beautyberry (<i>Callicarpa americana</i>)			Dead
7	Willow Oak (<i>Quercus phellos</i>)			Dead
8	American Beautyberry (<i>Callicarpa americana</i>)			Dead
9	<i>Quercus sp.</i>			Dead
10	American Beautyberry (<i>Callicarpa americana</i>)	0.56	3	
11	Shagbark Hickory (<i>Carya ovata</i>)	0.05	2	Resprout
12	Shagbark Hickory (<i>Carya ovata</i>)	0.27	3	Rodent damage
13	Shagbark Hickory (<i>Carya ovata</i>)	0.10	2	Top died back
14	Southern Red Oak (<i>Quercus falcata</i>)			Dead
15	<i>Quercus sp.</i>			Dead
16	Willow Oak (<i>Quercus phellos</i>)			Dead
17	American Beautyberry (<i>Callicarpa americana</i>)	0.54	3	
18	American Beautyberry (<i>Callicarpa americana</i>)	0.85	4	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Southern Red Oak (<i>Quercus falcata</i>)	10.0%
Shagbark Hickory (<i>Carya ovata</i>)	30.0%
American Beautyberry (<i>Callicarpa americana</i>)	50.0%
Cherrybark Oak (<i>Quercus pagoda</i>)	10.0%

Density:

Total Number of Trees 10 / 0.025 acres = 400 trees / acre

Survivability:

Total Number of Trees 10 / 18 trees x 100 = 56 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S3 Date: 8/19/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	Willow Oak (<i>Quercus phellos</i>)			Dead
2	American Beautyberry (<i>Callicarpa americana</i>)	0.66	4	
3	Persimmon (<i>Diospyros virginiana</i>)	0.47	3	Top died back
4	American Beautyberry (<i>Callicarpa americana</i>)	0.41	3	
5	Persimmon (<i>Diospyros virginiana</i>)			Dead
6	Shagbark Hickory (<i>Carya ovata</i>)	0.10	2	Reprout
7	Shagbark Hickory (<i>Carya ovata</i>)	0.33	3	
8	Shagbark Hickory (<i>Carya ovata</i>)			Dead
9	Unknown			Dead
10	Willow Oak (<i>Quercus phellos</i>)	0.66	4	
11	Unknown			Dead
12	Persimmon (<i>Diospyros virginiana</i>)	0.68	4	
13	Persimmon (<i>Diospyros virginiana</i>)	0.45	3	
14	Persimmon (<i>Diospyros virginiana</i>)	0.18	3	Resprout
15	Persimmon (<i>Diospyros virginiana</i>)	0.70	4	
16	Persimmon (<i>Diospyros virginiana</i>)	0.68	4	
17	Cherrybark Oak (<i>Quercus pagoda</i>)	0.47	3	
18	Elderberry (<i>Sambucus canadensis</i>)	0.58	4	Live stake
19	Elderberry (<i>Sambucus canadensis</i>)	0.66	4	Live stake
20	Silky Dogwood (<i>Cornus amomum</i>)	0.42	3	Live stake, deer browse
21	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
22	Elderberry (<i>Sambucus canadensis</i>)	0.51	3	Live stake
23	Silky Dogwood (<i>Cornus amomum</i>)	0.25	3	Live stake, deer browse
24	Elderberry (<i>Sambucus canadensis</i>)	0.48	3	Live stake
25	Elderberry (<i>Sambucus canadensis</i>)	0.51	3	Live stake
26	Silky Dogwood (<i>Cornus amomum</i>)	0.38	3	Live stake, deer browse
27	Silky Dogwood (<i>Cornus amomum</i>)	0.40	3	Live stake, deer browse
28	Silky Dogwood (<i>Cornus amomum</i>)	0.42	4	Live stake

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Elderberry (<i>Sambucus canadensis</i>)	22.7%
Silky Dogwood (<i>Cornus amomum</i>)	22.7%
American Beautyberry (<i>Callicarpa americana</i>)	9.1%
Willow Oak (<i>Quercus phellos</i>)	4.5%
Persimmon (<i>Diospyros virginiana</i>)	27.3%
Cherrybark Oak (<i>Quercus pagoda</i>)	4.5%
Shagbark Hickory (<i>Carya ovata</i>)	9.1%

Density:

$$\text{Total Number of Trees } \underline{22} \quad / \quad 0.025 \text{ acres} \quad = \quad \underline{880} \quad \text{trees / acre}$$

Survivability:

$$\text{Total Number of Trees } \underline{22} \quad / \quad 28 \text{ trees} \quad \times \quad 100 \quad = \quad \underline{79} \quad \% \text{ survivability}$$



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
River Birch (<i>Betula nigra</i>)	14.3%
American Beautyberry (<i>Callicarpa americana</i>)	14.3%
Willow Oak (<i>Quercus phellos</i>)	21.4%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	21.4%
Sugarberry (<i>Celtis laevigata</i>)	28.6%

Density:

Total Number of Trees 14 / 0.025 acres = 560 trees / acre

Survivability:

Total Number of Trees 14 / 12 trees x 100 = 117 % survivability*



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S5 Date: 8/19/2008

Plot Map

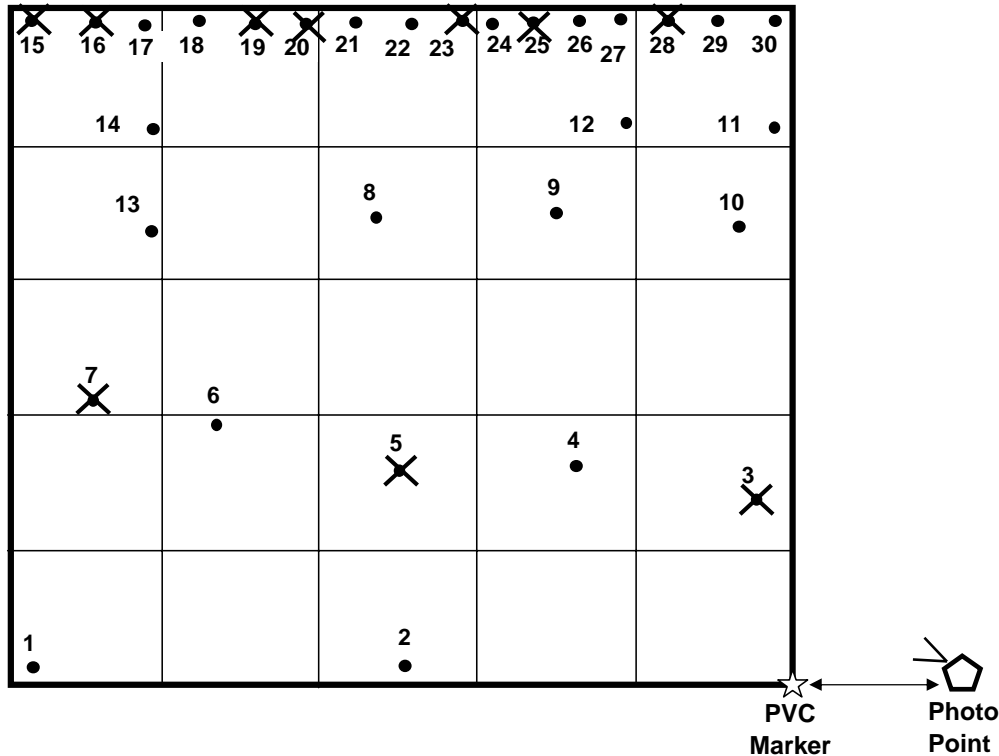

ID	Species	Height (m)	Vigor	Comment
1	River Birch (<i>Betula nigra</i>)	0.53	3	
2	River Birch (<i>Betula nigra</i>)	0.51	3	
3	<i>Quercus</i> sp.			Dead
4	Willow Oak (<i>Quercus phellos</i>)	0.44	3	
5	<i>Quercus</i> sp.			Dead
6	Sugarberry (<i>Celtis laevigata</i>)	0.21	3	Resprout
7	<i>Quercus</i> sp.			Dead
8	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.48	3	Top died back
9	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.56	3	Top died back
10	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.60	3	
11	Willow Oak (<i>Quercus phellos</i>)	0.50	3	
12	River Birch (<i>Betula nigra</i>)	0.58	3	
13	River Birch (<i>Betula nigra</i>)	0.47	3	
14	Sugarberry (<i>Celtis laevigata</i>)	0.68	4	
15	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
16	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
17	Silky Dogwood (<i>Cornus amomum</i>)	0.08	3	Live stake
18	Silky Dogwood (<i>Cornus amomum</i>)	0.18	3	Live stake
19	Black Willow (<i>Salix nigra</i>)			Live stake, dead
20	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
21	Silky Dogwood (<i>Cornus amomum</i>)	0.10	3	Live stake
22	Silky Dogwood (<i>Cornus amomum</i>)	0.10	3	Live stake
23	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
24	Silky Dogwood (<i>Cornus amomum</i>)	0.10	3	Live stake
25	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
26	Silky Dogwood (<i>Cornus amomum</i>)	0.10	3	Live stake
27	Silky Dogwood (<i>Cornus amomum</i>)	0.22	4	Live stake
28	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
29	Silky Dogwood (<i>Cornus amomum</i>)	0.11	3	Live stake
30	Elderberry (<i>Sambucus canadensis</i>)	0.18	3	Live stake
31	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.18	3	Resprout

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	38.1%
Elderberry (<i>Sambucus canadensis</i>)	4.8%
River Birch (<i>Betula nigra</i>)	19.0%
Willow Oak (<i>Quercus phellos</i>)	9.5%
Sugarberry (<i>Celtis laevigata</i>)	9.5%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	19.0%

Density:

Total Number of Trees 21 / 0.025 acres = 840 trees / acre

Survivability:

Total Number of Trees 21 / 31 trees x 100 = 68 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
River Birch (<i>Betula nigra</i>)	14.3%
American Beautyberry (<i>Callicarpa americana</i>)	28.6%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	57.1%

Density:

Total Number of Trees 7 / 0.025 acres = 280 trees / acre

Survivability:

Total Number of Trees 7 / 12 trees x 100 = 58 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S7 Date: 8/19/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.10	2	Resprout
2	Sugarberry (<i>Celtis laevigata</i>)	0.62	4	
3	Sugarberry (<i>Celtis laevigata</i>)	0.86	4	
4	Sugarberry (<i>Celtis laevigata</i>)	0.75	4	
5	Southern Red Oak (<i>Quercus falcata</i>)	0.57	3	
6	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.47	3	
7	American Beautyberry (<i>Callicarpa americana</i>)	0.44	3	
8	American Beautyberry (<i>Callicarpa americana</i>)	0.50	4	
9	American Beautyberry (<i>Callicarpa americana</i>)	0.55	4	
10	Willow Oak (<i>Quercus phellos</i>)	0.55	3	
11	Willow Oak (<i>Quercus phellos</i>)	0.21	3	Resprout
12	Willow Oak (<i>Quercus phellos</i>)	0.43	3	
13	Willow Oak (<i>Quercus phellos</i>)	0.45	3	Top died back
14	American Beautyberry (<i>Callicarpa americana</i>)	0.70	4	
15	American Beautyberry (<i>Callicarpa americana</i>)	0.46	3	
16	American Beautyberry (<i>Callicarpa americana</i>)	0.57	4	
17	American Beautyberry (<i>Callicarpa americana</i>)	0.46	3	Top died back
18	Silky Dogwood (<i>Cornus amomum</i>)	0.25	4	Live stake
19	Silky Dogwood (<i>Cornus amomum</i>)	0.45	4	Live stake
20	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
21	Silky Dogwood (<i>Cornus amomum</i>)	0.38	4	Live stake
22	Silky Dogwood (<i>Cornus amomum</i>)	0.34	4	Live stake
23	Silky Dogwood (<i>Cornus amomum</i>)	0.12	3	Live stake, deer browse
24	Silky Dogwood (<i>Cornus amomum</i>)	0.35	4	Live stake
25	Silky Dogwood (<i>Cornus amomum</i>)	0.23	3	Live stake, deer browse
26	Elderberry (<i>Sambucus canadensis</i>)	0.52	4	Live stake, deer browse
27	Elderberry (<i>Sambucus canadensis</i>)	0.58	4	Live stake
28	Elderberry (<i>Sambucus canadensis</i>)	0.41	4	Live stake
29	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.40	3	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	25.0%
Elderberry (<i>Sambucus canadensis</i>)	10.7%
American Beautyberry (<i>Callicarpa americana</i>)	25.0%
Sugarberry (<i>Celtis laevigata</i>)	10.7%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	10.7%
Southern Red Oak (<i>Quercus falcata</i>)	3.6%
Willow Oak (<i>Quercus phellos</i>)	14.3%

Density:

Total Number of Trees 28 / 0.025 acres = 1120 trees / acre

Survivability:

Total Number of Trees 28 / 29 trees x 100 = 97 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
American Beautyberry (<i>Callicarpa americana</i>)	75.0%
Willow Oak (<i>Quercus phellos</i>)	12.5%
Sugarberry (<i>Celtis laevigata</i>)	12.5%

Density:

Total Number of Trees 8 / 0.025 acres = 320 trees / acre

Survivability:

Total Number of Trees 8 / 12 trees x 100 = 67 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S9 Date: 8/20/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	Sugarberry (<i>Celtis laevigata</i>)	0.30	3	
2	Persimmon (<i>Diospyros virginiana</i>)	0.69	4	
3	Persimmon (<i>Diospyros virginiana</i>)	0.64	3	
4	Persimmon (<i>Diospyros virginiana</i>)	0.80	4	
5	Willow Oak (<i>Quercus phellos</i>)	0.60	3	
6	Willow Oak (<i>Quercus phellos</i>)	0.38	3	
7	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.43	3	
8	River Birch (<i>Betula nigra</i>)	0.49	3	
9	River Birch (<i>Betula nigra</i>)	0.55	3	
10	Persimmon (<i>Diospyros virginiana</i>)	0.79	4	
11	Willow Oak (<i>Quercus phellos</i>)	0.08	2	Resprout
12	Persimmon (<i>Diospyros virginiana</i>)	0.79	4	
13	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.35	2	
14	Willow Oak (<i>Quercus phellos</i>)	0.36	3	
15	River Birch (<i>Betula nigra</i>)	0.54	3	
16	River Birch (<i>Betula nigra</i>)	0.71	4	
17	Silky Dogwood (<i>Cornus amomum</i>)	0.28	3	
18	Silky Dogwood (<i>Cornus amomum</i>)	0.15	3	
19	Silky Dogwood (<i>Cornus amomum</i>)	0.09	2	
20	Elderberry (<i>Sambucus canadensis</i>)			Dead, live stake
21	Black Willow (<i>Salix nigra</i>)	0.42	3	Live stake
22	Silky Dogwood (<i>Cornus amomum</i>)			Dead, live stake
23	Silky Dogwood (<i>Cornus amomum</i>)			Dead, live stake
24	Silky Dogwood (<i>Cornus amomum</i>)	0.08	2	Live stake
25	Silky Dogwood (<i>Cornus amomum</i>)			Dead, live stake
26	Silky Dogwood (<i>Cornus amomum</i>)			Dead, live stake
27	Silky Dogwood (<i>Cornus amomum</i>)			Dead, live stake
28	Black Willow (<i>Salix nigra</i>)			Dead, live stake
29	Black Willow (<i>Salix nigra</i>)	0.99	4	Live stake
30	Black Willow (<i>Salix nigra</i>)			Dead, live stake
31	Black Willow (<i>Salix nigra</i>)	0.40	3	Live stake

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	17.4%
Black Willow (<i>Salix nigra</i>)	13.0%
River Birch (<i>Betula nigra</i>)	17.4%
Willow Oak (<i>Quercus phellos</i>)	17.4%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	8.7%
Persimmon (<i>Diospyros virginiana</i>)	21.7%
Sugarberry (<i>Celtis laevigata</i>)	4.3%

Density:

Total Number of Trees 23 / 0.025 acres = 920 trees / acre

Survivability:

Total Number of Trees 23 / 31 trees x 100 = 74 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
Sycamore (<i>Platanus occidentalis</i>)	44.4%
Willow Oak (<i>Quercus phellos</i>)	22.2%
Sugarberry (<i>Celtis laevigata</i>)	11.1%
Persimmon (<i>Diospyros virginiana</i>)	11.1%
American Beautyberry (<i>Callicarpa americana</i>)	11.1%

Density:

Total Number of Trees 9 / 0.025 acres = 360 trees / acre

Survivability:

Total Number of Trees 9 / 15 trees x 100 = 60 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S11 Date: 8/20/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	American Beautyberry (<i>Callicarpa americana</i>)	0.22	3	Top died back
2	Swamp Chestnut Oak (<i>Quercus michauxii</i>)			Dead
3	American Beautyberry (<i>Callicarpa americana</i>)			Dead
4	Willow Oak (<i>Quercus phellos</i>)	0.55	3	
5	American Beautyberry (<i>Callicarpa americana</i>)			Dead
6	Southern Red Oak (<i>Quercus falcata</i>)	0.24	2	
7	American Beautyberry (<i>Callicarpa americana</i>)	0.38	3	
8	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.38	3	
9	American Beautyberry (<i>Callicarpa americana</i>)	0.13	3	
10	Persimmon (<i>Diospyros virginiana</i>)	0.70	3	
11	Persimmon (<i>Diospyros virginiana</i>)	0.63	3	
12	American Beautyberry (<i>Callicarpa americana</i>)	0.43	3	
13	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.60	3	
14	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
15	Silky Dogwood (<i>Cornus amomum</i>)	0.28	3	Live stake
16	Silky Dogwood (<i>Cornus amomum</i>)	0.14	3	Live stake
17	Silky Dogwood (<i>Cornus amomum</i>)	0.18	3	Live stake
18	Silky Dogwood (<i>Cornus amomum</i>)	0.25	3	Live stake
19	Silky Dogwood (<i>Cornus amomum</i>)	0.21	3	Live stake
20	Silky Dogwood (<i>Cornus amomum</i>)	0.17	3	Live stake
21	Elderberry (<i>Sambucus canadensis</i>)	0.12	3	Live stake
22	Black Willow (<i>Salix nigra</i>)	0.24	3	Live stake
23	Sugarberry (<i>Celtis laevigata</i>)	0.44	3	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	31.6%
Elderberry (<i>Sambucus canadensis</i>)	5.3%
Black Willow (<i>Salix nigra</i>)	5.3%
American Beautyberry (<i>Callicarpa americana</i>)	21.1%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	10.5%
Willow Oak (<i>Quercus phellos</i>)	5.3%
Persimmon (<i>Diospyros virginiana</i>)	10.5%
Sugarberry (<i>Celtis laevigata</i>)	5.3%
Southern Red Oak (<i>Quercus falcata</i>)	5.3%

Density:

Total Number of Trees **19** / 0.025 acres = **760** trees / acre

Survivability:

Total Number of Trees **19** / 23 trees x 100 = **83** % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
River Birch (<i>Betula nigra</i>)	45.5%
Sycamore (<i>Platanus occidentalis</i>)	18.2%
American Beautyberry (<i>Callicarpa americana</i>)	9.1%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	18.2%
Sugarberry (<i>Celtis laevigata</i>)	9.1%

Density:

Total Number of Trees 11 / 0.025 acres = 440 trees / acre

Survivability:

Total Number of Trees 11 / 15 x 100 = 73 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S13 Date: 8/20/2008

Plot Map



ID	Species	Height (m)	Vigor	Comment
1	Sugarberry (<i>Celtis laevigata</i>)	0.42	3	
2	Sugarberry (<i>Celtis laevigata</i>)	0.39	3	
3	Unknown			Missing
4	American Beautyberry (<i>Callicarpa americana</i>)			Dead
5	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.54	2	
6	Sycamore (<i>Platanus occidentalis</i>)	0.70	4	
7	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.32	3	Deer browse
8	Possumhaw (<i>Viburnum nudum</i>)	0.39	3	
9	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.62	3	
10	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.58	3	
11	Sugarberry (<i>Celtis laevigata</i>)	0.30	3	
12	Possumhaw (<i>Viburnum nudum</i>)	0.25	3	
13	Sugarberry (<i>Celtis laevigata</i>)	0.46	3	
14	Sugarberry (<i>Celtis laevigata</i>)	0.34	3	
15	Possumhaw (<i>Viburnum nudum</i>)			Dead
16	Sugarberry (<i>Celtis laevigata</i>)	0.35	1	
17	Sugarberry (<i>Celtis laevigata</i>)	0.27	3	
18	American Beautyberry (<i>Callicarpa americana</i>)	0.38	4	
19	American Beautyberry (<i>Callicarpa americana</i>)	0.22	3	
20	American Beautyberry (<i>Callicarpa americana</i>)	0.54	3	
21	American Beautyberry (<i>Callicarpa americana</i>)	0.55	3	
22	Silky Dogwood (<i>Cornus amomum</i>)	0.13	3	Live stake
23	Silky Dogwood (<i>Cornus amomum</i>)	0.08	3	Live stake
24	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
25	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
26	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
27	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
28	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
29	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	10.0%
Sycamore (<i>Platanus occidentalis</i>)	5.0%
American Beautyberry (<i>Callicarpa americana</i>)	20.0%
Sugarberry (<i>Celtis laevigata</i>)	35.0%
Possumhaw (<i>Viburnum nudum</i>)	10.0%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	20.0%

Density:

Total Number of Trees 20 / 0.025 acres = 800 trees / acre

Survivability:

Total Number of Trees 20 / 29 x 100 = 69 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S14 Date: 8/20/2008

Plot Map

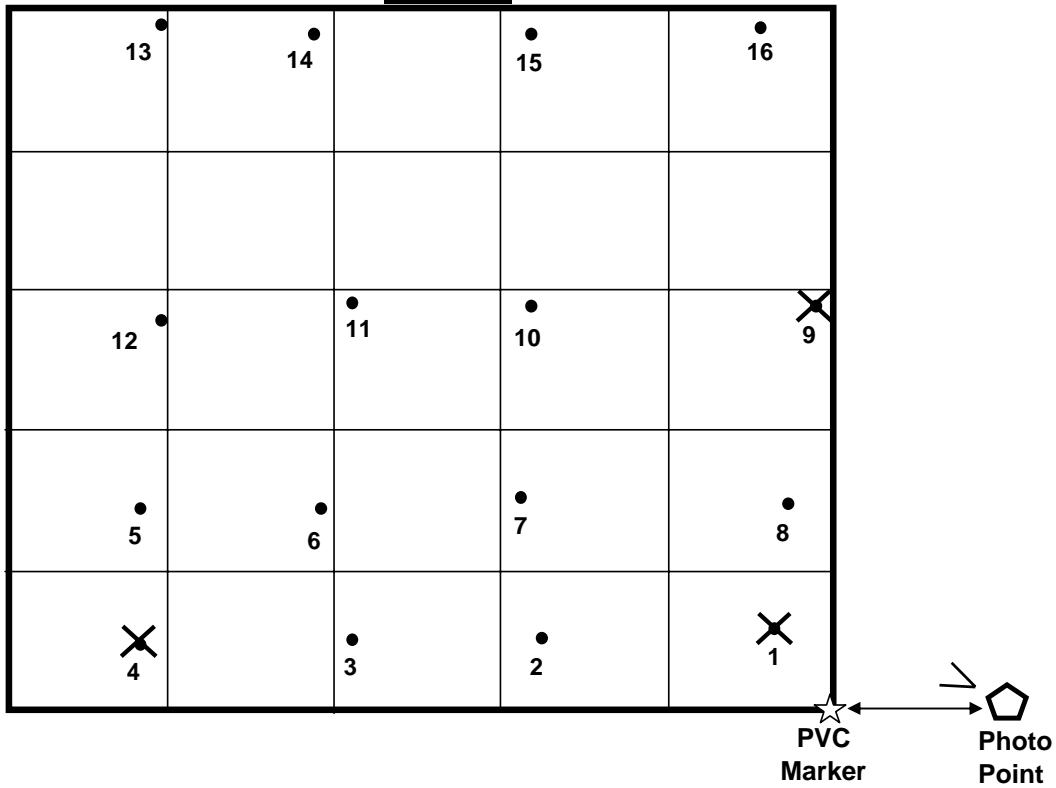

ID	Species	Height (m)	Vigor	Comment
1	American Beautyberry (<i>Callicarpa americana</i>)			Dead
2	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.60	3	
3	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.56	3	
4	<i>Quercus sp.</i>			Dead
5	Persimmon (<i>Diospyros virginiana</i>)	0.52	4	
6	River Birch (<i>Betula nigra</i>)	0.74	3	
7	American Beautyberry (<i>Callicarpa americana</i>)	0.56	3	
8	Persimmon (<i>Diospyros virginiana</i>)	0.71	4	
9	Willow Oak (<i>Quercus phellos</i>)			Dead
10	Persimmon (<i>Diospyros virginiana</i>)	0.67	3	
11	Persimmon (<i>Diospyros virginiana</i>)	0.66	3	
12	Persimmon (<i>Diospyros virginiana</i>)	0.57	3	
13	River Birch (<i>Betula nigra</i>)	0.47	3	
14	Persimmon (<i>Diospyros virginiana</i>)	0.57	3	
15	Persimmon (<i>Diospyros virginiana</i>)	0.55	3	
16	American Beautyberry (<i>Callicarpa americana</i>)	0.25	3	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
River Birch (<i>Betula nigra</i>)	15.4%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	15.4%
Persimmon (<i>Diospyros virginiana</i>)	53.8%
American Beautyberry (<i>Callicarpa americana</i>)	15.4%

Density:

Total Number of Trees 13 / 0.025 acres = 520 trees / acre

Survivability:

Total Number of Trees 13 / 16 x 100 = 81 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S15 Date: 8/20/2008

Plot Map

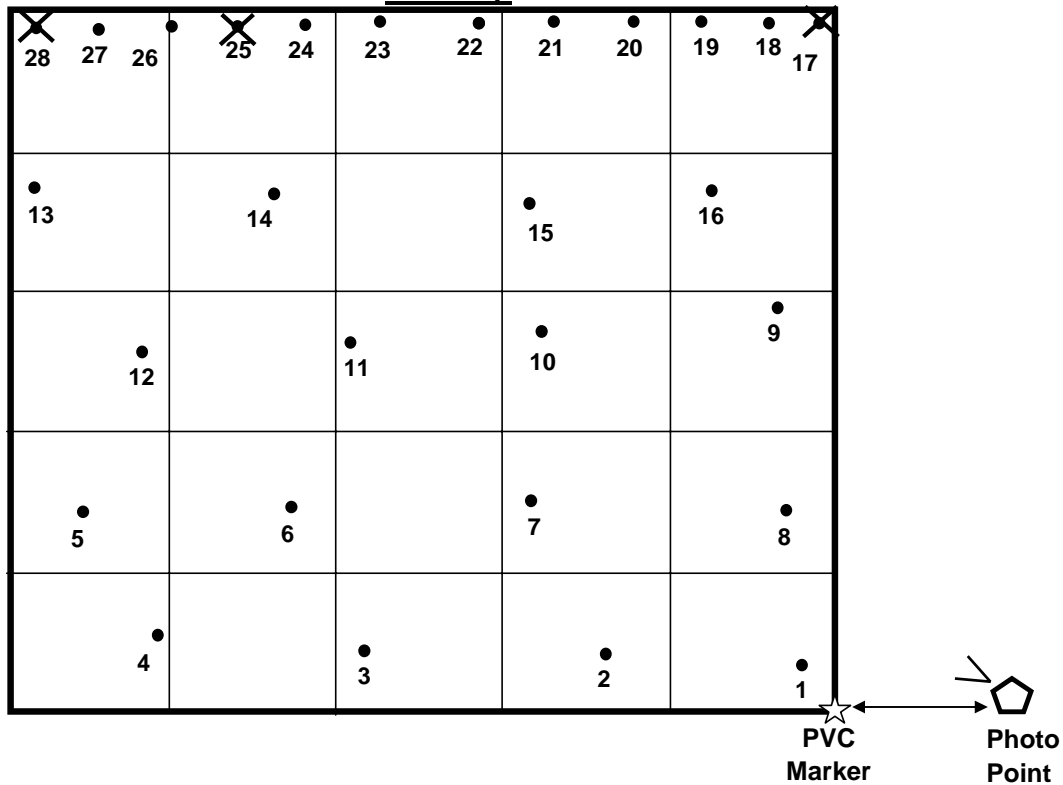

ID	Species	Height (m)	Vigor	Comment
1	River Birch (<i>Betula nigra</i>)	0.72	3	
2	River Birch (<i>Betula nigra</i>)	0.90	4	
3	River Birch (<i>Betula nigra</i>)	0.59	3	
4	River Birch (<i>Betula nigra</i>)	0.51	3	
5	Sugarberry (<i>Celtis laevigata</i>)	0.31	3	
6	Sugarberry (<i>Celtis laevigata</i>)	0.24	3	
7	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.55	3	
8	Sugarberry (<i>Celtis laevigata</i>)	0.35	3	
9	American Beautyberry (<i>Callicarpa americana</i>)	0.14	3	Resprout
10	Sycamore (<i>Platanus occidentalis</i>)	0.70	4	
11	Sycamore (<i>Platanus occidentalis</i>)	0.75	3	
12	Sycamore (<i>Platanus occidentalis</i>)	0.55	3	
13	Green Ash (<i>Fraxinus Pennsylvanica</i>)	0.52	3	
14	American Beautyberry (<i>Callicarpa americana</i>)	0.15	2	Resprout
15	American Beautyberry (<i>Callicarpa americana</i>)	0.34	3	
16	American Beautyberry (<i>Callicarpa americana</i>)	0.49	3	
17	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
18	Silky Dogwood (<i>Cornus amomum</i>)	0.11	3	Live stake
19	Silky Dogwood (<i>Cornus amomum</i>)	0.22	3	Live stake
20	Silky Dogwood (<i>Cornus amomum</i>)	0.09	3	Live stake
21	Silky Dogwood (<i>Cornus amomum</i>)	0.22	3	Live stake
22	Silky Dogwood (<i>Cornus amomum</i>)	0.15	3	Live stake
23	Silky Dogwood (<i>Cornus amomum</i>)	0.18	3	Live stake
24	Silky Dogwood (<i>Cornus amomum</i>)	0.17	3	Live stake
25	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
26	Silky Dogwood (<i>Cornus amomum</i>)	0.09	3	Live stake
27	Silky Dogwood (<i>Cornus amomum</i>)	0.08	3	Live stake
28	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Silky Dogwood (<i>Cornus amomum</i>)	36.0%
River Birch (<i>Betula nigra</i>)	16.0%
Sycamore (<i>Platanus occidentalis</i>)	12.0%
Sugarberry (<i>Celtis laevigata</i>)	12.0%
Green Ash (<i>Fraxinus pennsylvanica</i>)	4.0%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	4.0%
American Beautyberry (<i>Callicarpa americana</i>)	16.0%

Density:

Total Number of Trees 25 / 0.025 acres = 1000 trees / acre

Survivability:

Total Number of Trees 25 / 28 x 100 = 89 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
American Beautyberry (<i>Callicarpa americana</i>)	33.3%
Sycamore (<i>Platanus occidentalis</i>)	8.3%
River Birch (<i>Betula nigra</i>)	8.3%
Persimmon (<i>Diospyros virginiana</i>)	8.3%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	41.7%

Density:

Total Number of Trees 12 / 0.025 acres = 480 trees / acre

Survivability:

Total Number of Trees 12 / 15 x 100 = 80 % survivability



**Baseline
Monitoring**




**1st Year
Monitoring**

Vegetation Monitoring Worksheet

Site: Harrell Plot: S17 Date: 8/20/2008

Plot Map

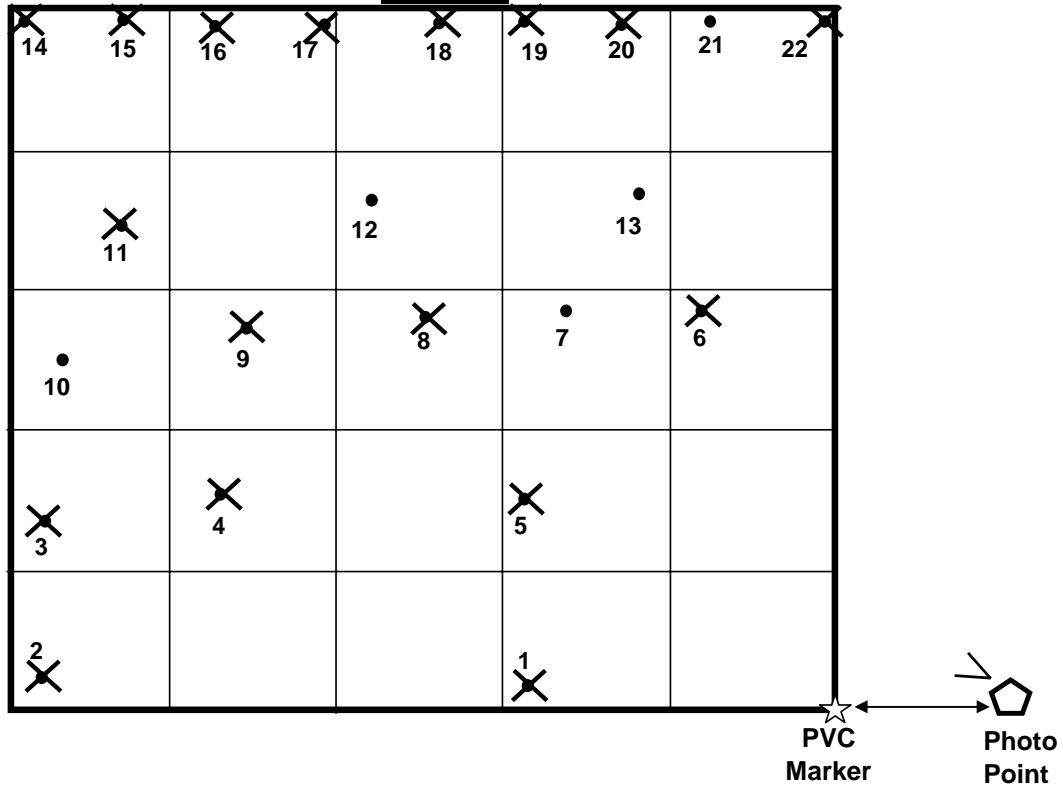

ID	Species	Height (m)	Vigor	Comment
1	Swamp Chestnut Oak (<i>Quercus michauxii</i>)			Dead
2	Sugarberry (<i>Celtis laevigata</i>)			Dead
3	Unknown			Dead
4	Willow Oak (<i>Quercus phellos</i>)			Dead
5	Sugarberry (<i>Celtis laevigata</i>)			Dead
6	Persimmon (<i>Diospyros virginiana</i>)			Dead
7	Persimmon (<i>Diospyros virginiana</i>)	0.79	3	
8	Persimmon (<i>Diospyros virginiana</i>)			Dead
9	Swamp Chestnut Oak (<i>Quercus michauxii</i>)			Dead
10	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.61	3	
11	Willow Oak (<i>Quercus phellos</i>)			Dead
12	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.01	1	Resprout, flag not on tree
13	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	0.56	3	
14	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead
15	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
16	Black Willow (<i>Salix nigra</i>)			Live stake, dead
17	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
18	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
19	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
20	Elderberry (<i>Sambucus canadensis</i>)			Live stake, dead
21	Elderberry (<i>Sambucus canadensis</i>)	0.11	3	Live stake, deer browse
22	Silky Dogwood (<i>Cornus amomum</i>)			Live stake, dead

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Elderberry (<i>Sambucus canadensis</i>)	20.0%
Persimmon (<i>Diospyros virginiana</i>)	20.0%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	60.0%

Density:

Total Number of Trees 5 / 0.025 acres = 200 trees / acre

Survivability:

Total Number of Trees 5 / 22 x 100 = 23 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
River Birch (<i>Betula nigra</i>)	62.5%
Willow Oak (<i>Quercus phellos</i>)	25.0%
Green Ash (<i>Fraxinus pennsylvanica</i>)	12.5%

Density:

Total Number of Trees 8 / 0.025 acres = 320 trees / acre

Survivability:

Total Number of Trees 8 / 17 x 100 = 47 % survivability



**Baseline
Monitoring**



**1st Year
Monitoring**

Species	Percent of Total
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	10.0%
Green Ash (<i>Fraxinus pennsylvanica</i>)	40.0%
Buttonbush (<i>Cephalanthus occidentalis</i>)	10.0%
Laurel Oak (<i>Quercus laurifolia</i>)	10.0%
Cherrybark Oak (<i>Quercus pagoda</i>)	20.0%
Beautyberry (<i>Callicarpa americana</i>)	10.0%

Density:

Total Number of Trees 10 / 0.025 acres = 400 trees / acre

Survivability:

Total Number of Trees 10 / 13 trees x 100 = 77 % survivability



Previous




Current

Vegetation Monitoring Worksheet

Site: Harrell Plot: 2 Date: 8/18/2008

Plot Map

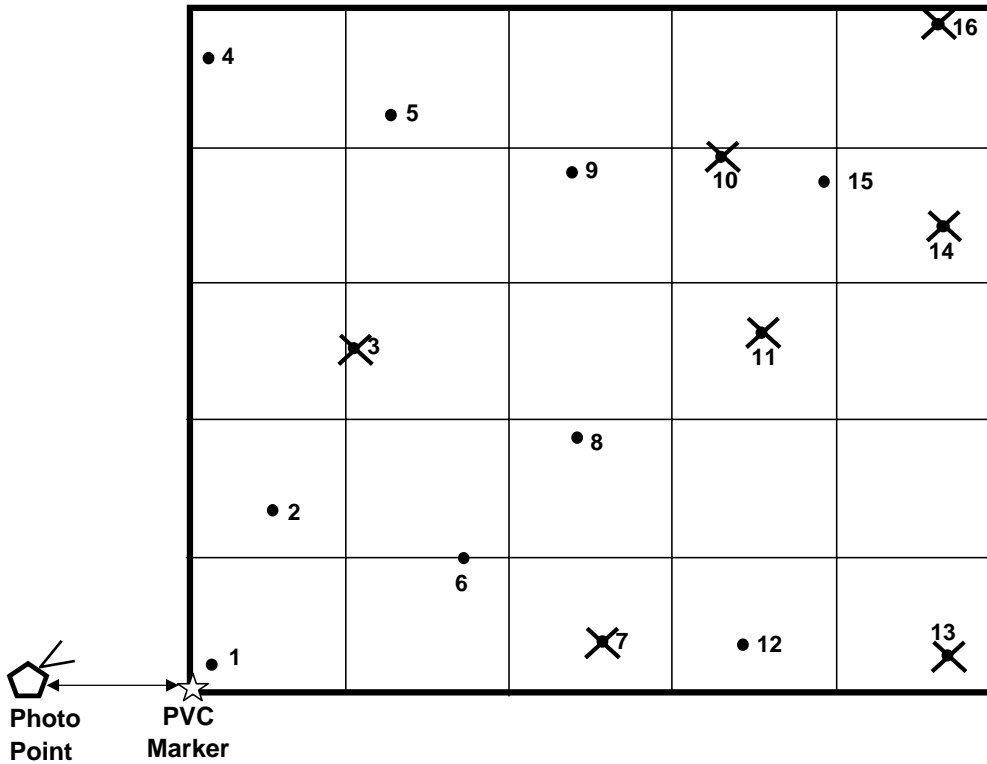

ID	Species	Height (m)	Vigor	Comment
1	Willow Oak (<i>Quercus phellos</i>)	0.30	3	
2	Laurel Oak (<i>Quercus laurifolia</i>)	0.78	4	
3	Unknown			Dead
4	Willow Oak (<i>Quercus phellos</i>)	0.78	4	
5	Cherrybark Oak (<i>Quercus pagoda</i>)	0.22	3	Top died back
6	Cherrybark Oak (<i>Quercus pagoda</i>)	0.59	3	
7	Cherrybark Oak (<i>Quercus pagoda</i>)			Dead
8	Cherrybark Oak (<i>Quercus pagoda</i>)	0.73	4	
9	Cherrybark Oak (<i>Quercus pagoda</i>)	0.36	3	Resprout
10	Unknown			Dead
11	Unknown			Dead
12	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.97	4	
13	Unknown			Dead
14	Unknown			Dead
15	Cherrybark Oak (<i>Quercus pagoda</i>)	0.26	3	Resprout
16	Unknown			Dead

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Willow Oak (<i>Quercus phellos</i>)	22.2%
Cherrybark Oak (<i>Quercus pagoda</i>)	55.6%
Buttonbush (<i>Cephalanthus occidentalis</i>)	11.1%
Laurel Oak (<i>Quercus laurifolia</i>)	11.1%

Density:

Total Number of Trees 9 / 0.025 acres = 360 trees / acre

Survivability:

Total Number of Trees 9 / 16 trees x 100 = 56 % survivability



Previous



Current

Species	Percent of Total
Bald Cypress (<i>Taxodium distichum</i>)	60.0%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	10.0%
Buttonbush (<i>Cephalanthus occidentalis</i>)	20.0%
Cherrybark Oak (<i>Quercus pagoda</i>)	10.0%

Density:

Total Number of Trees 10 / 0.025 acres = 400 trees / acre

Survivability:

Total Number of Trees 10 / 15 trees x 100 = 67 % survivability



Previous




Current

Vegetation Monitoring Worksheet

Site: Harrell Plot: 4 Date: 8/19/2008

Plot Map

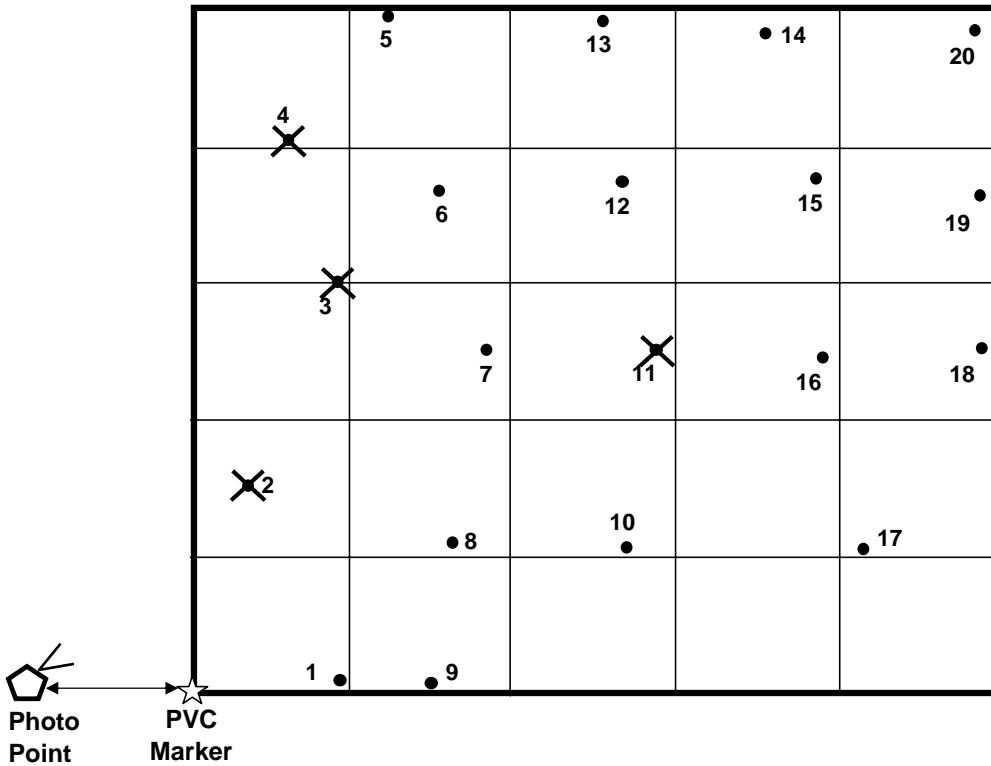

ID	Species	Height (m)	Vigor	Comment
1	Green Ash (<i>Fraxinus pennsylvanica</i>)	0.72	4	
2	Cherrybark Oak (<i>Quercus pagoda</i>)			Dead
3	Unknown			Dead
4	Unknown			Dead
5	Buttonbush (<i>Cephalanthus occidentalis</i>)	1.00	4	
6	Cherrybark Oak (<i>Quercus pagoda</i>)	0.44	3	Resprout
7	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.96	4	
8	Cherrybark Oak (<i>Quercus pagoda</i>)	0.72	4	
9	Buttonbush (<i>Cephalanthus occidentalis</i>)	1.07	4	
10	Laurel Oak (<i>Quercus laurifolia</i>)	0.83	4	
11	Unknown			Dead
12	Swamp Chestnut Oak (<i>Quercus michauxii</i>)	1.37	4	
13	Laurel Oak (<i>Quercus laurifolia</i>)	1.05	4	
14	Willow Oak (<i>Quercus phellos</i>)	0.65	4	
15	Cherrybark Oak (<i>Quercus pagoda</i>)	0.25	3	Resprout
16	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.93	4	
17	Cherrybark Oak (<i>Quercus pagoda</i>)	0.99	4	
18	Green Ash (<i>Fraxinus pennsylvanica</i>)	0.94	4	
19	Beautyberry (<i>Callicarpa americana</i>)	0.47	3	
20	Willow Oak (<i>Quercus phellos</i>)	0.64	3	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year


Species	Percent of Total
Green Ash (<i>Fraxinus pennsylvanica</i>)	12.5%
Cherrybark Oak (<i>Quercus pagoda</i>)	25.0%
Buttonbush (<i>Cephalanthus occidentalis</i>)	25.0%
Laurel Oak (<i>Quercus laurifolia</i>)	12.5%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	6.3%
Willow Oak (<i>Quercus phellos</i>)	12.5%
Beautyberry (<i>Callicarpa americana</i>)	6.3%

Density:

Total Number of Trees 16 / 0.025 acres = 640 trees / acre

Survivability:

Total Number of Trees 16 / 20 trees x 100 = 80 % survivability

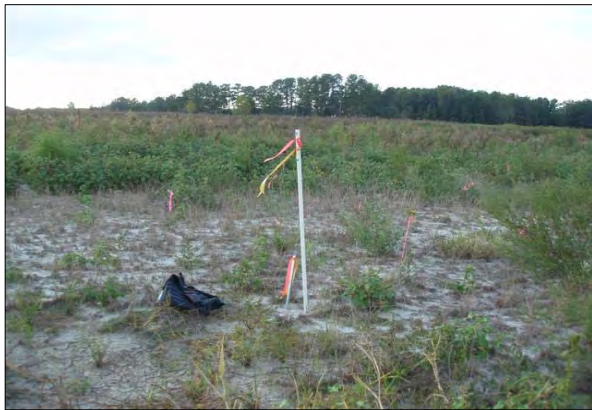

Previous



Current

Species	Percent of Total
Bald Cypress (<i>Taxodium distichum</i>)	28.6%
Green Ash (<i>Fraxinus pennsylvanica</i>)	28.6%
Cherrybark Oak (<i>Quercus pagoda</i>)	7.1%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	28.6%
Beautyberry (<i>Callicarpa americana</i>)	7.1%

Density:

Total Number of Trees 14 / 0.025 acres = 560 trees / acre

Survivability:

Total Number of Trees 14 / 15 trees x 100 = 93 % survivability



Previous



Current

Species	Percent of Total
Bald Cypress (<i>Taxodium distichum</i>)	20.0%
Willow Oak (<i>Quercus phellos</i>)	33.3%
Laurel Oak (<i>Quercus laurifolia</i>)	13.3%
Buttonbush (<i>Cephalanthus occidentalis</i>)	33.3%

Density:

Total Number of Trees 15 / 0.025 acres = 600 trees / acre

Survivability:

Total Number of Trees 15 / 18 trees x 100 = 83 % survivability



Previous



Current


Species	Percent of Total
Willow Oak (<i>Quercus phellos</i>)	50.0%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	33.3%
Cherrybark Oak (<i>Quercus pagoda</i>)	16.7%

Density:

Total Number of Trees 6 / 0.025 acres = 240 trees / acre

Survivability:

Total Number of Trees 6 / 17 trees x 100 = 35 % survivability

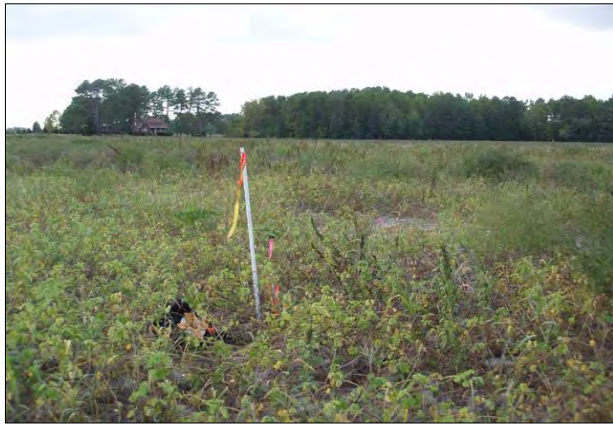

Previous




Current

Vegetation Monitoring Worksheet

Site: Harrell Plot: 8 Date: 8/18/2008

Plot Map

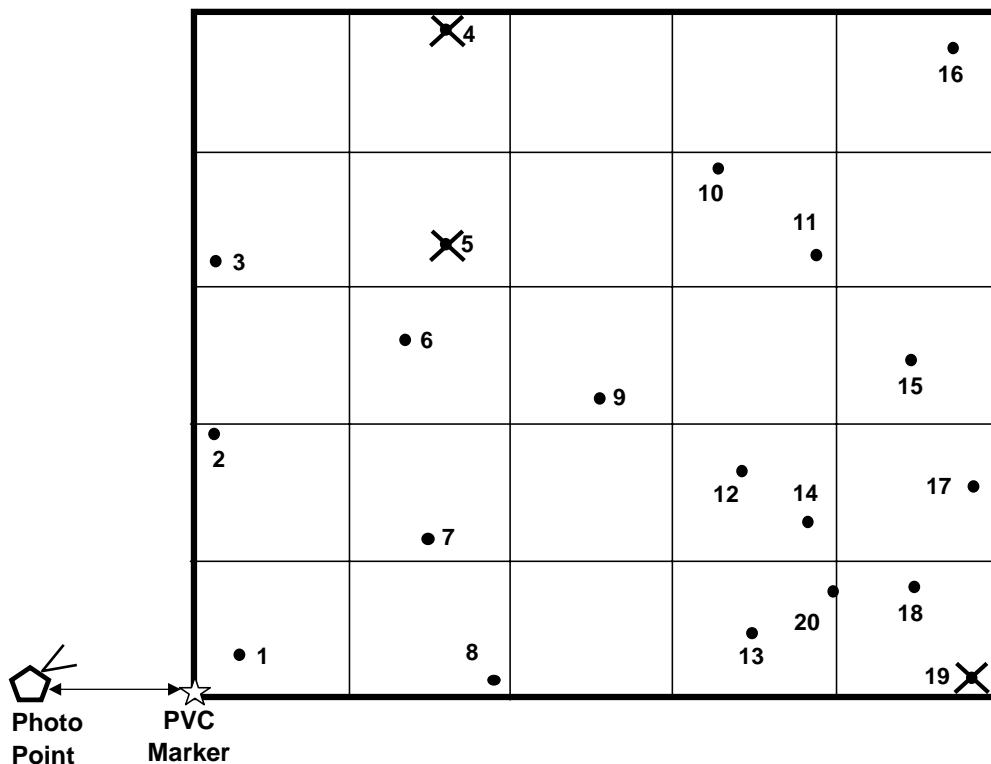

ID	Species	Height (m)	Vigor	Comment
1	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.03	2	Resprout
2	Water Hickory (<i>Carya aquatica</i>)	0.55	3	Deer browse
3	Water Hickory (<i>Carya aquatica</i>)	0.83	4	
4	Unknown			Dead
5	Unknown			Dead
6	Water Hickory (<i>Carya aquatica</i>)	0.48	3	
7	Bald Cypress (<i>Taxodium distichum</i>)	0.96	4	
8	Water Hickory (<i>Carya aquatica</i>)	0.70	3	
9	Bald Cypress (<i>Taxodium distichum</i>)	0.69	3	
10	Water Hickory (<i>Carya aquatica</i>)	0.78	3	
11	Water Hickory (<i>Carya aquatica</i>)	0.81	4	
12	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.54	4	
13	Bald Cypress (<i>Taxodium distichum</i>)	0.97	4	
14	Water Hickory (<i>Carya aquatica</i>)	0.72	4	
15	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.85	4	
16	Beautyberry (<i>Callicarpa americana</i>)	0.41	3	Top died back
17	Water Hickory (<i>Carya aquatica</i>)	0.64	3	
18	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.94	4	
19	Bald Cypress (<i>Taxodium distichum</i>)			Dead
20	Cherrybark Oak (<i>Quercus pagoda</i>)	0.40	4	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Water Hickory (<i>Carya aquatica</i>)	47.1%
Bald Cypress (<i>Taxodium distichum</i>)	17.6%
Buttonbush (<i>Cephalanthus occidentalis</i>)	23.5%
Beautyberry (<i>Callicarpa americana</i>)	5.9%
Cherrybark Oak (<i>Quercus pagoda</i>)	5.9%

Density:

Total Number of Trees 17 / 0.025 acres = 680 trees / acre

Survivability:

Total Number of Trees 17 / 20 trees x 100 = 85 % survivability



Previous



Current

Species	Percent of Total
Green Ash (<i>Fraxinus pennsylvanica</i>)	14.3%
Laurel Oak (<i>Quercus laurifolia</i>)	21.4%
Willow Oak (<i>Quercus phellos</i>)	7.1%
Cherrybark Oak (<i>Quercus pagoda</i>)	28.6%
Swamp Chestnut Oak (<i>Quercus michauxii</i>)	7.1%
Buttonbush (<i>Cephalanthus occidentalis</i>)	7.1%
Beautyberry (<i>Callicarpa americana</i>)	14.3%

Density:

Total Number of Trees 14 / 0.025 acres = 560 trees / acre

Survivability:

Total Number of Trees 14 / 16 trees x 100 = 88 % survivability



Previous



Current

Species	Percent of Total
Laurel Oak (<i>Quercus laurifolia</i>)	28.6%
Bald Cypress (<i>Taxodium distichum</i>)	7.1%
Green Ash (<i>Fraxinus pennsylvanica</i>)	21.4%
Cherrybark Oak (<i>Quercus pagoda</i>)	14.3%
Buttonbush (<i>Cephalanthus occidentalis</i>)	21.4%
Beautyberry (<i>Callicarpa americana</i>)	7.1%

Density:

Total Number of Trees 14 / 0.025 acres = 560 trees / acre

Survivability:

Total Number of Trees 14 / 15 trees x 100 = 93 % survivability



Previous



Current

Species	Percent of Total
Bald Cypress (<i>Taxodium distichum</i>)	42.9%
Water Hickory (<i>Carya aquatica</i>)	21.4%
Buttonbush (<i>Cephalanthus occidentalis</i>)	28.6%
Beautyberry (<i>Callicarpa americana</i>)	7.1%

Density:

Total Number of Trees 14 / 0.025 acres = 560 trees / acre

Survivability:

Total Number of Trees 14 / 17 trees x 100 = 82 % survivability



Previous




Current

Vegetation Monitoring Worksheet

Site: Harrell Plot: W12 Date: 8/18/2008

Plot Map

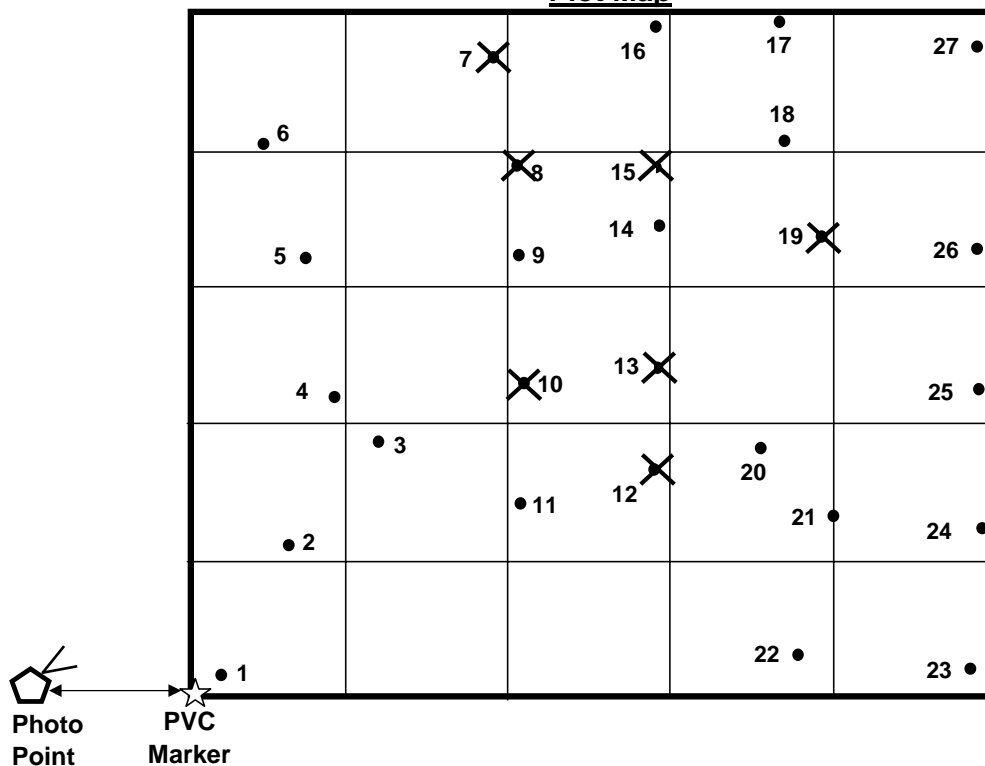

ID	Species	Height (m)	Vigor	Comment
1	Water Hickory (<i>Carya aquatica</i>)	1.00	4	
2	Bald Cypress (<i>Taxodium distichum</i>)	1.12	4	
3	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.52	3	Resprout, deer browse
4	Bald Cypress (<i>Taxodium distichum</i>)	0.62	3	
5	Bald Cypress (<i>Taxodium distichum</i>)	0.92	4	
6	Bald Cypress (<i>Taxodium distichum</i>)	0.98	4	
7	Beautyberry (<i>Callicarpa americana</i>)			Dead
8	Buttonbush (<i>Cephalanthus occidentalis</i>)			Dead
9	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.53	3	
10	Buttonbush (<i>Cephalanthus occidentalis</i>)			Dead
11	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.30	3	Top died back
12	Buttonbush (<i>Cephalanthus occidentalis</i>)			Missing
13	Unknown			Missing
14	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.55	3	
15	Buttonbush (<i>Cephalanthus occidentalis</i>)			Dead
16	Water Hickory (<i>Carya aquatica</i>)	0.75	4	
17	Water Hickory (<i>Carya aquatica</i>)	0.78	4	
18	Water Hickory (<i>Carya aquatica</i>)	0.72	4	
19	Buttonbush (<i>Cephalanthus occidentalis</i>)			Dead
20	Water Hickory (<i>Carya aquatica</i>)	0.50	3	
21	Bald Cypress (<i>Taxodium distichum</i>)	1.26	4	
22	Bald Cypress (<i>Taxodium distichum</i>)	0.99	4	
23	Bald Cypress (<i>Taxodium distichum</i>)	0.89	4	
24	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.35	1	
25	Buttonbush (<i>Cephalanthus occidentalis</i>)	0.89	3	Deer browse
26	Bald Cypress (<i>Taxodium distichum</i>)	1.29	4	
27	Bald Cypress (<i>Taxodium distichum</i>)	0.96	4	

Vigor: 4=excellent, 3=good, 2=weak, 1=unlikely to survive year

Species	Percent of Total
Water Hickory (<i>Carya aquatica</i>)	25.0%
Bald Cypress (<i>Taxodium distichum</i>)	45.0%
Buttonbush (<i>Cephalanthus occidentalis</i>)	30.0%

Density:

Total Number of Trees 20 / 0.025 acres = 800 trees / acre

Survivability:

Total Number of Trees 20 / 27 x 100 = 74 % survivability



Previous



Current

Appendix B

Stream and Wetland Photos

Appendix B1 – Stream and Wetland Photo Stations



Photo Point S1: View looking upstream near Station 12+75. 11/19/08 – MY-01



Photo Point S1: View looking downstream near Station 12+75. 11/19/08 – MY-01



Photo Point S2: View looking upstream from farm road near Station 21+30. 11/19/08 – MY-01



Photo Point S2: View looking downstream from farm road near Station 21+30. 11/19/08 - MY-01



Photo Point S3: View looking upstream near Station 27+60. 11/19/08 – MY-01



Point S3: View looking downstream near Station 27+60. 11/19/08 – MY-01



Photo Point S4: View of water quality treatment structure near Station 32+25. 11/19/08 – MY-01



Photo Point S5: View looking at log drop structures, near Station 33+35. 11/19/08 – MY-01



Photo Point S5: View looking downstream near Station 33+35. 11/19/08 – MY-01



Photo Point S6: View of incoming drainage ditch near Station 37+25. 11/19/08 – MY-01



Photo Point S7: View looking upstream near Station 39+00. 11/19/08 – MY-01



Photo Point S7: View looking downstream near Station 39+00. 11/19/08 – MY-01



Photo Point S8: View of log drop structure near Station 39+50. 11/19/08 – MY-01



Photo Point S9: View of water quality treatment structure near Station 41+75. 11/19/08 – MY-01



Photo Point S10: View looking upstream near Station 46+15. 11/19/08 – MY-01



Photo Point S10: View looking downstream near Station 46+15. 11/19/08 – MY-01



Photo Point S11: View of water quality treatment structure near Station 47+00. 11/19/08 - MY-01



Photo Point S12: View looking upstream near Station 52+00. 11/19/08 - MY-01



Photo Point S12: View looking downstream near Station 52+00. 11/19/08 – MY-01



Photo Point S13: View looking upstream near Station 61+50. 11/19/08 – MY-01



Photo Point S13: View of water quality treatment structure near Station 61+50. 11/19/08 - MY-01



Photo Point S13: View looking downstream near Station 61+50. 11/19/08 – MY-01



Photo Point S14: View of stream with water quality treatment structure in the background near Station 62+60. 11/19/08 - MY-01



Photo Point S15: View looking upstream near Station 69+00. 11/19/08 – MY-01



Photo Point S15: View looking downstream near Station 69+00. 11/19/08 – MY-01



Photo Point S16: View looking upstream near Station 76+75. 11/19/08 – MY-01



Photo Point S16: View looking downstream toward project end before the project stream joins Swift Creek near Station 76+75. 11/19/08 – MY-01



Photo Point W1: View looking north from southwest corner of wetland. 8/20/08 – MY-01



Photo Point W1: View looking east from southwest corner of wetland. 8/20/08 – MY-01



Photo Point W2: View looking east from northwest corner of wetland. 8/20/08 – MY-01



Photo Point W2: View looking southeast from northwest corner of wetland. 8/20/08 – MY-01



Photo Point W3: View looking east from middle corner of wetland. 8/20/08 – MY-01



Photo Point W3: View looking west from middle corner of wetland. 8/20/08 – MY-01



Photo Point W3: View looking southwest from middle corner of wetland. 8/20/08 – MY-01



Photo Point W4: View looking north toward Wetland Gauge 1. 8/20/08 – MY-01



Photo Point W5: View looking west toward the downstream end of site. 8/20/08 – MY-01

Appendix B2: Representative Stream Problem Area Photos



SP1 – Bed aggradation near Station 14+75. 11/19/08 – MY-01



SP2 – Bed degradation near Station 33+40. 11/19/08 – MY-01



SP3 – Floodplain erosion near Station 43+95. 11/19/08 – MY-01



SP4 – Dense vegetation in channel near Station 56+50. 11/19/08 – MY-01

Appendix C

Geomorphologic and Hydrologic Data

C1 - Stream Cross-Sections


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 1
Drainage Area (sq mi):	0.20
Date:	9/4/2008
Field Crew:	B. Roberts, A. Davis



Stream Type B5c

SUMMARY DATA	
Bankfull Elevation:	84.9
Bankfull Cross-Sectional Area:	13.4
Bankfull Width:	10.4
Flood Prone Area Elevation:	87.0
Flood Prone Width:	27
Max Depth at Bankfull:	2.1
Mean Depth at Bankfull:	1.3
W / D Ratio:	8.1
Entrenchment Ratio:	2.6
Bank Height Ratio:	1.0

Station	Elevation
0.0	87.95
0.3	87.95
3.4	88.05
7.1	88.03
10.4	88.02
12.7	87.69
14.2	87.42
17.0	87.02
22.3	86.05
26.3	85.17
28.1	84.73
29.5	83.71
30.4	83.22
31.1	82.87
31.9	82.76
32.7	82.76
33.4	82.76
33.6	82.76
33.9	82.82
34.4	83.16
35.3	83.62
36.1	84.10
38.5	85.21
39.3	85.31
41.5	86.05
44.4	86.92
46.0	87.10
49.3	87.23
51.9	87.38
56.0	87.51
58.0	87.62
59.5	87.61

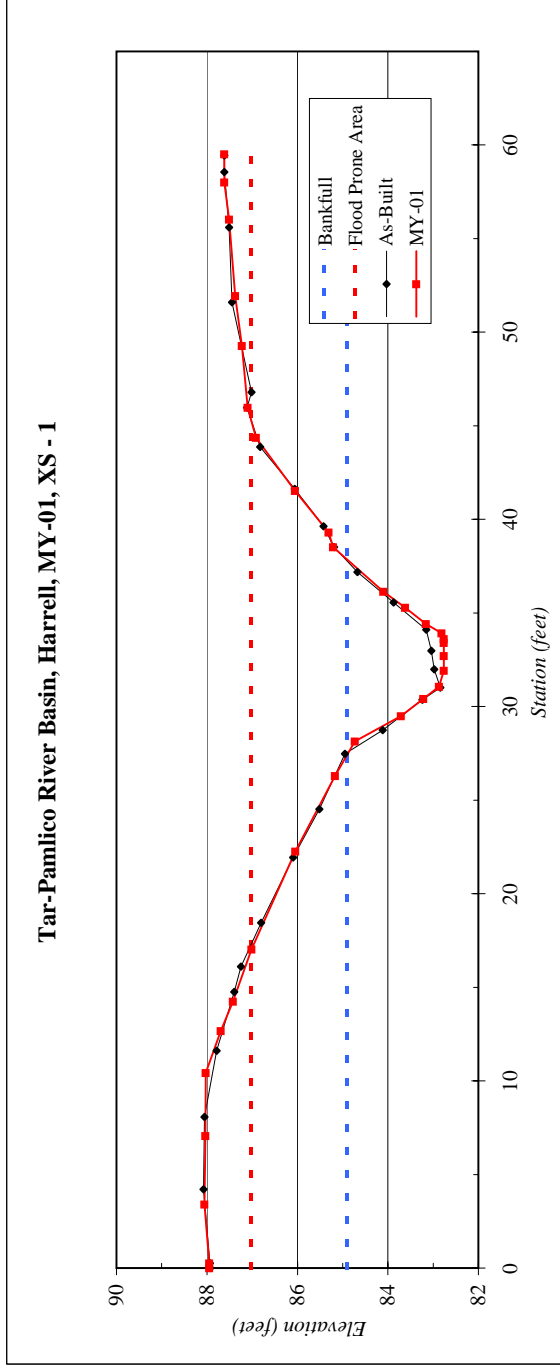

River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 2
Drainage Area (sq mi):	0.20
Date:	9/4/2008
Field Crew:	B. Roberts, A. Davis




Stream Type B5c

SUMMARY DATA	
Bankfull Elevation:	82.4
Bankfull Cross-Sectional Area:	12.9
Bankfull Width:	12.7
Flood Prone Area Elevation:	84.0
Flood Prone Width:	2.5
Max Depth at Bankfull:	1.7
Mean Depth at Bankfull:	1.0
W / D Ratio:	12.5
Entrenchment Ratio:	2.0
Bank Height Ratio:	1.0

Station	Elevation
0.0	86.37
0.5	86.28
4.2	86.01
7.3	86.19
9.8	86.15
12.4	85.93
14.9	85.32
16.8	85.30
19.5	84.74
22.4	84.10
24.7	83.49
26.5	82.76
27.8	81.94
29.6	81.18
30.0	81.20
30.6	81.47
32.6	81.54
33.6	81.07
34.7	80.77
35.4	80.69
36.2	80.81
37.3	81.15
38.5	81.66
39.1	82.20
40.8	82.69
48.1	85.35
51.7	85.89
55.1	86.22
57.6	86.01
58.9	85.82
62.9	85.89
67.5	86.09
68.0	86.34
70.2	86.22

Tar-Pamlico River Basin, Harrell, MY-01, XS - 2

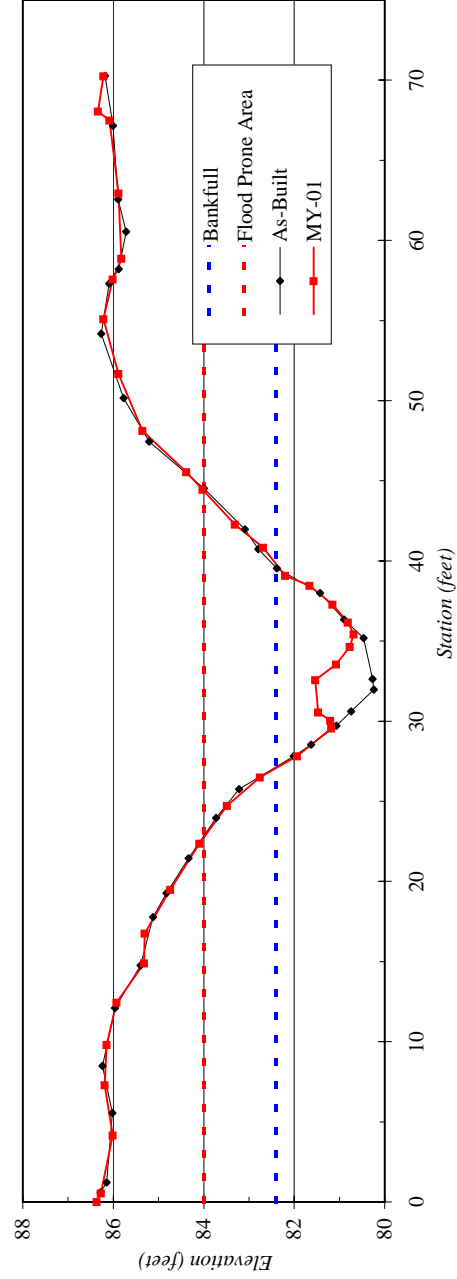


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 3
Drainage Area (sq mi):	0.23
Date:	9/4/2008
Field Crew:	B. Roberts, A. Davis



Stream Type C5

SUMMARY DATA	
Bankfull Elevation:	80.5
Bankfull Cross-Sectional Area:	12.6
Bankfull Width:	13.1
Flood Prone Area Elevation:	82.4
Flood Prone Width:	>55
Max Depth at Bankfull:	1.9
Mean Depth at Bankfull:	1.0
W / D Ratio:	13.6
Entrenchment Ratio:	>4
Bank Height Ratio:	1.0

Station	Elevation
0.0	81.87
1.1	81.87
2.2	81.93
3.9	81.63
5.1	81.39
6.3	81.12
7.7	80.89
9.5	80.81
11.3	81.10
12.6	80.86
13.3	80.64
14.6	80.58
16.3	80.71
18.0	80.63
19.8	80.70
21.0	80.62
21.6	80.42
22.4	80.28
23.0	80.38
23.6	80.02
24.5	79.65
25.6	79.18
25.9	78.93
26.5	78.70
27.1	78.56
27.8	78.64
28.2	78.78
28.9	78.82
29.6	79.04
45.5	80.37
48.0	80.40
50.5	80.41
52.1	80.46
53.5	80.76
54.5	80.89

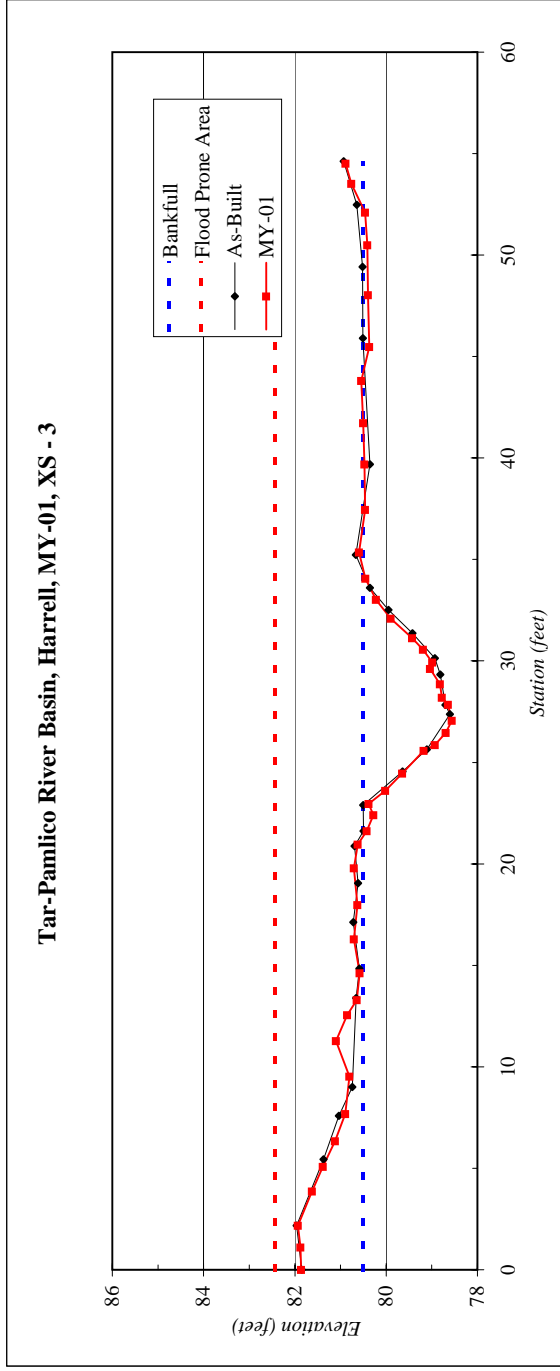


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 4
Drainage Area (sq mi):	0.23
Date:	9/4/2008
Field Crew:	B. Roberts, A. Davis



Station	Elevation
0.0	79.54
1.0	79.44
3.3	79.46
5.2	79.58
6.8	79.35
9.6	79.44
11.0	79.61
12.6	79.66
14.5	79.47
16.8	79.53
19.3	79.51
21.6	79.67
23.3	79.54
24.4	79.34
26.2	79.47
27.3	79.58
28.7	79.52
29.5	79.40
29.9	79.14
30.6	78.79
42.4	79.48
44.5	79.52
46.2	79.49
47.5	79.88
49.3	79.57
51.0	79.63
56.2	79.99
57.4	80.15
59.0	79.75
60.1	79.79
61.9	79.73
62.5	79.57
64.6	79.79
65.9	79.74
66.7	79.91

SUMMARY DATA	
Bankfull Elevation:	79.7
Bankfull Cross-Sectional Area:	10.8
Bankfull Width:	11.5
Flood Prone Area Elevation:	81.4
Flood Prone Width:	>67
Max Depth at Bankfull:	1.7
Mean Depth at Bankfull:	0.9
W / D Ratio:	12.2
Entrenchment Ratio:	>5
Bank Height Ratio:	1.0

Stream Type C5

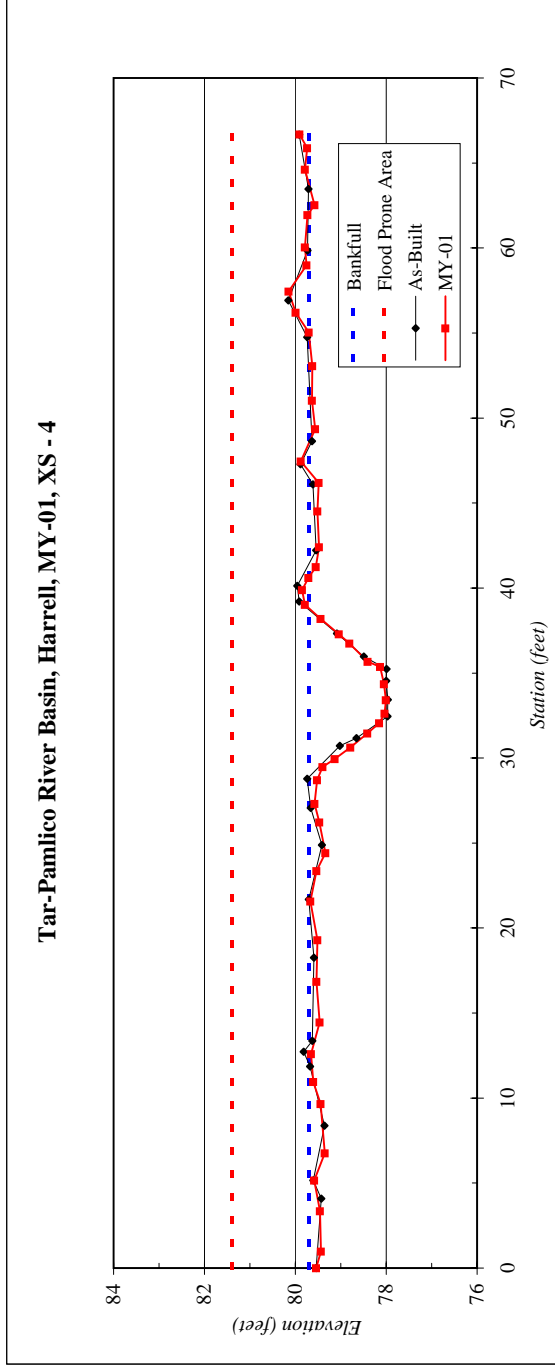


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 5
Drainage Area (sq mi):	0.23
Date:	9/4/2008
Field Crew:	B. Roberts, A. Davis



Station	Elevation
0.0	77.41
1.5	77.24
3.9	76.71
6.2	77.22
7.8	77.06
9.6	76.40
11.8	75.72
13.9	75.33
16.5	74.90
19.3	74.35
23.0	74.39
25.5	74.88
28.3	74.77
30.7	74.82
32.5	74.45
33.5	73.77
34.5	73.51
34.8	73.18
35.9	72.89
36.8	72.79
37.3	72.96
38.3	73.70
39.6	74.21
40.7	74.79
42.4	74.84
43.9	74.73
46.3	74.44
49.6	74.17
51.8	74.09
54.3	73.97
57.1	74.00
60.3	74.22
62.8	75.11
70.2	77.67
72.7	78.08
75.8	77.61
79.8	77.97
83.3	78.07
84.5	78.18

SUMMARY DATA	
Bankfull Elevation:	74.8
Bankfull Cross-Sectional Area:	10.2
Bankfull Width:	9.9
Flood Prone Area Elevation:	76.8
Flood Prone Width:	56
Max Depth at Bankfull:	2.0
Mean Depth at Bankfull:	1.0
W / D Ratio:	9.6
Entrenchment Ratio:	5.7
Bank Height Ratio:	1.0

Stream Type C5

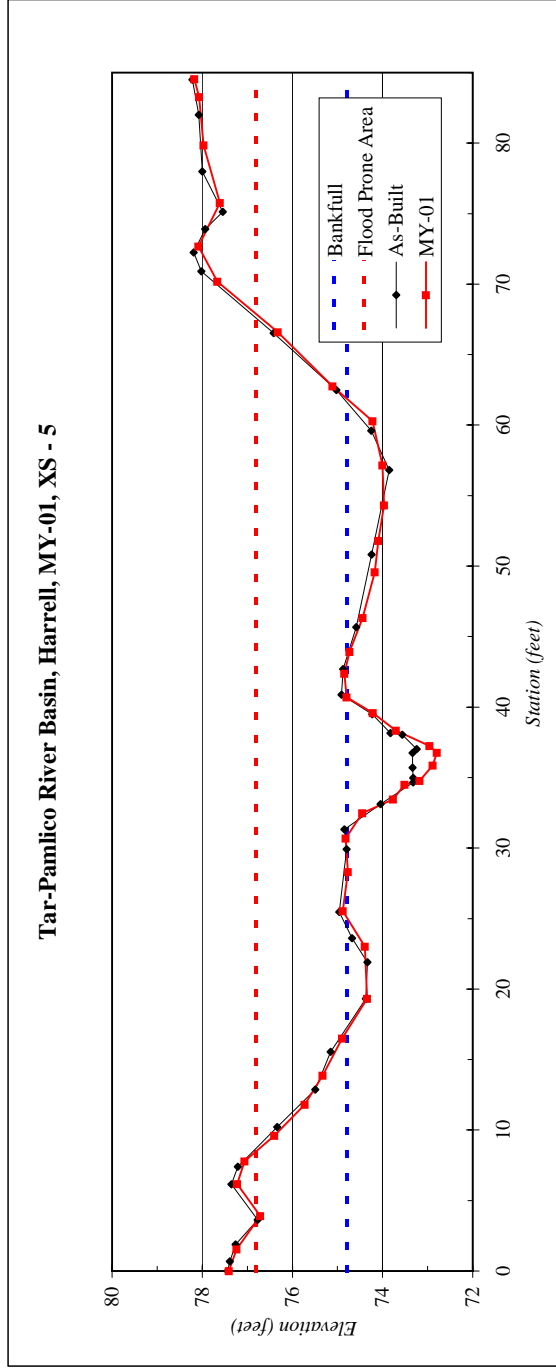


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 6
Drainage Area (sq mi):	0.42
Date:	9/5/2008
Field Crew:	B. Roberts, A. Davis



Station	Elevation
0.0	73.24
1.6	73.11
4.3	73.44
7.8	73.35
13.8	73.43
18.2	73.32
22.2	73.60
25.7	73.35
29.0	73.38
30.1	73.14
31.7	72.50
32.7	72.04
34.0	71.52
34.8	71.23
35.6	70.85
36.7	70.69
38.0	70.64
38.9	71.30
40.2	71.56
41.3	72.50
42.1	73.04
43.6	73.26
45.0	73.51
47.8	73.27
50.3	73.67
52.0	74.42
54.8	75.43
57.3	76.42
59.2	76.82
60.1	76.91

SUMMARY DATA	
Bankfull Elevation:	73.4
Bankfull Cross-Sectional Area:	20.8
Bankfull Width:	15.0
Flood Prone Area Elevation:	76.1
Flood Prone Width:	>60
Max Depth at Bankfull:	2.7
Mean Depth at Bankfull:	1.4
W / D Ratio:	10.8
Entrenchment Ratio:	>4
Bank Height Ratio:	1.0

Stream Type: C5

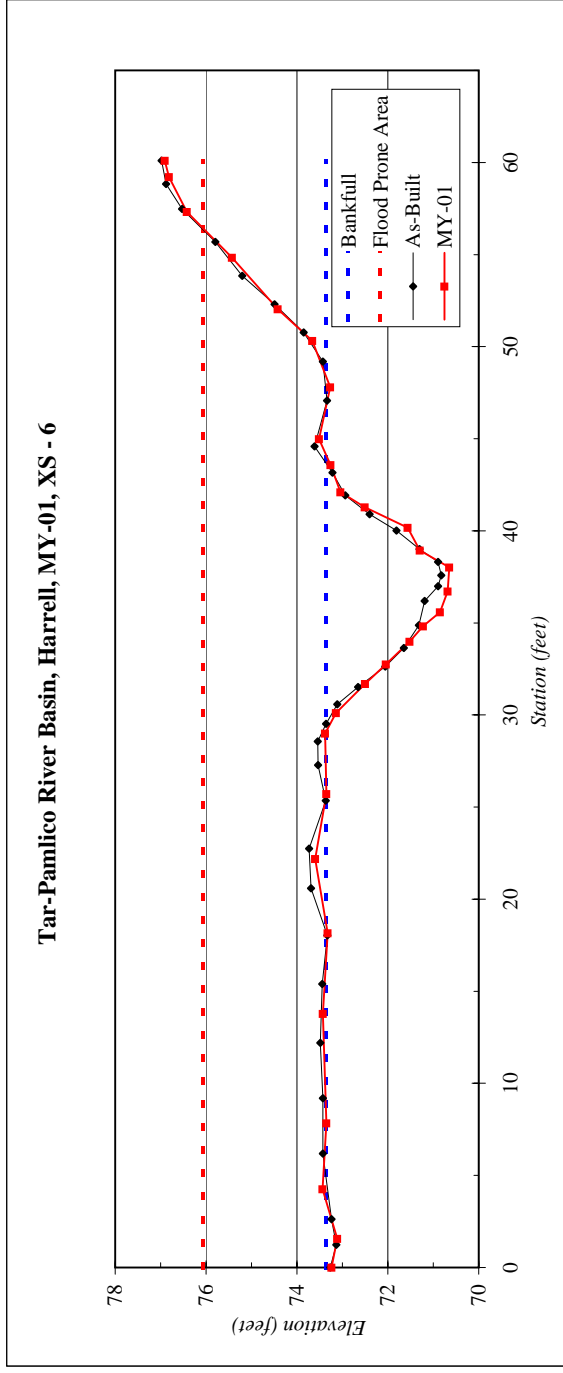

River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 7
Drainage Area (sq mi):	0.42
Date:	9/5/2008
Field Crew:	B. Roberts, A. Davis




Stream Type C5

Station	Elevation
0.0	72.11
0.9	72.03
5.4	71.99
8.7	72.14
12.4	72.14
14.3	72.29
16.9	72.04
19.4	71.98
22.4	72.14
24.6	72.15
26.4	72.06
27.6	71.79
28.5	71.40
29.5	70.89
30.3	70.36
31.0	70.22
31.8	69.90
32.3	69.69
32.8	69.42
33.7	69.29
34.6	69.44
35.0	69.76
35.4	70.16
36.8	70.81
37.9	71.44
39.3	71.96
40.3	72.33
42.7	72.39
46.4	72.15
50.2	72.20
54.4	72.13
59.1	72.00
60.7	72.17

SUMMARY DATA	
Bankfull Elevation:	71.9
Bankfull Cross-Sectional Area:	16.2
Bankfull Width:	12.0
Flood Prone Area Elevation:	74.5
Flood Prone Width:	>61
Max Depth at Bankfull:	2.6
Mean Depth at Bankfull:	1.4
W / D Ratio:	8.9
Entrenchment Ratio:	>5
Bank Height Ratio:	1.0

Tar-Pamlico River Basin, Harrell, MY-01, XS - 7

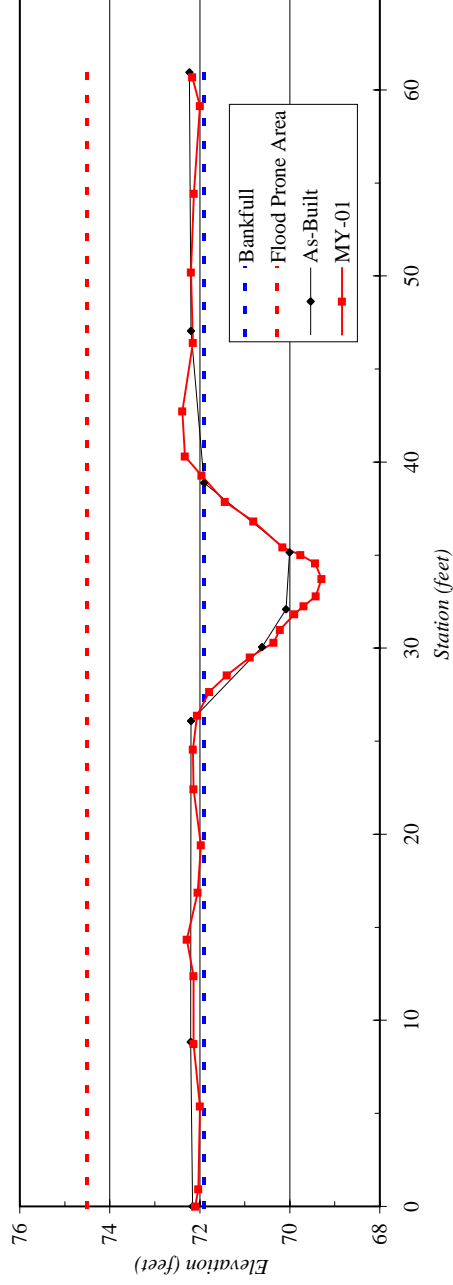


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 8
Drainage Area (sq mi):	0.42
Date:	9/5/2008
Field Crew:	B. Roberts, A. Davis



Stream Type C5

Station	Elevation
0.0	71.61
0.7	71.34
3.1	70.74
5.0	70.17
6.7	69.58
9.3	69.16
11.4	69.51
12.5	69.94
13.4	69.73
14.1	69.12
15.0	68.53
16.0	67.95
16.5	67.57
17.5	67.30
19.3	67.38
20.5	67.63
21.9	67.71
23.4	68.05
24.5	68.61
25.8	69.15
27.5	69.21
32.2	69.17
35.2	69.17
37.8	69.40
41.7	69.24
44.8	69.14
46.4	69.28
47.6	69.53
49.3	69.22
51.8	69.05
52.2	69.16

SUMMARY DATA	
Bankfull Elevation:	69.3
Bankfull Cross-Sectional Area:	15.8
Bankfull Width:	11.9
Flood Prone Area Elevation:	71.3
Flood Prone Width:	>50
Max Depth at Bankfull:	2.0
Mean Depth at Bankfull:	1.3
W / D Ratio:	9.0
Entrenchment Ratio:	>4
Bank Height Ratio:	1.0

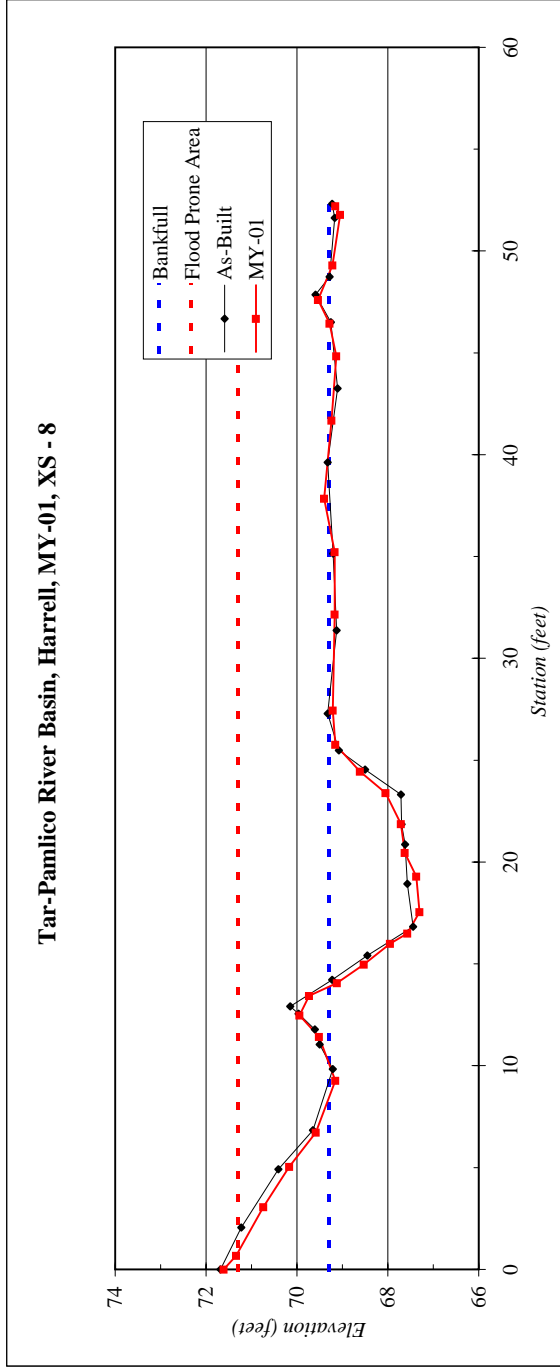


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 9
Drainage Area (sq mi):	0.42
Date:	9/5/2008
Field Crew:	B. Roberts, A. Davis



Station	Elevation
0.0	68.43
1.3	68.17
3.0	67.89
5.6	67.77
8.1	68.12
10.1	68.56
12.3	68.86
14.0	68.54
16.4	69.03
17.6	68.80
20.4	68.87
24.5	68.84
26.8	68.71
27.7	68.48
28.8	67.80
29.8	67.23
30.8	66.84
31.7	66.73
33.2	66.79
34.1	66.83
35.0	67.00
36.5	67.49
37.4	67.91
38.5	68.49
39.2	68.71
42.9	68.56
46.4	68.58
50.4	68.40
54.2	68.37
56.8	68.44
57.9	68.51

SUMMARY DATA	
Bankfull Elevation:	68.7
Bankfull Cross-Sectional Area:	15.2
Bankfull Width:	12.4
Flood Prone Area Elevation:	70.7
Flood Prone Width:	>58
Max Depth at Bankfull:	2.0
Mean Depth at Bankfull:	1.2
W / D Ratio:	10.1
Entrenchment Ratio:	>4.5
Bank Height Ratio:	1.0

Stream Type: C5

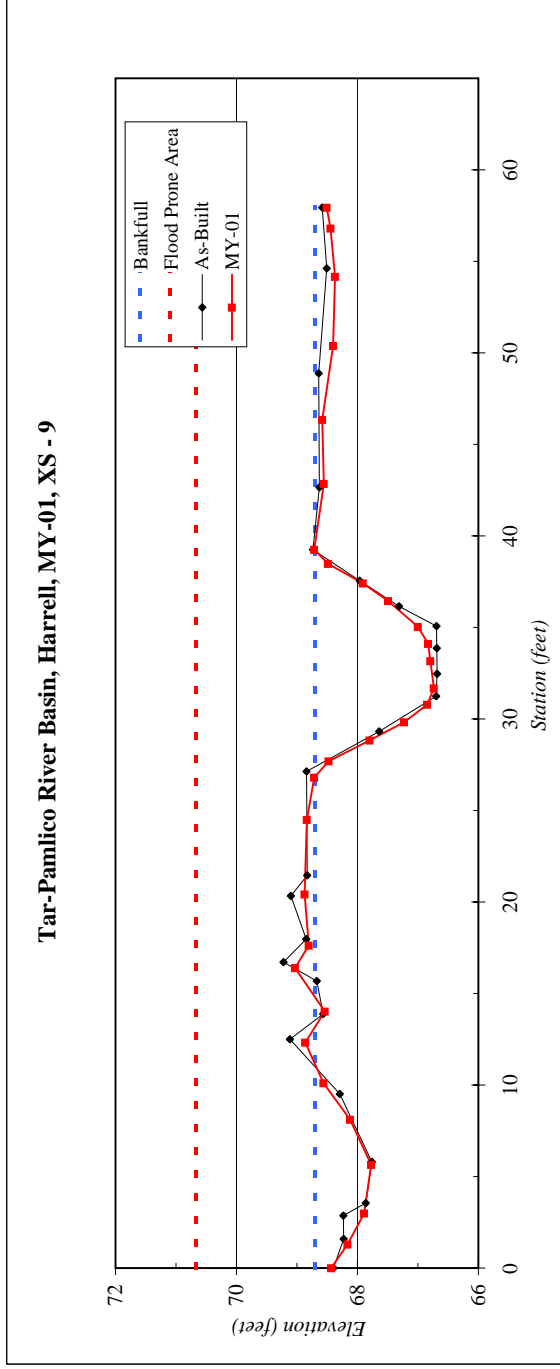


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 10
Drainage Area (sq mi):	0.61
Date:	9/23/2008
Field Crew:	B. Roberts, Z. Wendling



Station	Elevation
0.0	68.23
0.2	68.08
4.1	67.48
7.4	67.12
9.4	66.88
13.4	67.18
16.2	67.47
19.2	67.70
24.0	67.40
27.0	67.26
27.7	67.09
28.4	66.94
29.4	66.57
31.2	65.66
31.9	65.24
32.2	65.13
32.5	65.06
32.9	65.00
33.8	64.97
34.0	65.07
34.4	65.11
35.9	65.25
36.8	65.39
38.5	65.53
41.5	66.76
42.2	66.88
49.6	66.91
53.6	66.69
56.8	67.35
58.0	67.02
61.4	66.96
62.9	67.26
67.2	67.43

SUMMARY DATA	
Bankfull Elevation:	67.0
Bankfull Cross-Sectional Area:	16.9
Bankfull Width:	13.9
Flood Prone Area Elevation:	69.0
Flood Prone Width:	>67
Max Depth at Bankfull:	2.0
Mean Depth at Bankfull:	1.2
W / D Ratio:	11.4
Entrenchment Ratio:	>5
Bank Height Ratio:	1.0

Stream Type C5

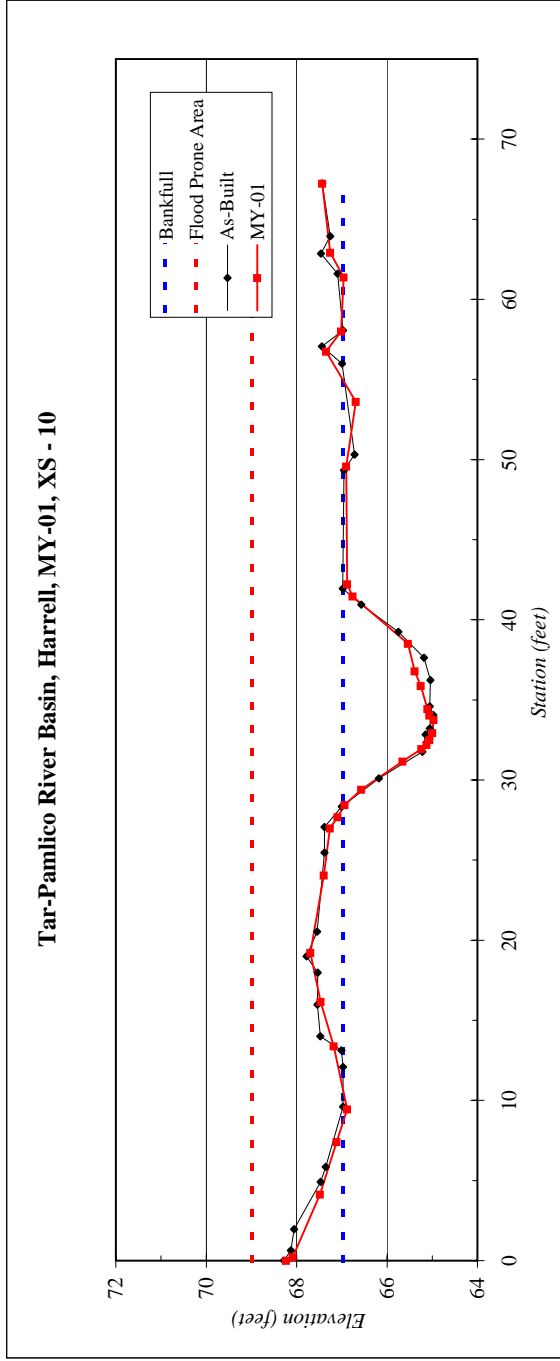


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 11
Drainage Area (sq mi):	0.61
Date:	9/23/2008
Field Crew:	B. Roberts, Z. Wendling



Station	Elevation
0.0	66.24
0.5	66.25
1.2	66.42
1.9	66.30
3.3	65.97
4.8	65.79
6.0	65.63
9.6	66.11
12.5	66.11
14.8	66.00
18.9	65.97
19.7	65.85
20.3	65.87
21.1	65.94
22.3	65.93
24.0	65.09
24.8	64.72
25.5	64.28
25.9	64.14
26.8	63.79
27.3	63.84
28.0	63.59
29.3	63.56
30.5	63.68
31.5	63.81
31.9	64.10
32.2	64.30
34.0	65.42
34.8	65.83
35.2	65.88
42.8	66.26
44.9	66.08
54.3	66.35
56.5	66.25
56.6	66.40

SUMMARY DATA	
Bankfull Elevation:	65.9
Bankfull Cross-Sectional Area:	18.7
Bankfull Width:	13.3
Flood Prone Area Elevation:	68.2
Flood Prone Width:	>57
Max Depth at Bankfull:	2.3
Mean Depth at Bankfull:	1.4
W / D Ratio:	9.5
Entrenchment Ratio:	>4.5
Bank Height Ratio:	1.0

Stream Type C5

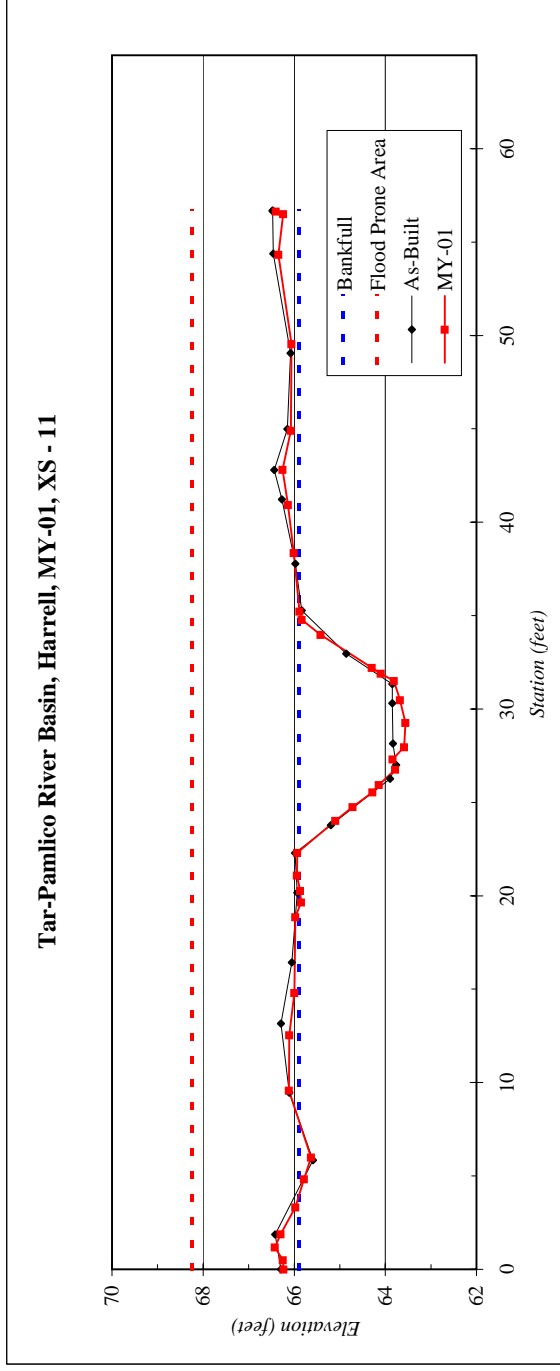


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 12
Drainage Area (sq mi):	0.61
Date:	9/23/2008
Field Crew:	B. Roberts, Z. Wendling



Stream Type: C5

Station	Elevation
0.0	65.45
0.6	65.23
4.1	65.18
5.3	64.77
7.4	64.94
13.0	65.05
14.7	65.06
19.1	65.15
20.2	65.02
22.2	63.82
23.1	63.30
23.4	63.12
23.6	63.04
24.3	62.78
24.7	62.64
26.1	62.83
27.0	62.98
27.9	63.01
28.3	63.00
28.7	63.06
29.0	63.02
29.4	62.92
30.9	62.92
31.8	63.05
33.0	63.45
36.6	64.98
38.0	65.11
39.8	65.09
45.2	64.66
50.3	64.50
55.4	64.57
57.3	64.83
60.4	64.67
60.5	64.80

SUMMARY DATA	
Bankfull Elevation:	65.1
Bankfull Cross-Sectional Area:	27.2
Bankfull Width:	18.3
Flood Prone Area Elevation:	67.6
Flood Prone Width:	>61
Max Depth at Bankfull:	2.5
Mean Depth at Bankfull:	1.5
W / D Ratio:	12.3
Entrenchment Ratio:	>3.5
Bank Height Ratio:	1.0

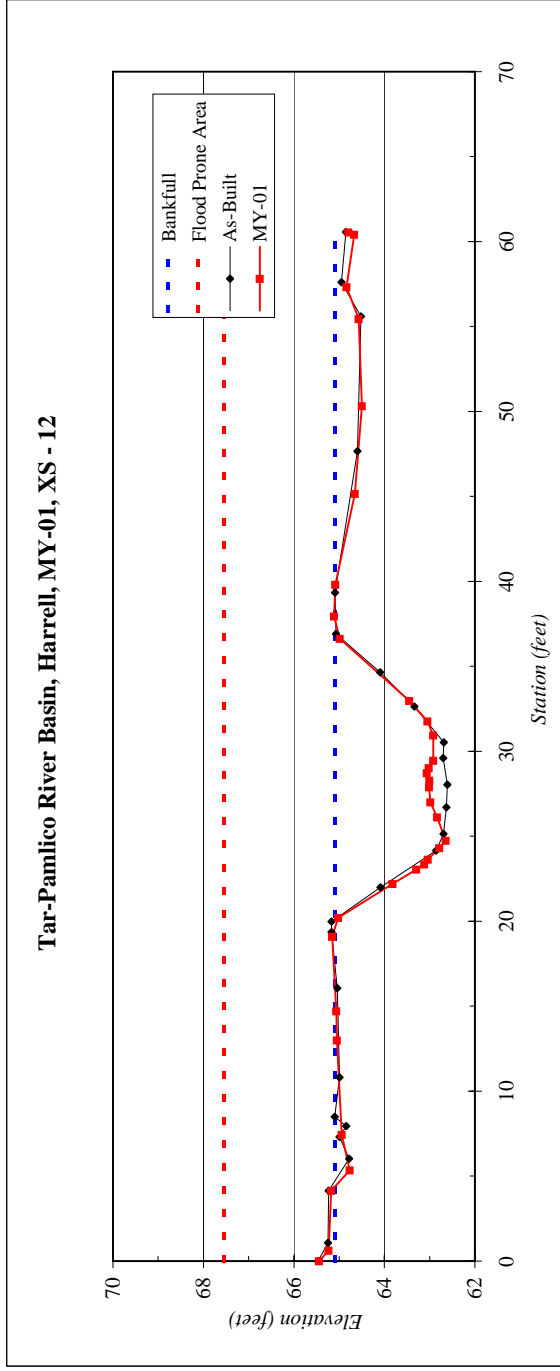

River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 13
Drainage Area (sq mi):	0.61
Date:	9/23/2008
Field Crew:	B. Roberts, Z. Wendling




Station	Elevation
0.0	63.54
0.7	63.48
9.6	63.77
15.2	63.75
24.6	63.74
24.9	63.72
25.8	63.27
26.3	63.08
29.2	61.81
29.7	61.73
30.6	61.70
31.3	61.63
31.6	61.54
32.5	61.45
33.2	61.53
34.0	61.68
34.5	61.82
35.1	62.08
37.0	63.08
38.2	63.79
38.9	63.94
41.0	63.94
44.9	63.73
49.8	63.74
51.7	63.77
56.1	63.71
56.8	63.85
59.9	64.05
60.0	64.17

SUMMARY DATA	
Bankfull Elevation:	63.8
Bankfull Cross-Sectional Area:	20.0
Bankfull Width:	13.4
Flood Prone Area Elevation:	66.1
Flood Prone Width:	>60
Max Depth at Bankfull:	2.3
Mean Depth at Bankfull:	1.5
W / D Ratio:	9.0
Entrenchment Ratio:	>4.5
Bank Height Ratio:	1.0

Stream Type C5

Tar-Pamlico River Basin, Harrell, MY-01, XS - 13

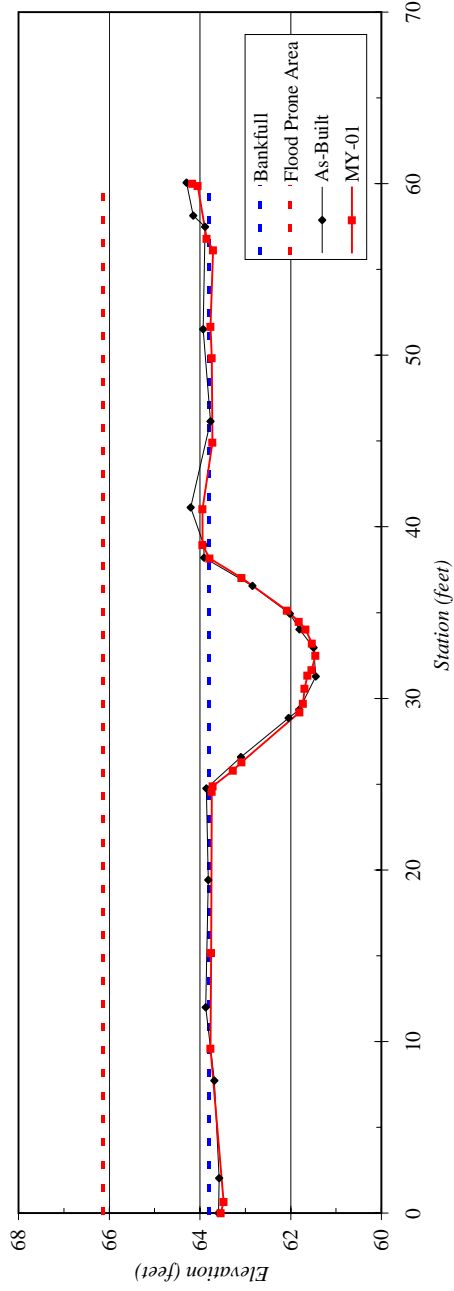


River Basin:	Tar-Pamlico
Watershed:	Harrell, MY-01
XS ID	XS - 14
Drainage Area (sq mi):	0.61
Date:	9/23/2008
Field Crew:	B. Roberts, Z. Wendling



Stream Type C5


Station	Elevation
0.0	62.75
2.3	62.68
4.9	62.93
8.4	62.75
13.0	62.72
17.1	62.69
21.0	62.88
23.0	62.86
24.4	62.21
26.9	61.01
27.5	60.79
29.2	60.72
30.6	60.65
32.6	60.93
34.0	61.39
35.4	62.18
36.8	62.83
38.7	62.94
46.6	62.59
47.9	62.82
48.8	62.51
57.8	62.43
58.7	62.74
62.0	62.82

SUMMARY DATA	
Bankfull Elevation:	62.8
Bankfull Cross-Sectional Area:	20.5
Bankfull Width:	14.0
Flood Prone Area Elevation:	64.9
Flood Prone Width:	>62
Max Depth at Bankfull:	2.1
Mean Depth at Bankfull:	1.5
W / D Ratio:	9.6
Entrenchment Ratio:	>4.5
Bank Height Ratio:	1.0

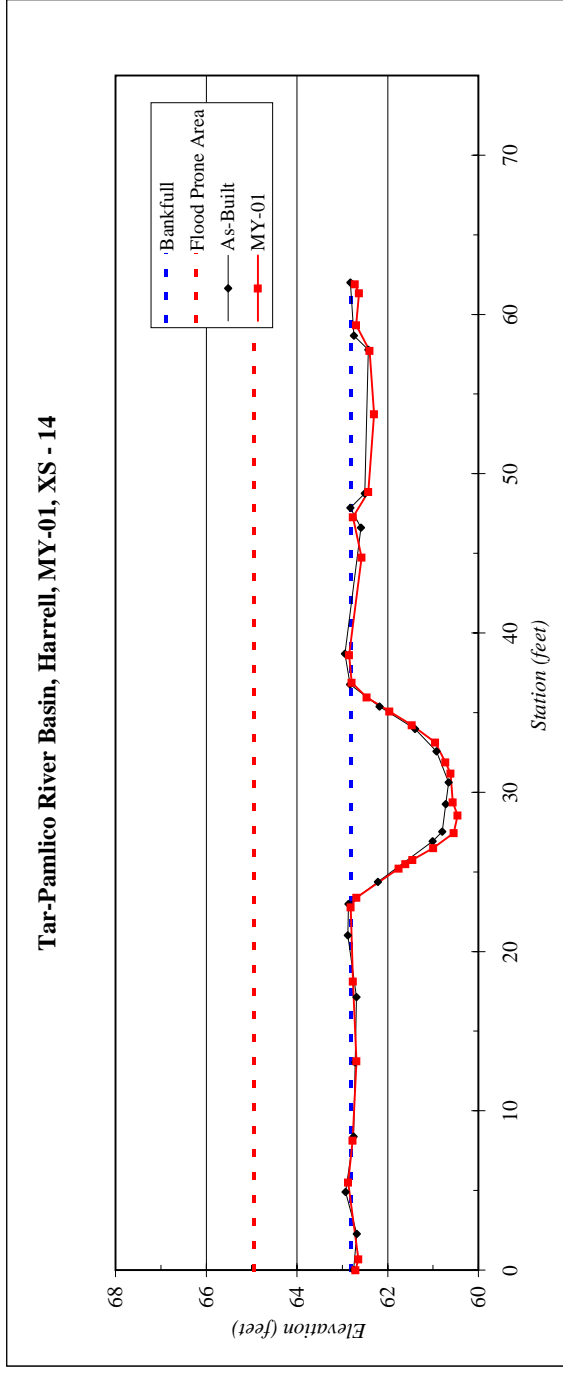


C2 - Stream Longitudinal Profiles

Longitudinal Profile Harrell Stream Restoration Reach 1 - Station 16+00 - 22+35




*Due to no flowing water in the channel, water surface and water surface slope were not recorded.

**Longitudinal Profile
Harrell Stream Restoration
Reach 2 - Station 25+00 - 29+90**




*Due to no flowing water in the channel, water surface and water surface slope were not recorded.

**Longitudinal Profile
Harrell Stream Restoration
Reach 3 - Station 38+60 - 48+50**

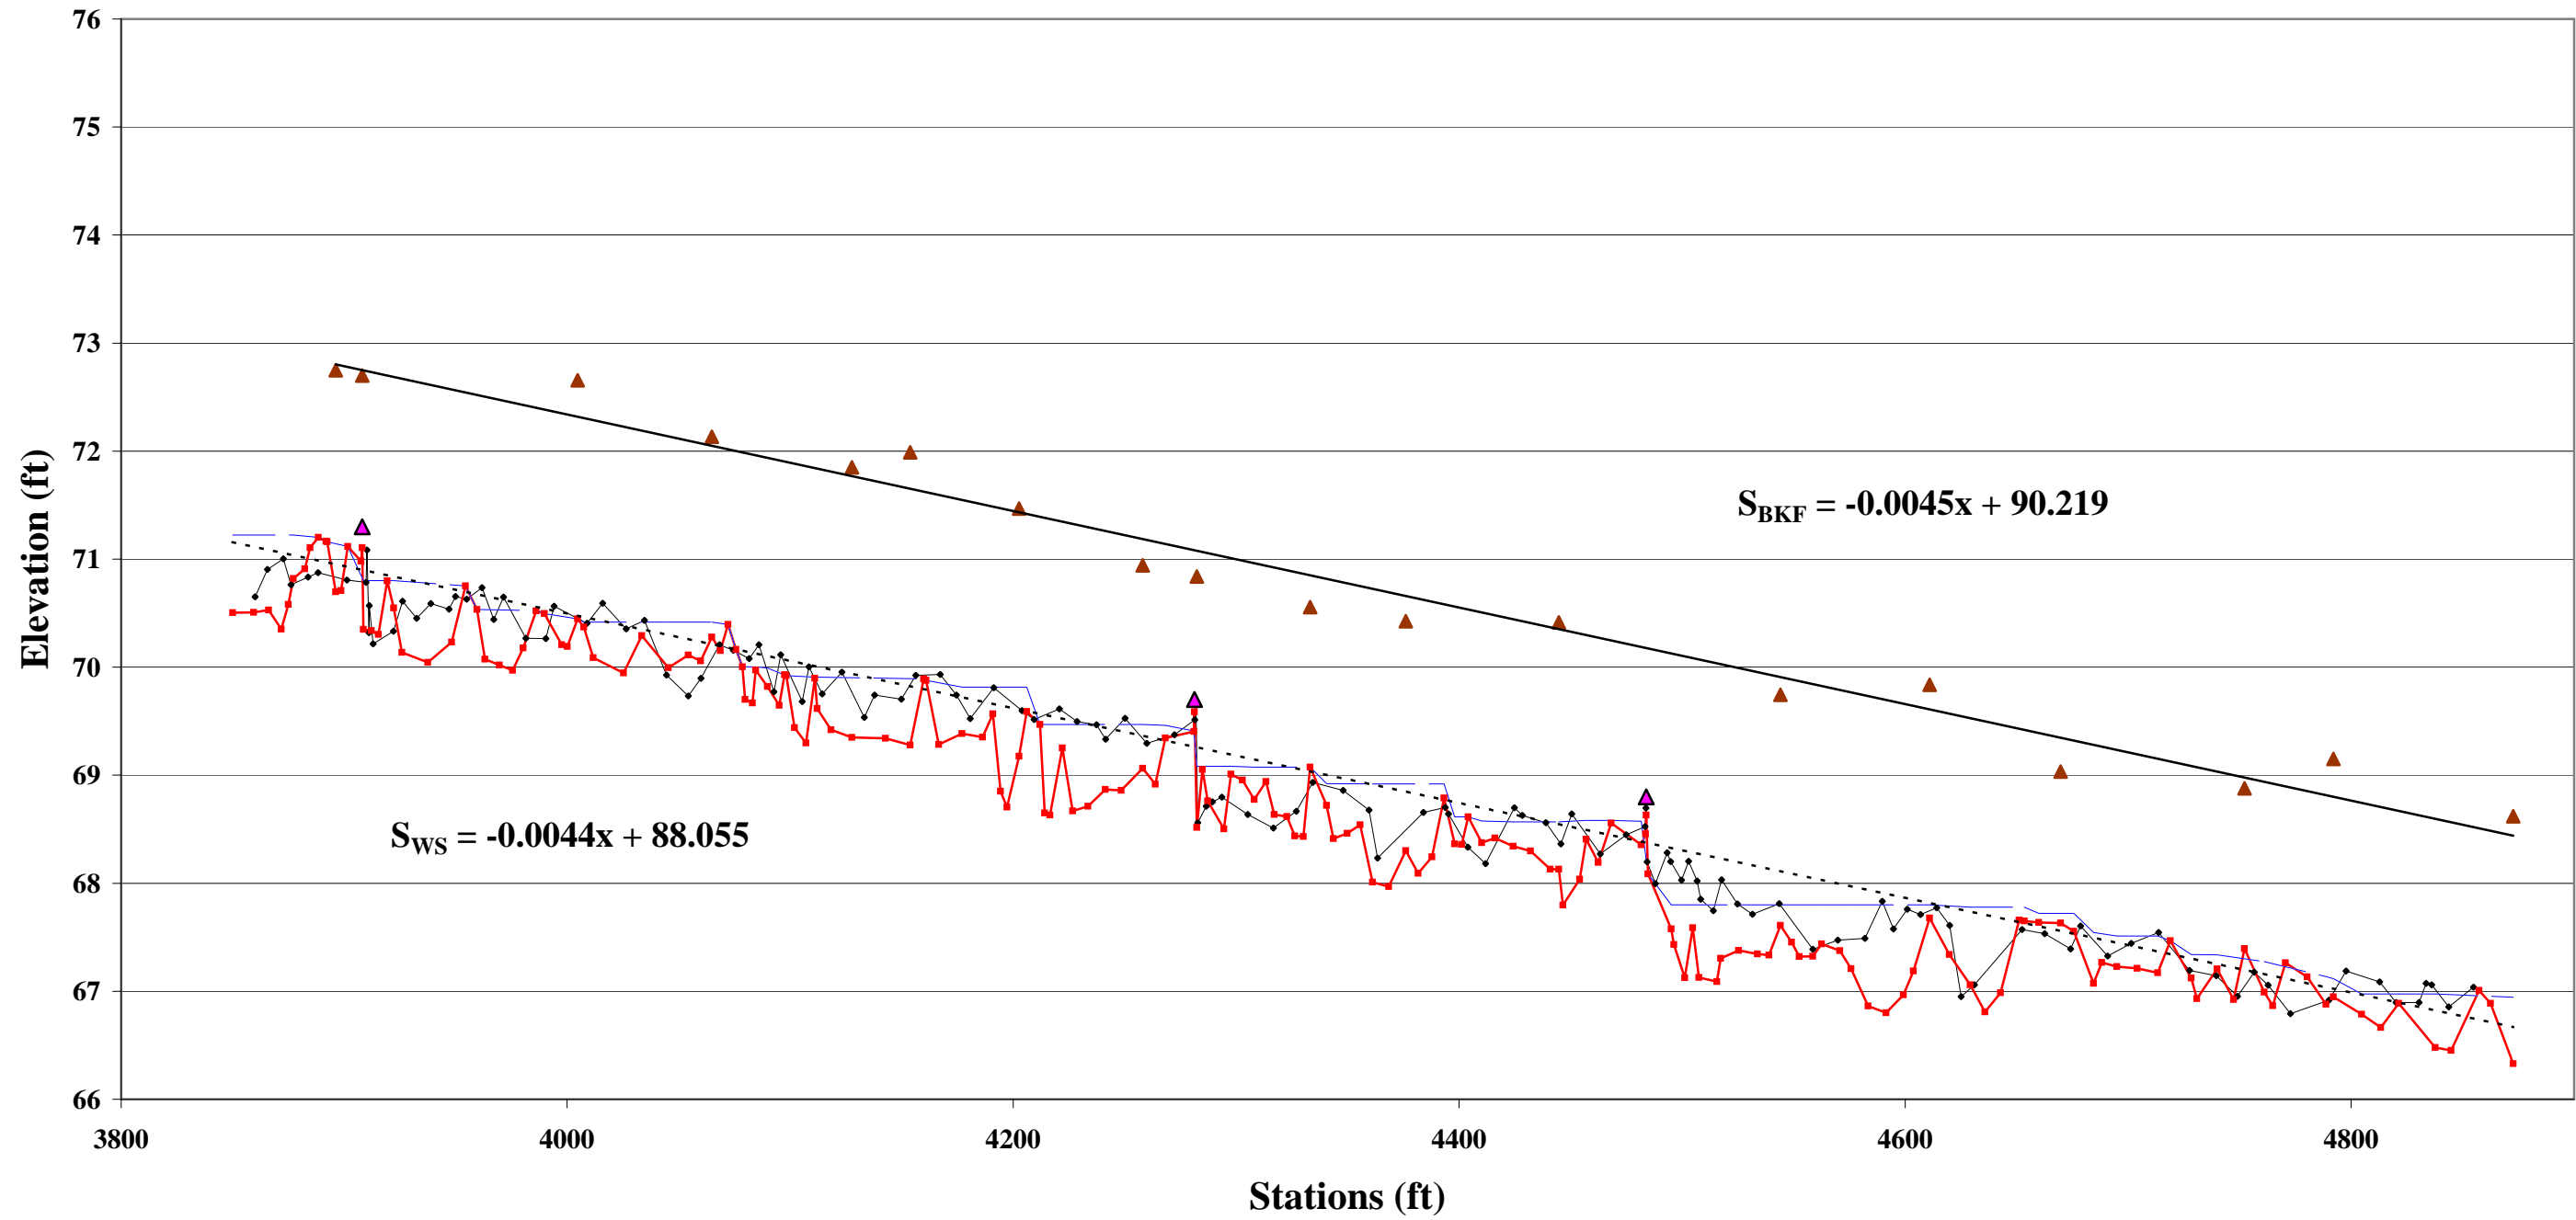


Longitudinal Profile
Harrell Stream Restoration MY-01
Reach 4 - Station 62+50 - 71+80

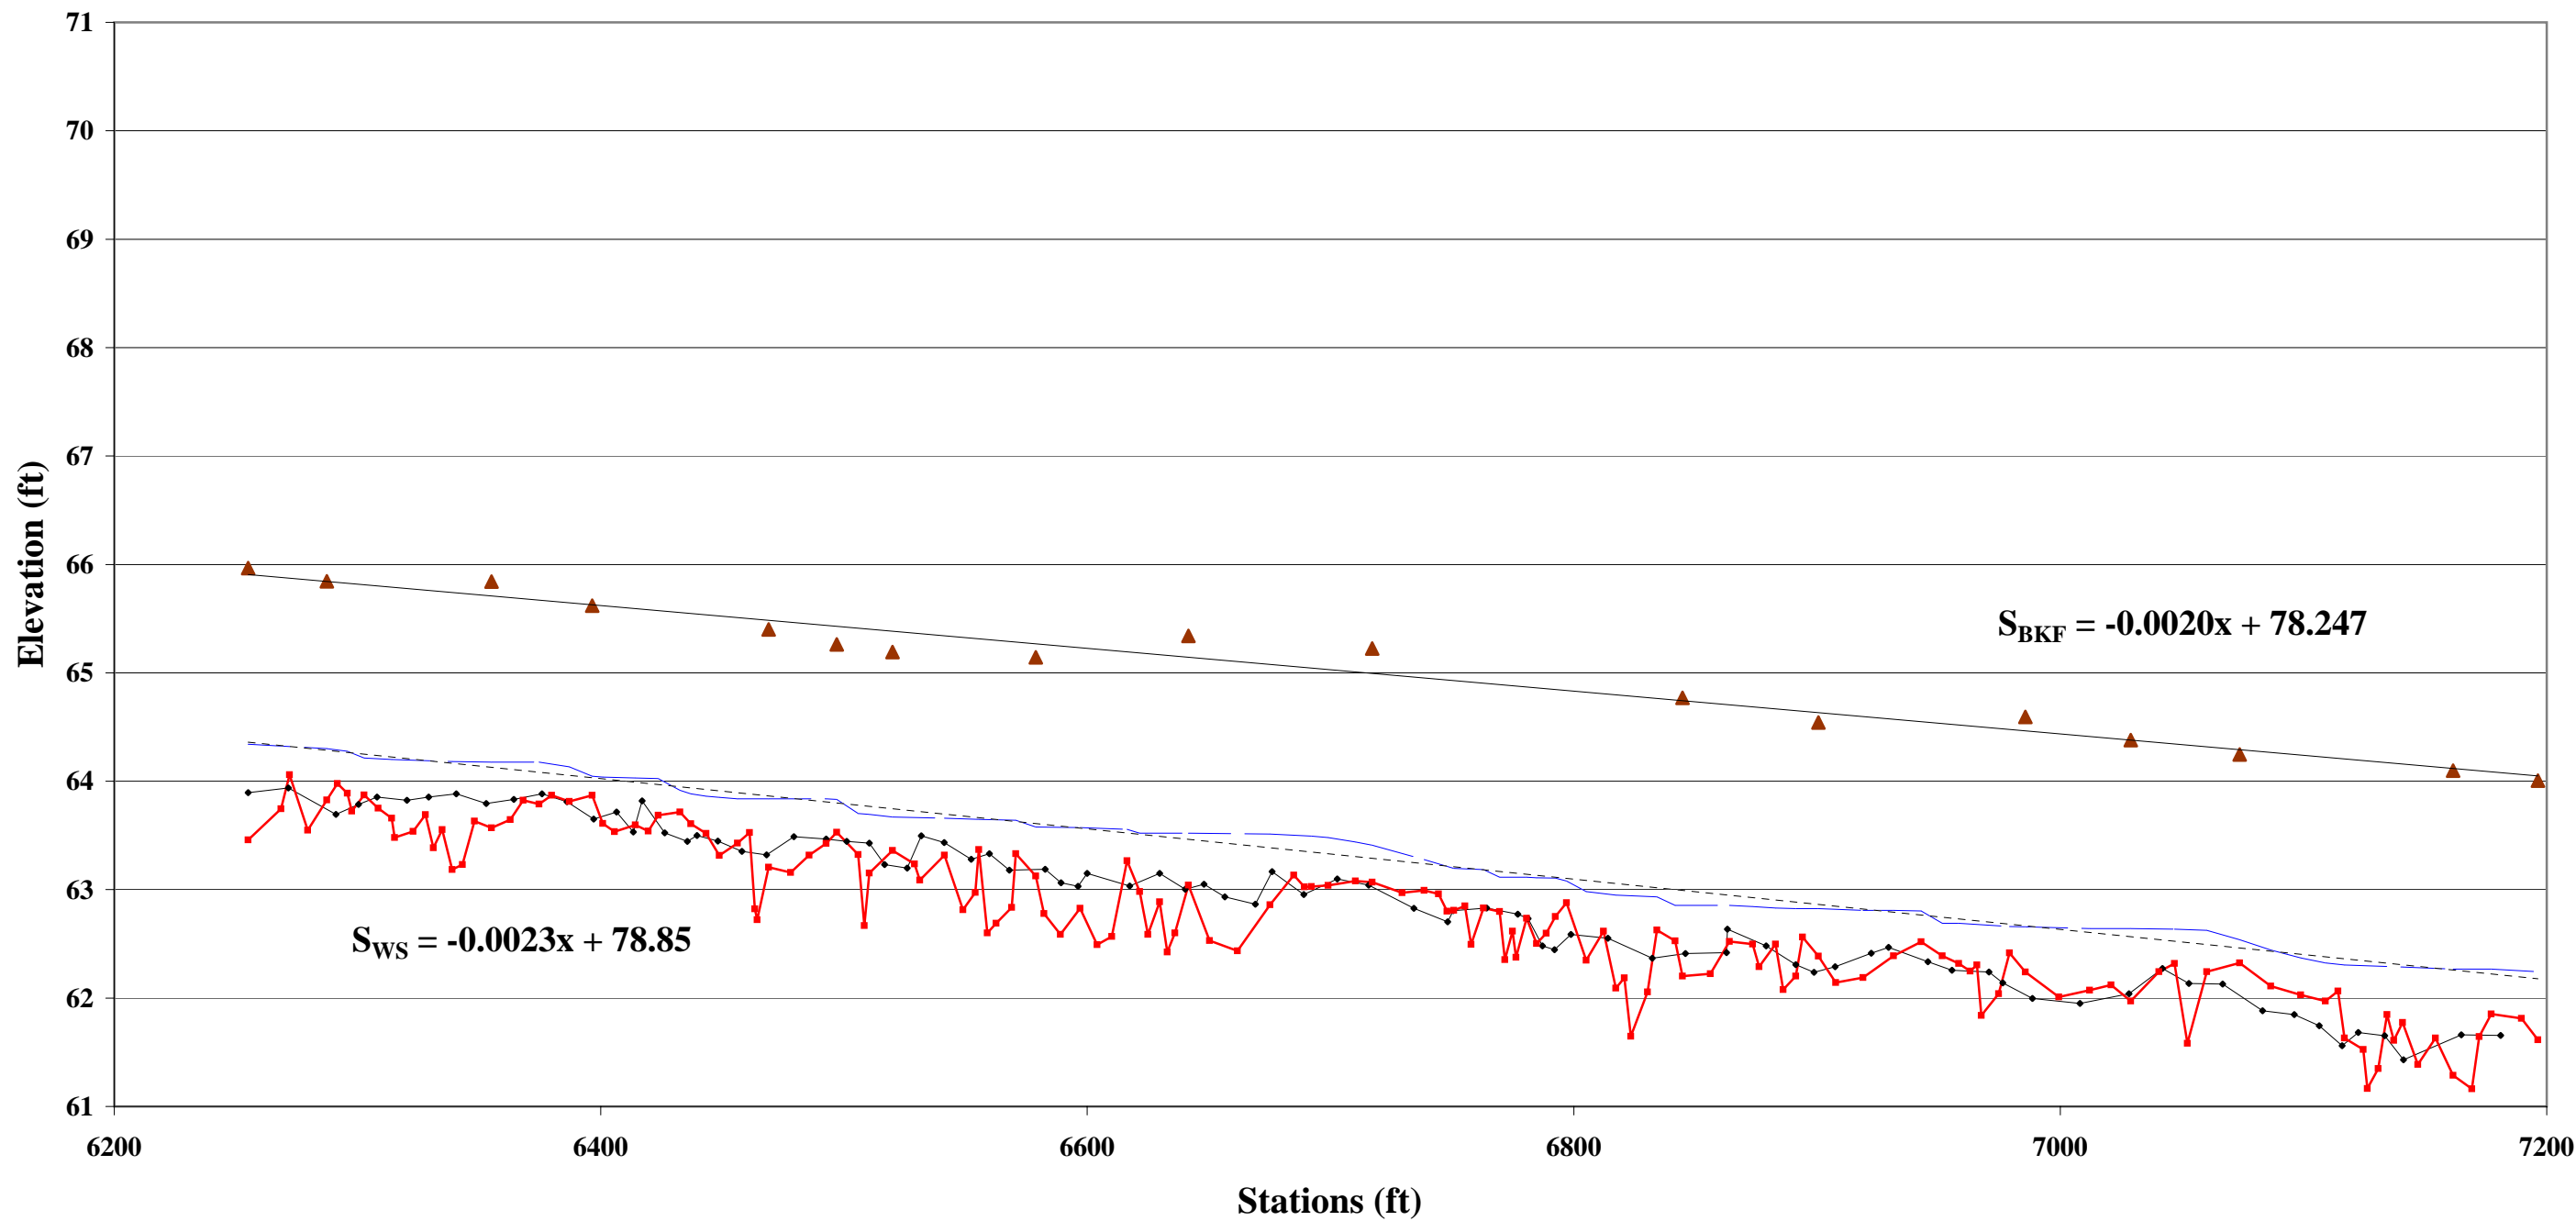

C3 - Stream Pebble Counts

Cross Section 1 - MY01			
Particle	Millimeter	S/C	Count
Silt/Clay	< 0.062	S/C	2
Very Fine	.062 - .125	S	2
Fine	.125 - .25	A	7
Medium	.25 - .50	N	9
Coarse	.50 - 1	D	18
Very Coarse	1 - 2	S	29
Very Fine	2 - 4		12
Fine	4 - 5.7	G	6
Fine	5.7 - 8	R	6
Medium	8 - 11.3	A	8
Medium	11.3 - 16	V	12
Coarse	16 - 22.6	E	9
Coarse	22.6 - 32	L	5
Very Coarse	32 - 45	S	1
Very Coarse	45 - 64		
Small	64 - 90	C	
Small	90 - 128	O	
Large	128 - 180	B	
Large	180 - 256	L	
Small	256 - 362	B	
Small	362 - 512	L	
Medium	512 - 1024	D	
Lrg- Very Lrg	1024 - 2048	R	
Bedrock	>2048	BDRK	
Total			126

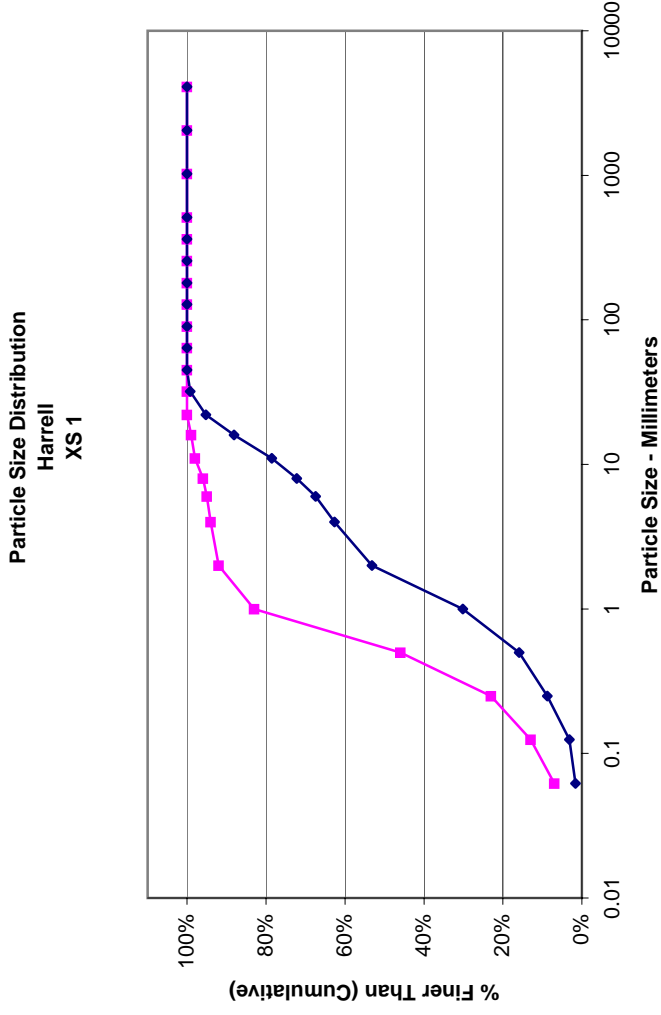



Size (mm)	Count
D16	0.5
D35	1.2
D50	1.8
D65	4.9
D84	14
D95	22


Size Distribution	
mean	2.6
dispersion	5.7
skewness	0.14

Type	Percentage
silt/clay	2%
sand	52%
gravel	47%
cobble	0%
boulder	0%
bedrock	0%
hardpan	0%
wood/det	0%
artificial	0%

Note:

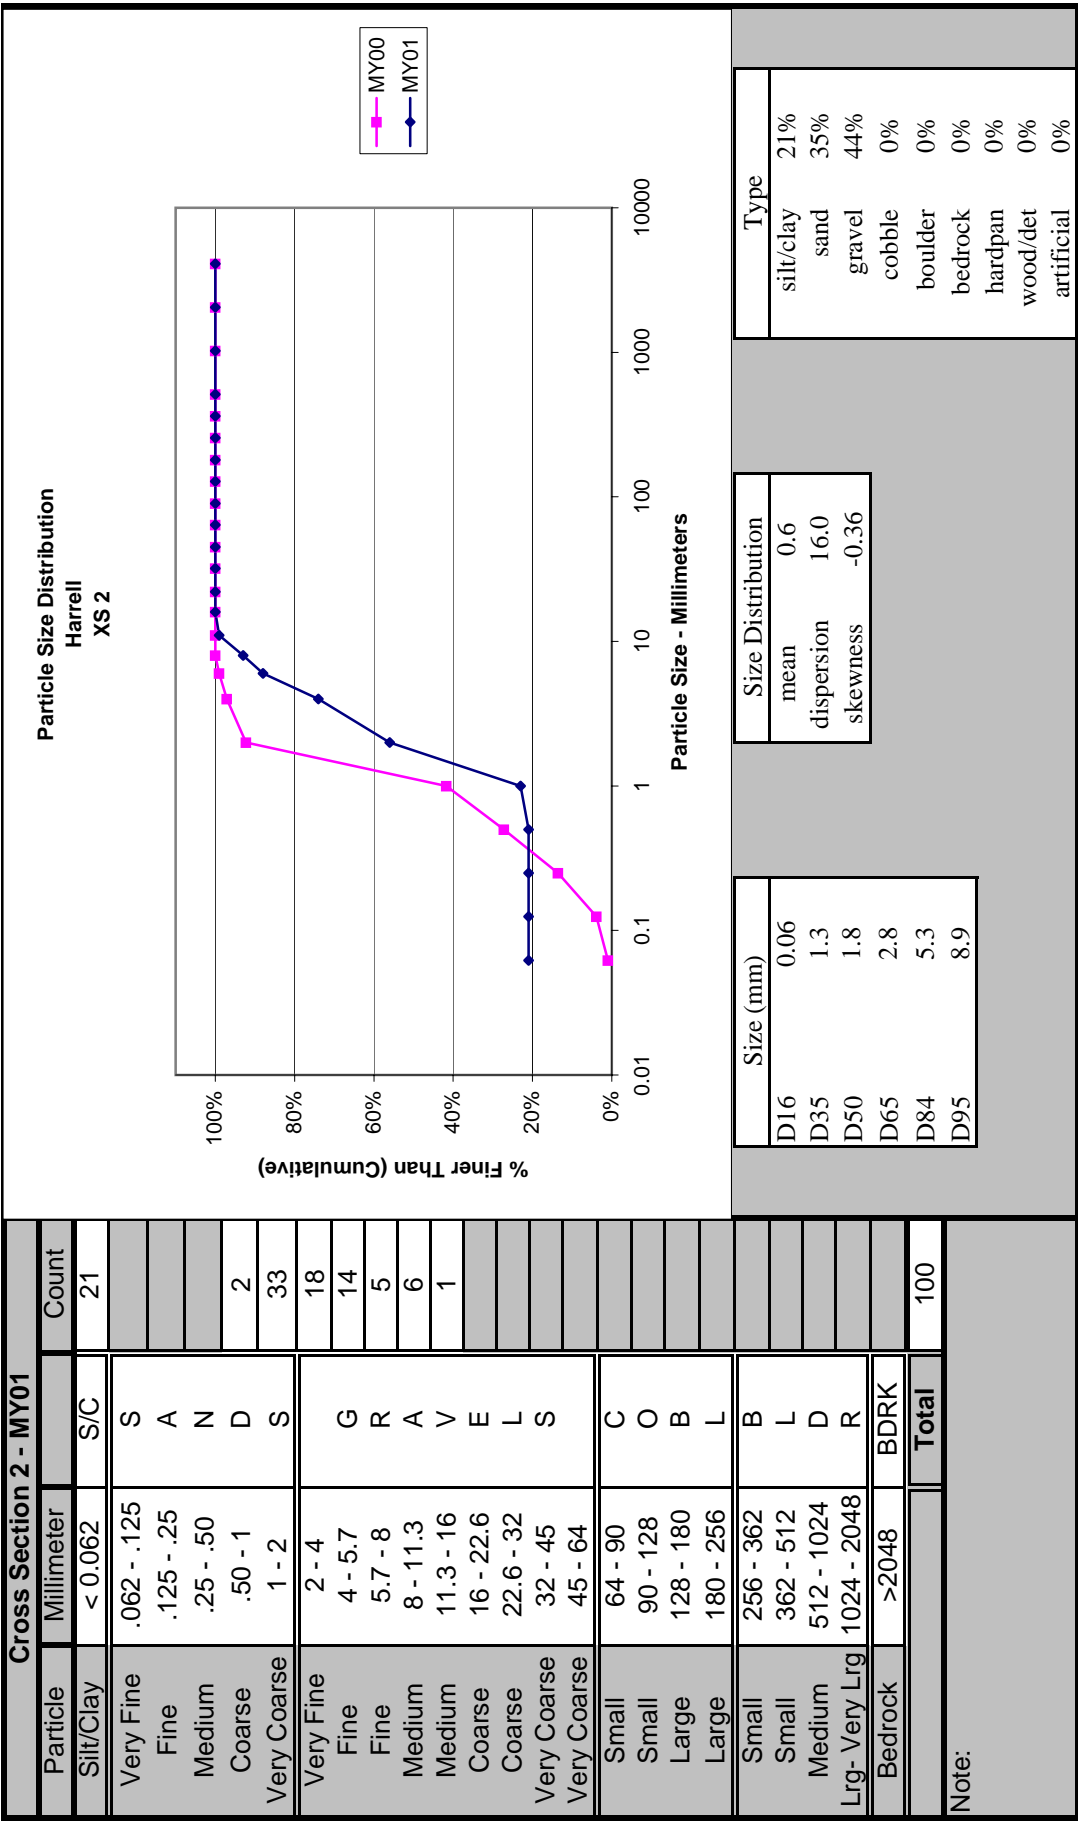

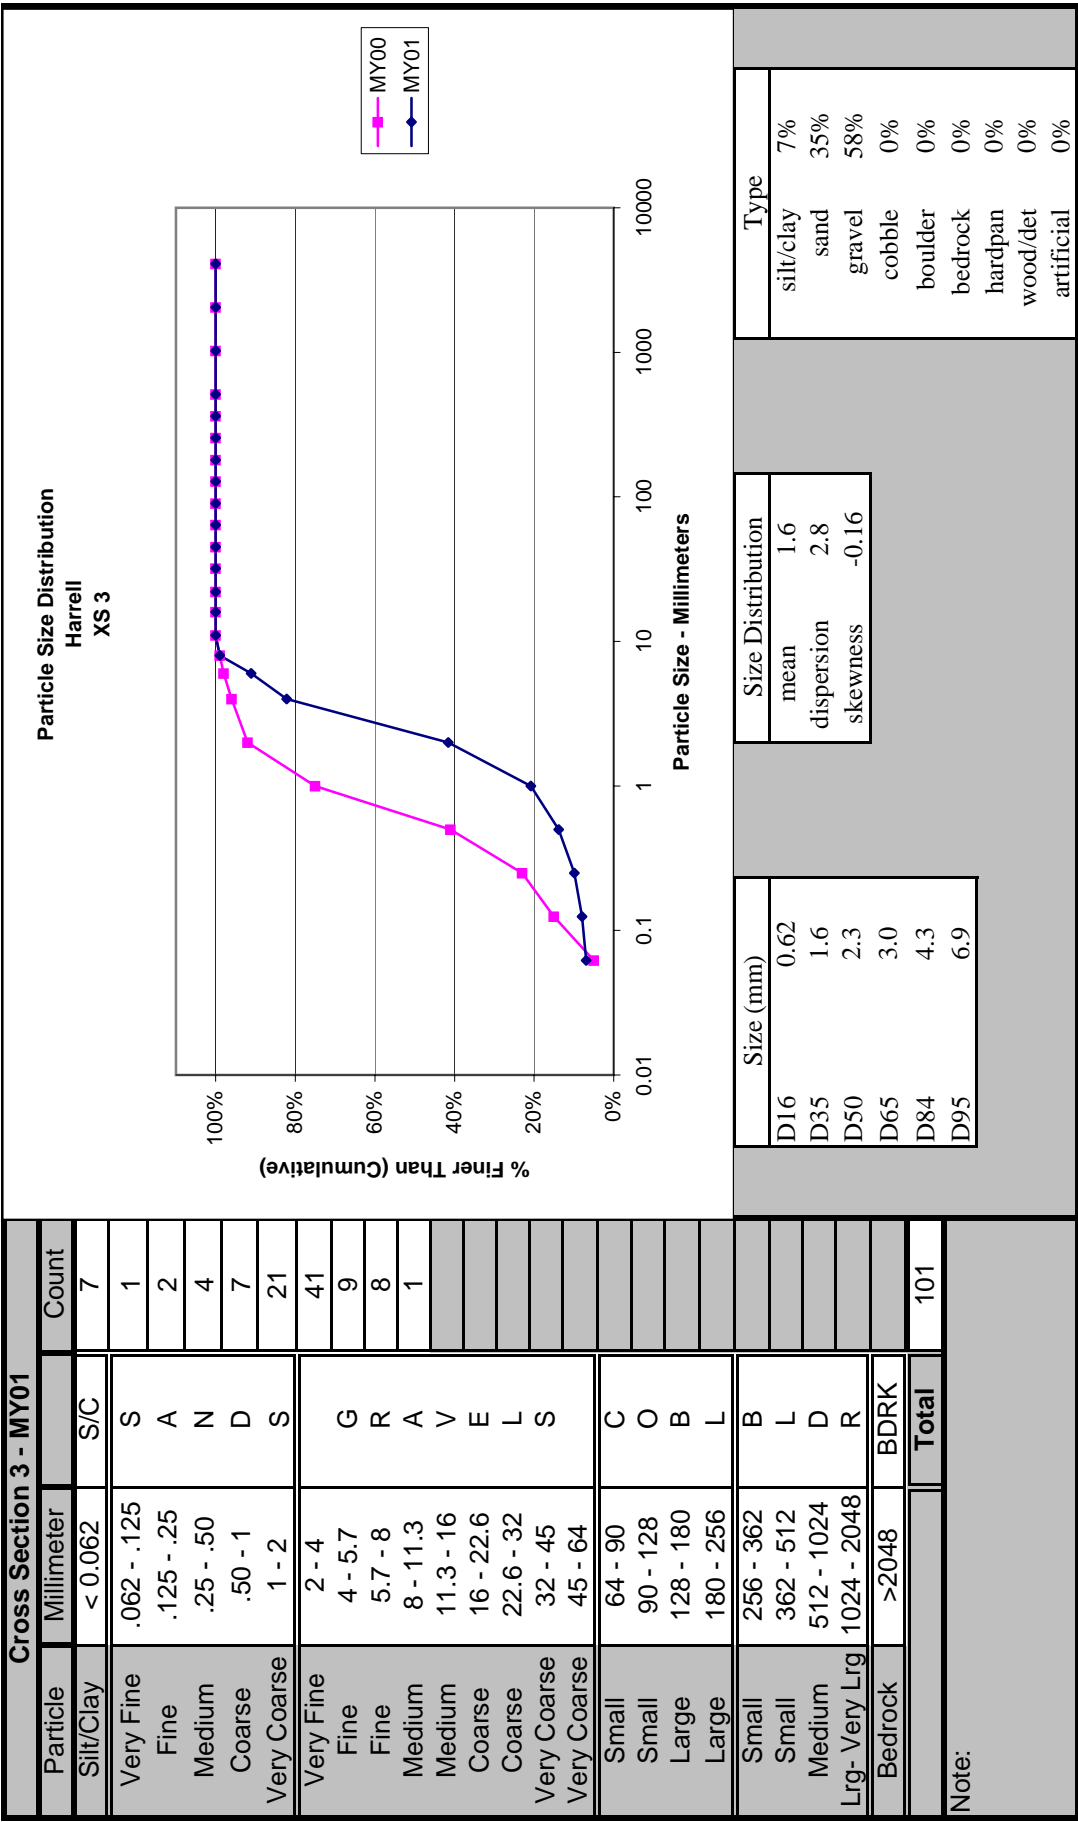


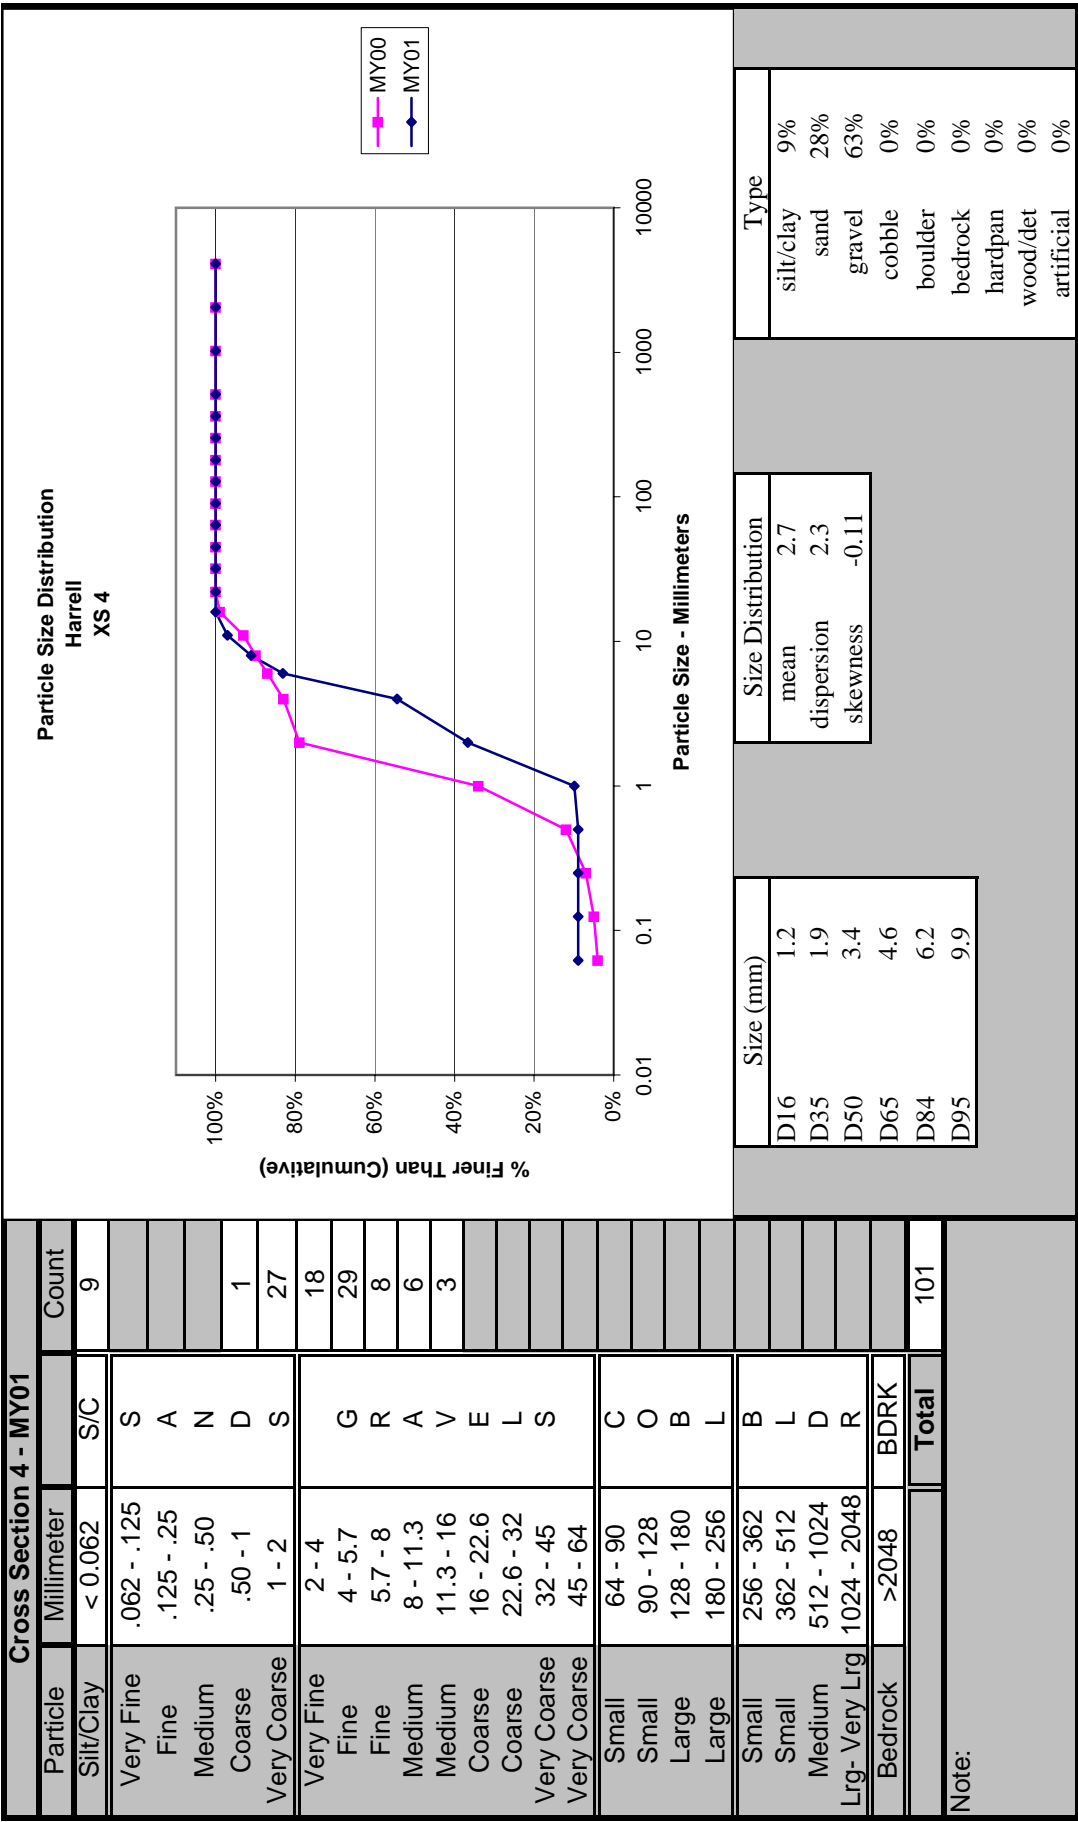


Size (mm)		Size Distribution		Type	
D16	1.2	mean	2.7	silt/clay	9%
D35	1.9	dispersion	2.3	sand	28%
D50	3.4	skewness	-0.11	gravel	63%
D65	4.6			cobble	0%
D84	6.2			boulder	0%
D95	9.9			bedrock	0%
				hardpan	0%
				wood/det	0%
				artificial	0%

Cross Section 4 - MY01				Count
Particle	Millimeter	S/C		
Silt/Clay	< 0.062			9
Very Fine	.062 - .125	S		
Fine	.125 - .25	A		
Medium	.25 - .50	N		1
Coarse	.50 - 1	D		
Very Coarse	1 - 2	S		27
Very Fine	2 - 4			18
Fine	4 - 5.7	G		29
Fine	5.7 - 8	R		8
Medium	8 - 11.3	A		6
Medium	11.3 - 16	V		3
Coarse	16 - 22.6	E		
Coarse	22.6 - 32	L		
Very Coarse	32 - 45	S		
Very Coarse	45 - 64			
Small	64 - 90	C		
Small	90 - 128	O		
Large	128 - 180	B		
Large	180 - 256	L		
Small	256 - 362	B		
Small	362 - 512	L		
Medium	512 - 1024	D		
Lrg- Very Lrg	1024 - 2048	R		
Bedrock	>2048	BDRK		
		Total		101

Note:

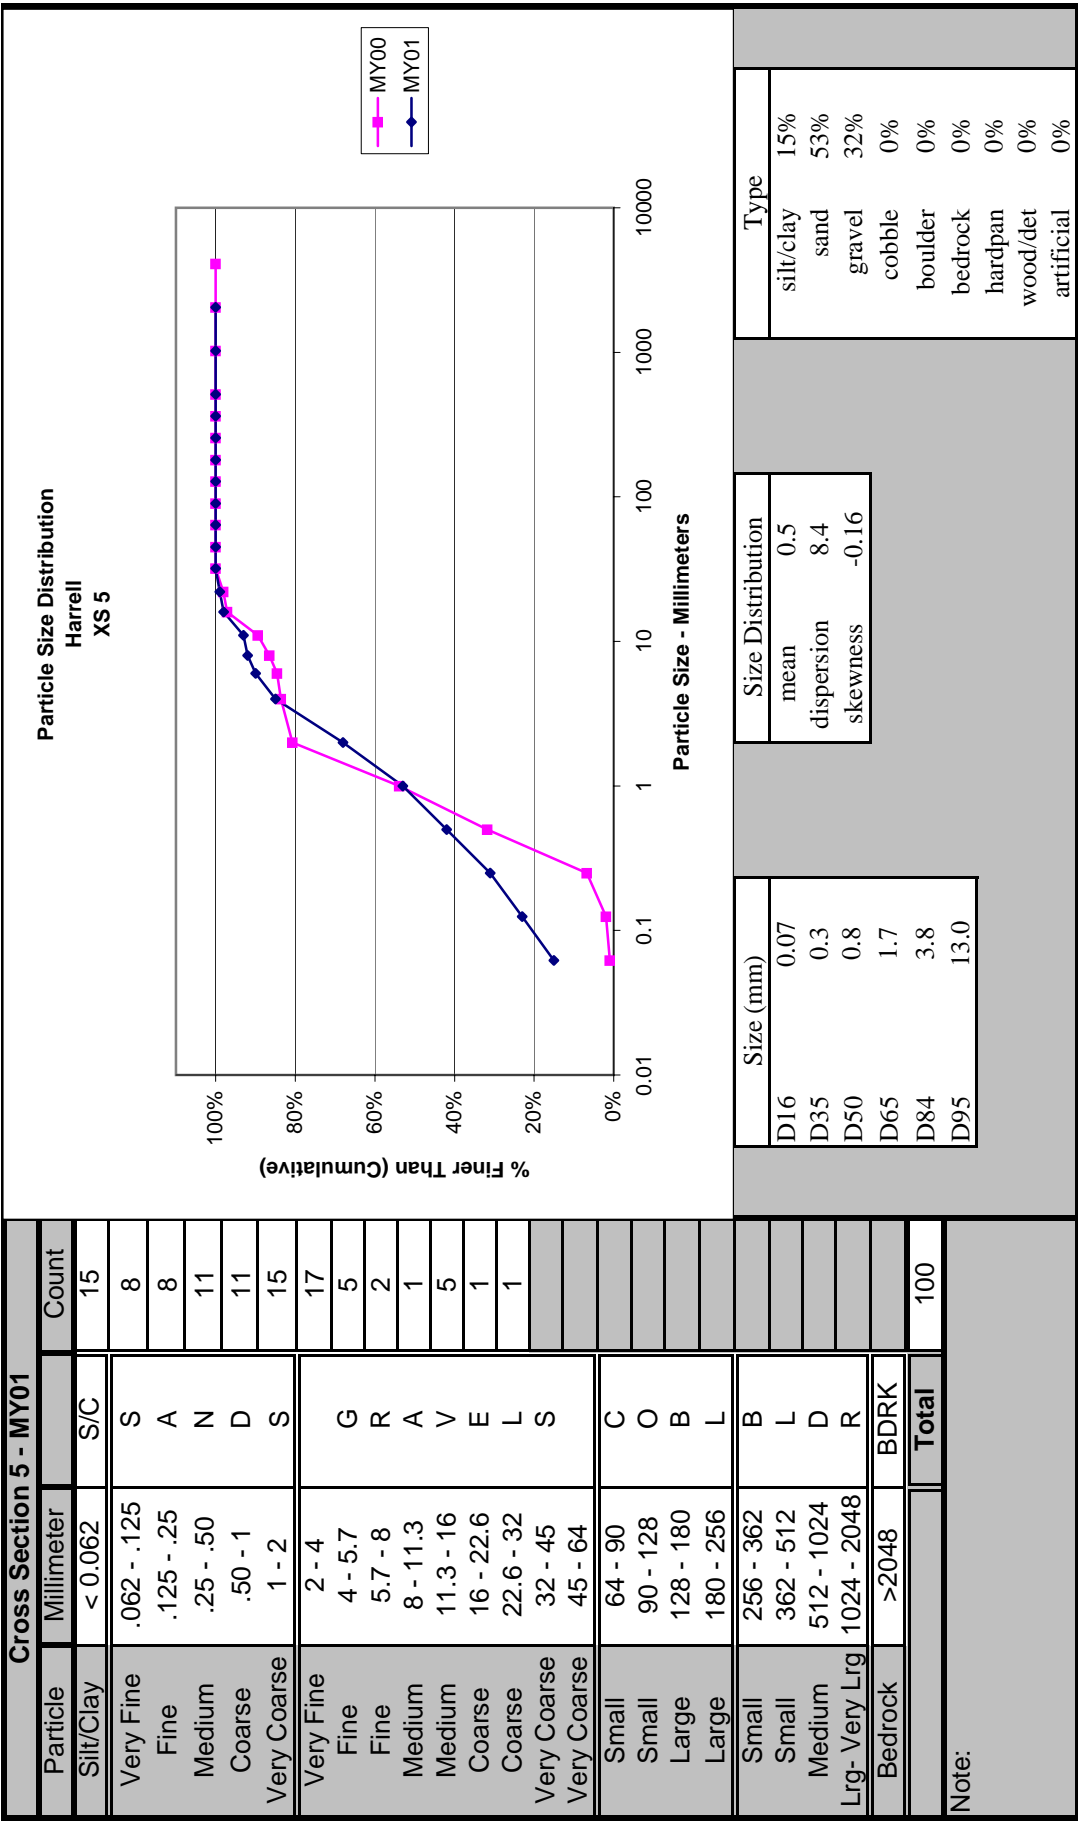

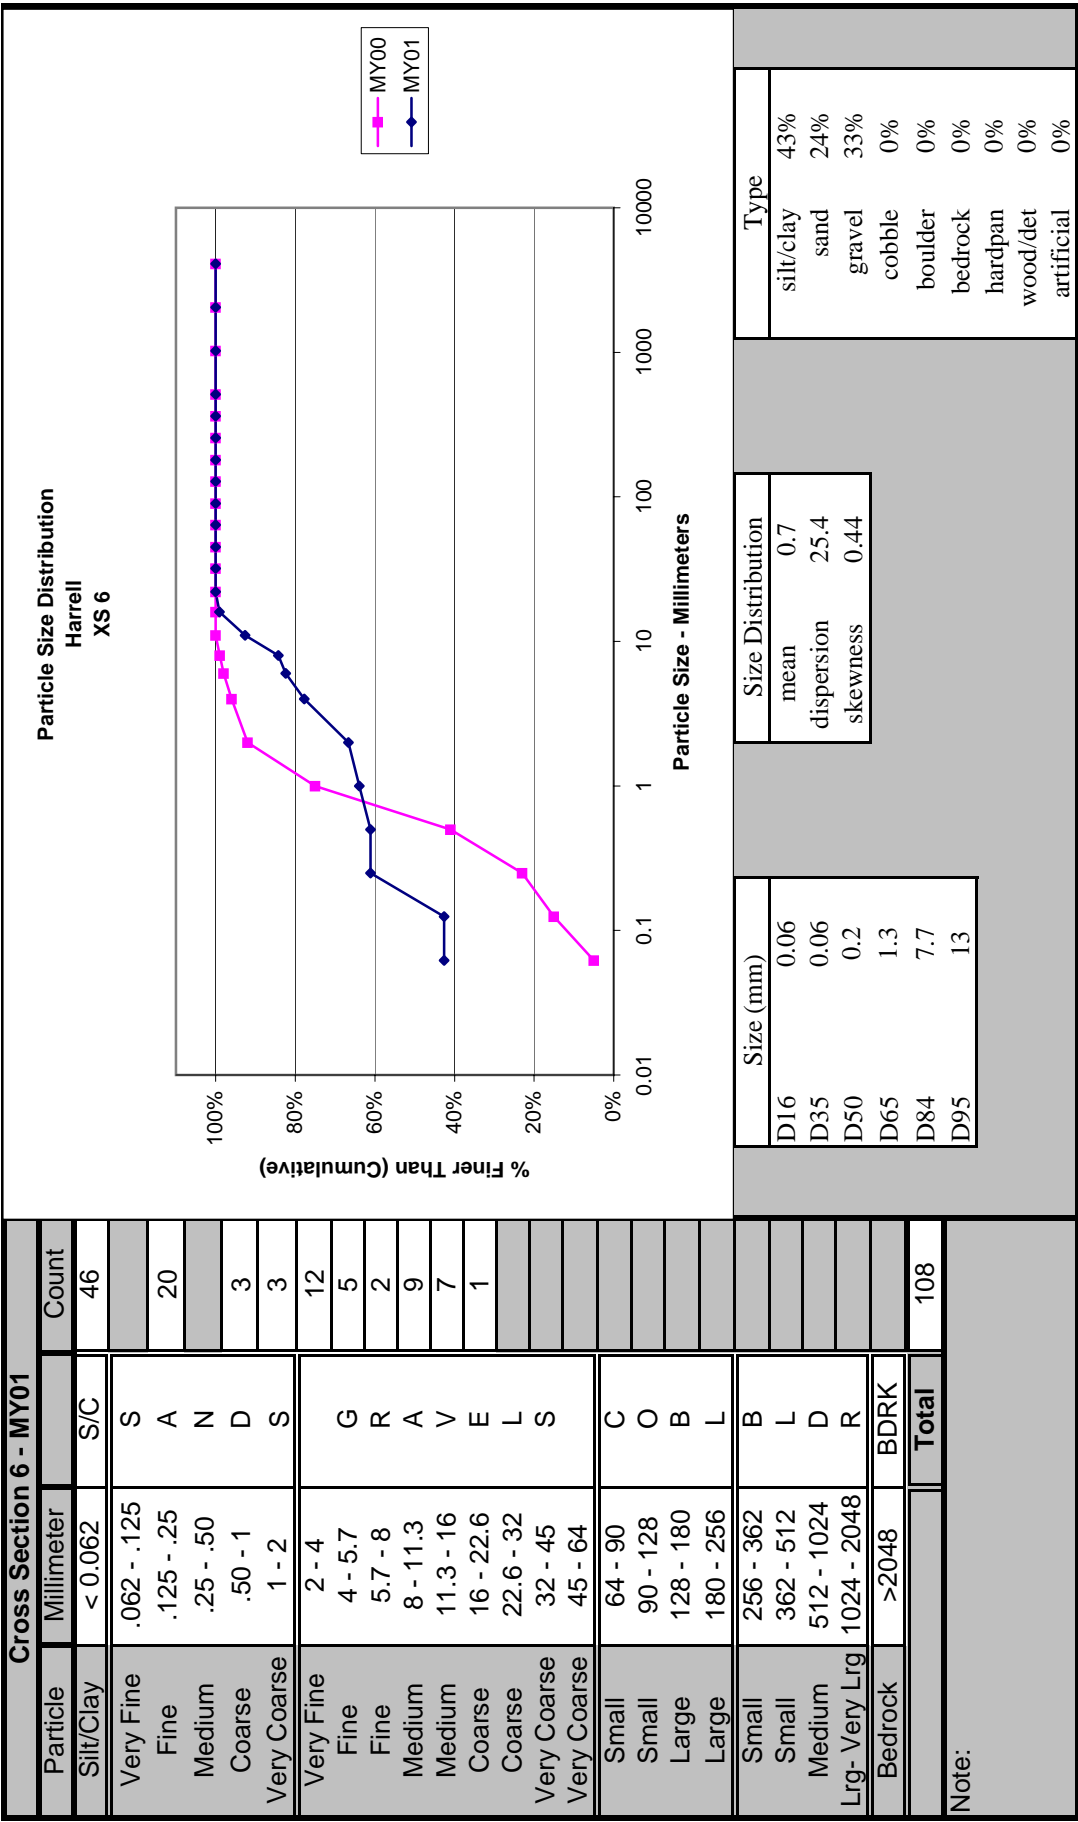


Size Distribution	
mean	0.7
dispersion	25.4
skewness	0.44


Size (mm)	
D16	0.06
D35	0.06
D50	0.2
D65	1.3
D84	7.7
D95	13


Type	Percentage
silt/clay	43%
sand	24%
gravel	33%
cobble	0%
boulder	0%
bedrock	0%
hardpan	0%
wood/det	0%
artificial	0%

Cross Section 6 - MY01			
Particle	Millimeter	S/C	Count
Silt/Clay	< 0.062	S/C	46
Very Fine	.062 - .125	S	
Fine	.125 - .25	A	20
Medium	.25 - .50	N	
Coarse	.50 - 1	D	3
Very Coarse	1 - 2	S	3
Very Fine	2 - 4		12
Fine	4 - 5.7	G	5
Fine	5.7 - 8	R	2
Medium	8 - 11.3	A	9
Medium	11.3 - 16	V	7
Coarse	16 - 22.6	E	1
Coarse	22.6 - 32	L	
Very Coarse	32 - 45	S	
Very Coarse	45 - 64		
Small	64 - 90	C	
Small	90 - 128	O	
Large	128 - 180	B	
Large	180 - 256	L	
Small	256 - 362	B	
Small	362 - 512	L	
Medium	512 - 1024	D	
Lrg- Very Lrg	1024 - 2048	R	
Bedrock	>2048	BDRK	
Total			108

Note:

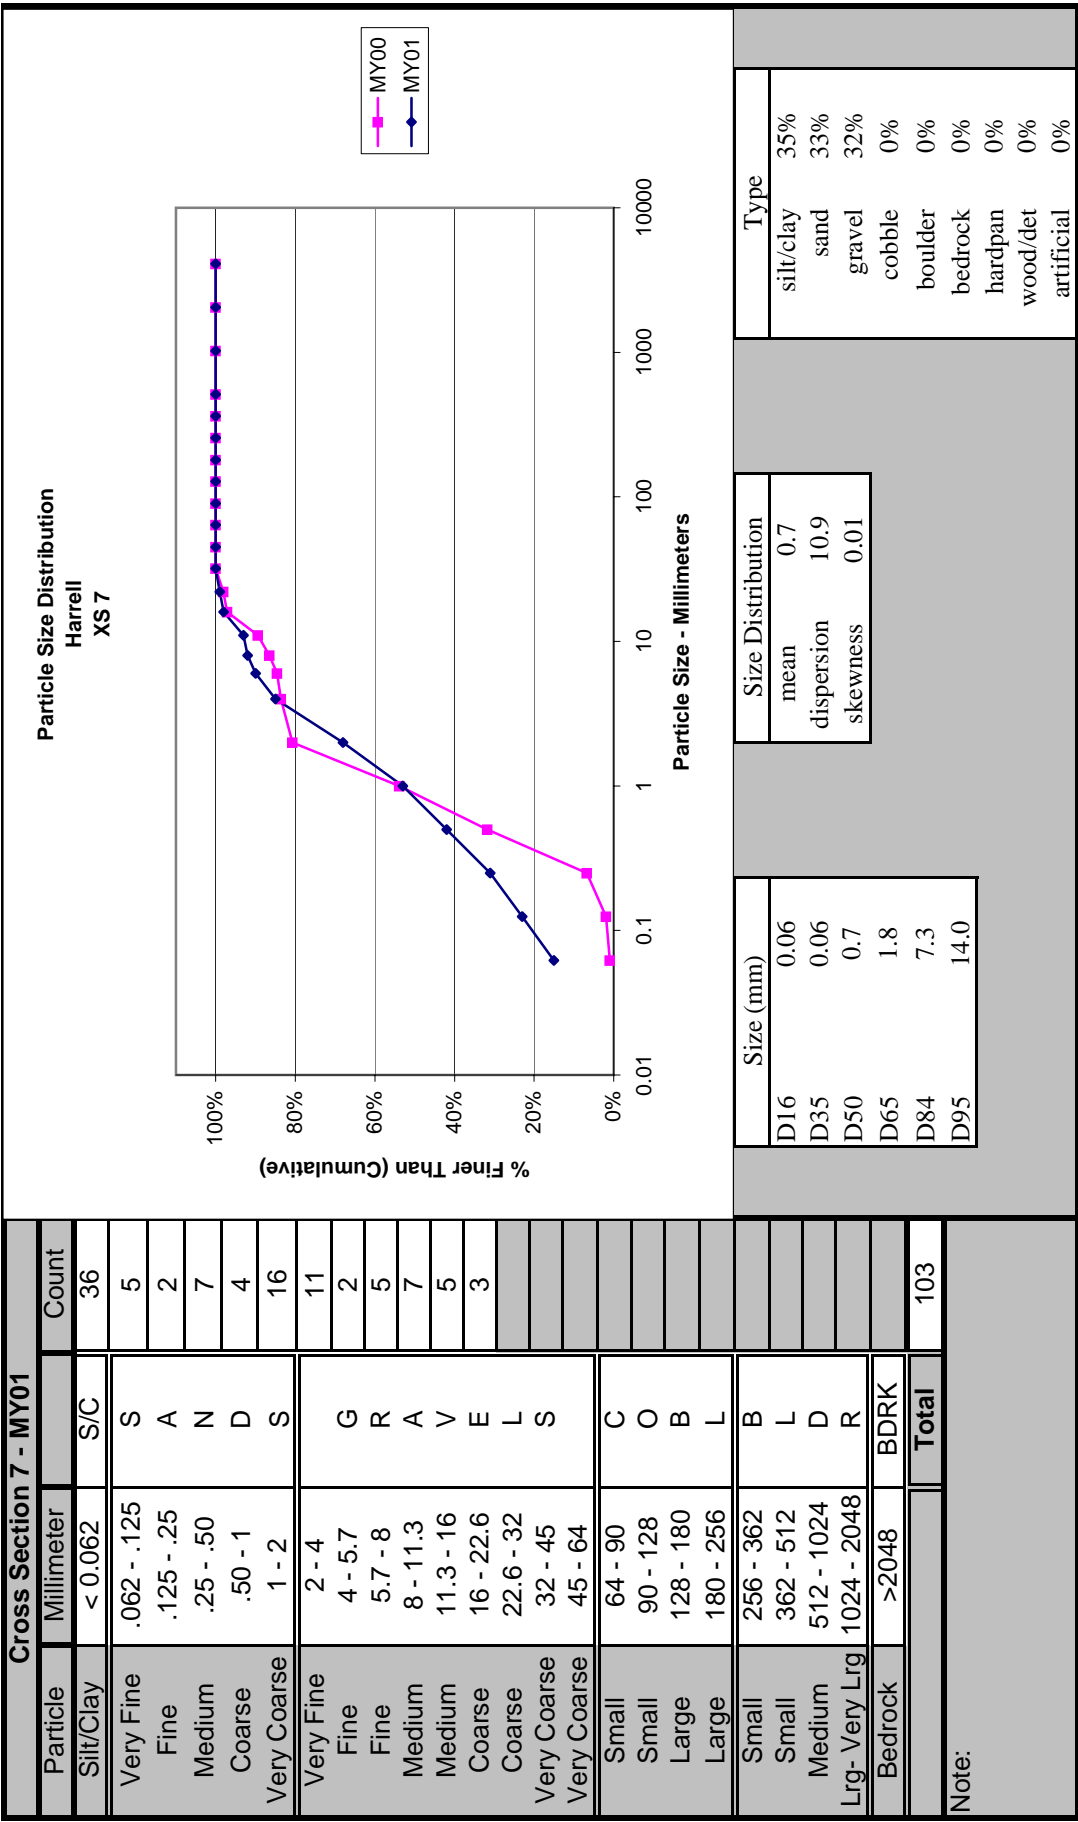

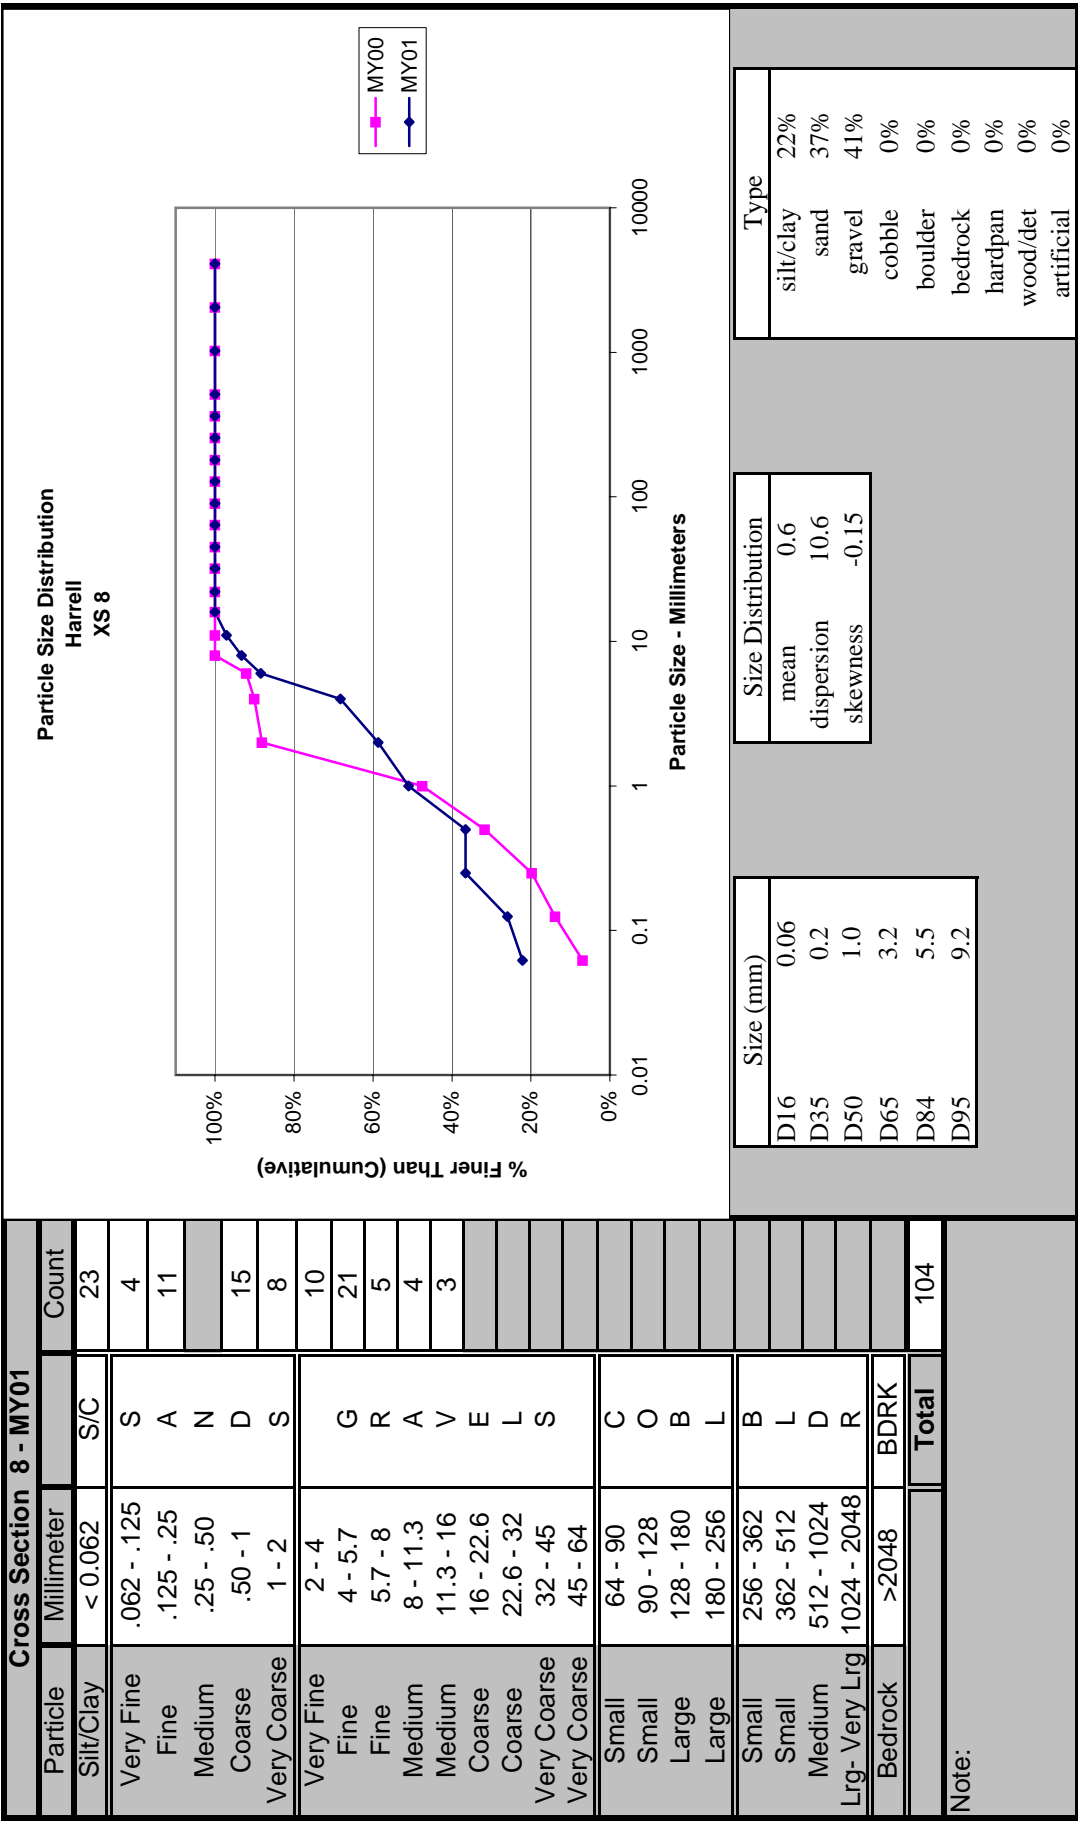

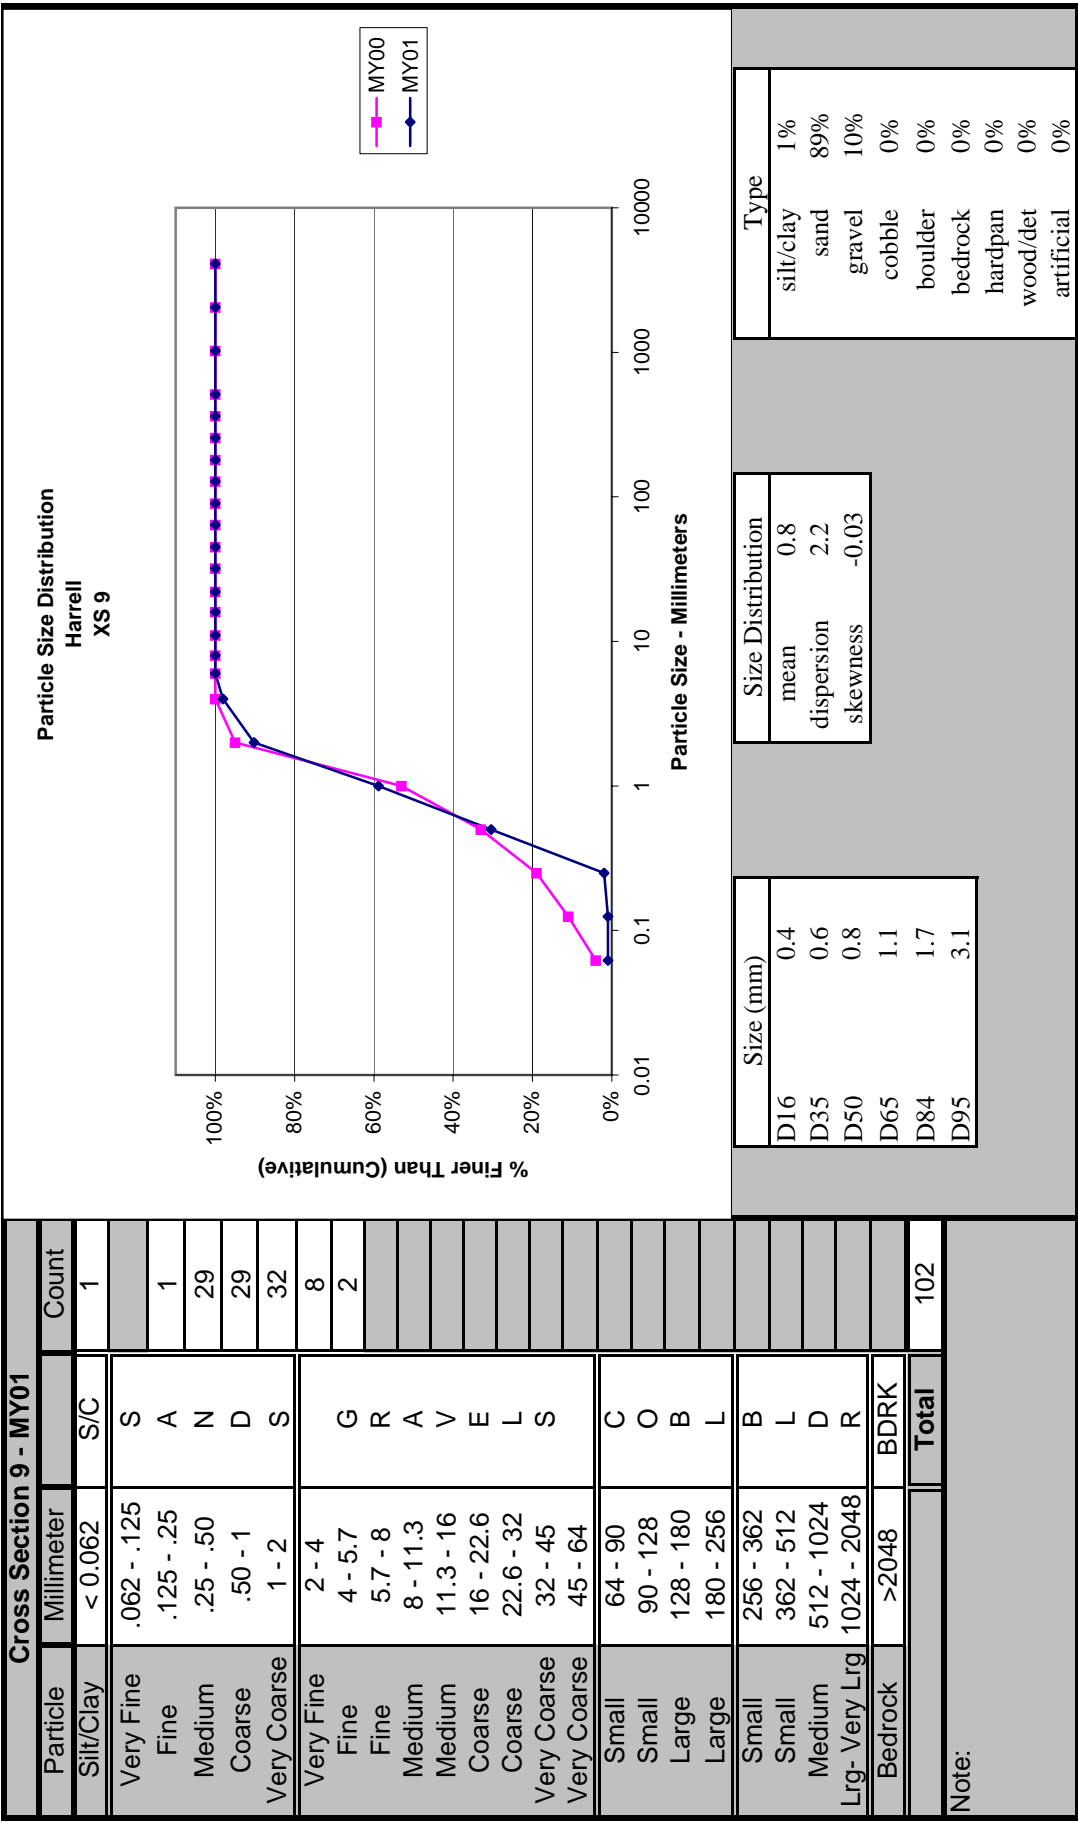


Size (mm)	
D16	0.4
D35	0.6
D50	0.8
D65	1.1
D84	1.7
D95	3.1

Size Distribution	
mean	0.8
dispersion	2.2
skewness	-0.03

Type	
silt/clay	1%
sand	89%
gravel	10%
cobble	0%
boulder	0%
bedrock	0%
hardpan	0%
wood/det	0%
artificial	0%

Cross Section 9 - MY01			
Particle	Millimeter	S/C	Count
Silt/Clay	< 0.062	S/C	1
Very Fine	.062 - .125	S	
Fine	.125 - .25	A	1
Medium	.25 - .50	N	29
Coarse	.50 - 1	D	29
Very Coarse	1 - 2	S	32
Very Fine	2 - 4		8
Fine	4 - 5.7	G	2
Fine	5.7 - 8	R	
Medium	8 - 11.3	A	
Medium	11.3 - 16	V	
Coarse	16 - 22.6	E	
Coarse	22.6 - 32	L	
Very Coarse	32 - 45	S	
Very Coarse	45 - 64		
Small	64 - 90	C	
Small	90 - 128	O	
Large	128 - 180	B	
Large	180 - 256	L	
Small	256 - 362	B	
Small	362 - 512	L	
Medium	512 - 1024	D	
Lrg- Very Lrg	1024 - 2048	R	
Bedrock	>2048	BDRK	
Total			102

Note:

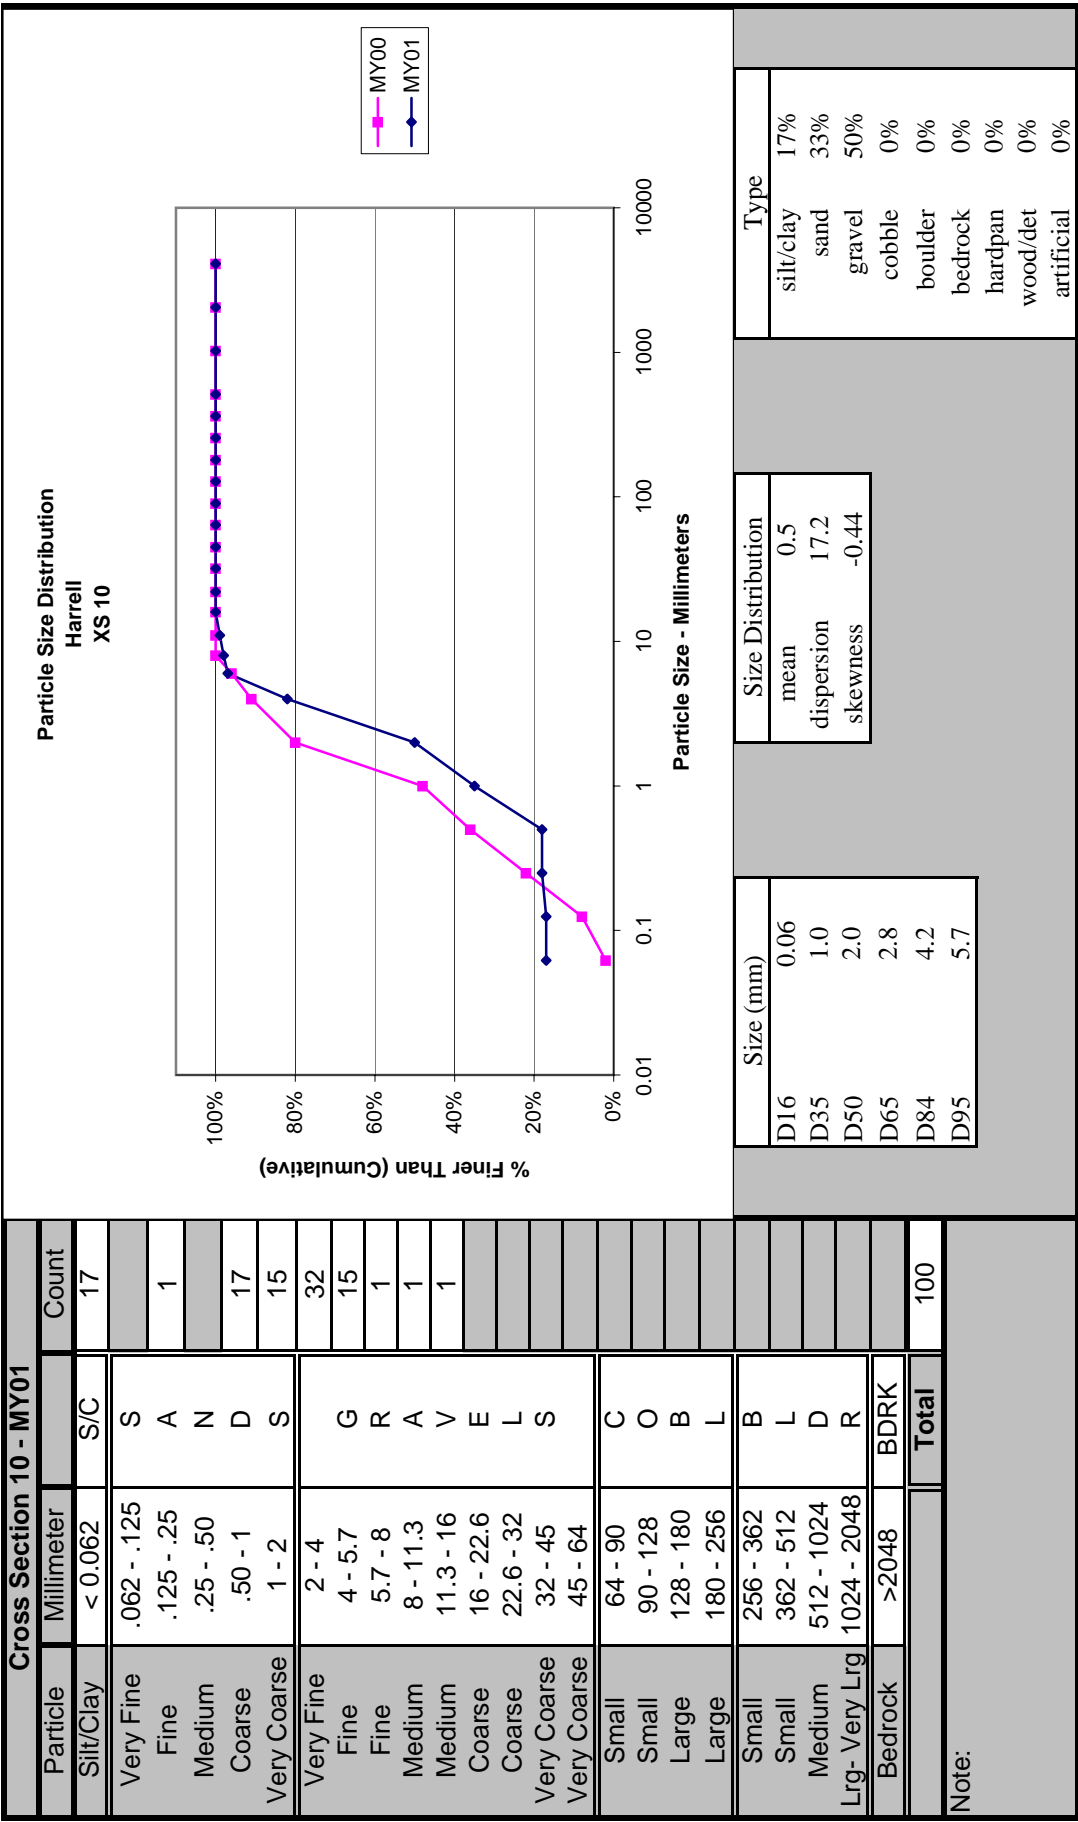


Note:

Cross Section 11 - MY01

Particle	Millimeter	S/C	Count
Silt/Clay	< 0.062	S/C	3
Very Fine	.062 - .125	S	
Fine	.125 - .25	A	
Medium	.25 - .50	N	1
Coarse	.50 - 1	D	5
Very Coarse	1 - 2	S	60
Very Fine	2 - 4		11
Fine	4 - 5.7	G	5
Fine	5.7 - 8	R	8
Medium	8 - 11.3	A	6
Medium	11.3 - 16	V	1
Coarse	16 - 22.6	E	1
Coarse	22.6 - 32	L	
Very Coarse	32 - 45	S	
Very Coarse	45 - 64		
Small	64 - 90	C	
Small	90 - 128	O	
Large	128 - 180	B	
Large	180 - 256	L	
Small	256 - 362	B	
Small	362 - 512	L	
Medium	512 - 1024	D	
Lrg- Very Lrg	1024 - 2048	R	
Bedrock	>2048	BDRK	
Total			101

Particle Size Distribution
Harrell
XS 11

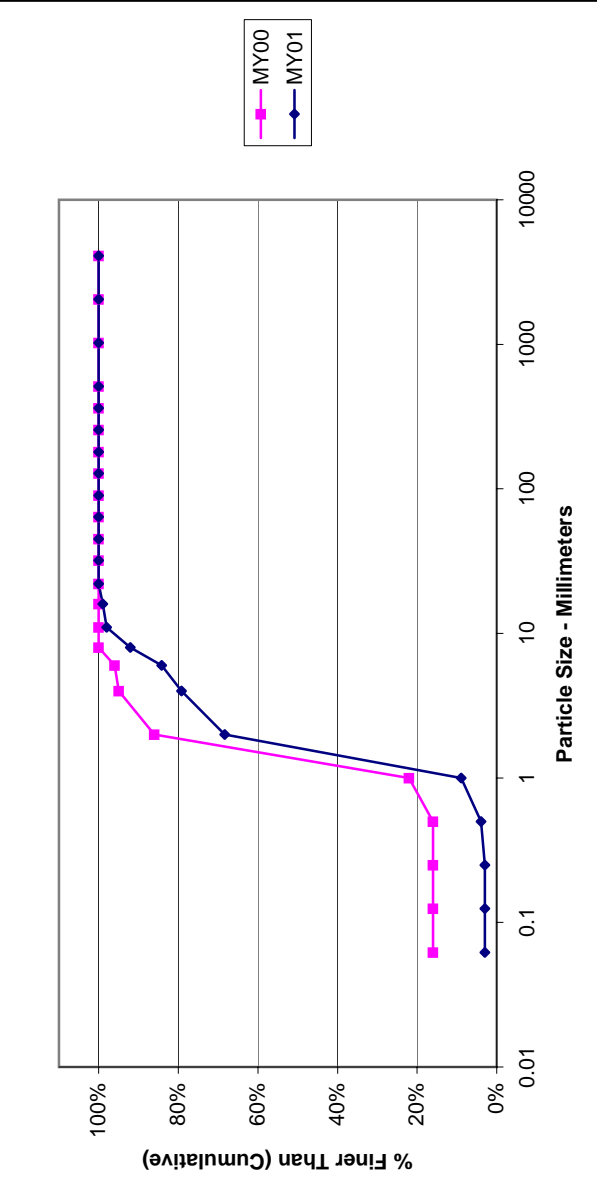



Size (mm)	Value
D16	1.1
D35	1.4
D50	1.6
D65	1.9
D84	5.9
D95	9.4


Size Distribution	
mean	2.5
dispersion	2.6
skewness	0.24

Type	Percentage
silt/clay	3%
sand	65%
gravel	32%
cobble	0%
boulder	0%
bedrock	0%
hardpan	0%
wood/det	0%
artificial	0%

Note:

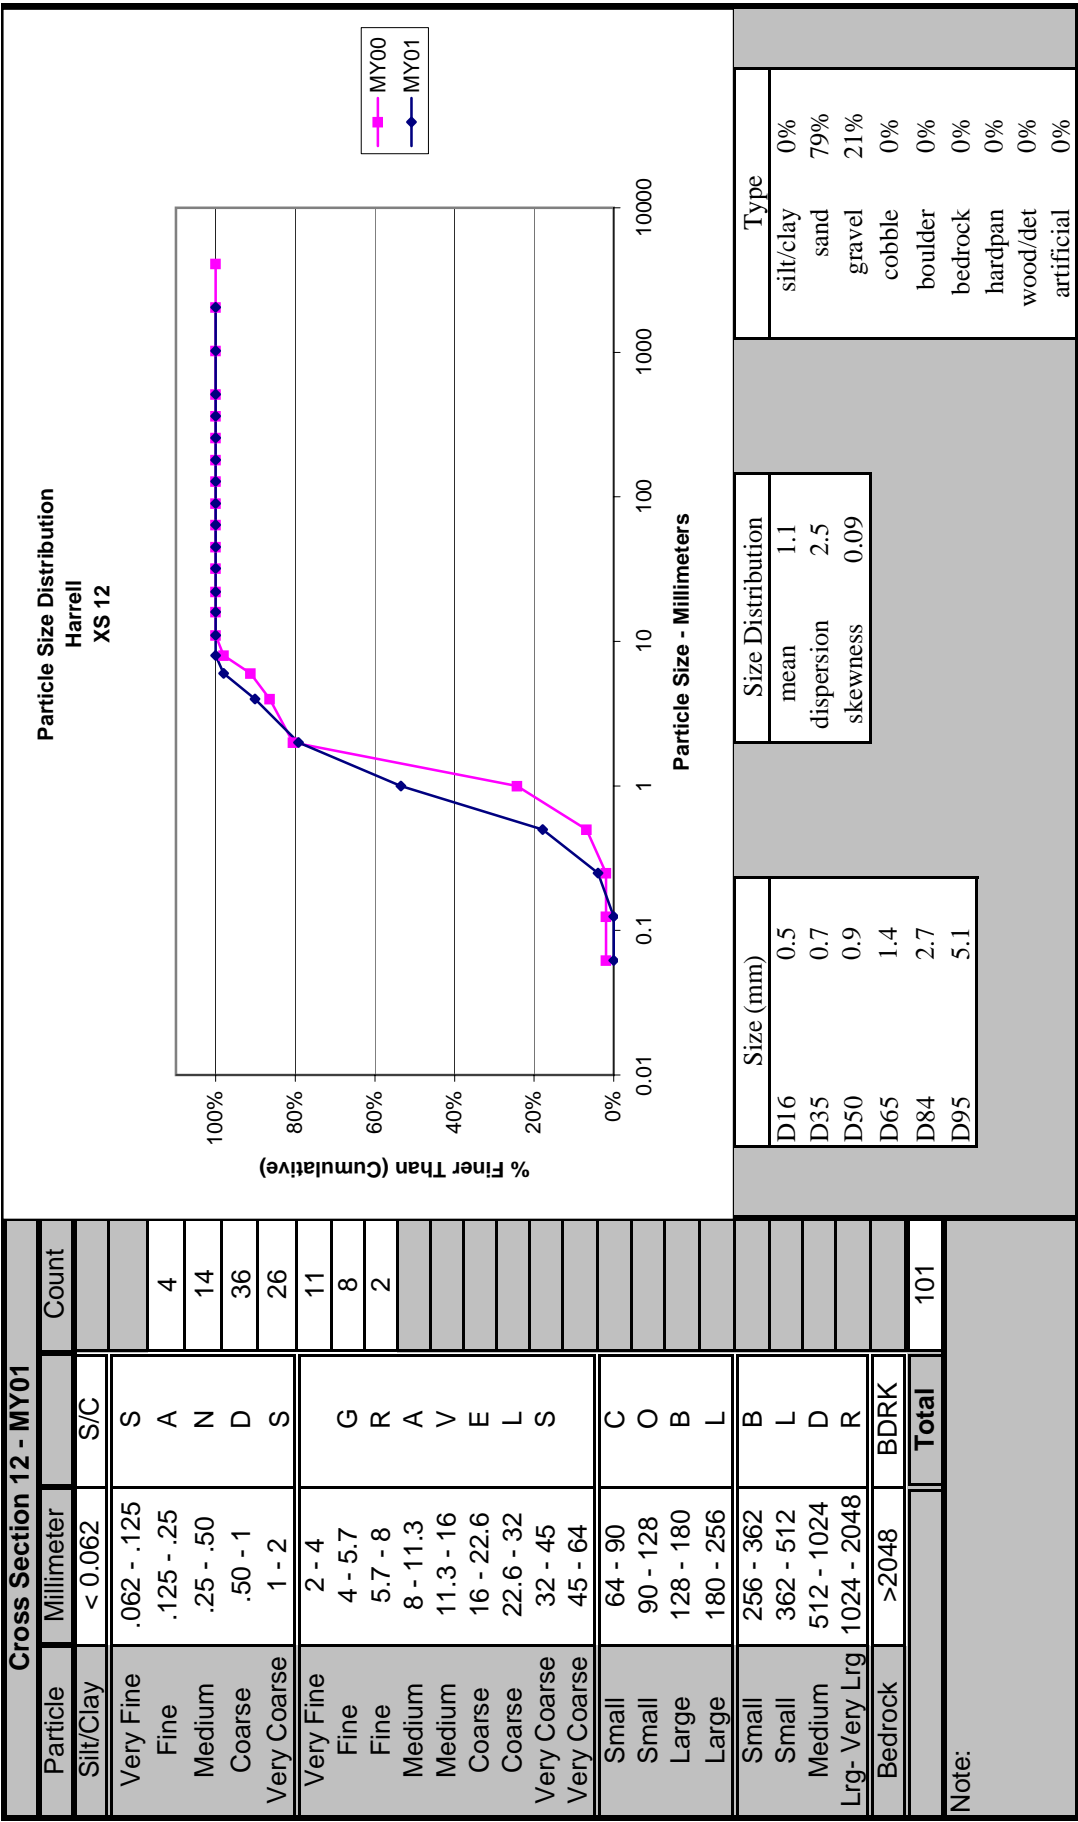


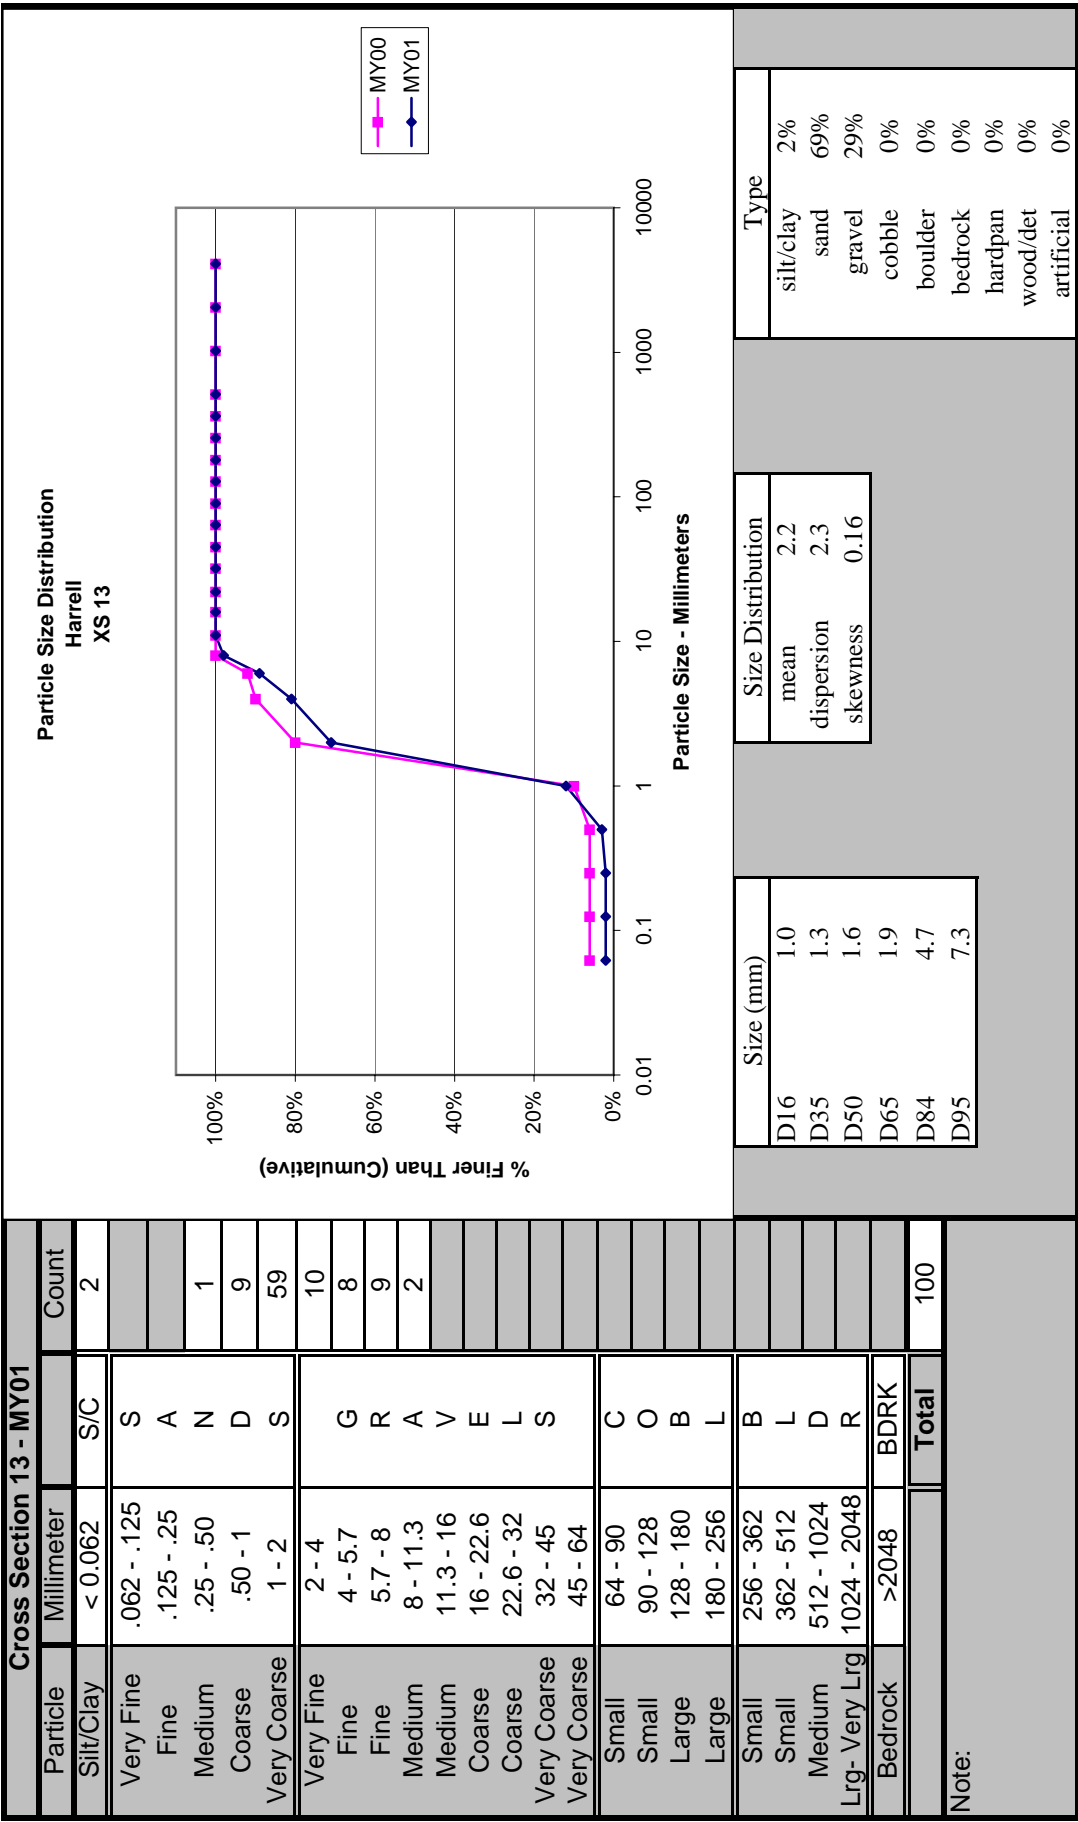

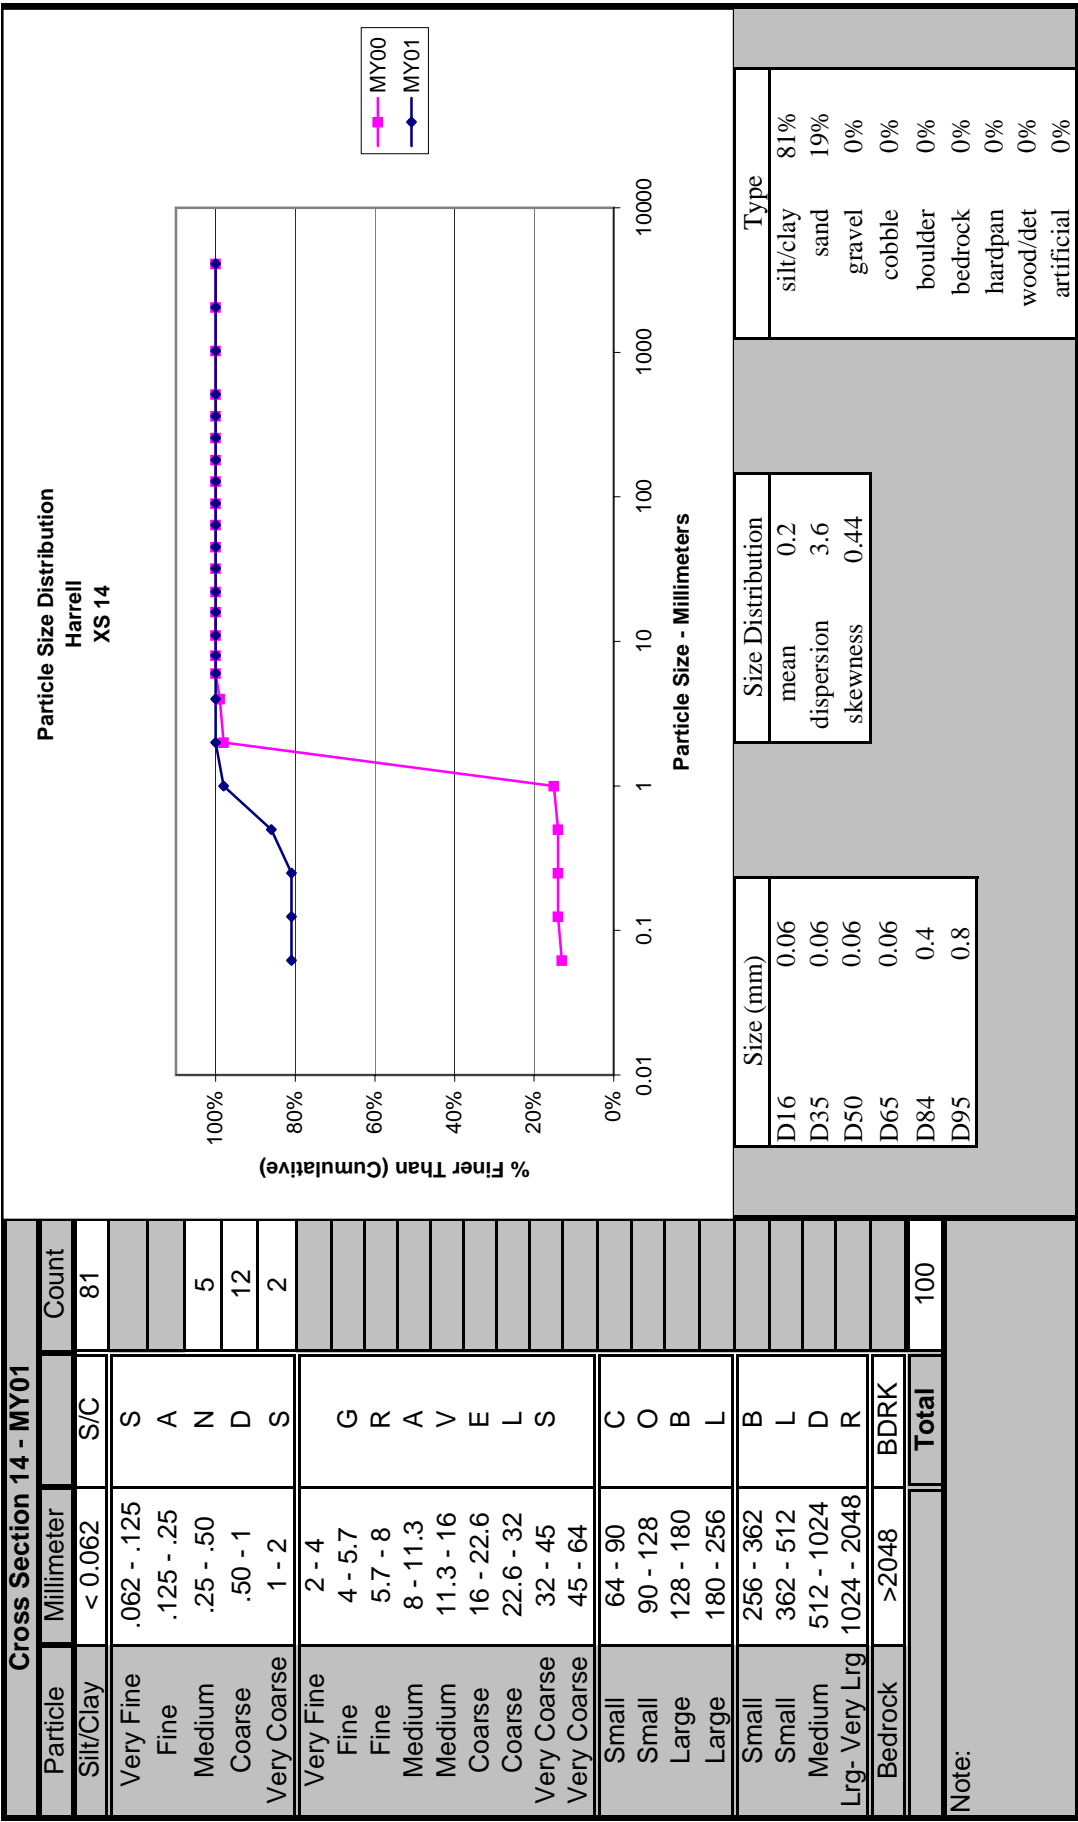


Appendix C4 - Stream and Wetland Hydrographs


Harrell
Stream Gauge
Stream Stage Hydrograph
10/29/07 to 02/18/08

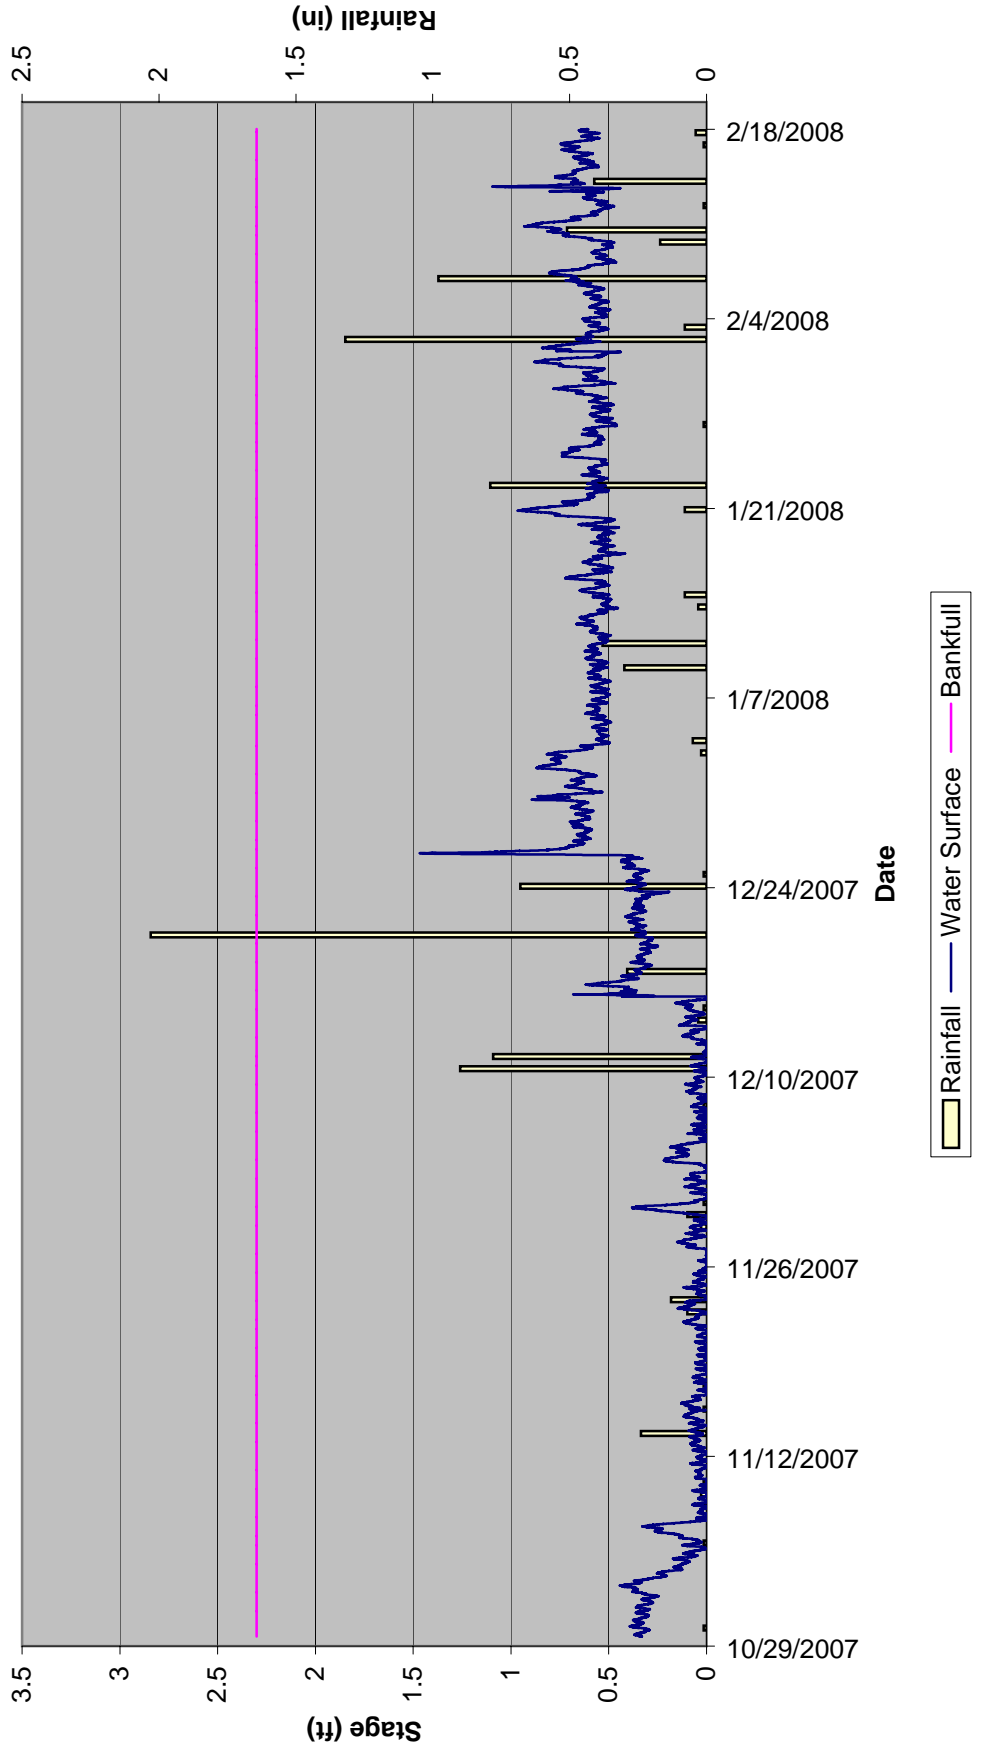


**Harrell
Stream Gauge
Stream Stage Hydrograph
02/18/08 to 05/15/08**

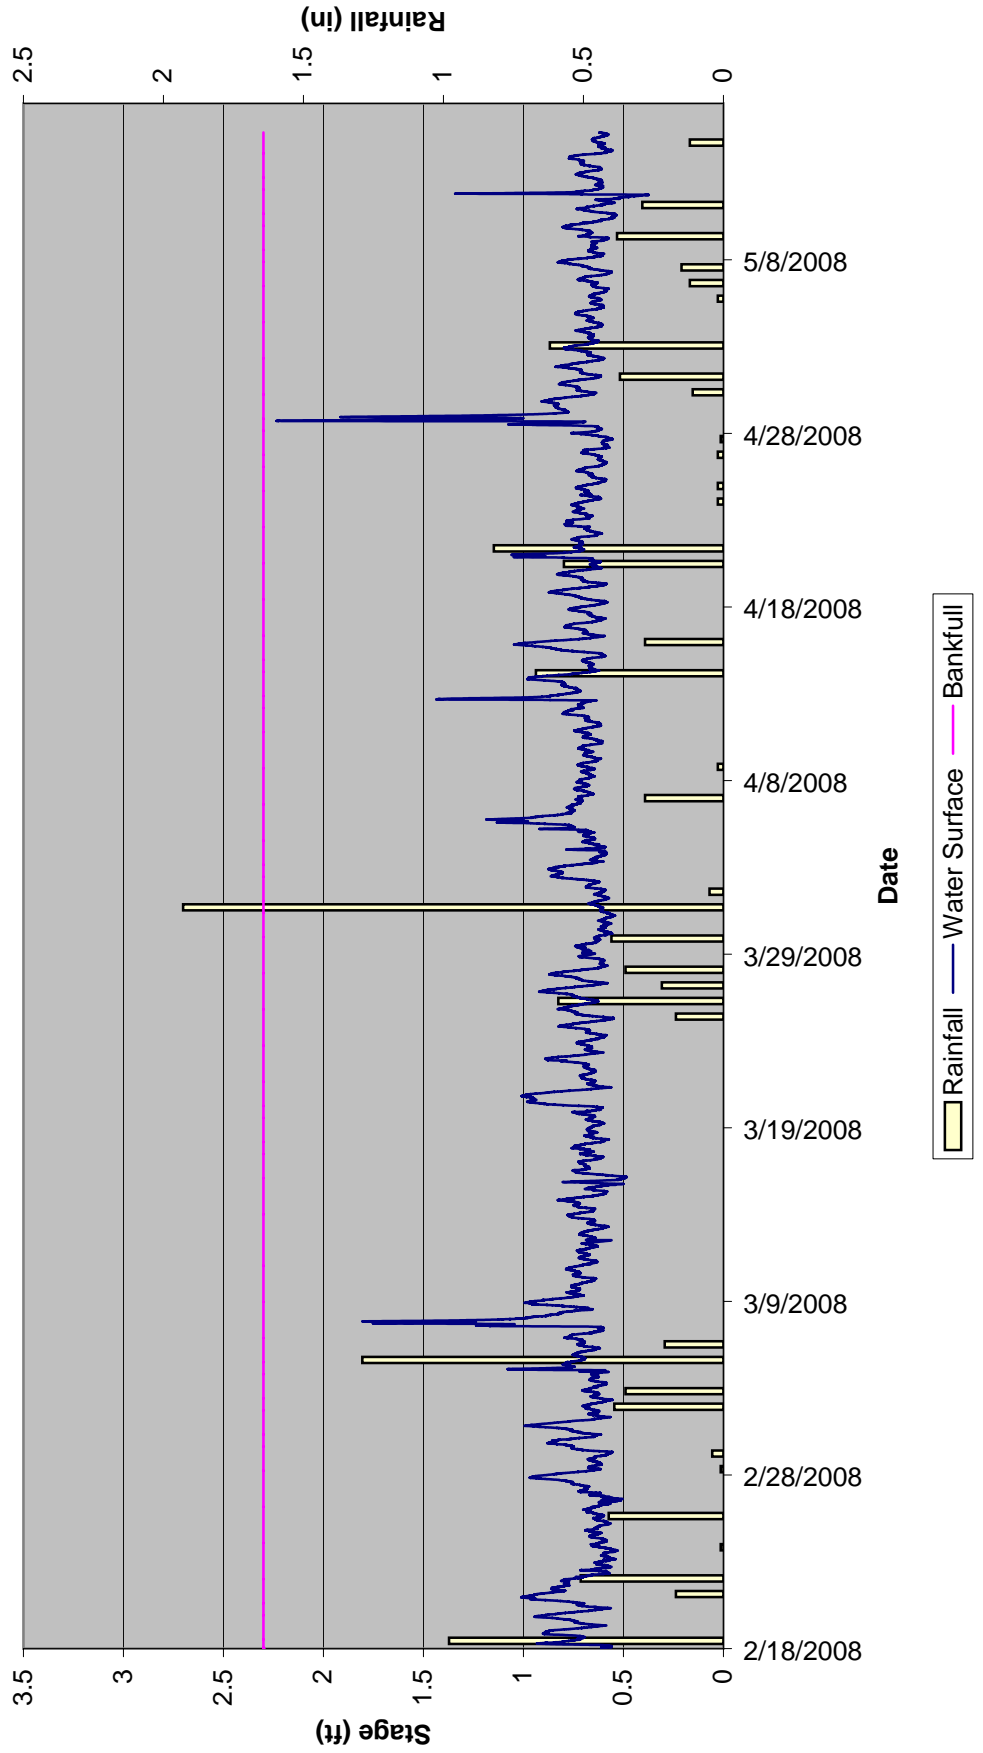


**Harrell
Stream Gauge
Stream Stage Hydrograph
05/15/08 to 09/03/08**

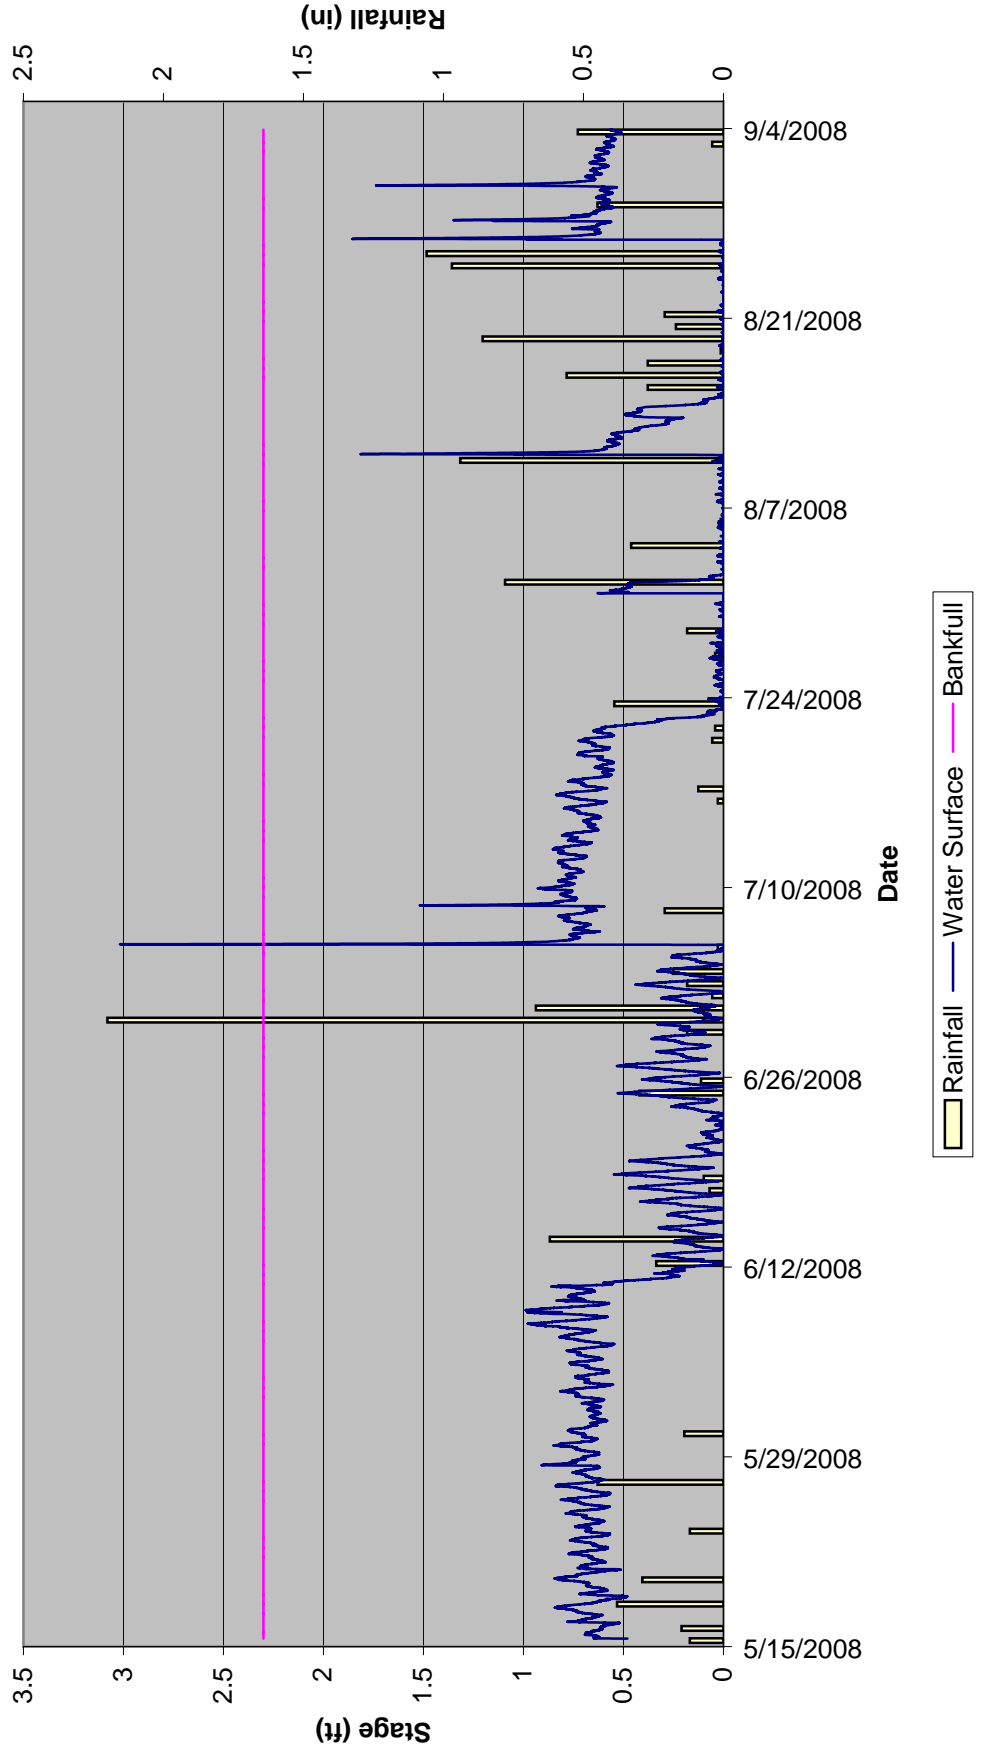

Harrell
Stream Gauge
Stream Stage Hydrograph
09/03/08 to 10/20/08

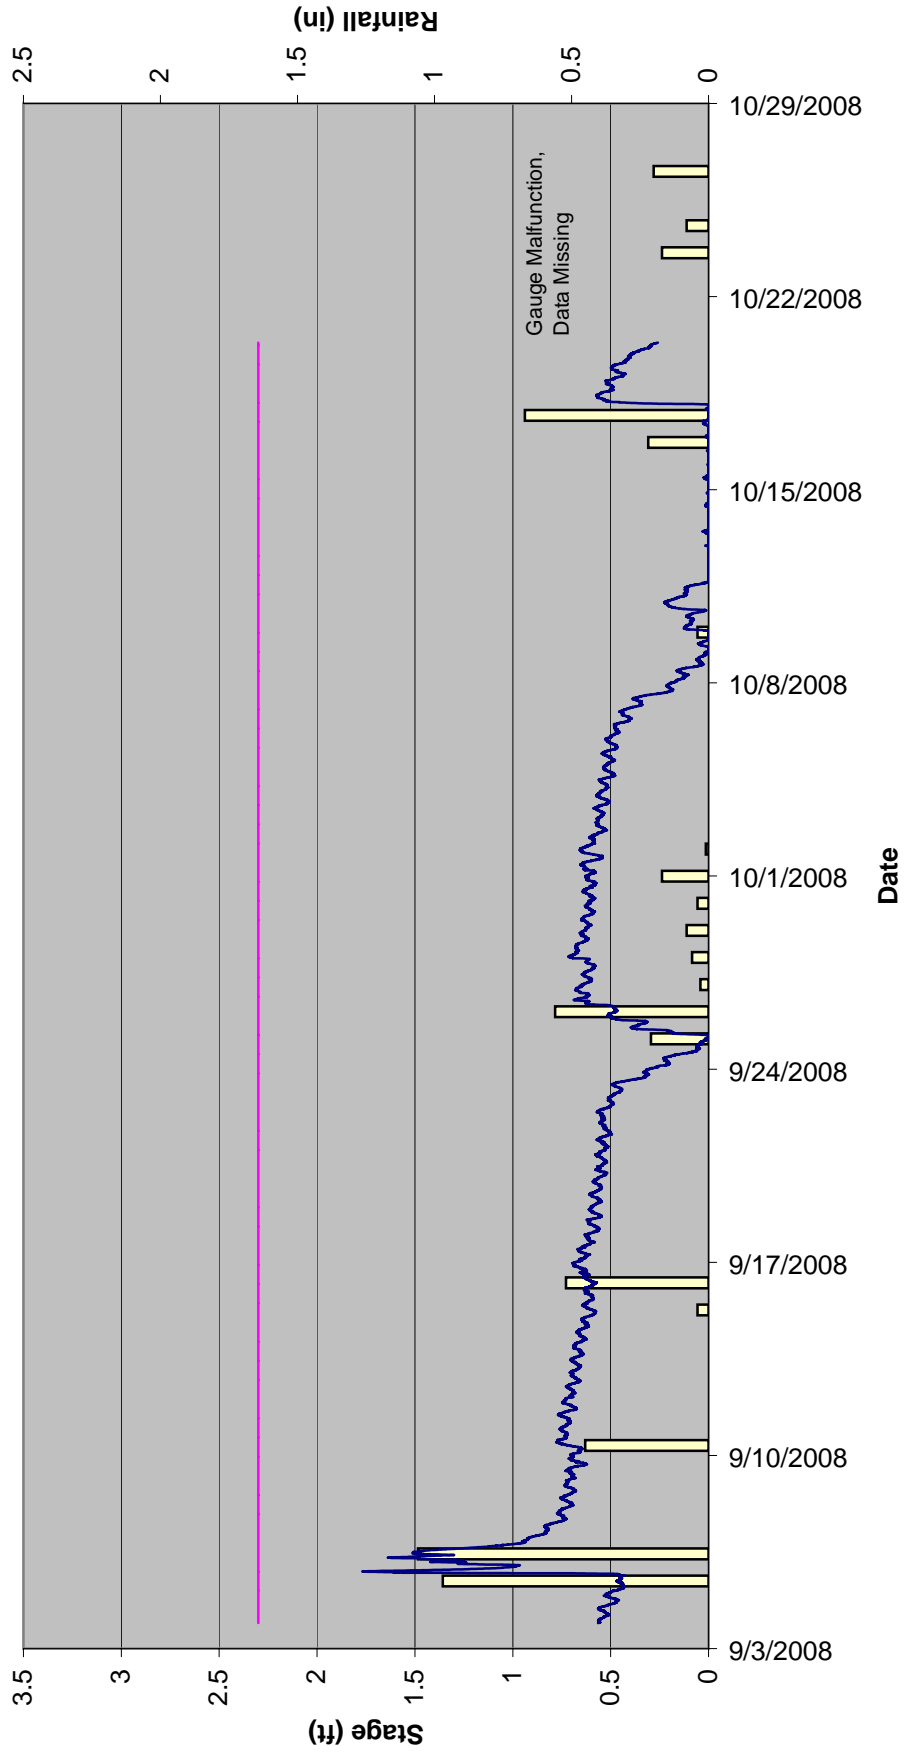


Harrell Farm Wetland Gauge 1 Wetland Hydrograph

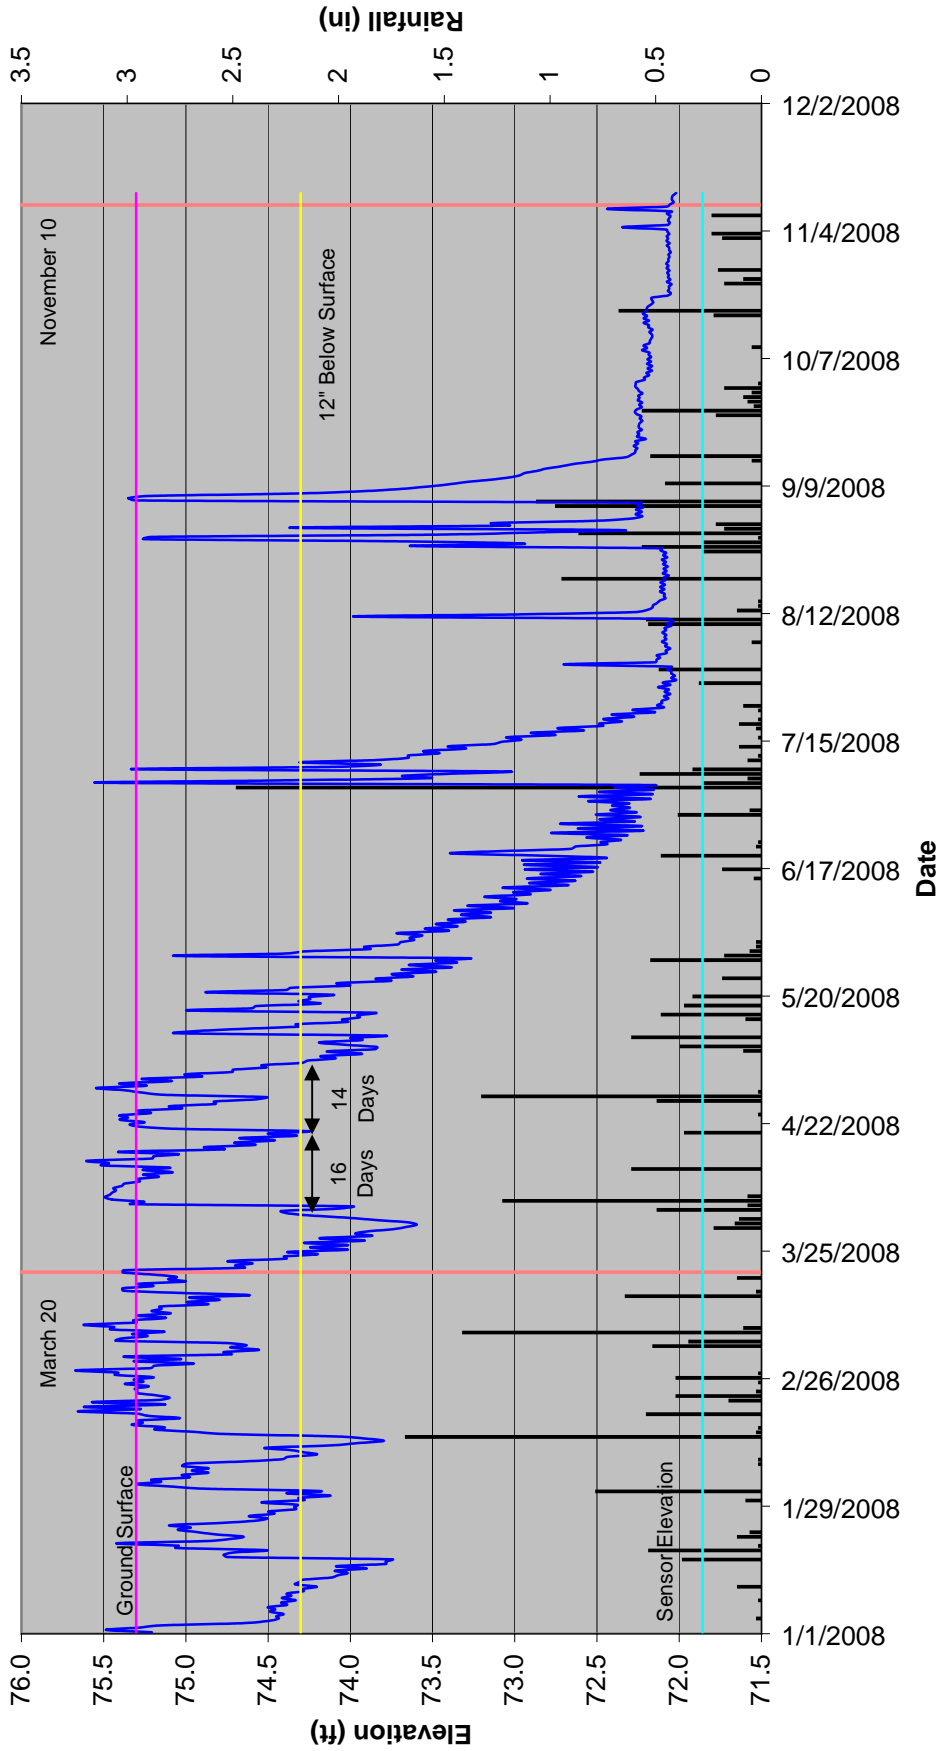


■ Rainfall — Groundwater Elevation

Harrell Farm Wetland Gauge 2 Wetland Hydrograph

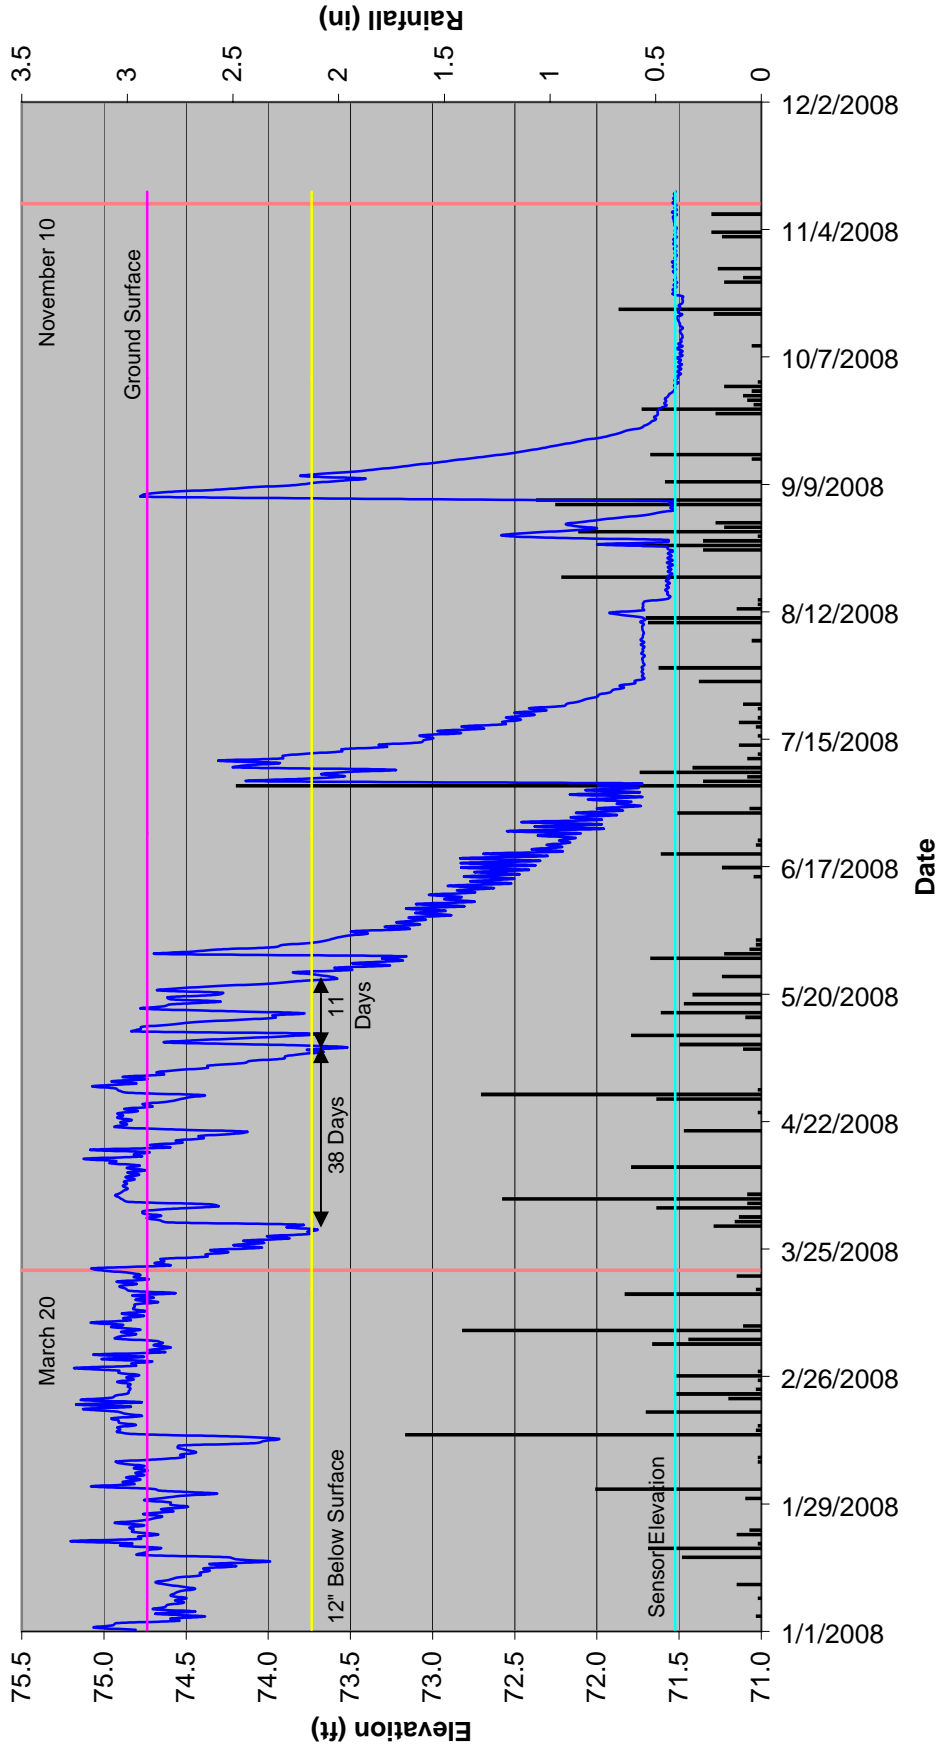


■ Rainfall — Groundwater Elevation

Harrell Farm Wetland Gauge 3 Wetland Hydrograph

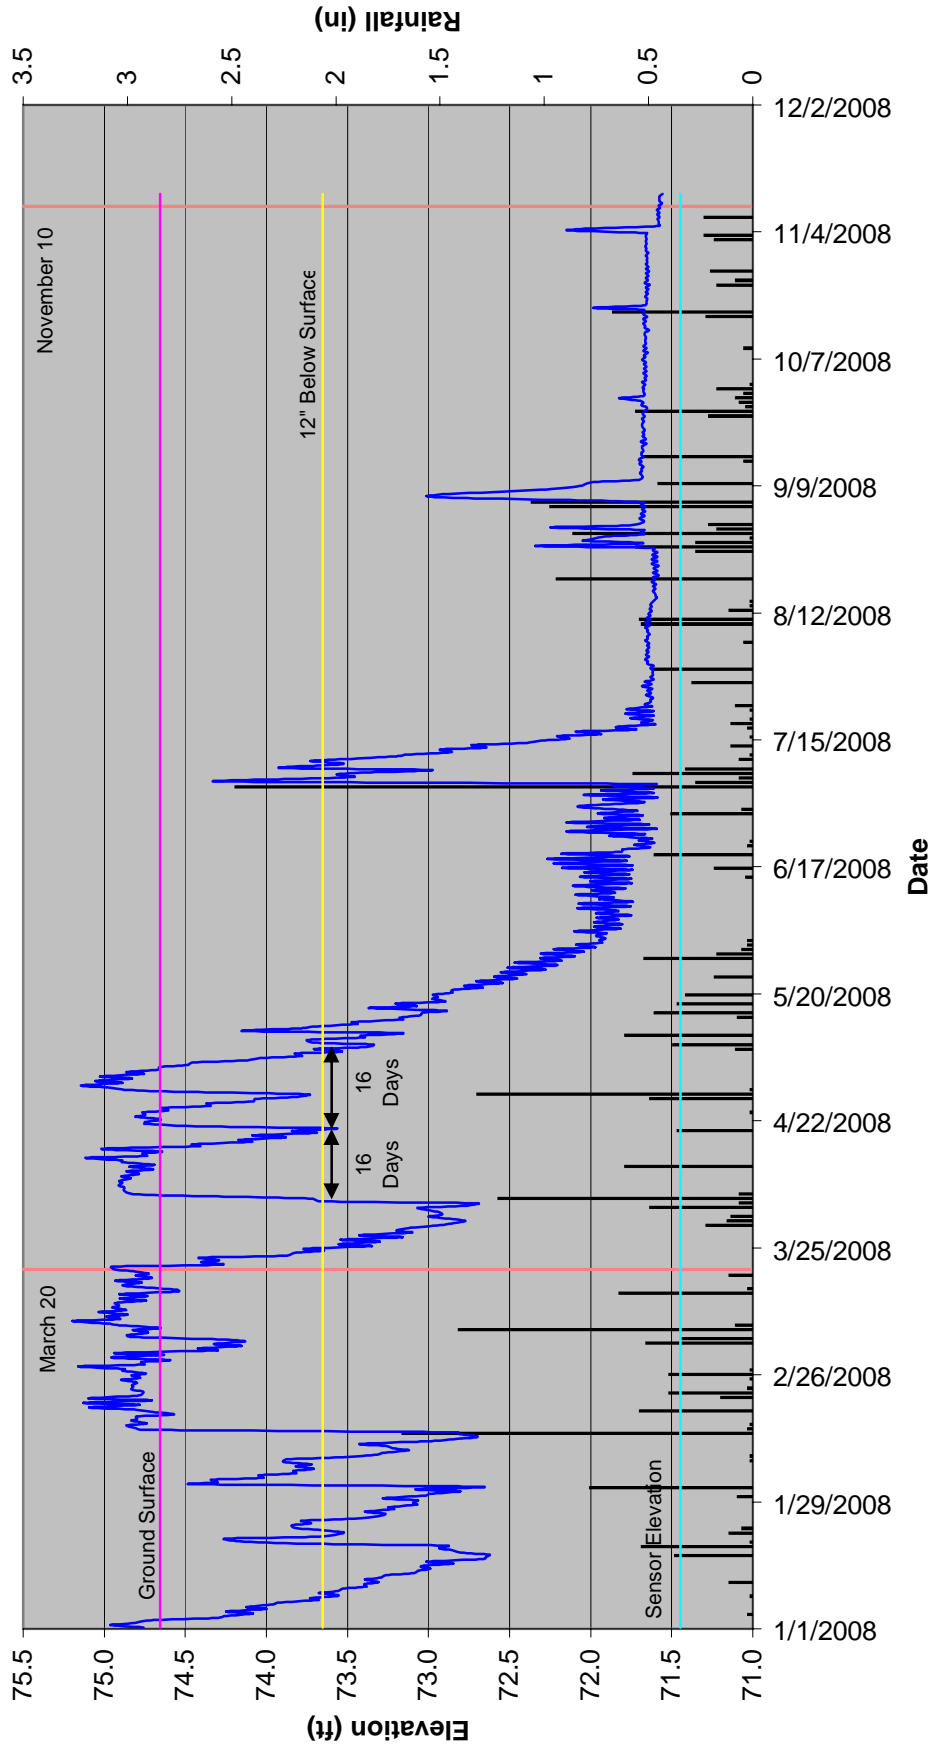


■ Rainfall — Groundwater Elevation

Harrell Farm
Wetland Gauge 4
Wetland Hydrograph

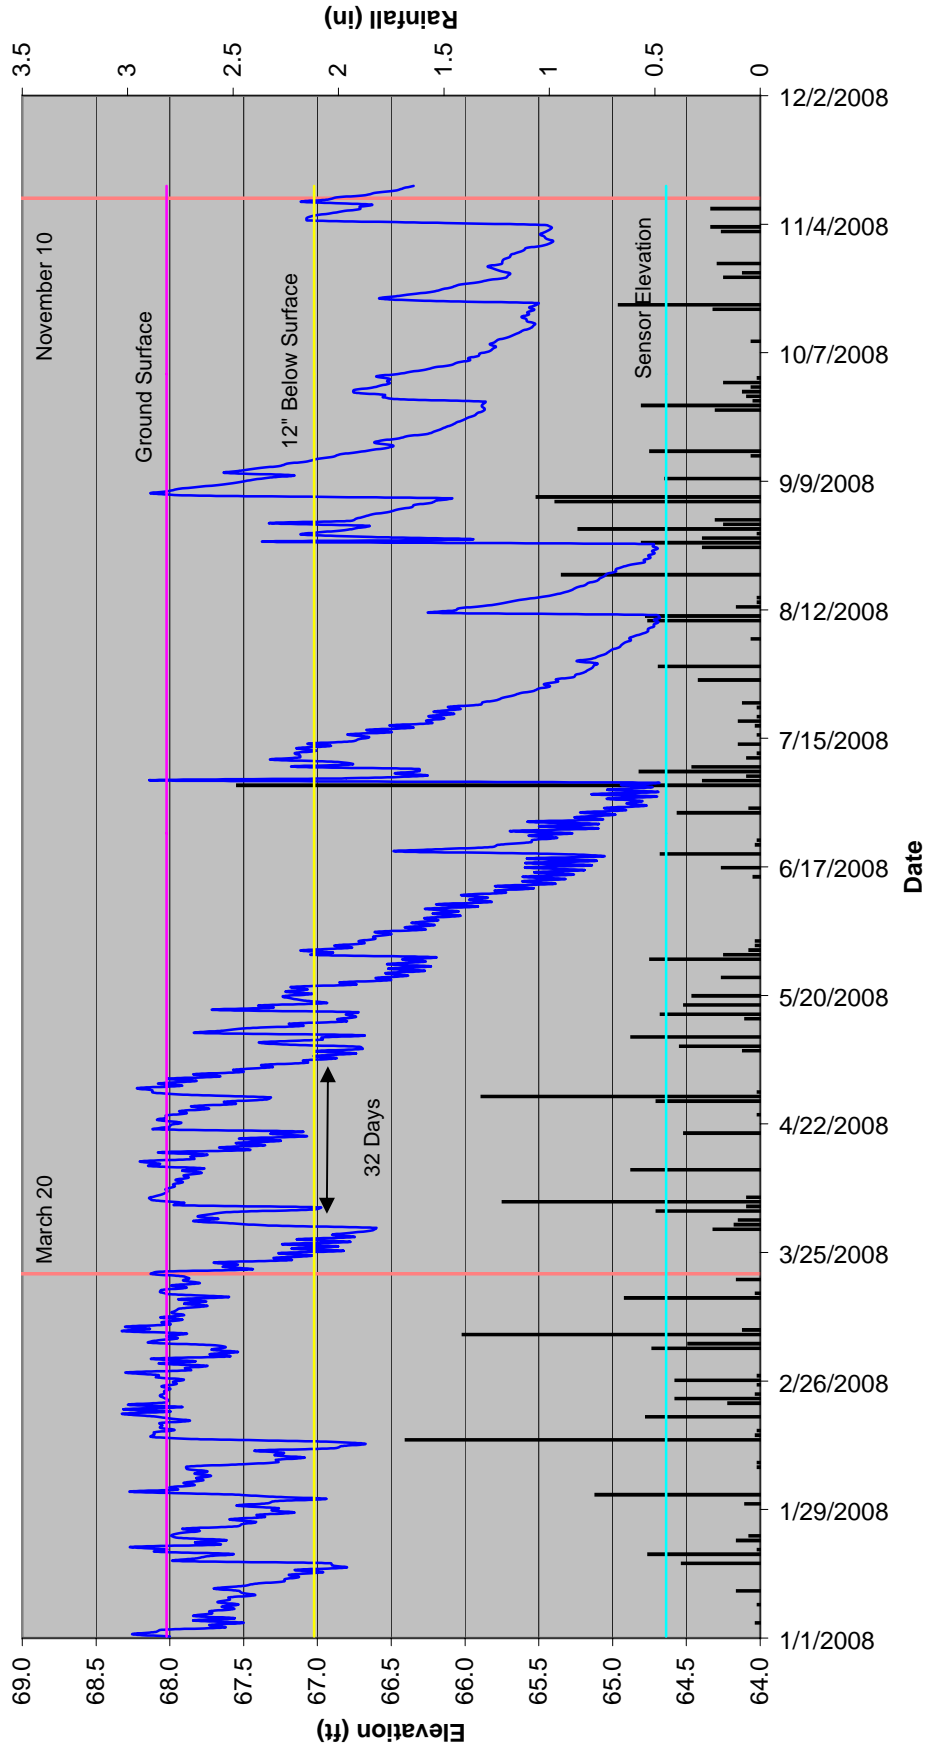


■ Rainfall — Groundwater Elevation

Harrell Farm 30-70 Percentile Graph 2007-2008
 Rocky Mount, NC Monthly Rainfall

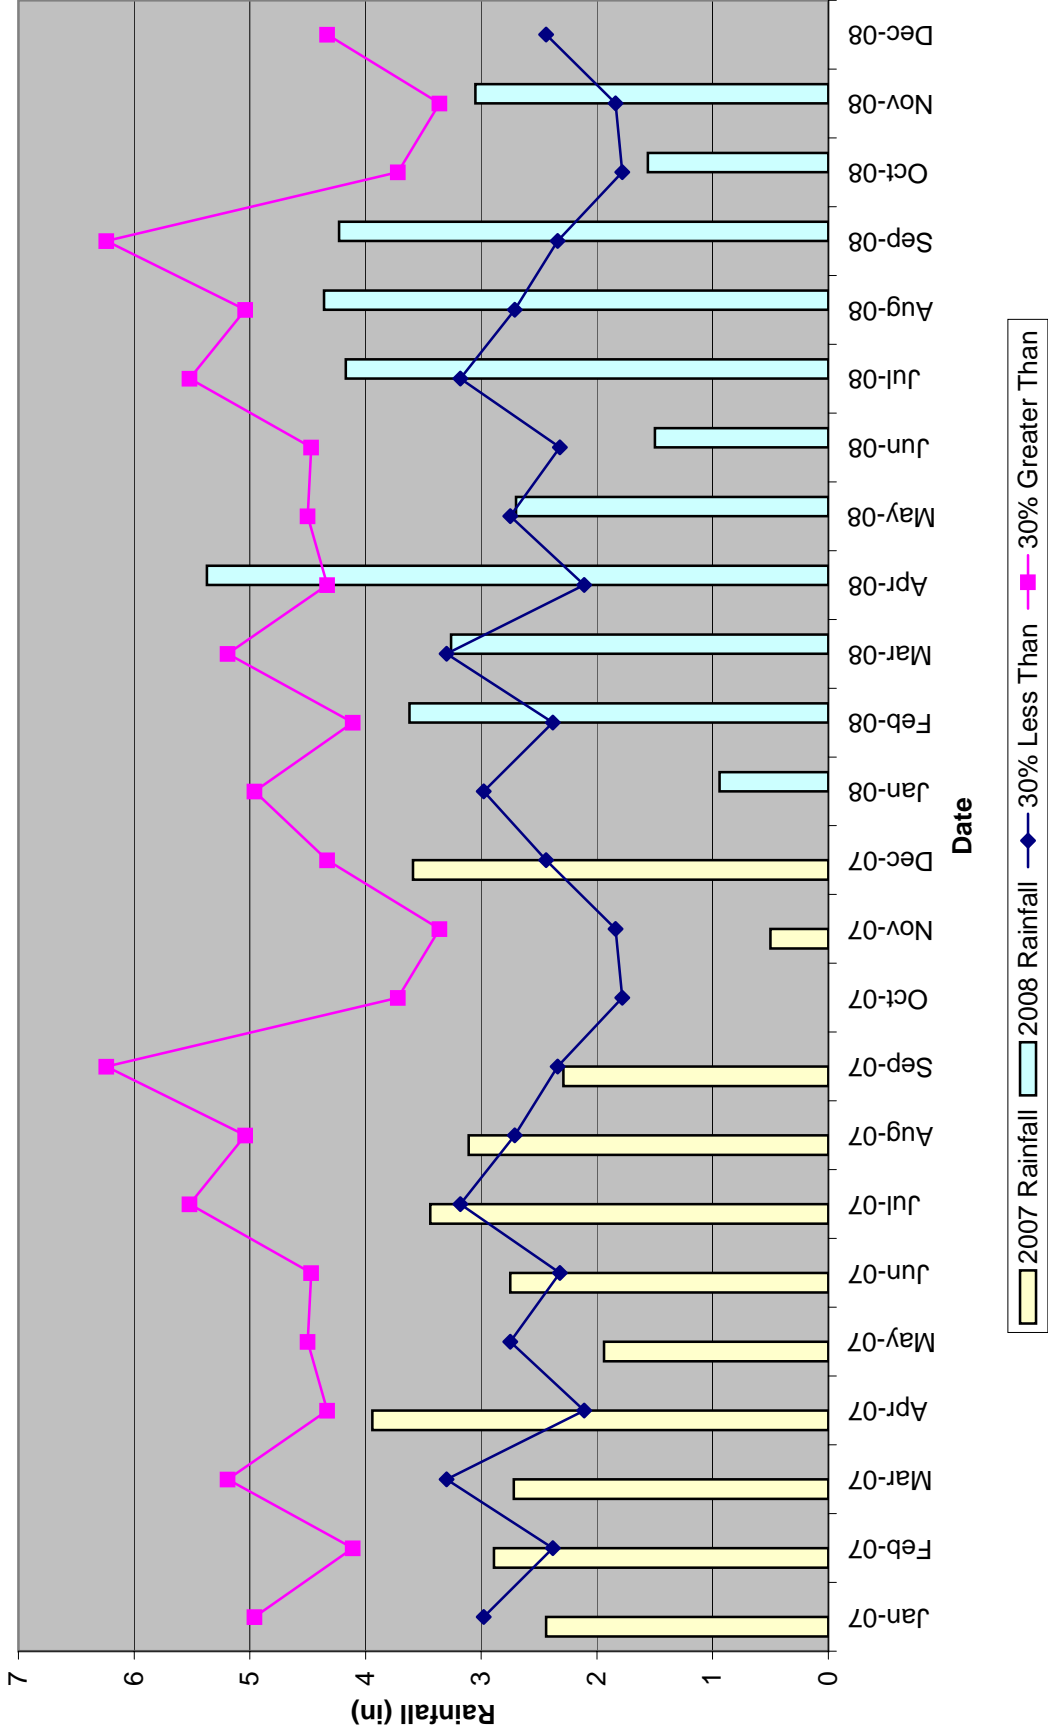

Appendix D
Current Conditions Plan View

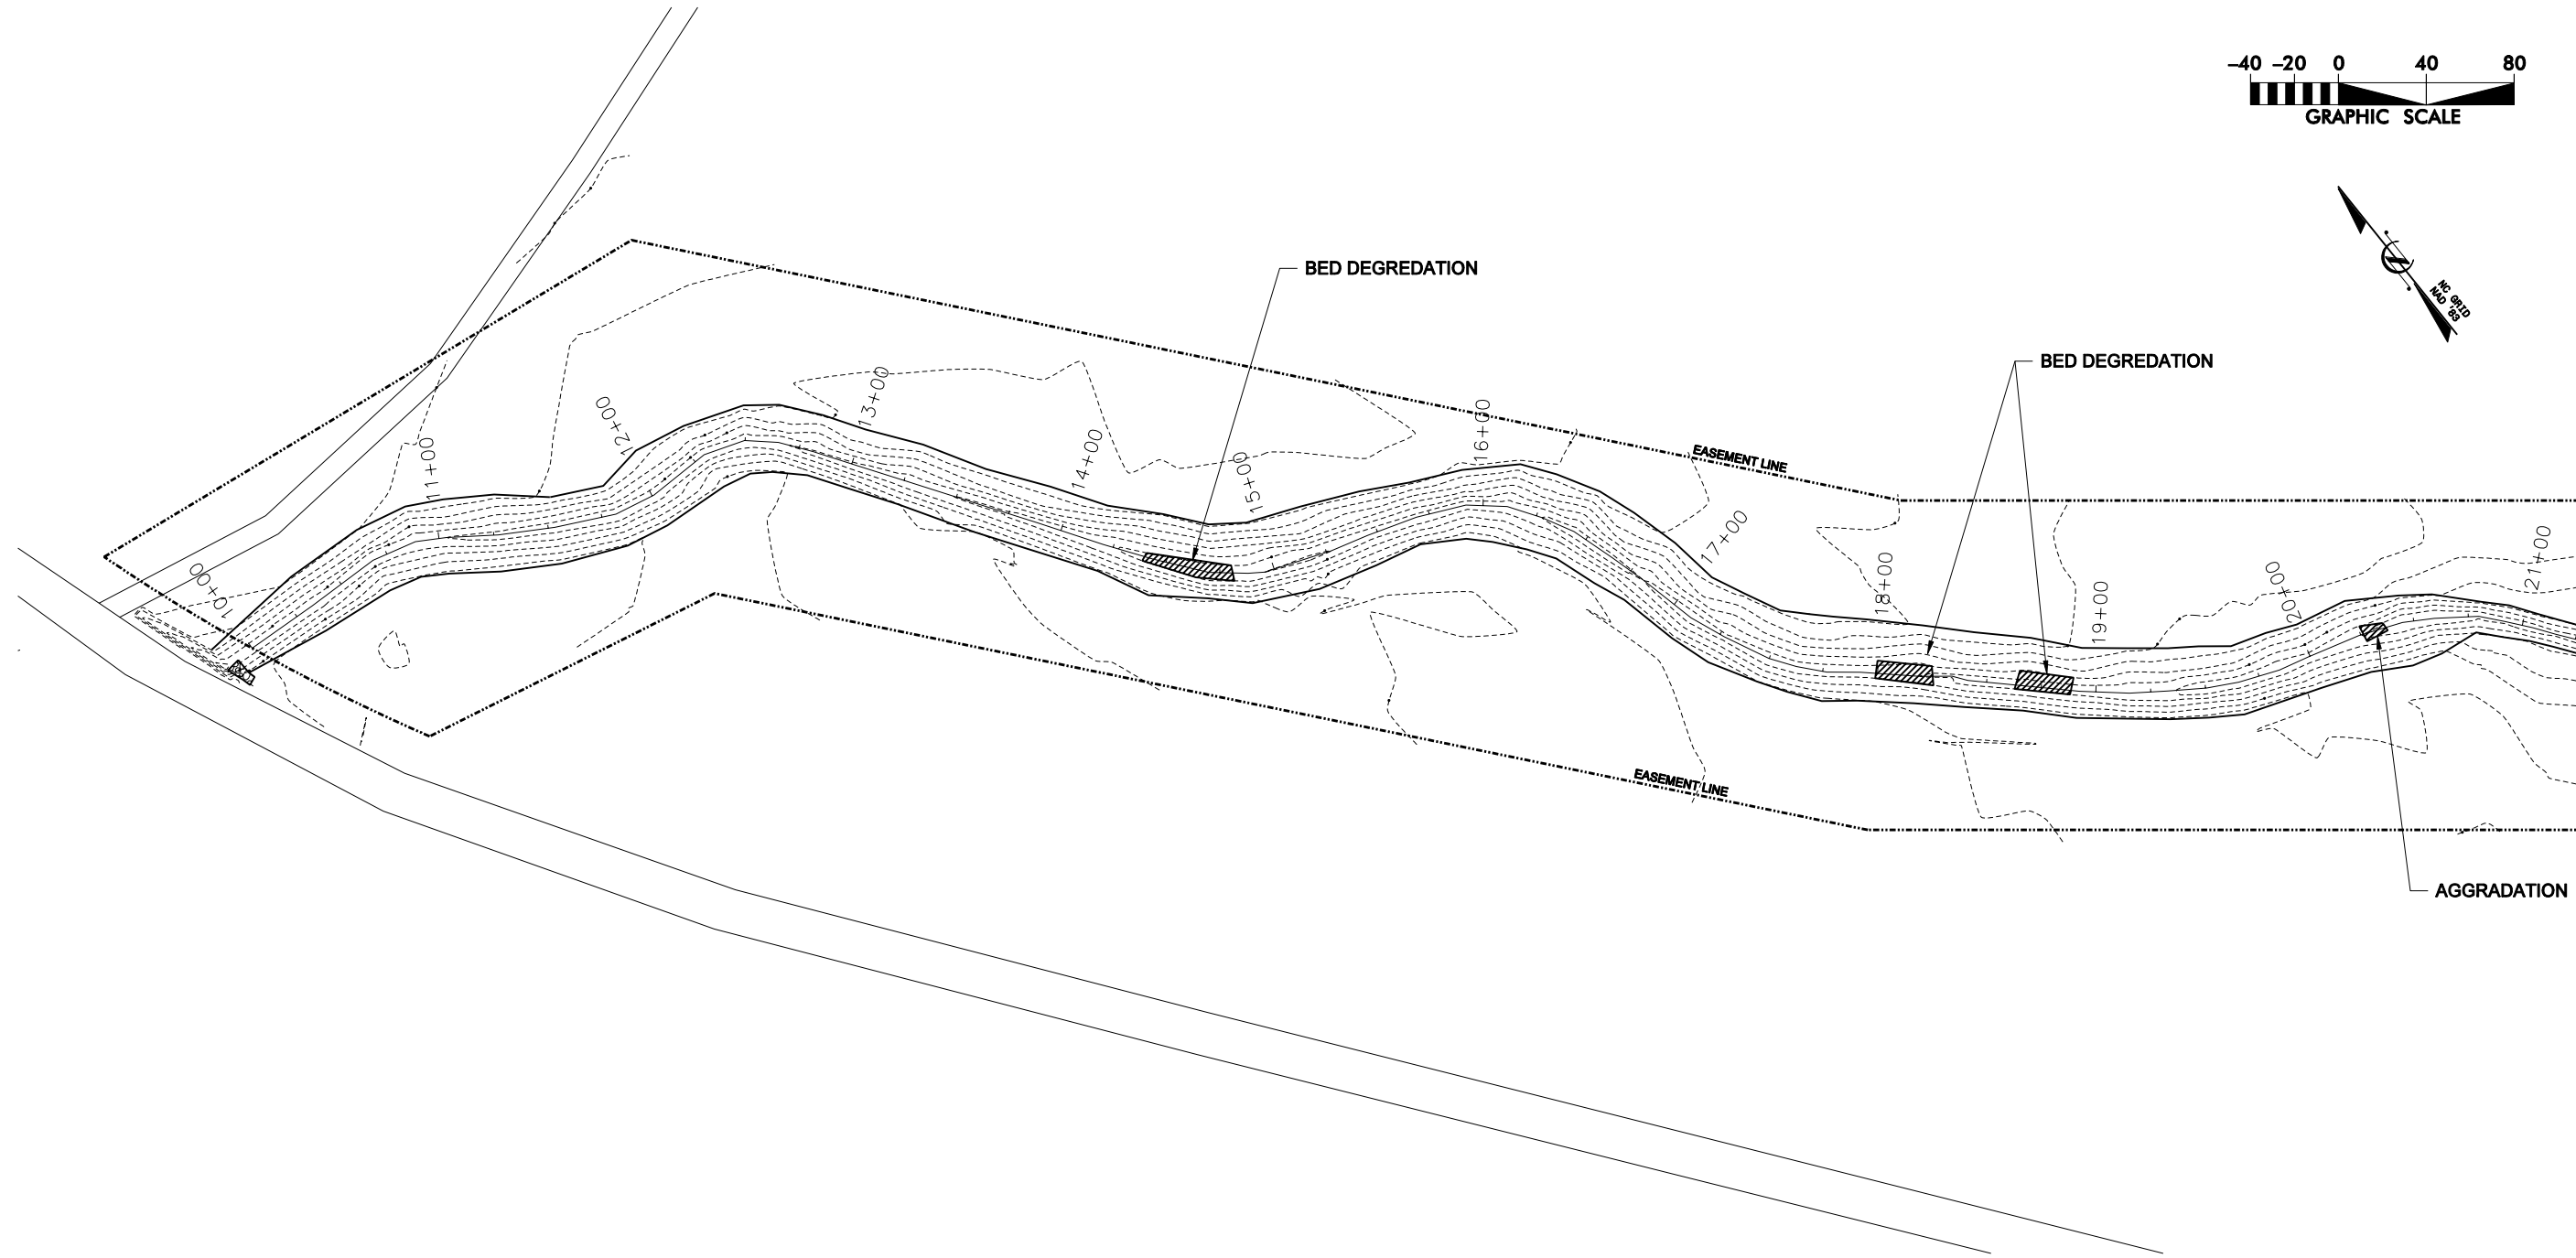

SYMBOL	DESCRIPTION	DATE	APPROVED






KCI
 ASSOCIATES OF, INC.
 ENGINEERS • PLANNERS • SCIENTISTS
 4601 SIX FORKS ROAD
 RALEIGH, NORTH CAROLINA 27609

HARRELL SITE
STREAM AND WETLAND RESTORATION
 EDGECOMBE CO., NORTH CAROLINA
 STATION 10+00 TO STATION 21+29

DATE: NOV 2008
 SCALE: 1"=80'
CURRENT CONDITIONS PLAN VIEW
 SHEET 1 OF 6

MATCHLINE - SEE SHEET 1

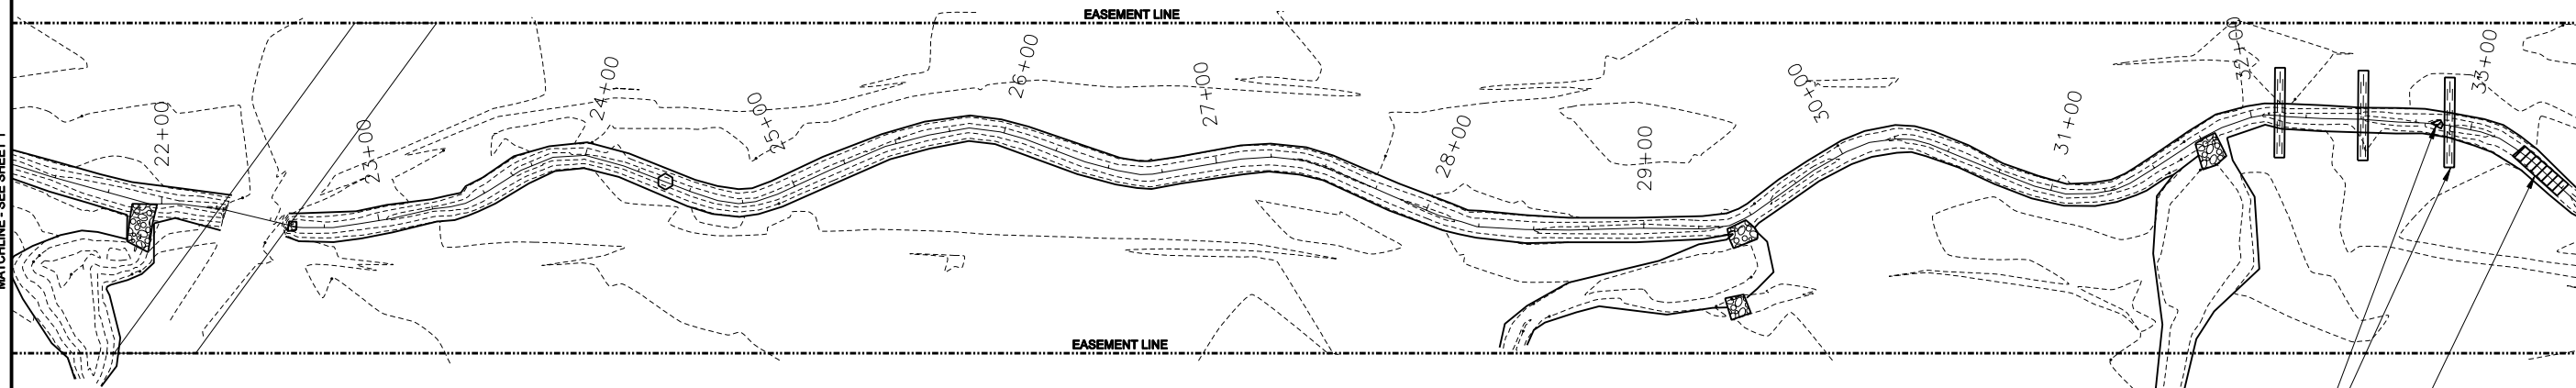

MATCHLINE - SEE SHEET 3




SYMBOL	DESCRIPTION	DATE	APPROVED



KCI
 ASSOCIATES OF NC
 ENGINEERS • PLANNERS • SCIENTISTS
 4601 SIX FORKS ROAD
 RALEIGH, NORTH CAROLINA 27609

**HARRELL SITE
 STREAM AND WETLAND RESTORATION**
 EDGECOMBE CO., NORTH CAROLINA
 STATION 21+29 TO STATION 33+64

DATE: NOV 2008
 SCALE: 1"=80'
**CURRENT
 CONDITIONS
 PLAN VIEW**
 SHEET 2 OF 6

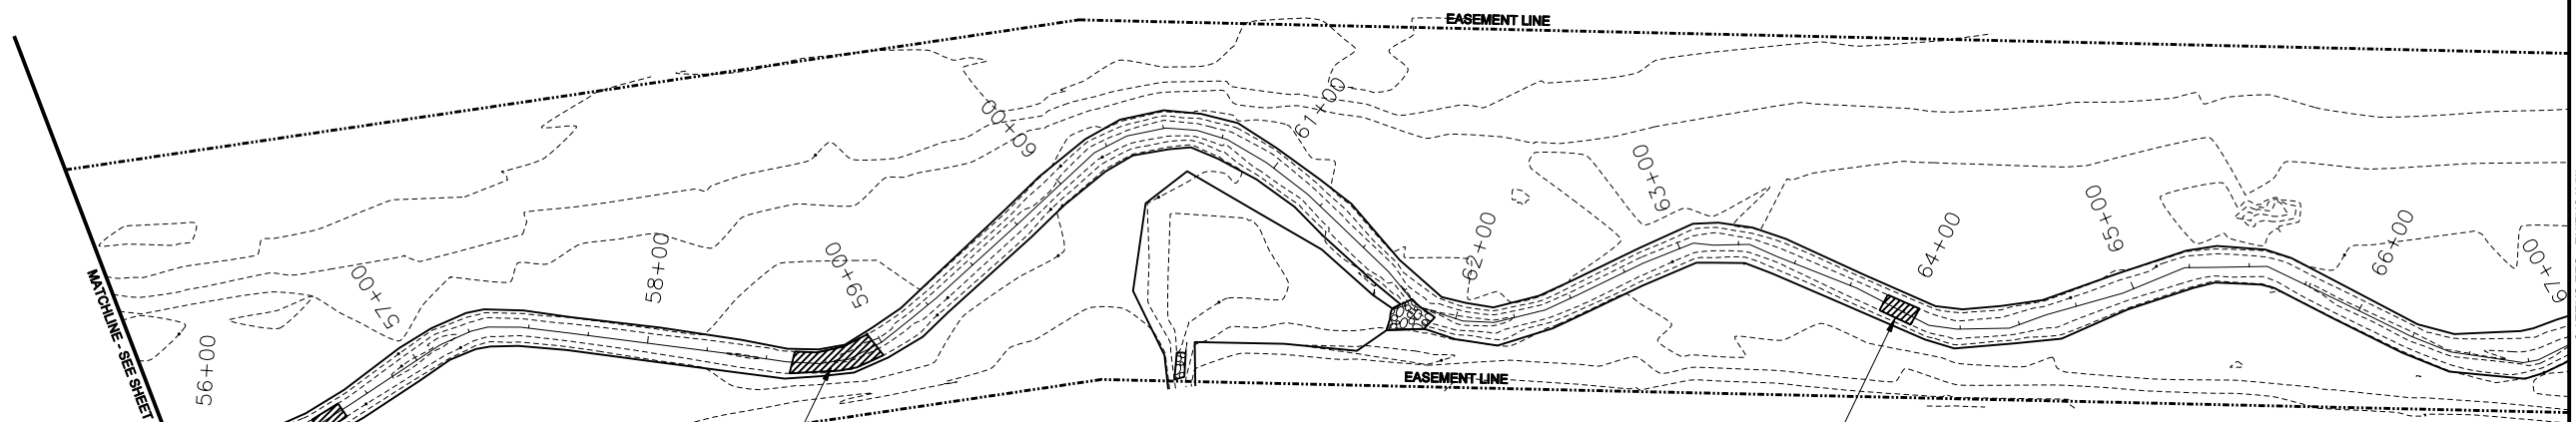

DENSE
VEGETATION
IN CHANNEL

DENSE
VEGETATION
IN CHANNEL


SYL	DESCRIPTION	DATE	APPROVED





KCI
ASSOCIATES OF NC
ENGINEERS • PLANNERS • SCIENTISTS
4601 SIX FORKS ROAD
RALEIGH, NORTH CAROLINA 27609

**HARRELL SITE
STREAM AND WETLAND RESTORATION**
EDGEcombe CO., NORTH CAROLINA
STATION 55+86 TO STATION 66+94

DATE: NOV 2008
SCALE: 1"=80'
**CURRENT
CONDITIONS
PLAN VIEW**
SHEET 5 OF 6

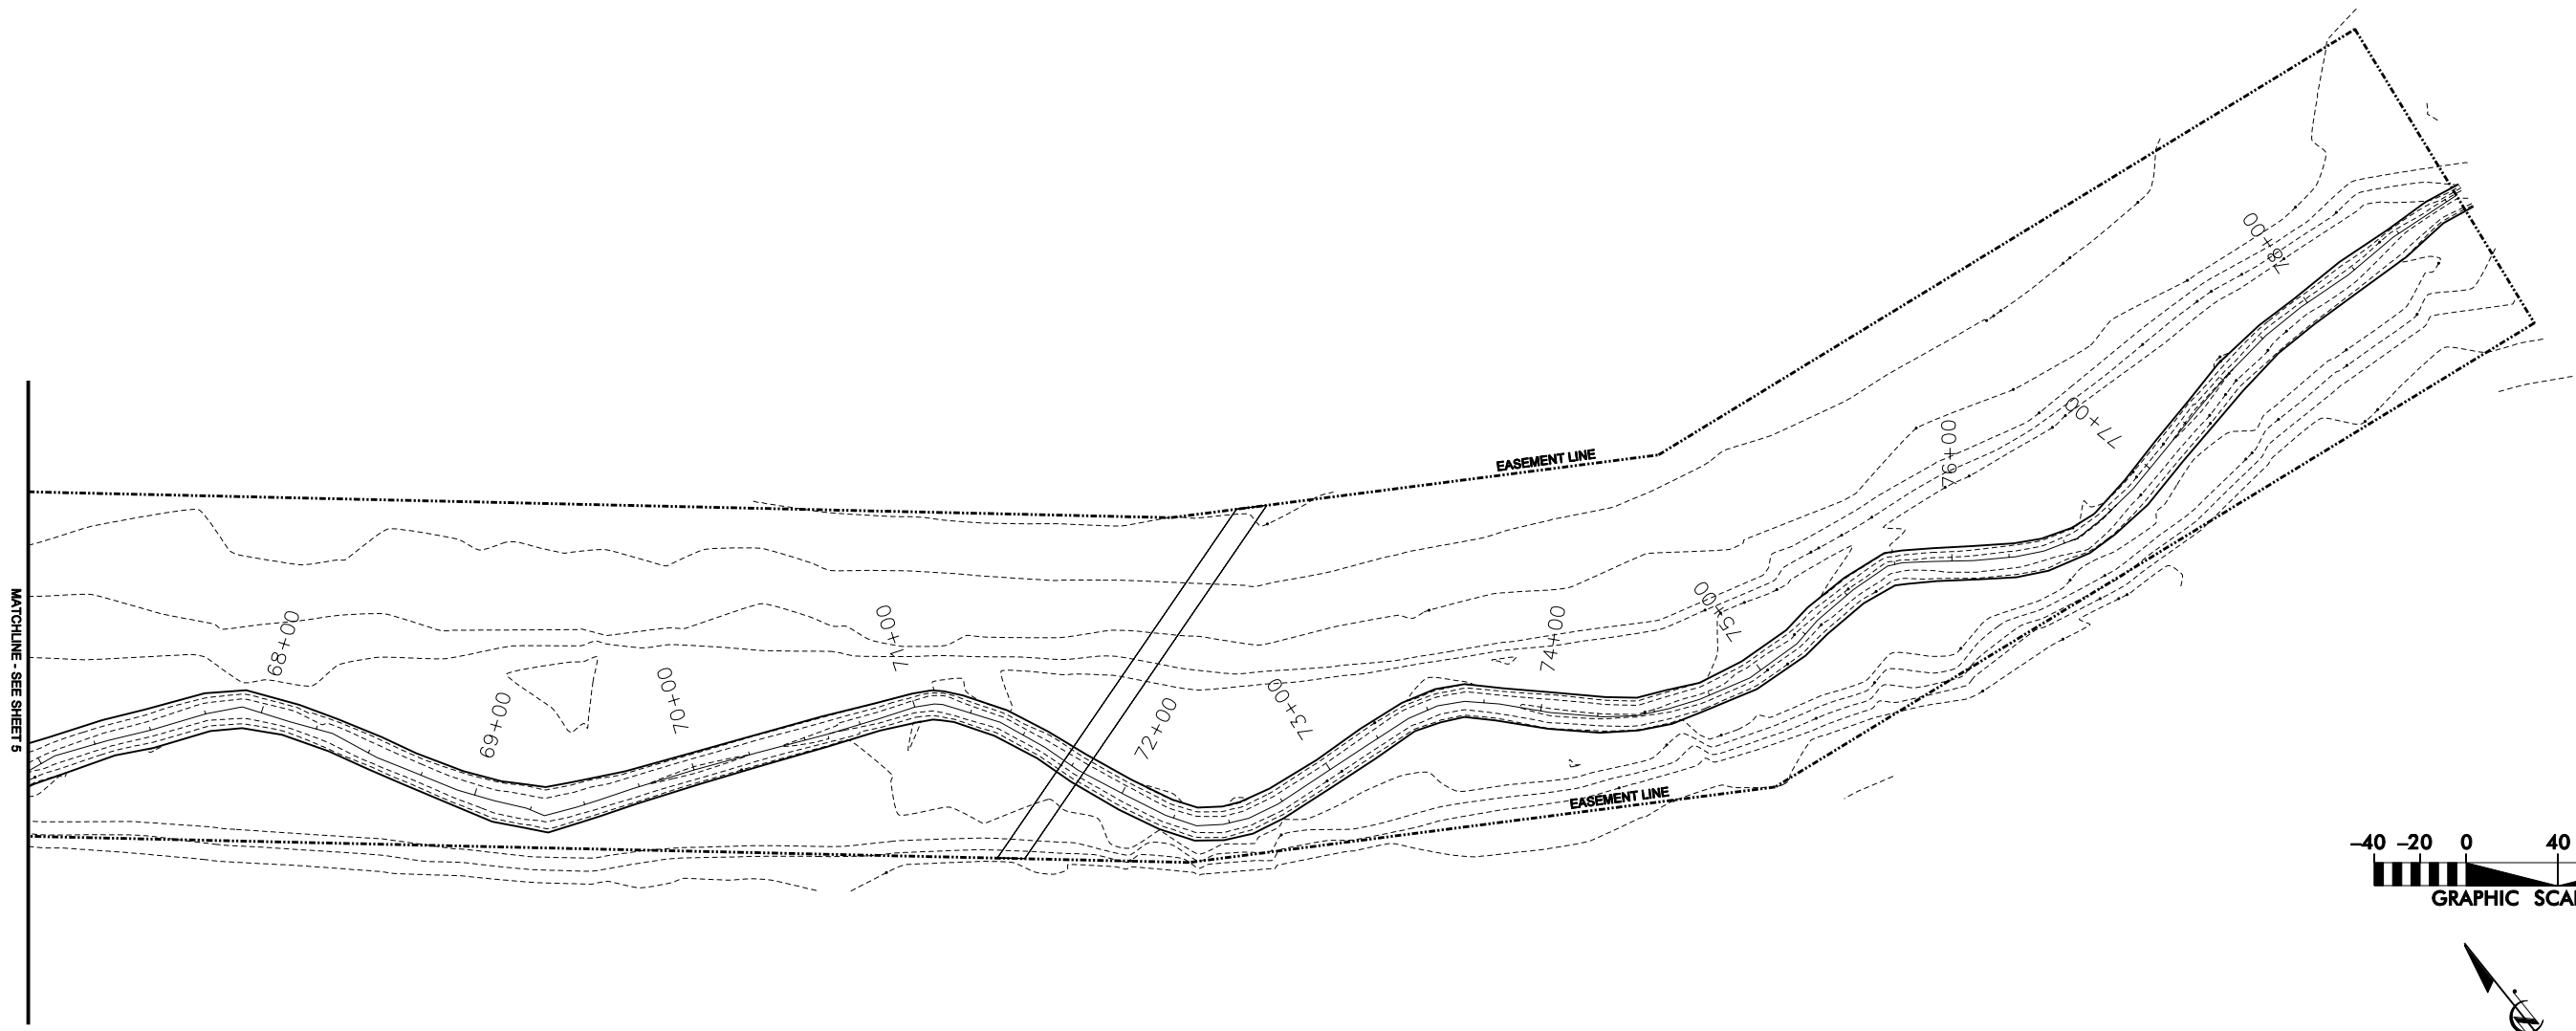

MATCHLINE - SEE SHEET 5



SYL	DESCRIPTION	DATE	APPROVED



KCI
ASSOCIATES OF NC
ENGINEERS • PLANNERS • SCIENTISTS
4601 SIX FORKS ROAD
RALEIGH, NORTH CAROLINA 27609

**HARRELL SITE
STREAM AND WETLAND RESTORATION**
EDGEcombe CO., NORTH CAROLINA
STATION 66+94 TO STATION 76+80

DATE: NOV 2008
SCALE: 1"=80'
**CURRENT
CONDITIONS
PLAN VIEW**
SHEET 6 OF 6
