

**Powell Property Wetland and Stream Mitigation Project  
Bertie County, NC**

**2011 Annual Monitoring Report  
Year 3**



**NCEEP Project Number D06065-B  
Chowan River Basin  
USGS Catalog Unit 03010203**

Submitted to  
NCDENR/Ecosystem Enhancement Program  
2728 Capital Blvd.  
Raleigh, NC 27604

Date: December, 2011

Monitoring:  
**Albemarle Restorations, LLC**  
P. O. Box 176  
Fairfield, NC 27826



## Table of Contents

Executive Summary .....	1
I. Project Background .....	2
1.0 Project Objectives .....	2
2.0 Project Structure, Restoration Type and Approach .....	2
3.0 Location and Setting .....	3
4.0 Project History and Background .....	5
5.0 Monitoring Plan View .....	6
II. Project Condition and Monitoring Results .....	9
1.0 Vegetation Assessment .....	9
1.1 Vegetation Discussion and Problem Areas .....	9
2.0 Wetland Assessment .....	10
2.1 Wetland Discussion and Problem Areas.....	10
2.15 Flow .....	10
2.2 Wetland Problem Areas Plan View (Integrated) .....	14
3.0 Project Success Discussion .....	14
III. Methodology Section .....	15

## List of Tables

Table ES-1. Project Success Summary .....	1
Table I. Project Restoration Components .....	3
Table II. Project Activity and Reporting History .....	5
Table III. Project Contacts .....	5
Table IV. Project Background .....	6
Table V. Species for Each Community Type .....	9
Table VI. Wetland Criteria Attainment by Community Type .....	14
Table C-1 Hydrologic Monitoring Results .....	Appendix A

## List of Figures

Figure 1. Composite Vicinity Map .....	4
Figure 2. Monitoring Plan View: Gauges and Vegetation Plots .....	7
Figure 3. Monitoring Plan View: Soils, Contours and Plant Communities .....	8
Figure F1. Water Flow at Gauges 2, 5 & 9 April .....	12
Figure F2. Water Flow at Gauges 2, 5 & 9 August .....	13
Figure 4. Composite Vegetation and Hydrology Monitoring Results .....	Appendix D

## Appendices

Appendix A	Vegetation Data and Site Photos
Appendix B	Geomorphologic Raw Data – N/A
Appendix C	Hydrologic Data Tables
Appendix D	Composite Vegetation and Hydrology Monitoring Results

## Executive Summary

The Powell Property Wetland and Stream Mitigation Site is a headwater riverine wetland and stream mitigation project located southeast of Powellsville, in Bertie County, North Carolina. It was constructed by Albemarle Restorations, LLC, under contract with EEP to provide 48.4 acres of riverine wetland mitigation credits and 3,310 linear feet of stream mitigation credits in the Chowan River Basin. Construction activities, in accordance with the approved restoration plan, began in June of 2008, and were completed in January of 2009. Planting took place in January of 2009.

Due to unsuccessful hydrology around Gauges 6 and 7 in 2010, subsoiling was done in September of 2010 as a remedial treatment to break up compacted soil and improve hydrology. Afterward, two additional water level monitoring gauges were installed around Gauge 7, bringing the total number of gauges on the project to twelve. They are located at varying elevations throughout the riverine wetland and stream valley areas of the site to measure surface and subsurface water elevations. Two more gauges are located in the headwater stream reference area to monitor flow and water level within the reference stream system. All twelve gauges on the project site indicated successful wetland hydrology for a minimum of 5% of the growing season. All but one gauge measured a hydroperiod of 8% or greater. Two separate flow events were documented during 2011.

A total of ten vegetation monitoring plots are located on the site, seven in the riverine wetland areas and three more situated to monitor the swamp run vegetation. One plot is entirely within the boundaries of the swamp run and two more are located so as to share both land forms. Each plot is a 10m X 10m square, as recommended by the CVS-EEP protocol for recording vegetation sampling. All ten plots met the third year survival success criterion which is a minimum of 320 stems per acre.

Table ES-1 shows the levels of success attained by each of the water level monitoring gauges and the vegetation plots. The success criterion for hydrology is maintained groundwater levels within 12 inches of the soil surface for 5% to 8% of the growing season (12 to 19 consecutive days). Table C-1 in Appendix C has a detailed breakdown of hydrologic success.

**Table ES-1. Project Success Summary**

Gauges show longest hydroperiod as % of growing season, Plots show Stems per Acre													Percent Success	
Success		1	2	3	4	5	6	7	7A	7B	8	9		10
Year 1 2009	Gauges %	6	15	6	2	15	2	3	Not Installed		39	24	14	70%
	Plot SPA	577	412	495	454	412	371	371			701	454	454	100%
Year 2 2010	Gauges %	8	11	7	6	15	3	2			16	17	12	80%
	Plot SPA	526	364	405	445	405	405	324			647	364	405	100%
Year 3 2011	Gauges %	13	26	26	9	26	26	8	6	8	26	26	21	100%
	Plot SPA	495	330	330	371	495	371	330	No Plot		577	371	454	100%
Year 4 2012	Gauges %								No Plot					
	Plot SPA								No Plot					
Year 5 2013	Gauges %								No Plot					
	Plot SPA								No Plot					

Gauge values shown in red did not meet minimum of 5% of the growing season

## **I. Project Background**

### **1.0 Project Objectives**

The goal of the Powell Property Mitigation Project was to create a riverine wetland system typically found in the middle to upper reaches of first or zero order tributary systems. The project is to serve as compensation for wetland loss in the Chowan River Basin. The restoration plan was developed and implemented to eliminate pattern drainage and restore topography and hydrology that more closely resembled that of similar undisturbed land. Construction resulted in the development of a broad, branched, frequently flooded swamp run following a historical path as evidenced by archived aerial photographs and signature topography. Subsequent planting was designed to restore a wetland forest ecosystem that is typically found in the immediate area characteristic of similar soils, topography and hydrology.

Ecological benefits of the restored riparian headwater system and its associated riverine wetlands are the following:

1. Water quality improvements, including nutrient, toxicant and sediment retention and reduction, increasing dissolved oxygen levels, as well as reducing excessive algae growth, and reducing surface water temperatures in receiving waters by providing permanent shading in the form of a shrub/scrub and forested headwater wetland system.
2. Wildlife habitat enhancement by adding to the existing adjacent forested areas creating a continuous travel corridor between habitat blocks and providing a wide range of habitat areas (open water, emergent, shrub/scrub and forested) for amphibians, reptiles, birds, insects and mammals.
3. Flood flow attenuation during storm events which reduces sedimentation and erosion downstream, and improves long term water quality within the Chowan River.
4. Passive outdoor recreation and educational opportunities for the landowner and the surrounding community.

### **2.0 Project Structure, Restoration Type, and Approach**

Table I lists the estimated wetland acreage to be restored on the Powell Property. The mitigation plan provides for the restoration of 48.4 acres of riverine wetlands and 3,310 linear feet of stream (swamp run) restoration. Prior to construction, the easement area was used entirely for row crop agriculture, primarily soy beans, corn, cotton and tobacco. The agricultural fields were drained by several ditches that traversed the site and one main drainage ditch that emptied into Quioccosin Swamp. Construction was done in accordance with the approved restoration plan and completed in January of 2009. Native tree and shrub species were planted in January of 2009 and the resulting riverine system is designed to emulate natural swamp run systems found within the Chowan River Basin.




<b>Table I. Project Restoration Components</b>				
<b>Powell Wetland and Stream Mitigation Site/EEP #D06065-B</b>				
<b>Restoration Type</b>	<b>Pre-Existing Acres/Linear Feet</b>	<b>Post Construction Acres/ Linear Feet</b>	<b>Credit Ratio (Restoration : WMU)</b>	<b>Total WMU's/SMU's</b>
Riverine Wetland	0.0 acres	48.4 acres	1:1	48.4 WMUs
Stream (Swamp Run)	0.0 linear feet	3,310 linear feet	1:1	3,310 SMUs

### **3.0 Location and Setting**

The Powell Property Mitigation Site is located in Bertie County, just north of Buzzard's Crossroads on Meadow Road (approximately 4.6 miles southeast of Powellsville). The easement area is situated on the eastern portion of the Powell farm and adds contiguous swamp run and forested wetlands to Quioccosin Swamp which flows to the Wiccacon River, a tributary of the Chowan River. The surrounding area is primarily forest and agricultural land with residential properties as a minor component.

Figure 1 is a location map for the project site. Directions to the site are as follows: from Powellsville (Hwy. 42), travel south on Sally Freeman Rd., turn left on Dilday Rd., right on Luther Brown Rd., then right on Meadow Rd. Access to the site is approximately 2 miles from this intersection, on the right.

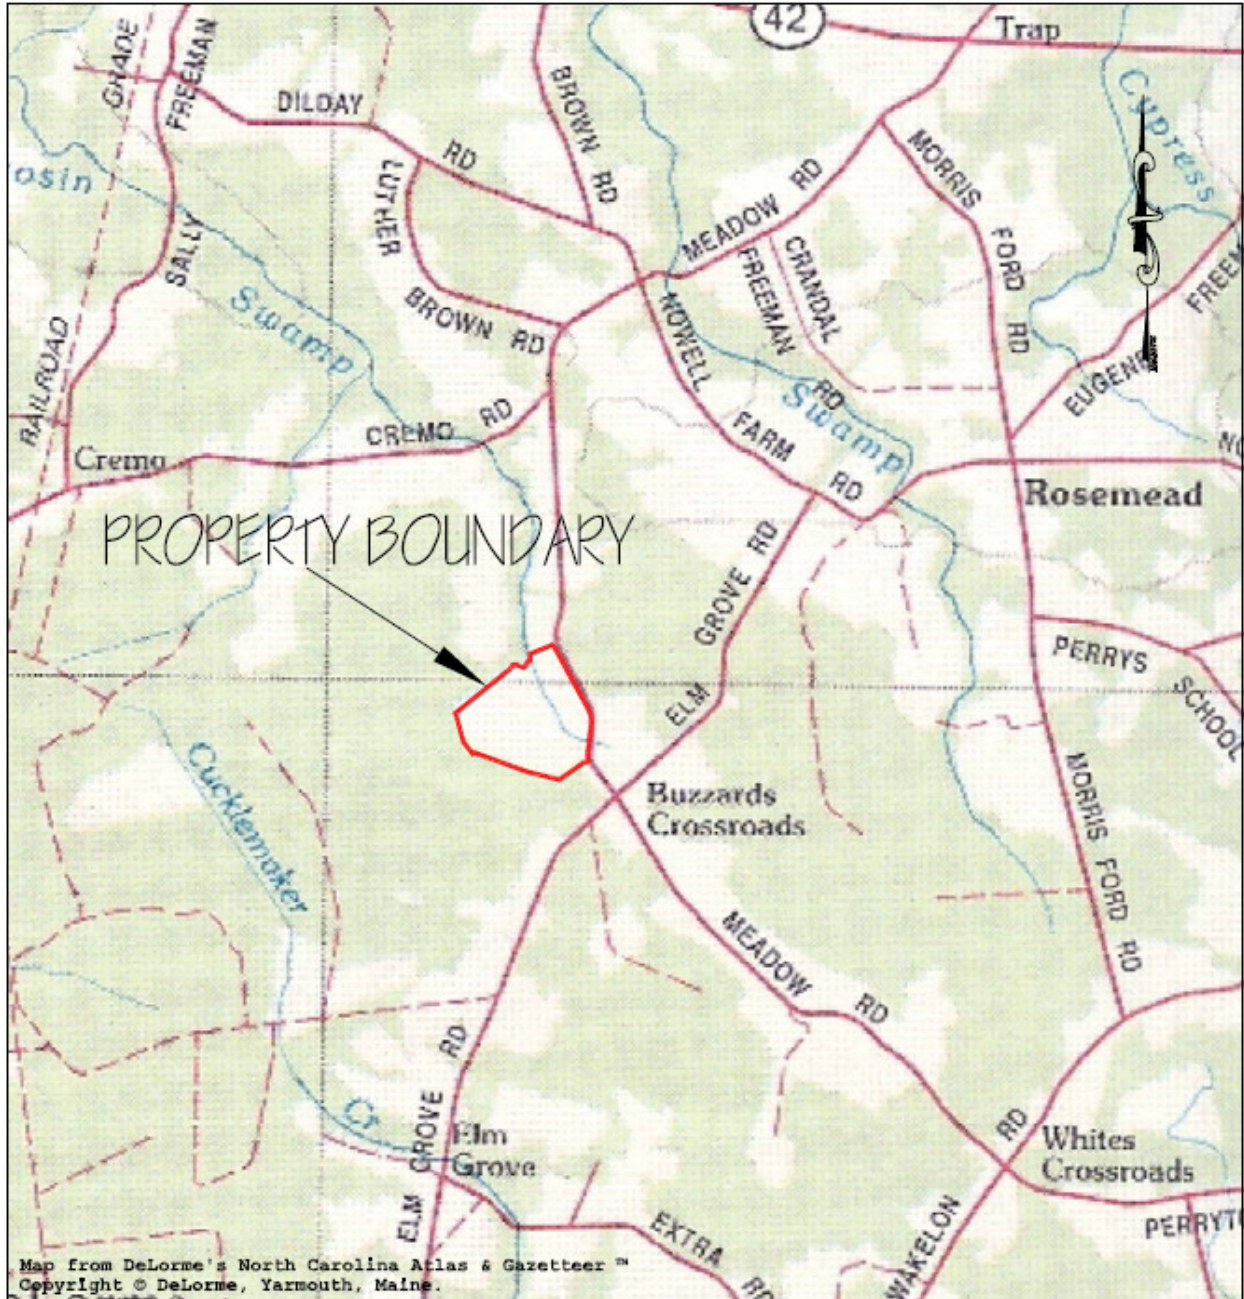

<b>VICINITY MAP</b>			<b>POWELL PROPERTY</b> RIVERINE WETLAND RESTORATION 48.4 ACRES (48.4 WMU'S)  STREAM RESTORATION 3,310 LINEAR FEET (3,310 SMU'S)  BERTIE COUNTY, NORTH CAROLINA CONTRACT # 16-006065-3
Scale: 1" = 4000'	4/2008	Drawn By: LMS	
PREPARED FOR <b>ALBEMARLE RESTORATIONS, LLC</b> WETLAND RESTORATION, STREAM RESTORATION, & WILDLIFE HABITAT CREATION 404 COURT STREET • GATESVILLE, NC 27638 (252) 333-0248 • FAX (252) 367-4892		<b>SCALE</b> 	

#### 4.0 Project History and Background

Table II provides the history of data collection and actual completion of various milestones of the Powell Property Wetland Mitigation Site.

<b>Table II. Project Activity and Reporting History Powell Wetland and Stream Mitigation Project/EEP #D06065-B</b>		
<b>Activity or Report</b>	<b>Data Collection Complete</b>	<b>Actual Completion or Delivery</b>
Restoration Plan	January 2008	May 2008
Final Design -90%	January 2008	May 2008
Construction	N/A	January 2009
Temporary S & E mix applied to entire project area	N/A	January 2009
Permanent seed mix applied to entire project area	N/A	January 2009
Containerized and Bare Root Planting	N/A	January 2009
Mitigation Plan/As-built	April 2009	June 2009
Year 1 monitoring	September 2009	March 2010
Year 2 monitoring	August 2010	August 2010
Year 3 monitoring	September 2011	December 2011
Year 4 monitoring		
Year 5 monitoring		

Points of contact for the various phases of the Powell Project are provided in Table III.

<b>Table III. Project Contacts Powell Wetland and Stream Mitigation Site/EEP #D06065-B</b>	
<b>Designer</b> Primary Project design POC	Ecotone, Inc. (Scott McGill 410-692-7500) 1204 Baldwin Mill Road Jarrettsville, MD 21804
<b>Construction Contractor</b> Construction contractor POC	Armstrong, Inc. (Tink Armstrong 252-943-2082) P. O. Box 96 25852 US Hwy 64 Pantego, NC 27860
<b>Planting Contractor</b> Planting contractor POC	Carolina Silvics, Inc. 908 Indian Trail Road Edenton, NC 27932 Mary-Margaret McKinney (252-482-8491)
<b>Seeding Contractor</b> Seed planting contractor POC	Armstrong, Inc. (Tink Armstrong 252-943-2082) P. O. Box 96 25852 US Hwy 64 Pantego, NC 27860
Seed mix sources	Ernst Conservation Seeds, LLP, Meadville, PA
Nursery stock suppliers	Arborgen, Blenheim, SC, Native Roots, Clinton, NC
<b>Monitoring Performers</b> Wetland and Vegetation POC	Woods, Water and Wildlife, Inc. (Ashby Brown 757-651-3162) P. O. Box 176 Fairfield, NC 27826

Project background information for the Powell project is provided in Table IV.

<b>Table IV. Project Background Powell Wetland and Stream Mitigation Site/EEP #D06065-B</b>	
Project County	Bertie County
Drainage Area	Approximately 871 Acres
Drainage impervious cover estimate (%)	0
Physiographic Region	Coastal Plain
Ecoregion	8.3.5 Southeastern Plains
Rosgen Classification of As-built	N/A
Cowardin Classification	PSS, PFO
Dominant Soil Types	Goldsboro, Lynchburg
Reference site ID	Quioccosin Swamp
USGS HUC for Project and Reference	03010203
NCDWQ Sub-basin for Project and Reference	03-01-01
NCDWQ classification for Project and Reference	C
Any portion of any project segment 303d listed?	No
Any portion of any project segment upstream of a 303d listed segment?	Yes, Wiccacon River
Reasons for 303d listing or stressor?	Non-Point Source
% of project easement fenced	None


## **5.0 Monitoring Plan View**

A total of twelve water level monitoring gauges are installed across the site. These gauges are suspended in two-inch pvc pipe that is set from two to four feet vertically in the ground. The gauges have been located to assess the groundwater levels throughout the year at various elevations and topographies within the site. Two more gauges are installed in an offsite riverine wetland area to serve as references for a naturally functioning riverine wetland and headwater swamp run. In addition, there is a rain gauge onsite to capture and record precipitation.

Vegetation monitoring is accomplished by surveying the ten permanent sampling plots. The plots are ten meters square and are situated to give an accurate sample of the planted and natural woody vegetation in both the riverine and swamp run communities. For each site, the data recorded matches that required of the *CVS-EEP Protocol for Recording Vegetation, v 4.0, 2006*, level 1-2.

Figures 2 and 3 provide plan views of the site showing the location of all monitoring features including gauges, sampling plots and the rain gauge as well as the vegetative communities.



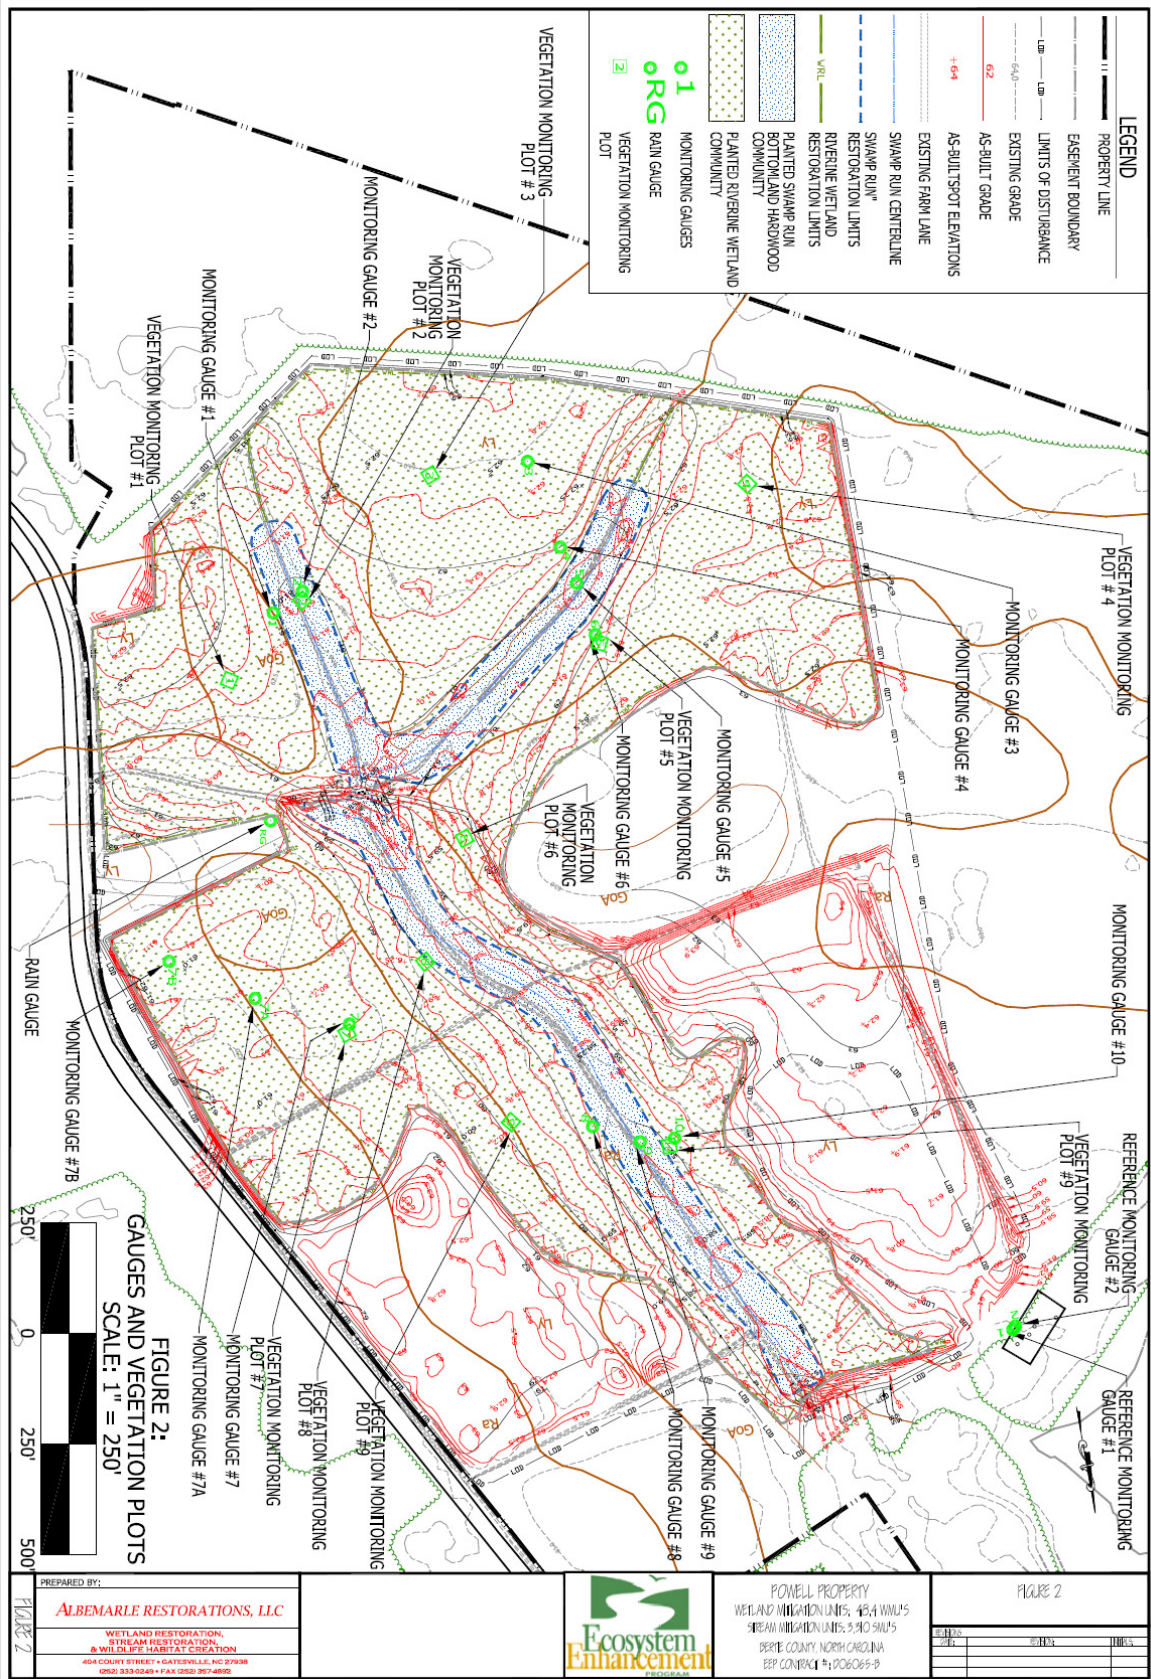





## II. Project Condition and Monitoring Results

### 1.0 Vegetation Assessment

The vegetation success criterion was developed in accordance with the CVS-EEP protocol. The Powell project was designed to include both riverine and bottomland hardwood plant communities. The project was planted with a mixture of tree and shrub species that would resemble that of naturally occurring swamp runs and adjacent riverine wetlands in the local area. The run and area immediately adjacent were planted heavily with cypress, willow and tupelo. The riverine wetland zone beyond the swamp run is populated by a broader mix of native hydrophytic tree and shrub species. The species mix was based on the vegetation noted at the reference site and all species are classified from FAC to OBL (Table V). The site was planted at a rate of 600 stems per acre in January of 2009.

<b>Table V. Species by Community Type</b> <b>Powell Wetland and Stream Mitigation Project/EEP #D06065-B</b> <b>Total Forested Wetland 55.9 Acres</b>		
Common Name	Scientific Name	Wetland Indicator Status
<b>Trees</b>		
Bald Cypress	Taxodium distichum	OBL
Water tupelo	Nyssa aquatica	OBL
Swamp Black Gum	Nyssa biflora	FAC
Willow Oak	Quercus phellos	FACW-
Swamp White Oak	Quercus bicolor	FACW+
Pin Oak	Quercus palustris	FACW
Water Oak	Quercus nigra	FAC
Swamp Chestnut Oak	Quercus michauxii	FACW-
<b>Shrubs</b>		
Staggerbush	Lyonia mariana	FAC
Tag Alder	Alnus serrulata	FACW+
Highbush Blueberry	Vaccinium corymbosum	FACW
Sweet Pepperbush	Clethra alnifolia	FACW
Virginia Sweetspire	Itea virginica	FACW+
Button Bush	Cephalanthus occidentalis	OBL
Swamp Bay	Persea palustris	FACW
Inkberry	Ilex glabra	FACW
Wax Myrtle	Myrica cerifera	FAC+
Black Willow	Salix nigra	OBL
Sweetbay Magnolia	Magnolia virginiana	FACW+

### 1.1 Vegetation Discussion and Problem Areas

All ten plots met the Year 3 success criterion of a minimum of 320 stems per acre. Over the entire project, the survival rate averaged 412 live stems per acre. Annual mortality continues to be light; the survival rate in 2010 averaged 429 stems per acre. Growth is very good as well as is the overall health of the forested community.

## **2.0 Wetland Assessment**

The hydrologic success criterion for any gauge is to achieve a minimum of 12 to 19 consecutive days where the groundwater level is within 12 inches of the soil surface during the growing season. This represents 5% to 8% of the growing season which for this site runs from March 22 to November 8, a period of 231 days (WETS Table for Lewiston, NC). All but one gauge, 7A, measured an 8% or longer hydroperiod during the year. Gauge 7A measured a 6% hydroperiod.

Because of inadequate hydroperiods around Gauges 6 and 7 in 2009 and 2010, those areas of the project were subsoiled in September of 2010 and replanted in January of 2011. Refer to Figure 4 in Appendix D for the location and extent of the subsoiling. To further identify the extent of the potential hydrology problems around Gauge 7, two additional gauges were installed in that area of the project. Refer to Figure 2 on page 7 for the locations of Gauges 7A and 7B. Gauges 7 and 7B, which is the farthest from the swamp run, measured a hydroperiod of 8% or greater. Gauge 7A, which is situated between them, measured a 6% hydroperiod. Gauge 6 measured a 26% hydroperiod.

## **2.1 Wetland Discussion and Problem Areas**

Rainfall for the first seven months of the year approximated normal rainfall patterns with only minor deficits recorded for a few of those months. As a result, all twelve monitoring gauges measured a significant hydroperiod in April of 2011. Near the end of September Hurricane Irene produced heavy rainfall that successfully recharged the watershed and produced another significant hydroperiod.

The subsoiling done in September of 2010 appears to have corrected the hydrologic problems around Gauges 6 and 7. Gauge 6 showed a remarkable improvement over the previous two years, measuring a 26% hydroperiod. Gauges 7A and 7B were added at the suggestion of EEP in order to further identify the extent of the unsuccessful hydrology in the portion of the project around Gauge 7. It appears that the subsoiling was successful in correcting the compacted soils. Gauge 7B which is nearest to the project boundary measured a 20-day hydroperiod in April when rainfall was near normal with only a minor deficit (.51" cumulative). That corresponds to an 8.6% hydroperiod which would suggest that under normal rainfall conditions, this area of the project will show successful hydrology.

### **2.15 Flow**


Refer to Figures F1 and F2 which are composite charts for Gauges 2, 5 & 9, for the following discussion of evidence of flow within the swamp runs. Figure F1 is a composite chart showing a period of flow in April, 2011 when the water level at Gauge 9 hit a maximum height of .61 feet above ground level which is a little more than 7 inches. Gauges 2 and 5 each measured water at approximately 3 inches above ground level. Flow on April 1, 2011 is video documented and correlates well to the data shown in Figure 1. This was a relatively minor flow event but prior to April, rainfall had been light and the reference area had very little water moving through it (refer to the photo in Appendix A).




Figure F2 is a composite chart showing flow in late August, 2011 after Hurricane Irene produced enough rainfall to recharge the watershed. As can be seen on the hydrographs, prior to that storm, the site was in a very dry summer condition. Water levels at Gauge 9 (farthest downstream) reached a maximum of 2.09 feet above ground level as a result of the storm. This event produced flow through the entire project and over the entire length of both branches at the upstream end of the project. Video evidence confirms this.

By comparison, Reference Gauge 11, which is in the center of the reference swamp run, showed water levels above ground that were similar to those at Gauge 9 during these two flow events, and the duration of flow at the reference gauge was nearly the same as on the project site. The data from Gauges 2, 5 and 9, taken in their entirety, show evidence of water flowing through the entire project. As a result, the Powell project serves as a fully functioning connector in the Quioccosin Swamp watershed.

**Figure F1.  
Monitoring Gauges 2, 5 & 9  
Indicating Flow in April, 2011**

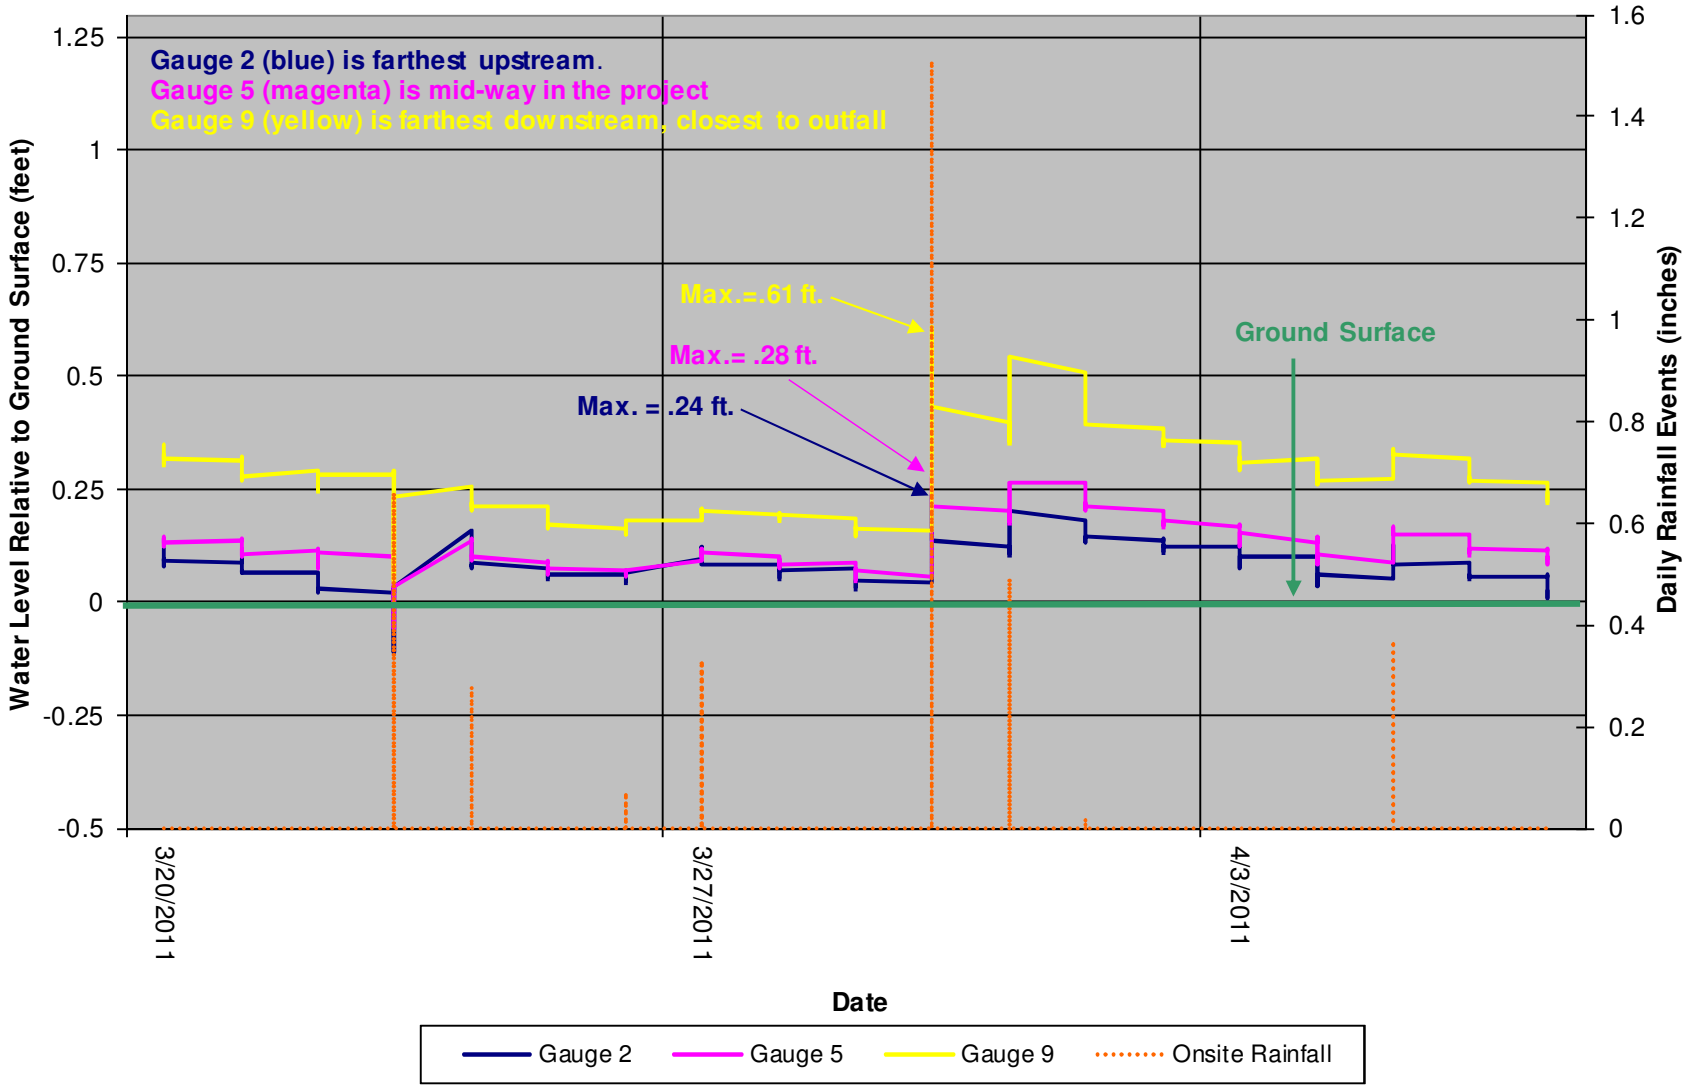

**Figure F2.  
Monitoring Gauges 2, 5 and 9  
Indicating Flow in August, 2011**

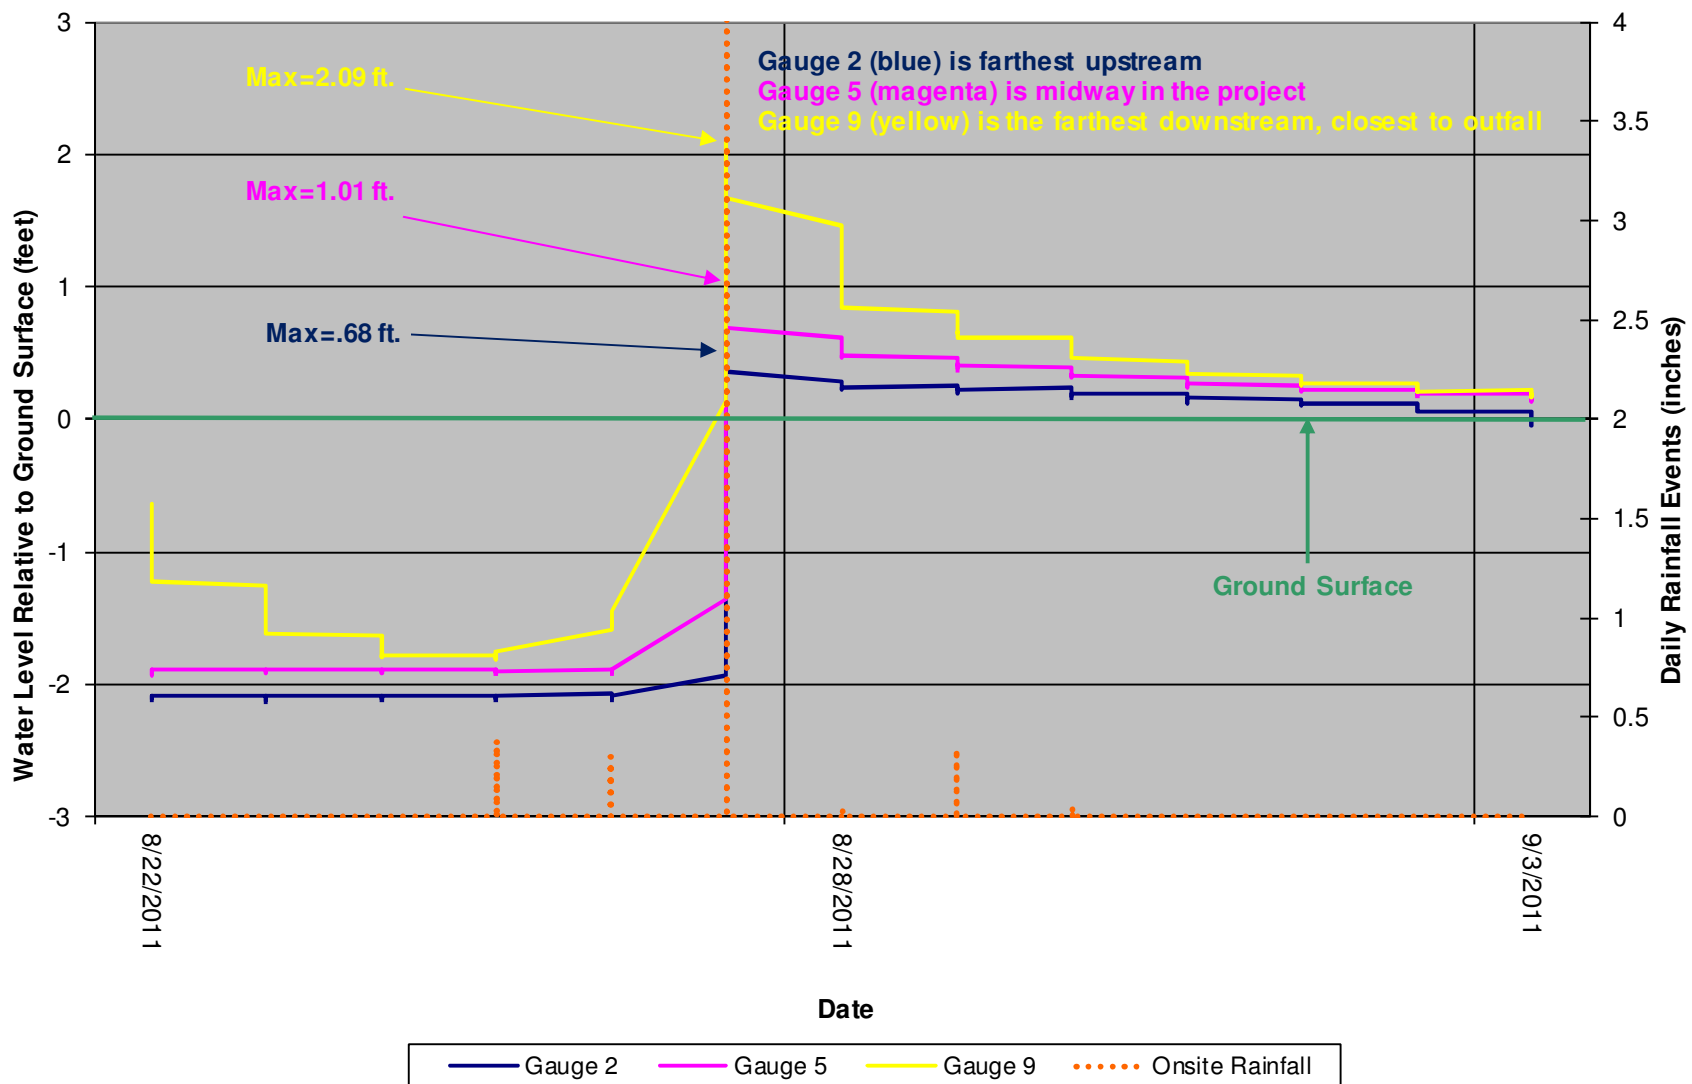

## 2.2 Wetland Monitoring Plan View (Integrated)

Figure 4 in Appendix D provides an overview of the areas where subsoiling has corrected hydrology problems around Gauges 6 and 7.

Table VI. 2011 Hydrology and Vegetation Criteria Success by Plot Powell Wetland and Stream Mitigation Project/EEP #D06065-B					
Gauge	Hydrology Success Met (% hydroperiod)	Hydrology Mean	Vegetation Plot	Vegetation Success Met (Stems/Acre)	Vegetation Mean
1	Y (13%)	100%	1	Y (495)	100%
2	Y (26%)		2	Y (330)	
3	Y (26%)		3	Y (330)	
4	Y (9%)		4	Y (371)	
5	Y (26%)		5	Y (495)	
6	Y (26%)		6	Y (371)	
7	Y (8%)		7	Y (330)	
7A	Y (6%)		No Plot		
7B	Y (8%)		No Plot		
8	Y (26%)		8	Y (577)	
9	Y (26%)		9	Y (371)	
10	Y (21%)		10	Y (454)	
11 (Ref)*	26%		No Plot		
12 (Ref)*	26%		No Plot		

\* Gauges 11 & 12 are reference gauges and not included in the hydrology mean

## 3.0 Project Success Discussion

After the third year of monitoring and corrective action in the form of subsoiling to correct hydrology issues, the wetland hydrology on the Powell project shows indications of successful restoration. Specifically, the hydrology within the swamp run has been restored and the project is functioning like a natural riparian headwater system. Flow of water across the site was successfully measured and documented on two separate occasions in 2011.

The reference gauges are measuring very similar above- and below-ground water patterns at the reference site as those measured on the project, confirming that the site is functioning like a natural system. Overall tree survival and growth is good.

Listed below are the field indicators from the approved mitigation plan that are to be used to help substantiate flow. Those shown in blue were observed and/or video or photo documented in 2009, 2010 or 2011.

- A natural line impressed on the bank
- Shelving

- Changes in soil characteristics
- Destruction of terrestrial vegetation
- Presence of litter and debris
- Wracking
- Vegetation matted down or absent
- Sediment sorting
- Leaf litter disturbed or washed away
- Scour
- Deposition
- Bed and bank formation
- Water staining
- Change in plant community

High water marks on bank vegetation were noted and photographed during December of 2009 after heavy rainfall. Matted vegetation was noted and photographed in April of 2010, the remnants of winter flooding. Further evidence of flow is deposition of small detritus after flow events as well as some scouring in the mid portion of the project. Wracking can be seen among the vegetation downstream after heavy rains. Sediment sorting can also be seen after heavy rains.

### **III. Methodology Section**

Year 3 monitoring for the Powell project occurred in September of 2011. Monitoring and vegetation sampling procedures were established in the mitigation plan for this project and no deviations were made.

# **Appendix A**

Vegetation Data Tables

Site Photos

# 1. Vegetation Data Tables

Table 1. Project Metadata

<b>Report Prepared By</b>	Ashby Brown
<b>Date Prepared</b>	11/29/2011 11:36
<b>DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----</b>	
<b>Vigor by Spp</b>	Frequency distribution of vigor classes listed by species.
<b>Damage by Spp</b>	Damage values tallied by type for each species.
<b>Damage by Plot</b>	Damage values tallied by type for each plot.
<b>ALL Stems by Plot and spp</b>	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
<b>PROJECT SUMMARY-----</b>	
<b>Project Code</b>	D06065B
<b>Project Name</b>	Powell
<b>Description</b>	Powell wetland and stream mitigation
<b>River Basin</b>	Chowan
<b>Sampled Plots</b>	10

Table 2. Vegetation Vigor by Species

	<b>Species</b>	<b>4</b>	<b>3</b>	<b>2</b>	<b>1</b>	<b>0</b>	<b>Missing</b>	<b>Unknown</b>
	Alnus serrulata	1						
	Celtis occidentalis		1					
	Cephalanthus occidentalis	5						
	Itea virginica	2	1	3				
	Nyssa biflora	2	2	6				
	Quercus bicolor	3	1					
	Quercus michauxii	5	2	2				
	Quercus phellos	14	5	1				
	Salix nigra	4	1					
	Taxodium distichum	17	14	2				
	Magnolia virginiana		1					
	Myrica	1	4					
<b>TOT:</b>	<b>12</b>	<b>54</b>	<b>32</b>	<b>14</b>				

Table 3. Vegetation Damage by Species

	Species	All Damage Categories	(no damage)	(other damage)
	<i>Alnus serrulata</i>	1	1	
	<i>Celtis occidentalis</i>	1	1	
	<i>Cephalanthus occidentalis</i>	5	5	
	<i>Itea virginica</i>	6	6	
	<i>Magnolia virginiana</i>	1	1	
	<i>Myrica</i>	5	5	
	<i>Nyssa biflora</i>	10	9	1
	<i>Quercus bicolor</i>	4	4	
	<i>Quercus michauxii</i>	9	9	
	<i>Quercus phellos</i>	20	20	
	<i>Salix nigra</i>	5	5	
	<i>Taxodium distichum</i>	33	33	
<b>TOT:</b>	<b>12</b>	<b>100</b>	<b>99</b>	<b>1</b>

Table 4. Vegetation Damage by Plot

	Plot	All Damage Categories	(no damage)	(other damage)
	1	12	12	
	2	8	8	
	3	8	8	
	4	9	9	
	5	12	12	
	6	9	9	
	7	8	8	
	8	14	13	1
	9	9	9	
	10	11	11	
<b>TOT:</b>	<b>10</b>	<b>100</b>	<b>99</b>	<b>1</b>



Table 5. Planted Stems by Plot and Species

Species	Total Planted Stems	# plots	avg# stems	Plot # for Year 3										
				1	2	3	4	5	6	7	8	9	10	
<i>Alnus serrulata</i>	1	1	1			1								
<i>Celtis occidentalis</i>	1	1	1									1		
<i>Cephalanthus occidentalis</i>	5	2	2.5	3								2		
<i>Itea virginica</i>	6	5	1.2	2		1	1					1		1
<i>Magnolia virginiana</i>	1	1	1					1						
<i>Myrica</i>	5	2	2.5					2		3				
<i>Nyssa biflora</i>	10	5	2		2		1	1	2			4		
<i>Quercus bicolor</i>	4	2	2						3	1				
<i>Quercus michauxii</i>	9	3	3		2			3						4
<i>Quercus phellos</i>	20	5	4	7	4	4			4	1				
<i>Salix nigra</i>	5	1	5									5		
<i>Taxodium distichum</i>	33	7	4.71			2	7	5		3	1	9	6	
<b>Totals</b>	<b>100</b>	<b>12</b>		<b>12</b>	<b>8</b>	<b>8</b>	<b>9</b>	<b>12</b>	<b>9</b>	<b>8</b>	<b>14</b>	<b>9</b>	<b>11</b>	
<b>Average Stems per Acre</b>				<b>495</b>	<b>330</b>	<b>330</b>	<b>371</b>	<b>495</b>	<b>371</b>	<b>330</b>	<b>577</b>	<b>371</b>	<b>454</b>	

Overall average stocking for the site in 2011 is 412 stems per acre.

**Outflow end of reference area in March 2011 shows very low water and dry conditions.**



**Lower end of project is not flowing in March 2011. View is looking upstream near Ga. 9.**





**Area around Ga. 7 in April after rainfall. Site holding water. View looking toward Ga. 7A.**



**Screenshot from April video #4 showing flow of sediment plume upstream from Ga. 6**





**Looking upstream near Gauge 9 in July (same view as second photo above).**



**Tree growth was good in 2011. View near Gauge 1.**



Table C-1


Longest consecutive successful hydrologic period in days (and % of Growing Season) and success at 5% and 8% of the growing season

Living Stems Per Acre at the end of the growing season for plots 1-10

Gauge (Plot)	Year 1					Year 2					Year 3					Year 4					Year 5					
	Days	%	5%	8%	SPA	Days	%	5%	8%	SPA	Days	%	5%	8%	SPA	Days	%	5%	8%	SPA	Days	%	5%	8%	SPA	
1	14	6	Y	N	577	18	8	Y	N	526	30	13	Y	Y	495											
2	34	15	Y	Y	412	25	11	Y	Y	364	59	26	Y	Y	330											
3	15	6	Y	N	495	17	7	Y	N	405	59	26	Y	Y	330											
4	4	2	N	N	454	15	6	Y	N	445	21	9	Y	Y	371											
5	35	15	Y	Y	412	34	15	Y	Y	405	59	26	Y	Y	495											
6	4	2	N	N	371	7	3	N	N	405	59	26	Y	Y	371											
7	7	3	N	N	371	4	2	N	N	324	19	8	Y	Y	330											
7A											13	6	Y	N												
7B											18	8	Y	Y												
8	39	17	Y	Y	701	38	16	Y	Y	647	59	26	Y	Y	577											
9	24	10	Y	Y	454	39	17	Y	Y	364	59	26	Y	Y	371											
10	14	6	Y	N	454	28	12	Y	Y	405	48	21	Y	Y	454											
11 (Ref)	53	23	Y	Y		38	16	Y	Y		59	26	Y	Y												
12 (Ref)	39	17	Y	Y		36	16	Y	Y		59	26	Y	Y												

5% of growing season is 12 days, 8% is 19 days  
 Hydrology is deemed successful if longest consecutive hydrologic period meets minimum of 5% of the growing season  
 Gauges 7A and 7B were installed in Year 3 (2011)

**Figure P-1**  
**2011 Reference Precipitation**

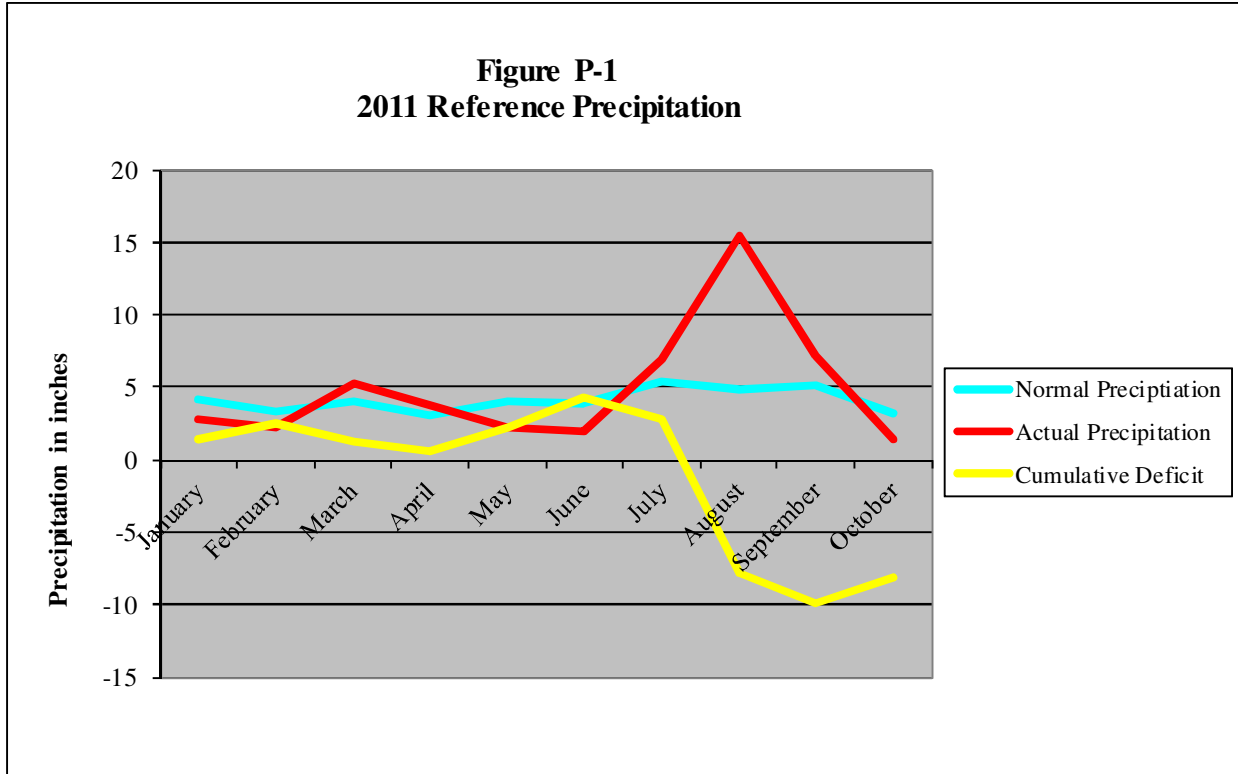

Total precipitation from January 1, 2011 through October 24, 2011 was above average (8.12” surplus) due to 15.5” falling in August as a result of Hurricane Irene. Total rainfall through July was 2.75” below normal.

## **Appendix B**

Geomorphologic Raw Data


Not used in this report

# **Appendix C**


Hydrologic Data Tables




# Powell Monitoring Gauge #1 (2238363)

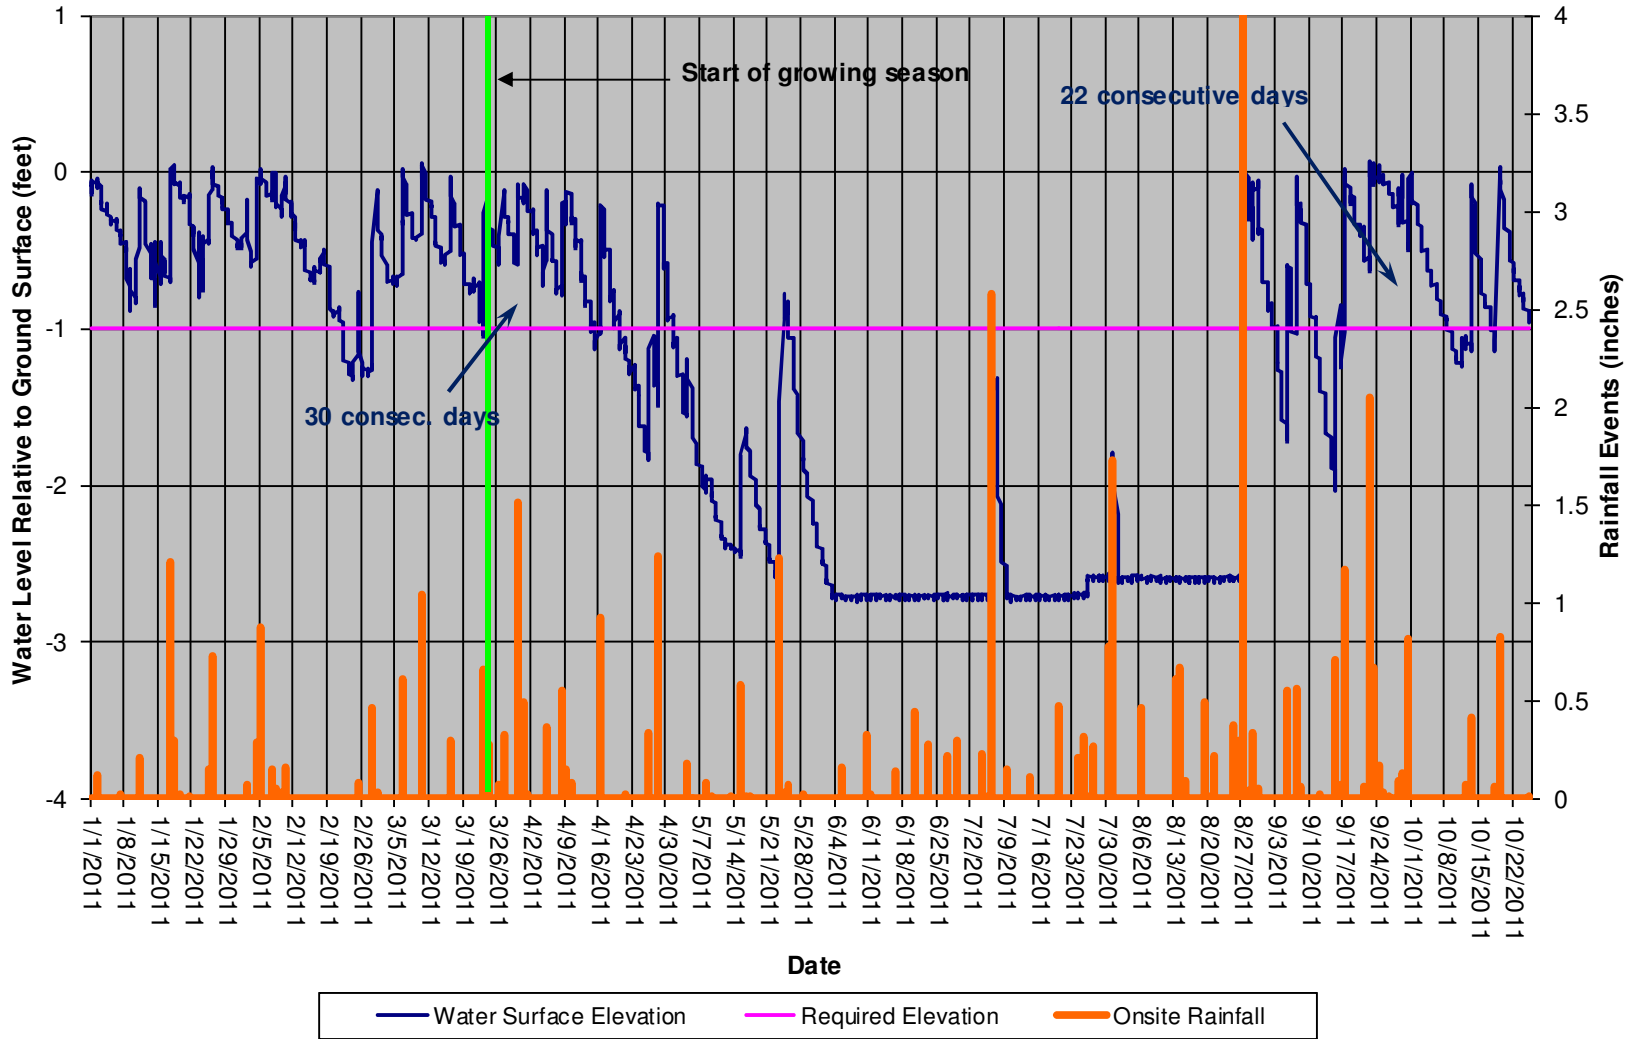


# Powell Monitoring Gauge #2 (2238364)

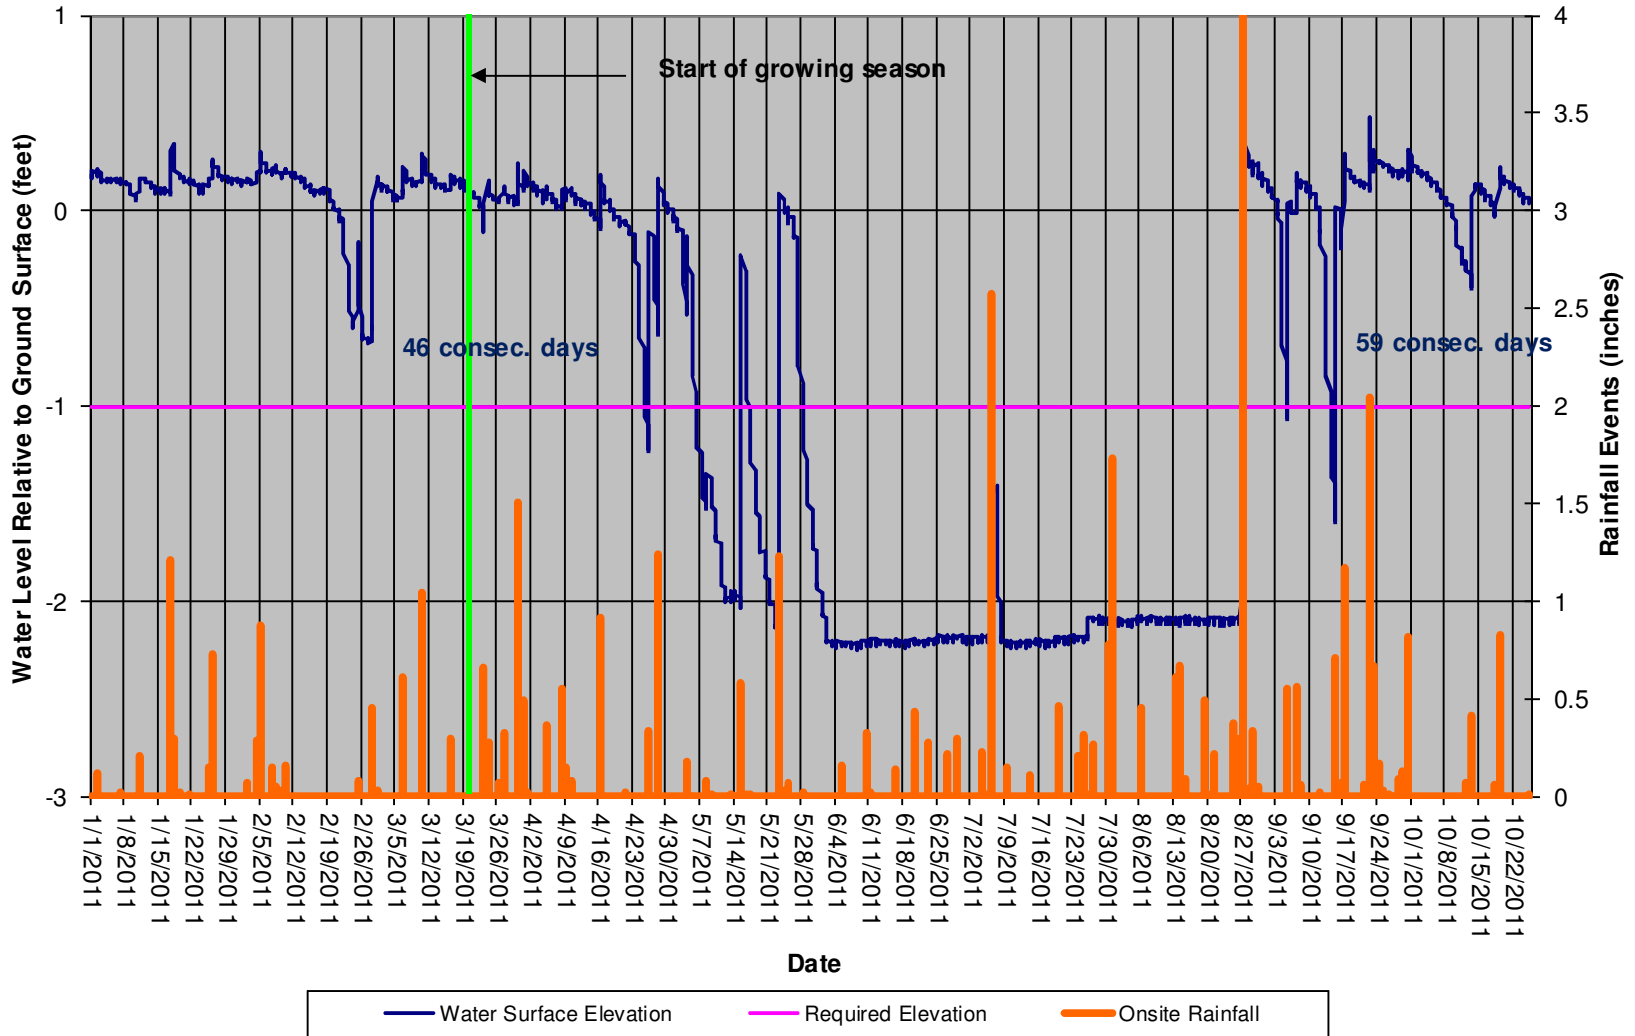


# Powell Monitoring Gauge #3 (2238365)

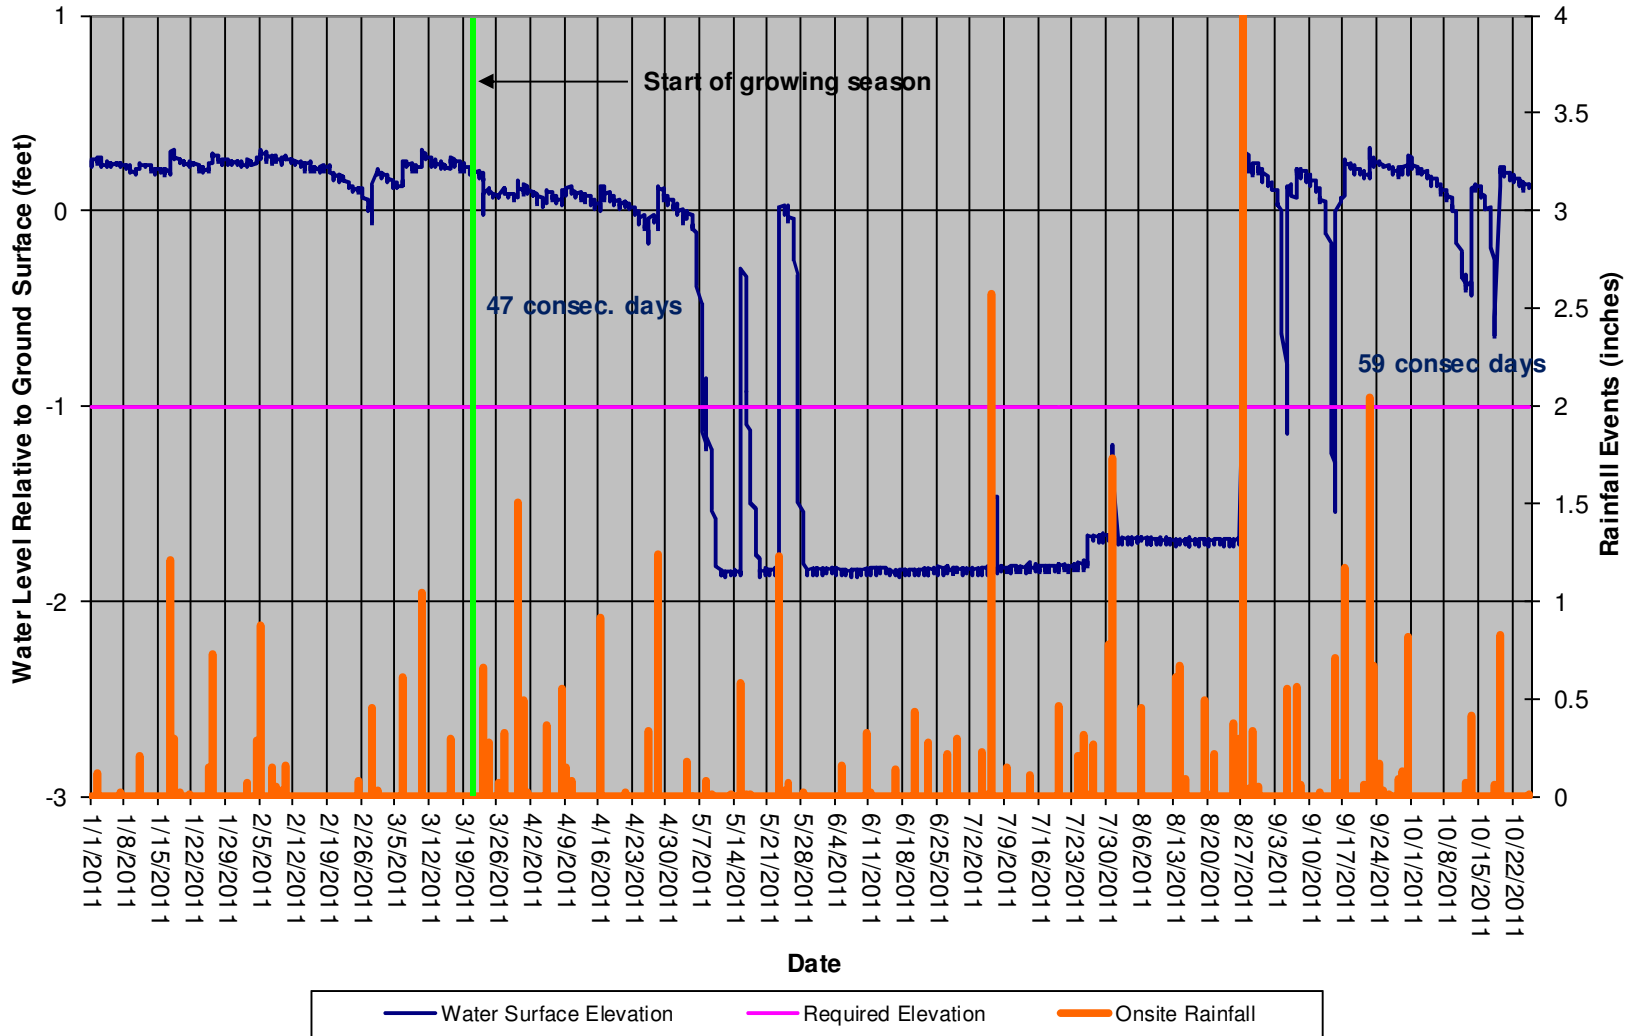


### Powell Monitoring Gauge #4 (2238366)

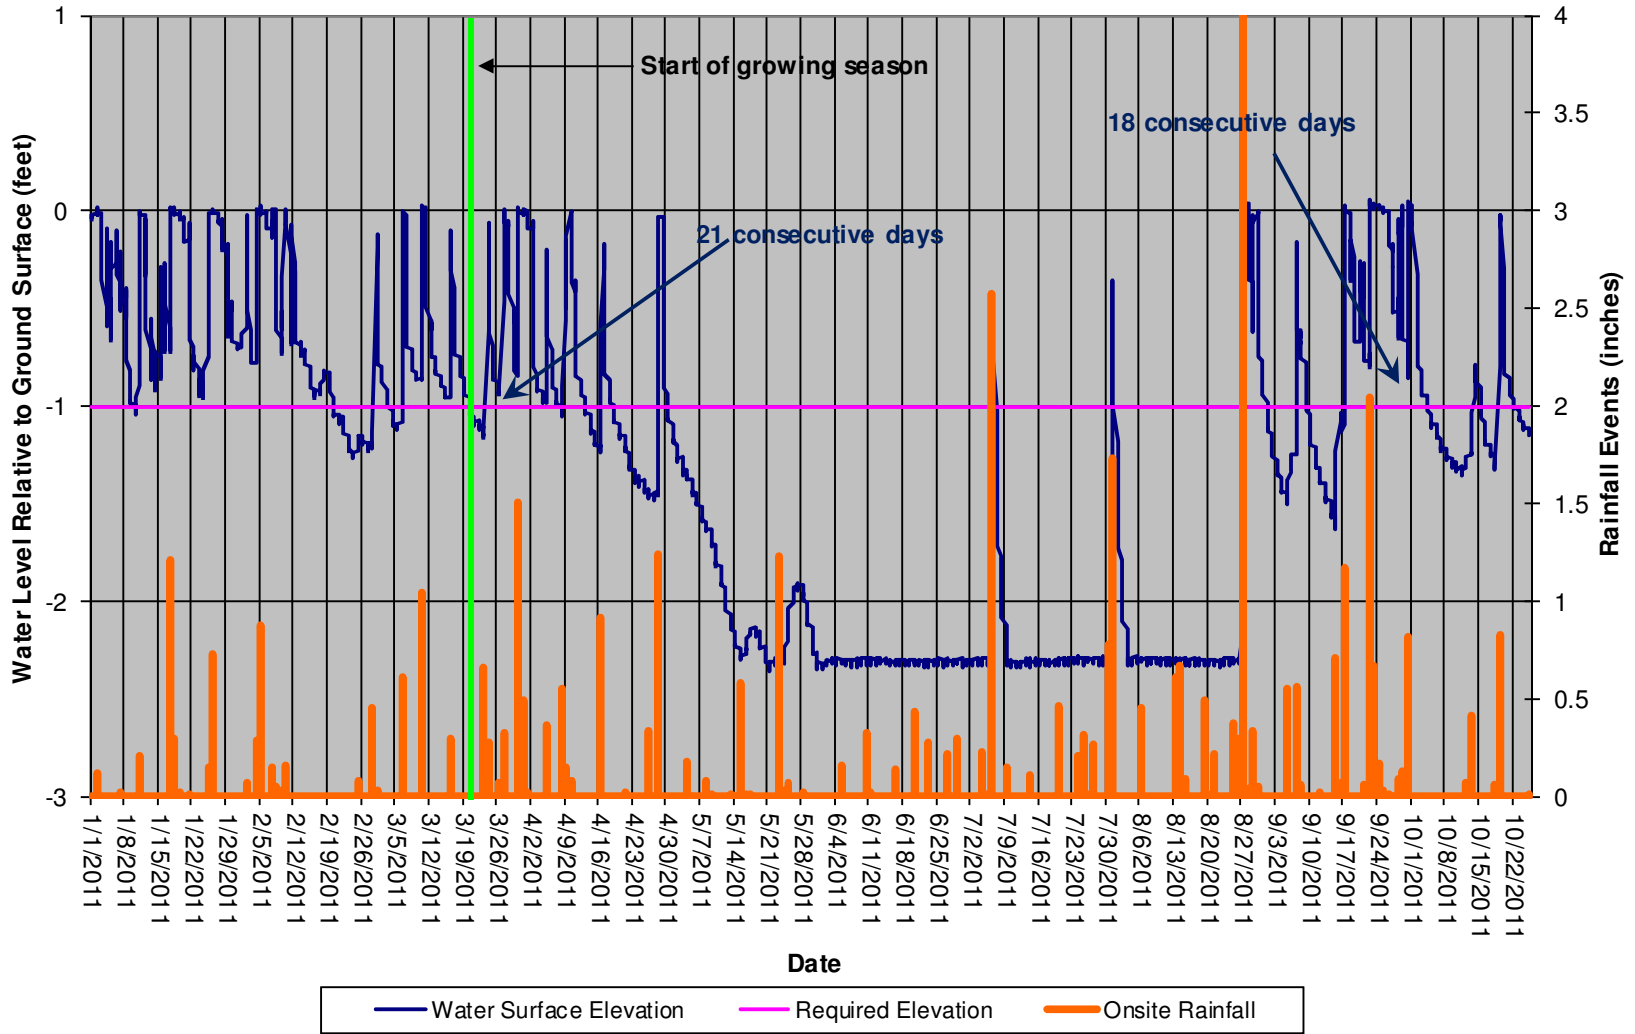


# Powell Monitoring Gauge #5 (2238367)

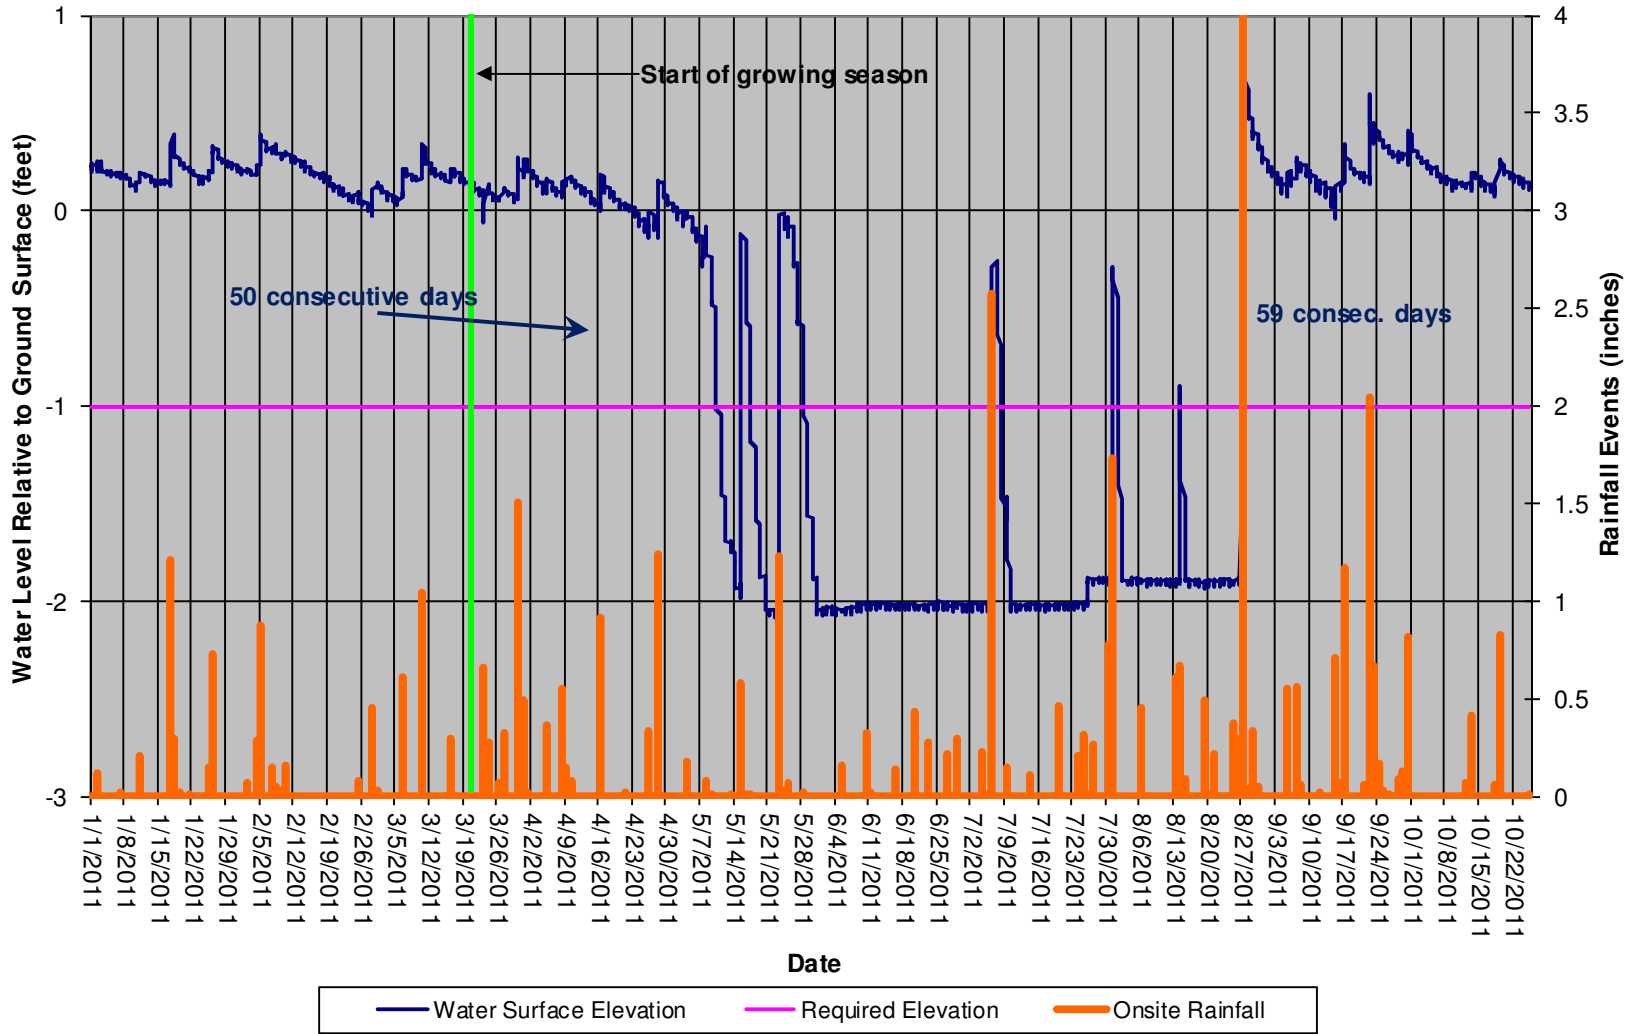


### Powell Monitoring Gauge #6 (2238368)

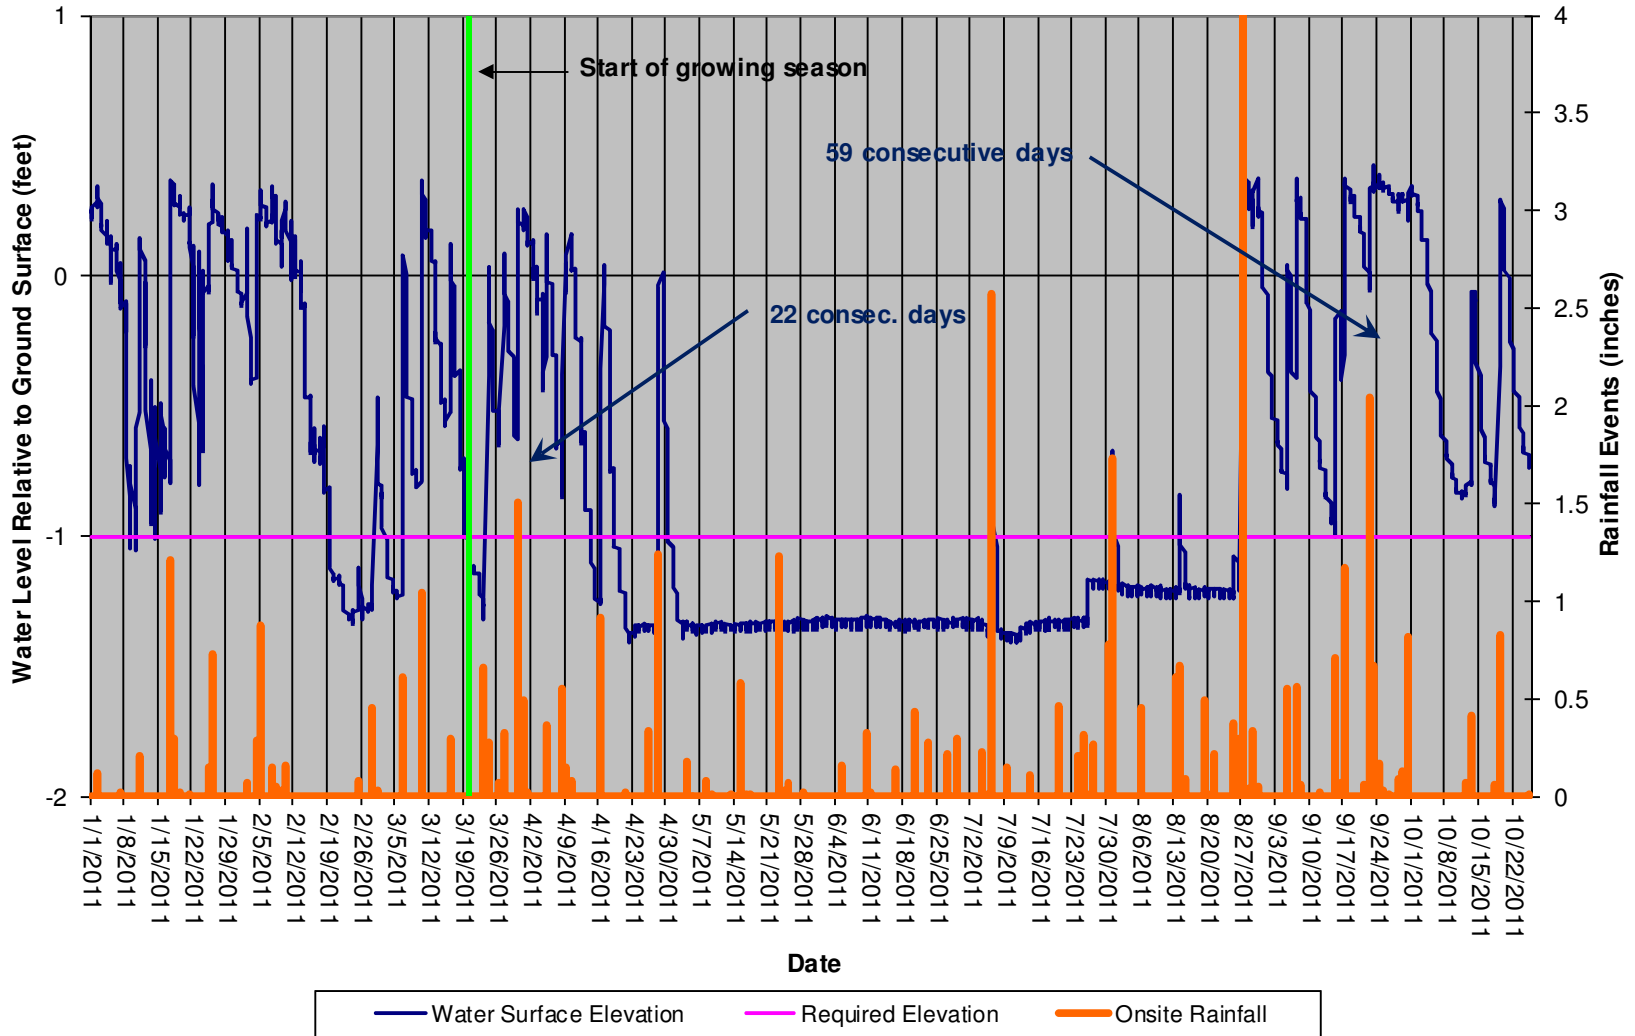

# Powell Monitoring Gauge #7 (2238369)

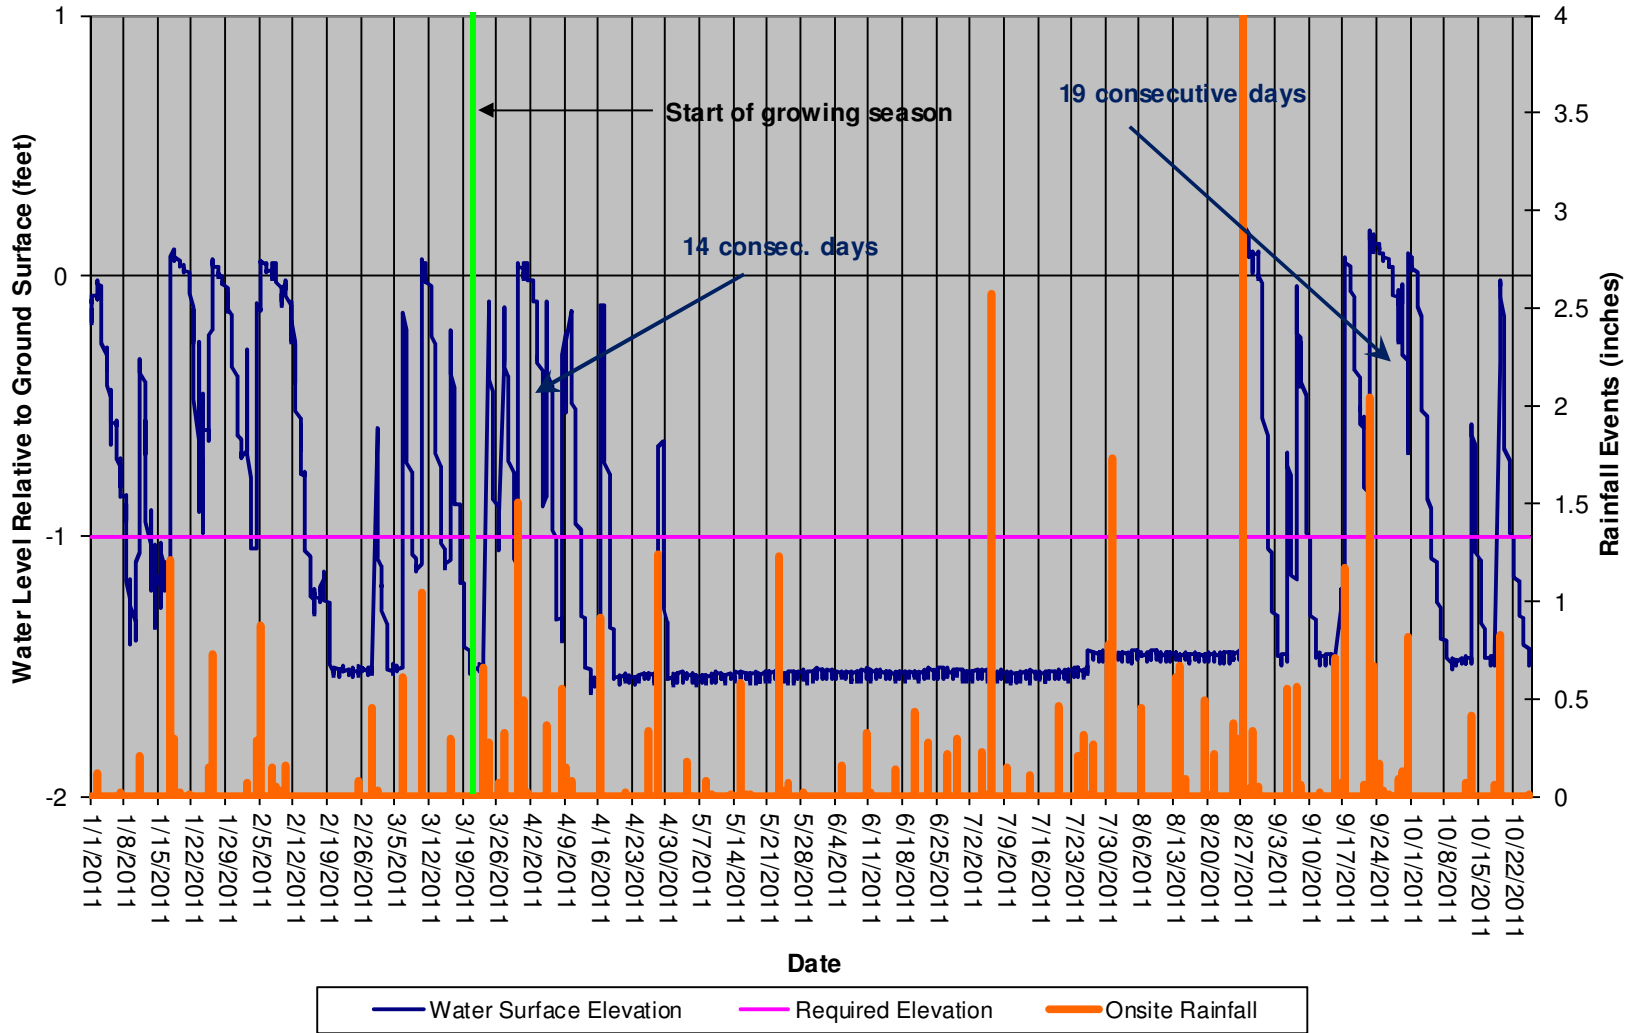


# Powell Monitoring Gauge #7 A (9669813)

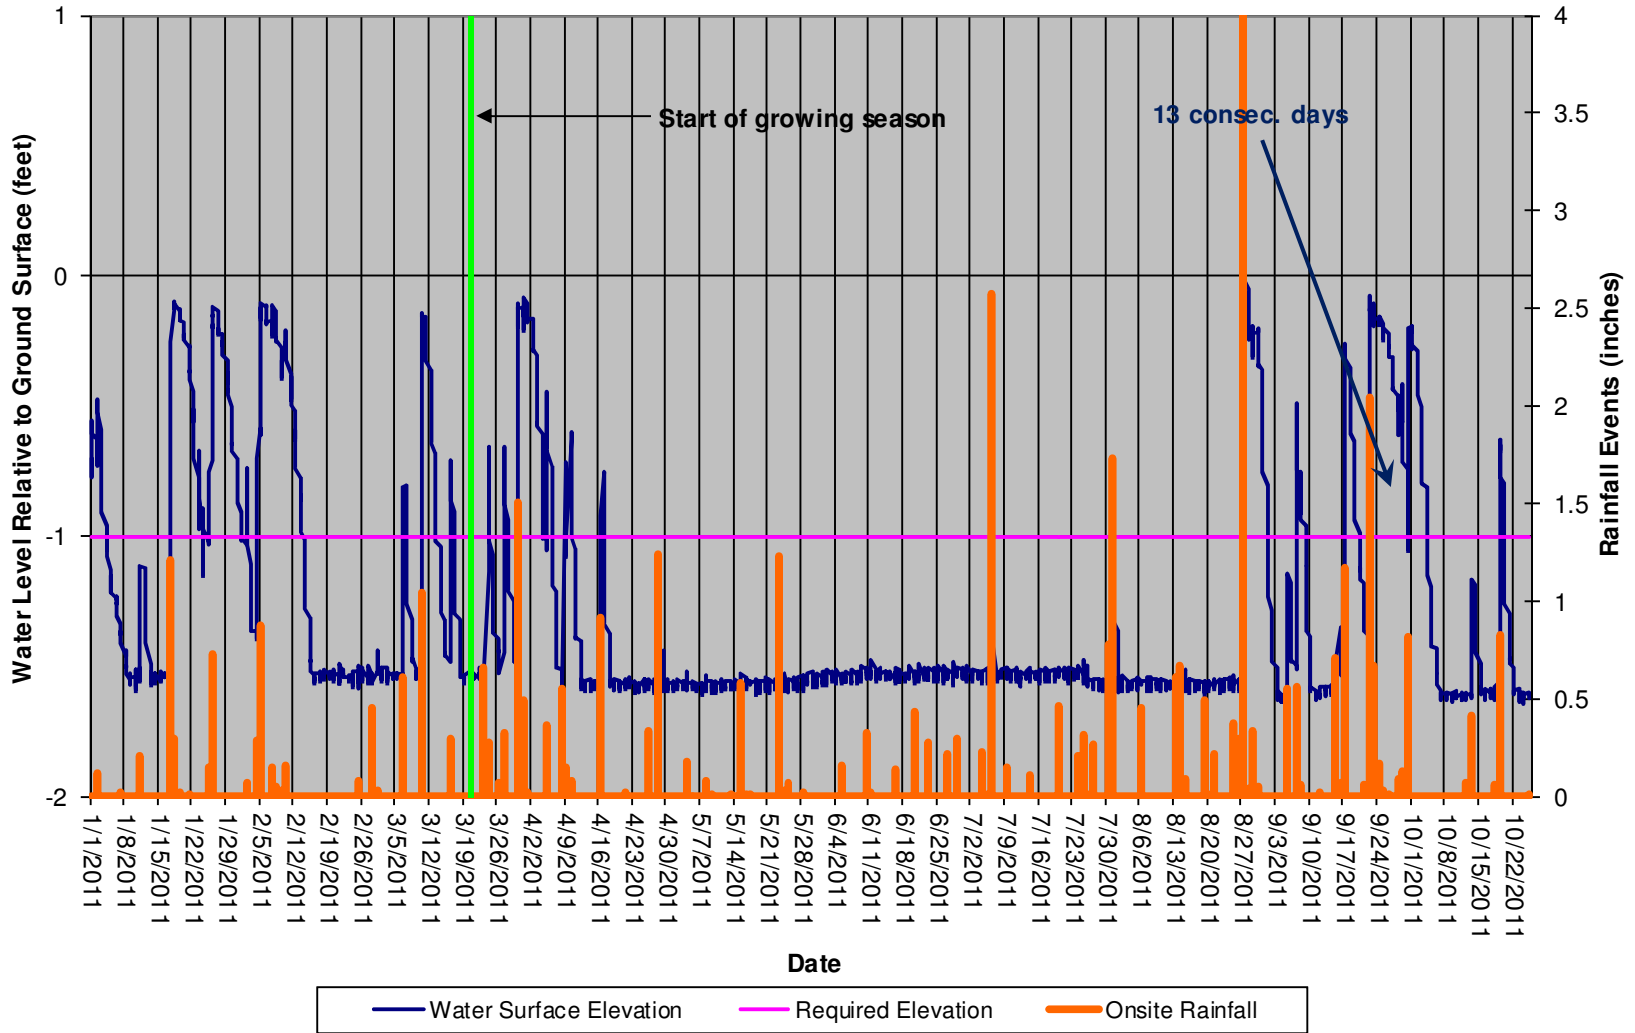





### Powell Monitoring Gauge #7 B (9669819)

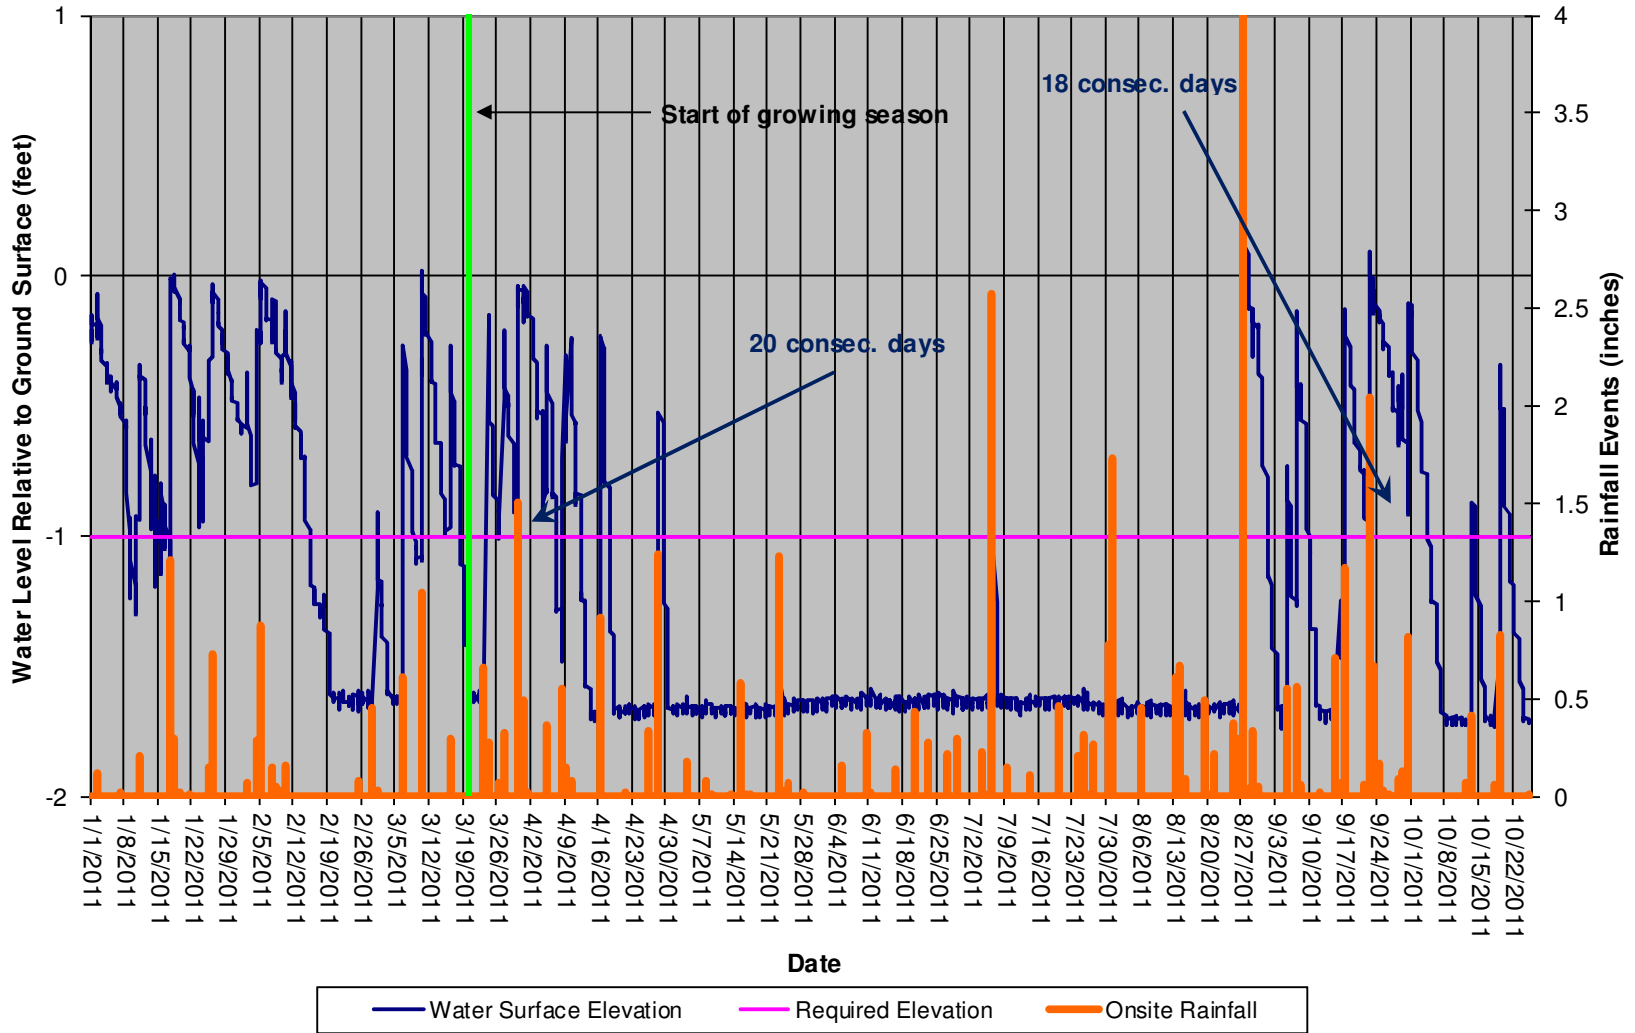


### Powell Monitoring Gauge #8 (2238370)

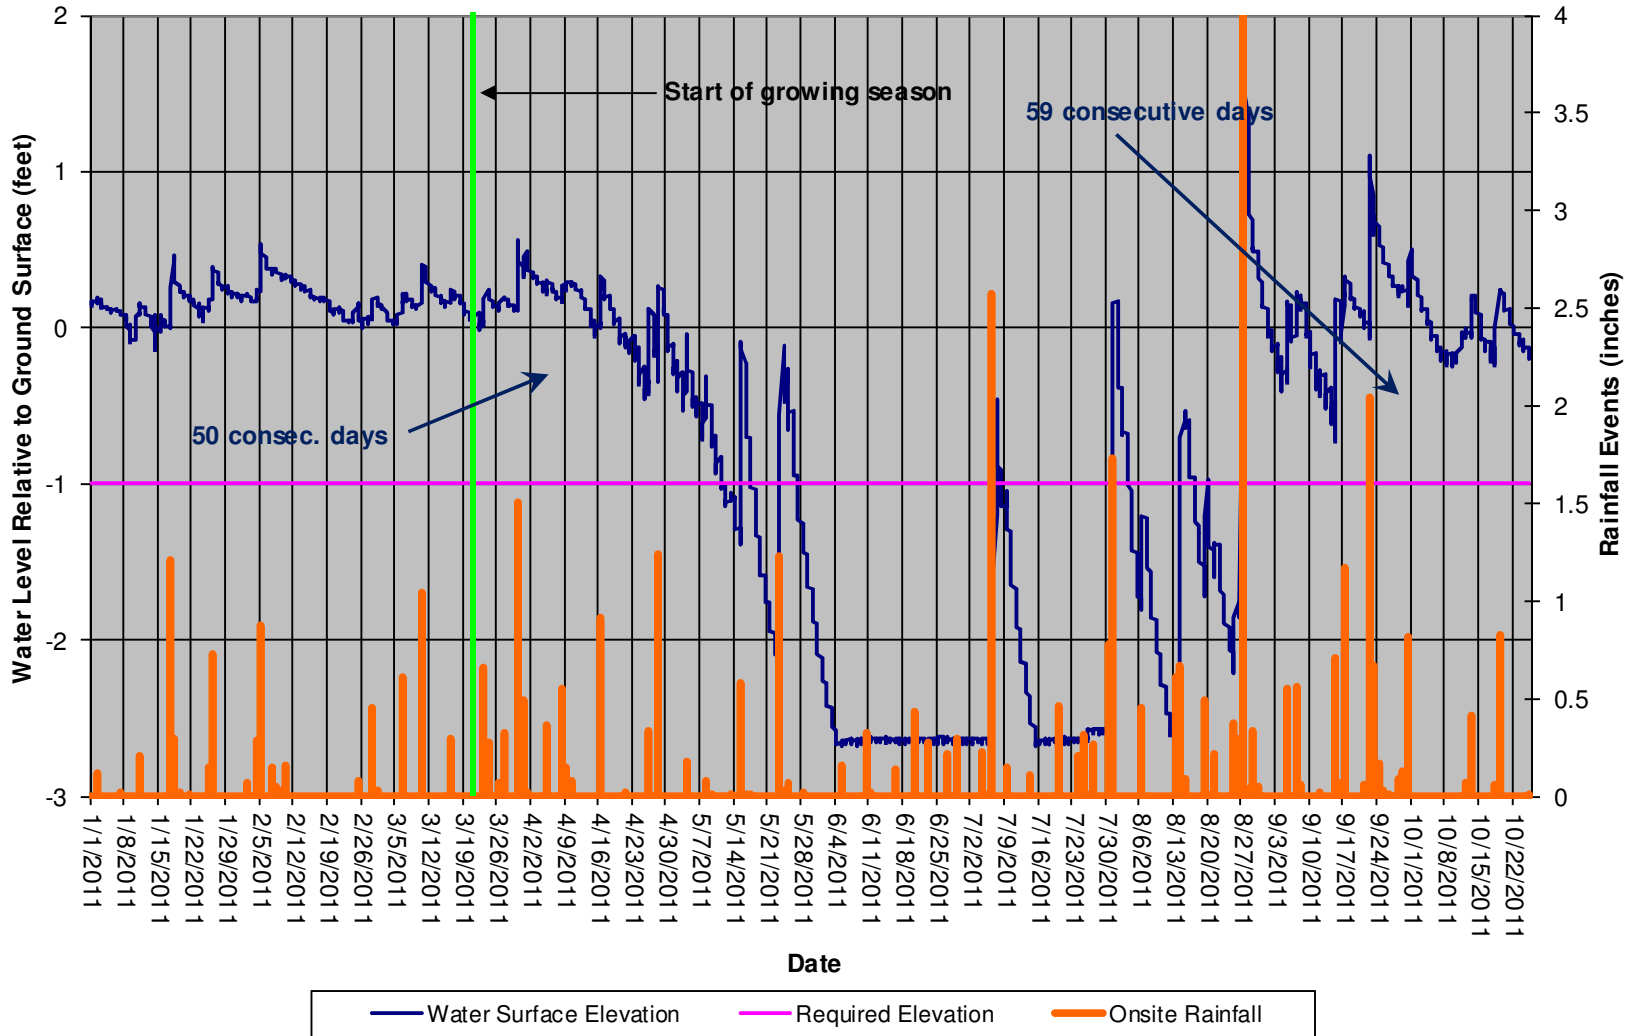



# Powell Monitoring Gauge #9 (2238371)

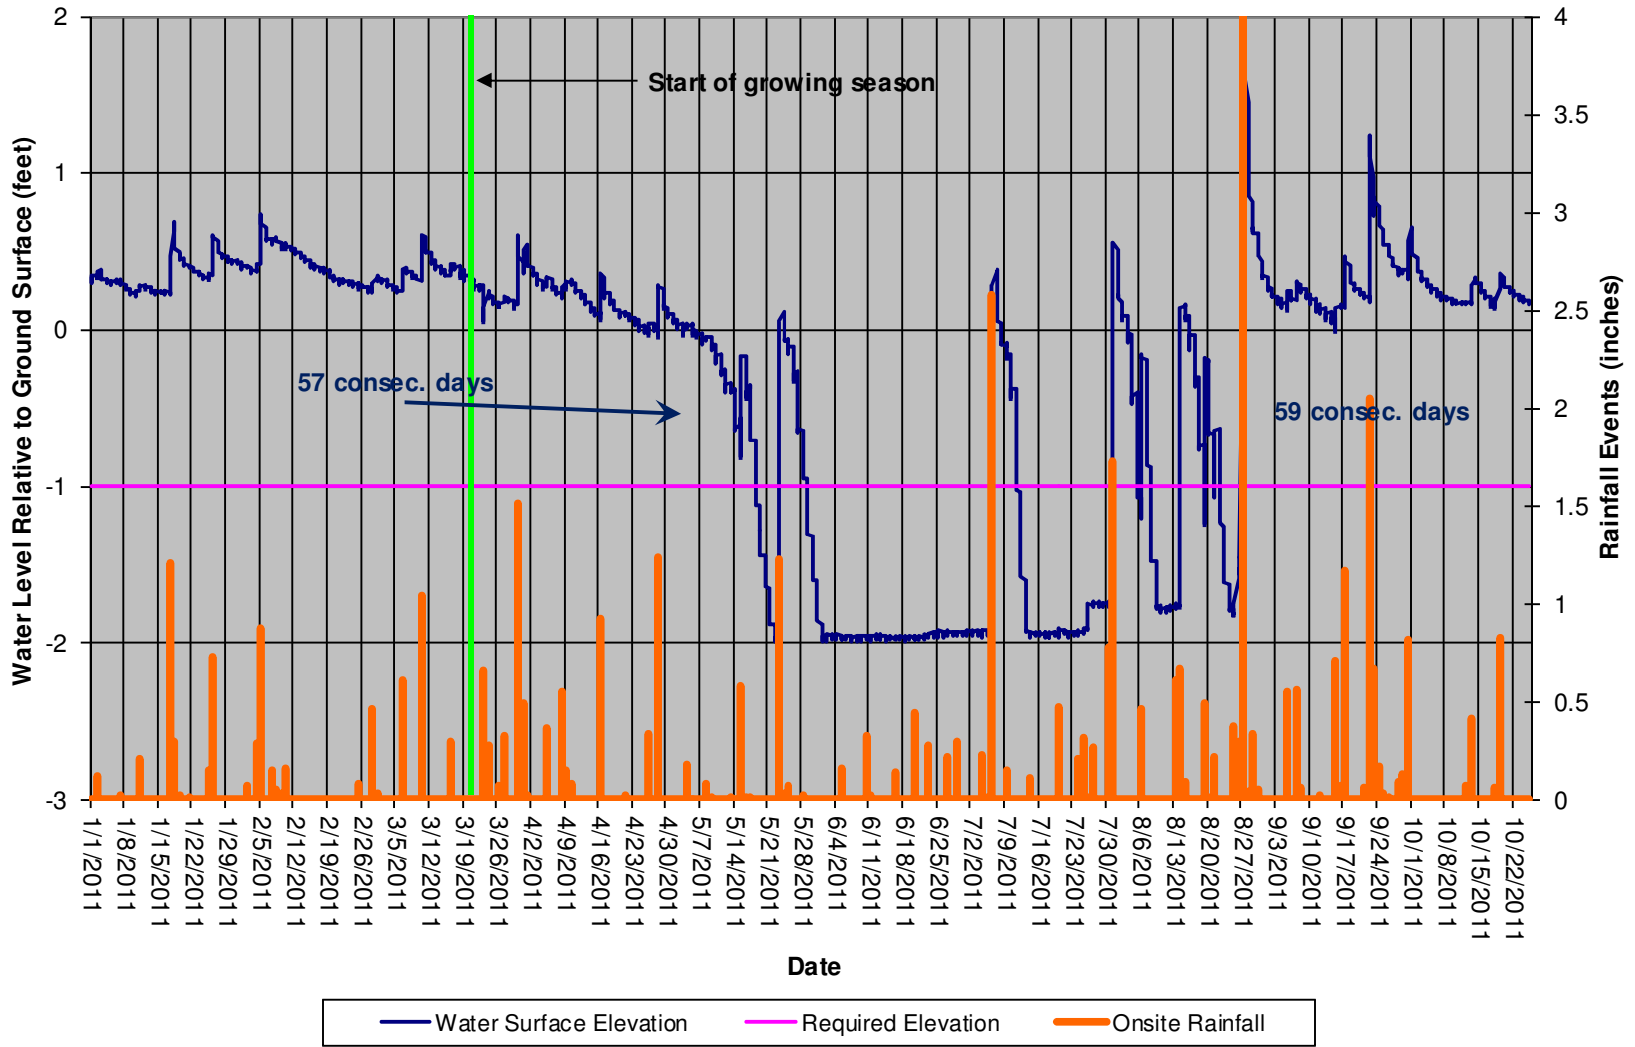


### Powell Monitoring Gauge #10 (2238372)

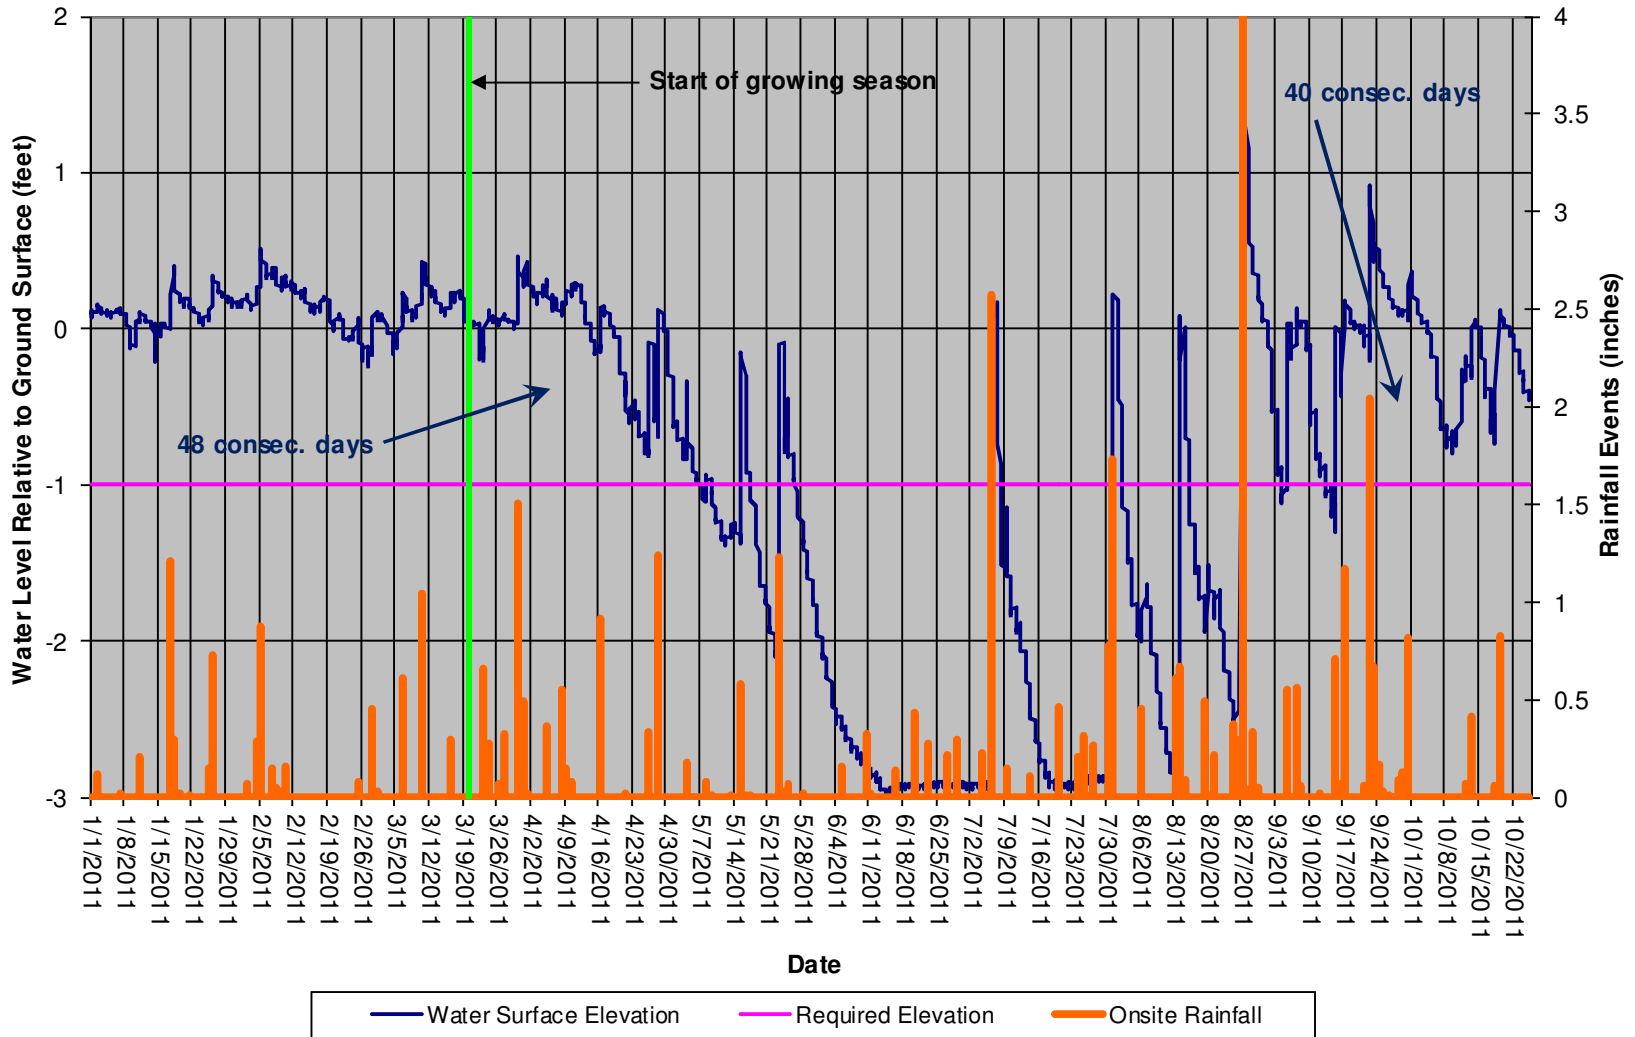

### Powell Monitoring Gauge #11 (2250036) Reference

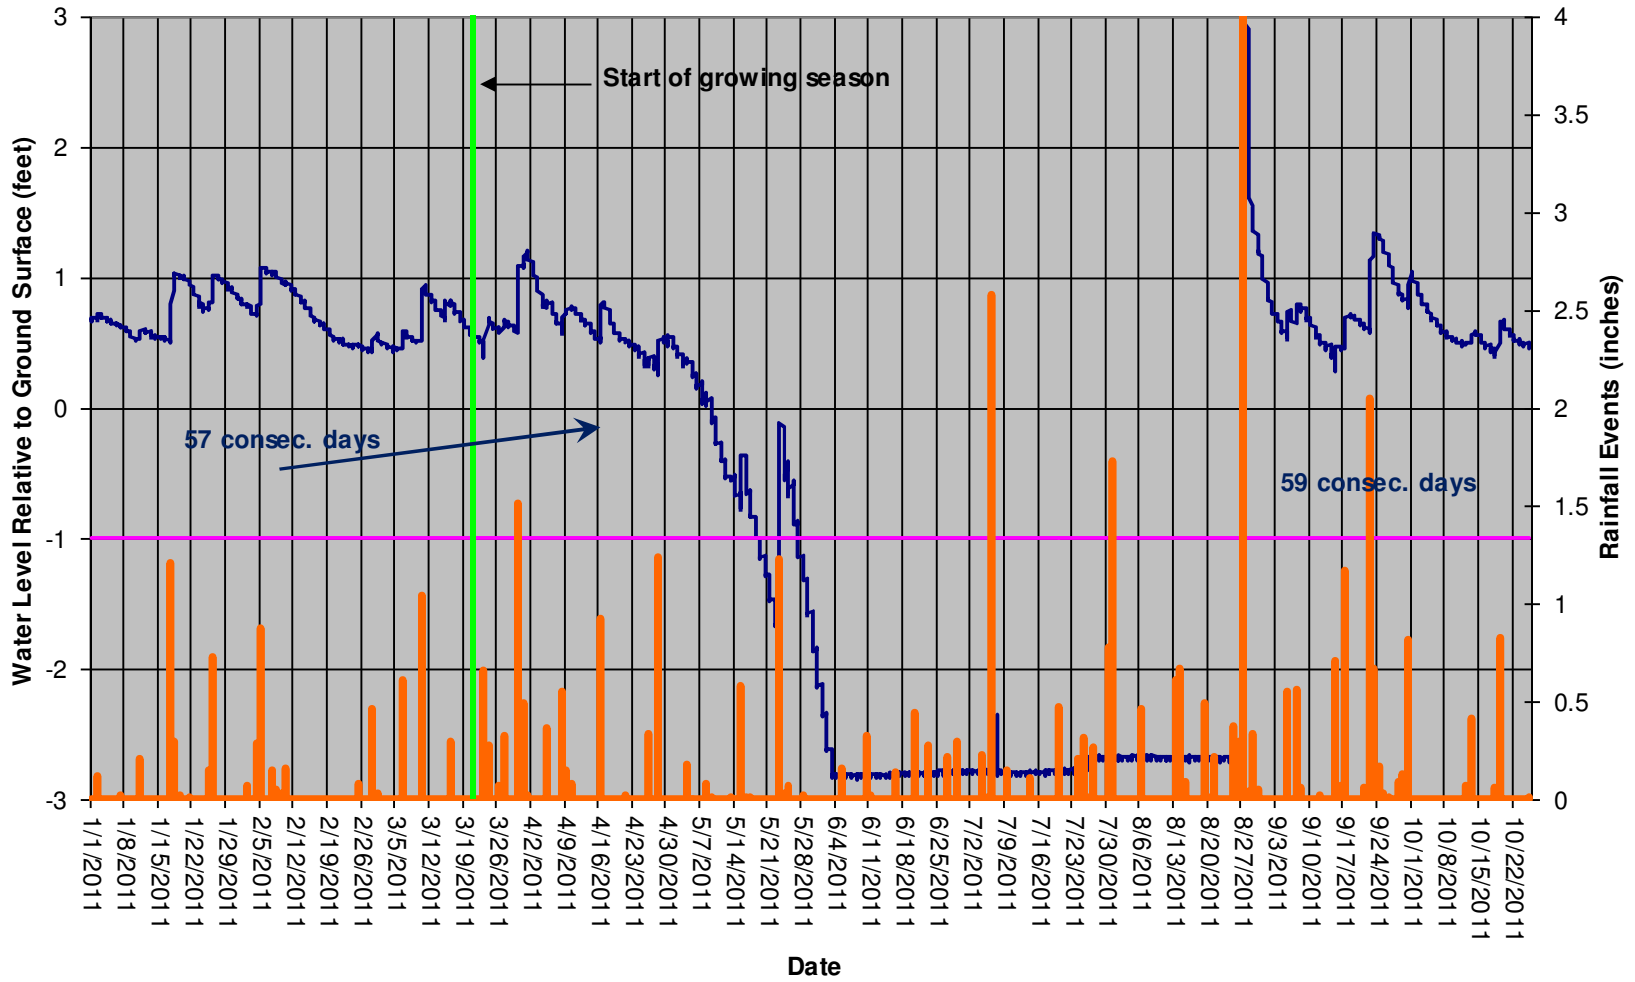


### Powell Monitoring Gauge #12 (2250037) Reference

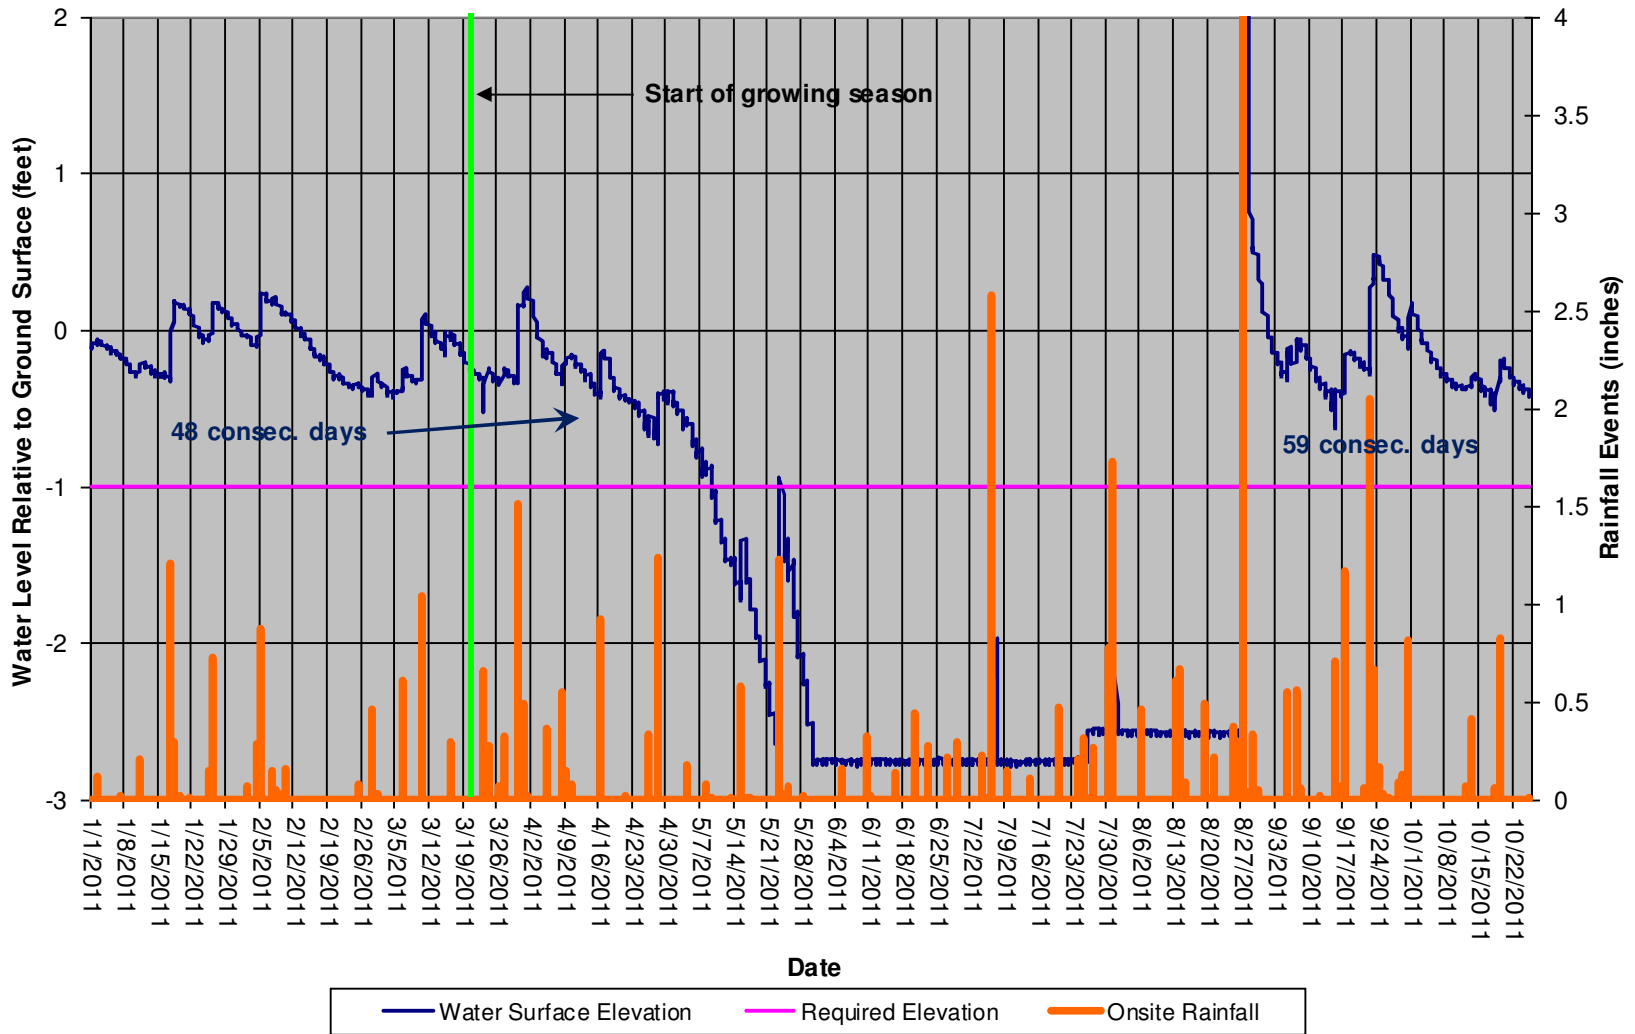

# **Appendix D**

Problem Areas Plan View (Integrated)

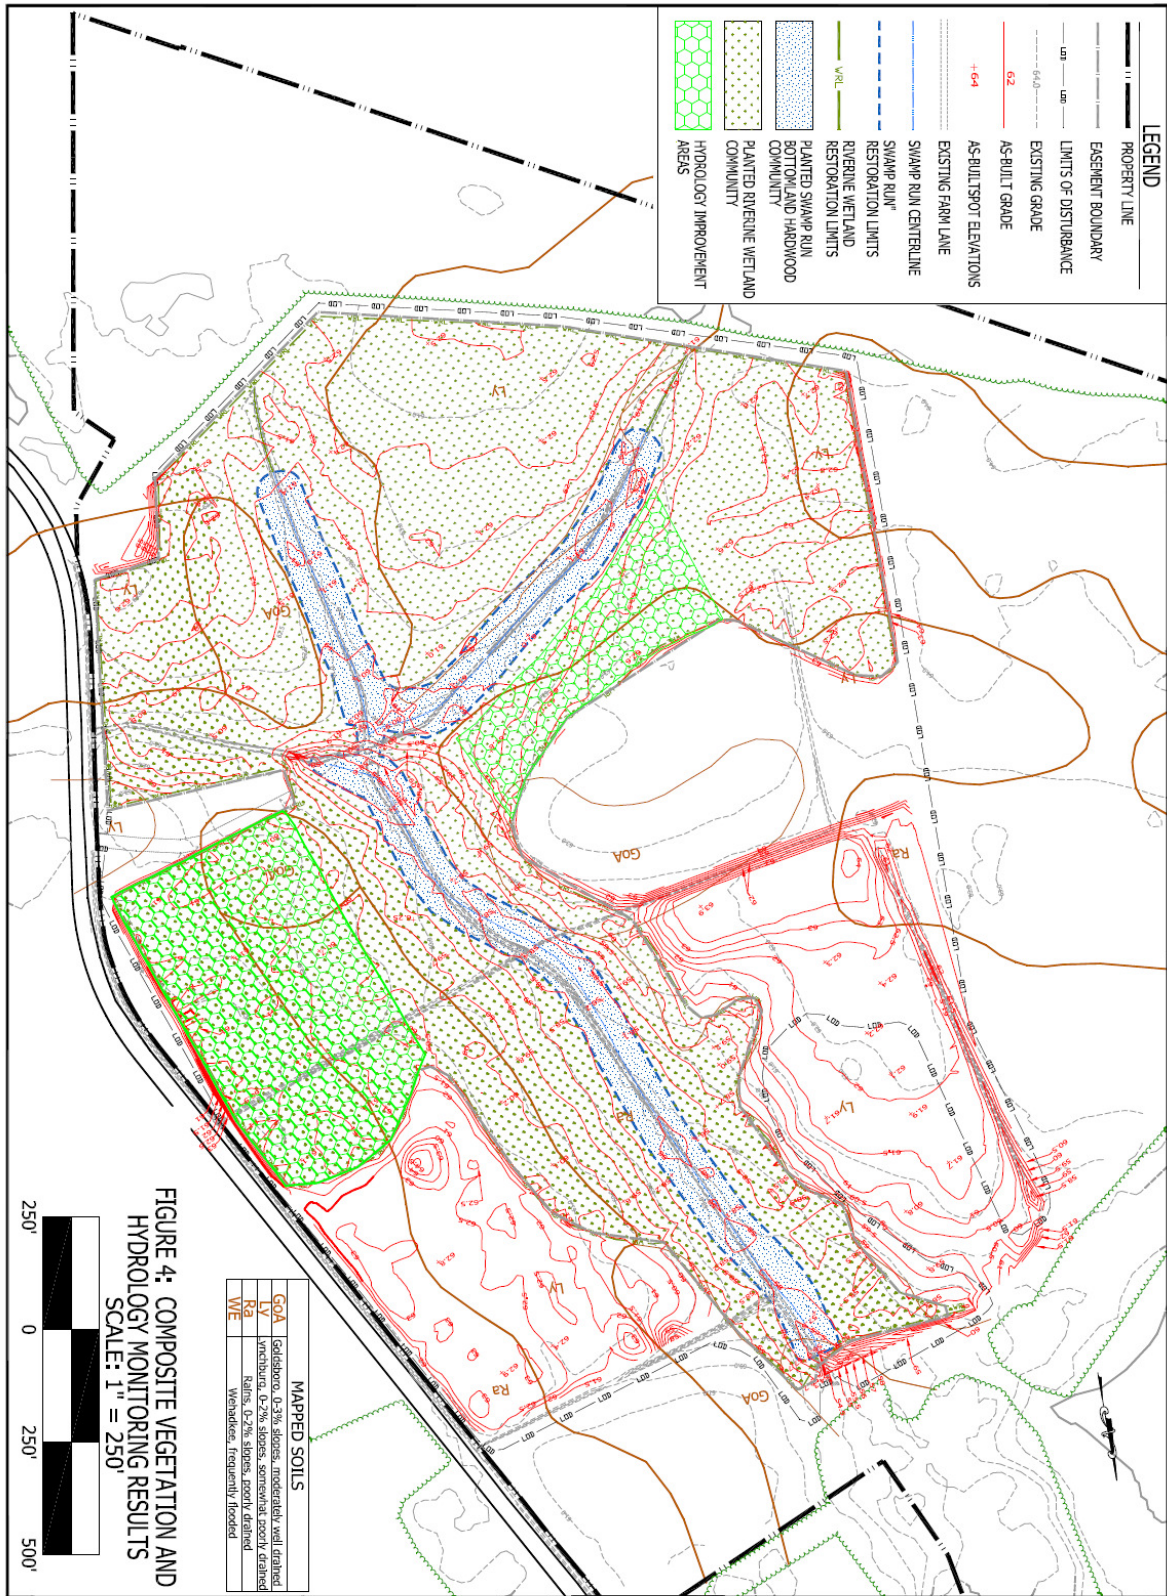


**LEGEND**

	PROPERTY LINE
	EASEMENT BOUNDARY
	LIMITS OF DISTURBANCE
	EXISTING GRADE
	AS-BUILT GRADE
	AS-BUILT SPOT ELEVATIONS
	EXISTING FARM LAINE
	SWAMP RUN CENTERLINE
	SWAMP RUN <sup>TM</sup> RESTORATION LIMITS
	RESTORATION LIMITS
	RESTORATION LIMITS
	RESTORATION LIMITS
	PLANTED SWAMP RUN BOTTOMLAND HARDWOOD COMMUNITY
	PLANTED RIVERINE WETLAND COMMUNITY
	HYDROLOGY IMPROVEMENT AREAS

**MAPPED SOILS**

GOA	Goldsboro, 0-3% slopes, moderately well drained
LV	Wachaura, 0-2% slopes, somewhat poorly drained
Ra	Rainfs, 0-2% slopes, poorly drained
WE	Wetshades, frequently flooded

**FIGURE 4: COMPOSITE VEGETATION AND HYDROLOGY MONITORING RESULTS**  
 SCALE: 1" = 250'



PREPARED BY:  
**ALBEMARLE RESTORATIONS, LLC**  
 WETLAND RESTORATION,  
 STREAM RESTORATION,  
 & WILDLIFE HABITAT CREATION  
 404 COURT STREET - GATHERVILLE, NC 27038  
 (336) 334-0404 FAX (336) 351-9882



**POWELL PROPERTY**  
 WETLAND MITIGATION UNITS: 48.4 WMU'S  
 STREAM MITIGATION UNITS: 3,310 SMU'S  
 BERTIE COUNTY, NORTH CAROLINA  
 EEP CONTRACT #: D06065-B

**FIGURE 4**  
 MONITORING YEAR 3 (2011)

REVISION	REVISION	INITIALS
