

UT Bear Creek (Phillips) Stream Restoration Monitoring Report

**EEP Project # 92719
EEP Contract # 004828
Monitoring Year 05**



Submitted to:



NCDENR-EEP, 1652 Mail Service Center, Raleigh, NC 27699-1652

**Data Collection: 2013
Construction Completed: 2006
Submitted: December 2013**

Monitoring Firm



**Landmark Center II, Suite 220
4601 Six Forks Road
Raleigh, NC 27609
Phone: (919) 278-2514
Fax: (919) 783-9266**

**Project Contact: Adam Spiller
Email: adam.spiller@kci.com
KCI Project No: 16121976_BC12**

Design Firm

**Environmental Services, Inc.
524 South New Hope Road
Raleigh, NC 27610
Phone (919) 212-1760**

TABLE OF CONTENTS

1.0	EXECUTIVE SUMMARY / PROJECT ABSTRACT	1
2.0	METHODOLOGY	2
3.0	REFERENCES	2

APPENDIX A – Project Vicinity Map and Background Tables

Figure 1.	Site Vicinity Map.....	4
Table 1a. and b.	Project Restoration Components.....	5
Table 2.	Project Activity and Reporting History	6
Table 3.	Project Contacts Table	6
Table 4.	Project Attribute Table.....	7

APPENDIX B – Visual Assessment Data

Figure 2.	Current Condition Plan View.....	9
Table 5a. and b.	Visual Stream Morphology Stability Assessment Table	11
Table 6.	Vegetation Condition Assessment Table	13
Stream Station Photos		14
Vegetation Monitoring Plot Photos.....		21

APPENDIX C – Vegetation Plot Data

Table 7.	Vegetation Plot Mitigation Success Summary Table	26
Table 8.	CVS Vegetation Metadata Table	27
Table 9.	CVS Stem Count Total and Planted by Plot and Species	28
Table 10.	Supplemental Planting Species List.....	30
Supplemental Planting Plan		31

APPENDIX D – Hydrologic Data

Table 11.	Verification of Bankfull Events	33
-----------	---------------------------------------	----

1.0 EXECUTIVE SUMMARY / PROJECT ABSTRACT

In 2002, the North Carolina Department of Transportation identified the Unnamed Tributary (UT) to Bear Creek Site (Phillips) in Chatham County, North Carolina as a potential stream restoration project. The 1.7-square mile watershed is located within the USGS 8-digit HUC 03030003 and the NCDWQ Sub-basin 03-06-12 of the Cape Fear River Basin. The project restored approximately 2,378 linear feet of channel - 1,921 feet on UT Bear Creek and 457 feet on unnamed tributary 2 (UT2) - and enhanced an additional 935 feet of channel on UT2. The NCDOT completed project construction in 2006, after which the project was transferred to the North Carolina Ecosystem Enhancement Program (EEP). Project goals and objectives are listed below:

Project Goals:

- Improve water quality.
- Improve riparian and in-stream habitat

Project Objectives:

- Excluding cattle from the stream channels.
- Increasing channel stability.
- Restoring dimension, pattern, and profile to UT Bear Creek and UT 2.

The riparian buffer was planted with five different species of bare root trees and two different species of live stakes. Seven vegetation monitoring plots were established in 2009, the first year of monitoring. These plots were set up following the Carolina Vegetation Survey (CVS) vegetation monitoring protocol. Based on the seven monitoring plots, the fifth-year monitoring counted an average of 399 planted stems/acre across the site. Plot 7 is the only plot that has a planted stem density less than the year five success criteria of 260 stems/acre. This plot has 202 planted stems/acre and 1,052 total stems/acre, including volunteers. The site's average stem density including volunteers is 1,549 stems/acre. Three prominent exotic invasive species found within the project buffer are Chinese privet (*Ligustrum sinense*), Japanese honeysuckle (*Lonicera japonica*), and microstegium (*Microstegium vimineum*), with the privet being especially thick in certain areas. The areas of privet have been mapped on the CCPV. Plot 4 contains one stem of princess tree (*Paulownia tomentosa*). The presence of this invasive species is limited and is not widespread throughout the site. Supplemental planting of the site was conducted in November of 2013. Five separate zones were planted throughout the easement totaling approximately 0.9 acres. Please see Appendix C for the Supplemental Planting List and Plan.

There are two hydrologic features on the site. The first, UT Bear Creek, has been restored by altering the dimension, pattern, and profile and is controlled vertically by numerous bedrock outcrops and cross vanes. The second feature is UT 2 and it has been divided into two reaches, UT 2A, which was enhanced, and UT 2B, which was restored. UT 2A is a straight channel that begins at Station 30+00. This reach already had banks stabilized by the mature trees that line both sides of the channel for the length of the reach. This reach was enhanced by planting native vegetation in the riparian buffer beyond the top of bank. UT 2B begins where UT 2A ends at the ford crossing at Station 39+75. This reach was restored by changing the dimension, pattern and profile of the channel from the ford to the confluence with UT Bear Creek.

During the fifth-year monitoring the site was also examined for stream stability and potential problem areas. UT Bear Creek is predominantly stable throughout the project. There is one area of floodplain erosion that has been noted in previous reports and is no longer active. The area has now filled in with vegetation. The beaver dam noted in previous year's monitoring reports that was creating backwater conditions in the lower portions of UT Bear Creek has been removed. The areas that had been flooded and had low planted stem density have been replanted. UT 2 is predominantly stable. There are two

localized areas of erosion and bed degradation on UT 2. The first is at the cross vane at Station 40+00 and the second area is along the channel at Station 43+00 where there is a small head cut.

Summary information/data related to the occurrence of items such as beaver or encroachment and statistics related to performance of various project and monitoring elements can be found in the tables and figures in the report appendices. Narrative background and supporting information formerly found in these reports can be found in the Baseline Monitoring Report (formerly Mitigation Plan) and in the Mitigation Plan (formerly the Restoration Plan) documents available on the EEP's website. All raw data supporting the tables and figures in the appendices are available from EEP upon request.

2.0 METHODOLOGY

The Level 2 CVS-EEP protocol (<http://cvs.bio.unc.edu/methods.htm>) was used to collect vegetation data from UT Bear Creek.

3.0 REFERENCES

Lee, M.T., R. K. Peet, S. D. Roberts, and T. R. Wentworth. 2006. CVS-EEP Protocol for Recording Vegetation, Version 4.0 (<http://cvs.bio.unc.edu/methods.htm>)

Weakley, A.S. 2006. Flora of the Carolinas, Virginia, Georgia, and Surrounding Areas. (http://www.herbarium.unc.edu/FloraArchives/WeakleyFlora_2006-Jan.pdf)

Appendix A

Project Vicinity Map and Background Tables

DIRECTIONS TO UT BEAR CREEK SITE:
From Raleigh, take US 440 West towards US 1 South. Take the exit for 64 East, then take 15/501 South towards Pittsboro. At the circle take a right onto West St. Then take a left onto NC 902. After going through the community of Bear Creek, take a right onto Edwards Hill Church Rd. The site is on the eastern side of the road. Enter the site through gate.

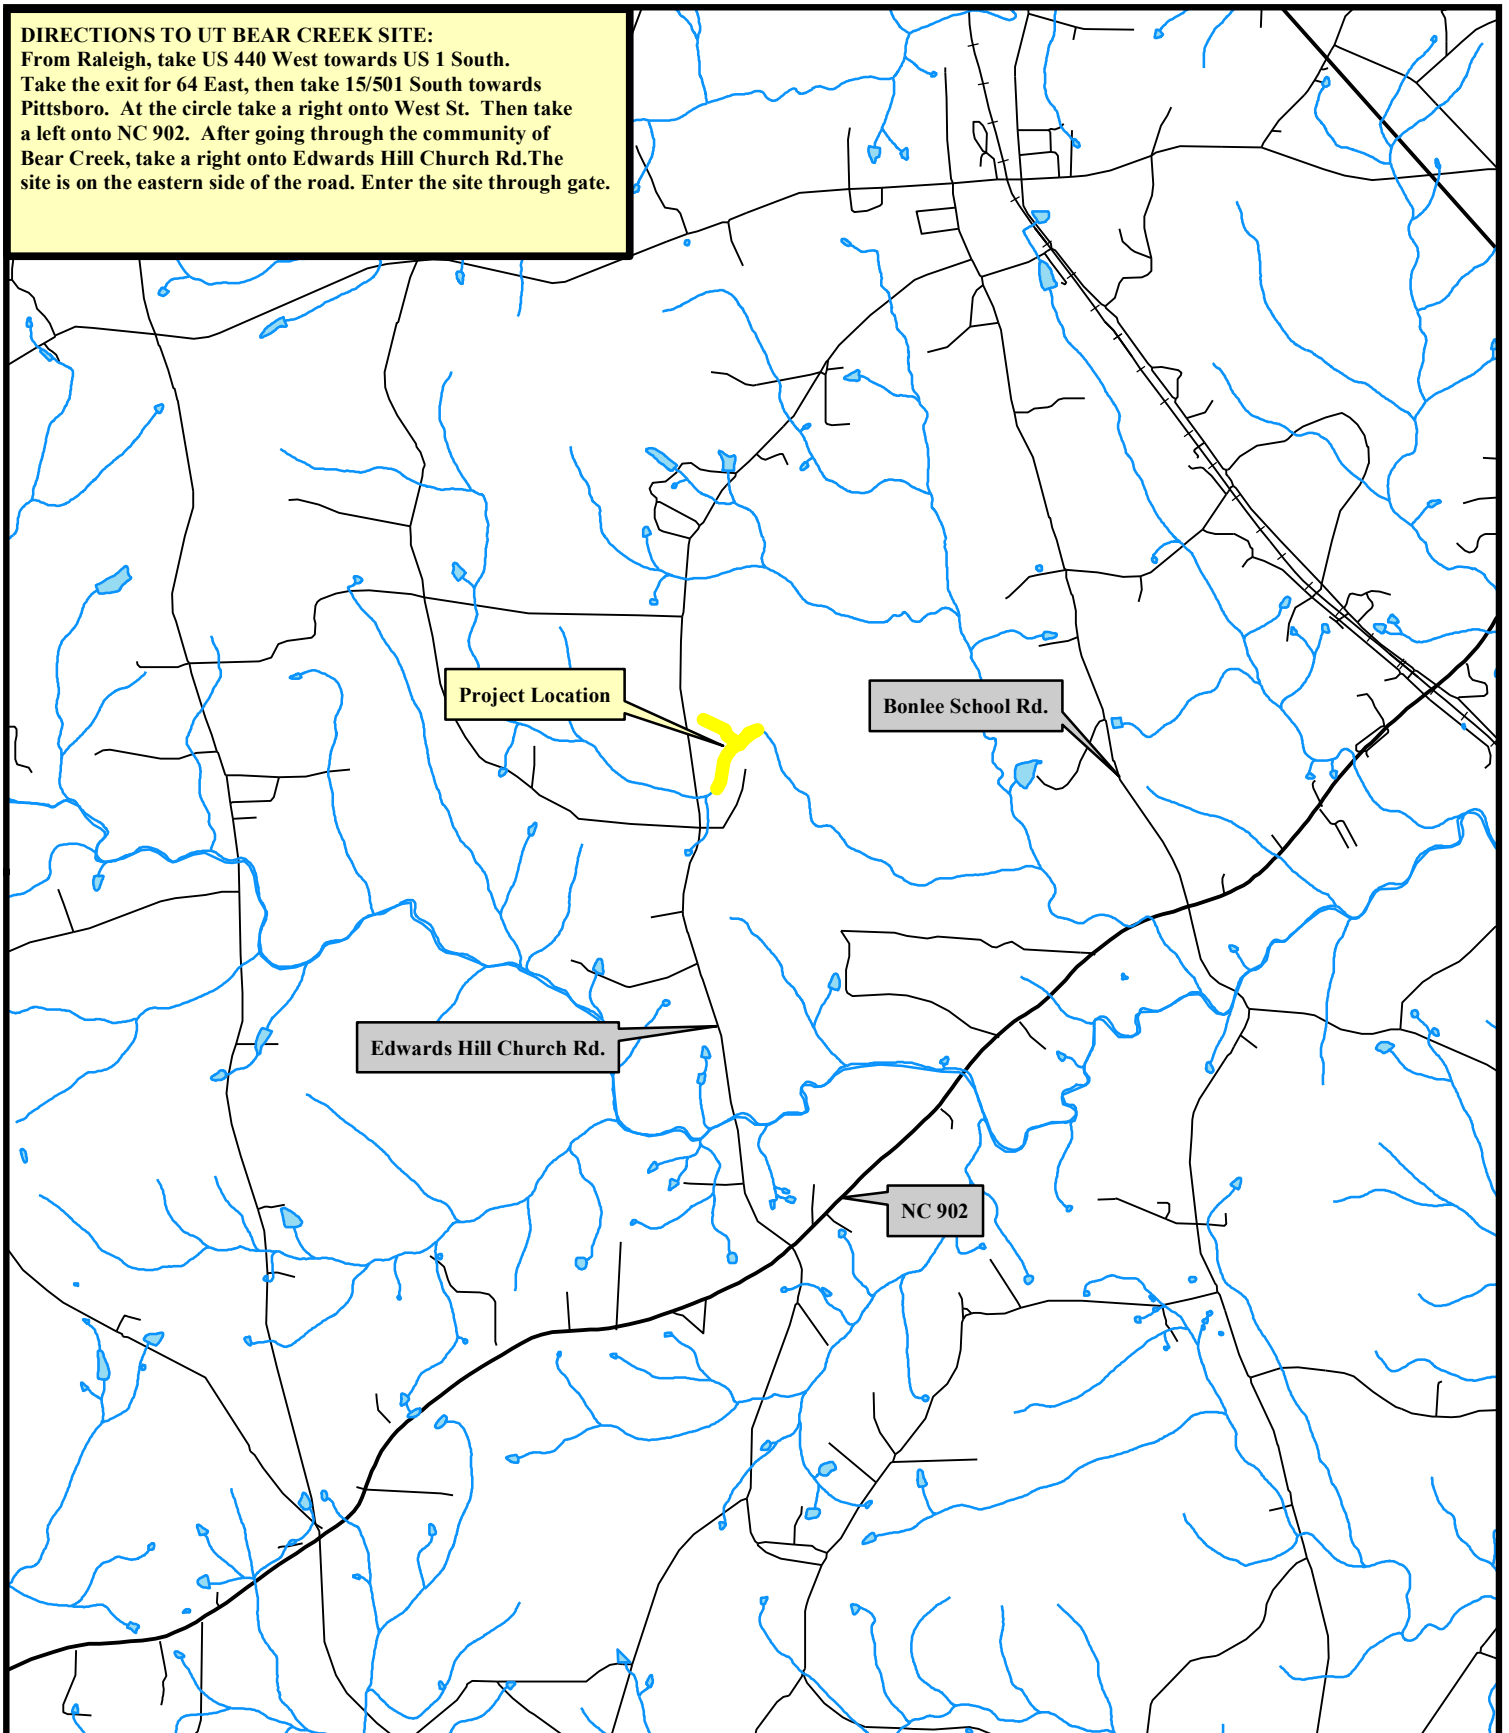


Figure 1. Site Vicinity Map
UT Bear Creek, Chatham County, EEP Project # 92719




Table 1a. Project Components								
Project Number and Name: 92719 - UT Bear Creek (Phillips)								
Project Component or Reach ID	Existing Feet/Acres	Restoration Level	Approach	Footage or Acreage	Stationing	Buffer Acres	BMP Elements	Comment
UT Bear Creek	1,926	R	P2	1,942	10+00 - 29+77			Linear footage does not include stream length in easement exceptions
UT2A	935	EII	-	900	30+00 - 39+75			Linear footage does not include stream length in easement exceptions
UT2B	420	R	P2	457	39+75 - 44+32			

Table 1b. Component Summations							
Project Number and Name: 92719 - UT Bear Creek (Phillips)							
Restoration Level	Stream (lf)	Riparian Wetland (Ac)		Non-Riparian (Ac)	Upland (Ac)	Buffer (Ac)	BMP
		Riverine	Non-Riverine				
Restoration	2,399						
Enhancement							
Enhancement I							
Enhancement II	900						
Creation							
Preservation							
HQ Preservation							
Totals	3,299						
MU Totals	2,759						

Table 2. Project Activity and Reporting History		
Project Number and Name: 92719 - UT Bear Creek (Phillips)		
Elapsed Time Since Grading Complete: 6 yr		
Elapsed Time Since Planting Complete: 6 yr		
Number of Reporting Years: 4		
Activity or Report	Data Collection Complete	Actual Completion or Delivery
Concept Plan		2002
Restoration Plan		Jun 03
Final Design - 90%		
Construction		2006
As-Built Survey		Mar 06
Live Stake Planting		
Riparian Buffer Planting		
Year 1 Monitoring	Oct 2009	Dec 2009
Year 2 Monitoring	Oct 2010	Dec 2010
Year 3 Monitoring	Oct 2011	Dec 2011
Year 4 Monitoring	Oct 2012	Nov 2012
Year 5 Monitoring	Oct 2013	Nov 2013
Supplemental Planting		Nov 2013

Table 3. Project Contacts Table	
Project Number and Name: 92719 - UT Bear Creek (Phillips)	
Design Firm	Environmental Services, Inc. 524 South New Hope Road Raleigh, North Carolina 27610 Contact: Mr. Ron Spears Phone: (919) 212-1760
Construction Contractor	Unknown
Planting Contractor	Unknown
Supplemental Planting Contractor	Carolina Silvics, inc. 908 Indian Trail Road Edenton, NC 27932
Monitoring Performers	
MY-01-05	KCI Associates of NC Landmark Center II, Suite 220 4601 Six Forks Rd. Raleigh, NC 27609 Contact: Mr. Adam Spiller Phone: (919) 278-2514 Fax: (919) 783-9266

Table 4. Project Attribute Table			
Project Number and Name: 92719 - UT Bear Creek (Phillips)			
Project County	Chatham County		
Physiographic Region	Piedmont		
Ecoregion	Carolina Slate Belt		
Project River Basin	Cape Fear		
USGS HUC for Project (14 digit)	03030003070050		
NCDWQ Sub-basin for Project	03-06-12		
Within extent of EEP Watershed Plan?	U		
WRC Class (Warm, Cool, Cold)	Warm		
% of project easement demarcated	100%		
Beaver activity observed during design phase?	Yes		
Restoration Component Attribute Table			
	UT Bear Creek	UT 2	
Drainage Area	1.7 sq. mi.	0.15 sq. mi.	
Stream Order	Second	First	
Restored length (feet)	1,921	457	
Perennial or Intermittent	Perennial	Perennial	
Watershed Type (Rural, Urban, Developing, etc.)	Rural		
Watershed LULC Distribution			
Urban	U		
Ag-Row Crop	U		
Ag-Livestock	U		
Forested	U		
Water/Wetlands	U		
Watershed impervious cover (%)	<10%		
NCDWQ AU/Index Number	U		
NCDWQ Classification	C (UT Bear Creek)		
303d listed?	No		
Upstream of a 303d listed segment?	No		
Reasons for 303d Listing or Stressor	-		
Total acreage of easement	11.9		
Total vegetated acreage within the easement	11.9		
Total planted acreage as part of the restoration	11.0		
Rosgen Classification of pre-existing	-	-	
Rosgen Classification of As-built	C4/5	C4/5	
Valley Type	U	U	
Valley Slope	U	U	
Valley side slope range (e.g. 2-3%)	U	U	
Valley toe slope range (e.g. 2-3%)	U	U	
Trout waters designation	No		
Species of concern, endangered etc.? (Y/N)	No		
Dominant soil series and characteristics			
Series	Cid-Lignum Complex		
Depth Clay%	-	-	
K	-	-	
T	-	-	

"N/A" is for items that do not apply.

"-" is for items that are unavailable.

"U" is for items that are unknown.

Appendix B

Visual Assessment Data



LEGEND

- EASEMENT BOUNDARY [dashed line symbol]
- DESIGNED STATIONED CENTERLINE AND TOP OF BANK [solid line with offset symbol]
- OLD STREAM CENTERLINE [dotted line symbol]
- PHOTO POINT [red circle with arrow symbol]
- ROCK CROSS VANE & J-HOOK [rock symbol]
- ROOTWAD [rootwad symbol]

PROJECT CONDITION

- STREAM BED DEGRADATION [pink line symbol]
- BANK EROSION [yellow line symbol]
- VEG PLOT ABOVE 320 TOTAL PLANTED STEMS/ACRE [green square symbol]
- VEG PLOT BELOW 320 TOTAL PLANTED STEMS/ACRE [yellow square symbol]
- LOW PLANTED STEM DENSITY [green hatched square symbol]
- INVASIVE SPECIES [green cross-hatched square symbol]
- VEG PLOT TOTAL / PLANTED STEM DENSITY 1376/376
- STRUCTURE PIPING P
- STRUCTURE NOT PROTECTING BANKS B

NOTE: ALL MAPPED INVASIVE SPECIES ARE CHINESE PRIVET (LIGUSTRUM SINENSE)

IMAGE SOURCE: NC 2010 STATEWIDE ORTHOIMAGERY



SYMBOL	DESCRIPTION	DATE	APPROVED



KCI
ASSOCIATES OF INC
ENGINEERS • PLANNERS • SCIENTISTS
4801 SIX FORKS ROAD
RALEIGH, NORTH CAROLINA 27609

UT BEAR CREEK (PHILLIPS)
CHATHAM COUNTY, NORTH CAROLINA
EEP PROJECT NUMBER 92719 - MY05
REACH: UT BEAR CREEK

DATE: NOV 2013
SCALE: 1" = 100'
CURRENT CONDITION PLAN VIEW
SHEET 1 OF 2

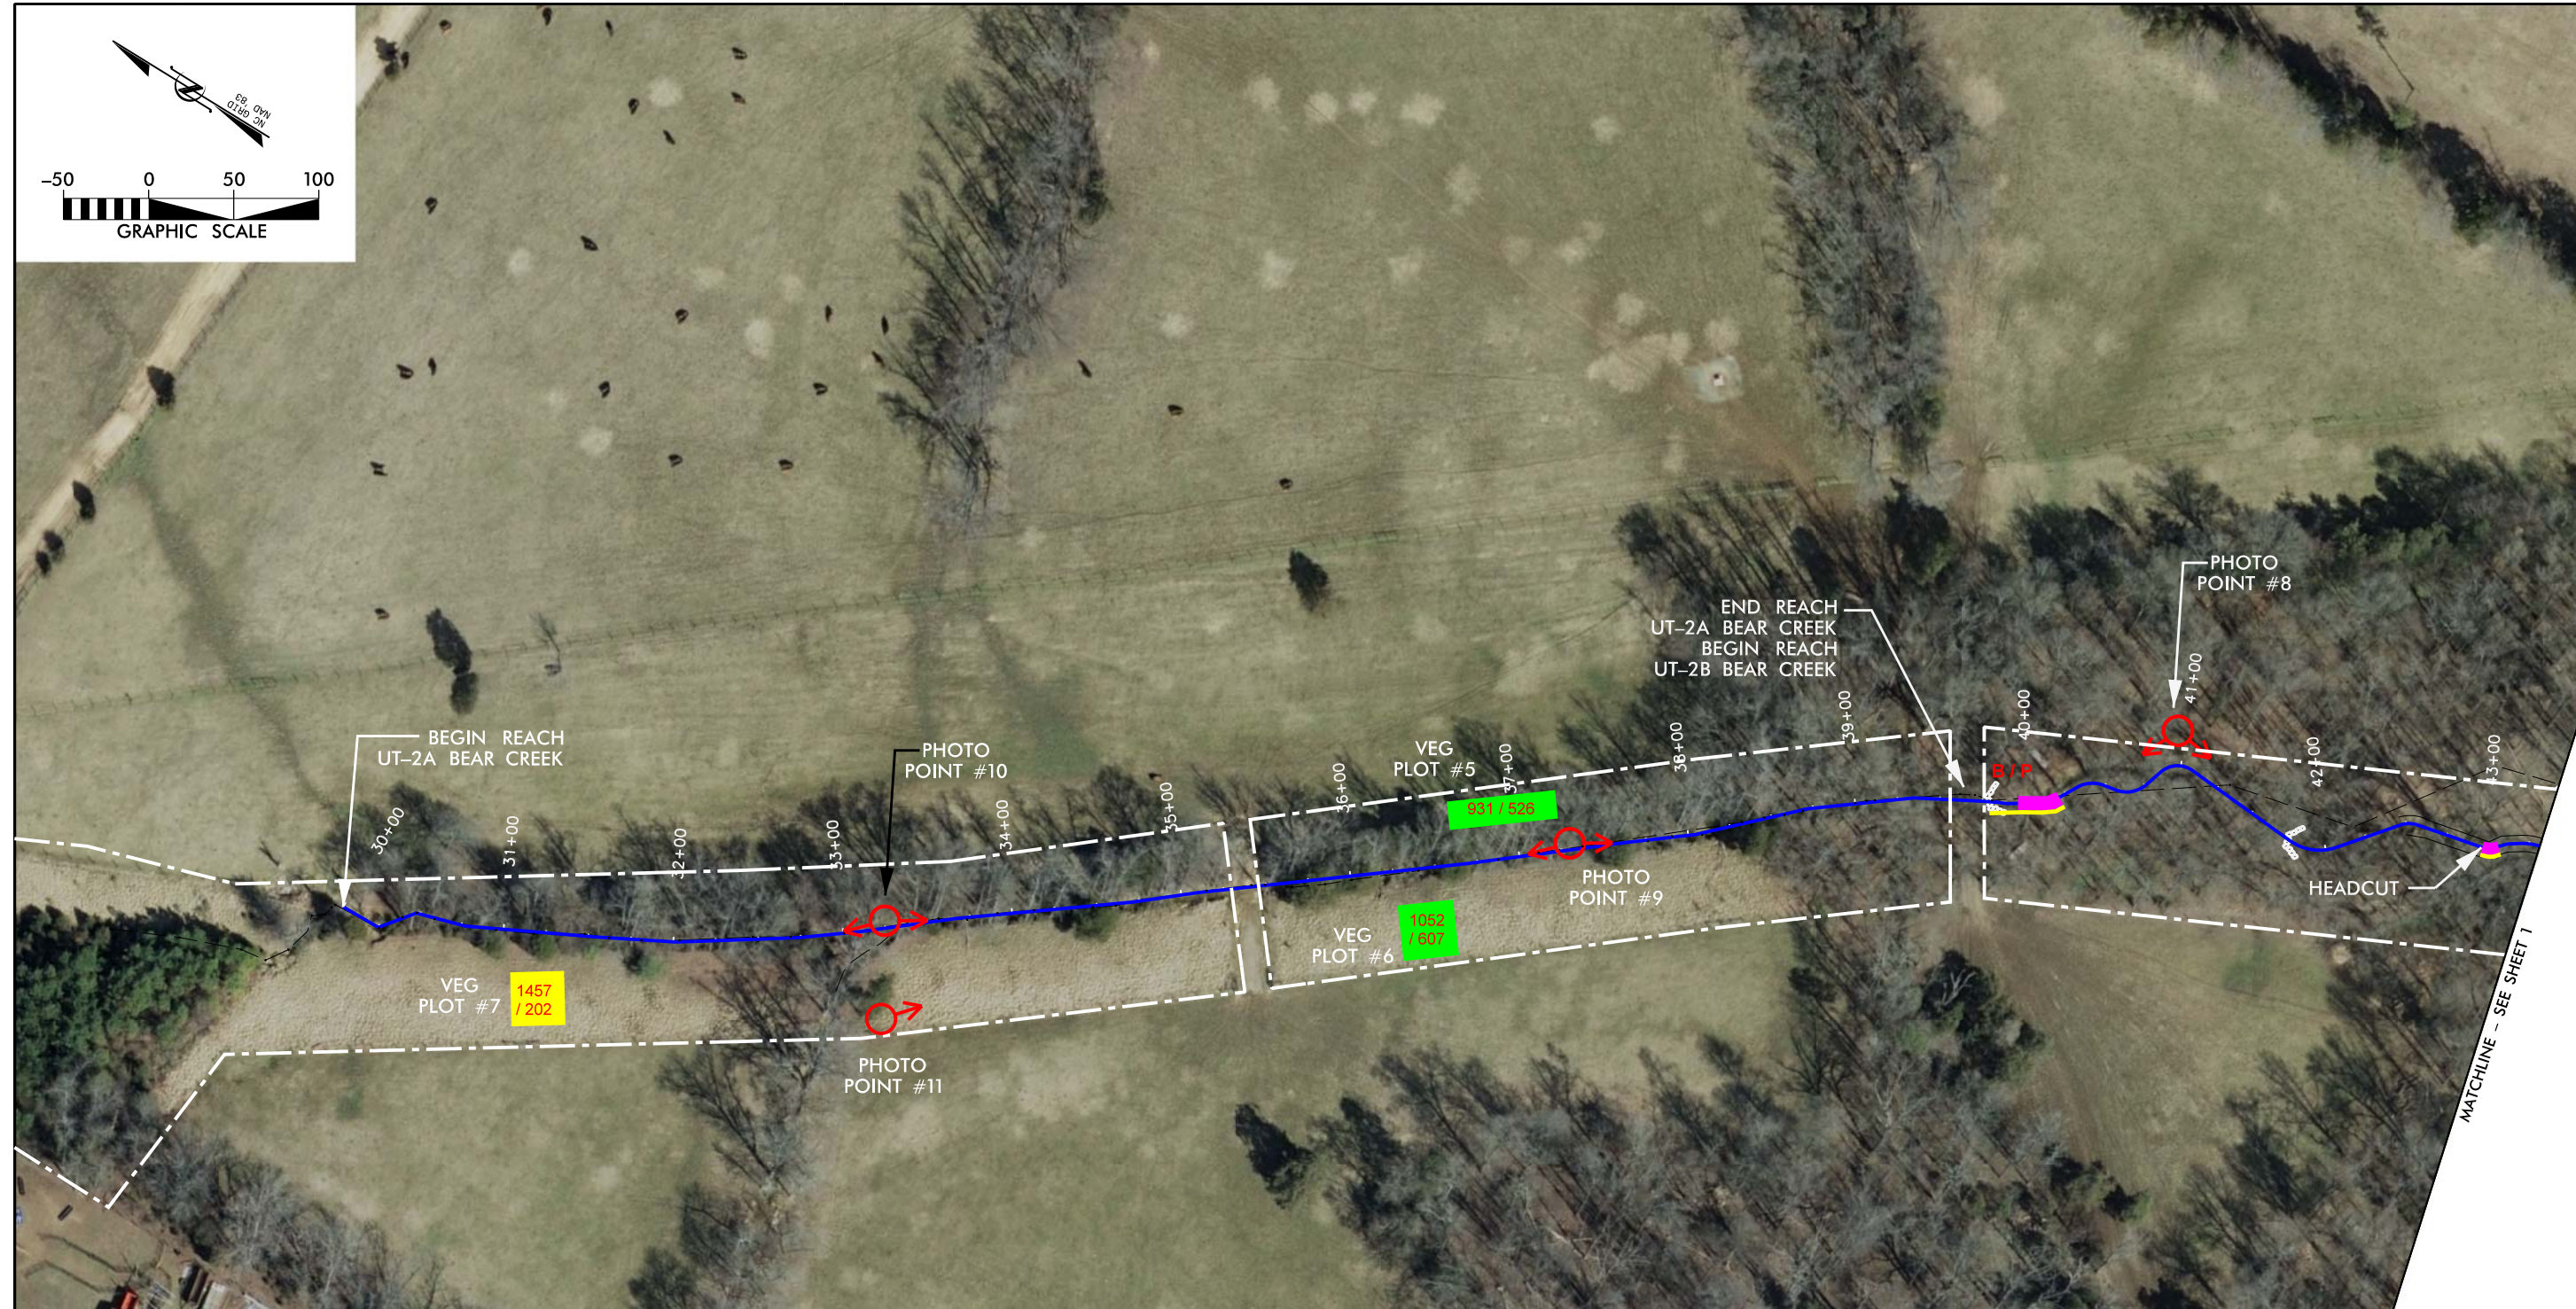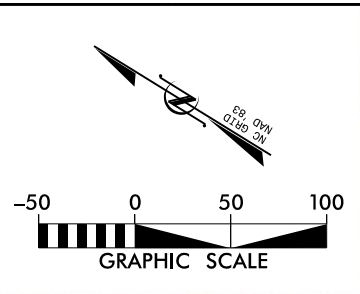

LEGEND

- EASEMENT BOUNDARY [Symbol]
- DESIGNED STATIONED CENTERLINE AND TOP OF BANK [Symbol]
- OLD STREAM CENTERLINE [Symbol]
- PHOTO POINT [Symbol]
- ROCK CROSS VANE & J-HOOK [Symbol]
- ROOTWAD [Symbol]

PROJECT CONDITION

- STREAM BED DEGRADATION [Symbol]
- BANK EROSION [Symbol]
- VEG PLOT ABOVE 320 TOTAL PLANTED STEMS/ACRE [Symbol]
- VEG PLOT BELOW 320 TOTAL PLANTED STEMS/ACRE [Symbol]
- LOW PLANTED STEM DENSITY [Symbol]
- INVASIVE SPECIES [Symbol]
- VEG PLOT TOTAL / PLANTED STEM DENSITY 1376/376
- STRUCTURE PIPING P
- STRUCTURE NOT PROTECTING BANKS B

NOTE: ALL MAPPED INVASIVE SPECIES ARE CHINESE PRIVET (LIGUSTRUM SINENSE)

SYN.	DESCRIPTION	DATE	APPROVED



KCI
ASSOCIATES OF INC
ENGINEERS • PLANNERS • SCIENTISTS
4801 SIX FORKS ROAD
RALEIGH, NORTH CAROLINA 27609

UT BEAR CREEK (PHILLIPS)
CHATHAM COUNTY, NORTH CAROLINA
EEP PROJECT NUMBER 92719 - MY05
REACHES: UT-2A AND UT-2B BEAR CREEK

DATE: NOV 2013
SCALE: 1" = 100'
CURRENT CONDITION PLAN VIEW
SHEET 2 OF 2

Table 5a. Visual Stream Morphology Stability Assessment							
Project Number and Name: 92719 - UT Bear Creek							
Assessed Length 1,921				Reach - UT Bear Creek			
Major Channel Category	Channel Category	Sub-Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%
		2. <u>Degradation</u> - Evidence of downcutting			0	0	100%
	2. Riffle Condition*	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate					N/A
	3. Meander Pool Condition*	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth ≥ 1.6)					N/A
		2. <u>Length</u> appropriate ($>30\%$ of centerline distance between tail of upstream riffle and head of downstream riffle)					N/A
	4. Thalweg Position*	1. Thalweg centering at upstream of meander bend (Run)					N/A
2. Thalweg centering at downstream of meander (Glide)						N/A	
2. Bank	1. Scoured/ Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			0	0	100%
	2. Undercut	Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.			0	0	100%
	3. Mass Wasting	Bank slumping, calving, or collapse			0	0	100%
Totals					0	0	100%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	9	9			100%
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	6	6			100%
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	9	9			100%
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	9	9			100%
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio ≥ 1.6 Rootwads/logs providing some cover at base-flow.	9	9			100%

* A longitudinal profile is not a component of monitoring UT Bear Creek. The visual assessment found a diverse bed morphology with pools and riffles that are strongly influenced by bedrock.

Table 5b. Visual Stream Morphology Stability Assessment							
Project Number and Name: 92719 - UT Bear Creek							
Assessed Length 457				Reach - UT 2B			
Major Channel Category	Channel Category	Sub-Metric	Number Stable, Performing as Intended	Total Number in As-built	Number of Unstable Segments	Amount of Unstable Footage	% Stable, Performing as Intended
1. Bed	1. Vertical Stability (Riffle and Run units)	1. <u>Aggradation</u> - Bar formation/growth sufficient to significantly deflect flow laterally (not to include point bars)			0	0	100%
		2. <u>Degradation</u> - Evidence of downcutting			1	20	96%
	2. Riffle Condition*	1. <u>Texture/Substrate</u> - Riffle maintains coarser substrate					N/A
	3. Meander Pool Condition*	1. <u>Depth</u> Sufficient (Max Pool Depth : Mean Bankfull Depth \geq 1.6)					N/A
		2. <u>Length</u> appropriate (>30% of centerline distance between tail of upstream riffle and head of downstream riffle)					N/A
	4. Thalweg Position*	1. Thalweg centering at upstream of meander bend (Run)					N/A
		2. Thalweg centering at downstream of meander (Glide)			N/A		
	2. Bank	1. Scoured/ Eroding	Bank lacking vegetative cover resulting simply from poor growth and/or scour and erosion			2	40
Banks undercut/overhanging to the extent that mass wasting appears likely. Does <u>NOT</u> include undercuts that are modest, appear sustainable and are providing habitat.					1	5	99%
2. Undercut					0	0	100%
		3. Mass Wasting	Bank slumping, calving, or collapse				
Totals					3	45	95%
3. Engineered Structures	1. Overall Integrity	Structures physically intact with no dislodged boulders or logs.	3	4			75%
	2. Grade Control	Grade control structures exhibiting maintenance of grade across the sill.	4	4			100%
	2a. Piping	Structures lacking any substantial flow underneath sills or arms.	3	4			75%
	3. Bank Protection	Bank erosion within the structures extent of influence does <u>not</u> exceed 15%. (See guidance for this table in EEP monitoring guidance document)	3	4			75%
	4. Habitat	Pool forming structures maintaining ~ Max Pool Depth : Mean Bankfull Depth ratio \geq 1.6 Rootwads/logs providing some cover at base-flow.	3	3			100%

* A longitudinal profile is not a monitoring component for this tributary. During the visual assessment the only water in the channel was from the UT Bear Creek backwater, which made the evaluation of bed features difficult.

Table 6. Vegetation Condition Assessment						
Project Number and Name: 92719 - UT Bear Creek (Phillips)						
Planted Acreage 11.0			Easement Acreage 11.9			
Vegetation Category	Definitions	Mapping Threshold	CCPV Depiction	Number of Polygons	Combined Acreage	% of Planted Acreage
1. Bare Areas	Very limited cover of both woody and herbaceous material.	0.1 acres	Pattern and Color	0	0.00	0.0%
2. Low Stem Density Areas	Woody stem densities clearly below target levels based on MY3, 4, or 5 stem count criteria.	0.1 acres	Pattern and Color	0	0.00	0.0%
Total				0	0.00	0.0%
3. Areas of Poor Growth Rates or Vigor	Areas with woody stems of a size class that are obviously small given the monitoring year.	0.25 acres	Pattern and Color	0	0.00	0.0%
Cumulative Total				0	0.00	0.0%
4. Invasive Areas of Concern	Areas or points (if too small to render as polygons at map scale).	1000 SF	Pattern and Color	14	0.62	5.2%
5. Easement Encroachment Areas	Areas or points (if too small to render as polygons at map scale).	none	Pattern and Color	0	0.00	0.0%

Stream Station Photos



PP#1 – MY01 – 11/17/09



PP#1 – MY05 – 11/22/2013



PP#2d – MY01 – 11/17/09



PP#2d – MY05 – 11/22/2013



PP#2u – MY01 – 11/17/09



PP#2u – MY05 – 11/22/2013



PP#3d – MY01 – 11/17/09



PP#3d – MY05 – 11/22/2013



PP#3u – MY01 – 11/17/09



PP#3u – MY05 – 11/22/2013



PP#4d – MY01 – 11/17/09



PP#4d – MY05 – 11/22/2013



PP#4u – MY01 – 11/17/09



PP#4u – MY05 – 11/22/2013



PP#5d – MY01 – 11/17/09



PP#5d – MY05 – 11/22/2013



PP#5u – MY01 – 11/17/09



PP#5u – MY05 – 11/22/2013



PP#6 – MY01 – 11/17/09



PP#6 – MY05 – 11/22/2013



PP #7d – MY01 – 11/17/09



PP#7d – MY05 – 11/22/2013



PP#7u – MY01 – 11/17/09



PP#7u – MY05 – 11/22/2013



PP#8d- MY01 - 11/17/09



PP#8d - MY05 - 11/22/2013



PP#8u - MY01 - 11/17/09



PP#8u - MY05 - 11/22/2013



PP#9d - MY01 - 11/17/09



PP#9d - MY05 - 11/22/2013



PP#9u – MY01 – 11/17/09



PP#9u – MY05 – 11/22/2013



PP#10d – MY01 – 11/17/09



PP#10d – MY05 – 11/22/2013



PP#10u – MY01 – 11/17/09



PP#10u – MY05 – 11/22/2013



PP#11 – MY01 – 11/17/09



PP#11 – MY05 – 11/22/2013

Vegetation Monitoring Plot Photos



Vegetation Plot 1: 7/16/13 – MY-05



Vegetation Plot 2: 7/16/13 – MY-05



Vegetation Plot 3: 7/16/13 – MY-05



Vegetation Plot 4: 7/16/13 – MY-05



Vegetation Plot 5: 7/16/13 – MY-05



Vegetation Plot 6: 7/16/13 – MY-05



Vegetation Plot 7: 7/16/13 – MY-05

Appendix C

Vegetation Plot Data

Table 7. Vegetation Plot Mitigation Success Summary Table

Project Number and Name: 92719 - UT Bear Creek (Phillips)

Vegetation Plot ID	Monitoring Year 05 Planted Stem Density (stems/acre)	Vegetation Survival Threshold Met?	Monitoring Year 05 Total Stem Density (stems/acre)
1	283	Yes	2,711
2	364	Yes	1,102
3	324	Yes	1,902
4	324	Yes	567
5	526	Yes	931
6	607	Yes	1,051
7	202	No	1,457

Table 8. CVS Vegetation Plot Metadata	
Project Number and Name: 92719 - UT Bear Creek (Phillips)	
Report Prepared By	April Helms
Date Prepared	10/30/2013 9:11
database name	KCI-2012-A.mdb
database location	M:\2007\12071067_2007 EEP OPEN END\Veg_database
computer name	12-CV76KF1
file size	59768832
DESCRIPTION OF WORKSHEETS IN THIS DOCUMENT-----	
Metadata	Description of database file, the report worksheets, and a summary of project(s) and project data.
Proj, planted	Each project is listed with its PLANTED stems per acre, for each year. This excludes live stakes.
Proj, total stems	Each project is listed with its TOTAL stems per acre, for each year. This includes live stakes, all planted stems, and all natural/volunteer stems.
Plots	List of plots surveyed with location and summary data (live stems, dead stems, missing, etc.).
Vigor	Frequency distribution of vigor classes for stems for all plots.
Vigor by Spp	Frequency distribution of vigor classes listed by species.
Damage	List of most frequent damage classes with number of occurrences and percent of total stems impacted by each.
Damage by Spp	Damage values tallied by type for each species.
Damage by Plot	Damage values tallied by type for each plot.
Planted Stems by Plot and Spp	A matrix of the count of PLANTED living stems of each species for each plot; dead and missing stems are excluded.
ALL Stems by Plot and spp	A matrix of the count of total living stems of each species (planted and natural volunteers combined) for each plot; dead and missing stems are excluded.
PROJECT SUMMARY-----	
Project Code	92719
Project Name	UT Bear Creak (Phillips)
Description	Stream Restoration and Enhancement in Chatham County, NC.
River Basin	Cape Fear
length(ft)	3,313
stream-to-edge width (ft)	40
area (sq m)	22294
Required Plots (calculated)	7
Sampled Plots	7

Table 9. CVS Stem Count Total and Planted by Plot and Species																							
Project Number and Name: 92719 – UT Bear Creek (Phillips)																							
		Current Plot Data (MY5 2013)																					
Scientific Name	Common Name	Species Type	92719-A-0001			92719-A-0002			92719-A-0003			92719-A-0004			92719-A-0005			92719-A-0006			92719-A-0007		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
<i>Acer rubrum</i>	red maple	Tree			4																		
<i>Asimina triloba</i>	pawpaw	Tree																					
<i>Baccharis</i>	baccharis	Shrub						1			1												
<i>Baccharis halimifolia</i>	eastern baccharis	Shrub																					
<i>Diospyros virginiana</i>	common persimmon	Tree				1	1	1															27
<i>Fraxinus pennsylvanica</i>	green ash	Tree	2	2	39	5	5	7	1	1	2	1	1	1	13	13	13	7	7	7	4	4	5
<i>Juglans nigra</i>	black walnut	Tree										1	1	2									
<i>Juniperus virginiana</i>	eastern redcedar	Tree									16									1			
<i>Ligustrum sinense</i>	Chinese privet	Exotic																					
<i>Liquidambar styraciflua</i>	sweetgum	Tree			3																		
<i>Morus</i>	mulberry	Tree																					
<i>Morus rubra</i>	red mulberry	Tree												1									
<i>Paulownia tomentosa</i>	princesstree	Exotic												1									
<i>Pinus taeda</i>	loblolly pine	Tree			1																		
<i>Platanus occidentalis</i>	American sycamore	Tree	5	5	12							1	1	2						3			
<i>Prunus serotina</i>	black cherry	Tree						1															
<i>Quercus falcata</i>	southern red oak	Tree																					
<i>Quercus lyrata</i>	overcup oak	Tree			1																		
<i>Quercus michauxii</i>	swamp chestnut oak	Tree				2	2	2				2	2	2				6	6	6			
<i>Quercus phellos</i>	willow oak	Tree				1	1	1	7	7	11	3	3	5				2	2	3	1	1	4
<i>Quercus rubra</i>	northern red oak	Tree																					
<i>Rhus</i>	sumac	shrub						5															
<i>Rhus copallinum</i>	flameleaf sumac	shrub																					
<i>Rhus glabra</i>	smooth sumac	shrub																					
<i>Robinia pseudoacacia</i>	black locust	Tree			3						8												
<i>Salix nigra</i>	black willow	Tree																					
<i>Sassafras</i>	sassafras																						
<i>Ulmus alata</i>	winged elm	Tree			4			7			9						6			9			
<i>Ulmus americana</i>	American elm	Tree																					
<i>Ulmus rubra</i>	slippery elm	Tree																					
Stem count			7	7	67	9	9	25	8	8	47	8	8	14	13	13	23	15	15	26	5	5	36
size (ares)			1			1			1			1			1			1			1		
size (ACRES)			0.02			0.02			0.02			0.02			0.02			0.02			0.02		
Species count			2	2	8	4	4	8	2	2	6	5	5	7	1	1	4	3	3	5	2	2	3
Stems per ACRE			283	283	2,711	364	364	1,012	324	324	1,902	324	324	567	526	526	931	607	607	1,052	202	202	1,457

P-LS – Planted Live Stakes

P-all – Planted Stems Total (with Live Stakes)

T – Total (Planted Including Live Stakes and Volunteers)



Table 9. CVS Stem Count Total and Planted by Plot and Species continued																	
Project Number and Name: 92719 – UT Bear Creek (Phillips)																	
			Annual Means														
Scientific Name	Common Name	Species Type	MY5 (2013)			MY4 (2012)			MY3 (2011)			MY2 (2010)			MY1 (2009)		
			PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T	PnoLS	P-all	T
Acer rubrum	red maple	Tree			5			5			6						2
Asimina triloba	pawpaw	Tree						2									
Baccharis	baccharis	Shrub			2			3			3						4
Baccharis halimifolia	eastern baccharis	Shrub											1				
Diospyros virginiana	common persimmon	Tree	1	1	28	1	1	16	1	1	15	1	1	1	1	1	17
Fraxinus pennsylvanica	green ash	Tree	33	33	74	35	35	115	35	35	105	35	35	57	36	36	135
Juglans nigra	black walnut	Tree	1	1	2	1	1	3	1	1	6	1	1	1			9
Juniperus virginiana	eastern redcedar	Tree			17			14			11						3
Ligustrum sinense	Chinese privet	Exotic															10
Liquidambar styraciflua	sweetgum	Tree			3			2			7			5			15
Morus	mulberry	Tree															2
Morus rubra	red mulberry	Tree			1												
Paulownia tomentosa	princesstree	Exotic			1			1									1
Pinus taeda	loblolly pine	Tree			1												
Platanus occidentalis	American sycamore	Tree	6	6	17	7	7	11	7	7	7	7	7	7	7	7	7
Prunus serotina	black cherry	Tree			1			1			1						2
Quercus falcata	southern red oak	Tree						1									
Quercus lyrata	overcup oak	Tree			1	1	1	2	1	1	1	1	1	1	1	1	1
Quercus michauxii	swamp chestnut oak	Tree	10	10	10	10	10	10	10	10	10	11	11	11	12	12	12
Quercus phellos	willow oak	Tree	14	14	24	14	14	27	14	14	31	14	14	23	14	14	23
Quercus rubra	northern red oak	Tree									1						
Rhus	sumac	shrub			5			5						1			
Rhus copallinum	flameleaf sumac	shrub									5						
Rhus glabra	smooth sumac	shrub															1
Robinia pseudoacacia	black locust	Tree			11			19			3						4
Salix nigra	black willow	Tree															1
Sassafras	sassafras							1									
Ulmus alata	winged elm	Tree			35			30			47			1			3
Ulmus americana	American elm	Tree															4
Ulmus rubra	slippery elm	Tree															39
	Stem count		65	65	238	69	69	268	69	69	259	70	70	109	71	71	295
	size (ares)			7			7			7			7			7	
	size (ACRES)			0.17			0.17			0.17			0.17			0.17	
	Species count		6	6	18	7	7	19	7	7	16	7	7	11	6	6	21
	Stems per ACRE		376	376	1,376	399	399	1,549	399	399	1,497	405	405	630	410	410	1,705

Table 10. Supplemental Planting Species List			
Project Number and Name: 92719 - UT Bear Creek (Phillips)			
Region/Community Type: Piedmont/Riparian			
Species	Type	Quantity	Percentage
<i>Acer barbatum</i>	Container		0%
<i>Acer negundo</i>	Container	13	6%
<i>Betula nigra</i>	Container	30	15%
<i>Carya glabra</i>	Container		0%
<i>Carya ovata</i>	Container		0%
<i>Carya tomentosa</i>	Container		0%
<i>Celtis laevigata</i>	Container		0%
<i>Fraxinus pennsylvanica</i>	Container	9	4%
<i>Liriodendron tulipifera</i>	Container	37	18%
<i>Nyssa sylvatica var sylvatica</i>	Container	20	10%
<i>Platanus occidentalis</i>	Container	35	17%
<i>Populus deltoides</i>	Container	9	4%
<i>Quercus coccinea</i>	Container		0%
<i>Quercus michauxii</i>	Container	5	2%
<i>Quercus nigra</i>	Container		0%
<i>Quercus falcata var. pagodafolia</i>	Container		0%
<i>Quercus palustris</i>	Container	15	7%
<i>Quercus phellos</i>	Container	15	7%
<i>Quercus rubra</i>	Container		0%
<i>Quercus shumardii</i>	Container		0%
<i>Ulmus americana</i>	Container	8	4%
<i>Diospyros virginiana</i>	Container	8	4%
<i>Ostrya virginiana</i>	Container		0%
TOTALS		204	100%

Supplemental Planting Plan
UT Bear Creek (Phillips)
EEP #32719
Chatham County, NC
 May 2013

Legend

- Site Entry
- Staging Area
- Site Access
- 2013_01 Planting Zones**
- Plant_Zone**
- Riparian
- Wetland (Bottomland)
- Wetland (Obligate)
- Conservation Easement

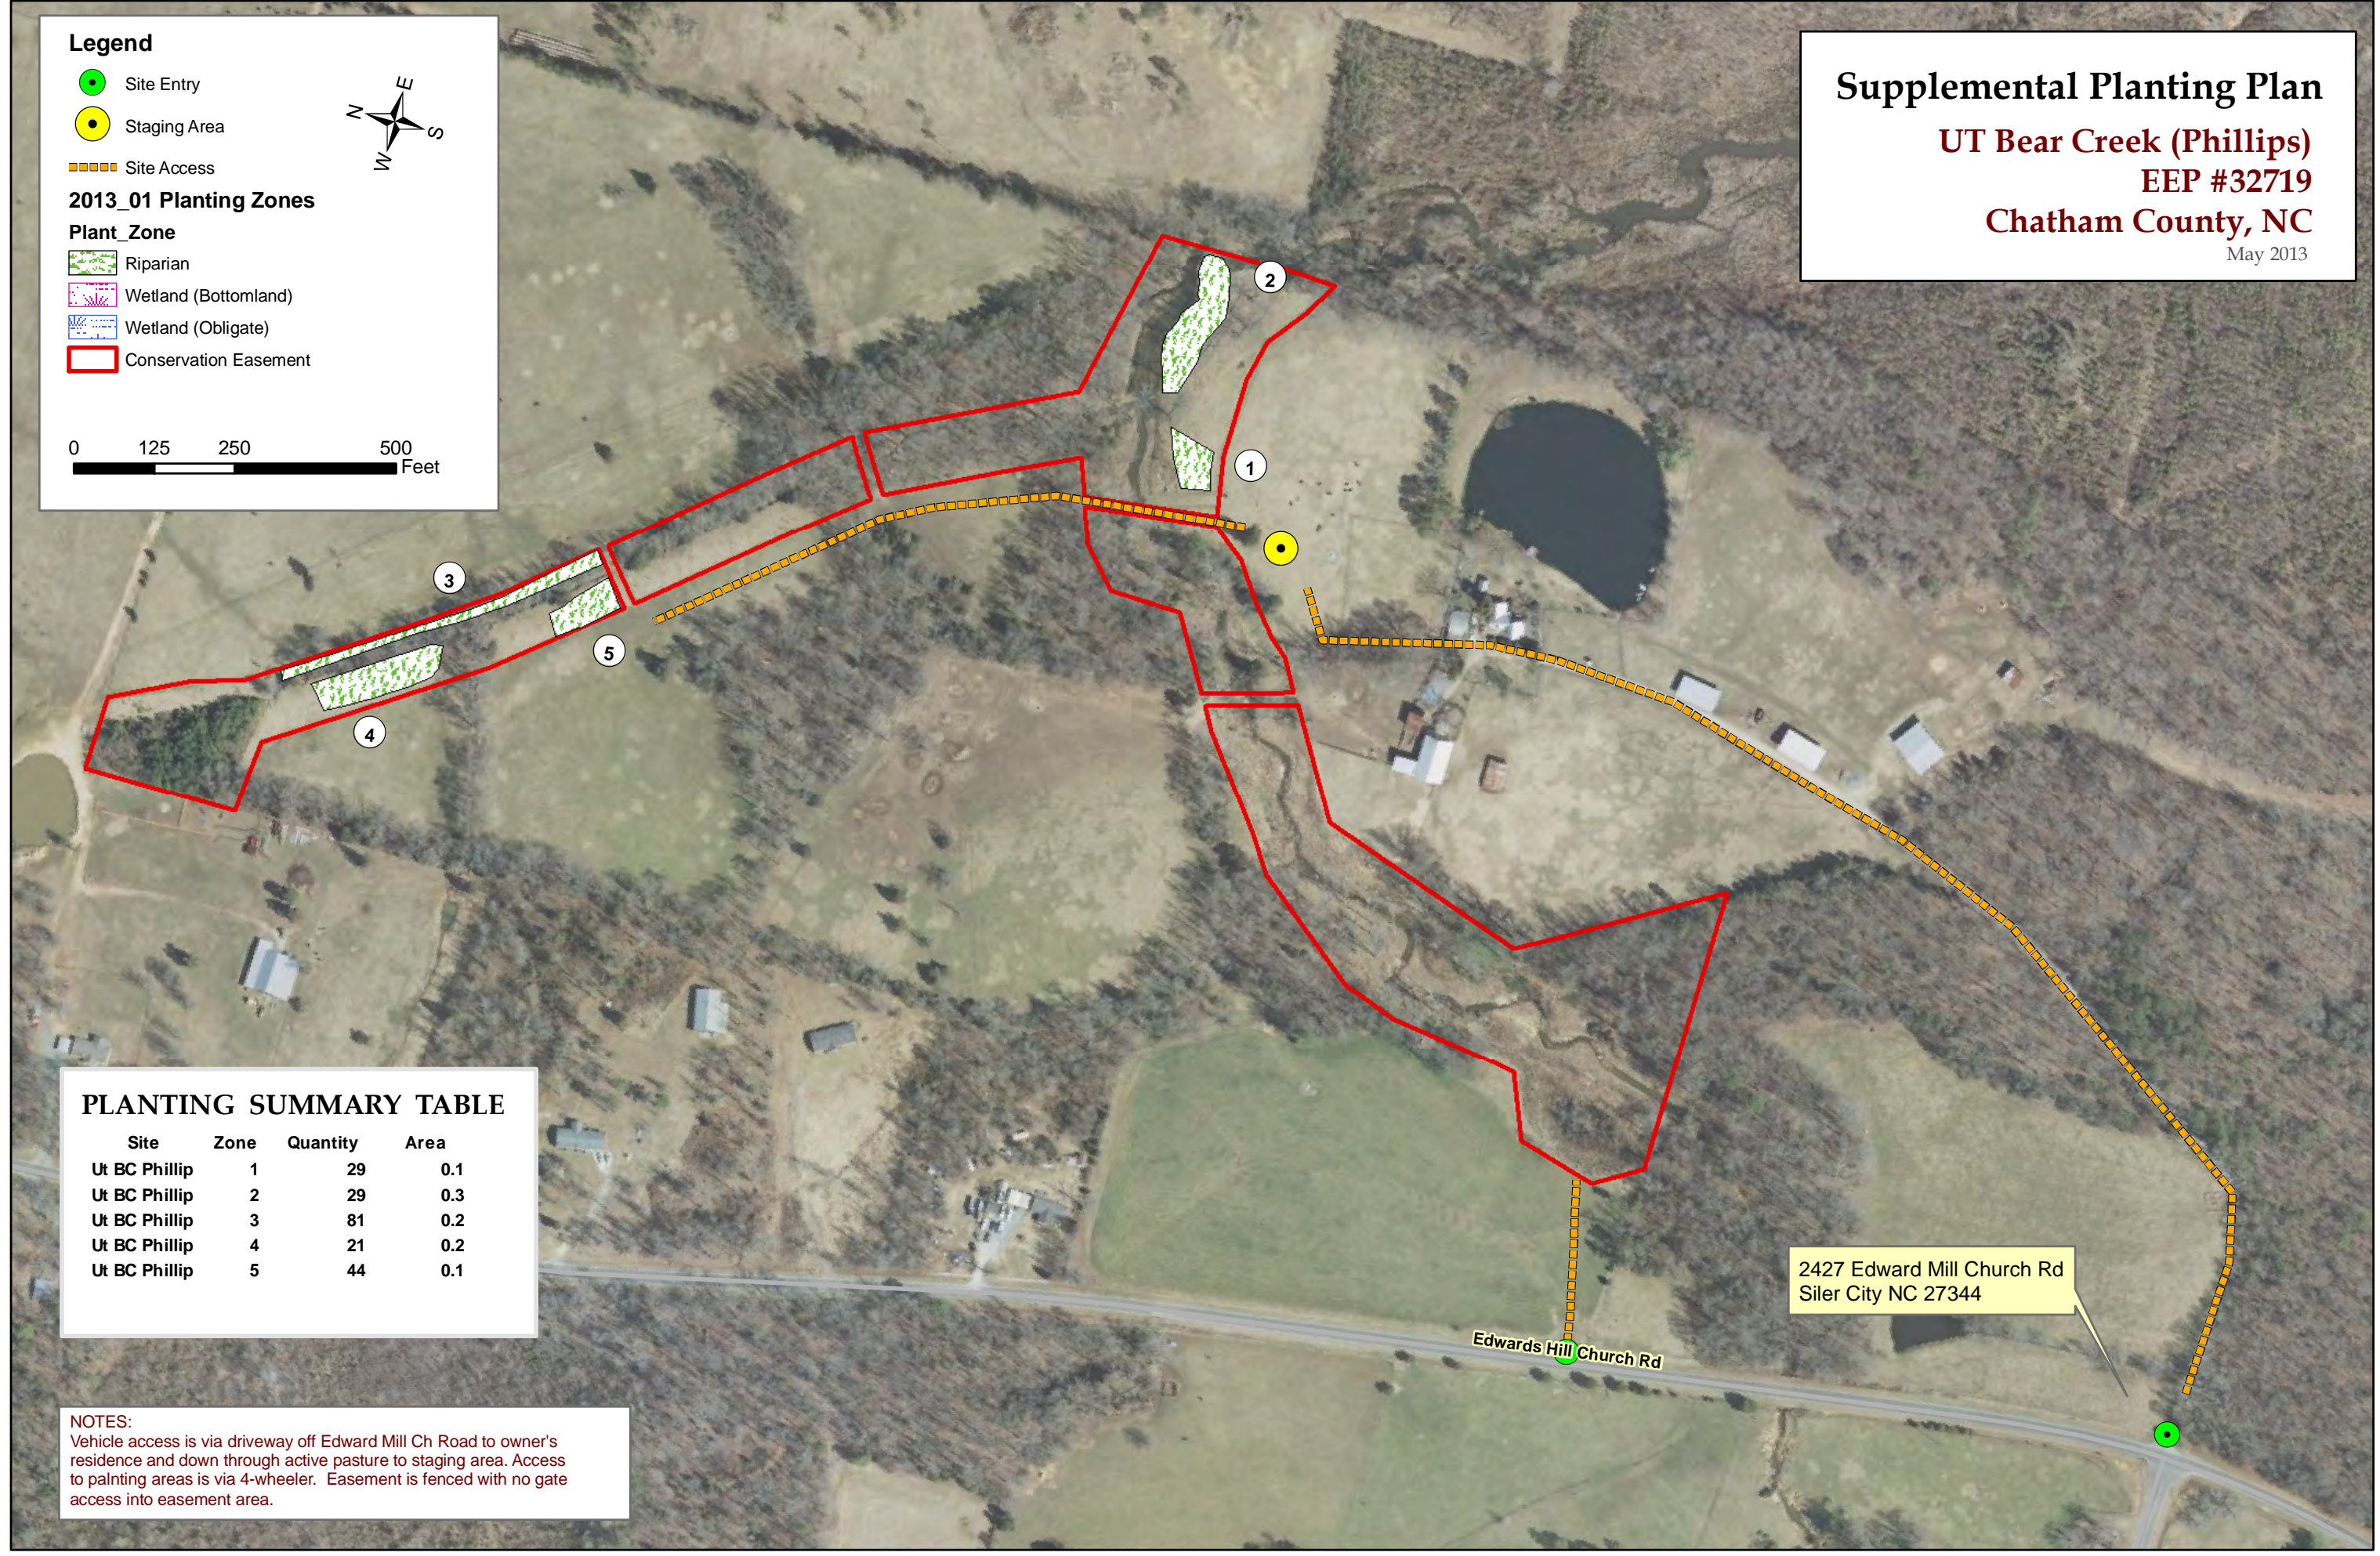

2427 Edward Mill Church Rd
 Siler City NC 27344

PLANTING SUMMARY TABLE

Site	Zone	Quantity	Area
Ut BC Phillip	1	29	0.1
Ut BC Phillip	2	29	0.3
Ut BC Phillip	3	81	0.2
Ut BC Phillip	4	21	0.2
Ut BC Phillip	5	44	0.1

NOTES:
 Vehicle access is via driveway off Edward Mill Ch Road to owner's residence and down through active pasture to staging area. Access to planting areas is via 4-wheeler. Easement is fenced with no gate access into easement area.

Appendix D

Hydrologic Data

Table 11. Verification of Bankfull Events			
Project Number and Name: 92719 - UT Bear Creek (Phillips)			
Date of Data Collection	Date of Occurrence	Method	Photo Number
11/17/2009	11/13/2009	Site visit to evaluate indicators of stage after storm events	N/A
10/8/2010	9/30/2010	Site visit to evaluate indicators of stage after storm	N/A
8/16/2011	unknown	Crest gauge	N/A
11/5/2012	unknown	Crest gauge	N/A

Due to the frequent beaver activity throughout the site, many parts of the site have had extended periods of backwater, therefore it has been difficult to determine bankfull events. From examining precipitation data in 2013 from the Siler City Airport weather station, it is likely that a 2.33” rain event on August 21, 2013 produced a bankfull event.
